HILLSBOROUGH COUNTY AVIATION AUTHORITY

PART 2 SUPPLEMENTAL CONTRACT C

FOR DESIGN-BUILD SERVICES

BETWEEN

HILLSBOROUGH COUNTY AVIATION AUTHORITY

AND

HENSEL PHELPS CONSTRUCTION CO.

PROJECT NOS. 8500 23 & 8515 24

AIRSIDE D DEVELOPMENT PROGRAM & CENTRALIZED CHECKED BAGGAGE SYSTEM

DATED FEBRUARY 5, 2025

SUPPLEMENTAL CONTRACT BETWEEN
OWNER AND DESIGN-BUILDER

TABLE OF ARTICLES

PART 2 SUPPLEMENTAL CONTRACT C

		PAGE
1.	GENERAL PROVISIONS	5
2.	BASIS OF COMPENSATION	5
3.	GUARANTEED COMPLETION DATE	6
4.	PAYMENTS	8
5.	SMALL BUSINESS ENTERPRISE (SBE) ASSURANCES	10
6.	UNBOUGHT SCOPE CONTINGENCY FUND	10
7.	TERMS AND CONDITIONS	12
8.	CONTRACT	13

ATTACHMENT 1 – GUARANTEED MAXIMUM PRICE (GMP) PROPOSAL
ATTACHMENT 2 – OWNER'S ALLOWANCES
ATTACHMENT 3 – HENSEL PHELPS SUBSTANTIAL COMPLETION AND MILESTONE SUMMARY
ATTACHMENT 4 – DESIGN-BUILDER'S ALLOWANCES

PART 2 SUPPLEMENTAL CONTRACT C

This Part 2 Supplemental Contract C (Contract) for design-build services is made and entered into this 5th day of February, 2026 by and between the Hillsborough County Aviation Authority, a public body corporate under the laws of the State of Florida, hereinafter referred to as the "Owner," and Hensel Phelps Construction Co., a Colorado Corporation, authorized to do business in the State of Florida, hereinafter referred to as the “Design-Builder”.

For the following Project: Airside D Development Program & Centralized Checked Baggage System

Authority Project Nos. 8500 23 & 8515 24

The Owner and Design-Builder agree as set forth below.

As part of the Part 2 Contract Between Owner and Design-Builder, dated December 5, 2024, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $91,066,666 and Substantial Completion date of December 17, 2025.

As part of the Change Order No. 1 ODP Between Owner and Design-Builder, dated April 18, 2025, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $90,016,106 and Substantial Completion date of December 17, 2025.

As part of the Change Order No. 2 Between Owner and Design-Builder, dated June 5, 2025, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $88,816,106 and Substantial Completion date of December 17, 2025.

As part of the Part 2 Supplemental Contract A Between Owner and Design-Builder, dated August 7, 2025, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $192,145,126 and Substantial Completion date of November 23, 2026.

As part of the Part 2 Supplemental Contract B Between Owner and Design-Builder, dated October 2, 2025, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $284,559,130.00 and established Substantial Completion of the Work for the structural steel elements no later than the Guaranteed Completion Date of March 30, 2027.

As part of the Change Order No. 3 Between Owner and Design-Builder, dated November 6, 2025 for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder replaced the Disadvantaged Business Enterprise (DBE) provisions with Small Business Enterprise (SBE) provisions and incorporated Supplemental Agreements A and B and Change Orders 1 and 2 into the Restated Part 2 Contract. The 12.8% DBE Goal for construction was revised to a 13.0% SBE Goal for construction.

As part of the Change Order No. 4 ODP Between Owner and Design-Builder, dated January 28, 2026, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $273,373,962.00.

As part of the Change Order No. 5 Between Owner and Design-Builder, dated January 28, 2026, for design-build services for Airside D Development Program & Westside Checked Baggage Screening System Relocation and Upgrades, Project Nos. 8500 23 & 8515 24, the Owner and Design-Builder established a GMP amount of $273,000,662.00.

ARTICLE 1
GENERAL PROVISIONS

The existing Part 2 Contract and all attachments, dated December 5, 2024, the Part 2 Supplemental Contract A and all attachments, dated August 7, 2025, the Part 2 Supplemental Contract B and all attachments, dated October 2, 2025, between Owner and Design-Builder, and Change Orders No. 1 ODP, 2, 3, 4 ODP & 5 as described above, are incorporated by reference herein to the extent not modified by this Part 2 Supplemental Contract C. The 100% Construction Drawings and Specifications for Airside D dated October 30, 2025 are incorporated by reference. The 100% Construction Drawings and Specifications for Centralized Checked Baggage Screening dated October 30, 2025 are incorporated by reference.

ARTICLE 2
BASIS OF COMPENSATION

Paragraph 21.2.1 of the Restated Part 2 Contract is deleted and replaced with the following:

21.2.1 For the Design-Builder's successful performance of the Work as described in the Contract Documents, the Owner will pay the Design-Builder the Cost of the Work plus the Design-Builder's 5.25% Fee up to the GMP Contract Sum of One Billion One Hundred Seventy Five Million One Hundred Twenty Two Thousand Eight Hundred Twelve and No Hundredth Dollars ($1,175,122,812), subject to additions and deductions by changes in the Work as provided in the Contract Documents.

The GMP amount is for the performance of the Work in accordance with the Part 2 Contract, as if fully contained herein, including but not limited to, Design-Builder's GMP proposal for the existing Part 2 Contract and all attachments, dated December 5, 2024, the Part 2 Supplemental Contract A and all attachments, dated August 7, 2025, the Part 2 Supplemental Contract B and all attachments, dated October 2, 2025, between Owner and Design-Builder, and Change Orders No. 1 ODP, 2, 3, 4 ODP & 5 as described above, and for Part 2 Supplemental Contract C, marked Attachment 1, as follows:

Attachment 1 - Part 2 Supplemental Contract A GMP proposal dated January 30, 2026, entitled "Supplemental C Submission Tampa International Airport Airside D Development Program & Centralized Checked Baggage System".

ARTICLE 3
GUARANTEED COMPLETION DATE

Article 23 of the Restated Part 2 Contract is deleted and replaced with the following:

23.1 The Design-Builder will commence the Work within 10 days of the date set by the Owner in a written Notice to Proceed. The Design-Builder will achieve Substantial Completion of the enabling Part 2 Contract Work no later than the Guaranteed Completion Date of December 17, 2025, subject to authorized adjustments and in accordance with the Contract Documents.

The Design-Builder will commence the Work within 10 days of the date set by the Owner in a written notice to proceed for Part 2 Supplemental Contract A. The Design-Builder will achieve Substantial Completion of the Part 2 Supplemental Contract A Work no later than the Guaranteed Completion Date of November 23, 2026 for Part 2 Supplemental Contract A subject to authorized adjustments and in accordance with the Contract Documents.

The Design-Builder will commence the Work within 10 days of the date set by the Owner in a written notice to proceed for Part 2 Supplemental Contract B. The Design-Builder will achieve Substantial Completion of the Work for the structural steel elements no later than the Guaranteed Completion Date of March 30, 2027 for Part 2 Supplemental Contract B subject to authorized adjustments and in accordance with the Contract Documents. The Centralized Checked Baggage System shall have no Substantial Completion Date established as part of the Part 2 Supplemental Contract B.

The Design-Builder will commence the Work within 10 days of the date set by the Owner in a written notice to proceed for Part 2 Supplemental Contract C. The Design-Builder will achieve Substantial Completion of the Work for the following milestones no later than the Guaranteed Completion Date of:

- April 8, 2027: Alstom early turnover.
- March 2, 2029: Supplemental C Project Substantial Completion (Phase 1)
- September 14, 2029: Supplemental C Project Substantial Completion (Phase 2 – Centralized Checked Baggage System 2-2).

subject to authorized adjustments and in accordance with the Contract Documents.

See ATTACHMENT 3 – HENSEL PHELPS SUBSTANTIAL COMPLETION AND MILESTONE SUMMARY.

23.2 It is mutually agreed between the parties that time is of the essence of this Contract and in the event the Supplemental A Work has not achieved Substantial Completion

by the Guaranteed Completion Date specified, it is agreed that from any money due or to become due to the Design-Builder or the Design-Builder's Surety, the Owner may retain the sum of Five Thousand and No One Hundredth Dollars ($5,000) per day, for each day thereafter, Sundays and holidays included, until the Work is substantially completed, not as a penalty but as liquidation of a reasonable portion of loss that will be incurred by the Owner if Work is not completed on or before the Guaranteed Completion Date(s).

It is mutually agreed between the parties that time is of the essence of this Contract and in the event the Supplemental B Work has not achieved Substantial Completion by the Guaranteed Completion Date specified, it is agreed that from any money due or to become due to the Design-Builder or the Design-Builder's Surety, the Owner may retain the sum of Five Thousand and No One Hundredth Dollars ($5,000) per day, for each day thereafter, Sundays and holidays included, until the Work is substantially completed, not as a penalty but as liquidation of a reasonable portion of loss that will be incurred by the Owner if Work is not completed on or before the Guaranteed Completion Date(s).

It is mutually agreed between the parties that time is of the essence of this Contract and in the event the Alstom early turnover Work has not achieved Substantial Completion by the Guaranteed Completion Date specified, it is agreed that from any money due or to become due to the Design-Builder or the Design-Builder's Surety, the Owner may retain the sum of Five Thousand and No One Hundredth Dollars ($5,000) per day, for each day thereafter, Sundays and holidays included, until the Alstom early turnover Work is substantially completed, not as a penalty but as liquidation of a reasonable portion of loss that will be incurred by the Owner if Work is not completed on or before the Guaranteed Completion Date.

- It is mutually agreed between the parties that time is of the essence of this Contract and in the event the Supplemental C Project Substantial Completion (Phase 1) Work has not achieved Substantial Completion by the Guaranteed Completion Date specified, it is agreed that from any money due or to become due to the Design-Builder or the Design-Builder's Surety, the Owner may retain the sum of Twenty Five Thousand and No One Hundredth Dollars ($25,000) per day, for each day thereafter, Sundays and holidays included, until the Supplemental C Project Substantial Completion (Phase 1) Work is substantially completed, not as a penalty but as liquidation of a reasonable portion of loss that will be incurred by the Owner if Work is not completed on or before the Guaranteed Completion Date.

  It is mutually agreed between the parties that time is of the essence of this Contract and in the event the Supplemental C Project Substantial Completion (Phase 2 – Centralized Checked Baggage System 2-2) Work has not achieved Substantial Completion by the Guaranteed Completion Date specified, it is agreed that from any money due or to become due to the Design-Builder or the Design-Builder's Surety,

the Owner may retain the sum of Five Thousand and No One Hundredth Dollars ($5,000) per day, for each day thereafter, Sundays and holidays included, until the Supplemental C Project Substantial Completion (Phase 2 – Centralized Checked Baggage System 2-2) Work is substantially completed, not as a penalty but as liquidation of a reasonable portion of loss that will be incurred by the Owner if Work is not completed on or before the Guaranteed Completion Date.

Multiple Substantial Completion Dates may be defined as part of this Contract. In addition, the Owner may retain different sums as liquidated damages if Work is not completed on or before the Substantial Completion Dates.

ARTICLE 4
PAYMENTS

Section 4.27 of the Restated Part 2 Contract is deleted and replaced with the following:

4.27 The Owner may decide not to approve payment and may withhold an application for payment, in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Owner's opinion, the representations required from Design-Builder cannot be made. If the Owner is unable to approve payment in the amount of the application, the Owner will notify the Design-Builder in writing of the Owner's reasons for withholding approval in whole or in part. If the Design-Builder and the Owner cannot agree on a revised amount, the Owner will approve payment for the amount for which the Owner is able to make such representations. The Owner may also decide not to approve payment or, because of subsequently discovered evidence or subsequent observations, may not approve the whole or a part of an application for payment previously issued, to such extent as may be necessary in the Owner's opinion to protect the Owner from loss because of:

4.27.1 Defective work not remedied;

4.27.2 Third-party claims filed or reasonable evidence indicating probable filing of such claims;

4.27.3 Damage to the Owner or another contractor;

4.27.4 Evidence that the Work will not be completed within the Contract Time;

4.27.5 Evidence that the unpaid balance would not be adequate to complete the Work;

4.27.6 Evidence that the unpaid balance would not be adequate to cover actual or liquidated damage for the anticipated delay;

4.27.7 Failure of the Design-Builder to carry out the Work in accordance with the Contract Documents;

4.27.8 Failure of the Design-Builder to achieve Substantial Completion of the Demo Second Half of Tunnel Structure Complete milestone by February 12, 2026;

4.27.9 Failure of the Design-Builder to achieve Substantial Completion of the Barrier Mounted AOA Fence Relocation Complete milestone by August 25, 2026;

4.27.10 Failure of the Design-Builder to achieve Substantial Completion of the Install of VGDS Found & Conduits Complete milestone by November 10, 2027;

4.27.11 Failure of the Design-Builder to achieve Substantial Completion of the Concessions White Box milestone by June 1, 2028;

4.27.12 Failure of the Design-Builder to achieve Substantial Completion of the Complete Delta Tenant Spaces White Box – Apron Level milestone by May 17, 2028;

4.27.13 Failure of the Design-Builder to achieve Substantial Completion of the Complete Delta Tenant Spaces White Box – Concourse Level milestone by April 14, 2028;

4.27.14 Failure of the Design-Builder to achieve Substantial Completion of the Complete Delta Tenant Spaces White Box – Mezzanine Level milestone by December 10, 2027;

4.27.15 Failure of the Design-Builder to achieve Substantial Completion of the Complete Paving & Utilities Interface for PBB Installation Start milestone by July 13, 2028.

4.27.16 Failure of the Design-Builder to achieve Substantial Completion of the SSCP Area Ready for TSA Equipment Installation milestone by August 21, 2028;

4.27.17 Failure of the Design-Builder to achieve Substantial Completion of the CBP Area Finishes Complete milestone by October 10, 2028; or

4.27.18 Failure of the Design-Builder to achieve Substantial Completion of the TSA ISAT BHS Testing Complete milestone by December 13, 2028;

See ATTACHMENT 3 – HENSEL PHELPS SUBSTANTIAL COMPLETION AND MILESTONE SUMMARY.

ARTICLE 5
SMALL BUSINESS ENTERPRISE (SBE) ASSURANCES

Section 28.3 of the Restated Part 2 Contract is deleted and replaced with the following:

28.3 SBE Goals. In compliance with the Owner's SBE Policy and Program, the Design-Builder's minimum SBE commitment is established as the sum total of the verified Letter(s) of Intent for each portion of the Project submitted with their response. The SBE goal stated below is the sum total of the certified SBE's listed in the Design-Builder's Fee and scope proposal which is attached hereto and which will be enforceable under the terms of this Contract. The Design-Builder will subcontract to certified DBEs at least 20.5% of the cumulative dollar value for the design Work earned under the Part 1 and this Part 2 Contract, and will subcontract to certified SBEs at least 12.2% of the dollar value of the construction Work earned under this Part 2 Contract.

ARTICLE 6
UNBOUGHT SCOPE CONTINGENCY FUND

Add the following to Article 4 of the Restated Part 2 Contract as Section 4.36

4.36 The Design-Builder's Unbought Scope Contingency Fund. A Design-Builder's Unbought Scope Contingency Fund of $11,235,700 is included as a specified amount in the GMP. It is further understood that the Unbought Scope Contingency Fund will only be utilized for the line-items identified in the attached unbought scope and cannot be utilized for any other scope items in the GMP. Upon completion of the buy-out of these unbought-scope items, all remaining funds in the Unbought Scope Contingency Fund shall be returned to the Owner. Use of contingency funds may be considered by the Owner for the following:

Item No.	Unbought Scope
1	**Demolition**
1.1	MT-D-S120D Opening
2	**Concrete**
2.1	Hot Weather Concreting (Chilled Water/Ice)
2.2	Flow fill at Slab On Grade ~~SOG~~
2.3	Supplemental Backfill ~~@~~ at Column Locations
2.4	3rd Party ~~FF~~ Floor Flatness Testing at Slab On Metal Deck ~~@ SOMD~~
3	**Masonry**
3.1	Masonry Dowels ~~&~~ and Wall Adjustments for Coordination
4	**Ornamental metals**
4.1	Owner Furnished Monitor Trim Details
4.2	Protection for Terrazzo Sequencing

5	**Roofing**
5.1	Roof Deck Shimming per ~~NRCA~~ National Roofing Contractors Association Standard
5.2	Roof Fall Protection - Permanent Recertification at ~~@~~ Project End
5.3	Infrared Survey for Roofing System
5.4	Roof Penetration Coordinated Additional
6	**Metal Panels & Siding**
6.1	Metal Panel Penetrations
7	**Acoustical Ceilings**
7.1	Ceiling Elevation Transition Coordination
8	**Interior Wall Panels**
8.1	Sign Coordination
8.2	Elevator Finish Coordination
8.3	~~MOT~~ Maintenance of Traffic/Dry-in Envelope Protection
9	**Fireproofing**
9.1	Patching of Fireproofing
9.2	Patching of Damaged Spray Fireproofing
9.3	Patching of Fireproofing ~~(CCBS)~~ Centralized Checked Baggage System
9.4	Patching of Damaged Spray Fireproofing
10	**Glass & Glazing**
10.1	Proprietary System Detail Coordination
10.2	CBP Compliance Testing/Certification
10.3	Window Protection and Maintenance
10.4	Field Chamber Testing
11	**Drywall & Related**
11.1	~~Temp.~~ Temporary Enclosures
11.2	Roof Protection
11.3	Interior Mock-up
11.4	Blocking for Art
11.5	Maintenance ~~& mods.~~ and Modifications of Dancefloor Scaffold
11.6	~~Ext~~ Exterior Weather Barriers
11.7	~~Temp~~ Temporary Construction Separation
11.8	T~~emp~~ Temporary Wall Area A/B ~~&~~ and ~~Rehab~~ Rehabilitation
11.9	~~Misc. arch. mods.~~ Miscellaneous Architectural Modifications
12	**Terrazzo**
12.1	Floor Leveling
12.2	Improved Floor Protection
12.3	~~Conc.~~ Concrete Moisture Mitigation
12.4	Escalator Transition
13	**Glass Handrail**
13.1	Additional Leading Edge Barriers for AHJ
13.2	Finish Material/~~struct.~~ Structural Substrate ~~reconc.~~ Reconciliation
13.3	Protection ~~GFRC~~ of Glass Fiber Reinforced Concrete

14	**Elevators & Escalators**
14.1	Composite Crew
14.2	Temporary Storage
14.3	Video/Audio Management System Design
14.4	Temporary Work Platforms
14.5	Cladding of Escalators
14.6	Elevator Operator During Construction
14.7	Elevator Usage/ Warranty During Construction
14.8	Elevator Usage Reinspection
14.9	Elevator Opening Protection for Construction
15	**Fire Protection**
15.1	Fire Sprinkler Systems Relocation for Interfaces
15.2	Fire Sprinkler Systems Relocation for Temp ~~FP~~ Fire Protection
16	**Sitework**
16.1	~~Vac~~ Vacuum Truck Excavation
16.2	SWPPP Maintenance & Relocations During Site Contractor ~~Demob~~ Demobilization
16.3	Curb, Gutter Repair/Replace
16.4	Landscape Area - Tree/Shrub/Grass/Irrigation Reestablishment
16.5	Municipal Comments on Utility Lines
16.6	~~GSE~~ Ground Support Equipment Marking Floor Striping
16.7	Bulletin 2 ~~FDC~~ Fire Department Connection Add
16.8	~~VDGS~~ Visual Docking Guidance System Poles
16.9	Gradation ~~&~~ and Cleaning Existing Stockpile Material
17	12 Months of ~~SWPPP Maint.~~ Storm Water Pollution Prevention Plan Maintenance
17.1	Reinforced Concrete Slab - Oil/Water Separator
17.2	Grease Trap Bearing Pads

All contingency fund charges will be tracked in a log by the Design-Builder. This log will be submitted, reviewed, and approved prior to the monthly application for payment. All payment of contingency funds is subject to approval by the Owner. All remaining funds in the Design-Builder's Unbought Scope contingency fund upon completion shall revert to the Owner. The Design-Builder's Unbought Scope contingency fund will not be used to fund liquidated damages.

ARTICLE 7
TERMS AND CONDITIONS

All other terms and conditions contained in the Part 2 Contract, Part 2 Supplemental Contract A, Part 2 Supplemental Contract B, Change Order No. 1 ODP, Change Order No. 2, Change Order No. 3, Change Order No. 4 ODP and Change Order No. 5, as modified by Part 2 Supplemental Contract C remain in full force and effect and are hereby ratified and confirmed.

ARTICLE 8
CONTRACT

This Contract is entered into as of the day and year first written above.

IN WITNESS WHEREOF, the parties hereto have set their hands and corporate seals by their proper officers, duly authorized to do so.

By the Design-Builder this _____ day of _____, 2026.

ATTEST:

_____

Hensel Phelps Construction Co.

By: _____

Title: _____

Print Name

_____

Print Address

_____

_____

Signed, sealed, and delivered
in the presence of:

_____
Witness

_____
Print Name

_____
Witness

_____
Print Name

Notary for Hensel Phelps Construction Co.

STATE OF _____
COUNTY OF _____

The foregoing instrument was acknowledged before me this ____ day of _____, 2026, by _____ in the capacity of _____, of _____ a _____
(Name of organization or company, if any) (Corporation / Partnership / Sole Proprietor / Other)
on _____ behalf. _____ _____
(Its / His / Her) (They are / He is / She is) (Personally known to me /not personally known to me)
_____ and _____ _____ take an oath.
and has produced the following document of identification) (they / he / she) (did / did not)

(*Seal of Notary*)

_____
Signature of Notary

By the Owner this 5th day of February, 2026.

HILLSBOROUGH COUNTY AVIATION AUTHORITY

(*Affix Corporate Seal*)

By: _____
Arthur F. Diehl III, Chairman

ATTEST:

_____
Jane Castor, Secretary

Signed, sealed, and delivered
in the presence of:

_____
Witness

_____
Print Name

_____
Witness

_____
Print Name

APPROVED AS TO FORM FOR LEGAL SUFFICIENCY:

By: _____
Michael Kamprath, Assistant General Counsel

Notary for Hillsborough County Aviation Authority

STATE OF FLORIDA
COUNTY OF HILLSBOROUGH

The foregoing instrument was acknowledged before me by means of □ physical presence or □ online authorization, this ____ day of _____, 202__, by Arthur F. Diehl III, in the capacity of Chairman, and by Jane Castor in the capacity of Secretary, for Hillsborough County Aviation Authority, a public body corporate under the laws of the State of Florida, on its behalf.

_____
Signature of Notary

_____
Print, Type, or Stamp Commissioned Name of Notary

HENSEL PHELPS
Plan. Build. Manage.

6557 Hazeltine National Dr., Suite One
Orlando, FL 32822
407-856-2400

January 30, 2026

James Hanney
Director of Procurement, Capital Programs and ITS
4100 George J. Bean Pkwy
Tampa, FL 33607

Subject: Supplemental C Submission
Tampa International Airport Airside D Development Program & Centralized Checked Baggage System

Dear Mr. Hanney:

Hensel Phelps is pleased to submit Supplemental C for the Tampa International Airport Airside D Development Program & Centralized Checked Baggage System Project. This GMP is based upon the design documents produced by HNTB, coordinated with Hillsborough County Aviation Authority stakeholders, and managed by Hensel Phelps as the Design Builder and is submitted for your approval.

The intention of this supplement is to incorporate into the scope for the project the remaining subcontractor trades for Airside D and the Centralized Checked Baggage System. This supplemental C will also re-baseline the contractor contingency for the remainder of the included scope. The general scope included in this package is as follows:

- Design/Builder General Conditions
- Airside D and CCBS Envelope Trades
- Airside D and CCBS Interior Trades

Should there be any questions or comments regarding the above list, please don't hesitate to contact the undersigned.

Sincerely,

HENSEL PHELPS CONSTRUCTION CO.

Drew Krizman
Program Director

GMP Supplemental C Table of Contents

Table of Contents

1. Cover Letter

2. Estimate
   a. Estimate Narrative
   b. Airside D Program Summary Costs
   c. CCBS Program Summary Costs
   d. Overall Program Summary Costs
   e. Airside D Estimate Detail
   f. CCBS Estimate Detail
   g. Contingency Reconciliation

3. General Conditions / General Requirements
   a. General Conditions Narrative
   b. General Conditions Report
   c. Staff Schedule
   d. Wage Tables

4. SBE Program
   a. SBE Participation Narrative
   b. SBE Participation Summary

5. Clarifications & Assumptions
   a. Clarifications & Assumptions

6. Design Assist Subcontractor Back-up
   a. Strucutral Steel – GMF Group
   b. Fiber Reinforcing – Strucutral
   c. Mechanical & Plumbing – BCH Mechanical
   d. Electrical – APG Electric
   e. Low Voltage – Mc Dean
   f. Pipe Bursting – Murphy Piping
   g. Baggage Handling – Daifuku

GMP Supplemental C Table of Contents

7. Bid Results – Wave 1 Subcontractors
   a. Demolition
   b. Concrete
   c. Masonry
   d. Ornamental Metals
   e. Waterproofing & Sealants
   f. Roofing
   g. Metal Panels & Siding
   h. Interior Wall Panels
   i. Sprayed Fireproofing
   j. Glass & Glazing
   k. Glass Handrail
   l. Drywall & Related
   m. Terrazzo
   n. Acoustical Ceilings
   o. Elevators & Escalators
   p. Fire Protection
   q. Sitework
   r. CA Services

8. Project Schedule
   a. Project Schedule – Critical Path (attached electronic file)
   b. Project Schedule – Full Schedule (attached electronic file)
   c. Project XER Schedule (attached electronic file)

9. Documents
   a. Bid Documents Reference

GMP Supplemental C Estimate Narrative

Supplemental C categorizes purchasing and allowances into three primary areas: Awarded Subcontract Values, Budget Values, and Allowance Values.

Estimate Values:

The estimating team completed a solicitation and competitive bid process for the following trades:

- Demolition
- Turnkey Concrete
- Masonry
- Ornamental Metals
- Sprayed Fireproofing & Insulation
- Metal Panels
- Roofing & Related
- Waterproofing, Caulking & Related
- Glass & Glazing
- Acoustical Ceilings
- Drywall & Related
- Terrazzo
- Elevators & Escalators
- Fire Protection
- Sitework
- Glass Handrail
- Interior Wall Panels

The results of the bidding process and subsequent purchasing meetings are included within this Supplemental. The remaining trades will be competitively bid in Q1 2026 or later based upon optimization of market conditions and production lead times.

This future package will include the following trades:

- Final Clean
- Scaffolding
- Millwork
- Doors, Frames & Hardware
- Overhead Doors
- Flooring
- Paint & Wallcovering
- Tile & Stone
- Access Flooring
- Building Specialties
- Signage
- Furniture, Fixtures & Equipment (FF&E)
- Interior Trees
- Airport Access Control
- Fencing
- Window Coverings
- Play Structures
- Additional packages as may be required based on subcontractor feedback

Allowance Values:

Allowance values and their justifications are fully explained in the Clarifications and Assumptions section of this GMP Supplemental submission.

Summary Sheets

Airside D Element Cumulative Summary

	Enabling Awarded Value	Supplemental A Awarded Value	Supplemental B Awarded Value	Supplemental C	Total
A10 - FOUNDATIONS	$ -	$ 15,815,835	$ -	$ 2,234,813	$ 18,050,648
B10 - SUPERSTRUCTURE	$ -	$ 208,588	$ 55,299,848	$ 20,412,948	$ 75,921,384
B20 - EXTERIOR CLOSURES	$ -	$ 15,788,536	$ -	$ 25,616,200	$ 41,404,736
B30 - ROOFING	$ -	$ -	$ -	$ 10,433,000	$ 10,433,000
C10 - INTERIOR CONSTRUCTION	$ -	$ -	$ -	$ 15,373,046	$ 15,373,046
C20 - STAIRS	$ -	$ -	$ -	$ 5,848,000	$ 5,848,000
C30 - INTERIOR FINISHES	$ -	$ -	$ -	$ 52,073,937	$ 52,073,937
D10 - CONVEYING	$ -	$ -	$ 2,520,841	$ 135,171,029	$ 137,691,870
D20 - PLUMBING	$ -	$ 1,679,048	$ -	$ 15,533,514	$ 17,212,562
D30 - HVAC	$ -	$ 8,059,535	$ -	$ 58,239,153	$ 66,298,688
D40 - FIRE PROTECTION	$ -	$ -	$ -	$ 5,461,440	$ 5,461,440
D50 - ELECTRICAL	$ -	$ 16,667,330	$ 3,650,380	$ 110,576,534	$ 130,894,244
E10 - EQUIPMENT	$ -	$ -	$ -	$ 1,662,000	$ 1,662,000
E20 - FURNISHINGS	$ -	$ -	$ -	$ 8,367,097	$ 8,367,097
F10 - SPECIAL CONSTRUCTION	$ -	$ -	$ -	$ -	$ -
F20 - FACILITY REMEDIATION	$ -	$ -	$ 484,000	$ -	$ 484,000
G10 - SITE PREPARATION	$ -	$ -	$ -	$ 24,597,200	$ 24,597,200
G20 - SITE IMPROVEMENTS	$ -	$ -	$ -	$ 223,449	$ 223,449
G30 - LIQUID AND GAS SITE UTILITIES	$ -	$ -	$ -	$ -	$ -
G40 - ELECTRICAL SITE IMPROVEMENTS	$ -	$ -	$ -	$ -	$ -
G90 - MISCELLANEOUS SITE CONSTRUCTION	$ 44,303,800	$ -	$ -	$ 434,150	$ 44,737,950
Z99 - ALLOWANCE	$ -	$ -	$ -	$ 11,636,972	$ 11,636,972
Subtotal	**$ 44,303,800**	**$ 58,218,872**	**$ 61,955,069**	**$ 503,894,480**	**$ 668,372,221**
Markups					
ESTIMATED COST OF WORK	**$ 5,491,000**	**$ 5,304,430**	**$ 420,392**	**$ 12,172,038**	**$ 23,387,860**
General Requirements	$ -	$ 5,304,430	$ 148,692	$ 10,965,800	$ 16,418,922
CCBS General Requirements (56%)	$ -	$ -	$ -	$ 1,206,238	$ 1,206,238
A & E Design Costs - With Part 1	$ -	$ -	$ -	$ -	$ -
Testing & Inspections	$ 5,491,000	$ -	$ 271,700	$ -	$ 5,762,700
COST OF WORK SUBTOTAL	**$ 32,524,870**	**$ 19,540,139**	**$ 7,716,465**	**$ 119,326,626**	**$ 179,108,100**
D/B Contingency	$ 3,540,471	$ 3,176,165	$ 3,239,657	$ 25,803,326	$ 35,759,619
D/B Contingency True-up from Previous Supplements	$ -	$ -	$ -	$ (1,193,723)	$ (1,193,723)
Sub Bonds	$ 1,062,141	$ 952,850	$ 935,632	$ 7,740,998	$ 10,691,621
General Conditions	$ 21,014,616	$ 15,351,124	$ 2,553,012	$ 57,430,992	$ 96,349,744
General Conditions CCBS (56%)	$ -	$ -	$ -	$ 6,317,409	$ 6,317,409
A & E Design Costs - Part 2 CA Services	$ 6,907,642	$ 60,000	$ 988,164	$ 20,140,345	$ 28,096,151
A & E Design Costs - Part 2 CA Services CCBS 56%	$ -	$ -	$ -	$ 3,087,279	$ 3,087,279
SUBTOTAL	**$ 7,746,996**	**$ 19,250,740**	**$ 5,581,758**	**$ 53,071,976**	**$ 85,651,470**
Contractor's Fee, Overhead & Insurance	$ 5,710,516	$ 5,762,443	$ 4,862,557	$ 44,079,764	$ 60,415,280
Permits	$ 123,480	$ 124,595	$ 105,138	$ 953,090	$ 1,306,303
Builder's Risk Insurance	$ 1,181,287		$ -	$ 2,112,000	$ 3,293,287
Builder's Risk Insurance Policy Lump Sum Delta		$ 12,533,462	$ -	$ -	$ 12,533,462
Contractor's Bonds	$ 731,713	$ 830,240	$ 614,063	$ 5,927,123	$ 8,103,139
OWNER ALLOWANCES	**$ 1,000,000**	**$ 1,014,839**	**$ 750,596**	**$ 49,205,538**	**$ 51,970,973**
Art Allowance By HCAA	$ -	$ -	$ -	$ -	$ -
Owner Allowance CCBS	$ -	$ -	$ -	$ 1,205,538	$ 1,205,538
Owner Allowance	$ 1,000,000	$ 1,014,839	$ 750,596	$ 48,000,000	$ 50,765,435
Subtotal	**$ 46,762,866**	**$ 45,110,148**	**$ 14,469,211**	**$ 233,776,179**	**$ 340,118,404**
Change Orders #1, 2, 3, 4, & 5	**$ (2,250,560)**	**$ -**	**$ -**	**$ -**	**$ (2,250,560)**
Grand Total	**$ 88,816,106**	**$ 103,329,020**	**$ 76,424,280**	**$ 737,670,659**	**$ 1,006,240,065**
	Enabling	Supplemental A	Supplemental B	Supplemental C	Current Project Total

CCBS Element Cumulative Summary

	Enabling Awarded Value	Supplemental A Awarded Value	Supplemental B Awarded Value	Supplemental C	Total
A10 - FOUNDATIONS	$ -	$ -	$ -	$ 69,992	$ 69,992
B10 - SUPERSTRUCTURE	$ -	$ -	$ 560,000	$ 3,303,018	$ 3,863,018
B20 - EXTERIOR CLOSURES	$ -	$ -	$ -	$ 254,800	$ 254,800
B30 - ROOFING	$ -	$ -	$ -	$ -	$ -
C10 - INTERIOR CONSTRUCTION	$ -	$ -	$ -	$ 271,062	$ 271,062
C20 - STAIRS	$ -	$ -	$ -	$ -	$ -
C30 - INTERIOR FINISHES	$ -	$ -	$ -	$ 1,603,754	$ 1,603,754
D10 - CONVEYING	$ -	$ -	$ 3,208,343	$ 106,871,797	$ 110,080,140
D20 - PLUMBING	$ -	$ -	$ -	$ 215,813	$ 215,813
D30 - HVAC	$ -	$ -	$ -	$ 2,118,094	$ 2,118,094
D40 - FIRE PROTECTION	$ -	$ -	$ -	$ 686,560	$ 686,560
D50 - ELECTRICAL	$ -	$ -	$ 4,645,938	$ 9,706,604	$ 14,352,542
E10 - EQUIPMENT	$ -	$ -	$ -	$ -	$ -
E20 - FURNISHINGS	$ -	$ -	$ -	$ 56,000	$ 56,000
F10 - SPECIAL CONSTRUCTION	$ -	$ -	$ -	$ -	$ -
F20 - FACILITY REMEDIATION	$ -	$ -	$ 616,000	$ -	$ 616,000
G10 - SITE PREPARATION	$ -	$ -	$ -	$ 800,800	$ 800,800
G20 - SITE IMPROVEMENTS	$ -	$ -	$ -	$ -	$ -
G30 - LIQUID AND GAS SITE UTILITIES	$ -	$ -	$ -	$ -	$ -
G40 - ELECTRICAL SITE IMPROVEMENTS	$ -	$ -	$ -	$ -	$ -
G90 - MISCELLANEOUS SITE CONSTRUCTION	$ -	$ -	$ -	$ -	$ -
Z99 - ALLOWANCE	$ -	$ -	$ -	$ 2,958,384	$ 2,958,384
Subtotal	**$ -**	**$ -**	**$ 9,030,281**	**$ 128,916,680**	**$ 137,946,961**
Markups					
ESTIMATED COST OF WORK	**$ -**	**$ -**	**$ 535,045**	**$ 1,535,212**	**$ 2,070,257**
General Requirements	$ -	$ -	$ 189,245	$ -	$ 189,245
CCBS General Requirements (56%)	$ -	$ -	$ -	$ 1,535,212	$ 1,535,212
A & E Design Costs - With Part 1	$ -	$ -	$ -	$ -	$ -
Testing & Inspections	$ -	$ -	$ 345,800	$ -	$ 345,800
COST OF WORK SUBTOTAL	**$ -**	**$ -**	**$ 5,099,523**	**$ 20,448,976**	**$ 25,548,499**
D/B Contingency	$ -	$ -	$ 669,573	$ 6,522,595	$ 7,192,168
D/B Contingency True-up from Previous Supplements	$ -	$ -	$ -	$ -	$ -
Sub Bonds	$ -	$ -	$ 143,480	$ 1,956,778	$ 2,100,258
General Conditions	$ -	$ -	$ 3,249,287	$ -	$ 3,249,287
General Conditions CCBS (56%)	$ -	$ -	$ -	$ 8,040,339	$ 8,040,339
A & E Design Costs - Part 2 CA Services	$ -	$ -	$ 1,037,183	$ -	$ 1,037,183
A & E Design Costs - Part 2 CA Services CCBS 56%	$ -	$ -	$ -	$ 3,929,265	$ 3,929,265
SUBTOTAL	**$ -**	**$ -**	**$ 1,167,832**	**$ 12,016,302**	**$ 13,184,134**
Contractor's Fee, Overhead & Insurance	$ -	$ -	$ 1,017,359	$ 10,468,597	$ 11,485,956
Permits	$ -	$ -	$ 21,997	$ 226,351	$ 248,348
Builder's Risk Insurance	$ -	$ -	$ -	$ -	$ -
Builder's Risk Insurance Policy Lump Sum Delta	$ -	$ -	$ -	$ -	$ -
Contractor's Bonds	$ -	$ -	$ 128,476	$ 1,321,354	$ 1,449,830
OWNER ALLOWANCES	**$ -**	**$ -**	**$ 157,042**	**$ 1,534,321**	**$ 1,691,363**
Art Allowance By HCAA	$ -	$ -	$ -	$ -	$ -
Owner Allowance	$ -	$ -	$ 157,042	$ 1,534,321	$ 1,691,363
Subtotal	**$ -**	**$ -**	**$ 6,959,442**	**$ 35,534,812**	**$ 42,494,254**
Change Orders #1, 2, 3, 4, & 5	**$ -**	**$ -**	**$ -**	**$ -**	**$ -**
Grand Total	**$ -**	**$ -**	**$ 15,989,723**	**$ 164,451,491**	**$ 180,441,214**
	Enabling	Supplemental A	Supplemental B	Supplemental C	Current Project Total

Overall Program Summary

	Enabling 100% CD's	Supplemental A Foundations & Long Lead	Supplemental B	ITB 1 Apron & Fueling	ITB 2 PBB	ITB 3 Guideway	Supplemental C	
A10 - FOUNDATIONS	$ -	$ 15,815,835	$ -	$ -	$ -	$ -	$ 2,304,805	$ 18,120,640
B10 - SUPERSTRUCTURE	$ -	$ 208,588	$ 55,859,848	$ -	$ -	$ -	$ 23,715,966	$ 79,784,402
B20 - EXTERIOR CLOSURES	$ -	$ 15,788,536	$ -	$ -	$ -	$ -	$ 25,871,000	$ 41,659,536
B30 - ROOFING	$ -	$ -	$ -	$ -	$ -	$ -	$ 10,433,000	$ 10,433,000
C10 - INTERIOR CONSTRUCTION	$ -	$ -	$ -	$ -	$ -	$ -	$ 15,644,108	$ 15,644,108
C20 - STAIRS	$ -	$ -	$ -	$ -	$ -	$ -	$ 5,848,000	$ 5,848,000
C30 - INTERIOR FINISHES	$ -	$ -	$ -	$ -	$ -	$ -	$ 53,677,691	$ 53,677,691
D10 - CONVEYING	$ -	$ -	$ 5,729,184	$ -	$ -	$ -	$ 242,042,826	$ 247,772,010
D20 - PLUMBING	$ -	$ 1,679,048	$ -	$ -	$ -	$ -	$ 15,749,327	$ 17,428,375
D30 - HVAC	$ -	$ 8,059,535	$ -	$ -	$ -	$ -	$ 60,357,247	$ 68,416,782
D40 - FIRE PROTECTION	$ -	$ -	$ -	$ -	$ -	$ -	$ 6,148,000	$ 6,148,000
D50 - ELECTRICAL	$ -	$ 16,667,330	$ 8,296,318	$ -	$ -	$ -	$ 120,283,138	$ 145,246,786
E10 - EQUIPMENT	$ -	$ -	$ -	$ -	$ -	$ -	$ 1,662,000	$ 1,662,000
E20 - FURNISHINGS	$ -	$ -	$ -	$ -	$ -	$ -	$ 8,423,097	$ 8,423,097
F10 - SPECIAL CONSTRUCTION	$ -	$ -	$ -	$ -	$ -	$ -	$ -	$ -
F20 - FACILITY REMEDIATION	$ -	$ -	$ 1,100,000	$ -	$ -	$ -	$ -	$ 1,100,000
G10 - SITE PREPARATION	$ -	$ -	$ -	$ -	$ -	$ -	$ 25,398,000	$ 25,398,000
G20 - SITE IMPROVEMENTS	$ -	$ -	$ -	$ -	$ -	$ -	$ 223,449	$ 223,449
G30 - LIQUID AND GAS SITE UTILITIES	$ -	$ -	$ -	$ -	$ -	$ -	$ -	$ -
G40 - ELECTRICAL SITE IMPROVEMENTS	$ -	$ -	$ -	$ -	$ -	$ -	$ -	$ -
G90 - MISCELLANEOUS SITE CONSTRUCTION	$ 44,303,800	$ -	$ -	$ -	$ -	$ -	$ 434,150	$ 44,737,950
Z99 - GENERAL REQUIREMENTS	$ -	$ -	$ -	$ -	$ -	$ -	$ 14,595,356	$ 14,595,356
Subtotal	**$ 44,303,800**	**$ 58,218,872**	**$ 70,985,350**	**$ -**	**$ -**	**$ -**	**$ 632,811,160**	**$ 806,319,182**
Markups								
ESTIMATED COST OF WORK	**$ 5,491,000**	**$ 5,304,430**	**$ 955,437**	**$ -**	**$ -**	**$ -**	**$ 13,707,250**	**$ 25,458,117**
LEED Silver Premium	$ -	$ -	$ -	$ -	$ -	$ -	$ -	**$ -**
General Requirements	$ -	$ 5,304,430	$ 337,937	$ -	$ -	$ -	$ 12,501,012	**$ 18,143,379**
CCBS General Requirements (44%)	$ -	$ -	$ -	$ -	$ -	$ -	$ 1,206,238	**$ 1,206,238**
A & E Design Costs - With Part 1	$ -	$ -	$ -	$ -	$ -	$ -	$ -	**$ -**
Testing & Inspections	$ 5,491,000	$ -	$ -	$ -	$ -	$ -	$ -	**$ 5,491,000**
Testing & Inspections - WCBSS	$ -	$ -	$ 617,500				$ -	**$ 617,500**
COST OF WORK SUBTOTAL	**$ 32,524,870**	**$ 19,540,139**	**$ 12,815,989**	**$ -**	**$ -**	**$ -**	**$ 139,775,603**	**$ 204,656,601**
ASD D/B Contingency	$ 3,540,471	$ 3,176,165	$ -	**$ -**	**$ -**	$ -	$ 25,803,326	**$ 32,519,962**
CCBS D/B Contingency	$ -	$ -	$ 3,909,230	**$ -**	**$ -**	$ -	$ 6,522,595	**$ 10,431,825**
D/B Contingency True-up from Previous Supplements							$ (1,193,723)	**$ (1,193,723)**
Airsides Realingments D/B Contingency	$ -	$ -	$ -	**$ -**	**$ -**	$ -	$ -	**$ -**
Tarriff Contingency - By Owner	$ -	$ -	$ -	**$ -**	**$ -**	$ -	$ -	**$ -**
Sub Bonds	$ 1,062,141	$ 952,850	$ 1,079,112	**$ -**	**$ -**	$ -	$ 9,697,776	**$ 12,791,880**
General Conditions	$ 21,014,616	$ 15,351,124	$ 5,802,299	**$ -**	**$ -**	$ -	$ 65,471,331	**$ 107,639,370**
General Conditions CCBS (56%)	$ -	$ -	$ -	**$ -**	**$ -**	$ -	$ 6,317,409	**$ 6,317,409**
A & E Design Costs - Part 2 CA Services	$ 6,907,642	$ 60,000	$ 2,025,347	**$ -**	**$ -**	$ -	$ 20,140,345	**$ 29,133,334**
A & E Design Costs - Part 2 CA Services CCBS	$ -	$ -	$ -	**$ -**	**$ -**	$ -	$ 7,016,544	**$ 7,016,544**
SUBTOTAL	**$ 7,746,996**	**$ 19,250,740**	**$ 6,749,590**	**$ -**	**$ -**	**$ -**	**$ 65,088,279**	**$ 98,835,605**
Contractor's Fee, Overhead & Insurance	$ 5,710,516	$ 5,762,443	$ 5,879,916	**$ -**	**$ -**	$ -	$ 54,548,361	**$ 71,901,236**
Permits	$ 123,480	$ 124,595	$ 127,135	**$ -**	**$ -**	$ -	$ 1,179,441	**$ 1,554,651**
Builder's Risk Insurance	$ 1,181,287	$ -	$ -	**$ -**	**$ -**	$ -	$ 2,112,000	**$ 3,293,287**
Builder's Risk Insurance Policy Lump Sum Delta	$ -	$ 12,533,462	$ -	**$ -**	**$ -**	$ -	$ -	**$ 12,533,462**
Contractor's Bonds	$ 731,713	$ 830,240	$ 742,539	**$ -**	**$ -**	$ -	$ 7,248,477	**$ 9,552,969**
HCAA ADD ON'S	**$ 1,000,000**	**$ 1,014,839**	**$ 907,638**	**$ -**	**$ -**	**$ -**	**$ 50,739,859**	**$ 53,662,336**
Art Allowance By HCAA	$ -	$ -	$ -	**$ -**	**$ -**	$ -	$ -	**$ -**
Owner Allowance	$ 1,000,000	$ 1,014,839	$ 907,638	$ -	$ -	$ -	$ 50,739,859	**$ 53,662,336**
HCAA AWARDS	$ -	$ -	$ -	$ -	$ -	$ -	$ -	**$ -**
ITB Awards	$ -	$ -	$ -	$ 81,549,326	$ 55,608,615	$ 22,214,398	$ -	**$ 159,372,339**
Subtotal	**$ 46,762,866**	**$ 45,110,148**	**$ 21,428,654**	**$ 81,549,326**	**$ 55,608,615**	**$ 22,214,398**	**$ 269,310,990**	**$ 541,984,997**
Change Orders	$ (2,250,560)							**$ (2,250,560)**
Grand Total	**$ 88,816,106**	**$ 103,329,020**	**$ 92,414,004**	**$ 81,549,326**	**$ 55,608,615**	**$ 22,214,398**	**$ 902,122,150**	**$ 1,346,053,619**
	Enabling	Supplemental A	Supplemental B	HCAA Award	HCAA Award	HCAA Award	Supplemental C	$ 1,346,053,619

GMP Estimate Detail

Airside D Program

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Client: Hillsborough County Airport Authority

Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
0	**Items**				
1	**ASD - 8500 23 Airside D Building**			**693.37**	**415,385,226**
1.1	**0145 - Testing Services**			**0.06**	**36,000**
1.1.1	Testing & Inspections - Geotech Inspections		1.00 lsum	36,000.00	36,000
1.2	**0174 - Final Cleaning**			**1.50**	**897,996**
1.2.1	Budget - Final Clean-Up from 90% Estimate		1.00 lsum	897,996.00	897,996
1.3	**0240 - Demolition**			**0.80**	**478,000**
1.3.1	Bid Result - Demolition - Northstar		1.00 lsum	478,000.00	478,000
1.4	**0300 - Turnkey Concrete**			**19.51**	**11,691,000**
1.4.1	Bid Result - Elevated Concrete - Liberty		1.00 lsum	11,691,000.00	11,691,000
1.5	**0420 - Masonry**			**3.59**	**2,153,000**
1.5.1	Bid Result - Masonry - TBD		1.00 lsum	2,153,000.00	2,153,000
1.6	**0510 - Structural & Misc Steel**			**2.97**	**1,777,423**
1.6.1	Structural & Miscellaneous Steel - GMF - Design Assist Partner		1.00 lsum	1,777,423.00	1,777,423
1.7	**0570 - Ornamental Metals**			**8.76**	**5,246,000**
1.7.1	Bid Result - Ornamental Metals - Acousti		1.00 lsum	5,246,000.00	5,246,000
1.8	**0610 - Rough Carpentry**			**1.10**	**660,505**
1.8.1	Budget - Rough Carpentry from 90% Estimate		1.00 lsum	660,505.00	660,505
1.9	**0640 - Millwork**			**10.28**	**6,157,704**
1.9.1	Budget - Millwork from 90% Estimate		1.00 lsum	5,085,704.00	5,085,704
1.9.2	Budget - Millwork Gate Podiums from 60% Estimate		1.00 lsum	1,072,000.00	1,072,000
1.10	**0710 - Waterproofing and Sealants**			**2.23**	**1,333,000**
1.10.1	Bid Result - Caulking & Waterproofing - Apex		1.00 lsum	1,333,000.00	1,333,000
1.11	**0730 - Roofing**			**17.41**	**10,433,000**
1.11.1	Bid Result - Roofing - Architectural Sheet Metal		1.00 lsum	10,433,000.00	10,433,000
1.12	**0745 - Metal Wall Panels & Siding**			**6.48**	**3,885,000**
1.12.1	Bid Result - Metal Panels - Cladding Systems		1.00 lsum	3,885,000.00	3,885,000
1.13	**0750 - Interior Wall Panels**			**3.12**	**1,867,000**
1.13.1	Bid Result - Wall Panels - Acousti		1.00 lsum	1,867,000.00	1,867,000
1.14	**0781 - Sprayed Fireproofing**			**6.58**	**3,943,000**
1.14.1	Bid Result - Sprayed Fireproofing & Insulation - Rolling Plains		1.00 lsum	3,943,000.00	3,943,000
1.15	**0810 - Doors, Frames and Hardware**			**6.75**	**4,042,800**
1.15.1	Allowance - Doors Frames & Hardware from 90% Estimate		1.00 lsum	4,042,800.00	4,042,800
1.16	**0833 - Overhead Doors**			**2.49**	**1,492,600**
1.16.1	Budget - Overhead Doors from 90% Estimate		1.00 lsum	1,492,600.00	1,492,600
1.17	**0880 - Glass and Glazing**			**29.16**	**17,469,000**
1.17.1	Bid Result - Glass & Glazing - West Tampa Glass		1.00 lsum	17,469,000.00	17,469,000
1.18	**0890 - Glass Handrail**			**3.66**	**2,195,000**
1.18.1	Bid Result - Glass Handrail - Stainless Fabricators		1.00 lsum	2,195,000.00	2,195,000
1.19	**0920 - Drywall & Related**			**35.81**	**21,452,000**
1.19.1	Bid Result - Drywall & Related - Kenpat		1.00 lsum	21,452,000.00	21,452,000
1.20	**0930 - Tile**			**8.61**	**5,160,730**
1.20.1	Budget - Tile from 90% Estimate		1.00 lsum	5,160,730.00	5,160,730

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimator: James Cobb
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Job Size: 597,998 sf
Client: Hillsborough County Airport Authority
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
1.21	**0940 - Terrazzo**			**9.76**	**5,848,000**
1.21.1	Bid Result - Terrazzo - David Allen		1.00 lsum	5,848,000.00	5,848,000
1.22	**0951 - Acoustical Ceilings**			**9.50**	**5,692,000**
1.22.1	Bid Result - Acoustical Ceilings - Acousti		1.00 lsum	5,692,000.00	5,692,000
1.23	**0965 - Resilient & Carpet Flooring**			**3.06**	**1,831,337**
1.23.1	Budget - Resilient & Carpet Flooring from 90% Estimate		1.00 lsum	1,831,337.00	1,831,337
1.24	**0967 - Specialty Flooring**			**1.25**	**750,454**
1.24.1	Budget - Speciality Flooring from 90% Estimate		1.00 lsum	750,454.00	750,454
1.25	**0990 - Painting & Wallcovering**			**5.97**	**3,579,286**
1.25.1	Budget - Paint & Walcovering from 90% Estimate		1.00 lsum	3,579,286.00	3,579,286
1.26	**1000 - Building Specialties**			**0.30**	**177,150**
1.26.1	Budget - Building Specialites from 90% Estimate		1.00 lsum	177,150.00	177,150
1.27	**1016 - Toilet Partitions & Accessories**			**2.32**	**1,387,314**
1.27.1	Budget Toilet Partitions & Accessories from 90% Estimate		1.00 lsum	1,387,314.00	1,387,314
1.28	**1026 - Wall Protection**			**1.18**	**708,419**
1.28.1	Budget - Wall Protection from 90% Estimate		1.00 lsum	708,419.00	708,419
1.29	**1027 - Access Flooring**			**0.39**	**235,915**
1.29.1	Budget - Access Flooring from 90% Estimate		1.00 lsum	235,915.00	235,915
1.30	**1040 - Building Signage**			**5.24**	**3,138,279**
1.30.1	Budget - Building Signage from 90% Estimate		1.00 lsum	3,138,279.00	3,138,279
1.31	**1052 - Fire Protection Specialties**			**0.14**	**83,070**
1.31.1	Budget - Fire Protection Specialites from 90% Estimate		1.00 lsum	83,070.00	83,070
1.32	**1099 - Miscellaneous Specialties**			**1.16**	**692,350**
1.32.1	Budget - Miscellaneous Specialties from 90% Estimate		1.00 lsum	692,350.00	692,350
1.33	**1116 - Loading Dock Equipment**			**0.13**	**75,000**
1.33.1	Budget - Loading Dock Equipment from 90% Estimate		1.00 lsum	75,000.00	75,000
1.34	**1120 - Commercial Equipment**			**2.48**	**1,487,000**
1.34.1	Budget - Commerical Equipmnet from 90% Estimate		1.00 lsum	1,487,000.00	1,487,000
1.35	**1168 - Play Structures**			**0.12**	**70,000**
1.35.1	Allowance - Play Structures from 90% Estimate		1.00 lsum	70,000.00	70,000
1.36	**1198 - Detention Equipment**			**0.17**	**100,000**
1.36.1	Budget - Detention Equipment from 90% Estimate		1.00 lsum	100,000.00	100,000
1.37	**1248 - Entrance Mats**			**0.33**	**200,000**
1.37.1	Budget - Entrance Mats from 90% Estimate		1.00 lsum	200,000.00	200,000
1.38	**1249 - Window Treatments**			**0.75**	**449,565**
1.38.1	Budget - Window Treatments from 90% Estimate		1.00 lsum	449,565.00	449,565
1.39	**1250 - Furnishings**			**10.95**	**6,560,532**
1.39.1	Allowance - Furnishings from 90% Estimate		1.00 lsum	6,560,532.00	6,560,532
1.40	**1280 - Interior Trees**			**1.74**	**1,043,000**
1.40.1	Budget - Interior Trees from 90% Estimate		1.00 lsum	1,043,000.00	1,043,000
1.41	**1420 - Elevator**			**14.47**	**8,669,000**
1.41.1	Bid Result - Elevators & Esclators - Schindler		1.00 lsum	8,669,000.00	8,669,000
1.42	**1454 - Baggage Conveying**			**88.49**	**53,010,039**

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Client: Hillsborough County Airport Authority
Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity		Total Unit Cost	Amount
1.42.1	BHS System - Diafuku - Design Assist Partner		1.00	lsum	53,010,039.00	53,010,039
1.43	**2100 - Fire Protection**				**8.22**	**4,922,000**
1.43.1	Bid Result - Fire Protection - Pye-Barker Fire & Safety		1.00	lsum	4,922,000.00	4,922,000
1.44	**2200 - Plumbing**				**25.65**	**15,363,946**
1.44.1	Plumbing - BCH - Design Assist Partner		1.00	lsum	15,363,946.00	15,363,946
1.45	**2300 - HVAC**				**93.68**	**56,119,936**
1.45.1	Mechanical - BCH - Design Assist Partner		1.00	lsum	56,119,936.00	56,119,936
1.46	**2600 - Electrical**				**96.14**	**57,594,681**
1.46.1	Electrical - APG - Design Assist Partner		1.00	lsum	55,778,706.00	55,778,706
1.46.2	Unbought Scope - APG - Copper Commodity Market Adjustment		1.00	lsum	1,815,975.00	1,815,975
1.47	**2700 - Low Voltage**				**75.71**	**45,355,235**
1.47.1	Low Voltage - MC Dean - Design Assist Partner		1.00	lsum	45,355,235.00	45,355,235
1.48	**3120 - Sitework**				**35.99**	**21,563,000**
1.48.1	Bid Result - Sitework - Crisdel		1.00	lsum	21,563,000.00	21,563,000
1.49	**3217 - Pavement Markings**				**0.10**	**62,547**
1.49.1	Budget - Pavement Markings from 90% Estimate		1.00	lsum	62,547.00	62,547
1.50	**3231 - Fencing**				**0.88**	**525,802**
1.50.1	Budget - Fencing from 90% Estimate		1.00	lsum	525,802.00	525,802
1.51	**3233 - Site Furnishings**				**0.72**	**434,150**
1.51.1	Budget - Site Furnishings from 90% Estimate		1.00	lsum	434,150.00	434,150
1.52	**3290 - Landscaping & Irrigation**				**0.37**	**223,449**
1.52.1	Budget - Landscape & Irrigation from 90% Estimate		1.00	lsum	223,449.00	223,449
1.53	**3300 - Site Utilities**				**3.22**	**1,927,000**
1.53.1	Pipe Bursting - Murphy Pipelines - Design Assist Partner		1.00	lsum	1,927,000.00	1,927,000
1.54	**9000 - Site Logistics Reconciliation**				**1.01**	**605,246**
1.54.1	Unbought Site Logistics Reconcilliaiton Credit		(1.00)	lsum	2,022,422.00	(2,022,422)
1.54.2	MBSI Extension (Rent) Through December 2029		1.00	lsum	211,600.00	211,600
1.54.3	Trailer Cleaning Extension Through December 2029		1.00	lsum	63,528.00	63,528
1.54.4	HP Site Logistics Through March 2029		1.00	lsum	809,737.00	809,737
1.54.5	Guard Extension November 2028 Through March 2029		1.00	lsum	602,426.00	602,426
1.54.6	Additional Overnight Guards Through March 2029		1.00	lsum	940,377.00	940,377
1.55	**9990 - Contractor Budgets**				**3.25**	**1,945,296**
1.55.1	HNTB ASD Bulletin #1		1.00	lsum	1,120,000.00	1,120,000
1.55.2	Crane Access Credit from Supplemental B - Precast Allowance Reconciliation		(1.00)	lsum	429,704.00	(429,704)
1.55.3	Crane Access Budget		1.00	lsum	800,000.00	800,000
1.55.4	Mechanical - Unbought Scope - Grease Ducts for Concessionares		1.00	lsum	455,000.00	455,000
1.56	**9999 - Contractor Allowances**				**17.67**	**10,584,470**
1.56.1	Owner Enclosure Consultant Allowance		1.00	lsum	200,000.00	200,000
1.56.2	ITB Contractor Fence Relocation Allowance		1.00	lsum	500,000.00	500,000
1.56.3	Trade Delta to Second Place Bids Allowance		1.00	lsum	5,000,000.00	5,000,000
1.56.4	CCBS Grouped Allowance		1.00	lsum	2,068,000.00	2,068,000

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Client: Hillsborough County Airport Authority
Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
1.56.5	Owners Art Infrastructure Allowance		1.00 lsum	1,000,000.00	1,000,000
1.56.6	Interior & Expanded Mock-Up (Airline Lounge Floor, Walls, Ceiling with Foundation & Support Steel)		1.00 allow	225,000.00	225,000
1.56.7	Municipal Utilities Permit Allowance		1.00 lsum	1,000,000.00	1,000,000
1.56.8	CBP Required UPS Allowance		1.00 lsum	591,470.00	591,470
2	**CCBS - 8515 24 Centralized Checked Baggage System**			**0.00**	**88,509,254**
2.1	**0174 - Final Cleaning**			**0.00**	**20,730**
2.1.1	Budget - Final Clean-Up from 90% Estimate		0.44 lsum	47,114.00	20,730
2.2	**0240 - Demolition**			**0.00**	**629,200**
2.2.1	Bid Result - Demolition - Northstar		0.44 lsum	1,430,000.00	629,200
2.3	**0300 - Turnkey Concrete**			**0.00**	**121,440**
2.3.1	Bid Result - Elevated Concrete - Liberty		0.44 lsum	276,000.00	121,440
2.4	**0420 - Masonry**			**0.00**	**52,800**
2.4.1	Bid Result - Masonry - TBD		0.44 lsum	120,000.00	52,800
2.5	**0510 - Structural & Misc Steel**			**0.00**	**1,571,931**
2.5.1	Structural & Miscellaneous Steel - GMF - Design Assist Partner		0.44 lsum	3,572,570.00	1,571,931
2.6	**0710 - Waterproofing and Sealants**			**0.00**	**14,080**
2.6.1	Bid Result - Caulking & Waterproofing - Apex		0.44 lsum	32,000.00	14,080
2.7	**0750 - Interior Wall Panels**			**0.00**	**200,200**
2.7.1	Bid Result - Wall Panels - Acousti		0.44 lsum	455,000.00	200,200
2.8	**0781 - Sprayed Fireproofing**			**0.00**	**149,600**
2.8.1	Bid Result - Sprayed Fireproofing & Insulation - Rolling Plains		0.44 lsum	340,000.00	149,600
2.9	**0810 - Doors, Frames and Hardware**			**0.00**	**95,234**
2.9.1	Allowance - Doors Frames & Hardware from 90% Estimate		0.44 lsum	216,440.00	95,234
2.10	**0833 - Overhead Doors**			**0.00**	**22,176**
2.10.1	Budget - Overhead Doors from 90% Estimate		0.44 lsum	50,400.00	22,176
2.11	**0920 - Drywall & Related**			**0.00**	**395,120**
2.11.1	Bid Result - Drywall & Related - Kenpat		0.44 lsum	898,000.00	395,120
2.12	**0930 - Tile**			**0.00**	**3,718**
2.12.1	Budget - Tile from 90% Estimate		0.44 lsum	8,449.00	3,718
2.13	**0951 - Acoustical Ceilings**			**0.00**	**436,040**
2.13.1	Bid Result - Acoustical Ceilings - Acousti		0.44 lsum	991,000.00	436,040
2.14	**0965 - Resilient & Carpet Flooring**			**0.00**	**44,705**
2.14.1	Budget - Resilient & Carpet Flooring from 90% Estimate		0.44 lsum	101,602.00	44,705
2.15	**0967 - Specialty Flooring**			**0.00**	**15,249**
2.15.1	Budget - Speciality Flooring from 90% Estimate		0.44 lsum	34,657.00	15,249
2.16	**0990 - Painting & Wallcovering**			**0.00**	**259,661**
2.16.1	Budget - Paint & Walcovering from 90% Estimate		0.44 lsum	590,138.00	259,661
2.17	**1040 - Building Signage**			**0.00**	**23,945**
2.17.1	Budget - Building Signage from 90% Estimate		0.44 lsum	38,920.00	17,125
2.17.2	Budget - CBP & Tennant Signage		0.44 lsum	15,500.00	6,820
2.18	**1052 - Fire Protection Specialties**			**0.00**	**4,743**
2.18.1	Budget - Fire Protection Specialites from 90% Estimate		0.44 lsum	10,780.00	4,743

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Client: Hillsborough County Airport Authority
Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
2.19	**1250 - Furnishings**			**0.00**	**44,000**
2.19.1	Allowance - Furnishings		0.44 lsum	100,000.00	44,000
2.20	**1330 - Engineered Special Structures**			**0.00**	**752,258**
2.20.1	Bid Result - Structural Repairs - Structural		0.44 lsum	1,709,677.00	752,258
2.21	**1454 - Baggage Conveying**			**0.00**	**73,491,990**
2.21.1	BHS System - Diafuku - Design Assist Partner		0.44 lsum	167,027,249.00	73,491,990
2.22	**2100 - Fire Protection**			**0.00**	**539,440**
2.22.1	Bid Result - Fire Protection - Pye-Barker Fire & Safety		0.44 lsum	1,226,000.00	539,440
2.23	**2200 - Plumbing**			**0.00**	**169,568**
2.23.1	Plumbing - BCH - Design Assist Partner		0.44 lsum	385,381.00	169,568
2.24	**2300 - HVAC**			**0.00**	**1,664,217**
2.24.1	Mechanical - BCH - Design Assist Partner		0.44 lsum	3,782,311.00	1,664,217
2.25	**2600 - Electrical**			**0.00**	**5,767,238**
2.25.1	Electrical - APG - Design Assist Partner		0.44 lsum	12,569,653.00	5,530,647
2.25.2	Unbought Scope - APG - Copper Commodity Market Adjustment		0.44 lsum	537,707.00	236,591
2.26	**2700 - Low Voltage**			**0.00**	**1,859,379**
2.26.1	Low Voltage - MC Dean - Design Assist Partner		0.44 lsum	4,225,862.00	1,859,379
2.27	**3217 - Pavement Markings**			**0.00**	**16,132**
2.27.1	Budget - Pavement Markings from 90% Estimate		0.44 lsum	36,663.00	16,132
2.28	**3231 - Fencing**			**0.00**	**38,862**
2.28.1	Budget - Fencing from 90% Estimate		0.44 lsum	88,323.00	38,862
2.29	**9990 - Contractor Budgets**			**0.00**	**105,600**
2.29.1	Sealing of Main Terminal Tug Lane		52,800.00 lsum	2.00	105,600
S.I	**Subtotal**				**503,894,480**

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 ASD CCBS Allocated
Client: Hillsborough County Airport Authority

Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:48 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
M.0	**Markups**				
M.1	**ESTIMATED COST OF WORK**			**20.35**	**$12,172,038**
M.1.1	General Requirements CCBS (44%)				1,206,238
M.1.1	General Requirements ASD				10,965,800
M.1.1	A & E Design Costs - With Part 1				
M.1.1	Testing & Inspections (Enabling & Sup B Funded)				
M.2	**COST OF WORK SUBTOTAL**			**199.54**	**$119,326,626**
M.2.1	D/B Contingency (5%)				25,803,326
M.2.1	D/B Contingency True-up from Previous Supplements				(1,193,723)
M.2.1	Allowance Sub Bonds (1.5%)				7,740,998
M.2.1	General Conditions CCBS (44%)				6,317,409
M.2.1	General Conditions ASD				57,430,992
M.2.1	A & E Design Costs - Part 2 CA Services ASD				20,140,345
M.2.1	A & E Design Costs - Part 2 CA Services CCBS (44%)				3,087,279
M.3	**SUBTOTAL**			**88.75**	**$53,071,976**
M.3.1	Contractor's Fee, Overhead & Insurance (6.937%) *				44,079,764
M.3.1	Permits (0.150%)				953,090
M.3.1	Builder's Risk Insurance Policy (Schedule Adj)				2,112,000
M.3.1	Builder's Risk Insurance Policy (Sup A Funded)				
M.3.1	Contractor's Bonds (0.810%)				5,927,123
M.4	**OWNER ALLOWANCES**			**82.28**	**$49,205,538**
M.4.1	Art Allowance by HCAA				
M.4.1	Owner Allowance (1% of all CCBS Dollars) 44%				1,205,538
M.4.1	Owner Allowance (Directed Amount)				48,000,000
S.A	**Total Markups**			**390.93**	**$233,776,179**
T	**ESTIMATE TOTAL**			**1,233.57**	**$737,670,659**

* Negotiated Percentage. All other costs are to be billed as actual expenses.

GMP Estimate Detail

Centralized Checked Baggage System

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 - CCBS
Client: Hillsborough County Airport Authority
Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:47 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
0	**Items**				
1	**CCBS - 8515 24 Centralized Checked Baggage System**			**0.00**	**128,916,680**
1.1	**0174 - Final Cleaning**			**0.00**	**26,384**
1.1.1	Budget - Final Clean-Up from 90% Estimate		0.56 lsum	47,114.00	26,384
1.2	**0240 - Demolition**			**0.00**	**800,800**
1.2.1	Bid Result - Demolition - Northstar		0.56 lsum	1,430,000.00	800,800
1.3	**0300 - Turnkey Concrete**			**0.00**	**154,560**
1.3.1	Bid Result - Elevated Concrete - Liberty		0.56 lsum	276,000.00	154,560
1.4	**0420 - Masonry**			**0.00**	**67,200**
1.4.1	Bid Result - Masonry - TBD		0.56 lsum	120,000.00	67,200
1.5	**0510 - Structural & Misc Steel**			**0.00**	**2,000,639**
1.5.1	Structural & Miscellaneous Steel - GMF - Design Assist Partner		0.56 lsum	3,572,570.00	2,000,639
1.6	**0710 - Waterproofing and Sealants**			**0.00**	**17,920**
1.6.1	Bid Result - Caulking & Waterproofing - Apex		0.56 lsum	32,000.00	17,920
1.7	**0750 - Interior Wall Panels**			**0.00**	**254,800**
1.7.1	Bid Result - Wall Panels - Acousti		0.56 lsum	455,000.00	254,800
1.8	**0781 - Sprayed Fireproofing**			**0.00**	**190,400**
1.8.1	Bid Result - Sprayed Fireproofing & Insulation - Rolling Plains		0.56 lsum	340,000.00	190,400
1.9	**0810 - Doors, Frames and Hardware**			**0.00**	**121,206**
1.9.1	Allowance - Doors Frames & Hardware from 90% Estimate		0.56 lsum	216,440.00	121,206
1.10	**0833 - Overhead Doors**			**0.00**	**28,224**
1.10.1	Budget - Overhead Doors from 90% Estimate		0.56 lsum	50,400.00	28,224
1.11	**0920 - Drywall & Related**			**0.00**	**502,880**
1.11.1	Bid Result - Drywall & Related - Kenpat		0.56 lsum	898,000.00	502,880
1.12	**0930 - Tile**			**0.00**	**4,731**
1.12.1	Budget - Tile from 90% Estimate		0.56 lsum	8,449.00	4,731
1.13	**0951 - Acoustical Ceilings**			**0.00**	**554,960**
1.13.1	Bid Result - Acoustical Ceilings - Acousti		0.56 lsum	991,000.00	554,960
1.14	**0965 - Resilient & Carpet Flooring**			**0.00**	**56,897**
1.14.1	Budget - Resilient & Carpet Flooring from 90% Estimate		0.56 lsum	101,602.00	56,897
1.15	**0967 - Specialty Flooring**			**0.00**	**19,408**
1.15.1	Budget - Speciality Flooring from 90% Estimate		0.56 lsum	34,657.00	19,408
1.16	**0990 - Painting & Wallcovering**			**0.00**	**330,477**
1.16.1	Budget - Paint & Walcovering from 90% Estimate		0.56 lsum	590,138.00	330,477
1.17	**1040 - Building Signage**			**0.00**	**30,475**
1.17.1	Budget - Building Signage from 90% Estimate		0.56 lsum	38,920.00	21,795
1.17.2	Budget - CBP & Tennant Signage		0.56 lsum	15,500.00	8,680
1.18	**1052 - Fire Protection Specialties**			**0.00**	**6,037**
1.18.1	Budget - Fire Protection Specialites from 90% Estimate		0.56 lsum	10,780.00	6,037
1.19	**1250 - Furnishings**			**0.00**	**56,000**
1.19.1	Allowance - Furnishings		0.56 lsum	100,000.00	56,000
1.20	**1330 - Engineered Special Structures**			**0.00**	**957,419**
1.20.1	Bid Result - Structural Repairs - Structural		0.56 lsum	1,709,677.00	957,419
1.21	**1454 - Baggage Conveying**			**0.00**	**106,871,797**

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail
Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 - CCBS
Client: Hillsborough County Airport Authority

Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:47 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
1.21.1	BHS System - Diafuku - Design Assist Partner		0.56 lsum	167,027,249.00	93,535,259
1.21.2	BHS System - Diafuku - TE-215		1.00 lsum	13,336,538.00	13,336,538
1.22	**2100 - Fire Protection**			**0.00**	**686,560**
1.22.1	Bid Result - Fire Protection - Pye-Barker Fire & Safety		0.56 lsum	1,226,000.00	686,560
1.23	**2200 - Plumbing**			**0.00**	**215,813**
1.23.1	Plumbing - BCH - Design Assist Partner		0.56 lsum	385,381.00	215,813
1.24	**2300 - HVAC**			**0.00**	**2,118,094**
1.24.1	Mechanical - BCH - Design Assist Partner		0.56 lsum	3,782,311.00	2,118,094
1.25	**2600 - Electrical**			**0.00**	**7,340,122**
1.25.1	Electrical - APG - Design Assist Partner		0.56 lsum	12,569,653.00	7,039,006
1.25.2	Unbought Scope - APG - Copper Commodity Market Adjustment		0.56 lsum	537,707.00	301,116
1.26	**2700 - Low Voltage**			**0.00**	**2,366,483**
1.26.1	Low Voltage - MC Dean - Design Assist Partner		0.56 lsum	4,225,862.00	2,366,483
1.27	**3217 - Pavement Markings**			**0.00**	**20,531**
1.27.1	Budget - Pavement Markings from 90% Estimate		0.56 lsum	36,663.00	20,531
1.28	**3231 - Fencing**			**0.00**	**49,461**
1.28.1	Budget - Fencing from 90% Estimate		0.56 lsum	88,323.00	49,461
1.29	**9990 - Contractor Budgets**			**0.00**	**134,400**
1.29.1	Sealing of Main Terminal Tug Lane		67,200.00 lsum	2.00	134,400
1.30	**9999 - Contractor Allowances**			**0.00**	**2,932,000**
1.30.1	CCBS Grouped Allowance		1.00 lsum	2,932,000.00	2,932,000

HENSEL PHELPS
Plan. Build. Manage.

Estimate Detail

Trade Rollup

Project: TPA Airside D - Supplement C
Estimate: Working - ASD Program Sup C R2 - CCBS
Client: Hillsborough County Airport Authority

Estimator: James Cobb
Job Size: 597,998 sf
Report Date: 1/23/2026 8:47 AM

Grouped by:

REF#	Sector \ Trade Rollup \ Items	WBS	Quantity	Total Unit Cost	Total Amount
S.I	**Subtotal**				**128,916,680**
M.0	**Markups**				
M.1	**ESTIMATED COST OF WORK**			**2.57**	**$1,535,212**
M.1.1	General Requirements (56%)				1,535,212
M.1.1	A & E Design Costs - With Part 1				
M.1.1	Testing & Inspections (Enabling & Sup B Funded)				
M.2	**COST OF WORK SUBTOTAL**			**34.20**	**$20,448,976**
M.2.1	D/B Contingency (5%)				6,522,595
M.2.1	Allowance Sub Bonds (1.5%)				1,956,778
M.2.1	General Conditions CCBC (56%)				8,040,339
M.2.1	A & E Design Costs - Part 2 CA Services CCBS (56%)				3,929,265
M.3	**SUBTOTAL**			**20.09**	**$12,016,302**
M.3.1	Contractor's Fee, Overhead & Insurance (6.937%) *				10,468,597
M.3.1	Permits (0.150%)				226,351
M.3.1	Builder's Risk Insurance Policy (Sup A Funded)				
M.3.1	Contractor's Bonds (0.810%)				1,321,354
M.4	**OWNER ALLOWANCES**			**2.57**	**$1,534,321**
M.4.1	Art Allowance by HCAA				
M.4.1	Owner Allowance (1% of all CCBS Dollars) 56%				1,534,321
S.A	**Total Markups**			**59.42**	**$35,534,812**
T	**ESTIMATE TOTAL**			**275.00**	**$164,451,491**

* Negotiated Percentage. All other costs are to be billed as actual expenses.

Contingency Reconciliation

ASD and CCBS 5% Contingency Summary								
	EN		**A**		**B**		**Total**	
Cost of Work	$	44,303,800	$	58,218,872	$	70,985,350	$	173,508,022
GR	$	5,491,000	$	5,304,430	$	955,437	$	11,750,867
Total	$	53,178,775	$	63,523,302	$	71,940,787	$	188,642,864
Contingency 5%	$	2,658,939	$	3,176,165	$	3,597,039	$	9,432,143
Entered in GMP	$	3,540,471	$	3,176,165	$	3,909,230	$	10,625,866
Reconciliation Value	$	(881,532)	$	(0)	$	(312,191)	$	(1,193,723)

A credit value of $1,193,723 as calculated above has been applied to this GMP to reconcile previous GMP and supplemental GMP contingency to 5% for the total program.

General Conditions

GMP Supplemental C General Conditions

The attached General Conditions and Staffing Budgets support a robust team for the remainder of the project as outlined in the attached schedule and staff chart. This staffing plan ensures the successful execution of the Airside D Program, providing the necessary personnel to meet project demands. All project general conditions and general requirements for the time period beginning January 1, 2027 through project completion on the attached schedule are included within this submission. General conditions and general requirements through December 31, 2026 were included in previous GMP submissions. No general conditions or general requirements for work at Airside A, Airside C, or Airside E forthcoming changes are included in this submission. No general conditions or general requirements for Airline Relocations are included in this submission. General conditions and general requirements for Airside and Airline Relocations scopes of work will be included in forthcoming supplemental D GMP submissions.

The General Conditions report is attached.

Please note that the gold cells in the following staff report identify reduced or deleted months of staffing that were included in previous GMP submissions. These reductions are credited back in this supplemental.

ASD/CCBS Methodology:

The Hensel Phelps General Conditions and General Requirements have been split between the Airside D project and the Centralized Check Baggage System project at a ratio of 80% ASD and 20% CCBS. This ratio was developed by taking the total number of staff months employed on the CCBS project and dividing it by the overall program staff months.

HENSEL PHELPS
Plan. Build. Manage.

Supplemental C General Conditions / General Requirements

Selfwork Duration:
Job Size: 597,998 sf
Client: Hillsborough County Airport Authority
Architect: HNTB

L = Lump Sum R = Rate A = Allowance
F = Full Job Duration S = Supp C Incrimental Funding
C = Duration in Staff Chart

Project: TPA Airside D - Supplement C
Estimate: Working - GCs - TIA Airside D Sup C Submission R1
Estimator: James Cobb
Report Date: 1/12/2026 8:19 AM

Sort Sequence:

GC's Sort/Phase/Items	Quantity	L/R/V/A	Duration	WH/Unit	Unit/WH	Labor Hours	Labor $ / Hour	Labor Unit Cost	Labor Amount	Material Unit Cost	Material Amount	Subcontract Unit Cost	Subcontract Amount	Equipment Unit Cost	Equipment Amount	Total Unit Cost	Total Amount
Items						**1,457,661**	**46.48**		**67,749,205**		**1,417,064**		**14,224,709**		**2,087,262**		**85,478,240**
GC - General Conditions Item						**1,340,301**	**50.39**		**67,543,260**		**952,845**		**2,081,520**		**1,211,115**		**71,788,740**
01-10-10.00 - Supervision and Administration						**554,423**	**121.83**		**67,543,260**								**67,543,260**
Add Adjustment for Partner Participation	615. mnth	R	C	173.330	0.01	106,598	175.4	30,402.	18,697,230							30,402.	18,697,230
Delete Adjustment for HPCC Bare Wages	(615.) mnth	R	C	173.330	0.01	(106,598)	85.28	14,781.	(9,090,315)							14,781.	(9,090,315)
Program Director (Position Not Billed to Part 2. Credit from Supp A)	(3.) mnth	R	C	173.330	0.01	(520)	177.98	30,848.44	(92,545)							30,848.44	(92,545)
Program Director	26. mnth	R	C	173.330	0.01	4,507	191.65	33,218.1	863,671							33,218.1	863,671
General Superintendent (Position Not Billed to Part 2. Credit from Supp A)	(3.) mnth	R	C	173.330	0.01	(520)	167.78	29,081.86	(87,246)							29,081.86	(87,246)
General Superintendent	26. mnth	R	C	173.330	0.01	4,507	180.67	31,315.81	814,211							31,315.81	814,211
Project Manager (Position Not Billed to Part 2. Credit from Supp A)	(3.75) mnth	R	C	173.330	0.01	(650)	155.21	26,902.48	(100,884)							26,902.48	(100,884)
Project Manager for Construction (Position Not Billed to Part 2. Credit from Supp A)	(3.) mnth	R	C	173.330	0.01	(520)	155.21	26,902.48	(80,707)							26,902.48	(80,707)
Project Manager for Construction	32. mnth	R	C	173.330	0.01	5,547	167.13	28,969.02	927,009							28,969.02	927,009
Project Manager	119. mnth	R	C	173.330	0.01	20,626	167.33	29,004.02	3,451,478							29,004.02	3,451,478
Project Superintendent	158. mnth	R	C	173.330	0.01	27,386	138.85	24,066.25	3,802,468							24,066.25	3,802,468
Senior Project Superintendent (Position Not Billed to Part 2. Credit from Supp A)	(3.) mnth	R	C	173.330	0.01	(520)	128.68	22,303.97	(66,912)							22,303.97	(66,912)
Senior Project Superintendent	32. mnth	R	C	173.330	0.01	5,547	138.56	24,017.27	768,553							24,017.27	768,553
Area Superintendent	381. mnth	R	C	173.330	0.01	66,039	114.83	19,903.16	7,583,103							19,903.16	7,583,103
Low Voltage / Special Systems Integrator (Position Not Billed to Part 2. Credit from Supp A)	(9.5) mnth	R	C	173.330	0.01	(1,647)	106.53	18,464.36	(175,411)							18,464.36	(175,411)
Low Voltage / Special Systems Integrator	28. mnth	R	C	173.330	0.01	4,853	114.71	19,882.72	556,716							19,882.72	556,716
MEP Systems Integrator (Position Not Billed to Part 2. Credit from Supp A)	(5.) mnth	R	C	173.330	0.01	(867)	106.53	18,464.36	(92,322)							18,464.36	(92,322)
MEP Systems Integrator	28. mnth	R	C	173.330	0.01	4,853	114.71	19,882.72	556,716							19,882.72	556,716
Project Engineer	288. mnth	R	C	173.330	0.01	49,919	95.34	16,525.33	4,759,294							16,525.33	4,759,294
Scheduler	27. mnth	R	C	173.330	0.01	4,680	122.14	21,169.67	571,581							21,169.67	571,581
Third Party Schedule Consultant	1. lsum	R	C					165,000.	165,000							165,000.	165,000
Safety Admin	24. mnth	R	C	173.330	0.01	4,160	49.52	8,583.56	206,005							8,583.56	206,005
Safety Engineer	48. mnth	R	C	173.330	0.01	8,320	89.08	15,439.53	741,097							15,439.53	741,097
Safety Manager (Sr.)	25. mnth	R	C	173.330	0.01	4,333	125.73	21,792.76	544,819							21,792.76	544,819
Safety Manager	27. mnth	R	C	173.330	0.01	4,680	126.35	21,900.81	591,322							21,900.81	591,322
CQC Admin	27. mnth	R	C	173.330	0.01	4,680	134.9	23,382.53	631,328							23,382.53	631,328
CQC Assistant	27. mnth	R	C	173.330	0.01	4,680	108.74	18,847.92	508,894							18,847.92	508,894
CQC Lead	146. mnth	R	C	173.330	0.01	25,306	134.9	23,382.53	3,413,849							23,382.53	3,413,849
CQC Manager	60. mnth	R	C	173.330	0.01	10,400	134.9	23,382.53	1,402,952							23,382.53	1,402,952
CQC Lead	60. mnth	R	C	173.330	0.01	10,400	135.57	23,498.45	1,409,907							23,498.45	1,409,907
Senior VDC Manager	2.3 mnth	R	C	173.330	0.01	399	153.74	26,647.46	61,289							26,647.46	61,289
VDC Engineer	76. mnth	R	C	173.330	0.01	13,173	111.48	19,322.36	1,468,500							19,322.36	1,468,500
VDC Manager	36. mnth	R	C	173.330	0.01	6,240	153.74	26,647.46	959,309							26,647.46	959,309
Document Control Engineer (Position Not Billed to Part 2. Credit from Supp A)	(3.75) mnth	R	C	173.330	0.01	(650)	72.45	12,557.13	(47,089)							12,557.13	(47,089)
Document Control Engineer (Position not filled & eliminated from program. Credit from Supp A)	(17.) mnth	R	C	173.330	0.01	(2,947)	72.45	12,557.13	(213,471)							12,557.13	(213,471)
Document Control Engineer	56. mnth	R	C	173.330	0.01	9,706	78.01	13,521.72	757,216							13,521.72	757,216
Document Control Manager (Position not filled & eliminated from program. Credit from Supp A)	(17.) mnth	R	C	173.330	0.01	(2,947)	72.45	12,557.13	(213,471)							12,557.13	(213,471)
LEED Coordinator	36. mnth	R	C	173.330	0.01	6,240	78.01	13,521.72	486,782							13,521.72	486,782
Office Engineer	452. mnth	R	C	173.330	0.01	78,345	78.07	13,531.21	6,116,108							13,531.21	6,116,108
Design Manager (Position Not Billed to Part 2. Credit from Supp A)	(4.) mnth	R	C	173.330	0.01	(693)	162.92	28,238.23	(112,953)							28,238.23	(112,953)
Design Manager	93. mnth	R	C	173.330	0.01	16,120	175.43	30,407.38	2,827,886							30,407.38	2,827,886
Senior Design Manager	2.7 mnth	R	C	173.330	0.01	468	175.43	30,407.38	82,100							30,407.38	82,100
Field Engineer	97. mnth	R	C	173.330	0.01	16,813	76.94	13,336.86	1,293,675							13,336.86	1,293,675
Field Engineer	483. mnth	R	C	173.330	0.01	83,718	76.6	13,277.09	6,412,834							13,277.09	6,412,834

HENSEL PHELPS
Plan. Build. Manage.

Supplemental C General Conditions / General Requirements

Selfwork Duration:
Job Size: 597,998 sf
Client: Hillsborough County Airport Authority
Architect: HNTB

L = Lump Sum R = Rate A = Allowance
F = Full Job Duration S = Supp C Incrimental Funding
C = Duration in Staff Chart

Project: TPA Airside D - Supplement C
Estimate: Working - GCs - TIA Airside D Sup C Submission R1
Estimator: James Cobb
Report Date: 1/12/2026 8:19 AM

Project Estimator	45.	mnth	R	C	173.330	0.01	7,800	131.8	22,844.84	1,028,018						22,844.84	1,028,018
Senior Estimator (Position Not Billed to Part 2. Credit from Supp A)	(4.)	mnth	R	C	173.330	0.01	(693)	122.4	21,215.18	(84,861)						21,215.18	(84,861)
Senior Estimator	33.	mnth	R	C	173.330	0.01	5,720	128.34	22,245.04	734,086						22,245.04	734,086
Admin / Secretary (Position Not Billed to Part 2. Credit from Supp A)	(2.)	mnth	R	C	173.330	0.01	(347)	45.99	7,971.24	(15,942)						7,971.24	(15,942)
Admin / Secretary	66.	mnth	R	C	173.330	0.01	11,440	49.52	8,583.56	566,515						8,583.56	566,515
SBE Coordinator	27.	mnth	R	C	173.330	0.01	4,680	49.52	8,583.56	231,756						8,583.56	231,756
Job Site Accountant (Position Not Billed to Part 2. Credit from Supp A)	(1.5)	mnth	R	C	173.330	0.01	(260)	31.6	5,476.4	(8,215)						5,476.4	(8,215)
Job Site Accountant	66.	mnth	R	C	173.330	0.01	11,440	99.86	17,308.82	1,142,382						17,308.82	1,142,382
CCBS Labors June 2026 to July 2029	13,200.	mh	R	S	1.000	1.	13,200	48.63	48.63	641,916						48.63	641,916
Intern	42.	mnth	R	C	173.330	0.01	7,280	34.07	5,905.42	248,028						5,905.42	248,028
01-10-20.00 - Misc Supervision and Administration													855,000		158,455		1,013,455
^^^Field Engineers' Equipment	580.	MNTH	L	S										268.75	155,875	268.75	155,875
Total Station Calibration	4.	EACH	L	S										645.	2,580	645.	2,580
Jobsite Travel	100.	TRIP	L	S								700.	70,000			700.	70,000
Moving & Relocate (AS/PE/LeadVDC)	15.	EACH	L	S								25,000.	375,000			25,000.	375,000
Moving & Relocate (OE/FE)	10.	EACH	L	S								15,000.	150,000			15,000.	150,000
Moving & Relocate (PM/PS/QCM/SM)	1.	EACH	L	S								50,000.	50,000			50,000.	50,000
Intern Housing	42.	MNTH	L	S								5,000.	210,000			5,000.	210,000
01-10-30.00 - Plans and Printing													10,000				10,000
Project Plans / Printing	20.	set	L	S								500.	10,000			500.	10,000
01-10-40.00 - Safety and First Aid							564,016					200,703					200,703
Safety Equipment - HCAA	1.	ls	L	S							25,800.	25,800				25,800.	25,800
Safety Equipment - Salaried	3,254.	mo	L	S	173.330	0.01	564,016				53.75	174,903				53.75	174,903
01-10-50.00 - Temporary Facilities							124,798					530,566	446,520				977,086
Aerial Photos	36.	ea	L	S									200.	7,200		200.	7,200
Misc Jobsite Signs - ASD	1.	ls	L	S							80,625.	80,625				80,625.	80,625
Misc Jobsite Signs - CCBS	1.	ls	L	S							53,750.	53,750				53,750.	53,750
Office Supplies & Equipment - HCAA	36.	mo	L	S	173.330	0.01	6,240				2,526.25	90,945				2,526.25	90,945
Office Supplies & Equipment - Hensel Phelps	36.	mo	L	S	173.330	0.01	6,240				3,359.38	120,938				3,359.38	120,938
Field Tablets w/ case (FE, QC, AS, ++) Data Service	540.	mo	L	S	173.330	0.01	93,598				69.88	37,733				69.88	37,733
Field Tablets w/ case (FE, QC, AS, ++)	13.	EACH	L	S							1,290.	16,770				1,290.	16,770
Jobsite Computers	50.	EACH	L	S							2,596.13	129,806				2,596.13	129,806
ASA Firewall (for Network) w/ Network	1.	info	L	S													0
Access Points w/ Network	1.	info	L	S													0
Internet Monthly Charges (Main Trailer & Baggage)	36.	mo	L	S	173.330	0.01	6,240						2,600.	93,600		2,600.	93,600
Cellular Phone Purchases	163.	EACH	L	S									800.	130,400		800.	130,400
Postage & Shipping	36.	mo	L	S	173.330	0.01	6,240						650.	23,400		650.	23,400
Trailer Equipment Insurance ($3,000,000 Value)	36.	mo	L	S	173.330	0.01	6,240						2,220.	79,920		2,220.	79,920
Trailer Furniture Relocation to HCAA Warehouse	1.	lsum	L	S									40,000.	40,000		40,000.	40,000
Trailer Repairs & Restoration	1.	lsum	L	S									72,000.	72,000		72,000.	72,000
01-10-60.00 - Building Services and Clean Up							4,160							180,000			180,000
Floor Protection - Skudo (Repairs) commercial, heavy traffic + protection board	24.	mo	L	S	173.330	0.01	4,160						7,500.	180,000		7,500.	180,000
01-10-70.00 - Inspection and Quality Control							6,240							590,000			590,000
Building Envelope Consultant	1.	LSUM	L	S									250,000.	250,000		250,000.	250,000
QC Program Supplies	36.	mo	L	S	173.330	0.01	6,240						5,000.	180,000		5,000.	180,000
Safety/QC BBQ	8.	ea	L	S									20,000.	160,000		20,000.	160,000
01-10-90.00 - Equipment and Transportation							86,665					221,576			1,052,660		1,274,236
Field Trucks - HP (12 each)	384.	mo	L	S	173.330	0.01	66,559				577.02	221,576			1,384.85	531,784	1,961.88	753,360
John Deer Gators or similar	72.	mo	L	S	173.330	0.01	12,480								1,277.1	91,951	1,277.1	91,951
Misc.Power Equip.	22.	mo	L	S	173.330	0.01	3,813								5,375.	118,250	5,375.	118,250
Small Tools - ASD	1.	LS	L	S											96,750.	96,750	96,750.	96,750
Small Tools - CCBS	1.	LS	L	S											107,500.	107,500	107,500.	107,500
Repairs & Maintenance	22.	mo	L	S	173.330	0.01	3,813								4,837.5	106,425	4,837.5	106,425
GR - General Requirements Item							**117,360**	**1.75**		**205,945**		**464,218**		**12,143,189**		**876,147**		**13,689,500**
01-10-20.00 - Misc Supervision and Administration														**125,000**				**125,000**

HENSEL PHELPS
Plan. Build. Manage.

Supplemental C General Conditions / General Requirements

Selfwork Duration:
Job Size: 597,998 sf
Client: Hillsborough County Airport Authority
Architect: HNTB

L = Lump Sum R = Rate A = Allowance
F = Full Job Duration S = Supp C Incrimental Funding
C = Duration in Staff Chart

Project: TPA Airside D - Supplement C
Estimate: Working - GCs - TIA Airside D Sup C Submission R1
Estimator: James Cobb
Report Date: 1/12/2026 8:19 AM

Professional Settlement Monitoring	1.	ls	L	S									125,000.	125,000			125,000.	125,000
01-10-40.00 - Safety and First Aid							**158**	**80.63**		**12,750**		**19,081**		**39,458**		**53,902**		**125,192**
First Aid Supplies	5.	ea	L	S							1,075.	5,375					1,075.	5,375
CARES Program	3.	ea	L	S									8,333.36	25,000	12,541.64	37,625	20,875.	62,625
PA System Expansion Speakers & Microphones	1.	ea	L	S									1,708.34	1,708	2,571.04	2,571	4,279.38	4,279
Backrails, Toeboards & Cable Rail Misc Maintenance	12.	mo	L	S	0.010	100.	0	47,000.	470.	5,640	505.25	6,063	470.	5,640	505.25	6,063	1,950.5	23,406
Toeboards Installation	7,900.	fl	L	S	0.020	50.	158	45.	0.9	7,110	0.97	7,643	0.9	7,110	0.97	7,643	3.74	29,507
01-10-50.00 - Temporary Facilities							**77,459**	**2.23**		**172,500**		**225,428**		**108,200**		**210,679**		**716,806**
CCBS Office Development	1.	lsum	L	S					2,000.	2,000	2,150.	2,150	2,000.	2,000	2,150.	2,150	8,300.	8,300
Guardshack Visitor & Safety Enhancements	1.	lsum	L	S					3,000.	3,000	3,225.	3,225	3,000.	3,000	3,225.	3,225	12,450.	12,450
Robotic Dog Storage Unit	36.	mo	L	S	173.330	0.01	6,240						750.	27,000			750.	27,000
Kitchen Consumables	36.	ls	L	S							5,590.	201,240					5,590.	201,240
Jobsite Plotter - Copies /Maintenance	36.	mo	L	S	173.330	0.01	6,240								268.75	9,675	268.75	9,675
Jobsite Printer - C3530i (HP Trailer Type 3)	36.	mo	L	S	173.330	0.01	6,240								693.38	24,962	693.38	24,962
Jobsite Printer - C3530i (HP Trailer Type 4)	36.	mo	L	S	173.330	0.01	6,240								693.38	24,962	693.38	24,962
Jobsite Printer - C3530i (HP Trailer Type 5)	36.	mo	L	S	173.330	0.01	6,240								693.38	24,962	693.38	24,962
Jobsite Printer - C7565i (HP Office Field Trailer)	36.	mo	L	S	173.330	0.01	6,240								693.38	24,962	693.38	24,962
Jobsite Printer - Copies /Maintenance (HP Office Field Trailer)	36.	mo	L	S	173.330	0.01	6,240								462.25	16,641	462.25	16,641
Jobsite Printer - Copies /Maintenance (HP Trailer Type 3)	36.	mo	L	S	173.330	0.01	6,240								231.13	8,321	231.13	8,321
Jobsite Printer - Copies /Maintenance (HP Trailer Type 4)	36.	mo	L	S	173.330	0.01	6,240								231.13	8,321	231.13	8,321
Jobsite Printer - Copies /Maintenance (HP Trailer Type 5)	36.	mo	L	S	173.330	0.01	6,240								231.13	8,321	231.13	8,321
Drinking Water for Trailers (Culligan Water Filter 5 Trailers)	48.	mo	L	S	173.330	0.01	8,320								1,128.75	54,180	1,128.75	54,180
Ice Service & Machines	36.	mo	L	S	173.330	0.01	6,240						600.	21,600			600.	21,600
Employee Parking Area Sidewalks 4'	1,300.	lf	L	S									42.	54,600			42.	54,600
Labor to move around plastic barriers	500.	hr	L	S	1.000	1.	500	35.	35.	17,500							35.	17,500
Low Profile Barricades with flashers	50.	ea	L	S							376.25	18,813					376.25	18,813
Temporary Walls for Baggage Coordination and Sequencing	1.	lsum	L	S					150,000.	150,000							150,000.	150,000
01-10-60.00 - Building Services and Clean Up							**18,720**					**52,245**		**1,739,720**				**1,791,965**
Water, cups, ice for clean up crew - Non-Peak	36.	mnth	L	S	173.330	0.01	6,240						2,500.	90,000			2,500.	90,000
Water, cups, ice for clean up crew - Peak	36.	mnth	L	S	173.330	0.01	6,240						7,500.	270,000			7,500.	270,000
Building Envelope Temporary Protection and Infill for A/C	1.	lsum	L	S									125,000.	125,000			125,000.	125,000
Dumpster Dump Fees (includes recycling premium)	1,860.	ea	L	S									650.	1,209,000			650.	1,209,000
Dumpster Rental (Metals Dumpster)	36.	mo	L	S	173.330	0.01	6,240						1,000.	36,000			1,000.	36,000
SWPPP Inspections and Maintenance	36.	MNTH	L	S							1,451.25	52,245					1,451.25	52,245
SWPPP Online Reporting	36.	MNTH	L	S									270.	9,720			270.	9,720
01-10-80.00 - Temp. Heat and Protection														**5,187,822**				**5,187,822**
Building Temp HVAC Electrical Feeds & Service Equipment	1.	LS	L	S									2,082,822.	2,082,822			2,082,822.	2,082,822
Building Temp HVAC	1.	LS	L	S									3,105,000.	3,105,000			3,105,000.	3,105,000
01-10-90.00 - Equipment and Transportation							**20,543**					**122,315**		**4,371,789**		**611,566**		**5,105,670**
Interior Scaffold / High Ceiling Dancefloor Daily Rent	270.	day	L	S	8.000	0.13	2,160						4,651.2	1,255,824			4,651.2	1,255,824
Interior Scaffold / High Ceiling Dancefloor Set-up & Tear Down	95,000.	sf	L	S									13.	1,235,000			13.	1,235,000
Interior Scaffold / LED Dancefloor Daily Rent	170.	day	L	S	8.000	0.13	1,360						4,651.2	790,704			4,651.2	790,704
Interior Scaffold / LED Dancefloor Set-up & Tear Down	32,000.	sf	L	S									13.	416,000			13.	416,000
Interior Scaffold / Stair Towers Daily Rent x3	270.	day	L	S	8.000	0.13	2,160						26.7	7,209			26.7	7,209
Interior Scaffold / Stair Towers Set-up & Tear Down	1.	each	L	S									4,802.	4,802			4,802.	4,802
Interior Scaffold / Train Tube Dancefloor Daily Rent	230.	day	L	S	8.000	0.13	1,840						490.	112,700			490.	112,700
Interior Scaffold / Train Tube Dancefloor Set-up & Tear Down	10,955.	sf	L	S									10.	109,550			10.	109,550
Stair Towers	4.	ea	L	S									110,000.	440,000			110,000.	440,000
Dust control equipment maintenance - (From 2026)	18.	mo	L	S	173.330	0.01	3,120				268.75	4,838			1,343.75	24,188	1,612.5	29,025
Dust Control Equipment Operator (18 mo.X 40/week)	3,117.	mh	L	S	1.000	1.	3,117				7.17	22,340			35.83	111,691	43.	134,031
General Exploratory Excavating - (From 2026)	25.	day	L	S	8.000	0.13	200				537.5	13,438			2,687.5	67,188	3,225.	80,625
Street Sweeper (inc. Fuel) - (From 2026)	18.	mo	L	S	173.330	0.01	3,120				2,687.5	48,375			13,437.5	241,875	16,125.	290,250
Temp Irrigation - (From 2026)	2.	mo	L	S	173.330	0.01	347				2,150.	4,300			10,750.	21,500	12,900.	25,800
Water Truck (Incl. Fuel) - (From 2026)	18.	mo	L	S	173.330	0.01	3,120				1,612.5	29,025			8,062.5	145,125	9,675.	174,150
08-74-19.50 - Biometric Identity Access														**570,000**				**570,000**
CCBS Portal and Site Utilization Allowance	1.	lsum	L	S									350,000.	350,000			350,000.	350,000

HENSEL PHELPS
Plan. Build. Manage.

Supplemental C General Conditions / General Requirements

Selfwork Duration:
Job Size: 597,998 sf
Client: Hillsborough County Airport Authority
Architect: HNTB

L = Lump Sum R = Rate A = Allowance
F = Full Job Duration S = Supp C Incrimental Funding
C = Duration in Staff Chart

Project: TPA Airside D - Supplement C
Estimate: Working - GCs - TIA Airside D Sup C Submission R1
Estimator: James Cobb
Report Date: 1/12/2026 8:19 AM

MOT for Drive Lane Work	1. lsum	L	S									125,000.	125,000			125,000.	125,000
MOT for Tug Path	1. lsum	L	S									75,000.	75,000			75,000.	75,000
Move/Relocation of Concrete K Barriers for Phasing for Tug Path	1. lsum											20,000.	20,000			20,000.	20,000
10-44-16.13 - Portable Fire Extinguishers		L	S			**480**	**43.12**		**20,695**		**45,150**		**1,200**				**67,045**
Fire Extinguishers & Stands (Maintain)	120. ea	L	S	2.000	0.5	240	43.12	86.23	10,348			10.	1,200			96.23	11,548
Fire Extinguishers & Stands (Purchase)	120. ea	L	S							376.25	45,150					376.25	45,150
Fire Extinguishers & Stands (Unload & Install)	120. ea	L	S	2.000	0.5	240	43.12	86.23	10,348							86.23	10,348
Subtotal	**599,084 sf**			**0.411**	**0.41**	**1,457,661**	**46.48**	**113.09**	**67,749,205**	**2.37**	**1,417,064**	**23.74**	**14,224,709**	**3.48**	**2,087,262**	**142.94**	**85,495,990**
ESTIMATE TOTAL	**599,084 sf**															**142.71**	**85,495,990**

^^ Field Engineers' Equipment - Enabling funding for FE equipment was for the full duration of the man-months included. FE Equipment correlates to included months only

Items listed as L =Lump Sum are for budgeting purposes only and shall be billed using actual costs plus mark-up's and indirects

General Conditions - $71,788,740
General Requirements - $13,707,250

Airside D (80%)	CCBS (20%)
General Conditions - $57,430,992	General Conditions - $14,357,748
General Requirements - $10,965,800	General Requirements - $2,741,450

FOUNDATIONS COMP | STRUCTURE COMP | SKIN COMPLETE | SUPP C SC | ASD FIRST FLIGHT | SUPP C FC

Project:				2024					2025										2026												2027												2028												2029												
Location:				AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL		
Date:				1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	61	62	63	64	65	
Project Manager for Design Assist	Office	PM	1 - Core													0.25	0.25	0.25	0.25	0.25	1	1	1	1	1												

FOUNDATIONS COMP

STRUCTURE COMP

SKIN COMPLETE

SUPP C SC

ASD FIRST FLIGHT

SUPP C FC

| Project: | | | | 2024 | | | | | 2025 | | | | | | | | | | | | | | | 2026 | | | | | | | | | | | | | | |

Airside D Wage Rates

	Negotiated Rate 2025	Negotiated Monthly Rate	GMP 3	6 MO 2025 Rate	12 MO 2026 Rate	12 MO 2027 Rate	12 MO 2028 Rate	8 MO 2029 Rate	Blended Rate
Program Director	$ 171.13	$ 29,661.96				$ 32,082.38	$ 33,365.67	$ 34,700.30	$ 33,218.10
General Superintendent	$ 161.33	$ 27,963.33				$ 30,245.14	$ 31,454.94	$ 32,713.14	$ 31,315.81
Project Manager	$ 149.24	$ 25,867.77				$ 27,978.58	$ 29,097.72	$ 30,261.63	$ 28,969.02
Project Superintendent	$ 123.73	$ 21,446.12				$ 23,196.12	$ 24,123.97	$ 25,088.93	$ 24,017.27
Area Superintendent	$ 102.43	$ 17,754.19				$ 19,202.93	$ 19,971.05	$ 20,769.89	$ 19,882.72
Assistant Project Manager= HP Project Engineer	$ 85.04	$ 14,739.98				$ 15,942.77	$ 16,580.48	$ 17,243.70	$ 16,507.14
Project Engineer = HP Office Engineer	$ 69.66	$ 12,074.17				$ 13,059.42	$ 13,581.80	$ 14,125.07	$ 13,521.72
Safety Manager	$ 112.27	$ 19,459.76				$ 21,047.68	$ 21,889.58	$ 22,765.17	$ 21,792.76
Safety Engineer	$ 79.54	$ 13,786.67				$ 14,911.66	$ 15,508.13	$ 16,128.45	$ 15,439.53
Office Engineer	$ 69.66	$ 12,074.17				$ 13,059.42	$ 13,581.80	$ 14,125.07	$ 13,521.72
Field Engineer	$ 68.40	$ 11,855.77				$ 12,823.20	$ 13,336.13	$ 13,869.58	$ 13,277.14
MEP Coordinator	$ 139.28	$ 24,141.40				$ 26,111.34	$ 27,155.79	$ 28,242.03	$ 27,035.68
VDC Engineer	$ 99.31	$ 17,213.40				$ 18,618.02	$ 19,362.74	$ 20,137.25	$ 19,277.09
Senior Estimator	$ 114.60	$ 19,863.62				$ 21,484.49	$ 22,343.87	$ 23,237.62	$ 22,245.04
Project Estimator	$ 117.69	$ 20,399.21				$ 22,063.78	$ 22,946.33	$ 23,864.19	$ 22,844.84
Lead Estimator	$ 103.00	$ 17,852.99				$ 19,309.79	$ 20,082.19	$ 20,885.47	$ 19,993.36
Estimator	$ 85.26	$ 14,778.12				$ 15,984.01	$ 16,623.37	$ 17,288.31	$ 16,549.84
Scheduler	$ 109.06	$ 18,903.37				$ 20,445.88	$ 21,263.72	$ 22,114.27	$ 21,169.67
Office Manager	$ 33.90	$ 5,875.89				$ 6,355.36	$ 6,609.57	$ 6,873.96	$ 6,580.34
Admin / Secretary	$ 44.22	$ 7,664.65				$ 8,290.09	$ 8,621.69	$ 8,966.56	$ 8,583.56
						$ -	$ -	$ -	$ -
Intern	$ 30.38	$ 5,265.77				$ 5,695.45	$ 5,923.27	$ 6,160.20	$ 5,897.07
						$ -	$ -	$ -	$ -
Partners						$ -	$ -	$ -	$ -
Job Site Accountant	$ 89.17	$ 15,455.84				$ 16,717.03	$ 17,385.71	$ 18,081.14	$ 17,308.82
Design Manager	$ 156.65	$ 27,152.14				$ 29,367.76	$ 30,542.47	$ 31,764.17	$ 30,407.38
Project Estimator	$ 110.14	$ 19,090.57				$ 20,648.36	$ 21,474.29	$ 22,333.26	$ 21,379.31
CQC Manager	$ 141.98	$ 24,609.39				$ 26,617.52	$ 27,682.22	$ 28,789.51	$ 27,559.78
CQC Lead	$ 120.46	$ 20,879.33				$ 22,583.09	$ 23,486.41	$ 24,425.87	$ 23,382.53
CQC Assistant	$ 96.62	$ 16,747.14				$ 18,113.71	$ 18,838.26	$ 19,591.79	$ 18,754.94
VDC Manager	$ 137.28	$ 23,794.74				$ 25,736.39	$ 26,765.85	$ 27,836.48	$ 26,647.46
Lead VDC Engineer	$ 112.97	$ 19,581.09				$ 21,178.91	$ 22,026.06	$ 22,907.11	$ 21,928.64

Centralized Checked Baggage System (CCBS) Wage Rates

	Negotiated Rate 2025	Negotiated Monthly Rate	GMP 3	6 MO 2025 Rate	12 MO 2026 Rate	12 MO 2027 Rate	12 MO 2028 Rate	12 MO 2029 Rate	Blended Rate
Program Director	$ 171.13	$ 29,661.96				$ 32,082.38	$ 33,365.67	$ 34,700.30	$ 33,382.78
General Superintendent	$ 161.33	$ 27,963.33				$ 30,245.14	$ 31,454.94	$ 32,713.14	$ 31,471.07
Project Manager	$ 149.24	$ 25,867.77				$ 27,978.58	$ 29,097.72	$ 30,261.63	$ 29,112.64
Project Superintendent	$ 123.73	$ 21,446.12				$ 23,196.12	$ 24,123.97	$ 25,088.93	$ 24,136.34
Area Superintendent	$ 102.43	$ 17,754.19				$ 19,202.93	$ 19,971.05	$ 20,769.89	$ 19,981.29
Assistant Project Manager= HP Project Engineer	$ 85.04	$ 14,739.98				$ 15,942.77	$ 16,580.48	$ 17,243.70	$ 16,588.98
Project Engineer = HP Office Engineer	$ 69.66	$ 12,074.17				$ 13,059.42	$ 13,581.80	$ 14,125.07	$ 13,588.76
Safety Manager	$ 112.27	$ 19,459.76				$ 21,047.68	$ 21,889.58	$ 22,765.17	$ 21,900.81
Safety Engineer	$ 79.54	$ 13,786.67				$ 14,911.66	$ 15,508.13	$ 16,128.45	$ 15,516.08
Office Engineer	$ 69.66	$ 12,074.17				$ 13,059.42	$ 13,581.80	$ 14,125.07	$ 13,588.76
Field Engineer	$ 68.40	$ 11,855.77				$ 12,823.20	$ 13,336.13	$ 13,869.58	$ 13,342.97
MEP Coordinator	$ 139.28	$ 24,141.40				$ 26,111.34	$ 27,155.79	$ 28,242.03	$ 27,169.72
VDC Engineer	$ 99.31	$ 17,213.40				$ 18,618.02	$ 19,362.74	$ 20,137.25	$ 19,372.67
Senior Estimator	$ 114.60	$ 19,863.62				$ 21,484.49	$ 22,343.87	$ 23,237.62	$ 22,355.33
Project Estimator	$ 117.69	$ 20,399.21				$ 22,063.78	$ 22,946.33	$ 23,864.19	$ 22,958.10
Lead Estimator	$ 103.00	$ 17,852.99				$ 19,309.79	$ 20,082.19	$ 20,885.47	$ 20,092.48
Estimator	$ 85.26	$ 14,778.12				$ 15,984.01	$ 16,623.37	$ 17,288.31	$ 16,631.90
Scheduler	$ 109.06	$ 18,903.37				$ 20,445.88	$ 21,263.72	$ 22,114.27	$ 21,274.62
Office Manager	$ 33.90	$ 5,875.89				$ 6,355.36	$ 6,609.57	$ 6,873.96	$ 6,612.96
Admin / Secretary	$ 44.22	$ 7,664.65				$ 8,290.09	$ 8,621.69	$ 8,966.56	$ 8,626.11
						$ -	$ -	$ -	$ -
Intern	$ 30.38	$ 5,265.77				$ 5,695.45	$ 5,923.27	$ 6,160.20	$ 5,926.31
						$ -	$ -	$ -	$ -
Partners						$ -	$ -	$ -	$ -
Job Site Accountant	$ 89.17	$ 15,455.84				$ 16,717.03	$ 17,385.71	$ 18,081.14	$ 17,394.63
Design Manager	$ 156.65	$ 27,152.14				$ 29,367.76	$ 30,542.47	$ 31,764.17	$ 30,558.13
Project Estimator	$ 110.14	$ 19,090.57				$ 20,648.36	$ 21,474.29	$ 22,333.26	$ 21,485.30
CQC Manager	$ 141.98	$ 24,609.39				$ 26,617.52	$ 27,682.22	$ 28,789.51	$ 27,696.42
CQC Lead	$ 120.46	$ 20,879.33				$ 22,583.09	$ 23,486.41	$ 24,425.87	$ 23,498.45
CQC Assistant	$ 96.62	$ 16,747.14				$ 18,113.71	$ 18,838.26	$ 19,591.79	$ 18,847.92
VDC Manager	$ 137.28	$ 23,794.74				$ 25,736.39	$ 26,765.85	$ 27,836.48	$ 26,779.58
Lead VDC Engineer	$ 112.97	$ 19,581.09				$ 21,178.91	$ 22,026.06	$ 22,907.11	$ 22,037.36

SBE Program

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C SBE Report

As a result of Prime Change Order 3 the previous Disadvantaged Business Enterprise (DBE) requirements have been replaced with Small Business Enterprise (SBE) requirements and the goal for construction was revised from 12.8% to 13%. The SBE goal has been revised in Supplement C to 12.2% based on ODP reductions as shown on following chart. The requirements of the program are stated within the Hillsborough County Aviation Authority Small Business Enterprise (SBE) Policy and Program dated September 4, 2025.

The following Participation Summary for anticipated participation for the SBE program. Further details on selected subcontractors will be provided in the Subcontractor Recommendation Letters that will be submitted for each trade. Letters of Intent for sub-tier vendors will be provided in the future as appropriate and in accordance with Tampa Airport's SBE Program.

SBE Participation Summary

Trade Description	Total Value	SBE Value	%
Enabling GMP	$ 88,816,106	$ 15,280,180	**17%**
Supplement A	$ 103,329,020	$ 28,310,816	**27%**
Supplement B	$ 92,414,004	$ 3,738,276	**4%**
Wave 1 Subcontractors			
Demolition - NorthStar			
Subtier 1 - To be submitted with Award Recommendation	$ 1,908,000	$ 190,800	**10%**
Concrete - Liberty			
Subtier 1 - To be submitted with Award Recommendation	$ 11,967,000	$ 2,154,060	**18%**
Masonry - Masonry Systems			
Subtier 1 - To be submitted with Award Recommendation	$ 2,273,000	$ 431,870	**19%**
Ornamental Metals - Acousti			
Subtier 1 - To be submitted with Award Recommendation	$ 5,246,000	$ 1,311,500	**25%**
Waterproofing - Apex			
Subtier 1 - To be submitted with Award Recommendation	$ 1,365,000	$ 245,700	**18%**
Roofing - Architectural Sheetmetal			
Subtier 1 - To be submitted with Award Recommendation	$ 10,433,000	$ 1,877,940	**18%**
Metal Panels - Cladding Systems			
Subtier 1 - To be submitted with Award Recommendation	$ 3,885,000	$ 3,885,000	**100%**
Interior Wall Panels - Acousti			
Subtier 1 - To be submitted with Award Recommendation	$ 2,322,000	$ 487,620	**21%**
Fireproofing - Rolling Plains			
Subtier 1 - To be submitted with Award Recommendation	$ 4,283,000	$ 642,450	**15%**
Glass & Glazing - West Tampa Glass			
Subtier 1 - To be submitted with Award Recommendation	$ 17,469,000	$ 3,668,490	**21%**
Glass Handrail - Stainless Fabricators			
Subtier 1 - To be submitted with Award Recommendation	$ 2,195,000	$ -	**0%**
Drywall - Kenpat			
Subtier 1 - To be submitted with Award Recommendation	$ 22,350,000	$ 4,917,000	**22%**
Terrazzo - David Allen			
Subtier 1 - To be submitted with Award Recommendation	$ 5,848,000	$ 877,200	**15%**
Acoustical Ceilings - Acousti			
Subtier 1 - To be submitted with Award Recommendation	$ 6,683,000	$ 1,202,940	**18%**
Elevators & Escalators - Schindler			

SBE Participation Summary

	Trade	Total Value	SBE Value	%
	Subtier 1 - To be submitted with Award Recommendation	$ 8,669,000	$ 260,070	**3%**
	Fire Protection - Pye-Barker Fire & Safety			
	Subtier 1 - To be submitted with Award Recommendation	$ 6,148,000	$ 1,229,600	**20%**
	Sitework - Crisdel			
	Subtier 1 - To be submitted with Award Recommendation	$ 21,563,000	$ 4,096,970	**19%**
	Engineered Special Structures - Structural			
	Subtier 1 - To be submitted with Award Recommendation	$ 1,709,677	$ -	**0%**
	Site Utilities - Murphy Pipelines			
	Subtier 1 - To be submitted with Award Recommendation	$ 1,927,000	$ -	**0%**
	Structural Steel - GMF			
Design Assist	Subtier 1 - To be submitted with Award Recommendation	$ 5,349,993	$ 2,234,500	**42%**
	Adjustment to GMF Supplement A Goal		$ (8,476,033)	
	ODP Reduction - GMF			
	Electrical - APG			
Design Assist	Subtier 1 - To be submitted with Award Recommendation	$ 70,702,041	$ 15,654,053	**22%**
	Low Voltage - MC Dean			
Design Assist	Subtier 1 - To be submitted with Award Recommendation	$ 49,581,097	$ 10,787,241	**22%**
	Mechanical & Plumbing - BCH			
Design Assist	Subtier 1 - To be submitted with Award Recommendation	$ 75,651,574	$ 11,749,928	**16%**
	Baggage Handling System - Daifuku			
Design Assist	Subtier 1 - To be submitted with Award Recommendation	$ 233,373,826	$ 35,372,851	**15%**
	Wave 2 Contractors			
	Final Cleaning - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 945,110	$ 141,767	**15%**
	Rough Carpentry - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 660,844	$ -	**0%**
	Millwork - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 6,157,704	$ 307,885	**5%**
	Doors, Frames & Hardware - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 4,259,240	$ 425,924	**10%**
	Tile - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 5,169,179	$ 258,459	**5%**
	Resilient & Carpet Flooring - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 1,932,940	$ 193,294	**10%**
	Specialty Flooring - TBD			
	Subtier 1 - To be submitted with Award Recommendation	$ 785,111	$ 78,511	**10%**

SBE Participation Summary

Trade	Total Value	SBE Value	%
Paint & Wallcovering - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 4,169,424	$ 416,942	**10%**
Building Specialties - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 177,150	$ 26,573	**15%**
Fire Protection Specialties - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 93,850	$ 9,385	**10%**
Miscellaneous Specialties - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 692,350	$ 69,235	**10%**
Loading Dock Equipment - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 75,000	$ -	**0%**
Commercial Equipment - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 1,487,000	$ -	**0%**
Play Structures - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 70,000	$ -	**0%**
Detention Equipment - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 100,000	$ 10,000	**10%**
Entrance Mats - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 200,000	$ 20,000	**10%**
Window Treatments - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 449,565	$ 44,957	**10%**
Furnishings - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 6,660,532	$ 3,996,319	**60%**
Interior Plants & Planters - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 1,043,000	$ 104,300	**10%**
Pavement Markings - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 99,210	$ -	**0%**
Fencing - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 614,125	$ 61,413	**10%**

SBE Participation Summary

Trade	Total Value	SBE Value	%
Site Furnishings - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 434,150	$ 21,708	**5%**
Landscaping & Irrigation - TBD			
Subtier 1 - To be submitted with Award Recommendation	$ 223,449	$ 22,345	**10%**
HNTB			
CA Services	$ 27,156,889	$ 3,201,192	**12%**
Hensel Phelps			
General Conditions / General Requirements	$ 85,495,990	$ 2,730,000	**3%**
Contractors Budgets			
Contractors Allowances	$ 15,461,766	$ -	**0%**
Totals Supplement C GMP:	$ 902,122,150	$ 106,941,957	11.9%
DRAFT PROJECTION PENDING FINAL BIDDING AND NEGOTIATIONS			
All GMP's (including COR 1,2,3):	$ 1,186,681,280	$ 154,271,229	13.0%
ODP Change Order Reductions			
COR 4	$ (11,185,168)	$ (11,185,168)	
COR 5	$ (373,300)	$ -	
ODP Reductions:	$ (11,558,468)	$ (11,185,168)	-0.9%
All GMP's (Through COR 5):	$ 1,175,122,812	$ 143,086,061	12.2%

Clarifications & Assumptions

GMP Supplemental C Clarifications and Assumptions

The following clarifications and assumptions are provided to convey the basis of the Supplement C GMP.

GENERAL INFORMATION

1) This Supplement contains no costs associated with the Airside E Baggage Handling System Optimization, any work taking place at the airsides as part of the Airside C & A-Sortation Baggage Handling System Screening Relocation, nor work associated with tenant relocations to Airside D. These portions of the project remain unfunded or remain to be designed awaiting the HCAA relocation matrix. Costs will be included in future Supplemental GMP submissions. Notwithstanding the foregoing, Design-Builder has responsibility for coordination of these projects.

2) This supplement includes the following items associated with the LED panel screens based on the baseline schedule submitted with this supplemental C:
   - General Requirements
   - General Conditions
   - LED features will be funded via WO from Owner's Allowance

3) This supplement does not include the following items associated with the LED panel screens based on the baseline schedule submitted with this supplemental C:
   - Costs associated with the content creator, their content creation, licensing, subscriptions, warranties, or similar items are not included in this supplement.
   - Electrical and telecommunications rooms, resultant modifications to building systems, or any other changes to the building necessary for LED panels.
   - Procurement, purchasing, shipping, storage, or timely conveyance to the installation area of the LED screen panels, racks, or similar items as they will be provided exclusively by Owner as is currently planned.
   - It is understood by HCAA and Design-Builder that the LED panel installation is contingent upon a dust-free environment.

4) No costs have been included to provide design, design services, design review, or permitting services for any tenant or stakeholder space.

5) No costs have been included for any work associated with incorporating tenant or stakeholder designs and models into the overall building models or final as-builts.

6) Design-Builder will review 100% design documents received from HCAA for tenant and stakeholder spaces for interface compatibility only.

7) This Supplement contains no costs associated with the Main Terminal Ticket Counter Modernization Project or modifications to any roadway signage.

8) This Supplement includes an Owner’s Allowance for the forthcoming Airline Relocation scope. This Supplement does not include modifications to any roadway signage for the forthcoming Airline Relocation scope. The baseline schedule included in this Supplement does not include any time associated with the forthcoming Airline Relocation scope.

9) All eligible remaining funds from the Part 1 Contract, Part 2 contract, Supplemental A, Supplemental B, and other subsequent GMPs may be transferred to other project GMPs, to support the overall program budget. These transfers will be coordinated with the Owner so that these accounting adjustments are controlled moves.

10) Pricing contained within this estimate does not include Buy American Act requirements.

11) Pricing contained within this estimate does not include Project Labor Agreements (PLA).

12) Costs associated with LEED certification within ASD have been included. Any certification above Certified will be additional cost.

13) All costs for development fees, impact fees, capacity fees, and facilities charges are to be paid by HCAA.

14) All costs from the utility companies associated with electrical, water, and sewer services including permits, impact fees, connection fees, equipment charges, consumption charges, and other such costs for temporary and permanent electrical power and water usage consumption for the project including on-site temporary office space are to be paid by Owner via direct invoice from the utility provider. The following exceptions to this provision are as follows:

    i) The sewer discharge fee for disposal of contaminated water will be paid via the contaminated soil and water management allowance.

15) Data service for the Design-Builder, the subcontractors, and the ITB contractors, including installation and consumption, will be via private service provider and all cost for this service will be paid by the respective end user.

16) No costs have been included in this supplement for establishing post-substantial completion maintenance agreements between HCAA and prospective construction contractors.

17) Operation Readiness and Airport Transfer (ORAT), managed by HCAA, has been incorporated into the program schedule with considerations and accommodations made to the best of Hensel Phelp's understanding at the time of this submission.

    a) If tenant or concessions spaces complete build-out early, no costs have been included for protection of, cleaning of, or re-cleaning of these spaces that do not immediately commence stocking, training, or ORAT activities.

18) This supplement is inclusive of all enacted tariffs up to the February 5, 2026 board award.

PROJECT SPECIFIC INFORMATION

1) The estimate is based on the construction schedule submitted with this Supplement. Further schedule development may be necessary as the impacts of the planned HCAA requested design changes for the LED screens and pools design and the FIS elevator core enhancements are not yet incorporated. Further, this schedule is based upon assumptions of durations for ITB and HCAA direct subcontractors and tenants.

2) The work of this Supplement is based on the project access (including the construction access drive) and security protocols approved in the Part 2 agreement in December 2024. If operational concerns arise, Design-Builder and HCAA Leadership shall undertake all reasonable efforts, through mutual consultation and coordination, prior to implementing any actions that may adversely affect the operation of the construction access drive. In the event the construction access drive becomes unavailable for any reason, a significant impact to project cost and schedule is anticipated. Accordingly, the Design Builder shall have the right to submit a claim for both cost and time adjustments, following the established claim procedures contained in the Part 2 Contract.

3) A Time Impact Analysis (TIA) for the LED pools and vertical elements has been incorporated into the CPM schedule included within this Supplement. Upon completion, procurement and coordination of these LED systems, a revised TIA inclusive of the fully designed system will be developed and submitted for approval via HCAA change order (in addition to cost elements) subject to the Part 2 contract terms.

4) Sales taxes are included pursuant to the statutory rates required of Hillsborough County and the State of Florida.

5) General Liability Insurance wrap-up program has been included.

6) As part of this submission, the Design Assist Subcontractors have provided quotations from various suppliers and subcontractors to substantiate costs within this Supplement. These quotations contain terms and conditions, inclusions, exclusions, and various other items that are communication between the Design Assist Subcontractor and the vendor and this communication is strictly between those two firms. Design-Builder and HCAA shall have no obligations based on language contained within this back-up as these items are for Design Assist Subcontractors to coordinate and manage. Notwithstanding the foregoing, all required flow down provisions will be included in the design-assist subcontracts.
7) This Supplement is based on the most responsive bidder. Failure of the most responsive bidder to come to terms with HCAA maintenance agreements, service contracts, material purchase orders and other such agreements post award is not the responsibility of Design-Builder and the Design Build team.
8) Any unused Supplement funds that are not considered an allowance in the estimate summary will be transitioned to the Design-Builder's contingency. For this submission of Supplemental C, the design builder's contingency has been calculated to 5% of the aggregate cost of the remaining work to be completed (including this supplement).
9) The clarification included in the Part 2 Contract Design-Builder's Clarifications and Assumptions regarding weather days is hereby superseded by the language included in the Prime Contract terms and conditions.
10) The full value of the builder's risk policy through September 30, 2028 was included with Supplemental A. Final builders risk insurance costs will be actualized based on the final contract value and final schedule durations.
11) Space allocation for HCAA art in public places installations have been incorporated into the project design. While an art allowance has been incorporated into this GMP for budgeting, provisions for additional time shall be negotiated with HCAA and incorporated by change order.
12) Intent of general conditions for hard cost goods can be transitioned / converted to a monthly lump sum rate upon agreement between HCAA and Design-Builder.
13) Portions of the Centralized Checked Baggage project scheduled to take place in public areas accessed by passengers and are understood to occur at night and in full cooperation with airport operations. Design-Builder and HCAA will work in cooperation to establish a 40 hour work week. Work in these areas that will take place behind temporary partitions and does not interface with public, or airport operations can be performed during normal business hours. For work scheduled to take place at the Departures Drive Aisle, Vertical Circulation Building (VCB), and Shuttle Station Platform, it is expected that at least 2 lanes of traffic may be shut down for each work shift, however, the shutdown lanes will not extend the entire length of the curbside, such that some doors will remain accessible to the public at all times.

DIVISION 1 – GENERAL REQUIREMENTS

1) Demolition and removal of office compound parking lot surface, trade partner parking lot surface, and construction access roadway are not included. All utilities supporting the office compound and guard booths are to remain, though stub-ups will be cut and capped upon removal of temporary building structures.
2) This Supplement includes an Owner's Allowance for the forthcoming Oversized Baggage System and associated enclosure (TE 207) scope. The baseline schedule included in this Supplement does not include any time associated with the forthcoming Oversized Baggage System and associated enclosure (TE 207) scope.
3) This Supplement includes an Owner's Allowance for the forthcoming TSA Break Room (TE 202) scope. The baseline schedule included in this Supplement does not include any time associated with the forthcoming TSA Break Room (TE 202) scope.
4) This Supplement includes an Owner's Allowance for the forthcoming Airside C and A-Sortation Screening Inclusion work taking place at the Airsides (TE 205B) scope. The baseline schedule included in this

Supplement does not include any time associated with the forthcoming Airside C and A-Sortation Screening Inclusion work taking place at the Airsides (TE 205B) scope.

5) This Supplement includes an Owner's Allowance for the forthcoming implementation of the desired BSM, plus a 1-year subscription (TE 217) scope. The baseline schedule included in this Supplement does not include any time associated with the forthcoming implementation of the desired BSM, plus a 1-year subscription (TE 217) scope.

DIVISION 2 – SITE CONSTRUCTION

DIVISION 3 – CONCRETE

DIVISION 6 – WOODS & PLASTICS

1) A ticket counter early production piece is included within the Supplement. Upon installation, Design-Builder will communicate the last available day for input into the design. Changes beyond this identified date may impact production of the remaining pieces, costs, and schedule.

DIVISION 9 – FINISHES

1) There are no finishes included by the Design-Build Team in areas indicated to receive floor finish CN00 (Unfinished Concrete, reference sheet AD-ID800, See 6524 Anchor Tenant Club Entry AD-ID912H and 6701 Anchor Tenant Club AD-ID913H). It is assumed that the Owner's Tenants will provide the finishes in these areas, including the Anchor Tenant Club Stair. (ref. Notes AD-A524 #3).

DIVISION 10 – SPECIALTIES

1) Wayfinding signage as indicated in the drawings and specifications is included. Any other signage not shown in the drawings and specifications has not been included in this supplement.

DIVISION 11 – EQUIPMENT

1) Furnishing, installation, and testing of E-gates (EQ-50) is to be completed by HCAA.

DIVISION 12 – FURNISHINGS

1) All interior, live plant landscaping shall be furnished and installed by HCAA. No irrigation has been incorporated into the design for live plants within the building.

2) No costs have been carried to modify/replace proprietary gate counters and signage at the existing Delta space at Airside E. It is assumed that the scope of work to make the space tenantable when Delta vacates is by others.

3) Budgets for the relocation of airlines moveable furnishings, equipment, and employees' personal affects have not been included in this supplement.

DIVISION 14 – CONVEYING SYSTEMS

1) Video and Messaging (VAM) system to individual elevators will mirror the functionality of the red curbside elevator program.

DIVISION 15 – MECHANICAL SYSTEMS

FIRE PROTECTION

1) The Design-Builder has gauged the existing capacity and flows for fire protection and deemed them acceptable. Should the capacity and flow change as a result of modifications post the date of this supplement, impacts will be investigated and addressed per contractual protocols.
2) For the Main Terminal work associated with the new BHS scope related to ASD, the Supplement includes reasonable modifications and adjustments to the fire protection at the Arrivals Level of the Main Terminal. Conflicts requiring modification of the fire protection system discovered during the Supplemental B tag and trace scope shall be compensated using the tag and trace allowance for electrical and low voltage established in Supplement B.

PLUMBING

1) Gas piping included from the gas meter location to the building. Gas service main and meter assembly by utility company. Upgrades to the existing gas piping network suppling the campus and Airside D is by the utility company.
2) For the Main Terminal work associated with the new BHS scope related to ASD, the Supplement includes reasonable modifications and adjustments to the plumbing at the Arrivals Level of the Main Terminal. Conflicts requiring modification of the plumbing system discovered during the Supplemental B tag and trace scope shall be compensated using the tag and trace allowance for electrical and low voltage established in Supplement B.
3) The estimate assumes that the sanitary system has the appropriate fall and acceptable conditions for ASD tie-in. Pipe bursting beyond the limits of construction has been added to the estimate based upon the current design. No additional rehabilitation, upgrades, or capacity improvements have been included to existing sanitary systems on the campus or lift stations. The Design Build team has completed their due diligence on this item and concluded that the pipe bursting is the most cost effective path.

HVAC

1) In addition to temporary cooling measures being utilized and incorporated into the estimate, it is the intent that the team will transition to the permanent HVAC system during construction to facilitate the installation of finishes. We have included provisions for temporary filters for construction and installation of final filters after construction.
2) For the Main Terminal work associated with the new BHS scope related to ASD, the Supplement includes reasonable modifications and adjustments to the HVAC system at the Arrivals Level of the Main Terminal. Conflicts requiring modification of the HVAC system discovered during the Supplemental B tag and trace scope shall be compensated using the tag and trace allowance for electrical and low voltage established in Supplement B.

DIVISION 16 – ELECTRICAL SYSTEMS

ELECTRICAL

1) Art lighting incorporated into 100% Contract Documents (CDs) by Design Team is not intended to capture all cost for art lighting. Future coordination with Artists teams will dictate necessary lighting for each art piece and costs associated will be covered via art infrastructure allowance.
2) For the Main Terminal work associated with the new electrical scope related to ASD, the Supplement includes reasonable modifications and adjustments to the electrical system at the Arrivals Level of the Main Terminal. Conflicts requiring modification of the electrical system discovered during the Supplemental B tag and trace scope shall be compensated using the tag and trace allowance for electrical established in Supplement B.

LOW VOLTAGE SYSTEMS

1) This Supplement does not contain costs associated with the procurement, furnishing, or supply of digital displays for ASD nor any other portion of the project. Digital displays are to be furnished and installed by HCAA or their direct subcontractors. Digital displays include but are not limited to televisions, Flight Information Display Systems (FIDS), Baggage Information Display Systems (BIDS), Visual Docking Guidance Systems (VDGS), digital advertising displays, digital passenger experience displays, personnel monitors, and other similar devices.
2) For the Main Terminal work associated with the new low voltage scope related to ASD, the Supplement includes reasonable modifications and adjustments to the low voltage system at the Arrivals Level of the Main Terminal. Conflicts requiring modification of the low voltage system discovered during the Supplemental B tag and trace scope shall be compensated using the tag and trace allowance for low voltage established in Supplement B.

DIVISION 34 – BAGGAGE HANDLING SYSTEMS

1) Costs included are based on proceeding with the Brock custom Variable Frequency Drive (VFD) Enclosure system distributed to HCAA on 11/13/25.
2) Warehousing costs and maintenance of warehousing are not included in this package. It is assumed that BHS warehousing needs are being provided by HCAA, through Final Completion of the project. All standard warehouse maintenance required to provide constant adequate use to the construction team will be the responsibility of HCAA.
3) Utilization of the existing baggage handling system (and associated equipment) will be required to accommodate phasing and certification of the new system. The material and labor included in this submission are based on all equipment functioning in a condition that allows for the certification of the new system.
4) It is understood that service to ticket counter induction points and bag claim carousels, including shutdowns, will be disrupted due to phasing requirements. Refer to the sequencing within the Contract Documents and the schedule for anticipated durations. Coordination with HCAA and Stakeholders will be required. Portering will be required and will be provided as part of this contract. Portering will be coordinated accordingly.
5) Salvage labor of existing baggage system components and relocation to storage is not included.

6) After Design-Builder completes the design for Airside E Optimization and Airside A and C modifications, Design-Builder will provide a forthcoming Supplemental D, inclusive of a construction schedule and all associated general conditions. This work will take place after Substantial Completion of the CCBS project.

7) Utilization of the laydown areas North of A-Sortation and Blue Quad 1, including the work required to re-purpose the Blue Quad 1 laydown space for access to the bag room, are included in this Supplement.

8) Utilization of 22 parking spaces within level 1 of the Long Term Parking Garage (LTPG) for Trade Partner shuttle parking is included in this Supplement. Shuttling will be performed by the Trade Partners.

9) It is understood that multiple adjacent Bag Claim Carousels can be taken out of operation for multiple project phases to accommodate the work that is required to take place above the Bag Claim ceilings, with the exception of Carousels 14 and 15 (Red Side), as one of these two carousels will need to be operational at all times. It is understood that there are project locations that require contractors to match existing finishes. However, if the appropriate quantity of attic stock is not available or the exact finish is no longer available, the work will be completed to the satisfaction of the Owner. Should the lack of resources result in the inability to match existing, and full replacement of adjacent finishes is required, Design-Builder reserves the right to additional compensation and time extension.

10) The 100% documents call for the recontrol/modification of existing conveyor for the BHS system. Unless expressly noted in the documents, it is assumed that the visual aesthetic of existing repurposed systems is acceptable.

11) At the direction of HCAA an owner's allowance has been added to account for the future work at Airside E. This owner's allowance has been based upon the submitted 50% estimate by Design-Builder for the Airside E BHS Optimization project.

12) Due to the existing systems being operational, the ability to test existing baggage conveyor systems for any hazardous materials was not feasible. Should hazardous materials be found at the decommissioning of the system, costs shall be covered via the Supplemental B hazardous abatement allowance.

Design Assist Subcontractor Back-up

Structural Steel

GMF Steel Group

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C Funding Summary

GMF Funding Summary

Estimate Value:	$70,958,359	
Less Supplemental A Funding:	$15,639,258	(ASD)
Less Supplemental B Funding:	$49,969,108	(ASD)
Supplemental C Funding:	$1,777,423	(ASD)
Supplemental C Funding:	$3,572,570	(CCBS)

GMF Funding Summary

Overall **- $70,958,359**

Supp A - **$15,639,258**

Supp B - **$49,969,108**

Supp C - **$5,349,993**

Base Contract Bond allowance funding - $492,063

Contingency Change Orders:

SCO 1 - $505,908 - Fabrication Acceleration - Contingency
SCO 2 - $4,704 - Crash Bars - Contingency

Re: 8500 23 Airside D 100% Design Estimate

Dear Sir:
We wish to submit for your approval the following budget estimate based on ASD 100% Construction Documents & CCBS 100% Construction Documents dated 10/30/2025. GMF Steel Group reserves the right to modify the budget based on receipt of additional information, specifications and/or drawings, which were not included in the bid package.

1) **8500 23 Airside D-Building $67,385,789.00**
2) **8515 24 CCBS Main Terminal.....$3,572,570.00**

Grand Total = $70,958,359

This proposal is also based on the provision of clear access to the job site for cranes and lifting equipment required to perform the work. Anchor bolts must be cleaned, oiled, and taped ready for column installation. The work schedule must be accomplished in a contiguous time-period once the job is started. Work stoppages by the customer or other crafts may result in additional charges.

If you have any questions, please contact us.

Sincerely,

Jason Davis

Jason Davis, *Chief Estimator*
GMF Steel Group
gmfsteel.com
jason.davis@gmfsteel.com
Phone: (863) 577-0210

Grand Total $70,958,859
Less Supplemental A Funding $15,639,258
Less Supplemental B Funding $49,969,108
$5,349,993

Supplemental C ASD - $1,777,423
Supplemental C CCBS - $3,572,570

For information only. Not a contract document

Design Assist Subcontractor Back-up

Fiber Reinforcing

Structural

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

Shakeil Williams
2001 Blount Rd, Pompano Beach, FL
Mobile: 954-242-2724

srwilliams@structural.net
www.structural.net

Proposal No. FY25-696258
Tampa International - Red Side Baggage Claim FRP
January 6, 2026

Nick Petterson
Hensel Phelps Construction
6557 Hazeline National Drive No. 1
Orlando, FL 32822

Dear: Mr. Petterson

Thank you for giving STRUCTURAL the opportunity to prepare a proposal for the investigation survey and the carbon fiber reinforced polymer strengthening system installation at the Red Side Baggage Claim at Tampa International Airport.

STRUCTURAL trusts we have provided adequate detail for your evaluation, and we have expressed our desire to work with Hensel Phelps and the Hillsborough Aviation Authority on this important project. The following outlines the project scope of services, working conditions, exclusions and support by others, safety considerations, estimated schedule, financials, suggested next step and attachments as they relate to this project.

SCOPE OF SERVICE

1. General Conditions (CFRP Strengthening System Installation)

a. Mobilization & Demobilization:
Mobilize all necessary labor, equipment, and materials to the site. Demobilize upon completion, including removal of all temporary facilities.

For information only. Not a contract document

b. **Set Up Mixing Station, Equipment & Layout:**
Establish a mixing station and lay out equipment for efficient workflow.
c. **Set Up Protection:**
Install protective measures to safeguard existing surfaces and adjacent areas.
d. **Clean Up:**
Perform daily and final clean-up of the work area to maintain safety and minimize disruption.
e. **Engineering:**
Provide delegated design and signed and sealed CFRP installation drawings and calculations per design criteria for permitting and/or review.

2. Investigation Survey and CFRP Layout (Phase 1- 4)

a. **Investigation / Survey and coordination with Structural Technologies:**
Perform detailed survey and layout of CFRP locations to identify and document equipment, obstructions requiring relocation, and existing conditions such as structural cracks, rough edges requiring smoothing, or other related encumbrances that could affect the pursuit of work. Structural will coordinate with Structural Technologies (ST) and Hensel Phelps to ensure all logistical requirements are met and operational functionality is maintained until final installation of the delegated strengthening system.

b. **Project preplanning & Project Coordination**
Conduct initial project kickoff meetings with the client and key stakeholders to clarify objectives, constraints, and expectations.

c. **Reporting and Recommendations**
A comprehensive investigation report will be prepared summarizing existing conditions and constraints, recommended repairs or modifications, preliminary design concepts and sketches, phasing and sequencing recommendations, and estimated quantities and materials, with all findings and recommendations presented to Hensel Phelps for review and approval.

3. FRP Beam & Girder Strengthening – Phase 1

a. **Surface Preparation:**
Prepare all designated surfaces (up to 3,338.2 SF) for FRP installation, including cleaning, profiling, and rounding corners (up to 1,088.2 LF).
b. **FRP Installation:**
Supply and install CFRP systems per drawings and specifications:
C220HM (Beams): Install up to 1,317.9 SF.
C440HM (Girders): Install up to 523.3 SF.
c. **FRP Embed Anchors:**
Drill and install up to 1,652 each 1" diameter x 6" deep anchors.
Install 7/8"x20" Anchors: Install up to 1,652 anchors as specified.
d. **Coating Application:**
Apply V-Wrap FPS fireproofing (up to 3,338.2 SF at 1" thickness) to all designated areas.

4. FRP Beam & Girder Strengthening – Phase 2

For information only. Not a contract document

a. **Surface Preparation:**
Prepare all designated surfaces (up to 1,968.7 SF) for FRP installation, including cleaning, profiling, and rounding corners (up to 614.4 LF).
b. **FRP Installation:**
Supply and install CFRP systems per drawings and specifications:
C220HM (Beams): Install up to 741.7 SF.
C440HM (Girders): Install up to 333.6 SF.
c. **FRP Embed Anchors:**
Drill and install up to 968 each 1" diameter x 6" deep anchors.
Install 7/8"x20" Anchors: Install up to 968 anchors as specified.
d. **Coating Application:**
Apply V-Wrap FPS fireproofing (up to 1,968.7 SF at 1" thickness) to all designated areas.

5. FRP Beam & Girder Strengthening – Phase 3

a. **Surface Preparation:**
Prepare all designated surfaces (up to 2,241.1 SF) for FRP installation, including cleaning, profiling, and rounding corners (up to 747.4 LF).
b. **FRP Installation:**
Supply and install CFRP systems per drawings and specifications:
C220HM (Beams): Install up to 950 SF.
C440HM (Girders): Install up to 297.1 SF.
c. **FRP Embed Anchors:**
Drill and install up to 1,138 each 1" diameter x 6" deep anchors.
Install 7/8"x20" Anchors: Install up to 1,138 anchors as specified.
d. **Coating Application:**
Apply V-Wrap FPS fireproofing (up to 2,241.6SF at 1" thickness) to all designated areas.

6. FRP Beam & Girder Strengthening – Phase 4

a. **Surface Preparation:**
Prepare all designated surfaces (up to 750.3 SF) for FRP installation, including cleaning, profiling, and rounding corners (up to 225.8LF).
b. **FRP Installation:**
Supply and install CFRP systems per drawings and specifications:
C220HM (Beams): Install up to 250 SF.
C440HM (Girders): Install up to 168.3 SF.
c. **FRP Embed Anchors:**
Drill and install up to 368 each 1" diameter x 6" deep anchors.
Install 7/8"x20" Anchors: Install up to 368 anchors as specified.
d. **Coating Application:**
Apply V-Wrap FPS fireproofing (up to 750.3 SF at 1" thickness) to all designated areas.

7. Miscellaneous Structural Repairs

Confidential: Any unauthorized use or distribution is prohibited.

For information only. Not a contract document

a. Epoxy Application:
Apply thickened epoxy at all locations where carbon fiber contacts steel (up to. 24 each, 6 per location).

8. Allowances

a. Structural Crack Repair:
Perform structural crack repair per ACI (American Concrete Institute RAP Bulletin1 (attached)) Provide for injection of cracks (1,230lf included) using Sikadur 35/31 or approved equivalent.

b. Smoothing out rough edges:
Allowance for smoothing rough edges necessary for proper CFRP installation (up to 750 LF).

c. Access development:
Allowance includes providing and maintaining temporary scaffolding as needed to ensure safe access to designated work areas.

WORKING CONDITIONS

1) This proposal is based on performing work during eight mobilizations, four locations with two mobilizations per location. First mobilization is for layout / survey and the second mobilization is for CFRP installation.
2) This proposal is based on performing all work in a maximum of eight phases.
3) This proposal is based on the following working hour assumptions:
   a) Nighttime work hours.
   b) Five (5) day week SMTWT.
4) This proposal is based on the following labor rate assumptions:
   a) Open shop labor without prevailing wages

SUPPORT BY OTHERS (at no cost to STRUCTURAL) SHALL INCLUDE THE FOLLOWING

1) Site utilities, including but not limited to:
   a) 110V 20-amp power electric available at existing outlets/panels.
   b) Toilet facilities.
   c) Potable water.
   d) Payment for all required utility costs.
2) General site support, including but not limited to:
   a) Parking for employees, service vehicles and 2nd tier sub-contractors.
   b) Temporary site office space and storage area (a minimum of 10’x10’ area).
   c) Use of General Contractor’s dumpster for general construction debris disposal.
3) Active work support, including but not limited to:
   a) Installation and removal of interior finishes protection, including floor and elevators from the exterior of the building to STRUCTURAL’s work area.
4) All permits will be billed at cost.
5) Unobstructed access to the work area, including but not limited to removal of mechanical and electrical appurtenances.

Confidential: Any unauthorized use or distribution is prohibited.

For information only. Not a contract document

6) This proposal includes costs for badging and background checks, with a rate of $60 per year per person.

SCOPE CLARIFICATIONS

1) No warranties will exceed 1 year.
2) Pricing is based on award of the full scope of work. STRUCTURAL reserves the right to modify pricing should a partial scope be awarded.
3) This proposal is based on providing FRP tension reinforcement equivalent to the specified additional steel reinforcing bars. Structural modeling or analysis to evaluate the slab or confirm the specified additional reinforcement is outside the scope of this proposal.

EXCLUSIONS

1. Bonds and associated costs.
2. Protection of finished work after crews have demobilized from the site.
3. Coordination between various trades, including those that may affect the scope of work performed under this proposal.
4. Any work specifically not included in this proposal.

PROJECT SAFETY CONSIDERATIONS

Safety is a core principle – there is nothing more important in what we do, 24/7. We owe it to our clients. We owe it to our employees. We owe it to the families of those that count on us. It's a moral and ethical requirement of our business.

STRUCTURAL's Frontline Safety Program in combination with a project-specific Safety Execution Plan will ensure that safety will be a primary measurement of success on this project.

SCHEDULE

STRUCTURAL anticipates a schedule of approximately 6 weeks for Phase 1.

STRUCTURAL anticipates a schedule of approximately 6 weeks for Phase 2.

STRUCTURAL anticipates a schedule of approximately 6 weeks for Phase 3.

STRUCTURAL anticipates a schedule of approximately 6 weeks for Phase 4.

Confidential: Any unauthorized use or distribution is prohibited.

For information only. Not a contract document

PRICE

Scope of service (Phase 1) $540,413.00

Scope of service (Phase 2) $396,961.00

Scope of service (Phase 3) $426,856.00

Scope of service (Phase 4) $258,447.00

Recommended Unit Prices

Structural crack injection (Anticipated Cost $35,000) .....$29.00 per LF

Smoothing out rough edges (Anticipated Cost $12,000) .....$16.00 per LF

Access development (Invoice +10% Not to Exceed Budget) $40,000.00

$1,709,677

EXPIRATION

This proposal may be withdrawn if not accepted within thirty (30) days of the date of this proposal.

Very Truly Yours,

STRUCTURAL PRESERVATION SYSTEMS, LLC.

Shakeil Williams
Estimator

Confidential: Any unauthorized use or distribution is prohibited.

For information only. Not a contract document

Design Assist Subcontractor Back-up

Mechanical

BCH Mechanical LLC

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C Funding Summary

BCH HVAC Funding Summary

Estimate Value:	$64,622,452
Less Supplemental A Funding:	$4,720,205 (ASD)
Less Supplemental B Funding:	$0
Supplemental C Funding:	$56,119,936 (ASD)
Supplemental C Funding:	$ 3,782,311 (CCBS)

BCH Plumbing Funding Summary

Estimate Value:	$17,731,465
Less Supplemental A Funding:	$1,982,137 (ASD)
Less Supplemental B Funding:	$0
Supplemental C Funding:	$15,363,946 (ASD)
Supplemental C Funding:	$ 385,381 (CCBS)

BCH Mechanical and Plumbing Funding Summary

Overall - $82,353,917

Mechanical and Plumbing

Supp A - $6,702,343 (BASE, SCO 2, 3)

BASE - $2,003,049 (Plumb and Mech Deep UG)
SCO 2 - $4,396,205 (Chiller)
SCO 3 - $303,090 (FN Bulletin 01)

Supp B - $0

Supp C - $75,651,574

Base Contract **- $14,222 Bond**
SCO 2 Bond - **$42,306 Bond**

Contingency Change Orders

SCO 1 - $2,715 - UG Fire Main Sleeve
SCO 4 - $18,665 - FN Bulletin 02

BCH Mechanical Office
6354 118th Avenue N.
Largo, Florida 33773
Phone: 727.546.3561
Fax: 727.545.1801

12/04/2025

Greg Cobb
Hensel Phelps
6557 Hazeltine National Drive Suite 1
Orlando, FL 32822

Email: gcobb@henselphelps.com

RE: Tampa International Airport Airside D Expansion & Baggage Handling System
4100 George J Bean Parkway, Tampa FL 33607

Dear Greg:

BCH Mechanical is pleased to offer the following HVAC/plumbing budget proposal for the above referenced projects. The 100% Tampa International Airport Airside D Expansion scope is based on the mechanical drawings AD-M001 through AD-M908, plumbing drawings AD-P001 through AD-P801 and associated mechanical/plumbing specifications. There are no addenda acknowledged. These mechanical/plumbing drawings were prepared by TLC Engineering Solutions dated 10/30/2025. The 100% Tampa International Airport Baggage Handling System Upgrade scope is based on the mechanical drawings MT-M001 through MT-M703, plumbing drawings MT-P001 through MT-P601. There are no addenda acknowledged. These mechanical/plumbing drawings were prepared by TLC Engineering Solutions dated 10/30/2025. Our price includes the following:

HVAC – Furnish and Install – Airside D

1. Galvanized type sheet metal ductwork per latest SMACNA standards including the following:
   a. 316 stainless steel ductwork for fume hood.
   b. Medium pressure galvanized rectangular ductwork for supply and return air
   c. Stainless steel exhaust ductwork from shower grille to main takeoff.
2. Insulation.
3. Chilled water, low temp glycol water and heating hot water pipe, valves, and fittings above grade.
4. Exterior condenser water piping to be Aquatherm.
5. Condensate piping to be type "L" hard copper pipe and fittings.
6. Fifteen (15) chilled water Air Handling Units with Heating Hot Water Reheat.
7. Ten (10) chilled water Air Handling Units including the following:
8. One (1) custom 100% outside air AHU w/ Energy Recovery Wheel.
9. Two (2) 100% outside air indoor solution AHU's.
10. Three (3) Field Erected FRP Cooling Towers.
11. Fans included as follows:
    a. Thirty (30) circulation fans with 3,800 CFM, direct drive with 1/2-HP motor.
    b. Ten (10) inline general exhaust fans.
    c. Two (2) ceiling type general exhaust fans.

For information only. Not a contract document

12. Twenty-five (25) wall mounted DX air conditioning units and associated condensing units.
13. Thirty-one (31) chilled water fan coil.
14. Nine (9) chilled water fan coil units.
15. Three (3) chilled water blower coil including the following:
16. Four (4) gas fired condensing boilers.
17. Twenty (20) pumps.
18. One Hundred Eighty-Three (183) variable air volume units.
19. Three (3) plate and frame heat exchangers.
20. One (1) 50-gallon glycol makeup package.
21. Three (3) air separators.
22. Three (3) expansion tanks.
23. One (1) 1750-gallon glycol system buffer tank.
24. Eighty-One (81) Variable Frequency Drives (VFDs).
25. Access doors in ductwork where required.
26. Air distribution and accessories.
27. Louvers including:
    a. Ten (10) Miami-Dade vertical blade louvers.
    b. Eleven (11) horizontal blade architectural return grilles.
    c. Twenty (20) Ruskin EME6625D vertically mounted mechanical louvers.
28. Chemical water treatment.
29. Equipment rigging and start up.
30. 3-D BIM coordination drawings.
31. Controls to include JCI.
32. Duct mounted smoke detectors (furnished by division 16).
33. Test and balance.
34. Equipment rigging and start up.
35. Fire safing of rated floor and wall partitions.
36. Permits.
37. $50,000 for water softener tank prefabricated canopy with approximate dimensions of 13.5' (L) x 14.5' (W) x 16' (H)

HVAC – Furnish and Install – Centralized Checked Baggage (CCSB)

1. Remove and relocate the following equipment:
    a. Twenty-Seven (27) VAV terminal units.
    b. One Hundred-Twelve (112) linear air devices and associated plenums.
    c. Five (5) recirculation fans.
    d. Two (2) condensing units.
2. Six (6) variable air volume units.
3. One (1) cassette chilled water fan coil with heating hot water unit.
4. One (1) split system DX wall mounted air conditioner.
5. Twenty-one (21) circulation fans.
6. Fourteen (14) hot taps for chilled and heating hot water supply/return connections to existing.
7. Air distribution and accessories.
8. Pre and final test and balance.
9. Fire safing of rated floor and wall partitions.

HVAC Bid – Airside D & CCSB **$ 64,622,452.00**

For information only. Not a contract document

Less Supplement A Funding:	**$ 4,720,210.00 (ASD)**
Less Supplement B Funding:	**$ 0**
Supplement C Funding:	**$56,119,936.00 (ASD)**
Supplement C Funding:	**$ 3,347,181.00 (CCSB)**

PLUMBING - Furnish and Install – Airside D

1. Sanitary waste and vent piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
2. Sanitary waste piping below grade to be Schedule 40 PVC DWV pipe and fittings with solvent welded joints.
3. Primary/Secondary storm piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
4. Primary storm piping below grade to be Schedule 40 PVC DWV pipe and fittings with solvent welded joints.
5. Grease waste piping above grade to be 304 stainless steel push fit pipe and fittings.
6. Grease waste piping below grade to be Schedule 40 PVC DWV pipe and fittings with solvent welded joints.
7. Domestic water piping above grade to be Type K hard copper pipe and wrought copper fittings with lead free soldered joints.
8. Domestic water piping below grade to be Type K hard copper tubing and wrought copper fittings and brazed joints.
9. Condensate piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
10. Condensate piping below grade to be Schedule 40 PVC DWV pipe and fittings with solvent welded joints.
11. Natural gas piping above grade to be Schedule 40 carbon steel pipe and fittings with threaded joints for pipe sizes 2" and smaller. Piping 2 ½" and larger to be Schedule 40 carbon steel pipe and fittings with welded joints.
12. Complete insulation systems.
13. Plumbing fixtures, equipment and drains.
14. Low voltage wiring for plumbing fixtures.
15. Fire safing of rated floor and wall penetrations.
16. Permits.
17. All work to be free of defects in workmanship and materials for a period of one (1) year warranty and is to meet all state, local and governing codes.

PLUMBING - Furnish and Install – Centralized Checked Baggage (CCBS)

1. Sanitary waste and vent piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
2. Storm piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
3. Domestic water piping above grade to be Type K hard copper pipe and wrought copper fittings with lead free soldered joints.
4. Condensate piping above grade to be no hub cast iron pipe and fittings with heavy duty couplings.
5. Pumped condensate piping above grade to be Type L hard copper pipe and wrought copper fittings with lead free soldered joints.
6. Complete insulation systems.

For information only. Not a contract document

7. Plumbing fixtures and equipment.
8. Internal examination of existing underground systems as indicated on MT-P101.
9. Permits.
10. All work to be free of defects in workmanship and materials for a period of one (1) year warranty and is to meet all state, local and governing codes.

Plumbing Bid – Airside D & CCSB	**$ 17,731,465.00**
Less Supplement A Funding:	**$ 1,982,137.00 (ASD)**
Less Supplement B Funding:	**$ 0**
Supplement C Funding:	**$15,363,946.00 (ASD)**
Supplement C Funding:	**$ 253,180.00 (CCSB)**

We appreciate the opportunity to provide this proposal and look forward to working with you on this project. If you have any questions, please do not hesitate to contact me here in the office at 727-546-3561.

Sincerely,

BCH Mechanical

Travis H. Lau

Travis Lau, PE
Vice President of Preconstruction

bids/December/1201R10-TPA Airside D (100% ASD & 100% CCBS)

For information only. Not a contract document

Design Assist Subcontractor Back-up

Electrical

APG Electric

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C Funding Summary

APG Funding Summary

Estimate Value:	$90,436,272	
Less Supplemental A Funding:	$17,689,208	(ASD)
Less Supplemental B Funding:	$ 4,398,705	(CCBS)
Supplemental C Funding:	$55,778,706	(ASD)
Supplemental C Funding:	$12,569,653	(CCBS)

APG Funding Summary

Overall - $90,436,272

Supp A - **$17,689,208** (SCO BASE, 2, 3, 4, 5, 6, 7)

BASE - $5,125,789 (Deep UG)
SCO #2 - $9,131,131 (ASD Long Lead Gear)
SCO #3 - $460,000 (ASD Insurance Requirements)
SCO #4 - $1,605,825 (APG Shallow UG)
SCO #5 - $707,234 (FN Bulletin 01)
SCO #6 - $258,528 (APG 90% vs 100% Gear)
SCO #7 - $400,701(FN Bulletin 02)

Supp B - **$4,398,705** (SCO 1, 8)

SCO 1 - $3,600,000 (Tag and Trace)
SCO 8 - $798,705 (CCBS Elec Gear)

Supp C - APG - **$68,348,359**

Bond Values

BASE - $89,702
SCO 1 - $63,000
SCO 2 - $136,967
SCO 3 - $30,361
SCO 4 - $12,044
SCO 6 - $4,524
SCO 8 - $13,977

4825 140th Avenue North, Clearwater, FL 33762-3822
Telephone (727) 530-0077 • Fax (727) 530-0045
www.apg.company

TAMPA INTERNATIONAL AIRPORT - AIRSIDE D DEVELOPMENT PROGRAM

AIRSIDE D - ESTIMATE TRACKING (12/12/2025)

SCOPE BREAKDOWN BID PACKAGE - D50 ELECTRICAL (ASD.BLDG/MT.SP)		30% SD ESTIMATE DATED 2/28/2025	60% DD ESTIMATE DATED 5/8/2025	90% CD ESTIMATE DATED 8/21/2025	100% CD ESTIMATE DATED 12/4/2025	VARIANCE FROM PREVIOUS ESTIMATE	VARIANCE NOTES (SEE VARIANCE REPORT FOR DETAIL)
D5010.10	PACKAGED GENERATOR ASSEMBLIES	VALIDATED	$206,491	$205,130	$136,438	-$68,692	
D5010.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$1,748,829	$1,584,315	$1,588,525	$4,210	
D5010.20	BATTERY EQUIPMENT	NONE INDICATED	NONE INDICATED	$14,714	$12,963	-$1,751	UPS decreased from 160kVA to 120kVA
D5010.20	VENDOR QUOTE ONLY (MATERIAL + TAX)	NONE INDICATED	NONE INDICATED	$399,506	$339,746	-$59,760	UPS decreased from 160kVA to 120kVA
D5010.70	TRANSFER SWITCHES	VALIDATED	$46,116	$45,752	$45,752	$0	
D5010.70	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5010.10	SEE D5010.10	SEE D5010.10	$0	
D5020.10	ELECTRICAL SERVICE ENTRANCE	VALIDATED	$361,107	$338,504	$338,504	$0	
D5020.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5020.30	SEE D5020.30	SEE D5020.30	$0	
D5020.30	POWER DISTRIBUTION	VALIDATED	$1,476,373	$1,636,656	$1,702,198	$65,542	Added gear and upsized equipment
D5020.30	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$6,069,481	$6,617,775	$6,811,576	$193,801	Added gear and upsized equipment
D5020.30	SUBCONTRACTOR QUOTE ONLY (TURNKEY)	VALIDATED	$175,000	$175,000	$171,565	-$3,435	
D5020.70	FACILITY GROUNDING	VALIDATED	$1,227,236	$1,145,562	$1,122,632	-$22,930	
D5020.90	ELECTRICAL SERVICE AND DISTRIBUTION SUPPLEMENTARY COMPONENTS	VALIDATED	$10,979,275	$10,882,780	$11,227,436	$344,656	Added feeders for new gear or upsized equipment
D5030.10	BRANCH WIRING SYSTEM	VALIDATED	$10,341,835	$11,130,950	$11,173,733	$42,783	
D5030.50	WIRING DEVICES	VALIDATED	$1,769,259	$2,258,212	$1,888,994	-$369,218	Assumption of missing devices were removed
D5040.10	LIGHTING CONTROL	VALIDATED	$784,641	$1,563,893	$1,348,988	-$214,905	Assumption of missing controls were removed
D5040.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5040.50	SEE D5040.50	SEE D5040.50	$0	
D5040.20	BRANCH WIRING AND LIGHTING	VALIDATED	$6,291,348	$7,727,524	$7,815,992	$88,468	Added fixtures
D5040.50	LIGHTING FIXTURES	VALIDATED	$3,906,326	$3,914,399	$4,035,235	$120,836	Added fixtures
D5040.50	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$9,119,800	$7,034,335	$7,198,962	$164,627	Added fixtures
D5080.10	LIGHTNING PROTECTION	VALIDATED	$60,954	$105,959	$105,959	$0	
D5080.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$287,650	$374,617	$322,450	-$52,167	Improved vendor pricing
D5080.70	TRANSIENT VOLTAGE SUPPRESSION	VALIDATED	$40,039	$37,454	$41,682	$4,228	
D5080.70	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5020.30	SEE D5020.30	SEE D5020.30	$0	
D5080.90	MISCELLANEOUS ELECTRICAL SYSTEMS SUPPLEMENTARY COMPONENTS	VALIDATED	$0	$0	$0	$0	
G4010	SITE ELECTRIC DISTRIBUTION SYSTEMS	VALIDATED	$2,127,971	$2,216,577	$2,338,229	$121,652	Added additional site conduits
G4010	VENDOR QUOTE ONLY (MATERIAL + TAX)	BY UTILITY	BY UTILITY	BY UTILITY	BY UTILITY	$0	
G4050	SITE LIGHTING	VALIDATED	$572,807	$687,100	$687,100	$0	
G4050	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$561,831	$392,833	$560,774	$167,941	Lighting pole vendor increases
G5050	TECHNOLOGY UNDERGROUND	NOT INC IN SCOPE	NOT INC IN SCOPE	NOT INC IN SCOPE	$1,294,890	$1,294,890	Added Tech Foundation to scope
F3030	DEMOLITION	NOT INC IN SCOPE	NOT INC IN SCOPE	NOT INC IN SCOPE	$279	$279	
COORD	BUILDING INFORMATION MODELING	VALIDATED	$815,872	$857,272	$960,272	$103,000	Added Tech Foundation and Alstom conduits
	SUBTOTAL (ELECTRICAL PACKAGE)	$0	$58,970,241	$61,346,818	$63,270,874	$1,924,056	
	OTHER ITEMS						
1	INSURANCE	CCIP	CCIP	CCIP	CCIP		
2	BOND COSTS	EXCLUDED	EXCLUDED	EXCLUDED	EXCLUDED		
3	FEE (15% OF SELF-PERFORMED WORK)	VALIDATED	$8,653,758	$8,705,252	$8,968,114	$262,862	
4	FEE (10% OF SUBCONTRACTED WORK)	VALIDATED	$127,852	$331,180	$348,345	$17,165	
	SUBTOTAL (OTHER ITEMS)	$0	$8,781,610	$9,036,432	$9,316,459	$280,027	
	TOTAL ELECTRICAL ASD.BLDG ESTIMATE	$63,429,790	$67,751,851	$70,383,250	$72,587,333	$2,204,083	Refer to list of trend logs added, sent to HP 12/2/25

For information only. Not a contract document

Less Supplement A Funding
$16,322,745 = $56,264,588

Final Pricing	Modified $	Modified %
Database Material	11,061,324.68	
Material Tax	829,599.35	7.500
Material Total	**11,890,924.03**	**7.500**
Field Labor	14,829,930.65	
Incidental Labor	6,215,624.80	
Labor Factoring	3,707,482.63	
Labor Total	**24,753,038.08**	
Equipment	1,412,367.25	
General Expenses	3,989,018.74	
Subcontracts	3,483,448.00	
Quotes	17,742,078.83	
Prime Cost	**63,270,874.93**	
Total Overhead	**.00**	**.000**
Net Cost	**63,270,874.93**	
Material Markup	1,783,638.60	15.000
Labor Markup	3,712,955.71	15.000
Equipment Markup	211,855.09	15.000
General Expense Markup	598,352.81	15.000
Subcontract Markup	348,344.80	10.000
Quotes Markup	2,661,311.82	15.000
Total Markup	**9,316,458.84**	**15.000**
Final Adj	-0.76	.000
Selling Price	**72,587,333.00**	
Final Price	**72,587,333.00**	

For information only. Not a contract document

4825 140th Avenue North, Clearwater, FL 33762-3822
Telephone (727) 530-0077 • Fax (727) 530-0045
www.apg.company

TAMPA INTERNATIONAL AIRPORT - AIRSIDE D DEVELOPMENT PROGRAM

MAIN TERMINAL BAGGAGE HANDLING - ESTIMATE TRACKING (12/12/2025)

	SCOPE BREAKDOWN BID PACKAGE - D50 ELECTRICAL (CCBSS.MT)	30% SD ESTIMATE DATED 2/28/2025	60% DD ESTIMATE DATED 5/8/2025	90% CD ESTIMATE DATED 8/21/2025	100% CD ESTIMATE DATED 10/30/2025	VARIANCE FROM PREVIOUS ESTIMATE	VARIANCE NOTES (SEE VARIANCE REPORT FOR DETAIL)
D5010.10	PACKAGED GENERATOR ASSEMBLIES	VALIDATED	$0	$46,864	$46,864	$0	
D5010.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$43,959	$43,959	$0	
D5010.20	BATTERY EQUIPMENT	VALIDATED	$0	$41,370	$59,669	$18,298	Added third UPS for oversized belts
D5010.20	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$546,948	$911,997	$365,049	Added third UPS for oversized belts
D5010.70	TRANSFER SWITCHES	VALIDATED	$0	$0	$0	$0	
D5010.70	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$0	$0	$0	
D5020.10	ELECTRICAL SERVICE ENTRANCE	VALIDATED	$0	$0	$0	$0	
D5020.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$0	$0	$0	
D5020.30	POWER DISTRIBUTION	VALIDATED	$150,474	$253,905	$315,778	$61,873	Added additional gear
D5020.30	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$538,634	$673,285	$694,526	$21,241	Added additional gear
D5020.30	SUBCONTRACTOR QUOTE ONLY (TURNKEY)	VALIDATED	$25,000	$45,000	$42,985	-$2,015	
D5020.70	FACILITY GROUNDING	VALIDATED	$0	$0	$20,568	$20,568	Added technology grounding
D5020.90	ELECTRICAL SERVICE AND DISTRIBUTION SUPPLEMENTARY COMPONENTS	VALIDATED	$2,284,654	$6,413,327	$8,074,629	$1,661,302	Added UPS, crossbelts, gear, and relocated feeders
D5030.10	BRANCH WIRING SYSTEM	VALIDATED	$2,487,942	$719,885	$1,016,173	$296,288	Significantly increased mechanical equipment
D5030.50	WIRING DEVICES	VALIDATED	$16,311	$17,973	$25,290	$7,317	
D5040.10	LIGHTING CONTROL	VALIDATED	$8,152	$0	$1,750	$1,750	
D5040.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5040.50	SEE D5040.50	SEE D5040.50	$0	
D5040.20	BRANCH WIRING AND LIGHTING	VALIDATED	$465,598	$959,284	$1,045,092	$85,808	Added lighting fixtures
D5040.50	LIGHTING FIXTURES	VALIDATED	$216,166	$296,393	$298,998	$2,605	Added lighting fixtures
D5040.50	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$15,975	$55,742	$68,509	$12,767	Added lighting fixtures
D5080.10	LIGHTNING PROTECTION	VALIDATED	$0	$0	$0	$0	
D5080.10	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$0	$0	$0	
D5080.70	TRANSIENT VOLTAGE SUPPRESSION	VALIDATED	$5,166	$6,876	$6,876	$0	
D5080.70	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	SEE D5020.30	SEE D5020.30	SEE D5020.30	$0	
D5080.90	MISCELLANEOUS ELECTRICAL SYSTEMS SUPPLEMENTARY COMPONENTS	VALIDATED	$0	$0	$0	$0	
G4010	SITE ELECTRIC DISTRIBUTION SYSTEMS	VALIDATED	$0	$0	$0	$0	
G4010	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$0	$0	$0	
G4050	SITE LIGHTING	VALIDATED	$0	$0	$0	$0	
G4050	VENDOR QUOTE ONLY (MATERIAL + TAX)	VALIDATED	$0	$0	$0	$0	
F3030	DEMOLITION	VALIDATED	$649,906	$2,217,808	$2,374,995	$157,187	Increased per site investigation
COORD	BUILDING INFORMATION MODELING	VALIDATED	$105,500	$355,500	$504,000	$148,500	Increase to model added equipment
	SUBTOTAL (ELECTRICAL PACKAGE)	$0	$6,969,478	$12,694,119	$15,552,658	$2,858,539	
	OTHER ITEMS						
1	INSURANCE	CCIP	CCIP	CCIP	CCIP		
2	BOND COSTS	EXCLUDED	EXCLUDED	EXCLUDED	EXCLUDED		
3	FEE (15% OF SELF-PERFORMED WORK)	VALIDATED	$1,025,847	$1,813,236	$2,223,044	$409,808	
4	FEE (10% OF SUBCONTRACTED WORK)	VALIDATED	$2,500	$60,588	$73,237	$12,649	
	SUBTOTAL (OTHER ITEMS)	$0	$1,028,347	$1,873,824	$2,296,281	$422,457	
	TOTAL ELECTRICAL WCBSS.MT ESTIMATE	$738,531	$7,997,825	$14,567,943	$17,848,939	$3,280,996	Refer to list of trend logs added, sent to HP 12/2/25

For information only. Not a contract document

Less Supplement B Funding
$5,279,286 = $12,569,653



Final Pricing	Modified $	Modified %
Database Material	3,468,138.76	
Material Tax	260,110.41	7.500
Material Total	**3,728,249.17**	**7.500**
Field Labor	6,530,622.69	
Incidental Labor	444,231.48	
Labor Factoring	1,632,686.87	
Labor Total	**8,607,541.04**	
Equipment	73,530.00	
General Expenses	596,519.87	
Subcontracts	732,365.00	
Quotes	1,814,454.08	
Prime Cost	**15,552,659.16**	
Total Overhead	**.00**	**.000**
Net Cost	**15,552,659.16**	
Material Markup	559,237.38	15.000
Labor Markup	1,291,131.16	15.000
Equipment Markup	11,029.50	15.000
General Expense Markup	89,477.98	15.000
Subcontract Markup	73,236.50	10.000
Quotes Markup	272,168.11	15.000
Total Markup	**2,296,280.62**	**15.000**
Final Adj	-0.79	.000
Selling Price	**17,848,939.00**	
Final Price	**17,848,939.00**	

For information only. Not a contract document

AIRSIDE D PROJECT COPPER ESCALATION IMPACT REPORT 1-22-26					
BREAKOUT	**PREVIOUS BUDGET (EXCL BOND)**	**REVISED BUDGET (EXCL BOND)**	**DELTA INCREASE (EXCL BOND)**	**ADDITIONAL BOND PREMIUM (1.75%)**	**TOTAL IMPACT**
AIRSIDE D (INCL SHUTTLE PLATFORM)	$ 72,587,333.00	$ 74,365,268.00	$ 1,777,935.00	$ 31,113.86	$ 1,809,048.86
CCBS	$ 17,848,939.00	$ 18,386,646.00	$ 537,707.00	$ 9,409.87	$ 547,116.87
AIRSIDE D BULLETIN #1	$ 221,510.00	$ 217,275.00	$ (4,235.00)	$ (74.11)	$ (4,309.11)
TECO SERVICE #5 FOR LED BOARDS	$ 706,798.00	$ 749,073.00	$ 42,275.00	$ 739.81	$ 43,014.81
TOTAL	**$ 91,364,580.00**	**$ 93,718,262.00**	**$ 2,353,682.00**	**$ 41,189.44**	**$ 2,394,871.44**

ASD - $1,815,975
CCBS - $537,707

For information only. Not a contract document

Design Assist Subcontractor Back-up

Low Voltage

MC Dean, Inc.

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C Funding Summary

MC Dean Funding Summary

Estimate Value:	$ 52,833,888
Less Supplemental A Funding:	$ 235,759 (ASD)
Less Supplemental B Funding:	$ 3,017,032 (CCBS)
Supplemental C Funding:	$ 45,355,235 (ASD)
Supplemental C Funding:	$ 4,225,862 (CCBS)

MC Dean Funding Summary

Overall **- $52,833,888**

Supp A - **$235,759 (BASE)**

Supp B - **$3,017,032 (SCO 1)**

SCO 1 - $3,017,032 - Tag and Trace

Supp C - **$49,581,097**

Bond

BASE - $1,768
SCO 1 - $21,119

6557 Hazeltine National Drive

Suite One

Orlando, FL 32822

ATTN: James G. Cobb

Dear Mr. Cobb,

M.C.Dean Inc is pleased to provide you with the pricing for the 100% Tampa Airside D Documents. The attached Excel sheet has a Summary Tab which identifies how our 100% number was assembled. There are four financial categories to consider: 90% pricing (green tabs), 100% adds (yellow tabs), awarded scopes and open Trends.

Only two of our subcontractors had changes: ASG for PA and ACCI for DAS. Their respective quotes are attached

The following pages have descriptions of changes.

Thank you for the opportunity,

Dmitri Lagoda

PE. RCDD.

© 2022. M.C. Dean, Inc. All rights reserved.

For information only. Not a contract document

Technology Cabling Infrastructure

1. Airside D
    a. Data Outlets (added 45 cables)
    b. (5) Fiber Optic Data Outlets
    c. Added (2) 24str fiber optic backbone cabling
        i. From ASD01480 to 6107
        ii. From ASD02180 to 6107
    d. Added (3) IDFs
        i. HCAA IDF - ALIAS 01180
        ii. HCAA MDF -ALIAS 01480
        iii. TENNANT IDF 1481
    e. Updated Media Converters

2. CCBS and Main Terminal
    a. Data Outlets (added 6 cables CCBS area)
    b. Data Outlets (added 163 cables)
    c. Fiber Tag/Trace and Demo
    d. Added (6) Wall Mounted Cabinets
    e. Backbone - Added (7) runs of FOC
        i. 24 Str
            1. From Oversize IDF to 1020
            2. From PLC Room 1604 to 1020
            3. From 1020 to 1001-104
            4. From Oversize IDF to 1020
        ii. 48 Str
            1. From 1001-004 to Oversize IDF
        iii. 72 str
            1. From TB02180 to 1001-104
            2. From TB04480 to Oversize IDF

© 2022. M.C. Dean, Inc. All rights reserved.

For information only. Not a contract document

Conduit

The tables below identify Conduit Changes from 100% validation drawing to 90% validation drawings

Fire Alarm System			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	DEV. QTY	DEV. QTY	
L1 - APRON	835	849	14
L1.5 - STERILE CORRIDOR	72	72	0
L2 - CONCOURSE	516	577	61
L3 - MEZZANINE	163	161	-2
MT			
WCBSS	70	70	0
TOTAL QTY	1656	1729	73

Fire Alarm System			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	CDT - FT	CDT - FT	
L1 - APRON	111975	112825	850
L1.5 - STERILE CORRIDOR	4137	4137	0
L2 - CONCOURSE	86023	89373	3350
L3 - MEZZANINE	64449	64319	-130
MT			
WCBSS	6637	6637	0
TOTAL LF	273221	277291	4070

Security System - CCTV			
	90% VALIDATION	100% CONST.	QTY ADDED
	DEV. QTY	DEV. QTY	
ASD	561	581	20
MT	136	151	15
TOTAL QTY	697	732	35

Security System - CCTV			
	90% VALIDATION	100% CONST.	QTY ADDED
	CDT - FT	CDT - FT	
ASD	103200	105450	2250
MT	14550	16050	1500
TOTAL LF	117750	121500	3750

Security System - ACS			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	DEV. QTY	DEV. QTY	
L1 - APRON	686	811	125
L1.5 - STERILE CORRIDOR	52	65	13
L2 - CONCOURSE	507	645	138
L3 - MEZZANINE	69	72	3
MT			
WCBSS	25	36	11
TOTAL QTY	1339	1629	290

Security System - ACS			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	CDT - FT	CDT - FT	
L1 - APRON	62330	65430	3100
L1.5 - STERILE CORRIDOR	3300	4870	1570
L2 - CONCOURSE	49820	56420	6600
L3 - MEZZANINE	1280	620	-660
MT			
WCBSS	2560	2840	280
TOTAL LF	119290	130180	10890

Telecom System			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	DEV. QTY	DEV. QTY	
L1 - APRON	666	614	-52
L1.5 - STERILE CORRIDOR	20	17	-3
L2 - CONCOURSE	352	360	8
L3 - MEZZANINE	47	72	25
MT			
WCBSS	54	54	0
TOTAL QTY	1139	1117	-22

Telecom System			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	CDT - FT	CDT - FT	
L1 - APRON	34239	34389	150
L1.5 - STERILE CORRIDOR	6950	6400	-550
L2 - CONCOURSE	55101	55640	539
L3 - MEZZANINE	3660	4820	1160
MT			
WCBSS	7850	7850	0
TOTAL LF	107800	109099	1299

© 2022. M.C. Dean, Inc. All rights reserved.

For information only. Not a contract document

Telecom System - Cable Tray			
	90% VALIDATION	100% CONST.	QTY ADDED
ASD	CDT - FT	CDT - FT	
L1 - APRON	3710	3710	0
L1.5 - STERILE CORRIDOR	0	0	0
L2 - CONCOURSE	990	990	0
L3 - MEZZANINE	350	350	0
MT			
WCBSS	1910	1910	0
TOTAL LF	6960	6960	0

DAS			
	90% VALIDATION	100% CONST.	QTY ADDED
	DEV. QTY	DEV. QTY	
ASD	86	86	0
MT	0	0	0
TOTAL QTY	86	86	0

DAS			
	90% VALIDATION	100% CONST.	QTY ADDED
	CDT - FT	CDT - FT	
ASD	8140	8500	360
MT	0	0	0
TOTAL LF	8140	8500	360

AV System			
	90% VALIDATION	100% CONST.	QTY ADDED
	DEV. QTY	DEV. QTY	
ASD	775	803	28
MT	14	14	0
TOTAL QTY	789	817	28

AV System			
	90% VALIDATION	100% CONST.	QTY ADDED
	CDT - FT	CDT - FT	
ASD	14970	16060	1090
MT	2800	2800	0
TOTAL LF	17770	18860	1090

© 2022. M.C. Dean, Inc. All rights reserved.

For information only. Not a contract document

BUSINESS UNIT	CATEGORY	SUBTOTAL	FEE (15%)	TOTAL	NOTES
ELECTRICAL	MATERIAL	$ 3,598,554.19	$ 539,783.13	$ 4,138,337.32	
ELECTRICAL	DIRECT LABOR	$ 12,792,898.32	$ 1,918,934.75	$ 14,711,833.07	
ELECTRICAL	SUPERVISION	$ 3,526,928.46	$ 529,039.27	$ 4,055,967.72	
ELECTRICAL	EQUIPMENT	$ 1,138,797.89	$ 170,819.68	$ 1,309,617.57	
ELECTRICAL	GENERAL EXP	$ 804,398.71	$ 120,659.81	$ 925,058.52	
ELECTRICAL	SUBC	$ 160,000.00	$ 16,000.00	$ 176,000.00	10% fee on subs
ELECTRICAL	QUOTES	$ 231,733.37	$ 34,760.01	$ 266,493.38	
ELECTRICAL	TOTAL	$ 22,253,310.95	$ 3,329,996.64	**$ 25,583,307.59**	
LOW VOLTAGE	MATERIAL	$ 1,888,909.49	$ 283,336.42	$ 2,172,245.92	
LOW VOLTAGE	DIRECT LABOR	$ 2,679,380.43	$ 401,907.07	$ 3,081,287.50	
LOW VOLTAGE	SUPERVISION	$ 4,176,677.72	$ 626,501.66	$ 4,803,179.38	
LOW VOLTAGE	EQUIPMENT	$ 541,377.17	$ 81,206.58	$ 622,583.75	
LOW VOLTAGE	GENERAL EXP	$ 555,082.74	$ 83,262.41	$ 638,345.15	
LOW VOLTAGE	SUBC	$ 5,501,416.80	$ 550,141.68	$ 6,051,558.48	10% fee on subs
LOW VOLTAGE	QUOTES	$ 172,823.00	$ 25,923.45	$ 198,746.45	
LOW VOLTAGE	TOTAL	$ 15,515,667.36	$ 2,052,279.26	**$ 17,567,946.62**	
SECURITY	MATERIAL	$ 161,340.33	$ 24,201.05	$ 185,541.38	
SECURITY	DIRECT LABOR	$ 1,239,389.69	$ 185,908.45	$ 1,425,298.14	
SECURITY	SUPERVISION	$ 1,209,585.69	$ 181,437.85	$ 1,391,023.54	
SECURITY	EQUIPMENT	$ 144,148.27	$ 21,622.24	$ 165,770.51	
SECURITY	GENERAL EXP	$ 1,223,239.32	$ 122,323.93	$ 1,345,563.25	
SECURITY	SUBC	$ -	$ -	$ -	
SECURITY	QUOTES	$ -	$ -	$ -	
SECURITY	TOTAL	$ 3,977,703.30	$ 535,493.53	**$ 4,513,196.83**	

For information only. Not a contract document

BUSINESS UNIT	TOTAL	ASD	CCBS
ELECTRICAL	$ 25,583,307.59	$ 23,945,464.24	$ 1,637,843.35
LOW VOLTAGE	$ 17,567,946.62	$ 16,653,710.68	$ 914,235.94
SECURITY	$ 4,513,196.83	$ 4,120,052.25	$ 393,144.58
US COST (FA & CCTV COND)	**$ (648,034.26)**	$ (606,547.10)	$ (41,487.15)
MCDEAN 90%	**$ 47,016,416.78**	**$ 44,112,680.07**	**$ 2,903,736.72**

100% DISCIPLINE	TOTAL	ASD	CCBS	NOTES
ELECTRICAL	$ 701,361.41	$ 625,398.52	$ 75,962.89	
LOW VOLTAGE (LV)	$ 412,456.40	$ 118,364.93	$ 294,091.46	
LV - FIRE ALARM	$ -	$ -	$ -	NO CHANGE FROM 90%
LV - ASG	$ 85,358.90	$ 84,918.90	$ 440.00	
LV - ACCI	$ 30,107.53	$ 30,107.53	$ -	
LV - AEM	$ -	$ -	$ -	NO CHANGE FROM 90%
SECURITY	$ 108,297.69	$ 98,550.90	$ 9,746.79	
100% CHANGE	**$ 1,337,581.93**	**$ 957,340.78**	**$ 380,241.14**	

DESCRIPTION	AWARDED	ASD	CCBS	NOTES
SUPPLEMENT A	$ 237,527.00	$ 237,527.00	$ -	
SUPPLEMENT B	$ 3,038,151.00	$ -	$ 3,038,151.00	T&M
AWARDED	**$ 3,275,678.00**	**$ 237,527.00**	**$ 3,038,151.00**	

TE # / PCO	DESCRIPTION	VALUE	ASD	CCBS	NOTES
119	Ascend Linds Non Accessible	$ 75,000.00	$ 75,000.00	$ -	never priced, HP budget
127	CBP Enhanced Passenger Processing	$ 14,868.00	$ 14,868.00	$ -	never priced, HP budget
208	OSR Room Renovation	$ 254,765.00	$ -	$ 254,765.00	
200	Smiths EDS Machines Cabling	$ 410,000.00	$ -	$ 410,000.00	
201	BIM Asset Tagging	$ 203,578.00	$ 193,578.00	$ 10,000.00	
205	Three additional EDS Machines	$ 246,000.00	$ -	$ 246,000.00	
PCO#003	AIRSIDE E - DESIGN ASSIST	$ 123,586.00	$ 123,586.00	$ -	
PCO#004	AIRSIDE E - CONSTRUCTION	$ 1,789,470.00	$ 1,789,470.00	$ -	T&M
	TOTAL	**$ 3,117,267.00**	**$ 2,196,502.00**	**$ 920,765.00**	

	TOTAL	ASD	CCBS
TOTAL MCD 100%	**$ 54,746,943.71**	**$ 47,504,049.85**	**$ 7,242,893.86**

	$ 45,070,020.85	$ 3,283,977.86	$	48,353,998.71
TE's Only	$ 283,446.00	$ 920,765.00	$	1,204,211.00
Totals	$ 45,353,466.85	$ 4,204,742.86	$	49,558,209.71

For information only. Not a contract document

Design Assist Subcontractor Back-up

Pipe Bursting

Murphy Piping Contractors

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

Murphy Piplines Contractors
Corporate Headquarters
510 Shotgun Rd, Suite 150, Sunrise, FL 33326

December 2, 2025

Kevin Curry
Southeast Region
Hensel Phelps
6557 Hazeltine National Drive, Suite One
Orlando, FL 32822

RE: Tampa International Airport (TPA) Gravity Sewer Pipe Bursting Proposal

Mr. Curry,

Murphy Pipeline Contractors (MPC) is pleased to submit the following estimate to Hensel Phelps for review in support of the TPA's gravity sewer pipe bursting needs for the Main Terminal Curbside Expansion program.

As one of the nation's most experienced trenchless contractors in the U.S., MPC brings a combination of national and local expertise to this project. Our extensive experience provides a solid foundation for our team to consistently deliver exceptional results and allows us to stand out as a premier contractor in the industry. We are confident that our Team will not only meet, but surpass, expectations for this pipe bursting project.

SCOPE UNDERSTANDING

Hensel Phelps is currently providing design-build services on the Main Terminal Curbside Expansion program at TPA located just southwest of the Tampa Airport Marriot (4100 George J Bean Pkwy, Tampa, FL 33607). This proposal includes gravity sewer pipe bursting from the existing SS MH-5 to the existing SS MH-9, totaling approximately 660 linear feet of gravity sewer main replacement. Hensel Phelps has requested to upsize the existing gravity mains to accommodate the airport expansion, as shown in the attached 100% Construction Drawings prepared by Brindley Pieters and Associates, Inc. (BPA). We appreciate the opportunity to support Hensel Phelps in this effort and have prepared the requested estimate for review.

MPC Assumptions:

- Hensel Phelps will provide design permits from the authorities having jurisdiction (AHJ), as needed.
- MPC will provide all labor, equipment, and tools required to complete the pipe bursting operation in accordance with accepted industry standards.

For information only. Not a contract document

- The estimate includes an 8" TPU Layflat bypass system to maintain service during the pipe bursting operation.
- This proposal excludes identification, handling, remediation, transportation, or disposal of contaminated soils, groundwater, or hazardous materials. Any impacts related to contaminated or unsuitable soils encountered during construction will require a change order.
- Restoration is limited to only those areas directly disturbed by MPC's construction activities. Restoration of pre-existing conditions or areas outside the contractor's work limits is excluded and, if required, will be addressed under a separate change order.
- Payment and Performance bond has been excluded. If required, the bond rate will be 2.0% of the contract price.

SCHEDULE AND FEES

MPC is prepared to begin work upon receipt of a purchase order, with project execution contingent on material availability. Conservatively, MPC estimates **seven (7) weeks** to complete the bypass and pipe bursting installation, including 1-2 weeks for mobilization/demobilization and 1-2 weeks for site restoration. Upon mutual agreement on the Notice to Proceed, MPC will provide project submittals and a detailed project schedule.

The **total estimated lump sum contract amount for this project is $1,927,100.00**. A detailed fee estimate can be found below for Hensel Phelp's review and evaluation.

Tampa International Airport (TPA) Gravity Sewer Pipe Bursting Proposal

Description	Unit	Estimated Quantity	Unit Price	Total Price
Mobilization / Demobilization	LS	1	$60,000.00	$60,000.00
General Conditions	LS	1	$70,000.00	$70,000.00
As-builts	LS	1	$30,000.00	$30,000.00
Traffic Control/MOT	LS	1	$40,000.00	$40,000.00
Bypass	LS	1	$230,000.00	$230,000.00
Pipe Bursting Operations	LF	660	$2,000.00	$1,320,000.00
Furnish and Install New Manhole	EA	3	$20,000.00	$60,000.00
Manhole Connections	EA	10	$5,000.00	$50,000.00
Post CCTV Inspection	LS	1	$7,000.00	$7,000.00
Site Restoration	LS	1	$60,000.00	$60,000.00
			Total Project Cost:	**$1,927,000.00**

CONCLUSION

For information only. Not a contract document

Murphy Piplines Contractors
Corporate Headquarters
510 Shotgun Rd, Suite 150, Sunrise, FL 33326

We look forward to the opportunity to partner with Hensel Phelps on this critical infrastructure improvement and to negotiating any additional items not specifically mentioned that could enhance the project and exceed your expectations.

Should you have any questions, please do not hesitate to contact me at (315) 794-1929 or marissa.maring@murphypipelines.com.

Respectfully submitted,



Marissa Maring
Murphy Pipeline Contractors
Director of Technical Projects

For information only. Not a contract document

Design Assist Subcontractor Back-up

Baggage Handling System

Daifuku

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

HENSEL PHELPS
Plan. Build. Manage.

GMP Supplemental C Funding Summary

Daifuku Funding Summary

Estimate Value:	$239,152,340
Less Supplemental A Funding:	$ 0
Less Supplemental B Funding:	$ 5,778,513 (CCBS)
Supplemental C Funding:	$ 53,010,039 (ASD)
Supplemental C Funding:	$ 180,363,787 (CCBS)
Supplemental C Funding:	$13,336,538 (CCBS) Not Subject to 56% / 44% Split
Supplemental C Funding:	$167,027,249 (CCBS) 56% / 44% Split

Daifuku Airport America Corporation
30100 Cabot Drive
Novi, MI 48377 USA
Phone: (248) 553-1000
www.daifukuatec.com

Daifuku North America

January 12, 2026

Nick Petterson | Project Manager
Hensel Phelps – Southeast Region
777 South Harbour Island Blvd, Suite 390
Tampa, FL 33602

Submitted via email to npetterson@henselphelps.com

Subject: TPA ASD and CCBS GMP Proposal – **REVISION 4**
Daifuku Proposal No. 22-04334

Revision 1 Changes: Added trend log items section and updated GMP summary.
Revision 2 Changes: Clarified inclusion of trend log items 205, 207 and show their cost in the GMP summary.
Revision 3 Changes: Updated GMP summary.
Revision 4 Changes: Removed OS line from the GMP scope of work under exclusions sections.

Dear Nick:

Daifuku Airport America Corporation is pleased to submit this firm Guaranteed Maximum Price (GMP) proposal for engineering, manufacturing, and installation of a comprehensive, turn-key Baggage Handling System (BHS) at Tampa International Airport (TPA). This proposal is strategically focused on addressing the specific operational and logistical requirements of the Airside D (ASD) expansion and the BHS upgrade of the Centralized Checked Baggage System (CCBS) in the main terminal.

This GMP serves as an updated and final revision to our previous budgetary estimate, submitted on October 23, 2025, which covered the respective 90% (ASD) and 90% (CCBS) design scopes. The cost contained herein is based on the final 100% BHS drawings and specification provided to Daifuku on October 31, 2025. Any future changes to the design will be priced separately and be awarded as a change order to the base contract.

Scope of Work
The primary scope of work for this project includes the following:

Airside D (ASD)

- Turnkey ASD BHS Provision: This includes detailed engineering, procurement, fabrication, and freight for the system, which includes approximately 330 conveyors, makeup units, and claim devices, all strictly adhering to project specifications and drawings.
- On-Site Installation: Execution of the mechanical and electrical installation of all BHS equipment.
- System Commissioning and Testing: Performance of testing and commissioning of the BHS, along with full support for all owner acceptance testing procedures.
- Maintenance Access Infrastructure: Provision of all necessary catwalks or maintenance access as defined in the project specification and drawings.

For information only. Not a contract document

- Documentation and Training: Delivery of all required operational manuals and comprehensive training in accordance with project specifications and requirements.

Centralized Checked Baggage System (CCBS)

- Existing System Demolition: Execution of the demolition and removal of approximately 9,600 linear feet of existing conveyor infrastructure, as detailed in the project drawings.
- Turnkey CCBS BHS Provision: Comprehensive delivery, including detailed engineering, procurement, fabrication, and freight, for the new BHS. This includes approximately:
  - 950 new conveyors
  - 80 temporary conveyors
  - 25 modified conveyors
  - 90 re-controlled conveyors
- On-Site Installation: Execution of the mechanical and electrical installation of all BHS equipment, including the necessary interlock interfaces with existing systems.
- Crossbelt System (XBM1 & XBM2) Integration: Provision and integration of a turnkey Crossbelt system totaling approximately 2,600 linear feet. This includes induction units, discharge chutes, and ATRs, all per project design and specifications.
- Integration of EDS and Search Tables:
  - Integration of Explosives Detection System (EDS) machines within the CBIS area, as specified.
  - Provision of stainless-steel search tables in the CBRA area, as defined in the project specifications.
- System Commissioning and Testing: Performance of testing and commissioning of the BHS, with full support for all owner and TSA acceptance testing.
- Maintenance Access Infrastructure: Provision of all necessary catwalks or maintenance access as defined in the project specification and drawings.
- Documentation and Training: Delivery of all required operational manuals and comprehensive training in accordance with project specifications and requirements.
- Portering Services: Inclusion of portering services as identified and scheduled within the current project plan.
- One year of onsite maintenance and operational support for the Crossbelt system after final system acceptance.

Trend Log Items Scope of Work

Our GMP includes the following trend log items:

- TE-166B – ASD Impact Protection – MUD Bull Rail
- TE-177 – T11 Re-Route
- TE-182 – Electric Hoists
- TE-190 – Catwalk/Rails – Alstom Maintenance
- TE-205A – A&C Work @ Main Terminal
- TE-215 – Unified BHS Warranty Request

Exclusions:

The OS line scope of work is not included in our GMP, specifically the following subsystems are not included in our price:

- OSM1 subsystem
- OSM1A subsystem

For information only. Not a contract document

- OSM1B subsystem
- TE1-20/24
- TE2-13/18
- TXM1-08
- TXM2-06
- Associated catwalk / handrail / ladders / TSA search tables / roller conveyors

Pricing
It should be noted that this GMP reflects an increase compared to our previous 90% Budgetary estimate. This adjustment is primarily attributable to the inclusion of approximately 150 additional conveyors, which were not part of the scope in the preceding budgetary milestones. We have attached a manifest showing all these new conveyors additions.

The final firm GMP for the above scope of work is as follows:

See attachment for detailed pricing information.

Liquidated Damages Concern
We must bring to your attention a critical constraint regarding the current Liquidated Damages (LD) provision of $25,000 per day. During our solicitation process, key potential subcontractors, specifically electrical and mechanical installation partners, have formally declined to contract under the current terms.

The unlimited exposure associated with uncapped liquidated damages prevents these trade partners from securing the necessary Payment and Performance (P&P) bonds. Without a defined cap on these damages, their insurers and surety partners view the risk as unquantifiable.

To ensure we can secure these critical subcontractors and provide the required bonding for the project, we request that Liquidated Damages be capped at 5% of our total contract value.

Minority Content Plan
Our strategy to ensure full compliance with the project's Disadvantaged Business Enterprise (DBE) and Small Business Enterprise (SBE) content requirement of 15% is outlined in the plan below.

Upon successful award of this contract, we commit to establishing formal subcontract agreements with the companies listed below to fulfill the minority content requirements.

For information only. Not a contract document

DAIFUKU
Automation that Inspires

Function	Name	Agency	Amount	%
Mechanical Installation	Jordim International	Florida UCP Directory	$ 24,500,000.00	10.2%
Electrical Installation	Miller Electric - content	Florida UCP Directory	$ 4,750,000.00	1.98%
Freight Services	Davis Freight Management	Florida UCP Directory	$ 2,000,000.00	0.83%
Safety Representative	Safety Resources Inc.	Florida UCP Directory	$ 1,500,000.00	0.63%
Site Labor	CRAS - Construction Recruiters America Staffing	Florida UCP Directory	$ 1,750,000.00	0.73%
Steel Fabrication	J&J United Industries	Florida UCP Directory	$ 2,000,000.00	0.83%
			$ 36,500,000.00	**15.22%**

Assumptions and Clarifications

Our GMP proposal assumes the following:

1. The provided pricing reflects a competitive bidding process. Our GMP incorporates the most qualified and favorable quotations received from multiple potential subcontractors, including those for electrical installation, mechanical installation, and Crossbelt vendors.
2. The cost associated with Supplement B is shown as a deduction to the final GMP.
3. The price of any product covered by this proposal is subject to adjustment by the same amount as any applicable tariff that any governmental entity may impose. No specific allowance for future tariffs has been included in this estimate, beyond any that may already be factored into the subcontractor quotes.

We deeply appreciate the trust Hensel Phelps and the Hillsborough County Aviation Authority have placed in us for this project. Our ultimate goal is to deliver it successfully, on time and within budget.

Please do not hesitate to contact me if you have any questions or concerns.

Sincerely,

Daifuku Airport America Corporation

Elyas Ahmadzai

Elyas Ahmadzai
Business Development Manager
(248) 419-7299 office | (248) 240-6340 mobile
eahmadzai@daifukuna.com

Attachments:

1. TPA ASD & CCBS GMP Summary

For information only. Not a contract document

DAIFUKU Automation that Inspires

BHS Summary Costs

Description	ASD	CCBS	Total
Subcontractors	$20,101,698	$96,935,711	$117,037,409
Subcontractor Fee (10%)	$2,010,170	$9,693,571	$11,703,741
Subcontractor Subtotal	$22,111,868	$106,629,282	$128,741,150
Self Performed Costs	$25,869,828	$65,944,827	$91,814,655
Self Performed Cost Fee (16%)	$4,139,173	$10,551,172	$14,690,345
Self Performed Subtotal	$30,009,001	$76,495,999	$106,505,000
Total BHS Estimate	$52,120,869	$183,125,281	**$235,246,150**
Spare Parts Allowance (5% of Estimated Material)	$889,170	$3,017,019	$3,906,190
	$53,010,138	$186,142,300	
Supplement B (Early Material) - Deduct			**-$5,778,513**
Fives Crossbelt Sorter Option - Deduct			**-$7,451,183**
Daifuku Crossbelt Sorter Option - Deduct		$239,152,438	**-$8,472,354**
TE-215 - Unified Warranty - Included			**$3,415,000**
TE-205A Airside A & C Sortation Improvements (Main Terminal) - Included			**$13,336,538**

Updated January 13, 2026

For information only. Not a contract document

Bid Results

Proposal Summaries
Wave 1 Subcontractors

00

HENSEL PHELPS
Plan. Build. Manage.

Demolition

Base Bid at a glance: 2,072,000 | 1,908,000 | ~~2,071,000~~

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL
	Bid Amount	*Quantities*			w/Below		w/Below		WITHDREW BID
	Bid Bond valid for 120 Days (Bids >$5M)				✔	NA	✔	NA	✔
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.50%	✔	3.00%	
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔
	SBE Participation / LOIs & FLUCP Certs Provided			10%	✔	10%	✔	100%	✔
	E-Verify Affidavit of Compliance				✔		✔		✔
	Anti-Trafficking Affidavit				✔		✔		✔
	HCAA NDA Form				✔		✔		✔
	Bid Package Addenda Acknowledged				✔		✔		✔
	Compass Registration				✔		✔		✔
	----				----		----		----
	----				----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔
02 41 19	**SELECTIVE DEMOLITION**				✔		✔		✔
	----				----		----		----
	----				----		----		----
	Bid Item No. 1 - Airside D Terminal				✔		w/Below		w/Below
	Subtotal Demolition				✔		✔		✔
	No Scope				✔		✔		✔
	----				----		----		----
	----				----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				-		-		**INCOMPLETE**

00

HENSEL PHELPS
Plan. Build. Manage.

Demolition

Base Bid at a glance: 2,072,000 | 1,908,000 | ~~2,071,000~~

				HPCC		Bidder #1		Bidder #2	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03								
LOCATION:	Tampa, FL								
OWNER:	Hillsborough County Aviation Authority								
BID DATE:	10/09/2025								
HP TRADE:		*Quantities*							
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----
	Bid Item No. 2 - Centralized Checked Baggage System				w/Below		w/Below		w/Below
	Subtotal Demolition				1,400,000		1,399,600		1,900,000
	Demo SOG - @ new foundation locations				✔		✔		✔
	Demo Slab cut for BHS inclines				✔		✔		✔
MT-D-S120F, MT-S417	Demo SOMD				✔		✔		✔
MT-D-A111E-J	Remove Existing CMU Walls - 02 41 19.L1				✔		✔		✔
	Remove Existing Concrete Pads - 02 41 19.G3				✔		✔		✔
MT-D-A111E-J	Remove existing base concrete curb - 02 41 19.G2				✔		✔		✔
	Remove Existing bollards - 02 41 19.J2				✔		✔		✔
	Remove Existing Impact protection metal rail - 02 41 19.J1				✔		✔		✔
	Remove Existing Access Door - 02 41 19.D2				✔		✔		✔
	Remove Existing Carpet Flooring - 02 41 19.E2				✔		✔		✔
	Remove Existing Guardrail - 02 41 19.J8				✔		✔		✔
	Remove Existing Interior Concrete Slab - 02 41 19.G1				✔		✔		✔
	Remove Existing Chain Link Fence - 02 41 19.T1				✔		✔		✔
	Remove Existing Overhead Door - 02 41 19.D3				✔		✔		✔
	REMOVE EXISTING PRECAST IMPACT PROTECTION BARRIER - 02 41 19.J7				✔		✔		✔
	REMOVE EXISTING TUG LANE PAINTING - 02 41 19.P1				✔		✔		✔
	REMOVE EXISTING OFFICE FURNITURE - 02 41 19.E9				✔		✔		✔
	REMOVE EXISTING REFRIGERATOR - 02 41 19.E10				✔		✔		✔
	REMOVE EXISTING TV SCREEN 02 41 19.H22				✔		✔		✔
	REMOVE EXISTING ACCESS PANEL - 02 41 19.D4				✔		✔		✔
	REMOVE EXISTING ELEVATED FLOORING SYSTEM - 02 41 19.C4				✔		✔		✔
	Glazing and storefront demo - 02 41 19.A1				✔		✔		✔
	Millwork demo - 02 41 19.C1 & 02 41 19.B1				✔		✔		✔
	Airline counter demo - 02 41 19.C2				✔		✔		✔
	Floor tile demo - 02 41 19.E1				✔		✔		✔
	ACT Ceiling Grid Demo - 02 41 19.E3				✔		✔		✔
	REMOVE EXISTING BELT ACCESS LADDER. REFER TO BHS DRAWINGS - 02 41 19.J4				✔		✔		✔
	REMOVE EXISTING INTERIOR DOOR AND WALL - 02 41 19.D1				✔		✔		✔
MT-D-A125/	02 41 19.J5 - Existing Structural Framing Demo				✔		✔		✔
02 41 19.J3	REMOVE EXISTING ELEVATED SCREENING PLATFORM. REFER TO STRUCTURAL DRAWINGS - 02 41 19.J3				✔		✔		✔
	Drywall Partition Demo - 02 41 19.B1				✔		✔		✔

Demolition

Base Bid at a glance: 2,072,000 | 1,908,000 | ~~2,071,000~~

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	

SEC	DESCRIPTION	*Quantities* QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL
MT-D-S110E-J, MT-D-S120C-H	Demo per plan				✔		✔		✔
MT-D-S130C	Demo per plan				✔		✔		✔
MT-D-A111E-J	Demo per plan				✔		✔		✔
MT-D-A121-1127	Demo per plan				✔		✔		✔
MT-D-A401-407	Demo per plan				✔		✔		✔
	Shoring where required				✔		✔		✔
Inclusion #28	Repair Fireproofing if damaged			No	W/ Fireproofing		No-Ok		No-Ok
	Work Hours: 10PM-4AM Only				✔		✔		✔
Note 1/MT-D-A110	Lead & Asbestos Survey				✔		✔		✔
	Part Time QC Manager				✔		✔		✔
	Full Time Safety Manager				✔		✔		✔
	Full Time Superintendent				✔		✔		✔
	Full Time Project Manager				✔		✔		✔
	10 mobilizations for CCBS				✔		✔		✔
	Exclusions				✔		✔		✔
	Remove, Package, Store - Metal Panel			No	W/ Metal Panel		No-Ok		No-Ok
	Right of way cold-form framing			No	W/ Drywall		No-Ok		No-Ok
	HVAC Demo			No	W/ Trade		No-Ok		No-Ok
	Plumbing Demo			No	W/ Trade		No-Ok		No-Ok
	Electrical Demo			No	W/ Trade		No-Ok		No-Ok
	Low Voltage Demo			No	W/ Trade		No-Ok		No-Ok
	Fire Protection Demo			No	W/ Trade		No-Ok		No-Ok
	Baggage Handling Demo			No	W/ Trade		No-Ok		No-Ok
	Baggage Handling Catwalks Demo			No	W/ Trade		No-Ok		No-Ok
	Temp Walls Demo			No	W/ Trade		No-Ok		No-Ok
	Signage Demo			No	W/ Trade		No-Ok		No-Ok
	ACT Ceilings (Ceiling grid by Demo Contractor)			No	W/ Trade		No-Ok		No-Ok
	REMOVE EXISTING RIGHT OF WAY COLDFORM FRAMING			No	W/ Trade		No-Ok		No-Ok
	Patch Fireproofing Caused by Demo				w/ Fireproofing		w/ Fireproofing		w/ Fireproofing
	Walk w/ Nick Comments				✔		✔		✔
	Unought Scope				✔		✔		✔
	MT-D-S120D Opening				30,000		30,000		30,000
	----				----		----		----
	----				----		----		----
	TOTAL - Bid Item No. 2 - Centralized Checked Baggage System				**1,430,000**		**~~1,430,000~~**		**1,930,000**

00

HENSEL PHELPS
Plan. Build. Manage.

Demolition

		Base Bid at a glance:			2,072,000		1,908,000		~~2,071,000~~
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**
LOCATION:	Tampa, FL								
OWNER:	Hillsborough County Aviation Authority								
BID DATE:	10/09/2025								
HP TRADE:		*Quantities*							
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below
	Subtotal Demolition				642,000		478,000		141,000
	Demo Temp Partitions				✔		✔		✔
	Remove Vinyl Signs				✔		✔		✔
	Demo Walls, Doors, Signage				✔		✔		✔
	Demo Temp Pedestals Over E-Gates Stub-Ups				✔		✔		✔
SP-D-A120N	Sawcut Terrazzo				✔		✔		✔
	Remove Exit Lights				✔		✔		✔
	----				----		----		----
	----				----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**642,000**		**478,000**		**141,000**

	BASE BID TOTAL				**2,072,000**		**1,908,000**		**INCOMPLETE**

HENSEL PHELPS
Plan. Build. Manage.

Concrete

Base Bid at a glance:					8,502,000		~~20,234,000~~		12,661,000		11,967,000		~~13,620,000~~		12,471,000
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**	
LOCATION:	Tampa, FL														
OWNER:	Hillsborough County Aviation Authority														
BID DATE:	10/09/2025														
HP TRADE:		*Quantities*													
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		INCOMPLETE		w/Below		w/Below		INCOMPLETE		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔		✔				✔
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	2.00%	✔	1.00%	✔	0.75	✔			1.15%	✔
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔				✔
	SBE Participation / LOIs & FLUCP Certs Provided			18%	✔	NONE		39%	✔	26%	✔	NONE		31%	✔
	E-Verify Affidavit of Compliance				✔				✔		✔				✔
	Anti-Trafficking Affidavit				✔				✔		✔				✔
	HCAA NDA Form				✔				✔		✔				✔
	Bid Package Addenda Acknowledged				✔				✔		✔				✔
	Compass Registration				✔				✔		✔				✔
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔		✔
03 10 00	**CONCRETE FORMING AND ACCESSORIES (COMPLETE)**				✔		✔		✔		✔		✔		✔
03 15 13	**WATERSTOPS (COMPLETE)**				✔		✔		✔		✔		✔		✔
03 20 00	**CONCRETE REINFORCING (COMPLETE)**				✔		✔		✔		✔		✔		✔
03 30 01	**CAST-IN-PLACE CONCRETE (COMPLETE)**				✔		✔		✔		✔		✔		✔
03 54 16	**HYDRAULIC CEMENT UNDERLAYMENT (AS APPLIES)**				✔		✔		✔		✔		✔		✔
03 92 50	**REPAIR MORTARS (AS APPLIES)**				✔		✔		✔		✔		✔		✔
05 01 00	**POST-INSTALLED STRUCTURAL ANCHORS (AS APPLIES)**				✔		✔		✔		✔		✔		✔
07 13 26	**SELF-ADHERING SHEET WATERPROOFING (AS APPLIES)**				✔		✔		✔		✔		✔		✔
08 31 23	**FLOOR DOORS (COMPLETE)**				✔		✔		✔		✔		✔		✔
31 23 19	**DEWATERING (AS APPLIES)**				✔		✔		✔		✔		✔		✔
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal				7,843,000		19,517,000		11,287,000		11,012,000		12,903,000		10,833,000
	Slab on Grade				✔				✔		✔				✔
	ASD SOG				✔				✔		✔				✔
	SOG Column Blockouts				✔				✔		✔				✔
	Cooling Tower SOG				✔				✔		✔				✔
RFI #181	Fiber mix in SOG				✔				✔		✔				391,000
	Slab Depressions per AD-SE110				✔				✔		✔				✔
	Ramps on Grade - Excluding Truck Court				✔				✔		✔				✔
	Slab on Metal Deck				✔				✔		✔				✔
	SOMD ASD				✔				✔		✔				✔
	Slab over foam - lightweight concrete				✔				✔		✔				✔
RFI #54	Mechanical Couplers				✔				✔		✔				✔
	Metal stair pan fill				✔				✔		✔				✔
	Walls				✔				✔		✔				✔
	Walls @ Cooling Tower				✔				✔		✔				✔
	Walls @ elevated slab apron level				✔				✔		✔				✔
	Walls @ slab over foam & ramps on grade - lightweigth concrete				✔				✔		✔				✔

Concrete

Base Bid at a glance: 8,502,000 | ~~20,234,000~~ | 12,661,000 | 11,967,000 | ~~13,620,000~~ | 12,471,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	Bidder #5 UP	Bidder #5 TOTAL
		Quantities													
	Pads & Curbs				✔				✔		✔				✔
	Concrete Equipment Pads				✔				✔		✔				✔
	Curbs				✔				✔		✔				✔
	Guideway				✔				✔		✔				✔
	Columns @ Foundations				✔				✔		✔				✔
	Guideway Beams				✔				✔		✔				✔
	Running Rails				✔				✔		✔				✔
	Coordination with Guideway Contractor				✔				✔		✔				✔
	Other Concrete Not Defined Above				✔				✔		✔				✔
	Mockup Pad				✔				✔		✔				✔
	Foundation to precast waterproofing				✔				191,000		191,000				191,000
	Vapor Barrier Upgraded for Waterproofing Compatibility				✔				76,000		76,000				76,000
	Cooling Tower Foundations				✔				✔		✔				✔
	Exterior Pad @ Cooling Tower				✔				✔		✔				✔
AD-A110B-J	Interior Bollards				✔				✔		✔				✔
AD-A110B-J	Interrior Removable Bollards				✔				✔		✔				7,000
11 14 10	Automatic Activation Bollards AD-A110B-J & AD-A451			No	w/ Site Specialties				No-Ok		No-Ok		No-Ok		No-Ok
Note 30/AD-S115H-J	Concrete encased Columns				✔				✔		✔				✔
	VDC LOD400				✔				✔		✔				✔
	Stair Nosings @ cast in place stair treads - install only?				✔				✔		✔				✔
	Cut Rigid Inclusion Cooling Tower - ductile iron piles				✔				✔		✔				✔
	Sheet Piling @ Cooling Towers				✔				336,000		✔				250,000
F1/AD-A701	Floor door				✔		10,000		10,000		✔		10,000		✔
	Column Blockouts Formwork				✔		110,000		110,000		✔		110,000		✔
	Male Formsaver F&I				✔		11,000		11,000		✔		11,000		11,000
	Grout Baseplates				✔		30,000		30,000		✔		30,000		30,000
	Full Time QC Manager				✔		47,000		✔		✔		47,000		47,000
	Full Time Safety Manager				✔				✔		✔				✔
	Full Time Superintendent				✔				✔		✔				✔
	Full Time Project Manager				✔				✔		✔				✔
	Unbought Scope				✔		✔		✔		✔		✔		✔
	Hot Weather Concreting (Chilled Water/Ice)				200,000		200,000		200,000		200,000		200,000		200,000
	Flowfill @ SOG				50,000		50,000		50,000		50,000		50,000		50,000
	Supplimental Backfill @ Column Locations	$1k/column			137,000		137,000		137,000		137,000		137,000		137,000
	3rd Party FF Testing @ SOMD				25,000		25,000		25,000		25,000		25,000		25,000
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**8,255,000**		**INCOMPLETE**		**12,463,000**		**11,691,000**		**INCOMPLETE**		**12,248,000**
	----				----		----		----		----		----		----

00

HENSEL PHELPS
Plan. Build. Manage.

Concrete

Base Bid at a glance: 8,502,000 ~~20,234,000~~ 12,661,000 11,967,000 ~~13,620,000~~ 12,471,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	Bidder #5 UP	Bidder #5 TOTAL
	Quantities														
	Bid Item No. 2 - Centralized Checked Baggage System				w/Below		INCOMPLETE		101,000		179,000		INCOMPLETE		106,000
	Turnkey Concrete				150,000				✔		✔				✔
	Foundaitons for new steel columns w/ anchor bolts				✔				✔		✔				✔
	Slab opening infill				✔				✔		✔				✔
	Patch/Repair SOG surface where pads removed	2,700	sf		✔				✔		✔				10,000
	SOMD	1,000	sf		✔				✔		✔				✔
	Concrete Housekeeping pads				✔				✔		✔				✔
MT-S120C-D,H	Elevated Slab 3" & 5"				✔				✔		✔				✔
Note 3/MT-D-S110E-J	Fill platform holes with grout				✔				✔		✔				✔
	Airside Badging - $60				✔				✔		✔				✔
	6 mobilizations				✔				✔		✔				10,000
	Work Hours: 10PM-4AM Only				✔				✔		✔				✔
	Unbought Scope				✔				✔		✔				✔
	MOT for Drive Lane Work				55,000		55,000		55,000		55,000		55,000		55,000
	MOT for Tug Path				42,000		42,000		42,000		42,000		42,000		42,000
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Centralized Checked Baggage System				**247,000**		**INCOMPLETE**		**198,000**		**276,000**		**INCOMPLETE**		**223,000**
	----				----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	Turnkey Concrete				✔		✔		✔		✔		✔		✔
	No Scope				✔		✔		✔		✔		✔		✔
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**-**		**-**		**-**		**-**		**-**		**-**
	BASE BID TOTAL				**8,502,000**		**INCOMPLETE**		**12,661,000**		**11,967,000**		**INCOMPLETE**		**12,471,000**
	----				----		----		----		----		----		----
	Base Bid - Additional Information				----		----		----		----		----		----
	Total Man-Hours within Base Bid				✔			hrs	48,620	hrs	33,433			hrs	46,212
	Total VDC Man-Hours included to comply with Appendix C				✔			hrs	340	hrs	500			hrs	314
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----

00

HENSEL PHELPS
Plan. Build. Manage.

Masonry

				Base Bid at a glance:		3,470,000		2,358,000		2,273,000		2,226,000	~~3,036,000~~
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03					**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**	**Bidder #4**
LOCATION:	Tampa, FL												
OWNER:	Hillsborough County Aviation Authority												
BID DATE:	10/09/2025												
HP TRADE:		*Quantities*											
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		w/Below		INCOMPLETE
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔		✔		✔
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.44%	✔	1.20%	✔	2.50%	✔	1.40%	✔
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔
	SBE Participation / LOIs & FLUCP Certs Provided			19%	✔	19%	✔	19%	✔	20%	✔	NONE	
	E-Verify Affidavit of Compliance				✔		✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔		✔		✔		
	HCAA NDA Form				✔		✔		✔		✔		
	Bid Package Addenda Acknowledged				✔		✔		✔		✔		✔
	Compass Registration				✔		✔		✔		✔		✔
	----				----		----		----		----		----
	----				----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔
03 30 00	**CAST-IN-PLACE CONCRETE (AS APPLIES)**				✔		✔		✔		✔		✔
04 22 00	**CONCRETE UNIT MASONRY (COMPLETE)**				✔		✔		✔		✔		✔
05 01 00	**POST-INSTALLED STRUCTURAL ANCHORS (AS APPLIES)**				✔		✔		✔		✔		✔
05 50 00	**METAL FABRICATIONS (AS APPLIES)**				✔		✔		✔		✔		✔
07 21 00	**THERMAL INSULATION (AS APPLIES)**				✔		✔		✔		✔		✔
	----				----		----		----		----		----
	----				----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below
	Subtotal Masonry				3,000,000		2,238,000		2,103,000		1,993,000		2,572,000
18/AD-S110A	12" CMU - WA18				✔		✔		✔		✔		✔
	12" Split-face CMU @ dumpster enclosure				✔		✔		✔		✔		✔
	8" CMU				✔		✔		✔		✔		✔
AD-A010	8" CMU rigid insulation - WA15 & WA16				✔		✔		✔		✔		✔
	8" CMU w/ WA15 Assembly				✔		✔		✔		✔		✔
	4" CMU Burnished w/ WA15 Assembly				✔		✔		✔		✔		✔
	4" CMU Burnished w/ WA16 Assembly				✔		✔		✔		✔		✔
Incl. #5	Glazed Block Rooms 6184, 6186, 6187 - AD-A801, AD-A210D				✔		45,000		✔		✔		76,000
07 21 00.F1	Foamed in place insulation				✔		✔		✔		✔		
	Grout HM Frames				✔		✔		✔		✔		✔
2.10/04 22 00	one-pice stainless steel flashing @ veneer wall				✔		✔		✔		✔		7,000
	VDC LOD400				✔		✔		✔		✔		
	Part Time QC Manager				✔		✔		✔		✔		✔
	Full Time Safety Manager				✔		✔		✔		✔		156,000
	Full Time Superintendent				✔		✔		✔		✔		✔

HENSEL PHELPS
Plan. Build. Manage.

Masonry

Base Bid at a glance:				3,470,000		2,358,000		2,273,000		2,226,000		~~3,036,000~~
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**
LOCATION:	Tampa, FL											
OWNER:	Hillsborough County Aviation Authority											
BID DATE:	10/09/2025											
HP TRADE:		*Quantities*										
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Full-time Project Manager				✔		✔		✔		109,000		100,000
	Unbought Scope				✔		✔		✔		✔		✔
	Masonry Dowels & Wall Adjustments for Coordination				50,000		50,000		50,000		50,000		50,000
	----				----		----		----		----		----
	----				----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**3,050,000**		**2,333,000**		**2,153,000**		**2,152,000**		**INCOMPLETE**
	----				----		----		----		----		----
	Bid Item No. 2 - Centralized Checked Baggage System				w/Below		w/Below		w/Below		w/Below		w/Below
	Subtotal Masonry				420,000		25,000		120,000		74,000		75,000
	CMU Wall infill - 04 22 00.N1				✔		✔		✔		✔		✔
	Airside Badging - $60				✔		✔		✔		✔		✔
	Work Hours: 10PM-4AM Only				✔		✔		✔		✔		✔
	----				----		----		----		----		----
	----				----		----		----		----		----
	TOTAL - Bid Item No. 2 - Centralized Checked Baggage System				**420,000**		**25,000**		**120,000**		**74,000**		**75,000**
	----				----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below
	Subtotal Masonry				✔		✔		✔		✔		✔
	No Scope				✔		✔		✔		✔		✔
	----				----		----		----		----		----
	----				----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**-**		**-**		**-**		**-**		**-**
	BASE BID TOTAL				**3,470,000**		**2,358,000**		**2,273,000**		**2,226,000**		**INCOMPLETE**

03.05

HENSEL PHELPS
Plan. Build. Manage.

ORNAMENTAL METALS

Base Bid at a glance:	7,051,000	5,246,000	7,776,000	6,478,000	6,231,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	0570 Ornamental Metals

				HPCC		Bidder #1		Bidder #2		Bidder #3		Bidder #4			
		Quantities													
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		No-Ok		✔		✔		✔		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	2.00%	✔	1.80%	✔	1.00%	✔	1.00%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			25%	✔	25%	✔	10%	LOW	25%	✔	N	None Provided		
	E-Verify Affidavit of Compliance				✔		✔		✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔		✔		✔		✔		
	HCAA NDA Form				✔		✔		✔		✔		✔		
	Compass Registration Completed				✔		✔		✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔		
05 40 00	**COLD-FORMED METAL FRAMING**				✔		✔		✔		✔		✔		
05 58 13	**COLUMN COVERS**				✔		✔		✔		✔		✔		
05 58 14	**EXTERIOR COLUMN COVERS**				✔		✔		✔		✔		✔		
05 70 00	**DECORATIVE METAL**				✔		✔		✔		✔		✔		
05 75 00	**DECORATIVE FORMED METAL**				✔		✔		✔		✔		✔		
06 10 00	**ROUGH CARPENTRY**				✔		✔		✔		✔		✔		
07 92 00	**JOINT SEALANTS**				✔		✔		✔		✔		✔		
09 22 16	**NON-STRUCTURAL METAL FRAMING**				✔		✔		✔		✔		✔		
10 26 00	**WALL AND DOOR PROTECTION**				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----

03.05

HENSEL PHELPS
Plan. Build. Manage.

ORNAMENTAL METALS

Base Bid at a glance: 7,051,000 | 5,246,000 | 7,776,000 | 6,478,000 | 6,231,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	0570 Ornamental Metals

SEC	DESCRIPTION	Quantities QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	UP	TOTAL
	----				----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below		
	Composite Cleanup Crew				✔		✔	N	60,000	N	60,000	N	60,000		
	Decorative Metals				1,951,000		1,289,000		1,400,000		2,111,000		1,673,000		
AD-ID115H	MP02 - Metal-Clad Wood Panels (FIS N. and S. Exit Lids)				✔		✔		✔		✔		✔		
C4/AD-ID20	MP03 - Custom Panels (TL11 Trim and transition to lid)				✔		✔		✔		✔		✔		
	MT01 - Stainless Steel Base at Laminate Wall Panels & Millwork				w/Millwork	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	MT01 - Stainless Steel Base at all other locations				✔		✔		✔		✔		✔		
	MT02 & MT03 - Wall Device Panels				✔		✔		✔		✔		✔		
	MT05 - Scuffmaster Aluminum Brow Trim				✔		✔	N	50,000		✔		✔		
	MT07 - Stainless Steel 16ga at RR Blocks				✔		✔		✔		✔		✔		
RFI #90	PBB Door Sills & Flashings				✔		✔		✔		✔		✔		
	Elevator Entry Jambs				✔		9,000	N	9,000	N	9,000	N	9,000		
	Column Covers				4,368,000	Moz	3,243,000		4,905,000	Gordon	3,601,000	Moz	3,700,000		
	CC01A through CC03 - Column Covers				✔		✔		✔		✔		✔		
	Unbought Scope - Owner-Furnished Monitor Trim Details	16	gates	15k	240,000	N	240,000	N	240,000	N	240,000	N	240,000		
	Unbought Scope - Protection for Terrazzo Sequencing	196	EA	2k	392,000	N	392,000	N	392,000	N	392,000	N	392,000		
	MT01 Base at Column Covers				✔		✔		✔		✔		✔		
	No base req'd at: MT02 Lid, Baggage Belts, Concession Roof				✔		✔		✔		✔		✔		
	Fireproofing Coordination / Removal and Patching				✔		✔		✔		✔		✔		
	Support Framing, Clips, etc.				✔		✔		✔		✔		✔		
	Wall and Door Protection				100,000		73,000		720,000		65,000		157,000		
	WP04 Floor Mounted Bumper Rail				✔		✔		✔		✔		✔		
	SS Bollards at Bottom of Ramps				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**7,051,000**		**5,246,000**		**7,776,000**		**6,478,000**		**6,231,000**		**INCOMPLETE**

03.05

HENSEL PHELPS
Plan. Build. Manage.

ORNAMENTAL METALS

Base Bid at a glance:				7,051,000		5,246,000		7,776,000		6,478,000		6,231,000		-
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		
LOCATION:	Tampa, FL													
OWNER:	Hillsborough County Aviation Authority													
BID DATE:	10/09/2025													
HP TRADE:	0570 Ornamental Metals	*Quantities*												
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	No Scope in CCBSS for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		-		-		-
	----				----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	No Scope in Airside D MT Shuttle Platform for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-
	BASE BID TOTAL				7,051,000		5,246,000		7,776,000		6,478,000		6,231,000		INCOMPLETE

00

HENSEL PHELPS
Plan. Build. Manage.

Waterproofing, Caulking, etc.

Base Bid at a glance:				912,000		1,836,000		1,365,000		~~179,000~~		~~357,000~~		-		-
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		
LOCATION:	Tampa, FL															
OWNER:	Hillsborough County Aviation Authority															
BID DATE:	10/09/2025															
HP TRADE:		*Quantities*														
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		INCOMPLETE		INCOMPLETE		INCOMPLETE		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔				✔				
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.50%	✔	1.50%	✔			1.50%	✔				
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔				✔				
	SBE Participation / LOIs & FLUCP Certs Provided			18%	✔	5%	✔	18%	✔	None		None		None			
	E-Verify Affidavit of Compliance				✔		✔		✔								
	Anti-Trafficking Affidavit				✔		✔		✔								
	HCAA NDA Form				✔		✔		✔								
	Bid Package Addenda Acknowledged				✔		✔		✔				✔				
	Compass Registration				✔		✔		✔								
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔				✔				
07 13 26	**SELF-ADHERING SHEET WATERPROOFING (AS APPLIES)**				✔		✔		✔				✔				
07 14 16	**COLD FLUID APPLIED WATERPROOFING (COMPLETE)**				✔		✔		✔				✔				
07 14 18	**FLUID-APPLIED WATERPROOFING DECK SYSTEM (COMPLETE)**				✔		✔		✔				✔				
07 19 00	**WATER REPELLENTS (COMPLETE)**				✔		✔		✔				✔				
07 27 26	**FLUID-APPLIED MEMBRANE AIR BARRIERS (COMPLETE)**				✔		✔		✔				✔				
07 92 00	**JOINT SEALANTS (AS APPLIES)**				✔		✔		✔				✔				
07 95 13.13	**INTERIOR EXPANSION JOINT COVER ASSEMBLIES (COMPLETE)**				✔		✔		✔				✔				
07 95 16	**EXTERIOR EXPANSION JOINT COVER ASSEMBLIES (COMPLETE)**				✔		✔		✔				✔				
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	Subtotal Waterproofing, Caulking, & Related				832,000		1,771,000		1,323,000		179,000		357,000				
	SOG Control Joints	40,000	LF		✔		✔		✔		✔						
	Column Isolation Joints				✔		✔		✔		✔						
	fluid Applied Membrane Air Barrier @ CMU Walls				✔		✔		✔								
	fluid Applied Membrane Air Barrier @ Exterior Metal Panels				✔		✔		✔				✔				
	fluid Applied Membrane Air Barrier @ Metal Panel Knife Edge (back side only)				✔		✔		✔								
	Sheet Waterproofing @ Planters				✔		✔		✔								
AD-A620/F4	CMU to Metal Panel Sealants & Backer Rod				✔		✔		✔				✔				
AD-A620/F5	Precast to Glazing Sealants & Backer Rod				✔		✔		✔				✔				
AD-A620/A1	Precast to Precast				✔		✔		✔		✔		✔				
AD-A625/A1	Precast to Metal Panel				✔		✔		✔				✔				
	Backer rod and sealant @ CMU walls (every 20' and 25' tall)				✔		✔		✔		✔						
G5/AD-A621	Precast Wall sealants @ Joints				✔		✔		✔		✔						
07 19 00	Precast Waterproofing per spec				✔		✔		✔								
AD-A110H&J	Precast Spray Foam Insulation @ WA30 Wall Type			No	w/ Fireproofing		No-Ok		No-Ok				No-Ok				
A1/AD-S563	1" Expansion Joint around elevator				✔		✔		✔								
	Exterior Expansion Joints				✔		✔		✔				✔				
	Interior Expansion Joints				✔		✔		✔				✔				

00

HENSEL PHELPS
Plan. Build. Manage.

Waterproofing, Caulking, etc.

Base Bid at a glance:				912,000		1,836,000		1,365,000		~~179,000~~		~~357,000~~		-		-
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		
LOCATION:	Tampa, FL															
OWNER:	Hillsborough County Aviation Authority															
BID DATE:	10/09/2025															
HP TRADE:		*Quantities*														
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
A1/AD-A627, A4/AD-A620	Silicone Coated Precompressed Foam - 07 92 00.E1				✔		✔		✔				✔				
A1/AD-A627	SILICONE TRANSFER SHEET				✔		✔		✔				✔				
A1/AD-S722	2" JOINT, FILL WITH COMPRESSIBLE FILL AND SEAL	4,000	LF		✔		✔		✔				✔				
G4/AD-A786	Joint Sealant @ Escalator Connection				✔		✔		✔								
A4/AD-A418	Drainage Panel @ Smoking Deck				✔		✔		✔								
	VDC LOD400				✔		✔		✔								
	Full Time QC Manager				✔		✔		✔								
	Part Time Safety Manager				✔		✔		✔								
	Full Time Superintendent				✔		✔		✔								
	Part Time Project Manager				✔		✔		✔								
	Unbought Scope				✔		✔		✔		✔		✔		✔		----
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**832,000**		**1,771,000**		**1,323,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**
									1,333,000								
	----				----		----		----		----		----		----		----
	Bid Item No. 2 - Centralized Checked Baggage System				w/Below		w/Below		w/Below		INCOMPLETE		INCOMPLETE		INCOMPLETE		
	Subtotal Waterproofing, Caulking, & Related				50,000		35,000		11,000								
	Joint Sealants @ Interior Storefront & Curtain Walls				✔		✔		✔								
	Joint Sealants @ Exterior Storefront & Curtain Walls				✔		✔		✔								
	Masonry Joint Sealants				✔		✔		✔								
	Concrete Joint Sealants				✔		✔		✔								
	Mobilizations for CCBS	6	ea		✔		✔		21,000								
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Centralized Checked Baggage System				**50,000**		**35,000**		**32,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**
	----				----		----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		INCOMPLETE		INCOMPLETE		INCOMPLETE		
	Subtotal Waterproofing, Caulking, & Related				30,000		30,000		10,000								
	Joint Sealants				✔		✔		✔								
	Air Barrier				✔		✔		✔								
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**30,000**		**30,000**		**10,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**
	BASE BID TOTAL				**912,000**		**1,836,000**		**1,365,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**

03.08

HENSEL PHELPS
Plan. Build. Manage.

Roofing

Base Bid at a glance:			13,434,000		~~11,523,000~~		10,433,000				11,116,000			
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03		**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**			
LOCATION:	Tampa, FL													
OWNER:	Hillsborough County Aviation Authority													
BID DATE:	10/09/2025													
HP TRADE:	0730 Roofing	*Quantities*												
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		**Incomplete**		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔		**Disqualified**		✔		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)				✔	1.20%	✔	2%	✔			1.15%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔				✔		
	SBE Participation / LOIs & FLUCP Certs Provided			18%	✔	N		30%	✔			18%	✔		
	Appendix K				✔		✔		✔				✔		
	E-Verify Affidavit of Compliance				✔		✔		✔				✔		
	Anti-Trafficking Affidavit				✔		✔		✔				✔		
	HCAA NDA Form				✔		✔		✔				✔		
	Compass Registration Completed				✔		✔		✔				✔		
	Bid Package Addenda Acknowledged - #01 through #06				✔		✔		✔				✔		
	----				----		----		----		----		----		----
	BIM- LOD400				✔		20,000		✔				20,000		
	Composite Clean up				✔		✔		✔				26,000		
	Staffing per Bid Package				✔		✔		✔				✔		
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔				✔		
05 12 00	**Structural Steel Framing (As Applies)**				✔		✔		✔				✔		
05 50 00	**Metal Fabrications (As Applies)**				✔		✔		✔				✔		
06 10 00	**Rough Carpentry (As Applies)**				✔		✔		✔				✔		
07 13 26	**Self-Adhering Sheet Waterproofing (As Applies)**				✔		✔		✔				✔		
07 21 00	**Thermal Insulation (As Applies)**				✔		✔		✔				✔		
07 41 13.16	**Standing-Seam Metal Roof Panels**				✔		✔		✔				✔		
07 54 19	**Polyvinyl-Chloride (PVC) Roofing (Complete)**				✔		✔		✔				✔		
07 62 00	**Sheet Metal Flashing & Trim (Complete)**				✔		✔		✔				✔		
07 71 29	**Manufactured Roof Expansion Joints (Complete)**				✔		✔		✔				✔		
07 72 00	**Roof Accessories (Complete)**				✔		✔		✔				✔		
07 92 00	**Joint Sealants (As Applies)**				✔		✔		✔				✔		
11 24 26	**Fall Protection- Interior (Complete)**				✔		✔		✔				✔		
11 24 29	**Fall Protection (Complete)**				✔		✔		✔				✔		
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below				w/Below		
07 54 19	***PVC Roofing-RS01***				12,609,000		880,000		1,598,000				1,377,000		
AD-A150	Level 5 Mid Roof				✔		✔		✔				✔		
AD-A150	Walk Pad				✔		✔		✔				✔		
Page 754	Warranty per spec- 150 mph wind rider				✔		✔		✔				(555,000)		
07 41 13.16	***Sheetmetal Roofing-RS02***				w/Above		9,075,000		8,325,000				9,905,000		
AD-A603-D1/A501/AD-	Standing Seam Metal Roof at Outbuildings Trash/TruckCourt, Cooling Tower				✔		✔		✔				✔		
AD-A150	Level 5 High and Mid Roof				✔		✔		✔				✔		
A-608/AS-ES00	Flashing and Counter flashing at Lighting poles	17	ea		✔		✔		✔				✔		
	Roof deck shimming per NRCA standards				✔		200,000		200,000				200,000		
	Warranty per spec- 150 mph wind rider				✔		✔		✔				✔		
	Other				✔		----		----		----		----		

03.08

HENSEL PHELPS
Plan. Build. Manage.

Roofing

Base Bid at a glance:				13,434,000		~~11,523,000~~		10,433,000				11,116,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		
LOCATION:	Tampa, FL													
OWNER:	Hillsborough County Aviation Authority													
BID DATE:	10/09/2025													
HP TRADE:	0730 Roofing		*Quantities*											
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
Inc #25	Temporary Sealing of deck, flashing at drains, etc.				✔		✔		✔				✔		
AD-A603-D5	Downspouts at Trash Enclosure				✔		✔		✔				✔		
	Sacrifical Roofing				✔		✔		✔				✔		
Inc #23	Temporary Roofing 58,000sf	58,000	sf		✔		368,000		✔				✔		
	PVC metal Cladding				✔		4,000		4,000				4,000		
	Future Tenant Curbs	20	ea		✔		50,000		50,000				50,000		
11 24 29	***Fall Protection***				736,000		670,000		w/Above				✔		
AD-A150	Exterior at Standing Seam and PVC				w/Above		✔		✔				✔		
	Sealants at roof tie backs				w/Above		✔		✔				✔		
11 24 26	***Fall Protection Interior Platforms***				✔		167,000		167,000				✔		
AD-ID130	Interior at concessions				✔		✔		✔				✔		
	Roof Fall Protection-Permanent Recertification @Project End				10,000		10,000		10,000				10,000		
	Infared Survey for Roofing System				25,000		25,000		25,000				25,000		
	Roof Penetration Coordinated Additional	542	ea		54,200		54,200		54,200				54,200		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**13,434,000**		**INCOMPLETE**		**10,433,000**		**INCOMPLETE**		**11,116,000**		**INCOMPLETE**

03.08

HENSEL PHELPS
Plan. Build. Manage.

Roofing

Base Bid at a glance: 13,434,000 | ~~11,523,000~~ | 10,433,000 | ———— | 11,116,000 | ————

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	0730 Roofing

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	UP	TOTAL
	----				----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade	N/A			N/A		N/A		N/A		N/A		N/A		
	No scope in CCBS for this scope of work				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		-		-		INCOMPLETE
	----				----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform	N/A			N/A		N/A		N/A		N/A		N/A		
	No scope in Shuttle Platform for this scope of work				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		INCOMPLETE
	BASE BID TOTAL				13,434,000		INCOMPLETE		10,433,000		INCOMPLETE		11,116,000		INCOMPLETE
	----				----		----		----		----		----		----
	Base Bid - Additional Information				----		----		----		----		----		----
	Total Man-Hours within Base Bid				✔		25,000		23,750				67,000		
	Total VDC Man-Hours included to comply with Appendix C				✔				200						
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----

03.07

HENSEL PHELPS
Plan. Build. Manage.

Metal Panels

Base Bid at a glance: 5,180,000 | 3,885,000 | 5,425,000 | 4,520,000 | 4,169,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	10/09/2025
HP TRADE:	0742 Metal Panels

SEC	DESCRIPTION	Quantities QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	Bidder #5 UP	Bidder #5 TOTAL	Bidder #6 UP	Bidder #6 TOTAL	Bidder #7 UP	Bidder #7 TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		**DISQUALIFIED**		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		No-Ok		✔		No-Ok		No-Ok		✔		Not Compliant		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)				✔	1.35%	✔	1.00%	✔	1.80%	✔	1.00%	✔	1.00%	✔	1.50%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			18%	✔	100%	✔	9%	Not compliant	18%	✔	100%	✔	25%	Not compliant	No	Not compliant		
	E-Verify Affidavit of Compliance				✔		✔		✔		✔		✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔		✔		✔		✔		✔		✔		
	HCAA NDA Form				✔		✔		✔		✔		✔		✔		✔		
	Exhibit K				✔		✔		✔		✔		✔		✔	No	Not compliant		
	Compass Registration Completed				✔		✔		✔		✔		✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		✔		✔		✔		✔		
	Comply with Staffing in Bid Package				✔		✔		✔		✔		53,000		✔		✔		
	BIM per VDC plan				✔		✔		✔		✔		✔		✔		✔		
	Composite Crew				✔		✔		✔		✔		10,000		✔		✔		
AD-A012	Mockup				✔		No-Ok		45,000		✔		✔		✔		✔		
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔						
05 40 00	**Cold-Formed Metal Framing (As Applies)**				✔		✔		✔		✔		✔						
07 42 13.16	**Metal Plate Wall Panels (Complete)**				✔		✔		✔		✔		✔						
07 42 13.19	**Insulated Metal Wall Panels (Complete)**				✔		✔		✔		✔		✔						
07 42 13.23	**Metal Composite Material Wall Panels (Complete)**				✔		✔		✔		✔		✔						
07 42 93	**Soffit Panels (Complete)**				✔		✔		✔		✔		✔						
07 92 00	**Joint Sealants (As Applies)**				✔		✔		✔		✔		✔						
09 22 16	**Non-Structural Metal Framing (As Applies)**				✔		✔		✔		✔		✔						
~~**07 48 00**~~	~~**Cladding Attachement & Supports Systems**~~	Not Found			No-Ok		No-Ok		No-Ok		No-Ok		No-Ok						

HENSEL PHELPS
Plan. Build. Manage.

Metal Panels

Base Bid at a glance:					5,180,000		3,885,000		5,425,000		4,520,000		4,169,000						
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #4**		**Bidder #5**		**Bidder #6**		**Bidder #7**		
LOCATION:	Tampa, FL																		
OWNER:	Hillsborough County Aviation Authority																		
BID DATE:	10/09/2025																		
HP TRADE:	0742 Metal Panels	*Quantities*																	
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
----	----				----		----		----		----		----						
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below						
07 42 13.19	***Insulated Metal Wall Panels***				5,160,000	16335sf	3,865,000	16028sf	5,360,000	14700sf	4,500,000	34700sf	4,086,000						
AD-A312	Joint at Metal panel and Soffit(FS02)				✔		✔		✔		✔		✔						
AD-A481	Sterile Corridor and Concourse				✔		✔		✔		✔		✔						
AD-A605	Exterior Wall				✔		✔		✔		✔		✔						
A-320/321/308	Shuttle/Tunnel Elevations/Soffit(FS03)				✔		✔		✔		✔		✔						
AD-A305/A360	Wall Panel around HM doors				✔		✔		✔		✔		✔						
AD-A417	Smoking Deck				✔		✔		✔		✔		✔						
AD-A700/A110	Fleet Manager/BHS Control room/Baggage Drop A				✔		✔		✔		✔		✔						
AD-A115J/A33	Wall Type WA25				✔		✔		✔		✔		✔						
07 42 13.23	***Metal Composite Material Wall Panels -FS01/FS02***				✔	27840sf	✔	38963sf	✔	46000sf	✔	35450sf	✔						
AD-A125A-F	Mid-Roof Fascia Above				✔		✔		✔		✔		✔						
AD-A150A-F	Level 5 Roof Fascia				✔		✔		✔		✔		✔						
AD-ID527- ID72	Gate bridges with integrated lighting				✔		✔		✔	1100sf	✔		✔						
07 42 13.16	***Metal Plate Wall Panels (Complete)***				✔	500sf	✔	495sf	✔	500sf	✔	450sf	✔						
AD-A417	Perforated metal at Smoking deck				✔		✔		✔				✔						
07 42 93	***Soffit Panels (Complete)***				✔	12,240	✔		✔	2700sf	✔		✔						
D-A220A-J/A60	Gutter Soffit				✔		✔		✔		✔		✔						
AD-A225A-D	Mid-Roof Gutter Soffit				✔		✔		✔		✔		✔						
	Metel Panel Penetrations				20,000		20,000		20,000		20,000		20,000						
	Underlayment			No	w/Waterproofing		No-Ok		No-Ok		No-Ok		No-Ok						No-Ok
----	----				----		----		----		----		----		----		----		----
----	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**5,180,000**		**3,885,000**		**5,425,000**		**4,520,000**		**4,169,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**
----	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**5,180,000**		**3,885,000**		**5,425,000**		**4,520,000**		**4,169,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**

03.07

HENSEL PHELPS
Plan. Build. Manage.

Metal Panels

	Base Bid at a glance:				5,180,000		3,885,000		5,425,000		4,520,000		4,169,000						
	PROJECT: TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #4**		**Bidder #5**		**Bidder #6**		**Bidder #7**		
	LOCATION: Tampa, FL																		
	OWNER: Hillsborough County Aviation Authority																		
	BID DATE: 10/09/2025																		
	HP TRADE: 0742 Metal Panels		*Quantities*																
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No work for this scope in CCBS				N/A		N/A		N/A		N/A		N/A		N/A		N/A		
	----				----		----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		-		-		-		-		**INCOMPLETE**
	----				----		----		----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No work for this scope in Shuttle Platform				N/A		N/A		N/A		N/A		N/A		N/A		N/A		
	----				----		----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-		-		**INCOMPLETE**
	BASE BID TOTAL				**5,180,000**		**3,885,000**		**5,425,000**		**4,520,000**		**4,169,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**

03.18

HENSEL PHELPS
Plan. Build. Manage.

INTERIOR WALL PANELS

	Base Bid at a glance:				5,003,000		2,322,000		2,353,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	Tuesday, November 11, 2025										
HP TRADE:	0741 Siding	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		No-Ok		No-Ok		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	2.00%	✔	1.00%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			21%	✔	21%	✔	21%	✔		
	E-Verify Affidavit of Compliance				✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔		✔		
	HCAA NDA Form				✔		✔		✔		
	Compass Registration Completed				✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		
	----				----		----		----		----
	----				----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		
05 70 00	**DECORATIVE METAL**				✔		✔		✔		
06 10 00	**ROUGH CARPENTRY**				✔		✔		✔		
08 81 13	**DECORATIVE GLASS GLAZING**				✔		✔		✔		
09 77 13	**STRETCHED-FABRIC WALL SYSTEMS**				✔		✔		✔		
09 78 00	**INTERIOR WALL PANELING**				✔		✔		✔		
	----				----		----		----		----

03.18

HENSEL PHELPS
Plan. Build. Manage.

INTERIOR WALL PANELS

	Base Bid at a glance:				5,003,000		2,322,000		2,353,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	Tuesday, November 11, 2025										
HP TRADE:	0741 Siding	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		
	Interior Wall Panels				4,320,000		1,624,000		1,705,000		
	GL01 - Custom Graphic Glass at RR Entry Vestibules	800	SF	450	✔	810	✔	860	✔		
	GL03 - Decorative Glass at Millwork				w/Millwork		No-Ok		No-Ok		
	GL04 - Decorative Glass in Elevator Cabs				w/Elevators		No-Ok		No-Ok		
	GL06 - Glass Wall Panels at Train Tubes	4,590	SF		✔	4,120	✔	4,010	✔		
	GL07A through GL07E - Glass Wall Panels at Elevators	3,400	SF		✔	2,866	✔	2,915	✔		
	Plywood Sheathing/Blocking for GWPs				✔		✔		✔		
	Unbought Scope Budget - Signage Coordination				75,000	N	75,000	N	75,000		
	Unbought Scope Budget - Elevator Finish Interface Coordination	42	STP	4,000	168,000	N	168,000	N	168,000		
	SF01 / SF02 / SF03 /SF04 - Stretched Fabric Panels				✔	2,650	✔	1,700	✔		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**4,563,000**		**1,867,000**		**1,948,000**		**INCOMPLETE**

03.18

HENSEL PHELPS
Plan. Build. Manage.

INTERIOR WALL PANELS

				Base Bid at a glance:		5,003,000		2,322,000		2,353,000	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	Tuesday, November 11, 2025										
HP TRADE:	0741 Siding		*Quantities*								
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		
	Interior Wall Panels				335,000		350,000		75,000		
MT-A310	Replacement Red GP1 Panels at BHS Room				✔		✔		✔		
MT-A122	Replacement Panels at Belt Room Exterior				✔		✔	N	225,000		
	Unbought Scope - MOT / Dry-In Envelope Protection				100,000	N	100,000	N	100,000		
	Replace Interior SS Base - Wood blocking				✔		✔		✔		
	Replace Exterior SS Base - Concrete Infill (field condition)				5,000	N	5,000	N	5,000		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**440,000**		**455,000**		**405,000**		**INCOMPLETE**
	----				----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		
	No Scope in Airside D MT Shuttle Platform for this Bid Package				No-Ok		No-Ok		No-Ok		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		**INCOMPLETE**
	BASE BID TOTAL				**5,003,000**		**2,322,000**		**2,353,000**		**INCOMPLETE**

03.06

HENSEL PHELPS
Plan. Build. Manage.

Fireproofing

Base Bid at a glance:				3,699,000		-		-		-		-		7,561,000		4,701,000		4,283,000		-	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		**Bidder #6**		**Bidder #7**			
LOCATION:	Tampa, FL																				
OWNER:	Hillsborough County Aviation Authority																				
BID DATE:	10/09/2025																				
HP TRADE:	0781 Applied Fireproofing & Spray Insulation	*Quantities*																			
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		**DISQUALIFIED**		**DISQUALIFIED**		**DISQUALIFIED**		**DISQUALIFIED**		**DISQUALIFIED**		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		Not Compliant		INCOMPLETE		No-Ok		✔		No-Ok		No-Ok		No-Ok		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)				✔	1.00%	✔		Not Bondable		Not Bondable		Not Bondable	1.75%	✔	1.00%	✔	1.25%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			15%	✔	2%								N		16%	✔	15%	✔		
	Appendix K				✔		✔								✔		✔		✔		
	E-Verify Affidavit of Compliance				✔		✔				✔		✔		✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔				✔		✔		✔		✔		✔		
	HCAA NDA Form				✔		✔				✔		✔		✔		✔		✔		
	Compass Registration Completed				✔		✔				✔		✔		✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #07				✔		✔						✔		✔		✔		✔		
	----				----		----		----		----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔										✔		✔		✔		
07 21 19	**Foamed-in-Place Insulation (As Applies)**				✔										✔		✔		✔		
07 81 00	**Applied Fireproofing (Complete)**				✔										✔		✔		✔		
07 81 23	**Intumescent Fireproofing (Complete)**				✔										✔		✔		✔		
07 84 43	**Joint Firestopping (Complete)**				✔										✔		✔		✔		
07 21 00	**Thermal Insulation**	AMD1			✔										✔		✔		✔		

HENSEL PHELPS
Plan. Build. Manage.

Fireproofing

	Base Bid at a glance:				3,699,000		-		-		-		-		7,561,000		4,701,000		4,283,000		-
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		**Bidder #6**		**Bidder #7**		
LOCATION:	Tampa, FL																				
OWNER:	Hillsborough County Aviation Authority																				
BID DATE:	10/09/2025																				
HP TRADE:	0781 Applied Fireproofing & Spray Insulation	*Quantities*																			
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	---				---		---		---		---		---		---		---		---		---		---
	VDC				✔										✔		✔		✔		
	Composite Crew				✔										150,000		✔		✔		
	Staffing per Bid Package				✔										✔		✔		✔		
	Generator				✔										✔		✔		30,000		
	Bid Item No. 1 - Airside D Terminal				w/Below										w/Below		w/Below		w/Below		
07 81 00	***Applied Fireproofing***				2,980,000										5,860,000		1,811,000		2,426,000		
AD-A016/G3	Rated Partition at Fireproofed Steel				✔										✔		✔		✔		
AD-A016/G5	Rated Shaft Walls at Fireproofed Steel and Deck				✔										✔		✔		✔		
AD-A016/G6	Rated Shaft Walls at Fireproofed Steel and Deck 2				✔										✔		✔		✔		
AD-A414	Exposed Structural beams in Train tubes				✔										✔		✔		✔		
AD-S135A-F	Low roofing				✔										✔		445,000		✔		
	High Density @Outbound Baggage & APM Maintenance per RFI				✔										✔		✔		✔		
	Patching of Damaged Fireproofing				505,000										505,000		505,000		505,000		
07 84 43	***Fire Resistive Joint Sealant***				✔										153,000		214,000		153,000		
AD-A013	Top of Floor Slab(G4,S2,S1,G42,G3,G2				✔										✔		✔		✔		
AD-A016/G1	Rated Partition at Fireproofed Deck				✔										✔		✔		✔		
AD-A016/G3	Rated Partition at Fireproofed Steel				✔										✔		✔		✔		
AD-A016/G5	Rated Shaft Walls at Fireproofed Steel and Deck				✔										✔		✔		✔		
	Joint firestopping at Drywall Partitions			No	w/Drywall										No-Ok		No-Ok		No-Ok		
07 21 00	***Thermal Insulation***	AMD1			✔										712,000		843,000		712,000		
AD-A700/A010	Foamed in place Masonry Insulation @ all WA18 walls(AD-A010)			No	w/Masonry										No-Ok		(37,000)		No-Ok		
07 21 19	***Spray Insulation with Fire-Resistive Coating***	AMD1			✔										✔		✔		✔		
AD-A607	Eave Assemblies				✔										✔		✔		✔		
AD-A622/F1	Curtain wall Head mullion at Fascia				✔										✔		✔		✔		
AD-A210/A010	Underslab spray inslulation over unconditioned areas-FL01	78,230	sf		✔										✔		✔		✔		
A-620/A110H/A	Wall Type W30- Backside of Precast wall				✔										✔		✔		✔		
	Patching of Damaged Spray Insulation				50,000										50,000		50,000		50,000		
07 81 23	***Intumescent Fireproofing***				✔										117,000		290,000		63,000		
AD-A220J/A41	Exposed Structural Columns in Train Tube				✔										✔		✔		✔		
AD-A210D/AD-A	Beam and Brace at CL2				✔										✔		✔		✔		
	Patching of Damaged Intumescent FIreproofing-ALLOWANCE 5%				✔										14,000		5,000		4,000		
	---				---		---		---		---		---		---		---		---		---
	TOTAL - Bid Item No. 1 - Airside D Terminal				**3,535,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**4,126,000**		**3,943,000**		**INCOMPLETE**

03.06

HENSEL PHELPS
Plan. Build. Manage.

Fireproofing

Base Bid at a glance:				3,699,000		-		-		-		-		7,561,000		4,701,000		4,283,000		-	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		**Bidder #6**		**Bidder #7**			
LOCATION:	Tampa, FL																				
OWNER:	Hillsborough County Aviation Authority																				
BID DATE:	10/09/2025																				
HP TRADE:	0781 Applied Fireproofing & Spray Insulation	*Quantities*																			
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
07 81 00	***Applied Fireproofing***				✔												292,000		23,000		
MT-S120D.Nt 3	All Steel to receive fireproofing				✔												✔		✔		
MT-D-A111E/N	Patching of Damaged Fireproofing				82,000												82,000		82,000		
07 84 43	***Fire Resistive Joint Sealant***				✔												20,000		82,000		
07 21 00	***Acoustical Spray Insulation***	AMD2			✔												96,000		71,000		
MT-A311/MT-A	CBIS Elevations				✔												✔		✔		
MT-A422	Leidos Offices				✔												✔		✔		
MT-A424/425-/	CBRA				✔												✔		✔		
	Patching of Damaged Spray Insulation				82,000												82,000		82,000		
07 21 19	***Spray Insulation with Fire-Resistive Coating***	AMD1			✔												3,000		✔		
MT-612 C1/MT	*Top connection Gyp Wall*				✔												✔		✔		
	Night work				✔												✔		✔		
	----				----		----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**164,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**575,000**		**340,000**		**INCOMPLETE**
	----				----		----		----		----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				----		----		----		----		----		----		----		----		
	No Scope in Shuttle Platform for this bid package				✔		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-		-		-		**INCOMPLETE**
	BASE BID TOTAL				**3,699,000**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**INCOMPLETE**		**4,701,000**		**4,283,000**		**INCOMPLETE**

03.10

HENSEL PHELPS
Plan. Build. Manage.

GLASS & GLAZING

				Base Bid at a glance:		21,843,000		17,469,000		~~19,687,000~~		18,702,000		19,786,000		19,718,000		20,786,000	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03					**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		**Bidder #6**	
LOCATION:	Tampa, FL																		
OWNER:	Hillsborough County Aviation Authority																		
BID DATE:	Tuesday, November 11, 2025																		
HP TRADE:	0880 Glass and Glazing																		
SEC	DESCRIPTION	QTY	UN	*Quantities*		UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount						w/Below		w/Below		**INCOMPLETE**		w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)						✔		✔	N	**Exterior Only**		✔		✔		✔		✔
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)					1.5%	✔	2.00%	✔	1.50%	✔	1.80%	✔	0.75%	✔	1.50%	✔	1.50%	✔
	Sales Tax Included (Hillsborough - 7.5%)						✔		✔		✔		✔		✔		✔		✔
	SBE Participation / LOIs & FLUCP Certs Provided					21%	✔	24%	✔	N		21%	✔	40%	✔	7%	LOW	15%	LOW
	E-Verify Affidavit of Compliance						✔	N	will provide	N			✔	N	will provide	N	will provide		✔
	Anti-Trafficking Affidavit						✔	N	will provide	N			✔	N	will provide	N	will provide		✔
	HCAA NDA Form						✔	N	will provide	N			✔	N	will provide	N	will provide		✔
	Compass Registration Completed						✔		✔	N			✔		✔		✔	N	will provide
	Bid Package Addenda Acknowledged - #01 through #06						✔		✔	N			✔		✔		✔		✔
	----						----		----		----		----		----		----		----
	----						----		----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**						✔		✔				✔		✔		✔		✔
05 73 16	**STRUCTURAL GLASS WALL RAILINGS (Addendum #02)**						✔		✔				✔		✔		✔		✔
06 10 00	**ROUGH CARPENTRY**						✔		✔				✔		✔		✔		✔
07 84 43	**JOINT FIRESTOPPING**						✔		✔				✔		✔		✔		✔
07 92 00	**JOINT SEALANTS**						✔		✔				✔		✔		✔		✔
08 34 73.13	**SOUND CONTROL WINDOW ASSEMBLIES**						✔		✔				✔		✔		✔		✔
08 41 13	**ALUMINUM-FRAMED ENTRANCES AND STOREFRONTS**						✔		✔				✔		✔		✔		✔
08 41 20	**STRUCTURAL GLASS FIN WALL**						✔		✔				✔		✔		✔		✔
08 41 26	**ALL-GLASS ENTRANCES AND STOREFRONTS**						✔		✔				✔		✔		✔		✔
08 42 29.23	**SLIDING AUTOMATIC ENTRANCES**						✔		✔				✔		✔		✔		✔
08 44 13	**GLAZED ALUMINUM CURTAIN WALLS**						✔		✔				✔		✔		✔		✔
08 44 16	**INTERIOR GLAZED ALUMINUM CURTAIN WALLS**						✔		✔				✔		✔		✔		✔
08 44 23	**STRUCTURAL-SEALANT-GLAZED CURTAIN WALLS**						✔		✔				✔		✔		✔		✔
08 56 53	**SECURITY WINDOWS**						✔		✔				✔		✔		✔		✔
08 71 00	**DOOR HARDWARE**						✔		✔				✔		✔		✔		✔
08 71 13	**AUTOMATIC DOOR OPERATORS**						✔	N	w/Below			N	w/Below	N	w/Below	N	w/Below	N	w/Below
08 80 00	**GLAZING**						✔		✔				✔		✔		✔		✔
08 81 13	**DECORATIVE GLASS GLAZING**						✔		✔				✔		✔		✔		✔
08 83 00	**MIRRORS**						✔		✔				✔		✔		✔		✔
08 88 53	**SECURITY GLAZING**						✔		✔				✔		✔		✔		✔
08 91 19	**FIXED LOUVERS**						✔		✔				✔		✔		✔		✔
10 22 46	**CANTILEVER GLASS PARTITION (Addendum #02)**						✔		✔				✔		✔		✔		✔
	----						----		----		----		----		----		----		----

HENSEL PHELPS
Plan. Build. Manage.

GLASS & GLAZING

					Base Bid at a glance:		21,843,000		17,469,000		~~19,687,000~~		18,702,000		19,786,000		19,718,000		20,786,000
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03																		
LOCATION:	Tampa, FL																		
OWNER:	Hillsborough County Aviation Authority																		
BID DATE:	Tuesday, November 11, 2025																		
HP TRADE:	0880 Glass and Glazing																		
					HPCC		Bidder #1		Bidder #2		Bidder #3		Bidder #4		Bidder #5		Bidder #6		
SEC	DESCRIPTION	QTY	UN		UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
		Quantities																		
	----					----		----		----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal					w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
Purch. Adjust	Material Escalation for full project duration					✔		413,000		✔		✔		✔		✔		✔		
	Full BIM/VDC Participation					✔		✔		✔		✔		✔		50,000		✔		
	Interior Glazing					9,015,000		5,840,000	N	6,500,000		7,165,000		7,412,000		5,589,000		6,917,000		
	GW01 - GW06 Glass Partitions					✔	41,870	✔	N	w/Above	44,900	✔	47,902	✔		✔		✔		
	RL01 System Gates					w/Glass Handrail	Y	(82,000)		No-Ok		No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Unbought Scope - Proprietary System Detail Coordination					350,000	N	350,000	N	350,000	N	350,000	N	350,000	N	350,000	N	350,000		
	Films on Glass - GF01 (GF03 Removed at 100%)					✔		✔	N	w/Above		✔		✔	N	40,000		✔		
	GL01, GL06, and GL07 Series Glazing					w/Int. Wall Panels		No-Ok	N	w/Above		No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	SSCP Area Fin Wall					✔		390,000	N	w/Above		✔		✔		✔		✔		
	GL03 Glazing integral to GW04 Walls					✔		✔	N	w/Above		✔		✔		✔		✔		
	GL03 Glazing at Millwork					w/Millwork		No-Ok	N	w/Above		No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	MR01 - MR03 Unframed Mirrors					✔		✔	N	w/Above		✔		✔		✔		✔		
	Interior HM Windows - W01, W02, W03, W04					✔		✔	N	w/Above		✔		✔		✔		✔		
08 34 73-3.4B	Field Testing of STC Windows					✔		10,000	N	40,000	N	40,000	N	40,000		40,000	N	40,000		
	Ballistic-Rated Glass at CBP Cashier					Not Shown		No-Ok	N	No-Ok		No-Ok		No-Ok		✔		No-Ok		
	Unbought Scope - CBP Compliance, Testing/Certification					50,000	N	50,000	N	50,000		50,000		50,000	N	50,000	N	50,000		
	Interior Glass Doors, hardware, lites					✔		✔	N	w/Above		✔		✔		✔		✔		
	Automatic Door Operators at Glass Doors (all on HM Openings)					w/Doors Fr HW	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Exterior Glazing					12,008,000		7,918,000		10,415,000		8,200,000		9,302,000		9,999,000		10,379,000		
	Unbought Scope - Window Protection Maintenance & Sequencing	1	LS		120k	120,000	N	120,000	N	120,000	N	120,000	N	120,000	N	120,000	N	120,000		
	Unbought Scope - Field / Chamber Test Addl. Conditions & Locations	1	LS		200k	200,000	N	200,000	N	200,000	N	200,000	N	200,000	N	200,000	N	200,000		
	10 Year Warranty on Exterior Systems					✔		277,000				✔	N	300,000		550,000		✔		
	Heat Soak all glass					✔		392,000	N	750,000	N	750,000	N	750,000	N	750,000	N	750,000		
	Field QC Testing per 08 44 13-3.4 and prep work					✔		✔				✔		✔	N	65,000	N	65,000		
	3rd Party to perform & certify testing					✔		53,000	N	53,000	N	53,000	N	53,000	N	53,000	N	53,000		
AD-A012	Standalone Mockup Curtainwall					✔		✔				✔		✔	N	65,000	N	65,000		
AD-A350	CW01 and CW02 Curtainwall System					✔	53,100 SF	✔		✔	49,300 SF	✔	50,691 SF	✔		✔		✔		
	Louver Integrated Curtainwall System					✔		✔		✔		✔		✔		✔		✔		
C5/AD-A621, E	Downspout stirrups, hangers, brackets					✔		✔				✔		✔		✔		✔		
C5/AD-A621, E	Downspouts - SS Material from Roof to Ground					✔		984,000	N	984,000	N	984,000	N	984,000	N	984,000	N	984,000		
	Downspout boots & tie in to storm					✔		67,000	N	125,000	N	125,000	N	125,000	N	125,000	N	125,000		
	Downspouts from Clerestory to Mid-Roof	24	EA		4k	100,000	N	100,000	N	100,000	N	100,000	N	100,000	N	100,000	N	100,000		
AD-A603	Downspouts at Trash Enclosure					w/Roofing	N	No-Ok	N	No-Ok	N	No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	Exterior Glass & Storefront Doors, hardware, lites					✔		✔		✔		✔		✔		✔		✔		
	Slab Edge Firesafing at CW Locations					✔		✔				✔		✔		✔		✔		
	Protection and Cleaning					✔		387,000			N	565,000		✔		588,000	N	588,000		
	----					----		----		----		----		----		----		----		----
	----					----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal					**21,843,000**		**17,469,000**		**INCOMPLETE**		**18,702,000**		**19,786,000**		**19,718,000**		**20,786,000**		**INCOMPLETE**

03.10

HENSEL PHELPS
Plan. Build. Manage.

GLASS & GLAZING

Base Bid at a glance: 21,843,000 | 17,469,000 | ~~19,687,000~~ | 18,702,000 | 19,786,000 | 19,718,000 | 20,786,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	Tuesday, November 11, 2025
HP TRADE:	0880 Glass and Glazing

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	Bidder #5 UP	Bidder #5 TOTAL	Bidder #6 UP	Bidder #6 TOTAL	UP	TOTAL
		Quantities																	
	----				----		----		----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No Scope in WCBSS for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		-		-		-		-		**INCOMPLETE**
	----				----		----		----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No Scope in Airside D MT Shuttle Platform for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-		-		**INCOMPLETE**
	BASE BID TOTAL				**21,843,000**		**17,469,000**		**INCOMPLETE**		**18,702,000**		**19,786,000**		**19,718,000**		**20,786,000**		**INCOMPLETE**

HENSEL PHELPS
Plan. Build. Manage.

GLASS & GLAZING

				Base Bid at a glance:		21,743,000		17,369,000		~~19,587,000~~		18,602,000		19,686,000		19,618,000		20,686,000			
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03					**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		**Bidder #6**			
LOCATION:	Tampa, FL																				
OWNER:	Hillsborough County Aviation Authority																				
BID DATE:	Tuesday, November 11, 2025																				
HP TRADE:	0880 Glass and Glazing																				
SEC	DESCRIPTION	QTY	UN		UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----					----		----		----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal					w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
Purch. Adjust	Material Escalation for full project duration					✔		413,000		✔		✔		✔		✔		✔		
	Full BIM/VDC Participation					✔		✔		✔		✔		✔		50,000		✔		
	Interior Glazing					9,015,000		5,840,000	N	6,500,000		7,165,000		7,412,000		5,589,000		6,917,000		
	GW01 - GW06 Glass Partitions					✔	41,870	✔	N	w/Above	44,900	✔	47,902	✔		✔		✔		
	RL01 System Gates					w/Glass Handrail	Y	(82,000)		No-Ok		No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Unbought Scope - Proprietary System Detail Coordination					350,000	N	350,000	N	350,000	N	350,000	N	350,000	N	350,000	N	350,000		
	Films on Glass - GF01 (GF03 Removed at 100%)					✔		✔	N	w/Above		✔		✔	N	40,000		✔		
	GL01, GL06, and GL07 Series Glazing					w/Int. Wall Panels		No-Ok	N	w/Above		No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	SSCP Area Fin Wall					✔		390,000	N	w/Above		✔		✔		✔		✔		
	GL03 Glazing integral to GW04 Walls					✔		✔	N	w/Above		✔		✔		✔		✔		
	GL03 Glazing at Millwork					w/Millwork		No-Ok	N	w/Above		No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	MR01 - MR03 Unframed Mirrors					✔		✔	N	w/Above		✔		✔		✔		✔		
	Interior HM Windows - W01, W02, W03, W04					✔		✔	N	w/Above		✔		✔		✔		✔		
08 34 73-3.4B	Field Testing of STC Windows					✔		10,000	N	40,000	N	40,000	N	40,000		40,000	N	40,000		
	Ballistic-Rated Glass at CBP Cashier					Not Shown		No-Ok	N	No-Ok		No-Ok		No-Ok		✔		No-Ok		
	Unbought Scope - CBP Compliance, Testing/Certification					50,000	N	50,000	N	50,000		50,000		50,000	N	50,000	N	50,000		
	Interior Glass Doors, hardware, lites					✔		✔	N	w/Above		✔		✔		✔		✔		
	Automatic Door Operators at Glass Doors (all on HM Openings)					w/Doors Fr HW	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Exterior Glazing					12,008,000		7,918,000		10,415,000		8,200,000		9,302,000		9,999,000		10,379,000		
	Unbought Scope - Window Protection Maintenance & Sequencing	1	LS	120k		120,000	N	120,000	N	120,000	N	120,000	N	120,000	N	120,000	N	120,000		
	Unbought Scope - Field / Chamber Test Addl. Conditions & Locations	1	LS	200k		200,000	N	200,000	N	200,000	N	200,000	N	200,000	N	200,000	N	200,000		
	10 Year Warranty on Exterior Systems					✔		277,000				✔	N	300,000		550,000		✔		
	Heat Soak all glass					✔		392,000	N	750,000	N	750,000	N	750,000	N	750,000	N	750,000		
	Field QC Testing per 08 44 13-3.4 and prep work					✔		✔				✔		✔	N	65,000	N	65,000		
	3rd Party to perform & certify testing					✔		53,000	N	53,000	N	53,000	N	53,000	N	53,000	N	53,000		
AD-A012	Standalone Mockup Curtainwall					✔		✔				✔		✔	N	65,000	N	65,000		
AD-A350	CW01 and CW02 Curtainwall System					✔	53,100 SF	✔		✔	49,300 SF	✔	50,691 SF	✔		✔		✔		
	Louver Integrated Curtainwall System					✔		✔		✔		✔		✔		✔		✔		
C5/AD-A621, E	Downspout stirrups, hangers, brackets					✔		✔				✔		✔		✔		✔		
C5/AD-A621, E	Downspouts - SS Material from Roof to Ground					✔		984,000	N	984,000	N	984,000	N	984,000	N	984,000	N	984,000		
	Downspout boots & tie in to storm					✔		67,000	N	125,000	N	125,000	N	125,000	N	125,000	N	125,000		
AD-A603	Downspouts at Trash Enclosure					w/Roofing	N	No-Ok	N	No-Ok	N	No-Ok		No-Ok	N	No-Ok	N	No-Ok		
	Exterior Glass & Storefront Doors, hardware, lites					✔		✔		✔		✔		✔		✔		✔		
	Slab Edge Firesafing at CW Locations					✔		✔				✔		✔		✔		✔		
	Protection and Cleaning					✔		387,000			N	565,000		✔		588,000	N	588,000		
	----					----		----		----		----		----		----		----		----
	----					----		----		----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal					**21,743,000**		**17,369,000**		**INCOMPLETE**		**18,602,000**		**19,686,000**		**19,618,000**		**20,686,000**		**INCOMPLETE**

03.17

HENSEL PHELPS
Plan. Build. Manage.

GLASS HANDRAIL

Base Bid at a glance:				4,080,000		2,644,000		2,195,000		2,444,000		2,231,000		2,844,000					
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**					
LOCATION:	Tampa, FL																		
OWNER:	Hillsborough County Aviation Authority																		
BID DATE:	Tuesday, November 11, 2025																		
HP TRADE:	0570 Ornamental Metals	*Quantities*																	
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL		
	Bid Amount				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	Bid Bond valid for 120 Days (Bids >$5M)				✔		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.80%	✔	2.25%	✔	1.80%	✔	1.65%	✔	2.50%	✔				
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔	N	107,000				
	SBE Participation / LOIs & FLUCP Certs Provided			21%	✔	10%	Not Included	0%	Not Included	21%	✔	0%	Not Included	0%	Not Included				
	E-Verify Affidavit of Compliance				✔		✔		✔		✔	N	will provide	N	will provide				
	Anti-Trafficking Affidavit				✔		✔		✔		✔	N	will provide	N	will provide				
	HCAA NDA Form				✔		✔		✔		✔	N	will provide	N	will provide				
	Compass Registration Completed				✔		✔		✔		✔	N	will provide	N	will provide				
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		✔	N	will provide		✔				
	----				----		----		----		----		----		----		----		
	----				----		----		----		----		----		----		----		
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔		✔				
05 70 00	**DECORATIVE METAL**				✔		✔		✔		✔	N	w/Below	N	w/Below				
05 73 00	**DECORATIVE METAL RAILINGS**				✔		✔		✔		✔		✔		✔				
05 73 13	**GLAZED DECORATIVE METAL RAILINGS**				✔		✔		✔		✔		✔		✔				
05 73 16	**STRUCTURAL GLASS WALL RAILINGS**				✔		✔		✔		✔		✔		✔				
07 92 00	**JOINT SEALANTS**				✔		✔		✔		✔	N	w/Below	N	w/Below				
~~**10 22 46**~~	~~**CANTILEVER GLASS PARTITION**~~ Removed Addendum 01				w/Glass		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	----				----		----		----		----		----		----		----		

03.17

HENSEL PHELPS
Plan. Build. Manage.

GLASS HANDRAIL

Base Bid at a glance:				4,080,000		2,644,000		2,195,000		2,444,000		2,231,000		2,844,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		
LOCATION:	Tampa, FL															
OWNER:	Hillsborough County Aviation Authority															
BID DATE:	Tuesday, November 11, 2025															
HP TRADE:	0570 Ornamental Metals		*Quantities*													
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	---				---		---		---		---		---		---		---
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	Glass Handrail				3,890,000		2,300,000		2,005,000		2,100,000		1,777,000		2,283,000		
	RL01/RL01A - Glass Railings	2,255	LF		✔		✔		✔		✔		✔		✔		
A5/AD-ID711	SS Shrouds to match guardrail shoe				✔		✔		✔		✔	N	30,000	N	30,000		
E4/AD-ID721	Swinging Gate in RL01 System at Gates	14	EA		✔		✔		✔		✔	N	80,000	N	80,000		
	RL02 - Decorative Stainless Railings	1,800	LF		✔		✔		✔		✔		✔		✔		
	RL03 - Galv. Steel Railings				w/Steel	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	RL04 - Illuminated SS Railing	150	LF		✔		✔		✔		✔		✔		✔		
	GW01 through GW06 Glass Walls				w/Glass	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Escalator Balustrades				✔	N	15,000		✔	N	15,000	N	15,000	N	15,000		
	Unbought Scope - Additional Leading Edge barriers for AHJ				25,000	N	25,000	N	25,000	N	25,000	N	25,000	N	25,000		
	Cleaning and Protection of all glass				✔	N	139,000		✔	N	139,000	N	139,000	N	139,000		
E2/AD-ID720	Unbought Scope - Finish Material / Struct. Substrate Tolerance Reconciliatio	4,055	LF	16	65,000	N	65,000	N	65,000	N	65,000	N	65,000	N	65,000		
	Unbought Scope - Sequencing/Protection at GFRG	800	LF	125	100,000	N	100,000	N	100,000	N	100,000	N	100,000	N	100,000		
	---				---		---		---		---		---		---		---
	---				---		---		---		---		---		---		---
	TOTAL - Bid Item No. 1 - Airside D Terminal				**4,080,000**		**2,644,000**		**2,195,000**		**2,444,000**		**2,231,000**		**2,844,000**		**INCOMPLETE**

03.17

HENSEL PHELPS
Plan. Build. Manage.

GLASS HANDRAIL

Base Bid at a glance:				4,080,000		2,644,000		2,195,000		2,444,000		2,231,000		2,844,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		**Bidder #5**		
LOCATION:	Tampa, FL															
OWNER:	Hillsborough County Aviation Authority															
BID DATE:	Tuesday, November 11, 2025															
HP TRADE:	0570 Ornamental Metals	*Quantities*														
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No Scope in CCBSS for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		-		-		-		INCOMPLETE
	----				----		----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below		
	No Scope in Airside D MT Shuttle Platform for this Bid Package				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----		----
	----				----		----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-		INCOMPLETE
	BASE BID TOTAL				4,080,000		2,644,000		2,195,000		2,444,000		2,231,000		2,844,000		INCOMPLETE

03.12

HENSEL PHELPS
Plan. Build. Manage.

DRYWALL & RELATED

Base Bid at a glance: 25,921,000 | 30,739,000 | 22,350,000 | 25,342,000 | 34,329,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	Tuesday, November 11, 2025
HP TRADE:	0920 Drywall & Related

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	UP	TOTAL
	Bid Amount	*Quantities*			w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔	NO	Not Provided		✔		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.00%	✔	1.47%	✔	1.50%	✔	1.00%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			22%	✔	22%	✔	22%	✔	0%	Not Provided	25%	✔		
	E-Verify Affidavit of Compliance				✔		✔		✔	NO	Not Provided		✔		
	Anti-Trafficking Affidavit				✔		✔		✔	NO	Not Provided		✔		
	HCAA NDA Form				✔		✔		✔	NO	Not Provided		✔		
	Compass Registration Completed				✔		✔		✔	NO	Not Provided		✔		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔		
05 40 00	**COLD-FORMED METAL FRAMING**				✔		✔		✔		✔		✔		
06 10 00	**ROUGH CARPENTRY**				✔		✔		✔		✔		✔		
06 16 00	**SHEATHING**				✔		✔		✔		✔		✔		
06 64 00	**PLASTIC PANELING**				✔		✔		✔		✔		✔		
07 21 00	**THERMAL INSULATION**				✔		✔		✔		✔		✔		
07 84 13	**PENETRATION FIRESTOPPING**				✔		✔		✔		✔		✔		
07 84 43	**JOINT FIRESTOPPING**				✔		✔		✔		✔		✔		
07 92 00	**JOINT SEALANTS**				✔		✔		✔		✔		✔		
07 95 13.13	**INTERIOR EXPANSION JOINT COVER ASSEMBLIES**				✔		✔		✔		✔		✔		
07 95 16	**EXTERIOR EXPANSION JOINT COVER ASSEMBLIES**				✔		✔		✔		✔		✔		
08 11 13	**HOLLOW METAL DOORS AND FRAMES**				✔		✔		✔		✔		✔		
08 11 14	**CBP HOLLOW METAL DOORS AND FRAMES**				✔		✔		✔		✔		✔		
08 31 13	**ACCESS PANELS - Added Addendum 03**				✔		✔		✔		✔		✔		
09 21 16.23	**GYPSUM BOARD SHAFT WALL ASSEMBLIES**				✔		✔		✔		✔		✔		
09 22 16	**NON-STRUCTURAL METAL FRAMING**				✔		✔		✔		✔		✔		
09 24 00	**CEMENT PLASTERING**				✔		✔		✔		✔		✔		
09 25 13.13	**ACRYLIC PLASTER FINISH**				✔		✔		✔		✔		✔		
09 27 13	**GLASS-FIBER REINFORCED PLASTER FABRICATIONS (GFRG)**				✔		✔		✔		✔		✔		
09 29 00	**GYPSUM BOARD**				✔		✔		✔		✔		✔		
09 77 00	**SPECIAL WALL SURFACES**				N/A	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
09 84 33	**SOUND-ABSORBING WALL UNITS**				N/A	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
10 26 41	**BULLET-RESISTANT PANELS**				✔		✔		✔		✔		✔		

HENSEL PHELPS
Plan. Build. Manage.

DRYWALL & RELATED

Base Bid at a glance:					25,921,000		30,739,000		22,350,000		25,342,000		34,329,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**				
LOCATION:	Tampa, FL																
OWNER:	Hillsborough County Aviation Authority																
BID DATE:	Tuesday, November 11, 2025																
HP TRADE:	0920 Drywall & Related	*Quantities*															
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL		
	----				----		----		----		----		----		----		
	----				----		----		----		----		----		----		
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		w/Below		w/Below				
	Material Escalation through 2028				✔		✔		694,000		✔		✔				
	Exterior Framing & Sheathing				3,800,000		3,723,000		1,673,000		2,789,000		6,100,000				
	Unbought Scope - Temporary Enclosure for Climate/Water Intrusion	1	LS	250k	250,000		250,000		250,000		250,000		250,000				
	Delegated Design & Engineering				✔		✔		✔		✔		✔				
AD-A010	WA20-25 / FS01-FS03 - Framing, Sheathing only				✔		✔		✔		✔		✔				
AD-A010	WA20-25 / FS01-FS03 - Hat Channel & Panel Clips				w/Metal Panels	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
AD-A010	WA15-16 - Insulation between CMU Layers				w/Masonry	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
AD-A012	Framing & Sheathing for Mockup Systems				✔		✔		✔		✔		✔				
A1 & A3/AD-ID7	CFMF Supports for GW01/GW03 Systems				Removed at 100%	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
AD-A607	Eave Assembly - Gutter Profile Framing & Sheathing				✔		✔		✔		✔		✔				
	Blocking for Metal Panel Edge / Roof Tie-In				✔		✔	N	175,000	N	175,000		✔				
	Access to High Roof for Gutter Framing				✔		✔		75,000		✔		✔				
	Unbought Scope - Roof Protection/Coordination for Access	1	LS	50k	50,000	N	50,000	N	50,000	N	50,000	N	50,000				
AD-A502	Cement Plaster (Stucco) at Maintenance Platform Walls				✔		✔		✔		✔		✔				
BP #36	Penetration Sealing for Air Barrier Testing (PBB Openings)				✔	N	72,000	N	72,000	N	72,000	N	72,000				
	Interior Partitions & Gypsum Ceilings				15,689,000		19,834,000		14,944,000		15,298,000		23,150,000				
	Unbought Scope - Interior Mock-Up (Airline Lounge Floor, Walls, Clg.)	1	LS	150k	150,000	N	150,000	N	150,000	N	150,000	N	150,000				
	Unbought Scope - Additional Blocking for Art Opportunity	1	LS	18k	18,000	N	18,000	N	18,000	N	18,000	N	18,000				
AD-A013	Interior Partitions - Acoust/Fire/STC Ratings, Secure Mesh per sched				✔		✔		✔		✔		✔				
	100% Update - 16ga minimum studs on all interior				✔		✔		✔		✔		✔				
	Exhibit D Priority Walls - MR Board				✔		✔		✔		✔		✔				
	Bullet-Resistant Board in CBP Spaces				✔		✔		✔		✔		✔				
	High Abuse Resitant Board in BOH Corridors				✔	16,500 SF	✔		✔		✔		✔				
	CL01 - Gypsum Board Ceilings (Rated & Non-Rated)				✔		✔		✔		✔		✔				
	F&I Access Panels per RCPs - 08 31 13 ACD-x Types				✔		✔		✔		✔		✔				
	Install Access Panels furnished by others				✔	N	45,000	N	45,000	N	45,000	N	45,000				
	Furnish scaffolding / own access for all work				✔		✔		✔		685,000		✔				
	Unbought Scope - Maintenance & Modifications to Dancefloor Scaffold				150,000	N	150,000	N	150,000	N	150,000	N	150,000				
	Blocking at Art Opportunity and other areas noted on plans				✔		✔		✔		✔		✔				
	FP01 - Resindeck at Concession Roof & Train Tube Areas				✔		✔		✔		✔		✔				
	PP02 - Plastic Paneling (Janitor Closets)				✔		✔		✔		✔		✔				
	Sheet Metal Cants at Elevator Beams				✔		✔	N	144,000	N	144,000		✔				
	Spray Foam at Door Frames				✔		✔		10,000		10,000		✔				
	Plywood Sheathing for Glass Wall Panels (see Alt. 2 Deduct)				✔		✔	N	47,000		✔		✔				
	Allowance for Addl. Re-finish and Repair Included ($150k)				✔		✔		✔	N	150,000		✔				

03.12

HENSEL PHELPS
Plan. Build. Manage.

DRYWALL & RELATED

				Base Bid at a glance:		25,921,000		30,739,000		22,350,000		25,342,000		34,329,000	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03														
LOCATION:	Tampa, FL					**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**	
OWNER:	Hillsborough County Aviation Authority														
BID DATE:	Tuesday, November 11, 2025														
HP TRADE:	0920 Drywall & Related		*Quantities*												
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	GFRG Fabrications				4,500,000		4,776,000		2,950,000		4,170,000		2,650,000		
	PF01 - Profiles as shown on AD-A764 through AD-A768				✔		✔		✔		✔		✔		
AD-A572	Arch. Forms at Concessions Area				✔		✔		✔		✔		✔		
	Level 5 Finish and prep for painting				✔		✔		✔		✔		✔		
	Discuss: custom molds, rigging & erection, access, diffuser coord.				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**24,607,000**		**29,068,000**		**21,447,000**		**24,156,000**		**32,635,000**		**INCOMPLETE**
									+$5000						

$21,452,000

03.12

HENSEL PHELPS
Plan. Build. Manage.

DRYWALL & RELATED

	Base Bid at a glance:				25,921,000		30,739,000		22,350,000		25,342,000		34,329,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**				
LOCATION:	Tampa, FL																
OWNER:	Hillsborough County Aviation Authority																
BID DATE:	Tuesday, November 11, 2025																
HP TRADE:	0920 Drywall & Related	*Quantities*															
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL		
	---				---		---		---		---		---		---		---
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below				
	Exterior Framing & Sheathing				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	No Scope in CCBSS				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	Interior Partitions & Gypsum Ceilings				860,000		1,220,000		454,000		732,000		1,100,000				
	Unbought Scope - Engineered Ext. Weather Barrier	2,100	SF	30	63,000	N	63,000	N	63,000	N	63,000	N	63,000				
	Unbought Scope - Temp Construction Separation	1	LS	211k	211,000	N	211,000	N	211,000	N	211,000	N	211,000				
	Unbought Scope - Temp Wall Protection Area A/B & Rehab	11,880	SF		37,000	N	37,000	N	37,000	N	37,000	N	37,000				
	Unbought Scope - Misc. Arch. Mods/Repairs	33,145	SF	4.00	133,000	N	133,000	N	133,000	N	133,000	N	133,000				
	All CCBS work at night (10pm-4am)				✔		✔		✔		✔		✔				
	ACT Ceiling Removal and Replacement				w/Acoust. Clg.	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
	Gypsum Ceiling Removal				w/Demolition	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
	Gypsum Ceilings per plan				✔		✔		✔		✔		✔				
	CFMF Modifications for BHS ROW				✔		✔		✔		✔		✔				
	GFRG Fabrications				No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
	No Scope in CCBSS				No-Ok	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok				
	---				---		---		---		---		---		---		---
	---				---		---		---		---		---		---		---
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**1,304,000**		**1,664,000**		**898,000**		**1,176,000**		**1,544,000**		**INCOMPLETE**		
	---				---		---		---		---		---		---		---
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below				
	Exterior Framing & Sheathing				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	No Scope in Airside D MT Shuttle Platform				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	Interior Partitions & Gypsum Ceilings				10,000		7,000		5,000	N	10,000		150,000				
	Alstom Header Mods				✔		✔		✔		✔		✔				
	GFRG Fabrications				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	No Scope in Airside D MT Shuttle Platform				No-Ok		No-Ok		No-Ok		No-Ok		No-Ok				
	---				---		---		---		---		---		---		---
	---				---		---		---		---		---		---		---
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**10,000**		**7,000**		**5,000**		**10,000**		**150,000**		**INCOMPLETE**		
	BASE BID TOTAL				**25,921,000**		**30,739,000**		**22,350,000**		**25,342,000**		**34,329,000**		**INCOMPLETE**		

03.13

HENSEL PHELPS
Plan. Build. Manage.

TERRAZZO

Base Bid at a glance: 6,798,000 | 5,848,000 | 6,140,000 | -

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	Tuesday, November 11, 2025
HP TRADE:	0940 Terrazzo

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	UP	TOTAL
		Quantities									
	Bid Amount				w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		No-Ok		No-Ok		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	1.00%	✔	2.00%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			15%	✔	15%	✔	5%	LOW		
	E-Verify Affidavit of Compliance				✔		✔		✔		
	Anti-Trafficking Affidavit				✔		✔		✔		
	HCAA NDA Form				✔		✔		✔		
	Compass Registration Completed				✔		✔	N	will provide		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		
	----				----		----		----		----
	----				----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		
09 61 43	**VAPOR-CONTROL FLOORING TREATMENT**				✔		✔		✔		
09 66 23	**RESINOUS MATRIX TERRAZZO FLOORING**				✔		✔		✔		
	----				----		----		----		----

03.13

HENSEL PHELPS
Plan. Build. Manage.

TERRAZZO

				Base Bid at a glance:		6,798,000		5,848,000		6,140,000	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03										
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	Tuesday, November 11, 2025										
HP TRADE:	0940 Terrazzo		*Quantities*		**HPCC**		**Bidder #1**		**Bidder #2**		
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----
	Bid Item No. 1 - Airside D Terminal				w/Below		w/Below		w/Below		
	Terrazzo				4,552,000		3,595,000		3,284,000		
	Unbought Scope - Floor Leveling QA (1/2" thk)	104,000	SF	12.00	1,248,000		1,248,000		1,248,000		
	Unbought Scope - Improved Floor Protection at Strategic Areas	104,000	SF	6.00	624,000		624,000		624,000		
	Unbought Scope - Concrete Moisture Mitigation	104,000	SF	3.35	348,000		348,000		348,000		
	Unbought Scope Budget - Escalator Transitions	8	EA	2,000	16,000		16,000		16,000		
	TR 01-07 - Master Terrazzo Flooring				✔	103,021	✔	103,650	✔		
	Finish to extend under column covers, planters, millwork, etc.				✔		✔		✔		
	Elevator Cab Floors				✔		✔		✔		
	Transition strips at all terrazzo/other finish interface				✔		✔		✔		
	Crack Suppression - 100% Coverage				✔		✔	N	345,000		
	Temp. Power over 110V - provide own generators				✔		✔		✔		
	TR 08A - Stair Treads (Sterile Corridor Stairs)				✔		✔		✔		
	TR 08B - Stair Treads (FIS Exit)				✔		✔		✔		
	Abrasive Nosings at Stair Treads				✔		✔		✔		
	Grouting and Caulking of Stair Treads				✔		✔		✔		
	All Supervision per Bid Package				✔		✔	N	255,000		
	MT01 Metal Base				w/Orn. Metals	N	No-Ok	N	No-Ok		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**6,788,000**		**5,831,000**		**6,120,000**		**INCOMPLETE**
							+$17,000				
							$5,848,000				

03.13

HENSEL PHELPS
Plan. Build. Manage.

TERRAZZO

				Base Bid at a glance:		6,798,000		5,848,000		6,140,000	
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03										
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	Tuesday, November 11, 2025										
HP TRADE:	0940 Terrazzo		*Quantities*								
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				No-Ok		No-Ok		No-Ok		
	No Scope in CCBSS				No-Ok		No-Ok		No-Ok		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**-**		**-**		**-**		**INCOMPLETE**
	----				----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		
	Terrazzo				10,000		17,000		20,000		
	Infill areas around existing blockouts				✔		✔		✔		
	Infill at Floor Door				✔		✔		✔		
SP-D-A120N	Sawcut, remove, modify existing terrazzo				✔		✔		✔		
	----				----		----		----		----
	----				----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**10,000**		**17,000**		**20,000**		**INCOMPLETE**
	BASE BID TOTAL				**6,798,000**		**5,848,000**		**6,140,000**		**INCOMPLETE**

03.11

HENSEL PHELPS
Plan. Build. Manage.

ACOUSTICAL CEILINGS

Base Bid at a glance:				8,076,000		6,683,000		7,388,000		8,270,000		7,883,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		
LOCATION:	Tampa, FL													
OWNER:	Hillsborough County Aviation Authority													
BID DATE:	Tuesday, November 11, 2025													
HP TRADE:	0951 Acoustical Ceilings	*Quantities*												
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		will provide	N	Not Provided		✔	N	Not Provided		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	2.00%	✔	1.50%	✔	1.47%	✔	2.25%	✔		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			18%	✔	18%	✔	0%	NONE	18%	✔	18%	✔		
	E-Verify Affidavit of Compliance				✔		✔	N	will provide		✔		✔		
	Anti-Trafficking Affidavit				✔		✔	N	will provide		✔		✔		
	HCAA NDA Form				✔		✔	N	will provide		✔		✔		
	Compass Registration Completed				✔		✔		✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔		✔		✔		
09 51 13	**ACOUSTICAL PANEL CEILINGS**				✔		✔		✔		✔		✔		
09 51 33	**ACOUSTICAL METAL PAN CEILINGS**				✔		✔		✔		✔		✔		
09 54 23	**LINEAR METAL CEILINGS**				✔		✔		✔		✔		✔		
09 54 26	**SUSPENDED WOOD CEILINGS**				✔		✔		✔		✔		✔		
09 84 36	**SOUND-ABSORBING CEILING UNITS**				None Found		✔		No-Ok		No-Ok		✔		
	----				----		----		----		----		----		----

03.11

HENSEL PHELPS
Plan. Build. Manage.

ACOUSTICAL CEILINGS

Base Bid at a glance: 8,076,000 | 6,683,000 | 7,388,000 | 8,270,000 | 7,883,000

PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03
LOCATION:	Tampa, FL
OWNER:	Hillsborough County Aviation Authority
BID DATE:	Tuesday, November 11, 2025
HP TRADE:	0951 Acoustical Ceilings

SEC	DESCRIPTION	QTY	UN	HPCC UP	HPCC TOTAL	Bidder #1 UP	Bidder #1 TOTAL	Bidder #2 UP	Bidder #2 TOTAL	Bidder #3 UP	Bidder #3 TOTAL	Bidder #4 UP	Bidder #4 TOTAL	UP	TOTAL
		Quantities													
	----				----		----		----		----		----		----
	Bid Item No. 1 - Airside D Terminal				6,997,000		w/Below		w/Below		w/Below		w/Below		
	CL01 Gypsum Ceilings				w/Drywall	N	No-Ok	N	No-Ok	N	No-Ok	N	No-Ok		
	Furnish scaffolding / own access for all work				✔		✔		✔		✔		1,015,000		
	Composite Cleanup Crew				✔		✔	N	61,000		✔		61,000		
	BIM/VDC Compliance Full				✔		✔		✔		✔	N	75,000		
	No attic stock requirement in spec				✔		✔		✔		✔		✔		
	Acoustical Panel Ceilings				✔		2,832,000		w/Below		w/Below		w/Below		
	CL02 - 24x72 Acoustical				✔		✔	51,112 S	642,000		717,000		430,000		
	CL03 - 24x24 Acoustical				✔		✔	42,228 S	309,000		446,000		286,000		
	CL05-A - 24x60 Acoustical				✔		✔	182,712	1,591,000		1,387,000		124,000		
	CL05-B - 24x60 Acoustical Faceted				✔		✔	-	w/Above		272,000		1,094,000		
	CL06 - 48x72 Acoustical - Removed 100%				REMOVED		No-Ok	-	No-Ok		No-Ok	N	No-Ok		
$$$	Ceiling Framing Subsytem due to beam spacing (095113-3.3B-7)				✔		✔	N	395,000		✔		✔		
HNTB Set	No transition details - CL05 to Gyp. To CL05 (discuss assumption)				✔		✔		✔		✔		✔		
RFIs	Unbought Scope - Ceiling Elevation Transition Coordination	1,200	LF	65	78,000		78,000		78,000		78,000		78,000		
	Acoustical Metal Pan Ceilings				✔		1,297,000		w/Below		w/Below		w/Below		
	CL07 - 24x60 Torsion Spring Metal				✔		✔	30,852 S	1,219,000		1,933,000		1,498,000		
	Linear Metal Ceilings				✔		✔		✔		✔		w/Below		
$$$	Trim/Transition Pieces from ACT to Gyp. Ceilings				✔		✔	N	512,000		✔		512,000		
A-570 & F1/A57	Cont. Curved LG Perf. Metal - Arch Forms perimeter				✔		✔		✔		✔	N	w/Above		
G3-C1/ID773	Standard Axiom vs Curved, Light Cove Trims at Columns ("Typ")				✔		✔		✔		✔	N	w/Above		
	Suspended Wood Ceilings				✔		w/Below		w/Below		w/Below		w/Below		
	CL04 - Wood Veneered Grille Panels (SSCP)				✔		1,479,000	16, 930 S	1,579,000		2,156,000		1,404,000		
$$$	Custom Wood Veneer "TBD" on Finish Legend - Ash/Poplar/**Red Oak**/Walnut				✔		✔		✔		✔		✔		
AD-A760	Utility Trough Metal piece				✔		✔	N	375,000		✔		375,000		
	Sound-Absorbing Ceiling Units				✔		6,000		w/Above		✔		w/Above		
	None Found				✔		✔		✔		✔		✔		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**7,075,000**		**5,692,000**		**6,761,000**		**6,989,000**		**6,952,000**		**INCOMPLETE**

03.11

HENSEL PHELPS
Plan. Build. Manage.

ACOUSTICAL CEILINGS

Base Bid at a glance:				8,076,000		6,683,000		7,388,000		8,270,000		7,883,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**		
LOCATION:	Tampa, FL													
OWNER:	Hillsborough County Aviation Authority													
BID DATE:	Tuesday, November 11, 2025													
HP TRADE:	0951 Acoustical Ceilings	*Quantities*												
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below		w/Below		w/Below		w/Below		w/Below		
	Acoustical Panel Ceilings				667,000		657,000		293,000		947,000		597,000		
	Night Work for all CCBS				✔		✔		✔		✔		✔		
MT-A223-228	AT-1 Ceilings Existing to Remain				✔		✔		✔		✔		✔		
	Removal and Storage of Existing ACT Ceilings				✔		✔		✔		✔		✔		
	Demo Ceiling Grid				w/Demo	N	No-Ok	N	No-Ok	N	No-Ok		No-Ok		
	F&I Ceiling Grid Modifications (New MEP, BHS, etc.)				✔		✔		✔		✔		✔		
	Allowance - MEP Relocation Coordination	42,000	GSF	3.50	147,000		147,000		147,000		147,000		147,000		
	Allowance - Owner Contractor / Tenant Coordination	42,000	GSF	1.00	42,000		42,000		42,000		42,000		42,000		
	Install New Ceiling Systems - CL-01				✔		✔		✔		✔		✔		
	Furnish New Ceiling Tiles (ACT & Metal) for Replacement				w/Below		w/Below		w/Below		w/Below		w/Below		
	Allowance - Replace Damaged Metal Ceilings	1,267	SF	95	120,000	14,000 S	120,000		120,000		120,000		120,000		
	Allowance - Replace Damaged ACT Ceilings	2,095	SF	12	25,000	28,000 S	25,000		25,000		25,000		25,000		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**1,001,000**		**991,000**		**627,000**		**1,281,000**		**931,000**		**INCOMPLETE**
	----				----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below		w/Below		w/Below		
	No Scope in Airside D MT Shuttle Platform for this Bid Package				✔		No-Ok		No-Ok		No-Ok		No-Ok		
	----				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**-**		**-**		**-**		**-**		**-**		**INCOMPLETE**
	BASE BID TOTAL				**8,076,000**		**6,683,000**		**7,388,000**		**8,270,000**		**7,883,000**		**INCOMPLETE**

03.14

HENSEL PHELPS
Plan. Build. Manage.

Elevators & Escalators

Base Bid at a glance:					10,666,000		8,669,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**			
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	10/09/2025										
HP TRADE:	1420 Elevators	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		**DISQUALIFIED**		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		Not Compliant		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)				✔	1.00%	✔				
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔				
	SBE Participation / LOIs & FLUCP Certs Provided-Apx K			3%	✔	5%	✔				
	E-Verify Affidavit of Compliance				✔		✔				
	Anti-Trafficking Affidavit				✔		✔				
	HCAA NDA Form				✔		✔				
	Compass Registration Completed				✔		✔				
	Bid Package Addenda Acknowledged - #01 through #05				✔		✔				
	---				---		---		---		---
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔				
Division 14	**Conveying Equipment (Complete)**				✔		✔				
Division 26	**Electrical (As applies)**				✔		✔				
Division 27	**Communications (As applies)**				✔		✔				
	---				---		---		---		---
	Staffing per bid Package				✔		✔				

03.14

HENSEL PHELPS
Plan. Build. Manage.

Elevators & Escalators

	Base Bid at a glance:				10,666,000		8,669,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	10/09/2025										
HP TRADE:	1420 Elevators	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Composite Crew				✔		200,000		----		---
	Lift Net Monitoring wiring- furnish and install				✔		✔				
	Temporary Storage				✔		280,000				
15 Total	**Bid Item No. 1 - Airside D Terminal**				w/Below		w/Below				
AD-A541-550	***Elevators-***				7,854,000		5,400,000				
AD-A784	***Service Elevator (01,04,05,08)-20 stops***	4	ea		✔		✔				
	Steel pipe handrail				✔		✔				
	Passenger (06,07,09,10,11)-25 stops	5	ea		✔		✔				
AD-A780	Cab Finishes/Special Call Buttons/Hall Lanterns				✔		✔				
	Passenger (12,13,14,15)-Club-12 stops	4	ea		✔		✔				
	Finishes			No	by/Future Tenant		No-Ok				
	Freight (02,03)-9 stops	2	ea		✔		✔				
AD-A783	*Stainless steel diamond plate floor*				✔		✔				
	All Elevators				----		----				
	Electrical Power, Phone, Comm, Lighting from elevator controller				✔		✔				
	Casings, Rails, motors, etc.				✔		✔				
	Msc Steel/Structural Steel supports not shown				✔		✔				
	Elevator/Hoistway Protection				✔		✔				
	Threshold header				✔		✔				
14 21 23	Video/Audio Management System Design				✔		300,000				
	Temporary Work Platform				✔		75,000				
	Safety Barricades				✔		✔				
	LiftNet Represenative for commissioning				No-Ok		No-Ok				
AD-A541/542	***Escalators- 2***				1,380,000		982,000				
AD-A786	Casings, Rails, motors, etc.				✔		✔				
	Msc Steel/Structural Steel supports not shown				✔		✔				
	Escalator Protection				✔		✔				
AD-ID507	Anti-Slide Devices				✔		✔				
	Power to Conveying Systems' control panels			No	w/Electrical		No-Ok				
	Low voltage systems to Conveying Systems' control panels			No	w/Electrical		No-Ok				
	Sealant and/or firesafing			No	w/Electrical		No-Ok				
	Grouting of Elevator Sills			No	w/Concrete		No-Ok				
	Furnish & Install Hoistway divider screen			No	w/Steel		No-Ok				
	Furnish & Install hoist beams, divider beams, and pit ladders			No	w/Steel		No-Ok				
	Sump pumps at elevator / escalator pits			No	w/Plumbing		No-Ok				
	Sump pit frames and covers			No	w/Steel		No-Ok				
	Furnish and install Terrazzo Tile Flooring			No	w/Terrazo		No-Ok				
ID-9115B	Transitions from Concrete to Esclator			No	w/Terrazo		No-Ok				

03.14

HENSEL PHELPS
Plan. Build. Manage.

Elevators & Escalators

	Base Bid at a glance:				10,666,000		8,669,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	10/09/2025										
HP TRADE:	1420 Elevators	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
ID327-F1/ID507	Cladding of Esclators-Brushed Stainless Steel				250,000		250,000				
	Elevator Operator during construction	110	MO		880,000		880,000				
ID921 Note I	Elevator Usage/Warranty during construction	110	MO		220,000		220,000				
	Elevator usage reinspection	5	ea		17,500		17,500				
	Elevator Opening Protection for construction	32	SP		64,000		64,000				---
	---				---		---		---		---
	TOTAL - Bid Item No. 1 - Airside D Terminal				**10,666,000**		**8,669,000**		**INCOMPLETE**		**INCOMPLETE**

03.14

HENSEL PHELPS
Plan. Build. Manage.

Elevators & Escalators

	Base Bid at a glance:				10,666,000		8,669,000				
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**		
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	10/09/2025										
HP TRADE:	1420 Elevators	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	---				---		---		---		---
	Bid Item No. 2 - Baggage Handling System Upgrade				---		---		---		
	No Scope in CCBS for this bid package				No-Ok		No-Ok		No-Ok		---
	---				---		---		---		---
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				-		-		-		**INCOMPLETE**
	---				---		---		---		---
	Bid Item No. 3 - Airside D MT Shuttle Platform				---		---		---		
	No Scope in Shuttle Platform for this bid package				No-Ok		No-Ok		No-Ok		---
	---				---		---		---		---
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		**INCOMPLETE**
	BASE BID TOTAL				**10,666,000**		**8,669,000**		**INCOMPLETE**		**INCOMPLETE**

03.15

HENSEL PHELPS
Plan. Build. Manage.

Fire Protection

Base Bid at a glance:				8,799,000						6,148,000		18,454,000			
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**		**Bidder #3**		**Bidder #4**			
LOCATION:	Tampa, FL														
OWNER:	Hillsborough County Aviation Authority														
BID DATE:	10/09/2025														
HP TRADE:	2100 Fire Protection	*Quantities*													
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		**DISQUALIFIED**		**DISQUALIFIED**		w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		**INCOMPLETE**		**INCOMPLETE**		✔		✔		
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)				✔		Not Provided		Not Bondable	2.00%	✔	1.50%	(280,000)		
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔		✔		✔		
	SBE Participation / LOIs & FLUCP Certs Provided			20%	✔		Not Provided	100%	✔	20%	✔	20%	✔		
	E-Verify Affidavit of Compliance-P				✔		Not Provided		✔		✔		✔		
	Anti-Trafficking Affidavit-Q				✔		Not Provided		✔		✔		✔		
	HCAA NDA Form-R				✔		Not Provided		✔		✔		✔		
	Appendix K				✔		Not Provided		✔		✔		✔		
	Compass Registration Completed				✔		Not Provided		✔		✔		✔		
	Bid Package Addenda Acknowledged - #01 through #06				✔		Not Provided		✔		✔		✔		
	Composit Crew				✔						✔		✔		
	Staffing Per Bid Package				✔						✔		✔		
	----				----		----		----		----		----		----
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔						✔		✔		
Division 21	**Fire Suppression (Complete)**				✔						✔		✔		
07 84 13	**Penetration Firestopping**				✔						✔		✔		
	Bid Item No. 1 - Airside D Terminal				8,122,000						w/Below		w/Below		
	Sprinklers				✔						4,763,000		14,246,000		
	16 Wet pipe sprinkler Systems				✔						✔		✔		
	Prepack System				✔						159,000		150,000		
AD-FP110	3 Pre Action Risers				✔						✔		✔		
	Fire pump complete w/VFD 100psi				✔						✔		✔		
21.31.13- 2.8	Remote alarm panel for Fire Pump				✔						✔		✔		
	Permitting				✔						✔		✔		
	Schedule 40 Pipe per RFI				✔						✔		✔		
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 1 - Airside D Terminal				**8,122,000**		**INCOMPLETE**		**INCOMPLETE**		**4,922,000**		**14,116,000**		**INCOMPLETE**

03.15

HENSEL PHELPS
Plan. Build. Manage.

Fire Protection

Base Bid at a glance:				8,799,000				6,148,000	18,454,000		
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**	**Bidder #3**	**Bidder #4**	
LOCATION:	Tampa, FL										
OWNER:	Hillsborough County Aviation Authority										
BID DATE:	10/09/2025										
HP TRADE:	2100 Fire Protection	*Quantities*									
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----		----		----		----
	Bid Item No. 2 - Baggage Handling System Upgrade				w/Below						w/Below		w/Below		
	Screening System Demolition				114,000						140,000		262,000		
MT-D-A111/Nt8	Demo and Reinstall Sprinkler Heads Exisiting in same location				✔						✔		✔		
MT-D-FP111/M	Demo and Reinstall Sprinkler Pipe				✔						✔		✔		
	Screening System New Work				508,000						1,031,000		4,021,000		
MT-FP111C	New Fire Sprinkler System				✔						✔		✔		
	Night work				✔						✔		✔		
	Fire Sprinkler Systems Relocation for Interferences	0			22,000						22,000		22,000		
	Fire Sprinkler Systems Relocation for Temp Fire Protection				33,000						33,000		33,000		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 2 - Baggage Handling System Upgrade				**677,000**		**INCOMPLETE**		**INCOMPLETE**		**1,226,000**		**4,338,000**		**INCOMPLETE**
	----				----		----		----		----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				N/A		N/A		N/A		N/A		N/A		N/A
	No work in Shuttle Platform for this scope of work				----		----		----		----		----		----
	----				----		----		----		----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				-		-		-		-		-		-
	BASE BID TOTAL				**8,799,000**		**INCOMPLETE**		**INCOMPLETE**		**6,148,000**		**18,454,000**		**INCOMPLETE**

00

HENSEL PHELPS
Plan. Build. Manage.

Sitework

Base Bid at a glance:				16,560,000		21,563,000		22,958,000
PROJECT: TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**
LOCATION: Tampa, FL								
OWNER: Hillsborough County Aviation Authority								
BID DATE: 10/09/2025								
HP TRADE:		*Quantities*						
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Amount				w/Below		w/Below		w/Below
	Bid Bond valid for 120 Days (Bids >$5M)				✔		✔		✔
	Payment & Performance Bond Rate / Surety Letter (Bids >$100k)			1.5%	✔	0.65	✔	0.50	✔
	Sales Tax Included (Hillsborough - 7.5%)				✔		✔		✔
	SBE Participation / LOIs & FLUCP Certs Provided			19%	✔	19%	✔	19%	✔
	E-Verify Affidavit of Compliance				✔		✔		✔
	Anti-Trafficking Affidavit				✔		✔		✔
	HCAA NDA Form				✔		✔		✔
	Bid Package Addenda Acknowledged				✔		✔		✔
	Compass Registration				✔		✔		✔
DIV 00 & 01	**GEN CONDITIONS & REQUIREMENTS**				✔		✔		✔
02 41 19	**SELECTIVE DEMOLITION (AS APPLIES)**				✔		✔		✔
03 30 00	**CAST-IN-PLACE CONCRETE (AS APPLIES)**				✔		✔		✔
21 11 00	**FACILITY FIRE-SUPRESSION WATER-SERVICE PIPING (AS APPLIES)**				✔		✔		✔
21 12 00	**FIRE SUPRESSION STANDPIPES (AS APPLIES)**				✔		✔		✔
31 05 10	**SITE PREPARATION (COMPLETE)**				✔		✔		✔
31 20 00	**EARTH MOVING (COMPLETE)**				✔		✔		✔
31 23 19	**DEWATERING (COMPLETE)**				✔		✔		✔
31 23 33	**TRENCHING AND BACKFILLING (COMPLETE)**				✔		✔		✔
31 41 16	**STEEL SHEET PILING (COMPLETE)**				✔		✔		✔
32 12 16	**ASPHALT PAVING (COMPLETE)**				✔		✔		✔
32 13 13	**CONCRETE PAVING (COMPLETE)**				✔		✔		✔
32 16 13	**CONCRETE CURBS AND GUTTERS (COMPLETE)**				✔		✔		✔
32 16 23	**SIDEWALKS (COMPLETE)**				✔		✔		✔
32 17 23	**PAVEMENT MARKINGS (COMPLETE)**				✔		✔		✔
33 05 00	**COMMON WORK RESULTS FOR UTILITIES (COMPLETE)**				✔		✔		✔
33 14 13	**WATER MAIN (COMPLETE)**				✔		✔		✔
33 31 11	**SANITARY SEWER (COMPLETE)**				✔		✔		✔
33 41 00	**STORM UTILITY DRAINAGE PIPING (COMPLETE)**				✔		✔		✔
33 49 00	**DRAINAGE STRUCTURES (COMPLETE)**				✔		✔		✔
34 71 13	**VEHICLE BARRIERS (COMPLETE)**				✔		✔		✔
	Bid Item No. 1 - Airside D Terminal				14,447,000		✔		✔

00

HENSEL PHELPS
Plan. Build. Manage.

Sitework

Base Bid at a glance:				16,560,000		21,563,000		22,958,000
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**
LOCATION:	Tampa, FL							
OWNER:	Hillsborough County Aviation Authority							
BID DATE:	10/09/2025							
HP TRADE:		*Quantities*						
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	Bid Item No. 1 - Blue Zone				✔		9,212,000		9,208,000
	Bid Item No. 1 - Yellow Zone				✔		10,475,000		11,874,000
	Earthwork				✔		✔		✔
	Dewatering				✔		✔		✔
	SWPPP Setup & Maintenance				✔		✔		✔
	Roadway Excavation & Grading				✔		✔		✔
	Top Soil & Fine Grading after removal of Excellence Drive, George Bean, Bessie Coleman				✔		✔		✔
AD-CD101-105	***Demolition***				✔		✔		✔
	Asphalt Demo - Bessie Coleman & Old Airside Entrance				✔		✔		✔
AD-C111	Crossover Demo				✔		✔		✔
	Concrete Paving Demo - Curb and Sidewalk				✔		✔		✔
	Fencing Demo				✔		✔		✔
	Demo underground structures - Truck Dock & Bessie Coleman				✔		✔		✔
	Signage Demo				✔		✔		✔
	Tree Demo				✔		✔		✔
AD-CD104-105	Demo Excellence Drive - Asphalt, Curb, Sidewalks, Fence				✔		✔		✔
	Curb & Gutter after George Bean Crosover Removal				✔		✔		✔
	Landscaping				✔		✔		✔
AD-C110	Sod Bessie Coleman and Excellence Dr				✔		✔		✔
	Utilities				✔		✔		✔
	Sewer				✔		✔		✔
	Water				✔		✔		✔
	Fire Line & Risers				✔		✔		✔
	Storm				✔		✔		✔
	Grease Traps	4	ea	No	w/ Plumbing		No-Ok		No-Ok
	Oil-Water Seperator	1	ea	No	w/ Plumbing		No-Ok		No-Ok
	Backflows for fire and water				✔		✔		✔
	Hydrants				✔		✔		✔
AD-CU105	Replace Existing Sewer line				✔		✔		✔
	Trench Drains				✔		✔		✔
	Concrete				✔		✔		✔
B2/AD-CP511	Gravity Wall				✔		✔		✔
AD-CP101	Truck Court Pads				✔		✔		✔
AD-CP101	2X2 Gate Arm Pads				✔		✔		✔
AD-CP101	Electrical Equipment Pads on top of transformer & generator pads				✔		✔		✔
AD-CP111	Truck Court Paving & Base				✔		✔		✔
	All curb and gutter				✔		✔		✔

00

HENSEL PHELPS
Plan. Build. Manage.

Sitework

Base Bid at a glance:				16,560,000		21,563,000		22,958,000
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03			**HPCC**		**Bidder #1**		**Bidder #2**
LOCATION:	Tampa, FL							
OWNER:	Hillsborough County Aviation Authority							
BID DATE:	10/09/2025							
HP TRADE:		*Quantities*						
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	4" & 6" Sidewalks				✔		✔		✔
AD-C111	Curb & Gutter @ George Bean after crossover removal				✔		✔		✔
AD-CP111	Trash Compactor Embeds @ trash compactor install only				✔		✔		✔
AD-S705	VDGS Foundations				✔		✔		✔
AD-CP101	Concrete Ramps				✔		✔		✔
	Dumpster Enclosure Foundation & Pad				✔		✔		✔
	Asphalt Paving				✔		✔		✔
	Asphalt Paving and Base				✔		✔		✔
	Asphalt Resurfacing				✔		✔		✔
AD-CM101	Striping				✔		✔		✔
	Signage				✔		✔		✔
	Parking Bumpers & Parking Stalls				✔		✔		✔
	Sitework Not Defined Above				✔		✔		✔
AD-A102	Premanufactured guardrail	2	ea		✔		✔		✔
INCL. #14	Install, maintain, remove crane road				✔		✔		✔
	Fencing			No	W/ Fencing	No	No-Ok	No	No-Ok
	VDC per Exhibit E				✔		✔		✔
Incl. 11	Dust Control				✔		✔		✔
	Truck Court Bollards & Removable Bollards				✔		✔		✔
	Full Time QC Manager				✔		✔		✔
	Full Time Safety Manager				✔		✔		✔
	Full Time Superintendent				✔		✔		✔
	Full Time Project Manager				✔		✔		✔
	Unbought Scope				✔		✔		✔
	Vac Truck Excavation				250,000		25,000		25,000
	SWPPP Maintenance & Relocations During Site Contractor Demob				72,000		72,000		72,000
	Curb, Gutter, Repair/Replace				15,000		2,500		2,500
	Landscape Area - Tree/Shrub/Grass/Irrigation Restablishment				75,000		75,000		75,000
	Municipal Comments on Utility Lines				1,000,000		1,000,000		1,000,000
	GSE Markings Floor Striping				22,000		22,000		22,000
	Bulletin 2 FDC Add				12,000		12,000		12,000
	VDGS Poles	16	ea		144,000		144,000		144,000
	Gradation & cleaning of existing stockpile material				200,000		200,000		200,000
	12 mnths SWPPP Maint.	12	mnth		60,000		60,000		60,000
	Reinforced Concrete Slab - Oil-Water Seperator	1	ea		73,000		73,000		73,000
	Grease Trap Bearing Pads	4	ea		190,000		190,000		190,000
	TOTAL - Bid Item No. 1 - Airside D Terminal				**16,560,000**		**21,563,000**		**22,958,000**

00

HENSEL PHELPS
Plan. Build. Manage.

Sitework

	Base Bid at a glance:				16,560,000		21,563,000		22,958,000
PROJECT:	TPA Airside D & Centralized Checked Baggage - Bid Package 03				**HPCC**		**Bidder #1**		**Bidder #2**
LOCATION:	Tampa, FL								
OWNER:	Hillsborough County Aviation Authority								
BID DATE:	10/09/2025								
HP TRADE:			*Quantities*						
SEC	DESCRIPTION	QTY	UN	UP	TOTAL	UP	TOTAL	UP	TOTAL
	----				----		----		----
	Bid Item No. 2 - Centralized Checked Baggage System				w/Below		w/Below		w/Below
	Subtotal Sitework				✔		✔		✔
	Scope of Work				✔		✔		✔
	----				----		----		----
	----				----		----		----
	TOTAL - Bid Item No. 2 - Centralized Checked Baggage System				**-**		**-**		**-**
	----				----		----		----
	Bid Item No. 3 - Airside D MT Shuttle Platform				w/Below		w/Below		w/Below
	Subtotal Sitework				✔		✔		✔
	Scope of Work				✔		✔		✔
	----				----		----		----
	----				----		----		----
	TOTAL - Bid Item No. 3 - Airside D MT Shuttle Platform				**-**		**-**		**-**
	BASE BID TOTAL				**16,560,000**		**21,563,000**		**22,958,000**

HNTB

Construction Administration Services

Nothing contained in the back up information, quotations or other documents attached to this Supplemental C package between Hensel Phelps and HCAA alters the terms and conditions of the Part 2 Contract between Design Builder and the Owner. The back up information, quotations and other documents are attached to this Supplemental C package for information only.

Tampa International Airport
Airside D Terminal - 8500 23 ASD
8515 24 CCBS
Construction Administration Services – Part 2C

January 21, 2026

RE: Construction Administration Services – Part 2C Scope and Fee Proposal v3

General Scope of Work:
At the request of Hensel Phelps (HP) and HCAA, HNTB and our associated design consultants are providing a written Scope and Fee Proposal to perform Construction Administration Services for construction associated with the completion of ASD and CCBS project elements from February 2026 to July 2029.

Detailed Description of Scope of Services:
The CA scope (CA Services) includes the following items:

1. Bulletin development and coordination associated with revisions required by Hensel Phelps. This does not include bulletins required for added or revised scope required by the Owner.
2. Meetings and Coordination
3. Continuation of Tag and Trace Services (See Part 2B)
4. Airsides Airline Relocation Tenant Improvement Design Services
5. Review and respond to RFIs and RFS (request for substitution)
6. Review and process submittals, including shop drawings, products data or samples
7. Attend weekly construction meetings (CA meeting, OAC meeting, MEP coordination meeting)
8. Interpret, review, evaluate, and update contract documents
9. Concessionaire Design Submission Reviews (30%, 60%, 90%) for up to 11 Concessions.
10. Mezzanine Lounge Design Submission Reviews (30%, 60%, 90%) for up to 2 Clubs
11. Site Observation Services
12. Punchlist Services
13. Closeout Services (4 months)

Exclusions and Clarifications:
1. CA Services for the 'Horizontal Pool' LED Display Panels is excluded. Once the final design is completed, HNTB will submit a proposal to provide Additional CA Services for the 'Horizontal Pool' LED Display Panels.
2. CA Services for the Concourses A & C CBIS scope is excluded. Once the final design is completed, HNTB will submit a proposal to provide Additional CA Services for the Concourses A & C CBIS scope.
3. CA Services for the Airside E BHS Optimization scope is excluded.
4. CA Services for the Airsides Airline Relocation Tenant Improvement scope has been included as an Owners Allowance. Once the final design is completed, HNTB will submit a fee proposal to

For information only. Not a contract document

provide CA Services for the Airsides Airline Relocation Tenant Improvement scopes to reconcile the allowance.

5. CA Services before February 2026 and after July 2029 are excluded. If HP requires CA Services outside of this period, HNTB will submit a proposal to provide Additional CA Services.
6. Any geotechnical services that are not "review and response" to RFIs or inquiries related to design plans and analysis of contractor provided supplementary field investigations and contamination services is excluded. If HP requires any other geotechnical services, HNTB shall provide a proposal to provide Additional CA Services for such geotechnical services.
7. Concession/Lounge Reviews Exclusions:
    a. · Review of 100% design submission
    b. · Review for code compliance
    c. · Review of PAL 3 tenant areas
    d. · Meetings with Concessionaires/Lounge Tenants
    e. · Meeting minutes
    f. · Review of Concessions/Lounge back of house areas (BOH), including offices, loading dock design and exterior storage design
    g. · Coordination with building design and modifications to Interior Architecture documents
8. PE stamping/sealing any BHSC drawings is excluded.

Disciplines/Firms Involved:

Discipline/Firm	General Scope
HNTB Architecture	CA for the noted design packages – ASD, CCBS, Project Management and Administration of the CA services
HNTB Structures	CA of structural elements of the noted design packages – ASD and CCBS
HNTB Civil	CA of civil elements of the noted design packages – ASD
BASE Consultants, Inc.	CA of structural elements of the noted design packages – ASD and CCBS
BNP Associates, Inc.	CA of baggage handling system elements of the noted design packages - ASD and CCBS. Including full-time, on-site engineer.
Brindley Pieters & Associates, Inc.	CA of civil and utilities elements of the noted design packages – ASD
Gartek Engineering Corporation	CA of public address system elements of the noted design packages – ASD
Gensler	CA of architectural interior elements of the noted design packages – ASD
ECS	CA of moisture and curtainwall protection elements of the noted design packages – ASD

For information only. Not a contract document

Discipline/Firm	General Scope
HLB Lighting Design, Inc.	CA of architectural lighting elements of the noted design packages – ASD
Jensen Hughes, Inc.	CA of code compliance and life safety elements of the noted design packages – ASD
Tierra, Inc.	CA of geotechnical analysis and design elements and contamination services of the noted design packages – ASD
TLC Engineering Solutions, Inc.	CA for mechanical, plumbing, fire protection and low voltage elements of the noted design packages - ASD and CCBS.
Voltair Consulting Engineers, Inc.	CA of electrical elements of the noted design packages - ASD and CCBS.

Schedule:
CA Services for each construction package shall commence upon issuance of the Notice to Proceed. Should CA Services exceed July 2029, additional services may be requested.

- NTP: February 2026
- Substantial Completion: April 2029 (38 months)
- Final Completion: June 2029
- Closeout End: November 2029

Proposed Fee Summary:
The following is our estimated Fee Proposal for each construction package. The design team will monitor the fee and notify HP in advance if the estimated fee is anticipated to exceed the amount indicated herein. See attached documents for a more detailed description of scope and fee.

HNTB Part 2C HP Supp C	Construction Package	Labor	Reimbursables	Total
	ASD - Airside D Terminal	$ 19,315,970	$ 824,376	$ 20,140,345
	CCBS - Centralized Checked Baggage System	$ 6,456,850	$ 559,694	$ 7,016,544
	Totals	**$ 25,772,820**	**$ 1,384,070**	**$ 27,156,889**

Attached Exhibits:
Exhibit A – ASD Element Fee Detail
Exhibit B – CCBS Element Fee Detail

SBE = $3,201,192

Sincerely,

Scott Steckler, VP – HNTB

For information only. Not a contract document

Cc: Wayne E. Johnson, AIA - Sr. PM – HNTB
Andres Chacon, Sr. PM – HNTB
Mary Cummings, Project Analyst – HNTB
Pratima Singh, Sr. POM – HNTB

For information only. Not a contract document

Exhibit A
ASD Element Fee Detail

Project Fee Proposal - Summary Sheet

Airside D Development Program

HCAA Project Number 8500 23 ASD Feb '26 - July '29

1/20/2026

Basic Design Services				30%	60%	70%	100%	Part 1 Total	Construction	SBE % of Fee	% SBE Goal	% Construction
Engineering & Preconstruction Services				Schematic	Design Dev.	Const. Docs	Const. Docs		Administration		Goal	Cost
	HNTB Architecture			$ -	$ -	$ -	$ -	$ -	$ 4,652,078.48			
	HNTB Structures			$ -	$ -	$ -	$ -	$ -	$ 1,532,324.40			
	HNTB Civil			$ -	$ -	$ -	$ -	$ -	$ 572,119.41			
	Base Engineering			$ -	$ -	$ -	$ -	$ -	$ 283,833.93	1.47%		
	Brindley Peters Associates			$ -	$ -	$ -	$ -	$ -	$ 118,980.61	0.62%		
	Diversified Professionals			$ -	$ -	$ -	$ -	$ -	$ -			
	ECS			$ -	$ -	$ -	$ -	$ -	$ 86,449.51			
	Gartek			$ -	$ -	$ -	$ -	$ -	$ 182,901.60	0.95%		
	Gensler			$ -	$ -	$ -	$ -	$ -	$ 4,450,869.76			
	HLB Lighting Design, Inc.			$ -	$ -	$ -	$ -	$ -	$ 487,946.41	2.53%		
	Jensen Hughes			$ -	$ -	$ -	$ -	$ -	$ 239,848.59			
	Tierra (Geotechnical)			$ -	$ -	$ -	$ -	$ -	$ 150,258.17	0.78%		
	TLC Engineering Solutions			$ -	$ -	$ -	$ -	$ -	$ 2,905,656.23			
	TransSolutions			$ -	$ -	$ -	$ -	$ -	$ -			
	VoltAir Consulting Engineers			$ -	$ -	$ -	$ -	$ -	$ 1,340,761.56	6.94%		
	BNP			$ -	$ -	$ -	$ -	$ -	$ 2,311,941.01			
	Ariel Business Group			$ -	$ -	$ -	$ -	$ -	$ -			
	Beck			$ -	$ -	$ -	$ -	$ -	$ -			
	CERM			$ -	$ -	$ -	$ -	$ -	$ -			
	Fronza & Francis			$ -	$ -	$ -	$ -	$ -	$ -			
	Hensel Phelps			$ -	$ -	$ -	$ -	$ -	$ -			
	Design Phase	Sub Total		$ -	$ -	$ -	$ -	-	$ 19,315,970	13.28%	8.60%	
Reimbursable Expenses												
	HNTB Architecture			$ -	$ -	$ -	$ -	$ -	$ 422,880.00			
	HNTB Structures			$ -	$ -	$ -	$ -	$ -	$ 31,040.00			
	HNTB Civil			$ -	$ -	$ -	$ -	$ -	$ 79,036.00			
	Base Engineering			$ -	$ -	$ -	$ -	$ -	$ 12,000.00			
	Brindley Peters Associates			$ -	$ -	$ -	$ -	$ -	$ -			
	Diversified Professionals			$ -	$ -	$ -	$ -	$ -	$ -			
	ECS			$ -	$ -	$ -	$ -	$ -	$ 40,350.00			
	Gartek			$ -	$ -	$ -	$ -	$ -	$ -			
	Gensler			$ -	$ -	$ -	$ -	$ -	$ 102,660.00			
	HLB Lighting Design, Inc.			$ -	$ -	$ -	$ -	$ -	$ 28,507.50			
	Jensen Hughes			$ -	$ -	$ -	$ -	$ -	$ 8,700.00			
	Tierra (Geotechnical)			$ -	$ -	$ -	$ -	$ -	$ -			
	TLC Engineering Solutions			$ -	$ -	$ -	$ -	$ -	$ -			
	TransSolutions			$ -	$ -	$ -	$ -	$ -	$ -			
	VoltAir Consulting Engineers			$ -	$ -	$ -	$ -	$ -	$ -			
	BNP			$ -	$ -	$ -	$ -	$ -	$ 99,202.00			
	Ariel Business Group			$ -	$ -	$ -	$ -	$ -	$ -			
	Beck			$ -	$ -	$ -	$ -	$ -	$ -			
	CERM			$ -	$ -	$ -	$ -	$ -	$ -			
	Fronza & Francis			$ -	$ -	$ -	$ -	$ -	$ -			
	Hensel Phelps			$ -	$ -	$ -	$ -	$ -	$ -			
Sub Total				$ -	$ -	$ -	$ -	-	$ 824,376			
Total Fee, Allowances, Reimbursable Expenses				$ -	$ -	$ -	$ -	-	$ 20,140,345			

For information only. Not a contract document

Exhibit B
CCBS Element Fee Detail

Project Fee Proposal - Summary Sheet

Airside D Development Program

HCAA Project Number 8515 24 CCBS Feb '26 - July '29

1/20/2026

Basic Design Services				30%	60%	70%	100%	Part 1 Total	Construction	SBE % of Fee	% SBE Goal	% Construction
Engineering & Preconstruction Services				Schematic	Design Dev.	Const. Docs	Const. Docs		Administration		Goal	Cost
	HNTB Architecture			$ -	$ -	$ -	$ -	-	$ 782,263.49			
	HNTB Structures			$ -	$ -	$ -	$ -	-	$ 31,890.14			
	HNTB Civil			$ -	$ -	$ -	$ -	-	$ -			
	Base Engineering			$ -	$ -	$ -	$ -	-	$ 157,480.55	2.44%		
	Brindley Peters Associates			$ -	$ -	$ -	$ -	-	$ -			
	Diversified Professionals			$ -	$ -	$ -	$ -	-	$ -			
	Echo UES Inc.			$ -	$ -	$ -	$ -	-	$ -			
	Gartek			$ -	$ -	$ -	$ -	-	$ -			
	Gensler			$ -	$ -	$ -	$ -	-	$ -			
	Heitmann			$ -	$ -	$ -	$ -	-	$ -			
	HLB Lighting Design, Inc.			$ -	$ -	$ -	$ -	-	$ -			
	Jensen Hughes			$ -		$ -	$ -	-	$ 57,652.84			
	Tierra (Geotechnical)			$ -	$ -	$ -	$ -	-	$ -			
	TLC Engineering Solutions			$ -	$ -	$ -	$ -	-	$ 565,985.56			
	TransSolutions			$ -	$ -	$ -	$ -	-	$ -			
	VoltAir Consulting Engineers			$ -	$ -	$ -	$ -	-	$ 479,029.12	7.42%		
	BNP			$ -	$ -		$ -	-	$ 4,382,548.64			
	Ariel Business Group			$ -	$ -	$ -	$ -	-	$ -			
	Beck			$ -	$ -	$ -	$ -	-	$ -			
	CERM			$ -	$ -	$ -	$ -	-	$ -			
	Fronza & Francis			$ -	$ -	$ -	$ -	-	$ -			
	Hensel Phelps			$ -	$ -	$ -	$ -	-	$ -			
	Design Phase	Sub Total		$ -	$ -	$ -	$ -	-	$ 6,456,850	9.86%	8.60%	
Reimbursable Expenses												
	HNTB Architecture			$ -	$ -	$ -	$ -	-	$ 119,500.00			
	HNTB Structures			$ -	$ -	$ -	$ -	-	$ -			
	HNTB Civil			$ -	$ -	$ -	$ -	-	$ -			
	Base Engineering			$ -	$ -	$ -	$ -	-	$ 12,000.00			
	Brindley Peters Associates			$ -	$ -	$ -	$ -	-	$ -			
	Diversified Professionals			$ -	$ -	$ -	$ -	-	$ -			
	Echo UES Inc.			$ -	$ -	$ -	$ -	-	$ -			
	Gartek			$ -	$ -	$ -	$ -	-	$ -			
	Gensler			$ -	$ -	$ -	$ -	-	$ -			
	Heitmann			$ -	$ -	$ -	$ -	-	$ -			
	HLB Lighting Design, Inc.			$ -	$ -	$ -	$ -	-	$ -			
	Jensen Hughes			$ -	$ -	$ -	$ -	-	$ -			
	Tierra (Geotechnical)			$ -	$ -	$ -	$ -	-	$ -			
	TLC Engineering Solutions			$ -	$ -	$ -	$ -	-	$ -			
	TransSolutions			$ -	$ -	$ -	$ -	-	$ -			
	VoltAir Consulting Engineers			$ -	$ -	$ -	$ -	-	$ -			
	BNP			$ -	$ -	$ -	$ -	-	$ 428,193.90			
	Ariel Business Group			$ -	$ -	$ -	$ -	-	$ -			
	Beck			$ -	$ -	$ -	$ -	-	$ -			
	CERM			$ -	$ -	$ -	$ -	-	$ -			
	Fronza & Francis			$ -	$ -	$ -	$ -	-	$ -			
	Hensel Phelps			$ -	$ -	$ -	$ -	-	$ -			
Sub Total				$ -	$ -	$ -	$ -	-	$ 559,694			
Total Fee, Allowances, Reimbursable Expenses				$ -	$ -	$ -	$ -	-	$ 7,016,544			

For information only. Not a contract document

Schedule

ID	Name	Dur	Start	Finish	TF
Airside D - Tampa International Airport		231d	24-Nov-25 A	21-Oct-26	0d
GI-FS-HAM-1010	Found. Concrete Scope - LOE	153d	24-Nov-25 A	01-Jul-26	0d
PR-P2-1B-7990	Issue/Process PO to Mill Order- Part 2 Supp. A	20d	03-Dec-25 A	31-Dec-25	0d
GI-FS-A1-6820	FRP Found. - Area 6	14d	16-Dec-25 A	06-Jan-26	4d
GI-FS-HAM-1030	Deep UG Plumbing & Mech. Scope - LOE	185d	16-Dec-25 A	04-Sep-26	0d
GI-FS-A1-6840	MEPF In-Wall R/I - Area 6	14d	16-Dec-25 A	06-Jan-26	4d
GI-FS-A2-5500	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.1	21d	23-Dec-25 A	22-Jan-26	10d
PR-P2-1A-1910	HNTB Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	11d	23-Dec-25 A	08-Jan-26	0d
PR-P2-1B-3705	Delivery of Allowance Long Lead - Steel Mill Order - Part 2 Supp. A (LOE)	84d	02-Jan-26	26-Mar-26	0d
PR-P2-1B-8000	Fab. & Ship Long Lead Mill Order - Part 2 Supp. A	84d	02-Jan-26	26-Mar-26	0d
GI-FS-A1-6850	Backfill Found. - Area 6	7d	07-Jan-26	15-Jan-26	4d
GI-FS-A1-6830	Install Waterproofing On Found. - Area 6	5d	07-Jan-26	13-Jan-26	5d
GI-FS-A1-6825	FRP Turndown - Area 6	5d	07-Jan-26	13-Jan-26	5d
PR-P2-1A-1710	HCAA Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	15d	09-Jan-26	29-Jan-26	0d
GI-FS-A1-6610	Excavate Area For Found. - Area 2.A	5d	16-Jan-26	22-Jan-26	4d
GI-FS-A1-6620	FRP Found. - Area 2.A	20d	19-Jan-26	13-Feb-26	4d
GI-FS-A1-6640	MEPF In-Wall R/I - Area 2.A	15d	19-Jan-26	06-Feb-26	6d
GI-FS-A1-6630	Install Waterproofing On Found. - Area 2.A	20d	20-Jan-26	16-Feb-26	4d
GI-FS-A2-5580	Inspect - Deep UG Conduit - Elec. - Area 2.B.1	2d	23-Jan-26	26-Jan-26	10d
GI-FS-A2-5590	Backfill - Deep UG Conduit - Elec. - Area 2.B.1	5d	27-Jan-26	02-Feb-26	10d
PR-P2-1A-1720	Fab. & Ship Rebar Found. Area 1 - Part 2 Supp. A	40d	30-Jan-26	10-Mar-26	0d
GI-FS-A1-6650	Backfill Found. - Area 2.A	7d	11-Feb-26	19-Feb-26	4d
GI-FS-A1-6970	Excavate Area For Found. - Area 2.B	3d	13-Feb-26	17-Feb-26	2d
GI-FS-A1-6980	FRP Found. - Area 2.B	11d	16-Feb-26	02-Mar-26	2d
GI-FS-A1-6990	Install Waterproofing On Found. - Area 2.B	10d	17-Feb-26	02-Mar-26	2d
GI-FS-A1-7000	MEPF In-Wall R/I - Area 2.B	7d	18-Feb-26	26-Feb-26	3d
GI-FS-A1-7010	Backfill Found. - Area 2.B	4d	02-Mar-26	05-Mar-26	2d
GI-FS-A1-1070	Excavate Area For Found. - Area 1.A	2d	06-Mar-26	09-Mar-26	2d
PR-P2-1A-1730	Delivery of Rebar Found. Area 1 Complete - Part 2 Supp. A	0d		10-Mar-26	0d
GI-FS-A1-1250	FRP Found. - Area 1.A	5d	11-Mar-26	17-Mar-26	0d
GI-FS-A1-1410	MEPF In-Wall R/I - Area 1.A	2d	11-Mar-26	12-Mar-26	2d
GI-FS-A1-1260	Install Waterproofing On Found. - Area 1.A	3d	12-Mar-26	16-Mar-26	0d
GI-FS-A1-1270	Backfill Found. - Area 1.A	3d	17-Mar-26	19-Mar-26	0d
GI-FS-A1-7020	Excavate Area For Found. - Area 1.B	3d	17-Mar-26	19-Mar-26	0d
GI-FS-A1-7030	FRP Found. - Area 1.B	7d	18-Mar-26	26-Mar-26	0d
GI-FS-A1-7040	MEPF In-Wall R/I - Area 1.B	3d	19-Mar-26	23-Mar-26	3d
GI-FS-A1-7050	Install Waterproofing On Found. - Area 1.B	4d	23-Mar-26	26-Mar-26	0d
PR-P2-1B-3700	Delivery of Steel Mill Order to GMF Shop - Part 2 Supp. A	0d		26-Mar-26	0d
GI-FS-A1-7060	Backfill Found. - Area 1.B	3d	27-Mar-26	31-Mar-26	0d
GI-FS-A1-6660	Excavate Area For Found. - Area 3	5d	01-Apr-26	07-Apr-26	0d
GI-FS-A1-6670	FRP Found. - Area 3	20d	02-Apr-26	29-Apr-26	0d
GI-FS-A1-6680	Install Waterproofing On Found. - Area 3	20d	03-Apr-26	30-Apr-26	0d
GI-FS-A1-6690	MEPF In-Wall R/I - Area 3	15d	03-Apr-26	23-Apr-26	1d
GI-FS-A1-6700	Backfill Found. - Area 3	10d	22-Apr-26	05-May-26	0d
GI-FS-A1-6710	Excavate Area For Found. - Area 5	5d	06-May-26	12-May-26	0d
GI-FS-A1-6720	FRP Found. - Area 5	15d	07-May-26	28-May-26	0d
GI-FS-A1-6740	MEPF In-Wall R/I - Area 5	10d	08-May-26	21-May-26	1d
GI-FS-A1-6730	Install Waterproofing On Found. - Area 5	15d	08-May-26	29-May-26	0d
GI-FS-A1-6750	Backfill Found. - Area 5	7d	26-May-26	03-Jun-26	0d
GI-FS-A1-6760	Excavate Area For Found. - Area 4	5d	04-Jun-26	10-Jun-26	0d
GI-FS-A1-6770	FRP Found. - Area 4	15d	05-Jun-26	25-Jun-26	0d
GI-FS-A1-6780	Install Waterproofing On Found. - Area 4	15d	08-Jun-26	26-Jun-26	0d
GI-FS-A1-6790	MEPF In-Wall R/I - Area 4	10d	09-Jun-26	22-Jun-26	0d
GI-FS-A1-6800	Backfill Found. - Area 4	7d	23-Jun-26	01-Jul-26	0d
MLS-400	MLS - CIP Concrete Found. Complete	0d		01-Jul-26	0d
GI-FS-A4-6290	Excavate - Deep UG LV Conduit - Low Voltage - Area 4.1	3d	02-Jul-26	07-Jul-26	0d
GI-FS-A4-6310	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 4.1	2d	08-Jul-26	09-Jul-26	0d
GI-FS-A4-6320	Inspect - Deep UG LV Conduit - Low Voltage - Area 4.1	2d	10-Jul-26	13-Jul-26	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement A Critical Path - December 2025 CPM Update

Filters: Supplement A Critical Path, Not Completed
Supplement A Critical Path Filters:
ASD1-Major Elements Supplement A,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 07:57 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp A Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
GI-FS-A4-6330	Backfill - Deep UG LV Conduit - Low Voltage - Area 4.1	3d	14-Jul-26	16-Jul-26	0d
GI-FS-A4-6690	Excavate - Deep UG Sanitary - Plumbing - Area 4.1	4d	17-Jul-26	22-Jul-26	0d
GI-FS-A4-6700	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.1	4d	23-Jul-26	28-Jul-26	0d
GI-FS-A4-6710	Inspect - Deep UG Sanitary - Plumbing - Area 4.1	2d	27-Jul-26	28-Jul-26	0d
GI-FS-A4-6720	Backfill - Deep UG Sanitary - Plumbing - Area 4.1	3d	29-Jul-26	31-Jul-26	0d
GI-FS-A4-6090	Excavate - Deep UG Sanitary - Plumbing - Area 4.2	4d	03-Aug-26	06-Aug-26	0d
GI-FS-A4-6110	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.2	4d	07-Aug-26	12-Aug-26	0d
GI-FS-A4-6170	Inspect - Deep UG Sanitary - Plumbing - Area 4.2	2d	11-Aug-26	12-Aug-26	0d
GI-FS-A4-6190	Backfill - Deep UG Sanitary - Plumbing - Area 4.2	3d	13-Aug-26	17-Aug-26	0d
GI-FS-A4-6390	Excavate - Deep UG Sanitary - Plumbing - Area 4.3	6d	18-Aug-26	25-Aug-26	0d
GI-FS-A4-6440	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.3	6d	26-Aug-26	02-Sep-26	0d
GI-FS-A4-6490	Inspect - Deep UG Sanitary - Plumbing - Area 4.3	2d	01-Sep-26	02-Sep-26	0d
GI-FS-A4-6510	Backfill - Deep UG Sanitary - Plumbing - Area 4.3	2d	03-Sep-26	04-Sep-26	0d
GI-FS-4350	Prep & Submit Pre-Substantial Completion Documentation - Found. Scope	20d	08-Sep-26	05-Oct-26	0d
GI-FS-4360	Substantial Completion Final Clean - Found. Scope	5d	06-Oct-26	12-Oct-26	0d
GI-FS-4370	Final Insp. - Found. Scope	5d	13-Oct-26	19-Oct-26	0d
GI-FS-4380	HP Pre Substantial Completion QC Insp. - Found. Scope	2d	16-Oct-26	19-Oct-26	0d
GI-FS-4390	Substantial Completion Insp. - Found. Scope	2d	20-Oct-26	21-Oct-26	0d
MLS-SUPP.C-04	MLS 4 - Supplement A Substantial Completion	0d		21-Oct-26 C	0d

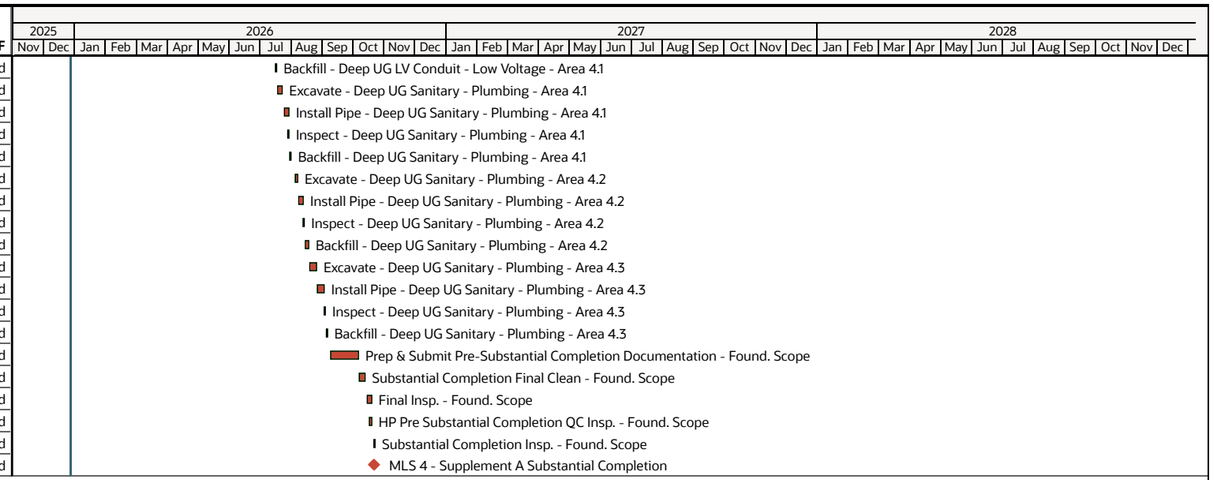

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement A Critical Path - December 2025 CPM Update

Filters: Supplement A Critical Path, Not Completed
Supplement A Critical Path Filters:
ASD1-Major Elements Supplement A,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 07:57 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp A Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
Airside D - Tampa International Airport		492d	02-Oct-25 A	10-Sep-27	0d
CCBS-HAM-30	CCBS - Supp B General Conditions/Requirements - LOE	492d	02-Oct-25 A	10-Sep-27	0d
CCBS-HAM-40	CCBS - Supp B Contingency/Allowance/Budget - LOE	492d	02-Oct-25 A	10-Sep-27	0d
CCBS-LOE-1000	Tag & Trace Elec.& Low Voltage (LOE)	481d	20-Oct-25 A	10-Sep-27	0d
PR-P2-1B-3760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	58d	31-Oct-25 A	26-Jan-26	3d
PR-P2-1B-3810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	63d	31-Oct-25 A	02-Feb-26	9d
PR-P2-1B-4810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	48d	31-Oct-25 A	12-Jan-26	3d
TT-SQ1-SG1-A3-10	Tag & Trace - Sequence 1 - Stage 1 - Area 3	30d	16-Nov-25 A	31-Dec-25	0d
TT-SQ1-SG1-A4-10	Tag & Trace - Sequence 1 - Stage 1 - Area 4	29d	20-Nov-25 A	05-Jan-26	0d
TT-SQ1-SG1-A5-10	Tag & Trace - Sequence 1 - Stage 1 - Area 5	22d	03-Dec-25 A	05-Jan-26	0d
D1084	Review & Approve (HCAA) General Mech. Assembly Detail Drawings	30d	05-Dec-25 A	19-Jan-26	0d
D1093	Review & Approve (HCAA) Mech Plan & Elev Dwg Set [01-01-01]	16d	18-Dec-25 A	12-Jan-26	0d
D1123	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-05]	15d	29-Dec-25	19-Jan-26	6d
PR-P2-1B-3720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 Supp. B	5d	29-Dec-25	05-Jan-26	5d
A110560	Review & Approve (HNTB) Mech. Catalog Cut/Equip. Specs	10d	29-Dec-25	12-Jan-26	0d
TT-SQ1-SG2-A1-10	Tag & Trace - Sequence 1 - Stage 2 - Area 1	10d	06-Jan-26	19-Jan-26	0d
PR-P2-1B-3725	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 Supp. B	20d	06-Jan-26	02-Feb-26	5d
TT-SQ1-SG2-A2-10	Tag & Trace - Sequence 1 - Stage 2 - Area 2	10d	12-Jan-26	23-Jan-26	0d
D1083	Review & Approve (HCAA) Mech. Catalog Cut/Equip. Specs	15d	13-Jan-26	02-Feb-26	0d
PR-P2-1B-4820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 Supp. B	5d	13-Jan-26	19-Jan-26	3d
D1094	Fab. & Deliver Conveyor Batch 1 (15) [01-01-01]	120d	13-Jan-26	30-Jun-26	0d
D1095	Prep & Submit Header Steel Dwg Set [01-01-01]	10d	20-Jan-26	02-Feb-26	0d
D1096	Fab. & Deliver Conveyor Batch 2 (14) [01-01-01]	120d	20-Jan-26	08-Jul-26	0d
PR-P2-1B-4830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 Supp. B	20d	20-Jan-26	16-Feb-26	3d
D1128	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-01]	20d	20-Jan-26	16-Feb-26	6d
TT-SQ1-SG2-A3-10	Tag & Trace - Sequence 1 - Stage 2 - Area 3	10d	26-Jan-26	06-Feb-26	0d
PR-P2-1B-3770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 Supp. B	5d	27-Jan-26	02-Feb-26	3d
PR-P2-1B-3728	Return From Approval Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	0d		02-Feb-26	5d
D1101	Fab. & Deliver HSD T18A 1 [01-01-02]	130d	03-Feb-26	05-Aug-26	0d
PR-P2-1B-3780	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 Supp. B	20d	03-Feb-26	02-Mar-26	3d
D3556	Review & Approve (HP) Header Steel Dwg Set [01-01-01]	5d	03-Feb-26	09-Feb-26	0d
PR-P2-1B-3730	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	10d	03-Feb-26	16-Feb-26	5d
PR-P2-1B-3820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 Supp. B	5d	03-Feb-26	09-Feb-26	9d
TT-SQ1-SG2-A4-10	Tag & Trace - Sequence 1 - Stage 2 - Area 4	10d	09-Feb-26	20-Feb-26	0d
D3566	Review & Approve (HNTB) Header Steel Dwg Set [01-01-01]	10d	10-Feb-26	23-Feb-26	0d
PR-P2-1B-3830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 Supp. B	20d	10-Feb-26	09-Mar-26	9d
PR-P2-1B-4840	Return From Approval Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	0d		16-Feb-26	3d
PR-P2-1B-4850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	10d	17-Feb-26	02-Mar-26	3d
PR-P2-1B-3740	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	5d	17-Feb-26	23-Feb-26	5d
D3716	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-01]	5d	17-Feb-26	23-Feb-26	6d
TT-SQ1-SG2-A5-10	Tag & Trace - Sequence 1 - Stage 2 - Area 5	10d	23-Feb-26	06-Mar-26	0d
PR-P2-1B-3742	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0d		23-Feb-26	5d
D3726	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-01]	10d	24-Feb-26	09-Mar-26	6d
PR-P2-1B-3744	Fab. of Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	71d	24-Feb-26	03-Jun-26	5d
D1097	Review & Approve (HCAA) Header Steel Dwg Set [01-01-01]	15d	24-Feb-26	16-Mar-26	0d
PR-P2-1B-3790	Return From Approval Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	0d		02-Mar-26	3d
PR-P2-1B-4870	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	5d	03-Mar-26	09-Mar-26	3d
PR-P2-1B-3800	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	10d	03-Mar-26	16-Mar-26	3d
TT-SQ1-SG2-A6-10	Tag & Trace - Sequence 1 - Stage 2 - Area 6	10d	09-Mar-26	20-Mar-26	0d
PR-P2-1B-3840	Return From Approval Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	0d		09-Mar-26	9d
PR-P2-1B-4872	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0d		09-Mar-26	3d
PR-P2-1B-4874	Fab. of Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	76d	10-Mar-26	24-Jun-26	3d
PR-P2-1B-3850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	10d	10-Mar-26	23-Mar-26	9d
D1129	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-01]	15d	10-Mar-26	30-Mar-26	6d
D1098	Fab. & Deliver Header Steel/Platform/Sills [01-01-01]	80d	17-Mar-26	08-Jul-26	0d
PR-P2-1B-3802	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	5d	17-Mar-26	23-Mar-26	3d
TT-SQ1-SG3-A1-10	Tag & Trace - Sequence 1 - Stage 3 - Area 1	10d	23-Mar-26	03-Apr-26	0d

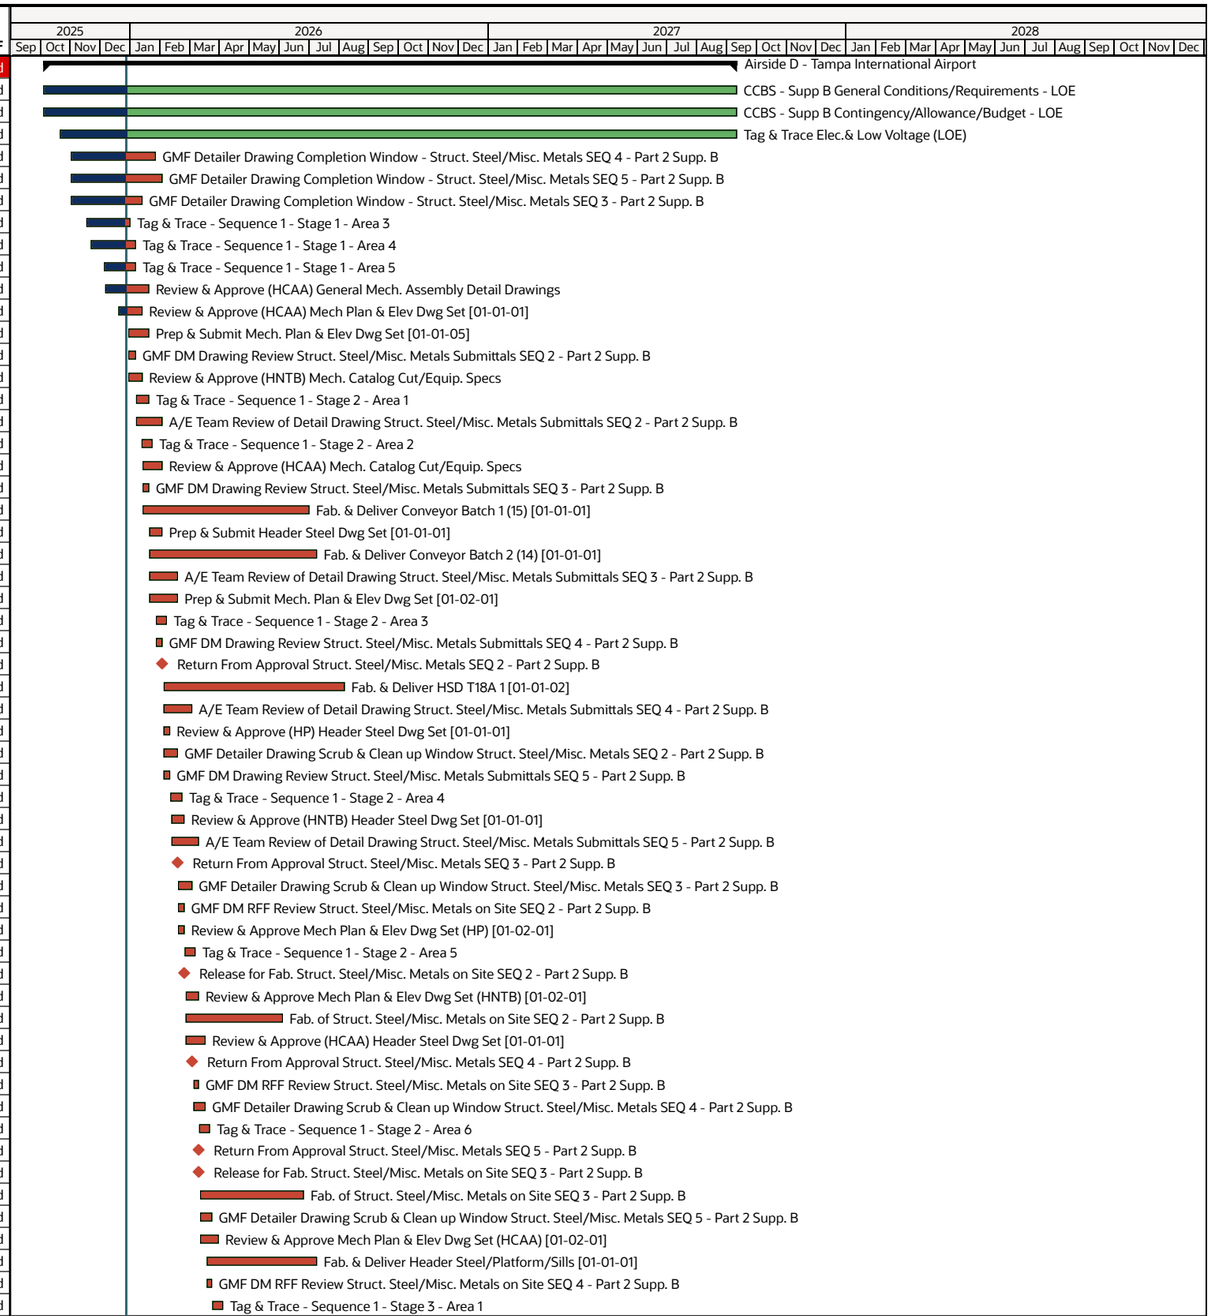

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement B Critical Path - December 2025 CPM Update

Filters: Supplement B Critical Path, Not Completed
Supplement B Critical Path Filters:
ASD1-Major Elements Supplement B,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:03 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp B Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
PR-P2-1B-3804	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0d		23-Mar-26	3d
PR-P2-1B-4880	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	5d	24-Mar-26	30-Mar-26	9d
PR-P2-1B-7670	Fab. of Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	37d	27-Mar-26	18-May-26	0d
PR-P2-1B-4882	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	0d		30-Mar-26	9d
D1130	Prep & Submit Header Steel Dwg Set [01-02-01]	20d	31-Mar-26	27-Apr-26	6d
TT-SQ1-SG3-A2-10	Tag & Trace - Sequence 1 - Stage 3 - Area 2	10d	06-Apr-26	17-Apr-26	0d
PR-P2-1B-3806	Fab. of Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	76d	07-Apr-26	23-Jul-26	3d
TT-SQ1-SG3-A3-10	Tag & Trace - Sequence 1 - Stage 3 - Area 3	10d	20-Apr-26	01-May-26	0d
PR-P2-1B-4284	Fab. of Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	76d	24-Apr-26	11-Aug-26	9d
D3736	Review & Approve Header Steel Dwg Set (HP) [01-02-01]	5d	28-Apr-26	04-May-26	6d
TT-SQ1-SG3-A4-10	Tag & Trace - Sequence 1 - Stage 3 - Area 4	10d	04-May-26	15-May-26	0d
D3746	Review & Approve Header Steel Dwg Set (HNTB) [01-02-01]	10d	05-May-26	18-May-26	6d
TT-SQ1-SG3-A5-10	Tag & Trace - Sequence 1 - Stage 3 - Area 5	10d	18-May-26	01-Jun-26	0d
PR-P2-1B-7680	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	0d		18-May-26	0d
GI-FS-110	Steel Framing Erection - Structure & Slabs (LOE)	181d	19-May-26	04-Feb-27	10d
D1132	Review & Approve Header Steel Dwg Set (HCAA) [01-02-01]	15d	19-May-26	09-Jun-26	6d
MLS-80	MLS - Structural Steel Erection Start	0d	19-May-26		0d
GI-FS-SQN-130	Erect & Bolt/Weld - NOVEMBER - Steel Seq. S1	8d	19-May-26	29-May-26	0d
GI-FS-SQN-150	Install Stairs - NOVEMBER - Steel Seq. S1	5d	01-Jun-26	05-Jun-26	0d
GI-FS-140	Steel Deck & Detailed Metal Decks - Structure & Slabs (LOE)	193d	01-Jun-26	04-Mar-27	10d
TT-SQ1-SG3-A6-10	Tag & Trace - Sequence 1 - Stage 3 - Area 6	10d	02-Jun-26	15-Jun-26	0d
PR-P2-1B-3746	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0d		03-Jun-26	5d
GI-FS-SQN-170	Elevator Steel - NOVEMBER - Steel Seq. S1	3d	08-Jun-26	10-Jun-26	0d
D1133	Fab. & Deliver Header Steel/Platform/Sills [01-02-01]	80d	10-Jun-26	01-Oct-26	6d
GI-FS-SQA-10	Erect & Bolt/Weld Lower Steel - SEQ ALPHA - Steel (S2)	15d	11-Jun-26	01-Jul-26	0d
TT-SQ1-SG3-A7-10	Tag & Trace - Sequence 1 - Stage 3 - Area 7	10d	16-Jun-26	29-Jun-26	0d
PR-P2-1B-4876	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0d		26-Jun-26	3d
TT-SQ1-SG3-A8-10	Tag & Trace - Sequence 1 - Stage 3 - Area 8	10d	30-Jun-26	14-Jul-26	0d
GI-FS-SQA-120	Erect & Bolt/Weld Upper Steel - SEQ ALPHA - Steel (S3)	11d	02-Jul-26	17-Jul-26	0d
D1099	Prep Mech. Matl for Install [01-01-01]	20d	09-Jul-26	05-Aug-26	0d
TT-SQ1-SG3-A9-10	Tag & Trace - Sequence 1 - Stage 3 - Area 9	10d	15-Jul-26	28-Jul-26	0d
GI-FS-SQA-30	Install Stairs - SEQ ALPHA - Steel	4d	20-Jul-26	23-Jul-26	0d
GI-FS-SQA-20	Deck & Detail - SEQ ALPHA - Steel (S2 & S3)	20d	20-Jul-26	14-Aug-26	0d
PR-P2-1B-3808	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0d		23-Jul-26	3d
GI-FS-SQA-50	Elevator Steel - SEQ ALPHA - Steel	3d	24-Jul-26	28-Jul-26	0d
TT-SQ1-SG3-A10-10	Tag & Trace - Sequence 1 - Stage 3 - Area 10	10d	29-Jul-26	11-Aug-26	0d
GI-FS-SQB-10	Erect & Bolt/Weld - SEQ BRAVO - Steel (S4)	12d	29-Jul-26	13-Aug-26	0d
D1107	Prep Mech. Matl for Install [01-01-02]	20d	06-Aug-26	02-Sep-26	0d
D1687	Prep & Submit Cross Belt Sorter XBM1 Elec. Drawings	80d	11-Aug-26	03-Dec-26	7d
PR-P2-1B-4286	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 5- Part 2 Supp. B	0d		11-Aug-26	9d
TT-SQ1-SG3-A11-10	Tag & Trace - Sequence 1 - Stage 3 - Area 11	10d	12-Aug-26	25-Aug-26	0d
GI-FS-SQB-20	Install Stairs - SEQ BRAVO - Steel	4d	14-Aug-26	19-Aug-26	0d
GI-FS-SQA-40	Turn Over to MEPF Contractors - SEQ ALPHA - Steel (S2 & S3)	0d		14-Aug-26	0d
GI-FS-SQB-50	Elevator Steel - SEQ BRAVO - Steel	3d	20-Aug-26	24-Aug-26	0d
GI-FS-SQC-10	Erect & Bolt/Weld - SEQ CHARLIE - Steel (S5)	12d	25-Aug-26	10-Sep-26	0d
TT-SQ1-SG3-A12-10	Tag & Trace - Sequence 1 - Stage 3 - Area 12	10d	26-Aug-26	09-Sep-26	0d
TT-SQ1-SG3-A13-10	Tag & Trace - Sequence 1 - Stage 3 - Area 13	10d	10-Sep-26	23-Sep-26	0d
GI-FS-SQC-30	Install Stairs - SEQ CHARLIE - Steel	4d	11-Sep-26	16-Sep-26	0d
GI-FS-SQC-50	Elevator Steel - SEQ CHARLIE - Steel	3d	17-Sep-26	21-Sep-26	0d
GI-FS-SQD-10	Erect & Bolt/Weld Lower Steel - SEQ DELTA - Steel (S7)	8d	22-Sep-26	01-Oct-26	10d
GI-FS-SQI-10	Erect & Bolt/Weld - SEQ INDIA - Steel (S6)	6d	22-Sep-26	29-Sep-26	0d
TT-SQ1-SG3-A14-10	Tag & Trace - Sequence 1 - Stage 3 - Area 14	10d	24-Sep-26	07-Oct-26	0d
GI-FS-SQI-30	Install Stairs - SEQ INDIA - Steel	5d	30-Sep-26	06-Oct-26	0d
D1134	Prep Mech. Matl for Install [01-02-01]	20d	02-Oct-26	29-Oct-26	6d
GI-FS-SQD-70	Erect & Bolt/Weld Upper Steel - SEQ DELTA - Steel (10)	9d	02-Oct-26	14-Oct-26	10d
GI-FS-SQI-50	Elevator Steel - SEQ INDIA - Steel	3d	07-Oct-26	09-Oct-26	0d
TT-SQ1-SG3-A15-10	Tag & Trace - Sequence 1 - Stage 3 - Area 15	10d	08-Oct-26	21-Oct-26	0d

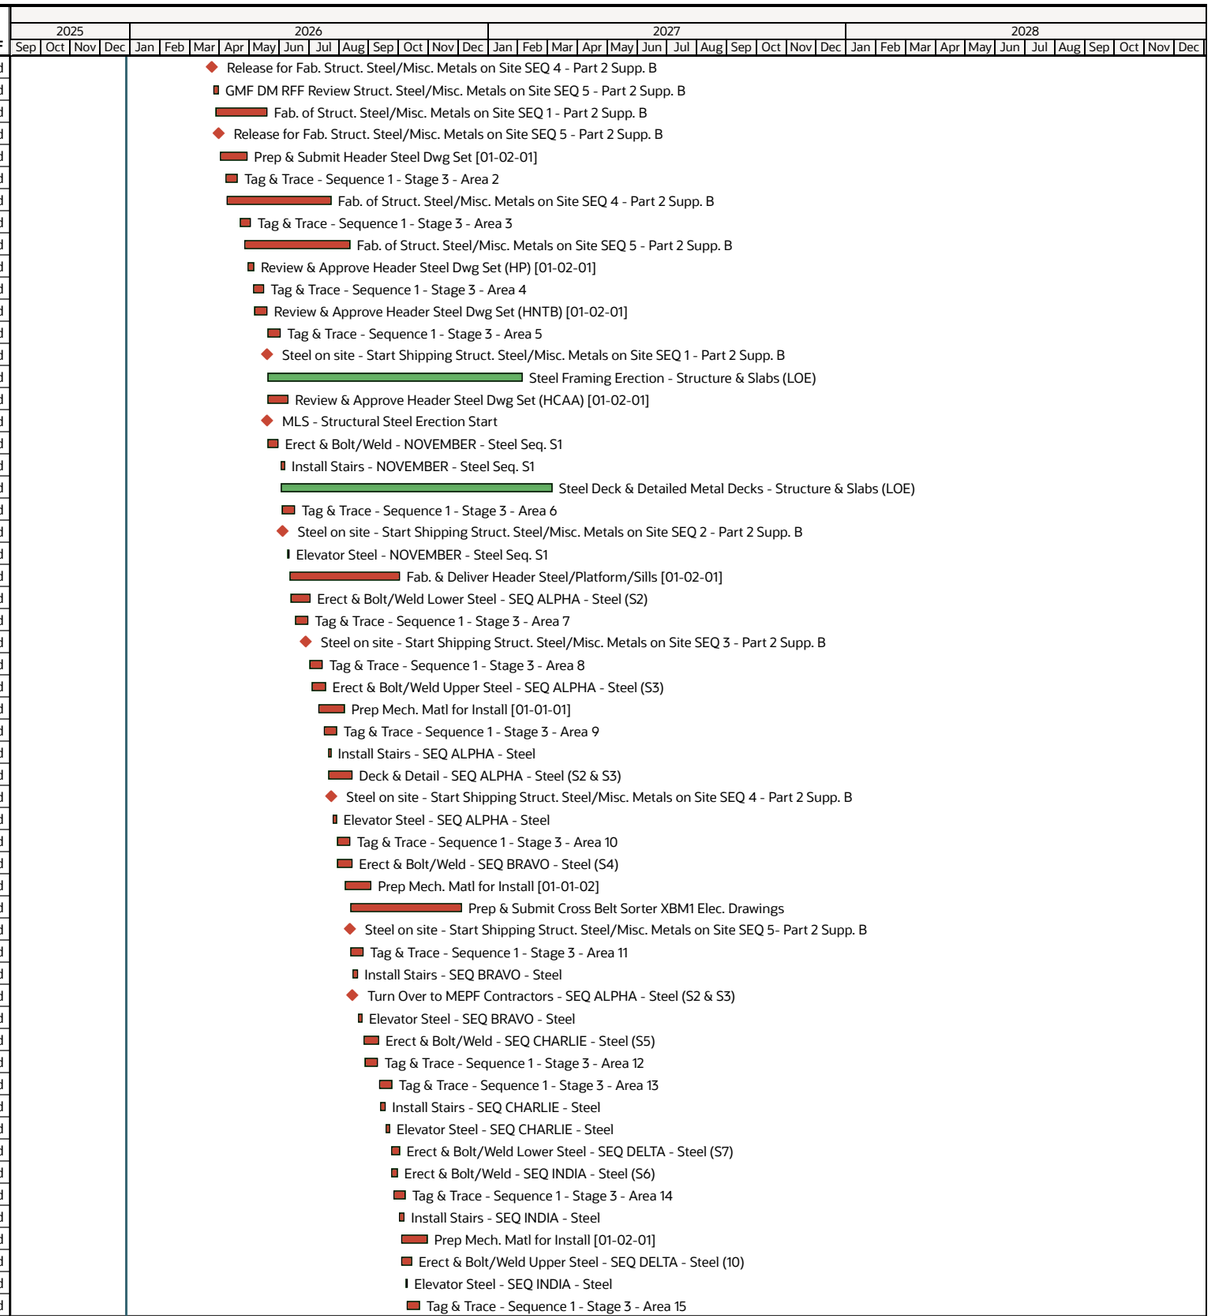

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

Supplement B Critical Path - December 2025 CPM Update

Filters: Supplement B Critical Path, Not Completed
Supplement B Critical Path Filters:
ASD1-Major Elements Supplement B,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:03 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp B Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
GI-FS-SQJ-70	Erect & Bolt/Weld Lower Steel - SEQ JULIET - Steel (S8)	8d	12-Oct-26	21-Oct-26	0d
GI-FS-SQD-30	Install Stairs - SEQ DELTA - Steel	5d	15-Oct-26	21-Oct-26	10d
TT-SQ1-SG3-A16-10	Tag & Trace - Sequence 1 - Stage 3 - Area 16	10d	22-Oct-26	04-Nov-26	0d
GI-FS-SQJ-10	Erect & Bolt/Weld Upper Steel - SEQ JULIET - Steel (S9)	7d	22-Oct-26	30-Oct-26	0d
GI-FS-SQD-50	Elevator Steel - SEQ DELTA - Steel	3d	22-Oct-26	26-Oct-26	10d
GI-FS-SQE-10	Erect & Bolt/Weld - SEQ ECHO - Steel (S12)	6d	27-Oct-26	03-Nov-26	10d
GI-FS-SQJ-30	Install Stairs - SEQ JULIET - Steel	5d	02-Nov-26	06-Nov-26	0d
GI-FS-SQJ-20	Deck & Detail - SEQ JULIET - Steel (S8 & S9)	20d	02-Nov-26	01-Dec-26	7d
GI-FS-SQE-30	Install Stairs - SEQ ECHO - Steel	5d	04-Nov-26	10-Nov-26	10d
TT-SQ1-SG3-A17-10	Tag & Trace - Sequence 1 - Stage 3 - Area 17	10d	05-Nov-26	18-Nov-26	0d
GI-FS-SQJ-50	Elevator Steel - SEQ JULIET - Steel	3d	09-Nov-26	11-Nov-26	0d
GI-FS-SQE-50	Elevator Steel - SEQ ECHO - Steel	3d	11-Nov-26	13-Nov-26	10d
GI-FS-SQK-10	Erect & Bolt/Weld Lower Steel - SEQ KILO - Steel (S11)	14d	12-Nov-26	03-Dec-26	0d
GI-FS-SQF-10	Erect & Bolt/Weld - SEQ FOXTROT - Steel (S14)	11d	16-Nov-26	02-Dec-26	10d
TT-SQ1-SG3-A18-10	Tag & Trace - Sequence 1 - Stage 3 - Area 18	10d	19-Nov-26	04-Dec-26	0d
GI-FS-SQJ-40	Turn Over to MEPF Contractors - SEQ JULIET - Steel (S8 & S9)	0d		01-Dec-26	7d
GI-FS-SQF-30	Install Stairs - SEQ FOXTROT - Steel	4d	03-Dec-26	08-Dec-26	10d
D6146	Review & Approve (HP) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	04-Dec-26	23-Dec-26	7d
GI-FS-SQK-70	Erect & Bolt/Weld Upper Steel - SEQ KILO - Steel (S13)	8d	04-Dec-26	15-Dec-26	0d
TT-SQ1-SG3-A19-10	Tag & Trace - Sequence 1 - Stage 3 - Area 19	10d	07-Dec-26	18-Dec-26	0d
GI-FS-SQF-50	Elevator Steel - SEQ FOXTROT - Steel	3d	09-Dec-26	11-Dec-26	10d
GI-FS-SQG-70	Erect & Bolt/Weld Lower Steel - SEQ GOLF - Steel (S16)	9d	14-Dec-26	24-Dec-26	10d
ASD-SK-700	Architectural Pre-Cast Wall Panels (LOE)	106d	15-Dec-26	13-May-27	10d
GI-FS-SQK-20	Deck & Detail - SEQ KILO - Steel (S11 & S13)	20d	16-Dec-26	14-Jan-27	0d
GI-FS-SQL-10	Erect & Bolt/Weld - SEQ LIMA - Steel (S15)	13d	16-Dec-26	05-Jan-27	0d
GI-FS-SQK-50	Elevator Steel - SEQ KILO - Steel	3d	16-Dec-26	18-Dec-26	0d
TT-SQ1-SG3-A20-10	Tag & Trace - Sequence 1 - Stage 3 - Area 20	10d	21-Dec-26	05-Jan-27	0d
D6156	Review & Approve (HNTB) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	24-Dec-26	14-Jan-27	7d
GI-FS-SQG-10	Erect & Bolt/Weld Upper Steel - SEQ GOLF - Steel (S18)	9d	28-Dec-26	08-Jan-27	10d
TT-SQ1-SG3-A21-10	Tag & Trace - Sequence 1 - Stage 3 - Area 21	10d	06-Jan-27	19-Jan-27	0d
GI-FS-SQL-20	Deck & Detail - SEQ LIMA - Steel (S15)	20d	06-Jan-27	02-Feb-27	0d
GI-FS-SQL-30	Install Stairs - SEQ LIMA - Steel	5d	06-Jan-27	12-Jan-27	0d
GI-FS-SQG-20	Install Stairs - SEQ GOLF - Steel	5d	11-Jan-27	15-Jan-27	10d
GI-FS-SQL-50	Elevator Steel - SEQ LIMA - Steel	3d	13-Jan-27	15-Jan-27	0d
GI-FS-SQK-40	Turn Over to MEPF Contractors - SEQ KILO - Steel (S11 & S13)	0d		14-Jan-27	0d
D1688	Review & Approve (HCAA) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	15-Jan-27	03-Feb-27	7d
GI-FS-SQG-50	Elevator Steel - SEQ GOLF - Steel	3d	18-Jan-27	20-Jan-27	10d
GI-FS-SQM-70	Erect & Bolt/Weld - SEQ MIKE - Steel (S17)	6d	18-Jan-27	25-Jan-27	0d
TT-SQ1-SG3-A22-10	Tag & Trace - Sequence 1 - Stage 3 - Area 22	10d	20-Jan-27	02-Feb-27	0d
GI-FS-SQH-10	Erect & Bolt/Weld - SEQ HOTEL - Steel (S19)	11d	21-Jan-27	04-Feb-27	10d
GI-FS-SQM-80	Deck & Detail - SEQ MIKE - Steel (S17)	20d	26-Jan-27	22-Feb-27	0d
TT-SQ1-SG3-A23-10	Tag & Trace - Sequence 1 - Stage 3 - Area 23	10d	03-Feb-27	16-Feb-27	0d
D1690	Fab. & Deliver XBM1 Power Panels (13)	80d	04-Feb-27	26-May-27	7d
D1691	Fab. & Deliver XBM1 Field Control Panels, Elect Field Devices, Cabling	80d	04-Feb-27	26-May-27	7d
GI-FS-SQH-30	Deck & Detail - SEQ HOTEL - Steel (S19)	20d	05-Feb-27	04-Mar-27	10d
GI-FS-SQL-40	Turn Over to MEPF Contractors - SEQ LIMA - Steel (S15)	0d		05-Feb-27	0d
TT-SQ1-SG3-A24-10	Tag & Trace - Sequence 1 - Stage 3 - Area 24	10d	17-Feb-27	02-Mar-27	0d
GI-FS-SQM-100	Turn Over to MEPF Contractors - SEQ MIKE - Steel (S17)	0d		22-Feb-27	0d
TT-SQ1-SG3-A25-10	Tag & Trace - Sequence 1 - Stage 3 - Area 25	10d	03-Mar-27	16-Mar-27	0d
GI-FS-SQH-40	Turn Over to MEPF Contractors - SEQ HOTEL - Steel (S19)	0d		04-Mar-27	10d
MLS-95	MLS - Structural Steel Erection Complete	0d		04-Mar-27	10d
TT-SQ1-SG3-A26-10	Tag & Trace - Sequence 1 - Stage 3 - Area 26	10d	17-Mar-27	30-Mar-27	0d
TT-SQ1-SG3-A27-10	Tag & Trace - Sequence 1 - Stage 3 - Area 27	10d	31-Mar-27	13-Apr-27	0d
TT-SQ1-SG3-A28-10	Tag & Trace - Sequence 1 - Stage 3 - Area 28	10d	14-Apr-27	27-Apr-27	0d
TT-SQ1-SG3-A29-10	Tag & Trace - Sequence 1 - Stage 3 - Area 29	10d	28-Apr-27	11-May-27	0d
SK-Q2-LO-150	Pre-Cast System - Q2 Lower	10d	30-Apr-27	13-May-27	10d
TT-SQ1-SG3-A30-10	Tag & Trace - Sequence 1 - Stage 3 - Area 30	10d	12-May-27	25-May-27	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement B Critical Path - December 2025 CPM Update

Filters: Supplement B Critical Path, Not Completed
Supplement B Critical Path Filters:
ASD1-Major Elements Supplement B,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:03 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp B Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
TT-SQ1-SG3-A31-10	Tag & Trace - Sequence 1 - Stage 3 - Area 31	10d	26-May-27	09-Jun-27	0d
TT-SQ1-SG3-A32-10	Tag & Trace - Sequence 1 - Stage 3 - Area 32	10d	10-Jun-27	23-Jun-27	0d
TT-SQ2-SG1-A1-10	Tag & Trace - Sequence 2 - Stage 1 - Area 1	10d	24-Jun-27	08-Jul-27	0d
TT-SQ2-SG1-A2-10	Tag & Trace - Sequence 2 - Stage 1 - Area 2	10d	09-Jul-27	22-Jul-27	0d
MLS-210	MLS - Pre-Cast/Curtainwall Facade Start	0d	21-Jul-27		0d
TT-SQ2-SG1-A3-10	Tag & Trace - Sequence 2 - Stage 1 - Area 3	10d	23-Jul-27	05-Aug-27	0d
TT-SQ2-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 2 - Stage 1 - Area 3	5d	06-Aug-27	12-Aug-27	0d
TT-SQ2-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 2 - Stage 1 - Area 3	10d	13-Aug-27	26-Aug-27	0d
MLS-100	MLS - Pre-Cast/Curtainwall Facade Complete	0d		24-Aug-27	0d
TT-SQ2-SG1-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 2 - Stage 1 - Area 3	10d	27-Aug-27	10-Sep-27	0d
MLS-SUPP.C-06	MLS 6 - Supplement B Substantial Completion	0d		10-Sep-27 C	0d

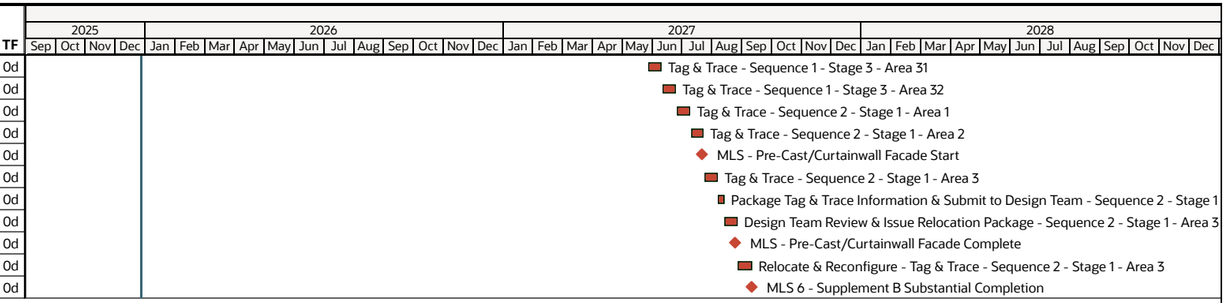

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement B Critical Path - December 2025 CPM Update

Filters: Supplement B Critical Path, Not Completed
Supplement B Critical Path Filters:
ASD1-Major Elements Supplement B,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:03 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp B Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
Airside D - Tampa International Airport		1,337d	13-Dec-24 A	20-Mar-30	0d
ASD-HAM-20	ASD - Contingency/Allowance/Budget - LOE	1,337d	13-Dec-24 A	20-Mar-30	0d
ASD-HAM-10	ASD - General Conditions/Requirements - LOE	1,337d	13-Dec-24 A	20-Mar-30	0d
HA-2C-W1-70	HCAA Review Supp. C for Board - Part 2 Supp. C - Core & Shell Pkg.	37d	15-Dec-25 A	05-Feb-26	0d
2C-W1-PC-860	Purchasing Meeting - Elec. & Site Elec. Trade Partner - P2 Supp. C Wv 1 Pur & Contr	1d	05-Jan-26	05-Jan-26	9d
2C-W1-PC-2480	Purchasing Meeting - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	1d	06-Jan-26	06-Jan-26	9d
2C-W1-PC-2490	Draft, Review, & Issue Change Order - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	3d	07-Jan-26	09-Jan-26	9d
2C-W1-PC-2510	Change Order Negotiation - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	10d	12-Jan-26	23-Jan-26	9d
HA-2C-W1-80	Board Date (NTP) - Part 2 Supp. C - Core & Shell Pkg. (2.5.26)	0d		05-Feb-26	0d
HA-BA-60	Part 2 Supplemental C Agreement - HCAA Board Approval (2.5.2026)	0d		05-Feb-26	5d
2C-W1-PC-780	Contract Execution - Elev./Escalators Trade Partner - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	0d
2C-W1-PC-960	Change Order Execution - Low Voltage System Trade Partner - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	9d
2C-W1-PC-2520	Change Order Execution - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	0d
2C-W1-PC-790	Contract Exec Complete - Elev./Escalators Trade Partner - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	0d
2C-W1-PC-2530	Change Order Execution Complete - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	0d
2C-W1-PC-970	Change Order Execution Complete - Low Voltage System Trade Partner - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	9d
PR-P1-1C1-810	Prep Elev. 01-11 Submittals - ASD	50d	13-Feb-26	23-Apr-26	0d
D1507	Prep & Submit Mech. Plan & Elev Dwg Set - Sector K	20d	13-Feb-26	12-Mar-26	0d
PR-P2-1C2-8160	Prep Airport Access Controls Submittals (Contractor) - CCBS	20d	13-Feb-26	12-Mar-26	9d
D1086	Prep & Submit Cross Belt Mech. Catalog Cut/Equip. Specs	15d	13-Feb-26	05-Mar-26	7d
D3436	Review & Approve (HP) Cross Belt Mech. Catalog Cut/Equip. Specs	5d	06-Mar-26	12-Mar-26	7d
D1512	Prep & Submit Mech. Plan & Elev Dwg Set - Sector J	20d	13-Mar-26	09-Apr-26	0d
PR-P2-1C2-8170	Review & Submit Airport Access Controls Submittals (HP) - CCBS	5d	13-Mar-26	19-Mar-26	9d
D3446	Review & Approve (HNTB) Cross Belt Mech. Catalog Cut/Equip. Specs	10d	13-Mar-26	26-Mar-26	7d
PR-P2-1C2-8180	Review & Approve Airport Access Controls Submittals (HNTB) - CCBS	10d	20-Mar-26	02-Apr-26	9d
D1087	Review & Approve (HCAA) Cross Belt Mech. Catalog Cut/Equip. Specs	15d	27-Mar-26	16-Apr-26	7d
PR-P2-1C2-8190	Review & Approve Airport Access Controls Submittals (HCAA) - CCBS	15d	03-Apr-26	23-Apr-26	9d
D1531	Prep & Submit Mech. Plan & Elev Dwg Set - Sector F	35d	10-Apr-26	29-May-26	0d
D1224	Prep & Submit Mech. Plan & Elev Dwg Set (XBM1) [01-03-01]	80d	17-Apr-26	10-Aug-26	7d
PR-P1-1C1-815	Review & Submit Elev. 01-11 Submittals (HP) - ASD	10d	24-Apr-26	07-May-26	0d
PR-P1-1C1-1310	Review & Approve Elev. 01-11 Submittals (HNTB) - ASD	10d	08-May-26	21-May-26	0d
PR-P1-1C1-1315	Review & Approve Elev. 01-11 Submittals (HCAA) - ASD	15d	22-May-26	12-Jun-26	0d
D1062	Prep & Submit Estimated Parts List	30d	27-May-26	08-Jul-26	5d
D1564	Prep & Submit Mech. Plan & Elev Dwg Set - Sector E	30d	01-Jun-26	13-Jul-26	0d
A108720	Low Voltage Ceiling & In-Wall Rough-In - PLC Room	10d	04-Jun-26	17-Jun-26	9d
TC-GP-290	Demo Old Bessie Coleman Blvd & Rough Grade Area	10d	11-Jun-26	24-Jun-26	3d
PR-P1-1C1-3830	Fab. & Ship Elev. 06-07 - ASD	154d	13-Jun-26	16-Nov-26	2d
A108740	Hang, Tape, & Finish New Walls - PLC Room	5d	18-Jun-26	24-Jun-26	9d
A108770	Install Flooring - PLC Room	10d	25-Jun-26	09-Jul-26	9d
TC-FS-120	Install New Temp Barrier Mounted AOA Fence (Includes TSA Inspections)	20d	30-Jun-26	28-Jul-26	0d
D3036	Review & Approve (HP) Estimated Parts List	5d	09-Jul-26	15-Jul-26	5d
A108780	Apply Final Paint - PLC Room	5d	10-Jul-26	16-Jul-26	9d
D1595	Prep & Submit Mech. Plan & Elev Dwg Set - Sector B	20d	14-Jul-26	10-Aug-26	0d
BG-OPS-TC-40	Ticket Counter T18 - Out of Service (LOE)	53d	14-Jul-26	25-Sep-26	0d
D3046	Review & Approve (HNTB) Estimated Parts List	10d	16-Jul-26	29-Jul-26	5d
A108790	Install OFCI Equip. & Furniture - PLC Room	5d	17-Jul-26	23-Jul-26	9d
TC-FS-50	Remove Temp AOA Fence (Installed During Enabling)	20d	29-Jul-26	25-Aug-26	0d
D1066	Review & Approve (HCAA) Estimated Parts List	15d	30-Jul-26	19-Aug-26	5d
BI-ROW-BCC-180	Post-BHS Fire Sprinkler System Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BG-DM-MCP-4020	Post-BHS Elec. Systems Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BI-ROW-BCC-650	Post-BHS Technology & Data Systems Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BI-ROW-BCC-640	Post-BHS HVAC & Plumbing Systems Modifications [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
B	BHS - Mech & Elec. Install [01-01-01]	15d	06-Aug-26	26-Aug-26	0d
D1618	Prep & Submit Mech. Plan & Elev Dwg Set - Sector C	30d	11-Aug-26	22-Sep-26	0d
GI-FS-SQA-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ ALPHA - SOMD	6d	17-Aug-26	24-Aug-26	0d
GI-FS-SQA-SOG-130	FRP Guideway Structure Column	10d	17-Aug-26	28-Aug-26	1d
GI-FS-SQA-SOMD-20	MEPF Hangers & Block Outs Club - SEQ ALPHA - SOMD	6d	17-Aug-26	24-Aug-26	0d
GI-FS-SQA-SOMD-30	FRP Pour 1 Concourse - SEQ ALPHA - SOMD	6d	25-Aug-26	01-Sep-26	0d

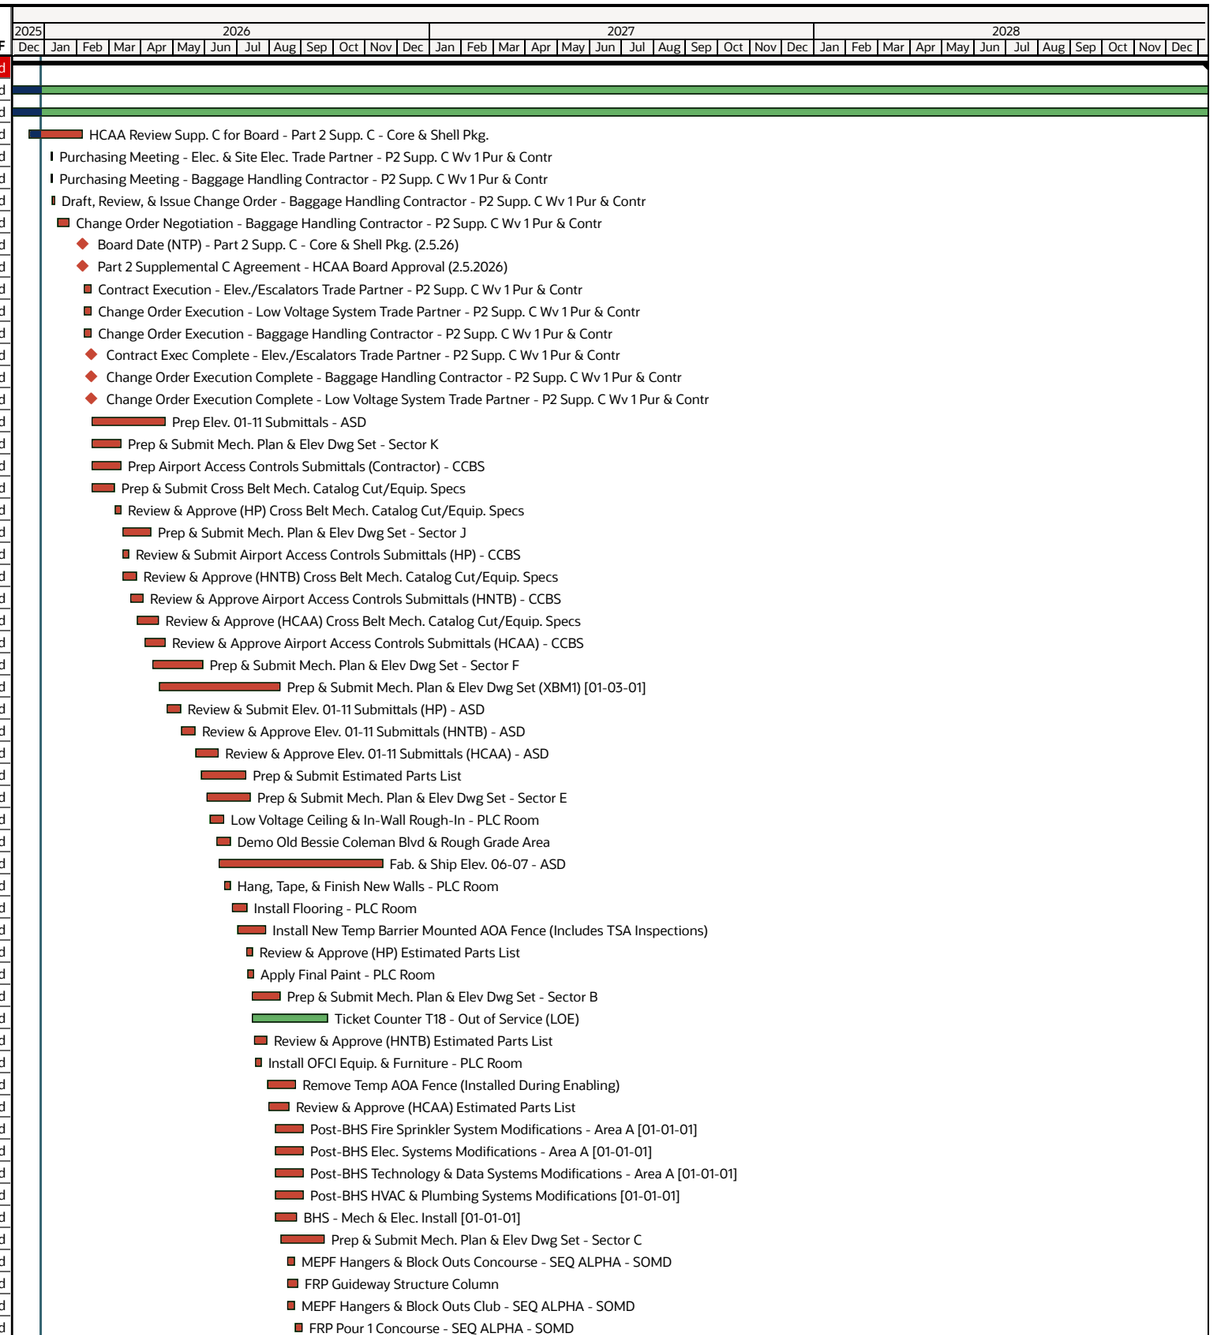

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
C	BHS - T-T18 Tie-in & Overall Testing [01-01-01]	5d	27-Aug-26	02-Sep-26	0d
GI-FS-SQA-SOG-150	Install Guideway Structure Deck Shoring	5d	31-Aug-26	04-Sep-26	1d
GI-FS-SQA-SOMD-50	FRP Pour 2 Concourse - SEQ ALPHA - SOMD	6d	02-Sep-26	10-Sep-26	0d
A105680	HVAC & Plumbing Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105690	Technology & Data Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105670	Elec. Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105700	Fire Protection System Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A1	BHS - Mech / Elec. Demo & Install of C11 & T18 [01-01-02]	7d	03-Sep-26	14-Sep-26	0d
BG-OPS-TC-30	Ticket Counter C11E - Out of Service (LOE)	10d	03-Sep-26	17-Sep-26	0d
GI-FS-SQA-SOG-200	FRP Guideway Structure Deck	5d	08-Sep-26	14-Sep-26	1d
B1	BHS - Testing [01-01-02]	8d	08-Sep-26	17-Sep-26	0d
BG-BI-ROW-90	Demo MCP 5 Feeder Back to Source [HMCP-3] [01-01-02]	10d	09-Sep-26	22-Sep-26	3d
GI-FS-SQA-SOMD-60	FRP Pour 3 Concourse - SEQ ALPHA - SOMD	6d	11-Sep-26	18-Sep-26	0d
A104130	Infill C11-01 Penetration Along Grid L [01-01-02]	4d	15-Sep-26	18-Sep-26	0d
GI-FS-SQA-SOG-210	Guideway Structure Deck Cure	7d	15-Sep-26	23-Sep-26	1d
A105740	Fire Protection Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105720	HVAC & Plumbing Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105730	Technology & Data Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105710	Elec. Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A3	BHS - Mech / Elec. Demo & Install of T18 [01-01-03]	5d	18-Sep-26	24-Sep-26	0d
RI-C2-SP-1370	Install Train Tube Metal Deck - SMP/Train Tube - INTR - C2	5d	21-Sep-26	25-Sep-26	0d
A104150	Infill T18 Penetration Along Grid L [01-01-03]	5d	21-Sep-26	25-Sep-26	0d
D5696	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector C	5d	23-Sep-26	29-Sep-26	0d
GI-FS-SQA-SOG-250	Guideway Structure Shoring Removal	5d	24-Sep-26	30-Sep-26	1d
D1788	BHS - Testing T18 [01-01-03]	1d	25-Sep-26	25-Sep-26	0d
RI-C2-SP-1420	Install Temp Tunnel Peel & Stick - SMP/Train Tube - INTR - C2	10d	28-Sep-26	09-Oct-26	0d
A3.5	BHS - Mech / Elec. Demo & Install of TC2 [01-01-03]	5d	28-Sep-26	02-Oct-26	0d
D5706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector C	10d	30-Sep-26	13-Oct-26	0d
GI-FS-SQA-SOG-10	Underground MEPF - Pour 1 - SEQ ALPHA - SOG	5d	01-Oct-26	07-Oct-26	1d
D1793	Internal Commissioning / Functional Testing / Owner Testing [01-01-03]	1d	05-Oct-26	05-Oct-26	0d
A4	BHS - Mech / Elec. Demo & Install of T17 [01-01-04]	5d	06-Oct-26	12-Oct-26	0d
GI-FS-SQA-SOG-30	FRP Pour 1 - SEQ ALPHA - SOG	7d	08-Oct-26	16-Oct-26	1d
RI-C2-SP-1230	Layout Walls/Top Track - SMP/Train Tube - INTR - C2	5d	12-Oct-26	16-Oct-26	0d
D1800	Internal Commissioning / Functional Testing / Owner Testing (T17 03/04, T17 04 FSD) [01-01-04]	1d	12-Oct-26	12-Oct-26	0d
D1801	Mech Remove Stainless Shrouding (T17 01/02) [01-01-04]	1d	13-Oct-26	13-Oct-26	0d
D1619	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector C	15d	14-Oct-26	03-Nov-26	0d
D1802	Elec. Recontrol (Reverse) (T17 01/02) [01-01-04]	2d	14-Oct-26	15-Oct-26	0d
D1805	Mech Stainless Shrouding (T17 01/02) [01-01-04]	1d	16-Oct-26	16-Oct-26	0d
D1804	Internal Commissioning / Functional Testing / Owner Testing (T17 01/02) [01-01-04]	1d	16-Oct-26	16-Oct-26	0d
D1806	Elec. Demo (T17 03/04) [01-01-04]	1d	19-Oct-26	19-Oct-26	0d
RI-C2-SP-1320	Frame Walls Train Tube A - SMP/Train Tube - INTR - C2	15d	19-Oct-26	06-Nov-26	0d
D1807	Mech Demo (T17 03/04) [01-01-04]	1d	20-Oct-26	20-Oct-26	0d
A107620	Install Temp Partition Walls Around T15 & T16 Counters [01-01-05]	2d	21-Oct-26	22-Oct-26	0d
RI-AP2-300	Layout Walls/Top Track - Overall Rough-in - INTR - AP 2	5d	22-Oct-26	28-Oct-26	1d
A5	BHS - Mech / Elec. Demo & Install of T15 [01-01-05]	5d	23-Oct-26	29-Oct-26	0d
RI-AP2-5720	Install Block Walls/Masonry Door Frames - INTR - AP 2	15d	29-Oct-26	18-Nov-26	1d
D1813	Internal Commissioning / Functional Testing / Owner Testing T15 [01-01-05]	1d	30-Oct-26	30-Oct-26	0d
B5	BHS - Mech / Elec. Demo & Install of T16 [01-01-05]	4d	02-Nov-26	05-Nov-26	0d
D1622	Prep & Submit Header Steel Dwg Set - Sector C	20d	04-Nov-26	03-Dec-26	0d
D1820	Internal Commissioning / Functional Testing / Owner Testing T16 [01-01-05]	1d	06-Nov-26	06-Nov-26	0d
A6	BHS - Mech / Elec. Demo & Install of TC2 [01-02-01]	4d	09-Nov-26	12-Nov-26	0d
RI-C2-SP-1390	Frame Walls Train Tube B - SMP/Train Tube - INTR - C2	15d	09-Nov-26	01-Dec-26	0d
D1828	Internal Commissioning / Functional Testing / Owner Testing [01-02-01]	1d	13-Nov-26	13-Nov-26	0d
D1832	Elec. Install MPP A1, FCP A1, MPP A9, FCP A9 [01-02-02]	9d	16-Nov-26	30-Nov-26	10d
D1835	Mech Install (AS7 3B/3D, AX9 01) [01-02-02]	1d	16-Nov-26	16-Nov-26	0d
PR-P1-1C1-3850	Delivery of Elev. 06-07 on Site - ASD	0d		16-Nov-26	2d
D1837	Elec. Install (AS7 3B/3D, AX9 01) [01-02-02]	12d	17-Nov-26	04-Dec-26	0d
PR-P1-1C1-3840	Off Site Staging of Elev. 06-07 - ASD	497d	17-Nov-26	11-Apr-28	2d

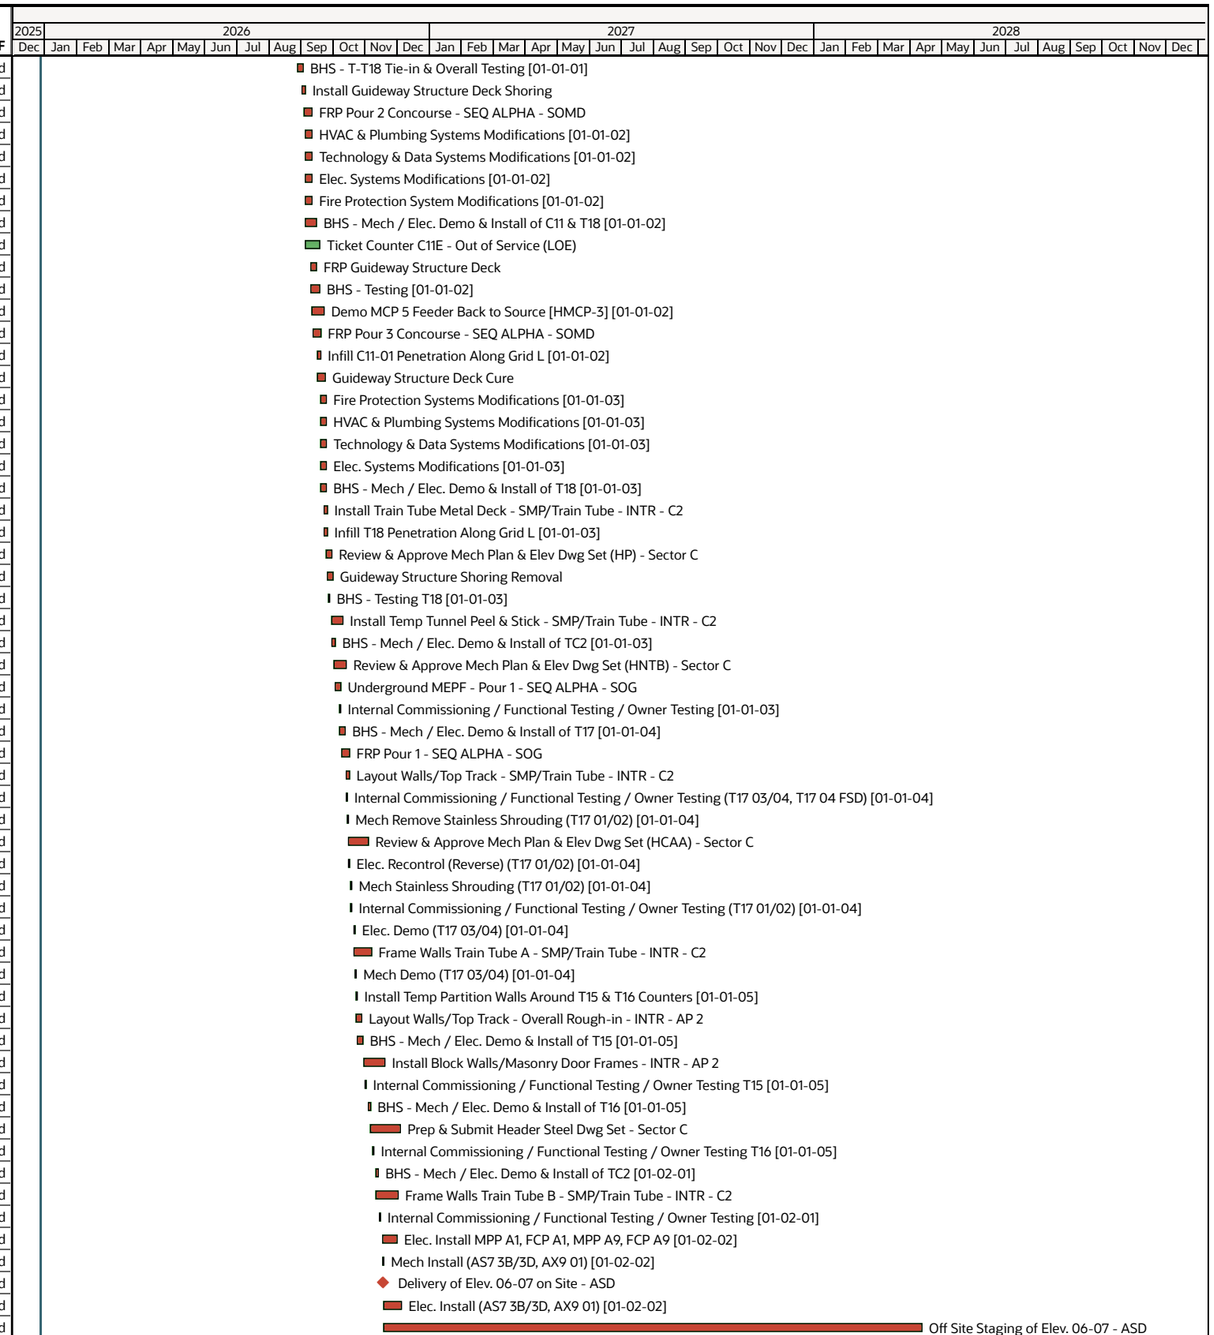

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
RI-AP3-5760	Install Block Walls/Masonry Door Frames - Overall Rough-in - INTR - AP 3	15d	19-Nov-26	11-Dec-26	1d
RI-C2-SP-1430	Install Fall Protection Anchors Train A & Train B - SMP/Train Tube - INTR - C2	5d	02-Dec-26	08-Dec-26	0d
GI-FS-SQJ-SOMD-10	MEPF Hangers & Block Outs Club - SEQ JULIET - SOMD	6d	02-Dec-26	09-Dec-26	7d
GI-FS-SQJ-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ JULIET - SOMD	6d	02-Dec-26	09-Dec-26	7d
D5716	Review & Approve Header Steel Dwg Set (HP) - Sector C	5d	04-Dec-26	10-Dec-26	0d
D1838	Elec. Install (AX9 12/15, C8A 11/12, T12 25/26) [01-02-02]	6d	07-Dec-26	14-Dec-26	0d
D1839	Internal Commissioning / Functional Testing / Owner Testing (AS7 3B/3D, AX9 01) [01-02-02]	1d	07-Dec-26	07-Dec-26	5d
RI-C2-SP-1260	Install Fireproofing - SMP/Train Tube - INTR - C2	5d	09-Dec-26	15-Dec-26	0d
GI-FS-SQJ-SOMD-30	FRP Pour 1 Concourse - SEQ JULIET - SOMD	6d	10-Dec-26	17-Dec-26	7d
GI-FS-SQJ-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ JULIET - SOMD	6d	10-Dec-26	17-Dec-26	7d
D5726	Review & Approve Header Steel Dwg Set (HNTB) - Sector C	10d	11-Dec-26	24-Dec-26	0d
RI-AP3-5770	Elec. Rough-in Block Walls - Overall Rough-in - INTR - AP 3	15d	14-Dec-26	05-Jan-27	1d
D1841	Internal Commissioning / Functional Testing / Owner Testing (AX9 12/15, C8A 11/12, T12 25/26) [01...	1d	15-Dec-26	15-Dec-26	0d
D1843	Mech Install (T-T12 24/25 & 27/28, T-AX9 11, Temp Diverter Plate PS-AX8 01) [01-02-03]	3d	16-Dec-26	18-Dec-26	0d
BG-OPS-TC-90	TA2 - Out of Service [Contingency Porters Required] (LOE)	4d	16-Dec-26	21-Dec-26	0d
RI-C2-SP-1280	Install Elec. OH Rough-in - SMP/Train Tube - INTR - C2	10d	16-Dec-26	30-Dec-26	0d
D1846	Mech Demo (T12 24/25, TA2 06) [01-02-03]	1d	16-Dec-26	16-Dec-26	2d
RI-C2-SP-1290	Low Voltage Rough-in Ceilings - SMP/Train Tube - INTR - C2	10d	16-Dec-26	30-Dec-26	0d
D1844	Elec. Install (T12 24, T 25/28, AX9 11) [01-02-03]	3d	16-Dec-26	18-Dec-26	0d
D1845	Elec. Demo (T12 24/25, TA2 06) [01-02-03]	1d	16-Dec-26	16-Dec-26	2d
GI-FS-SQJ-SOMD-50	FRP Pour 2 Concourse - SEQ JULIET - SOMD	6d	18-Dec-26	28-Dec-26	7d
D1847	Internal Commissioning / Functional Testing / Owner Testing [01-02-03]	1d	21-Dec-26	21-Dec-26	0d
D1852	Mec Install (AX9 10/11, TA1 12/14) [01-02-04]	4d	22-Dec-26	28-Dec-26	0d
BG-OPS-TC-100	TA1 - Out of Service [Contingency Porters Required] (LOE)	5d	22-Dec-26	29-Dec-26	0d
D1850	Elec. Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1d	22-Dec-26	22-Dec-26	3d
D1851	Mech Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1d	22-Dec-26	22-Dec-26	3d
D1853	Elec. Install (AX9 10/11, TA1 12/14) [01-02-04]	4d	22-Dec-26	28-Dec-26	0d
D1633	Review & Approve Header Steel Dwg Set (HCAA) - Sector C	15d	28-Dec-26	18-Jan-27	0d
D1854	Internal Commissioning / Functional Testing / Owner Testing [01-02-04]	1d	29-Dec-26	29-Dec-26	0d
GI-FS-SQJ-SOMD-70	7 Day Concrete Cure - Concourse - SEQ JULIET - SOMD	7d	29-Dec-26	05-Jan-27	9d
D1856	Elec. Demo [01-03-01]	30d	30-Dec-26	10-Feb-27	0d
BG-MLS-OPS-20	MEM1 - Permanently Out of Service	0d		30-Dec-26	0d
D1857	Mech Demo [01-03-01]	30d	30-Dec-26	10-Feb-27	0d
RI-C2-SP-1350	Install Sheathing - SMP/Train Tube - INTR - C2	6d	31-Dec-26	08-Jan-27	0d
RI-AP3-1404	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 3	5d	06-Jan-27	12-Jan-27	1d
RI-C11-R1-10	Layout Walls/Top Track - Overall/Restrooms - INTR - C11	10d	06-Jan-27	19-Jan-27	7d
BI-ROW-BR-P8-100	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS8 [01-03-01]	15d	07-Jan-27	27-Jan-27	0d
RI-C2-SP-1340	Install Vapor Barrier System - SMP/Train Tube - INTR - C2	10d	11-Jan-27	22-Jan-27	0d
RI-AP3-PDS-5800	Install Fire Sprinkler Hangers - PDS Room 6097 - INTF - AP 3	2d	13-Jan-27	14-Jan-27	1d
RI-AP3-1240	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 3	2d	13-Jan-27	14-Jan-27	1d
RI-AP3-PDS-5810	Install CHW Hangers - PDS Room 6097 - INTF - AP 3	2d	15-Jan-27	18-Jan-27	1d
GI-FS-SQK-SOMD-10	MEPF & BHS Hangers & Block Outs Concourse - SEQ KILO - SOMD	6d	15-Jan-27	22-Jan-27	0d
D1634	Fab. & Deliver Header Steel/Platform/Sills - Sector C	80d	19-Jan-27	10-May-27	0d
RI-AP3-PDS-5820	Install Plumbing Hangers - PDS Room 6097 - INTF - AP 3	2d	19-Jan-27	20-Jan-27	1d
RI-C11-R1-6140	Install Fire Sprinkler Hangers - Overall/Restrooms - INTR - C11	2d	20-Jan-27	21-Jan-27	7d
RI-AP3-PDS-5830	Install Elec. Hangers - PDS Room 6097 - INTF - AP 3	2d	21-Jan-27	22-Jan-27	1d
RI-C11-R1-6150	Install Duct Hangers - Overall/Restrooms - INTR - C11	2d	22-Jan-27	25-Jan-27	7d
GI-FS-SQK-SOMD-20	FRP Pour 1 Concourse - SEQ KILO - SOMD	6d	25-Jan-27	01-Feb-27	0d
RI-AP3-PDS-5840	Install Fireproofing - PDS Room 6097 - INTF - AP 3	5d	25-Jan-27	29-Jan-27	1d
RI-C2-SP-1360	Install Metal Panel Support Hat Channel- SMP/Train Tube - INTR - C2	4d	25-Jan-27	28-Jan-27	0d
RI-C11-R1-6160	Install CHW Hangers - Overall/Restrooms - INTR - C11	2d	26-Jan-27	27-Jan-27	7d
RI-C11-R1-6170	Install Plumbing Hangers - Overall/Restrooms - INTR - C11	5d	28-Jan-27	03-Feb-27	7d
BI-ROW-BR-P7-70	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS7 [01-03-01]	15d	28-Jan-27	17-Feb-27	9d
D1862	Mech Install (Sector J) [01-03-01]	30d	28-Jan-27	10-Mar-27	0d
RI-C2-SP-1400	Metal Panel Wall System Scan - SMP/Train Tube - INTR - C2	5d	29-Jan-27	04-Feb-27	0d
RI-AP3-PDS-5860	Install CHW OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	01-Feb-27	05-Feb-27	1d
RI-AP3-PDS-5870	Install Plumbing OH Rough-in - PDS Room 6097 - INTF - AP 3	2d	01-Feb-27	02-Feb-27	1d
GI-FS-SQK-SOMD-40	FRP Pour 2 Concourse - SEQ KILO - SOMD	6d	02-Feb-27	09-Feb-27	0d

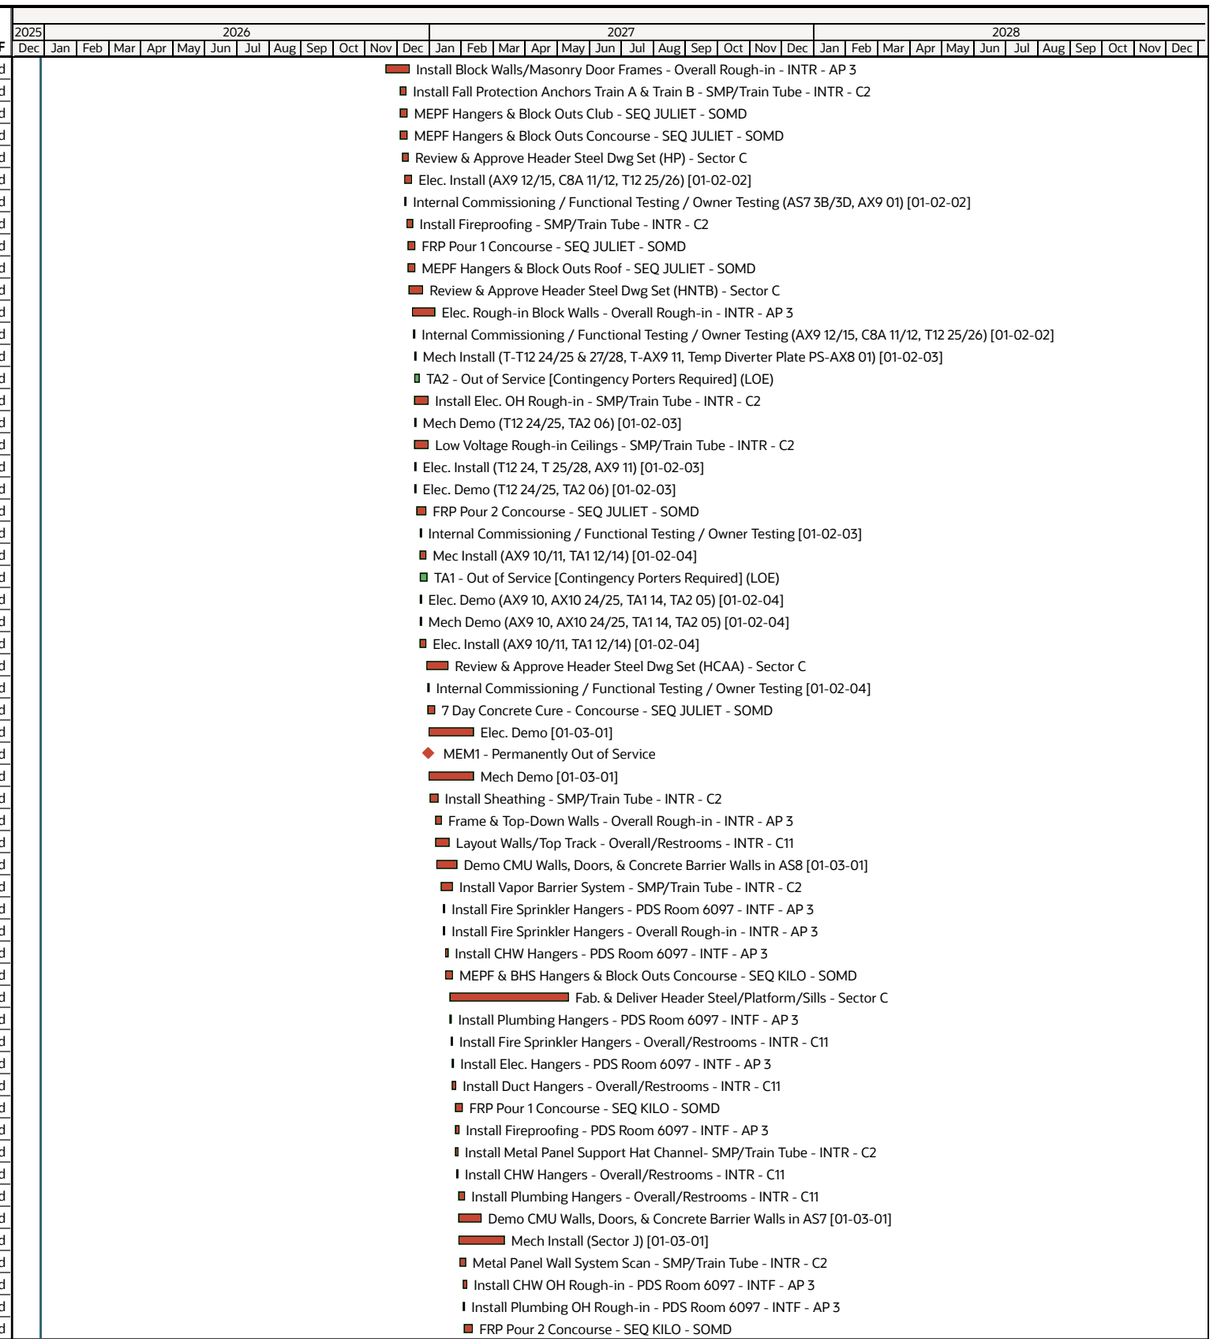

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
RI-C11-R1-6180	Install Elec. Hangers - Overall/Restrooms - INTR - C11	2d	04-Feb-27	05-Feb-27	7d
RI-C2-SP-1410	Metal Panel Wall System Fab. - SMP/Train Tube - INTR - C2	20d	05-Feb-27	04-Mar-27	0d
GI-FS-SQL-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ LIMA - SOMD	6d	08-Feb-27	15-Feb-27	0d
RI-AP3-PDS-5880	Install Duct OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	08-Feb-27	12-Feb-27	1d
RI-C11-R1-6190	Install Fireproofing - Overall/Restrooms - INTR - C11	3d	08-Feb-27	10-Feb-27	7d
GI-FS-SQK-SOMD-50	FRP Pour 3 Concourse - SEQ KILO - SOMD	6d	10-Feb-27	17-Feb-27	0d
RI-C11-R1-6250	Fire Sprinkler Mains & Branch Line Rough-in - Overall/Restrooms - INTR - C11	10d	11-Feb-27	24-Feb-27	7d
RI-AP3-PDS-5890	Fire Sprinkler Mains & Branch Line Rough-in - PDS Room 6097 - INTF - AP 3	5d	15-Feb-27	19-Feb-27	1d
GI-FS-SQL-SOMD-30	FRP Pour 1 Concourse - SEQ LIMA - SOMD	6d	16-Feb-27	23-Feb-27	0d
GI-FS-SQK-SOMD-60	FRP Pour 4 Concourse - SEQ KILO - SOMD	6d	18-Feb-27	25-Feb-27	0d
BI-ROW-BR-P7-130	Demo BHS Access Platform in AS7 [01-03-01]	3d	18-Feb-27	22-Feb-27	9d
RI-AP3-PDS-5910	Install Elec. OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	22-Feb-27	26-Feb-27	1d
GI-FS-SQM-SOMD-50	MEPF Hangers & Block Outs Concourse - SEQ MIKE - SOMD	6d	23-Feb-27	02-Mar-27	0d
BI-ROW-BR-P7-140	Patch & Seal Concrete @ Former BHS Access Platform in AS7 [01-03-01]	3d	23-Feb-27	25-Feb-27	9d
GI-FS-SQL-SOMD-40	FRP Pour 2 Concourse - SEQ LIMA - SOMD	6d	24-Feb-27	03-Mar-27	0d
RI-C11-R1-6210	Install CHW OH Rough-in - Overall/Restrooms - INTR - C11	8d	25-Feb-27	08-Mar-27	9d
RI-C11-R1-6200	Install Plumbing OH Rough-in - Overall/Restrooms - INTR - C11	10d	25-Feb-27	10-Mar-27	7d
GI-FS-SQK-SOMD-80	7 Day Concrete Cure - Concourse - SEQ KILO - SOMD	7d	26-Feb-27	04-Mar-27	0d
RI-AP3-PDS-5930	FRP Alstom PDS Elec. Pads - PDS Room 6097 - INTF - AP 3	5d	01-Mar-27	05-Mar-27	1d
RI-AP3-PDS-5920	Install Low Voltage OH Rough-in - PDS Room 6097 - INTF - AP 3	2d	01-Mar-27	02-Mar-27	4d
GI-FS-SQM-SOMD-70	FRP Pour 1 Concourse - SEQ MIKE - SOMD	6d	03-Mar-27	10-Mar-27	0d
GI-FS-SQL-SOMD-50	7 Day Concrete Cure - SEQ LIMA - SOMD	7d	04-Mar-27	10-Mar-27	0d
RI-C8-2520	Dancefloor Install Phase 2 - Overall - INTR - C8 Ph2	33d	05-Mar-27	20-Apr-27	0d
FN-C2-SP-1440	Install Metal Wall Panels - SMP/Train Tube - INTR - C2	20d	05-Mar-27	01-Apr-27	0d
GI-FS-SQH-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ HOTEL - SOMD	6d	05-Mar-27	12-Mar-27	10d
RI-AP3-PDS-5990	Patch Fireproofing - PDS Room 6097 - INTF - AP 3	2d	08-Mar-27	09-Mar-27	1d
FN-AP3-PDS-660	Prime & One Coat Paint - PDS Room 6097 - INTF - AP 3	5d	10-Mar-27	16-Mar-27	1d
GI-FS-SQL-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ LIMA - SOMD	6d	11-Mar-27	18-Mar-27	0d
GI-FS-SQM-SOMD-80	FRP Pour 2 Concourse - SEQ MIKE - SOMD	6d	11-Mar-27	18-Mar-27	0d
RI-C11-R1-6220	Install Duct OH Rough-in - Overall/Restrooms - INTR - C11	8d	11-Mar-27	22-Mar-27	7d
D1867	Mech Install (Sector H) [01-03-01]	75d	11-Mar-27	24-Jun-27	0d
GI-FS-SQH-SOMD-30	FRP Pour 1 Concourse - SEQ HOTEL - SOMD	6d	15-Mar-27	22-Mar-27	10d
FN-AP3-PDS-680	Install Doors & Hardware - PDS Room 6097 - INTF - AP 3	2d	17-Mar-27	18-Mar-27	1d
SK-RO-450	Install TPO Roofing - Mid Roof TPO 1.A	15d	19-Mar-27	08-Apr-27	0d
FN-AP3-PDS-690	Install Light Fixtures & Trim - PDS Room 6097 - INTF - AP 3	5d	19-Mar-27	25-Mar-27	1d
FN-AP3-PDS-800	Install Coil Roll-Up Doors (6097E & 6097C) - PDS Room 6097 - INTF - AP 3	5d	19-Mar-27	25-Mar-27	10d
GI-FS-SQM-SOMD-90	7 Day Concrete Cure - SEQ MIKE - SOMD	7d	19-Mar-27	25-Mar-27	0d
GI-FS-SQH-SOMD-40	FRP Pour 2 Concourse - SEQ HOTEL - SOMD	6d	23-Mar-27	30-Mar-27	10d
RI-C11-R1-6230	Install Elec. OH Rough-in - Overall Rough-in - INTR - C11	15d	23-Mar-27	12-Apr-27	7d
FN-AP3-PDS-710	Install Fire Alarm Trim - PDS Room 6097 - INTF - AP 3	2d	26-Mar-27	29-Mar-27	5d
GI-FS-SQM-SOMD-60	MEPF Hangers & Block Outs Roof - SEQ MIKE - SOMD	6d	26-Mar-27	02-Apr-27	0d
FN-AP3-PDS-720	Install Low Volt Trim - PDS Room 6097 - INTF - AP 3	2d	26-Mar-27	29-Mar-27	1d
FN-AP3-PDS-730	Install Mech. Trim - PDS Room 6097 - INTF - AP 3	2d	30-Mar-27	31-Mar-27	1d
FN-AP3-PDS-750	Install BCU -1-6097 - PDS Room 6097 - INTF - AP 3	2d	01-Apr-27	02-Apr-27	1d
FN-AP3-PDS-700	Install Fire Protection Trim - PDS Room 6097 - INTF - AP 3	2d	01-Apr-27	02-Apr-27	1d
FN-C2-SP-1290	Install Ceiling Light Fixtures & Trim - SMP/Train Tube - INTR - C2	5d	02-Apr-27	08-Apr-27	0d
FN-AP3-PDS-760	Install RF Flooring & Base - PDS Room 6097 - INTF - AP 3	3d	05-Apr-27	07-Apr-27	1d
SK-RO-460	Install ISO Board & Peel & Stick - High Roof Metal - Phase 1.A	15d	05-Apr-27	23-Apr-27	0d
GI-FS-SQH-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ HOTEL - SOMD	6d	07-Apr-27	14-Apr-27	10d
MLS-1010	MLS - Alstom PDS/UPS Rooms Complete	0d		07-Apr-27	1d
MLS-1000	MLS - Alstom Train Tubes Complete	0d		08-Apr-27	0d
SK-RO-60	Install TPO Roofing - Mid Roof TPO 1.B	15d	09-Apr-27	29-Apr-27	0d
RI-C11-R1-6300	Install BAS OH Rough-in - Overall Rough-in - INTR - C11	10d	13-Apr-27	26-Apr-27	7d
GI-FS-SQH-SOMD-50	FRP Pour 2 Ster. Corr. - SEQ HOTEL - SOMD	6d	15-Apr-27	22-Apr-27	10d
RI-C8-2530	Dancefloor Install Phase 3 - Overall - INTR - C8 Ph3	36d	21-Apr-27	10-Jun-27	0d
RI-C2-1450	Install Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1-1	7d	26-Apr-27	04-May-27	0d
RI-C11-R1-6270	Install CHW Insulation - Overall/Restrooms - INTR - C11	5d	27-Apr-27	03-May-27	7d
VC-ESC-AP5-2280	Set Escalator Trusses - Escalator (#3 & #4) - INTR - AP 5	5d	30-Apr-27	06-May-27	0d

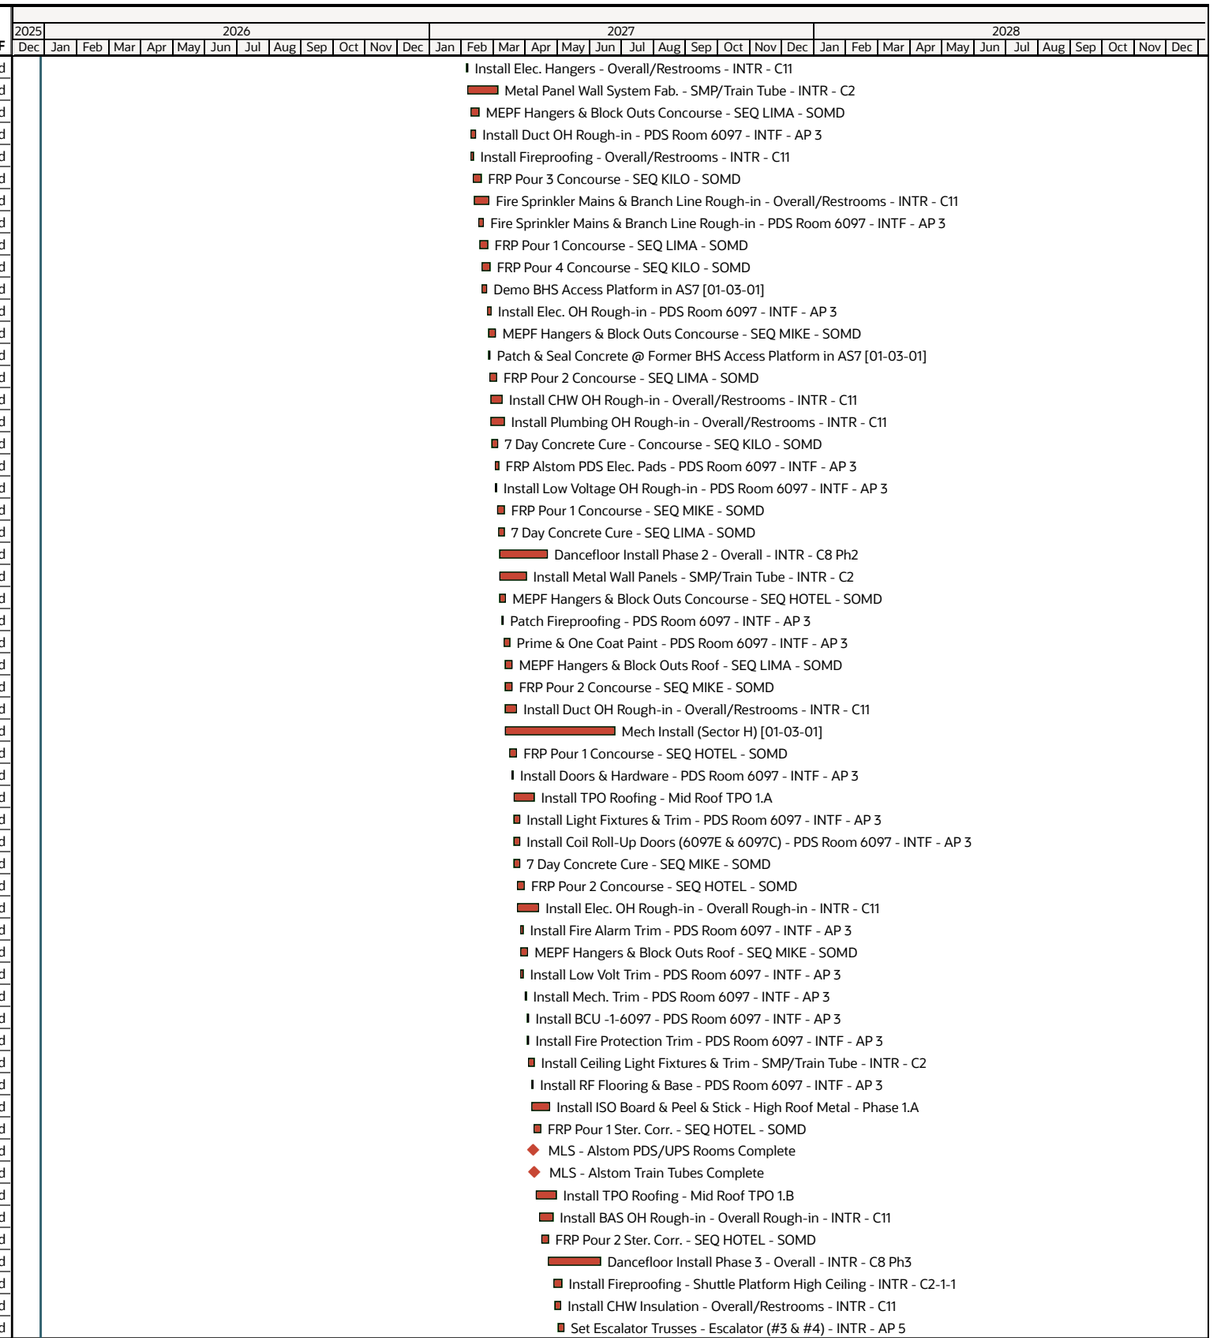

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
MLS-SK-RO-370	Quadrant 2 Structure Ready for Precast - Exterior Roof & Facade	0d	30-Apr-27		10d
RI-C11-R1-6280	Install Plumbing Insulation - Overall/Restrooms - INTR - C11	5d	04-May-27	10-May-27	7d
RI-C2-1560	Install Dancefloor - Shuttle Platform High Ceiling - INTR - C2-1	11d	05-May-27	19-May-27	0d
SK-Q2-LO-30	Exterior CFMF Framing (Eave/Gutter/Wall) - Q2 Lower	20d	07-May-27	04-Jun-27	0d
BG-AP9-BS-10	Layout & Install Hangers & Steel - AP9	32d	11-May-27	24-Jun-27	0d
RI-C11-R1-1930	Frame & Top-Down Walls - Overall/Restrooms - INTR - C11	15d	11-May-27	01-Jun-27	7d
RI-C2-1340	Install Elec. OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15d	20-May-27	10-Jun-27	0d
D1879	Elec. MPP Install (MPP-XBM1-A 13 Enclosures) [01-03-01]	120d	27-May-27	15-Nov-27	7d
D1880	Elec. Install (XBM1 Cross Belt) [01-03-01]	120d	27-May-27	15-Nov-27	7d
SK-Q2-LO-60	Install Exterior Sheathing (Eave/Gutter/Wall) - Q2 Lower	10d	28-May-27	11-Jun-27	0d
SK-Q2-LO-80	Air Barrier (Eave/Gutter/Wall) - Q2 Lower	10d	07-Jun-27	18-Jun-27	0d
RI-C2-1310	Low Voltage Rough-in Ceilings - Shuttle Platform High Ceiling - INTR - C2-1	15d	11-Jun-27	01-Jul-27	0d
RI-C8-2470	Dancefloor Install Phase 1 - Overall - INTR - C8 Ph1	31d	11-Jun-27	26-Jul-27	0d
RI-C2-1520	Install BAS OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15d	11-Jun-27	01-Jul-27	0d
SK-Q1-LO-580	Metal Panel Wall System Scan - Q2 Lower	5d	21-Jun-27	25-Jun-27	0d
D1870	Mech Install (Sector G) [01-03-01]	35d	25-Jun-27	13-Aug-27	0d
RI-AP9-3700	Patch Fireproofing - Overall Rough-in - INTR - AP 9	5d	25-Jun-27	01-Jul-27	0d
D1869	Elec. Install (Sector G) [01-03-01]	33d	25-Jun-27	11-Aug-27	2d
SK-Q2-LO-190	Curtain Wall System - Q2.A Lower	16d	28-Jun-27	20-Jul-27	0d
RI-C2-1320	Fire Sprinkler Mains & Branch Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	8d	02-Jul-27	14-Jul-27	0d
RI-AP9-3380	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 9	3d	02-Jul-27	07-Jul-27	0d
RI-AP4-1420	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 4	15d	08-Jul-27	28-Jul-27	5d
RI-AP9-3390	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 9	10d	15-Jul-27	28-Jul-27	0d
RI-C2-1360	Frame & Top-Down High Walls - Shuttle Platform High Ceiling - INTR - C2-1	10d	15-Jul-27	28-Jul-27	0d
D1871	Internal Commissioning / Functional Testing (Main Terminal Core) [01-03-01]	30d	19-Jul-27	27-Aug-27	0d
SK-Q1-UP-630	Curtain Wall System - Q1 Upper	5d	21-Jul-27	27-Jul-27	0d
SK-Q2-LO-120	Curtain Wall System - Q2.B Lower	15d	21-Jul-27	10-Aug-27	0d
RI-C8-2570	Install Elec. Hangers - Phase 1 - C8 Ph1	5d	27-Jul-27	02-Aug-27	0d
RI-C8-2560	Install Fire Sprinkler Hangers - Phase 1 - C8 Ph1	5d	27-Jul-27	02-Aug-27	0d
SK-Q1-UP-640	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q1 Upper	20d	28-Jul-27	24-Aug-27	0d
RI-C2-1470	Install Sign Supports & Backing - Shuttle Platform High Ceiling - INTR - C2-1	5d	29-Jul-27	04-Aug-27	0d
RI-AP4-1430	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 4	10d	29-Jul-27	11-Aug-27	5d
RI-AP9-3400	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 9	10d	29-Jul-27	11-Aug-27	0d
RI-C8-2580	Install Low Voltage Hangers - Phase 1 - C8 Ph1	5d	29-Jul-27	04-Aug-27	0d
RI-C8-2610	Fire Sprinkler Mains & Branch Rough-in - Overall - INTR - C8 Ph1	20d	03-Aug-27	30-Aug-27	2d
RI-C8-2590	Install Elec. OH Rough-in - Overall Rough-in - INTR - C8 Ph1 Ph1	20d	03-Aug-27	30-Aug-27	2d
RI-C8-2600	Low Voltage Rough-in Ceilings - Overall - INTR - C8 Ph1	15d	05-Aug-27	25-Aug-27	5d
RI-C8-3080	Frame Drywall Ceiling - Inner Soffit - Phase 1 - C8 Ph1	20d	05-Aug-27	01-Sep-27	0d
RI-C2-1260	Elec. Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5d	05-Aug-27	11-Aug-27	0d
RI-C8-3090	Install ACT Ceiling Grid Supports - Phase 1 - C8 Ph1	20d	05-Aug-27	01-Sep-27	0d
SK-Q2-LO-130	Install Doors & Windows - Q2 Lower	10d	11-Aug-27	24-Aug-27	0d
RI-C2-1210	Install Wall Insulation - Overall Rough-in - INTR - C2	5d	11-Aug-27	17-Aug-27	5d
U&P-UND-60	Install Underground Storm S-806 to S-825 (Inc Roof & Condensate Pipes) - Quadrant 2	15d	11-Aug-27	31-Aug-27	0d
RI-AP4-5820	Install CHW/Glycol OH Rough-in - Overall Rough-in - INTR - AP 4	5d	12-Aug-27	18-Aug-27	5d
RI-AP9-3410	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 9	20d	12-Aug-27	09-Sep-27	0d
RI-C2-1300	Low Voltage Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5d	12-Aug-27	18-Aug-27	0d
FN-C2-SRR-940	Insulate Ceilings & Soffits - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5d	18-Aug-27	24-Aug-27	5d
RI-C2-1350	Patch Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1	2d	19-Aug-27	20-Aug-27	0d
RI-AP4-1440	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 4	10d	19-Aug-27	01-Sep-27	5d
D1875	Owner Testing (Main Terminal Core) [01-03-01]	10d	23-Aug-27	03-Sep-27	0d
RI-C2-1460	Install Wall Insulation - Shuttle Platform High Ceiling - INTR - C2-1	5d	23-Aug-27	27-Aug-27	0d
MLS-920	MLS - Temp Building Conditioning Available	0d		24-Aug-27	0d
MLS-SUPP.C-09	MLS 9 - Building Dry-in Complete - Exterior Roof & Facade	0d		24-Aug-27 C	0d
FN-C2-SRR-970	Hang Hard Lid Ceilings - Support RR - INTF - C2	2d	25-Aug-27	26-Aug-27	5d
FN-AP7-ER-610	Hang, Tape & Finish Drywall - Dist. Elec. Room 6197 - INTRF - AP 7	15d	25-Aug-27	15-Sep-27	0d
FN-MC1-MR-200	Hang, Tape & Finish Drywall - Mech. Room - INTF - Club 1	15d	25-Aug-27	15-Sep-27	10d
FN-C2-SR-1260	Hang Drywall Walls - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	27-Aug-27	02-Sep-27	5d
FN-C2-CL-520	Hang Drywall Walls - Delta Airlines Club Entry/In-Flight Lounge - INTF - C2	5d	27-Aug-27	02-Sep-27	5d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
FN-C2-SP-1490	Install High Ceiling Grid - APM Platform Area - INTF - C2	5d	30-Aug-27	03-Sep-27	0d
U&P-UND-70	Install Underground Sanitary MH-202 to S-201 - Quadrant 2	20d	01-Sep-27	29-Sep-27	0d
RI-C8-2540	Frame Drywall Ceiling - Outter Soffit - Phase 1 - C8 Ph1	20d	02-Sep-27	30-Sep-27	0d
FN-C2-SRR-960	Hang Drywall Walls - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	10d	03-Sep-27	17-Sep-27	5d
BI-ROW-BR-P4-20	Demo Exist. Free-Standing Bollards Surrounding AS1 thru AS4 & Existing Elec. Room [01-03-03]	10d	07-Sep-27	20-Sep-27	5d
A109160	Fire Protection Systems Modifications [01-03-02]	5d	07-Sep-27	13-Sep-27	10d
B7	BHS - Mech / Elec. Demo & Install of AS3 CBRA Loop (01-03-02)	11d	07-Sep-27	21-Sep-27	0d
A109170	Elec. Systems Modifications [01-03-02]	5d	07-Sep-27	13-Sep-27	10d
BI-ROW-BR-P4-30	Install Temp Lighting in AS4 [01-03-03]	3d	07-Sep-27	09-Sep-27	5d
FN-C2-SP-1210	Install Device Tiles High - APM Platform Area - INTF - C2	5d	07-Sep-27	13-Sep-27	0d
A7	BHS - Mech / Elec. Demo & Install of T3 & BX2 Lines (01-03-02)	3d	07-Sep-27	09-Sep-27	0d
RI-AP4-1450	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 4	20d	10-Sep-27	07-Oct-27	0d
BI-ROW-BR-P4-40	Demo/Relocate Existing Elec. Devices, Lighting & Conduit (Including Attached to Platform) in AS4 [01-...	15d	10-Sep-27	30-Sep-27	6d
BI-ROW-BR-P4-80	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring (Including Attached to Platform) ...	15d	10-Sep-27	30-Sep-27	6d
FN-C2-SP-1430	Install High GFRP - APM Platform Area - INTF - C2	10d	14-Sep-27	27-Sep-27	0d
RI-MC1-IDF-7250	Hang, Tape & Finish Drywall - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5d	16-Sep-27	22-Sep-27	10d
FN-MC1-ER-3290	Hang, Tape & Finish Drywall - Elec. Room 6676 - INTRF - Club 1	5d	16-Sep-27	22-Sep-27	10d
FN-AP7-ER-620	Prime & First Coat - Dist. Elec. Room 6197 - INTRF - AP 7	5d	16-Sep-27	22-Sep-27	0d
RI-C8-1760	Install ACT Ceiling Grid - Phase 1 - C8 Ph1	20d	17-Sep-27	14-Oct-27	0d
FN-C1-O4-470	Hang Drywall - Delta Airlines Operations #4 - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-525	Hang Drywall - Concession Storage - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-685	Hang Drywall - Employee Port/Term. Mgr. Office - INTF - C1	2d	20-Sep-27	21-Sep-27	5d
FN-C1-O2-525	Hang Drywall - Un. Airline Ops. - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-250	Hang Drywall - Support Corr./HCAA Storage - INTF - Conc. 1	3d	20-Sep-27	22-Sep-27	5d
BI-ROW-BR-P3-30	Remove Moveable Concrete Barriers Along South Wall of AS3 [01-03-03]	1d	21-Sep-27	21-Sep-27	10d
BI-ROW-BR-P4-50	Patch & Seal Concrete @ Former Bollard Locations Outside of AS1 thru AS4 & Existing Elec. Room [01-...	5d	21-Sep-27	27-Sep-27	5d
BI-ROW-BR-P3-20	Demo Southeast Portion of EDS Platform for T-TXM2 ROW [01-03-03]	3d	21-Sep-27	23-Sep-27	10d
A104190	Delivery of TSA AS3 Temp EDS Machine	1d	22-Sep-27	22-Sep-27	0d
A104200	TSA Install of AS3 Temp EDS Machine	3d	23-Sep-27	27-Sep-27	0d
FN-AP7-ER-710	Install Door & Hardware - Dist. Elec. Room 6197 - INTRF - AP 7	2d	23-Sep-27	24-Sep-27	8d
FN-AP7-ER-640	Set Elec. Switchgear & Equip. - Dist. Elec. Room 6197 - INTRF - AP 7	10d	23-Sep-27	06-Oct-27	0d
FN-C3-SS-30	Hang Drywall Walls - SSCP Check Points - INTF - C3	5d	23-Sep-27	29-Sep-27	5d
BG-TST-270	Site Acceptance Test - AS3 Temp EDS Machine (SAT) (SUM) - BHS Testing & Integration	5d	28-Sep-27	04-Oct-27	0d
FN-C2-SP-1500	Install Low Ceiling Grid - APM Platform Area - INTF - C2	10d	28-Sep-27	11-Oct-27	0d
D1887	Internal Commissioning / Functional Testing (AS3 CBRA Loop Temp) [01-03-02]	5d	28-Sep-27	04-Oct-27	0d
U&P-UND-170	Install Underground Sanitary MH-201 to S-202 - Quadrant 2	5d	30-Sep-27	06-Oct-27	0d
RI-C3-IDF-6680	Hang, Tape & Finish Drywall - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5d	30-Sep-27	06-Oct-27	5d
BI-ROW-BR-P3-50	Install Temp Lighting in AS3 [01-03-03]	3d	01-Oct-27	05-Oct-27	10d
BI-ROW-BR-P4-120	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS4 [01-03-03]	15d	01-Oct-27	21-Oct-27	8d
BI-ROW-BR-P4-170	Demo Feeders to (3) EDS UPS Machines in AS4 [01-03-03]	5d	01-Oct-27	07-Oct-27	6d
BI-ROW-BR-P3-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring at T-TXM2 Opening on CMU Wal...	5d	01-Oct-27	07-Oct-27	6d
B8	BHS - Mech / Elec. Demo & Install of T5 / C5 [01-03-03]	2d	05-Oct-27	06-Oct-27	0d
D1903	Internal Commissioning / Functional Testing / Owner Testing (C5 06/08) [01-03-03]	1d	07-Oct-27	07-Oct-27	0d
RI-C1-MDF-6970	Hang, Tape & Finish Drywall - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5d	07-Oct-27	13-Oct-27	5d
RI-MC1-IDF-1060	Hang, Tape & Finish Drywall - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5d	07-Oct-27	13-Oct-27	5d
RI-C1-MDF-6480	Hang, Tape & Finish Drywall - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5d	07-Oct-27	13-Oct-27	5d
RI-AP7-ER-880	Install Elec. OH Rough-in - Dist. Elec. Room 6197 - INTRF - AP 7	15d	07-Oct-27	27-Oct-27	0d
U&P-UND-80	Install Building Roof Drain Laterals - Quadrant 2	5d	07-Oct-27	13-Oct-27	0d
D1905	Elec. Install MPP / FCP (A10, A11, A14, A15, B12, B16) [01-03-03]	16d	08-Oct-27	29-Oct-27	8d
RI-AP5-290	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 5	20d	08-Oct-27	04-Nov-27	0d
C9	BHS - Mech / Elec. Demo [01-03-03]	6d	08-Oct-27	15-Oct-27	0d
RI-C8-2620	Complete Fire Sprinkler OH Rough-in - Phase 1 - C8 Ph1	10d	08-Oct-27	21-Oct-27	0d
FN-C2-SP-1400	Install Device Tiles Low - APM Platform Area - INTF - C2	15d	12-Oct-27	01-Nov-27	0d
RI-C8-2630	Complete Elec. OH Rough-in - Phase 1 - C8 Ph1	10d	12-Oct-27	25-Oct-27	0d
U&P-GP-130	Install Underground Fire Protection STA-32+00 to STA-25+00 - Quadrant 2	10d	14-Oct-27	27-Oct-27	0d
FN-AP12-BAS-2020	Hang, Tape & Finish Drywall - INTF - BAS Control Room 6078 - AP12	15d	14-Oct-27	03-Nov-27	5d
RI-AP12-IDF-4980	Hang, Tape & Finish Drywall - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5d	14-Oct-27	20-Oct-27	5d
RI-C8-2640	Complete Low Voltage OH Rough-in - Phase 1 - C8 Ph1	5d	15-Oct-27	21-Oct-27	2d

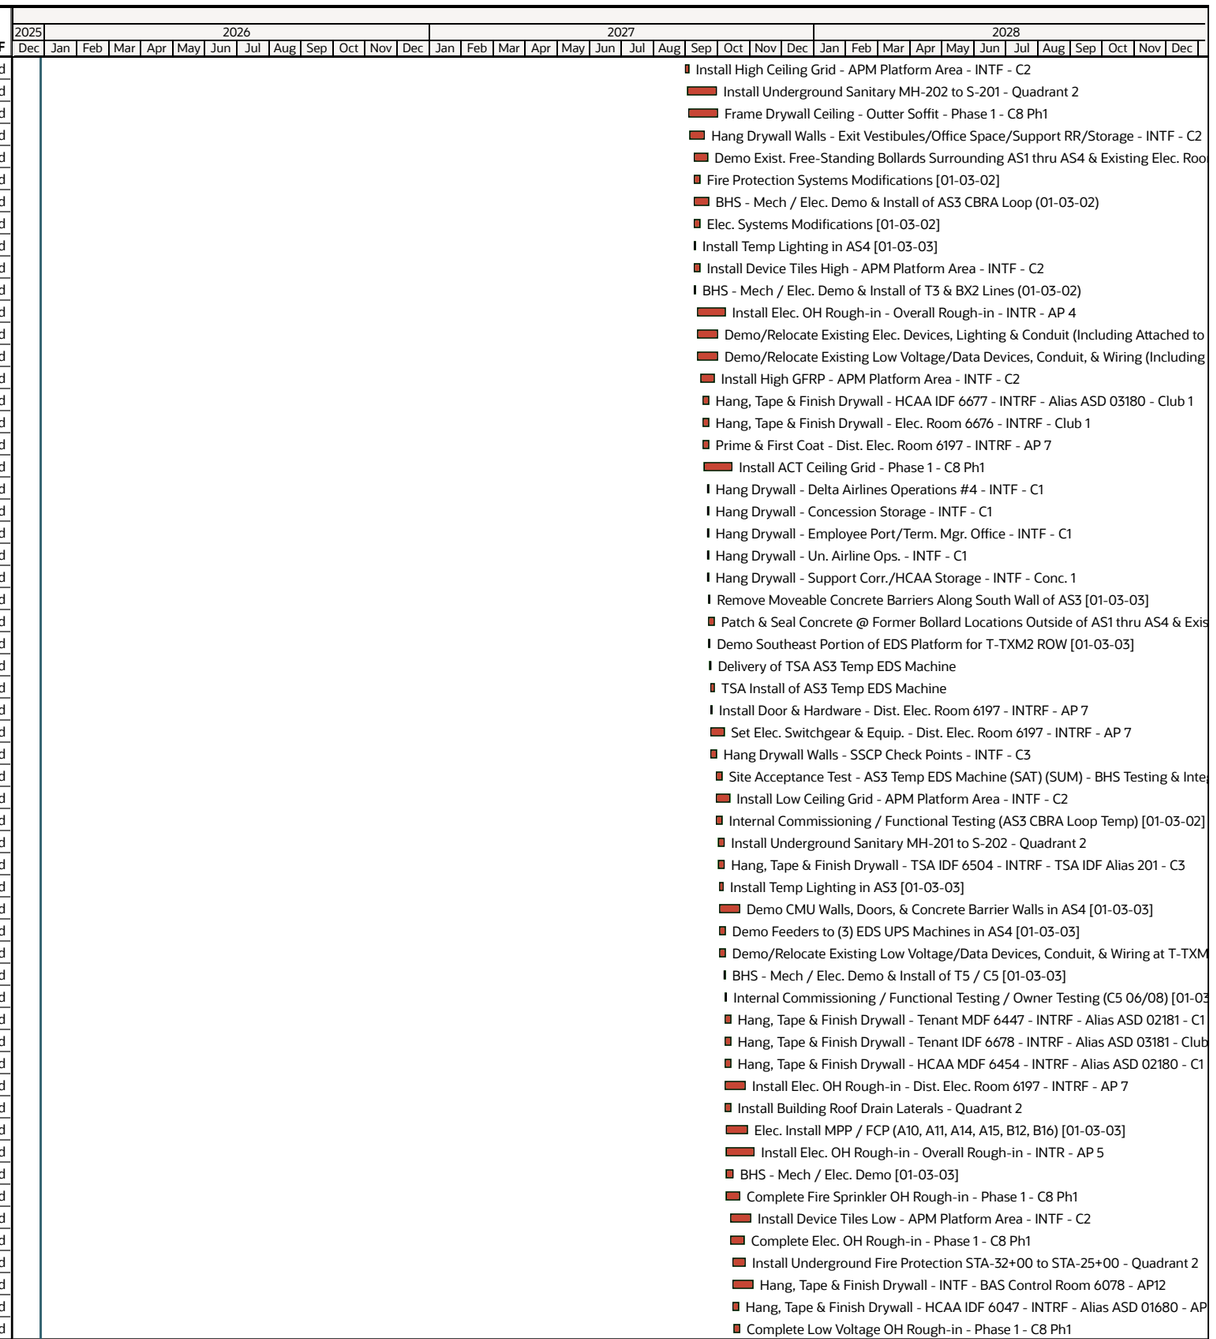

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
D9	BHS - Mech / Elec. Install [01-03-03]	13d	18-Oct-27	03-Nov-27	0d
BI-ROW-BR-P4-140	Demo & Remove AHU-B11, Associated Ductwork, & Associated Chilled Water Piping [01-03-03]	5d	22-Oct-27	28-Oct-27	8d
RI-C8-2550	Hang, Tape & Finish Drywall Ceiling - Phase 1 - C8 Ph1	20d	26-Oct-27	22-Nov-27	0d
FN-AP7-ER-650	Install Elec. Panels & Transformers - Dist. Elec. Room 6197 - INTRF - AP 7	10d	28-Oct-27	10-Nov-27	0d
U&P-GP-60	VDGS Found. & Conduit - Quadrant 2	10d	28-Oct-27	10-Nov-27	0d
BI-ROW-BR-P4-150	Demo Housekeeping Pad Beneath Former AHU-B11 [01-03-03]	2d	29-Oct-27	01-Nov-27	8d
BI-ROW-BR-P4-160	Patch & Seal Concrete @ Former AHU-B11 Housekeeping Pad [01-03-03]	3d	02-Nov-27	04-Nov-27	8d
FN-C2-SP-1530	Install Ceiling Light Fixtures & Low Trim - APM Platform Area - INTF - C2	15d	02-Nov-27	22-Nov-27	0d
FN-AP11-ER-2676	Hang, Tape & Finish Drywall - Dist. Elec. Room #6003 - INTF - AP 11	15d	04-Nov-27	24-Nov-27	5d
D1910	Internal Commissioning / Functional Testing [01-03-03]	7d	04-Nov-27	12-Nov-27	0d
RI-AP8-1900	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 8	20d	05-Nov-27	06-Dec-27	0d
RI-AP5-4760	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 5	10d	05-Nov-27	18-Nov-27	10d
FN-AP7-ER-655	Elec. Feeder Wire Measurements & Procurement - Dist. Elec. Room 6197 - INTRF - AP 7	10d	11-Nov-27	24-Nov-27	0d
D1914	Elec. Demo (T8 12/13) [01-03-03]	1d	15-Nov-27	15-Nov-27	0d
D1913	Mech Demo (T8 12/13) [01-03-03]	1d	16-Nov-27	16-Nov-27	0d
D1932	Commissioning / Testing (XBM1 Cross Belt) [01-03-04]	20d	16-Nov-27	15-Dec-27	7d
D1912	Mech Install (T8 12) [01-03-03]	2d	17-Nov-27	18-Nov-27	0d
D1915	Elec. Install (T8 12) [01-03-03]	2d	19-Nov-27	22-Nov-27	0d
D1917	Internal Commissioning / Functional Testing / Owner Testing (T8 12) [01-03-03]	1d	22-Nov-27	22-Nov-27	0d
RI-C8-1770	Install ACT Ceiling Device Tiles (Close-in) - Phase 1- C8 Ph1	10d	23-Nov-27	08-Dec-27	0d
FN-C2-SP-1220	Install Ceiling Light Fixtures & High Trim - APM Platform Area - INTF - C2	10d	23-Nov-27	08-Dec-27	0d
A10	BHS - Mech / Elec. Demo & Install of AS4 02/04, C9 10, T10 04/09, T11 04/09, T18 15/17 (01-03-04)	10d	23-Nov-27	08-Dec-27	0d
FN-AP8-ER-2510	Hang, Tape & Finish Drywall - Dist. Elec. Room 6290 - INTRF - AP 8	15d	29-Nov-27	17-Dec-27	5d
FN-AP7-ER-660	Pull & Terminate Elec. - Dist. Elec. Room 6197 - INTRF - AP 7	20d	29-Nov-27	27-Dec-27	0d
FN-CN-2410	Finish/Trim-Out High Ceiling Install - Overall - INTF - C8 Ph 1	20d	02-Dec-27	30-Dec-27	0d
RI-AP7-MR-458	Pull & Terminate to Mech. Equip. - Mech. Room - INTR - AP 7	10d	06-Dec-27	17-Dec-27	0d
RI-AP8-1890	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 8	10d	07-Dec-27	20-Dec-27	10d
RI-AP7-1380	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 7	20d	07-Dec-27	05-Jan-28	0d
RI-AP8-3060	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 8	20d	07-Dec-27	05-Jan-28	0d
B10	BHS - Inspection (01-03-04)	5d	09-Dec-27	15-Dec-27	0d
FN-C2-SP-1230	Drop Remaining Ceiling Tile High - APM Platform Area - INTF - C2	5d	09-Dec-27	15-Dec-27	0d
D1933	Owner Testing (XBM1 Cross Belt) [01-03-04]	4d	16-Dec-27	21-Dec-27	7d
C10	BHS - Mech / Elec. Demo & Install of T10 10/15, T11 10/12, TC2 02/04, MCP 04 & 35 (01-03-04)	10d	16-Dec-27	30-Dec-27	0d
RI-C8-3100	Install ACT Remaining Tiles (Close-in) - Phase 1- C8 Ph1	20d	16-Dec-27	14-Jan-28	0d
FN-C2-SP-1520	Drop Remaining Ceiling Tile Low - APM Platform Area - INTF - C2	10d	16-Dec-27	30-Dec-27	0d
RI-AP7-MR-570	Patch Fireproofing - Mech. Room - INTR - AP 7	5d	20-Dec-27	27-Dec-27	0d
D1934	Go Live (XBM1 Cross Belt) [01-03-04]	1d	22-Dec-27	22-Dec-27	7d
FN-AP7-MR-430	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 7	15d	28-Dec-27	18-Jan-28	0d
FN-C2-SP-1540	Hang High Drywall - APM Platform Area - INTF - C2	10d	03-Jan-28	14-Jan-28	0d
D1930	Internal Commissioning / Functional Testing / Owner Testing [01-03-04]	2d	03-Jan-28	04-Jan-28	0d
D1939	Elec. Install / Recontrol (T13 01/04) [01-03-05]	2d	04-Jan-28	05-Jan-28	1d
D1938	Mech Install (T13 05/06) [01-03-05]	1d	05-Jan-28	05-Jan-28	1d
D1936	Elec. Demo (T13 05/06) [01-03-05]	1d	05-Jan-28	05-Jan-28	0d
RI-AP7-1390	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 7	10d	06-Jan-28	19-Jan-28	0d
RI-AP8-1920	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 8	5d	06-Jan-28	12-Jan-28	0d
RI-AP7-2520	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 7	20d	06-Jan-28	02-Feb-28	0d
D1937	Mech Demo (T13 05/06) [01-03-05]	1d	06-Jan-28	06-Jan-28	0d
D1940	Internal Commissioning / Functional Testing / Owner Testing [01-03-05]	1d	07-Jan-28	07-Jan-28	0d
A11	BHS - Mech / Elec. Demo & Install of T14 06/10, OS1 07 (01-03-06)	26d	10-Jan-28	14-Feb-28	0d
FN-CN-2500	Apply Final Paint High Ceiling - Overall - INTF - C8 Ph 1	8d	12-Jan-28	21-Jan-28	0d
RI-AP8-1930	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	10d	13-Jan-28	26-Jan-28	0d
RI-AP8-1970	Elec. Rough-in Walls & Columns - Overall Rough-in - INTR - AP 8	10d	13-Jan-28	26-Jan-28	3d
FN-C2-SP-1550	Tape & Finish High Level Walls - APM Platform Area - INTF - C2	10d	17-Jan-28	28-Jan-28	0d
FN-AP6-ER-2540	Hang, Tape & Finish Drywall - Elec. Room 6200 - INTRF - AP 6	15d	19-Jan-28	08-Feb-28	0d
RI-AP7-1370	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 7	10d	20-Jan-28	02-Feb-28	0d
D1981	Elec. Install (XBM2 Cross Belt) [02-01-01C]	100d	24-Jan-28	12-Jun-28	2d
D1980	Mech Install (XBM2 Cross Belt) [02-01-01C]	100d	24-Jan-28	12-Jun-28	2d
RI-C8-2650	Dancefloor Removal Phase 1 - Overall - INTR - C8 Ph1	21d	24-Jan-28	21-Feb-28	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
RI-AP8-1960	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 8	3d	27-Jan-28	31-Jan-28	0d
RI-AP8-1940	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	3d	27-Jan-28	31-Jan-28	0d
FN-C2-SP-1560	Prime & One Coat High Walls - APM Platform Area - INTF - C2	7d	31-Jan-28	08-Feb-28	0d
FN-AP8-IB-2250	Install Wall Insulation - Baggage Claim 1 - INTF - AP 8	5d	01-Feb-28	07-Feb-28	0d
FN-AP8-IB-2240	Insulate Ceilings & Soffits - Baggage Claim 1 - INTF - AP 8	7d	01-Feb-28	09-Feb-28	8d
RI-AP7-1400	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 7	10d	03-Feb-28	16-Feb-28	2d
RI-AP7-1440	Install HM Door Frames - Overall Rough-in - INTR - AP 7	3d	03-Feb-28	07-Feb-28	9d
RI-AP7-1410	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 7	5d	03-Feb-28	09-Feb-28	0d
FN-AP8-IB-2270	Hang Drywall Walls - Baggage Claim 1 - INTF - AP 8	5d	08-Feb-28	14-Feb-28	5d
FN-AP8-PM-1700	Install Wall Insulation - CBP Primary - INTF - AP 8	5d	08-Feb-28	14-Feb-28	0d
FN-AP6-ER-2550	Prime & First Coat - Elec. Room 6200 - INTRF - AP 6	5d	09-Feb-28	15-Feb-28	0d
FN-C2-SP-1060	Trim Diffusers/Louvers - APM Platform Area - INTF - C2	5d	09-Feb-28	15-Feb-28	0d
RI-AP7-1430	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7d	10-Feb-28	18-Feb-28	0d
FN-AP8-IB-2260	Hang Hard Lid Ceilings - Baggage Claim 1 - INTF - AP 8	5d	15-Feb-28	21-Feb-28	5d
D1948	Internal Commissioning / Functional Testing / Owner Testing (T10 & T14) [01-03-06]	2d	15-Feb-28	16-Feb-28	0d
VC-EL-AP8-3110	Hang Machine Room Side 1st Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	15-Feb-28	16-Feb-28	0d
RI-C2-1490	Remove Dancefloor - APM Platform Area - INTF - C2	5d	16-Feb-28	22-Feb-28	0d
FN-AP6-ER-2570	Set Elec. Switchgear & Equip. - Elec. Room 6200 - INTRF - AP 6	10d	16-Feb-28	29-Feb-28	0d
D1953	Elec. Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-03-06]	3d	17-Feb-28	21-Feb-28	0d
VC-EL-AP8-3120	Inspect 1st Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	17-Feb-28	18-Feb-28	0d
D1952	Elec. MPP Install (MPP-B10, FCP-B10, MPP-B13, FCP-B13, MPP-B15, FCP-B15) [01-03-06]	45d	17-Feb-28	19-Apr-28	5d
D1954	Mech Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-03-06]	3d	17-Feb-28	21-Feb-28	0d
RI-AP7-1450	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 7	10d	21-Feb-28	03-Mar-28	0d
VC-EL-AP8-3130	Hang Machine Room Side 2nd Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	21-Feb-28	22-Feb-28	0d
D1955	Mech Install [01-03-06]	45d	22-Feb-28	24-Apr-28	0d
FN-AP8-PM-1720	Hang Drywall Walls - CBP Primary - INTF - AP 8	5d	22-Feb-28	28-Feb-28	5d
D1956	Elec. Install [01-03-06]	45d	22-Feb-28	24-Apr-28	0d
FN-CN-1630	Place Back 12 Line Grout Joint - Overall - INTF - C8 - Ph 1	5d	22-Feb-28	28-Feb-28	0d
VC-EL-AP8-3140	Tape/Finish 2 Hr Rated Wall - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	23-Feb-28	29-Feb-28	0d
FN-C2-SP-1580	Install Platform Level Ceiling Grid - APM Platform Area - INTF - C2	5d	23-Feb-28	29-Feb-28	0d
FN-CN-2570	Layout - Overall - INTF - C8 - Ph 1	5d	29-Feb-28	06-Mar-28	0d
VC-EL-AP8-2880	Install Elev. Safety Rail/Net - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	29-Feb-28	06-Mar-28	5d
RI-AP6-ER-2600	Install Elec. OH Rough-in - Elec. Room 6200 - INTRF - AP 6	20d	01-Mar-28	28-Mar-28	0d
VC-EL-AP8-3150	Frame 2 Hr Rated Lid with Shaft Liner - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	01-Mar-28	02-Mar-28	0d
FN-C2-SP-1570	Install Platform Level Device Tiles - APM Platform Area - INTF - C2	10d	01-Mar-28	14-Mar-28	0d
VC-EL-AP8-3160	Insulate Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	03-Mar-28	06-Mar-28	0d
RI-AP6-150	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 6	10d	06-Mar-28	17-Mar-28	10d
RI-AP7-2500	Install Ltg for Future Tenant Spaces - Overall Rough-in - INTR - AP 7	15d	06-Mar-28	24-Mar-28	1d
FN-AP7-SC-10	Install Wall Insulation - Overall/Support Corridors - INTF - AP 7	5d	06-Mar-28	10-Mar-28	0d
FN-CN-2540	Frame Interior Partitions - Overall - INTF - C8 - Ph 1	15d	07-Mar-28	27-Mar-28	0d
FN-CN-3190	Install Column Signage Supports/Backing - Overall - INTF - C8 - Ph 1	5d	07-Mar-28	13-Mar-28	10d
VC-EL-AP8-3170	Inspect Ceiling Insulation - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	07-Mar-28	08-Mar-28	0d
FN-CN-3240	Frame Column Covers - Overall - INTF - C8 - Ph 1	15d	07-Mar-28	27-Mar-28	0d
VC-EL-AP8-3020	Install Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	07-Mar-28	13-Mar-28	5d
VC-EL-AP8-3200	Hang 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	09-Mar-28	10-Mar-28	0d
FN-AP7-SC-20	Hang Drywall Walls - Overall/Support Corridors - INTF - AP 7	5d	13-Mar-28	17-Mar-28	10d
VC-EL-AP8-3190	Inspect 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	13-Mar-28	14-Mar-28	0d
FN-AP7-SD-1150	Install Wall Insulation - CBP Second. - INTF - AP 7	5d	13-Mar-28	17-Mar-28	0d
VC-EL-AP8-2890	Rough-in Elec. In Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	8d	14-Mar-28	23-Mar-28	5d
VC-EL-AP8-3180	Hang 2nd Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	15-Mar-28	16-Mar-28	0d
FN-C2-SP-1410	Drop Remaining Ceiling Tile - Platform Level - APM Platform Area - INTF - C2	10d	15-Mar-28	28-Mar-28	0d
VC-EL-AP8-3230	Tape/Finish Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	17-Mar-28	23-Mar-28	0d
FN-AP7-SR-200	Install Wall Insulation - CBP Support Restrooms - INTF - AP 7	5d	20-Mar-28	24-Mar-28	0d
FN-AP7-SC-30	Tape & Finish Walls - Overall/Support Corridors - INTF - AP 7	10d	20-Mar-28	31-Mar-28	10d
FN-AP7-SD-1170	Hang Drywall Walls - CBP Second. - INTF - AP 7	5d	20-Mar-28	24-Mar-28	10d
VC-EL-AP8-2920	Install Elev. Pit Ltg/Outlets - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	24-Mar-28	30-Mar-28	5d
VC-EL-AP8-3220	1st Coat Paint Machine Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	24-Mar-28	27-Mar-28	0d
VC-EL-AP8-2930	Install Temp Power for Elevator Release - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	24-Mar-28	30-Mar-28	10d

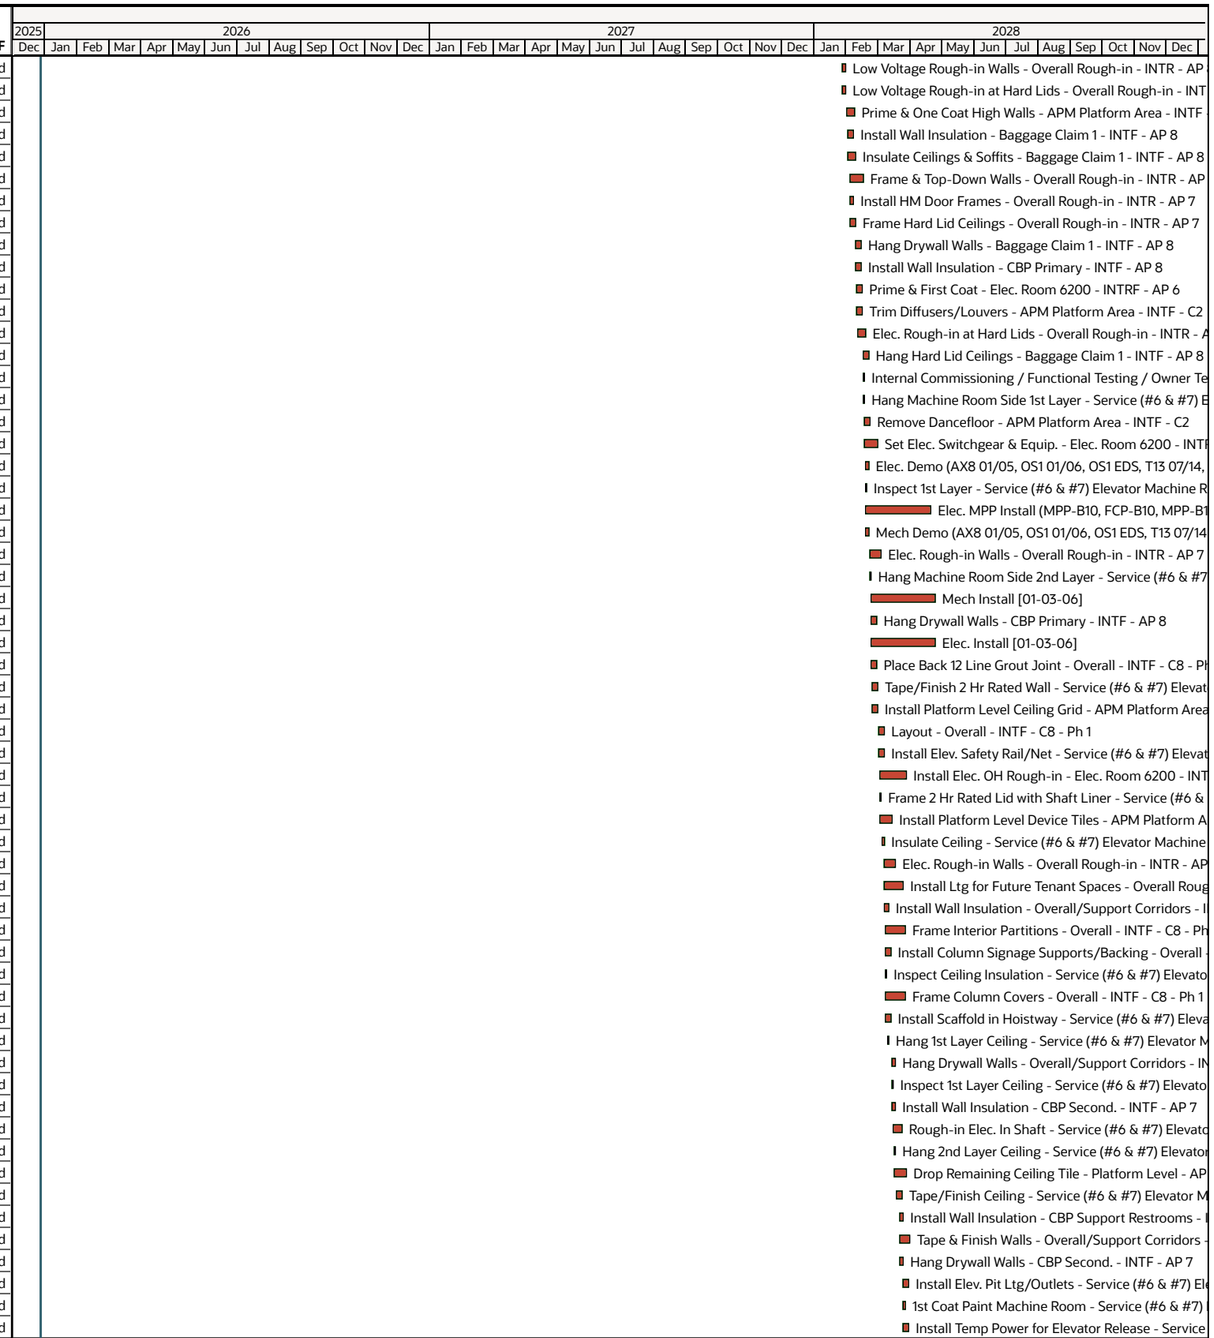

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
FN-AP7-O3-930	Install Wall Insulation - Delta Airlines Operations #2 & #3 - INTF - AP 7	5d	27-Mar-28	31-Mar-28	0d
RI-AP7-1420	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7d	27-Mar-28	04-Apr-28	1d
FN-AP7-SR-210	Hang Drywall Walls/Ceilings - CBP Support Restrooms - INTF - AP 7	5d	27-Mar-28	31-Mar-28	10d
VC-EL-AP8-3250	Install Door & Hardware - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	28-Mar-28	29-Mar-28	1d
FN-CN-2580	Elec. In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	28-Mar-28	10-Apr-28	0d
VC-EL-AP8-2900	Elec. Wall Rough Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	3d	28-Mar-28	30-Mar-28	0d
FN-AP6-ER-2580	Install Elec. Panels & Transformers - Elec. Room 6200 - INTRF - AP 6	15d	29-Mar-28	18-Apr-28	0d
FN-C2-SP-1480	Hang Platform Level Drywall - APM Platform Area - INTF - C2	10d	29-Mar-28	11-Apr-28	0d
VC-EL-AP8-3210	Set Elev. Controllers - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	30-Mar-28	05-Apr-28	1d
VC-EL-AP8-2910	Install Elec. OH Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	31-Mar-28	06-Apr-28	0d
VC-EL-AP8-3030	Remove Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	31-Mar-28	06-Apr-28	5d
FN-CN-2600	Low Voltage In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	31-Mar-28	13-Apr-28	0d
FN-AP7-SC-40	Prime & One Coat Walls - Overall/Support Corridors - INTF - AP 7	7d	03-Apr-28	11-Apr-28	10d
FN-AP6-CR-10	Install Wall Insulation - Overall - INTF - AP 6	5d	03-Apr-28	07-Apr-28	0d
FN-CN-2590	Fire Alarm In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	05-Apr-28	18-Apr-28	0d
FN-AP7-SD-1140	Insulate Ceilings & Soffits - CBP Second. - INTF - AP 7	7d	05-Apr-28	13-Apr-28	1d
VC-EL-AP8-3240	Install Elev. Pathways/Wire Elev. - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	10d	07-Apr-28	20-Apr-28	0d
FN-AP6-CR-220	Install Wall Insulation - CBP Secondary - INTF - AP 6	5d	10-Apr-28	14-Apr-28	0d
D1957	Internal Commissioning / Functional Testing / Owner Testing [01-03-06]	12d	11-Apr-28	26-Apr-28	0d
FN-AP7-SC-50	Install ACT Ceiling Grid - Overall/Support Corridors - INTF - AP 7	20d	12-Apr-28	09-May-28	10d
FN-C2-SP-1010	Tape & Finish Platform Level Walls - APM Platform Area - INTF - C2	10d	12-Apr-28	25-Apr-28	0d
FN-AP7-SD-1160	Hang Hard Lid Ceilings - CBP Second. - INTF - AP 7	5d	14-Apr-28	20-Apr-28	1d
VC-EL-AP8-2940	Install Elev. Rails - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	14-Apr-28	20-Apr-28	0d
FN-AP6-O2-220	Install Wall Insulation - Delta Airlines Operations #1- INTF - AP 6	5d	17-Apr-28	21-Apr-28	0d
FN-CN-2610	Hang, Tape & Finish Drywall Partitions - Overall - INTF - C8 - Ph 1	10d	19-Apr-28	02-May-28	0d
FN-AP6-ER-2590	Elec. Feeder Wire Measurements & Procurement - Elec. Room 6200 - INTRF - AP 6	10d	19-Apr-28	02-May-28	0d
VC-EL-AP8-3400	Set Elev. Equip. in Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	2d	21-Apr-28	24-Apr-28	0d
FN-AP7-SD-1180	Tape & Finish Ceilings - CBP Second. - INTF - AP 7	10d	21-Apr-28	04-May-28	6d
FN-AP7-O3-940	Hang Drywall Walls - Delta Airlines Operations #2 & #3 - INTF - AP 7	5d	21-Apr-28	27-Apr-28	1d
FN-AP6-CR-440	Install Wall Insulation - Exit Passageway 6195 - INTF - AP 6	5d	24-Apr-28	28-Apr-28	0d
VC-EL-AP8-3420	Install Hoistway Elec. Cabling - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	25-Apr-28	01-May-28	0d
VC-EL-AP8-3410	Install Platform & Weights - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	25-Apr-28	01-May-28	0d
FN-C2-SP-1020	Prime & One Coat Platform Level Walls - APM Platform Area - INTF - C2	7d	26-Apr-28	04-May-28	0d
D1960	Elec. Install (TA1 03/04 & 08/09) [02-01-01A]	2d	27-Apr-28	28-Apr-28	0d
FN-AP6-CR-230	Hang Drywall Walls - CBP Secondary - INTF - AP 6	5d	28-Apr-28	04-May-28	1d
FN-AP6-CR-450	Hang Drywall Walls - Exit Passageway 6195 - INTF - AP 6	5d	01-May-28	05-May-28	0d
D1961	Mech Demo (TA1 15/16 & 19) [02-01-01A]	1d	01-May-28	01-May-28	0d
VC-EL-AP8-3440	Install Elev. Doors - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3d	02-May-28	04-May-28	0d
VC-EL-AP8-3430	Install Elev. Equip in Pit - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	02-May-28	08-May-28	0d
D1962	Mech Install (TA1 03/04 & 08/09) [02-01-01A]	2d	02-May-28	03-May-28	0d
FN-AP6-ER-2600	Pull & Terminate Elec. - Elec. Room 6200 - INTRF - AP 6	20d	03-May-28	31-May-28	0d
FN-CN-2620	Install Terrazzo Flooring at Circ./Restroom Vestibules/Concessions Ph.1 - Overall - INTF - C8	20d	03-May-28	31-May-28	0d
D1963	Elec. Demo (TA1 15/16 & 19, MCP-13) [02-01-01A]	1d	04-May-28	04-May-28	0d
D1965	Internal Commissioning / Functional Testing / Owner Testing [02-01-01A]	1d	05-May-28	05-May-28	0d
FN-AP6-CR-250	Hang Drywall Ceilings - CBP Secondary - INTF - AP 6	5d	05-May-28	11-May-28	1d
FN-AP8-PM-2020	Field Measure & Fab. Decorative Glass Panels (Exterior EL-7 & EL-6) - CBP Primary - INTF - AP 8	70d	05-May-28	14-Aug-28	0d
FN-AP7-SD-1200	Apply Prime, First, Paint Ceilings - CBP Second. - INTF - AP 7	7d	05-May-28	15-May-28	6d
FN-C2-SP-1050	Install Terrazzo Flooring at APM/Circulation/SSCP Queue - APM Platform Area - INTF - C2	20d	05-May-28	02-Jun-28	0d
FN-AP6-CR-470	Hang Drywall Ceilings - Exit Passageway 6195 - INTF - AP 6	5d	08-May-28	12-May-28	0d
D1967	Elec. Demo (T12 26) [02-01-01B]	1d	08-May-28	08-May-28	0d
FN-AP6-O2-230	Hang Drywall Walls - Delta Airlines Operations #1- INTF - AP 6	5d	08-May-28	12-May-28	0d
D1968	Elec. Install (C8A 13) [02-01-01B]	1d	09-May-28	09-May-28	0d
D1969	Internal Commissioning / Functional Testing / Owner Testing [02-01-01B]	1d	10-May-28	10-May-28	0d
D1970	Mech Demo (T12 26) [02-01-01B]	1d	11-May-28	11-May-28	0d
D1971	Mech Install (C8A 13) [02-01-01B]	1d	12-May-28	12-May-28	0d
D1976	Elec. Conveyor Demo, MCP-07, MCP-09, MCP-17 (Reconnect ControlNet as Required) [02-01-01C]	5d	15-May-28	19-May-28	2d
FN-AP6-O2-240	Tape & Finish Walls - Delta Airlines Operations #1- INTF - AP 6	10d	15-May-28	26-May-28	0d
D1977	Elec. Install [02-01-01C]	20d	15-May-28	12-Jun-28	0d

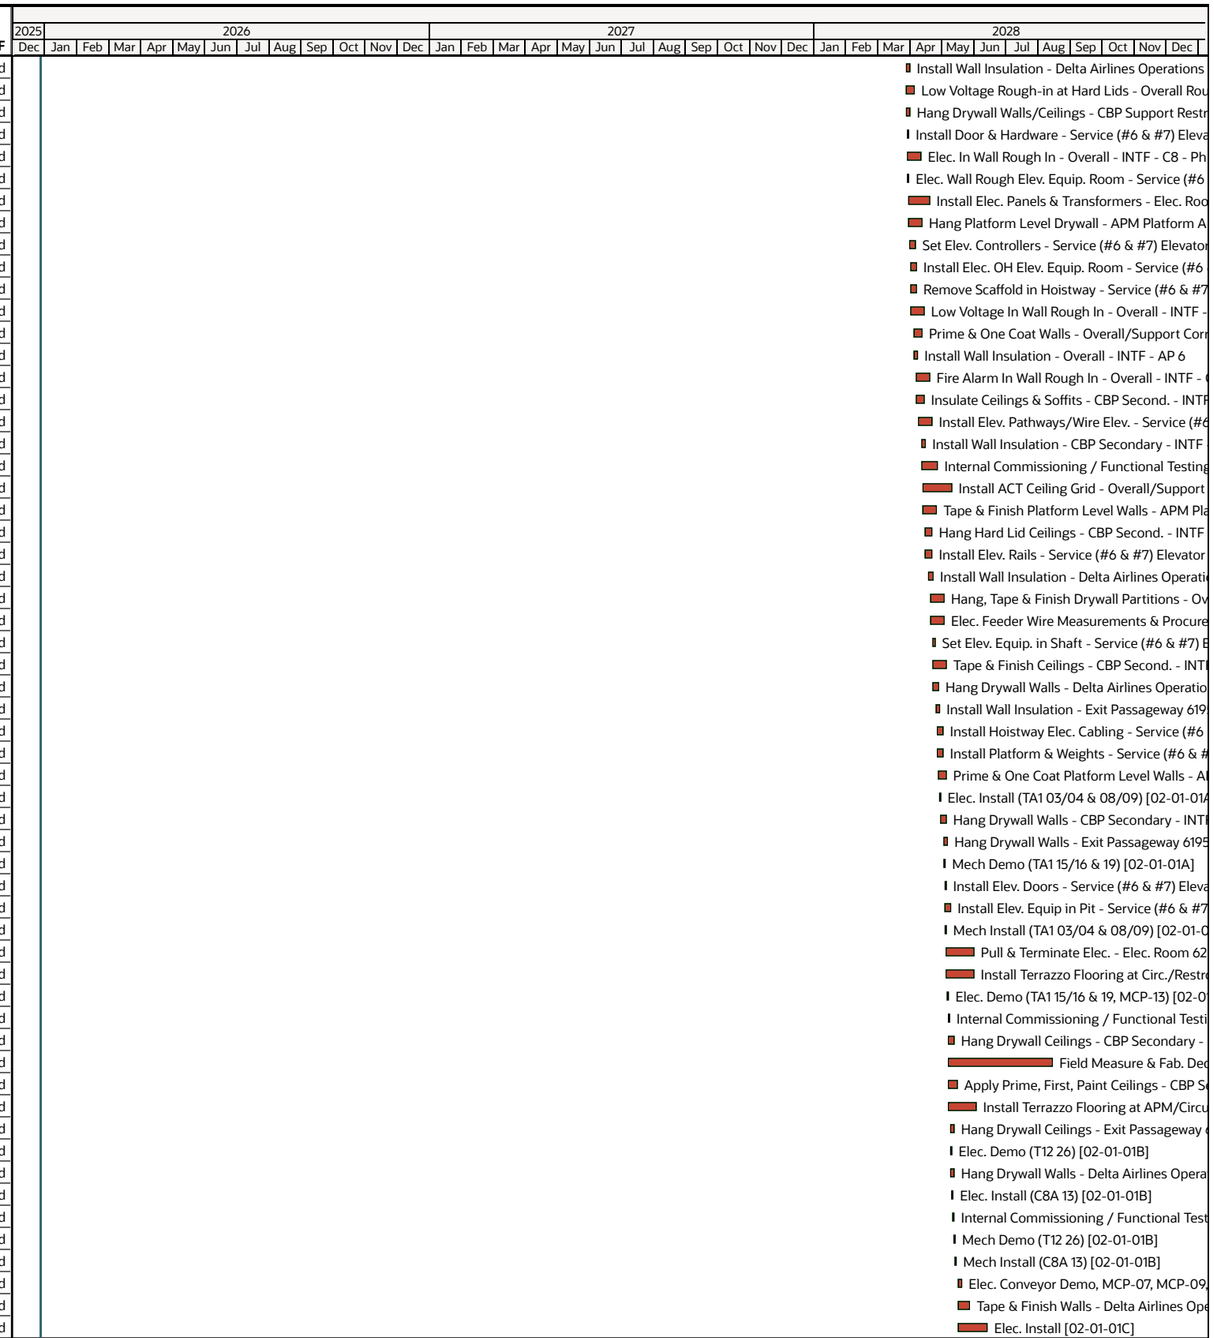

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
D1975	Mech Install [02-01-01C]	20d	15-May-28	12-Jun-28	0d
D1974	Mech Demo [02-01-01C]	5d	15-May-28	19-May-28	2d
FN-AP7-SD-1230	Install ACT Ceiling Grid - CBP Second. - INTF - AP 7	10d	16-May-28	30-May-28	6d
MLS-CN-20	Concessions News/Convenience C8.6 - Turnover C8	0d	25-May-28		4d
MLS-CN-170	Concessions Quick Serve C9.2 - Turnover C9	0d	25-May-28		4d
MLS-CN-160	Concessions Coffee C8.8 - Turnover C8	0d	25-May-28		4d
MLS-CN-180	Concessions Quick Serve C9.3 Turnover - C9	0d	25-May-28		4d
MLS-CN-10	Concessions Retail C8.1 - Turnover C8	0d	25-May-28		4d
MLS-CN-70	Concessions Retail C9.4 - Turnover C9	0d	25-May-28		4d
MLS-CN-190	Concessions Quick Serve C9.1 - Turnover C9	0d	25-May-28		4d
MLS-CN-50	Concessions Gourmet Market C8.5 - Turnover C8	0d	25-May-28		4d
MLS-CN-60	Concessions Retail C8.3 - Turnover C8	0d	25-May-28		4d
FN-AP6-O2-450	Install Doors & Hardware - Delta Airlines Operations #1- INTF - AP 6	3d	30-May-28	01-Jun-28	0d
FN-AP7-SD-1250	Install Ceiling Light Fixtures & Trim - CBP Second. - INTF - AP 7	10d	31-May-28	13-Jun-28	6d
MLS-CN-40	Concessions Retail C8.2 - Turnover C8	0d	01-Jun-28		0d
MLS-SUPP.C-10	MLS 10 - Concessions White Box	0d		01-Jun-28 C	0d
FN-CN-2660	Install Column Covers - Overall - INTF - C8 - Ph 1	36d	01-Jun-28	21-Jul-28	0d
MLS-CN-250	Concessions Future Retail C8.7 - Turnover C8	0d	01-Jun-28		0d
FN-AP6-ER-2610	Third Party Elec. Testing - Elec. Room 6200 - INTRF - AP 6	3d	01-Jun-28	05-Jun-28	0d
MLS-CN-130	Common Use Club Entry C11.1 - Turnover C11	0d	01-Jun-28		0d
MLS-AP-120	Delta Airlines Operations A6.1 Turnover - AP6	0d	02-Jun-28		0d
FN-C2-SP-1080	Install Column Covers at APM/Circulation - APM Platform Area - INTF - C2	10d	05-Jun-28	16-Jun-28	0d
FN-C2-SP-1030	Install Low Voltage Trim - APM Platform Area - INTF - C2	7d	05-Jun-28	13-Jun-28	3d
FN-C2-SP-1160	Install Fire Alarm Trim - APM Platform Area - INTF - C2	5d	05-Jun-28	09-Jun-28	10d
D1978	Internal Commissioning / Functional Testing / Owner Testing [02-01-01C]	7d	06-Jun-28	14-Jun-28	0d
FN-AP6-ER-2620	Install Light Fixtures & Trim - Elec. Room 6200 - INTRF - AP 6	10d	06-Jun-28	19-Jun-28	0d
FN-AP7-SD-1270	Install Low Voltage Trim - CBP Second. - INTF - AP 7	7d	14-Jun-28	22-Jun-28	6d
FN-AP7-SD-1410	Install Fire Alarm Trim - CBP Second. - INTF - AP 7	5d	14-Jun-28	20-Jun-28	10d
D1982	Commissioning / Testing (XBM2 Cross Belt) [02-01-01C]	20d	15-Jun-28	13-Jul-28	0d
FN-C2-SP-1100	Install Light Fixtures & Trim Walls/Columns - APM Platform Area - INTF - C2	5d	19-Jun-28	23-Jun-28	0d
FN-AP6-ER-2650	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Elec. Room 6200 - INTRF - AP 6	2d	20-Jun-28	21-Jun-28	0d
FN-AP7-SD-1280	Install Fire Protection Trim - CBP Second. - INTF - AP 7	3d	21-Jun-28	23-Jun-28	10d
FN-AP6-ER-2660	APG QC Procedure for Perm Power Available for Dist. - Elec. Room 6200 - INTRF - AP 6	15d	22-Jun-28	13-Jul-28	0d
FN-AP7-SD-1290	Drop Ceiling Tile - CBP Second. - INTF - AP 7	5d	23-Jun-28	29-Jun-28	6d
FN-C2-SP-1130	Install Low Voltage Trim Walls/Columns - APM Platform Area - INTF - C2	5d	26-Jun-28	30-Jun-28	0d
FN-C2-SP-1470	Install BAS Trim Walls/Columns - APM Platform Area - INTF - C2	5d	26-Jun-28	30-Jun-28	0d
FN-AP7-SD-1320	Install Access Floors - CBP Second. - INTF - AP 7	20d	30-Jun-28	28-Jul-28	6d
FN-C2-SP-1170	Install Fire Alarm Trim Walls/Columns - APM Platform Area - INTF - C2	5d	03-Jul-28	10-Jul-28	0d
FN-C2-SP-1110	Apply All Final Paint - APM Platform Area - INTF - C2	10d	11-Jul-28	24-Jul-28	0d
MLS-290	MLS - Permanent Power AP6 Elec. Room #6200	0d		13-Jul-28	0d
D1983	Owner Testing (XBM2 Cross Belt) [02-01-01C]	4d	14-Jul-28	19-Jul-28	0d
FN-CN-2640	Install Low Voltage Trim - Overall - INTF - C8 - Ph 1	5d	17-Jul-28	21-Jul-28	5d
D1984	Go Live (XBM2 Cross Belt) [02-01-01C]	1d	20-Jul-28	20-Jul-28	0d
A12	BHS - Mech / Elec. Demo & Install of C6 04/05 (02-01-2A)	3d	21-Jul-28	25-Jul-28	0d
FN-CN-2630	Install Elec. Trim - Overall - INTF - C8 - Ph 1	5d	24-Jul-28	28-Jul-28	0d
FN-CN-2650	Install Fire Alarm Trim - Overall - INTF - C8 - Ph 1	5d	24-Jul-28	28-Jul-28	0d
FN-C2-SR-1470	Apply Final Paint - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	25-Jul-28	31-Jul-28	0d
D1991	Internal Commissioning / Functional Testing / Owner Testing [02-01-02A]	1d	25-Jul-28	25-Jul-28	0d
A13	BHS - Mech / Elec. Demo & Install of T12E 01/03 [02-01-02B]	3d	26-Jul-28	28-Jul-28	0d
D2000	Internal Commissioning / Functional Testing / Owner Testing [02-01-02B]	1d	28-Jul-28	28-Jul-28	0d
FN-CN-2670	Terrazzo Final Polish at Circ./Restroom Vestibules/Concessions Ph.1 - Overall - INTF - C8	20d	31-Jul-28	25-Aug-28	0d
FN-AP7-SC-70	Install Flooring & Base - Overall/Support Corridors - INTF - AP 7	10d	31-Jul-28	11-Aug-28	6d
A14	BHS - Mech / Elec. Demo & Install of C5 17 (02-01-02C)	2d	31-Jul-28	01-Aug-28	0d
FN-C2-SR-1490	Install FF&E- HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	01-Aug-28	07-Aug-28	0d
D2007	Internal Commissioning / Functional Testing [02-01-02C]	1d	02-Aug-28	02-Aug-28	0d
A15	BHS - Mech / Elec. Demo & Install of C5 09/10, T8 11, OSRM6 01, OSRM7 01 (02-01-02D)	10d	03-Aug-28	16-Aug-28	0d
FN-C2-SR-1500	Install Signage - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	08-Aug-28	14-Aug-28	0d
FN-AP6-CR-380	Install Flooring & Base - CBP Secondary - INTF - AP 6	10d	14-Aug-28	25-Aug-28	6d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
FN-AP8-PM-2030	Install Decorative Glass (GL07A,B,C,D,E) - (Exterior EL-7 & EL-6) - CBP Primary - INTF - AP 8	15d	15-Aug-28	05-Sep-28	0d
FN-C3-SS-250	Install Signage - SSCP Check Points - INTF - C3	5d	15-Aug-28	21-Aug-28	0d
D2015	Internal Commissioning / Functional Testing / Owner Testing [02-01-02D]	2d	17-Aug-28	18-Aug-28	0d
A16	BHS - Mech / Elec. Demo & Install of T15 06, C8 11 (02-01-03A)	2d	21-Aug-28	22-Aug-28	0d
MLS-SUPP.C-12	MLS 12 - SSCP Area Ready for TSA Equipment	0d		21-Aug-28 C	0d
D2023	Internal Commissioning / Functional Testing / Owner Testing[02-01-03A]	1d	23-Aug-28	23-Aug-28	0d
A17	BHS - Mech / Elec. Demo & Install of C6A 03/13, C8A 02/10, ALM2 01/02, CLM2 06, OSRM5B 08/09 ...	16d	24-Aug-28	15-Sep-28	0d
FN-AP6-CR-390	Polish Exposed Concrete - CBP Secondary - INTF - AP 6	5d	28-Aug-28	01-Sep-28	6d
FN-AP6-CR-640	Install BAS Trim Walls - CBP Secondary - INTF - AP 6	5d	05-Sep-28	11-Sep-28	6d
FN-AP6-CR-400	Install Low Voltage Trim Walls - CBP Secondary - INTF - AP 6	5d	05-Sep-28	11-Sep-28	6d
FN-AP8-PM-1980	Terrazzo Final Polish - CBP Primary - INTF - AP 8	5d	06-Sep-28	12-Sep-28	0d
FN-AP6-CR-410	Apply Final Paint - CBP Secondary - INTF - AP 6	10d	12-Sep-28	25-Sep-28	6d
FN-AP8-PM-1880	Apply Final Paint - CBP Primary - INTF - AP 8	10d	13-Sep-28	26-Sep-28	0d
FN-FI-1540	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 11	12d	13-Sep-28	28-Sep-28	5d
D2029	Internal Commissioning / Functional Testing /Owner Testing [02-01-03B]	5d	18-Sep-28	22-Sep-28	0d
D2031	Internal Pre-TRR / Internal System Level Testing [02-01-03B]	20d	25-Sep-28	20-Oct-28	0d
COM-ELE-400	Lighting Controls Programming Interior/White Light- Light. Controls Elec. Commissioning	5d	26-Sep-28	02-Oct-28	10d
FN-AP6-CR-420	Install Signage - CBP Secondary - INTF - AP 6	5d	26-Sep-28	02-Oct-28	6d
ORAT-10	ORAT Initiation - Operational Readiness Activation & Transition (ORAT)	110d	26-Sep-28	02-Mar-29	0d
FN-AP8-PM-1930	Install FF&E - CBP Primary - INTF - AP 8	10d	27-Sep-28	10-Oct-28	0d
FN-FI-1550	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 9	12d	29-Sep-28	16-Oct-28	5d
COM-ELE-410	Lighting Controls Programming Theatrical Light. Controls Elec. Commissioning	5d	03-Oct-28	09-Oct-28	10d
FN-AP8-PM-1950	Install Signage & Dimensional Text - CBP Primary - INTF - AP 8	5d	04-Oct-28	10-Oct-28	0d
COM-ELE-390	Lighting Controls Programming RGB Light. Controls Elec. Commissioning	5d	10-Oct-28	16-Oct-28	10d
MLS-SUPP.C-13	MLS 13 - CBP Area Finishes Complete	0d		10-Oct-28 C	0d
COM-ELE-340	Perform Pre-FPT - Light. Controls Elec. Commissioning	5d	17-Oct-28	23-Oct-28	10d
FN-FI-1560	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 8	15d	17-Oct-28	06-Nov-28	5d
D2032	Owner Witnessed Testing / Pre-TRR [02-01-03B]	15d	23-Oct-28	10-Nov-28	0d
COM-ELE-350	Perform FPT - Light. Controls Elec. Commissioning	15d	24-Oct-28	13-Nov-28	10d
FN-FI-1570	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 7	15d	07-Nov-28	29-Nov-28	5d
FN-FI-1580	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 6	10d	07-Nov-28	20-Nov-28	5d
FN-FI-1110	Install Signage - Sterile Corr. 8	5d	07-Nov-28	13-Nov-28	5d
D2033	TRR [02-01-03B]	10d	13-Nov-28	28-Nov-28	0d
FN-MLS-SC-200	Sterile Level Internal Punchlist	20d	14-Nov-28	13-Dec-28	5d
COM-COT-60	ASD - COT Elec.Final Inspections - IST/Life Safety	10d	14-Nov-28	29-Nov-28	10d
COM-COT-70	ASD - COT Fire Alarm Final Inspections - IST/Life Safety	10d	21-Nov-28	06-Dec-28	10d
FN-FI-730	Install Signage - Sterile Corr. 6	5d	21-Nov-28	29-Nov-28	5d
D2034	ISAT Travel Day [02-01-03B]	1d	29-Nov-28	29-Nov-28	0d
D2035	ISAT [02-01-03B]	10d	30-Nov-28	13-Dec-28	0d
FN-FI-920	Install Signage - Sterile Corr. 7	5d	30-Nov-28	06-Dec-28	10d
MLS-SUPP.C-14	MLS 14 - TSA ISAT BHS Testing Complete	0d		13-Dec-28 C	0d
FN-MLS-SC-190	Sterile Level Finishes Complete	0d		13-Dec-28	5d
COM-COT-80	ASD - COT AHJ Life Safety Final Inspections (TCO) - IST/Life Safety	5d	14-Dec-28	20-Dec-28	5d
D2036	TRN [02-01-03B]	3d	14-Dec-28	18-Dec-28	0d
A18	BHS - Mech / Elec. Demo & Install of T8 01/06 (02-01-04A)	3d	19-Dec-28	21-Dec-28	0d
D2043	Internal Commissioning / Functional Testing / Owner Testing [02-01-04A]	1d	21-Dec-28	21-Dec-28	0d
COM-COT-90	ASD - COT Building Final Inspections (TCO) - IST/Life Safety	5d	21-Dec-28	28-Dec-28	5d
A109770	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS3 [02-01-1A]	15d	22-Dec-28	15-Jan-29	3d
A19	BHS - Mech / Elec. Demo & Install of C5 05/06, TF1 01/03, T5 11, T-T5 16/17 (02-01-04B)	10d	22-Dec-28	08-Jan-29	0d
TC-FS-110	Install New AOA Fence (Excellence Drive/Trailer City)	10d	29-Dec-28	12-Jan-29	5d
D2051	Internal Commissioning / Functional Testing / Owner Testing [02-01-04B]	3d	08-Jan-29	10-Jan-29	0d
BG-DM-MCP-C-510	Demo & Remove MCP C5	1d	09-Jan-29	09-Jan-29	1d
BG-DM-MCP-C-500	Demo MCP C5 Feeder Back to Source [HMCP-7]	10d	09-Jan-29	22-Jan-29	1d
BG-DM-MCP-C-530	Demo, Patch & Seal Concrete @ Former MCP C5 Housekeeping Pad	5d	10-Jan-29	16-Jan-29	1d
A20	BHS - Mech/Elec. Demo (BX4 02/05, MCP BX4) & Install of (T5 14/15) [02-01-04C]	5d	11-Jan-29	17-Jan-29	0d
TC-FS-130	Remove Temp AOA Fence (Final)	20d	15-Jan-29	09-Feb-29	5d
D2058	Internal Commissioning/Functional Testing/Owner Testing [02-01-04C]	1d	18-Jan-29	18-Jan-29	0d
D2063	Elec. MPP Install (B17) [02-02-01A]	9d	19-Jan-29	31-Jan-29	4d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
A21	Mech/Elec. Demo/Install C3 11, T1 11, T1A 01/03, T5A 06/08, TXM2 01/03, TE1 05/08, TE2 03/04, ...	13d	19-Jan-29	06-Feb-29	0d
FN-CN-3160	Install Resin Deck on Concourse 9 Lid - Architectural Forms (LED Screens) - INTF - C8	10d	05-Feb-29	16-Feb-29	0d
FN-CN-3170	Install Resin Deck on Concourse 10 Lid - Architectural Forms (LED Screens) - INTF - C8	10d	05-Feb-29	16-Feb-29	0d
D2066	Internal Commissioning/Functional Testing/Owner Testing [02-02-01A]	3d	05-Feb-29	07-Feb-29	0d
A109780	Demo Ceiling Tile and Erect Temp Walls	4d	05-Feb-29	08-Feb-29	2d
BG-OPS-TC-130	T4 - Out of Service - American Airlines Shift to T6 (LOE)	1d	08-Feb-29	08-Feb-29	0d
D2071	Internal Commissioning/Functional Testing/Owner Testing [02-02-01B]	1d	08-Feb-29	08-Feb-29	0d
A22	BHS - Mech/Elec. Demo & Install of T-T4 06 (02-02-01B)	1d	08-Feb-29	08-Feb-29	0d
A23	BHS - Mech/Elec. Demo & Install (02-02-02A)	20d	09-Feb-29	08-Mar-29	2d
BG-DM-MCP-BX-400	Demo MCP BX4 Feeder Back to Source [HMCP-6]	10d	09-Feb-29	22-Feb-29	7d
BG-OPS-TC-140	C2 - Out of Service - American Airlines Shift to T6 (LOE)	23d	09-Feb-29	13-Mar-29	0d
D2075	Elec. Recontrol (C2 01/08) [02-02-02A]	5d	09-Feb-29	15-Feb-29	0d
D2078	Elec. MPP Install (B13) [02-02-02A]	16d	16-Feb-29	09-Mar-29	0d
FN-MLS-CN-310	Concourse Level Finishes Complete	0d		16-Feb-29	0d
MLS-370	MLS - ASD Construction Complete (HP Ready for C of O)	0d		16-Feb-29 C	0d
COM-COT-100	ASD - COT AHJ Life Safety Final Inspections (CO)- IST/Life Safety	5d	19-Feb-29	23-Feb-29	0d
BG-DM-MCP-BX-410	Demo & Remove MCP BX4	1d	23-Feb-29	23-Feb-29	7d
BG-DM-MCP-BX-430	Demo, Patch & Seal Concrete @ Former MCP BX4 Housekeeping Pad	5d	26-Feb-29	02-Mar-29	7d
COM-COT-110	ASD - COT Building Final Inspections (CO) - IST/Life Safety	5d	26-Feb-29	02-Mar-29	0d
MLS-SUPP.C-15	MLS 15 - Supplement C Project Substantial Completion (Phase 1)	0d		02-Mar-29 C	0d
D2081	Internal Commissioning/Functional Testing/Owner Testing [02-02-02A]	5d	07-Mar-29	13-Mar-29	0d
A24	BHS - Mech/Elec. Demo & Install of T5 04 & T-T5 16/17 (02-02-02B)	2d	14-Mar-29	15-Mar-29	0d
D2089	Internal Commissioning/Functional Testing/Owner Testing [02-02-02B]	1d	16-Mar-29	16-Mar-29	0d
MLS-180	MLS - Airside D Terminal Ready for First Flight	0d		16-Mar-29 C	0d
MLS-1100	MLS - Architectural LEDs Install & Testing Complete	0d		16-Mar-29	0d
MLS-950	MLS - ASD Construction Complete (HCAA Stakeholders Ready for C of O)	0d		16-Mar-29	0d
A25	BHS - Mech/Elec. Demo & Install of C4 08/09, T11A 12/15, T5A 01/03 (02-02-02C)	9d	19-Mar-29	29-Mar-29	0d
D2095	Internal Commissioning/Functional Testing/Owner Testing [02-02-02C]	2d	29-Mar-29	30-Mar-29	0d
D2098	Elec. Recontrol (T4 01/03) [02-02-02D]	4d	02-Apr-29	05-Apr-29	0d
A26	BHS - Mech/Elec. Demo (T4 04/08) & Install of C3 11, T4 04/06, C1 07/09 (02-02-02D)	5d	02-Apr-29	06-Apr-29	1d
D2103	Internal Commissioning/Functional Testing/Owner Testing [02-02-02D]	2d	06-Apr-29	09-Apr-29	0d
A27	BHS - Mech/Elec. Demo & Install of TE1 09/11, T-TE1 12/16, T-TE2 05/07 (02-02-02E)	7d	10-Apr-29	18-Apr-29	0d
D2106	Elec. Recontrol (C1 01/05) [02-02-02E]	3d	10-Apr-29	12-Apr-29	5d
D2113	Internal Commissioning/Functional Testing/Owner Testing (C1) [02-02-02E]	1d	16-Apr-29	16-Apr-29	4d
D2115	Internal Commissioning/Functional Testing/Owner Testing (TE1/TE2) [02-02-02E]	2d	19-Apr-29	20-Apr-29	0d
D2122	Internal Commissioning/Functional Testing/Owner Testing [02-02-02F]	1d	23-Apr-29	23-Apr-29	0d
A28	BHS - Mech/Elec. Demo & Install of C3 06 (02-02-02F)	1d	23-Apr-29	23-Apr-29	0d
A29	BHS - Mech/Elec. Demo & Install of T3 04/11 (02-02-02G)	5d	24-Apr-29	30-Apr-29	0d
D2129	Internal Commissioning/Functional Testing/Owner Testing [02-02-02G]	1d	01-May-29	01-May-29	0d
D2132	Elec. Recontrol (T3 02/03) [02-02-03A]	2d	02-May-29	03-May-29	0d
A30	BHS - Mech/Elec. Demo & Install of T3 02/03 02-02-03A	2d	02-May-29	03-May-29	0d
A31	BHS - Mech/Elec. Demo & Install of T1 10, T-SS8 06/07, TXM1 07/08 02-02-03A	4d	03-May-29	08-May-29	0d
D2140	Internal Commissioning/Functional Testing/Owner Testing [02-02-03A]	1d	09-May-29	09-May-29	0d
D2146	Demo EDS Machine (SS7) [02-02-03B]	2d	10-May-29	11-May-29	0d
A32	BHS - Mech/Elec. Demo & Install of SS7 06/07 & T-SS8 05 (02-02-03B)	2d	10-May-29	11-May-29	0d
D2150	Internal Commissioning/Functional Testing/Owner Testing [02-02-03B]	1d	14-May-29	14-May-29	0d
D2152	Elec. Demo [02-02-03C]	10d	15-May-29	29-May-29	0d
D2153	Mech Demo [02-02-03C]	10d	30-May-29	12-Jun-29	0d
D2156	Elec. Install (T1 07/09) [02-02-03C]	3d	06-Jun-29	08-Jun-29	0d
D2157	Mech Install (T1 07/09) [02-02-03C]	3d	06-Jun-29	08-Jun-29	0d
D2158	Internal Commissioning/Functional Testing (T1 07/09) [02-02-03C]	1d	11-Jun-29	11-Jun-29	0d
D2159	Elec. Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-03C]	15d	11-Jun-29	29-Jun-29	3d
D2160	Mech Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-03C]	15d	11-Jun-29	29-Jun-29	3d
D2166	Elec. Recontrol (T2 01/04) [02-02-04A]	3d	12-Jun-29	14-Jun-29	0d
A33	BHS - Mech/Elec. Demo & Install T2 05/07 (02-02-04A)	3d	12-Jun-29	14-Jun-29	0d
D2154	ControlNet Rework/Elec Demo (MCP-T3, MCP-AS1, MCP-CX1/CX3, MCP-MCP-BX1, MCP-CX2) [02-02...	15d	13-Jun-29	03-Jul-29	1d
A110480	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS1 [02-02-03C]	15d	13-Jun-29	03-Jul-29	1d
D2172	Internal Commissioning/Functional Testing/Owner Testing [02-02-04A]	1d	15-Jun-29	15-Jun-29	0d

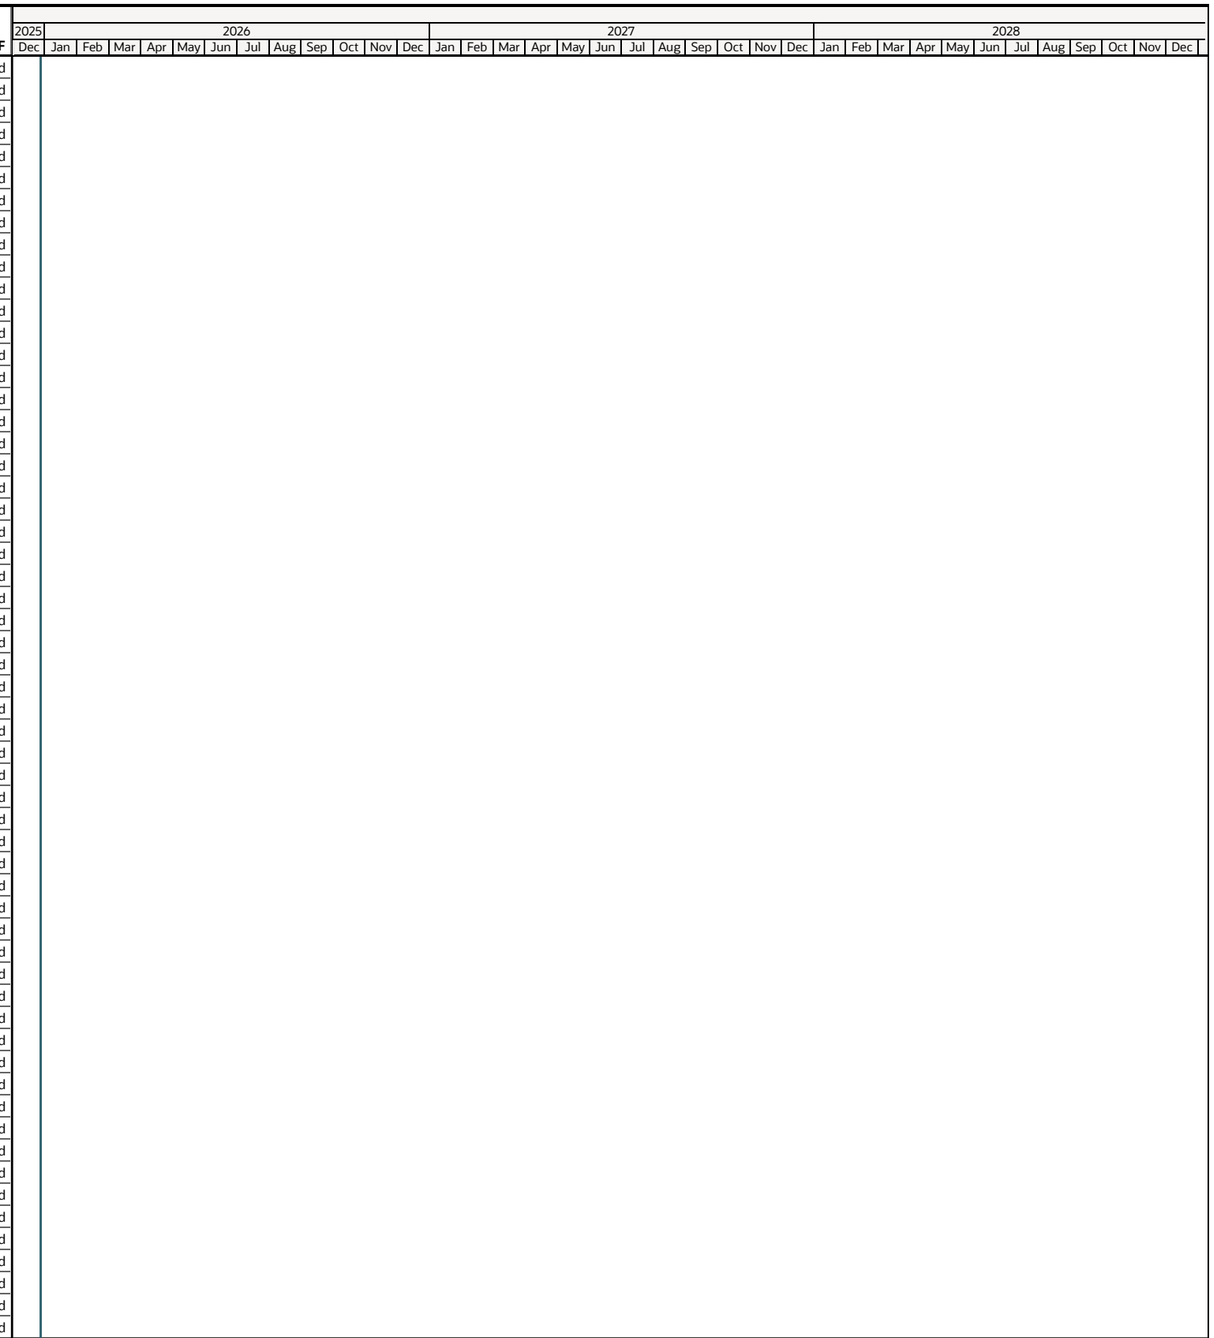

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

ID	Name	Dur	Start	Finish	TF
D2174	Elec. Recontrol (T1 01/04) [02-02-04B]	3d	18-Jun-29	20-Jun-29	0d
A34	BHS - Mech/Elec. Demo & Install T1 05/06 (02-02-04B)	3d	18-Jun-29	20-Jun-29	0d
D2179	Internal Commissioning/Functional Testing/Owner Training [02-02-04B]	1d	21-Jun-29	21-Jun-29	0d
D2182	ControlNet Rework/Elec Demo (MCP-T1/T2, MCP-AS2) [02-02-05]	5d	22-Jun-29	28-Jun-29	0d
A110490	Demo EDS Access Platform in AS1 [02-02-03C]	5d	27-Jun-29	03-Jul-29	1d
B35	BHS - Mech/Elec. Demo & Install of (AS2 01/07, T1 07/09, T2 06/10, SS7 01/04, T-SS8 05/07) [02-0...	10d	29-Jun-29	13-Jul-29	0d
D2163	Elec. Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18) [02-02-03C]	20d	02-Jul-29	30-Jul-29	3d
D2162	Elec. Install (MPP-AOS, FCP-AOS, MPP-BOS, FCP-BOS) [02-02-03C]	20d	05-Jul-29	01-Aug-29	1d
D2164	Mech Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18, Inspection Tables) [02-02-03C]	20d	05-Jul-29	01-Aug-29	1d
BG-DM-MCP-AS-220	Demo Exist. Housekeeping Pad Beneath Former MCP AS2	1d	16-Jul-29	16-Jul-29	0d
BG-DM-MCP-AS-230	Patch & Seal Concrete @ Former MCP AS2 Housekeeping Pad	3d	17-Jul-29	19-Jul-29	0d
A35	BHS - Mech/Elec. Demo & Install of TE1 15/16, TE2 09/10, TXM1 01/06 (02-02-05)	13d	20-Jul-29	07-Aug-29	0d
D2190	Mech Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10d	02-Aug-29	15-Aug-29	1d
D2189	Elec. Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10d	02-Aug-29	15-Aug-29	1d
D2187	Internal Commissioning/Functional Testing [02-02-05]	2d	08-Aug-29	09-Aug-29	0d
D2188	Owner Testing [02-02-05]	1d	09-Aug-29	09-Aug-29	0d
A36	BHS - Mech/Elec. Demo & Install of (TE1 12) [02-02-06]	3d	10-Aug-29	14-Aug-29	0d
D2201	Internal Commissioning/Functional Testing/Owner Testing [02-02-06]	1d	15-Aug-29	15-Aug-29	0d
D2191	Internal Commissioning / Functional Testing- Oversized Screening [02-02-05]	5d	16-Aug-29	22-Aug-29	1d
A37	BHS - Mech/Elec. Demo & Install of (T-TE2 05, EX2 07) & (TE2 05, TE2 16/17) [02-02-07]	5d	16-Aug-29	22-Aug-29	0d
D2192	Owner / TRR Testing- Oversized Screening [02-02-05]	5d	23-Aug-29	29-Aug-29	1d
D2208	Internal Commissioning/Functional Testing/Owner Testing [02-02-07]	1d	23-Aug-29	23-Aug-29	0d
A38	BHS - Mech/Elec. Demo & Install of (T-TE2 06/07, T-TE1 14/16, EX2 01/06, EX2 08/15) [02-02-08]	4d	24-Aug-29	29-Aug-29	0d
D2193	ISAT Travel Day [02-02-05]	1d	30-Aug-29	30-Aug-29	1d
FCPL-160	CCBS Post-ISAT - Internal Completion/Punchlist Development	15d	30-Aug-29	20-Sep-29	0d
D2194	ISAT Testing (Oversized Screening) [02-02-05]	4d	31-Aug-29	06-Sep-29	1d
D2195	TRN (Oversized Screening) [02-02-05]	5d	07-Sep-29	13-Sep-29	1d
MLS-SUPP.C-16	MLS 16 - Supplement C Project Substantial Completion (Phase 2 - CCBS 2-2)	0d		13-Sep-29 C	1d
FCPL-170	Owner Final Commissioning/Punchlist Development Phase 2 (ASD & CCBS)	65d	21-Sep-29	24-Dec-29	0d
FCPL-180	Owner Final Commissioning/Punchlist Completion Phase 2 (ASD & CCBS)	60d	26-Dec-29	20-Mar-30	0d

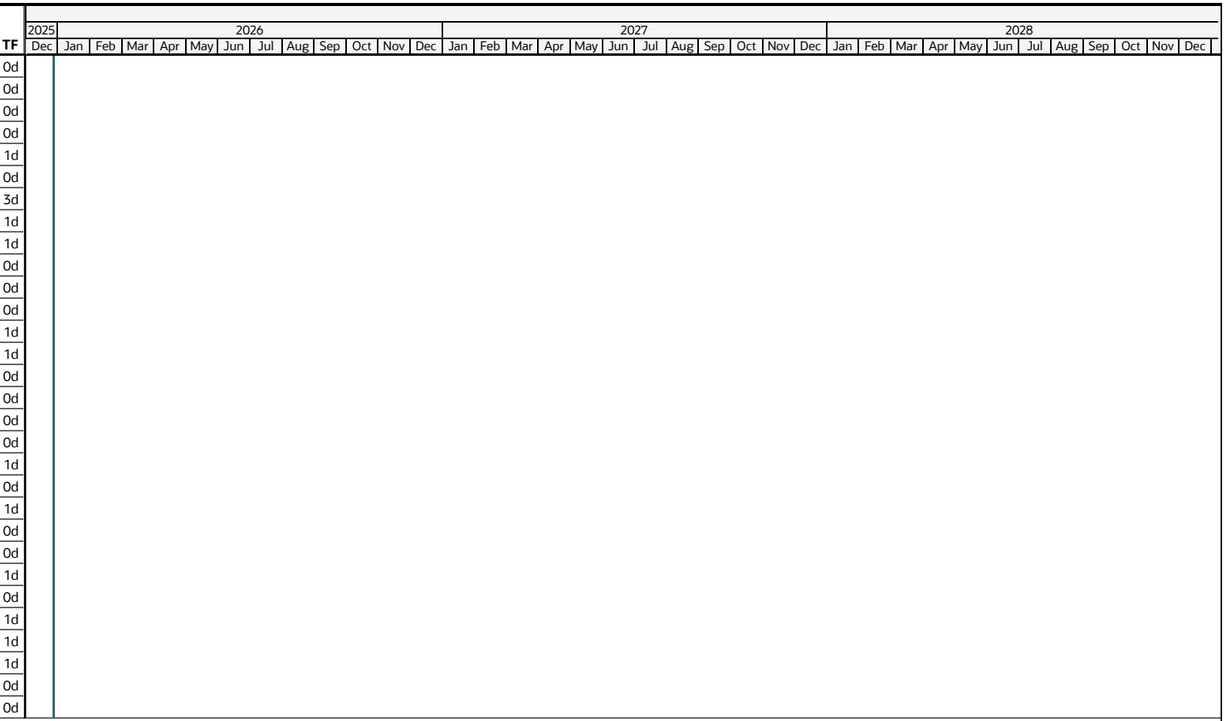

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


Supplement C Critical Path - December 2025 CPM Update

Filters: Supplement C Critical Path, Not Completed
Supplement C Critical Path Flters:
ASD1-Major Elements Supplement C,
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:09 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: Supp C Critical Path
Printed By: Jill Spinnenweber

	ID	Name	Dur	Start	Finish	TF
1	WBS - Airside D - Tampa International Airport		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
2	WBS - PROJECT TIME TABLE SUMMARY		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
3	PTTS-10	Project Timetable Summary to Substantial Completion (LOE)	1,417.0d	3-Aug-23 A	2-Mar-29	0.0d
4	WBS - Airside D - SOV LOE's		1,339.0d	13-Dec-24 A	21-Mar-30	0.0d
5	ASD-HAM-20	ASD - Contingency/Allowance/Budget - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
6	ASD-HAM-10	ASD - General Conditions / Requirements - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
7	CCBS-HAM-30	CCBS - Supp B General Conditions / Requirements - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
8	CCBS-HAM-40	CCBS - Supp B Contingency/Allowance/Budget - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
9	GI-HAM-10	Ground Improvements Scope LOE - DIP/LTP	63.0d	27-Oct-25 A	27-Jan-26	46.0d
10	GI-FS-HAM-1010	Found. Concrete Scope - LOE	153.0d	24-Nov-25 A	1-Jul-26	0.0d
11	GI-FS-HAM-1030	Deep UG Plumbing & Mech. Scope - LOE	185.0d	16-Dec-25 A	4-Sep-26	0.0d
12	GI-FS-HAM-1020	Deep UG Elec. & Comm. Scope - LOE	165.0d	16-Dec-25 A	7-Aug-26	112.0d
13	WBS - TAMPA AIRSIDE D TERMINAL		979.0d	9-Dec-24 A	15-Oct-28	349.0d
14	WBS - ASD - DESIGN & ENGINEERING PHASE		267.0d	9-Sep-25 A	25-Sep-26	860.0d
15	WBS - Airside E Optimization		21.0d	24-Dec-25 A	23-Jan-26	1,032.0d
16	WBS - ASE Optimization 90%		10.0d	24-Dec-25 A	8-Jan-26	1,043.0d
17	WBS - ASE Optimization 90% Submittal To HCAA		10.0d	24-Dec-25 A	8-Jan-26	1,043.0d
18	DS-AE-520	Review by HCAA - ASE Optimization 90% Subm.	10.0d	24-Dec-25 A	8-Jan-26	1,042.0d
19	WBS - ASE Optimization 100%		21.0d	24-Dec-25 A	23-Jan-26	1,032.0d
20	WBS - ASE Optimization 100% Documents		21.0d	24-Dec-25 A	23-Jan-26	1,032.0d
21	DS-AE-530	Design Docs. - ASE Optimization 100%	21.0d	24-Dec-25 A	23-Jan-26	1,031.0d
22	WBS - A-Sortation & Airside C Screening Integration		105.0d	9-Sep-25 A	6-Feb-26	947.0d
23	DS-AA-640	HNTB - Design Deliverables 15%, 30%, 60%, 90% & 100%	105.0d	9-Sep-25 A	6-Feb-26	946.0d
24	DS-AA-110	Owner Proposal Review - A-Sortation & Airside C Screening Integration	52.0d	14-Oct-25 A	29-Dec-25	974.0d
25	DS-AA-630	NTP - A-Sortation & Airside C Screening Integration (Second $150k)	1.0d	29-Dec-25	29-Dec-25	807.0d
26	WBS - ASD Bulletin - LED Digital Technology Updates		200.0d	15-Dec-25 A	25-Sep-26	309.0d
27	WBS - ASD - Bulletin - LED Digital Technology Updates - Design Development		200.0d	15-Dec-25 A	25-Sep-26	309.0d
28	ASD-Bull-DT-330	HCAA RFQ Award Content Designers - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	247.0d
29	ASD-Bull-DT-100	Develop Design Documents - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	309.0d
30	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades		131.0d	10-Nov-25 A	15-May-26	582.0d
31	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades Design Development		131.0d	10-Nov-25 A	15-May-26	582.0d
32	ASD-Bull-ET-50	HP/HNTB Prepare & Submit Proposal - ASD Bulletin - FIS Elevator Tower Finish ...	131.0d	10-Nov-25 A	15-May-26	582.0d
33	WBS - ASD - PRECONSTRUCTION PHASE		301.0d	9-Dec-24 A	13-Feb-26	404.0d
34	WBS - HCAA Board Approval Milestones		301.0d	9-Dec-24 A	13-Feb-26	404.0d
35	WBS - HCAA Board Award of Part 2 Supplement C Wave 1 - Core & Shell Package		42.0d	8-Dec-25 A	5-Feb-26	410.0d
36	HA-2C-W1-70	HCAA Review Supp. C for Board - Part 2 Supp. C - Core & Shell Pkg.	37.0d	15-Dec-25 A	5-Feb-26	0.0d
37	WBS - Part 2 Supplement C Wave 1 Purchasing & Contracting		33.0d	8-Dec-25 A	23-Jan-26	419.0d
38	WBS - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		15.0d	8-Dec-25 A	29-Dec-25	122.0d
39	2C-W1-PC-830	Contract Negoation - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purcha...	15.0d	8-Dec-25 A	29-Dec-25	122.0d
40	WBS - Elevators/Escalators Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		12.0d	11-Dec-25 A	29-Dec-25	27.0d
41	2C-W1-PC-770	Contract Negoation - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purch...	12.0d	11-Dec-25 A	29-Dec-25	27.0d
42	WBS - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		15.0d	8-Dec-25 A	29-Dec-25	413.0d

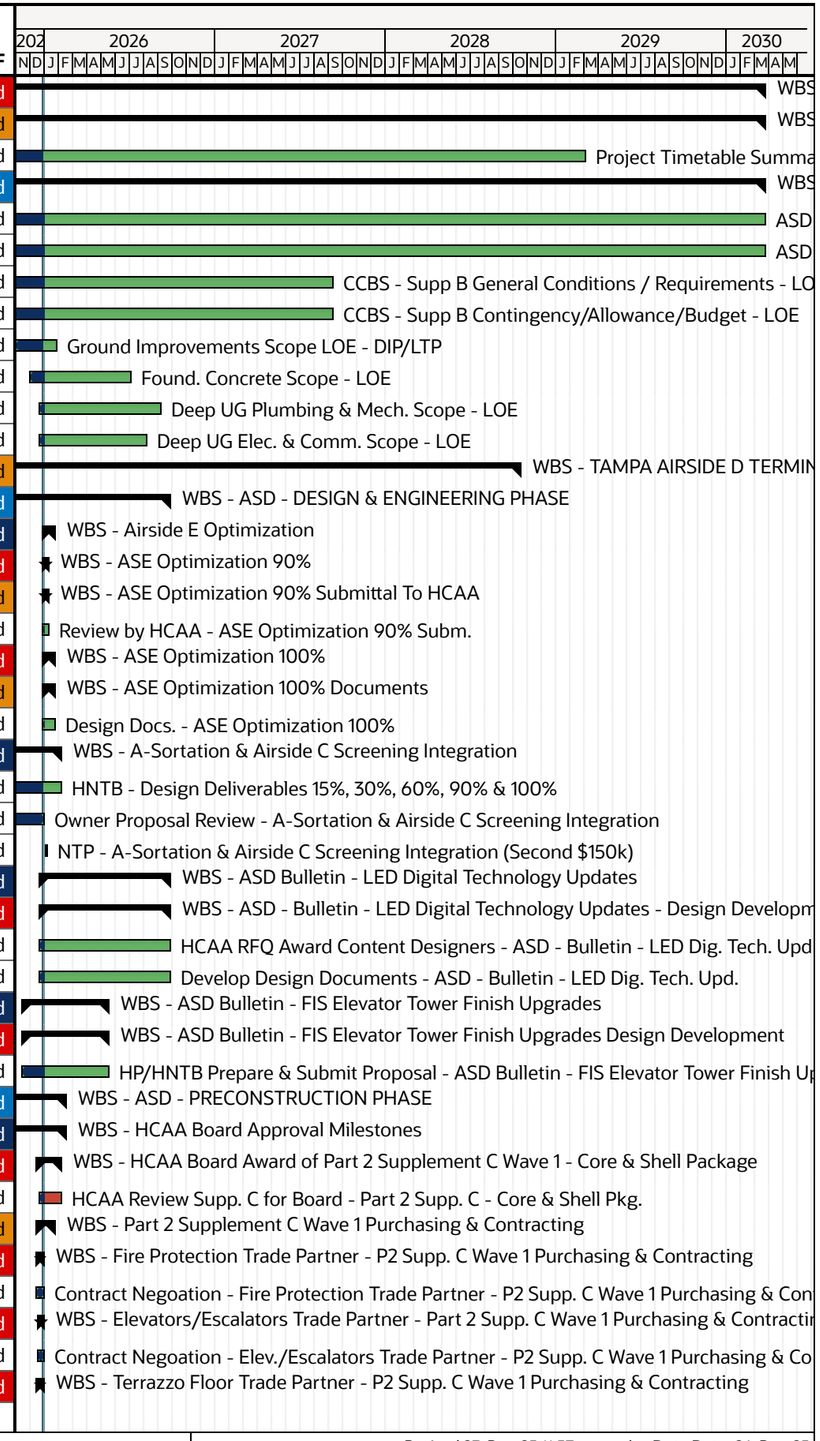

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Development Program

30 Day Look Ahead Schedule

December 2025 - DD 12.26.25

Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:57 a.m. | **Data Date:** 26-Dec-25

HP Project ID No: 8023226 | Region Code: HP-800

HCAA Package #8500 23


View Name: Schedule Submission to HCAA (Owner)

Printed By: Alex Melguizovski

	ID	Name	Dur	Start	Finish	TF
43	2C-W1-PC-2090	Contract Negoation - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchas...	15.0d	8-Dec-25 A	29-Dec-25	413.0d
44	WBS - Roofing Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	17-Dec-25 A	2-Jan-26	115.0d
45	2C-W1-PC-100	Contract Negoation - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	11.0d	17-Dec-25 A	2-Jan-26	115.0d
46	WBS - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		14.0d	9-Dec-25 A	29-Dec-25	53.0d
47	2C-W1-PC-1250	Contract Negoation - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wav...	14.0d	9-Dec-25 A	29-Dec-25	53.0d
48	WBS - Interior Wall Panels (Specialties/Decorative Glass) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contra...		14.0d	9-Dec-25 A	29-Dec-25	434.0d
49	2C-W1-PC-400	Contract Negoation - Interior Wall Panels (Specialties/Decorative Glass) Trade P...	14.0d	9-Dec-25 A	29-Dec-25	434.0d
50	WBS - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		14.0d	9-Dec-25 A	29-Dec-25	421.0d
51	2C-W1-PC-2150	Contract Negoation - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Pu...	14.0d	9-Dec-25 A	29-Dec-25	421.0d
52	WBS - Glass Handrail Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		10.0d	29-Dec-25	12-Jan-26	428.0d
53	2C-W1-PC-460	Contract Development, Review, & Issuance - Glass Handrail Trade Partner - P2 ...	10.0d	29-Dec-25	12-Jan-26	428.0d
54	WBS - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		25.0d	8-Dec-25 A	13-Jan-26	53.0d
55	2C-W1-PC-1180	Contract Development, Review, & Issuance - Masonry Trade Partner - P2 Supp. ...	15.0d	8-Dec-25 A	29-Dec-25	53.0d
56	2C-W1-PC-1190	Contract Negoation - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	53.0d
57	WBS - Demolition Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		12.0d	19-Dec-25 A	7-Jan-26	82.0d
58	2C-W1-PC-2450	Contract Negoation - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasing...	12.0d	19-Dec-25 A	7-Jan-26	82.0d
59	WBS - Concrete SOG & SOMD Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		24.0d	9-Dec-25 A	13-Jan-26	118.0d
60	2C-W1-PC-30	Contract Development, Review, & Issuance - Concrete Trade Partner - P2 Supp. ...	14.0d	9-Dec-25 A	29-Dec-25	118.0d
61	2C-W1-PC-40	Contract Negoation - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	118.0d
62	WBS - Interior/Exterior Metal Wall Panels Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	19-Dec-25 A	6-Jan-26	113.0d
63	2C-W1-PC-280	Contract Negoation - Interior/Exterior Metal Wall Panels Trade Partner - P2 Sup...	11.0d	19-Dec-25 A	6-Jan-26	113.0d
64	WBS - Spray Fireproofing & Insulation (K-13) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	18-Dec-25 A	5-Jan-26	104.0d
65	2C-W1-PC-160	Contract Negoation - Spray Fireproofing & Insulation (K-13) Trade Partner - P2 ...	11.0d	18-Dec-25 A	5-Jan-26	104.0d
66	WBS - Drywall & Related Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	18-Dec-25 A	5-Jan-26	97.0d
67	2C-W1-PC-530	Contract Negoation - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Purc...	11.0d	18-Dec-25 A	5-Jan-26	97.0d
68	WBS - Glass & Glazing/Curtainwall Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		9.0d	19-Dec-25 A	2-Jan-26	105.0d
69	2C-W1-PC-340	Contract Negoation - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C W...	9.0d	19-Dec-25 A	2-Jan-26	105.0d
70	WBS - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		10.0d	29-Dec-25	12-Jan-26	89.0d
71	2C-W1-PC-1060	Contract Development, Review, & Issuance - Sitework Trade Partner - P2 Supp. ...	10.0d	29-Dec-25	12-Jan-26	89.0d
72	WBS - Waterproofing, Caulks, & Sealants Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		10.0d	29-Dec-25	12-Jan-26	109.0d
73	2C-W1-PC-210	Contract Development, Review, & Issuance - Waterproofing, Caulks, & Sealants ...	10.0d	29-Dec-25	12-Jan-26	109.0d
74	WBS - Electrical & Site Electrical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		11.0d	5-Jan-26	19-Jan-26	94.0d
75	2C-W1-PC-860	Purchasing Meeting - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 Purc...	1.0d	5-Jan-26	5-Jan-26	9.0d
76	2C-W1-PC-870	Draft, Review, & Issue Change Order - Elec. & Site Elec. Trade Partner - P2 Supp...	10.0d	6-Jan-26	19-Jan-26	94.0d
77	WBS - Baggage Handling Contractor - Part 2 Supp. C Wave 1 Purchasing & Contracting		14.0d	6-Jan-26	23-Jan-26	9.0d
78	2C-W1-PC-2480	Purchasing Meeting - Baggage Handling Contractor - P2 Supp. C Wave 1 Purch...	1.0d	6-Jan-26	6-Jan-26	9.0d
79	2C-W1-PC-2490	Draft, Review, & Issue Change Order - Baggage Handling Contractor - P2 Supp. ...	3.0d	7-Jan-26	9-Jan-26	9.0d
80	2C-W1-PC-2510	Change Order Negotiation - Baggage Handling Contractor - P2 Supp. C Wave 1 ...	10.0d	12-Jan-26	23-Jan-26	9.0d
81	WBS - Low Voltage System Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		4.0d	7-Jan-26	12-Jan-26	17.0d
82	2C-W1-PC-920	Purchasing Meeting - Low Voltage System Trade Partner - P2 Supp. C Wave 1 P...	1.0d	7-Jan-26	7-Jan-26	17.0d
83	2C-W1-PC-930	Draft, Review, & Issue Change Order - Low Voltage System Trade Partner - P2 S...	3.0d	8-Jan-26	12-Jan-26	17.0d
84	WBS - Plumbing/Mechanical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		14.0d	5-Jan-26	22-Jan-26	71.0d



	ID	Name	Dur	Start	Finish	TF
85	2C-W1-PC-1520	Purchasing Meeting - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1 Purc…	1.0d	5-Jan-26	5-Jan-26	55.0d
86	2C-W1-PC-1530	Draft, Review, & Issue Change Order - Plumbing/Mech. Trade Partner - P2 Sup…	3.0d	6-Jan-26	8-Jan-26	71.0d
87	2C-W1-PC-1550	Change Order Negoation - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1…	10.0d	9-Jan-26	22-Jan-26	71.0d
88	WBS - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting-1		4.0d	8-Jan-26	13-Jan-26	359.0d
89	2C-W1-PC-2600	Purchasing Meeting - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchas…	1.0d	8-Jan-26	8-Jan-26	352.0d
90	2C-W1-PC-2610	Draft & Issue LOI - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing…	3.0d	9-Jan-26	13-Jan-26	359.0d
91	WBS - Structural Steel Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		14.0d	6-Jan-26	23-Jan-26	62.0d
92	2C-W1-PC-2660	Purchasing Meeting - Structural Steel Trade Partner - P2 Supp. C Wave 1 Purch…	1.0d	6-Jan-26	6-Jan-26	55.0d
93	2C-W1-PC-2670	Draft, Review, & Issue Change Order - Structural Steel Trade Partner - P2 Supp. …	3.0d	7-Jan-26	9-Jan-26	62.0d
94	2C-W1-PC-2680	Change Order Negoation - Structural Steel Trade Partner - P2 Supp. C Wave 1 P…	10.0d	12-Jan-26	23-Jan-26	62.0d
95	WBS - Part 2 Supplement C Wave 2- Finishes Package		9.0d	22-Dec-25 A	5-Jan-26	18.0d
96	HA-2C-W2-90	Bid Packaging - Part 2 Supp. C Wave 2 - Finishes Pkg	9.0d	22-Dec-25 A	5-Jan-26	18.0d
97	WBS - HCAA Alternative Procurement Preconstruction		301.0d	9-Dec-24 A	13-Feb-26	50.0d
98	WBS - Concessions Program Preconstruction (by Others)		279.0d	9-Dec-24 A	14-Jan-26	4.0d
99	HA-AL-CP-100	Concessions - Concessions Development	279.0d	9-Dec-24 A	14-Jan-26	4.0d
100	WBS - Artwork Preconstruction (Coordination with DB Team)		105.0d	16-Sep-25 A	13-Feb-26	50.0d
101	HA-AL-AW-20	Artwork - Issue Call for Artists (AS D Part 1 Awarded August 2023)	105.0d	16-Sep-25 A	13-Feb-26	50.0d
102	WBS - ASD - CITY OF TAMPA PERMITTING		44.0d	25-Nov-25 A	29-Jan-26	359.0d
103	WBS - ASD Building Permit		40.0d	25-Nov-25 A	23-Jan-26	64.0d
104	ASDEF-PER-ASD-640	COT Comment Response Subm. Review #1 - ASD Building Permit	29.0d	25-Nov-25 A	8-Jan-26	64.0d
105	ASDEF-PER-ASD-645	ASD COT Revision #1 Comments Received - ASD Building Permit	1.0d	9-Jan-26	9-Jan-26	64.0d
106	ASDEF-PER-ASD-646	Design Team Respond to Revision #1 Comments - ASD Building Permit	10.0d	12-Jan-26	23-Jan-26	64.0d
107	WBS - CCBS Permit Main Terminal Building		16.0d	19-Dec-25 A	13-Jan-26	66.0d
108	ASDEF-PER-MTB-770	COT Revision #1 Review - Main Terminal Build. Permit / CCBS	15.0d	19-Dec-25 A	12-Jan-26	66.0d
109	ASDEF-PER-MTB-772	MT BHS COT Revision #1 Comments Received - Main Terminal Build. Permit / …	1.0d	13-Jan-26	13-Jan-26	66.0d
110	WBS - Main Terminal Shuttle TI Permit		31.0d	16-Dec-25 A	29-Jan-26	359.0d
111	ASDEF-PER-MTS-820	COT Initial Subm. Review - Main Terminal Shuttle TI Permit	31.0d	16-Dec-25 A	29-Jan-26	359.0d
112	WBS - ASD - GOVERNMENTAL/MUNICIPAL/FAA/SWFWMD/FDEP PERMITTING		137.0d	29-Aug-25 A	16-Mar-26	753.0d
113	WBS - City of Tampa Utilities		137.0d	29-Aug-25 A	16-Mar-26	753.0d
114	WBS - City of Tampa Water Department		137.0d	29-Aug-25 A	16-Mar-26	44.0d
115	WBS - Part 1 Supplement C - Core & Shell Package		137.0d	29-Aug-25 A	16-Mar-26	44.0d
116	PM-P2-2B-40	Water Commitment Letter - Part 2 Supp. C COT WD -Core, Shell & Finishes	137.0d	29-Aug-25 A	16-Mar-26	44.0d
117	WBS - City of Tampa Solid Waste		132.0d	29-Aug-25 A	9-Mar-26	758.0d
118	WBS - Part 2 Agreement - Enabling Package		132.0d	29-Aug-25 A	9-Mar-26	758.0d
119	WBS - Core & Shell		132.0d	29-Aug-25 A	9-Mar-26	758.0d
120	PM-P2-2B-130	Core & Shell Solid Waste Design Review Complete - Part 2 Supp. C COT	132.0d	29-Aug-25 A	9-Mar-26	758.0d
121	WBS - FDEP		73.0d	21-Oct-25 A	4-Feb-26	723.0d
122	WBS - Part 1 Supplement C - Core & Shell Package		73.0d	21-Oct-25 A	4-Feb-26	723.0d
123	PM-FD-P2-2B-10	Drawing Pkg. Approval - FDEP Part 2 Supp. C- Core, Shell & Finishes	73.0d	21-Oct-25 A	4-Feb-26	723.0d
124	WBS - City of Tampa Construction Services		76.0d	19-Sep-25 A	8-Jan-26	232.0d
125	WBS - Part 1 Supplement C - Core & Shell Package		76.0d	19-Sep-25 A	8-Jan-26	232.0d
126	PM-P2-2B-20	Drawing Pkg. Approval - COT Const. Svs. -Part 1 Supp. C Core & Shell	76.0d	19-Sep-25 A	8-Jan-26	232.0d

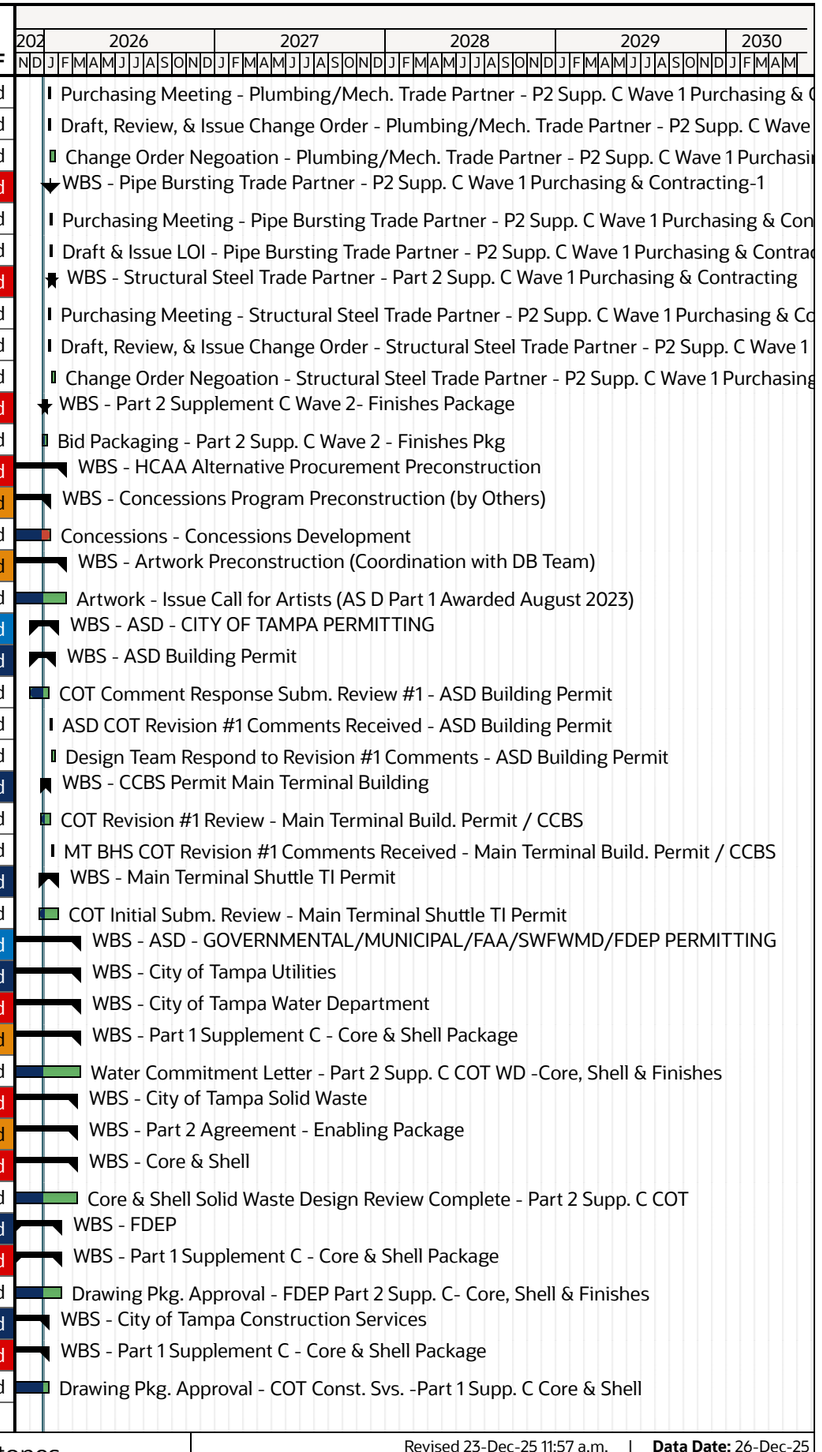

HENSEL PHELPS
Plan. Build. Manage.


Airside D - Tampa International Airport

ASD Development Program
30 Day Look Ahead Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:57 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
127	WBS - ASD - PROCUREMENT PHASE		148.0d	20-Oct-25 A	19-May-26	960.0d
128	WBS - Contractor Furnished & Install (CFCI)		148.0d	20-Oct-25 A	19-May-26	960.0d
129	WBS - Part 2 Supplement A - DIP / LTP, Foundations Package & Long Lead		59.0d	30-Oct-25 A	26-Jan-26	358.0d
130	WBS - DIP / LTP Area 6-1 Shop Drawings		14.0d	17-Dec-25 A	7-Jan-26	53.0d
131	PR-P2-1A-1880	HCAA Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DI...	14.0d	17-Dec-25 A	7-Jan-26	53.0d
132	WBS - Foundations Package		59.0d	30-Oct-25 A	26-Jan-26	356.0d
133	WBS - Rebar Foundations Area 2		29.0d	30-Nov-25 A	29-Dec-25	23.0d
134	PR-P2-1A-290	Fab. & Ship Rebar Found. Area 2 - Part 2 Supp. A	29.0d	30-Nov-25 A	29-Dec-25	23.0d
135	PR-P2-1A-430	Delivery of Rebar Found. Area 2 Complete - Part 2 Supp. A	0.0d		29-Dec-25	23.0d
136	WBS - Rebar Foundations Area 1		11.0d	23-Dec-25 A	8-Jan-26	0.0d
137	PR-P2-1A-1910	HNTB Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	11.0d	23-Dec-25 A	8-Jan-26	0.0d
138	WBS - Rebar Foundations Area 3		12.0d	23-Dec-25 A	9-Jan-26	15.0d
139	PR-P2-1A-1930	HNTB Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	12.0d	23-Dec-25 A	9-Jan-26	15.0d
140	WBS - Rebar Foundations Area 5		9.0d	23-Dec-25 A	6-Jan-26	49.0d
141	PR-P2-1A-1950	HNTB Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	49.0d
142	WBS - Rebar Foundations Area 4		9.0d	23-Dec-25 A	6-Jan-26	69.0d
143	PR-P2-1A-1970	HNTB Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	69.0d
144	WBS - Anchor Bolts		40.0d	26-Nov-25 A	26-Jan-26	351.0d
145	WBS - Anchor Bolts Pkg #3 Area 4		23.0d	23-Dec-25 A	26-Jan-26	92.0d
146	PR-P2-1A-1320	Procurement of Material - Area 4 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	92.0d
147	WBS - Anchor Bolts Pkg #3 Area 5		23.0d	23-Dec-25 A	26-Jan-26	72.0d
148	PR-P2-1A-1410	Procurement of Material - Area 5 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	72.0d
149	WBS - Anchor Bolts Pkg #4 Area 6-1 Cooling Tower		38.0d	26-Nov-25 A	22-Jan-26	353.0d
150	PR-P2-1A-1430	GMF Detailer Drawing Completion Window - Area 6-1 CT - Part 2 Supp. A - Anc...	38.0d	26-Nov-25 A	22-Jan-26	353.0d
151	WBS - Embeds		58.0d	30-Oct-25 A	23-Jan-26	357.0d
152	WBS - Embeds - Pkg. #2 - Area 6.1 - Cooling Tower (If needed)		58.0d	30-Oct-25 A	23-Jan-26	357.0d
153	PR-P2-1A-1620	Embeds Pkg #2 - GMF Detailer Drawing Completion Window - Area 6.1 - Part 2...	39.0d	30-Oct-25 A	26-Dec-25 A	
154	PR-P2-1A-1625	Embeds Pkg #2 - GMF DM Drawing Review - Area 6.1 - Part 2 Supp. A	2.0d	29-Dec-25	30-Dec-25	357.0d
155	PR-P2-1A-1630	Embeds Pkg #2 - A/E Team Review of Detail Drawing - Area 6.1 - Part 2 Supp. A	15.0d	31-Dec-25	21-Jan-26	357.0d
156	PR-P2-1A-1640	Embeds Pkg #2 - Return From Approval - Area 6.1 - Part 2 Supp. A	0.0d		21-Jan-26	357.0d
157	PR-P2-1A-1650	Embeds Pkg #2 - GMF Detailer Drawing Scrub & Clean up Window - Area 6.1 - ...	2.0d	22-Jan-26	23-Jan-26	357.0d
158	WBS - Underground Waterproofing		24.0d	5-Dec-25 A	29-Dec-25	14.0d
159	PR-P2-1A-310	Fab. & Ship Underground Waterproofing Products - Part 2 Supp. A	24.0d	5-Dec-25 A	29-Dec-25	14.0d
160	WBS - Transformer Procurement - ASD		45.0d	13-Nov-25 A	20-Jan-26	270.0d
161	PR-P1-1C1-70	Prep Transformer Submittals (Contractor) - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	270.0d
162	PR-P1-1C1-75	Review & Submit Transformer Submittals (HP) - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	270.0d
163	WBS - Long Lead Electrical		45.0d	13-Nov-25 A	20-Jan-26	229.0d
164	WBS - Generator		45.0d	13-Nov-25 A	20-Jan-26	229.0d
165	PR-P2-1B-180	Prep & Submit Generator Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	229.0d
166	PR-P2-1B-7910	HP Approve Generator Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	229.0d
167	WBS - Gear, Metering, SPD & Coordination Study		39.0d	13-Nov-25 A	12-Jan-26	166.0d
168	PR-P2-1B-120	Prep & Submit Gear Submittals - Part 2 Supp. A	34.0d	13-Nov-25 A	5-Jan-26	166.0d

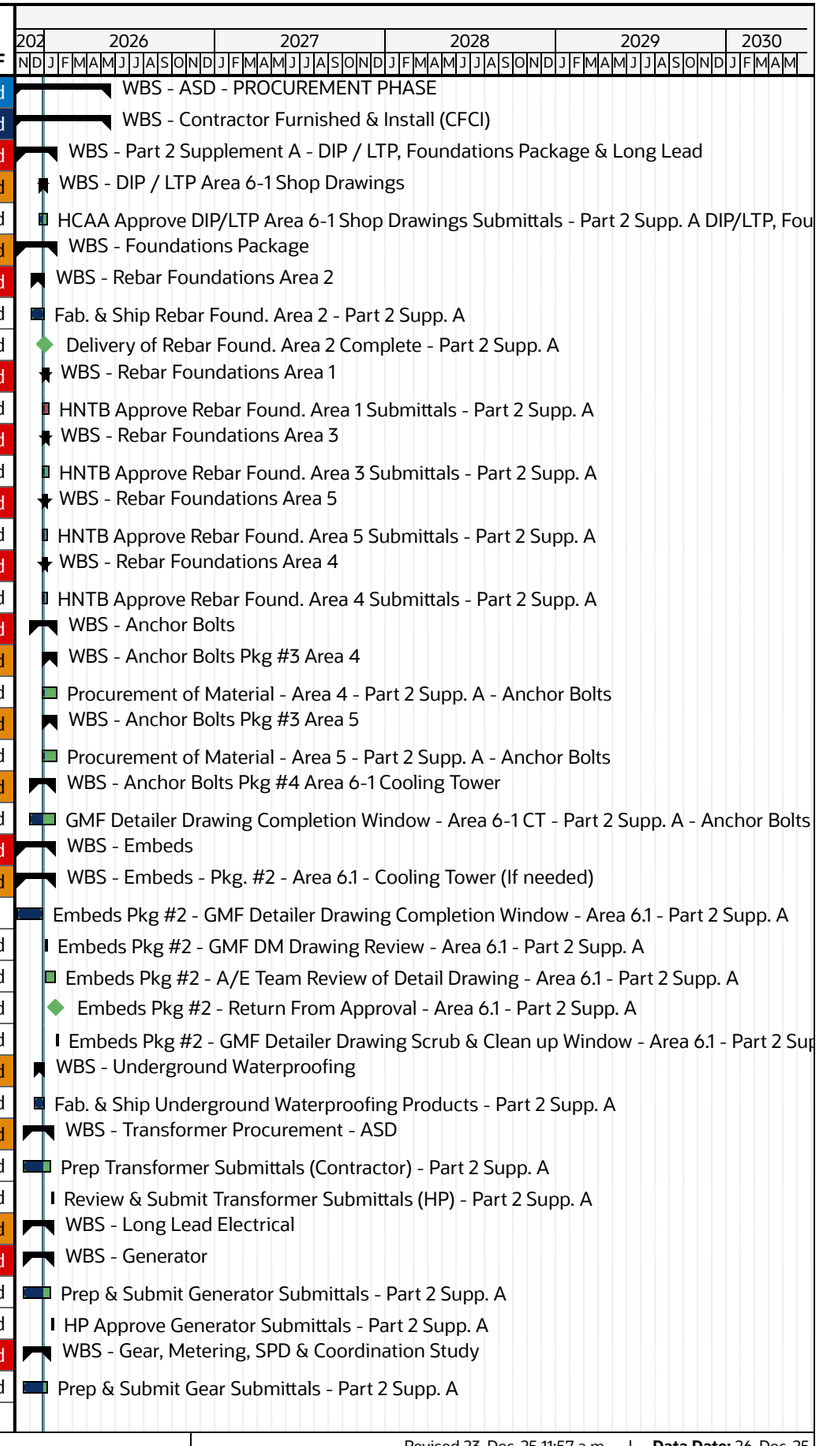


	ID	Name	Dur	Start	Finish	TF
169	PR-P2-1B-7930	HP Approve Gear Submittals - Part 2 Supp. A	5.0d	6-Jan-26	12-Jan-26	166.0d
170	WBS - UPS Package		45.0d	13-Nov-25 A	20-Jan-26	170.0d
171	PR-P2-1B-3000	Prep & Submit UPS Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	170.0d
172	PR-P2-1B-7950	HP Approve UPS Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	170.0d
173	WBS - Long Lead Mechanical		45.0d	12-Nov-25 A	19-Jan-26	363.0d
174	WBS - Chillers Procurement		45.0d	12-Nov-25 A	19-Jan-26	363.0d
175	PR-P2-1B-100	Prep & Submit Chillers Submittals - Part 2 Supp. A	30.0d	12-Nov-25 A	26-Dec-25 A	
176	PR-P2-1B-7970	HP Approve Chillers Submittals - Part 2 Supp. A	5.0d	29-Dec-25	5-Jan-26	363.0d
177	PR-P2-1B-7980	HNTB Approve Chillers Submittals - Part 2 Supp. A	10.0d	6-Jan-26	19-Jan-26	363.0d
178	WBS - Long Lead Mill Order		20.0d	3-Dec-25 A	31-Dec-25	0.0d
179	PR-P2-1B-7990	Issue / Process PO to Mill - Part 2 Supp. A	20.0d	3-Dec-25 A	31-Dec-25	0.0d
180	WBS - Part 2 Supplement B - ASD Steel & Precast		139.0d	31-Oct-25 A	19-May-26	308.0d
181	WBS - Structural Steel / Misc. Metals Procurement		139.0d	31-Oct-25 A	19-May-26	308.0d
182	WBS - Structural Steel Seq 1		20.0d	19-Dec-25 A	19-Jan-26	23.0d
183	PR-P2-1B-7620	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	19-Dec-25 A	19-Jan-26	23.0d
184	PR-P2-1B-7630	Return From Approval Struct. Steel/Misc. Metals SEQ 1 - Part 2 Supp. B	0.0d		19-Jan-26	23.0d
185	WBS - Structural Steel Seq 2		43.0d	31-Oct-25 A	5-Jan-26	5.0d
186	PR-P2-1B-3710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 2 - ...	38.0d	31-Oct-25 A	26-Dec-25 A	
187	PR-P2-1B-3720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 S...	5.0d	29-Dec-25	5-Jan-26	5.0d
188	WBS - Structural Steel Seq 3		53.0d	31-Oct-25 A	19-Jan-26	3.0d
189	PR-P2-1B-4810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 3 - ...	48.0d	31-Oct-25 A	12-Jan-26	3.0d
190	PR-P2-1B-4820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 S...	5.0d	13-Jan-26	19-Jan-26	3.0d
191	WBS - Structural Steel Seq 4		58.0d	31-Oct-25 A	26-Jan-26	3.0d
192	PR-P2-1B-3760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 4 - ...	58.0d	31-Oct-25 A	26-Jan-26	3.0d
193	WBS - Structural Steel Seq 5		63.0d	31-Oct-25 A	2-Feb-26	9.0d
194	PR-P2-1B-3810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 5 - ...	63.0d	31-Oct-25 A	2-Feb-26	9.0d
195	WBS - Structural Steel Seq 6		73.0d	31-Oct-25 A	16-Feb-26	36.0d
196	PR-P2-1B-3860	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 6 - ...	73.0d	31-Oct-25 A	16-Feb-26	36.0d
197	WBS - Structural Steel Seq 7		68.0d	31-Oct-25 A	9-Feb-26	29.0d
198	PR-P2-1B-3910	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 7 - ...	68.0d	31-Oct-25 A	9-Feb-26	29.0d
199	WBS - Structural Steel Seq 8		78.0d	31-Oct-25 A	23-Feb-26	45.0d
200	PR-P2-1B-3960	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 8 - ...	78.0d	31-Oct-25 A	23-Feb-26	45.0d
201	WBS - Structural Steel Seq 9		88.0d	31-Oct-25 A	9-Mar-26	43.0d
202	PR-P2-1B-4710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 9 - ...	88.0d	31-Oct-25 A	9-Mar-26	43.0d
203	WBS - Structural Steel Seq 10		93.0d	31-Oct-25 A	16-Mar-26	30.0d
204	PR-P2-1B-4760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 10 ...	93.0d	31-Oct-25 A	16-Mar-26	30.0d
205	WBS - Structural Steel Seq 11		98.0d	31-Oct-25 A	23-Mar-26	48.0d
206	PR-P2-1B-4010	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 11 ...	98.0d	31-Oct-25 A	23-Mar-26	48.0d
207	WBS - Structural Steel Seq 12		103.0d	31-Oct-25 A	30-Mar-26	35.0d
208	PR-P2-1B-6970	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 12 ...	103.0d	31-Oct-25 A	30-Mar-26	35.0d
209	WBS - Structural Steel Seq 13		108.0d	31-Oct-25 A	6-Apr-26	45.0d
210	PR-P2-1B-7060	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 13 ...	108.0d	31-Oct-25 A	6-Apr-26	45.0d

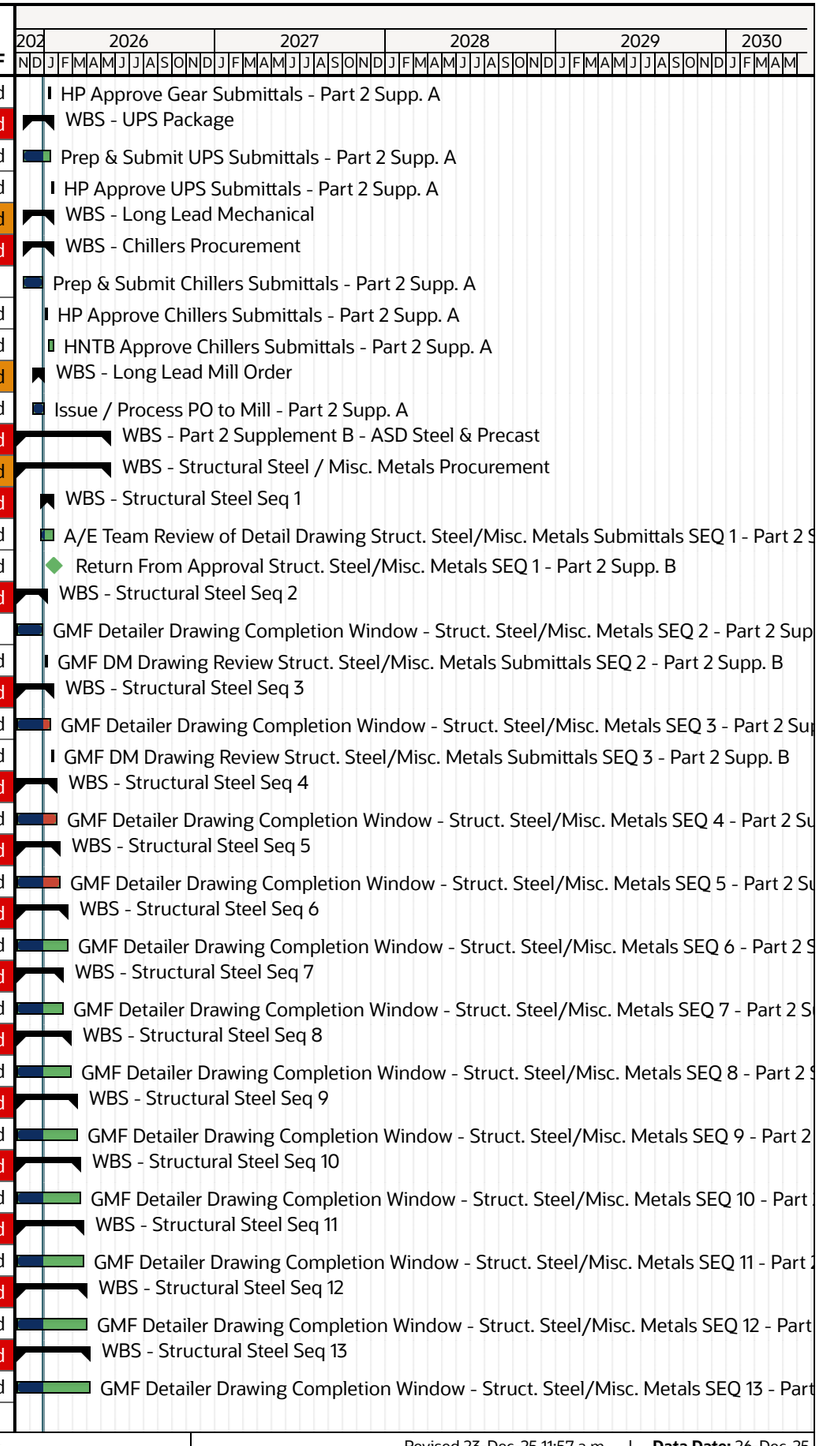


	ID	Name	Dur	Start	Finish	TF
211	WBS - Structural Steel Seq 14		113.0d	31-Oct-25 A	13-Apr-26	43.0d
212	PR-P2-1B-7150	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 14 ...	113.0d	31-Oct-25 A	13-Apr-26	43.0d
213	WBS - Structural Steel Seq 15		119.0d	31-Oct-25 A	21-Apr-26	42.0d
214	PR-P2-1B-7240	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 15 ...	119.0d	31-Oct-25 A	21-Apr-26	42.0d
215	WBS - Structural Steel Seq 16		124.0d	31-Oct-25 A	28-Apr-26	49.0d
216	PR-P2-1B-7330	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 16 ...	124.0d	31-Oct-25 A	28-Apr-26	49.0d
217	WBS - Structural Steel Seq 17		129.0d	31-Oct-25 A	5-May-26	48.0d
218	PR-P2-1B-7420	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 17 ...	129.0d	31-Oct-25 A	5-May-26	48.0d
219	WBS - Structural Steel Seq 18		134.0d	31-Oct-25 A	12-May-26	49.0d
220	PR-P2-1B-7510	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 18 ...	134.0d	31-Oct-25 A	12-May-26	49.0d
221	WBS - Structural Steel Seq 19		139.0d	31-Oct-25 A	19-May-26	57.0d
222	PR-P2-1B-7690	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 19 ...	139.0d	31-Oct-25 A	19-May-26	57.0d
223	WBS - Structural Steel Seq 20 (Cooling Tower)		124.0d	31-Oct-25 A	28-Apr-26	323.0d
224	PR-P2-1B-7820	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals (Cooling...	124.0d	31-Oct-25 A	28-Apr-26	323.0d
225	WBS - Precast Procurement		26.0d	17-Dec-25 A	23-Jan-26	21.0d
226	WBS - Elevator Cores		26.0d	17-Dec-25 A	23-Jan-26	21.0d
227	PR-P2-1B-7780	HNTB Review & Approve Elevator Cores Submittals - Part 2 Supp. B	11.0d	17-Dec-25 A	2-Jan-26	21.0d
228	PR-P2-1B-6720	HCAA Review & Approve Elevator Cores - Part 2 Supp. B	15.0d	5-Jan-26	23-Jan-26	21.0d
229	WBS - Part 1 Supplement C Wave 1 - Core & Shell Procurement		132.0d	20-Oct-25 A	27-Apr-26	976.0d
230	WBS - Baggage Handling System Procurement - ASD		132.0d	20-Oct-25 A	27-Apr-26	976.0d
231	WBS - General BHS Submittals & Procurement - ASD		63.0d	20-Oct-25 A	20-Jan-26	1,045.0d
232	WBS - Quality Control Manual Submittals - ASD		63.0d	20-Oct-25 A	20-Jan-26	263.0d
233	A109250	Prep & Submit Quality Control Manual - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
234	A109260	Review & Approve (HP) Quality Control Manual - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
235	A109270	Review & Approve (HNTB) Quality Control Manual - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
236	WBS - Environmental Requirements Submittals - ASD		63.0d	20-Oct-25 A	20-Jan-26	1,045.0d
237	A109310	Prep & Submit Environmental Requirements - ASD	48.0d	20-Oct-25 A	29-Dec-25	1,044.0d
238	A109340	Review & Approve (HP) Environmental Requirements - ASD	5.0d	30-Dec-25	6-Jan-26	1,044.0d
239	A109380	Review & Approve (HNTB) Environmental Requirements - ASD	10.0d	7-Jan-26	20-Jan-26	1,044.0d
240	WBS - Project Organizational Chart & Management Team Submittals - ASD		63.0d	20-Oct-25 A	20-Jan-26	263.0d
241	A109300	Prep & Submit Project Organizational Chart & Management Team - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
242	A109320	Review & Approve (HP) Project Organizational Chart & Management Team - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
243	A109400	Review & Approve (HNTB) Project Organizational Chart & Management Team - ...	10.0d	7-Jan-26	20-Jan-26	263.0d
244	WBS - Detailed Master Schedule Submittals - ASD		63.0d	20-Oct-25 A	20-Jan-26	263.0d
245	A109290	Prep & Submit Detailed Master Schedule - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
246	A109330	Review & Approve (HP) Detailed Master Schedule - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
247	A109420	Review & Approve (HNTB) Detailed Master Schedule - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
248	WBS - O&M Manual Submittals - ASD		36.0d	18-Nov-25 A	12-Jan-26	653.0d
249	A109350	Prep & Submit O&M Manual - Draft - ASD	31.0d	18-Nov-25 A	5-Jan-26	653.0d
250	A109440	Review & Approve (HP) O&M Manual - Draft - ASD	5.0d	6-Jan-26	12-Jan-26	653.0d
251	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - ASD		111.0d	18-Nov-25 A	27-Apr-26	861.0d
252	WBS - General Electrical/Controls/Software Engineering Submittals - ASD		111.0d	18-Nov-25 A	27-Apr-26	861.0d

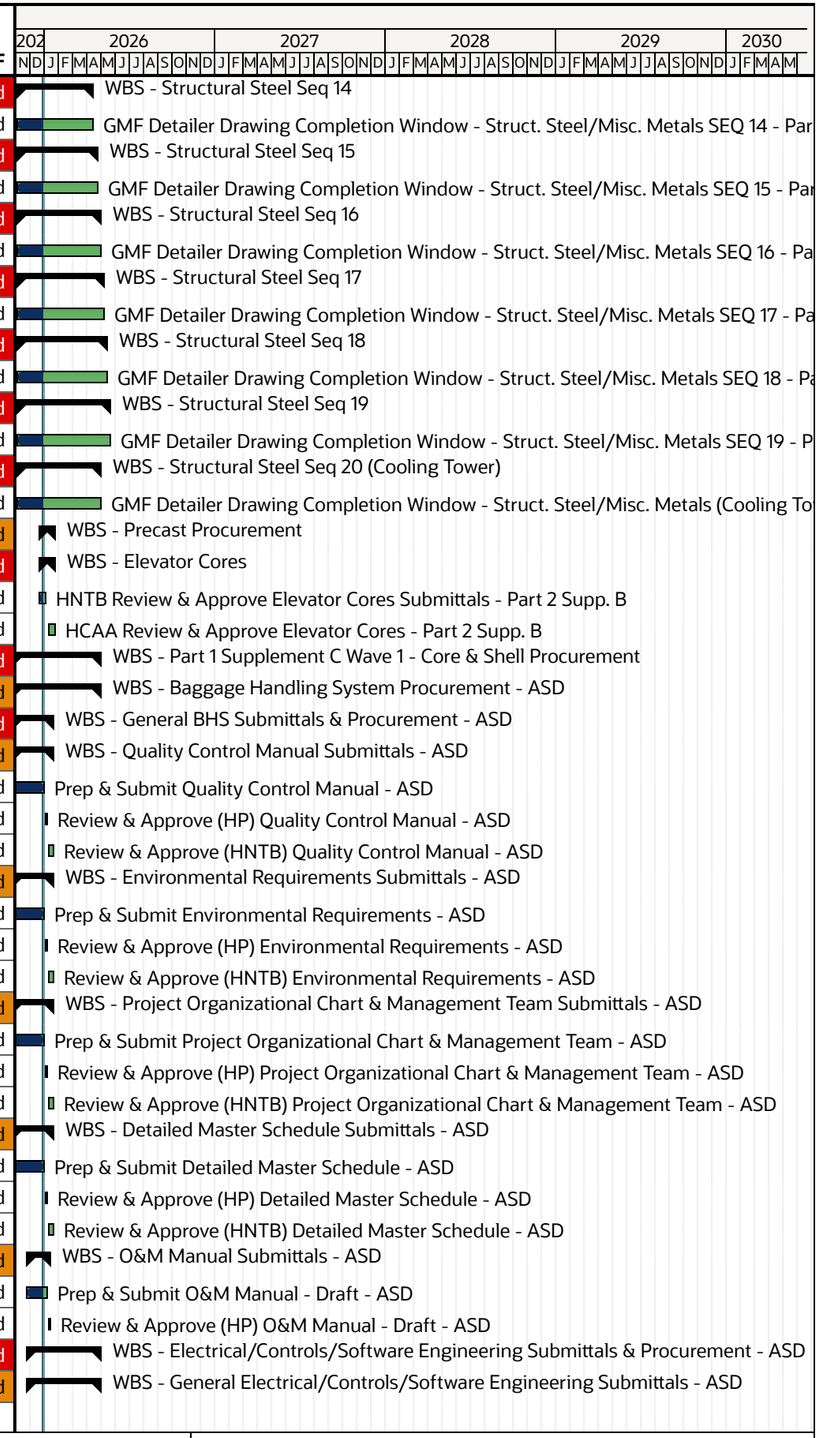

	ID	Name	Dur	Start	Finish	TF
253	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		42.0d	18-Nov-25 A	20-Jan-26	373.0d
254	A110050	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	27.0d	18-Nov-25 A	29-Dec-25	373.0d
255	A110070	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
256	A110160	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
257	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		15.0d	30-Dec-25	20-Jan-26	930.0d
258	A110020	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	30-Dec-25	20-Jan-26	929.0d
259	WBS - Functional Specification Submittals		111.0d	18-Nov-25 A	27-Apr-26	535.0d
260	A110060	Prep & Submit Functional Specification [180 days prior to pre-TRR]	111.0d	18-Nov-25 A	27-Apr-26	535.0d
261	WBS - VDC Coordination		29.0d	8-Dec-25 A	19-Jan-26	188.0d
262	WBS - Deep Underground - VDC Coordination		29.0d	8-Dec-25 A	19-Jan-26	188.0d
263	WBS - Deep UG East VDC Coordination		21.0d	8-Dec-25 A	29-Dec-25	168.0d
264	WBS - Mechanical Shop Drawings - Deep UG East VDC Coordination		21.0d	8-Dec-25 A	29-Dec-25	168.0d
265	PR-VDC-DU-4100	Fab. & Ship Deep UG East Mech. Shop Drawings	21.0d	8-Dec-25 A	29-Dec-25	168.0d
266	WBS - Deep UG West VDC Coordination		15.0d	29-Dec-25	19-Jan-26	188.0d
267	WBS - Plumbing Shop Drawings - Deep UG West VDC Coordination		15.0d	29-Dec-25	19-Jan-26	73.0d
268	PR-VDC-DU-4360	Prep & Submit Deep UG West Plumbing Shop Drawings	10.0d	29-Dec-25	12-Jan-26	73.0d
269	PR-VDC-DU-4370	Review & Approve (HP) Deep UG West Plumbing Shop Drawings	5.0d	13-Jan-26	19-Jan-26	73.0d
270	WBS - Electrical & Low Voltage Shop Drawings - Deep UG West VDC Coordination		15.0d	29-Dec-25	19-Jan-26	188.0d
271	PR-VDC-DU-4410	Prep & Submit Deep UG West Elec. Shop Drawings	10.0d	29-Dec-25	12-Jan-26	91.0d
272	PR-VDC-DU-4420	Review & Approve (HP) Deep UG West Elec.Shop Drawings	5.0d	13-Jan-26	19-Jan-26	188.0d
273	WBS - ASD - CONSTRUCTION PHASE		975.0d	13-Dec-24 A	15-Oct-28	106.0d
274	WBS - Enabling		296.0d	13-Dec-24 A	12-Feb-26	785.0d
275	WBS - Hammocks		296.0d	13-Dec-24 A	12-Feb-26	785.0d
276	EN-HAM-10	Enabling Scope (GCs/Markups) - (LOE)	296.0d	13-Dec-24 A	12-Feb-26	785.0d
277	WBS - Ground Improvements		27.0d	15-Dec-25 A	22-Jan-26	85.0d
278	WBS - Rigid Inclusions - Area 2		5.0d	29-Dec-25	5-Jan-26	98.0d
279	GI-A2-120	Cut Dip RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
280	GI-A2-130	Install Grout & Install Steel Caps - RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
281	WBS - Rigid Inclusions - Area 1		18.0d	15-Dec-25 A	9-Jan-26	41.0d
282	GI-A1-20	DIP Install - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
283	GI-A1-30	Excavate - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
284	GI-A1-40	Cut Dip & Install Grout - RI DIPS Area 1 - 12/13 Line	2.0d	6-Jan-26	7-Jan-26	41.0d
285	GI-A1-50	Install Steel Caps - RI DIPS Area 1 - 12/13 Line	2.0d	8-Jan-26	9-Jan-26	41.0d
286	WBS - Rigid Inclusions - Area 3		24.0d	15-Dec-25 A	19-Jan-26	51.0d
287	GI-A3-140	DIP Install - RI DIPS Area 3	20.0d	15-Dec-25 A	13-Jan-26	46.0d
288	GI-A3-100	Excavate - RI DIPS Area 3	14.0d	15-Dec-25 A	5-Jan-26	51.0d
289	GI-A3-110	Cut Dip & Install Grout - RI DIPS Area 3	5.0d	6-Jan-26	12-Jan-26	51.0d
290	GI-A3-120	Install Steel Caps - RI DIPS Area 3	5.0d	13-Jan-26	19-Jan-26	51.0d
291	WBS - Rigid Inclusions - Area 5		19.0d	15-Dec-25 A	12-Jan-26	81.0d
292	GI-A5-100	DIP Install - RI DIPS Area 5	19.0d	15-Dec-25 A	12-Jan-26	47.0d
293	GI-A5-110	Excavate - RI DIPS Area 5	14.0d	15-Dec-25 A	5-Jan-26	82.0d
294	GI-A5-120	Cut Dip & Install Grout - RI DIPS Area 5	2.0d	6-Jan-26	7-Jan-26	82.0d

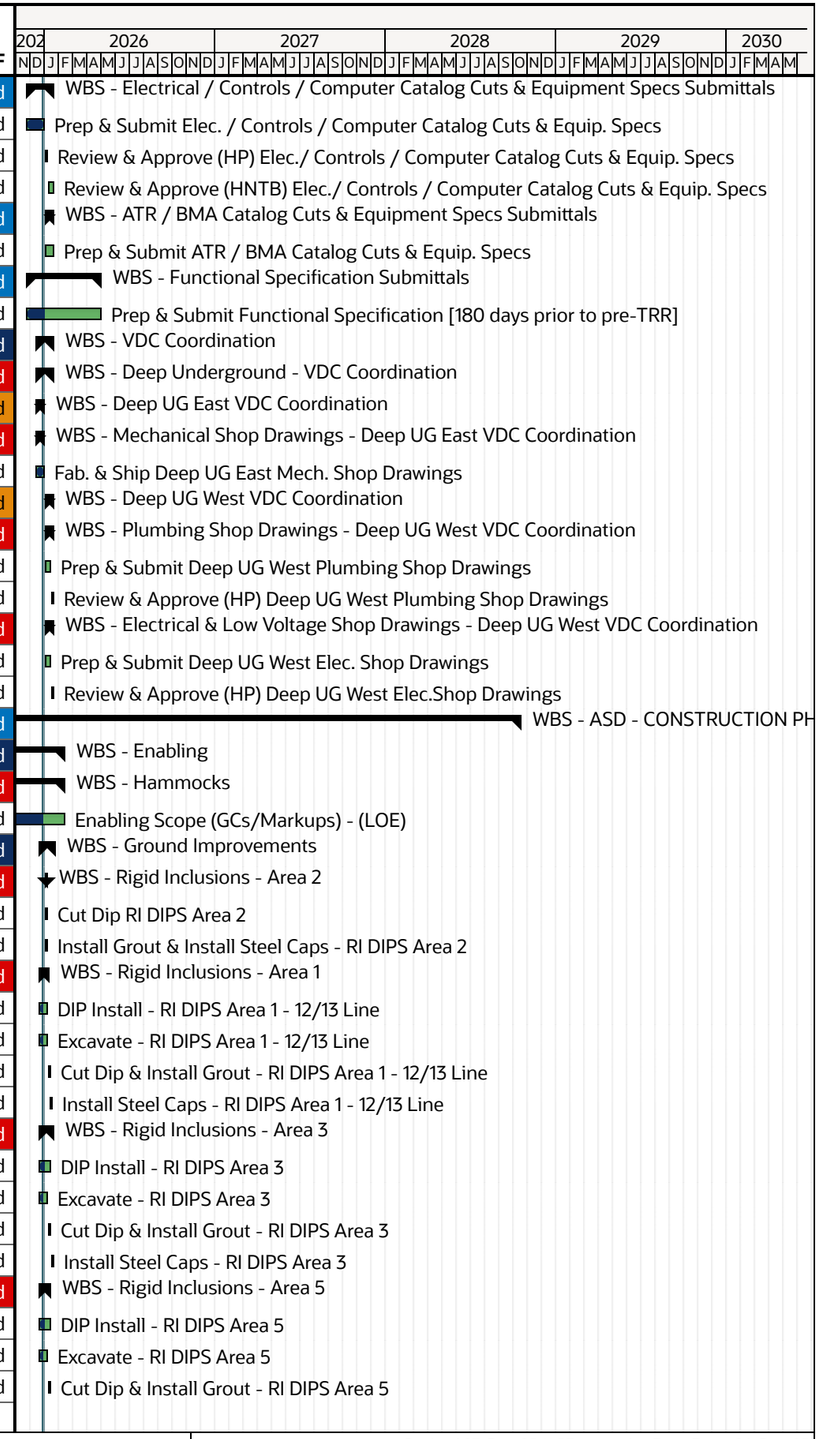

	ID	Name	Dur	Start	Finish	TF
295	GI-A5-130	Install Steel Caps - RI DIPS Area 5	2.0d	8-Jan-26	9-Jan-26	82.0d
296	WBS - Rigid Inclusions - Area 4		7.0d	14-Jan-26	22-Jan-26	46.0d
297	GI-A4-90	Excavate - RI DIPS Area 4	5.0d	14-Jan-26	20-Jan-26	46.0d
298	GI-A4-100	Cut Dip & Install Grout - RI DIPS Area 4	2.0d	21-Jan-26	22-Jan-26	46.0d
299	WBS - Rigid Inclusions - Area 6-1 Cooling Tower		5.0d	14-Jan-26	20-Jan-26	49.0d
300	GI-A6-1-100	DIP Install - RI DIPS Area 6 - 1	4.0d	14-Jan-26	19-Jan-26	49.0d
301	GI-A6-1-110	Excavate - RI DIPS Area 6 - 1	3.0d	14-Jan-26	16-Jan-26	49.0d
302	GI-A6-1-120	Cut Dip & Install Grout - RI DIPS Area 6 - 1	2.0d	19-Jan-26	20-Jan-26	49.0d
303	WBS - Foundations & Deep Underground		27.0d	16-Dec-25 A	23-Jan-26	129.0d
304	WBS - Foundations - Area 6		21.0d	16-Dec-25 A	15-Jan-26	4.0d
305	GI-FS-A1-6820	FRP Found. - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
306	GI-FS-A1-6840	MEPF In-Wall R/I - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
307	GI-FS-A1-6825	FRP Turndown - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
308	GI-FS-A1-6830	Install Waterproofing On Found. - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
309	GI-FS-A1-6850	Backfill Found. - Area 6	7.0d	7-Jan-26	15-Jan-26	4.0d
310	WBS - Foundations - Area 2		5.0d	16-Jan-26	22-Jan-26	4.0d
311	GI-FS-A1-6610	Excavate Area For Found. - Area 2.A	5.0d	16-Jan-26	22-Jan-26	4.0d
312	WBS - Deep Underground MEP - All Areas		23.0d	22-Dec-25 A	23-Jan-26	129.0d
313	WBS - Deep Underground MEP - Area 2		22.0d	22-Dec-25 A	22-Jan-26	116.0d
314	GI-FS-A2-5570	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.2	6.0d	22-Dec-25 A	30-Dec-25	30.0d
315	GI-FS-A2-5500	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.1	21.0d	23-Dec-25 A	22-Jan-26	10.0d
316	GI-FS-A2-5610	Inspect - Deep UG Sanitary - Plumber - Area 2.B.2	2.0d	29-Dec-25	30-Dec-25	30.0d
317	GI-FS-A2-6980	Excavate - Deep UG Piping - Mech. - Area 2.B	4.0d	30-Dec-25	5-Jan-26	120.0d
318	GI-FS-A2-5630	Backfill - Deep UG Sanitary - Plumber - Area 2.B.2	3.0d	31-Dec-25	5-Jan-26	30.0d
319	GI-FS-A2-6990	Install - Deep UG Piping - Mech. - Area 2.B	4.0d	6-Jan-26	9-Jan-26	120.0d
320	GI-FS-A2-7120	Excavate - Deep UG Water Main - Plumbing - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
321	GI-FS-A2-7080	Excavate - Deep UG Fire Main - Fire - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
322	GI-FS-A2-5420	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.1	5.0d	8-Jan-26	14-Jan-26	102.0d
323	GI-FS-A2-7000	Inspect - Deep UG Piping - Mech. - Area 2.B	2.0d	12-Jan-26	13-Jan-26	120.0d
324	GI-FS-A2-5440	Inspect - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	13-Jan-26	14-Jan-26	102.0d
325	GI-FS-A2-7130	Install Pipe - Deep UG Water Main - Plumbing - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
326	GI-FS-A2-7090	Install Pipe - Deep UG Fire Main - Fire - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
327	GI-FS-A2-7010	Backfill - Deep UG Piping - Mech. - Area 2.B	3.0d	14-Jan-26	16-Jan-26	120.0d
328	GI-FS-A2-5450	Backfill - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	15-Jan-26	16-Jan-26	102.0d
329	GI-FS-A2-7140	Inspect - Deep UG Water Main - Plumbing - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
330	GI-FS-A2-7100	Inspect - Deep UG Fire Main - Fire - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
331	GI-FS-A2-7150	Backfill - Deep UG Water Main - Plumbing - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
332	GI-FS-A2-7110	Backfill - Deep UG Fire Main - Fire - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
333	WBS - Deep Underground MEP - Area 1		14.0d	6-Jan-26	23-Jan-26	65.0d
334	GI-FS-A1-7070	Excavate - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	6-Jan-26	14-Jan-26	30.0d
335	GI-FS-A1-5650	Excavate - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	6-Jan-26	14-Jan-26	65.0d
336	GI-FS-A1-7080	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	15-Jan-26	23-Jan-26	30.0d

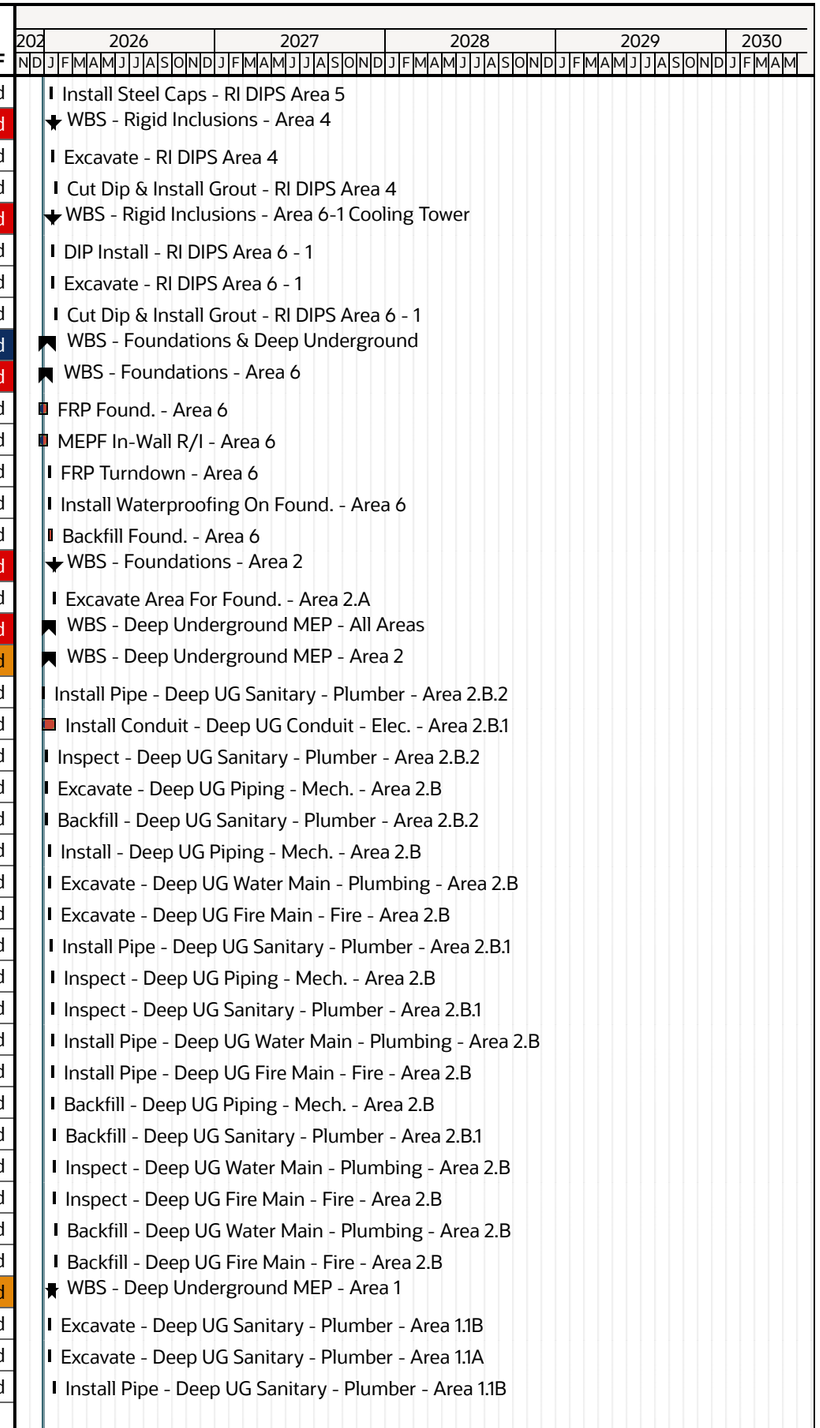


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
30 Day Look Ahead Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:57 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
337	GI-FS-A1-5710	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	15-Jan-26	23-Jan-26	65.0d
338	GI-FS-A1-7090	Inspect - Deep UG Sanitary - Plumber - Area 1.1B	2.0d	22-Jan-26	23-Jan-26	30.0d
339	GI-FS-A1-5750	Inspect - Deep UG Sanitary - Plumber - Area 1.1A	2.0d	22-Jan-26	23-Jan-26	65.0d
340	WBS - Deep Underground MEP - Area 6		6.0d	16-Jan-26	23-Jan-26	129.0d
341	GI-FS-A6-5690	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.4	6.0d	16-Jan-26	23-Jan-26	129.0d
342	WBS - Civil		15.0d	29-Dec-25	19-Jan-26	72.0d
343	WBS - Performance Park North Craft Parking Lot		15.0d	29-Dec-25	19-Jan-26	72.0d
344	CP-FS-150	Layout/Survey - PP North Craft Parking Lot	3.0d	29-Dec-25	31-Dec-25	72.0d
345	CP-FS-160	Install BMP SWPPP Measures - PP North Craft Parking Lot	5.0d	2-Jan-26	8-Jan-26	72.0d
346	CP-FS-170	Install Dust Control Measure - Wheel/Tire Wash - PP North Craft Parking Lot	2.0d	9-Jan-26	12-Jan-26	72.0d
347	CP-FS-200	Demolish Fencing - PP North Craft Parking Lot	5.0d	13-Jan-26	19-Jan-26	72.0d
348	WBS - Invitation To Bid (ITB)		1,187.0d	19-Jun-25 A	15-Oct-28	148.0d
349	WBS - ITB -1 - Apron Pavement & Hydrant Fueling Construction		1,187.0d	19-Jun-25 A	15-Oct-28	148.0d
350	WBS - Inter Project Relationships (IPR)		1,187.0d	19-Jun-25 A	15-Oct-28	148.0d
351	IPR-ITB1-MLS31	ITB1 Overall Project Duration SC 9.30.2028	1,187.0d	19-Jun-25 A	15-Oct-28 C	148.0d
352	WBS - ITB - 3 - Guideway Superstructure Construction		556.0d	25-Aug-25 A	16-Mar-27	169.0d
353	WBS - Inter Project Relationships (IPR)		556.0d	25-Aug-25 A	16-Mar-27	169.0d
354	IPR-ASD-ITB3-210	ITB 3 - Total Project Duration SC 2.16.2027 (By Others)	556.0d	25-Aug-25 A	16-Mar-27	169.0d
355	WBS - ASD - COMMISSIONING PHASE		15.0d	29-Dec-25	19-Jan-26	785.0d
356	WBS - ASD - Commissioning - Administrative		15.0d	29-Dec-25	19-Jan-26	785.0d
357	COM-ADM-100	Develop & Submit Cx Plan (Design) - Admin Commissioning	15.0d	29-Dec-25	19-Jan-26	785.0d
358	WBS - CENTRALIZED CHECKED BAGGAGE SYSTEM RELOCATION AND UPGRADES		481.0d	20-Oct-25 A	10-Sep-27	612.0d
359	WBS - CCBS - PROCUREMENT PHASE		107.0d	20-Oct-25 A	23-Mar-26	986.0d
360	WBS - Owner Furnished Contractor Installed (OFCI)		46.0d	14-Nov-25 A	22-Jan-26	81.0d
361	WBS - Tag & Trace Submittals		46.0d	14-Nov-25 A	22-Jan-26	81.0d
362	WBS - Low Volt Tag & Trace Submittals		46.0d	14-Nov-25 A	22-Jan-26	81.0d
363	A64150	Prep & Submit Product Data for Low Voltage Tag & Trace Relocation	31.0d	14-Nov-25 A	31-Dec-25	81.0d
364	A106450	Review & Approve (HP) Product Data for Low Voltage Tag & Trace Relocation	5.0d	2-Jan-26	8-Jan-26	81.0d
365	A64160	Review & Approve (HNTB) Product Data for Low Voltage Tag & Trace Relocation	10.0d	9-Jan-26	22-Jan-26	81.0d
366	WBS - Contractor Furnished & Install (CFCI)		107.0d	20-Oct-25 A	23-Mar-26	986.0d
367	WBS - Part 2 Supplement B - Centralized Checked Baggage Etc.		107.0d	20-Oct-25 A	23-Mar-26	986.0d
368	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supp. B		107.0d	20-Oct-25 A	23-Mar-26	986.0d
369	WBS - General BHS Submittals & Procurement - Part 2 Supp. B		63.0d	20-Oct-25 A	20-Jan-26	777.0d
370	WBS - System Inspection, Functional Specification, and Test Plan Submittals		36.0d	18-Nov-25 A	12-Jan-26	135.0d
371	D1056	Prep & Submit System Inspection, Functional Specification, & Test Plan	31.0d	18-Nov-25 A	5-Jan-26	135.0d
372	A101440	Review & Approve (HP) System Inspection, Functional Specification, & Test Plan	5.0d	6-Jan-26	12-Jan-26	135.0d
373	WBS - Quality Control Manual Submittals - Part 2 Supp. B		63.0d	20-Oct-25 A	20-Jan-26	139.0d
374	A101190	Prep & Submit Quality Control Manual	48.0d	20-Oct-25 A	29-Dec-25	139.0d
375	A101380	Review & Approve (HP) Quality Control Manual	5.0d	30-Dec-25	6-Jan-26	139.0d
376	A106570	Review & Approve (HNTB) Quality Control Manual	10.0d	7-Jan-26	20-Jan-26	139.0d
377	WBS - Environmental Requirements Submittals - Part 2 Supp. B		63.0d	20-Oct-25 A	20-Jan-26	777.0d
378	A101290	Prep & Submit Environmental Requirements	48.0d	20-Oct-25 A	29-Dec-25	777.0d

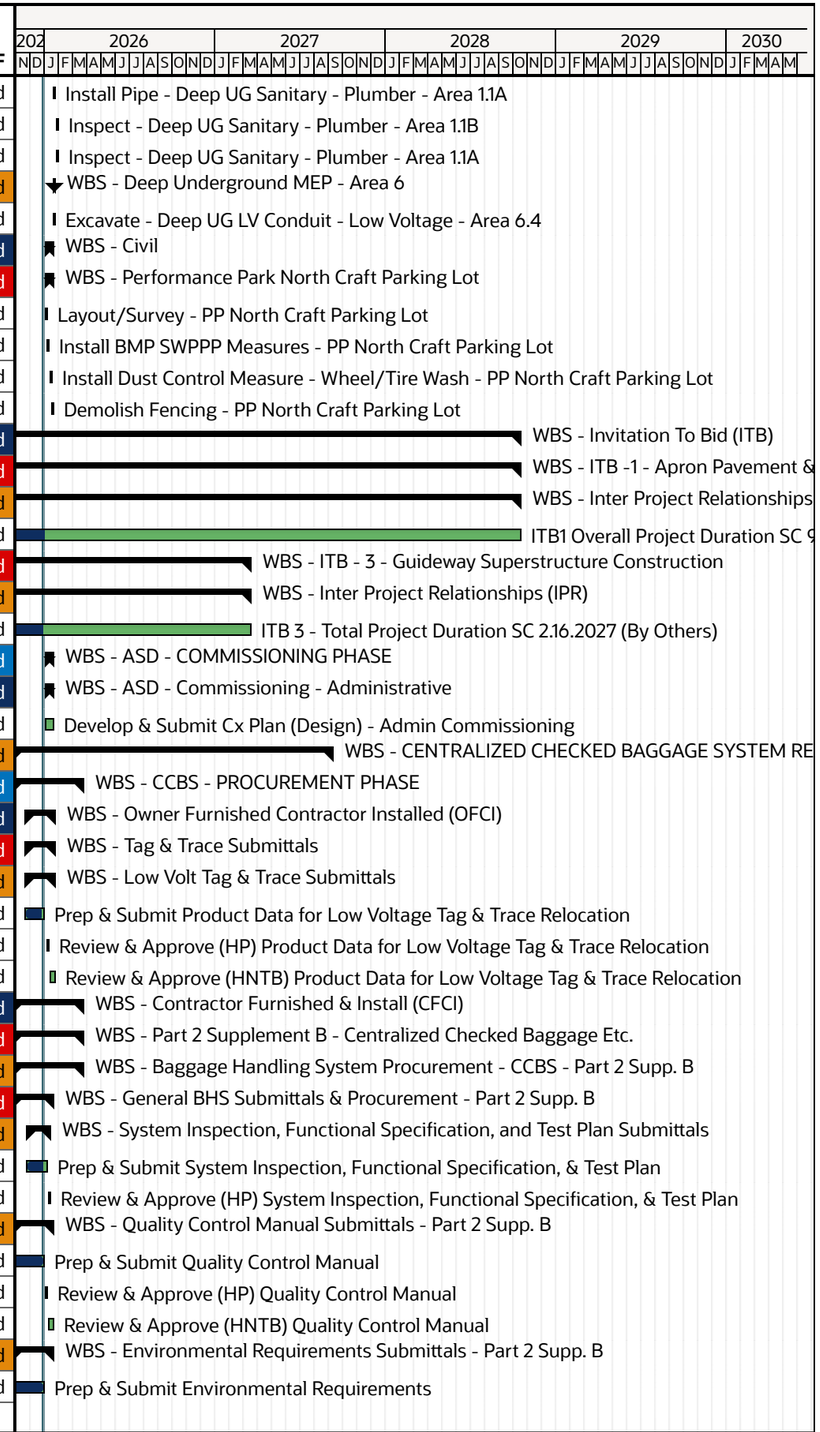


	ID	Name	Dur	Start	Finish	TF
379	A101430	Review & Approve (HP) Environmental Requirements	5.0d	30-Dec-25	6-Jan-26	777.0d
380	A106610	Review & Approve (HNTB) Environmental Requirements	10.0d	7-Jan-26	20-Jan-26	777.0d
381	WBS - Project Organizational Chart & Management Team Submittals - Part 2 Supp. B		63.0d	20-Oct-25 A	20-Jan-26	118.0d
382	A101280	Prep & Submit Project Organizational Chart & Management Team	48.0d	20-Oct-25 A	29-Dec-25	118.0d
383	A101370	Review & Approve (HP) Project Organizational Chart & Management Team	5.0d	30-Dec-25	6-Jan-26	118.0d
384	A106630	Review & Approve (HNTB) Project Organizational Chart & Management Team	10.0d	7-Jan-26	20-Jan-26	118.0d
385	WBS - Detailed Master Schedule Submittals - Part 2 Supp. B		63.0d	20-Oct-25 A	20-Jan-26	118.0d
386	A101220	Prep & Submit Detailed Master Schedule	48.0d	20-Oct-25 A	29-Dec-25	118.0d
387	A101420	Review & Approve (HP) Detailed Master Schedule	5.0d	30-Dec-25	6-Jan-26	118.0d
388	A106670	Review & Approve (HNTB) Detailed Master Schedule	10.0d	7-Jan-26	20-Jan-26	118.0d
389	WBS - Phasing Schedule Submittals - Part 2 Supp. B		36.0d	18-Nov-25 A	12-Jan-26	114.0d
390	A101270	Prep & Submit Phasing Schedule	31.0d	18-Nov-25 A	5-Jan-26	114.0d
391	A101410	Review & Approve (HP) Phasing Schedule	5.0d	6-Jan-26	12-Jan-26	114.0d
392	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supp. B		45.0d	18-Nov-25 A	23-Jan-26	46.0d
393	WBS - General Mechanical BHS Submittals & Procurement - Part 2 Supp. B		41.0d	18-Nov-25 A	19-Jan-26	50.0d
394	WBS - Mechanical Catalog Cut / Equipment Specs Submittals - Part 2 Supp. B		23.0d	9-Dec-25 A	12-Jan-26	0.0d
395	A110550	Revise & Resubmit (Daifuku) Mech. Catalog Cut / Equip. Specs	13.0d	9-Dec-25 A	26-Dec-25 A	
396	A110560	Review & Approve (HNTB) Mech. Catalog Cut / Equip. Specs	10.0d	29-Dec-25	12-Jan-26	0.0d
397	WBS - Motor Schedule Submittals - Part 2 Supp. B		36.0d	18-Nov-25 A	12-Jan-26	55.0d
398	A101610	Prep & Submit Motor Schedule	31.0d	18-Nov-25 A	5-Jan-26	55.0d
399	A106830	Review & Approve (HP) Motor Schedule	5.0d	6-Jan-26	12-Jan-26	55.0d
400	WBS - General Mechanical Assembly Detail Drawings Submittals - Part 2 Supp. B		30.0d	5-Dec-25 A	19-Jan-26	0.0d
401	D1084	Review & Approve (HCAA) General Mech. Assembly Detail Drawings	30.0d	5-Dec-25 A	19-Jan-26	0.0d
402	WBS - Seq 1-Stage 1-Step 1 - Part 2 Supp. B		16.0d	18-Dec-25 A	12-Jan-26	0.0d
403	WBS - BHS Mechanical Submittals [01-01-01]		16.0d	18-Dec-25 A	12-Jan-26	0.0d
404	D1093	Review & Approve (HCAA) Mech Plan & Elev Dwg Set [01-01-01]	16.0d	18-Dec-25 A	12-Jan-26	0.0d
405	WBS - Seq 1 - Stage 1 - Step 2		27.0d	16-Dec-25 A	23-Jan-26	16.0d
406	WBS - BHS Mechanical Submittals [01-01-02]		27.0d	16-Dec-25 A	23-Jan-26	16.0d
407	D3576	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-02]	12.0d	16-Dec-25 A	2-Jan-26	16.0d
408	D1102	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-02]	15.0d	5-Jan-26	23-Jan-26	16.0d
409	WBS - Seq 1 - Stage 1 - Step 3		27.0d	16-Dec-25 A	23-Jan-26	21.0d
410	WBS - BHS Mechanical Submittals [01-01-03]		27.0d	16-Dec-25 A	23-Jan-26	21.0d
411	D3626	Review & Approve Mech Plan & Elev Dwg Set (HNTB)t [01-01-03]	12.0d	16-Dec-25 A	2-Jan-26	21.0d
412	D1109	Review & Approve Mech Plan & Elev Dwg Set (HCAA)t [01-01-03]	15.0d	5-Jan-26	23-Jan-26	21.0d
413	WBS - Seq 1 - Stage 1 - Step 4		27.0d	16-Dec-25 A	23-Jan-26	18.0d
414	WBS - BHS Mechanical Submittals [01-01-04]		27.0d	16-Dec-25 A	23-Jan-26	18.0d
415	D3666	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-04]	12.0d	16-Dec-25 A	2-Jan-26	18.0d
416	D1116	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-04]	15.0d	5-Jan-26	23-Jan-26	18.0d
417	WBS - Seq 1 - Stage 1 - Step 5		15.0d	29-Dec-25	19-Jan-26	6.0d
418	WBS - BHS Mechanical Submittals [01-01-05]		15.0d	29-Dec-25	19-Jan-26	6.0d
419	D1123	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-05]	15.0d	29-Dec-25	19-Jan-26	6.0d
420	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		101.0d	28-Oct-25 A	23-Mar-26	986.0d

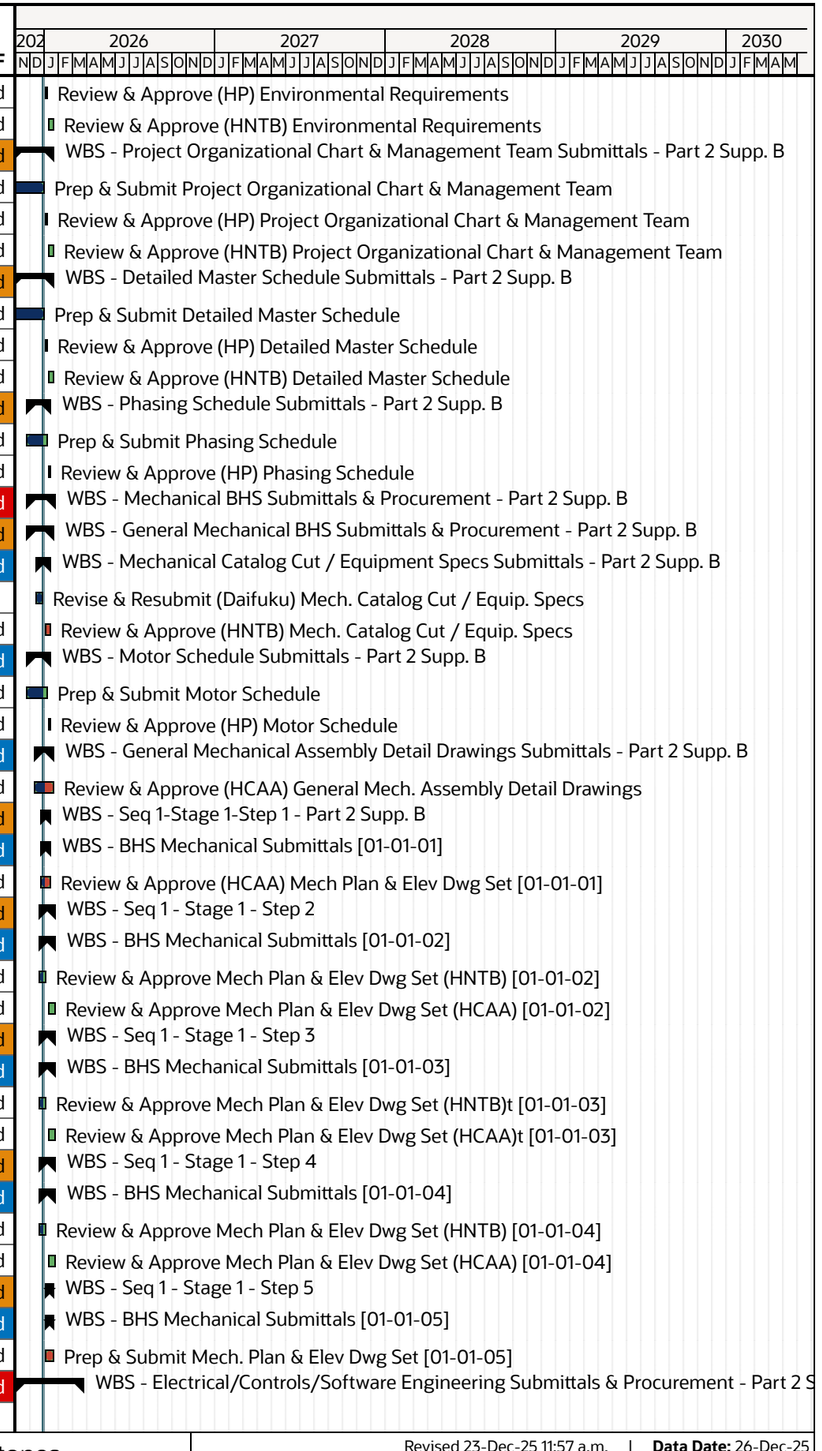


	ID	Name	Dur	Start	Finish	TF
421	WBS - General Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		101.0d	28-Oct-25 A	23-Mar-26	986.0d
422	WBS - Operator Interface / Control Station Typicals Submittals		15.0d	29-Dec-25	19-Jan-26	1,031.0d
423	A101900	Prep & Submit Operator Interface / Control Station Typicals	15.0d	29-Dec-25	19-Jan-26	1,030.0d
424	WBS - Cross-Belt Sorter XBM2 Elect Drawing Sets Submittals		16.0d	29-Dec-25	20-Jan-26	416.0d
425	A92270	Prep & Submit Cross-Belt Sorter XBM2 Elect Drawing Sets	1.0d	29-Dec-25	29-Dec-25	416.0d
426	A107280	Review & Approve (HP) Cross-Belt Sorter XBM2 Elect Dwg Sets	5.0d	30-Dec-25	6-Jan-26	416.0d
427	A107290	Review & Approve (HNTB) Cross-Belt Sorter XBM2 Elect Dwg Sets	10.0d	7-Jan-26	20-Jan-26	416.0d
428	WBS - Electrical Installation Catalog Cuts & Equipment Specs Submittals		52.0d	28-Oct-25 A	13-Jan-26	368.0d
429	A101910	Prep & Submit Elec. Install Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	368.0d
430	A107300	Review & Approve (HP) Elec.Install Catalog Cuts & Equip. Specs	10.0d	30-Dec-25	13-Jan-26	368.0d
431	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		57.0d	28-Oct-25 A	20-Jan-26	373.0d
432	A101930	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	373.0d
433	A101990	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
434	A107320	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
435	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		15.0d	29-Dec-25	19-Jan-26	973.0d
436	A101890	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	29-Dec-25	19-Jan-26	972.0d
437	WBS - Factory Acceptance Test Plan & Agenda Submittals		15.0d	29-Dec-25	19-Jan-26	596.0d
438	A101870	Prep & Submit Factory Acceptance Test Plan & Agenda [40 days prior to FAT da...	15.0d	29-Dec-25	19-Jan-26	596.0d
439	WBS - Cross-Belt Sorter Functional Specification Submittals		16.0d	29-Dec-25	20-Jan-26	600.0d
440	A101840	Prep & Submit Cross-Belt Sorter Functional Specification	1.0d	29-Dec-25	29-Dec-25	600.0d
441	A101980	Review & Approve (HP) Cross-Belt Sorter Functional Specification	5.0d	30-Dec-25	6-Jan-26	600.0d
442	A107460	Review & Approve (HNTB) Cross-Belt Sorter Functional Specification	10.0d	7-Jan-26	20-Jan-26	600.0d
443	WBS - Cross-Belt Sorter Control System Description of Operations Submittals		16.0d	29-Dec-25	20-Jan-26	600.0d
444	A101810	Prep & Submit Cross-Belt Sorter Control System Description of Operations	1.0d	29-Dec-25	29-Dec-25	600.0d
445	A101970	Review & Approve (HP) Cross-Belt Sorter Control System Description of Operati...	5.0d	30-Dec-25	6-Jan-26	600.0d
446	A107480	Review & Approve (HNTB) Cross-Belt Sorter Control System Description of Ope...	10.0d	7-Jan-26	20-Jan-26	600.0d
447	WBS - Functional Specification Submittals		86.0d	18-Nov-25 A	23-Mar-26	80.0d
448	A101960	Prep & Submit Functional Specification [180 days prior to pre-TRR]	86.0d	18-Nov-25 A	23-Mar-26	80.0d
449	WBS - Seq 1 - Stage 1 - Step 1		15.0d	29-Dec-25	19-Jan-26	64.0d
450	D1695	Prep & Submit Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-B17 [01-01-...	15.0d	29-Dec-25	19-Jan-26	64.0d
451	WBS - Electrical Long Lead System Procurement - CCBS - Part 2 Supp. B		10.0d	29-Dec-25	12-Jan-26	11.0d
452	A108940	Prep & Submit Long Lead Elec. Equip. Submittals - Part 2 Supp. B	5.0d	29-Dec-25 C	5-Jan-26	11.0d
453	A108950	Review & Approve (HP) Long Lead Elec.Equip. Submittals - Part 2 Supp. B	5.0d	6-Jan-26	12-Jan-26	11.0d
454	WBS - CCBS - CONSTRUCTION PHASE		481.0d	20-Oct-25 A	10-Sep-27	0.0d
455	WBS - Main Terminal CCBS Consolidation		481.0d	20-Oct-25 A	10-Sep-27	0.0d
456	WBS - CCBS - Building Infrastructure		481.0d	20-Oct-25 A	10-Sep-27	0.0d
457	WBS - BHS ROW Prep		481.0d	20-Oct-25 A	10-Sep-27	0.0d
458	WBS - Tag & Trace		481.0d	20-Oct-25 A	10-Sep-27	0.0d
459	CCBS-LOE-1000	Tag & Trace Elec.& Low Voltage (LOE)	481.0d	20-Oct-25 A	10-Sep-27	0.0d
460	WBS - Tag & Trace - Sequence 1 - Stage 1		45.0d	16-Nov-25 A	22-Jan-26	96.0d
461	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 1		36.0d	19-Nov-25 A	13-Jan-26	103.0d
462	TT-SQ1-SG1-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	19-Nov-25 A	29-Dec-25	103.0d

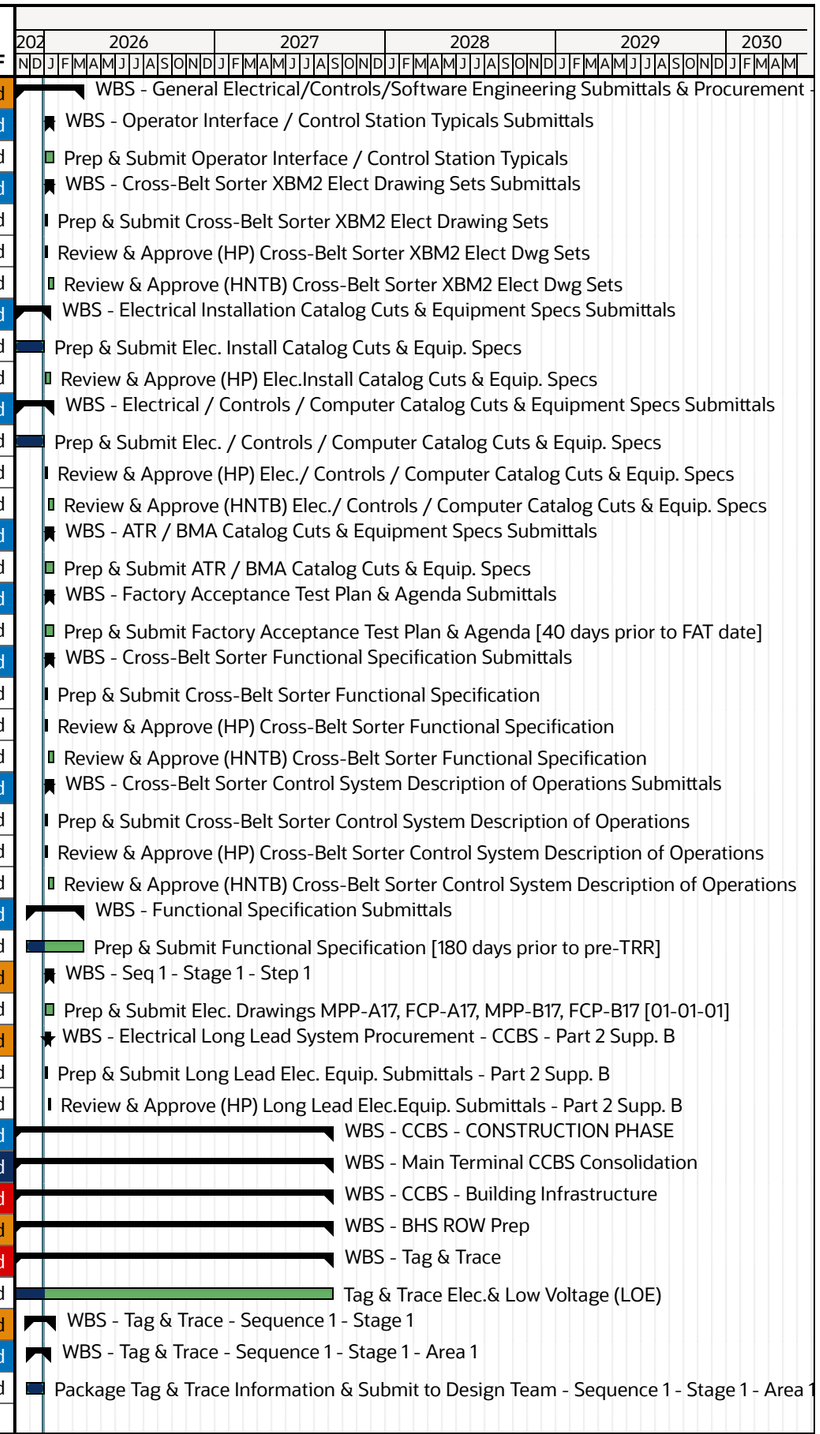

	ID	Name	Dur	Start	Finish	TF
463	TT-SQ1-SG1-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 1	10.0d	30-Dec-25	13-Jan-26	103.0d
464	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 2		36.0d	20-Nov-25 A	14-Jan-26	102.0d
465	TT-SQ1-SG1-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	20-Nov-25 A	30-Dec-25	102.0d
466	TT-SQ1-SG1-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 2	10.0d	31-Dec-25	14-Jan-26	102.0d
467	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 3		45.0d	16-Nov-25 A	22-Jan-26	96.0d
468	TT-SQ1-SG1-A3-10	Tag & Trace - Sequence 1 - Stage 1 - Area 3	30.0d	16-Nov-25 A	31-Dec-25	0.0d
469	TT-SQ1-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	2-Jan-26	8-Jan-26	96.0d
470	TT-SQ1-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 3	10.0d	9-Jan-26	22-Jan-26	96.0d
471	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 4		34.0d	20-Nov-25 A	12-Jan-26	94.0d
472	TT-SQ1-SG1-A4-10	Tag & Trace - Sequence 1 - Stage 1 - Area 4	29.0d	20-Nov-25 A	5-Jan-26	0.0d
473	TT-SQ1-SG1-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
474	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 5		27.0d	3-Dec-25 A	12-Jan-26	94.0d
475	TT-SQ1-SG1-A5-10	Tag & Trace - Sequence 1 - Stage 1 - Area 5	22.0d	3-Dec-25 A	5-Jan-26	0.0d
476	TT-SQ1-SG1-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
477	WBS - Tag & Trace - Sequence 1 - Stage 2		14.0d	6-Jan-26	23-Jan-26	0.0d
478	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 1		10.0d	6-Jan-26	19-Jan-26	0.0d
479	TT-SQ1-SG2-A1-10	Tag & Trace - Sequence 1 - Stage 2 - Area 1	10.0d	6-Jan-26	19-Jan-26	0.0d
480	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 2		10.0d	12-Jan-26	23-Jan-26	0.0d
481	TT-SQ1-SG2-A2-10	Tag & Trace - Sequence 1 - Stage 2 - Area 2	10.0d	12-Jan-26	23-Jan-26	0.0d

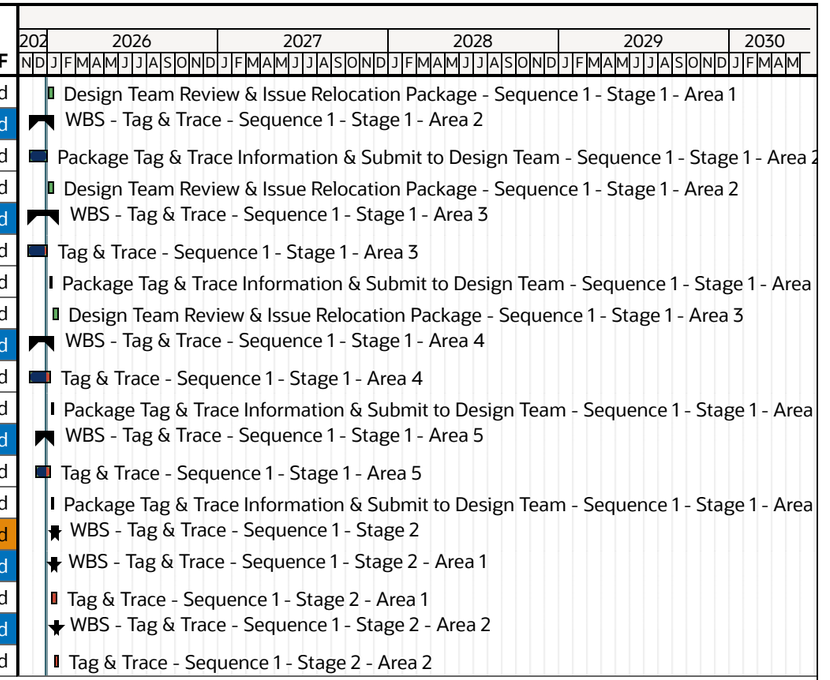

	ID	Name	Dur	Start	Finish	TF
1	WBS - Airside D - Tampa International Airport		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
2	WBS - PROJECT TIME TABLE SUMMARY		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
3	PTTS-10	Project Timetable Summary to Substantial Completion (LOE)	1,417.0d	3-Aug-23 A	2-Mar-29	0.0d
4	WBS - Airside D - Supplement C Contractual Milestones		0.0d	12-Feb-26	12-Feb-26	0.0d
5	MLS-SUPP.C-02	MLS 2 - Demo Second Half of Tunnel Structure Complete	0.0d		12-Feb-26 C	0.0d
6	WBS - Airside D - Other Major Milestones		24.0d	27-Jan-26	2-Mar-26	773.0d
7	MLS-380	MLS - Ground Improvements (DIPS) Complete	0.0d		27-Jan-26	46.0d
8	MLS-60	MLS - ASD - Enabling Scope Complete	0.0d		12-Feb-26	785.0d
9	WBS - Electrical Milestones		0.0d	2-Mar-26	2-Mar-26	71.0d
10	MLS-360	MLS - Temp Power to Building	0.0d		2-Mar-26	71.0d
11	WBS - Airside D - SOV LOE's		1,339.0d	13-Dec-24 A	21-Mar-30	0.0d
12	ASD-HAM-20	ASD - Contingency/Allowance/Budget - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
13	ASD-HAM-10	ASD - General Conditions / Requirements - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
14	CCBS-HAM-30	CCBS - Supp B General Conditions / Requirements - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
15	CCBS-HAM-40	CCBS - Supp B Contingency/Allowance/Budget - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
16	GI-HAM-10	Ground Improvements Scope LOE - DIP/LTP	63.0d	27-Oct-25 A	27-Jan-26	46.0d
17	GI-FS-HAM-1010	Found. Concrete Scope - LOE	153.0d	24-Nov-25 A	1-Jul-26	0.0d
18	GI-FS-HAM-1030	Deep UG Plumbing & Mech. Scope - LOE	185.0d	16-Dec-25 A	4-Sep-26	0.0d
19	GI-FS-HAM-1020	Deep UG Elec. & Comm. Scope - LOE	165.0d	16-Dec-25 A	7-Aug-26	112.0d
20	PR-P2-1B-3705	Delivery of Allowance Long Lead - Steel Mill Order - Part 2 Supp. A (LOE)	84.0d	2-Jan-26	26-Mar-26	0.0d
21	WBS - TAMPA AIRSIDE D TERMINAL		979.0d	9-Dec-24 A	15-Oct-28	364.0d
22	WBS - ASD - DESIGN & ENGINEERING PHASE		267.0d	9-Sep-25 A	25-Sep-26	885.0d
23	WBS - Airside E Optimization		46.0d	24-Dec-25 A	27-Feb-26	1,032.0d
24	WBS - ASE Optimization 90%		10.0d	24-Dec-25 A	8-Jan-26	1,043.0d
25	WBS - ASE Optimization 90% Submittal To HCAA		10.0d	24-Dec-25 A	8-Jan-26	1,043.0d
26	DS-AE-520	Review by HCAA - ASE Optimization 90% Subm.	10.0d	24-Dec-25 A	8-Jan-26	1,042.0d
27	WBS - ASE Optimization 100%		46.0d	24-Dec-25 A	27-Feb-26	1,032.0d
28	WBS - ASE Optimization 100% Documents		26.0d	24-Dec-25 A	30-Jan-26	1,032.0d
29	DS-AE-530	Design Docs. - ASE Optimization 100%	21.0d	24-Dec-25 A	23-Jan-26	1,031.0d
30	DS-AE-550	Incorporate Comments into Design - ASE Optimization 100%	5.0d	26-Jan-26	30-Jan-26	1,031.0d
31	WBS - ASE Optimization 100% QA/QC		8.0d	2-Feb-26	11-Feb-26	1,032.0d
32	DS-AE-560	Sr. Technical Review - ASE Optimization 100% QA/QC	3.0d	2-Feb-26	4-Feb-26	1,031.0d
33	DS-AE-570	DQC - ASE Optimization 100% QA/QC	3.0d	2-Feb-26	4-Feb-26	1,031.0d
34	DS-AE-580	Post Docs. - ASE Optimization 100% QA/QC	1.0d	5-Feb-26	5-Feb-26	1,031.0d
35	DS-AE-590	IDR - ASE Optimization 100% QA/QC	3.0d	6-Feb-26	10-Feb-26	1,031.0d
36	DS-AE-600	Visual Check - ASE Optimization 100% QA/QC	1.0d	11-Feb-26	11-Feb-26	1,031.0d
37	WBS - ASE Optimization 100% Submittal To HCAA		12.0d	12-Feb-26	27-Feb-26	1,032.0d
38	DS-AE-620	Complete Docs. & Assemble Pkg. - ASE Optimization 100% Subm.	1.0d	12-Feb-26	12-Feb-26	1,031.0d
39	DS-AE-630	Subm. Due to HCAA - ASE Optimization 100% Subm.	1.0d	13-Feb-26	13-Feb-26	1,031.0d
40	DS-AE-670	100% Review by HCAA - ASE Optimization 100% Subm.	10.0d	16-Feb-26	27-Feb-26	1,031.0d
41	WBS - A-Sortation & Airside C Screening Integration		105.0d	9-Sep-25 A	6-Feb-26	947.0d
42	DS-AA-640	HNTB - Design Deliverables 15%, 30%, 60%, 90% & 100%	105.0d	9-Sep-25 A	6-Feb-26	946.0d

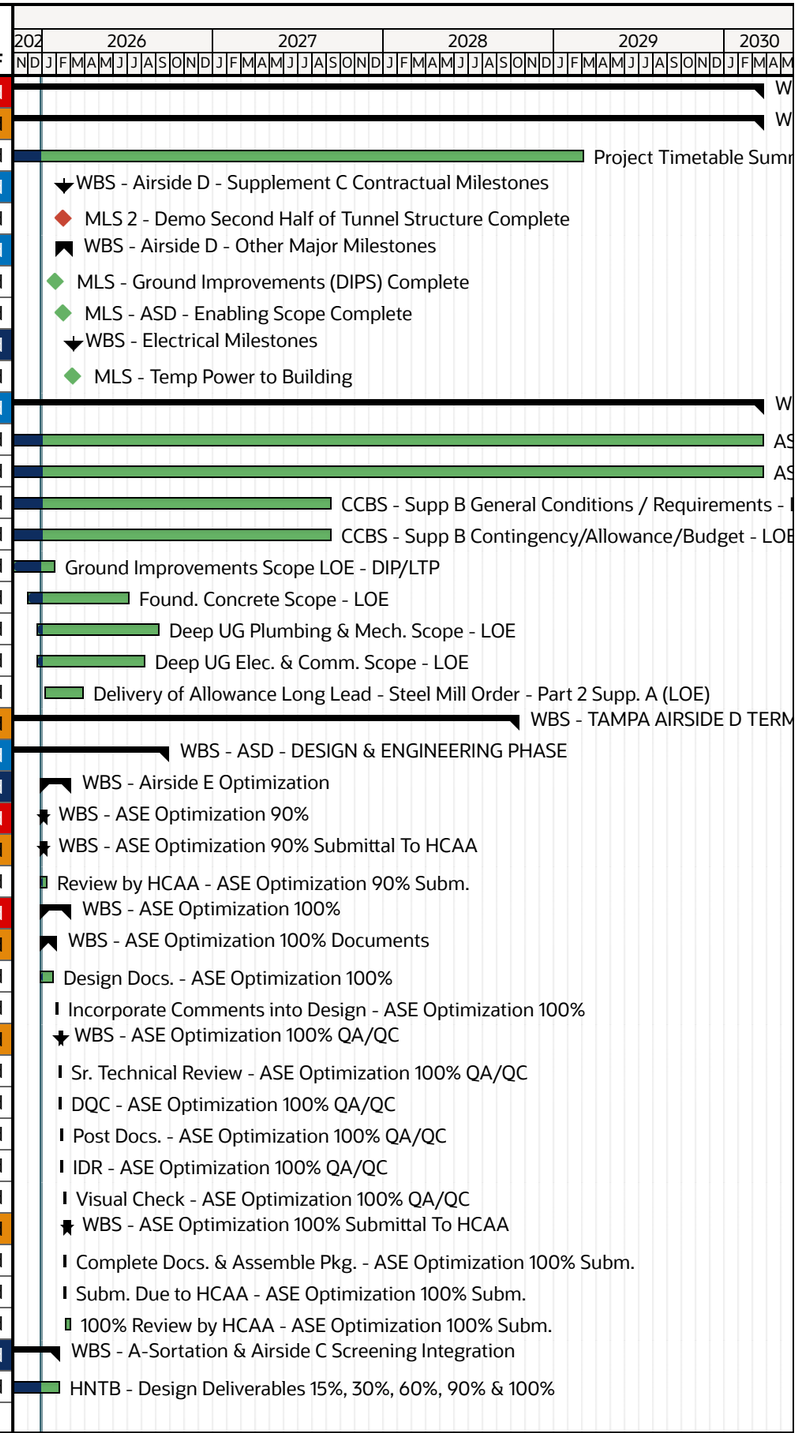

HENSEL PHELPS
Plan. Build. Manage.


Airside D - Tampa International Airport

ASD Development Program
90 Day Look Ahead Schedule
December 2025 - DD 12.26.25

Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:55 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
43	DS-AA-110	Owner Proposal Review - A-Sortation & Airside C Screening Integration	52.0d	14-Oct-25 A	29-Dec-25	974.0d
44	DS-AA-630	NTP - A-Sortation & Airside C Screening Integration (Second $150k)	1.0d	29-Dec-25	29-Dec-25	807.0d
45	WBS - ASD Bulletin - LED Digital Technology Updates		200.0d	15-Dec-25 A	25-Sep-26	309.0d
46	WBS - ASD - Bulletin - LED Digital Technology Updates - Design Development		200.0d	15-Dec-25 A	25-Sep-26	309.0d
47	ASD-Bull-DT-330	HCAA RFQ Award Content Designers - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	247.0d
48	ASD-Bull-DT-100	Develop Design Documents - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	309.0d
49	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades		131.0d	10-Nov-25 A	15-May-26	582.0d
50	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades Design Development		131.0d	10-Nov-25 A	15-May-26	582.0d
51	ASD-Bull-ET-50	HP/HNTB Prepare & Submit Proposal - ASD Bulletin - FIS Elevator Tower Finish ...	131.0d	10-Nov-25 A	15-May-26	582.0d
52	WBS - ASD - PRECONSTRUCTION PHASE		330.0d	9-Dec-24 A	26-Mar-26	558.0d
53	WBS - HCAA Board Approval Milestones		330.0d	9-Dec-24 A	26-Mar-26	558.0d
54	HA-BA-60	Part 2 Supplemental C Agreement - HCAA Board Approval (2.5.2026)	0.0d		5-Feb-26	5.0d
55	WBS - HCAA Board Award of Part 2 Supplement C Wave 1 - Core & Shell Package		57.0d	8-Dec-25 A	26-Feb-26	410.0d
56	HA-2C-W1-70	HCAA Review Supp. C for Board - Part 2 Supp. C - Core & Shell Pkg.	37.0d	15-Dec-25 A	5-Feb-26	0.0d
57	HA-2C-W1-80	Board Date (NTP) - Part 2 Supp. C - Core & Shell Pkg. (2.5.26)	0.0d		5-Feb-26	0.0d
58	HA-2C-W1-90	HCAA Contract Supp. C Execution - Part 2 Supp. C - Core & Shell Pkg.	15.0d	6-Feb-26	26-Feb-26	51.0d
59	WBS - Part 2 Supplement C Wave 1 Purchasing & Contracting		52.0d	8-Dec-25 A	19-Feb-26	415.0d
60	WBS - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		47.0d	8-Dec-25 A	12-Feb-26	95.0d
61	2C-W1-PC-830	Contract Negoation - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purcha...	15.0d	8-Dec-25 A	29-Dec-25	122.0d
62	2C-W1-PC-840	Contract Execution - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchas...	5.0d	6-Feb-26	12-Feb-26	95.0d
63	2C-W1-PC-850	Contract Execution Complete - Fire Protection Trade Partner - P2 Supp. C Wave...	0.0d		12-Feb-26	95.0d
64	WBS - Elevators/Escalators Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		44.0d	11-Dec-25 A	12-Feb-26	0.0d
65	2C-W1-PC-770	Contract Negoation - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purch...	12.0d	11-Dec-25 A	29-Dec-25	27.0d
66	2C-W1-PC-780	Contract Execution - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purcha...	5.0d	6-Feb-26	12-Feb-26	0.0d
67	2C-W1-PC-790	Contract Execution Complete - Elev./Escalators Trade Partner - P2 Supp. C Wav...	0.0d		12-Feb-26	0.0d
68	WBS - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		47.0d	8-Dec-25 A	12-Feb-26	386.0d
69	2C-W1-PC-2090	Contract Negoation - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchas...	15.0d	8-Dec-25 A	29-Dec-25	413.0d
70	2C-W1-PC-2100	Contract Execution - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	6-Feb-26	12-Feb-26	386.0d
71	2C-W1-PC-2110	Contract Execution Complete - Terrazzo Floor Trade Partner - P2 Supp. C Wave ...	0.0d		12-Feb-26	386.0d
72	WBS - Roofing Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		40.0d	17-Dec-25 A	12-Feb-26	91.0d
73	2C-W1-PC-100	Contract Negoation - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	11.0d	17-Dec-25 A	2-Jan-26	115.0d
74	2C-W1-PC-110	Contract Execution - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	91.0d
75	2C-W1-PC-120	Contract Execution Complete - Roofing Trade Partner - P2 Supp. C Wave 1 Purc...	0.0d		12-Feb-26	91.0d
76	WBS - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		46.0d	9-Dec-25 A	12-Feb-26	26.0d
77	2C-W1-PC-1250	Contract Negoation - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wav...	14.0d	9-Dec-25 A	29-Dec-25	53.0d
78	2C-W1-PC-1260	Contract Execution - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave...	5.0d	6-Feb-26	12-Feb-26	26.0d
79	2C-W1-PC-1270	Contract Execution Complete - Acoustical Panel Ceilings Trade Partner - P2 Sup...	0.0d		12-Feb-26	26.0d
80	WBS - Interior Wall Panels (Specialties/Decorative Glass) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contra...		46.0d	9-Dec-25 A	12-Feb-26	407.0d
81	2C-W1-PC-400	Contract Negoation - Interior Wall Panels (Specialties/Decorative Glass) Trade P...	14.0d	9-Dec-25 A	29-Dec-25	434.0d
82	2C-W1-PC-410	Contract Execution - Interior Wall Panels (Specialties/Decorative Glass) Trade P...	5.0d	6-Feb-26	12-Feb-26	407.0d
83	2C-W1-PC-420	Contract Execution Complete - Interior Wall Panels (Specialties/Decorative Glas...	0.0d		12-Feb-26	407.0d
84	WBS - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		46.0d	9-Dec-25 A	12-Feb-26	394.0d

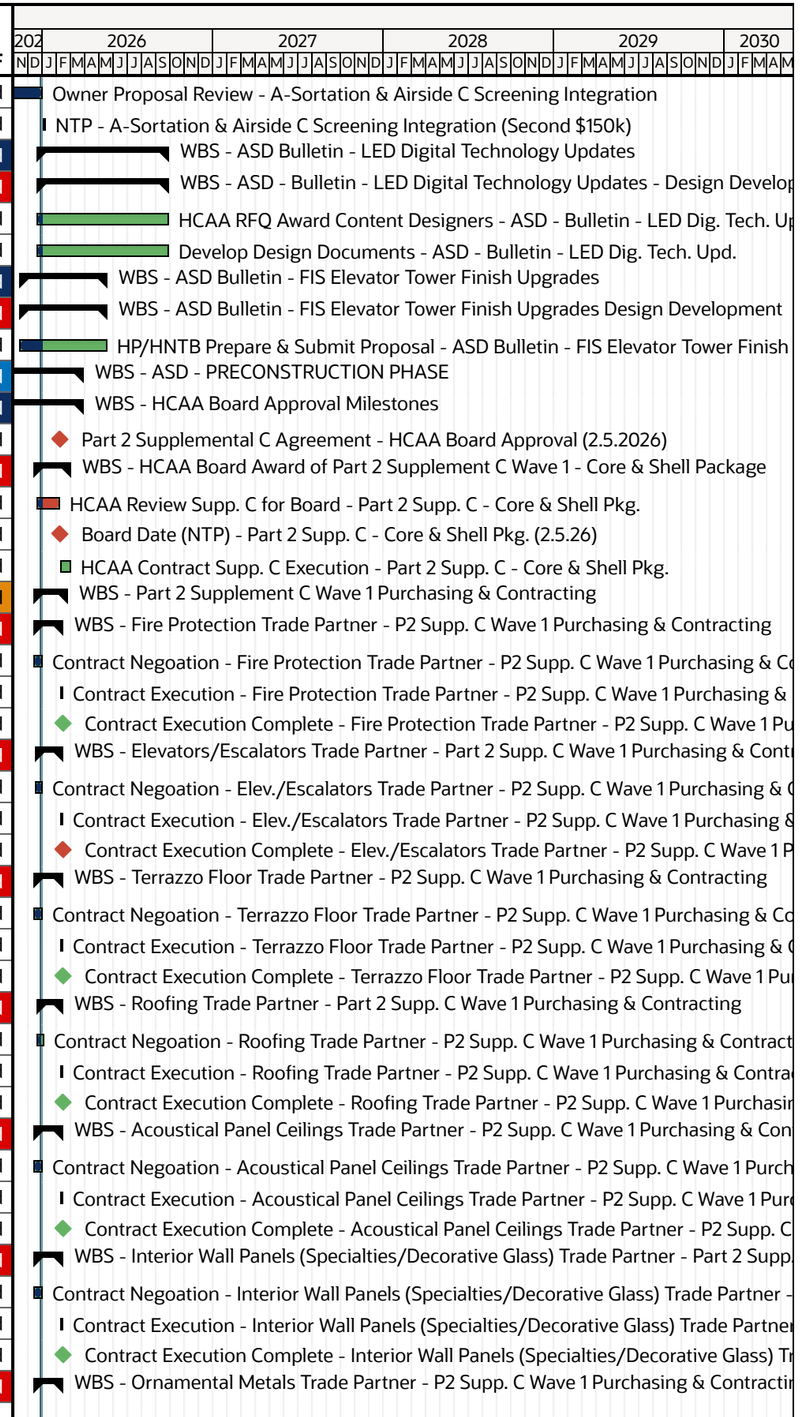

	ID	Name	Dur	Start	Finish	TF
85	2C-W1-PC-2150	Contract Negoation - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Pu...	14.0d	9-Dec-25 A	29-Dec-25	421.0d
86	2C-W1-PC-2160	Contract Execution - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Pur...	5.0d	6-Feb-26	12-Feb-26	394.0d
87	2C-W1-PC-2170	Contract Execution Complete - Ornamental Metals Trade Partner - P2 Supp. C ...	0.0d		12-Feb-26	394.0d
88	WBS - Glass Handrail Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		33.0d	29-Dec-25	12-Feb-26	420.0d
89	2C-W1-PC-460	Contract Development, Review, & Issuance - Glass Handrail Trade Partner - P2 ...	10.0d	29-Dec-25	12-Jan-26	428.0d
90	2C-W1-PC-470	Contract Negoation - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purcha...	10.0d	13-Jan-26	26-Jan-26	428.0d
91	2C-W1-PC-480	Contract Execution - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	6-Feb-26	12-Feb-26	420.0d
92	2C-W1-PC-490	Contract Execution Complete - Glass Handrail Trade Partner - P2 Supp. C Wave ...	0.0d		12-Feb-26	420.0d
93	WBS - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		47.0d	8-Dec-25 A	12-Feb-26	36.0d
94	2C-W1-PC-1180	Contract Development, Review, & Issuance - Masonry Trade Partner - P2 Supp. ...	15.0d	8-Dec-25 A	29-Dec-25	53.0d
95	2C-W1-PC-1190	Contract Negoation - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	53.0d
96	2C-W1-PC-1200	Contract Execution - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	36.0d
97	2C-W1-PC-1210	Contract Execution Complete - Masonry Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	36.0d
98	WBS - Demolition Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		38.0d	19-Dec-25 A	12-Feb-26	61.0d
99	2C-W1-PC-2450	Contract Negoation - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasing...	12.0d	19-Dec-25 A	7-Jan-26	82.0d
100	2C-W1-PC-2460	Contract Execution - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasing ...	5.0d	6-Feb-26	12-Feb-26	61.0d
101	2C-W1-PC-2470	Contract Execution Complete - Demolition Trade Partner - P2 Supp. C Wave 1 P...	0.0d		12-Feb-26	61.0d
102	WBS - Concrete SOG & SOMD Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		46.0d	9-Dec-25 A	12-Feb-26	101.0d
103	2C-W1-PC-30	Contract Development, Review, & Issuance - Concrete Trade Partner - P2 Supp. ...	14.0d	9-Dec-25 A	29-Dec-25	118.0d
104	2C-W1-PC-40	Contract Negoation - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	118.0d
105	2C-W1-PC-50	Contract Execution - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	101.0d
106	2C-W1-PC-60	Contract Execution Complete - Concrete Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	101.0d
107	WBS - Interior/Exterior Metal Wall Panels Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		38.0d	19-Dec-25 A	12-Feb-26	91.0d
108	2C-W1-PC-280	Contract Negoation - Interior/Exterior Metal Wall Panels Trade Partner - P2 Sup...	11.0d	19-Dec-25 A	6-Jan-26	113.0d
109	2C-W1-PC-290	Contract Execution - Interior/Exterior Metal Wall Panels Trade Partner - P2 Sup...	5.0d	6-Feb-26	12-Feb-26	91.0d
110	2C-W1-PC-300	Contract Execution Complete - Interior/Exterior Metal Wall Panels Trade Partne...	0.0d		12-Feb-26	91.0d
111	WBS - Spray Fireproofing & Insulation (K-13) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		39.0d	18-Dec-25 A	12-Feb-26	81.0d
112	2C-W1-PC-160	Contract Negoation - Spray Fireproofing & Insulation (K-13) Trade Partner - P2 ...	11.0d	18-Dec-25 A	5-Jan-26	104.0d
113	2C-W1-PC-170	Contract Execution - Spray Fireproofing & Insulation (K-13) Trade Partner - P2 ...	5.0d	6-Feb-26	12-Feb-26	81.0d
114	2C-W1-PC-180	Contract Execution Complete - Spray Fireproofing & Insulation (K-13) Trade Par...	0.0d		12-Feb-26	81.0d
115	WBS - Drywall & Related Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		39.0d	18-Dec-25 A	12-Feb-26	74.0d
116	2C-W1-PC-530	Contract Negoation - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Purc...	11.0d	18-Dec-25 A	5-Jan-26	97.0d
117	2C-W1-PC-540	Contract Execution - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Purc...	5.0d	6-Feb-26	12-Feb-26	74.0d
118	2C-W1-PC-550	Contract Execution Complete - Drywall & Related Trade Partner - P2 Supp. C W...	0.0d		12-Feb-26	74.0d
119	WBS - Glass & Glazing/Curtainwall Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		38.0d	19-Dec-25 A	12-Feb-26	81.0d
120	2C-W1-PC-340	Contract Negoation - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C W...	9.0d	19-Dec-25 A	2-Jan-26	105.0d
121	2C-W1-PC-350	Contract Execution - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C W...	5.0d	6-Feb-26	12-Feb-26	81.0d
122	2C-W1-PC-360	Contract Execution Complete - Glass & Glazing/Curtainwall Trade Partner - P2 ...	0.0d		12-Feb-26	81.0d
123	WBS - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		33.0d	29-Dec-25	12-Feb-26	81.0d
124	2C-W1-PC-1060	Contract Development, Review, & Issuance - Sitework Trade Partner - P2 Supp. ...	10.0d	29-Dec-25	12-Jan-26	89.0d
125	2C-W1-PC-1070	Contract Negoation - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	13-Jan-26	26-Jan-26	89.0d
126	2C-W1-PC-1080	Contract Execution - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	81.0d




	ID	Name	Dur	Start	Finish	TF
127	2C-W1-PC-1090	Contract Execution Complete - Sitework Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	81.0d
128	WBS - Waterproofing, Caulks, & Sealants Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		33.0d	29-Dec-25	12-Feb-26	101.0d
129	2C-W1-PC-210	Contract Development, Review, & Issuance - Waterproofing, Caulks, & Sealants ...	10.0d	29-Dec-25	12-Jan-26	109.0d
130	2C-W1-PC-220	Contract Negoation - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	10.0d	13-Jan-26	26-Jan-26	109.0d
131	2C-W1-PC-230	Contract Execution - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	5.0d	6-Feb-26	12-Feb-26	101.0d
132	2C-W1-PC-240	Contract Execution Complete - Waterproofing, Caulks, & Sealants Trade Partner...	0.0d		12-Feb-26	101.0d
133	WBS - Electrical & Site Electrical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		29.0d	5-Jan-26	12-Feb-26	91.0d
134	2C-W1-PC-860	Purchasing Meeting - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 Purc...	1.0d	5-Jan-26	5-Jan-26	9.0d
135	2C-W1-PC-870	Draft, Review, & Issue Change Order - Elec. & Site Elec. Trade Partner - P2 Supp...	10.0d	6-Jan-26	19-Jan-26	94.0d
136	2C-W1-PC-890	Change Order Negoation - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 ...	10.0d	20-Jan-26	2-Feb-26	94.0d
137	2C-W1-PC-900	Change Order Execution - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 ...	5.0d	6-Feb-26	12-Feb-26	91.0d
138	2C-W1-PC-910	Change Order Execution Complete - Elec. & Site Elec. Trade Partner - P2 Supp. ...	0.0d		12-Feb-26	91.0d
139	WBS - Baggage Handling Contractor - Part 2 Supp. C Wave 1 Purchasing & Contracting		28.0d	6-Jan-26	12-Feb-26	0.0d
140	2C-W1-PC-2480	Purchasing Meeting - Baggage Handling Contractor - P2 Supp. C Wave 1 Purch...	1.0d	6-Jan-26	6-Jan-26	9.0d
141	2C-W1-PC-2490	Draft, Review, & Issue Change Order - Baggage Handling Contractor - P2 Supp. ...	3.0d	7-Jan-26	9-Jan-26	9.0d
142	2C-W1-PC-2510	Change Order Negotiation - Baggage Handling Contractor - P2 Supp. C Wave 1 ...	10.0d	12-Jan-26	23-Jan-26	9.0d
143	2C-W1-PC-2520	Change Order Execution - Baggage Handling Contractor - P2 Supp. C Wave 1 P...	5.0d	6-Feb-26	12-Feb-26	0.0d
144	2C-W1-PC-2530	Change Order Execution Complete - Baggage Handling Contractor - P2 Supp. C...	0.0d		12-Feb-26	0.0d
145	WBS - Low Voltage System Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		27.0d	7-Jan-26	12-Feb-26	9.0d
146	2C-W1-PC-920	Purchasing Meeting - Low Voltage System Trade Partner - P2 Supp. C Wave 1 P...	1.0d	7-Jan-26	7-Jan-26	17.0d
147	2C-W1-PC-930	Draft, Review, & Issue Change Order - Low Voltage System Trade Partner - P2 S...	3.0d	8-Jan-26	12-Jan-26	17.0d
148	2C-W1-PC-950	Change Order Negoation - Low Voltage System Trade Partner - P2 Supp. C Wav...	10.0d	13-Jan-26	26-Jan-26	17.0d
149	2C-W1-PC-960	Change Order Execution - Low Voltage System Trade Partner - P2 Supp. C Wav...	5.0d	6-Feb-26	12-Feb-26	9.0d
150	2C-W1-PC-970	Change Order Execution Complete - Low Voltage System Trade Partner - P2 Su...	0.0d		12-Feb-26	9.0d
151	WBS - Plumbing/Mechanical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		29.0d	5-Jan-26	12-Feb-26	61.0d
152	2C-W1-PC-1520	Purchasing Meeting - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1 Purc...	1.0d	5-Jan-26	5-Jan-26	55.0d
153	2C-W1-PC-1530	Draft, Review, & Issue Change Order - Plumbing/Mech. Trade Partner - P2 Sup...	3.0d	6-Jan-26	8-Jan-26	71.0d
154	2C-W1-PC-1550	Change Order Negoation - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1...	10.0d	9-Jan-26	22-Jan-26	71.0d
155	2C-W1-PC-1560	Change Order Execution - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1 ...	5.0d	6-Feb-26	12-Feb-26	61.0d
156	2C-W1-PC-1570	Change Order Execution Complete - Plumbing/Mech. Trade Partner - P2 Supp. ...	0.0d		12-Feb-26	61.0d
157	WBS - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting-1		29.0d	8-Jan-26	17-Feb-26	359.0d
158	2C-W1-PC-2600	Purchasing Meeting - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchas...	1.0d	8-Jan-26	8-Jan-26	352.0d
159	2C-W1-PC-2610	Draft & Issue LOI - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing...	3.0d	9-Jan-26	13-Jan-26	359.0d
160	2C-W1-PC-2620	Contract Development, Review, & Issuance - Pipe Bursting Trade Partner - P2 S...	10.0d	14-Jan-26	27-Jan-26	359.0d
161	2C-W1-PC-2630	Contract Negoation - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasi...	10.0d	28-Jan-26	10-Feb-26	359.0d
162	2C-W1-PC-2640	Contract Execution - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	11-Feb-26	17-Feb-26	359.0d
163	2C-W1-PC-2650	Contract Execution Complete - Pipe Bursting Trade Partner - P2 Supp. C Wave ...	0.0d		17-Feb-26	359.0d
164	WBS - Structural Steel Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		33.0d	6-Jan-26	19-Feb-26	58.0d
165	2C-W1-PC-2660	Purchasing Meeting - Structural Steel Trade Partner - P2 Supp. C Wave 1 Purch...	1.0d	6-Jan-26	6-Jan-26	55.0d
166	2C-W1-PC-2670	Draft, Review, & Issue Change Order - Structural Steel Trade Partner - P2 Supp. ...	3.0d	7-Jan-26	9-Jan-26	62.0d
167	2C-W1-PC-2680	Change Order Negoation - Structural Steel Trade Partner - P2 Supp. C Wave 1 P...	10.0d	12-Jan-26	23-Jan-26	62.0d
168	2C-W1-PC-2690	Change Order Execution - Structural Steel Trade Partner - P2 Supp. C Wave 1 P...	5.0d	26-Jan-26	30-Jan-26	62.0d

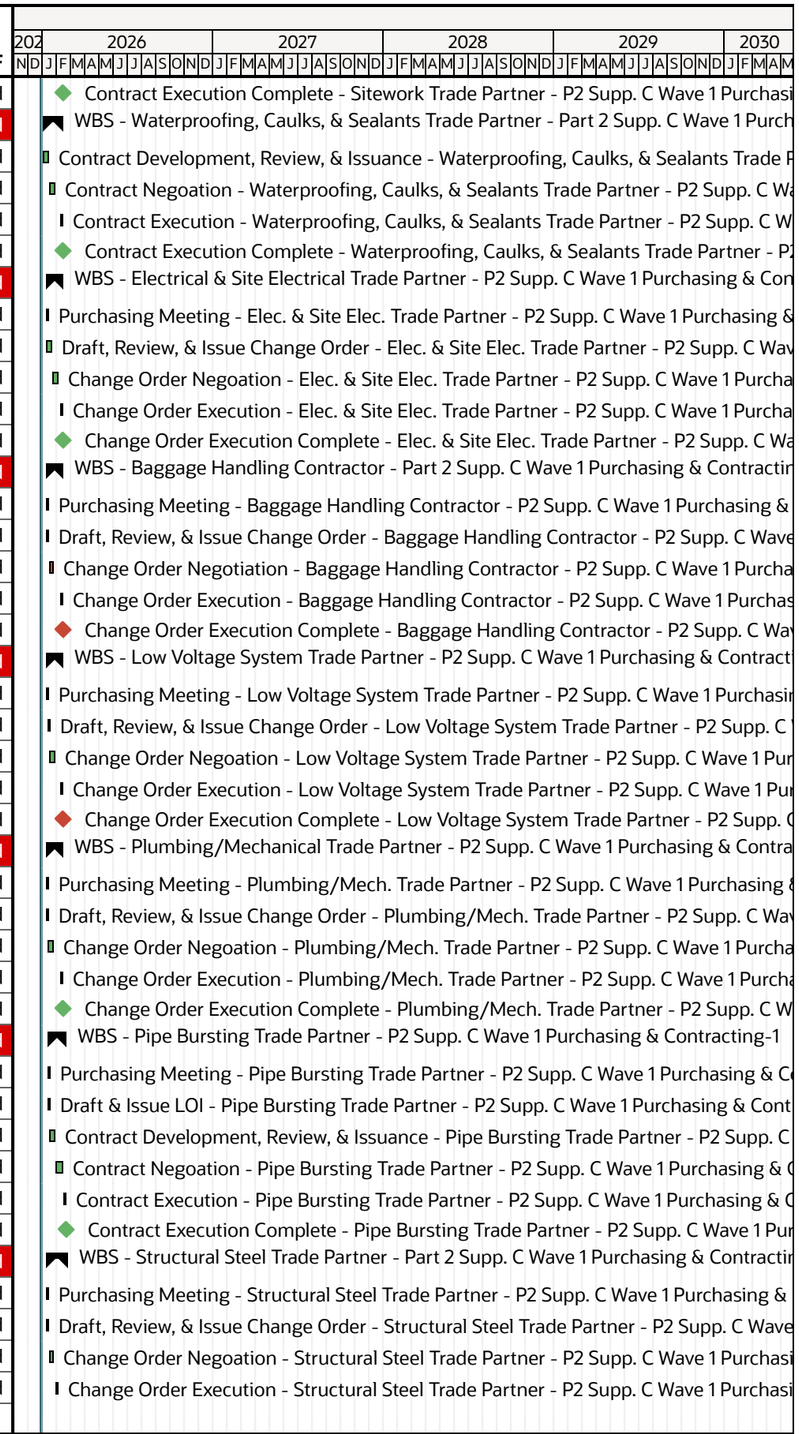


	ID	Name	Dur	Start	Finish	TF
169	A105770	Change Order Execution Complete - Structural Steel Trade Partner - P2 Supp. C...	10.0d	6-Feb-26	19-Feb-26	58.0d
170	WBS - Part 2 Supplement C Wave 2- Finishes Package		67.0d	22-Dec-25 A	26-Mar-26	558.0d
171	HA-2C-W2-90	Bid Packaging - Part 2 Supp. C Wave 2 - Finishes Pkg	9.0d	22-Dec-25 A	5-Jan-26	18.0d
172	HA-2C-W2-100	Bidding Period - Part 2 Supp. C Wave 2 - Finishes Pkg	22.0d	6-Jan-26	4-Feb-26	18.0d
173	HA-2C-W2-110	Bid Review/Bid Selection - Part 2 Supp. C Wave 2 - Finishes Pkg	12.0d	5-Feb-26	20-Feb-26	18.0d
174	WBS - Part 2 Supplement C Wave 2 Purchasing and Contracting		23.0d	24-Feb-26	26-Mar-26	558.0d
175	WBS - Doors, Frames, & Hardware - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	24-Feb-26	13-Mar-26	19.0d
176	2C-W2-PC-1270	Purchasing Meeting - Doors, Frames, & Hardware Trade Partner - P2 Supp. C W...	1.0d	24-Feb-26	24-Feb-26	14.0d
177	2C-W2-PC-1280	Draft & Issue LOI - Doors, Frames, & Hardware Trade Partner - P2 Supp. C Wave...	3.0d	25-Feb-26	27-Feb-26	19.0d
178	2C-W2-PC-1290	Contract Development, Review, & Issuance - Doors, Frames, & Hardware Trade ...	10.0d	2-Mar-26	13-Mar-26	19.0d
179	WBS - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	25-Feb-26	16-Mar-26	18.0d
180	2C-W2-PC-370	Purchasing Meeting - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing &...	1.0d	25-Feb-26	25-Feb-26	14.0d
181	2C-W2-PC-380	Draft & Issue LOI - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	3.0d	26-Feb-26	2-Mar-26	18.0d
182	2C-W2-PC-390	Contract Development, Review, & Issuance - Flooring Trade Partner - P2 Supp. ...	10.0d	3-Mar-26	16-Mar-26	18.0d
183	WBS - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	26-Feb-26	17-Mar-26	355.0d
184	2C-W2-PC-10	Purchasing Meeting - Architectural Millwork Trade Partner - P2 Supp. C Wave 2...	1.0d	26-Feb-26	26-Feb-26	19.0d
185	2C-W2-PC-20	Draft & Issue LOI - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 Pu...	3.0d	27-Feb-26	3-Mar-26	355.0d
186	2C-W2-PC-30	Contract Development, Review, & Issuance - Architectural Millwork Trade Partn...	10.0d	4-Mar-26	17-Mar-26	355.0d
187	WBS - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	27-Feb-26	18-Mar-26	155.0d
188	2C-W2-PC-250	Purchasing Meeting - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purc...	1.0d	27-Feb-26	27-Feb-26	19.0d
189	2C-W2-PC-260	Draft & Issue LOI - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purchasi...	3.0d	2-Mar-26	4-Mar-26	155.0d
190	2C-W2-PC-270	Contract Development, Review, & Issuance - Overhead Doors Trade Partner - P...	10.0d	5-Mar-26	18-Mar-26	155.0d
191	WBS - Airport Access Controls Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	3-Mar-26	20-Mar-26	479.0d
192	2C-W2-PC-70	Purchasing Meeting - Airport Access Controls Trade Partner - P2 Supp. C Wave ...	1.0d	3-Mar-26	3-Mar-26	19.0d
193	2C-W2-PC-80	Draft & Issue LOI - Airport Access Controls Trade Partner - P2 Supp. C Wave 2 P...	3.0d	4-Mar-26	6-Mar-26	479.0d
194	2C-W2-PC-90	Contract Development, Review, & Issuance - Airport Access Controls Trade Part...	10.0d	9-Mar-26	20-Mar-26	479.0d
195	WBS - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	4-Mar-26	23-Mar-26	380.0d
196	2C-W2-PC-310	Purchasing Meeting - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasi...	1.0d	4-Mar-26	4-Mar-26	19.0d
197	2C-W2-PC-320	Draft & Issue LOI - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasing ...	3.0d	5-Mar-26	9-Mar-26	380.0d
198	2C-W2-PC-330	Contract Development, Review, & Issuance - Tile & Stone Trade Partner - P2 Su...	10.0d	10-Mar-26	23-Mar-26	380.0d
199	WBS - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	5-Mar-26	24-Mar-26	398.0d
200	2C-W2-PC-610	Purchasing Meeting - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing &...	1.0d	5-Mar-26	5-Mar-26	19.0d
201	2C-W2-PC-620	Draft & Issue LOI - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	3.0d	6-Mar-26	10-Mar-26	398.0d
202	2C-W2-PC-630	Contract Development, Review, & Issuance - Signage Trade Partner - P2 Supp. ...	10.0d	11-Mar-26	24-Mar-26	398.0d
203	WBS - Toilet Partitions & Accessories Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		14.0d	6-Mar-26	25-Mar-26	367.0d
204	2C-W2-PC-670	Purchasing Meeting - Toilet Partitions & Accessories Trade Partner - P2 Supp. C...	1.0d	6-Mar-26	6-Mar-26	19.0d
205	2C-W2-PC-680	Draft & Issue LOI - Toilet Partitions & Accessories Trade Partner - P2 Supp. C W...	3.0d	9-Mar-26	11-Mar-26	367.0d
206	2C-W2-PC-690	Contract Development, Review, & Issuance - Toilet Partitions & Accessories Tra...	10.0d	12-Mar-26	25-Mar-26	367.0d
207	WBS - Building Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	10-Mar-26	13-Mar-26	567.0d
208	2C-W2-PC-730	Purchasing Meeting - Building Specialties Trade Partner - P2 Supp. C Wave 2 P...	1.0d	10-Mar-26	10-Mar-26	19.0d
209	2C-W2-PC-740	Draft & Issue LOI - Building Specialties Trade Partner - P2 Supp. C Wave 2 Purc...	3.0d	11-Mar-26	13-Mar-26	567.0d
210	WBS - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	11-Mar-26	16-Mar-26	22.0d




	ID	Name	Dur	Start	Finish	TF
211	2C-W2-PC-190	Purchasing Meeting - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave ...	1.0d	11-Mar-26	11-Mar-26	19.0d
212	2C-W2-PC-200	Draft & Issue LOI - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave 2 P...	3.0d	12-Mar-26	16-Mar-26	22.0d
213	WBS - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	12-Mar-26	17-Mar-26	456.0d
214	2C-W2-PC-490	Purchasing Meeting - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchas...	1.0d	12-Mar-26	12-Mar-26	144.0d
215	2C-W2-PC-500	Draft & Issue LOI - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasing...	3.0d	13-Mar-26	17-Mar-26	456.0d
216	WBS - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	13-Mar-26	18-Mar-26	443.0d
217	2C-W2-PC-1150	Purchasing Meeting - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	1.0d	13-Mar-26	13-Mar-26	144.0d
218	2C-W2-PC-1160	Draft & Issue LOI - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	3.0d	16-Mar-26	18-Mar-26	443.0d
219	WBS - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		5.0d	17-Mar-26	23-Mar-26	146.0d
220	2C-W2-PC-790	Purchasing Meeting - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 ...	1.0d	17-Mar-26	17-Mar-26	144.0d
221	2C-W2-PC-800	Draft & Issue LOI - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 Pur...	4.0d	18-Mar-26	23-Mar-26	146.0d
222	WBS - Window Coverings Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	18-Mar-26	23-Mar-26	497.0d
223	2C-W2-PC-1030	Purchasing Meeting - Window Coverings Trade Partner - P2 Supp. C Wave 2 Pu...	1.0d	18-Mar-26	18-Mar-26	359.0d
224	2C-W2-PC-1040	Draft & Issue LOI - Window Coverings Trade Partner - P2 Supp. C Wave 2 Purch...	3.0d	19-Mar-26	23-Mar-26	497.0d
225	WBS - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	19-Mar-26	24-Mar-26	361.0d
226	2C-W2-PC-850	Purchasing Meeting - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & C...	1.0d	19-Mar-26	19-Mar-26	359.0d
227	2C-W2-PC-860	Draft & Issue LOI - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Contr...	3.0d	20-Mar-26	24-Mar-26	361.0d
228	WBS - Interior Plants & Planters Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		4.0d	20-Mar-26	25-Mar-26	489.0d
229	2C-W2-PC-1090	Purchasing Meeting - Interior Plants & Planters Trade Partner - P2 Supp. C Wav...	1.0d	20-Mar-26	20-Mar-26	439.0d
230	2C-W2-PC-1100	Draft & Issue LOI - Interior Plants & Planters Trade Partner - P2 Supp. C Wave 2 ...	3.0d	23-Mar-26	25-Mar-26	489.0d
231	WBS - Bird Control Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		1.0d	24-Mar-26	24-Mar-26	440.0d
232	2C-W2-PC-1210	Purchasing Meeting - Bird Control Specialties Trade Partner - P2 Supp. C Wave ...	1.0d	24-Mar-26	24-Mar-26	439.0d
233	WBS - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		1.0d	25-Mar-26	25-Mar-26	440.0d
234	2C-W2-PC-550	Purchasing Meeting - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purch...	1.0d	25-Mar-26	25-Mar-26	439.0d
235	WBS - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		1.0d	26-Mar-26	26-Mar-26	467.0d
236	2C-W2-PC-910	Purchasing Meeting - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purch...	1.0d	26-Mar-26	26-Mar-26	466.0d
237	WBS - HCAA Alternative Procurement Preconstruction		329.0d	9-Dec-24 A	25-Mar-26	50.0d
238	WBS - Concessions Program Preconstruction (by Others)		279.0d	9-Dec-24 A	14-Jan-26	4.0d
239	HA-AL-CP-100	Concessions - Concessions Development	279.0d	9-Dec-24 A	14-Jan-26	4.0d
240	WBS - Artwork Preconstruction (Coordination with DB Team)		133.0d	16-Sep-25 A	25-Mar-26	50.0d
241	HA-AL-AW-20	Artwork - Issue Call for Artists (AS D Part 1 Awarded August 2023)	105.0d	16-Sep-25 A	13-Feb-26	50.0d
242	HA-AL-AW-30	Artwork - Artist Outreach Conference (SkyCenter One)	5.0d	16-Feb-26	20-Feb-26	50.0d
243	HA-AL-AW-40	Artwork - Deadline for Submissions	20.0d	23-Feb-26	20-Mar-26	50.0d
244	HA-AL-AW-50	Artwork -Technical Evaluation Committee	3.0d	23-Mar-26	25-Mar-26	50.0d
245	WBS - ASD - CITY OF TAMPA PERMITTING		81.0d	25-Nov-25 A	23-Mar-26	359.0d
246	WBS - ASD Building Permit		77.0d	25-Nov-25 A	17-Mar-26	44.0d
247	ASDEF-PER-ASD-640	COT Comment Response Subm. Review #1 - ASD Building Permit	29.0d	25-Nov-25 A	8-Jan-26	64.0d
248	ASDEF-PER-ASD-645	ASD COT Revision #1 Comments Received - ASD Building Permit	1.0d	9-Jan-26	9-Jan-26	64.0d
249	ASDEF-PER-ASD-646	Design Team Respond to Revision #1 Comments - ASD Building Permit	10.0d	12-Jan-26	23-Jan-26	64.0d
250	ASDEF-PER-ASD-647	Submit ASD Revision #2 to COT - ASD Building Permit	1.0d	26-Jan-26	26-Jan-26	64.0d
251	ASDEF-PER-ASD-648	ASD COT Review #2 - ASD Building Permit	15.0d	27-Jan-26	16-Feb-26	64.0d
252	ASDEF-PER-ASD-650	Anticipated ASD Permit Approval By COT - ASD Building Permit	1.0d	17-Mar-26	17-Mar-26	44.0d

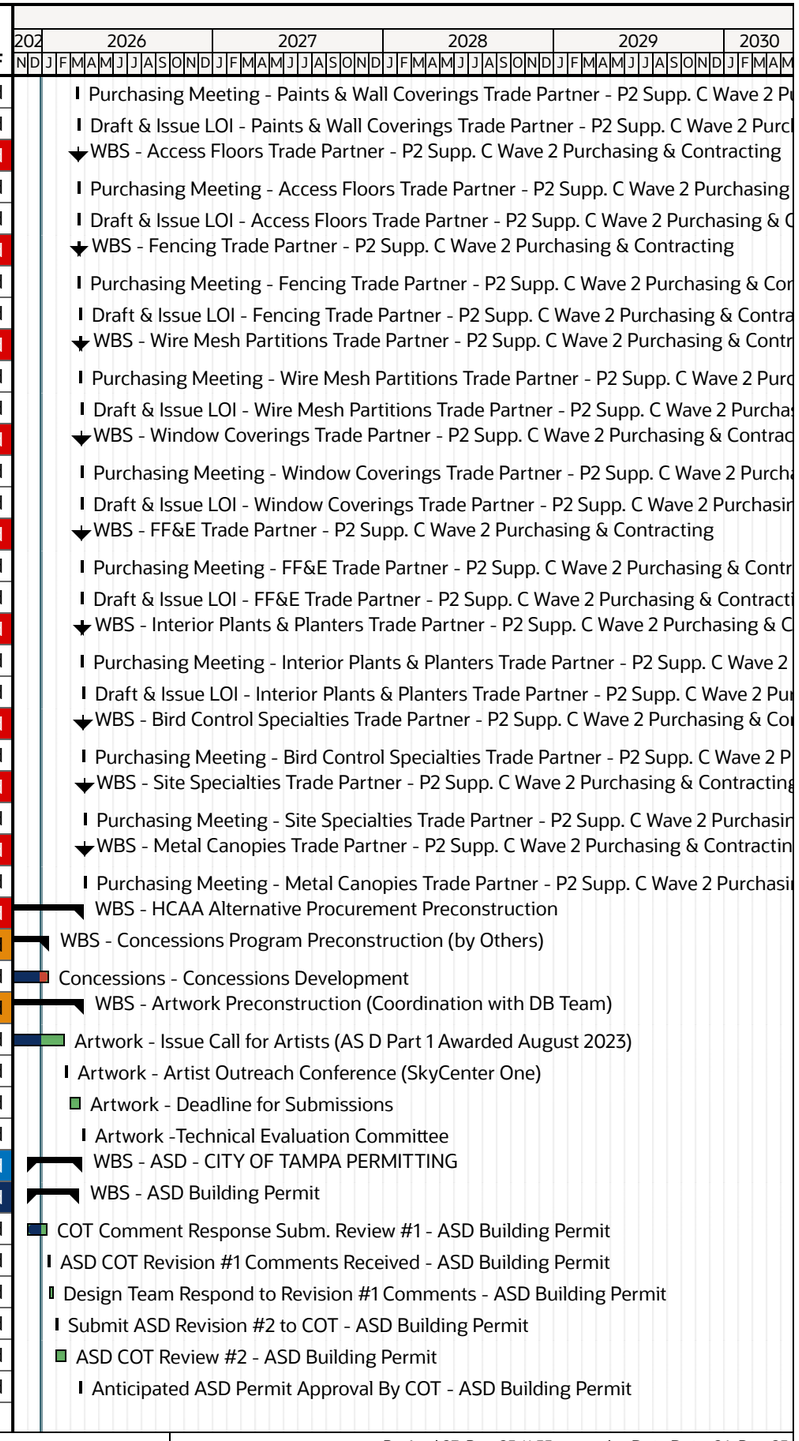


ID	Name	Dur	Start	Finish	TF
253	WBS - CCBS Permit Main Terminal Building	38.0d	19-Dec-25 A	12-Feb-26	66.0d
254	ASDEF-PER-MTB-770 — COT Revision #1 Review - Main Terminal Build. Permit / CCBS	15.0d	19-Dec-25 A	12-Jan-26	66.0d
255	ASDEF-PER-MTB-772 — MT BHS COT Revision #1 Comments Received - Main Terminal Build. Permit / ...	1.0d	13-Jan-26	13-Jan-26	66.0d
256	ASDEF-PER-MTB-773 — Design Team Respond to Revision #1 Comments - Main Terminal Build. Permit ...	10.0d	14-Jan-26	27-Jan-26	66.0d
257	ASDEF-PER-MTB-774 — Submit MT/BHS revision #2 to COT - Main Terminal Build. Permit / CCBS	1.0d	28-Jan-26	28-Jan-26	66.0d
258	ASDEF-PER-MTB-775 — Revision #2 COT Review - Main Terminal Build. Permit / CCBS	10.0d	29-Jan-26	11-Feb-26	66.0d
259	ASDEF-PER-MTB-780 — Anticipated MT/CCBS Permit Approval By COT - Main Terminal Build. Permit / ...	1.0d	12-Feb-26	12-Feb-26	66.0d
260	WBS - Main Terminal Shuttle TI Permit	68.0d	16-Dec-25 A	23-Mar-26	359.0d
261	ASDEF-PER-MTS-820 — COT Initial Subm. Review - Main Terminal Shuttle TI Permit	31.0d	16-Dec-25 A	29-Jan-26	359.0d
262	ASDEF-PER-MTS-830 — COT Initial Subm. Review Comments Received - Main Terminal Shuttle TI Permit	1.0d	30-Jan-26	30-Jan-26	359.0d
263	ASDEF-PER-MTS-840 — Design Team Respond to Initial Comments - Main Terminal Shuttle TI Permit	9.0d	2-Feb-26	12-Feb-26	359.0d
264	ASDEF-PER-MTS-850 — Submit MT Shuttle Comment Response to COT - Main Terminal Shuttle TI Permit	1.0d	13-Feb-26	13-Feb-26	359.0d
265	ASDEF-PER-MTS-860 — COT Revision #1 Review - Main Terminal Shuttle TI Permit	15.0d	16-Feb-26	6-Mar-26	359.0d
266	ASDEF-PER-MTS-865 — COT Revision #1 Review Comments - Main Terminal Shuttle TI Permit	1.0d	9-Mar-26	9-Mar-26	359.0d
267	ASDEF-PER-MTS-867 — Design Team Respond to Revision #1 Comments - Main Terminal Shuttle TI Per...	9.0d	10-Mar-26	20-Mar-26	359.0d
268	ASDEF-PER-MTS-868 — Submit MT Shuttle TI revision #2 to COT - Main Terminal Shuttle TI Permit	1.0d	23-Mar-26	23-Mar-26	359.0d
269	WBS - ASD - GOVERNMENTAL/MUNICIPAL/FAA/SWFWMD/FDEP PERMITTING	143.0d	29-Aug-25 A	24-Mar-26	747.0d
270	WBS - City of Tampa Utilities	143.0d	29-Aug-25 A	24-Mar-26	747.0d
271	WBS - City of Tampa Water Department	137.0d	29-Aug-25 A	16-Mar-26	44.0d
272	WBS - Part 1 Supplement C - Core & Shell Package	137.0d	29-Aug-25 A	16-Mar-26	44.0d
273	PM-P2-2B-40 — Water Commitment Letter - Part 2 Supp. C COT WD -Core, Shell & Finishes	137.0d	29-Aug-25 A	16-Mar-26	44.0d
274	WBS - City of Tampa Waste Water Department	61.0d	29-Dec-25	24-Mar-26	359.0d
275	WBS - Part 1 Supplement C- Core & Shell Package	61.0d	29-Dec-25	24-Mar-26	359.0d
276	PM-P2-2B-60 — Wastewater Commitment Letter - COT Core, Shell & Finishes	31.0d	29-Dec-25	10-Feb-26	359.0d
277	PM-P2-2B-90 — Wastewater Design Review Complete - COT Core, Shell & Finishes	30.0d	11-Feb-26	24-Mar-26	359.0d
278	WBS - City of Tampa Solid Waste	132.0d	29-Aug-25 A	9-Mar-26	758.0d
279	WBS - Part 2 Agreement - Enabling Package	132.0d	29-Aug-25 A	9-Mar-26	758.0d
280	WBS - Core & Shell	132.0d	29-Aug-25 A	9-Mar-26	758.0d
281	PM-P2-2B-130 — Core & Shell Solid Waste Design Review Complete - Part 2 Supp. C COT	132.0d	29-Aug-25 A	9-Mar-26	758.0d
282	WBS - FDEP	73.0d	21-Oct-25 A	4-Feb-26	723.0d
283	WBS - Part 1 Supplement C - Core & Shell Package	73.0d	21-Oct-25 A	4-Feb-26	723.0d
284	PM-FD-P2-2B-10 — Drawing Pkg. Approval - FDEP Part 2 Supp. C- Core, Shell & Finishes	73.0d	21-Oct-25 A	4-Feb-26	723.0d
285	WBS - City of Tampa Construction Services	121.0d	19-Sep-25 A	12-Mar-26	212.0d
286	WBS - Part 1 Supplement C - Core & Shell Package	121.0d	19-Sep-25 A	12-Mar-26	212.0d
287	PM-P2-2B-20 — Drawing Pkg. Approval - COT Const. Svs. -Part 1 Supp. C Core & Shell	76.0d	19-Sep-25 A	8-Jan-26	232.0d
288	WBS - Part 1 Supplement C - Core, Shell Package Trade Permits	45.0d	6-Feb-26	12-Mar-26	212.0d
289	PM-P2-2B-30 — Trade Permit Place Holder - Fire Protection & Security - Part 1 Supp. C Core & S...	25.0d	6-Feb-26	12-Mar-26	212.0d
290	WBS - ASD - PROCUREMENT PHASE	148.0d	20-Oct-25 A	19-May-26	975.0d
291	WBS - Contractor Furnished & Install (CFCI)	148.0d	20-Oct-25 A	19-May-26	975.0d
292	WBS - Part 2 Supplement A - DIP / LTP, Foundations Package & Long Lead	102.0d	30-Oct-25 A	26-Mar-26	349.0d
293	WBS - DIP / LTP Area 6-1 Shop Drawings	14.0d	17-Dec-25 A	7-Jan-26	53.0d
294	PR-P2-1A-1880 — HCAA Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DI...	14.0d	17-Dec-25 A	7-Jan-26	53.0d

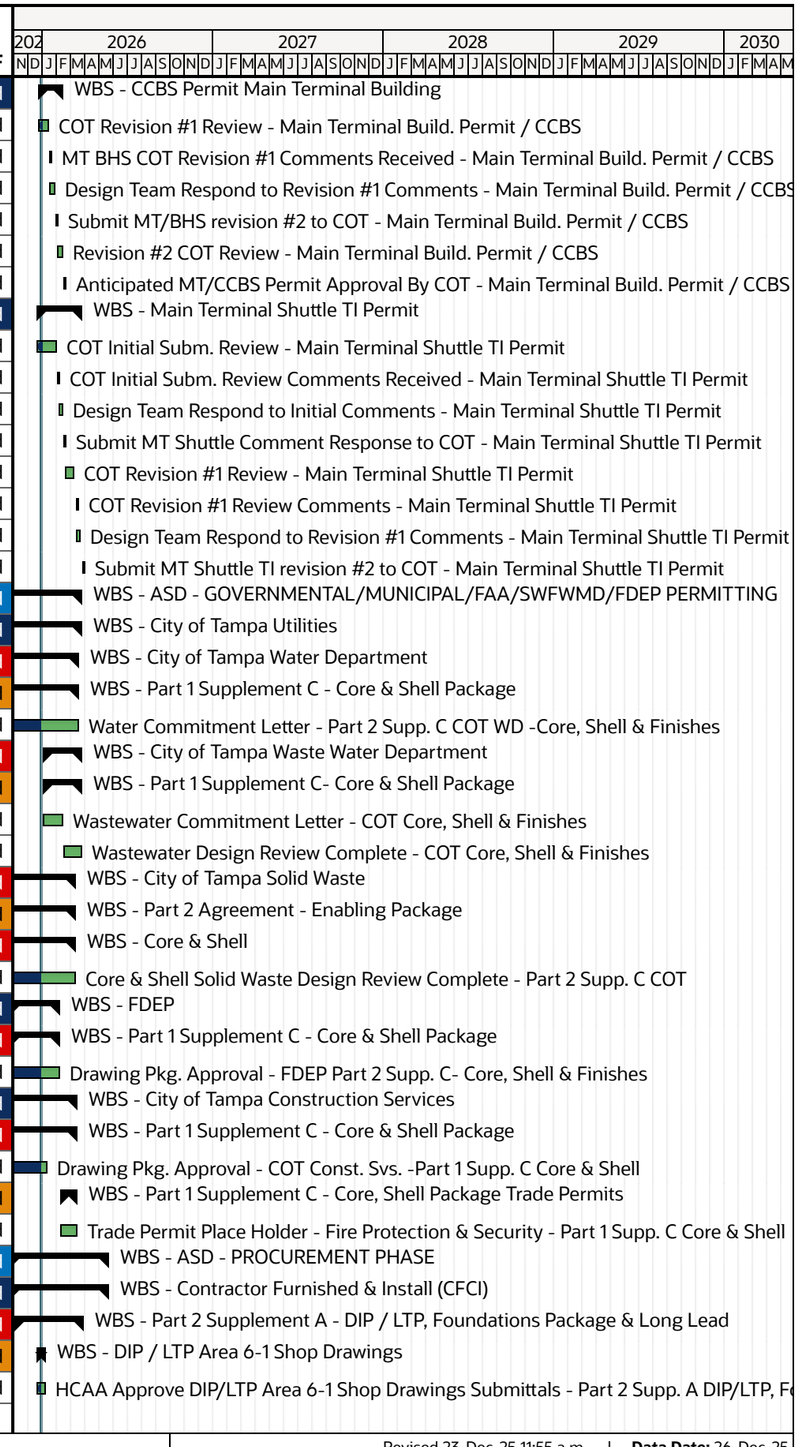


	ID	Name	Dur	Start	Finish	TF
295	WBS - Foundations Package		98.0d	30-Oct-25 A	20-Mar-26	353.0d
296	WBS - Rebar Foundations Area 2		29.0d	30-Nov-25 A	29-Dec-25	23.0d
297	PR-P2-1A-290	Fab. & Ship Rebar Found. Area 2 - Part 2 Supp. A	29.0d	30-Nov-25 A	29-Dec-25	23.0d
298	PR-P2-1A-430	Delivery of Rebar Found. Area 2 Complete - Part 2 Supp. A	0.0d		29-Dec-25	23.0d
299	WBS - Rebar Foundations Area 1		54.0d	23-Dec-25 A	10-Mar-26	0.0d
300	PR-P2-1A-1910	HNTB Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	11.0d	23-Dec-25 A	8-Jan-26	0.0d
301	PR-P2-1A-1710	HCAA Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	15.0d	9-Jan-26	29-Jan-26	0.0d
302	PR-P2-1A-1720	Fab. & Ship Rebar Found. Area 1 - Part 2 Supp. A	40.0d	30-Jan-26	10-Mar-26	0.0d
303	PR-P2-1A-1730	Delivery of Rebar Found. Area 1 Complete - Part 2 Supp. A	0.0d		10-Mar-26	0.0d
304	WBS - Rebar Foundations Area 3		55.0d	23-Dec-25 A	11-Mar-26	15.0d
305	PR-P2-1A-1930	HNTB Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	12.0d	23-Dec-25 A	9-Jan-26	15.0d
306	PR-P2-1A-1750	HCAA Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	15.0d	12-Jan-26	30-Jan-26	15.0d
307	PR-P2-1A-1760	Fab. & Ship Rebar Found. Area 3 - Part 2 Supp. A	40.0d	31-Jan-26	11-Mar-26	21.0d
308	PR-P2-1A-1770	Delivery of Rebar Found. Area 3 Complete - Part 2 Supp. A	0.0d		11-Mar-26	21.0d
309	WBS - Rebar Foundations Area 5		46.0d	23-Dec-25 A	26-Feb-26	49.0d
310	PR-P2-1A-1950	HNTB Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	49.0d
311	PR-P2-1A-1790	HCAA Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	15.0d	7-Jan-26	27-Jan-26	49.0d
312	PR-P2-1A-1800	Fab. & Ship Rebar Found. Area 5 - Part 2 Supp. A	30.0d	28-Jan-26	26-Feb-26	69.0d
313	PR-P2-1A-1810	Delivery of Rebar Found. Area 5 Complete - Part 2 Supp. A	0.0d		26-Feb-26	69.0d
314	WBS - Rebar Foundations Area 4		46.0d	23-Dec-25 A	26-Feb-26	69.0d
315	PR-P2-1A-1970	HNTB Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	69.0d
316	PR-P2-1A-1830	HCAA Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	15.0d	7-Jan-26	27-Jan-26	69.0d
317	PR-P2-1A-1840	Fab. & Ship Rebar Found. Area 4 - Part 2 Supp. A	30.0d	28-Jan-26	26-Feb-26	97.0d
318	PR-P2-1A-1850	Delivery of Rebar Found. Area 4 Complete - Part 2 Supp. A	0.0d		26-Feb-26	97.0d
319	WBS - Anchor Bolts		79.0d	26-Nov-25 A	20-Mar-26	353.0d
320	WBS - Anchor Bolts Pkg #3 Area 4		23.0d	23-Dec-25 A	26-Jan-26	92.0d
321	PR-P2-1A-1320	Procurement of Material - Area 4 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	92.0d
322	PR-P2-1A-1330	Steel on site - Abs - Start Shipping - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		26-Jan-26	92.0d
323	WBS - Anchor Bolts Pkg #3 Area 5		23.0d	23-Dec-25 A	26-Jan-26	72.0d
324	PR-P2-1A-1410	Procurement of Material - Area 5 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	72.0d
325	PR-P2-1A-1420	Steel on site - Abs - Start Shipping - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		26-Jan-26	72.0d
326	WBS - Anchor Bolts Pkg #4 Area 6-1 Cooling Tower		79.0d	26-Nov-25 A	20-Mar-26	353.0d
327	PR-P2-1A-1430	GMF Detailer Drawing Completion Window - Area 6-1 CT - Part 2 Supp. A - Anc...	38.0d	26-Nov-25 A	22-Jan-26	353.0d
328	PR-P2-1A-1440	GMF DM Drawing Review - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	2.0d	23-Jan-26	26-Jan-26	353.0d
329	PR-P2-1A-1450	HP & A/E Team Review of Detail Drawing - Area 6-1 CT - Part 2 Supp. A - Anch...	13.0d	27-Jan-26	12-Feb-26	353.0d
330	PR-P2-1A-1460	Return From Approval - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		12-Feb-26	353.0d
331	PR-P2-1A-1470	GMF Detailer Drawing Scrub & Clean up Window - Area 6-1 CT - Part 2 Supp. A ...	2.0d	13-Feb-26	16-Feb-26	353.0d
332	PR-P2-1A-1480	GMF DM RFF Review - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	1.0d	17-Feb-26	17-Feb-26	353.0d
333	PR-P2-1A-1490	Release for Fab. - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		17-Feb-26	353.0d
334	PR-P2-1A-1500	Procurement of Material - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	23.0d	18-Feb-26	20-Mar-26	353.0d
335	PR-P2-1A-1510	Steel on site - Abs - Start Shipping - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		20-Mar-26	353.0d
336	WBS - Embeds		94.0d	30-Oct-25 A	16-Mar-26	357.0d

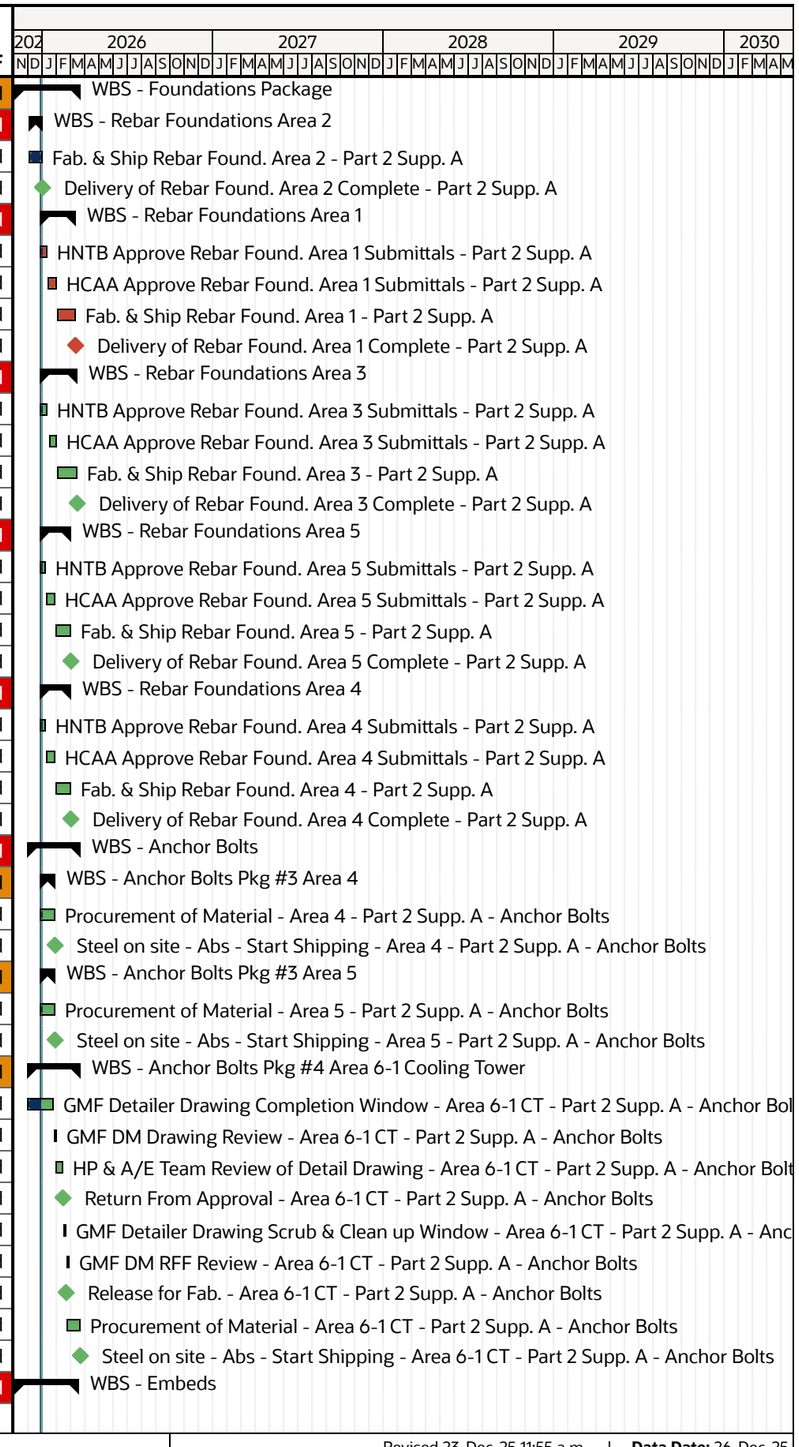

	ID	Name	Dur	Start	Finish	TF
337	WBS - Embeds - Pkg. #2 - Area 6.1 - Cooling Tower (If needed)		94.0d	30-Oct-25 A	16-Mar-26	357.0d
338	PR-P2-1A-1620	Embeds Pkg #2 - GMF Detailer Drawing Completion Window - Area 6.1 - Part 2...	39.0d	30-Oct-25 A	26-Dec-25 A	
339	PR-P2-1A-1625	Embeds Pkg #2 - GMF DM Drawing Review - Area 6.1 - Part 2 Supp. A	2.0d	29-Dec-25	30-Dec-25	357.0d
340	PR-P2-1A-1630	Embeds Pkg #2 - A/E Team Review of Detail Drawing - Area 6.1 - Part 2 Supp. A	15.0d	31-Dec-25	21-Jan-26	357.0d
341	PR-P2-1A-1640	Embeds Pkg #2 - Return From Approval - Area 6.1 - Part 2 Supp. A	0.0d		21-Jan-26	357.0d
342	PR-P2-1A-1650	Embeds Pkg #2 - GMF Detailer Drawing Scrub & Clean up Window - Area 6.1 - ...	2.0d	22-Jan-26	23-Jan-26	357.0d
343	PR-P2-1A-1660	Embeds Pkg #2 - GMF DM RFF Review - Area 6.1 - Part 2 Supp. A	1.0d	26-Jan-26	26-Jan-26	357.0d
344	PR-P2-1A-1670	Embeds Pkg #2 - Release for Fab. - Area 6.1 - Part 2 Supp. A	0.0d		26-Jan-26	357.0d
345	PR-P2-1A-1680	Embeds Pkg #2 - Fab. of Embeds - Area 6.1 - Part 2 Supp. A	35.0d	27-Jan-26	16-Mar-26	357.0d
346	PR-P2-1A-1690	Embeds Pkg #2 - Steel on Site - Start Shipping Embeds- Area 6.1 - Part 2 Supp. A	0.0d		16-Mar-26	357.0d
347	WBS - Underground Waterproofing		24.0d	5-Dec-25 A	29-Dec-25	14.0d
348	PR-P2-1A-310	Fab. & Ship Underground Waterproofing Products - Part 2 Supp. A	24.0d	5-Dec-25 A	29-Dec-25	14.0d
349	WBS - Transformer Procurement - ASD		70.0d	13-Nov-25 A	24-Feb-26	270.0d
350	PR-P1-1C1-70	Prep Transformer Submittals (Contractor) - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	270.0d
351	PR-P1-1C1-75	Review & Submit Transformer Submittals (HP) - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	270.0d
352	PR-P1-1C1-210	Review & Approve Transformer Submittals (HNTB) - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	270.0d
353	PR-P1-1C1-215	Review & Approve Transformer Submittals (HCAA) - ASD	15.0d	4-Feb-26	24-Feb-26	270.0d
354	WBS - Long Lead Electrical		70.0d	13-Nov-25 A	24-Feb-26	229.0d
355	WBS - Generator		70.0d	13-Nov-25 A	24-Feb-26	229.0d
356	PR-P2-1B-180	Prep & Submit Generator Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	229.0d
357	PR-P2-1B-7910	HP Approve Generator Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	229.0d
358	PR-P2-1B-7920	HNTB Approve Generator Submittals - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	229.0d
359	PR-P2-1B-200	HCAA Approve Generator Submittals - Part 2 Supp. A	15.0d	4-Feb-26	24-Feb-26	229.0d
360	WBS - Gear, Metering, SPD & Coordination Study		64.0d	13-Nov-25 A	16-Feb-26	166.0d
361	PR-P2-1B-120	Prep & Submit Gear Submittals - Part 2 Supp. A	34.0d	13-Nov-25 A	5-Jan-26	166.0d
362	PR-P2-1B-7930	HP Approve Gear Submittals - Part 2 Supp. A	5.0d	6-Jan-26	12-Jan-26	166.0d
363	PR-P2-1B-7940	HNTB Approve Gear Submittals - Part 2 Supp. A	10.0d	13-Jan-26	26-Jan-26	166.0d
364	PR-P2-1B-390	HCAA Approve Gear Submittals - Part 2 Supp. A	15.0d	27-Jan-26	16-Feb-26	166.0d
365	WBS - UPS Package		70.0d	13-Nov-25 A	24-Feb-26	170.0d
366	PR-P2-1B-3000	Prep & Submit UPS Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	170.0d
367	PR-P2-1B-7950	HP Approve UPS Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	170.0d
368	PR-P2-1B-7960	HNTB Approve UPS Submittals - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	170.0d
369	PR-P2-1B-3100	HCAA Approve UPS Submittals - Part 2 Supp. A	15.0d	4-Feb-26	24-Feb-26	170.0d
370	WBS - Long Lead Mechanical		60.0d	12-Nov-25 A	9-Feb-26	363.0d
371	WBS - Chillers Procurement		60.0d	12-Nov-25 A	9-Feb-26	363.0d
372	PR-P2-1B-100	Prep & Submit Chillers Submittals - Part 2 Supp. A	30.0d	12-Nov-25 A	26-Dec-25 A	
373	PR-P2-1B-7970	HP Approve Chillers Submittals - Part 2 Supp. A	5.0d	29-Dec-25	5-Jan-26	363.0d
374	PR-P2-1B-7980	HNTB Approve Chillers Submittals - Part 2 Supp. A	10.0d	6-Jan-26	19-Jan-26	363.0d
375	PR-P2-1B-280	HCAA Approve Chillers Submittals - Part 2 Supp. A	15.0d	20-Jan-26	9-Feb-26	363.0d
376	WBS - Long Lead Mill Order		80.0d	3-Dec-25 A	26-Mar-26	0.0d
377	PR-P2-1B-7990	Issue / Process PO to Mill - Part 2 Supp. A	20.0d	3-Dec-25 A	31-Dec-25	0.0d
378	PR-P2-1B-8000	Fab. & Ship Long Lead Mill Order - Part 2 Supp. A	84.0d	2-Jan-26	26-Mar-26	0.0d

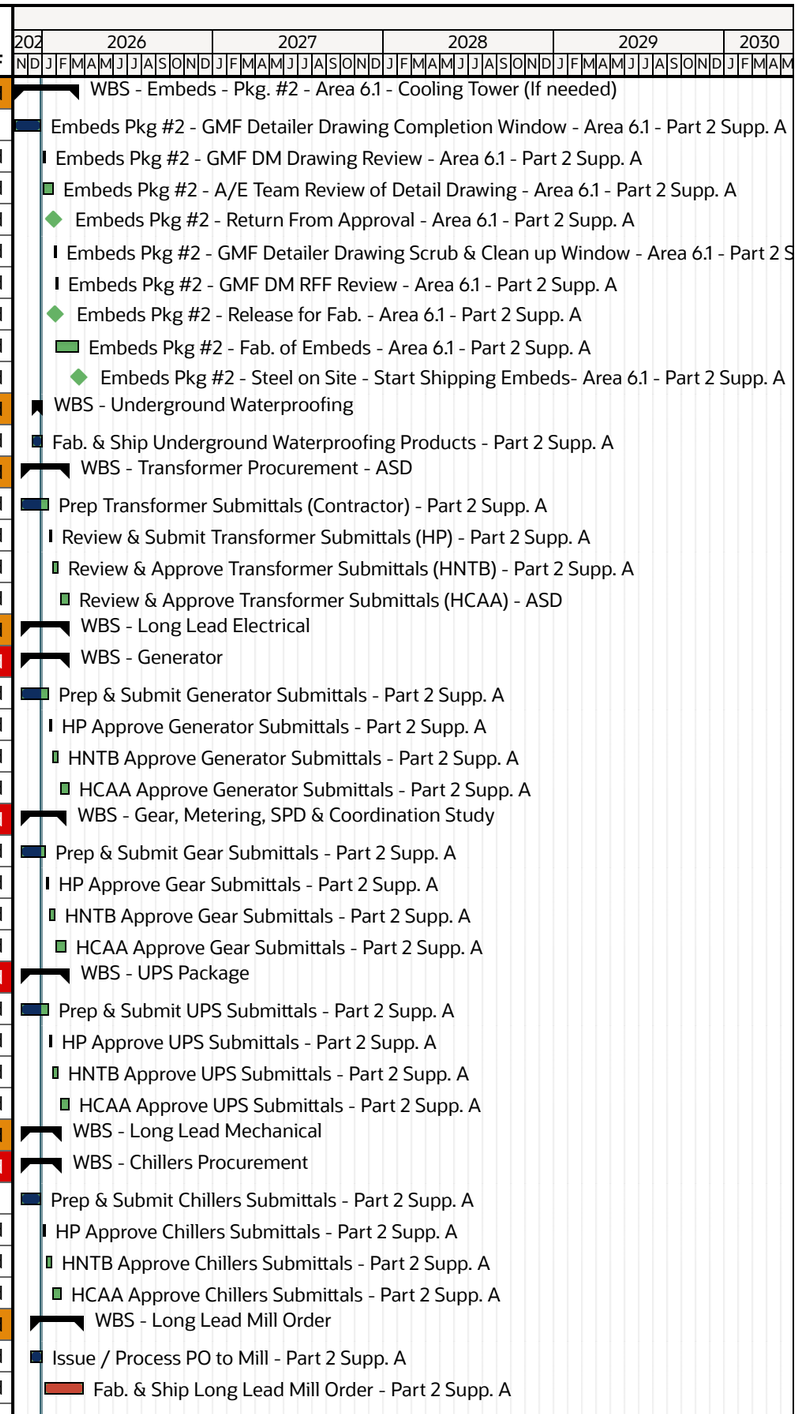

	ID	Name	Dur	Start	Finish	TF
379	PR-P2-1B-3700	Delivery of Steel Mill Order to GMF Shop - Part 2 Supp. A	0.0d		26-Mar-26	0.0d
380	WBS - Part 2 Supplement B - ASD Steel & Precast		139.0d	31-Oct-25 A	19-May-26	308.0d
381	WBS - Structural Steel / Misc. Metals Procurement		139.0d	31-Oct-25 A	19-May-26	308.0d
382	WBS - Structural Steel Seq 1		38.0d	19-Dec-25 A	12-Feb-26	23.0d
383	PR-P2-1B-7620	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	19-Dec-25 A	19-Jan-26	23.0d
384	PR-P2-1B-7630	Return From Approval Struct. Steel/Misc. Metals SEQ 1 - Part 2 Supp. B	0.0d		19-Jan-26	23.0d
385	PR-P2-1B-7640	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	20-Jan-26	2-Feb-26	23.0d
386	PR-P2-1B-7650	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	8.0d	3-Feb-26	12-Feb-26	23.0d
387	PR-P2-1B-7660	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	0.0d		12-Feb-26	23.0d
388	WBS - Structural Steel Seq 2		78.0d	31-Oct-25 A	23-Feb-26	5.0d
389	PR-P2-1B-3710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 2 - ...	38.0d	31-Oct-25 A	26-Dec-25 A	
390	PR-P2-1B-3720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 S...	5.0d	29-Dec-25	5-Jan-26	5.0d
391	PR-P2-1B-3725	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 2...	20.0d	6-Jan-26	2-Feb-26	5.0d
392	PR-P2-1B-3728	Return From Approval Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	0.0d		2-Feb-26	5.0d
393	PR-P2-1B-3730	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	3-Feb-26	16-Feb-26	5.0d
394	PR-P2-1B-3740	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	5.0d	17-Feb-26	23-Feb-26	5.0d
395	PR-P2-1B-3742	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0.0d		23-Feb-26	5.0d
396	WBS - Structural Steel Seq 3		88.0d	31-Oct-25 A	9-Mar-26	3.0d
397	PR-P2-1B-4810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 3 - ...	48.0d	31-Oct-25 A	12-Jan-26	3.0d
398	PR-P2-1B-4820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 S...	5.0d	13-Jan-26	19-Jan-26	3.0d
399	PR-P2-1B-4830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 3...	20.0d	20-Jan-26	16-Feb-26	3.0d
400	PR-P2-1B-4840	Return From Approval Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	0.0d		16-Feb-26	3.0d
401	PR-P2-1B-4850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	17-Feb-26	2-Mar-26	3.0d
402	PR-P2-1B-4870	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	5.0d	3-Mar-26	9-Mar-26	3.0d
403	PR-P2-1B-4872	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0.0d		9-Mar-26	3.0d
404	WBS - Structural Steel Seq 4		98.0d	31-Oct-25 A	23-Mar-26	3.0d
405	PR-P2-1B-3760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 4 - ...	58.0d	31-Oct-25 A	26-Jan-26	3.0d
406	PR-P2-1B-3770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 S...	5.0d	27-Jan-26	2-Feb-26	3.0d
407	PR-P2-1B-3780	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 4...	20.0d	3-Feb-26	2-Mar-26	3.0d
408	PR-P2-1B-3790	Return From Approval Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	0.0d		2-Mar-26	3.0d
409	PR-P2-1B-3800	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	3-Mar-26	16-Mar-26	3.0d
410	PR-P2-1B-3802	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	5.0d	17-Mar-26	23-Mar-26	3.0d
411	PR-P2-1B-3804	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0.0d		23-Mar-26	3.0d
412	WBS - Structural Steel Seq 5		98.0d	31-Oct-25 A	23-Mar-26	9.0d
413	PR-P2-1B-3810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 5 - ...	63.0d	31-Oct-25 A	2-Feb-26	9.0d
414	PR-P2-1B-3820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 S...	5.0d	3-Feb-26	9-Feb-26	9.0d
415	PR-P2-1B-3830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 5...	20.0d	10-Feb-26	9-Mar-26	9.0d
416	PR-P2-1B-3840	Return From Approval Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	0.0d		9-Mar-26	9.0d
417	PR-P2-1B-3850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	10-Mar-26	23-Mar-26	9.0d
418	WBS - Structural Steel Seq 6		98.0d	31-Oct-25 A	23-Mar-26	36.0d
419	PR-P2-1B-3860	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 6 - ...	73.0d	31-Oct-25 A	16-Feb-26	36.0d
420	PR-P2-1B-3870	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 6 - Part 2 S...	5.0d	17-Feb-26	23-Feb-26	36.0d

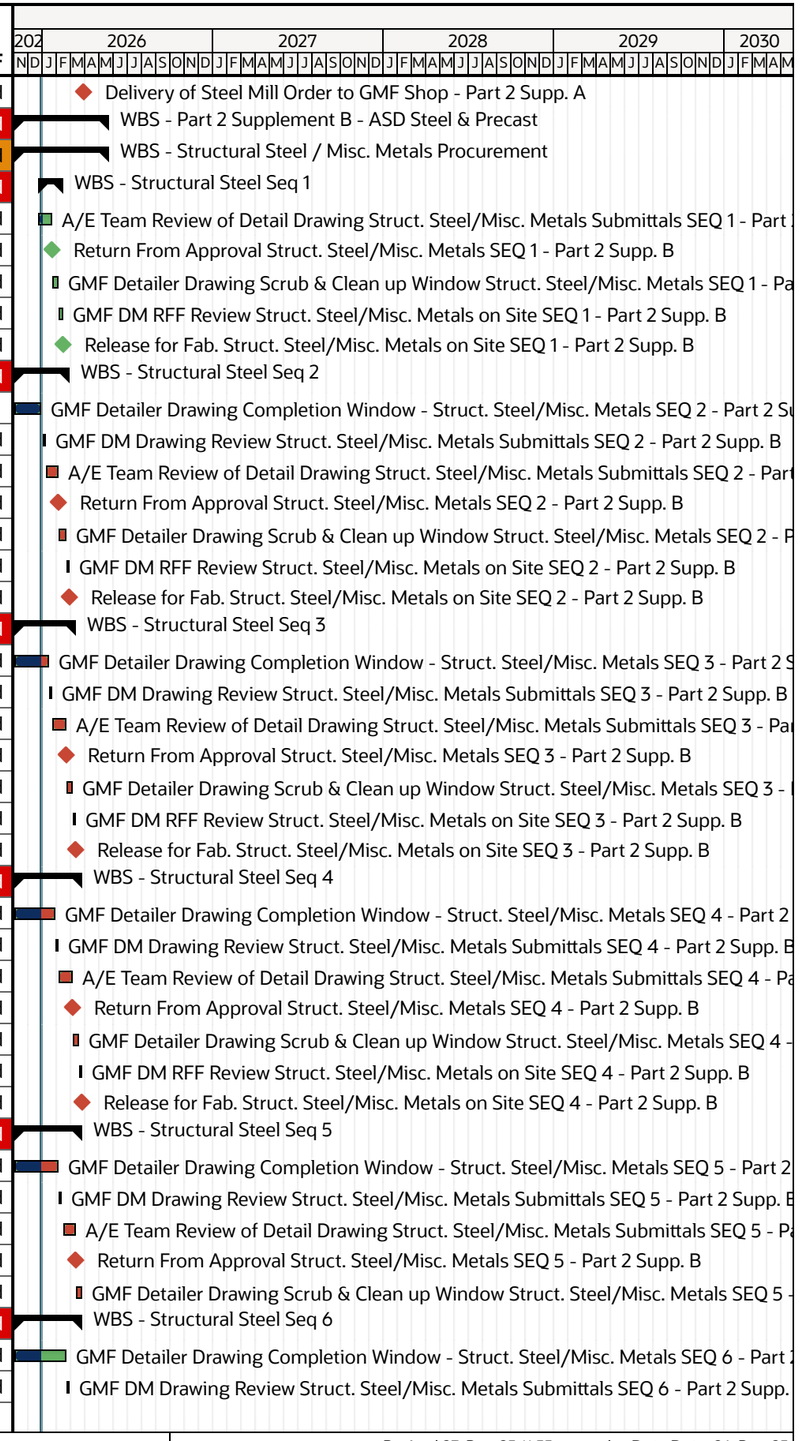

	ID	Name	Dur	Start	Finish	TF
421	PR-P2-1B-3880	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 6...	20.0d	24-Feb-26	23-Mar-26	36.0d
422	PR-P2-1B-3890	Return From Approval Struct. Steel/Misc. Metals SEQ 6 - Part 2 Supp. B	0.0d		23-Mar-26	36.0d
423	WBS - Structural Steel Seq 7		93.0d	31-Oct-25 A	16-Mar-26	29.0d
424	PR-P2-1B-3910	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 7 - ...	68.0d	31-Oct-25 A	9-Feb-26	29.0d
425	PR-P2-1B-3920	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 7 - Part 2 S...	5.0d	10-Feb-26	16-Feb-26	29.0d
426	PR-P2-1B-3930	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 7...	20.0d	17-Feb-26	16-Mar-26	29.0d
427	PR-P2-1B-3940	Return From Approval Struct. Steel/Misc. Metals SEQ 7 - Part 2 Supp. B	0.0d		16-Mar-26	29.0d
428	WBS - Structural Steel Seq 8		83.0d	31-Oct-25 A	2-Mar-26	45.0d
429	PR-P2-1B-3960	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 8 - ...	78.0d	31-Oct-25 A	23-Feb-26	45.0d
430	PR-P2-1B-3970	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 8 - Part 2 S...	5.0d	24-Feb-26	2-Mar-26	45.0d
431	WBS - Structural Steel Seq 9		93.0d	31-Oct-25 A	16-Mar-26	43.0d
432	PR-P2-1B-4710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 9 - ...	88.0d	31-Oct-25 A	9-Mar-26	43.0d
433	PR-P2-1B-4720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 9 - Part 2 S...	5.0d	10-Mar-26	16-Mar-26	43.0d
434	WBS - Structural Steel Seq 10		98.0d	31-Oct-25 A	23-Mar-26	30.0d
435	PR-P2-1B-4760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 10 ...	93.0d	31-Oct-25 A	16-Mar-26	30.0d
436	PR-P2-1B-4770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 10 -Part 2 ...	5.0d	17-Mar-26	23-Mar-26	30.0d
437	WBS - Structural Steel Seq 11		98.0d	31-Oct-25 A	23-Mar-26	48.0d
438	PR-P2-1B-4010	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 11 ...	98.0d	31-Oct-25 A	23-Mar-26	48.0d
439	WBS - Structural Steel Seq 12		103.0d	31-Oct-25 A	30-Mar-26	35.0d
440	PR-P2-1B-6970	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 12 ...	103.0d	31-Oct-25 A	30-Mar-26	35.0d
441	WBS - Structural Steel Seq 13		108.0d	31-Oct-25 A	6-Apr-26	45.0d
442	PR-P2-1B-7060	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 13 ...	108.0d	31-Oct-25 A	6-Apr-26	45.0d
443	WBS - Structural Steel Seq 14		113.0d	31-Oct-25 A	13-Apr-26	43.0d
444	PR-P2-1B-7150	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 14 ...	113.0d	31-Oct-25 A	13-Apr-26	43.0d
445	WBS - Structural Steel Seq 15		119.0d	31-Oct-25 A	21-Apr-26	42.0d
446	PR-P2-1B-7240	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 15 ...	119.0d	31-Oct-25 A	21-Apr-26	42.0d
447	WBS - Structural Steel Seq 16		124.0d	31-Oct-25 A	28-Apr-26	49.0d
448	PR-P2-1B-7330	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 16 ...	124.0d	31-Oct-25 A	28-Apr-26	49.0d
449	WBS - Structural Steel Seq 17		129.0d	31-Oct-25 A	5-May-26	48.0d
450	PR-P2-1B-7420	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 17 ...	129.0d	31-Oct-25 A	5-May-26	48.0d
451	WBS - Structural Steel Seq 18		134.0d	31-Oct-25 A	12-May-26	49.0d
452	PR-P2-1B-7510	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 18 ...	134.0d	31-Oct-25 A	12-May-26	49.0d
453	WBS - Structural Steel Seq 19		139.0d	31-Oct-25 A	19-May-26	57.0d
454	PR-P2-1B-7690	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 19 ...	139.0d	31-Oct-25 A	19-May-26	57.0d
455	WBS - Structural Steel Seq 20 (Cooling Tower)		124.0d	31-Oct-25 A	28-Apr-26	323.0d
456	PR-P2-1B-7820	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals (Cooling...	124.0d	31-Oct-25 A	28-Apr-26	323.0d
457	WBS - Precast Procurement		67.0d	17-Dec-25 A	23-Mar-26	174.0d
458	WBS - Exterior Arch Precast Panels		60.0d	29-Dec-25	23-Mar-26	174.0d
459	PR-P2-1B-6740	Prep & Submit Exterior Arch Precast Panel Submittals - Part 2 Supp. B	30.0d	29-Dec-25	9-Feb-26	174.0d
460	PR-P2-1B-6750	HP Review & Submit Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	10-Feb-26	23-Feb-26	174.0d
461	PR-P2-1B-7790	HNTB Review & Approve Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	24-Feb-26	9-Mar-26	174.0d
462	PR-P2-1B-6760	HCAA Review & Approve Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	10-Mar-26	23-Mar-26	174.0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
90 Day Look Ahead Schedule
December 2025 - DD 12.26.25

Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:55 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
463	WBS - Elevator Cores		66.0d	17-Dec-25 A	20-Mar-26	21.0d
464	PR-P2-1B-7780	HNTB Review & Approve Elevator Cores Submittals - Part 2 Supp. B	11.0d	17-Dec-25 A	2-Jan-26	21.0d
465	PR-P2-1B-6720	HCAA Review & Approve Elevator Cores - Part 2 Supp. B	15.0d	5-Jan-26	23-Jan-26	21.0d
466	PR-P2-1B-6730	Fab. & Ship Elevator Cores - Part 2 Supp. B	56.0d	24-Jan-26	20-Mar-26	31.0d
467	PR-P2-1B-6780	Delivery of Elevator Cores on Site- Part 2 Supp. B	0.0d		20-Mar-26	31.0d
468	WBS - Part 1 Supplement C Wave 1 - Core & Shell Procurement		132.0d	20-Oct-25 A	27-Apr-26	991.0d
469	WBS - Concrete Procurement SOG & SOMD - ASD		30.0d	13-Feb-26	26-Mar-26	101.0d
470	PR-P1-1C1-450	Prep Concrete Submittal (Contractor)- SOG & SOMD - ASD	20.0d	13-Feb-26	12-Mar-26	101.0d
471	PR-P1-1C1-455	Review & Submit Concrete Submittal (HP) - SOG & SOMD - ASD	10.0d	13-Mar-26	26-Mar-26	101.0d
472	WBS - Masonry Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	36.0d
473	PR-P2-1C1-6850	Prep Masonry Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	36.0d
474	WBS - Column Covers Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	394.0d
475	PR-P2-1C1-700	Prep Column Covers Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	394.0d
476	WBS - Interior Metal Specialties Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	537.0d
477	PR-P2-1C1-6910	Prep Interior Metal Specialties Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	537.0d
478	WBS - Wall & Door Protection Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	567.0d
479	PR-P2-1C1-7850	Prep Wall & Door Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	567.0d
480	WBS - Waterproofing, Caulks & Sealants Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	101.0d
481	PR-P1-1C1-600	Prep Water Proofing, Caulks & Sealants Submittals (Contractor) - ASD	20.0d	13-Feb-26	12-Mar-26	101.0d
482	PR-P1-1C1-605	Review & Submit Water Proofing, Caulks & Sealants Submittals (HP)- ASD	10.0d	13-Mar-26	26-Mar-26	101.0d
483	WBS - Interior/Exterior Metal Wall Panels Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
484	PR-P1-1C1-610	Interior/Exterior Metal Wall Panels Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
485	WBS - Roofing Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
486	PR-P1-1C1-580	Prep Roofing Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
487	WBS - Fall Protection (Roofing Contractor) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	133.0d
488	PR-P2-1C1-7480	Prep Fall Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
489	WBS - Spray Fireproofing & Insulation (K-13) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	81.0d
490	PR-P1-1C1-590	Prep Spray Fireproofing & Insulation Submittals (Contractor) - ASD	20.0d	13-Feb-26	12-Mar-26	81.0d
491	PR-P1-1C1-595	Review & Submit Spray Fireproofing & Insulation Submittals (HP)- ASD	10.0d	13-Mar-26	26-Mar-26	81.0d
492	WBS - Louvers Procurement (Mechanical) - ASD		30.0d	13-Feb-26	26-Mar-26	273.0d
493	PR-P2-1C1-940	Prep Louvers Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	273.0d
494	WBS - Automatic/Glass Door, Frames, & Hardware Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	175.0d
495	PR-P2-1C1-660	Prep Automatic/Glass Door & Hardware Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	175.0d
496	WBS - Drywall & Related Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	74.0d
497	PR-P1-1C1-670	Prep Drywall & Related Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	74.0d
498	WBS - Acoustical Metal Panel Ceilings Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	430.0d
499	PR-P2-1C1-720	Prep Acoustical Metal Panel Ceilings Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	430.0d
500	WBS - Acoustical Panel Ceilings Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	244.0d
501	PR-P2-1C1-7970	Prep Acoustical Panel Ceilings Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	244.0d
502	WBS - Suspended Wood Ceiling Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	435.0d
503	PR-P2-1C1-7910	Prep Suspended Wood Ceiling Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	435.0d
504	WBS - Escalators - ES-01 & ES-03 Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	133.0d




	ID	Name	Dur	Start	Finish	TF
505	PR-P1-1C1-790	Prep Escalators 1 & 3 Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
506	WBS - Escalators - ES-02 & ES-04 Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	133.0d
507	PR-P1-1C1-800	Prep Escalators 2 & 4 Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
508	WBS - Fire Suppression Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	95.0d
509	PR-P1-1C1-820	Prep Fire Suppression Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	95.0d
510	WBS - Landscaping & Irrigation (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	386.0d
511	PR-P1-1C1-850	Prep Landscaping & Irrigation Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
512	WBS - Roadway Work (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	415.0d
513	PR-P1-1C1-10	Prep Roadway Work (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	415.0d
514	WBS - UG Sanitary (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	96.0d
515	PR-P1-1C1-3070	Prep UG Sanitary (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	96.0d
516	WBS - Concrete Mix Design Curbs & Sidewalks (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	510.0d
517	PR-P1-1C1-3130	Prep Concrete Mix Design (Curbs & Sidewalks Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	510.0d
518	WBS - UG Fire Suppression (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	166.0d
519	PR-P1-1C1-3190	Prep UG Fire Suppression (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	166.0d
520	WBS - Grease Traps (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	307.0d
521	PR-P1-1C1-3250	Prep Grease Traps (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	307.0d
522	WBS - Oil/Water Separator (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	307.0d
523	PR-P1-1C1-3310	Prep Oil/Water Separator (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	307.0d
524	WBS - Concrete Mix Design Paving (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	432.0d
525	PR-P1-1C1-3370	Prep Concrete Mix Design (Paving Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	432.0d
526	WBS - Asphalt Paving (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	606.0d
527	PR-P1-1C1-3430	Prep Asphalt Paving (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	606.0d
528	WBS - Pavement Striping (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	611.0d
529	PR-P1-1C1-3490	Prep Pavement Striping (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	611.0d
530	WBS - Potable Water Systems (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	166.0d
531	PR-P1-1C1-3550	Prep Potable Water Systems (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	166.0d
532	WBS - Storm Structures (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	81.0d
533	PR-P1-1C1-3010	Prep Storm Structures (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	81.0d
534	WBS - Exterior Metal Framing - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
535	PR-P2-1C1-880	Prep Exterior Metal Framing Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
536	WBS - Structural Steel Dumpster Procurement - ASD		25.0d	13-Feb-26	19-Mar-26	174.0d
537	PR-P2-1C1-870	Prep Struct. Steel Dumpster Submittals (Contractor) - ASD	15.0d	13-Feb-26	5-Mar-26	174.0d
538	PR-P2-1C1-875	Review & Submit Struct. Steel Dumpster Submittals (HP) - ASD	10.0d	6-Mar-26	19-Mar-26	174.0d
539	WBS - Boilers Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	424.0d
540	PR-P2-1C1-90	Prep Boilers Submittals (Contractor) - Part 2 Supp. ASD	30.0d	13-Feb-26	26-Mar-26	424.0d
541	WBS - HVAC System Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	198.0d
542	PR-P1-1C1-3670	Prep HVAC System Submittals (Contractor) - Part 2 Supp. A	30.0d	13-Feb-26	26-Mar-26	198.0d
543	WBS - Air Handling Unit Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	244.0d
544	PR-P1-1C1-50	Prep Air Handling Units Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	244.0d
545	WBS - Materials & Equip for Cooling Tower Fans Procurement - ASD		21.0d	13-Feb-26	13-Mar-26	290.0d
546	PR-P2-1C1-80	Prep Cooling Tower Fans Submittals (Contractor) - ASD	21.0d	13-Feb-26	13-Mar-26	290.0d




	ID	Name	Dur	Start	Finish	TF
547	WBS - Natural Gas Equip. Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	432.0d
548	PR-P2-1C1-160	Prep Natural Gas Equip. Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	432.0d
549	WBS - Water Softening System Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	388.0d
550	PR-P2-1C1-170	Prep Water Softening System Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	388.0d
551	WBS - Pumps Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	397.0d
552	PR-P2-1C1-110	Prep Pumps Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	397.0d
553	WBS - Electrical & Site Electrical Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
554	PR-P1-1C1-830	Prep Elec. & Site Elec. Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
555	WBS - Special Exterior Lighting Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	393.0d
556	PR-P2-1C1-140	Prep Special Exterior LTNG Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	393.0d
557	WBS - Lightning Protection Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
558	PR-P2-1C1-130	Prep Lightning Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
559	WBS - Low Voltage System Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
560	PR-P1-1C1-840	Prep Low Voltage System Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
561	WBS - Terrazzo Floor Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	386.0d
562	PR-P2-1C1-680	Prep Terrazzo Floor Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
563	WBS - Terrazzo Monumental Stair Treads Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	386.0d
564	PR-P2-1C1-440	Prep Terrazzo Monumental Stair Treads Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
565	WBS - Interior Handrail - ASD		30.0d	6-Feb-26	19-Mar-26	118.0d
566	PR-P2-1C1-910	Prep Interior Handrail Submittals (Contractor) - ASD	30.0d	6-Feb-26	19-Mar-26	118.0d
567	WBS - Exterior Insulation - ASD		30.0d	13-Feb-26	26-Mar-26	91.0d
568	PR-P2-1C1-890	Prep Exterior Insulation Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
569	WBS - Expansion Joint Procurement - ASD		25.0d	13-Feb-26	19-Mar-26	288.0d
570	PR-P2-1C1-960	Prep Expansion Joint Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	288.0d
571	WBS - Demolition Safety Plan Submittal - ASD		25.0d	13-Feb-26	19-Mar-26	61.0d
572	PR-P2-1C1-7840	Submit Demolition Safety Plan (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	61.0d
573	WBS - Ductwork/Mechanical Systems - ASD		25.0d	13-Feb-26	19-Mar-26	151.0d
574	PR-P2-1C1-8280	Prep Ductwork/Mech. Systems Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	151.0d
575	WBS - Plumbing Systems - ASD		25.0d	13-Feb-26	19-Mar-26	149.0d
576	PR-P2-1C1-8400	Prep Plumbing Systems Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	149.0d
577	WBS - Pedestrian Control Signage (Sitework) Procurement - ASD		30.0d	13-Feb-26	26-Mar-26	548.0d
578	PR-P1-1C1-3610	Prep Pedestrian Control Signage (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	548.0d
579	WBS - Baggage Handling System Procurement - ASD		132.0d	20-Oct-25 A	27-Apr-26	991.0d
580	WBS - General BHS Submittals & Procurement - ASD		110.0d	20-Oct-25 A	26-Mar-26	1,013.0d
581	WBS - Quality Control Manual Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
582	A109250	Prep & Submit Quality Control Manual - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
583	A109260	Review & Approve (HP) Quality Control Manual - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
584	A109270	Review & Approve (HNTB) Quality Control Manual - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
585	A109280	Review & Approve (HCAA) Quality Control Manual - ASD	15.0d	21-Jan-26	10-Feb-26	263.0d
586	WBS - Environmental Requirements Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	1,045.0d
587	A109310	Prep & Submit Environmental Requirements - ASD	48.0d	20-Oct-25 A	29-Dec-25	1,044.0d
588	A109340	Review & Approve (HP) Environmental Requirements - ASD	5.0d	30-Dec-25	6-Jan-26	1,044.0d

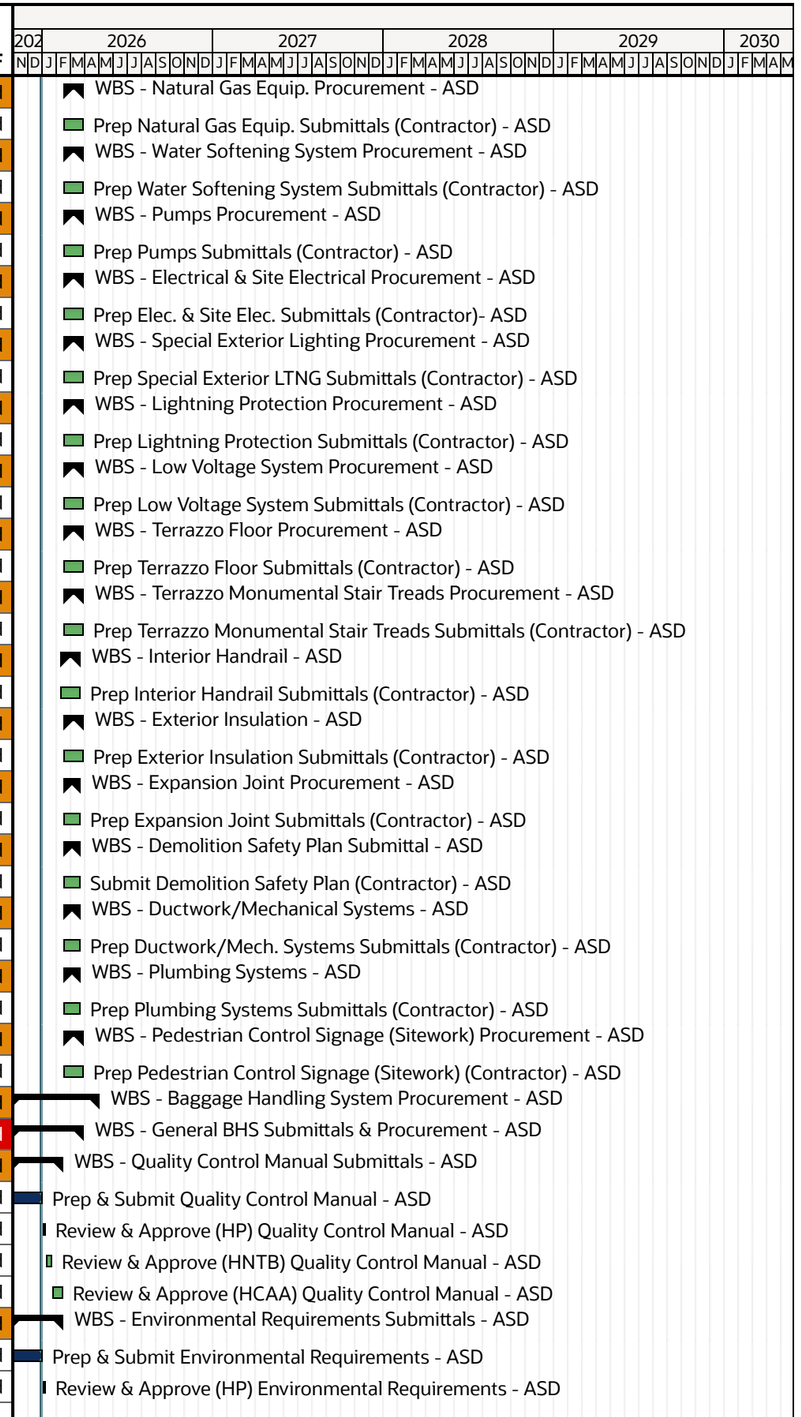


	ID	Name	Dur	Start	Finish	TF
589	A109380	Review & Approve (HNTB) Environmental Requirements - ASD	10.0d	7-Jan-26	20-Jan-26	1,044.0d
590	A109390	Review & Approve (HCAA) Environmental Requirements - ASD	15.0d	21-Jan-26	10-Feb-26	1,044.0d
591	WBS - Project Organizational Chart & Management Team Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
592	A109300	Prep & Submit Project Organizational Chart & Management Team - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
593	A109320	Review & Approve (HP) Project Organizational Chart & Management Team - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
594	A109400	Review & Approve (HNTB) Project Organizational Chart & Management Team - ...	10.0d	7-Jan-26	20-Jan-26	263.0d
595	A109410	Review & Approve (HCAA) Project Organizational Chart & Management Team - ...	15.0d	21-Jan-26	10-Feb-26	263.0d
596	WBS - Detailed Master Schedule Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
597	A109290	Prep & Submit Detailed Master Schedule - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
598	A109330	Review & Approve (HP) Detailed Master Schedule - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
599	A109420	Review & Approve (HNTB) Detailed Master Schedule - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
600	A109430	Review & Approve (HCAA) Detailed Master Schedule - ASD	15.0d	21-Jan-26	10-Feb-26	263.0d
601	WBS - O&M Manual Submittals - ASD		86.0d	18-Nov-25 A	23-Mar-26	653.0d
602	A109350	Prep & Submit O&M Manual - Draft - ASD	31.0d	18-Nov-25 A	5-Jan-26	653.0d
603	A109440	Review & Approve (HP) O&M Manual - Draft - ASD	5.0d	6-Jan-26	12-Jan-26	653.0d
604	A109450	Review & Approve (HNTB) O&M Manual - Draft - ASD	10.0d	13-Jan-26	26-Jan-26	653.0d
605	A109360	Review & Approve (HCAA) O&M Manual - Draft - ASD	15.0d	27-Jan-26	16-Feb-26	653.0d
606	A109370	Submit O&M Manual - Final - ASD	25.0d	17-Feb-26	23-Mar-26	653.0d
607	WBS - Baggage Tag Verification Report Submittals - ASD		25.0d	13-Feb-26	19-Mar-26	906.0d
608	D2916	Prep & Submit Baggage Tag Verification Report - ASD	10.0d	13-Feb-26	26-Feb-26	905.0d
609	A109460	Review & Approve (HP) Baggage Tag Verification Report - ASD	5.0d	27-Feb-26	5-Mar-26	905.0d
610	A109470	Review & Approve (HNTB) Baggage Tag Verification Report - ASD	10.0d	6-Mar-26	19-Mar-26	905.0d
611	WBS - Configuration Management Plan Submittals - ASD		30.0d	13-Feb-26	26-Mar-26	886.0d
612	A109500	Prep & Submit Configuration Management Plan - ASD	30.0d	13-Feb-26	26-Mar-26	885.0d
613	WBS - O&M Training Plan & Proposed Agenda Submittals		30.0d	13-Feb-26	26-Mar-26	632.0d
614	D3096	Prep & Submit O&M Training Plan & Proposed Agenda	15.0d	13-Feb-26	5-Mar-26	632.0d
615	A109600	Review & Approve (HP) O&M Training Plan & Proposed Agenda	5.0d	6-Mar-26	12-Mar-26	632.0d
616	A109610	Review & Approve (HNTB) O&M Training Plan & Proposed Agenda	10.0d	13-Mar-26	26-Mar-26	632.0d
617	WBS - Mechanical BHS Submittals & Procurement - ASD		25.0d	13-Feb-26	19-Mar-26	372.0d
618	WBS - General Mechanical BHS Submittals & Procurement - ASD		25.0d	13-Feb-26	19-Mar-26	372.0d
619	WBS - Sector M - General Mechanical BHS Submittals & Procurement - ASD		25.0d	13-Feb-26	19-Mar-26	362.0d
620	WBS - Mechanical Submittals - Sector M		25.0d	13-Feb-26	19-Mar-26	362.0d
621	D1495	Prep & Submit Mech. Plan & Elev Dwg Set - Sector M	20.0d	13-Feb-26	12-Mar-26	362.0d
622	D5476	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector M	5.0d	13-Mar-26	19-Mar-26	362.0d
623	WBS - Sector L		25.0d	13-Feb-26	19-Mar-26	367.0d
624	WBS - Mechanical Submittals - Sector L		25.0d	13-Feb-26	19-Mar-26	367.0d
625	D1501	Prep & Submit Mech. Plan & Elev Dwg Set - Sector L	20.0d	13-Feb-26	12-Mar-26	367.0d
626	D5496	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector L	5.0d	13-Mar-26	19-Mar-26	367.0d
627	WBS - Sector K		25.0d	13-Feb-26	19-Mar-26	372.0d
628	WBS - Mechanical Submittals - Sector K		25.0d	13-Feb-26	19-Mar-26	372.0d
629	D1507	Prep & Submit Mech. Plan & Elev Dwg Set - Sector K	20.0d	13-Feb-26	12-Mar-26	0.0d
630	D5516	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector K	5.0d	13-Mar-26	19-Mar-26	372.0d

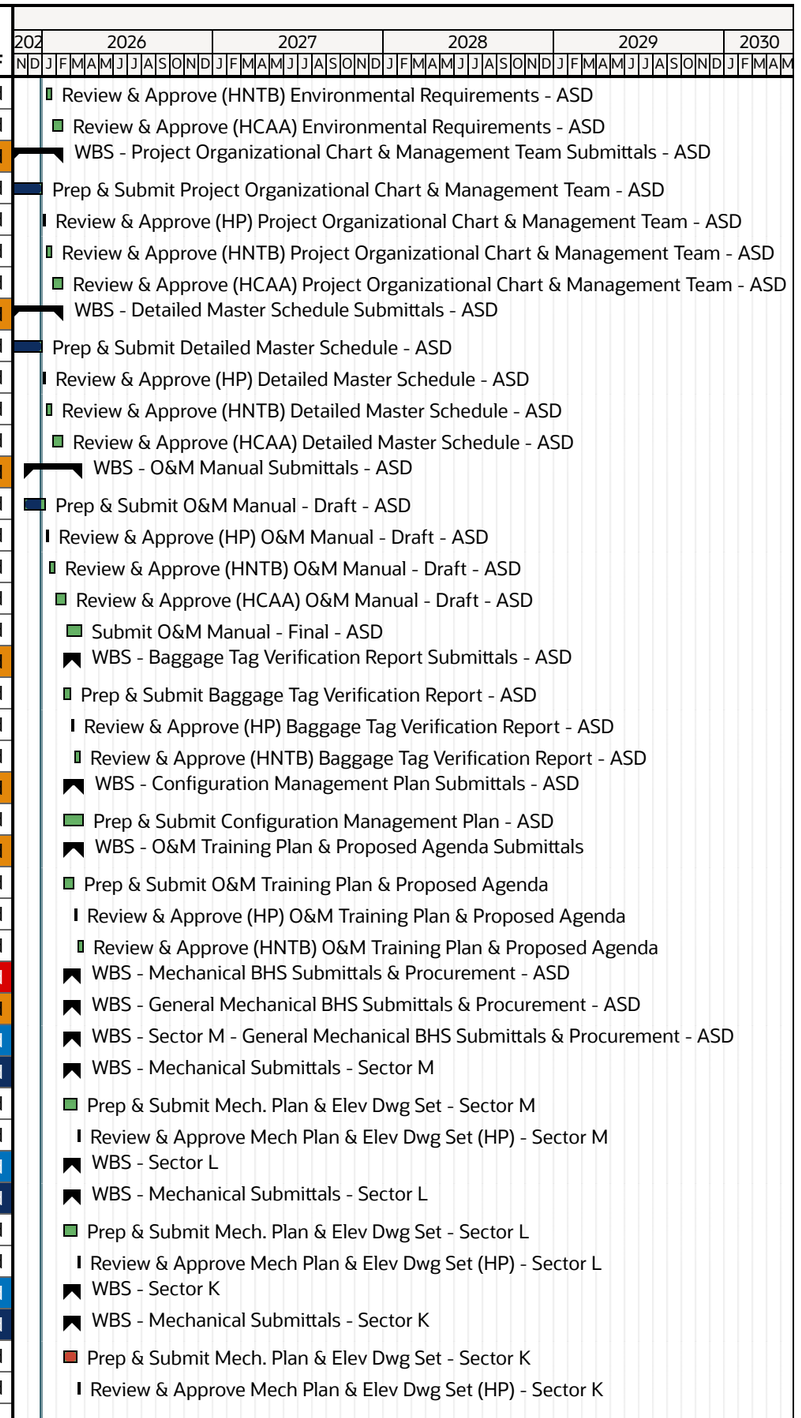

	ID	Name	Dur	Start	Finish	TF
631	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - ASD		111.0d	18-Nov-25 A	27-Apr-26	891.0d
632	WBS - General Electrical/Controls/Software Engineering Submittals - ASD		111.0d	18-Nov-25 A	27-Apr-26	891.0d
633	WBS - Factory Acceptance Test Plan & Agenda		30.0d	13-Feb-26	26-Mar-26	901.0d
634	D5986	Prep & Submit Factory Acceptance Test Plan & Agenda	15.0d	13-Feb-26	5-Mar-26	900.0d
635	D6006	HP Review & Approve Factory Acceptance Test Plan & Agenda	5.0d	6-Mar-26	12-Mar-26	900.0d
636	D6016	HNTB Review & Approve Factory Acceptance Test Plan & Agenda	10.0d	13-Mar-26	26-Mar-26	900.0d
637	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		57.0d	18-Nov-25 A	10-Feb-26	373.0d
638	A110050	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	27.0d	18-Nov-25 A	29-Dec-25	373.0d
639	A110070	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
640	A110160	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
641	A110170	Review & Approve (HCAA) Elec. / Controls / Computer Catalog Cuts & Equip. S...	15.0d	21-Jan-26	10-Feb-26	373.0d
642	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		45.0d	30-Dec-25	3-Mar-26	930.0d
643	A110020	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	30-Dec-25	20-Jan-26	929.0d
644	A110090	Review & Approve (HP) ATR / BMA Catalog Cuts & Equip. Specs	5.0d	21-Jan-26	27-Jan-26	929.0d
645	A110180	Review & Approve (HNTB) ATR / BMA Catalog Cuts & Equip. Specs	10.0d	28-Jan-26	10-Feb-26	929.0d
646	A110190	Review & Approve (HCAA) ATR / BMA Catalog Cuts & Equip. Specs	15.0d	11-Feb-26	3-Mar-26	929.0d
647	WBS - Lower-Level Network Architecture Drawings Submittals		60.0d	30-Dec-25	24-Mar-26	383.0d
648	A110040	Prep & Submit Lower-Level Network Architecture Drawings	30.0d	30-Dec-25	10-Feb-26	383.0d
649	A110210	Review & Approve (HP) Lower-Level Network Architecture Drawings	5.0d	11-Feb-26	17-Feb-26	383.0d
650	A110200	Review & Approve (HNTB) Lower-Level Network Architecture Drawings	10.0d	18-Feb-26	3-Mar-26	383.0d
651	A110110	Review & Approve (HCAA) Lower-Level Network Architecture Drawings	15.0d	4-Mar-26	24-Mar-26	383.0d
652	WBS - Upper-Level Network Architecture Drawings Submittals		30.0d	11-Feb-26	24-Mar-26	807.0d
653	A110010	Prep & Submit Upper-Level Network Architecture Drawings	30.0d	11-Feb-26	24-Mar-26	807.0d
654	WBS - Functional Specification Submittals		111.0d	18-Nov-25 A	27-Apr-26	535.0d
655	A110060	Prep & Submit Functional Specification [180 days prior to pre-TRR]	111.0d	18-Nov-25 A	27-Apr-26	535.0d
656	WBS - Cybersecurity Plan Submittals		25.0d	13-Feb-26	19-Mar-26	211.0d
657	A110370	Prep & Submit Cybersecurity Plan [5 days prior to beneficial use by phase]	20.0d	13-Feb-26	12-Mar-26	211.0d
658	A110390	Review & Approve (HP) Cybersecurity Plan	5.0d	13-Mar-26	19-Mar-26	211.0d
659	WBS - VDC Coordination		74.0d	8-Dec-25 A	23-Mar-26	239.0d
660	WBS - Deep Underground - VDC Coordination		58.0d	8-Dec-25 A	28-Feb-26	184.0d
661	WBS - Deep UG East VDC Coordination		21.0d	8-Dec-25 A	29-Dec-25	168.0d
662	WBS - Mechanical Shop Drawings - Deep UG East VDC Coordination		21.0d	8-Dec-25 A	29-Dec-25	168.0d
663	PR-VDC-DU-4100	Fab. & Ship Deep UG East Mech. Shop Drawings	21.0d	8-Dec-25 A	29-Dec-25	168.0d
664	WBS - Deep UG West VDC Coordination		44.0d	29-Dec-25	28-Feb-26	184.0d
665	WBS - Plumbing Shop Drawings - Deep UG West VDC Coordination		44.0d	29-Dec-25	28-Feb-26	73.0d
666	PR-VDC-DU-4360	Prep & Submit Deep UG West Plumbing Shop Drawings	10.0d	29-Dec-25	12-Jan-26	73.0d
667	PR-VDC-DU-4370	Review & Approve (HP) Deep UG West Plumbing Shop Drawings	5.0d	13-Jan-26	19-Jan-26	73.0d
668	PR-VDC-DU-4380	Review & Approve (HNTB) Deep UG West Plumbing Shop Drawings	10.0d	20-Jan-26	2-Feb-26	73.0d
669	PR-VDC-DU-4390	Review & Approve (HCAA) Deep UG West Plumbing Shop Drawings	15.0d	3-Feb-26	23-Feb-26	73.0d
670	PR-VDC-DU-4400	Fab. & Ship Deep UG West Plumbing Shop Drawings	5.0d	24-Feb-26	28-Feb-26	102.0d
671	WBS - Electrical & Low Voltage Shop Drawings - Deep UG West VDC Coordination		40.0d	29-Dec-25	23-Feb-26	188.0d
672	PR-VDC-DU-4410	Prep & Submit Deep UG West Elec. Shop Drawings	10.0d	29-Dec-25	12-Jan-26	91.0d

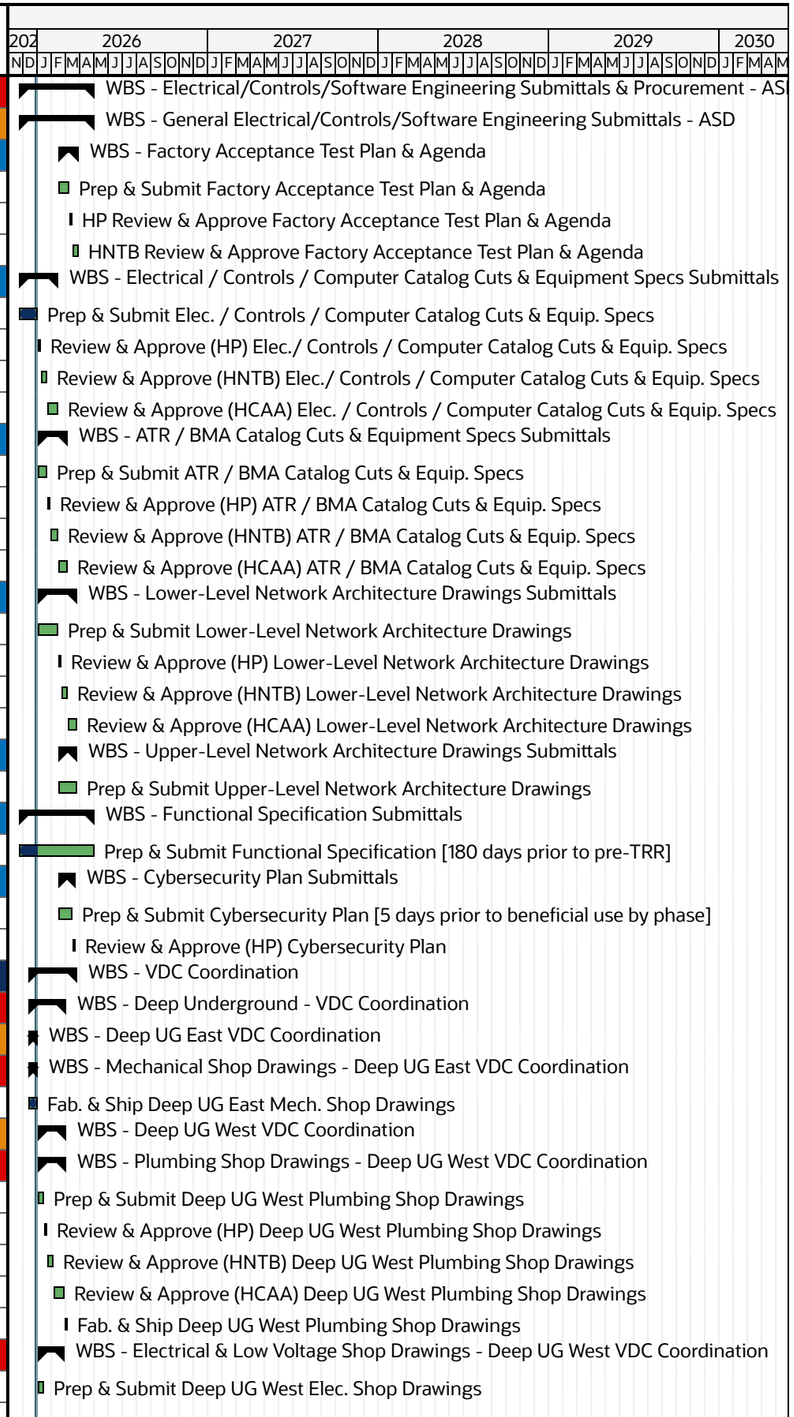


	ID	Name	Dur	Start	Finish	TF
673	PR-VDC-DU-4420	Review & Approve (HP) Deep UG West Elec.Shop Drawings	5.0d	13-Jan-26	19-Jan-26	188.0d
674	PR-VDC-DU-4430	Review & Approve (HNTB) Deep UG West Elec.Shop Drawings	10.0d	20-Jan-26	2-Feb-26	188.0d
675	PR-VDC-DU-4440	Review & Approve (HCAA) Deep UG West Elec. Shop Drawings	15.0d	3-Feb-26	23-Feb-26	188.0d
676	PR-VDC-DU-4450	Deep UG West Elec. Shop Drawings Approved	0.0d		23-Feb-26	263.0d
677	WBS - Shallow Underground - VDC Coordination		60.0d	29-Dec-25	23-Mar-26	239.0d
678	PR-VDC-ST-400	Model, Coordinate & Sign-off Shallow UG East - VDC Coordination	21.0d	29-Dec-25	27-Jan-26	147.0d
679	PR-VDC-ST-410	Model, Coordinate & Sign-off Shallow UG West - VDC Coordination	21.0d	20-Jan-26	17-Feb-26	239.0d
680	WBS - Shallow UG East - VDC Coordination		24.0d	28-Jan-26	2-Mar-26	147.0d
681	WBS - Mechanical Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d
682	PR-VDC-SU-4580	Prep & Submit Shallow UG East Mech. Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
683	PR-VDC-SU-4590	Review & Approve (HP) Shallow UG East Mech. Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
684	PR-VDC-SU-4560	Review & Approve (HNTB) Shallow UG East Mech. Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
685	PR-VDC-SU-4570	Review & Approve (HCAA) Shallow UG East Mech. Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
686	PR-VDC-SU-4600	Shallow UG East Mech. Shop Drawings Approved	0.0d		25-Feb-26	211.0d
687	WBS - Electrical Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d
688	PR-VDC-SU-4660	Prep & Submit Shallow UG East Elec. Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
689	PR-VDC-SU-4670	Review & Approve (HP) Shallow UG East Elec.Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
690	PR-VDC-SU-4680	Review & Approve (HNTB) Shallow UG East Elec. Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
691	PR-VDC-SU-4690	Review & Approve (HCAA) Shallow UG East Elec. Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
692	PR-VDC-SU-4700	Shallow UG East Elec. Shop Drawings Approved	0.0d		25-Feb-26	211.0d
693	WBS - Low Voltage Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d
694	PR-VDC-SU-4710	Prep & Submit Shallow UG East Low Voltage Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
695	PR-VDC-SU-4720	Review & Approve (HP) Shallow UG East Low Voltage Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
696	PR-VDC-SU-4730	Review & Approve (HNTB) Shallow UG East Low Voltage Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
697	PR-VDC-SU-4740	Review & Approve (HCAA) Shallow UG East Low Voltage Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
698	PR-VDC-SU-4750	Shallow UG East Low Voltage Shop Drawings Approved	0.0d		25-Feb-26	211.0d
699	WBS - Plumbing Shop Drawings - Shallow UG East - VDC Coordination		24.0d	28-Jan-26	2-Mar-26	147.0d
700	PR-VDC-SU-4610	Prep & Submit Shallow UG East Plumbing Shop Drawings	1.0d	28-Jan-26	28-Jan-26	147.0d
701	PR-VDC-SU-4620	Review & Approve (HP) Shallow UG East Plumbing Shop Drawings	5.0d	29-Jan-26	4-Feb-26	147.0d
702	PR-VDC-SU-4630	Review & Approve (HNTB) Shallow UG East Plumbing Shop Drawings	5.0d	5-Feb-26	11-Feb-26	147.0d
703	PR-VDC-SU-4640	Review & Approve (HCAA) Shallow UG East Plumbing Shop Drawings	10.0d	12-Feb-26	25-Feb-26	147.0d
704	PR-VDC-SU-4650	Shallow UG East Plumbing Shop Drawings Approved	5.0d	26-Feb-26	2-Mar-26	206.0d
705	WBS - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
706	WBS - Mechanical Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
707	PR-VDC-SU-4830	Prep & Submit Shallow UG West Mech. Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
708	PR-VDC-SU-4840	Review & Approve (HP) Shallow UG West Mech. Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
709	PR-VDC-SU-4810	Review & Approve (HNTB) Shallow UG West Mech. Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
710	PR-VDC-SU-4820	Review & Approve (HCAA) Shallow UG West Mech. Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
711	PR-VDC-SU-4850	Fab. & Ship Shallow UG West Mech. Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
712	WBS - Electrical Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
713	PR-VDC-SU-4910	Prep & Submit Shallow UG West Elec. Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
714	PR-VDC-SU-4920	Review & Approve (HP) Shallow UG West Elec.Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d

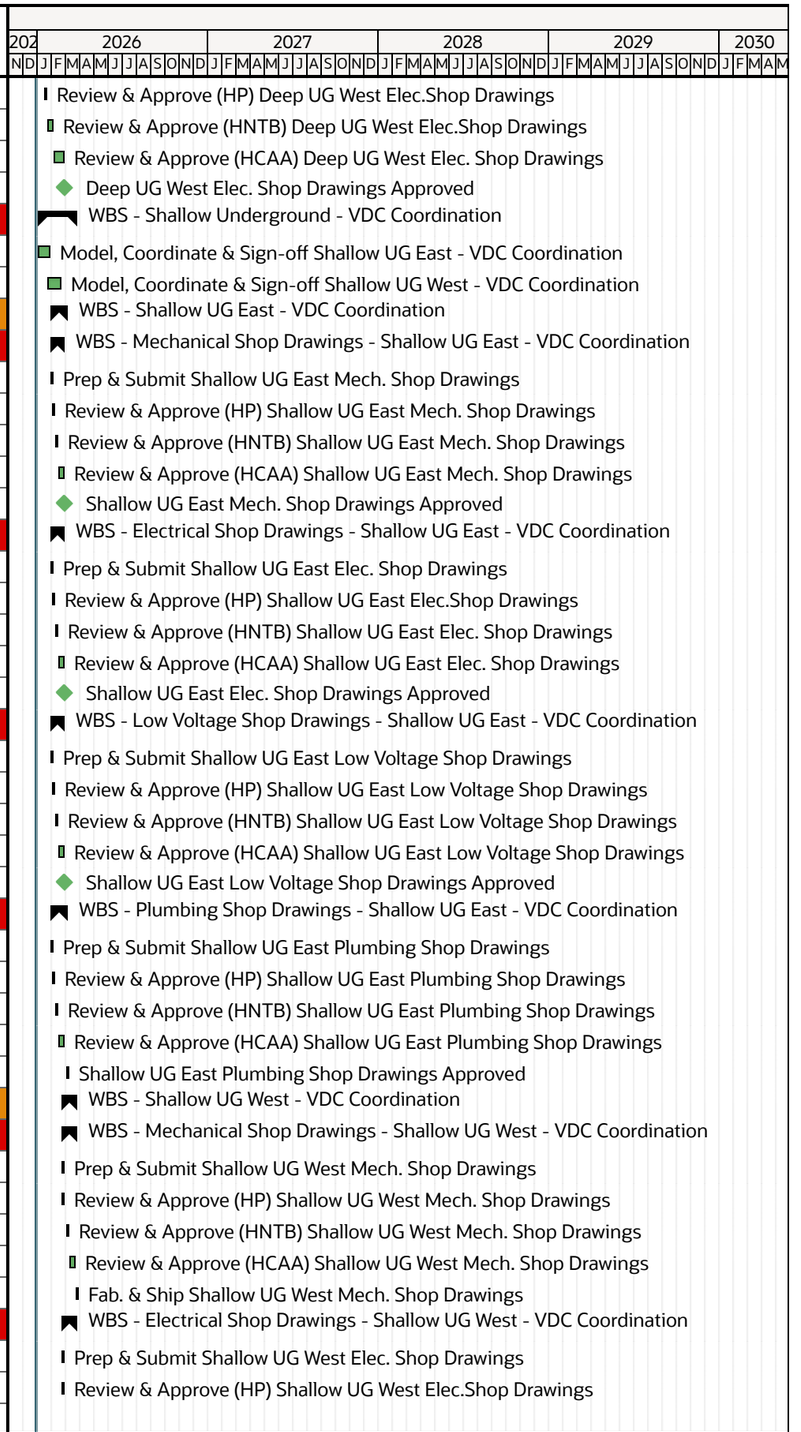

	ID	Name	Dur	Start	Finish	TF
715	PR-VDC-SU-4930	Review & Approve (HNTB) Shallow UG West Elec. Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
716	PR-VDC-SU-4940	Review & Approve (HCAA) Shallow UG West Elec. Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
717	PR-VDC-SU-4950	Fab. & Ship Shallow UG West Elec. Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
718	WBS - Low Voltage Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
719	PR-VDC-SU-4960	Prep & Submit Shallow UG West Low Voltage Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
720	PR-VDC-SU-4970	Review & Approve (HP) Shallow UG West Low Voltage Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
721	PR-VDC-SU-4980	Review & Approve (HNTB) Shallow UG West Low Voltage Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
722	PR-VDC-SU-4990	Review & Approve (HCAA) Shallow UG West Low Voltage Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
723	PR-VDC-SU-5000	Fab. & Ship Shallow UG West Low Voltage Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
724	WBS - Plumbing Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
725	PR-VDC-SU-4860	Prep & Submit Shallow UG West Plumbing Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
726	PR-VDC-SU-4870	Review & Approve (HP) Shallow UG West Plumbing Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
727	PR-VDC-SU-4880	Review & Approve (HNTB) Shallow UG West Plumbing Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
728	PR-VDC-SU-4890	Review & Approve (HCAA) Shallow UG West Plumbing Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
729	PR-VDC-SU-4900	Fab. & Ship Shallow UG West Plumbing Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
730	WBS - Overhead - VDC Coordination		60.0d	29-Dec-25	23-Mar-26	111.0d
731	PR-VDC-ST-10	Model, Coordinate & Sign-off Level 1, Area 1 - OH VDC Coordination	35.0d	29-Dec-25	16-Feb-26	23.0d
732	PR-VDC-ST-20	Model, Coordinate & Sign-off Level 1, Area 2 - OH VDC Coordination	40.0d	5-Jan-26	27-Feb-26	23.0d
733	WBS - Level 1, Area 1 - OH VDC Coordination		25.0d	17-Feb-26	23-Mar-26	111.0d
734	WBS - Mechanical Shop Drawings - Level 1, Area 1		25.0d	17-Feb-26	23-Mar-26	108.0d
735	PR-VDC-L1A1-10	Prep & Submit Level 1, Area 1 Mech. Shop Drawings	10.0d	17-Feb-26	2-Mar-26	108.0d
736	PR-VDC-L1A1-20	Review & Approve (HP) Level 1, Area 1 Mech. Shop Drawings	5.0d	3-Mar-26	9-Mar-26	108.0d
737	PR-VDC-L1A1-30	Review & Approve (HNTB) Level 1, Area 1 Mech. Shop Drawings	10.0d	10-Mar-26	23-Mar-26	108.0d
738	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 1		25.0d	17-Feb-26	23-Mar-26	103.0d
739	PR-VDC-L1A1-60	Prep & Submit Level 1, Area 1 Fire Sprinkler Shop Drawings	10.0d	17-Feb-26	2-Mar-26	103.0d
740	PR-VDC-L1A1-70	Review & Approve (HP) Level 1, Area 1 Fire Sprinkler Shop Drawings	5.0d	3-Mar-26	9-Mar-26	103.0d
741	PR-VDC-L1A1-80	Review & Approve (HNTB) Level 1, Area 1 Fire Sprinkler Shop Drawings	10.0d	10-Mar-26	23-Mar-26	103.0d
742	WBS - Electrical Shop Drawings - Level 1, Area 1		25.0d	17-Feb-26	23-Mar-26	111.0d
743	PR-VDC-L1A1-160	Prep & Submit Level 1, Area 1 Elec. Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
744	PR-VDC-L1A1-170	Review & Approve (HP) Level 1, Area 1 Elec.Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
745	PR-VDC-L1A1-180	Review & Approve (HNTB) Level 1, Area 1 Elec. Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
746	WBS - Low Voltage Shop Drawings - Level 1, Area 1		25.0d	17-Feb-26	23-Mar-26	111.0d
747	PR-VDC-L1A1-210	Prep & Submit Level 1, Area 1 Low Voltage Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
748	PR-VDC-L1A1-220	Review & Approve (HP) Level 1, Area 1 Low Voltage Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
749	PR-VDC-L1A1-230	Review & Approve (HNTB) Level 1, Area 1 Low Voltage Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
750	WBS - Plumbing Shop Drawings - Level 1, Area 1		25.0d	17-Feb-26	23-Mar-26	111.0d
751	PR-VDC-L1A1-110	Prep & Submit Level 1, Area 1 Plumbing Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
752	PR-VDC-L1A1-120	Review & Approve (HP) Level 1, Area 1 Plumbing Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
753	PR-VDC-L1A1-130	Review & Approve (HNTB) Level 1, Area 1 Plumbing Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
754	WBS - Level 1, Area 2 - OH VDC Coordination		15.0d	2-Mar-26	20-Mar-26	94.0d
755	WBS - Mechanical Shop Drawings - Level 1, Area 2		15.0d	2-Mar-26	20-Mar-26	94.0d
756	PR-VDC-L1A2-330	Prep & Submit Level 1, Area 2 Mech. Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d




	ID	Name	Dur	Start	Finish	TF
757	PR-VDC-L1A2-340	Review & Approve (HP) Level 1, Area 2 Mech. Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
758	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 2		15.0d	2-Mar-26	20-Mar-26	94.0d
759	PR-VDC-L1A2-260	Prep & Submit Level 1, Area 2 Fire Sprinkler Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
760	PR-VDC-L1A2-270	Review & Approve (HP) Level 1, Area 2 Fire Sprinkler Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
761	WBS - Plumbing Shop Drawings - Level 1, Area 2		15.0d	2-Mar-26	20-Mar-26	94.0d
762	PR-VDC-L1A2-360	Prep & Submit Level 1, Area 2 Plumbing Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
763	PR-VDC-L1A2-370	Review & Approve (HP) Level 1, Area 2 Plumbing Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
764	WBS - Electrical Shop Drawings - Level 1, Area 2		15.0d	2-Mar-26	20-Mar-26	94.0d
765	PR-VDC-L1A2-410	Prep & Submit Level 1, Area 2 Elec. Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
766	PR-VDC-L1A2-420	Review & Approve (HP) Level 1, Area 2 Elec.Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
767	WBS - Low Voltage Shop Drawings - Level 1, Area 2		15.0d	2-Mar-26	20-Mar-26	94.0d
768	PR-VDC-L1A2-460	Prep & Submit Level 1, Area 2 Low Voltage Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
769	PR-VDC-L1A2-470	Review & Approve (HP) Level 1, Area 2 Low Voltage Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
770	WBS - ASD - CONSTRUCTION PHASE		975.0d	13-Dec-24 A	15-Oct-28	106.0d
771	WBS - Enabling		296.0d	13-Dec-24 A	12-Feb-26	785.0d
772	WBS - Hammocks		296.0d	13-Dec-24 A	12-Feb-26	785.0d
773	EN-HAM-10	Enabling Scope (GCs/Markups) - (LOE)	296.0d	13-Dec-24 A	12-Feb-26	785.0d
774	WBS - Phase C Work Area		10.0d	30-Jan-26	12-Feb-26	0.0d
775	WBS - Area 1		10.0d	30-Jan-26	12-Feb-26	0.0d
776	EN-DM-A1-130	Demo Second Half of Tunnel Structure - Phase C Area 1	10.0d	30-Jan-26	12-Feb-26	0.0d
777	WBS - Ground Improvements		30.0d	15-Dec-25 A	27-Jan-26	82.0d
778	WBS - Rigid Inclusions - Area 2		5.0d	29-Dec-25	5-Jan-26	98.0d
779	GI-A2-120	Cut Dip RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
780	GI-A2-130	Install Grout & Install Steel Caps - RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
781	WBS - Rigid Inclusions - Area 1		18.0d	15-Dec-25 A	9-Jan-26	41.0d
782	GI-A1-20	DIP Install - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
783	GI-A1-30	Excavate - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
784	GI-A1-40	Cut Dip & Install Grout - RI DIPS Area 1 - 12/13 Line	2.0d	6-Jan-26	7-Jan-26	41.0d
785	GI-A1-50	Install Steel Caps - RI DIPS Area 1 - 12/13 Line	2.0d	8-Jan-26	9-Jan-26	41.0d
786	WBS - Rigid Inclusions - Area 3		24.0d	15-Dec-25 A	19-Jan-26	51.0d
787	GI-A3-140	DIP Install - RI DIPS Area 3	20.0d	15-Dec-25 A	13-Jan-26	46.0d
788	GI-A3-100	Excavate - RI DIPS Area 3	14.0d	15-Dec-25 A	5-Jan-26	51.0d
789	GI-A3-110	Cut Dip & Install Grout - RI DIPS Area 3	5.0d	6-Jan-26	12-Jan-26	51.0d
790	GI-A3-120	Install Steel Caps - RI DIPS Area 3	5.0d	13-Jan-26	19-Jan-26	51.0d
791	WBS - Rigid Inclusions - Area 5		19.0d	15-Dec-25 A	12-Jan-26	81.0d
792	GI-A5-100	DIP Install - RI DIPS Area 5	19.0d	15-Dec-25 A	12-Jan-26	47.0d
793	GI-A5-110	Excavate - RI DIPS Area 5	14.0d	15-Dec-25 A	5-Jan-26	82.0d
794	GI-A5-120	Cut Dip & Install Grout - RI DIPS Area 5	2.0d	6-Jan-26	7-Jan-26	82.0d
795	GI-A5-130	Install Steel Caps - RI DIPS Area 5	2.0d	8-Jan-26	9-Jan-26	82.0d
796	WBS - Rigid Inclusions - Area 4		9.0d	14-Jan-26	26-Jan-26	46.0d
797	GI-A4-90	Excavate - RI DIPS Area 4	5.0d	14-Jan-26	20-Jan-26	46.0d
798	GI-A4-80	DIP Install - RI DIPS Area 4	9.0d	14-Jan-26	26-Jan-26	46.0d

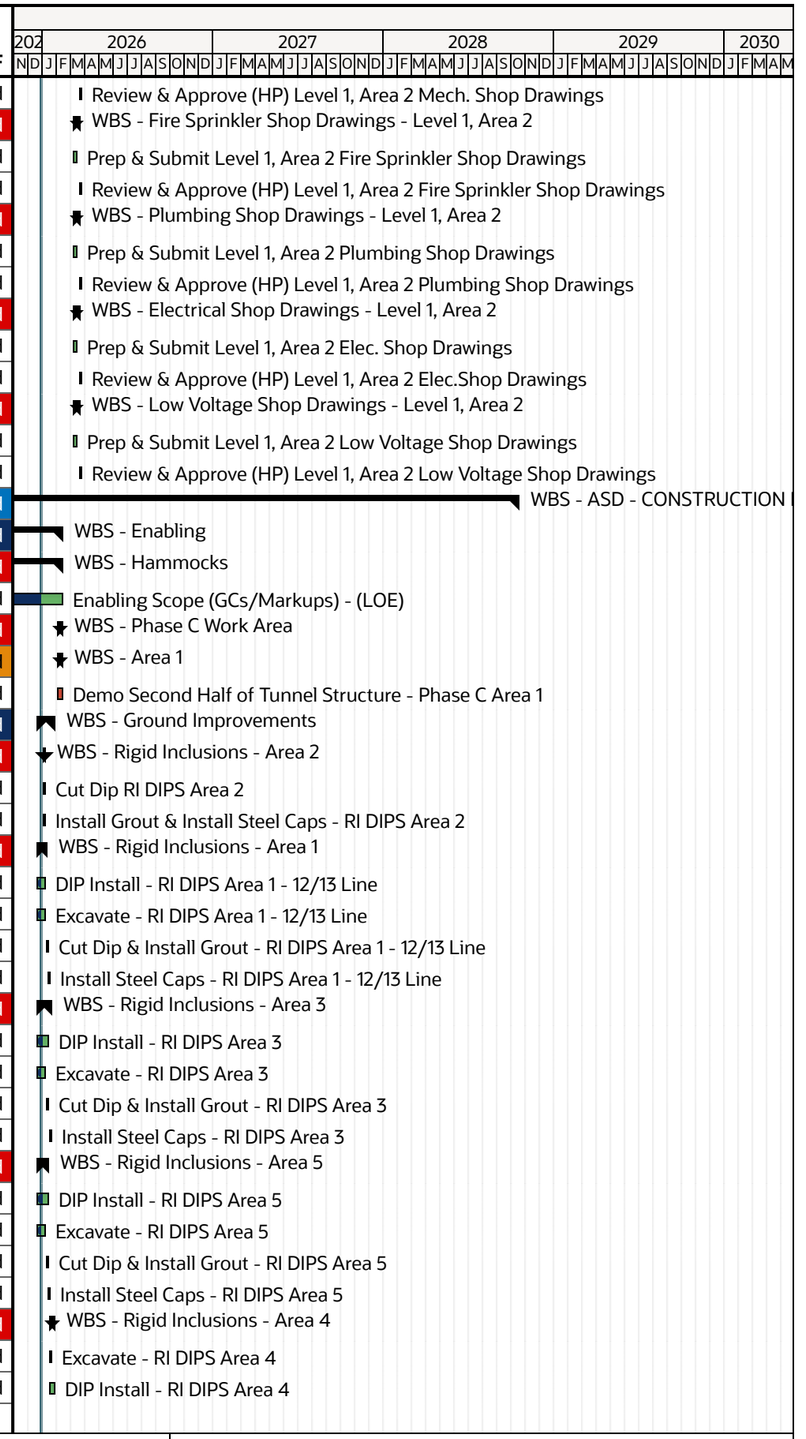


	ID	Name	Dur	Start	Finish	TF
799	GI-A4-100	Cut Dip & Install Grout - RI DIPS Area 4	2.0d	21-Jan-26	22-Jan-26	46.0d
800	GI-A4-110	Install Steel Caps - RI DIPS Area 4	2.0d	23-Jan-26	26-Jan-26	46.0d
801	WBS - Rigid Inclusions - Area 6-1 Cooling Tower		10.0d	14-Jan-26	27-Jan-26	46.0d
802	GI-A6-1-100	DIP Install - RI DIPS Area 6 - 1	4.0d	14-Jan-26	19-Jan-26	49.0d
803	GI-A6-1-110	Excavate - RI DIPS Area 6 - 1	3.0d	14-Jan-26	16-Jan-26	49.0d
804	GI-A6-1-120	Cut Dip & Install Grout - RI DIPS Area 6 - 1	2.0d	19-Jan-26	20-Jan-26	49.0d
805	GI-A6-1-130	Install Steel Caps - RI DIPS Area 6 - 1	2.0d	26-Jan-26	27-Jan-26	46.0d
806	WBS - Foundations & Deep Underground		71.0d	16-Dec-25 A	26-Mar-26	140.0d
807	WBS - Milestones		57.0d	7-Jan-26	26-Mar-26	105.0d
808	GI-FS-A5-6390	28 Day Cure on All Concrete for Steel - Area 6	28.0d	7-Jan-26	3-Feb-26	199.0d
809	MLS-GI-FS1040	Found. Area 6 - Ready for Steel	0.0d		3-Feb-26	142.0d
810	GI-FS-A2-4470	28 Day Cure on All Concrete for Steel - Area 2.A	28.0d	14-Feb-26	13-Mar-26	88.0d
811	GI-FS-A1-6960	28 Day Cure on All Concrete for Steel - Elevator & Escalator Pits	28.0d	27-Feb-26	26-Mar-26	25.0d
812	MLS-GI-FS6950	Elevator Pits - Ready for Precast	0.0d		26-Mar-26	17.0d
813	WBS - Elevator / Escalator Pits		31.0d	23-Jan-26	6-Mar-26	31.0d
814	GI-FS-A1-6910	Excavate Area For Found. - Elevator & Escalator Pits	5.0d	23-Jan-26	29-Jan-26	17.0d
815	GI-FS-A1-6920	FRP Found. - Elevator & Escalator Pits	20.0d	30-Jan-26	26-Feb-26	17.0d
816	GI-FS-A1-6930	Install Waterproofing On Found. - Elevator & Escalator Pits	20.0d	2-Feb-26	27-Feb-26	31.0d
817	GI-FS-A1-6940	MEPF In-Wall R/I - Elevator & Escalator Pits	15.0d	2-Feb-26	20-Feb-26	31.0d
818	GI-FS-A1-6950	Backfill Found. - Elevator & Escalator Pits	10.0d	23-Feb-26	6-Mar-26	31.0d
819	WBS - Foundations - Area 6		21.0d	16-Dec-25 A	15-Jan-26	4.0d
820	GI-FS-A1-6820	FRP Found. - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
821	GI-FS-A1-6840	MEPF In-Wall R/I - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
822	GI-FS-A1-6825	FRP Turndown - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
823	GI-FS-A1-6830	Install Waterproofing On Found. - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
824	GI-FS-A1-6850	Backfill Found. - Area 6	7.0d	7-Jan-26	15-Jan-26	4.0d
825	WBS - Foundations - Area 2		35.0d	16-Jan-26	5-Mar-26	2.0d
826	GI-FS-A1-6610	Excavate Area For Found. - Area 2.A	5.0d	16-Jan-26	22-Jan-26	4.0d
827	GI-FS-A1-6620	FRP Found. - Area 2.A	20.0d	19-Jan-26	13-Feb-26	4.0d
828	GI-FS-A1-6640	MEPF In-Wall R/I - Area 2.A	15.0d	19-Jan-26	6-Feb-26	6.0d
829	GI-FS-A1-6630	Install Waterproofing On Found. - Area 2.A	20.0d	20-Jan-26	16-Feb-26	4.0d
830	GI-FS-A1-6650	Backfill Found. - Area 2.A	7.0d	11-Feb-26	19-Feb-26	4.0d
831	GI-FS-A1-6970	Excavate Area For Found. - Area 2.B	3.0d	13-Feb-26	17-Feb-26	2.0d
832	GI-FS-A1-6980	FRP Found. - Area 2.B	11.0d	16-Feb-26	2-Mar-26	2.0d
833	GI-FS-A1-6990	Install Waterproofing On Found. - Area 2.B	10.0d	17-Feb-26	2-Mar-26	2.0d
834	GI-FS-A1-7000	MEPF In-Wall R/I - Area 2.B	7.0d	18-Feb-26	26-Feb-26	3.0d
835	GI-FS-A1-7010	Backfill Found. - Area 2.B	4.0d	2-Mar-26	5-Mar-26	2.0d
836	WBS - Foundations - Area 1		15.0d	6-Mar-26	26-Mar-26	0.0d
837	GI-FS-A1-1070	Excavate Area For Found. - Area 1.A	2.0d	6-Mar-26	9-Mar-26	2.0d
838	GI-FS-A1-1250	FRP Found. - Area 1.A	5.0d	11-Mar-26	17-Mar-26	0.0d
839	GI-FS-A1-1410	MEPF In-Wall R/I - Area 1.A	2.0d	11-Mar-26	12-Mar-26	2.0d
840	GI-FS-A1-1260	Install Waterproofing On Found. - Area 1.A	3.0d	12-Mar-26	16-Mar-26	0.0d




	ID	Name	Dur	Start	Finish	TF
841	GI-FS-A1-7020	Excavate Area For Found. - Area 1.B	3.0d	17-Mar-26	19-Mar-26	0.0d
842	GI-FS-A1-1270	Backfill Found. - Area 1.A	3.0d	17-Mar-26	19-Mar-26	0.0d
843	GI-FS-A1-7030	FRP Found. - Area 1.B	7.0d	18-Mar-26	26-Mar-26	0.0d
844	GI-FS-A1-7040	MEPF In-Wall R/I - Area 1.B	3.0d	19-Mar-26	23-Mar-26	3.0d
845	GI-FS-A1-7050	Install Waterproofing On Found. - Area 1.B	4.0d	23-Mar-26	26-Mar-26	0.0d
846	WBS - Deep Underground MEP - All Areas		67.0d	22-Dec-25 A	26-Mar-26	140.0d
847	WBS - Deep Underground MEP - Area 2		63.0d	22-Dec-25 A	20-Mar-26	90.0d
848	GI-FS-A2-5570	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.2	6.0d	22-Dec-25 A	30-Dec-25	30.0d
849	GI-FS-A2-5500	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.1	21.0d	23-Dec-25 A	22-Jan-26	10.0d
850	GI-FS-A2-5610	Inspect - Deep UG Sanitary - Plumber - Area 2.B.2	2.0d	29-Dec-25	30-Dec-25	30.0d
851	GI-FS-A2-6980	Excavate - Deep UG Piping - Mech. - Area 2.B	4.0d	30-Dec-25	5-Jan-26	120.0d
852	GI-FS-A2-5630	Backfill - Deep UG Sanitary - Plumber - Area 2.B.2	3.0d	31-Dec-25	5-Jan-26	30.0d
853	GI-FS-A2-6990	Install - Deep UG Piping - Mech. - Area 2.B	4.0d	6-Jan-26	9-Jan-26	120.0d
854	GI-FS-A2-7120	Excavate - Deep UG Water Main - Plumbing - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
855	GI-FS-A2-7080	Excavate - Deep UG Fire Main - Fire - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
856	GI-FS-A2-5420	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.1	5.0d	8-Jan-26	14-Jan-26	102.0d
857	GI-FS-A2-7000	Inspect - Deep UG Piping - Mech. - Area 2.B	2.0d	12-Jan-26	13-Jan-26	120.0d
858	GI-FS-A2-5440	Inspect - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	13-Jan-26	14-Jan-26	102.0d
859	GI-FS-A2-7130	Install Pipe - Deep UG Water Main - Plumbing - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
860	GI-FS-A2-7090	Install Pipe - Deep UG Fire Main - Fire - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
861	GI-FS-A2-7010	Backfill - Deep UG Piping - Mech. - Area 2.B	3.0d	14-Jan-26	16-Jan-26	120.0d
862	GI-FS-A2-5450	Backfill - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	15-Jan-26	16-Jan-26	102.0d
863	GI-FS-A2-7140	Inspect - Deep UG Water Main - Plumbing - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
864	GI-FS-A2-7100	Inspect - Deep UG Fire Main - Fire - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
865	GI-FS-A2-7150	Backfill - Deep UG Water Main - Plumbing - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
866	GI-FS-A2-7110	Backfill - Deep UG Fire Main - Fire - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
867	GI-FS-A2-5580	Inspect - Deep UG Conduit - Elec. - Area 2.B.1	2.0d	23-Jan-26	26-Jan-26	10.0d
868	GI-FS-A2-5590	Backfill - Deep UG Conduit - Elec. - Area 2.B.1	5.0d	27-Jan-26	2-Feb-26	10.0d
869	GI-FS-A2-5780	Excavate - Deep UG Conduit - Elec. - Area 2.A.2	5.0d	3-Feb-26	9-Feb-26	71.0d
870	GI-FS-A2-7160	TECO 30 Day Advanced Notice to Schedule Conduit Pathways Install for PDS R...	1.0d	3-Feb-26	3-Feb-26	82.0d
871	GI-FS-A2-5840	Install Conduit - Deep UG Conduit - Elec. - Area 2.A.2	10.0d	10-Feb-26	23-Feb-26	79.0d
872	GI-FS-A2-5460	Excavate - Deep UG Sanitary - Plumber - Area 2.A.1	5.0d	20-Feb-26	26-Feb-26	99.0d
873	GI-FS-A2-5790	Excavate - Deep UG Sanitary - Plumber - Area 2.A.2	3.0d	20-Feb-26	24-Feb-26	103.0d
874	GI-FS-A2-5620	Excavate - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	20-Feb-26	26-Feb-26	96.0d
875	GI-FS-A2-5890	Inspect - Deep UG Conduit - Elec. - Area 2.A.2	2.0d	20-Feb-26	23-Feb-26	79.0d
876	GI-FS-A2-5900	Backfill - Deep UG Conduit - Elec. - Area 2.A.2	7.0d	24-Feb-26	4-Mar-26	79.0d
877	GI-FS-A2-5820	Install Pipe - Deep UG Sanitary - Plumber - Area 2.A.2	3.0d	25-Feb-26	27-Feb-26	103.0d
878	GI-FS-A2-5850	Inspect - Deep UG Sanitary - Plumber - Area 2.A.2	2.0d	26-Feb-26	27-Feb-26	103.0d
879	GI-FS-A2-5490	Install Pipe - Deep UG Sanitary - Plumber - Area 2.A.1	5.0d	27-Feb-26	5-Mar-26	99.0d
880	GI-FS-A2-5670	Install Conduit - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	27-Feb-26	5-Mar-26	96.0d
881	GI-FS-A2-5860	Backfill - Deep UG Sanitary - Plumber - Area 2.A.2	2.0d	2-Mar-26	3-Mar-26	103.0d
882	GI-FS-A2-7240	Excavate - Deep UG Sanitary- Plumber - Area 2.B.4	6.0d	3-Mar-26	10-Mar-26	58.0d

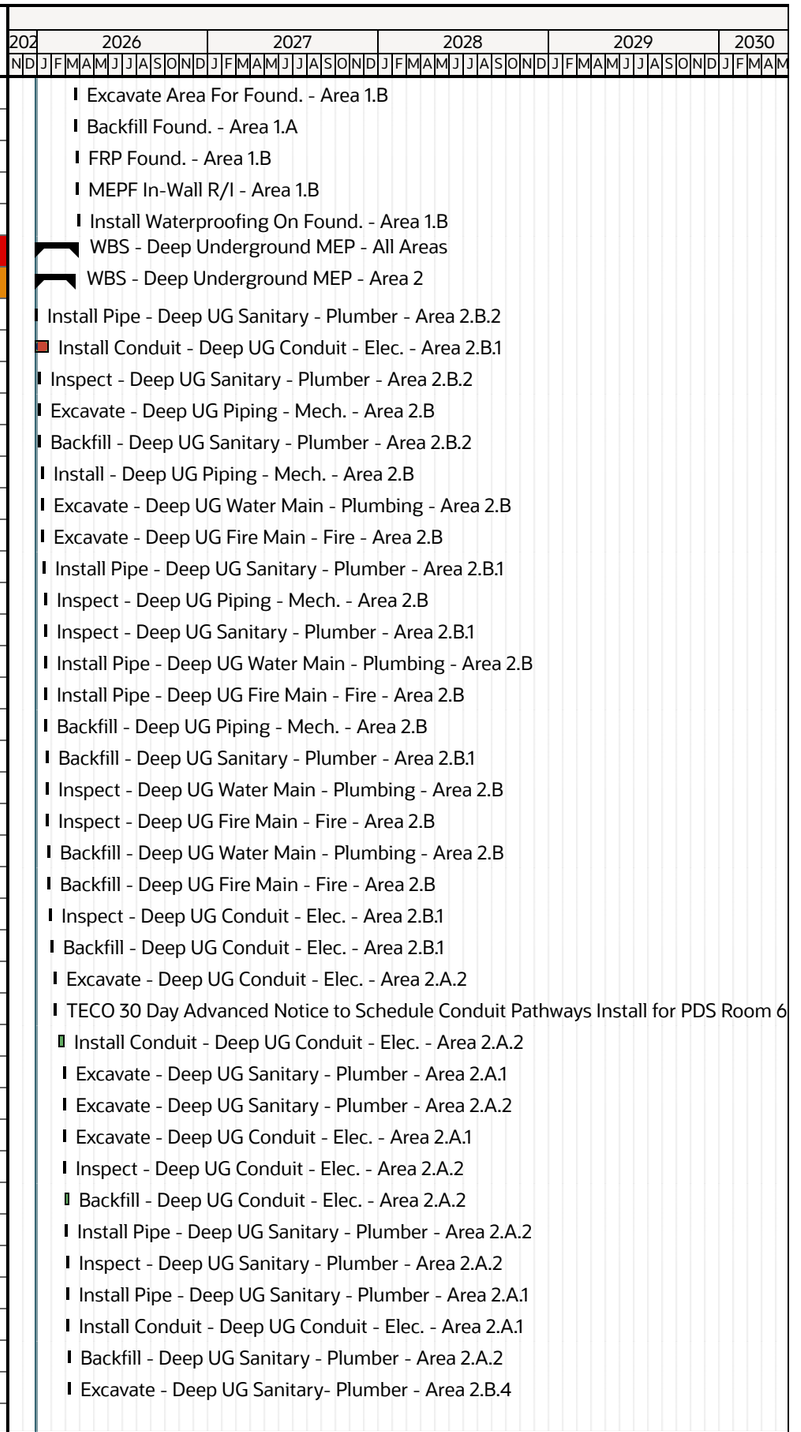

	ID	Name	Dur	Start	Finish	TF
883	GI-FS-A2-7210	Excavate - Deep UG Sanitary- Plumber - Area 2.B.3	6.0d	3-Mar-26	10-Mar-26	58.0d
884	GI-FS-A2-5510	Inspect - Deep UG Sanitary - Plumber - Area 2.A.1	2.0d	4-Mar-26	5-Mar-26	99.0d
885	GI-FS-A2-5680	Inspect - Deep UG Conduit - Elec. - Area 2.A.1	2.0d	4-Mar-26	5-Mar-26	96.0d
886	GI-FS-A2-5530	Backfill - Deep UG Sanitary - Plumber - Area 2.A.1	2.0d	6-Mar-26	9-Mar-26	99.0d
887	GI-FS-A2-6730	Excavate - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	6-Mar-26	10-Mar-26	21.0d
888	GI-FS-A2-7170	TECO Install Conduit pathways for PDS Room 6097	10.0d	6-Mar-26	19-Mar-26	58.0d
889	GI-FS-A2-6610	Excavate - Deep UG LV Conduit - Low Voltage - Area 2.B	6.0d	6-Mar-26	13-Mar-26	21.0d
890	GI-FS-A2-5700	Backfill - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	6-Mar-26	12-Mar-26	96.0d
891	GI-FS-A2-6740	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	11-Mar-26	13-Mar-26	21.0d
892	GI-FS-A2-7190	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.3	5.0d	11-Mar-26	17-Mar-26	58.0d
893	GI-FS-A2-7200	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.4	5.0d	11-Mar-26	17-Mar-26	58.0d
894	GI-FS-A2-6750	Inspect - Deep UG Conduit - Elec. - Area 2.B.2	2.0d	16-Mar-26	17-Mar-26	21.0d
895	GI-FS-A2-7250	Inspect - Deep UG Sanitary - Plumber - Area 2.B.4	2.0d	16-Mar-26	17-Mar-26	58.0d
896	GI-FS-A2-7220	Inspect - Deep UG Sanitary - Plumber - Area 2.B.3	2.0d	16-Mar-26	17-Mar-26	58.0d
897	GI-FS-A2-6630	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 2.B	5.0d	16-Mar-26	20-Mar-26	21.0d
898	GI-FS-A2-6760	Backfill - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	18-Mar-26	20-Mar-26	21.0d
899	GI-FS-A2-7260	Backfill - Deep UG Sanitary - Plumber - Area 2.B.4	2.0d	18-Mar-26	19-Mar-26	58.0d
900	GI-FS-A2-7230	Backfill - Deep UG Sanitary - Plumber - Area 2.B.3	2.0d	18-Mar-26	19-Mar-26	58.0d
901	GI-FS-A2-6640	Inspect - Deep UG LV Conduit - Low Voltage - Area 2.B	2.0d	19-Mar-26	20-Mar-26	21.0d
902	WBS - Deep Underground MEP - Area 1		16.0d	6-Jan-26	27-Jan-26	65.0d
903	GI-FS-A1-7070	Excavate - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	6-Jan-26	14-Jan-26	30.0d
904	GI-FS-A1-5650	Excavate - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	6-Jan-26	14-Jan-26	65.0d
905	GI-FS-A1-7080	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	15-Jan-26	23-Jan-26	30.0d
906	GI-FS-A1-5710	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	15-Jan-26	23-Jan-26	65.0d
907	GI-FS-A1-7090	Inspect - Deep UG Sanitary - Plumber - Area 1.1B	2.0d	22-Jan-26	23-Jan-26	30.0d
908	GI-FS-A1-5750	Inspect - Deep UG Sanitary - Plumber - Area 1.1A	2.0d	22-Jan-26	23-Jan-26	65.0d
909	GI-FS-A1-7100	Backfill - Deep UG Sanitary - Plumber - Area 1.1B	2.0d	26-Jan-26	27-Jan-26	30.0d
910	GI-FS-A1-5770	Backfill - Deep UG Sanitary - Plumber - Area 1.1A	2.0d	26-Jan-26	27-Jan-26	65.0d
911	WBS - Deep Underground MEP - Area 6		50.0d	16-Jan-26	26-Mar-26	140.0d
912	GI-FS-A6-5690	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.4	6.0d	16-Jan-26	23-Jan-26	129.0d
913	GI-FS-A6-5720	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.4	4.0d	26-Jan-26	29-Jan-26	129.0d
914	GI-FS-A6-5730	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.4	2.0d	28-Jan-26	29-Jan-26	129.0d
915	GI-FS-A6-5740	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.4	5.0d	30-Jan-26	5-Feb-26	129.0d
916	GI-FS-A6-5870	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.2	6.0d	6-Feb-26	13-Feb-26	150.0d
917	GI-FS-A6-6080	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.1	4.0d	6-Feb-26	11-Feb-26	129.0d
918	GI-FS-A6-6100	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.1	3.0d	12-Feb-26	16-Feb-26	129.0d
919	GI-FS-A6-6150	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.1	2.0d	13-Feb-26	16-Feb-26	129.0d
920	GI-FS-A6-5910	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.2	6.0d	16-Feb-26	23-Feb-26	150.0d
921	GI-FS-A6-6160	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.1	4.0d	17-Feb-26	20-Feb-26	129.0d
922	GI-FS-A6-5950	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.2	2.0d	20-Feb-26	23-Feb-26	150.0d
923	GI-FS-A6-5960	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.2	7.0d	24-Feb-26	4-Mar-26	150.0d
924	GI-FS-A6-5920	Excavate - Deep UG Conduit - Elec. - Area 6.2	5.0d	5-Mar-26	11-Mar-26	106.0d

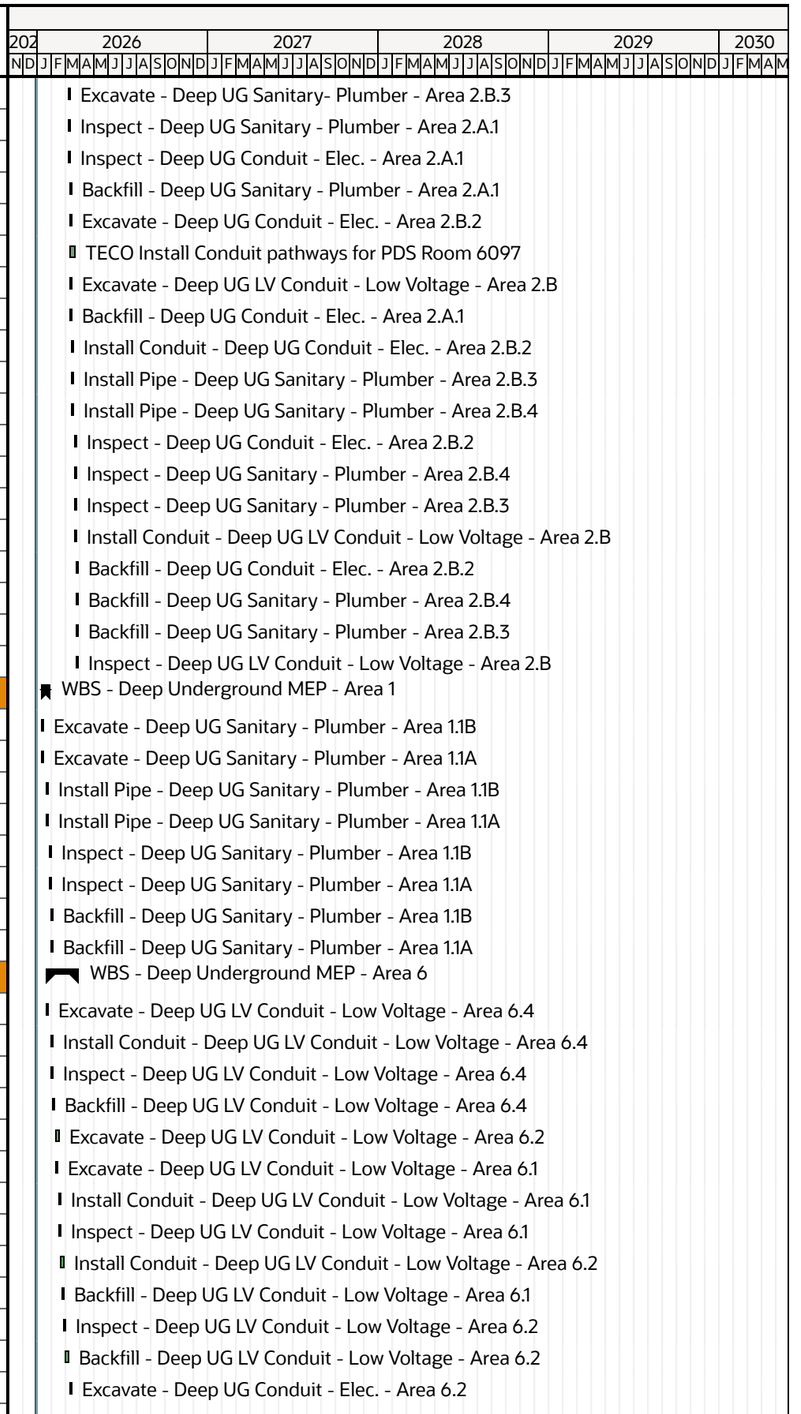

	ID	Name	Dur	Start	Finish	TF
925	GI-FS-A6-5990	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	5-Mar-26	6-Mar-26	150.0d
926	GI-FS-A6-6030	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	9-Mar-26	10-Mar-26	150.0d
927	GI-FS-A6-6040	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	9-Mar-26	10-Mar-26	150.0d
928	GI-FS-A6-6530	Excavate - Deep UG Sanitary - Plumber - Area 6.1	4.0d	10-Mar-26	13-Mar-26	108.0d
929	GI-FS-A6-6050	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	11-Mar-26	12-Mar-26	150.0d
930	GI-FS-A6-5940	Install Conduit - Deep UG Conduit - Elec. - Area 6.2	5.0d	12-Mar-26	18-Mar-26	106.0d
931	GI-FS-A6-6400	Excavate - Deep UG Conduit - Elec. - Area 6.1	5.0d	13-Mar-26	19-Mar-26	100.0d
932	GI-FS-A6-6550	Install Pipe - Deep UG Sanitary - Plumber - Area 6.1	4.0d	16-Mar-26	19-Mar-26	108.0d
933	GI-FS-A6-5970	Inspect - Deep UG Conduit - Elec. - Area 6.2	2.0d	17-Mar-26	18-Mar-26	106.0d
934	GI-FS-A6-6570	Inspect - Deep UG Sanitary - Plumber - Area 6.1	2.0d	18-Mar-26	19-Mar-26	108.0d
935	GI-FS-A6-5980	Backfill - Deep UG Conduit - Elec. - Area 6.2	5.0d	19-Mar-26	25-Mar-26	106.0d
936	GI-FS-A6-6430	Install Conduit - Deep UG Conduit - Elec. - Area 6.1	5.0d	20-Mar-26	26-Mar-26	100.0d
937	GI-FS-A6-6580	Backfill - Deep UG Sanitary - Plumber - Area 6.1	2.0d	20-Mar-26	23-Mar-26	108.0d
938	GI-FS-A6-6460	Inspect - Deep UG Conduit - Elec. - Area 6.1	2.0d	25-Mar-26	26-Mar-26	100.0d
939	WBS - Deep Underground MEP - Area 3		15.0d	10-Feb-26	2-Mar-26	71.0d
940	GI-FS-A3-6840	Directional Bore to Anchor Tenant Operations Area for Temp Power	5.0d	10-Feb-26	16-Feb-26	71.0d
941	GI-FS-A3-6830	Pull Feeders/Set Transformers/Temp Panels Power On	10.0d	17-Feb-26	2-Mar-26	71.0d
942	WBS - Civil		61.0d	29-Dec-25	24-Mar-26	359.0d
943	WBS - Truck Court		25.0d	18-Feb-26	24-Mar-26	359.0d
944	WBS - Underground Utilities - Truck Court		25.0d	18-Feb-26	24-Mar-26	359.0d
945	WBS - Pipe Bursting		25.0d	18-Feb-26	24-Mar-26	359.0d
946	UND-PB-2710	Mobilize - Pipe Bursting	25.0d	18-Feb-26	24-Mar-26	359.0d
947	WBS - Performance Park North Craft Parking Lot		60.0d	29-Dec-25	23-Mar-26	105.0d
948	CP-FS-150	Layout/Survey - PP North Craft Parking Lot	3.0d	29-Dec-25	31-Dec-25	72.0d
949	CP-FS-160	Install BMP SWPPP Measures - PP North Craft Parking Lot	5.0d	2-Jan-26	8-Jan-26	72.0d
950	CP-FS-170	Install Dust Control Measure - Wheel/Tire Wash - PP North Craft Parking Lot	2.0d	9-Jan-26	12-Jan-26	72.0d
951	CP-FS-200	Demolish Fencing - PP North Craft Parking Lot	5.0d	13-Jan-26	19-Jan-26	72.0d
952	CP-FS-140	Removal of Unsuitable Material - PP North Craft Parking Lot	10.0d	20-Jan-26	2-Feb-26	72.0d
953	CP-FS-190	Remove & Relocate P219 Stockpile - PP North Craft Parking Lot	10.0d	3-Feb-26	16-Feb-26	72.0d
954	CP-FS-350	Remove Existing Stockpiles/Unsuitable Material East of Performance Park - PP ...	10.0d	17-Feb-26	2-Mar-26	115.0d
955	CP-FS-210	Clear & Grub Remaining Debris & Vegetation - PP North Craft Parking Lot	5.0d	17-Feb-26	23-Feb-26	72.0d
956	CP-FS-220	Cut Existing Grade & Level to Base Elevation - PP North Craft Parking Lot	10.0d	24-Feb-26	9-Mar-26	72.0d
957	CP-FS-360	Restore Vegetation East of Performance Park - PP North Craft Parking Lot	5.0d	3-Mar-26	9-Mar-26	115.0d
958	CP-FS-250	Fill & Compact Subgrade Layer - PP North Craft Parking Lot	10.0d	10-Mar-26	23-Mar-26	72.0d
959	CP-FS-230	Install Base - Conex Laydown Area - PP North Craft Parking Lot	5.0d	10-Mar-26	16-Mar-26	72.0d
960	CP-FS-240	Install 8" Base W/Grid - ITB Laydown Area - PP North Craft Parking Lot	5.0d	17-Mar-26	23-Mar-26	72.0d
961	WBS - Invitation To Bid (ITB)		844.0d	19-Jun-25 A	15-Oct-28	106.0d
962	WBS - ITB -1 - Apron Pavement & Hydrant Fueling Construction		844.0d	19-Jun-25 A	15-Oct-28	106.0d
963	WBS - Inter Project Relationships (IPR)		844.0d	19-Jun-25 A	15-Oct-28	106.0d
964	IPR-ITB1-MLS31	ITB1 Overall Project Duration SC 9.30.2028	1,187.0d	19-Jun-25 A	15-Oct-28 C	148.0d
965	IPR-ITB1-MLS20	MLS20 - Fuel Main Install Complete (Crisdel)	0.0d		30-Jan-26 C	0.0d
966	WBS - ITB - 3 - Guideway Superstructure Construction		395.0d	25-Aug-25 A	16-Mar-27	121.0d

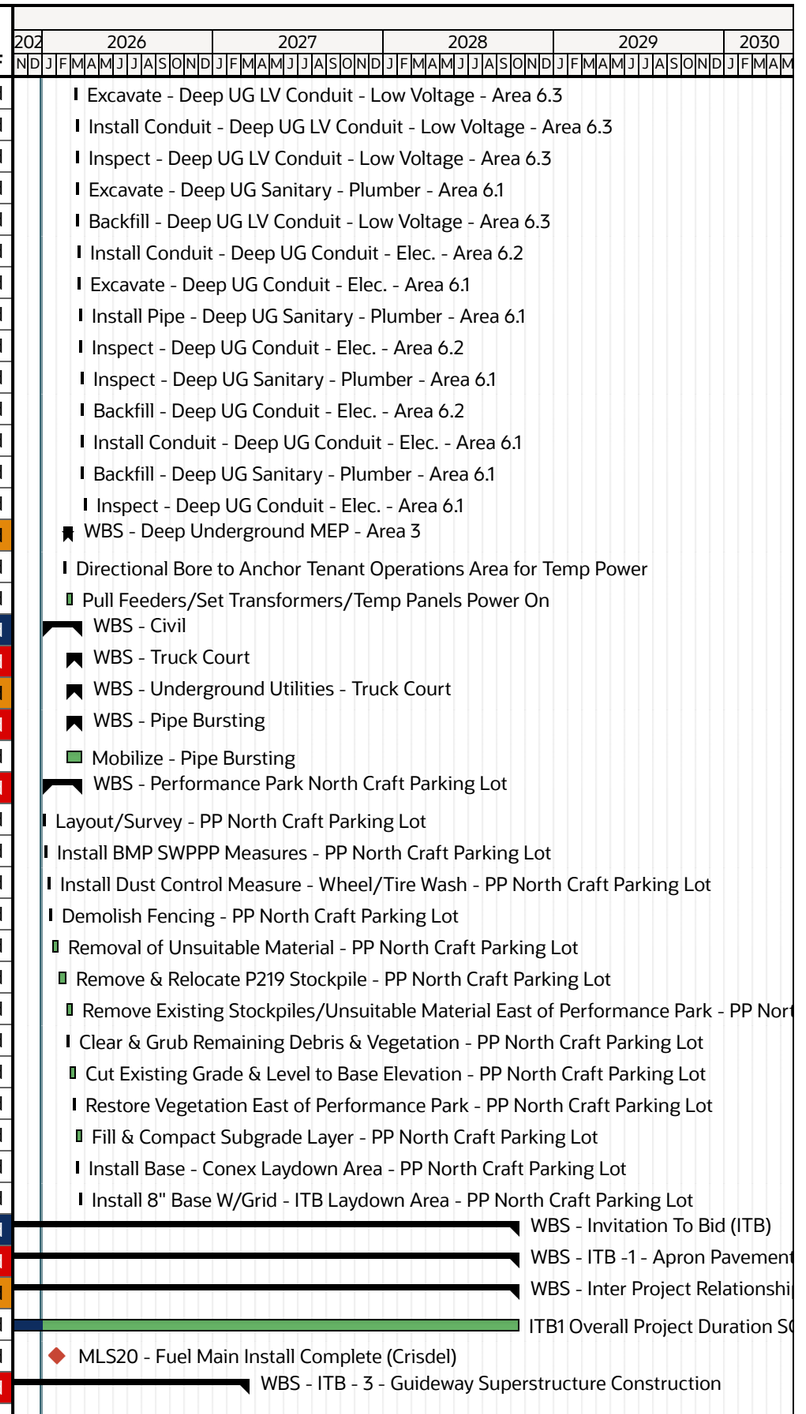


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
90 Day Look Ahead Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:55 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
967	WBS - Inter Project Relationships (IPR)		395.0d	25-Aug-25 A	16-Mar-27	121.0d
968	IPR-ASD-ITB3-210	ITB 3 - Total Project Duration SC 2.16.2027 (By Others)	556.0d	25-Aug-25 A	16-Mar-27	169.0d
969	IPR-ASD-ITB3-90	ITB 3 - Pier 2 Drilled Shafts (By Others)	14.0d	4-Feb-26 C	23-Feb-26	272.0d
970	IPR-ASD-ITB3-140	ITB 3 - Pier 1 Drilled Shafts (By Others)	11.0d	24-Feb-26 C	10-Mar-26	272.0d
971	WBS - ASD - COMMISSIONING PHASE		50.0d	29-Dec-25	9-Mar-26	785.0d
972	WBS - ASD - Commissioning - Administrative		50.0d	29-Dec-25	9-Mar-26	785.0d
973	COM-ADM-100	Develop & Submit Cx Plan (Design) - Admin Commissioning	15.0d	29-Dec-25	19-Jan-26	785.0d
974	COM-ADM-110	Review & Approve Cx Plan (Design) - Admin Commissioning	20.0d	20-Jan-26	16-Feb-26	785.0d
975	COM-ADM-120	Approved Sequence of Operations - Admin Commissioning	0.0d		16-Feb-26	785.0d
976	COM-ADM-130	Develop & Submit Cx Plan (Construction) - Admin Commissioning	15.0d	17-Feb-26	9-Mar-26	785.0d
977	WBS - CENTRALIZED CHECKED BAGGAGE SYSTEM RELOCATION AND UPGRADES		481.0d	20-Oct-25 A	10-Sep-27	642.0d
978	WBS - CCBS - PROCUREMENT PHASE		110.0d	20-Oct-25 A	26-Mar-26	1,013.0d
979	WBS - Owner Furnished Contractor Installed (OFCI)		61.0d	14-Nov-25 A	12-Feb-26	81.0d
980	WBS - Tag & Trace Submittals		61.0d	14-Nov-25 A	12-Feb-26	81.0d
981	WBS - Low Volt Tag & Trace Submittals		61.0d	14-Nov-25 A	12-Feb-26	81.0d
982	A64150	Prep & Submit Product Data for Low Voltage Tag & Trace Relocation	31.0d	14-Nov-25 A	31-Dec-25	81.0d
983	A106450	Review & Approve (HP) Product Data for Low Voltage Tag & Trace Relocation	5.0d	2-Jan-26	8-Jan-26	81.0d
984	A64160	Review & Approve (HNTB) Product Data for Low Voltage Tag & Trace Relocation	10.0d	9-Jan-26	22-Jan-26	81.0d
985	A64170	HCAA Review & Approve Product Data for Low Voltage Tag & Trace Relocation	15.0d	23-Jan-26	12-Feb-26	81.0d
986	WBS - Contractor Furnished & Install (CFCI)		110.0d	20-Oct-25 A	26-Mar-26	1,013.0d
987	WBS - Part 2 Supplement B - Centralized Checked Baggage Etc.		107.0d	20-Oct-25 A	23-Mar-26	1,016.0d
988	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supp. B		107.0d	20-Oct-25 A	23-Mar-26	1,016.0d
989	WBS - General BHS Submittals & Procurement - Part 2 Supp. B		82.0d	20-Oct-25 A	16-Feb-26	773.0d
990	WBS - System Inspection, Functional Specification, and Test Plan Submittals		61.0d	18-Nov-25 A	16-Feb-26	135.0d
991	D1056	Prep & Submit System Inspection, Functional Specification, & Test Plan	31.0d	18-Nov-25 A	5-Jan-26	135.0d
992	A101440	Review & Approve (HP) System Inspection, Functional Specification, & Test Plan	5.0d	6-Jan-26	12-Jan-26	135.0d
993	A106430	Review & Approve (HNTB) System Inspection, Functional Specification, & Test ...	10.0d	13-Jan-26	26-Jan-26	135.0d
994	D1061	Review & Approve (HCAA) System Inspection, Functional Specification, & Test ...	15.0d	27-Jan-26	16-Feb-26	135.0d
995	WBS - Quality Control Manual Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	139.0d
996	A101190	Prep & Submit Quality Control Manual	48.0d	20-Oct-25 A	29-Dec-25	139.0d
997	A101380	Review & Approve (HP) Quality Control Manual	5.0d	30-Dec-25	6-Jan-26	139.0d
998	A106570	Review & Approve (HNTB) Quality Control Manual	10.0d	7-Jan-26	20-Jan-26	139.0d
999	A106580	Review & Approve (HCAA) Quality Control Manual	15.0d	21-Jan-26	10-Feb-26	139.0d
1000	WBS - Environmental Requirements Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	777.0d
1001	A101290	Prep & Submit Environmental Requirements	48.0d	20-Oct-25 A	29-Dec-25	777.0d
1002	A101430	Review & Approve (HP) Environmental Requirements	5.0d	30-Dec-25	6-Jan-26	777.0d
1003	A106610	Review & Approve (HNTB) Environmental Requirements	10.0d	7-Jan-26	20-Jan-26	777.0d
1004	A106620	Review & Approve (HCAA) Environmental Requirements	15.0d	21-Jan-26	10-Feb-26	777.0d
1005	WBS - Project Organizational Chart & Management Team Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	118.0d
1006	A101280	Prep & Submit Project Organizational Chart & Management Team	48.0d	20-Oct-25 A	29-Dec-25	118.0d
1007	A101370	Review & Approve (HP) Project Organizational Chart & Management Team	5.0d	30-Dec-25	6-Jan-26	118.0d
1008	A106630	Review & Approve (HNTB) Project Organizational Chart & Management Team	10.0d	7-Jan-26	20-Jan-26	118.0d

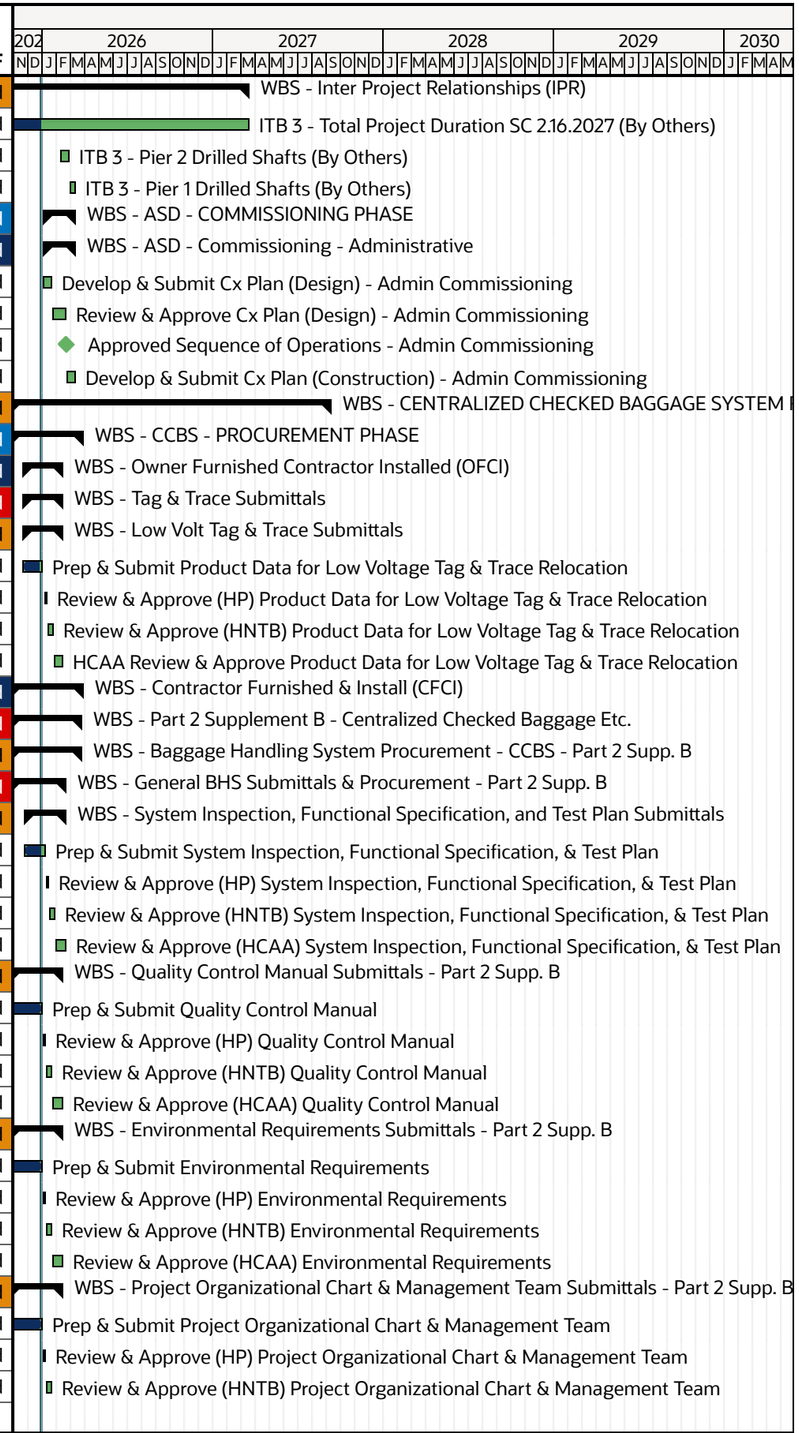


	ID	Name	Dur	Start	Finish	TF
1009	A106640	Review & Approve (HCAA) Project Organizational Chart & Management Team	15.0d	21-Jan-26	10-Feb-26	118.0d
1010	WBS - Detailed Master Schedule Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	118.0d
1011	A101220	Prep & Submit Detailed Master Schedule	48.0d	20-Oct-25 A	29-Dec-25	118.0d
1012	A101420	Review & Approve (HP) Detailed Master Schedule	5.0d	30-Dec-25	6-Jan-26	118.0d
1013	A106670	Review & Approve (HNTB) Detailed Master Schedule	10.0d	7-Jan-26	20-Jan-26	118.0d
1014	A106680	Review & Approve (HCAA) Detailed Master Schedule	15.0d	21-Jan-26	10-Feb-26	118.0d
1015	WBS - Phasing Schedule Submittals - Part 2 Supp. B		61.0d	18-Nov-25 A	16-Feb-26	114.0d
1016	A101270	Prep & Submit Phasing Schedule	31.0d	18-Nov-25 A	5-Jan-26	114.0d
1017	A101410	Review & Approve (HP) Phasing Schedule	5.0d	6-Jan-26	12-Jan-26	114.0d
1018	A106770	Review & Approve (HNTB) Phasing Schedule	10.0d	13-Jan-26	26-Jan-26	114.0d
1019	A106780	Review & Approve (HCAA) Phasing Schedule	15.0d	27-Jan-26	16-Feb-26	114.0d
1020	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supp. B		85.0d	18-Nov-25 A	20-Mar-26	216.0d
1021	WBS - General Mechanical BHS Submittals & Procurement - Part 2 Supp. B		81.0d	18-Nov-25 A	16-Mar-26	220.0d
1022	WBS - Mechanical Catalog Cut / Equipment Specs Submittals - Part 2 Supp. B		38.0d	9-Dec-25 A	2-Feb-26	0.0d
1023	A110550	Revise & Resubmit (Daifuku) Mech. Catalog Cut / Equip. Specs	13.0d	9-Dec-25 A	26-Dec-25 A	
1024	A110560	Review & Approve (HNTB) Mech. Catalog Cut / Equip. Specs	10.0d	29-Dec-25	12-Jan-26	0.0d
1025	D1083	Review & Approve (HCAA) Mech. Catalog Cut / Equip. Specs	15.0d	13-Jan-26	2-Feb-26	0.0d
1026	WBS - Motor Schedule Submittals - Part 2 Supp. B		61.0d	18-Nov-25 A	16-Feb-26	55.0d
1027	A101610	Prep & Submit Motor Schedule	31.0d	18-Nov-25 A	5-Jan-26	55.0d
1028	A106830	Review & Approve (HP) Motor Schedule	5.0d	6-Jan-26	12-Jan-26	55.0d
1029	A106840	Review & Approve (HNTB) Motor Schedule	10.0d	13-Jan-26	26-Jan-26	55.0d
1030	A101660	Review & Approve (HCAA) Motor Schedule	15.0d	27-Jan-26	16-Feb-26	55.0d
1031	WBS - CBRA Egress Pathway Landing Submittals - Part 2 Supp. B		50.0d	6-Jan-26	16-Mar-26	220.0d
1032	A101580	Prep & Submit CBRA Egress Pathway Landing	20.0d	6-Jan-26	2-Feb-26	220.0d
1033	A101670	Review & Approve (HP) CBRA Egress Pathway Landing	5.0d	3-Feb-26	9-Feb-26	220.0d
1034	A106850	Review & Approve (HNTB) CBRA Egress Pathway Landing	10.0d	10-Feb-26	23-Feb-26	220.0d
1035	A106860	Review & Approve (HCAA) CBRA Egress Pathway Landing	15.0d	24-Feb-26	16-Mar-26	220.0d
1036	WBS - General Mechanical Assembly Detail Drawings Submittals - Part 2 Supp. B		30.0d	5-Dec-25 A	19-Jan-26	0.0d
1037	D1084	Review & Approve (HCAA) General Mech. Assembly Detail Drawings	30.0d	5-Dec-25 A	19-Jan-26	0.0d
1038	WBS - Seq 1-Stage 1-Step 1 - Part 2 Supp. B		61.0d	18-Dec-25 A	16-Mar-26	0.0d
1039	WBS - BHS Mechanical Submittals [01-01-01]		61.0d	18-Dec-25 A	16-Mar-26	0.0d
1040	D1093	Review & Approve (HCAA) Mech Plan & Elev Dwg Set [01-01-01]	16.0d	18-Dec-25 A	12-Jan-26	0.0d
1041	D1095	Prep & Submit Header Steel Dwg Set [01-01-01]	10.0d	20-Jan-26	2-Feb-26	0.0d
1042	D3556	Review & Approve (HP) Header Steel Dwg Set [01-01-01]	5.0d	3-Feb-26	9-Feb-26	0.0d
1043	D3566	Review & Approve (HNTB) Header Steel Dwg Set [01-01-01]	10.0d	10-Feb-26	23-Feb-26	0.0d
1044	D1097	Review & Approve (HCAA) Header Steel Dwg Set [01-01-01]	15.0d	24-Feb-26	16-Mar-26	0.0d
1045	WBS - Seq 1 - Stage 1 - Step 2		67.0d	16-Dec-25 A	20-Mar-26	16.0d
1046	WBS - BHS Mechanical Submittals [01-01-02]		67.0d	16-Dec-25 A	20-Mar-26	16.0d
1047	D3576	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-02]	12.0d	16-Dec-25 A	2-Jan-26	16.0d
1048	D1102	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-02]	15.0d	5-Jan-26	23-Jan-26	16.0d
1049	D1103	Prep & Submit Header Steel Dwg Set [01-01-02]	10.0d	26-Jan-26	6-Feb-26	16.0d
1050	D3596	Review & Approve Header Steel Dwg Set (HP) [01-01-02]	5.0d	9-Feb-26	13-Feb-26	16.0d

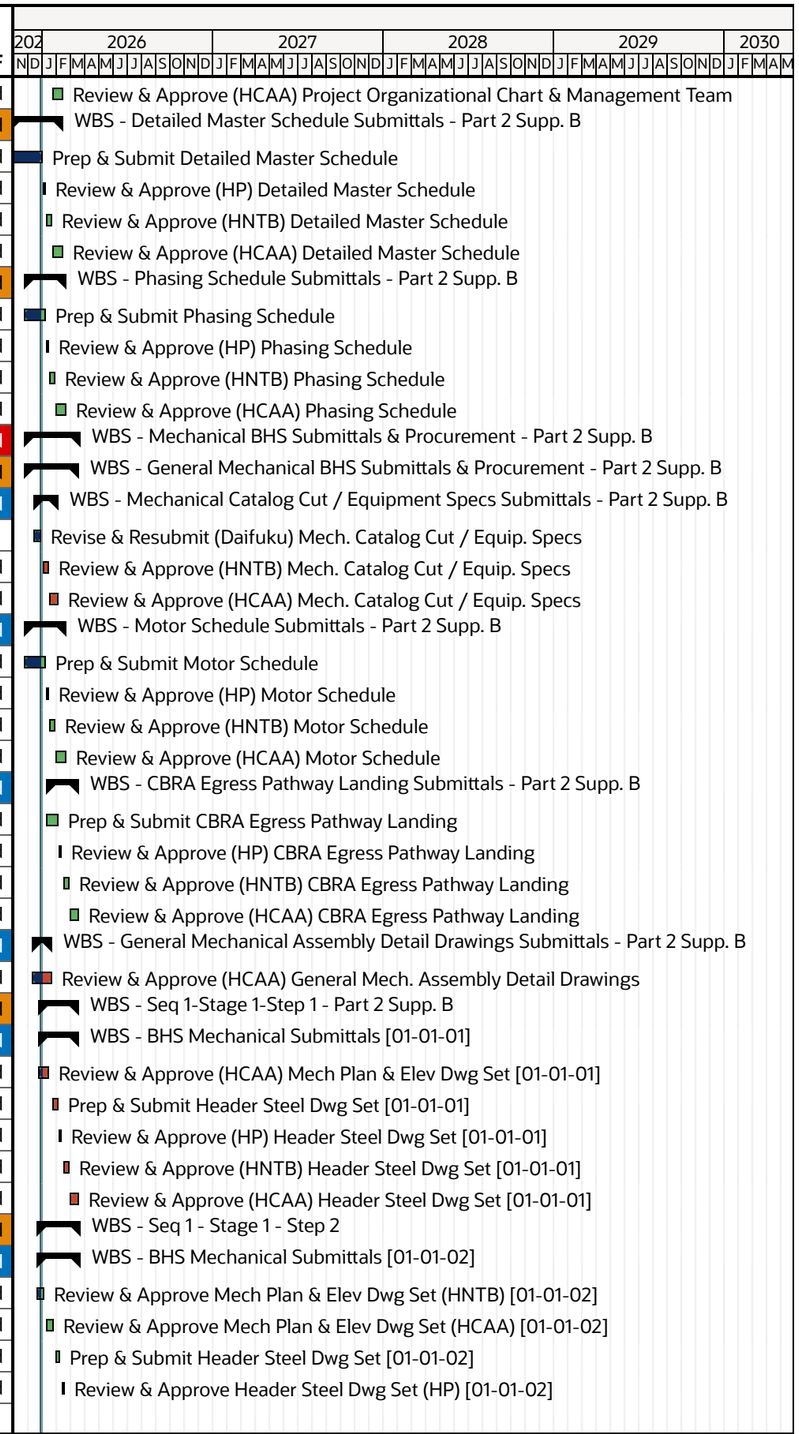


	ID	Name	Dur	Start	Finish	TF
1051	D3606	Review & Approve Header Steel Dwg Set (HNTB) [01-01-02]	10.0d	16-Feb-26	27-Feb-26	16.0d
1052	D1105	Review & Approve Header Steel Dwg Set (HCAA) [01-01-02]	15.0d	2-Mar-26	20-Mar-26	16.0d
1053	WBS - Seq 1 - Stage 1 - Step 3		57.0d	16-Dec-25 A	6-Mar-26	21.0d
1054	WBS - BHS Mechanical Submittals [01-01-03]		57.0d	16-Dec-25 A	6-Mar-26	21.0d
1055	D3626	Review & Approve Mech Plan & Elev Dwg Set (HNTB)t [01-01-03]	12.0d	16-Dec-25 A	2-Jan-26	21.0d
1056	D1109	Review & Approve Mech Plan & Elev Dwg Set (HCAA)t [01-01-03]	15.0d	5-Jan-26	23-Jan-26	21.0d
1057	D1110	Prep & Submit Header Steel Dwg Sett [01-01-03]	10.0d	26-Jan-26	6-Feb-26	21.0d
1058	D3636	Review & Approve Header Steel Dwg Set (HP)t [01-01-03]	10.0d	9-Feb-26	20-Feb-26	21.0d
1059	D3646	Review & Approve Header Steel Dwg Set (HNTB)t [01-01-03]	10.0d	23-Feb-26	6-Mar-26	21.0d
1060	WBS - Seq 1 - Stage 1 - Step 4		67.0d	16-Dec-25 A	20-Mar-26	38.0d
1061	WBS - BHS Mechanical Submittals [01-01-04]		67.0d	16-Dec-25 A	20-Mar-26	38.0d
1062	D3666	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-04]	12.0d	16-Dec-25 A	2-Jan-26	18.0d
1063	D1116	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-04]	15.0d	5-Jan-26	23-Jan-26	18.0d
1064	D1117	Prep & Submit Header Steel Dwg Set [01-01-04]	10.0d	26-Jan-26	6-Feb-26	38.0d
1065	D3676	Review & Approve Header Steel Dwg Set (HP) [01-01-04]	5.0d	9-Feb-26	13-Feb-26	38.0d
1066	D3686	Review & Approve Header Steel Dwg Set (HNTB) [01-01-04]	10.0d	16-Feb-26	27-Feb-26	38.0d
1067	D1120	Review & Approve Header Steel Dwg Set (HCAA) [01-01-04]	15.0d	2-Mar-26	20-Mar-26	38.0d
1068	WBS - Seq 1 - Stage 1 - Step 5		45.0d	29-Dec-25	2-Mar-26	25.0d
1069	WBS - BHS Mechanical Submittals [01-01-05]		45.0d	29-Dec-25	2-Mar-26	25.0d
1070	D1123	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-05]	15.0d	29-Dec-25	19-Jan-26	6.0d
1071	D3696	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-05]	5.0d	20-Jan-26	26-Jan-26	25.0d
1072	D3706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-05]	10.0d	27-Jan-26	9-Feb-26	25.0d
1073	D1124	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-05]	15.0d	10-Feb-26	2-Mar-26	25.0d
1074	WBS - Seq 1 - Stage 2 - Step 1		35.0d	20-Jan-26	9-Mar-26	6.0d
1075	WBS - BHS Mechanical Submittals [01-02-01]		35.0d	20-Jan-26	9-Mar-26	6.0d
1076	D1128	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-01]	20.0d	20-Jan-26	16-Feb-26	6.0d
1077	D3716	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-01]	5.0d	17-Feb-26	23-Feb-26	6.0d
1078	D3726	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-01]	10.0d	24-Feb-26	9-Mar-26	6.0d
1079	WBS - Seq 1 - Stage 2 - Step 2		35.0d	20-Jan-26	9-Mar-26	11.0d
1080	WBS - BHS Mechanical Submittals [01-02-02]		35.0d	20-Jan-26	9-Mar-26	11.0d
1081	D1135	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-02]	20.0d	20-Jan-26	16-Feb-26	11.0d
1082	D3756	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-02]	5.0d	17-Feb-26	23-Feb-26	11.0d
1083	D3766	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-02]	10.0d	24-Feb-26	9-Mar-26	11.0d
1084	WBS - Seq 1 - Stage 2 - Step 3		35.0d	20-Jan-26	9-Mar-26	31.0d
1085	WBS - BHS Mechanical Submittals [01-02-03]		35.0d	20-Jan-26	9-Mar-26	31.0d
1086	D1142	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-03]	20.0d	20-Jan-26	16-Feb-26	30.0d
1087	D3796	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-03]	5.0d	17-Feb-26	23-Feb-26	31.0d
1088	D3806	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-03]	10.0d	24-Feb-26	9-Mar-26	31.0d
1089	WBS - Seq 1 - Stage 2 - Step 4		40.0d	20-Jan-26	16-Mar-26	30.0d
1090	WBS - BHS Mechanical Submittals [01-02-04]		40.0d	20-Jan-26	16-Mar-26	30.0d
1091	D1149	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-04]	20.0d	20-Jan-26	16-Feb-26	30.0d
1092	D3836	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-04]	10.0d	17-Feb-26	2-Mar-26	30.0d

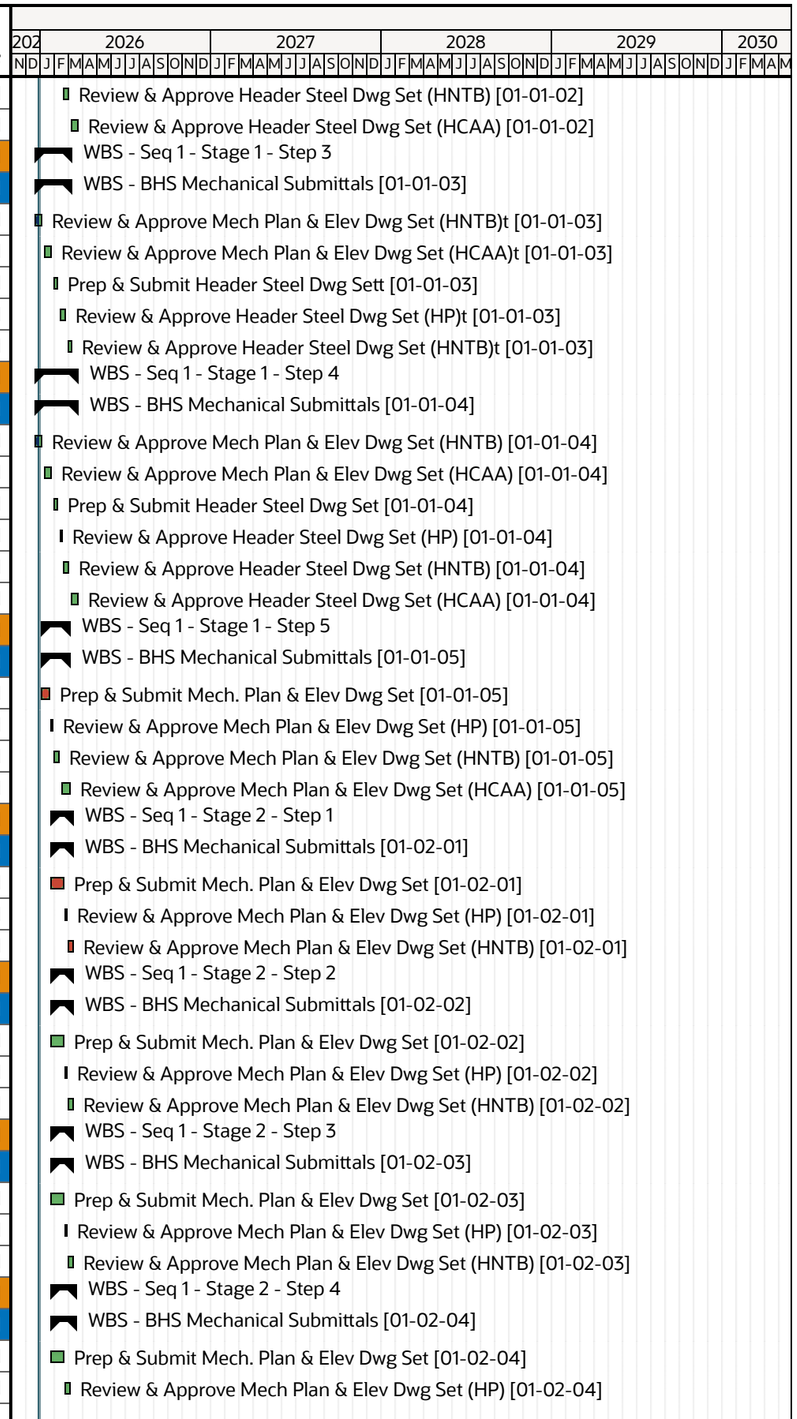


	ID	Name	Dur	Start	Finish	TF
1093	D3846	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-04]	10.0d	3-Mar-26	16-Mar-26	30.0d
1094	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		101.0d	28-Oct-25 A	23-Mar-26	1,016.0d
1095	WBS - General Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		101.0d	28-Oct-25 A	23-Mar-26	1,016.0d
1096	WBS - Operator Interface / Control Station Typicals Submittals		45.0d	29-Dec-25	2-Mar-26	1,031.0d
1097	A101900	Prep & Submit Operator Interface / Control Station Typicals	15.0d	29-Dec-25	19-Jan-26	1,030.0d
1098	A107240	Review & Approve (HP) Operator Interface / Control Station Typicals	5.0d	20-Jan-26	26-Jan-26	1,030.0d
1099	A107250	Review & Approve (HNTB) Operator Interface / Control Station Typicals	10.0d	27-Jan-26	9-Feb-26	1,030.0d
1100	A102030	Review & Approve (HCAA) Operator Interface / Control Station Typicals	15.0d	10-Feb-26	2-Mar-26	1,030.0d
1101	WBS - Cross-Belt Sorter XBM2 Elect Drawing Sets Submittals		32.0d	29-Dec-25	11-Feb-26	495.0d
1102	A92270	Prep & Submit Cross-Belt Sorter XBM2 Elect Drawing Sets	1.0d	29-Dec-25	29-Dec-25	416.0d
1103	A107280	Review & Approve (HP) Cross-Belt Sorter XBM2 Elect Dwg Sets	5.0d	30-Dec-25	6-Jan-26	416.0d
1104	A107290	Review & Approve (HNTB) Cross-Belt Sorter XBM2 Elect Dwg Sets	10.0d	7-Jan-26	20-Jan-26	416.0d
1105	A92280	Review & Approve (HCAA) Cross-Belt Sorter XBM2 Elect Dwg Sets	15.0d	21-Jan-26	10-Feb-26	416.0d
1106	A92890	Fab./ Del XBM2 Field Control Panels (?), Elect Field Devices, Cabling	1.0d	11-Feb-26	11-Feb-26	495.0d
1107	WBS - Electrical Installation Catalog Cuts & Equipment Specs Submittals		77.0d	28-Oct-25 A	17-Feb-26	368.0d
1108	A101910	Prep & Submit Elec. Install Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	368.0d
1109	A107300	Review & Approve (HP) Elec.Install Catalog Cuts & Equip. Specs	10.0d	30-Dec-25	13-Jan-26	368.0d
1110	A107310	Review & Approve (HNTB) Elec. Install Catalog Cuts & Equip. Specs	10.0d	14-Jan-26	27-Jan-26	368.0d
1111	A102010	Review & Approve (HCAA) Elec. Install Catalog Cuts & Equip. Specs	15.0d	28-Jan-26	17-Feb-26	368.0d
1112	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		72.0d	28-Oct-25 A	10-Feb-26	373.0d
1113	A101930	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	373.0d
1114	A101990	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
1115	A107320	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
1116	A107330	Review & Approve (HCAA) Elec. / Controls / Computer Catalog Cuts & Equip. S...	15.0d	21-Jan-26	10-Feb-26	373.0d
1117	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		45.0d	29-Dec-25	2-Mar-26	973.0d
1118	A101890	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	29-Dec-25	19-Jan-26	972.0d
1119	A102020	Review & Approve (HP) ATR / BMA Catalog Cuts & Equip. Specs	5.0d	20-Jan-26	26-Jan-26	972.0d
1120	A107340	Review & Approve (HNTB) ATR / BMA Catalog Cuts & Equip. Specs	10.0d	27-Jan-26	9-Feb-26	972.0d
1121	A107350	Review & Approve (HCAA) ATR / BMA Catalog Cuts & Equip. Specs	15.0d	10-Feb-26	2-Mar-26	972.0d
1122	WBS - Lower-Level Network Architecture Drawings Submittals		60.0d	29-Dec-25	23-Mar-26	89.0d
1123	A101920	Prep & Submit Lower-Level Network Architecture Drawings	30.0d	29-Dec-25	9-Feb-26	89.0d
1124	A107370	Review & Approve (HP) Lower-Level Network Architecture Drawings	5.0d	10-Feb-26	16-Feb-26	89.0d
1125	A107360	Review & Approve (HNTB) Lower-Level Network Architecture Drawings	10.0d	17-Feb-26	2-Mar-26	89.0d
1126	A102080	Review & Approve (HCAA) Lower-Level Network Architecture Drawings	15.0d	3-Mar-26	23-Mar-26	89.0d
1127	WBS - Factory Acceptance Test Plan & Agenda Submittals		45.0d	29-Dec-25	2-Mar-26	596.0d
1128	A101870	Prep & Submit Factory Acceptance Test Plan & Agenda [40 days prior to FAT da...	15.0d	29-Dec-25	19-Jan-26	596.0d
1129	A102050	Review & Approve (HP) Factory Acceptance Test Plan & Agenda	5.0d	20-Jan-26	26-Jan-26	596.0d
1130	A107380	Review & Approve (HNTB) Factory Acceptance Test Plan & Agenda	10.0d	27-Jan-26	9-Feb-26	596.0d
1131	A107390	Review & Approve (HCAA) Factory Acceptance Test Plan & Agenda	15.0d	10-Feb-26	2-Mar-26	596.0d
1132	WBS - Upper-Level Network Architecture Drawings Submittals		60.0d	29-Dec-25	23-Mar-26	384.0d
1133	A101880	Prep & Submit Upper-Level Network Architecture Drawings	30.0d	29-Dec-25	9-Feb-26	384.0d
1134	A102070	Review & Approve (HP) Upper-Level Network Architecture Drawings	5.0d	10-Feb-26	16-Feb-26	384.0d

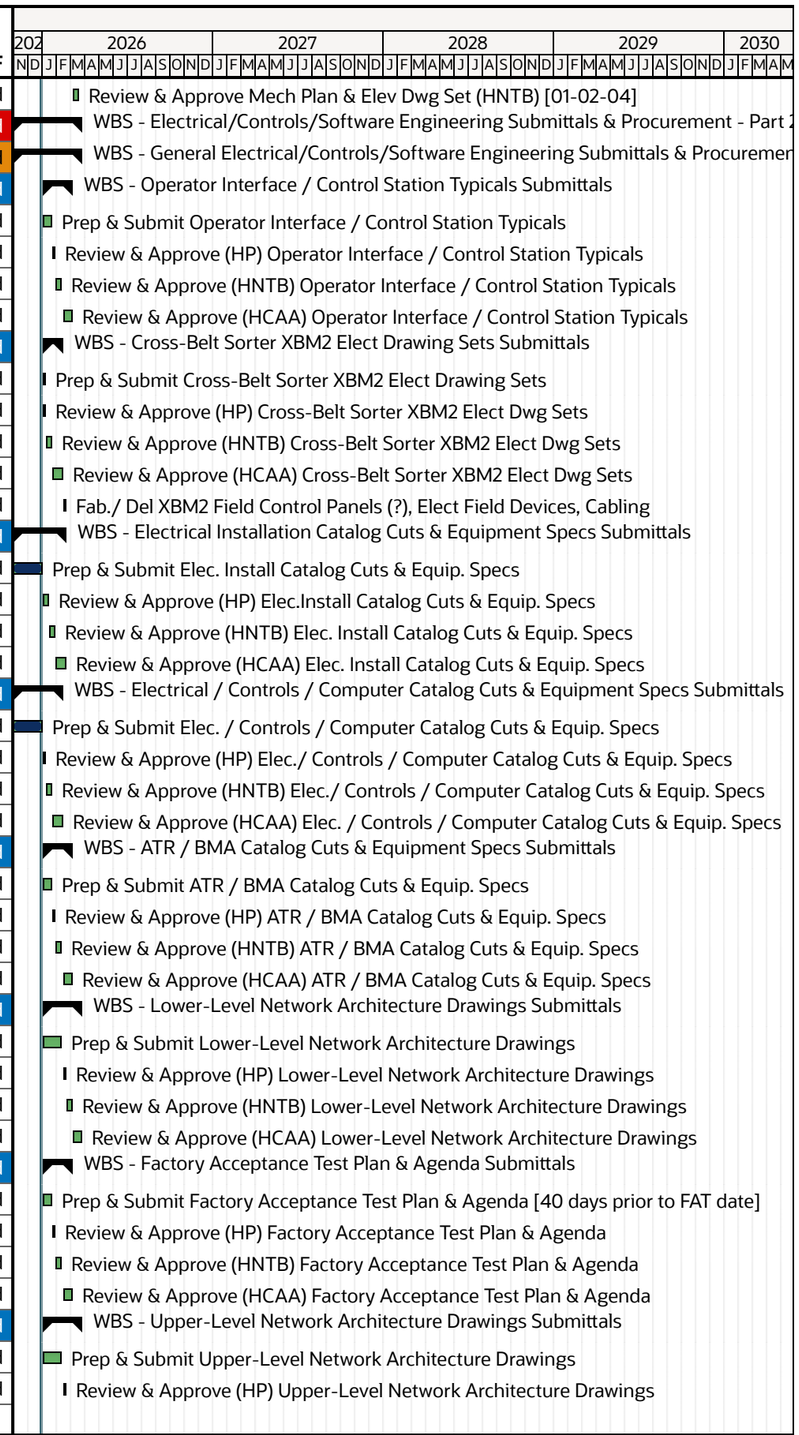


	ID	Name	Dur	Start	Finish	TF
1135	A107420	Review & Approve (HNTB) Upper-Level Network Architecture Drawings	10.0d	17-Feb-26	2-Mar-26	384.0d
1136	A107430	Review & Approve (HCAA) Upper-Level Network Architecture Drawings	15.0d	3-Mar-26	23-Mar-26	384.0d
1137	WBS - Cross-Belt Sorter Functional Specification Submittals		31.0d	29-Dec-25	10-Feb-26	600.0d
1138	A101840	Prep & Submit Cross-Belt Sorter Functional Specification	1.0d	29-Dec-25	29-Dec-25	600.0d
1139	A101980	Review & Approve (HP) Cross-Belt Sorter Functional Specification	5.0d	30-Dec-25	6-Jan-26	600.0d
1140	A107460	Review & Approve (HNTB) Cross-Belt Sorter Functional Specification	10.0d	7-Jan-26	20-Jan-26	600.0d
1141	A107470	Review & Approve (HCAA) Cross-Belt Sorter Functional Specification	15.0d	21-Jan-26	10-Feb-26	600.0d
1142	WBS - Cross-Belt Sorter Control System Description of Operations Submittals		31.0d	29-Dec-25	10-Feb-26	600.0d
1143	A101810	Prep & Submit Cross-Belt Sorter Control System Description of Operations	1.0d	29-Dec-25	29-Dec-25	600.0d
1144	A101970	Review & Approve (HP) Cross-Belt Sorter Control System Description of Operati...	5.0d	30-Dec-25	6-Jan-26	600.0d
1145	A107480	Review & Approve (HNTB) Cross-Belt Sorter Control System Description of Ope...	10.0d	7-Jan-26	20-Jan-26	600.0d
1146	A107490	Review & Approve (HCAA) Cross-Belt Sorter Control System Description of Ope...	15.0d	21-Jan-26	10-Feb-26	600.0d
1147	WBS - Power Requirements and MCP/MPP/CSC/FCP Sizes Submittals		60.0d	29-Dec-25	23-Mar-26	74.0d
1148	A101940	Prep & Submit Power Requirements & MCP/MPP/CSC/FCP Sizes	45.0d	29-Dec-25	2-Mar-26	14.0d
1149	A107520	Review & Approve (HP) Power Requirements & MCP/MPP/CSC/FCP Sizes	5.0d	3-Mar-26	9-Mar-26	74.0d
1150	A107530	Review & Approve (HNTB) Power Requirements & MCP/MPP/CSC/FCP Sizes	10.0d	10-Mar-26	23-Mar-26	74.0d
1151	WBS - Functional Specification Submittals		86.0d	18-Nov-25 A	23-Mar-26	80.0d
1152	A101960	Prep & Submit Functional Specification [180 days prior to pre-TRR]	86.0d	18-Nov-25 A	23-Mar-26	80.0d
1153	WBS - Cybersecurity Plan Submittals		50.0d	29-Dec-25	9-Mar-26	120.0d
1154	A101850	Prep & Submit Cybersecurity Plan [5 days prior to beneficial use by phase]	20.0d	29-Dec-25	26-Jan-26	120.0d
1155	A102060	Review & Approve (HP) Cybersecurity Plan	5.0d	27-Jan-26	2-Feb-26	120.0d
1156	A107600	Review & Approve (HNTB) Cybersecurity Plan	10.0d	3-Feb-26	16-Feb-26	120.0d
1157	A107610	Review & Approve (HCAA) Cybersecurity Plan	15.0d	17-Feb-26	9-Mar-26	120.0d
1158	WBS - Seq 1 - Stage 1 - Step 1		45.0d	29-Dec-25	2-Mar-26	64.0d
1159	D1695	Prep & Submit Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-B17 [01-01-...	15.0d	29-Dec-25	19-Jan-26	64.0d
1160	D5866	Review & Approve (HP) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-B1...	5.0d	20-Jan-26	26-Jan-26	64.0d
1161	D5876	Review & Approve (HNTB) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-...	10.0d	27-Jan-26	9-Feb-26	64.0d
1162	D1696	Review & Approve (HCAA) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-...	15.0d	10-Feb-26	2-Mar-26	64.0d
1163	WBS - Seq 1 - Stage 1 - Step 2		40.0d	20-Jan-26	16-Mar-26	80.0d
1164	D1698	Prep & Submit Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	10.0d	20-Jan-26	2-Feb-26	80.0d
1165	D5886	Review & Approve (HP) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	5.0d	3-Feb-26	9-Feb-26	80.0d
1166	D5896	Review & Approve (HNTB) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	10.0d	10-Feb-26	23-Feb-26	80.0d
1167	D1699	Review & Approve (HCAA) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	15.0d	24-Feb-26	16-Mar-26	80.0d
1168	WBS - Seq 1 - Stage 1 - Step 4		25.0d	3-Feb-26	9-Mar-26	92.0d
1169	D1701	Prep & Submit Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	10.0d	3-Feb-26	16-Feb-26	92.0d
1170	D5906	Review & Approve (HP) Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	5.0d	17-Feb-26	23-Feb-26	92.0d
1171	D5916	Review & Approve (HNTB) Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	10.0d	24-Feb-26	9-Mar-26	92.0d
1172	WBS - Seq 1 - Stage 2 - Step 1		25.0d	17-Feb-26	23-Mar-26	106.0d
1173	D1704	Prep & Submit Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	10.0d	17-Feb-26	2-Mar-26	106.0d
1174	D5926	Review & Approve (HP) Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	5.0d	3-Mar-26	9-Mar-26	106.0d
1175	D5936	Review & Approve (HNTB) Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	10.0d	10-Mar-26	23-Mar-26	106.0d
1176	WBS - Seq 1 - Stage 2 - Step 2		15.0d	3-Mar-26	23-Mar-26	106.0d

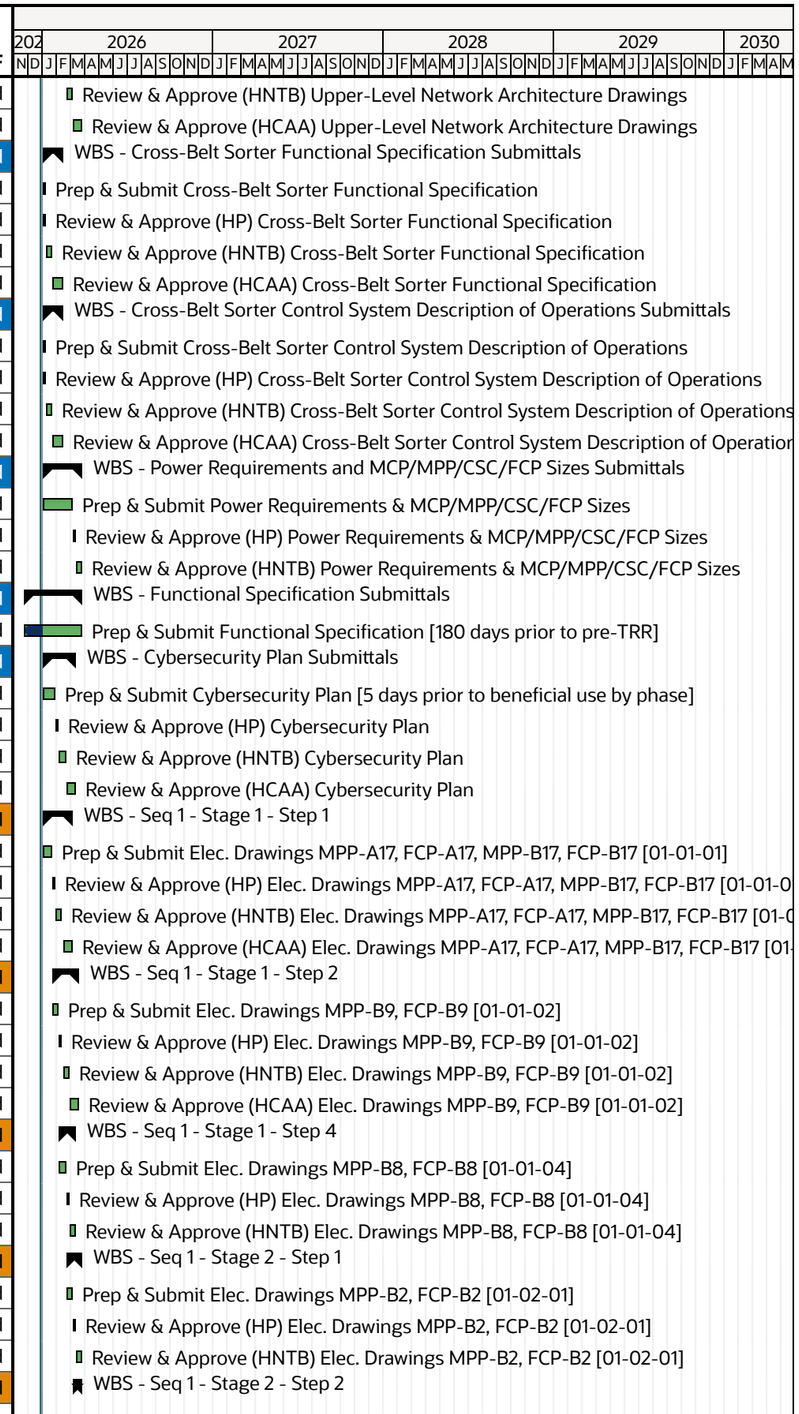


	ID	Name	Dur	Start	Finish	TF
1177	D1707	Prep & Submit Elec. Drawings MPP-A1, FCP-A1, MPP-A9, FCP-A9 [01-02-02]	15.0d	3-Mar-26	23-Mar-26	106.0d
1178	WBS - Electrical Long Lead System Procurement - CCBS - Part 2 Supp. B		35.0d	29-Dec-25	16-Feb-26	11.0d
1179	A108940	Prep & Submit Long Lead Elec. Equip. Submittals - Part 2 Supp. B	5.0d	29-Dec-25 C	5-Jan-26	11.0d
1180	A108950	Review & Approve (HP) Long Lead Elec.Equip. Submittals - Part 2 Supp. B	5.0d	6-Jan-26	12-Jan-26	11.0d
1181	A108960	Review & Approve (HNTB) Long Lead Elec. Equip. Submittals - Part 2 Supp. B	10.0d	13-Jan-26	26-Jan-26	11.0d
1182	A108970	Review & Approve (HCAA) Long Lead Elec. Equip. Submittals - Part 2 Supp. B	15.0d	27-Jan-26	16-Feb-26	11.0d
1183	WBS - Part 2 Supplement C Wave 1 - Core & Shell Procurement		63.0d	29-Dec-25	26-Mar-26	983.0d
1184	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supplement C Wave 1		48.0d	20-Jan-26	26-Mar-26	983.0d
1185	WBS - General BHS Submittals & Procurement - Part 2 Supplement C Wave 1		48.0d	20-Jan-26	26-Mar-26	983.0d
1186	WBS - O&M Training Plan & Proposed Agenda Submittals		45.0d	20-Jan-26	23-Mar-26	110.0d
1187	D1065	Prep & Submit O&M Training Plan & Proposed Agenda	15.0d	20-Jan-26	9-Feb-26	110.0d
1188	A101390	Review & Approve (HP) O&M Training Plan & Proposed Agenda	5.0d	10-Feb-26	16-Feb-26	110.0d
1189	A106390	Review & Approve (HNTB) O&M Training Plan & Proposed Agenda	10.0d	17-Feb-26	2-Mar-26	110.0d
1190	D1067	Review & Approve (HCAA) O&M Training Plan & Proposed Agenda	15.0d	3-Mar-26	23-Mar-26	110.0d
1191	WBS - Final Parts List Submittals		30.0d	13-Feb-26	26-Mar-26	983.0d
1192	A101210	Prep & Submit Final Parts List[90 days prior to beneficial use of Equip.]	30.0d	13-Feb-26	26-Mar-26	982.0d
1193	WBS - Configuration Management Plan Submittals		30.0d	13-Feb-26	26-Mar-26	548.0d
1194	A101170	Prep & Submit Configuration Management Plan	30.0d	13-Feb-26	26-Mar-26	548.0d
1195	WBS - Baggage Tag Verification Report Submittals		25.0d	13-Feb-26	19-Mar-26	568.0d
1196	D1049	Prep & Submit Baggage Tag Verification Report	10.0d	13-Feb-26	26-Feb-26	568.0d
1197	A101490	Review & Approve (HP) Baggage Tag Verification Report	5.0d	27-Feb-26	5-Mar-26	568.0d
1198	A106550	Review & Approve (HNTB) Baggage Tag Verification Report	10.0d	6-Mar-26	19-Mar-26	568.0d
1199	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supplement C Wave 1		30.0d	13-Feb-26	26-Mar-26	42.0d
1200	WBS - General Mechanical BHS Submittals & Procurement		30.0d	13-Feb-26	26-Mar-26	7.0d
1201	WBS - Cross Belt Mechanical Catalog Cut / Equipment Specs		30.0d	13-Feb-26	26-Mar-26	7.0d
1202	D1086	Prep & Submit Cross Belt Mech. Catalog Cut / Equip. Specs	15.0d	13-Feb-26	5-Mar-26	7.0d
1203	D3436	Review & Approve (HP) Cross Belt Mech. Catalog Cut / Equip. Specs	5.0d	6-Mar-26	12-Mar-26	7.0d
1204	D3446	Review & Approve (HNTB) Cross Belt Mech. Catalog Cut / Equip. Specs	10.0d	13-Mar-26	26-Mar-26	7.0d
1205	WBS - Seq 1 - Stage 3 - Step 1		30.0d	13-Feb-26	26-Mar-26	42.0d
1206	WBS - Seq 1 - Stage 3 - Step 1 - Sector J		30.0d	13-Feb-26	26-Mar-26	42.0d
1207	WBS - BHS Mechanical Submittals (Sector J) [01-03-01]		30.0d	13-Feb-26	26-Mar-26	42.0d
1208	D1168	Prep & Submit Mech. Plan & Elev Dwg Set (Sector J) [01-03-01]	25.0d	13-Feb-26	19-Mar-26	38.0d
1209	D3876	Review & Approve Mech Plan & Elev Dwg Set (HP) (Sector J) [01-03-01]	5.0d	20-Mar-26	26-Mar-26	42.0d
1210	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supplement C Wave 1		30.0d	13-Feb-26	26-Mar-26	563.0d
1211	WBS - General Electrical/Controls/Software Engineering Submittals & Procurement		30.0d	13-Feb-26	26-Mar-26	563.0d
1212	WBS - Cross-Belt Electrical Catalog Cut / Equipment Specs Submittals		30.0d	13-Feb-26	26-Mar-26	209.0d
1213	A91270	Prep & Submit Cross-Belt Elec Catalog Cut / Equip. Specs	15.0d	13-Feb-26	5-Mar-26	209.0d
1214	A91280	Review & Approve (HP) Cross-Belt Elec. Catalog Cut / Equip. Specs	5.0d	6-Mar-26	12-Mar-26	209.0d
1215	A106790	Review & Approve (HNTB) Cross-Belt Elec. Catalog Cut / Equip. Specs	10.0d	13-Mar-26	26-Mar-26	209.0d
1216	WBS - Factory Acceptance Test Plan & Agenda		30.0d	13-Feb-26	26-Mar-26	563.0d
1217	D1648	Prep & Submit Factory Acceptance Test Plan & Agenda	15.0d	13-Feb-26	5-Mar-26	563.0d
1218	D5966	HP Review & Approve Factory Acceptance Test Plan & Agenda	5.0d	6-Mar-26	12-Mar-26	563.0d

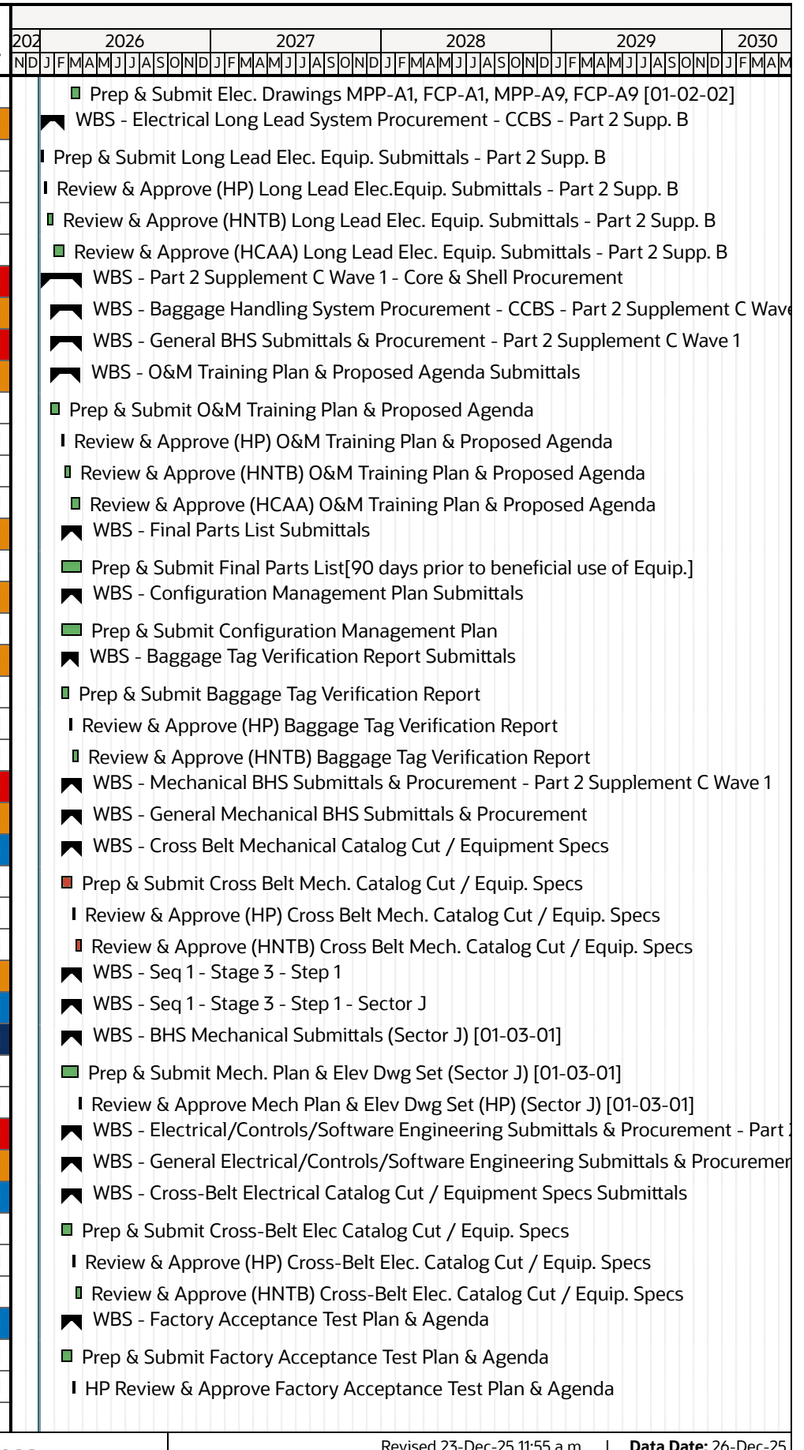


ID	Name	Dur	Start	Finish	TF
1219	D5976 HNTB Review & Approve Factory Acceptance Test Plan & Agenda	10.0d	13-Mar-26	26-Mar-26	563.0d
1220	WBS - Concrete Procurement SOG & SOMD - CCBS	30.0d	13-Feb-26	26-Mar-26	212.0d
1221	PR-P1-1C1-2480 Prep Concrete Submittal (Contractor)- CCBS	20.0d	13-Feb-26	12-Mar-26	212.0d
1222	PR-P1-1C1-2510 Review & Submit Concrete Submittal (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	212.0d
1223	WBS - Masonry Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	54.0d
1224	PR-P2-1C1-8030 Prep Masonry Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	54.0d
1225	WBS - Wall & Door Protection Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	949.0d
1226	PR-P2-1C1-8090 Prep Wall & Door Protection Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	948.0d
1227	WBS - Spray Fireproofing & Insulation (K-13) Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	913.0d
1228	PR-P1-1C1-2530 Prep Spray Fireproofing & Insulation Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	912.0d
1229	PR-P1-1C1-2810 Review & Submit Spray Fireproofing & Insulation Submittals (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	912.0d
1230	WBS - Drywall & Related Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	717.0d
1231	PR-P1-1C1-2610 Prep Drywall & Related Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	717.0d
1232	WBS - Acoustical Panel Ceilings Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	931.0d
1233	PR-P2-1C1-8580 Prep Acoustical Panel Ceiling Selective Demo Submittals (Contractor) - CCBS	5.0d	13-Feb-26	19-Feb-26	26.0d
1234	PR-P2-1C1-8220 Prep Acoustical Panel Ceilings Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	930.0d
1235	PR-P2-1C1-8590 Review & Submit Acoustical Panel Ceiling Selective Demo Submittals (HP) - CCBS	10.0d	20-Feb-26	5-Mar-26	26.0d
1236	PR-P2-1C1-8600 Review & Approve Acoustical Panel Ceiling Selective Demo Submittals (HNTB) -...	10.0d	6-Mar-26	19-Mar-26	26.0d
1237	WBS - Fire Suppression Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	942.0d
1238	PR-P1-1C1-2650 Prep Fire Suppression Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	941.0d
1239	WBS - Roadway Work (Sitework) Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	958.0d
1240	PR-P1-1C1-2770 Prep Roadway Work Submittals (Sitework) (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	957.0d
1241	WBS - Exterior Metal Framing - CCBS	30.0d	13-Feb-26	26-Mar-26	700.0d
1242	PR-P2-1C1-8150 Prep Exterior Metal Framing Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	700.0d
1243	WBS - Electrical Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	259.0d
1244	PR-P1-1C1-2690 Prep Elec Submittals (Contractor) - CCBS	15.0d	13-Feb-26	5-Mar-26	259.0d
1245	PR-P1-1C1-2890 Review & Submit Elec.Submittals (HP) - CCBS	5.0d	6-Mar-26	12-Mar-26	259.0d
1246	PR-P1-1C1-2720 Review & Approve Elec. Submittals (HNTB) - CCBS	10.0d	13-Mar-26	26-Mar-26	259.0d
1247	WBS - Low Voltage System Procurement - CCBS	30.0d	13-Feb-26	26-Mar-26	18.0d
1248	PR-P1-1C1-2730 Prep Low Voltage System Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	18.0d
1249	PR-P1-1C1-2910 Review & Submit Low Voltage System Submittals (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	18.0d
1250	WBS - Demolition Safety Plan Submittal - CCBS	30.0d	13-Feb-26	26-Mar-26	68.0d
1251	PR-P2-1C1-8620 Prep Demolition Submittals (Contractor) - CCBS	10.0d	13-Feb-26	26-Feb-26	68.0d
1252	PR-P2-1C1-8630 Review & Submit Demolition Submittals (HP) - CCBS	10.0d	27-Feb-26	12-Mar-26	68.0d
1253	PR-P2-1C1-8640 Review & Approve Demolition Submittals (HNTB) - CCBS	10.0d	13-Mar-26	26-Mar-26	68.0d
1254	WBS - Ductwork/Mechanical Systems - CCBS	30.0d	13-Feb-26	26-Mar-26	959.0d
1255	PR-P2-1C1-8340 Prep Ductwork/Mech. Systems Submittals (Contractor) - CCBS	25.0d	13-Feb-26	19-Mar-26	958.0d
1256	PR-P2-1C1-8350 Review & Submit Ductwork/Mech. Systems Submittals (HP) - CCBS	5.0d	20-Mar-26	26-Mar-26	958.0d
1257	WBS - Plumbing Systems - CCBS	25.0d	13-Feb-26	19-Mar-26	954.0d
1258	PR-P2-1C1-8460 Prep Plumbing Systems Submittals (Contractor) - CCBS	25.0d	13-Feb-26	19-Mar-26	953.0d
1259	WBS - Carbon Fiber Reinforcement Polymer (CFRP) - CCBS	59.0d	29-Dec-25	21-Mar-26	65.0d
1260	PR-P2-1C1-8520 Prep CFRP Submittals (Contractor) - CCBS	25.0d	29-Dec-25	2-Feb-26	54.0d

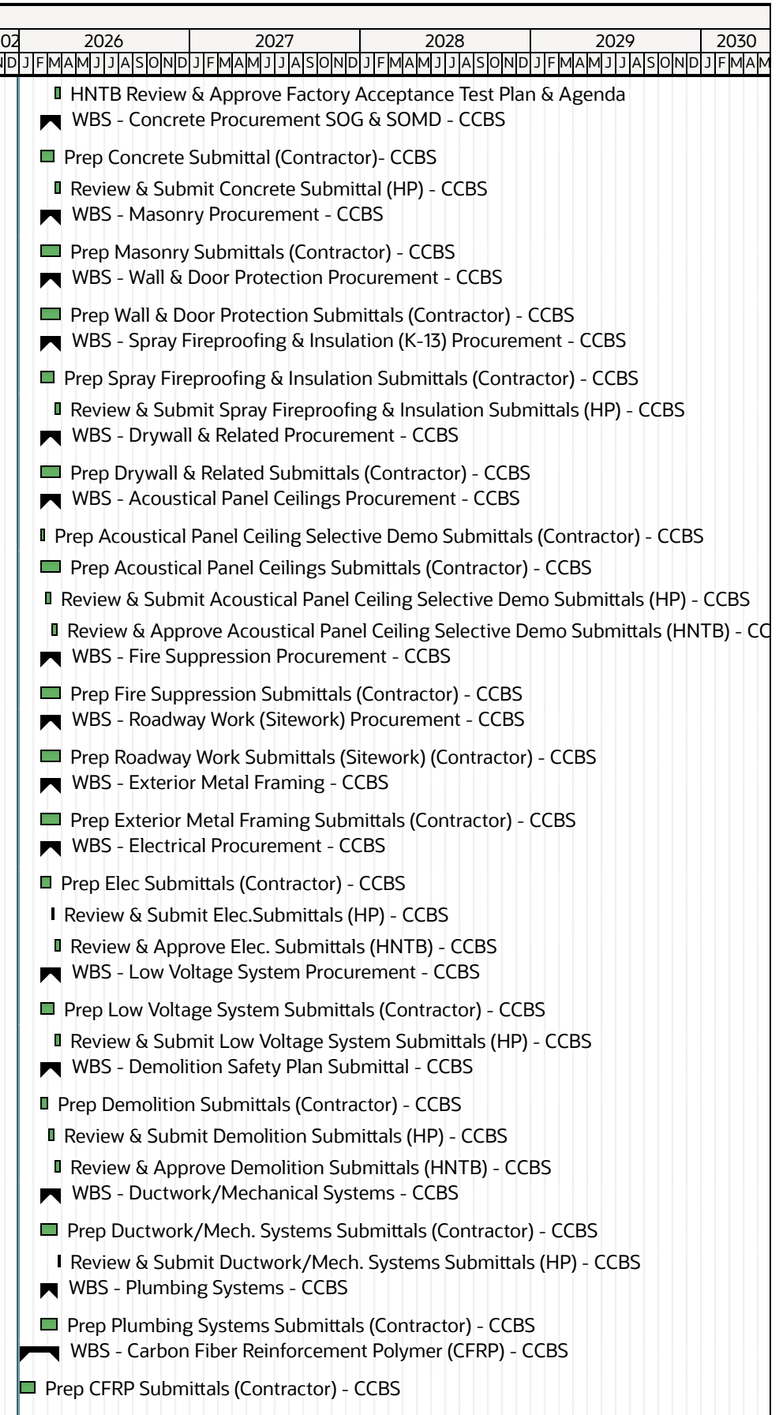


ID	Name	Dur	Start	Finish	TF
1261	PR-P2-1C1-8530	Review & Submit CFRP Submittals (HP) - CCBS	5.0d	3-Feb-26	9-Feb-26	54.0d
1262	PR-P2-1C1-8540	Review & Approve CFRP Submittals (HNTB) - CCBS	10.0d	10-Feb-26	23-Feb-26	54.0d
1263	PR-P2-1C1-8550	Review & Approve CFRP Submittals (HCAA) - CCBS	15.0d	24-Feb-26	16-Mar-26	54.0d
1264	PR-P2-1C1-8560	Fab. & Ship CFRP Systems - CCBS	5.0d	17-Mar-26	21-Mar-26	92.0d
1265	PR-P2-1C1-8570	Delivery of CFRP on Site - CCBS	0.0d		21-Mar-26	92.0d
1266	WBS - Structural Steel Procurement - CCBS		25.0d	20-Feb-26	26-Mar-26	58.0d
1267	WBS - Structural Steel Procurement - T17 [01-01-04]		25.0d	20-Feb-26	26-Mar-26	58.0d
1268	BG-PR-2C-ST-210	Prep T17 Structural Steel Detailed Drawings (Contractor) [01-01-04]	20.0d	20-Feb-26	19-Mar-26	58.0d
1269	BG-PR-2C-ST-250	Review & Submit T17 Structural Steel Detailed Drawings (HP) [01-01-04]	5.0d	20-Mar-26	26-Mar-26	58.0d
1270	WBS - Part 2 Supplement C Wave 2 - Finishes Procurement		25.0d	13-Feb-26	19-Mar-26	9.0d
1271	WBS - Airport Access Controls Procurement - CCBS		25.0d	13-Feb-26	19-Mar-26	9.0d
1272	PR-P2-1C2-8160	Prep Airport Access Controls Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	9.0d
1273	PR-P2-1C2-8170	Review & Submit Airport Access Controls Submittals (HP) - CCBS	5.0d	13-Mar-26	19-Mar-26	9.0d
1274	WBS - CCBS - CONSTRUCTION PHASE		481.0d	20-Oct-25 A	10-Sep-27	0.0d
1275	WBS - Main Terminal CCBS Consolidation		481.0d	20-Oct-25 A	10-Sep-27	0.0d
1276	WBS - Operational Impact Windows		0.0d	27-Feb-26	27-Feb-26	376.0d
1277	BG-MLS-OPS-10	Tug Lane Crossover Between OS Line & Pod 5 - Permanently Shut Down	0.0d		27-Feb-26	376.0d
1278	WBS - BHS Testing & Integration		1.0d	13-Feb-26	13-Feb-26	60.0d
1279	WBS - ISAT - Full System		1.0d	13-Feb-26	13-Feb-26	60.0d
1280	BG-TST-30	Site Survey Data Collection Planning Checklist provided to the PROJECT SPON…	1.0d	13-Feb-26	13-Feb-26	60.0d
1281	WBS - Construction Phases		35.0d	6-Feb-26	26-Mar-26	369.0d
1282	WBS - Seq 1 - Stage 1 - Step 1		5.0d	27-Feb-26	5-Mar-26	51.0d
1283	A106020	Pre-Test & Balance Pre-HVAC Demo/Modification [01-01-01]	5.0d	27-Feb-26	5-Mar-26	51.0d
1284	WBS - Seq 1 - Stage 3 - Step 1		35.0d	6-Feb-26	26-Mar-26	369.0d
1285	WBS - North Tug Lane [01-03-01]		8.0d	6-Feb-26	17-Feb-26	234.0d
1286	WBS - Electrical - North Tug Lane [01-03-01]		8.0d	6-Feb-26	17-Feb-26	234.0d
1287	BG-BI-ROW-170	Rough-In New Conduit for Relocation at T-18A Wall Opening [01-03-01]	2.0d	6-Feb-26	9-Feb-26	234.0d
1288	BG-BI-ROW-180	Pull Wire & Terminate w/ Shutdowns for Relocation at T-18A Wall Opening [01-…	5.0d	10-Feb-26	16-Feb-26	234.0d
1289	BG-BI-ROW-190	Demo Exist. Conduit at T-18A Wall Opening [01-03-01]	1.0d	17-Feb-26	17-Feb-26	234.0d
1290	WBS - AS8 (Pod 8) [01-03-01]		20.0d	27-Feb-26	26-Mar-26	369.0d
1291	WBS - Structural - AS8 (Pod 8) [01-03-01]		19.0d	27-Feb-26	25-Mar-26	370.0d
1292	BI-ROW-BR-P5-20	Remove Moveable Concrete Barriers at OH Door Openings in AS5 thru AS8 [01…	2.0d	27-Feb-26	2-Mar-26	210.0d
1293	BI-ROW-BR-P5-40	Demo Exist. Metal Rail Impact Protection & Bollards Around East Pods [01-03-…	2.0d	3-Mar-26	4-Mar-26	363.0d
1294	BI-ROW-BR-P8-130	Demo Housekeeping Pad Beneath Former AHU-B9 [01-03-01]	2.0d	24-Mar-26	25-Mar-26	370.0d
1295	WBS - Architectural - AS8 (Pod 8) [01-03-01]		2.0d	27-Feb-26	2-Mar-26	210.0d
1296	BI-ROW-BR-P5-10	Set-Up Temp Barriers Around AS5 thru AS8 & Tug Lane Crossover Near Existin…	2.0d	27-Feb-26	2-Mar-26	210.0d
1297	WBS - Electrical - AS8 (Pod 8) [01-03-01]		20.0d	27-Feb-26	26-Mar-26	187.0d
1298	BI-ROW-BR-P5-140	Install Temp Lighting Throughout East End of Main Terminal [01-03-01]	5.0d	27-Feb-26	5-Mar-26	187.0d
1299	BI-ROW-BR-P8-70	Demo/Relocate Existing Elec. Devices, Lighting, & Conduit in AS8 [01-03-01]	15.0d	6-Mar-26	26-Mar-26	187.0d
1300	WBS - Mechanical/Plumbing - AS8 (Pod 8) [01-03-01]		12.0d	6-Mar-26	23-Mar-26	222.0d
1301	BI-ROW-BR-P8-10	Demo Exist. Wall Louvers & Wall-Mounted Circulation Fan in AS8 [01-03-01]	2.0d	6-Mar-26	9-Mar-26	210.0d
1302	BI-ROW-BR-P8-20	Demo & Cap Existing High Supply Ductwork in AS8 [01-03-01]	5.0d	10-Mar-26	16-Mar-26	222.0d

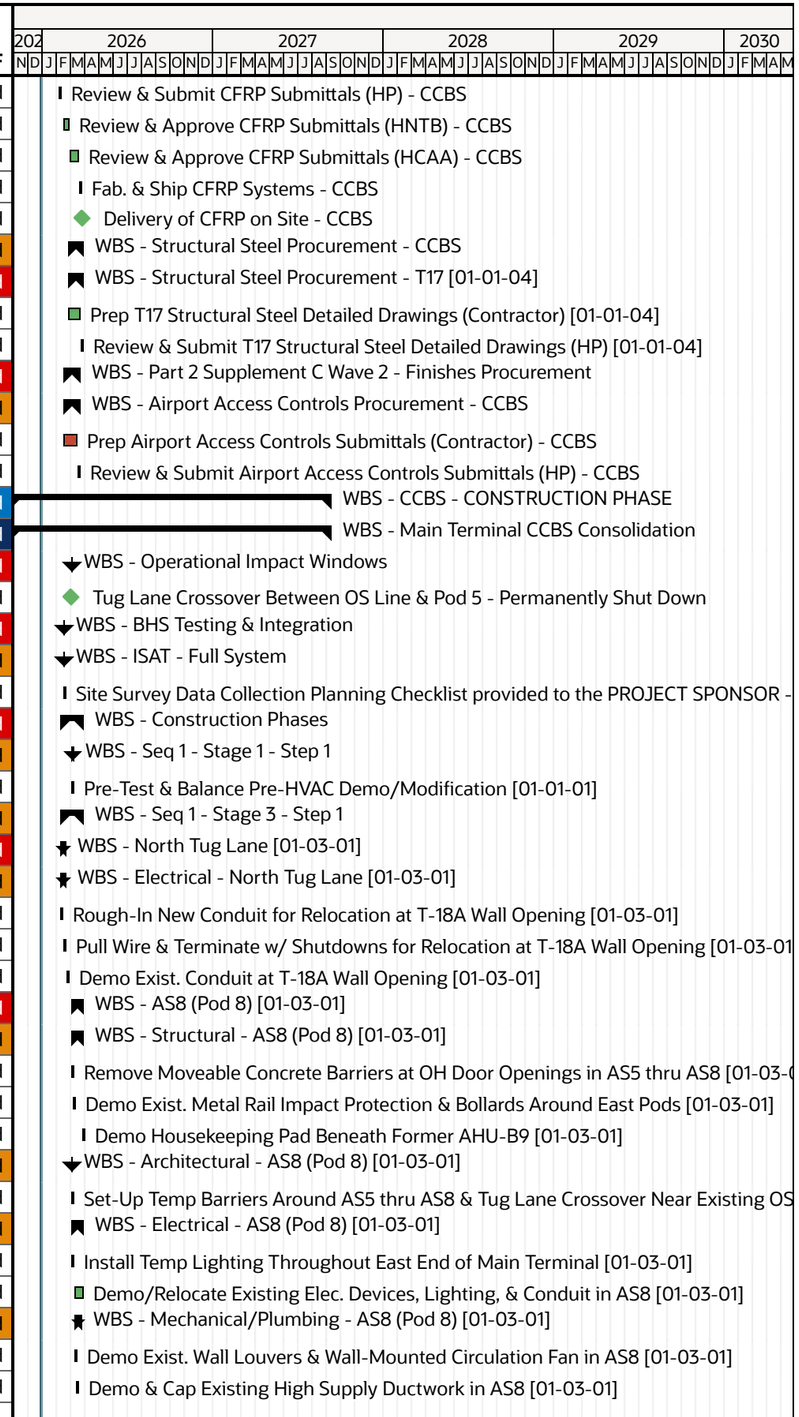


	ID	Name	Dur	Start	Finish	TF
1303	BI-ROW-BR-P8-120	Demo & Remove AHU-B9, Associated Ductwork, & Associated Chilled Water Pi...	5.0d	17-Mar-26	23-Mar-26	222.0d
1304	WBS - Technology - AS8 (Pod 8) [01-03-01]		15.0d	27-Feb-26	19-Mar-26	202.0d
1305	BI-ROW-BR-P8-30	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS8 - Area G [...	10.0d	27-Feb-26	12-Mar-26	207.0d
1306	BI-ROW-BR-P8-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring in AS8 - ...	15.0d	27-Feb-26	19-Mar-26	202.0d
1307	WBS - AS7 (Pod 7)		10.0d	13-Mar-26	26-Mar-26	221.0d
1308	WBS - Mechanical/Plumbing - AS7 (Pod 7) [01-03-01]		2.0d	24-Mar-26	25-Mar-26	222.0d
1309	BI-ROW-BR-P7-10	Demo Exist. Wall Louver in AS7 [01-03-01]	2.0d	24-Mar-26	25-Mar-26	222.0d
1310	WBS - Technology - AS7 (Pod 7) [01-03-01]		10.0d	13-Mar-26	26-Mar-26	221.0d
1311	BI-ROW-BR-P7-30	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS7 - Area F [...	10.0d	13-Mar-26	26-Mar-26	221.0d
1312	WBS - AS5 (Pod 5)		14.0d	5-Mar-26	24-Mar-26	363.0d
1313	WBS - Structural - AS5 (Pod 5) [01-03-01]		14.0d	5-Mar-26	24-Mar-26	363.0d
1314	BI-ROW-BR-P5-80	Demo (12) Existing Free-Standing Bollards Surrounding OS Line - Area H [01-0...	4.0d	5-Mar-26	10-Mar-26	363.0d
1315	BI-ROW-BR-P5-260	Patch & Seal Concrete @ Former Metal Rail & Bollard Locations Surrounding O...	5.0d	11-Mar-26	17-Mar-26	363.0d
1316	BI-ROW-BR-P5-120	Remove Existing Tug Lane Striping at Tug Crossover Between AS5 & OS Line - ...	5.0d	18-Mar-26	24-Mar-26	363.0d
1317	WBS - Bag Claim Ceiling - Carousels C12 & C13		5.0d	6-Mar-26	12-Mar-26	346.0d
1318	WBS - Mechanical/Plumbing - Bag Claim Ceiling (C12 & C13) [01-03-01]		5.0d	6-Mar-26	12-Mar-26	346.0d
1319	A109000	Test & Balance Pre-HVAC Demo/Modification [01-03-01]	5.0d	6-Mar-26	12-Mar-26	346.0d
1320	WBS - CCBS - Building Infrastructure		481.0d	20-Oct-25 A	10-Sep-27	0.0d
1321	WBS - BHS ROW Prep		481.0d	20-Oct-25 A	10-Sep-27	0.0d
1322	WBS - Tag & Trace		481.0d	20-Oct-25 A	10-Sep-27	0.0d
1323	CCBS-LOE-1000	Tag & Trace Elec.& Low Voltage (LOE)	481.0d	20-Oct-25 A	10-Sep-27	0.0d
1324	WBS - Tag & Trace - Sequence 1 - Stage 1		47.0d	16-Nov-25 A	26-Jan-26	94.0d
1325	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 1		36.0d	19-Nov-25 A	13-Jan-26	103.0d
1326	TT-SQ1-SG1-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	19-Nov-25 A	29-Dec-25	103.0d
1327	TT-SQ1-SG1-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 1	10.0d	30-Dec-25	13-Jan-26	103.0d
1328	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 2		36.0d	20-Nov-25 A	14-Jan-26	102.0d
1329	TT-SQ1-SG1-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	20-Nov-25 A	30-Dec-25	102.0d
1330	TT-SQ1-SG1-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 2	10.0d	31-Dec-25	14-Jan-26	102.0d
1331	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 3		45.0d	16-Nov-25 A	22-Jan-26	96.0d
1332	TT-SQ1-SG1-A3-10	Tag & Trace - Sequence 1 - Stage 1 - Area 3	30.0d	16-Nov-25 A	31-Dec-25	0.0d
1333	TT-SQ1-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	2-Jan-26	8-Jan-26	96.0d
1334	TT-SQ1-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 3	10.0d	9-Jan-26	22-Jan-26	96.0d
1335	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 4		44.0d	20-Nov-25 A	26-Jan-26	94.0d
1336	TT-SQ1-SG1-A4-10	Tag & Trace - Sequence 1 - Stage 1 - Area 4	29.0d	20-Nov-25 A	5-Jan-26	0.0d
1337	TT-SQ1-SG1-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
1338	TT-SQ1-SG1-A4-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 4	10.0d	13-Jan-26	26-Jan-26	94.0d
1339	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 5		37.0d	3-Dec-25 A	26-Jan-26	94.0d
1340	TT-SQ1-SG1-A5-10	Tag & Trace - Sequence 1 - Stage 1 - Area 5	22.0d	3-Dec-25 A	5-Jan-26	0.0d
1341	TT-SQ1-SG1-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
1342	TT-SQ1-SG1-A5-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 5	10.0d	13-Jan-26	26-Jan-26	94.0d
1343	WBS - Tag & Trace - Sequence 1 - Stage 2		54.0d	6-Jan-26	20-Mar-26	293.0d
1344	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 1		35.0d	6-Jan-26	23-Feb-26	312.0d

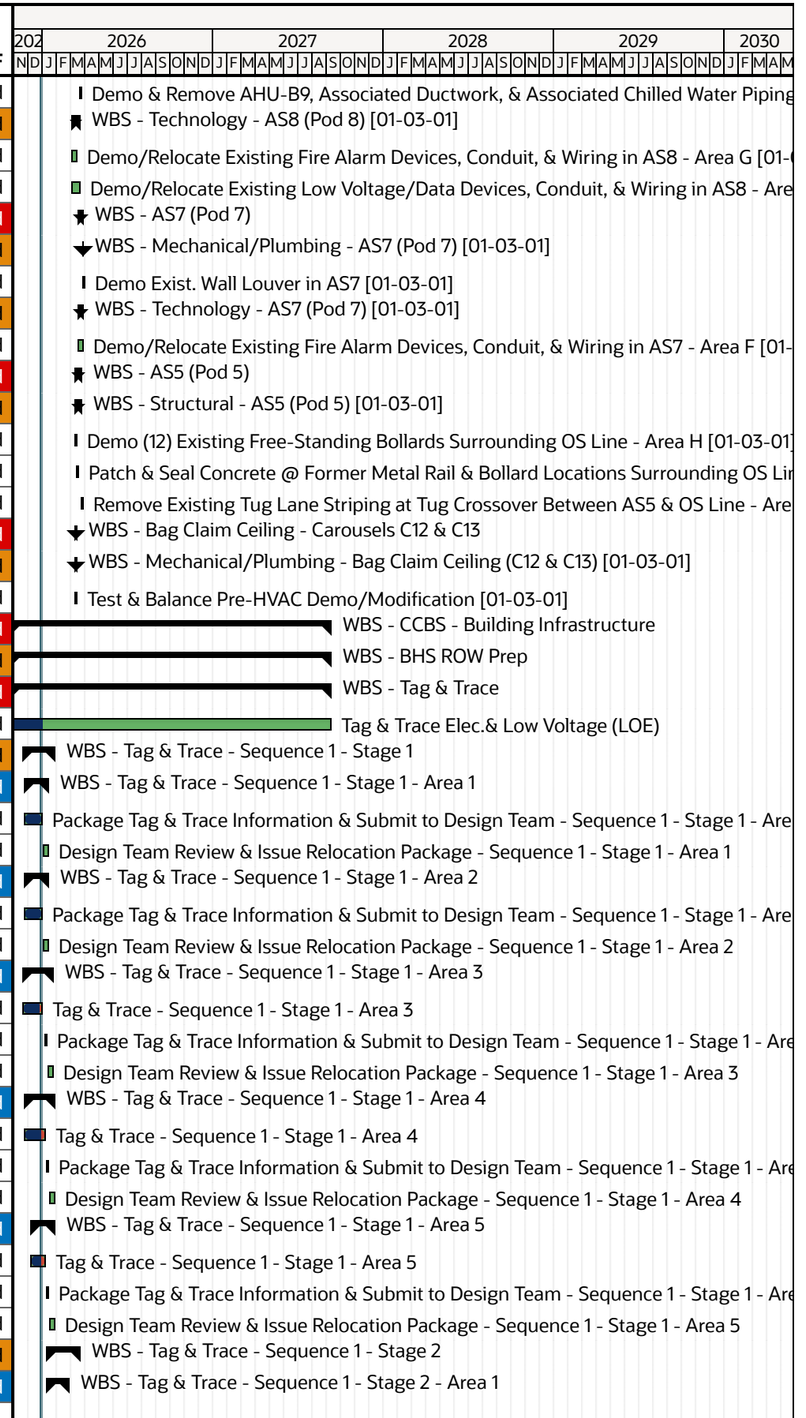

ID	Name	Dur	Start	Finish	TF
1345	TT-SQ1-SG2-A1-10	Tag & Trace - Sequence 1 - Stage 2 - Area 1	10.0d	6-Jan-26	19-Jan-26	0.0d
1346	TT-SQ1-SG2-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	20-Jan-26	26-Jan-26	312.0d
1347	TT-SQ1-SG2-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 1	10.0d	27-Jan-26	9-Feb-26	312.0d
1348	TT-SQ1-SG2-A1-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 1	10.0d	10-Feb-26	23-Feb-26	312.0d
1349	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 2		35.0d	12-Jan-26	27-Feb-26	199.0d
1350	TT-SQ1-SG2-A2-10	Tag & Trace - Sequence 1 - Stage 2 - Area 2	10.0d	12-Jan-26	23-Jan-26	0.0d
1351	TT-SQ1-SG2-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	26-Jan-26	30-Jan-26	199.0d
1352	TT-SQ1-SG2-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 2	10.0d	2-Feb-26	13-Feb-26	199.0d
1353	TT-SQ1-SG2-A2-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 2	10.0d	16-Feb-26	27-Feb-26	199.0d
1354	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 3		35.0d	26-Jan-26	13-Mar-26	189.0d
1355	TT-SQ1-SG2-A3-10	Tag & Trace - Sequence 1 - Stage 2 - Area 3	10.0d	26-Jan-26	6-Feb-26	0.0d
1356	TT-SQ1-SG2-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	9-Feb-26	13-Feb-26	189.0d
1357	TT-SQ1-SG2-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 Stage 2 - Area 3	10.0d	16-Feb-26	27-Feb-26	189.0d
1358	TT-SQ1-SG2-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 3	10.0d	2-Mar-26	13-Mar-26	189.0d
1359	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 4		25.0d	9-Feb-26	13-Mar-26	191.0d
1360	TT-SQ1-SG2-A4-10	Tag & Trace - Sequence 1 - Stage 2 - Area 4	10.0d	9-Feb-26	20-Feb-26	0.0d
1361	TT-SQ1-SG2-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	23-Feb-26	27-Feb-26	191.0d
1362	TT-SQ1-SG2-A4-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 4	10.0d	2-Mar-26	13-Mar-26	191.0d
1363	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 5		15.0d	23-Feb-26	13-Mar-26	181.0d
1364	TT-SQ1-SG2-A5-10	Tag & Trace - Sequence 1 - Stage 2 - Area 5	10.0d	23-Feb-26	6-Mar-26	0.0d
1365	TT-SQ1-SG2-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	9-Mar-26	13-Mar-26	181.0d
1366	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 6		10.0d	9-Mar-26	20-Mar-26	0.0d
1367	TT-SQ1-SG2-A6-10	Tag & Trace - Sequence 1 - Stage 2 - Area 6	10.0d	9-Mar-26	20-Mar-26	0.0d

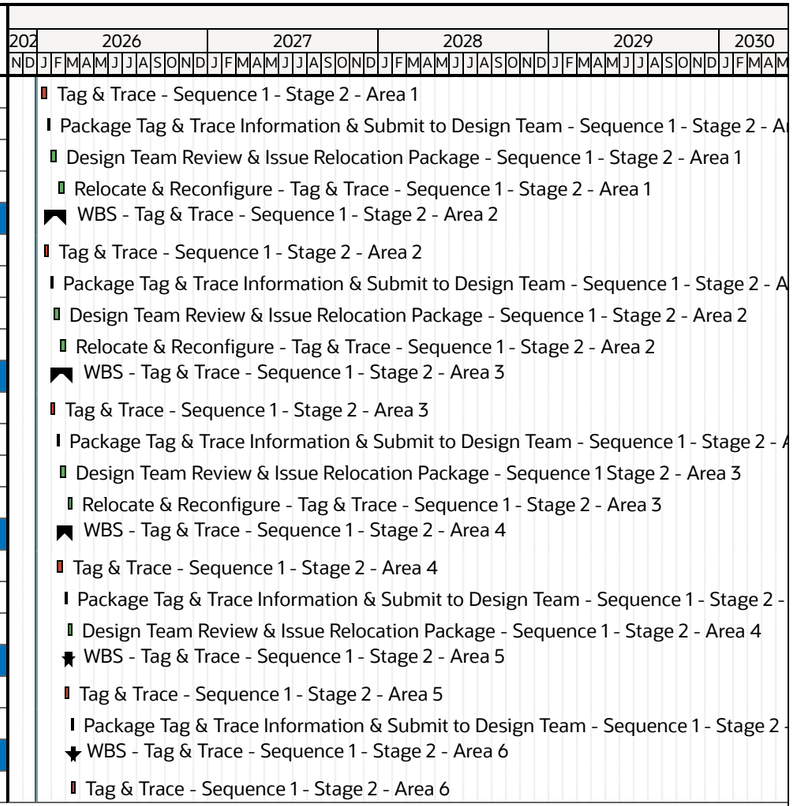

ID	Name	Dur	Start	Finish	TF
Airside D - Tampa International Airport		1,689d	03-Aug-23 A	20-Mar-30	0d
PTTS-10	Project Timetable Summary to Substantial Completion (LOE)	1,419d	03-Aug-23 A	02-Mar-29	0d
HA-AL-CP-100	Concessions - Concessions Development	279d	09-Dec-24 A	14-Jan-26	4d
ASD-HAM-20	ASD - Contingency/Allowance/Budget - LOE	1,337d	13-Dec-24 A	20-Mar-30	0d
ASD-HAM-10	ASD - General Conditions/Requirements - LOE	1,337d	13-Dec-24 A	20-Mar-30	0d
CCBS-HAM-30	CCBS - Supp B General Conditions/Requirements - LOE	492d	02-Oct-25 A	10-Sep-27	0d
CCBS-HAM-40	CCBS - Supp B Contingency/Allowance/Budget - LOE	492d	02-Oct-25 A	10-Sep-27	0d
CCBS-LOE-1000	Tag & Trace Elec.& Low Voltage (LOE)	481d	20-Oct-25 A	10-Sep-27	0d
PR-P2-1B-3760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	58d	31-Oct-25 A	26-Jan-26	3d
PR-P2-1B-3810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	63d	31-Oct-25 A	02-Feb-26	9d
PR-P2-1B-4810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	48d	31-Oct-25 A	12-Jan-26	3d
TT-SQ1-SG1-A3-10	Tag & Trace - Sequence 1 - Stage 1 - Area 3	30d	16-Nov-25 A	31-Dec-25	0d
TT-SQ1-SG1-A4-10	Tag & Trace - Sequence 1 - Stage 1 - Area 4	29d	20-Nov-25 A	05-Jan-26	0d
GI-FS-HAM-1010	Found. Concrete Scope - LOE	153d	24-Nov-25 A	01-Jul-26	0d
TT-SQ1-SG1-A5-10	Tag & Trace - Sequence 1 - Stage 1 - Area 5	22d	03-Dec-25 A	05-Jan-26	0d
PR-P2-1B-7990	Issue/Process PO to Mill Order- Part 2 Supp. A	20d	03-Dec-25 A	31-Dec-25	0d
D1084	Review & Approve (HCAA) General Mech. Assembly Detail Drawings	30d	05-Dec-25 A	19-Jan-26	0d
HA-2C-W1-70	HCAA Review Supp. C for Board - Part 2 Supp. C - Core & Shell Pkg.	37d	15-Dec-25 A	05-Feb-26	0d
GI-FS-A1-6820	FRP Found. - Area 6	14d	16-Dec-25 A	06-Jan-26	4d
GI-FS-HAM-1030	Deep UG Plumbing & Mech. Scope - LOE	185d	16-Dec-25 A	04-Sep-26	0d
GI-FS-A1-6840	MEPF In-Wall R/I - Area 6	14d	16-Dec-25 A	06-Jan-26	4d
D1093	Review & Approve (HCAA) Mech Plan & Elev Dwg Set [01-01-01]	16d	18-Dec-25 A	12-Jan-26	0d
GI-FS-A2-5500	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.1	21d	23-Dec-25 A	22-Jan-26	10d
PR-P2-1A-1910	HNTB Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	11d	23-Dec-25 A	08-Jan-26	0d
D1123	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-05]	15d	29-Dec-25	19-Jan-26	6d
PR-P2-1B-3720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 Supp. B	5d	29-Dec-25	05-Jan-26	5d
A110560	Review & Approve (HNTB) Mech. Catalog Cut/Equip. Specs	10d	29-Dec-25	12-Jan-26	0d
PR-P2-1B-3705	Delivery of Allowance Long Lead - Steel Mill Order - Part 2 Supp. A (LOE)	84d	02-Jan-26	26-Mar-26	0d
PR-P2-1B-8000	Fab. & Ship Long Lead Mill Order - Part 2 Supp. A	84d	02-Jan-26	26-Mar-26	0d
2C-W1-PC-860	Purchasing Meeting - Elec. & Site Elec. Trade Partner - P2 Supp. C Wv 1 Pur & Contr	1d	05-Jan-26	05-Jan-26	9d
2C-W1-PC-2480	Purchasing Meeting - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	1d	06-Jan-26	06-Jan-26	9d
TT-SQ1-SG2-A1-10	Tag & Trace - Sequence 1 - Stage 2 - Area 1	10d	06-Jan-26	19-Jan-26	0d
PR-P2-1B-3725	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 Supp. B	20d	06-Jan-26	02-Feb-26	5d
2C-W1-PC-2490	Draft, Review, & Issue Change Order - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	3d	07-Jan-26	09-Jan-26	9d
GI-FS-A1-6850	Backfill Found. - Area 6	7d	07-Jan-26	15-Jan-26	4d
GI-FS-A1-6830	Install Waterproofing On Found. - Area 6	5d	07-Jan-26	13-Jan-26	5d
GI-FS-A1-6825	FRP Turndown - Area 6	5d	07-Jan-26	13-Jan-26	5d
PR-P2-1A-1710	HCAA Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	15d	09-Jan-26	29-Jan-26	0d
2C-W1-PC-2510	Change Order Negotiation - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	10d	12-Jan-26	23-Jan-26	9d
TT-SQ1-SG2-A2-10	Tag & Trace - Sequence 1 - Stage 2 - Area 2	10d	12-Jan-26	23-Jan-26	0d
D1083	Review & Approve (HCAA) Mech. Catalog Cut/Equip. Specs	15d	13-Jan-26	02-Feb-26	0d
PR-P2-1B-4820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 Supp. B	5d	13-Jan-26	19-Jan-26	3d
D1094	Fab. & Deliver Conveyor Batch 1 (15) [01-01-01]	120d	13-Jan-26	30-Jun-26	0d
HA-AL-CP-120	Concessions - Leasing Model/Business Structure (HCAA)	102d	15-Jan-26	08-Jun-26	4d
GI-FS-A1-6610	Excavate Area For Found. - Area 2.A	5d	16-Jan-26	22-Jan-26	4d
GI-FS-A1-6620	FRP Found. - Area 2.A	20d	19-Jan-26	13-Feb-26	4d
GI-FS-A1-6640	MEPF In-Wall R/I - Area 2.A	15d	19-Jan-26	06-Feb-26	6d
D1095	Prep & Submit Header Steel Dwg Set [01-01-01]	10d	20-Jan-26	02-Feb-26	0d
D1096	Fab. & Deliver Conveyor Batch 2 (14) [01-01-01]	120d	20-Jan-26	08-Jul-26	0d
GI-FS-A1-6630	Install Waterproofing On Found. - Area 2.A	20d	20-Jan-26	16-Feb-26	4d
PR-P2-1B-4830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 Supp. B	20d	20-Jan-26	16-Feb-26	3d
D1128	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-01]	20d	20-Jan-26	16-Feb-26	6d
GI-FS-A2-5580	Inspect - Deep UG Conduit - Elec. - Area 2.B.1	2d	23-Jan-26	26-Jan-26	10d
TT-SQ1-SG2-A3-10	Tag & Trace - Sequence 1 - Stage 2 - Area 3	10d	26-Jan-26	06-Feb-26	0d
PR-P2-1B-3770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 Supp. B	5d	27-Jan-26	02-Feb-26	3d
GI-FS-A2-5590	Backfill - Deep UG Conduit - Elec. - Area 2.B.1	5d	27-Jan-26	02-Feb-26	10d
EN-DM-A1-130	Demo Second Half of Tunnel Structure - Phase C Area 1	10d	30-Jan-26	12-Feb-26	0d
PR-P2-1A-1720	Fab. & Ship Rebar Found. Area 1 - Part 2 Supp. A	40d	30-Jan-26	10-Mar-26	0d
IPR-ITB1-MLS20	MLS20 - Fuel Main Install Complete (Crisdel)	0d		30-Jan-26 C	0d
PR-P2-1B-3728	Return From Approval Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	0d		02-Feb-26	5d

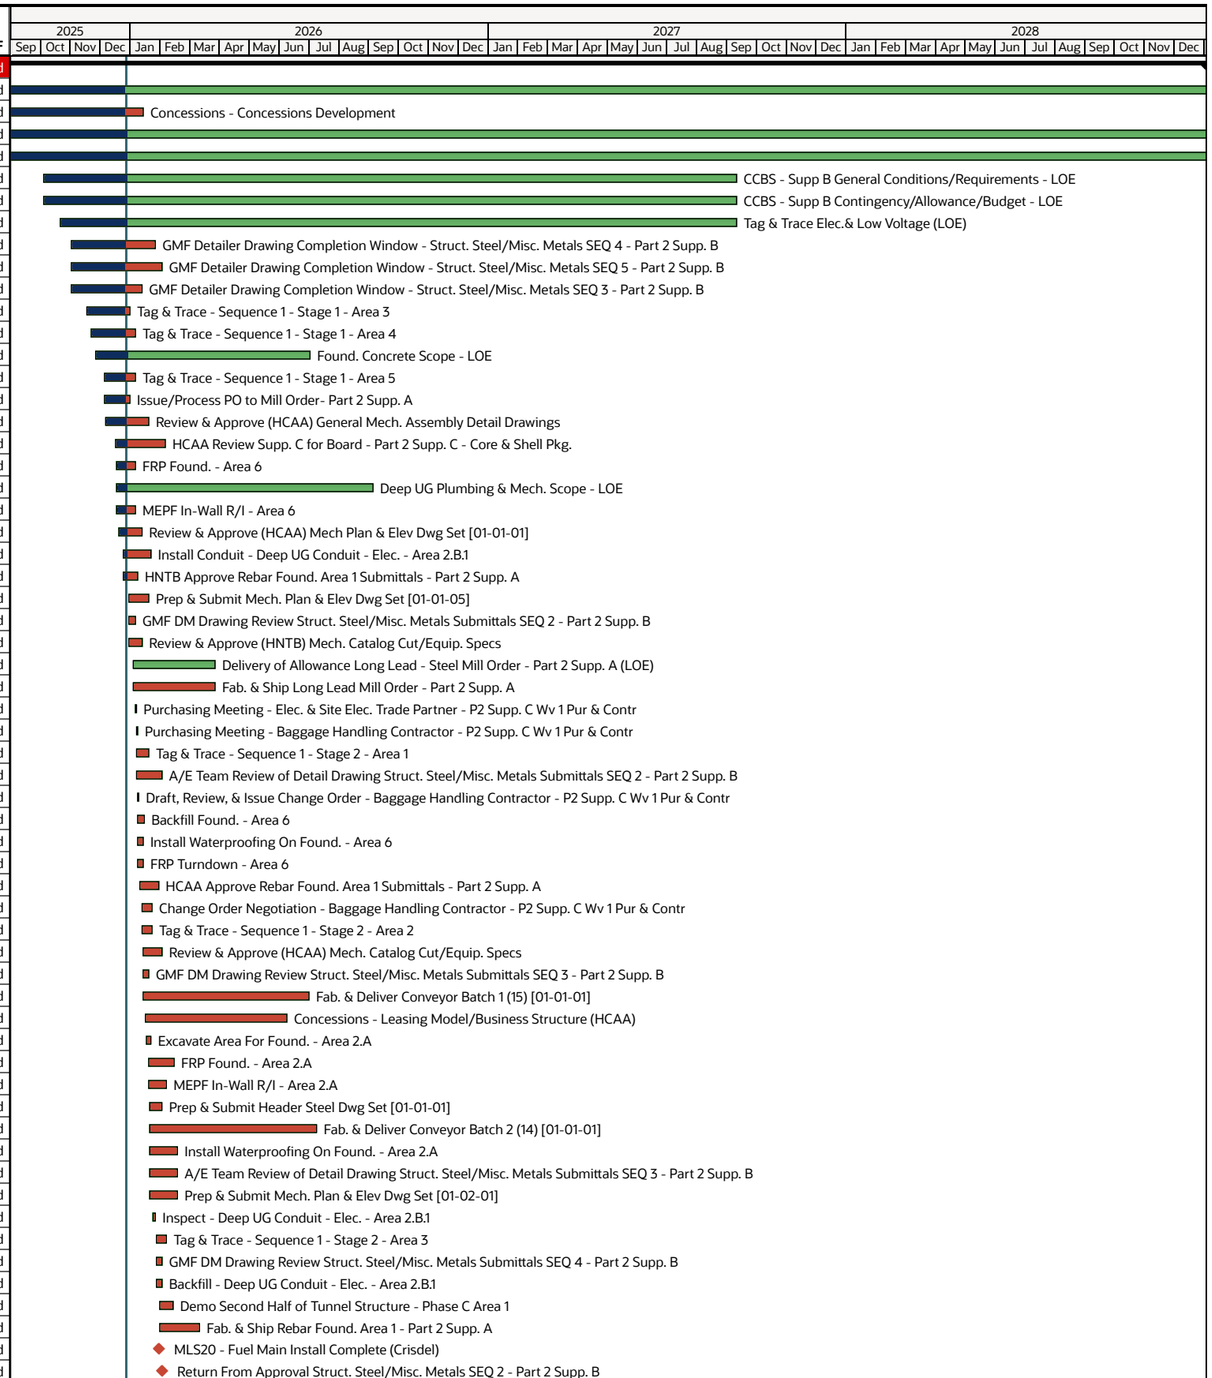

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
D1101	Fab. & Deliver HSD T18A 1 [01-01-02]	130d	03-Feb-26	05-Aug-26	0d
PR-P2-1B-3780	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 Supp. B	20d	03-Feb-26	02-Mar-26	3d
D3556	Review & Approve (HP) Header Steel Dwg Set [01-01-01]	5d	03-Feb-26	09-Feb-26	0d
PR-P2-1B-3730	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	10d	03-Feb-26	16-Feb-26	5d
PR-P2-1B-3820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 Supp. B	5d	03-Feb-26	09-Feb-26	9d
HA-2C-W1-80	Board Date (NTP) - Part 2 Supp. C - Core & Shell Pkg. (2.5.26)	0d		05-Feb-26	0d
HA-BA-60	Part 2 Supplemental C Agreement - HCAA Board Approval (2.5.2026)	0d		05-Feb-26	5d
2C-W1-PC-780	Contract Execution - Elev./Escalators Trade Partner - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	0d
2C-W1-PC-960	Change Order Execution - Low Voltage System Trade Partner - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	9d
2C-W1-PC-2520	Change Order Execution - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	5d	06-Feb-26	12-Feb-26	0d
TT-SQ1-SG2-A4-10	Tag & Trace - Sequence 1 - Stage 2 - Area 4	10d	09-Feb-26	20-Feb-26	0d
D3566	Review & Approve (HNTB) Header Steel Dwg Set [01-01-01]	10d	10-Feb-26	23-Feb-26	0d
PR-P2-1B-3830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 Supp. B	20d	10-Feb-26	09-Mar-26	9d
GI-FS-A1-6650	Backfill Found. - Area 2.A	7d	11-Feb-26	19-Feb-26	4d
MLS-SUPP.C-02	MLS 2 - Demo Second Half of Tunnel Structure Complete	0d		12-Feb-26 C	0d
2C-W1-PC-790	Contract Exec Complete - Elev./Escalators Trade Partner - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	0d
2C-W1-PC-2530	Change Order Execution Complete - Baggage Handling Contractor - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	0d
2C-W1-PC-970	Change Order Execution Complete - Low Voltage System Trade Partner - P2 Supp. C Wv 1 Pur & Contr	0d		12-Feb-26	9d
PR-P1-1C1-810	Prep Elev. 01-11 Submittals - ASD	50d	13-Feb-26	23-Apr-26	0d
GI-FS-A1-6970	Excavate Area For Found. - Area 2.B	3d	13-Feb-26	17-Feb-26	2d
D1507	Prep & Submit Mech. Plan & Elev Dwg Set - Sector K	20d	13-Feb-26	12-Mar-26	0d
PR-P2-1C2-8160	Prep Airport Access Controls Submittals (Contractor) - CCBS	20d	13-Feb-26	12-Mar-26	9d
D1086	Prep & Submit Cross Belt Mech. Catalog Cut/Equip. Specs	15d	13-Feb-26	05-Mar-26	7d
GI-FS-A1-6980	FRP Found. - Area 2.B	11d	16-Feb-26	02-Mar-26	2d
PR-P2-1B-4840	Return From Approval Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	0d		16-Feb-26	3d
PR-P2-1B-4850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	10d	17-Feb-26	02-Mar-26	3d
GI-FS-A1-6990	Install Waterproofing On Found. - Area 2.B	10d	17-Feb-26	02-Mar-26	2d
PR-P2-1B-3740	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	5d	17-Feb-26	23-Feb-26	5d
D3716	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-01]	5d	17-Feb-26	23-Feb-26	6d
GI-FS-A1-7000	MEPF In-Wall R/I - Area 2.B	7d	18-Feb-26	26-Feb-26	3d
TT-SQ1-SG2-A5-10	Tag & Trace - Sequence 1 - Stage 2 - Area 5	10d	23-Feb-26	06-Mar-26	0d
PR-P2-1B-3742	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0d		23-Feb-26	5d
D3726	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-01]	10d	24-Feb-26	09-Mar-26	6d
PR-P2-1B-3744	Fab. of Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	71d	24-Feb-26	03-Jun-26	5d
D1097	Review & Approve (HCAA) Header Steel Dwg Set [01-01-01]	15d	24-Feb-26	16-Mar-26	0d
GI-FS-A1-7010	Backfill Found. - Area 2.B	4d	02-Mar-26	05-Mar-26	2d
PR-P2-1B-3790	Return From Approval Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	0d		02-Mar-26	3d
PR-P2-1B-4870	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	5d	03-Mar-26	09-Mar-26	3d
PR-P2-1B-3800	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	10d	03-Mar-26	16-Mar-26	3d
D3436	Review & Approve (HP) Cross Belt Mech. Catalog Cut/Equip. Specs	5d	06-Mar-26	12-Mar-26	7d
GI-FS-A1-1070	Excavate Area For Found. - Area 1.A	2d	06-Mar-26	09-Mar-26	2d
TT-SQ1-SG2-A6-10	Tag & Trace - Sequence 1 - Stage 2 - Area 6	10d	09-Mar-26	20-Mar-26	0d
PR-P2-1B-3840	Return From Approval Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	0d		09-Mar-26	9d
PR-P2-1B-4872	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0d		09-Mar-26	3d
PR-P2-1B-4874	Fab. of Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	76d	10-Mar-26	24-Jun-26	3d
PR-P2-1B-3850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	10d	10-Mar-26	23-Mar-26	9d
D1129	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-01]	15d	10-Mar-26	30-Mar-26	6d
PR-P2-1A-1730	Delivery of Rebar Found. Area 1 Complete - Part 2 Supp. A	0d		10-Mar-26	0d
GI-FS-A1-1250	FRP Found. - Area 1.A	5d	11-Mar-26	17-Mar-26	0d
GI-FS-A1-1410	MEPF In-Wall R/I - Area 1.A	2d	11-Mar-26	12-Mar-26	2d
GI-FS-A1-1260	Install Waterproofing On Found. - Area 1.A	3d	12-Mar-26	16-Mar-26	0d
D1512	Prep & Submit Mech. Plan & Elev Dwg Set - Sector J	20d	13-Mar-26	09-Apr-26	0d
PR-P2-1C2-8170	Review & Submit Airport Access Controls Submittals (HP) - CCBS	5d	13-Mar-26	19-Mar-26	9d
D3446	Review & Approve (HNTB) Cross Belt Mech. Catalog Cut/Equip. Specs	10d	13-Mar-26	26-Mar-26	7d
GI-FS-A1-1270	Backfill Found. - Area 1.A	3d	17-Mar-26	19-Mar-26	0d
D1098	Fab. & Deliver Header Steel/Platform/Sills [01-01-01]	80d	17-Mar-26	08-Jul-26	0d
GI-FS-A1-7020	Excavate Area For Found. - Area 1.B	3d	17-Mar-26	19-Mar-26	0d
PR-P2-1B-3802	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	5d	17-Mar-26	23-Mar-26	3d
GI-FS-A1-7030	FRP Found. - Area 1.B	7d	18-Mar-26	26-Mar-26	0d
GI-FS-A1-7040	MEPF In-Wall R/I - Area 1.B	3d	19-Mar-26	23-Mar-26	3d

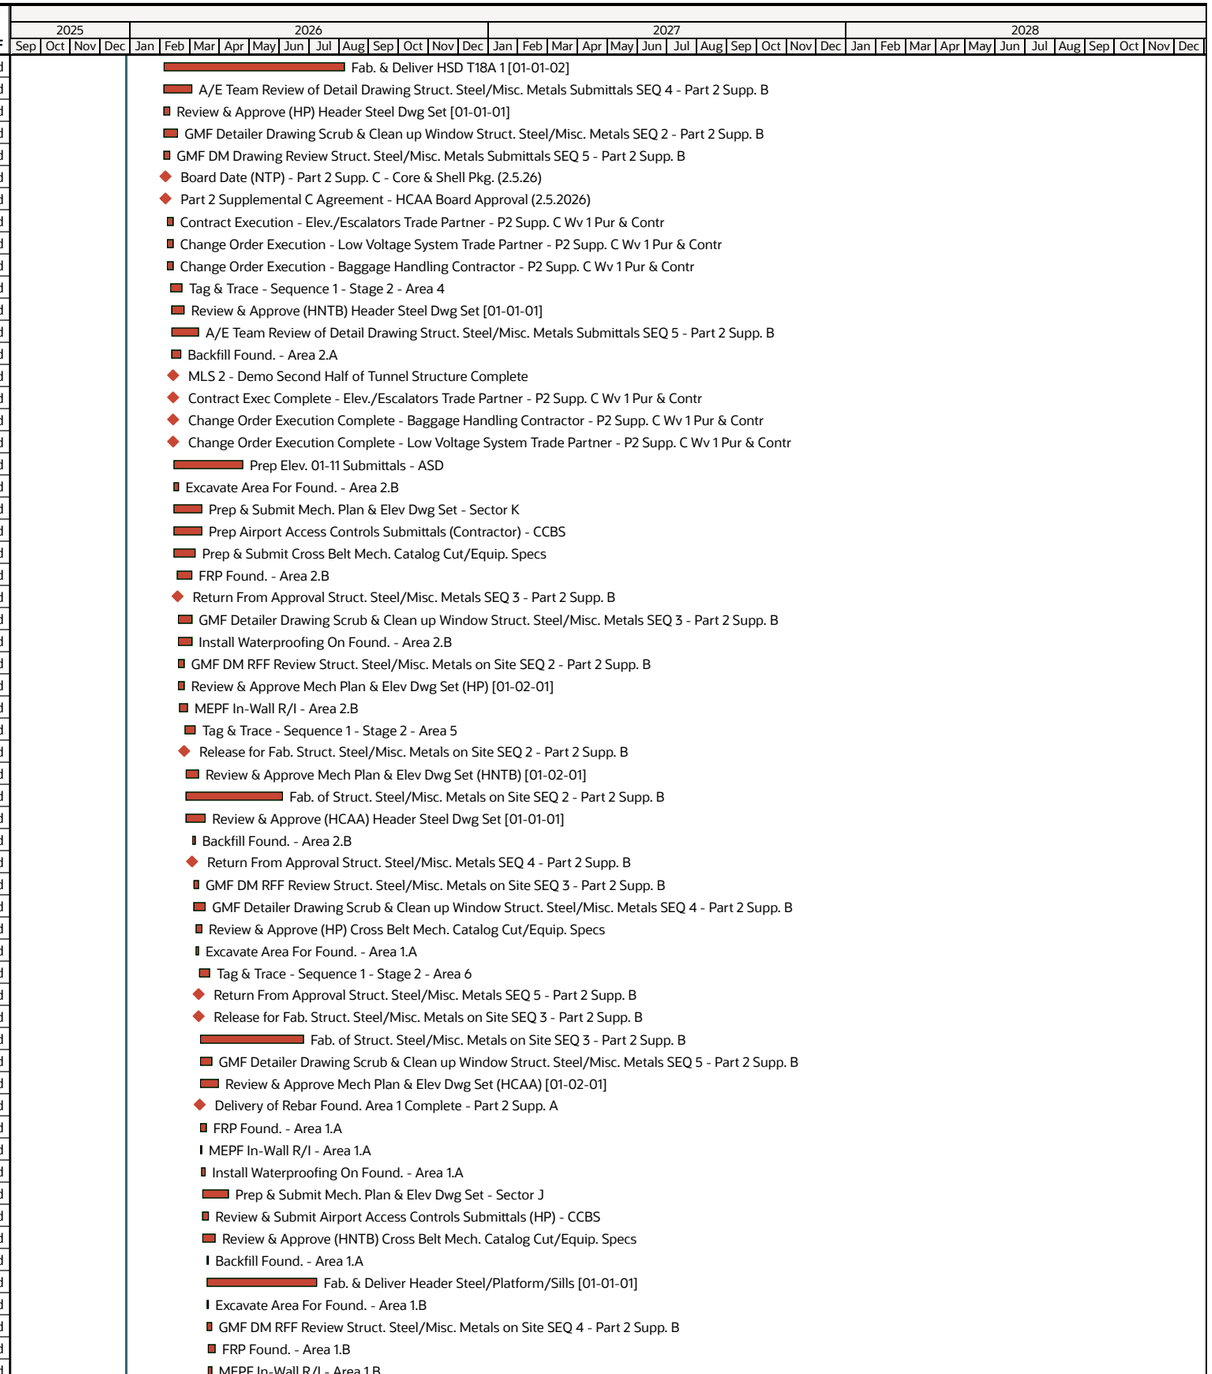

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
PR-P2-1C2-8180	Review & Approve Airport Access Controls Submittals (HNTB) - CCBS	10d	20-Mar-26	02-Apr-26	9d
GI-FS-A1-7050	Install Waterproofing On Found. - Area 1.B	4d	23-Mar-26	26-Mar-26	0d
TT-SQ1-SG3-A1-10	Tag & Trace - Sequence 1 - Stage 3 - Area 1	10d	23-Mar-26	03-Apr-26	0d
PR-P2-1B-3804	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0d		23-Mar-26	3d
PR-P2-1B-4880	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	5d	24-Mar-26	30-Mar-26	9d
PR-P2-1B-3700	Delivery of Steel Mill Order to GMF Shop - Part 2 Supp. A	0d		26-Mar-26	0d
PR-P2-1B-7670	Fab. of Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	37d	27-Mar-26	18-May-26	0d
GI-FS-A1-7060	Backfill Found. - Area 1.B	3d	27-Mar-26	31-Mar-26	0d
D1087	Review & Approve (HCAA) Cross Belt Mech. Catalog Cut/Equip. Specs	15d	27-Mar-26	16-Apr-26	7d
PR-P2-1B-4882	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	0d		30-Mar-26	9d
D1130	Prep & Submit Header Steel Dwg Set [01-02-01]	20d	31-Mar-26	27-Apr-26	6d
GI-FS-A1-6660	Excavate Area For Found. - Area 3	5d	01-Apr-26	07-Apr-26	0d
GI-FS-A1-6670	FRP Found. - Area 3	20d	02-Apr-26	29-Apr-26	0d
GI-FS-A1-6680	Install Waterproofing On Found. - Area 3	20d	03-Apr-26	30-Apr-26	0d
GI-FS-A1-6690	MEPF In-Wall R/I - Area 3	15d	03-Apr-26	23-Apr-26	1d
PR-P2-1C2-8190	Review & Approve Airport Access Controls Submittals (HCAA) - CCBS	15d	03-Apr-26	23-Apr-26	9d
TT-SQ1-SG3-A2-10	Tag & Trace - Sequence 1 - Stage 3 - Area 2	10d	06-Apr-26	17-Apr-26	0d
PR-P2-1B-3806	Fab. of Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	76d	07-Apr-26	23-Jul-26	3d
D1531	Prep & Submit Mech. Plan & Elev Dwg Set - Sector F	35d	10-Apr-26	29-May-26	0d
D1224	Prep & Submit Mech. Plan & Elev Dwg Set (XBM1) [01-03-01]	80d	17-Apr-26	10-Aug-26	7d
TT-SQ1-SG3-A3-10	Tag & Trace - Sequence 1 - Stage 3 - Area 3	10d	20-Apr-26	01-May-26	0d
GI-FS-A1-6700	Backfill Found. - Area 3	10d	22-Apr-26	05-May-26	0d
PR-P2-1B-4284	Fab. of Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	76d	24-Apr-26	11-Aug-26	9d
PR-P1-1C1-815	Review & Submit Elev. 01-11 Submittals (HP) - ASD	10d	24-Apr-26	07-May-26	0d
D3736	Review & Approve Header Steel Dwg Set (HP) [01-02-01]	5d	28-Apr-26	04-May-26	6d
TT-SQ1-SG3-A4-10	Tag & Trace - Sequence 1 - Stage 3 - Area 4	10d	04-May-26	15-May-26	0d
D3746	Review & Approve Header Steel Dwg Set (HNTB) [01-02-01]	10d	05-May-26	18-May-26	6d
GI-FS-A1-6710	Excavate Area For Found. - Area 5	5d	06-May-26	12-May-26	0d
GI-FS-A1-6720	FRP Found. - Area 5	15d	07-May-26	28-May-26	0d
GI-FS-A1-6740	MEPF In-Wall R/I - Area 5	10d	08-May-26	21-May-26	1d
GI-FS-A1-6730	Install Waterproofing On Found. - Area 5	15d	08-May-26	29-May-26	0d
PR-P1-1C1-1310	Review & Approve Elev. 01-11 Submittals (HNTB) - ASD	10d	08-May-26	21-May-26	0d
TT-SQ1-SG3-A5-10	Tag & Trace - Sequence 1 - Stage 3 - Area 5	10d	18-May-26	01-Jun-26	0d
PR-P2-1B-7680	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	0d		18-May-26	0d
GI-FS-110	Steel Framing Erection - Structure & Slabs (LOE)	181d	19-May-26	04-Feb-27	10d
D1132	Review & Approve Header Steel Dwg Set (HCAA) [01-02-01]	15d	19-May-26	09-Jun-26	6d
MLS-80	MLS - Structural Steel Erection Start	0d	19-May-26		0d
GI-FS-SQN-130	Erect & Bolt/Weld - NOVEMBER - Steel Seq. S1	8d	19-May-26	29-May-26	0d
PR-P1-1C1-1315	Review & Approve Elev. 01-11 Submittals (HCAA) - ASD	15d	22-May-26	12-Jun-26	0d
GI-FS-A1-6750	Backfill Found. - Area 5	7d	26-May-26	03-Jun-26	0d
D1062	Prep & Submit Estimated Parts List	30d	27-May-26	08-Jul-26	5d
GI-FS-SQN-150	Install Stairs - NOVEMBER - Steel Seq. S1	5d	01-Jun-26	05-Jun-26	0d
D1564	Prep & Submit Mech. Plan & Elev Dwg Set - Sector E	30d	01-Jun-26	13-Jul-26	0d
GI-FS-140	Steel Deck & Detailed Metal Decks - Structure & Slabs (LOE)	193d	01-Jun-26	04-Mar-27	10d
TT-SQ1-SG3-A6-10	Tag & Trace - Sequence 1 - Stage 3 - Area 6	10d	02-Jun-26	15-Jun-26	0d
PR-P2-1B-3746	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0d		03-Jun-26	5d
GI-FS-A1-6760	Excavate Area For Found. - Area 4	5d	04-Jun-26	10-Jun-26	0d
A108720	Low Voltage Ceiling & In-Wall Rough-In - PLC Room	10d	04-Jun-26	17-Jun-26	9d
GI-FS-A1-6770	FRP Found. - Area 4	15d	05-Jun-26	25-Jun-26	0d
GI-FS-SQN-170	Elevator Steel - NOVEMBER - Steel Seq. S1	3d	08-Jun-26	10-Jun-26	0d
GI-FS-A1-6780	Install Waterproofing On Found. - Area 4	15d	08-Jun-26	26-Jun-26	0d
HA-AL-CP-130	Concessions - RFP Development (HCAA)	132d	09-Jun-26	15-Dec-26	4d
GI-FS-A1-6790	MEPF In-Wall R/I - Area 4	10d	09-Jun-26	22-Jun-26	0d
D1133	Fab. & Deliver Header Steel/Platform/Sills [01-02-01]	80d	10-Jun-26	01-Oct-26	6d
GI-FS-SQA-10	Erect & Bolt/Weld Lower Steel - SEQ ALPHA - Steel (S2)	15d	11-Jun-26	01-Jul-26	0d
TC-GP-290	Demo Old Bessie Coleman Blvd & Rough Grade Area	10d	11-Jun-26	24-Jun-26	3d
PR-P1-1C1-3830	Fab. & Ship Elev. 06-07 - ASD	154d	13-Jun-26	16-Nov-26	2d
TT-SQ1-SG3-A7-10	Tag & Trace - Sequence 1 - Stage 3 - Area 7	10d	16-Jun-26	29-Jun-26	0d
A108740	Hang, Tape, & Finish New Walls - PLC Room	5d	18-Jun-26	24-Jun-26	9d
GI-FS-A1-6800	Backfill Found. - Area 4	7d	23-Jun-26	01-Jul-26	0d

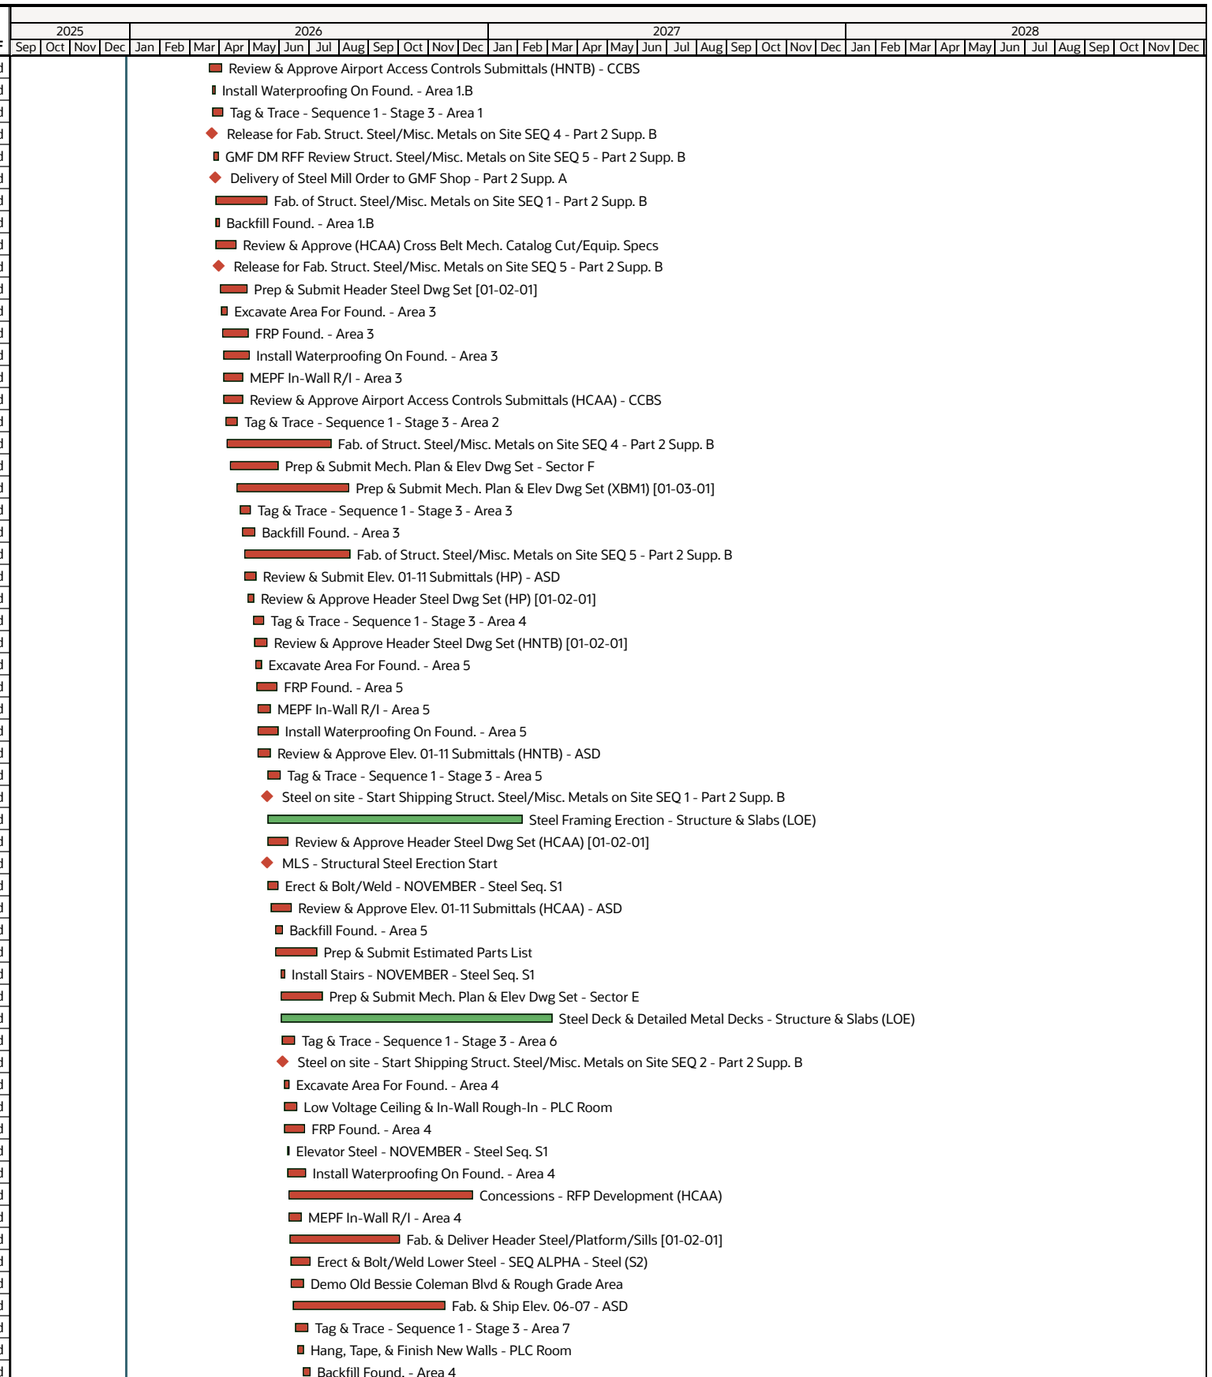

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
A108770	Install Flooring - PLC Room	10d	25-Jun-26	09-Jul-26	9d
PR-P2-1B-4876	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0d		26-Jun-26	3d
TC-FS-120	Install New Temp Barrier Mounted AOA Fence (Includes TSA Inspections)	20d	30-Jun-26	28-Jul-26	0d
TT-SQ1-SG3-A8-10	Tag & Trace - Sequence 1 - Stage 3 - Area 8	10d	30-Jun-26	14-Jul-26	0d
IPR-ITB1-MLS21	MLS21 - New Apron Cured & Ready for AOA Fence Relocation (Crisdel)	0d		30-Jun-26 C	0d
MLS-400	MLS - CIP Concrete Found. Complete	0d		01-Jul-26	0d
GI-FS-SQA-120	Erect & Bolt/Weld Upper Steel - SEQ ALPHA - Steel (S3)	11d	02-Jul-26	17-Jul-26	0d
GI-FS-A4-6290	Excavate - Deep UG LV Conduit - Low Voltage - Area 4.1	3d	02-Jul-26	07-Jul-26	0d
GI-FS-A4-6310	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 4.1	2d	08-Jul-26	09-Jul-26	0d
D1099	Prep Mech. Matl for Install [01-01-01]	20d	09-Jul-26	05-Aug-26	0d
D3036	Review & Approve (HP) Estimated Parts List	5d	09-Jul-26	15-Jul-26	5d
GI-FS-A4-6320	Inspect - Deep UG LV Conduit - Low Voltage - Area 4.1	2d	10-Jul-26	13-Jul-26	0d
A108780	Apply Final Paint - PLC Room	5d	10-Jul-26	16-Jul-26	9d
D1595	Prep & Submit Mech. Plan & Elev Dwg Set - Sector B	20d	14-Jul-26	10-Aug-26	0d
GI-FS-A4-6330	Backfill - Deep UG LV Conduit - Low Voltage - Area 4.1	3d	14-Jul-26	16-Jul-26	0d
BG-OPS-TC-40	Ticket Counter T18 - Out of Service (LOE)	53d	14-Jul-26	25-Sep-26	0d
TT-SQ1-SG3-A9-10	Tag & Trace - Sequence 1 - Stage 3 - Area 9	10d	15-Jul-26	28-Jul-26	0d
D3046	Review & Approve (HNTB) Estimated Parts List	10d	16-Jul-26	29-Jul-26	5d
A108790	Install OFCI Equip. & Furniture - PLC Room	5d	17-Jul-26	23-Jul-26	9d
GI-FS-A4-6690	Excavate - Deep UG Sanitary - Plumbing - Area 4.1	4d	17-Jul-26	22-Jul-26	0d
GI-FS-SQA-30	Install Stairs - SEQ ALPHA - Steel	4d	20-Jul-26	23-Jul-26	0d
GI-FS-SQA-20	Deck & Detail - SEQ ALPHA - Steel (S2 & S3)	20d	20-Jul-26	14-Aug-26	0d
GI-FS-A4-6700	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.1	4d	23-Jul-26	28-Jul-26	0d
PR-P2-1B-3808	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0d		23-Jul-26	3d
GI-FS-SQA-50	Elevator Steel - SEQ ALPHA - Steel	3d	24-Jul-26	28-Jul-26	0d
GI-FS-A4-6710	Inspect - Deep UG Sanitary - Plumbing - Area 4.1	2d	27-Jul-26	28-Jul-26	0d
TT-SQ1-SG3-A10-10	Tag & Trace - Sequence 1 - Stage 3 - Area 10	10d	29-Jul-26	11-Aug-26	0d
GI-FS-SQB-10	Erect & Bolt/Weld - SEQ BRAVO - Steel (S4)	12d	29-Jul-26	13-Aug-26	0d
GI-FS-A4-6720	Backfill - Deep UG Sanitary - Plumbing - Area 4.1	3d	29-Jul-26	31-Jul-26	0d
TC-FS-50	Remove Temp AOA Fence (Installed During Enabling)	20d	29-Jul-26	25-Aug-26	0d
D1066	Review & Approve (HCAA) Estimated Parts List	15d	30-Jul-26	19-Aug-26	5d
GI-FS-A4-6090	Excavate - Deep UG Sanitary - Plumbing - Area 4.2	4d	03-Aug-26	06-Aug-26	0d
D1107	Prep Mech. Matl for Install [01-01-02]	20d	06-Aug-26	02-Sep-26	0d
BI-ROW-BCC-180	Post-BHS Fire Sprinkler System Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BG-DM-MCP-4020	Post-BHS Elec. Systems Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BI-ROW-BCC-650	Post-BHS Technology & Data Systems Modifications - Area A [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
BI-ROW-BCC-640	Post-BHS HVAC & Plumbing Systems Modifications [01-01-01]	20d	06-Aug-26	02-Sep-26	5d
B	BHS - Mech & Elec. Install [01-01-01]	15d	06-Aug-26	26-Aug-26	0d
GI-FS-A4-6110	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.2	4d	07-Aug-26	12-Aug-26	0d
D1618	Prep & Submit Mech. Plan & Elev Dwg Set - Sector C	30d	11-Aug-26	22-Sep-26	0d
D1687	Prep & Submit Cross Belt Sorter XBM1 Elec. Drawings	80d	11-Aug-26	03-Dec-26	7d
GI-FS-A4-6170	Inspect - Deep UG Sanitary - Plumbing - Area 4.2	2d	11-Aug-26	12-Aug-26	0d
PR-P2-1B-4286	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 5- Part 2 Supp. B	0d		11-Aug-26	9d
TT-SQ1-SG3-A11-10	Tag & Trace - Sequence 1 - Stage 3 - Area 11	10d	12-Aug-26	25-Aug-26	0d
GI-FS-A4-6190	Backfill - Deep UG Sanitary - Plumbing - Area 4.2	3d	13-Aug-26	17-Aug-26	0d
GI-FS-SQB-20	Install Stairs - SEQ BRAVO - Steel	4d	14-Aug-26	19-Aug-26	0d
GI-FS-SQA-40	Turn Over to MEPF Contractors - SEQ ALPHA - Steel (S2 & S3)	0d		14-Aug-26	0d
GI-FS-SQA-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ ALPHA - SOMD	6d	17-Aug-26	24-Aug-26	0d
GI-FS-SQA-SOG-130	FRP Guideway Structure Column	10d	17-Aug-26	28-Aug-26	1d
GI-FS-SQA-SOMD-20	MEPF Hangers & Block Outs Club - SEQ ALPHA - SOMD	6d	17-Aug-26	24-Aug-26	0d
GI-FS-A4-6390	Excavate - Deep UG Sanitary - Plumbing - Area 4.3	6d	18-Aug-26	25-Aug-26	0d
GI-FS-SQB-50	Elevator Steel - SEQ BRAVO - Steel	3d	20-Aug-26	24-Aug-26	0d
GI-FS-SQC-10	Erect & Bolt/Weld - SEQ CHARLIE - Steel (S5)	12d	25-Aug-26	10-Sep-26	0d
GI-FS-SQA-SOMD-30	FRP Pour 1 Concourse - SEQ ALPHA - SOMD	6d	25-Aug-26	01-Sep-26	0d
MLS-SUPP.C-03	MLS 3 - Barrier Mounted AOA Fence Relocation Complete	0d		25-Aug-26 C	0d
GI-FS-A4-6440	Install Pipe - Deep UG Sanitary - Plumbing - Area 4.3	6d	26-Aug-26	02-Sep-26	0d
TT-SQ1-SG3-A12-10	Tag & Trace - Sequence 1 - Stage 3 - Area 12	10d	26-Aug-26	09-Sep-26	0d
C	BHS - T-T18 Tie-in & Overall Testing [01-01-01]	5d	27-Aug-26	02-Sep-26	0d
GI-FS-SQA-SOG-150	Install Guideway Structure Deck Shoring	5d	31-Aug-26	04-Sep-26	1d
GI-FS-A4-6490	Inspect - Deep UG Sanitary - Plumbing - Area 4.3	2d	01-Sep-26	02-Sep-26	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
GI-FS-SQA-SOMD-50	FRP Pour 2 Concourse - SEQ ALPHA - SOMD	6d	02-Sep-26	10-Sep-26	0d
GI-FS-A4-6510	Backfill - Deep UG Sanitary - Plumbing - Area 4.3	2d	03-Sep-26	04-Sep-26	0d
A105680	HVAC & Plumbing Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105690	Technology & Data Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105670	Elec. Systems Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A105700	Fire Protection System Modifications [01-01-02]	5d	03-Sep-26	10-Sep-26	5d
A1	BHS - Mech / Elec. Demo & Install of C11 & T18 [01-01-02]	7d	03-Sep-26	14-Sep-26	0d
BG-OPS-TC-30	Ticket Counter C11E - Out of Service (LOE)	10d	03-Sep-26	17-Sep-26	0d
GI-FS-SQA-SOG-200	FRP Guideway Structure Deck	5d	08-Sep-26	14-Sep-26	1d
GI-FS-4350	Prep & Submit Pre-Substantial Completion Documentation - Found. Scope	20d	08-Sep-26	05-Oct-26	0d
B1	BHS - Testing [01-01-02]	8d	08-Sep-26	17-Sep-26	0d
BG-BI-ROW-90	Demo MCP 5 Feeder Back to Source [HMCP-3] [01-01-02]	10d	09-Sep-26	22-Sep-26	3d
TT-SQ1-SG3-A13-10	Tag & Trace - Sequence 1 - Stage 3 - Area 13	10d	10-Sep-26	23-Sep-26	0d
GI-FS-SQC-30	Install Stairs - SEQ CHARLIE - Steel	4d	11-Sep-26	16-Sep-26	0d
GI-FS-SQA-SOMD-60	FRP Pour 3 Concourse - SEQ ALPHA - SOMD	6d	11-Sep-26	18-Sep-26	0d
A104130	Infill C11-01 Penetration Along Grid L [01-01-02]	4d	15-Sep-26	18-Sep-26	0d
GI-FS-SQA-SOG-210	Guideway Structure Deck Cure	7d	15-Sep-26	23-Sep-26	1d
GI-FS-SQC-50	Elevator Steel - SEQ CHARLIE - Steel	3d	17-Sep-26	21-Sep-26	0d
A105740	Fire Protection Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105720	HVAC & Plumbing Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105730	Technology & Data Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A105710	Elec. Systems Modifications [01-01-03]	5d	18-Sep-26	24-Sep-26	6d
A3	BHS - Mech / Elec. Demo & Install of T18 [01-01-03]	5d	18-Sep-26	24-Sep-26	0d
RI-C2-SP-1370	Install Train Tube Metal Deck - SMP/Train Tube - INTR - C2	5d	21-Sep-26	25-Sep-26	0d
A104150	Infill T18 Penetration Along Grid L [01-01-03]	5d	21-Sep-26	25-Sep-26	0d
GI-FS-SQD-10	Erect & Bolt/Weld Lower Steel - SEQ DELTA - Steel (S7)	8d	22-Sep-26	01-Oct-26	10d
GI-FS-SQI-10	Erect & Bolt/Weld - SEQ INDIA - Steel (S6)	6d	22-Sep-26	29-Sep-26	0d
D5696	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector C	5d	23-Sep-26	29-Sep-26	0d
TT-SQ1-SG3-A14-10	Tag & Trace - Sequence 1 - Stage 3 - Area 14	10d	24-Sep-26	07-Oct-26	0d
GI-FS-SQA-SOG-250	Guideway Structure Shoring Removal	5d	24-Sep-26	30-Sep-26	1d
D1788	BHS - Testing T18 [01-01-03]	1d	25-Sep-26	25-Sep-26	0d
RI-C2-SP-1420	Install Temp Tunnel Peel & Stick - SMP/Train Tube - INTR - C2	10d	28-Sep-26	09-Oct-26	0d
A3.5	BHS - Mech / Elec. Demo & Install of TC2 [01-01-03]	5d	28-Sep-26	02-Oct-26	0d
D5706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector C	10d	30-Sep-26	13-Oct-26	0d
GI-FS-SQI-30	Install Stairs - SEQ INDIA - Steel	5d	30-Sep-26	06-Oct-26	0d
GI-FS-SQA-SOG-10	Underground MEPF - Pour 1 - SEQ ALPHA - SOG	5d	01-Oct-26	07-Oct-26	1d
D1134	Prep Mech. Matl for Install [01-02-01]	20d	02-Oct-26	29-Oct-26	6d
GI-FS-SQD-70	Erect & Bolt/Weld Upper Steel - SEQ DELTA - Steel (10)	9d	02-Oct-26	14-Oct-26	10d
D1793	Internal Commissioning / Functional Testing / Owner Testing [01-01-03]	1d	05-Oct-26	05-Oct-26	0d
GI-FS-4360	Substantial Completion Final Clean - Found. Scope	5d	06-Oct-26	12-Oct-26	0d
A4	BHS - Mech / Elec. Demo & Install of T17 [01-01-04]	5d	06-Oct-26	12-Oct-26	0d
GI-FS-SQI-50	Elevator Steel - SEQ INDIA - Steel	3d	07-Oct-26	09-Oct-26	0d
TT-SQ1-SG3-A15-10	Tag & Trace - Sequence 1 - Stage 3 - Area 15	10d	08-Oct-26	21-Oct-26	0d
GI-FS-SQA-SOG-30	FRP Pour 1 - SEQ ALPHA - SOG	7d	08-Oct-26	16-Oct-26	1d
RI-C2-SP-1230	Layout Walls/Top Track - SMP/Train Tube - INTR - C2	5d	12-Oct-26	16-Oct-26	0d
D1800	Internal Commissioning / Functional Testing / Owner Testing (T17 03/04, T17 04 FSD) [01-01-04]	1d	12-Oct-26	12-Oct-26	0d
GI-FS-SQJ-70	Erect & Bolt/Weld Lower Steel - SEQ JULIET - Steel (S8)	8d	12-Oct-26	21-Oct-26	0d
D1801	Mech Remove Stainless Shrouding (T17 01/02) [01-01-04]	1d	13-Oct-26	13-Oct-26	0d
GI-FS-4370	Final Insp. - Found. Scope	5d	13-Oct-26	19-Oct-26	0d
D1619	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector C	15d	14-Oct-26	03-Nov-26	0d
D1802	Elec. Recontrol (Reverse) (T17 01/02) [01-01-04]	2d	14-Oct-26	15-Oct-26	0d
GI-FS-SQD-30	Install Stairs - SEQ DELTA - Steel	5d	15-Oct-26	21-Oct-26	10d
D1805	Mech Stainless Shrouding (T17 01/02) [01-01-04]	1d	16-Oct-26	16-Oct-26	0d
GI-FS-4380	HP Pre Substantial Completion QC Insp. - Found. Scope	2d	16-Oct-26	19-Oct-26	0d
D1804	Internal Commissioning / Functional Testing / Owner Testing (T17 01/02) [01-01-04]	1d	16-Oct-26	16-Oct-26	0d
D1806	Elec. Demo (T17 03/04) [01-01-04]	1d	19-Oct-26	19-Oct-26	0d
RI-C2-SP-1320	Frame Walls Train Tube A - SMP/Train Tube - INTR - C2	15d	19-Oct-26	06-Nov-26	0d
GI-FS-4390	Substantial Completion Insp. - Found. Scope	2d	20-Oct-26	21-Oct-26	0d
D1807	Mech Demo (T17 03/04) [01-01-04]	1d	20-Oct-26	20-Oct-26	0d
A107620	Install Temp Partition Walls Around T15 & T16 Counters [01-01-05]	2d	21-Oct-26	22-Oct-26	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
MLS-SUPP.C-04	MLS 4 - Supplement A Substantial Completion	0d		21-Oct-26 C	0d
TT-SQ1-SG3-A16-10	Tag & Trace - Sequence 1 - Stage 3 - Area 16	10d	22-Oct-26	04-Nov-26	0d
GI-FS-SQJ-10	Erect & Bolt/Weld Upper Steel - SEQ JULIET - Steel (S9)	7d	22-Oct-26	30-Oct-26	0d
RI-AP2-300	Layout Walls/Top Track - Overall Rough-in - INTR - AP 2	5d	22-Oct-26	28-Oct-26	1d
GI-FS-SQD-50	Elevator Steel - SEQ DELTA - Steel	3d	22-Oct-26	26-Oct-26	10d
A5	BHS - Mech / Elec. Demo & Install of T15 [01-01-05]	5d	23-Oct-26	29-Oct-26	0d
GI-FS-SQE-10	Erect & Bolt/Weld - SEQ ECHO - Steel (S12)	6d	27-Oct-26	03-Nov-26	10d
RI-AP2-5720	Install Block Walls/Masonry Door Frames - INTR - AP 2	15d	29-Oct-26	18-Nov-26	1d
D1813	Internal Commissioning / Functional Testing / Owner Testing T15 [01-01-05]	1d	30-Oct-26	30-Oct-26	0d
GI-FS-SQJ-30	Install Stairs - SEQ JULIET - Steel	5d	02-Nov-26	06-Nov-26	0d
GI-FS-SQJ-20	Deck & Detail - SEQ JULIET - Steel (S8 & S9)	20d	02-Nov-26	01-Dec-26	7d
B5	BHS - Mech / Elec. Demo & Install of T16 [01-01-05]	4d	02-Nov-26	05-Nov-26	0d
D1622	Prep & Submit Header Steel Dwg Set - Sector C	20d	04-Nov-26	03-Dec-26	0d
GI-FS-SQE-30	Install Stairs - SEQ ECHO - Steel	5d	04-Nov-26	10-Nov-26	10d
TT-SQ1-SG3-A17-10	Tag & Trace - Sequence 1 - Stage 3 - Area 17	10d	05-Nov-26	18-Nov-26	0d
D1820	Internal Commissioning / Functional Testing / Owner Testing T16 [01-01-05]	1d	06-Nov-26	06-Nov-26	0d
A6	BHS - Mech / Elec. Demo & Install of TC2 [01-02-01]	4d	09-Nov-26	12-Nov-26	0d
GI-FS-SQJ-50	Elevator Steel - SEQ JULIET - Steel	3d	09-Nov-26	11-Nov-26	0d
RI-C2-SP-1390	Frame Walls Train Tube B - SMP/Train Tube - INTR - C2	15d	09-Nov-26	01-Dec-26	0d
GI-FS-SQE-50	Elevator Steel - SEQ ECHO - Steel	3d	11-Nov-26	13-Nov-26	10d
GI-FS-SQK-10	Erect & Bolt/Weld Lower Steel - SEQ KILO - Steel (S11)	14d	12-Nov-26	03-Dec-26	0d
D1828	Internal Commissioning / Functional Testing / Owner Testing [01-02-01]	1d	13-Nov-26	13-Nov-26	0d
GI-FS-SQF-10	Erect & Bolt/Weld - SEQ FOXTROT - Steel (S14)	11d	16-Nov-26	02-Dec-26	10d
D1832	Elec. Install MPP A1, FCP A1, MPP A9, FCP A9 [01-02-02]	9d	16-Nov-26	30-Nov-26	10d
D1835	Mech Install (AS7 3B/3D, AX9 01) [01-02-02]	1d	16-Nov-26	16-Nov-26	0d
PR-P1-1C1-3850	Delivery of Elev. 06-07 on Site - ASD	0d		16-Nov-26	2d
D1837	Elec. Install (AS7 3B/3D, AX9 01) [01-02-02]	12d	17-Nov-26	04-Dec-26	0d
PR-P1-1C1-3840	Off Site Staging of Elev. 06-07 - ASD	497d	17-Nov-26	11-Apr-28	2d
RI-AP3-5760	Install Block Walls/Masonry Door Frames - Overall Rough-in - INTR - AP 3	15d	19-Nov-26	11-Dec-26	1d
TT-SQ1-SG3-A18-10	Tag & Trace - Sequence 1 - Stage 3 - Area 18	10d	19-Nov-26	04-Dec-26	0d
GI-FS-SQJ-40	Turn Over to MEPF Contractors - SEQ JULIET - Steel (S8 & S9)	0d		01-Dec-26	7d
RI-C2-SP-1430	Install Fall Protection Anchors Train A & Train B - SMP/Train Tube - INTR - C2	5d	02-Dec-26	08-Dec-26	0d
GI-FS-SQJ-SOMD-10	MEPF Hangers & Block Outs Club - SEQ JULIET - SOMD	6d	02-Dec-26	09-Dec-26	7d
GI-FS-SQJ-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ JULIET - SOMD	6d	02-Dec-26	09-Dec-26	7d
GI-FS-SQF-30	Install Stairs - SEQ FOXTROT - Steel	4d	03-Dec-26	08-Dec-26	10d
D6146	Review & Approve (HP) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	04-Dec-26	23-Dec-26	7d
D5716	Review & Approve Header Steel Dwg Set (HP) - Sector C	5d	04-Dec-26	10-Dec-26	0d
GI-FS-SQK-70	Erect & Bolt/Weld Upper Steel - SEQ KILO - Steel (S13)	8d	04-Dec-26	15-Dec-26	0d
D1838	Elec. Install (AX9 12/15, C8A 11/12, T12 25/26) [01-02-02]	6d	07-Dec-26	14-Dec-26	0d
TT-SQ1-SG3-A19-10	Tag & Trace - Sequence 1 - Stage 3 - Area 19	10d	07-Dec-26	18-Dec-26	0d
D1839	Internal Commissioning / Functional Testing / Owner Testing (AS7 3B/3D, AX9 01) [01-02-02]	1d	07-Dec-26	07-Dec-26	5d
GI-FS-SQF-50	Elevator Steel - SEQ FOXTROT - Steel	3d	09-Dec-26	11-Dec-26	10d
RI-C2-SP-1260	Install Fireproofing - SMP/Train Tube - INTR - C2	5d	09-Dec-26	15-Dec-26	0d
GI-FS-SQJ-SOMD-30	FRP Pour 1 Concourse - SEQ JULIET - SOMD	6d	10-Dec-26	17-Dec-26	7d
GI-FS-SQJ-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ JULIET - SOMD	6d	10-Dec-26	17-Dec-26	7d
D5726	Review & Approve Header Steel Dwg Set (HNTB) - Sector C	10d	11-Dec-26	24-Dec-26	0d
GI-FS-SQG-70	Erect & Bolt/Weld Lower Steel - SEQ GOLF - Steel (S16)	9d	14-Dec-26	24-Dec-26	10d
RI-AP3-5770	Elec. Rough-in Block Walls - Overall Rough-in - INTR - AP 3	15d	14-Dec-26	05-Jan-27	1d
ASD-SK-700	Architectural Pre-Cast Wall Panels (LOE)	106d	15-Dec-26	13-May-27	10d
D1841	Internal Commissioning / Functional Testing / Owner Testing (AX9 12/15, C8A 11/12, T12 25/26) [01...	1d	15-Dec-26	15-Dec-26	0d
GI-FS-SQK-20	Deck & Detail - SEQ KILO - Steel (S11 & S13)	20d	16-Dec-26	14-Jan-27	0d
D1843	Mech Install (T-T12 24/25 & 27/28, T-AX9 11, Temp Diverter Plate PS-AX8 01) [01-02-03]	3d	16-Dec-26	18-Dec-26	0d
BG-OPS-TC-90	TA2 - Out of Service [Contingency Porters Required] (LOE)	4d	16-Dec-26	21-Dec-26	0d
RI-C2-SP-1280	Install Elec. OH Rough-in - SMP/Train Tube - INTR - C2	10d	16-Dec-26	30-Dec-26	0d
GI-FS-SQL-10	Erect & Bolt/Weld - SEQ LIMA - Steel (S15)	13d	16-Dec-26	05-Jan-27	0d
D1846	Mech Demo (T12 24/25, TA2 06) [01-02-03]	1d	16-Dec-26	16-Dec-26	2d
RI-C2-SP-1290	Low Voltage Rough-in Ceilings - SMP/Train Tube - INTR - C2	10d	16-Dec-26	30-Dec-26	0d
D1844	Elec. Install (T12 24, T 25/28, AX9 11) [01-02-03]	3d	16-Dec-26	18-Dec-26	0d
GI-FS-SQK-50	Elevator Steel - SEQ KILO - Steel	3d	16-Dec-26	18-Dec-26	0d
D1845	Elec. Demo (T12 24/25, TA2 06) [01-02-03]	1d	16-Dec-26	16-Dec-26	2d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update


Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical

Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
GI-FS-SQJ-SOMD-50	FRP Pour 2 Concourse - SEQ JULIET - SOMD	6d	18-Dec-26	28-Dec-26	7d
TT-SQ1-SG3-A20-10	Tag & Trace - Sequence 1 - Stage 3 - Area 20	10d	21-Dec-26	05-Jan-27	0d
D1847	Internal Commissioning / Functional Testing / Owner Testing [01-02-03]	1d	21-Dec-26	21-Dec-26	0d
D1852	Mec Install (AX9 10/11, TA1 12/14) [01-02-04]	4d	22-Dec-26	28-Dec-26	0d
BG-OPS-TC-100	TA1 - Out of Service [Contingency Porters Required] (LOE)	5d	22-Dec-26	29-Dec-26	0d
D1850	Elec. Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1d	22-Dec-26	22-Dec-26	3d
D1851	Mech Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1d	22-Dec-26	22-Dec-26	3d
D1853	Elec. Install (AX9 10/11, TA1 12/14) [01-02-04]	4d	22-Dec-26	28-Dec-26	0d
D6156	Review & Approve (HNTB) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	24-Dec-26	14-Jan-27	7d
HA-AL-CP-150	Concessions - Concessionaires RFP Solicitation (HCAA)	177d	24-Dec-26	02-Sep-27	4d
D1633	Review & Approve Header Steel Dwg Set (HCAA) - Sector C	15d	28-Dec-26	18-Jan-27	0d
GI-FS-SQG-10	Erect & Bolt/Weld Upper Steel - SEQ GOLF - Steel (S18)	9d	28-Dec-26	08-Jan-27	10d
D1854	Internal Commissioning / Functional Testing / Owner Testing [01-02-04]	1d	29-Dec-26	29-Dec-26	0d
GI-FS-SQJ-SOMD-70	7 Day Concrete Cure - Concourse - SEQ JULIET - SOMD	7d	29-Dec-26	05-Jan-27	9d
D1856	Elec. Demo [01-03-01]	30d	30-Dec-26	10-Feb-27	0d
BG-MLS-OPS-20	MEM1 - Permanently Out of Service	0d		30-Dec-26	0d
D1857	Mech Demo [01-03-01]	30d	30-Dec-26	10-Feb-27	0d
RI-C2-SP-1350	Install Sheathing - SMP/Train Tube - INTR - C2	6d	31-Dec-26	08-Jan-27	0d
TT-SQ1-SG3-A21-10	Tag & Trace - Sequence 1 - Stage 3 - Area 21	10d	06-Jan-27	19-Jan-27	0d
RI-AP3-1404	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 3	5d	06-Jan-27	12-Jan-27	1d
GI-FS-SQL-20	Deck & Detail - SEQ LIMA - Steel (S15)	20d	06-Jan-27	02-Feb-27	0d
RI-C11-R1-10	Layout Walls/Top Track - Overall/Restrooms - INTR - C11	10d	06-Jan-27	19-Jan-27	7d
GI-FS-SQL-30	Install Stairs - SEQ LIMA - Steel	5d	06-Jan-27	12-Jan-27	0d
BI-ROW-BR-P8-100	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS8 [01-03-01]	15d	07-Jan-27	27-Jan-27	0d
GI-FS-SQG-20	Install Stairs - SEQ GOLF - Steel	5d	11-Jan-27	15-Jan-27	10d
RI-C2-SP-1340	Install Vapor Barrier System - SMP/Train Tube - INTR - C2	10d	11-Jan-27	22-Jan-27	0d
GI-FS-SQL-50	Elevator Steel - SEQ LIMA - Steel	3d	13-Jan-27	15-Jan-27	0d
RI-AP3-PDS-5800	Install Fire Sprinkler Hangers - PDS Room 6097 - INTF - AP 3	2d	13-Jan-27	14-Jan-27	1d
RI-AP3-1240	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 3	2d	13-Jan-27	14-Jan-27	1d
GI-FS-SQK-40	Turn Over to MEPF Contractors - SEQ KILO - Steel (S11 & S13)	0d		14-Jan-27	0d
RI-AP3-PDS-5810	Install CHW Hangers - PDS Room 6097 - INTF - AP 3	2d	15-Jan-27	18-Jan-27	1d
D1688	Review & Approve (HCAA) Cross Belt Sorter XBM1 Elect Dwg Sets	14d	15-Jan-27	03-Feb-27	7d
GI-FS-SQK-SOMD-10	MEPF & BHS Hangers & Block Outs Concourse - SEQ KILO - SOMD	6d	15-Jan-27	22-Jan-27	0d
GI-FS-SQG-50	Elevator Steel - SEQ GOLF - Steel	3d	18-Jan-27	20-Jan-27	10d
GI-FS-SQM-70	Erect & Bolt/Weld - SEQ MIKE - Steel (S17)	6d	18-Jan-27	25-Jan-27	0d
D1634	Fab. & Deliver Header Steel/Platform/Sills - Sector C	80d	19-Jan-27	10-May-27	0d
RI-AP3-PDS-5820	Install Plumbing Hangers - PDS Room 6097 - INTF - AP 3	2d	19-Jan-27	20-Jan-27	1d
RI-C11-R1-6140	Install Fire Sprinkler Hangers - Overall/Restrooms - INTR - C11	2d	20-Jan-27	21-Jan-27	7d
TT-SQ1-SG3-A22-10	Tag & Trace - Sequence 1 - Stage 3 - Area 22	10d	20-Jan-27	02-Feb-27	0d
GI-FS-SQH-10	Erect & Bolt/Weld - SEQ HOTEL - Steel (S19)	11d	21-Jan-27	04-Feb-27	10d
RI-AP3-PDS-5830	Install Elec. Hangers - PDS Room 6097 - INTF - AP 3	2d	21-Jan-27	22-Jan-27	1d
RI-C11-R1-6150	Install Duct Hangers - Overall/Restrooms - INTR - C11	2d	22-Jan-27	25-Jan-27	7d
GI-FS-SQK-SOMD-20	FRP Pour 1 Concourse - SEQ KILO - SOMD	6d	25-Jan-27	01-Feb-27	0d
RI-AP3-PDS-5840	Install Fireproofing - PDS Room 6097 - INTF - AP 3	5d	25-Jan-27	29-Jan-27	1d
RI-C2-SP-1360	Install Metal Panel Support Hat Channel- SMP/Train Tube - INTR - C2	4d	25-Jan-27	28-Jan-27	0d
RI-C11-R1-6160	Install CHW Hangers - Overall/Restrooms - INTR - C11	2d	26-Jan-27	27-Jan-27	7d
GI-FS-SQM-80	Deck & Detail - SEQ MIKE - Steel (S17)	20d	26-Jan-27	22-Feb-27	0d
RI-C11-R1-6170	Install Plumbing Hangers - Overall/Restrooms - INTR - C11	5d	28-Jan-27	03-Feb-27	7d
BI-ROW-BR-P7-70	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS7 [01-03-01]	15d	28-Jan-27	17-Feb-27	9d
D1862	Mech Install (Sector J) [01-03-01]	30d	28-Jan-27	10-Mar-27	0d
RI-C2-SP-1400	Metal Panel Wall System Scan - SMP/Train Tube - INTR - C2	5d	29-Jan-27	04-Feb-27	0d
RI-AP3-PDS-5860	Install CHW OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	01-Feb-27	05-Feb-27	1d
RI-AP3-PDS-5870	Install Plumbing OH Rough-in - PDS Room 6097 - INTF - AP 3	2d	01-Feb-27	02-Feb-27	1d
GI-FS-SQK-SOMD-40	FRP Pour 2 Concourse - SEQ KILO - SOMD	6d	02-Feb-27	09-Feb-27	0d
TT-SQ1-SG3-A23-10	Tag & Trace - Sequence 1 - Stage 3 - Area 23	10d	03-Feb-27	16-Feb-27	0d
D1690	Fab. & Deliver XBM1 Power Panels (13)	80d	04-Feb-27	26-May-27	7d
RI-C11-R1-6180	Install Elec. Hangers - Overall/Restrooms - INTR - C11	2d	04-Feb-27	05-Feb-27	7d
D1691	Fab. & Deliver XBM1 Field Control Panels, Elect Field Devices, Cabling	80d	04-Feb-27	26-May-27	7d
GI-FS-SQH-30	Deck & Detail - SEQ HOTEL - Steel (S19)	20d	05-Feb-27	04-Mar-27	10d
RI-C2-SP-1410	Metal Panel Wall System Fab. - SMP/Train Tube - INTR - C2	20d	05-Feb-27	04-Mar-27	0d

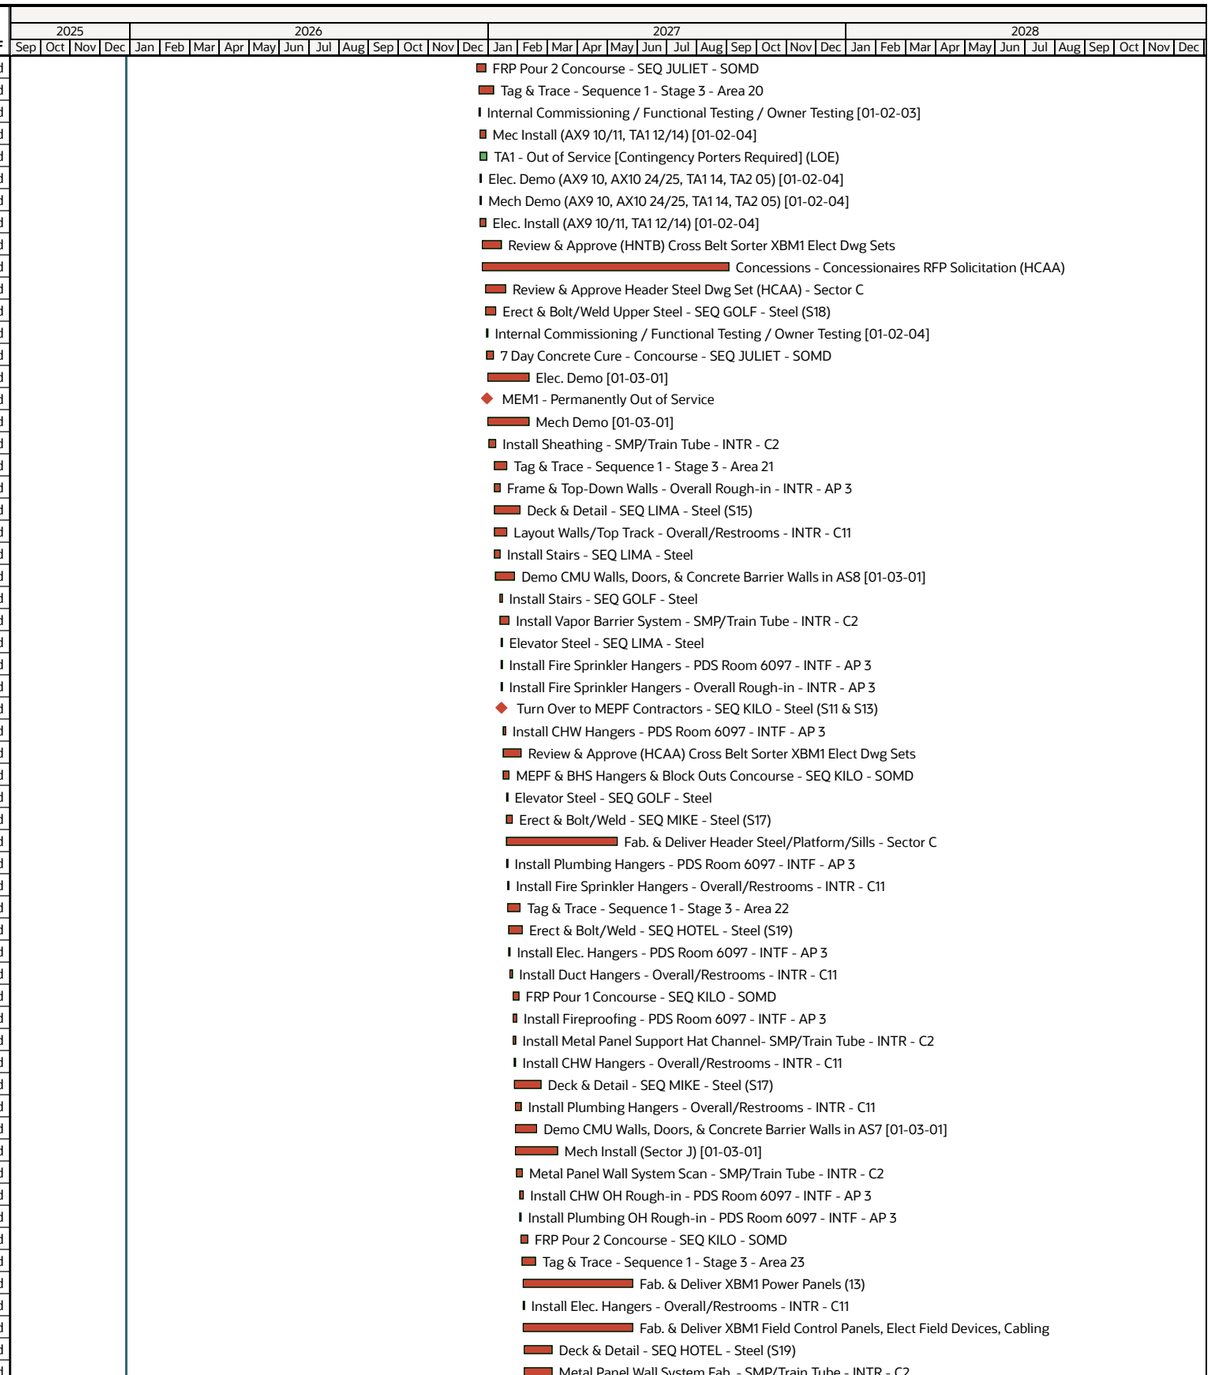

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
GI-FS-SQL-40	Turn Over to MEPF Contractors - SEQ LIMA - Steel (S15)	0d		05-Feb-27	0d
GI-FS-SQL-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ LIMA - SOMD	6d	08-Feb-27	15-Feb-27	0d
RI-AP3-PDS-5880	Install Duct OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	08-Feb-27	12-Feb-27	1d
RI-C11-R1-6190	Install Fireproofing - Overall/Restrooms - INTR - C11	3d	08-Feb-27	10-Feb-27	7d
GI-FS-SQK-SOMD-50	FRP Pour 3 Concourse - SEQ KILO - SOMD	6d	10-Feb-27	17-Feb-27	0d
RI-C11-R1-6250	Fire Sprinkler Mains & Branch Line Rough-in - Overall/Restrooms - INTR - C11	10d	11-Feb-27	24-Feb-27	7d
RI-AP3-PDS-5890	Fire Sprinkler Mains & Branch Line Rough-in - PDS Room 6097 - INTF - AP 3	5d	15-Feb-27	19-Feb-27	1d
GI-FS-SQL-SOMD-30	FRP Pour 1 Concourse - SEQ LIMA - SOMD	6d	16-Feb-27	23-Feb-27	0d
TT-SQ1-SG3-A24-10	Tag & Trace - Sequence 1 - Stage 3 - Area 24	10d	17-Feb-27	02-Mar-27	0d
GI-FS-SQK-SOMD-60	FRP Pour 4 Concourse - SEQ KILO - SOMD	6d	18-Feb-27	25-Feb-27	0d
BI-ROW-BR-P7-130	Demo BHS Access Platform in AS7 [01-03-01]	3d	18-Feb-27	22-Feb-27	9d
RI-AP3-PDS-5910	Install Elec. OH Rough-in - PDS Room 6097 - INTF - AP 3	5d	22-Feb-27	26-Feb-27	1d
GI-FS-SQM-100	Turn Over to MEPF Contractors - SEQ MIKE - Steel (S17)	0d		22-Feb-27	0d
GI-FS-SQM-SOMD-50	MEPF Hangers & Block Outs Concourse - SEQ MIKE - SOMD	6d	23-Feb-27	02-Mar-27	0d
BI-ROW-BR-P7-140	Patch & Seal Concrete @ Former BHS Access Platform in AS7 [01-03-01]	3d	23-Feb-27	25-Feb-27	9d
GI-FS-SQL-SOMD-40	FRP Pour 2 Concourse - SEQ LIMA - SOMD	6d	24-Feb-27	03-Mar-27	0d
RI-C11-R1-6210	Install CHW OH Rough-in - Overall/Restrooms - INTR - C11	8d	25-Feb-27	08-Mar-27	9d
RI-C11-R1-6200	Install Plumbing OH Rough-in - Overall/Restrooms - INTR - C11	10d	25-Feb-27	10-Mar-27	7d
GI-FS-SQK-SOMD-80	7 Day Concrete Cure - Concourse - SEQ KILO - SOMD	7d	26-Feb-27	04-Mar-27	0d
RI-AP3-PDS-5930	FRP Alstom PDS Elec. Pads - PDS Room 6097 - INTF - AP 3	5d	01-Mar-27	05-Mar-27	1d
RI-AP3-PDS-5920	Install Low Voltage OH Rough-in - PDS Room 6097 - INTF - AP 3	2d	01-Mar-27	02-Mar-27	4d
TT-SQ1-SG3-A25-10	Tag & Trace - Sequence 1 - Stage 3 - Area 25	10d	03-Mar-27	16-Mar-27	0d
GI-FS-SQM-SOMD-70	FRP Pour 1 Concourse - SEQ MIKE - SOMD	6d	03-Mar-27	10-Mar-27	0d
GI-FS-SQL-SOMD-50	7 Day Concrete Cure - SEQ LIMA - SOMD	7d	04-Mar-27	10-Mar-27	0d
GI-FS-SQH-40	Turn Over to MEPF Contractors - SEQ HOTEL - Steel (S19)	0d		04-Mar-27	10d
MLS-95	MLS - Structural Steel Erection Complete	0d		04-Mar-27	10d
RI-C8-2520	Dancefloor Install Phase 2 - Overall - INTR - C8 Ph2	33d	05-Mar-27	20-Apr-27	0d
FN-C2-SP-1440	Install Metal Wall Panels - SMP/Train Tube - INTR - C2	20d	05-Mar-27	01-Apr-27	0d
GI-FS-SQH-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ HOTEL - SOMD	6d	05-Mar-27	12-Mar-27	10d
RI-AP3-PDS-5990	Patch Fireproofing - PDS Room 6097 - INTF - AP 3	2d	08-Mar-27	09-Mar-27	1d
FN-AP3-PDS-660	Prime & One Coat Paint - PDS Room 6097 - INTF - AP 3	5d	10-Mar-27	16-Mar-27	1d
GI-FS-SQL-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ LIMA - SOMD	6d	11-Mar-27	18-Mar-27	0d
GI-FS-SQM-SOMD-80	FRP Pour 2 Concourse - SEQ MIKE - SOMD	6d	11-Mar-27	18-Mar-27	0d
RI-C11-R1-6220	Install Duct OH Rough-in - Overall/Restrooms - INTR - C11	8d	11-Mar-27	22-Mar-27	7d
D1867	Mech Install (Sector H) [01-03-01]	75d	11-Mar-27	24-Jun-27	0d
GI-FS-SQH-SOMD-30	FRP Pour 1 Concourse - SEQ HOTEL - SOMD	6d	15-Mar-27	22-Mar-27	10d
FN-AP3-PDS-680	Install Doors & Hardware - PDS Room 6097 - INTF - AP 3	2d	17-Mar-27	18-Mar-27	1d
TT-SQ1-SG3-A26-10	Tag & Trace - Sequence 1 - Stage 3 - Area 26	10d	17-Mar-27	30-Mar-27	0d
SK-RO-450	Install TPO Roofing - Mid Roof TPO 1.A	15d	19-Mar-27	08-Apr-27	0d
FN-AP3-PDS-690	Install Light Fixtures & Trim - PDS Room 6097 - INTF - AP 3	5d	19-Mar-27	25-Mar-27	1d
FN-AP3-PDS-800	Install Coil Roll-Up Doors (6097E & 6097C) - PDS Room 6097 - INTF - AP 3	5d	19-Mar-27	25-Mar-27	10d
GI-FS-SQM-SOMD-90	7 Day Concrete Cure - SEQ MIKE - SOMD	7d	19-Mar-27	25-Mar-27	0d
GI-FS-SQH-SOMD-40	FRP Pour 2 Concourse - SEQ HOTEL - SOMD	6d	23-Mar-27	30-Mar-27	10d
RI-C11-R1-6230	Install Elec. OH Rough-in - Overall Rough-in - INTR - C11	15d	23-Mar-27	12-Apr-27	7d
FN-AP3-PDS-710	Install Fire Alarm Trim - PDS Room 6097 - INTF - AP 3	2d	26-Mar-27	29-Mar-27	5d
GI-FS-SQM-SOMD-60	MEPF Hangers & Block Outs Roof - SEQ MIKE - SOMD	6d	26-Mar-27	02-Apr-27	0d
FN-AP3-PDS-720	Install Low Volt Trim - PDS Room 6097 - INTF - AP 3	2d	26-Mar-27	29-Mar-27	1d
FN-AP3-PDS-730	Install Mech. Trim - PDS Room 6097 - INTF - AP 3	2d	30-Mar-27	31-Mar-27	1d
TT-SQ1-SG3-A27-10	Tag & Trace - Sequence 1 - Stage 3 - Area 27	10d	31-Mar-27	13-Apr-27	0d
FN-AP3-PDS-750	Install BCU -1-6097 - PDS Room 6097 - INTF - AP 3	2d	01-Apr-27	02-Apr-27	1d
FN-AP3-PDS-700	Install Fire Protection Trim - PDS Room 6097 - INTF - AP 3	2d	01-Apr-27	02-Apr-27	1d
FN-C2-SP-1290	Install Ceiling Light Fixtures & Trim - SMP/Train Tube - INTR - C2	5d	02-Apr-27	08-Apr-27	0d
FN-AP3-PDS-760	Install RF Flooring & Base - PDS Room 6097 - INTF - AP 3	3d	05-Apr-27	07-Apr-27	1d
SK-RO-460	Install ISO Board & Peel & Stick - High Roof Metal - Phase 1.A	15d	05-Apr-27	23-Apr-27	0d
GI-FS-SQH-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ HOTEL - SOMD	6d	07-Apr-27	14-Apr-27	10d
MLS-1010	MLS - Alstom PDS/UPS Rooms Complete	0d		07-Apr-27	1d
MLS-1000	MLS - Alstom Train Tubes Complete	0d		08-Apr-27	0d
MLS-SUPP.C-07	MLS 7 - Alstom Early Turnover	0d		08-Apr-27 C	0d
SK-RO-60	Install TPO Roofing - Mid Roof TPO 1.B	15d	09-Apr-27	29-Apr-27	0d
RI-C11-R1-6300	Install BAS OH Rough-in - Overall Rough-in - INTR - C11	10d	13-Apr-27	26-Apr-27	7d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
TT-SQ1-SG3-A28-10	Tag & Trace - Sequence 1 - Stage 3 - Area 28	10d	14-Apr-27	27-Apr-27	0d
GI-FS-SQH-SOMD-50	FRP Pour 2 Ster. Corr. - SEQ HOTEL - SOMD	6d	15-Apr-27	22-Apr-27	10d
RI-C8-2530	Dancefloor Install Phase 3 - Overall - INTR - C8 Ph3	36d	21-Apr-27	10-Jun-27	0d
RI-C2-1450	Install Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1-1	7d	26-Apr-27	04-May-27	0d
RI-C11-R1-6270	Install CHW Insulation - Overall/Restrooms - INTR - C11	5d	27-Apr-27	03-May-27	7d
TT-SQ1-SG3-A29-10	Tag & Trace - Sequence 1 - Stage 3 - Area 29	10d	28-Apr-27	11-May-27	0d
VC-ESC-AP5-2280	Set Escalator Trusses - Escalator (#3 & #4) - INTR - AP 5	5d	30-Apr-27	06-May-27	0d
MLS-SK-RO-370	Quadrant 2 Structure Ready for Precast - Exterior Roof & Facade	0d	30-Apr-27		10d
SK-Q2-LO-150	Pre-Cast System - Q2 Lower	10d	30-Apr-27	13-May-27	10d
RI-C11-R1-6280	Install Plumbing Insulation - Overall/Restrooms - INTR - C11	5d	04-May-27	10-May-27	7d
RI-C2-1560	Install Dancefloor - Shuttle Platform High Ceiling - INTR - C2-1	11d	05-May-27	19-May-27	0d
SK-Q2-LO-30	Exterior CFMF Framing (Eave/Gutter/Wall) - Q2 Lower	20d	07-May-27	04-Jun-27	0d
BG-AP9-BS-10	Layout & Install Hangers & Steel - AP9	32d	11-May-27	24-Jun-27	0d
RI-C11-R1-1930	Frame & Top-Down Walls - Overall/Restrooms - INTR - C11	15d	11-May-27	01-Jun-27	7d
TT-SQ1-SG3-A30-10	Tag & Trace - Sequence 1 - Stage 3 - Area 30	10d	12-May-27	25-May-27	0d
RI-C2-1340	Install Elec. OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15d	20-May-27	10-Jun-27	0d
TT-SQ1-SG3-A31-10	Tag & Trace - Sequence 1 - Stage 3 - Area 31	10d	26-May-27	09-Jun-27	0d
D1879	Elec. MPP Install (MPP-XBM1-A 13 Enclosures) [01-03-01]	120d	27-May-27	15-Nov-27	7d
D1880	Elec. Install (XBM1 Cross Belt) [01-03-01]	120d	27-May-27	15-Nov-27	7d
SK-Q2-LO-60	Install Exterior Sheathing (Eave/Gutter/Wall) - Q2 Lower	10d	28-May-27	11-Jun-27	0d
SK-Q2-LO-80	Air Barrier (Eave/Gutter/Wall) - Q2 Lower	10d	07-Jun-27	18-Jun-27	0d
TT-SQ1-SG3-A32-10	Tag & Trace - Sequence 1 - Stage 3 - Area 32	10d	10-Jun-27	23-Jun-27	0d
RI-C2-1310	Low Voltage Rough-in Ceilings - Shuttle Platform High Ceiling - INTR - C2-1	15d	11-Jun-27	01-Jul-27	0d
RI-C8-2470	Dancefloor Install Phase 1 - Overall - INTR - C8 Ph1	31d	11-Jun-27	26-Jul-27	0d
RI-C2-1520	Install BAS OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15d	11-Jun-27	01-Jul-27	0d
SK-Q1-LO-580	Metal Panel Wall System Scan - Q2 Lower	5d	21-Jun-27	25-Jun-27	0d
TT-SQ2-SG1-A1-10	Tag & Trace - Sequence 2 - Stage 1 - Area 1	10d	24-Jun-27	08-Jul-27	0d
D1870	Mech Install (Sector G) [01-03-01]	35d	25-Jun-27	13-Aug-27	0d
RI-AP9-3700	Patch Fireproofing - Overall Rough-in - INTR - AP 9	5d	25-Jun-27	01-Jul-27	0d
D1869	Elec. Install (Sector G) [01-03-01]	33d	25-Jun-27	11-Aug-27	2d
SK-Q2-LO-190	Curtain Wall System - Q2.A Lower	16d	28-Jun-27	20-Jul-27	0d
RI-C2-1320	Fire Sprinkler Mains & Branch Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	8d	02-Jul-27	14-Jul-27	0d
RI-AP9-3380	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 9	3d	02-Jul-27	07-Jul-27	0d
RI-AP4-1420	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 4	15d	08-Jul-27	28-Jul-27	5d
TT-SQ2-SG1-A2-10	Tag & Trace - Sequence 2 - Stage 1 - Area 2	10d	09-Jul-27	22-Jul-27	0d
RI-AP9-3390	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 9	10d	15-Jul-27	28-Jul-27	0d
RI-C2-1360	Frame & Top-Down High Walls - Shuttle Platform High Ceiling - INTR - C2-1	10d	15-Jul-27	28-Jul-27	0d
D1871	Internal Commissioning / Functional Testing (Main Terminal Core) [01-03-01]	30d	19-Jul-27	27-Aug-27	0d
MLS-210	MLS - Pre-Cast/Curtainwall Facade Start	0d	21-Jul-27		0d
SK-Q1-UP-630	Curtain Wall System - Q1 Upper	5d	21-Jul-27	27-Jul-27	0d
SK-Q2-LO-120	Curtain Wall System - Q2.B Lower	15d	21-Jul-27	10-Aug-27	0d
TT-SQ2-SG1-A3-10	Tag & Trace - Sequence 2 - Stage 1 - Area 3	10d	23-Jul-27	05-Aug-27	0d
RI-C8-2570	Install Elec. Hangers - Phase 1 - C8 Ph1	5d	27-Jul-27	02-Aug-27	0d
RI-C8-2560	Install Fire Sprinkler Hangers - Phase 1 - C8 Ph1	5d	27-Jul-27	02-Aug-27	0d
SK-Q1-UP-640	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q1 Upper	20d	28-Jul-27	24-Aug-27	0d
RI-C2-1470	Install Sign Supports & Backing - Shuttle Platform High Ceiling - INTR - C2-1	5d	29-Jul-27	04-Aug-27	0d
RI-AP4-1430	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 4	10d	29-Jul-27	11-Aug-27	5d
RI-AP9-3400	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 9	10d	29-Jul-27	11-Aug-27	0d
RI-C8-2580	Install Low Voltage Hangers - Phase 1 - C8 Ph1	5d	29-Jul-27	04-Aug-27	0d
RI-C8-2610	Fire Sprinkler Mains & Branch Rough-in - Overall - INTR - C8 Ph1	20d	03-Aug-27	30-Aug-27	2d
RI-C8-2590	Install Elec. OH Rough-in - Overall Rough-in - INTR - C8 Ph1 Ph1	20d	03-Aug-27	30-Aug-27	2d
RI-C8-2600	Low Voltage Rough-in Ceilings - Overall - INTR - C8 Ph1	15d	05-Aug-27	25-Aug-27	5d
RI-C8-3080	Frame Drywall Ceiling - Inner Soffit - Phase 1 - C8 Ph1	20d	05-Aug-27	01-Sep-27	0d
RI-C2-1260	Elec. Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5d	05-Aug-27	11-Aug-27	0d
RI-C8-3090	Install ACT Ceiling Grid Supports - Phase 1 - C8 Ph1	20d	05-Aug-27	01-Sep-27	0d
TT-SQ2-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 2 - Stage 1 - Area 3	5d	06-Aug-27	12-Aug-27	0d
SK-Q2-LO-130	Install Doors & Windows - Q2 Lower	10d	11-Aug-27	24-Aug-27	0d
RI-C2-1210	Install Wall Insulation - Overall Rough-in - INTR - C2	5d	11-Aug-27	17-Aug-27	5d
U&P-UND-60	Install Underground Storm S-806 to S-825 (Inc Roof & Condensate Pipes) - Quadrant 2	15d	11-Aug-27	31-Aug-27	0d
RI-AP4-5820	Install CHW/Glycol OH Rough-in - Overall Rough-in - INTR - AP 4	5d	12-Aug-27	18-Aug-27	5d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
RI-AP9-3410	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 9	20d	12-Aug-27	09-Sep-27	0d
RI-C2-1300	Low Voltage Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5d	12-Aug-27	18-Aug-27	0d
TT-SQ2-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 2 - Stage 1 - Area 3	10d	13-Aug-27	26-Aug-27	0d
FN-C2-SRR-940	Insulate Ceilings & Soffits - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5d	18-Aug-27	24-Aug-27	5d
RI-C2-1350	Patch Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1	2d	19-Aug-27	20-Aug-27	0d
RI-AP4-1440	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 4	10d	19-Aug-27	01-Sep-27	5d
D1875	Owner Testing (Main Terminal Core) [01-03-01]	10d	23-Aug-27	03-Sep-27	0d
RI-C2-1460	Install Wall Insulation - Shuttle Platform High Ceiling - INTR - C2-1	5d	23-Aug-27	27-Aug-27	0d
MLS-920	MLS - Temp Building Conditioning Available	0d		24-Aug-27	0d
MLS-SUPP.C-09	MLS 9 - Building Dry-in Complete - Exterior Roof & Facade	0d		24-Aug-27 C	0d
MLS-100	MLS - Pre-Cast/Curtainwall Facade Complete	0d		24-Aug-27	0d
FN-C2-SRR-970	Hang Hard Lid Ceilings - Support RR - INTF - C2	2d	25-Aug-27	26-Aug-27	5d
FN-AP7-ER-610	Hang, Tape & Finish Drywall - Dist. Elec. Room 6197 - INTRF - AP 7	15d	25-Aug-27	15-Sep-27	0d
FN-MC1-MR-200	Hang, Tape & Finish Drywall - Mech. Room - INTF - Club 1	15d	25-Aug-27	15-Sep-27	10d
FN-C2-SR-1260	Hang Drywall Walls - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	27-Aug-27	02-Sep-27	5d
TT-SQ2-SG1-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 2 - Stage 1 - Area 3	10d	27-Aug-27	10-Sep-27	0d
FN-C2-CL-520	Hang Drywall Walls - Delta Airlines Club Entry/In-Flight Lounge - INTF - C2	5d	27-Aug-27	02-Sep-27	5d
FN-C2-SP-1490	Install High Ceiling Grid - APM Platform Area - INTF - C2	5d	30-Aug-27	03-Sep-27	0d
U&P-UND-70	Install Underground Sanitary MH-202 to S-201 - Quadrant 2	20d	01-Sep-27	29-Sep-27	0d
RI-C8-2540	Frame Drywall Ceiling - Outter Soffit - Phase 1 - C8 Ph1	20d	02-Sep-27	30-Sep-27	0d
HA-AL-CP-160	Concessions - Concessionaires Design/Permitting Period (HCAA)	183d	03-Sep-27	23-May-28	4d
FN-C2-SRR-960	Hang Drywall Walls - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	10d	03-Sep-27	17-Sep-27	5d
BI-ROW-BR-P4-20	Demo Exist. Free-Standing Bollards Surrounding AS1 thru AS4 & Existing Elec. Room [01-03-03]	10d	07-Sep-27	20-Sep-27	5d
A109160	Fire Protection Systems Modifications [01-03-02]	5d	07-Sep-27	13-Sep-27	10d
B7	BHS - Mech / Elec. Demo & Install of AS3 CBRA Loop (01-03-02)	11d	07-Sep-27	21-Sep-27	0d
A109170	Elec. Systems Modifications [01-03-02]	5d	07-Sep-27	13-Sep-27	10d
BI-ROW-BR-P4-30	Install Temp Lighting in AS4 [01-03-03]	3d	07-Sep-27	09-Sep-27	5d
FN-C2-SP-1210	Install Device Tiles High - APM Platform Area - INTF - C2	5d	07-Sep-27	13-Sep-27	0d
A7	BHS - Mech / Elec. Demo & Install of T3 & BX2 Lines (01-03-02)	3d	07-Sep-27	09-Sep-27	0d
RI-AP4-1450	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 4	20d	10-Sep-27	07-Oct-27	0d
BI-ROW-BR-P4-40	Demo/Relocate Existing Elec. Devices, Lighting & Conduit (Including Attached to Platform) in AS4 [01-...	15d	10-Sep-27	30-Sep-27	6d
BI-ROW-BR-P4-80	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring (Including Attached to Platform) ...	15d	10-Sep-27	30-Sep-27	6d
MLS-SUPP.C-06	MLS 6 - Supplement B Substantial Completion	0d		10-Sep-27 C	0d
FN-C2-SP-1430	Install High GFRP - APM Platform Area - INTF - C2	10d	14-Sep-27	27-Sep-27	0d
RI-MC1-IDF-7250	Hang, Tape & Finish Drywall - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5d	16-Sep-27	22-Sep-27	10d
FN-MC1-ER-3290	Hang, Tape & Finish Drywall - Elec. Room 6676 - INTRF - Club 1	5d	16-Sep-27	22-Sep-27	10d
FN-AP7-ER-620	Prime & First Coat - Dist. Elec. Room 6197 - INTRF - AP 7	5d	16-Sep-27	22-Sep-27	0d
RI-C8-1760	Install ACT Ceiling Grid - Phase 1 - C8 Ph1	20d	17-Sep-27	14-Oct-27	0d
FN-C1-O4-470	Hang Drywall - Delta Airlines Operations #4 - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-525	Hang Drywall - Concession Storage - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-685	Hang Drywall - Employee Port/Term. Mgr. Office - INTF - C1	2d	20-Sep-27	21-Sep-27	5d
FN-C1-O2-525	Hang Drywall - Un. Airline Ops. - INTF - C1	3d	20-Sep-27	22-Sep-27	5d
FN-C1-SR-250	Hang Drywall - Support Corr./HCAA Storage - INTF - Conc. 1	3d	20-Sep-27	22-Sep-27	5d
BI-ROW-BR-P3-30	Remove Moveable Concrete Barriers Along South Wall of AS3 [01-03-03]	1d	21-Sep-27	21-Sep-27	10d
BI-ROW-BR-P4-50	Patch & Seal Concrete @ Former Bollard Locations Outside of AS1 thru AS4 & Existing Elec. Room [01-...	5d	21-Sep-27	27-Sep-27	5d
BI-ROW-BR-P3-20	Demo Southeast Portion of EDS Platform for T-TXM2 ROW [01-03-03]	3d	21-Sep-27	23-Sep-27	10d
A104190	Delivery of TSA AS3 Temp EDS Machine	1d	22-Sep-27	22-Sep-27	0d
A104200	TSA Install of AS3 Temp EDS Machine	3d	23-Sep-27	27-Sep-27	0d
FN-AP7-ER-710	Install Door & Hardware - Dist. Elec. Room 6197 - INTRF - AP 7	2d	23-Sep-27	24-Sep-27	8d
FN-AP7-ER-640	Set Elec. Switchgear & Equip. - Dist. Elec. Room 6197 - INTRF - AP 7	10d	23-Sep-27	06-Oct-27	0d
FN-C3-SS-30	Hang Drywall Walls - SSCP Check Points - INTF - C3	5d	23-Sep-27	29-Sep-27	5d
BG-TST-270	Site Acceptance Test - AS3 Temp EDS Machine (SAT) (SUM) - BHS Testing & Integration	5d	28-Sep-27	04-Oct-27	0d
FN-C2-SP-1500	Install Low Ceiling Grid - APM Platform Area - INTF - C2	10d	28-Sep-27	11-Oct-27	0d
D1887	Internal Commissioning / Functional Testing (AS3 CBRA Loop Temp) [01-03-02]	5d	28-Sep-27	04-Oct-27	0d
U&P-UND-170	Install Underground Sanitary MH-201 to S-202 - Quadrant 2	5d	30-Sep-27	06-Oct-27	0d
RI-C3-IDF-6680	Hang, Tape & Finish Drywall - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5d	30-Sep-27	06-Oct-27	5d
BI-ROW-BR-P3-50	Install Temp Lighting in AS3 [01-03-03]	3d	01-Oct-27	05-Oct-27	10d
BI-ROW-BR-P4-120	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS4 [01-03-03]	15d	01-Oct-27	21-Oct-27	8d
BI-ROW-BR-P4-170	Demo Feeders to (3) EDS UPS Machines in AS4 [01-03-03]	5d	01-Oct-27	07-Oct-27	6d
BI-ROW-BR-P3-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring at T-TXM2 Opening on CMU Wal...	5d	01-Oct-27	07-Oct-27	6d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
B8	BHS - Mech / Elec. Demo & Install of T5 / C5 [01-03-03]	2d	05-Oct-27	06-Oct-27	0d
D1903	Internal Commissioning / Functional Testing / Owner Testing (C5 06/08) [01-03-03]	1d	07-Oct-27	07-Oct-27	0d
RI-C1-MDF-6970	Hang, Tape & Finish Drywall - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5d	07-Oct-27	13-Oct-27	5d
RI-MC1-IDF-1060	Hang, Tape & Finish Drywall - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5d	07-Oct-27	13-Oct-27	5d
RI-C1-MDF-6480	Hang, Tape & Finish Drywall - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5d	07-Oct-27	13-Oct-27	5d
RI-AP7-ER-880	Install Elec. OH Rough-in - Dist. Elec. Room 6197 - INTRF - AP 7	15d	07-Oct-27	27-Oct-27	0d
U&P-UND-80	Install Building Roof Drain Laterals - Quadrant 2	5d	07-Oct-27	13-Oct-27	0d
D1905	Elec. Install MPP / FCP (A10, A11, A14, A15, B12, B16) [01-03-03]	16d	08-Oct-27	29-Oct-27	8d
RI-AP5-290	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 5	20d	08-Oct-27	04-Nov-27	0d
C9	BHS - Mech / Elec. Demo [01-03-03]	6d	08-Oct-27	15-Oct-27	0d
RI-C8-2620	Complete Fire Sprinkler OH Rough-in - Phase 1 - C8 Ph1	10d	08-Oct-27	21-Oct-27	0d
FN-C2-SP-1400	Install Device Tiles Low - APM Platform Area - INTF - C2	15d	12-Oct-27	01-Nov-27	0d
RI-C8-2630	Complete Elec. OH Rough-in - Phase 1 - C8 Ph1	10d	12-Oct-27	25-Oct-27	0d
U&P-GP-130	Install Underground Fire Protection STA-32+00 to STA-25+00 - Quadrant 2	10d	14-Oct-27	27-Oct-27	0d
FN-AP12-BAS-2020	Hang, Tape & Finish Drywall - INTF - BAS Control Room 6078 - AP12	15d	14-Oct-27	03-Nov-27	5d
RI-AP12-IDF-4980	Hang, Tape & Finish Drywall - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5d	14-Oct-27	20-Oct-27	5d
RI-C8-2640	Complete Low Voltage OH Rough-in - Phase 1 - C8 Ph1	5d	15-Oct-27	21-Oct-27	2d
D9	BHS - Mech / Elec. Install [01-03-03]	13d	18-Oct-27	03-Nov-27	0d
BI-ROW-BR-P4-140	Demo & Remove AHU-B11, Associated Ductwork, & Associated Chilled Water Piping [01-03-03]	5d	22-Oct-27	28-Oct-27	8d
RI-C8-2550	Hang, Tape & Finish Drywall Ceiling - Phase 1 - C8 Ph1	20d	26-Oct-27	22-Nov-27	0d
FN-AP7-ER-650	Install Elec. Panels & Transformers - Dist. Elec. Room 6197 - INTRF - AP 7	10d	28-Oct-27	10-Nov-27	0d
U&P-GP-60	VDGS Found. & Conduit - Quadrant 2	10d	28-Oct-27	10-Nov-27	0d
BI-ROW-BR-P4-150	Demo Housekeeping Pad Beneath Former AHU-B11 [01-03-03]	2d	29-Oct-27	01-Nov-27	8d
BI-ROW-BR-P4-160	Patch & Seal Concrete @ Former AHU-B11 Housekeeping Pad [01-03-03]	3d	02-Nov-27	04-Nov-27	8d
FN-C2-SP-1530	Install Ceiling Light Fixtures & Low Trim - APM Platform Area - INTF - C2	15d	02-Nov-27	22-Nov-27	0d
FN-AP11-ER-2676	Hang, Tape & Finish Drywall - Dist. Elec. Room #6003 - INTF - AP 11	15d	04-Nov-27	24-Nov-27	5d
D1910	Internal Commissioning / Functional Testing [01-03-03]	7d	04-Nov-27	12-Nov-27	0d
RI-AP8-1900	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 8	20d	05-Nov-27	06-Dec-27	0d
RI-AP5-4760	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 5	10d	05-Nov-27	18-Nov-27	10d
MLS-SUPP.C-05	MLS 5 - Install of VGDS Found. & Conduits Complete	0d		10-Nov-27 C	0d
FN-AP7-ER-655	Elec. Feeder Wire Measurements & Procurement - Dist. Elec. Room 6197 - INTRF - AP 7	10d	11-Nov-27	24-Nov-27	0d
D1914	Elec. Demo (T8 12/13) [01-03-03]	1d	15-Nov-27	15-Nov-27	0d
D1913	Mech Demo (T8 12/13) [01-03-03]	1d	16-Nov-27	16-Nov-27	0d
D1932	Commissioning / Testing (XBM1 Cross Belt) [01-03-04]	20d	16-Nov-27	15-Dec-27	7d
D1912	Mech Install (T8 12) [01-03-03]	2d	17-Nov-27	18-Nov-27	0d
D1915	Elec. Install (T8 12) [01-03-03]	2d	19-Nov-27	22-Nov-27	0d
D1917	Internal Commissioning / Functional Testing / Owner Testing (T8 12) [01-03-03]	1d	22-Nov-27	22-Nov-27	0d
RI-C8-1770	Install ACT Ceiling Device Tiles (Close-in) - Phase 1- C8 Ph1	10d	23-Nov-27	08-Dec-27	0d
FN-C2-SP-1220	Install Ceiling Light Fixtures & High Trim - APM Platform Area - INTF - C2	10d	23-Nov-27	08-Dec-27	0d
A10	BHS - Mech / Elec. Demo & Install of AS4 02/04, C9 10, T10 04/09, T11 04/09, T18 15/17 (01-03-04)	10d	23-Nov-27	08-Dec-27	0d
FN-AP8-ER-2510	Hang, Tape & Finish Drywall - Dist. Elec. Room 6290 - INTRF - AP 8	15d	29-Nov-27	17-Dec-27	5d
FN-AP7-ER-660	Pull & Terminate Elec. - Dist. Elec. Room 6197 - INTRF - AP 7	20d	29-Nov-27	27-Dec-27	0d
FN-CN-2410	Finish/Trim-Out High Ceiling Install - Overall - INTF - C8 Ph 1	20d	02-Dec-27	30-Dec-27	0d
RI-AP7-MR-458	Pull & Terminate to Mech. Equip. - Mech. Room - INTR - AP 7	10d	06-Dec-27	17-Dec-27	0d
RI-AP8-1890	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 8	10d	07-Dec-27	20-Dec-27	10d
RI-AP7-1380	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 7	20d	07-Dec-27	05-Jan-28	0d
RI-AP8-3060	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 8	20d	07-Dec-27	05-Jan-28	0d
B10	BHS - Inspection (01-03-04)	5d	09-Dec-27	15-Dec-27	0d
FN-C2-SP-1230	Drop Remaining Ceiling Tile High - APM Platform Area - INTF - C2	5d	09-Dec-27	15-Dec-27	0d
D1933	Owner Testing (XBM1 Cross Belt) [01-03-04]	4d	16-Dec-27	21-Dec-27	7d
C10	BHS - Mech / Elec. Demo & Install of T10 10/15, T11 10/12, TC2 02/04, MCP 04 & 35 (01-03-04)	10d	16-Dec-27	30-Dec-27	0d
RI-C8-3100	Install ACT Remaining Tiles (Close-in) - Phase 1- C8 Ph1	20d	16-Dec-27	14-Jan-28	0d
FN-C2-SP-1520	Drop Remaining Ceiling Tile Low - APM Platform Area - INTF - C2	10d	16-Dec-27	30-Dec-27	0d
RI-AP7-MR-570	Patch Fireproofing - Mech. Room - INTR - AP 7	5d	20-Dec-27	27-Dec-27	0d
D1934	Go Live (XBM1 Cross Belt) [01-03-04]	1d	22-Dec-27	22-Dec-27	7d
FN-AP7-MR-430	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 7	15d	28-Dec-27	18-Jan-28	0d
FN-C2-SP-1540	Hang High Drywall - APM Platform Area - INTF - C2	10d	03-Jan-28	14-Jan-28	0d
D1930	Internal Commissioning / Functional Testing / Owner Testing [01-03-04]	2d	03-Jan-28	04-Jan-28	0d
D1939	Elec. Install / Recontrol (T13 01/04) [01-03-05]	2d	04-Jan-28	05-Jan-28	1d
D1938	Mech Install (T13 05/06) [01-03-05]	1d	05-Jan-28	05-Jan-28	1d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
D1936	Elec. Demo (T13 05/06) [01-03-05]	1d	05-Jan-28	05-Jan-28	0d
RI-AP7-1390	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 7	10d	06-Jan-28	19-Jan-28	0d
RI-AP8-1920	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 8	5d	06-Jan-28	12-Jan-28	0d
RI-AP7-2520	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 7	20d	06-Jan-28	02-Feb-28	0d
D1937	Mech Demo (T13 05/06) [01-03-05]	1d	06-Jan-28	06-Jan-28	0d
D1940	Internal Commissioning / Functional Testing / Owner Testing [01-03-05]	1d	07-Jan-28	07-Jan-28	0d
A11	BHS - Mech / Elec. Demo & Install of T14 06/10, OS1 07 (01-03-06)	26d	10-Jan-28	14-Feb-28	0d
FN-CN-2500	Apply Final Paint High Ceiling - Overall - INTF - C8 Ph 1	8d	12-Jan-28	21-Jan-28	0d
RI-AP8-1930	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	10d	13-Jan-28	26-Jan-28	0d
RI-AP8-1970	Elec. Rough-in Walls & Columns - Overall Rough-in - INTR - AP 8	10d	13-Jan-28	26-Jan-28	3d
FN-C2-SP-1550	Tape & Finish High Level Walls - APM Platform Area - INTF - C2	10d	17-Jan-28	28-Jan-28	0d
FN-AP6-ER-2540	Hang, Tape & Finish Drywall - Elec. Room 6200 - INTRF - AP 6	15d	19-Jan-28	08-Feb-28	0d
RI-AP7-1370	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 7	10d	20-Jan-28	02-Feb-28	0d
D1981	Elec. Install (XBM2 Cross Belt) [02-01-01C]	100d	24-Jan-28	12-Jun-28	2d
D1980	Mech Install (XBM2 Cross Belt) [02-01-01C]	100d	24-Jan-28	12-Jun-28	2d
RI-C8-2650	Dancefloor Removal Phase 1 - Overall - INTR - C8 Ph1	21d	24-Jan-28	21-Feb-28	0d
RI-AP8-1960	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 8	3d	27-Jan-28	31-Jan-28	0d
RI-AP8-1940	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	3d	27-Jan-28	31-Jan-28	0d
FN-C2-SP-1560	Prime & One Coat High Walls - APM Platform Area - INTF - C2	7d	31-Jan-28	08-Feb-28	0d
FN-AP8-IB-2250	Install Wall Insulation - Baggage Claim 1 - INTF - AP 8	5d	01-Feb-28	07-Feb-28	0d
FN-AP8-IB-2240	Insulate Ceilings & Soffits - Baggage Claim 1 - INTF - AP 8	7d	01-Feb-28	09-Feb-28	8d
RI-AP7-1400	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 7	10d	03-Feb-28	16-Feb-28	2d
RI-AP7-1440	Install HM Door Frames - Overall Rough-in - INTR - AP 7	3d	03-Feb-28	07-Feb-28	9d
RI-AP7-1410	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 7	5d	03-Feb-28	09-Feb-28	0d
FN-AP8-IB-2270	Hang Drywall Walls - Baggage Claim 1 - INTF - AP 8	5d	08-Feb-28	14-Feb-28	5d
FN-AP8-PM-1700	Install Wall Insulation - CBP Primary - INTF - AP 8	5d	08-Feb-28	14-Feb-28	0d
FN-AP6-ER-2550	Prime & First Coat - Elec. Room 6200 - INTRF - AP 6	5d	09-Feb-28	15-Feb-28	0d
FN-C2-SP-1060	Trim Diffusers/Louvers - APM Platform Area - INTF - C2	5d	09-Feb-28	15-Feb-28	0d
RI-AP7-1430	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7d	10-Feb-28	18-Feb-28	0d
FN-AP8-IB-2260	Hang Hard Lid Ceilings - Baggage Claim 1 - INTF - AP 8	5d	15-Feb-28	21-Feb-28	5d
D1948	Internal Commissioning / Functional Testing / Owner Testing (T10 & T14) [01-03-06]	2d	15-Feb-28	16-Feb-28	0d
VC-EL-AP8-3110	Hang Machine Room Side 1st Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	15-Feb-28	16-Feb-28	0d
RI-C2-1490	Remove Dancefloor - APM Platform Area - INTF - C2	5d	16-Feb-28	22-Feb-28	0d
FN-AP6-ER-2570	Set Elec. Switchgear & Equip. - Elec. Room 6200 - INTRF - AP 6	10d	16-Feb-28	29-Feb-28	0d
D1953	Elec. Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-03-06]	3d	17-Feb-28	21-Feb-28	0d
VC-EL-AP8-3120	Inspect 1st Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	17-Feb-28	18-Feb-28	0d
D1952	Elec. MPP Install (MPP-B10, FCP-B10, MPP-B13, FCP-B13, MPP-B15, FCP-B15) [01-03-06]	45d	17-Feb-28	19-Apr-28	5d
D1954	Mech Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-03-06]	3d	17-Feb-28	21-Feb-28	0d
RI-AP7-1450	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 7	10d	21-Feb-28	03-Mar-28	0d
VC-EL-AP8-3130	Hang Machine Room Side 2nd Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	21-Feb-28	22-Feb-28	0d
D1955	Mech Install [01-03-06]	45d	22-Feb-28	24-Apr-28	0d
FN-AP8-PM-1720	Hang Drywall Walls - CBP Primary - INTF - AP 8	5d	22-Feb-28	28-Feb-28	5d
D1956	Elec. Install [01-03-06]	45d	22-Feb-28	24-Apr-28	0d
FN-CN-1630	Place Back 12 Line Grout Joint - Overall - INTF - C8 - Ph 1	5d	22-Feb-28	28-Feb-28	0d
VC-EL-AP8-3140	Tape/Finish 2 Hr Rated Wall - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	23-Feb-28	29-Feb-28	0d
FN-C2-SP-1580	Install Platform Level Ceiling Grid - APM Platform Area - INTF - C2	5d	23-Feb-28	29-Feb-28	0d
FN-CN-2570	Layout - Overall - INTF - C8 - Ph 1	5d	29-Feb-28	06-Mar-28	0d
VC-EL-AP8-2880	Install Elev. Safety Rail/Net - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	29-Feb-28	06-Mar-28	5d
RI-AP6-ER-2600	Install Elec. OH Rough-in - Elec. Room 6200 - INTRF - AP 6	20d	01-Mar-28	28-Mar-28	0d
VC-EL-AP8-3150	Frame 2 Hr Rated Lid with Shaft Liner - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	01-Mar-28	02-Mar-28	0d
FN-C2-SP-1570	Install Platform Level Device Tiles - APM Platform Area - INTF - C2	10d	01-Mar-28	14-Mar-28	0d
VC-EL-AP8-3160	Insulate Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	03-Mar-28	06-Mar-28	0d
RI-AP6-150	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 6	10d	06-Mar-28	17-Mar-28	10d
RI-AP7-2500	Install Ltg for Future Tenant Spaces - Overall Rough-in - INTR - AP 7	15d	06-Mar-28	24-Mar-28	1d
FN-AP7-SC-10	Install Wall Insulation - Overall/Support Corridors - INTF - AP 7	5d	06-Mar-28	10-Mar-28	0d
FN-CN-2540	Frame Interior Partitions - Overall - INTF - C8 - Ph 1	15d	07-Mar-28	27-Mar-28	0d
FN-CN-3190	Install Column Signage Supports/Backing - Overall - INTF - C8 - Ph 1	5d	07-Mar-28	13-Mar-28	10d
VC-EL-AP8-3170	Inspect Ceiling Insulation - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	07-Mar-28	08-Mar-28	0d
FN-CN-3240	Frame Column Covers - Overall - INTF - C8 - Ph 1	15d	07-Mar-28	27-Mar-28	0d
VC-EL-AP8-3020	Install Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	07-Mar-28	13-Mar-28	5d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
VC-EL-AP8-3200	Hang 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	09-Mar-28	10-Mar-28	0d
FN-AP7-SC-20	Hang Drywall Walls - Overall/Support Corridors - INTF - AP 7	5d	13-Mar-28	17-Mar-28	10d
VC-EL-AP8-3190	Inspect 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	13-Mar-28	14-Mar-28	0d
FN-AP7-SD-1150	Install Wall Insulation - CBP Second. - INTF - AP 7	5d	13-Mar-28	17-Mar-28	0d
VC-EL-AP8-2890	Rough-in Elec. In Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	8d	14-Mar-28	23-Mar-28	5d
VC-EL-AP8-3180	Hang 2nd Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	15-Mar-28	16-Mar-28	0d
FN-C2-SP-1410	Drop Remaining Ceiling Tile - Platform Level - APM Platform Area - INTF - C2	10d	15-Mar-28	28-Mar-28	0d
VC-EL-AP8-3230	Tape/Finish Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	17-Mar-28	23-Mar-28	0d
FN-AP7-SR-200	Install Wall Insulation - CBP Support Restrooms - INTF - AP 7	5d	20-Mar-28	24-Mar-28	0d
FN-AP7-SC-30	Tape & Finish Walls - Overall/Support Corridors - INTF - AP 7	10d	20-Mar-28	31-Mar-28	10d
FN-AP7-SD-1170	Hang Drywall Walls - CBP Second. - INTF - AP 7	5d	20-Mar-28	24-Mar-28	10d
VC-EL-AP8-2920	Install Elev. Pit Ltg/Outlets - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	24-Mar-28	30-Mar-28	5d
VC-EL-AP8-3220	1st Coat Paint Machine Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	24-Mar-28	27-Mar-28	0d
VC-EL-AP8-2930	Install Temp Power for Elevator Release - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	24-Mar-28	30-Mar-28	10d
FN-AP7-O3-930	Install Wall Insulation - Delta Airlines Operations #2 & #3 - INTF - AP 7	5d	27-Mar-28	31-Mar-28	0d
RI-AP7-1420	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7d	27-Mar-28	04-Apr-28	1d
FN-AP7-SR-210	Hang Drywall Walls/Ceilings - CBP Support Restrooms - INTF - AP 7	5d	27-Mar-28	31-Mar-28	10d
VC-EL-AP8-3250	Install Door & Hardware - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2d	28-Mar-28	29-Mar-28	1d
FN-CN-2580	Elec. In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	28-Mar-28	10-Apr-28	0d
VC-EL-AP8-2900	Elec. Wall Rough Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	3d	28-Mar-28	30-Mar-28	0d
FN-AP6-ER-2580	Install Elec. Panels & Transformers - Elec. Room 6200 - INTRF - AP 6	15d	29-Mar-28	18-Apr-28	0d
FN-C2-SP-1480	Hang Platform Level Drywall - APM Platform Area - INTF - C2	10d	29-Mar-28	11-Apr-28	0d
VC-EL-AP8-3210	Set Elev. Controllers - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	30-Mar-28	05-Apr-28	1d
VC-EL-AP8-2910	Install Elec. OH Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5d	31-Mar-28	06-Apr-28	0d
VC-EL-AP8-3030	Remove Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	31-Mar-28	06-Apr-28	5d
FN-CN-2600	Low Voltage In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	31-Mar-28	13-Apr-28	0d
FN-AP7-SC-40	Prime & One Coat Walls - Overall/Support Corridors - INTF - AP 7	7d	03-Apr-28	11-Apr-28	10d
FN-AP6-CR-10	Install Wall Insulation - Overall - INTF - AP 6	5d	03-Apr-28	07-Apr-28	0d
FN-CN-2590	Fire Alarm In Wall Rough In - Overall - INTF - C8 - Ph 1	10d	05-Apr-28	18-Apr-28	0d
FN-AP7-SD-1140	Insulate Ceilings & Soffits - CBP Second. - INTF - AP 7	7d	05-Apr-28	13-Apr-28	1d
VC-EL-AP8-3240	Install Elev. Pathways/Wire Elev. - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	10d	07-Apr-28	20-Apr-28	0d
FN-AP6-CR-220	Install Wall Insulation - CBP Secondary - INTF - AP 6	5d	10-Apr-28	14-Apr-28	0d
D1957	Internal Commissioning / Functional Testing / Owner Testing [01-03-06]	12d	11-Apr-28	26-Apr-28	0d
FN-AP7-SC-50	Install ACT Ceiling Grid - Overall/Support Corridors - INTF - AP 7	20d	12-Apr-28	09-May-28	10d
FN-C2-SP-1010	Tape & Finish Platform Level Walls - APM Platform Area - INTF - C2	10d	12-Apr-28	25-Apr-28	0d
FN-AP7-SD-1160	Hang Hard Lid Ceilings - CBP Second. - INTF - AP 7	5d	14-Apr-28	20-Apr-28	1d
VC-EL-AP8-2940	Install Elev. Rails - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	14-Apr-28	20-Apr-28	0d
FN-AP6-O2-220	Install Wall Insulation - Delta Airlines Operations #1- INTF - AP 6	5d	17-Apr-28	21-Apr-28	0d
FN-CN-2610	Hang, Tape & Finish Drywall Partitions - Overall - INTF - C8 - Ph 1	10d	19-Apr-28	02-May-28	0d
FN-AP6-ER-2590	Elec. Feeder Wire Measurements & Procurement - Elec. Room 6200 - INTRF - AP 6	10d	19-Apr-28	02-May-28	0d
VC-EL-AP8-3400	Set Elev. Equip. in Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	2d	21-Apr-28	24-Apr-28	0d
FN-AP7-SD-1180	Tape & Finish Ceilings - CBP Second. - INTF - AP 7	10d	21-Apr-28	04-May-28	6d
FN-AP7-O3-940	Hang Drywall Walls - Delta Airlines Operations #2 & #3 - INTF - AP 7	5d	21-Apr-28	27-Apr-28	1d
FN-AP6-CR-440	Install Wall Insulation - Exit Passageway 6195 - INTF - AP 6	5d	24-Apr-28	28-Apr-28	0d
VC-EL-AP8-3420	Install Hoistway Elec. Cabling - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	25-Apr-28	01-May-28	0d
VC-EL-AP8-3410	Install Platform & Weights - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	25-Apr-28	01-May-28	0d
FN-C2-SP-1020	Prime & One Coat Platform Level Walls - APM Platform Area - INTF - C2	7d	26-Apr-28	04-May-28	0d
D1960	Elec. Install (TA1 03/04 & 08/09) [02-01-01A]	2d	27-Apr-28	28-Apr-28	0d
FN-AP6-CR-230	Hang Drywall Walls - CBP Secondary - INTF - AP 6	5d	28-Apr-28	04-May-28	1d
FN-AP6-CR-450	Hang Drywall Walls - Exit Passageway 6195 - INTF - AP 6	5d	01-May-28	05-May-28	0d
D1961	Mech Demo (TA1 15/16 & 19) [02-01-01A]	1d	01-May-28	01-May-28	0d
VC-EL-AP8-3440	Install Elev. Doors - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3d	02-May-28	04-May-28	0d
VC-EL-AP8-3430	Install Elev. Equip in Pit - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5d	02-May-28	08-May-28	0d
D1962	Mech Install (TA1 03/04 & 08/09) [02-01-01A]	2d	02-May-28	03-May-28	0d
FN-AP6-ER-2600	Pull & Terminate Elec. - Elec. Room 6200 - INTRF - AP 6	20d	03-May-28	31-May-28	0d
FN-CN-2620	Install Terrazzo Flooring at Circ./Restroom Vestibules/Concessions Ph.1 - Overall - INTF - C8	20d	03-May-28	31-May-28	0d
D1963	Elec. Demo (TA1 15/16 & 19, MCP-13) [02-01-01A]	1d	04-May-28	04-May-28	0d
D1965	Internal Commissioning / Functional Testing / Owner Testing [02-01-01A]	1d	05-May-28	05-May-28	0d
FN-AP6-CR-250	Hang Drywall Ceilings - CBP Secondary - INTF - AP 6	5d	05-May-28	11-May-28	1d
FN-AP8-PM-2020	Field Measure & Fab. Decorative Glass Panels (Exterior EL-7 & EL-6) - CBP Primary - INTF - AP 8	70d	05-May-28	14-Aug-28	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
FN-AP7-SD-1200	Apply Prime, First, Paint Ceilings - CBP Second. - INTF - AP 7	7d	05-May-28	15-May-28	6d
FN-C2-SP-1050	Install Terrazzo Flooring at APM/Circulation/SSCP Queue - APM Platform Area - INTF - C2	20d	05-May-28	02-Jun-28	0d
FN-AP6-CR-470	Hang Drywall Ceilings - Exit Passageway 6195 - INTF - AP 6	5d	08-May-28	12-May-28	0d
D1967	Elec. Demo (T12 26) [02-01-01B]	1d	08-May-28	08-May-28	0d
FN-AP6-O2-230	Hang Drywall Walls - Delta Airlines Operations #1- INTF - AP 6	5d	08-May-28	12-May-28	0d
D1968	Elec. Install (C8A 13) [02-01-01B]	1d	09-May-28	09-May-28	0d
D1969	Internal Commissioning / Functional Testing / Owner Testing [02-01-01B]	1d	10-May-28	10-May-28	0d
D1970	Mech Demo (T12 26) [02-01-01B]	1d	11-May-28	11-May-28	0d
D1971	Mech Install (C8A 13) [02-01-01B]	1d	12-May-28	12-May-28	0d
D1976	Elec. Conveyor Demo, MCP-07, MCP-09, MCP-17 (Reconnect ControlNet as Required) [02-01-01C]	5d	15-May-28	19-May-28	2d
FN-AP6-O2-240	Tape & Finish Walls - Delta Airlines Operations #1- INTF - AP 6	10d	15-May-28	26-May-28	0d
D1977	Elec. Install [02-01-01C]	20d	15-May-28	12-Jun-28	0d
D1975	Mech Install [02-01-01C]	20d	15-May-28	12-Jun-28	0d
D1974	Mech Demo [02-01-01C]	5d	15-May-28	19-May-28	2d
FN-AP7-SD-1230	Install ACT Ceiling Grid - CBP Second. - INTF - AP 7	10d	16-May-28	30-May-28	6d
HA-AL-CP-168	Concessions - Construction NTP	1d	24-May-28	24-May-28	4d
MLS-CN-20	Concessions News/Convenience C8.6 - Turnover C8	0d	25-May-28		4d
MLS-CN-170	Concessions Quick Serve C9.2 - Turnover C9	0d	25-May-28		4d
MLS-CN-160	Concessions Coffee C8.8 - Turnover C8	0d	25-May-28		4d
MLS-CN-180	Concessions Quick Serve C9.3 Turnover - C9	0d	25-May-28		4d
MLS-CN-10	Concessions Retail C8.1 - Turnover C8	0d	25-May-28		4d
MLS-CN-70	Concessions Retail C9.4 - Turnover C9	0d	25-May-28		4d
MLS-CN-190	Concessions Quick Serve C9.1 - Turnover C9	0d	25-May-28		4d
MLS-CN-50	Concessions Gourmet Market C8.5 - Turnover C8	0d	25-May-28		4d
MLS-CN-60	Concessions Retail C8.3 - Turnover C8	0d	25-May-28		4d
FN-AP6-O2-450	Install Doors & Hardware - Delta Airlines Operations #1- INTF - AP 6	3d	30-May-28	01-Jun-28	0d
FN-AP7-SD-1250	Install Ceiling Light Fixtures & Trim - CBP Second. - INTF - AP 7	10d	31-May-28	13-Jun-28	6d
MLS-CN-40	Concessions Retail C8.2 - Turnover C8	0d	01-Jun-28		0d
MLS-SUPP.C-10	MLS 10 - Concessions White Box	0d		01-Jun-28 C	0d
FN-CN-2660	Install Column Covers - Overall - INTF - C8 - Ph 1	36d	01-Jun-28	21-Jul-28	0d
MLS-CN-250	Concessions Future Retail C8.7 - Turnover C8	0d	01-Jun-28		0d
FN-AP6-ER-2610	Third Party Elec. Testing - Elec. Room 6200 - INTRF - AP 6	3d	01-Jun-28	05-Jun-28	0d
MLS-CN-130	Common Use Club Entry C11.1 - Turnover C11	0d	01-Jun-28		0d
MLS-AP-120	Delta Airlines Operations A6.1 Turnover - AP6	0d	02-Jun-28		0d
MLS-AP-125	Delta Airlines Operations A6.1 - AP6 - Construction Period	200d	02-Jun-28	16-Mar-29	0d
FN-C2-SP-1080	Install Column Covers at APM/Circulation - APM Platform Area - INTF - C2	10d	05-Jun-28	16-Jun-28	0d
FN-C2-SP-1030	Install Low Voltage Trim - APM Platform Area - INTF - C2	7d	05-Jun-28	13-Jun-28	3d
FN-C2-SP-1160	Install Fire Alarm Trim - APM Platform Area - INTF - C2	5d	05-Jun-28	09-Jun-28	10d
D1978	Internal Commissioning / Functional Testing / Owner Testing [02-01-01C]	7d	06-Jun-28	14-Jun-28	0d
FN-AP6-ER-2620	Install Light Fixtures & Trim - Elec. Room 6200 - INTRF - AP 6	10d	06-Jun-28	19-Jun-28	0d
FN-AP7-SD-1270	Install Low Voltage Trim - CBP Second. - INTF - AP 7	7d	14-Jun-28	22-Jun-28	6d
FN-AP7-SD-1410	Install Fire Alarm Trim - CBP Second. - INTF - AP 7	5d	14-Jun-28	20-Jun-28	10d
D1982	Commissioning / Testing (XBM2 Cross Belt) [02-01-01C]	20d	15-Jun-28	13-Jul-28	0d
FN-C2-SP-1100	Install Light Fixtures & Trim Walls/Columns - APM Platform Area - INTF - C2	5d	19-Jun-28	23-Jun-28	0d
FN-AP6-ER-2650	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Elec. Room 6200 - INTRF - AP 6	2d	20-Jun-28	21-Jun-28	0d
FN-AP7-SD-1280	Install Fire Protection Trim - CBP Second. - INTF - AP 7	3d	21-Jun-28	23-Jun-28	10d
FN-AP6-ER-2660	APG QC Procedure for Perm Power Available for Dist. - Elec. Room 6200 - INTRF - AP 6	15d	22-Jun-28	13-Jul-28	0d
FN-AP7-SD-1290	Drop Ceiling Tile - CBP Second. - INTF - AP 7	5d	23-Jun-28	29-Jun-28	6d
FN-C2-SP-1130	Install Low Voltage Trim Walls/Columns - APM Platform Area - INTF - C2	5d	26-Jun-28	30-Jun-28	0d
FN-C2-SP-1470	Install BAS Trim Walls/Columns - APM Platform Area - INTF - C2	5d	26-Jun-28	30-Jun-28	0d
FN-AP7-SD-1320	Install Access Floors - CBP Second. - INTF - AP 7	20d	30-Jun-28	28-Jul-28	6d
FN-C2-SP-1170	Install Fire Alarm Trim Walls/Columns - APM Platform Area - INTF - C2	5d	03-Jul-28	10-Jul-28	0d
FN-C2-SP-1110	Apply All Final Paint - APM Platform Area - INTF - C2	10d	11-Jul-28	24-Jul-28	0d
MLS-SUPP.C-08	MLS 8 - Complete Paving & Utilities Interface for PBB Installation Start	0d		13-Jul-28 C	0d
IPR-ASD-ITB2-50	ASD - Glycol, Power, Data & LV Ready for ITB2 PBB Install (HP)	0d		13-Jul-28	0d
MLS-290	MLS - Permanent Power AP6 Elec. Room #6200	0d		13-Jul-28	0d
D1983	Owner Testing (XBM2 Cross Belt) [02-01-01C]	4d	14-Jul-28	19-Jul-28	0d
FN-CN-2640	Install Low Voltage Trim - Overall - INTF - C8 - Ph 1	5d	17-Jul-28	21-Jul-28	5d
D1984	Go Live (XBM2 Cross Belt) [02-01-01C]	1d	20-Jul-28	20-Jul-28	0d
A12	BHS - Mech / Elec. Demo & Install of C6 04/05 (02-01-2A)	3d	21-Jul-28	25-Jul-28	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
FN-CN-2630	Install Elec. Trim - Overall - INTF - C8 - Ph 1	5d	24-Jul-28	28-Jul-28	0d
FN-CN-2650	Install Fire Alarm Trim - Overall - INTF - C8 - Ph 1	5d	24-Jul-28	28-Jul-28	0d
FN-C2-SR-1470	Apply Final Paint - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	25-Jul-28	31-Jul-28	0d
D1991	Internal Commissioning / Functional Testing / Owner Testing [02-01-02A]	1d	25-Jul-28	25-Jul-28	0d
A13	BHS - Mech / Elec. Demo & Install of T12E 01/03 [02-01-02B]	3d	26-Jul-28	28-Jul-28	0d
D2000	Internal Commissioning / Functional Testing / Owner Testing [02-01-02B]	1d	28-Jul-28	28-Jul-28	0d
FN-CN-2670	Terrazzo Final Polish at Circ./Restroom Vestibules/Concessions Ph.1 - Overall - INTF - C8	20d	31-Jul-28	25-Aug-28	0d
FN-AP7-SC-70	Install Flooring & Base - Overall/Support Corridors - INTF - AP 7	10d	31-Jul-28	11-Aug-28	6d
A14	BHS - Mech / Elec. Demo & Install of C5 17 (02-01-02C)	2d	31-Jul-28	01-Aug-28	0d
FN-C2-SR-1490	Install FF&E- HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	01-Aug-28	07-Aug-28	0d
D2007	Internal Commissioning / Functional Testing [02-01-02C]	1d	02-Aug-28	02-Aug-28	0d
A15	BHS - Mech / Elec. Demo & Install of C5 09/10, T8 11, OSRM6 01, OSRM7 01 (02-01-02D)	10d	03-Aug-28	16-Aug-28	0d
FN-C2-SR-1500	Install Signage - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5d	08-Aug-28	14-Aug-28	0d
FN-AP6-CR-380	Install Flooring & Base - CBP Secondary - INTF - AP 6	10d	14-Aug-28	25-Aug-28	6d
FN-AP8-PM-2030	Install Decorative Glass (GL07A,B,C,D,E) - (Exterior EL-7 & EL-6) - CBP Primary - INTF - AP 8	15d	15-Aug-28	05-Sep-28	0d
FN-C3-SS-250	Install Signage - SSCP Check Points - INTF - C3	5d	15-Aug-28	21-Aug-28	0d
D2015	Internal Commissioning / Functional Testing / Owner Testing [02-01-02D]	2d	17-Aug-28	18-Aug-28	0d
A16	BHS - Mech / Elec. Demo & Install of T15 06, C8 11 (02-01-03A)	2d	21-Aug-28	22-Aug-28	0d
MLS-SUPP.C-12	MLS 12 - SSCP Area Ready for TSA Equipment	0d		21-Aug-28 C	0d
D2023	Internal Commissioning / Functional Testing / Owner Testing[02-01-03A]	1d	23-Aug-28	23-Aug-28	0d
A17	BHS - Mech / Elec. Demo & Install of C6A 03/13, C8A 02/10, ALM2 01/02, CLM2 06, OSRM5B 08/09 ...	16d	24-Aug-28	15-Sep-28	0d
FN-AP6-CR-390	Polish Exposed Concrete - CBP Secondary - INTF - AP 6	5d	28-Aug-28	01-Sep-28	6d
ASD-Bull-DT-400	Install LED Dancefloor for LED Screens - Architectural Forms (LED Screens) - INTF - C8	20d	28-Aug-28	25-Sep-28	0d
FN-AP6-CR-640	Install BAS Trim Walls - CBP Secondary - INTF - AP 6	5d	05-Sep-28	11-Sep-28	6d
FN-AP6-CR-400	Install Low Voltage Trim Walls - CBP Secondary - INTF - AP 6	5d	05-Sep-28	11-Sep-28	6d
FN-AP8-PM-1980	Terrazzo Final Polish - CBP Primary - INTF - AP 8	5d	06-Sep-28	12-Sep-28	0d
FN-AP6-CR-410	Apply Final Paint - CBP Secondary - INTF - AP 6	10d	12-Sep-28	25-Sep-28	6d
FN-AP8-PM-1880	Apply Final Paint - CBP Primary - INTF - AP 8	10d	13-Sep-28	26-Sep-28	0d
FN-FI-1540	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 11	12d	13-Sep-28	28-Sep-28	5d
D2029	Internal Commissioning / Functional Testing /Owner Testing [02-01-03B]	5d	18-Sep-28	22-Sep-28	0d
D2031	Internal Pre-TRR / Internal System Level Testing [02-01-03B]	20d	25-Sep-28	20-Oct-28	0d
COM-ELE-400	Lighting Controls Programming Interior/White Light- Light. Controls Elec. Commissioning	5d	26-Sep-28	02-Oct-28	10d
ASD-Bull-DT-390	HP Install LED Panel (21000sqft/1500 per week) - Architectural Forms (LED Screens) - INTF - C8	70d	26-Sep-28	05-Jan-29	0d
FN-AP6-CR-420	Install Signage - CBP Secondary - INTF - AP 6	5d	26-Sep-28	02-Oct-28	6d
ORAT-10	ORAT Initiation - Operational Readiness Activation & Transition (ORAT)	110d	26-Sep-28	02-Mar-29	0d
FN-AP8-PM-1930	Install FF&E - CBP Primary - INTF - AP 8	10d	27-Sep-28	10-Oct-28	0d
FN-FI-1550	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 9	12d	29-Sep-28	16-Oct-28	5d
COM-ELE-410	Lighting Controls Programming Theatrical Light. Controls Elec. Commissioning	5d	03-Oct-28	09-Oct-28	10d
FN-AP8-PM-1950	Install Signage & Dimensional Text - CBP Primary - INTF - AP 8	5d	04-Oct-28	10-Oct-28	0d
COM-ELE-390	Lighting Controls Programming RGB Light. Controls Elec. Commissioning	5d	10-Oct-28	16-Oct-28	10d
MLS-SUPP.C-13	MLS 13 - CBP Area Finishes Complete	0d		10-Oct-28 C	0d
COM-ELE-340	Perform Pre-FPT - Light. Controls Elec. Commissioning	5d	17-Oct-28	23-Oct-28	10d
FN-FI-1560	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 8	15d	17-Oct-28	06-Nov-28	5d
D2032	Owner Witnessed Testing / Pre-TRR [02-01-03B]	15d	23-Oct-28	10-Nov-28	0d
COM-ELE-350	Perform FPT - Light. Controls Elec. Commissioning	15d	24-Oct-28	13-Nov-28	10d
FN-FI-1570	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 7	15d	07-Nov-28	29-Nov-28	5d
FN-FI-1580	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 6	10d	07-Nov-28	20-Nov-28	5d
FN-FI-1110	Install Signage - Sterile Corr. 8	5d	07-Nov-28	13-Nov-28	5d
D2033	TRR [02-01-03B]	10d	13-Nov-28	28-Nov-28	0d
FN-MLS-SC-200	Sterile Level Internal Punchlist	20d	14-Nov-28	13-Dec-28	5d
COM-COT-60	ASD - COT Elec.Final Inspections - IST/Life Safety	10d	14-Nov-28	29-Nov-28	10d
COM-COT-70	ASD - COT Fire Alarm Final Inspections - IST/Life Safety	10d	21-Nov-28	06-Dec-28	10d
FN-FI-730	Install Signage - Sterile Corr. 6	5d	21-Nov-28	29-Nov-28	5d
D2034	ISAT Travel Day [02-01-03B]	1d	29-Nov-28	29-Nov-28	0d
D2035	ISAT [02-01-03B]	10d	30-Nov-28	13-Dec-28	0d
FN-FI-920	Install Signage - Sterile Corr. 7	5d	30-Nov-28	06-Dec-28	10d
MLS-SUPP.C-14	MLS 14 - TSA ISAT BHS Testing Complete	0d		13-Dec-28 C	0d
FN-MLS-SC-190	Sterile Level Finishes Complete	0d		13-Dec-28	5d
COM-COT-80	ASD - COT AHJ Life Safety Final Inspections (TCO) - IST/Life Safety	5d	14-Dec-28	20-Dec-28	5d
D2036	TRN [02-01-03B]	3d	14-Dec-28	18-Dec-28	0d



HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
A18	BHS - Mech / Elec. Demo & Install of T8 01/06 (02-01-04A)	3d	19-Dec-28	21-Dec-28	0d
D2043	Internal Commissioning / Functional Testing / Owner Testing [02-01-04A]	1d	21-Dec-28	21-Dec-28	0d
COM-COT-90	ASD - COT Building Final Inspections (TCO) - IST/Life Safety	5d	21-Dec-28	28-Dec-28	5d
A109770	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS3 [02-01-1A]	15d	22-Dec-28	15-Jan-29	3d
A19	BHS - Mech / Elec. Demo & Install of C5 05/06, TF1 01/03, T5 11, T-T5 16/17 (02-01-04B)	10d	22-Dec-28	08-Jan-29	0d
TC-FS-110	Install New AOA Fence (Excellence Drive/Trailer City)	10d	29-Dec-28	12-Jan-29	5d
ASD-Bull-DT-410	Remove LED Dancefloor for LED Screens - Architectural Forms (LED Screens) - INTF - C8	20d	08-Jan-29	02-Feb-29	0d
D2051	Internal Commissioning / Functional Testing / Owner Testing [02-01-04B]	3d	08-Jan-29	10-Jan-29	0d
BG-DM-MCP-C-510	Demo & Remove MCP C5	1d	09-Jan-29	09-Jan-29	1d
BG-DM-MCP-C-500	Demo MCP C5 Feeder Back to Source [HMCP-7]	10d	09-Jan-29	22-Jan-29	1d
BG-DM-MCP-C-530	Demo, Patch & Seal Concrete @ Former MCP C5 Housekeeping Pad	5d	10-Jan-29	16-Jan-29	1d
A20	BHS - Mech/Elec. Demo (BX4 02/05, MCP BX4) & Install of (T5 14/15) [02-01-04C]	5d	11-Jan-29	17-Jan-29	0d
TC-FS-130	Remove Temp AOA Fence (Final)	20d	15-Jan-29	09-Feb-29	5d
D2058	Internal Commissioning/Functional Testing/Owner Testing [02-01-04C]	1d	18-Jan-29	18-Jan-29	0d
D2063	Elec. MPP Install (B17) [02-02-01A]	9d	19-Jan-29	31-Jan-29	4d
A21	Mech/Elec. Demo/Install C3 11, T1 11, T1A 01/03, T5A 06/08, TXM2 01/03, TE1 05/08, TE2 03/04, ...	13d	19-Jan-29	06-Feb-29	0d
FN-CN-3160	Install Resin Deck on Concourse 9 Lid - Architectural Forms (LED Screens) - INTF - C8	10d	05-Feb-29	16-Feb-29	0d
FN-CN-3170	Install Resin Deck on Concourse 10 Lid - Architectural Forms (LED Screens) - INTF - C8	10d	05-Feb-29	16-Feb-29	0d
D2066	Internal Commissioning/Functional Testing/Owner Testing [02-02-01A]	3d	05-Feb-29	07-Feb-29	0d
A109780	Demo Ceiling Tile and Erect Temp Walls	4d	05-Feb-29	08-Feb-29	2d
BG-OPS-TC-130	T4 - Out of Service - American Airlines Shift to T6 (LOE)	1d	08-Feb-29	08-Feb-29	0d
D2071	Internal Commissioning/Functional Testing/Owner Testing [02-02-01B]	1d	08-Feb-29	08-Feb-29	0d
A22	BHS - Mech/Elec. Demo & Install of T-T4 06 (02-02-01B)	1d	08-Feb-29	08-Feb-29	0d
A23	BHS - Mech/Elec. Demo & Install (02-02-02A)	20d	09-Feb-29	08-Mar-29	2d
BG-DM-MCP-BX-400	Demo MCP BX4 Feeder Back to Source [HMCP-6]	10d	09-Feb-29	22-Feb-29	7d
BG-OPS-TC-140	C2 - Out of Service - American Airlines Shift to T6 (LOE)	23d	09-Feb-29	13-Mar-29	0d
D2075	Elec. Recontrol (C2 01/08) [02-02-02A]	5d	09-Feb-29	15-Feb-29	0d
D2078	Elec. MPP Install (B13) [02-02-02A]	16d	16-Feb-29	09-Mar-29	0d
FN-MLS-CN-310	Concourse Level Finishes Complete	0d		16-Feb-29	0d
MLS-370	MLS - ASD Construction Complete (HP Ready for C of O)	0d		16-Feb-29 C	0d
ASD-Bull-DT-360	HCAA Certify Content & Hardware - Horizontal LED Screens - INTF - C8 (Working from Manlift)	20d	19-Feb-29	16-Mar-29	0d
COM-COT-100	ASD - COT AHJ Life Safety Final Inspections (CO)- IST/Life Safety	5d	19-Feb-29	23-Feb-29	0d
BG-DM-MCP-BX-410	Demo & Remove MCP BX4	1d	23-Feb-29	23-Feb-29	7d
BG-DM-MCP-BX-430	Demo, Patch & Seal Concrete @ Former MCP BX4 Housekeeping Pad	5d	26-Feb-29	02-Mar-29	7d
COM-COT-110	ASD - COT Building Final Inspections (CO) - IST/Life Safety	5d	26-Feb-29	02-Mar-29	0d
MLS-SUPP.C-15	MLS 15 - Supplement C Project Substantial Completion (Phase 1)	0d		02-Mar-29 C	0d
D2081	Internal Commissioning/Functional Testing/Owner Testing [02-02-02A]	5d	07-Mar-29	13-Mar-29	0d
A24	BHS - Mech/Elec. Demo & Install of T5 04 & T-T5 16/17 (02-02-02B)	2d	14-Mar-29	15-Mar-29	0d
D2089	Internal Commissioning/Functional Testing/Owner Testing [02-02-02B]	1d	16-Mar-29	16-Mar-29	0d
MLS-180	MLS - Airside D Terminal Ready for First Flight	0d		16-Mar-29 C	0d
MLS-1100	MLS - Architectural LEDs Install & Testing Complete	0d		16-Mar-29	0d
MLS-950	MLS - ASD Construction Complete (HCAA Stakeholders Ready for C of O)	0d		16-Mar-29	0d
A25	BHS - Mech/Elec. Demo & Install of C4 08/09, T11A 12/15, T5A 01/03 (02-02-02C)	9d	19-Mar-29	29-Mar-29	0d
D2095	Internal Commissioning/Functional Testing/Owner Testing [02-02-02C]	2d	29-Mar-29	30-Mar-29	0d
D2098	Elec. Recontrol (T4 01/03) [02-02-02D]	4d	02-Apr-29	05-Apr-29	0d
A26	BHS - Mech/Elec. Demo (T4 04/08) & Install of C3 11, T4 04/06, C1 07/09 (02-02-02D)	5d	02-Apr-29	06-Apr-29	1d
D2103	Internal Commissioning/Functional Testing/Owner Testing [02-02-02D]	2d	06-Apr-29	09-Apr-29	0d
A27	BHS - Mech/Elec. Demo & Install of TE1 09/11, T-TE1 12/16, T-TE2 05/07 (02-02-02E)	7d	10-Apr-29	18-Apr-29	0d
D2106	Elec. Recontrol (C1 01/05) [02-02-02E]	3d	10-Apr-29	12-Apr-29	5d
D2113	Internal Commissioning/Functional Testing/Owner Testing (C1) [02-02-02E]	1d	16-Apr-29	16-Apr-29	4d
D2115	Internal Commissioning/Functional Testing/Owner Testing (TE1/TE2) [02-02-02E]	2d	19-Apr-29	20-Apr-29	0d
D2122	Internal Commissioning/Functional Testing/Owner Testing [02-02-02F]	1d	23-Apr-29	23-Apr-29	0d
A28	BHS - Mech/Elec. Demo & Install of C3 06 (02-02-02F)	1d	23-Apr-29	23-Apr-29	0d
A29	BHS - Mech/Elec. Demo & Install of T3 04/11 (02-02-02G)	5d	24-Apr-29	30-Apr-29	0d
D2129	Internal Commissioning/Functional Testing/Owner Testing [02-02-02G]	1d	01-May-29	01-May-29	0d
D2132	Elec. Recontrol (T3 02/03) [02-02-03A]	2d	02-May-29	03-May-29	0d
A30	BHS - Mech/Elec. Demo & Install of T3 02/03 02-02-03A	2d	02-May-29	03-May-29	0d
A31	BHS - Mech/Elec. Demo & Install of T1 10, T-SS8 06/07, TXM1 07/08 02-02-03A	4d	03-May-29	08-May-29	0d
D2140	Internal Commissioning/Functional Testing/Owner Testing [02-02-03A]	1d	09-May-29	09-May-29	0d
D2146	Demo EDS Machine (SS7) [02-02-03B]	2d	10-May-29	11-May-29	0d

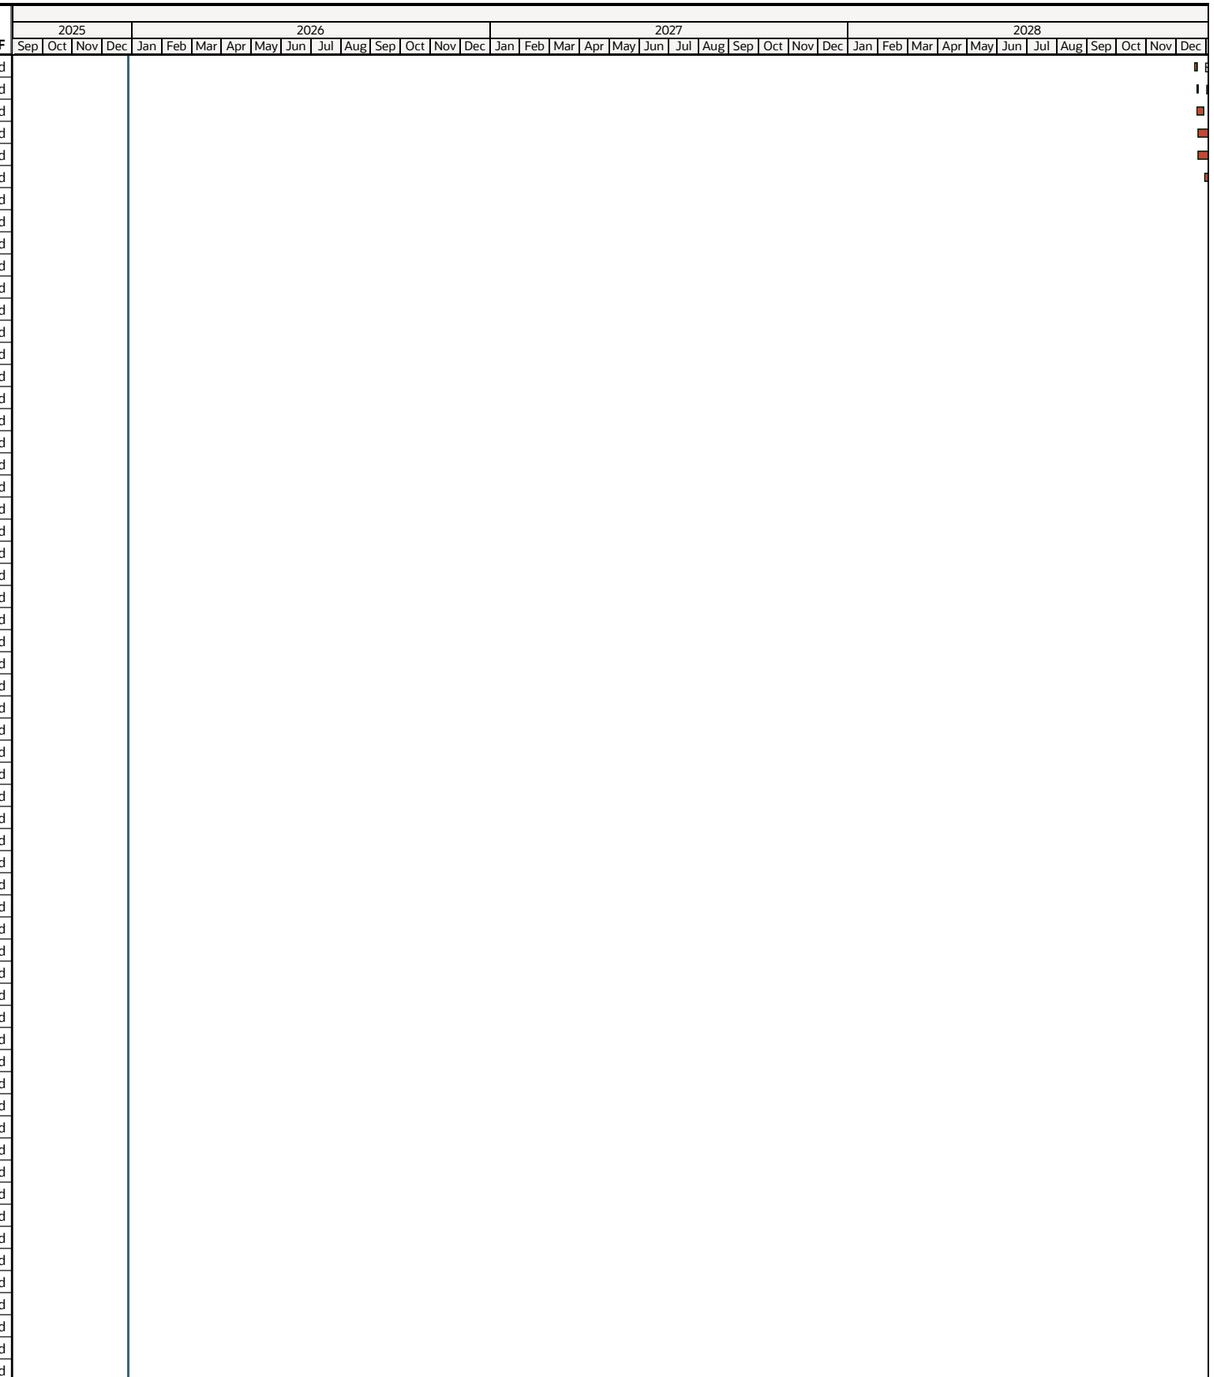

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport


ASD Critical Path Schedule - December 2025 CPM Update

Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical
Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

ID	Name	Dur	Start	Finish	TF
A32	BHS - Mech/Elec. Demo & Install of SS7 06/07 & T-SS8 05 (02-02-03B)	2d	10-May-29	11-May-29	0d
D2150	Internal Commissioning/Functional Testing/Owner Testing [02-02-03B]	1d	14-May-29	14-May-29	0d
D2152	Elec. Demo [02-02-03C]	10d	15-May-29	29-May-29	0d
D2153	Mech Demo [02-02-03C]	10d	30-May-29	12-Jun-29	0d
D2156	Elec. Install (T1 07/09) [02-02-03C]	3d	06-Jun-29	08-Jun-29	0d
D2157	Mech Install (T1 07/09) [02-02-03C]	3d	06-Jun-29	08-Jun-29	0d
D2158	Internal Commissioning/Functional Testing (T1 07/09) [02-02-03C]	1d	11-Jun-29	11-Jun-29	0d
D2159	Elec. Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-03C]	15d	11-Jun-29	29-Jun-29	3d
D2160	Mech Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-03C]	15d	11-Jun-29	29-Jun-29	3d
D2166	Elec. Recontrol (T2 01/04) [02-02-04A]	3d	12-Jun-29	14-Jun-29	0d
A33	BHS - Mech/Elec. Demo & Install T2 05/07 (02-02-04A)	3d	12-Jun-29	14-Jun-29	0d
D2154	ControlNet Rework/Elec Demo (MCP-T3, MCP-AS1, MCP-CX1/CX3, MCP-MCP-BX1, MCP-CX2) [02-02...	15d	13-Jun-29	03-Jul-29	1d
A110480	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS1 [02-02-03C]	15d	13-Jun-29	03-Jul-29	1d
D2172	Internal Commissioning/Functional Testing/Owner Testing [02-02-04A]	1d	15-Jun-29	15-Jun-29	0d
D2174	Elec. Recontrol (T1 01/04) [02-02-04B]	3d	18-Jun-29	20-Jun-29	0d
A34	BHS - Mech/Elec. Demo & Install T1 05/06 (02-02-04B)	3d	18-Jun-29	20-Jun-29	0d
D2179	Internal Commissioning/Functional Testing/Owner Training [02-02-04B]	1d	21-Jun-29	21-Jun-29	0d
D2182	ControlNet Rework/Elec Demo (MCP-T1/T2, MCP-AS2) [02-02-05]	5d	22-Jun-29	28-Jun-29	0d
A110490	Demo EDS Access Platform in AS1 [02-02-03C]	5d	27-Jun-29	03-Jul-29	1d
B35	BHS - Mech/Elec. Demo & Install of (AS2 01/07, T1 07/09, T2 06/10, SS7 01/04, T-SS8 05/07) [02-0...	10d	29-Jun-29	13-Jul-29	0d
D2163	Elec. Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18) [02-02-03C]	20d	02-Jul-29	30-Jul-29	3d
D2162	Elec. Install (MPP-AOS, FCP-AOS, MPP-BOS, FCP-BOS) [02-02-03C]	20d	05-Jul-29	01-Aug-29	1d
D2164	Mech Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18, Inspection Tables) [02-02-03C]	20d	05-Jul-29	01-Aug-29	1d
BG-DM-MCP-AS-220	Demo Exist. Housekeeping Pad Beneath Former MCP AS2	1d	16-Jul-29	16-Jul-29	0d
BG-DM-MCP-AS-230	Patch & Seal Concrete @ Former MCP AS2 Housekeeping Pad	3d	17-Jul-29	19-Jul-29	0d
A35	BHS - Mech/Elec. Demo & Install of TE1 15/16, TE2 09/10, TXM1 01/06 (02-02-05)	13d	20-Jul-29	07-Aug-29	0d
D2190	Mech Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10d	02-Aug-29	15-Aug-29	1d
D2189	Elec. Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10d	02-Aug-29	15-Aug-29	1d
D2187	Internal Commissioning/Functional Testing [02-02-05]	2d	08-Aug-29	09-Aug-29	0d
D2188	Owner Testing [02-02-05]	1d	09-Aug-29	09-Aug-29	0d
A36	BHS - Mech/Elec. Demo & Install of (TE1 12) [02-02-06]	3d	10-Aug-29	14-Aug-29	0d
D2201	Internal Commissioning/Functional Testing/Owner Testing [02-02-06]	1d	15-Aug-29	15-Aug-29	0d
D2191	Internal Commissioning / Functional Testing- Oversized Screening [02-02-05]	5d	16-Aug-29	22-Aug-29	1d
A37	BHS - Mech/Elec. Demo & Install of (T-TE2 05, EX2 07) & (TE2 05, TE2 16/17) [02-02-07]	5d	16-Aug-29	22-Aug-29	0d
D2192	Owner / TRR Testing- Oversized Screening [02-02-05]	5d	23-Aug-29	29-Aug-29	1d
D2208	Internal Commissioning/Functional Testing/Owner Testing [02-02-07]	1d	23-Aug-29	23-Aug-29	0d
A38	BHS - Mech/Elec. Demo & Install of (T-TE2 06/07, T-TE1 14/16, EX2 01/06, EX2 08/15) [02-02-08]	4d	24-Aug-29	29-Aug-29	0d
D2193	ISAT Travel Day [02-02-05]	1d	30-Aug-29	30-Aug-29	1d
FCPL-160	CCBS Post-ISAT - Internal Completion/Punchlist Development	15d	30-Aug-29	20-Sep-29	0d
D2194	ISAT Testing (Oversized Screening) [02-02-05]	4d	31-Aug-29	06-Sep-29	1d
D2195	TRN (Oversized Screening) [02-02-05]	5d	07-Sep-29	13-Sep-29	1d
MLS-SUPP.C-16	MLS 16 - Supplement C Project Substantial Completion (Phase 2 - CCBS 2-2)	0d		13-Sep-29 C	1d
FCPL-170	Owner Final Commissioning/Punchlist Development Phase 2 (ASD & CCBS)	65d	21-Sep-29	24-Dec-29	0d
FCPL-180	Owner Final Commissioning/Punchlist Completion Phase 2 (ASD & CCBS)	60d	26-Dec-29	20-Mar-30	0d
MLS-190	MLS - Overall Project Final Completion	0d		20-Mar-30 C	0d

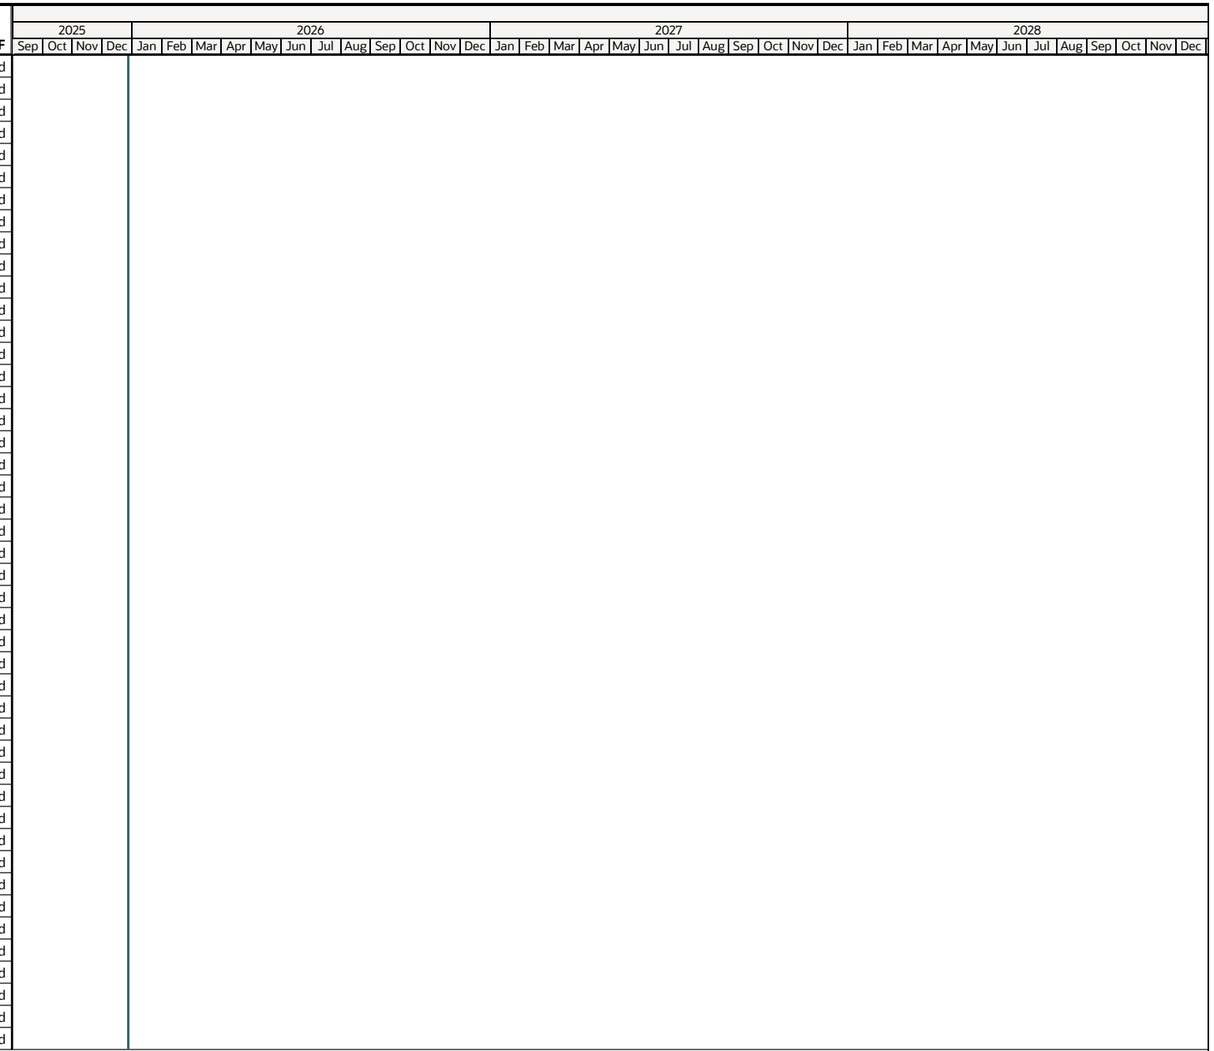

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Critical Path Schedule - December 2025 CPM Update


Filters: ASD Critical Path, Not Completed
ASD Critical Path Filter:
Total Float less than or equal to 10 days

Current
Progress
Critical

Milestones
Summary

Revised 02-Jan-26 08:16 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | **Region Code:** HP-800
HCAA Package #8500 23
View Name: ASD Critical Path
Printed By: Jill Spinnenweber
Filters: ASD Critical Path, Not Completed

	ID	Name	Dur	Start	Finish	TF
1	WBS - Airside D - Tampa International Airport		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
2	WBS - PROJECT TIME TABLE SUMMARY		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
3	PTTS-10	Project Timetable Summary to Substantial Completion (LOE)	1,417.0d	3-Aug-23 A	2-Mar-29	0.0d
4	MLS-05	MLS - ASD Project Start	0.0d	3-Aug-23 A		
5	MLS-10	MLS - Design Kickoff Mtg.	0.0d	8-Aug-23 A		
6	MLS-190	MLS - Overall Project Final Completion	0.0d		21-Mar-30 C	0.0d
7	WBS - Airside D - Supplement C Contractual Milestones		966.0d	25-Nov-25	14-Sep-29	0.0d
8	MLS-SUPP.C-01	MLS 1 - Enabling Substantial Completion	0.0d		25-Nov-25 A	
9	MLS-SUPP.C-02	MLS 2 - Demo Second Half of Tunnel Structure Complete	0.0d		12-Feb-26 C	0.0d
10	MLS-SUPP.C-03	MLS 3 - Barrier Mounted AOA Fence Relocation Complete	0.0d		25-Aug-26 C	0.0d
11	MLS-SUPP.C-04	MLS 4 - Supplement A Substantial Completion	0.0d		21-Oct-26 C	0.0d
12	MLS-SUPP.C-07	MLS 7 - Alstom Early Turnover	0.0d		8-Apr-27 C	0.0d
13	MLS-SUPP.C-09	MLS 9 - Building Dry-in Complete - Exterior Roof & Facade	0.0d		24-Aug-27 C	0.0d
14	MLS-SUPP.C-06	MLS 6 - Supplement B Substantial Completion	0.0d		10-Sep-27 C	0.0d
15	MLS-SUPP.C-05	MLS 5 - Install of VGDS Found. & Conduits Complete	0.0d		10-Nov-27 C	0.0d
16	MLS-SUPP.C-10	MLS 10 - Concessions White Box	0.0d		1-Jun-28 C	0.0d
17	MLS-SUPP.C-11	MLS 11 - Tenant White Box (Delta, Unnassigned Airlines, Etc)	0.0d		2-Jun-28 C	14.0d
18	MLS-SUPP.C-08	MLS 8 - Complete Paving & Utilities Interface for PBB Installation Start	0.0d		13-Jul-28 C	0.0d
19	MLS-SUPP.C-12	MLS 12 - SSCP Area Ready for TSA Equipment	0.0d		21-Aug-28 C	0.0d
20	MLS-SUPP.C-13	MLS 13 - CBP Area Finishes Complete	0.0d		10-Oct-28 C	0.0d
21	MLS-SUPP.C-14	MLS 14 - TSA ISAT BHS Testing Complete	0.0d		13-Dec-28 C	0.0d
22	MLS-SUPP.C-15	MLS 15 - Supplement C Project Substantial Completion (Phase 1)	0.0d		2-Mar-29 C	0.0d
23	MLS-SUPP.C-16	MLS 16 - Supplement C Project Substantial Completion (Phase 2 - CCBS 2-2)	0.0d		14-Sep-29 C	0.0d
24	WBS - Airside D - Other Major Milestones		1,367.0d	30-Oct-23 A	16-Mar-29	98.0d
25	MLS-20	MLS - City Of Tampa Permitting Office Kick-Off Mtg.	0.0d	30-Oct-23 A		
26	MLS-30	MLS - Notice to Proceed/Enabling Construction Start	0.0d	13-Dec-24 A		
27	MLS-40	MLS - Approval Of FAA 7460 For Crane Plan	0.0d	27-Dec-24 A		
28	MLS-70	MLS - Ground Improvements Start	0.0d	3-Nov-25 A		
29	MLS-390	MLS - CIP Concrete Found. Start	0.0d	1-Dec-25 A		
30	MLS-380	MLS - Ground Improvements (DIPS) Complete	0.0d		27-Jan-26	46.0d
31	MLS-60	MLS - ASD - Enabling Scope Complete	0.0d		12-Feb-26	785.0d
32	MLS-80	MLS - Structural Steel Erection Start	0.0d	19-May-26		0.0d
33	MLS-400	MLS - CIP Concrete Found. Complete	0.0d		1-Jul-26	0.0d
34	MLS-125	MLS - Temp Facade Mockup Complete	0.0d		24-Aug-26	81.0d
35	MLS-95	MLS - Structural Steel Erection Complete	0.0d		4-Mar-27	16.0d
36	MLS-210	MLS - Pre-Cast / Curtainwall Facade Start	0.0d	21-Jul-27		0.0d
37	MLS-100	MLS - Pre-Cast / Curtainwall Facade Complete	0.0d		24-Aug-27	0.0d
38	MLS-1240	MLS - ASD Roof Complete	0.0d		17-Dec-27	413.0d
39	MLS-1080	MLS - Complete GSE Paving Areas	0.0d		7-Mar-28	101.0d
40	MLS-250	MLS - Start Commissioning (Start-Ups)	0.0d	7-Aug-28		135.0d
41	MLS-470	MLS - Turnover of Telecom/Main Equip. Rooms to HCAA	0.0d		10-Aug-28	63.0d
42	MLS-140	MLS - TSA Checkpoint Complete (SSCP)	0.0d		31-Oct-28	74.0d

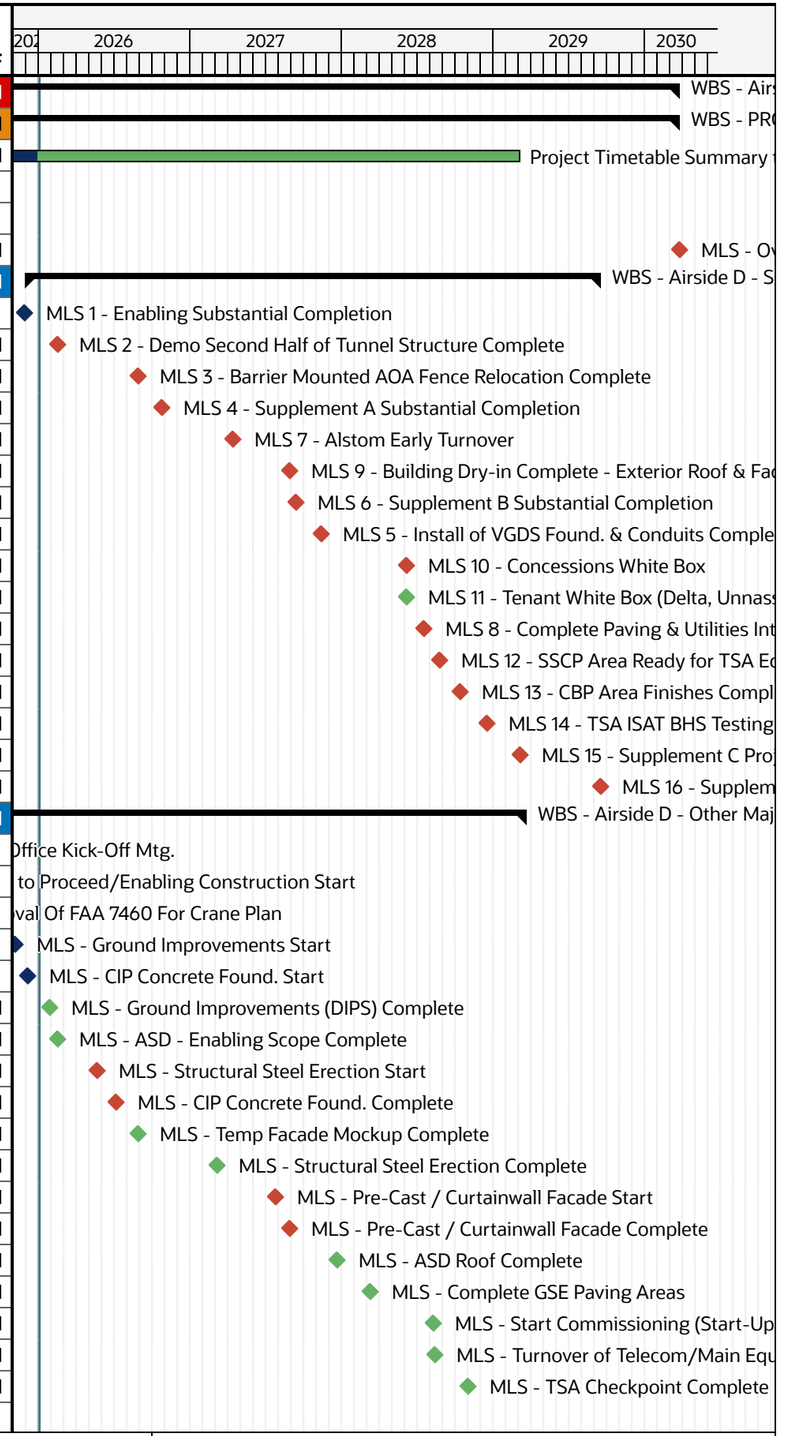


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:01 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
43	MLS-185	MLS - Elevator/Escalator Install Complete	0.0d		27-Nov-28	57.0d
44	MLS-230	MLS - Fire Alarm Install Complete	0.0d		6-Dec-28	50.0d
45	MLS-270	MLS - Commissioning Complete	0.0d		7-Dec-28	49.0d
46	MLS-1040	MLS - ASD/Guideway BHS System Complete	0.0d		8-Dec-28	48.0d
47	MLS-1090	MLS - All AOA Fence Modifications Complete	0.0d		9-Feb-29	25.0d
48	MLS-370	MLS - ASD Construction Complete (HP Ready for C of O)	0.0d		16-Feb-29 C	0.0d
49	MLS-180	MLS - Airside D Terminal Ready for First Flight	0.0d		16-Mar-29 C	0.0d
50	MLS-950	MLS - ASD Construction Complete (HCAA Stakeholders Ready for C of O)	0.0d		16-Mar-29	0.0d
51	MLS-1100	MLS - Architectural LEDs Install & Testing Complete	0.0d		16-Mar-29	0.0d
52	WBS - Electrical Milestones		617.0d	2-Mar-26	3-Aug-28	16.0d
53	MLS-360	MLS - Temp Power to Building	0.0d		2-Mar-26	71.0d
54	MLS-110	MLS - Permanent Power on From Utility (TECO)	0.0d		14-Sep-26	354.0d
55	MLS-220	MLS - Permanent Power AP1 Main/EER Elec. Rooms #6081/6082	0.0d		21-Sep-27	166.0d
56	MLS-350	MLS - Permanent Power CL1 Elec. Room #6676	0.0d		11-Jan-28	137.0d
57	MLS-320	MLS - Permanent Power AP7 Distribution Elec. Room #6196	0.0d		8-Feb-28	110.0d
58	MLS-340	MLS - Permanent Power AP11 Distribution Elec. Room #6003	0.0d		4-Apr-28	70.0d
59	MLS-330	MLS - Permanent Power AP8 Distribution Elec. Room #6290	0.0d		25-Apr-28	55.0d
60	MLS-290	MLS - Permanent Power AP6 Elec. Room #6200	0.0d		13-Jul-28	0.0d
61	MLS-310	MLS - Permanent Power AP6 CBP Elec. Room #6175	0.0d		3-Aug-28	16.0d
62	MLS-960	MLS - Permanent Power Available (Entire Building)	0.0d		3-Aug-28	16.0d
63	WBS - Mechanical Milestones		338.0d	26-Mar-27	25-Jul-28	143.0d
64	MLS-920	MLS - Temp Building Conditioning Available	0.0d		24-Aug-27	0.0d
65	MLS-940	MLS - Temp Building Conditioning - (LOE)	233.0d	25-Aug-27	25-Jul-28	143.0d
66	MLS-870	MLS - Mech. Start-Up AP12 CUP Room #6079	0.0d		25-Feb-28	248.0d
67	MLS-880	MLS - Mech. Start-Up CN2 AHU Room #6459	0.0d		25-Feb-28	138.0d
68	MLS-840	MLS - Mech. Start-Up AP7 AHU Room #6190	0.0d		1-Mar-28	121.0d
69	MLS-860	MLS - Mech. Start-Up AP10 AHU Room #6007	0.0d		14-Apr-28	89.0d
70	MLS-850	MLS - Mech. Start-Up AP5 Trash Room #6299	0.0d		5-May-28	198.0d
71	MLS-910	MLS - Mech. Start-Up CL1 AHU Room #6682	0.0d		10-May-28	85.0d
72	MLS-900	MLS - Permanent Conditioned Air Available (Entire Building)	0.0d		25-Jul-28	143.0d
73	MLS-890	MLS - Mech. Start-Up AP6 AHU Room #6191	0.0d		25-Jul-28	24.0d
74	WBS - Duct Milestones		155.0d	26-Mar-27	3-Nov-27	210.0d
75	MLS-830	MLS - Duct Insulation Complete - Club Level	0.0d		26-Mar-27	365.0d
76	MLS-790	MLS - Duct Install Complete - Club Level	0.0d		14-May-27	330.0d
77	MLS-700	MLS - Duct Install Complete - Sterile Level	0.0d		27-May-27	145.0d
78	MLS-720	MLS - Duct Insulation Complete - Sterile Level	0.0d		2-Jun-27	162.0d
79	MLS-750	MLS - Duct Install Complete - Concourse Level	0.0d		8-Jul-27	193.0d
80	MLS-800	MLS - Duct Insulation Complete - Concourse Level	0.0d		24-Aug-27	122.0d
81	MLS-780	MLS - Duct Insulation Complete - Apron Level	0.0d		22-Oct-27	143.0d
82	MLS-730	MLS - Duct Install Complete - Apron Level	0.0d		3-Nov-27	65.0d
83	WBS - Pipe Milestones		155.0d	28-Apr-27	8-Dec-27	187.0d
84	MLS-810	MLS - MECH Piping Complete - Club Level	0.0d		28-Apr-27	242.0d

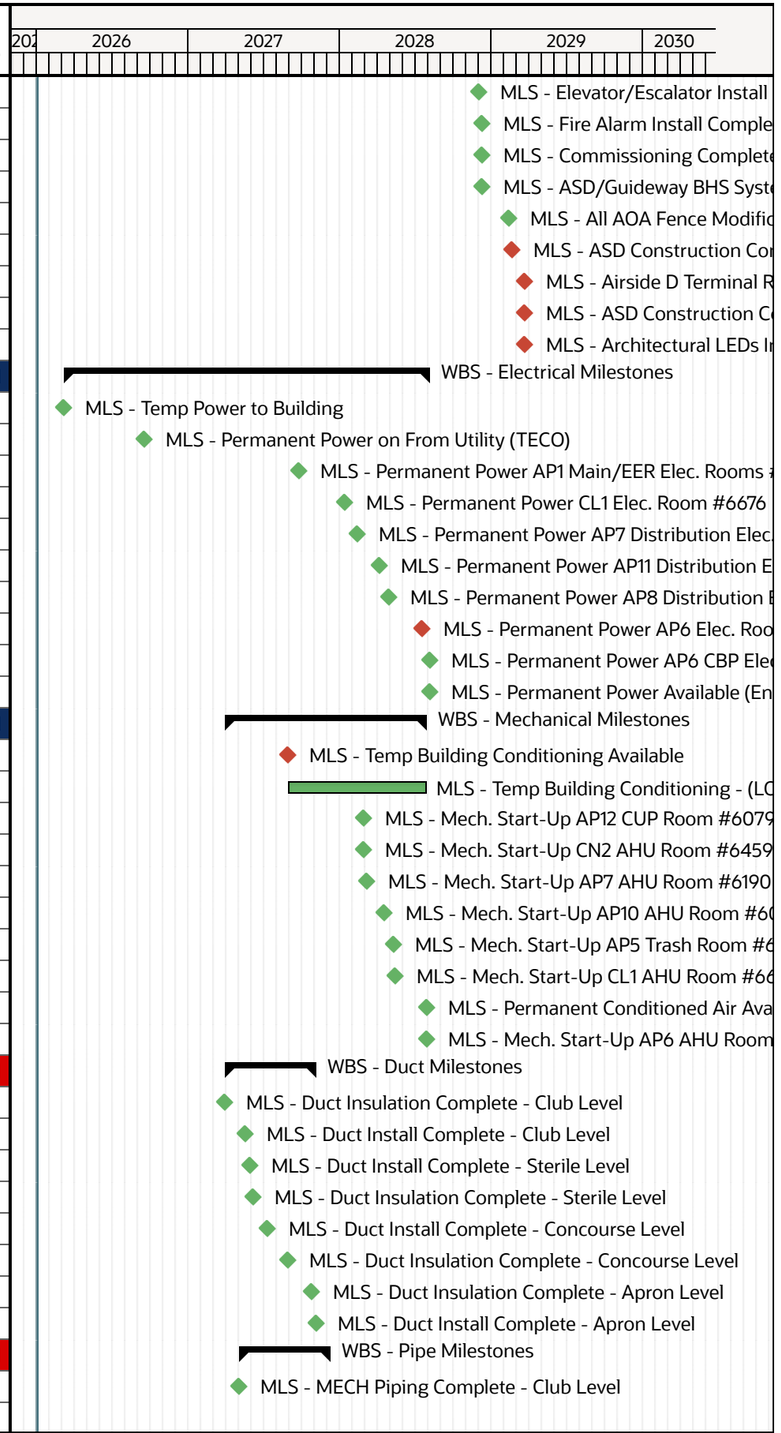


	ID	Name	Dur	Start	Finish	TF
85	MLS-710	MLS - MECH Piping Complete - Concourse Level	0.0d		9-Jun-27	213.0d
86	MLS-770	MLS - MECH Piping Insulation Complete - Concourse Level	0.0d		29-Jul-27	274.0d
87	MLS-820	MLS - MECH Piping Insulation Complete - Club Level	0.0d		17-Aug-27	265.0d
88	MLS-740	MLS - MECH Piping Complete - Apron Level	0.0d		17-Nov-27	100.0d
89	MLS-760	MLS - MECH Piping Insulation Complete - Apron Level	0.0d		8-Dec-27	117.0d
90	WBS - Airside D - SOV LOE's		1,339.0d	13-Dec-24 A	21-Mar-30	0.0d
91	ASD-HAM-10	ASD - General Conditions / Requirements - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
92	ASD-HAM-20	ASD - Contingency/Allowance/Budget - LOE	1,338.0d	13-Dec-24 A	21-Mar-30	0.0d
93	EN-HAM-50	Enabling - Demo Apron Concrete - (LOE)	94.0d	27-Jan-25 A	6-Jun-25 A	
94	EN-HAM-40	Performance Park/Office Trailers - (LOE)	211.0d	27-Jan-25 A	20-Nov-25 A	
95	EN-HAM-70	Enabling Apron Site Work - (LOE)	65.0d	18-Aug-25 A	17-Nov-25 A	
96	CCBS-HAM-30	CCBS - Supp B General Conditions / Requirements - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
97	CCBS-HAM-40	CCBS - Supp B Contingency/Allowance/Budget - LOE	492.0d	2-Oct-25 A	10-Sep-27	0.0d
98	GI-HAM-10	Ground Improvements Scope LOE - DIP/LTP	63.0d	27-Oct-25 A	27-Jan-26	46.0d
99	GI-FS-HAM-1010	Found. Concrete Scope - LOE	153.0d	24-Nov-25 A	1-Jul-26	0.0d
100	GI-FS-HAM-1030	Deep UG Plumbing & Mech. Scope - LOE	185.0d	16-Dec-25 A	4-Sep-26	0.0d
101	GI-FS-HAM-1020	Deep UG Elec. & Comm. Scope - LOE	165.0d	16-Dec-25 A	7-Aug-26	112.0d
102	PR-P2-1B-3705	Delivery of Allowance Long Lead - Steel Mill Order - Part 2 Supp. A (LOE)	84.0d	2-Jan-26	26-Mar-26	0.0d
103	PR-P2-1B-2335	Delivery of Allowance Long Lead Mech. Chillers on Site - Part 2 Supp. A (LOE)	251.0d	10-Feb-26	22-Oct-26	508.0d
104	PR-P2-1B-465	Allowance Long Lead Elec.- Fab. & Ship Gear - Part 2 Supp. A (LOE)	365.0d	17-Feb-26	24-Feb-27	232.0d
105	A109790	Allowance Long Lead Elec. Equip. - Fab. & Ship Part 2 Supp. B (LOE)	110.0d	17-Feb-26	7-Jun-26	15.0d
106	GI-FS-110	Steel Framing Erection - Structure & Slabs (LOE)	181.0d	19-May-26	4-Feb-27	16.0d
107	ASD-HAM-MU-100	Allowance ASD Mock-Up (LOE)	58.0d	1-Jun-26	20-Aug-26	81.0d
108	WBS - MLS - Alstom Area Milestones		141.0d	7-Apr-27	26-Oct-27	610.0d
109	MLS-1010	MLS - Alstom PDS/UPS Rooms Complete	0.0d		7-Apr-27	1.0d
110	MLS-1000	MLS - Alstom Train Tubes Complete	0.0d		8-Apr-27	0.0d
111	MLS-1020	MLS - Alstom Maintenance / Support Rooms Complete	0.0d		20-Jul-27	421.0d
112	MLS-1030	MLS - Alstom Facility Power Available	0.0d		26-Oct-27	609.0d
113	WBS - HCAA Board Approvals		551.0d	3-Aug-23	2-Oct-25 A	
114	MLS-BA-10	HCAA Board Approval Award Part 1 Agreement - 8.3.23	0.0d		3-Aug-23 A	
115	MLS-BA-20	Part 1 Agreement Design Notice to Proceed - 8.4.23	0.0d		4-Aug-23 A	
116	MLS-BA-30	HCAA Board Approval Enabling Pkg. - 12.5.24	0.0d		5-Dec-24 A	
117	MLS-BA-40	ITB 1 Pkg. - 6.5.25	0.0d		5-Jun-25 A	
118	MLS-BA-60	Part 2 Supp. A Agreement - Ground Improvement & Found. Pkg. - 8.7.25	0.0d		7-Aug-25 A	
119	MLS-BA-80	ITB 2 & 3 Pkg.s - 8.7.25	0.0d		7-Aug-25 A	
120	MLS-BA-90	HCAA June Board Approval of NST Credit Purchase Agreement - 8.7.25	0.0d		7-Aug-25 A	
121	MLS-BA-100	Part 2 Supp. B Agreement - Centralized Checked Baggage - 10.2.25	0.0d		2-Oct-25 A	
122	MLS-BA-110	Part 2 Supplement B - Board Approval	0.0d		2-Oct-25 A	
123	WBS - Design Milestones		260.0d	13-Aug-24	21-Aug-25 A	
124	MLS-DM-10	100% Enabling Pkg./BOD Due To HCAA Complete	0.0d		13-Aug-24 A	
125	MLS-DM-20	30% SD - ITB Pkg.s Submittals Due To HCAA Complete	0.0d		1-Oct-24 A	
126	MLS-DM-30	30% SD Final - 30% SD Due To HCAA Complete	0.0d		21-Nov-24 A	

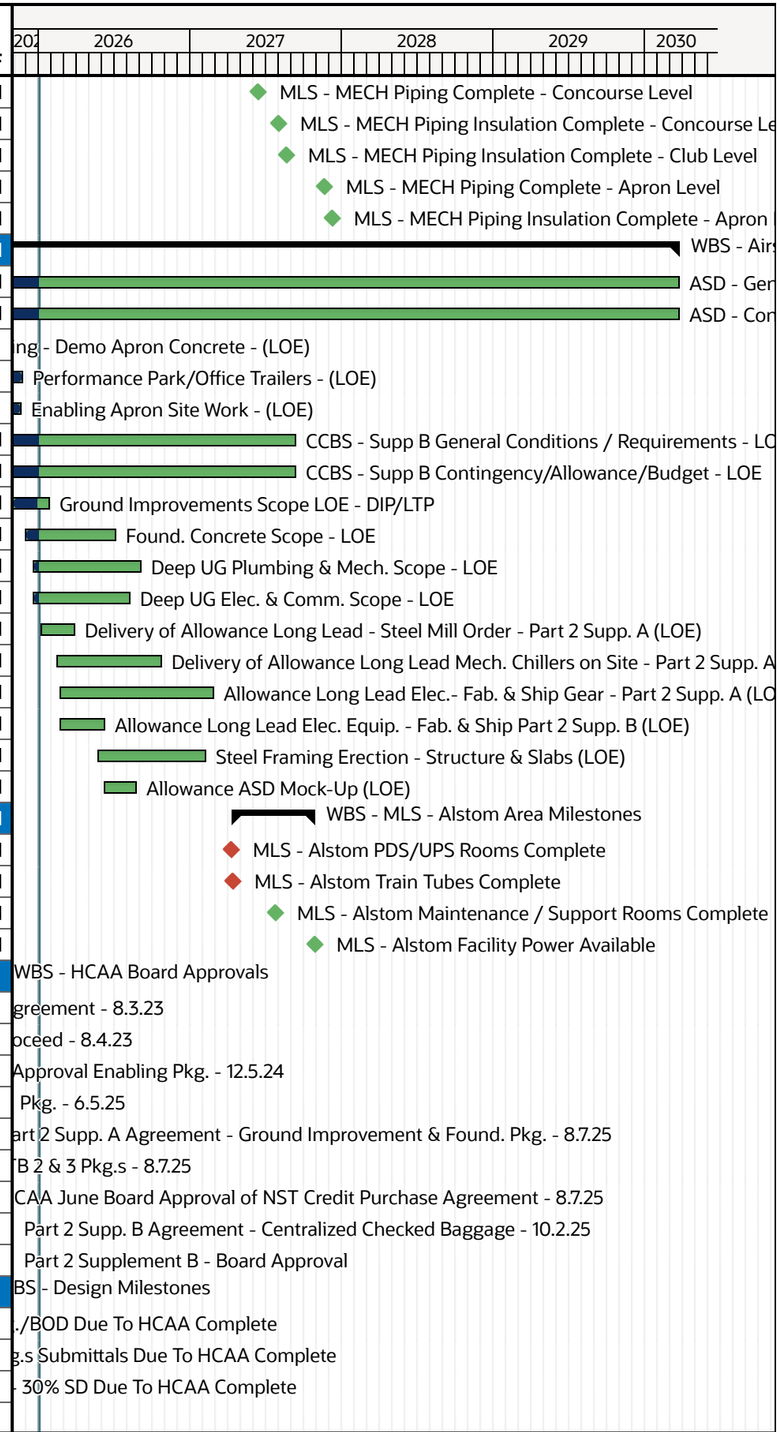


	ID	Name	Dur	Start	Finish	TF
127	MLS-DM-40	FAA/60% DD - ITB 1 Pkg. Submittals Due To HCAA Complete	0.0d		20-Dec-24 A	
128	MLS-DM-140	FAA/60% DD - ITB 3 Pkg. Submittals Due To HCAA Complete	0.0d		20-Dec-24 A	
129	MLS-DM-220	TSA SD/15% BHS Submission Complete	0.0d		20-Dec-24 A	
130	MLS-DM-130	FAA/60% DD - ITB 2 Pkg. Submittals Due To HCAA Complete	0.0d		10-Jan-25 A	
131	MLS-DM-50	60% Early Found. - 60% DD Subm. Due To HCAA Complete	0.0d		11-Feb-25 A	
132	MLS-DM-190	TSA CBIS 30% Deliverable Complete	0.0d		17-Mar-25 A	
133	MLS-DM-60	IFB/90% CD - ITB 1 Pkg. Subm. Due To HCAA Complete	0.0d		20-Mar-25 A	
134	MLS-DM-80	100% Early Found. - 100% DD Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
135	MLS-DM-160	IFB/90% CD - ITB 3 Pkg. Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
136	MLS-DM-150	ITB/90% CD - ITB 2 Pkg. Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
137	MLS-DM-170	Final Addendum CD - ITB 1 Subm. Due To HCAA Complete	0.0d		22-Apr-25 A	
138	MLS-DM-70	60% DD - 60% DD Due To HCAA Complete	0.0d		8-May-25 A	
139	MLS-DM-90	Final Addendum CD - ITB 2 Subm. Due To HCAA Complete	0.0d		16-May-25 A	
140	MLS-DM-180	Final Addendum CD - ITB 3 Subm. Due To HCAA Complete	0.0d		16-May-25 A	
141	MLS-DM-100	75% Long Lead Pkg. - Procurement Subm. Due To HCAA Complete	0.0d		12-Jun-25 A	
142	MLS-DM-110	90% CD's/Permit - Final CD's Due To HCAA Complete	0.0d		21-Aug-25 A	
143	MLS-DM-200	TSA 70% BHS Submission Complete	0.0d		21-Aug-25 A	
144	WBS - Request For Information (RFI)		46.0d	17-Jul-25 A	19-Sep-25 A	
145	RFI-EN-00078	RFI - EN - 00078 - Trailer 4 Drainage Clarification	46.0d	17-Jul-25 A	19-Sep-25 A	
146	WBS - TAMPA AIRSIDE D TERMINAL		1,686.0d	3-Aug-23 A	21-Mar-30	0.0d
147	WBS - ASD - DESIGN & ENGINEERING PHASE		1,161.0d	3-Aug-23 A	28-Feb-28	525.0d
148	WBS - PDD Validation		148.0d	3-Aug-23 A	4-Mar-24 A	
149	WBS - Design Kickoff		24.0d	3-Aug-23 A	6-Sep-23 A	
150	DS-PDD-10	Summary/Analysis -PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
151	DS-PDD-20	Aircraft Planning - PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
152	DS-PDD-30	Building Footprint Development -PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
153	WBS - Design Charrette #1		22.0d	7-Aug-23 A	6-Sep-23 A	
154	DS-PDD-60	Forms & Mass Coord. - Validation Design Charrette #1	20.0d	7-Aug-23 A	1-Sep-23 A	
155	DS-PDD-70	Charrette In KC - Validation Design Charrette #1	2.0d	5-Sep-23 A	6-Sep-23 A	
156	WBS - Design Presentation #1 HCAA		3.0d	5-Sep-23 A	7-Sep-23 A	
157	DS-PDD-80	Design Presentation #1 - Steering Committee Mtg. Prep	2.0d	5-Sep-23 A	6-Sep-23 A	
158	DS-PDD-90	Design Presentation #1 - Steering Committee Mtg. #1 - Building Program	1.0d	7-Sep-23 A	7-Sep-23 A	
159	WBS - Design Presentation #2 HCAA		30.0d	3-Aug-23 A	14-Sep-23 A	
160	DS-PDD-40	BHS Kickoff Prep & Coord. - Design Presentation #2	28.0d	3-Aug-23 A	12-Sep-23 A	
161	DS-PDD-150	VTC Discussion - Design Presentation #2	1.0d	13-Sep-23 A	13-Sep-23 A	
162	DS-PDD-160	BHS Kickoff CBIS Mtg. - Design Presentation #2	1.0d	14-Sep-23 A	14-Sep-23 A	
163	WBS - Design Presentation #3 - Terminal Program		33.0d	3-Aug-23 A	19-Sep-23 A	
164	DS-PDD-50	Presentation Prep & Coord. - Design Presentation #3	32.0d	3-Aug-23 A	18-Sep-23 A	
165	DS-PDD-180	Building Space Program Allocation Mtg. - 9/19/23 - Design Presentation #3	1.0d	19-Sep-23 A	19-Sep-23 A	
166	WBS - Design Presentation #4 - CBP/Concessions Update		11.0d	7-Sep-23 A	21-Sep-23 A	
167	DS-PDD-100	Presentation Prep & Coord. - Design Presentation #4	10.0d	7-Sep-23 A	20-Sep-23 A	
168	DS-PDD-210	Stakeholder Engagement Kickoff Mtg. - Design Presentation #4	1.0d	21-Sep-23 A	21-Sep-23 A	

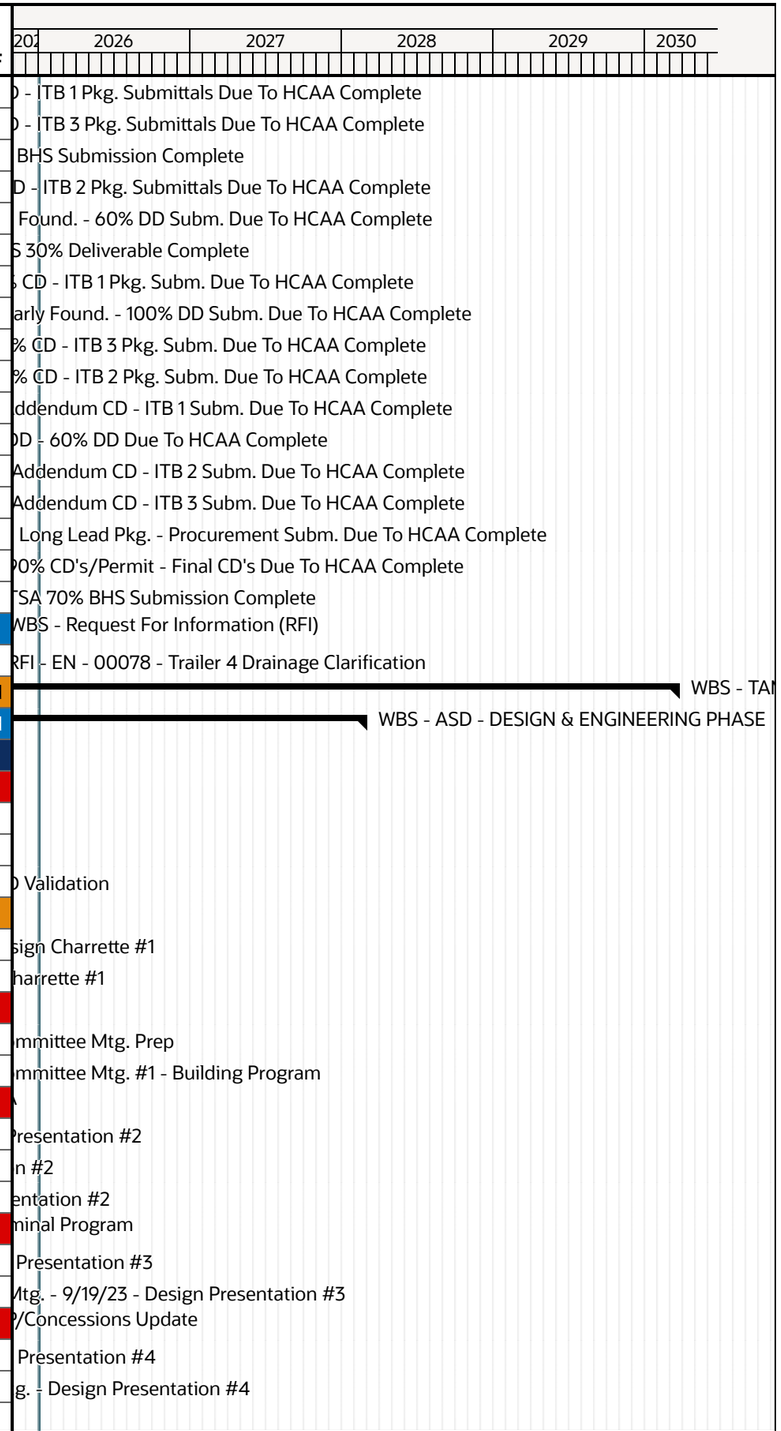


	ID	Name	Dur	Start	Finish	TF
169	WBS - Design Presentation #5 - Aircraft Layout		16.0d	7-Sep-23 A	28-Sep-23 A	
170	DS-PDD-110	Aircraft Diagrams & Layout - Design Presentation #5	15.0d	7-Sep-23 A	27-Sep-23 A	
171	DS-PDD-250	Site Review Mtg. - Design Presentation #5	1.0d	28-Sep-23 A	28-Sep-23 A	
172	WBS - Design Presentation - 9/27/23 Benchmarking		14.0d	8-Sep-23 A	27-Sep-23 A	
173	DS-PDD-120	Benchmarking - Alstom/BHS Coord.	13.0d	8-Sep-23 A	26-Sep-23 A	
174	DS-PDD-230	Mtg. With HCAA - 9/27/23	1.0d	27-Sep-23 A	27-Sep-23 A	
175	WBS - Design Presentation #6 - Aircraft Parking Lot		15.0d	8-Sep-23 A	28-Sep-23 A	
176	DS-PDD-130	Aircraft Layout Coord. - Design Presentation #6	14.0d	8-Sep-23 A	27-Sep-23 A	
177	DS-PDD-260	Mtg. With HCAA - 9/28/23 - Design Presentation #6	1.0d	28-Sep-23 A	28-Sep-23 A	
178	WBS - VDC - BIM		4.0d	22-Sep-23 A	27-Sep-23 A	
179	DS-PDD-220	VDC - BIM Coord.	3.0d	22-Sep-23 A	26-Sep-23 A	
180	DS-PDD-240	BIM Coord. Mtg.	1.0d	27-Sep-23 A	27-Sep-23 A	
181	WBS - Design Presentation #7 - CUP/Resiliency		25.0d	8-Sep-23 A	12-Oct-23 A	
182	DS-PDD-140	White Paper Studies/Preparation - Design Presentation #7	24.0d	8-Sep-23 A	11-Oct-23 A	
183	DS-PDD-320	White Paper/Studies/CUP Presentation Follow Up - Design Presentation #7	1.0d	12-Oct-23 A	12-Oct-23 A	
184	WBS - Design Presentation #8 - Building Form		68.0d	29-Sep-23 A	8-Jan-24 A	
185	DS-PDD-270	Building Forms & Interior Coord. - Design Presentation #8	8.0d	29-Sep-23 A	10-Oct-23 A	
186	DS-PDD-290	Building Forms/Interiors Mtg. - Design Presentation #8	1.0d	11-Oct-23 A	11-Oct-23 A	
187	DS-PDD-570	Building Form Analysis - Design Presentation #8	29.0d	22-Nov-23 A	5-Jan-24 A	
188	DS-PDD-930	Building Form Follow Up Mtg. - Design Presentation #8	1.0d	8-Jan-24 A	8-Jan-24 A	
189	WBS - Design Presentation #9 - Visioning Workshop 10/12/23		10.0d	29-Sep-23 A	12-Oct-23 A	
190	DS-PDD-280	Visioning Prep & Coord. - Design Presentation #9	8.0d	29-Sep-23 A	10-Oct-23 A	
191	DS-PDD-300	Visioning & Programming Workshop - Design Presentation #9	2.0d	11-Oct-23 A	12-Oct-23 A	
192	WBS - APM/MW Study		39.0d	13-Oct-23 A	8-Dec-23 A	
193	DS-PDD-340	APM Vs. Moving Walk Concept	20.0d	13-Oct-23 A	9-Nov-23 A	
194	DS-PDD-490	APM Vs. Moving Walk Analysis	13.0d	10-Nov-23 A	30-Nov-23 A	
195	DS-PDD-610	APM Vs. Moving Walk Review	2.0d	1-Dec-23 A	4-Dec-23 A	
196	DS-PDD-640	APM Vs. Moving Walk Presentation	1.0d	5-Dec-23 A	5-Dec-23 A	
197	DS-PDD-650	APM Vs. Moving Walk Decision (HCAA)	3.0d	6-Dec-23 A	8-Dec-23 A	
198	WBS - BHS - MT Study		76.0d	14-Sep-23 A	3-Jan-24 A	
199	DS-PDD-170	PDD Validation BHS MT Study - Site Visits - Analysis	25.0d	14-Sep-23 A	18-Oct-23 A	
200	DS-PDD-380	BHS MT Site Walk	1.0d	19-Oct-23 A	19-Oct-23 A	
201	DS-PDD-390	BHS MT Documentation Study Completion	2.0d	20-Oct-23 A	23-Oct-23 A	
202	DS-PDD-400	BHS VTC Internal QA/QC	3.0d	24-Oct-23 A	26-Oct-23 A	
203	DS-PDD-420	BHS VTC Finalize Document	1.0d	27-Oct-23 A	27-Oct-23 A	
204	DS-PDD-430	BHS MT Study QA/QC	5.0d	30-Oct-23 A	3-Nov-23 A	
205	DS-PDD-470	BHS MT Study Compilation & Final Document	4.0d	6-Nov-23 A	9-Nov-23 A	
206	DS-PDD-500	BHS Subm. To HCAA	1.0d	10-Nov-23 A	10-Nov-23 A	
207	DS-PDD-510	BHS Review (HCAA)	19.0d	13-Nov-23 A	11-Dec-23 A	
208	DS-PDD-680	BHS Final Presentation (HCAA)	1.0d	12-Dec-23 A	12-Dec-23 A	
209	DS-PDD-720	BHS Owner Review & Determination	13.0d	13-Dec-23 A	2-Jan-24 A	
210	DS-PDD-840	HCAA Determination ON 1/3/24	1.0d	3-Jan-24 A	3-Jan-24 A	

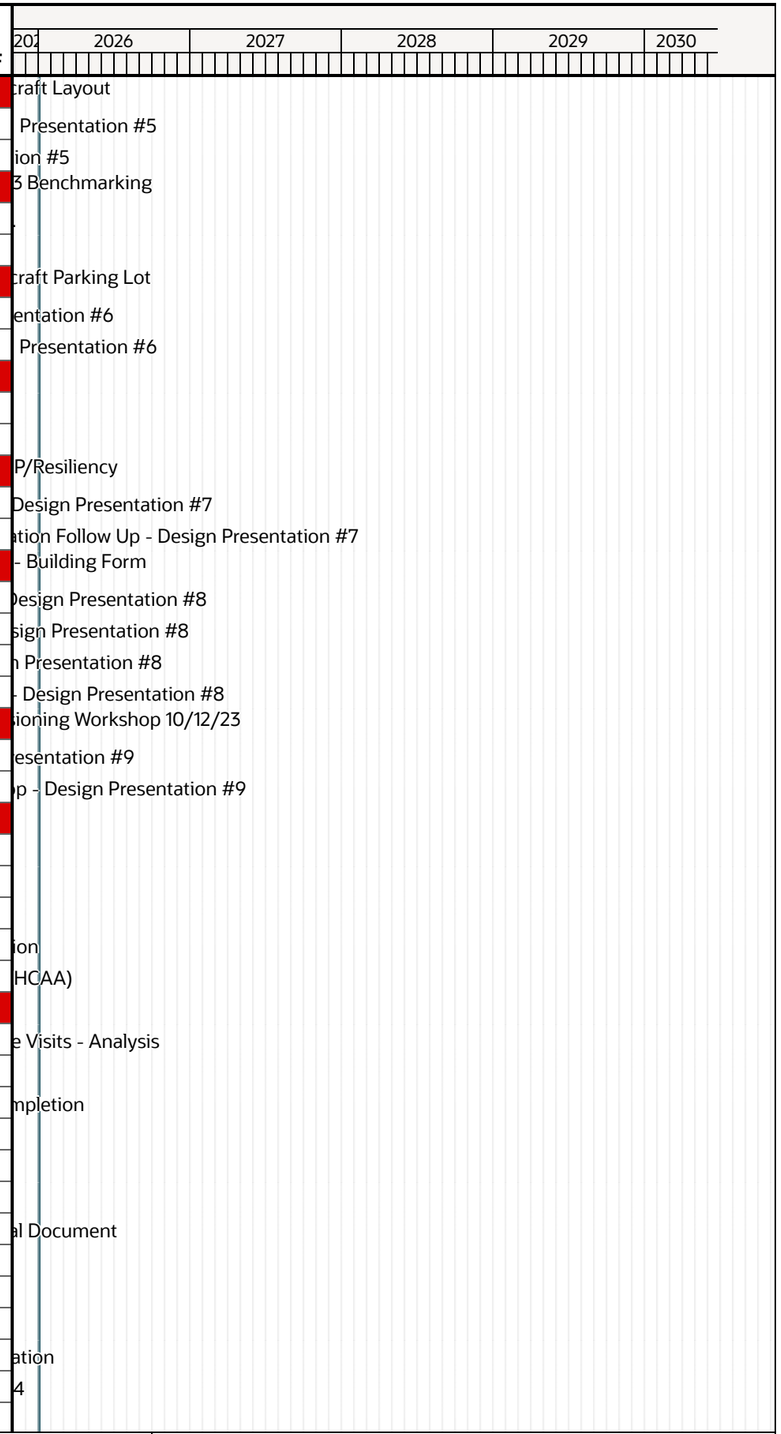


	ID	Name	Dur	Start	Finish	TF
211	WBS - Design Presentation #10 - Aircraft Parking		27.0d	11-Oct-23 A	16-Nov-23 A	
212	DS-PDD-310	Aircraft Parking Development - Design Presentation #10	15.0d	11-Oct-23 A	31-Oct-23 A	
213	DS-PDD-440	Aircraft Parking Exhibit If Northside Development - Design Presentation #10	5.0d	1-Nov-23 A	7-Nov-23 A	
214	DS-PDD-480	Aircraft Parking Presentation - Design Presentation #10	4.0d	8-Nov-23 A	13-Nov-23 A	
215	DS-PDD-520	Aircraft Parking Presentation - Airline Anchor Discussion - Design Presentation ...	1.0d	14-Nov-23 A	14-Nov-23 A	
216	DS-PDD-530	Aircraft Layout 3B Decision Made 11/16/23 - Design Presentation #10	2.0d	15-Nov-23 A	16-Nov-23 A	
217	WBS - Presentations		116.0d	19-Sep-23 A	4-Mar-24 A	
218	WBS - Executive Meeting		3.0d	17-Nov-23 A	21-Nov-23 A	
219	DS-PDD-550	Status Report	2.0d	17-Nov-23 A	20-Nov-23 A	
220	DS-PDD-560	Executive Mtg.	1.0d	21-Nov-23 A	21-Nov-23 A	
221	WBS - Design Presentation Kickoff Meeting - Airline Relocation		21.0d	19-Sep-23 A	17-Oct-23 A	
222	DS-PDD-190	Airline Relocation Coord.	20.0d	19-Sep-23 A	16-Oct-23 A	
223	DS-PDD-360	Airline Relocation Mtg. 10/17/23	1.0d	17-Oct-23 A	17-Oct-23 A	
224	WBS - AHJ Meeting With City Of Tampa		10.0d	12-Oct-23 A	25-Oct-23 A	
225	DS-PDD-330	AHJ Mtg. With City Of Tampa	9.0d	12-Oct-23 A	24-Oct-23 A	
226	DS-PDD-410	AHJ Mtg. - 10/25/23	1.0d	25-Oct-23 A	25-Oct-23 A	
227	WBS - CUP Study/Resiliency		48.0d	13-Oct-23 A	21-Dec-23 A	
228	DS-PDD-350	CUP Study	29.0d	13-Oct-23 A	24-Nov-23 A	
229	DS-PDD-590	CUP Study Review	5.0d	27-Nov-23 A	1-Dec-23 A	
230	DS-PDD-630	CUP Discussion & Questions	6.0d	4-Dec-23 A	11-Dec-23 A	
231	DS-PDD-690	CUP Presentation	1.0d	12-Dec-23 A	12-Dec-23 A	
232	DS-PDD-730	CUP Review & Determination	6.0d	13-Dec-23 A	20-Dec-23 A	
233	DS-PDD-810	CUP Determined (HCAA)	1.0d	21-Dec-23 A	21-Dec-23 A	
234	WBS - Line Of Site		70.0d	22-Nov-23 A	4-Mar-24 A	
235	DS-PDD-580	Siteline/Building Form Analysis	9.0d	22-Nov-23 A	6-Dec-23 A	
236	DS-PDD-660	Siteline/Building Form Overview	3.0d	7-Dec-23 A	11-Dec-23 A	
237	DS-PDD-700	Line Of Site Presentation	1.0d	12-Dec-23 A	12-Dec-23 A	
238	DS-PDD-740	Siteline Pkg. Determination For FAA	10.0d	13-Dec-23 A	27-Dec-23 A	
239	DS-PDD-820	Subm. To FAA	1.0d	27-Dec-23 A	27-Dec-23 A	
240	DS-PDD-830	FAA Review & Determination (45 Day Per FAA)	46.0d	28-Dec-23 A	1-Mar-24 A	
241	DS-PDD-960	Confirmation Of Line Of Site Presentation	1.0d	4-Mar-24 A	4-Mar-24 A	
242	WBS - Apron Grading And Finished Floor Elevations		6.0d	13-Dec-23 A	20-Dec-23 A	
243	DS-PDD-750	Grading & Finish Floor Elevation Analysis	4.0d	13-Dec-23 A	18-Dec-23 A	
244	DS-PDD-780	Grading & Finish Floor Presentation	1.0d	19-Dec-23 A	19-Dec-23 A	
245	DS-PDD-800	Finish Floor Determination	1.0d	20-Dec-23 A	20-Dec-23 A	
246	WBS - PDD Validation Report		181.0d	20-Sep-23 A	4-Jun-24 A	
247	DS-PDD-200	PDD Outline - Template	20.0d	20-Sep-23 A	17-Oct-23 A	
248	DS-PDD-370	PDD Validation Development	11.0d	18-Oct-23 A	1-Nov-23 A	
249	DS-PDD-450	PDD Draft	1.0d	2-Nov-23 A	2-Nov-23 A	
250	DS-PDD-460	PDD Document	8.0d	3-Nov-23 A	14-Nov-23 A	
251	DS-PDD-540	PDD Discipline Check/Sr. Technical Review	9.0d	15-Nov-23 A	29-Nov-23 A	
252	DS-PDD-600	PDD - Post Docs. To Bluebeam	1.0d	30-Nov-23 A	30-Nov-23 A	

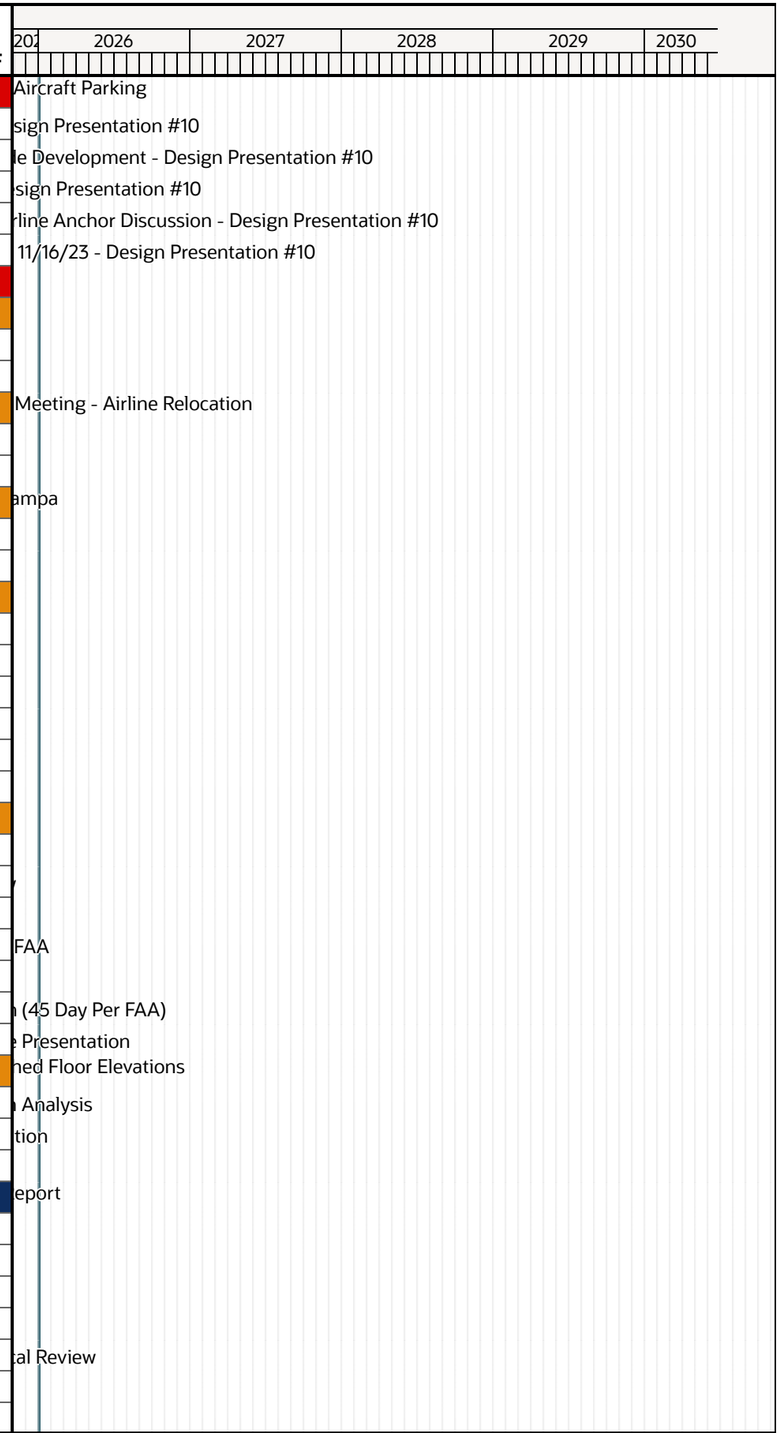


	ID	Name	Dur	Start	Finish	TF
253	DS-PDD-620	PDD - QA/QC	5.0d	1-Dec-23 A	7-Dec-23 A	
254	DS-PDD-670	PDD Docs. Complete	2.0d	8-Dec-23 A	11-Dec-23 A	
255	DS-PDD-710	Table Top Review	1.0d	12-Dec-23 A	12-Dec-23 A	
256	DS-PDD-760	Submit PDD Validation Report To HCAA	1.0d	13-Dec-23 A	13-Dec-23 A	
257	DS-PDD-770	PDD Validation HCAA Review	3.0d	14-Dec-23 A	18-Dec-23 A	
258	DS-PDD-790	PDD Validation With HCAA	1.0d	19-Dec-23 A	19-Dec-23 A	
259	WBS - Airline Anchor Tenant Designation		109.0d	4-Jan-24 A	4-Jun-24 A	
260	DS-PDD-850	Anchor Airline Tenant Determination	108.0d	4-Jan-24 A	4-Jun-24 A	
261	DS-PDD-860	Fleet Mix Design Confirmation	21.0d	5-Jan-24 A	2-Feb-24 A	
262	DS-PDD-870	Hold Room Design	21.0d	5-Jan-24 A	2-Feb-24 A	
263	DS-PDD-880	Gate Design	21.0d	5-Jan-24 A	2-Feb-24 A	
264	DS-PDD-890	Technology	21.0d	5-Jan-24 A	2-Feb-24 A	
265	DS-PDD-900	Operations/Administration Design	21.0d	5-Jan-24 A	2-Feb-24 A	
266	DS-PDD-910	FIS Design	21.0d	5-Jan-24 A	2-Feb-24 A	
267	DS-PDD-920	Airline Club Design	21.0d	5-Jan-24 A	2-Feb-24 A	
268	DS-PDD-940	Review Requirements For Airline Prior To BOD	10.0d	5-Feb-24 A	16-Feb-24 A	
269	DS-PDD-950	Docs. Airline Requirements For BOD	2.0d	19-Feb-24 A	20-Feb-24 A	
270	WBS - ASD - BOD		86.0d	3-Jan-24 A	1-May-24 A	
271	WBS - ASD - BOD Program Development		30.0d	3-Jan-24 A	13-Feb-24 A	
272	DS-BOD-10	Program SF Development & Prep	4.0d	3-Jan-24 A	8-Jan-24 A	
273	DS-BOD-20	Program SF Mtg. with HCAA Executives & Ricondo	1.0d	9-Jan-24 A	9-Jan-24 A	
274	DS-BOD-30	Program SF Workshop Development	3.0d	10-Jan-24 A	12-Jan-24 A	
275	DS-BOD-40	Program SF Workshop With HCAA - 1/16/24	1.0d	16-Jan-24 A	16-Jan-24 A	
276	DS-BOD-50	Program SF Analysis/Review/Presentation Prep	19.0d	17-Jan-24 A	12-Feb-24 A	
277	DS-BOD-60	Program SF Confirmation/Presentation - 2/13/24	1.0d	13-Feb-24 A	13-Feb-24 A	
278	WBS - ASD - BOD Documents		44.0d	14-Feb-24 A	15-Apr-24 A	
279	DS-BOD-70	Refine SF & Development Terminal BOD Plans	19.0d	14-Feb-24 A	11-Mar-24 A	
280	DS-BOD-80	Truck Loading Dock Layout & CUP Coord. - 2/20/24	5.0d	14-Feb-24 A	20-Feb-24 A	
281	DS-BOD-90	Conceptual Interior Design Development	19.0d	15-Feb-24 A	12-Mar-24 A	
282	DS-BOD-100	Finalize Floor Plan Adjacencies	6.0d	19-Feb-24 A	26-Feb-24 A	
283	DS-BOD-110	Finalize Gate Tower Locations	6.0d	19-Feb-24 A	26-Feb-24 A	
284	DS-BOD-120	Building Form Development	6.0d	19-Feb-24 A	26-Feb-24 A	
285	DS-BOD-130	Loading Dock Coord. Development	24.0d	21-Feb-24 A	25-Mar-24 A	
286	DS-BOD-140	Building Form Coord. Mtg. - 2/27/24	1.0d	27-Feb-24 A	27-Feb-24 A	
287	DS-BOD-150	Preliminary Hold Room Design Development	14.0d	27-Feb-24 A	15-Mar-24 A	
288	DS-BOD-160	BOD Target Program Accepted (BHS-Transfer Bus Hold Room)	1.0d	28-Feb-24 A	28-Feb-24 A	
289	DS-BOD-170	Struct. Grid & Floor To Floor Heights	9.0d	29-Feb-24 A	12-Mar-24 A	
290	DS-BOD-180	Final PDD & BOD Program Docs.	24.0d	29-Feb-24 A	2-Apr-24 A	
291	DS-BOD-190	FAA Approval Of Line Of Site	10.0d	13-Mar-24 A	26-Mar-24 A	
292	DS-BOD-200	Conceptual Interior Design Mtg. - 3/12/24	18.0d	13-Mar-24 A	5-Apr-24 A	
293	DS-BOD-210	Preliminary Hold Room Design Mtg. - 3/19/24	1.0d	19-Mar-24 A	19-Mar-24 A	
294	DS-BOD-220	Submit Draft Design To HP For Cost Estimating	1.0d	19-Mar-24 A	19-Mar-24 A	

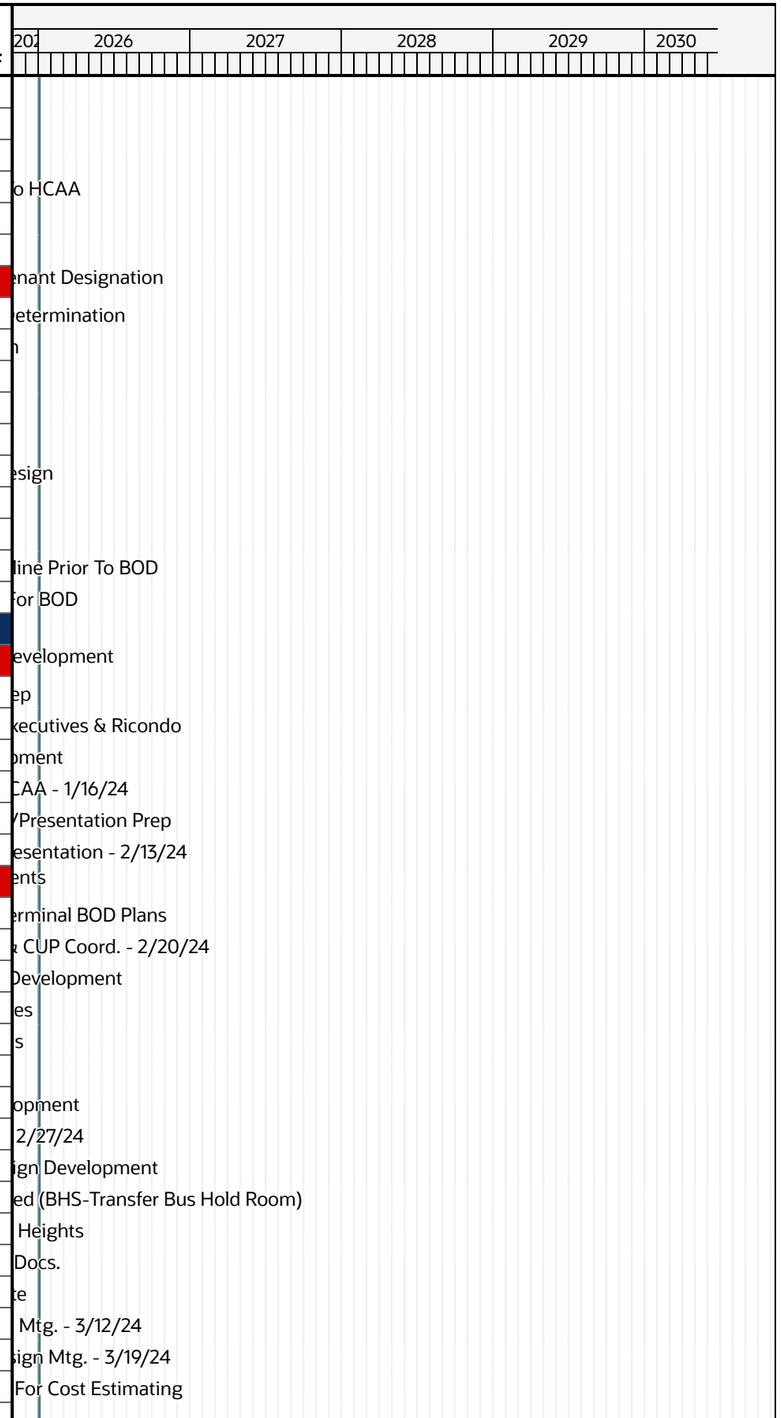


	ID	Name	Dur	Start	Finish	TF
295	DS-BOD-230	Preliminary Cost Estimate Pkg. To HP	20.0d	19-Mar-24 A	15-Apr-24 A	
296	DS-BOD-240	Loading Dock Bessie Coleman Coord. Mtg. - 3/26/24	1.0d	26-Mar-24 A	26-Mar-24 A	
297	WBS - ASD - BOD Review QA/QC		11.0d	3-Apr-24 A	17-Apr-24 A	
298	DS-BOD-250	BOD Review - QA/QC DQC - Post Docs.	1.0d	3-Apr-24 A	3-Apr-24 A	
299	DS-BOD-260	BOD Review - QA/QC - DQC	3.0d	3-Apr-24 A	5-Apr-24 A	
300	DS-BOD-270	Sr. Technical Review Discipline QC	3.0d	3-Apr-24 A	5-Apr-24 A	
301	DS-BOD-280	Post Docs. to Bluebeam IDR Review	1.0d	8-Apr-24 A	8-Apr-24 A	
302	DS-BOD-290	BOD/Validation QA/QC - IDR	5.0d	8-Apr-24 A	12-Apr-24 A	
303	DS-BOD-300	Docs. Complete - Visual Check	2.0d	15-Apr-24 A	16-Apr-24 A	
304	DS-BOD-310	QAR Check	1.0d	17-Apr-24 A	17-Apr-24 A	
305	WBS - ASD - BOD Submittal To HCAA		10.0d	18-Apr-24 A	1-May-24 A	
306	DS-BOD-320	Submit BOD Report Due To HCAA	1.0d	18-Apr-24 A	18-Apr-24 A	
307	DS-BOD-330	ASD - BOD Subm. - HCAA Review	9.0d	19-Apr-24 A	1-May-24 A	
308	WBS - Budget Reconciliation		90.0d	23-Apr-24 A	27-Aug-24 A	
309	DS-BR-10	HCAA Hold On Airside D 30% Progress	1.0d	23-Apr-24 A	23-Apr-24 A	
310	DS-BR-20	Cost Reduction Effort	23.0d	24-Apr-24 A	24-May-24 A	
311	DS-BR-30	Update Plans - Building Stacking	4.0d	28-May-24 A	31-May-24 A	
312	DS-BR-40	HP Cost Estimating	9.0d	3-Jun-24 A	14-Jun-24 A	
313	DS-BR-50	HCAA Administration Mtg. - NTP 6/10/24	1.0d	10-Jun-24 A	10-Jun-24 A	
314	DS-BR-60	Executive Team Decision Day	23.0d	11-Jun-24 A	15-Jul-24 A	
315	WBS - Revised BOD		14.0d	11-Jun-24 A	28-Jun-24 A	
316	DS-BR-RBOD-10	Develop Concept Plans (3 Massing/Form Options)	10.0d	11-Jun-24 A	24-Jun-24 A	
317	DS-BR-RBOD-20	FIS Study & Concept Options	10.0d	11-Jun-24 A	24-Jun-24 A	
318	DS-BR-RBOD-30	Concept Plan Presentation	1.0d	25-Jun-24 A	25-Jun-24 A	
319	DS-BR-RBOD-40	Respond To FIS Comments	3.0d	25-Jun-24 A	27-Jun-24 A	
320	DS-BR-RBOD-50	Respond To Presentation Comments	2.0d	26-Jun-24 A	27-Jun-24 A	
321	DS-BR-RBOD-60	Executive Mtg. - Decision On The Massing Options	1.0d	28-Jun-24 A	28-Jun-24 A	
322	DS-BR-RBOD-70	Executive Mtg. - FIS Direction	1.0d	28-Jun-24 A	28-Jun-24 A	
323	WBS - Program SF Development		16.0d	1-Jul-24 A	23-Jul-24 A	
324	DS-BR-70	Revise Program SF Analysis	5.0d	1-Jul-24 A	8-Jul-24 A	
325	DS-BR-110	Program SF Mtg.	1.0d	9-Jul-24 A	9-Jul-24 A	
326	DS-BR-120	Update Program SF Development Plan	9.0d	10-Jul-24 A	22-Jul-24 A	
327	DS-BR-160	Program Area Confirmation Mtg.	1.0d	23-Jul-24 A	23-Jul-24 A	
328	WBS - MEP/Truck Court Coordination		16.0d	1-Jul-24 A	23-Jul-24 A	
329	DS-BR-80	MEP Revision	15.0d	1-Jul-24 A	22-Jul-24 A	
330	DS-BR-90	Develop Truck Court Layout	15.0d	1-Jul-24 A	22-Jul-24 A	
331	DS-BR-150	Truck Court/MEP Mtg. - GDWY Alignment	1.0d	23-Jul-24 A	23-Jul-24 A	
332	WBS - Apron Level Development		13.0d	1-Jul-24 A	18-Jul-24 A	
333	DS-BR-100	Apron Lvl. Development With New Scheme	12.0d	1-Jul-24 A	17-Jul-24 A	
334	DS-BR-140	Apron Lvl. Civil Focus Team/Mtg.	1.0d	18-Jul-24 A	18-Jul-24 A	
335	WBS - Finalize BOD		2.0d	24-Jul-24 A	25-Jul-24 A	
336	DS-BR-170	Finalize BOD Docs.	1.0d	24-Jul-24 A	24-Jul-24 A	

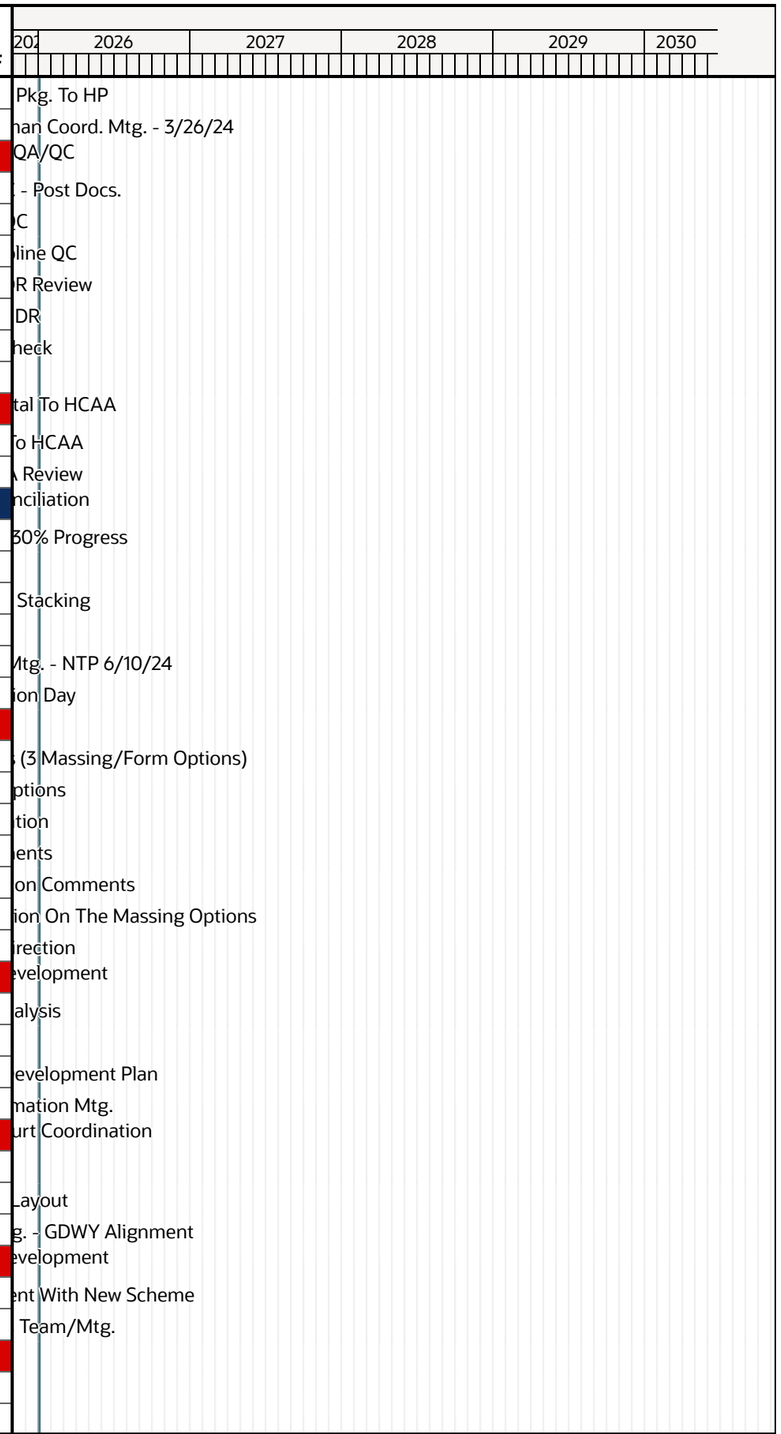


	ID	Name	Dur	Start	Finish	TF
337	DS-BR-180	BOD Docs. Ready For QA/QC	1.0d	24-Jul-24 A	24-Jul-24 A	
338	DS-BR-200	BOD - CBP Mtg. Workshop	1.0d	25-Jul-24 A	25-Jul-24 A	
339	WBS - Revised BOD Review QA/QC		22.0d	12-Jul-24 A	12-Aug-24 A	
340	DS-BR-130	Docs. To HP For Pricing	22.0d	12-Jul-24 A	12-Aug-24 A	
341	DS-BR-190	BOD Review - DQC - Post Docs.	1.0d	25-Jul-24 A	25-Jul-24 A	
342	DS-BR-210	BOD Review - DQC	3.0d	26-Jul-24 A	30-Jul-24 A	
343	DS-BR-220	BOD Review - Sr. Technical Review Discipline QC	3.0d	26-Jul-24 A	30-Jul-24 A	
344	DS-BR-230	BOD Review - Post Docs. To Bluebeam IDR Review	1.0d	31-Jul-24 A	31-Jul-24 A	
345	DS-BR-240	BOD QA/QC - IDR	5.0d	1-Aug-24 A	7-Aug-24 A	
346	DS-BR-250	BOD Review - Docs. Complete - Visual Check	2.0d	8-Aug-24 A	9-Aug-24 A	
347	DS-BR-260	BOD Review - QAR Check	1.0d	12-Aug-24 A	12-Aug-24 A	
348	WBS - ASD - Revised BOD Submittal To HCAA		11.0d	13-Aug-24 A	27-Aug-24 A	
349	DS-BR-270	Submit Revised BOD Report Due To HCAA	1.0d	13-Aug-24 A	13-Aug-24 A	
350	DS-BR-280	ASD - BOD - HCAA Review	10.0d	14-Aug-24 A	27-Aug-24 A	
351	WBS - Main Terminal Ticket Counter Relocation		279.0d	19-Apr-24 A	22-May-25 A	
352	WBS - MT - Ticketing Counter Relocation - Evaluation		55.0d	19-Apr-24 A	5-Jul-24 A	
353	DS-MT-10	HCAA Ticket Counter Relo. Coord. With Ricondo - Ticket Counter Relo.	14.0d	19-Apr-24 A	8-May-24 A	
354	DS-MT-20	Kick Off Mtg. With HCAA - Ricondo Presentation - Ticket Counter Relo.	1.0d	9-May-24 A	9-May-24 A	
355	DS-MT-30	Develop Initial List Of Questions & Review Program - Ticket Counter Relo.	13.0d	10-May-24 A	29-May-24 A	
356	DS-MT-40	Site Walk - Ticket Counter Relo.	1.0d	30-May-24 A	30-May-24 A	
357	DS-MT-50	Evaluate Ricondo Program - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
358	DS-MT-60	Develop Ticket Counter Matrix - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
359	DS-MT-70	Develop Plans Identifying Relocation Of Ticket Counters - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
360	DS-MT-80	Submit Draft Plans & Matrix for Review (Including HP) - Ticket Counter Relo.	1.0d	13-Jun-24 A	13-Jun-24 A	
361	DS-MT-90	Develop Presentation Of Evaluation Of Program/Scope To HCAA - Ticket Count…	4.0d	14-Jun-24 A	19-Jun-24 A	
362	DS-MT-100	Presentation To HCAA - Ticket Counter Relo.	1.0d	20-Jun-24 A	20-Jun-24 A	
363	DS-MT-110	HCAA Review & Comment - Ticket Counter Relo.	10.0d	21-Jun-24 A	5-Jul-24 A	
364	WBS - MT - Ticketing Counter Relocation - Concept Design/Stakeholder Engagement		52.0d	21-Jun-24 A	4-Sep-24 A	
365	DS-MT-120	Incorporate Comments from HCAA - Ticket Counter Relo. - Concept Design	10.0d	21-Jun-24 A	5-Jul-24 A	
366	DS-MT-130	Confirmation of Proprietary Use Component for Each Airline - Ticket Counter R…	5.0d	8-Jul-24 A	12-Jul-24 A	
367	DS-MT-140	Airline Stakeholder Mtg.s/Questionnaires - Ticket Counter Relo. - Concept Design	20.0d	15-Jul-24 A	9-Aug-24 A	
368	DS-MT-150	Provide Update to HCAA - Airline Matrix - Ticket Counter Relo. - Concept Design	17.0d	12-Aug-24 A	4-Sep-24 A	
369	DS-MT-160	Confirmation of BHS System Determination (East End Sortation) - Ticket Count…	1.0d	19-Aug-24 A	19-Aug-24 A	
370	WBS - MT - Ticketing Counter Relocation - Focus Team Meeting		24.0d	5-Sep-24 A	8-Oct-24 A	
371	DS-MT-170	Mtg. With HCAA Regarding Ticket Counter/Airline Relocation - Ticket Counter R…	1.0d	5-Sep-24 A	5-Sep-24 A	
372	DS-MT-180	BHS Coord. - Ticket Counter Relo.	8.0d	6-Sep-24 A	17-Sep-24 A	
373	DS-MT-190	Develop Phasing Plan/Matrix for Each Ticket Counter Relo.	8.0d	6-Sep-24 A	17-Sep-24 A	
374	DS-MT-200	Submit Matrix & Questions To HCAA. - Ticket Counter Relo.	1.0d	18-Sep-24 A	18-Sep-24 A	
375	DS-MT-210	Update Plans. - Ticket Counter Relo.	4.0d	19-Sep-24 A	24-Sep-24 A	
376	DS-MT-220	Mtg. With HCAA (Tony O'Brian). - Ticket Counter Relo.	1.0d	25-Sep-24 A	25-Sep-24 A	
377	DS-MT-230	Update Docs. Based on Communication From HCAA. - Ticket Counter Relo.	7.0d	26-Sep-24 A	4-Oct-24 A	
378	DS-MT-240	Mtg. With HP/Gensler/HNTB. - Ticket Counter Relo.	1.0d	7-Oct-24 A	7-Oct-24 A	

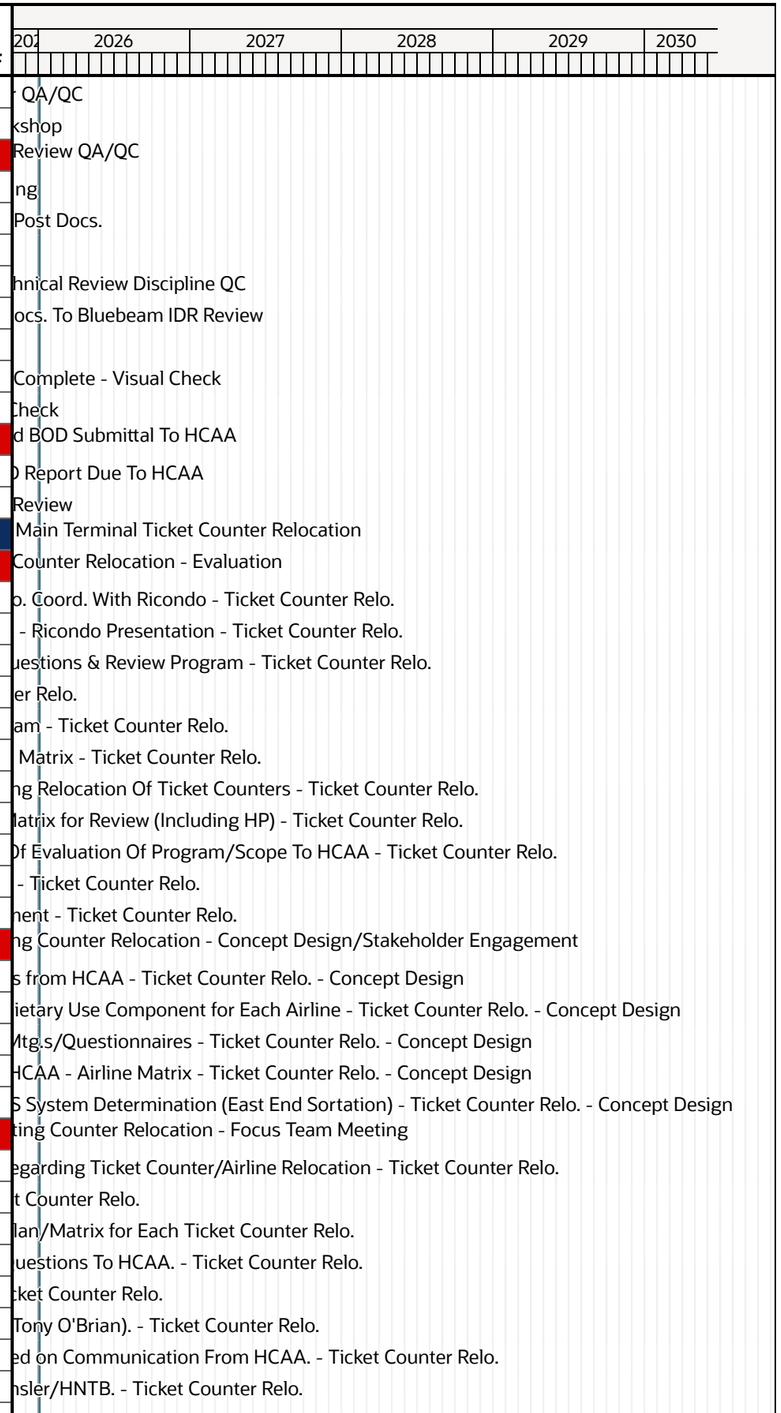

	ID	Name	Dur	Start	Finish	TF
379	DS-MT-250	Airside D Support Spaces Presentation. - Ticket Counter Relo.	1.0d	8-Oct-24 A	8-Oct-24 A	
380	WBS - MT - Ticketing Counter Relocation - SD - 30%		50.0d	26-Sep-24 A	6-Dec-24 A	
381	WBS - MT - Ticketing Counter Relocation - SD - 30% Docs		41.0d	26-Sep-24 A	21-Nov-24 A	
382	DS-MT-SD-10	SD - 30% - MT Ticket Counter Relo. SD	7.0d	26-Sep-24 A	4-Oct-24 A	
383	DS-MT-SD-20	SD 30% Hurricane Milton Impact (10/7-10/11) - MT Ticket Counter Relo. SD	5.0d	7-Oct-24 A	11-Oct-24 A	
384	DS-MT-SD-30	30% Architecture Docs. Complete - MT Ticket Counter Relo. SD	10.0d	14-Oct-24 A	25-Oct-24 A	
385	DS-MT-SD-40	30% Cost Estimating Pkg. - MT Ticket Counter Relo. SD	22.0d	23-Oct-24 A	21-Nov-24 A	
386	WBS - MT - Ticketing Counter Relocation - SD - 30% QA/QC		17.0d	28-Oct-24 A	19-Nov-24 A	
387	DS-MT-SD-50	30% DQC - MT Ticket Counter Relo. SD	5.0d	28-Oct-24 A	1-Nov-24 A	
388	DS-MT-SD-60	30% Sr. Technical Review - MT Ticket Counter Relo. SD	5.0d	28-Oct-24 A	1-Nov-24 A	
389	DS-MT-SD-70	30% Post to Bluebeam Session - MT Ticket Counter Relo. SD	1.0d	4-Nov-24 A	4-Nov-24 A	
390	DS-MT-SD-80	30% IDR - MT Ticket Counter Relo. SD	7.0d	5-Nov-24 A	13-Nov-24 A	
391	DS-MT-SD-90	30% Visual Check - MT Ticket Counter Relo. SD	2.0d	14-Nov-24 A	15-Nov-24 A	
392	DS-MT-SD-100	30% QA Check - MT Ticket Counter Relo. SD	2.0d	18-Nov-24 A	19-Nov-24 A	
393	WBS - MT - Ticketing Counter Relocation - SD - 30% Submittal To HCAA		11.0d	20-Nov-24 A	6-Dec-24 A	
394	DS-MT-SD-110	30% Complete Docs. & Assemble Pkg. - MT Ticket Counter Relo. SD	1.0d	20-Nov-24 A	20-Nov-24 A	
395	DS-MT-SD-120	30% Subm. To HCAA - MT Ticket Counter Relo. SD	1.0d	21-Nov-24 A	21-Nov-24 A	
396	DS-MT-SD-130	30% HCAA Review - MT Ticket Counter Relo. SD	9.0d	22-Nov-24 A	6-Dec-24 A	
397	WBS - MT - Ticketing Counter Relocation - DD - 60%		126.0d	22-Nov-24 A	22-May-25 A	
398	WBS - MT - Ticketing Counter Relocation - DD - 60% Docs		95.0d	22-Nov-24 A	9-Apr-25 A	
399	DS-MT-DD-10	60% Docs - MT Ticket Counter Relo. DD	95.0d	22-Nov-24 A	9-Apr-25 A	
400	WBS - MT - Ticketing Counter Relocation - DD - 60% QA/QC		19.0d	10-Apr-25 A	6-May-25 A	
401	DS-MT-DD-20	60% - Cost Estimating Pkg. - MT Ticket Counter Relo. - DD	19.0d	10-Apr-25 A	6-May-25 A	
402	DS-MT-DD-30	60% - DQC - MT Ticket Counter Relo. - DD	3.0d	10-Apr-25 A	14-Apr-25 A	
403	DS-MT-DD-40	60% - Post to Bluebeam Session - MT Ticket Counter Relo. - DD	1.0d	15-Apr-25 A	15-Apr-25 A	
404	DS-MT-DD-50	60% - IDR - MT Ticket Counter Relo. - DD	12.0d	16-Apr-25 A	1-May-25 A	
405	DS-MT-DD-60	60% - Visual Check - MT Ticket Counter Relo. - DD	2.0d	2-May-25 A	5-May-25 A	
406	DS-MT-DD-70	60% - QA Check - MT Ticket Counter Relo. - DD	1.0d	6-May-25 A	6-May-25 A	
407	WBS - MT - Ticketing Counter Relocation - DD - 60% Submittal To HCAA		12.0d	7-May-25 A	22-May-25 A	
408	DS-MT-DD-80	60% - Complete Docs. & Assemble Pkg. - MT Ticket Counter Relo. - DD	1.0d	7-May-25 A	7-May-25 A	
409	DS-MT-DD-90	60% - Subm. To HCAA - MT Ticket Counter Relo. - DD	1.0d	8-May-25 A	8-May-25 A	
410	DS-MT-DD-100	60% - HCAA Review - MT Ticket Counter Relo. - DD	10.0d	9-May-25 A	22-May-25 A	
411	WBS - Enabling Package		215.0d	5-Jan-24 A	4-Nov-24 A	
412	WBS - Enabling Package/Apron Demo 60% (Footprint +50')		89.0d	5-Jan-24 A	8-May-24 A	
413	DS-EN-10	Gate Layout - Building Outline (4 Gate - Late Opening) - Enabling Pkg/Apron D...	30.0d	5-Jan-24 A	15-Feb-24 A	
414	DS-EN-20	North Site Development & Coord. - Enabling Pkg/Apron Demo 60%	30.0d	5-Jan-24 A	15-Feb-24 A	
415	DS-EN-30	Submit Fee Proposal for Review & Approval - Enabling Pkg/Apron Demo 60%	22.0d	16-Feb-24 A	18-Mar-24 A	
416	DS-EN-40	SWFWMD Mtg. Prep - 3/27/24 - Enabling Pkg/Apron Demo 60%	29.0d	16-Feb-24 A	27-Mar-24 A	
417	DS-EN-50	Civil Docs. - Enabling Pkg/Apron Demo 60%	20.0d	27-Feb-24 A	25-Mar-24 A	
418	DS-EN-60	Define Civil Apron Limits - Enabling Pkg/Apron Demo 60%	30.0d	27-Feb-24 A	8-Apr-24 A	
419	DS-EN-70	Building Outline/Footprint - Enabling Pkg/Apron Demo 60%	15.0d	27-Feb-24 A	18-Mar-24 A	
420	DS-EN-80	Apron Demo 60% NTP - Enabling Pkg/Apron Demo 60%	1.0d	19-Mar-24 A	19-Mar-24 A	

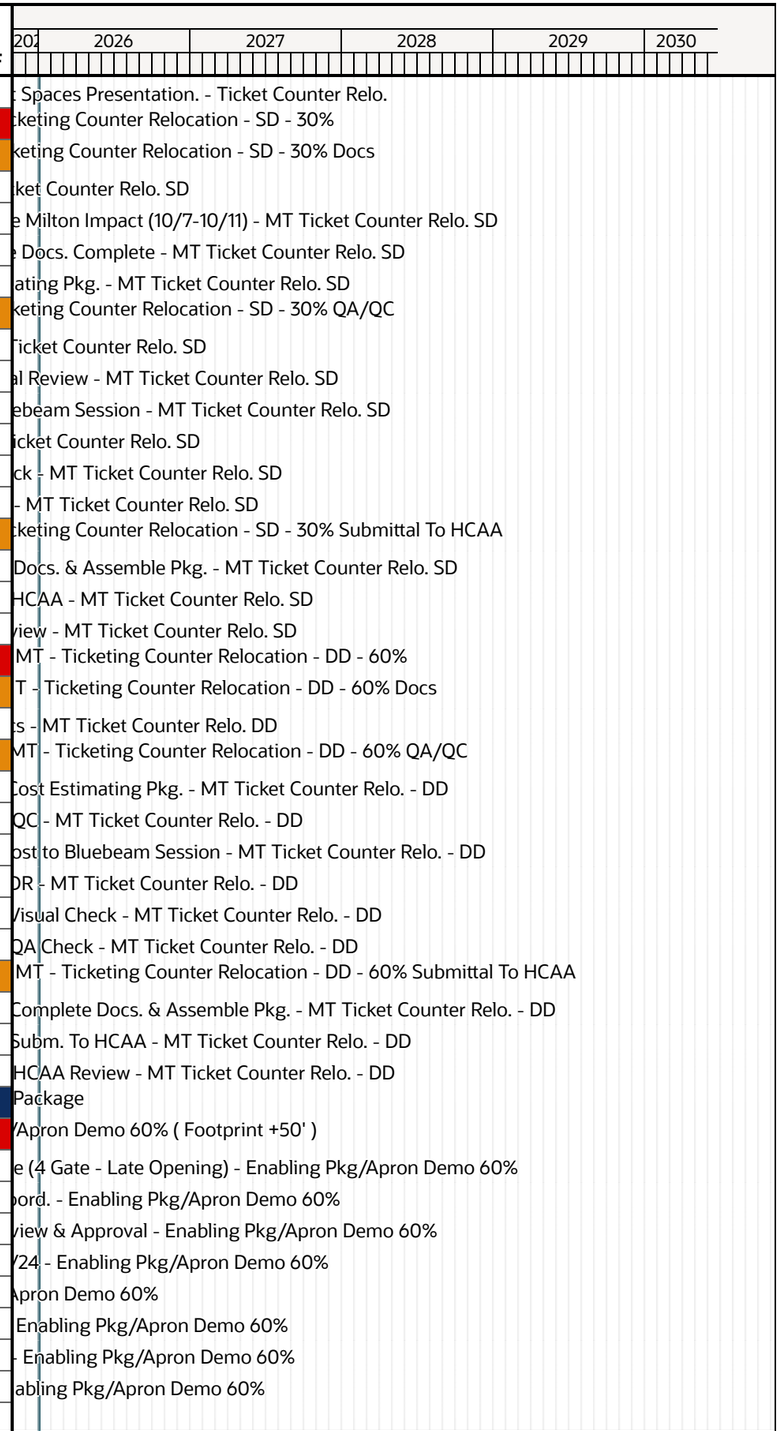


	ID	Name	Dur	Start	Finish	TF
421	DS-EN-90	Develop Struct. Grid - Enabling Pkg/Apron Demo 60%	16.0d	19-Mar-24 A	9-Apr-24 A	
422	DS-EN-100	Survey - Geotech - Site Investigation - Enabling Pkg/Apron Demo 60%	20.0d	20-Mar-24 A	16-Apr-24 A	
423	DS-EN-110	Utility Coord. - Enabling Pkg/Apron Demo 60%	22.0d	20-Mar-24 A	18-Apr-24 A	
424	DS-EN-120	North Site Drainage Design - Enabling Pkg/Apron Demo 60%	25.0d	20-Mar-24 A	23-Apr-24 A	
425	DS-EN-130	North Site Utility & Paving Plans - Enabling Pkg/Apron Demo 60%	25.0d	20-Mar-24 A	23-Apr-24 A	
426	DS-EN-140	North Site Trailer Layout & Design - Enabling Pkg/Apron Demo 60%	20.0d	20-Mar-24 A	16-Apr-24 A	
427	DS-EN-150	SWFWMD Mtg. - 3/28/24 - Enabling Pkg/Apron Demo 60%	1.0d	28-Mar-24 A	28-Mar-24 A	
428	DS-EN-160	Finalize Civil Demo Docs. - Enabling Pkg/Apron Demo 60%	5.0d	9-Apr-24 A	15-Apr-24 A	
429	DS-EN-170	Civil Docs. - Apron D Site - Enabling Pkg/Apron Demo 60%	16.0d	9-Apr-24 A	30-Apr-24 A	
430	DS-EN-180	Identify Pilot Hole Locations - Enabling Pkg/Apron Demo 60%	10.0d	10-Apr-24 A	23-Apr-24 A	
431	DS-EN-190	Submit Survey Information to The Design Team - Enabling Pkg/Apron Demo 60%	5.0d	17-Apr-24 A	23-Apr-24 A	
432	DS-EN-200	Finalize Architectural Docs. - Enabling Pkg/Apron Demo 60%	10.0d	17-Apr-24 A	30-Apr-24 A	
433	DS-EN-210	Finalize Struct. Docs. - Enabling Pkg/Apron Demo 60%	5.0d	24-Apr-24 A	30-Apr-24 A	
434	DS-EN-220	Finalize Civil Docs. - North Site - Enabling Pkg/Apron Demo 60%	5.0d	24-Apr-24 A	30-Apr-24 A	
435	WBS - APN - Enabling Package 60% Submittal		6.0d	1-May-24 A	8-May-24 A	
436	DS-EN-230	Enabling Pkg. 60% Document - QA/QC	5.0d	1-May-24 A	7-May-24 A	
437	DS-EN-240	Enabling Pkg. 60% Draft HCAA Review	1.0d	8-May-24 A	8-May-24 A	
438	WBS - APN - Enabling Package 100% Submittal		49.0d	9-May-24 A	17-Jul-24 A	
439	DS-EN-250	Incorporate Comments from HCAA Review into Document - APN Enabling Pckg...	12.0d	9-May-24 A	24-May-24 A	
440	DS-EN-260	APN Enabling Pckg. 100% - HCAA Review & Comments - APN Enabling Pckg. 1...	17.0d	9-May-24 A	3-Jun-24 A	
441	DS-EN-270	HCAA Comments Received 6/4/24 - APN Enabling Pckg. 100%	1.0d	4-Jun-24 A	4-Jun-24 A	
442	DS-EN-280	Comment Resolution Subm. - APN Enabling Pckg. 100%	9.0d	5-Jun-24 A	17-Jun-24 A	
443	DS-EN-290	Incorporate HCAA Comments - APN Enabling Pckg. 100%	10.0d	5-Jun-24 A	18-Jun-24 A	
444	DS-EN-300	Incorporate New Building Footprint into Enabling Pkg. - APN Enabling Pckg. 10...	6.0d	11-Jun-24 A	18-Jun-24 A	
445	DS-EN-310	Civil Design Subm. - APN Enabling Pckg. 100%	20.0d	19-Jun-24 A	17-Jul-24 A	
446	DS-EN-320	Architectural Design Subm. - APN Enabling Pckg. 100%	20.0d	19-Jun-24 A	17-Jul-24 A	
447	WBS - APN - Enabling Package 100% Review QA/QC		21.0d	12-Jul-24 A	9-Aug-24 A	
448	DS-EN-330	Submit Draft Design To HP For Cost Estimating Review - APN Enabling Pckg. 1...	1.0d	12-Jul-24 A	12-Jul-24 A	
449	DS-EN-340	DQC Review - APN Enabling Pckg. 100%	5.0d	18-Jul-24 A	24-Jul-24 A	
450	DS-EN-350	Enabling Pkg. Sr. Technical Review - APN Enabling Pckg. 100%	5.0d	18-Jul-24 A	24-Jul-24 A	
451	DS-EN-360	Submit Document to Bluebeam - APN Enabling Pckg. 100%	1.0d	25-Jul-24 A	25-Jul-24 A	
452	DS-EN-370	IDR - APN Enabling Pckg. 100%	7.0d	26-Jul-24 A	5-Aug-24 A	
453	DS-EN-380	Docs. Complete Visual Check - APN Enabling Pckg. 100%	2.0d	6-Aug-24 A	7-Aug-24 A	
454	DS-EN-390	QA Review - APN Enabling Pckg. 100%	2.0d	8-Aug-24 A	9-Aug-24 A	
455	WBS - APN - Enabling Package Submittal To HCAA		12.0d	12-Aug-24 A	27-Aug-24 A	
456	DS-EN-400	Complete Docs. & Assemble Pkg. - APN Enabling Pckg. 100%	1.0d	12-Aug-24 A	12-Aug-24 A	
457	DS-EN-410	Submit Enabling/Demo Pkg. To HCAA - APN Enabling Pckg. 100%	1.0d	13-Aug-24 A	13-Aug-24 A	
458	DS-EN-420	Submit to City Of Tampa & HCAA Review - APN Enabling Pckg. 100%	10.0d	14-Aug-24 A	27-Aug-24 A	
459	WBS - APN - Enabling Permit And Comment Resolution		58.0d	14-Aug-24 A	4-Nov-24 A	
460	DS-EN-430	Bidding RFI's - APN - Enabling Permit & Comment Resol.	20.0d	14-Aug-24 A	11-Sep-24 A	
461	DS-EN-440	HCAA Comments Received - APN - Enabling Permit & Comment Resol.	5.0d	28-Aug-24 A	4-Sep-24 A	
462	DS-EN-450	Comment Resolution Subm. - APN - Enabling Permit & Comment Resol.	14.0d	5-Sep-24 A	24-Sep-24 A	




	ID	Name	Dur	Start	Finish	TF
463	DS-EN-460	Contractor Bid Date - APN - Enabling Permit & Comment Resol.	1.0d	12-Sep-24 A	12-Sep-24 A	
464	DS-EN-470	HCAA Comment Resolution Mtg. #1 - APN - Enabling Permit & Comment Resol.	1.0d	25-Sep-24 A	25-Sep-24 A	
465	DS-EN-480	Follow Up Comment Resolution Clarification - APN - Enabling Permit & Comme...	16.0d	26-Sep-24 A	17-Oct-24 A	
466	DS-EN-490	Submit to COT Building Department - APN - Enabling Permit & Comment Resol.	1.0d	2-Oct-24 A	2-Oct-24 A	
467	DS-EN-500	COT Building Department Comments Received - APN - Enabling Permit & Com...	12.0d	3-Oct-24 A	18-Oct-24 A	
468	DS-EN-510	HCAA Comment Resolution Mtg. #2 - APN - Enabling Permit & Comment Resol.	1.0d	18-Oct-24 A	18-Oct-24 A	
469	DS-EN-520	Respond To COT Building Comments - APN - Enabling Permit & Comment Resol.	10.0d	21-Oct-24 A	1-Nov-24 A	
470	DS-EN-530	Submit to COT Including All Comment Resolution - APN - Enabling Permit & Co...	1.0d	4-Nov-24 A	4-Nov-24 A	
471	WBS - Design Assist Procurement		65.0d	11-Nov-24 A	13-Feb-25 A	
472	WBS - Request for Proposal		56.0d	11-Nov-24 A	31-Jan-25 A	
473	DS-DAP-100	Assemble Design Assist RFP Pkg. - Design Assist Procurement	5.0d	11-Nov-24 A	15-Nov-24 A	
474	DS-DAP-200	Review DA RFP Pkg. with HCAA - Design Assist Procurement	4.0d	18-Nov-24 A	22-Nov-24 A	
475	DS-DAP-300	Address DA RFP Pkg. Comments from HCAA - Design Assist Procurement	4.0d	25-Nov-24 A	29-Nov-24 A	
476	DS-DAP-400	Issue DA RFP to Bidders - Design Assist Procurement	0.0d		2-Dec-24 A	
477	DS-DAP-410	RFI's Due from Bidders - Design Assist Procurement	0.0d		10-Dec-24 A	
478	DS-DAP-420	Addendum Issued - Design Assist Procurement	5.0d		17-Dec-24 A	
479	DS-DAP-440	Bids Due - Design Assist Procurement	0.0d		9-Jan-25 A	
480	DS-DAP-450	HP Review Bids & Shortlist for Interviews - Design Assist Procurement	12.0d	16-Jan-25 A	31-Jan-25 A	
481	WBS - Interviews		8.0d	3-Feb-25	13-Feb-25 A	
482	DS-DAP-460	Steel Contractors Complete - HP & HCAA Interview	0.0d		3-Feb-25 A	
483	DS-DAP-470	Mech. & Plumbing Contractors Complete - HP & HCAA Interview	0.0d		4-Feb-25 A	
484	DS-DAP-490	Low Voltage Contractors Complete - HP & HCAA Interview	0.0d		10-Feb-25 A	
485	DS-DAP-480	Elec. Contractors Complete - HP & HCAA Interview	0.0d		11-Feb-25 A	
486	DS-DAP-500	Ground Improvement Contractors Complete - HP & HCAA Interview	0.0d		11-Feb-25 A	
487	DS-DAP-510	BHS Handling Contractors Complete - HP & HCAA Interview	0.0d		13-Feb-25 A	
488	WBS - Contract Award		8.0d	3-Feb-25	13-Feb-25 A	
489	DS-DAP-530	Steel Contract GMF Complete - Award Design Assist	0.0d		3-Feb-25 A	
490	DS-DAP-520	Mech. & Plumbing Contract BCH Mech. Complete - Award Design Assist	0.0d		4-Feb-25 A	
491	DS-DAP-550	Low Voltage Contract MC Dean Complete - Award Design Assist	0.0d		11-Feb-25 A	
492	DS-DAP-540	Elec. Contract APG Complete - Award Design Assist	0.0d		11-Feb-25 A	
493	DS-DAP-560	Ground Improvement Contract Menard Complete - Award Design Assist	0.0d		12-Feb-25 A	
494	DS-DAP-570	BHS Handling Contract Daifuku Complete - Award Design Assist	0.0d		13-Feb-25 A	
495	WBS - ASD - 30% Schematic Design		137.0d	17-Jul-24 A	30-Jan-25 A	
496	DS-SD-ASD-10	ASD - 30% Schematic Design NTP - ITB's	1.0d	17-Jul-24 A	17-Jul-24 A	
497	WBS - ASD - 30% Design		136.0d	18-Jul-24 A	30-Jan-25 A	
498	WBS - ASD - 30% Design Documents		136.0d	18-Jul-24 A	30-Jan-25 A	
499	WBS - Airside D Terminal		52.0d	14-Aug-24 A	25-Oct-24 A	
500	DS-SD-ASD-80	Architectural Design - ASD 30% DD	47.0d	14-Aug-24 A	18-Oct-24 A	
501	DS-SD-ASD-120	Floor Plan Development (Restrooms/Retail) - ASD 30% DD	5.0d	14-Aug-24 A	20-Aug-24 A	
502	DS-SD-ASD-130	Architectural Look & Feel - ASD 30% DD	7.0d	14-Aug-24 A	22-Aug-24 A	
503	DS-SD-ASD-140	PBB Locations & Gate Layout 30% Review - ASD 30% DD	4.0d	23-Aug-24 A	28-Aug-24 A	
504	DS-SD-ASD-160	Holdroom Layout & Gate Portal Location - ASD 30% DD	8.0d	29-Aug-24 A	10-Sep-24 A	

	ID	Name	Dur	Start	Finish	TF
505	DS-SD-ASD-240	Building Footprint Refinement - ASD 30% DD	5.0d	11-Sep-24 A	17-Sep-24 A	
506	DS-SD-ASD-290	Exterior Door Locations (OHD) - ASD 30% DD	10.0d	18-Sep-24 A	1-Oct-24 A	
507	DS-SD-ASD-330	Architectural Coord. & Implementation - ASD 30% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
508	DS-SD-ASD-340	Hurricane Milton Impact (10/7-10/11) - ASD SD 30%	5.0d	7-Oct-24 A	11-Oct-24 A	
509	DS-SD-ASD-360	Architecture Docs. Complete - ASD 30% DD	10.0d	14-Oct-24 A	25-Oct-24 A	
510	WBS - CBP		59.0d	25-Jul-24 A	16-Oct-24 A	
511	DS-SD-ASD-60	CBP Workshop #1	1.0d	25-Jul-24 A	25-Jul-24 A	
512	DS-SD-ASD-70	CBP Development	24.0d	26-Jul-24 A	28-Aug-24 A	
513	DS-SD-ASD-170	CBP Workshop #2	1.0d	29-Aug-24 A	29-Aug-24 A	
514	DS-SD-ASD-180	CBP Design Implementation	33.0d	30-Aug-24 A	16-Oct-24 A	
515	WBS - TSA		45.0d	14-Aug-24 A	16-Oct-24 A	
516	DS-SD-ASD-90	TSA Screening	45.0d	14-Aug-24 A	16-Oct-24 A	
517	WBS - Civil Coordination		45.0d	14-Aug-24 A	16-Oct-24 A	
518	DS-SD-ASD-100	Civil Coord. Design	45.0d	14-Aug-24 A	16-Oct-24 A	
519	WBS - Structural Design		45.0d	14-Aug-24 A	16-Oct-24 A	
520	DS-SD-ASD-110	Struct. Design	45.0d	14-Aug-24 A	16-Oct-24 A	
521	WBS - White Papers		35.0d	5-Sep-24 A	23-Oct-24 A	
522	DS-SD-ASD-190	Solar Power - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
523	DS-SD-ASD-200	CUP At Airside vs. MTCE CUP - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
524	DS-SD-ASD-210	Resiliency - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
525	DS-SD-ASD-220	Electrochromatic Glazing - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
526	DS-SD-ASD-350	Incorporate Information Into 30% Design - White Paper	10.0d	10-Oct-24 A	23-Oct-24 A	
527	WBS - APN - 30% Apron Site		136.0d	18-Jul-24 A	30-Jan-25 A	
528	WBS - PBB Layout		23.0d	29-Aug-24 A	1-Oct-24 A	
529	DS-SD-ASD-150	PBB Initial Layout 30% Apron Site	8.0d	29-Aug-24 A	10-Sep-24 A	
530	DS-SD-ASD-230	PBB Refinement 30% Apron Site	5.0d	11-Sep-24 A	17-Sep-24 A	
531	DS-SD-ASD-280	PBB Found. Location 30% Apron Site	5.0d	18-Sep-24 A	24-Sep-24 A	
532	DS-SD-ASD-310	PBB Layout Confirmation 30% Apron Site	5.0d	25-Sep-24 A	1-Oct-24 A	
533	WBS - Architectural Coordination		64.0d	18-Jul-24 A	16-Oct-24 A	
534	DS-SD-ASD-20	Truck Court Layout & Retaining Wall - Arch. Coord.	43.0d	18-Jul-24 A	17-Sep-24 A	
535	DS-SD-ASD-250	Building Footprint Identified for Civil - Arch. Coord.	1.0d	18-Sep-24 A	18-Sep-24 A	
536	DS-SD-ASD-260	FF Elevation Established for Civil - Arch. Coord.	1.0d	18-Sep-24 A	18-Sep-24 A	
537	DS-SD-ASD-270	Civil Layout & Refinement - Arch. Coord.	21.0d	18-Sep-24 A	16-Oct-24 A	
538	DS-SD-ASD-320	Exterior Door Locations (OHD) - Arch. Coord.	1.0d	2-Oct-24 A	2-Oct-24 A	
539	WBS - Wind Study		90.0d	23-Sep-24 A	30-Jan-25 A	
540	DS-SD-ASD-300	Wind Study (Expert Opinion)	20.0d	23-Sep-24 A	18-Oct-24 A	
541	DS-SD-ASD-370	Wind Study Summary - Recap Overview	2.0d	21-Oct-24 A	22-Oct-24 A	
542	DS-SD-ASD-380	Wind Study Model	25.0d	21-Oct-24 A	25-Nov-24 A	
543	DS-SD-ASD-470	Wind Study Analysis - Full Report	10.0d	26-Nov-24 A	10-Dec-24 A	
544	DS-SD-ASD-510	Wind Study HNTB Review Analysis	10.0d	11-Dec-24 A	24-Dec-24 A	
545	DS-SD-ASD-520	Wind Study Update Superstructure	10.0d	26-Dec-24 A	9-Jan-25 A	
546	DS-SD-ASD-530	Wind Study Update Found.	10.0d	10-Jan-25 A	23-Jan-25 A	

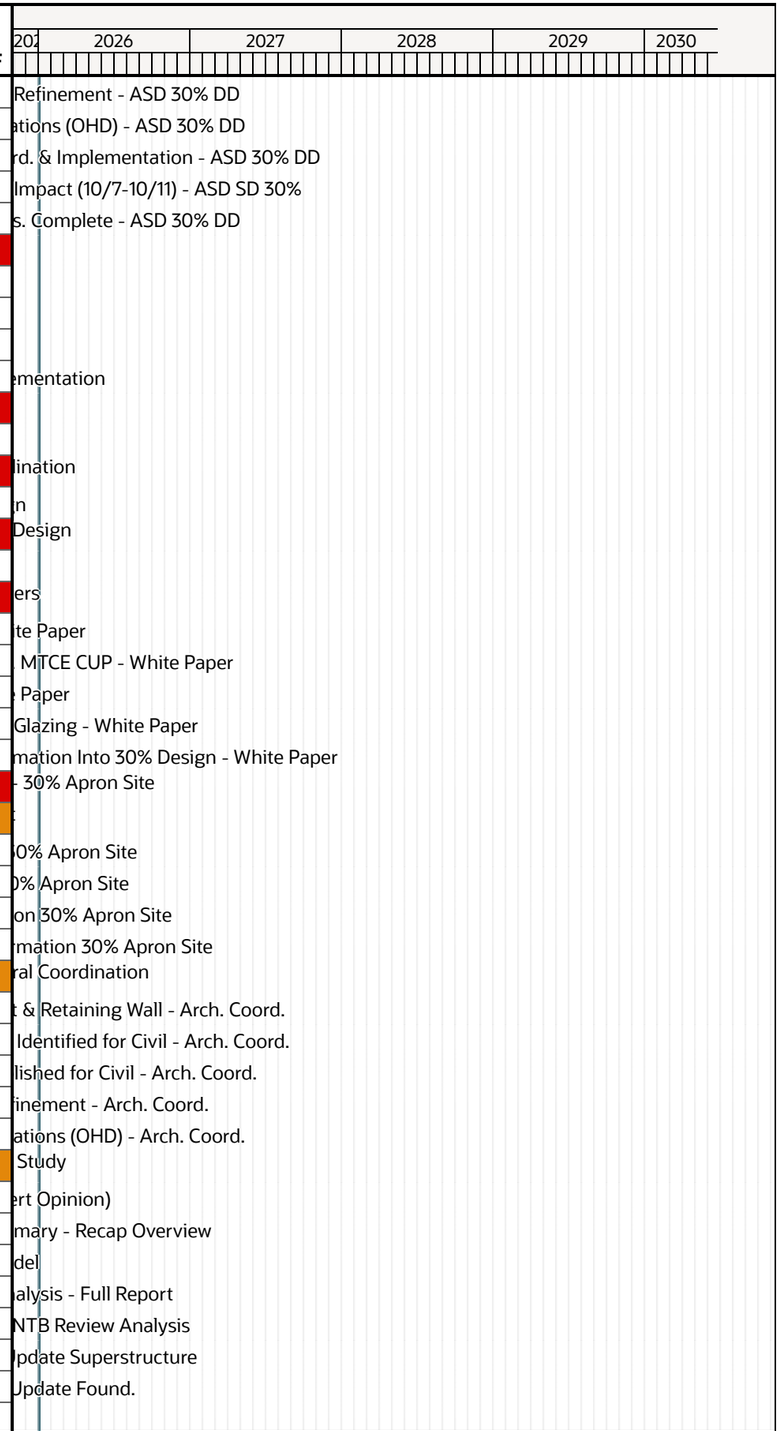


	ID	Name	Dur	Start	Finish	TF
547	DS-SD-ASD-540	Wind Study Finalize Found.	5.0d	24-Jan-25 A	30-Jan-25 A	
548	WBS - Civil Plans		50.0d	18-Jul-24 A	26-Sep-24 A	
549	DS-SD-ASD-30	Civil Paving/Hydrant Fueling 30% Design Apron Site	50.0d	18-Jul-24 A	26-Sep-24 A	
550	DS-SD-ASD-40	Civil Apron Demo Plans	50.0d	18-Jul-24 A	26-Sep-24 A	
551	DS-SD-ASD-50	Civil Site Utilities	50.0d	18-Jul-24 A	26-Sep-24 A	
552	WBS - Preliminary Cost Estimate		1.0d	23-Oct-24 A	23-Oct-24 A	
553	DS-SD-ASD-390	Preliminary Set To HP For Cost Estimating	1.0d	23-Oct-24 A	23-Oct-24 A	
554	WBS - ASD - 30% Review QA/QC		17.0d	28-Oct-24 A	19-Nov-24 A	
555	DS-SD-ASD-400	DQC - ASD 30%	5.0d	28-Oct-24 A	1-Nov-24 A	
556	DS-SD-ASD-410	Sr. Technical Review - ASD 30%	5.0d	28-Oct-24 A	1-Nov-24 A	
557	DS-SD-ASD-420	Post to Bluebeam Session - ASD 30%	1.0d	4-Nov-24 A	4-Nov-24 A	
558	DS-SD-ASD-430	IDR Comments - ASD 30%	5.0d	5-Nov-24 A	11-Nov-24 A	
559	DS-SD-ASD-440	IDR - Pick Up Comments - ASD 30%	2.0d	12-Nov-24 A	13-Nov-24 A	
560	DS-SD-ASD-450	Visual Check - ASD 30%	2.0d	14-Nov-24 A	15-Nov-24 A	
561	DS-SD-ASD-460	QA Check - ASD 30%	2.0d	18-Nov-24 A	19-Nov-24 A	
562	WBS - ASD - 30% Submittal To HCAA		11.0d	20-Nov-24 A	6-Dec-24 A	
563	DS-SD-ASD-480	ASD - Docs. Complete & Assemble Pkg.	1.0d	20-Nov-24 A	20-Nov-24 A	
564	DS-SD-ASD-490	ASD - 30% Subm. Due To HCAA	1.0d	21-Nov-24 A	21-Nov-24 A	
565	DS-SD-ASD-500	ASD - 30% HCAA Review	9.0d	22-Nov-24 A	6-Dec-24 A	
566	WBS - ASD - 60% Design Development		130.0d	21-Nov-24 A	28-May-25 A	
567	DS-DD-ASD-10	ASD - 60% DD NTP	1.0d	21-Nov-24 A	21-Nov-24 A	
568	WBS - ASD - 60% Design		130.0d	21-Nov-24 A	28-May-25 A	
569	WBS - ASD - 60% Design Documents		117.0d	21-Nov-24 A	8-May-25 A	
570	WBS - Airside D Terminal		96.0d	21-Nov-24 A	9-Apr-25 A	
571	DS-DD-ASD-20	Civil Design - ASD 60% DD Airside D Terminal	71.0d	21-Nov-24 A	5-Mar-25 A	
572	DS-DD-ASD-30	Struct. Design - ASD 60% DD Airside D Terminal	71.0d	21-Nov-24 A	5-Mar-25 A	
573	DS-DD-ASD-40	Architectural Design - ASD 60% DD Airside D Terminal	75.0d	22-Nov-24 A	12-Mar-25 A	
574	DS-DD-ASD-60	Ground Improvements Pkg. Coord. - ASD 60% DD Airside D Terminal	70.0d	22-Nov-24 A	5-Mar-25 A	
575	DS-DD-ASD-270	ASCEND Passenger Experience Extension - ASD 60% DD Airside D Terminal	20.0d	13-Mar-25 A	9-Apr-25 A	
576	WBS - Wind Study Report		74.0d	26-Nov-24 A	12-Mar-25 A	
577	DS-DD-ASD-220	Analysis Full Report - ASD 60% DD Wind Study Report	10.0d	26-Nov-24 A	10-Dec-24 A	
578	DS-DD-ASD-230	HNTB Review Analysis - ASD 60% DD Wind Study Report	10.0d	11-Dec-24 A	24-Dec-24 A	
579	DS-DD-ASD-240	Update Superstructure - ASD 60% DD Wind Study Report	10.0d	26-Dec-24 A	9-Jan-25 A	
580	DS-DD-ASD-100	Wind Tunnel - ASD 60% DD Wind Study Report	26.0d	31-Dec-24 A	5-Feb-25 A	
581	DS-DD-ASD-260	Finalize Found. - ASD 60% DD Wind Study Report	15.0d	10-Jan-25 A	30-Jan-25 A	
582	DS-DD-ASD-110	Incorporate White Paper Into 60% - ASD 60% DD Wind Study Report	25.0d	6-Feb-25 A	12-Mar-25 A	
583	WBS - APN - Apron Site		75.0d	22-Nov-24 A	12-Mar-25 A	
584	DS-DD-ASD-50	Civil Design Docs. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
585	DS-DD-ASD-70	Architectural/Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
586	DS-DD-ASD-80	MEP/Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
587	DS-DD-ASD-90	Struct./Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
588	WBS - Preliminary Cost Estimate		23.0d	8-Apr-25 A	8-May-25 A	

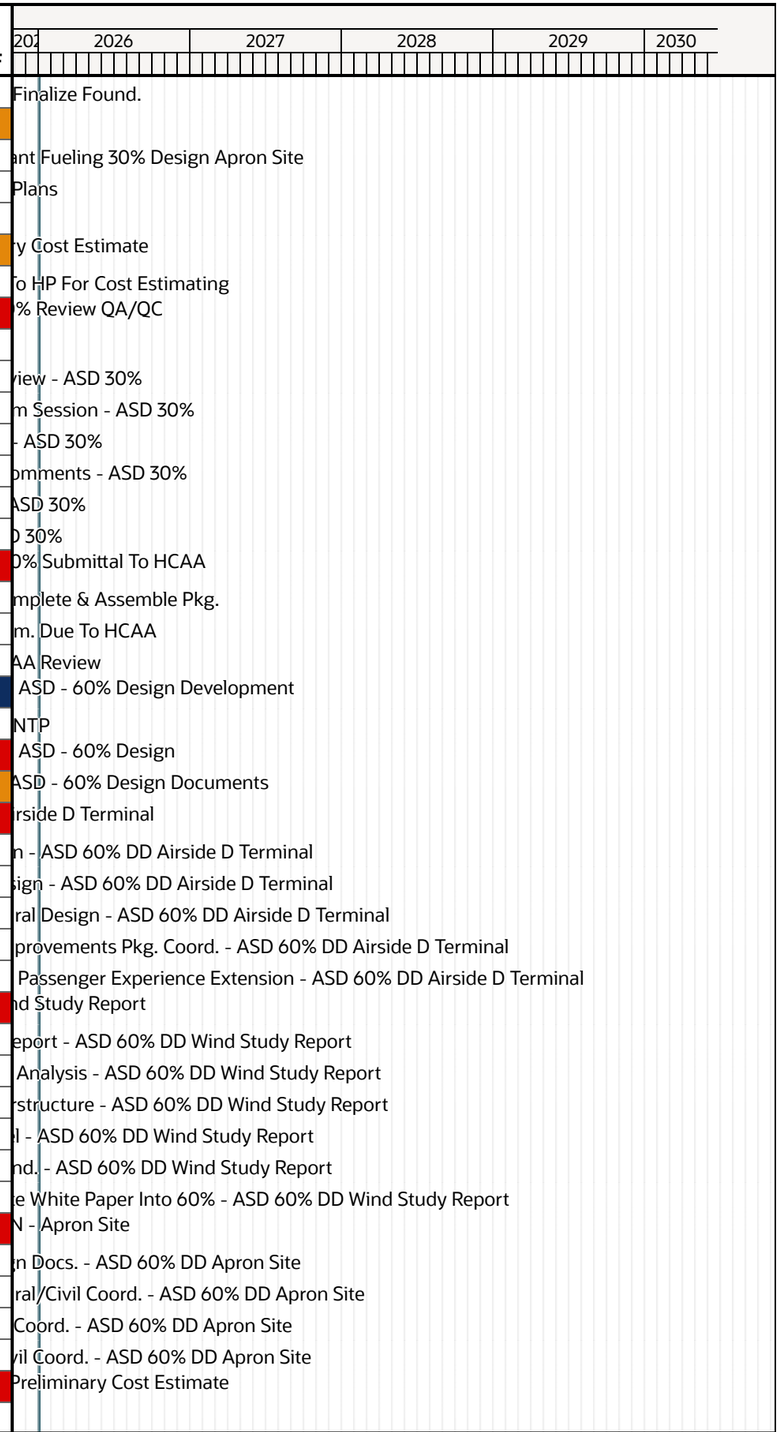


	ID	Name	Dur	Start	Finish	TF
589	DS-DD-ASD-120	Preliminary Set to HP For Cost Estimating - ASD 60% DD	23.0d	8-Apr-25 A	8-May-25 A	
590	WBS - ASD - 60% Review QA/QC		19.0d	10-Apr-25 A	6-May-25 A	
591	DS-DD-ASD-130	Design Review - DQC - ASD 60% Review QA/QC	5.0d	10-Apr-25 A	16-Apr-25 A	
592	DS-DD-ASD-140	Sr. Technical Review - ASD 60% Review QA/QC	5.0d	10-Apr-25 A	16-Apr-25 A	
593	DS-DD-ASD-150	Post Docs. - ASD 60% Review QA/QC	1.0d	17-Apr-25 A	17-Apr-25 A	
594	DS-DD-ASD-160	IDR - ASD 60% Review QA/QC	9.0d	18-Apr-25 A	30-Apr-25 A	
595	DS-DD-ASD-170	Visual Check - ASD 60% Review QA/QC	2.0d	1-May-25 A	2-May-25 A	
596	DS-DD-ASD-180	QAR Check - ASD 60% Review QA/QC	2.0d	5-May-25 A	6-May-25 A	
597	WBS - ASD - 60% Submittal To HCAA		15.0d	7-May-25 A	28-May-25 A	
598	DS-DD-ASD-190	Complete Docs. & Assemble Pkg. - ASD 60% Subm. to HCAA	1.0d	7-May-25 A	7-May-25 A	
599	DS-DD-ASD-200	Airside D Subm. Due - ASD 60% Subm. to HCAA	1.0d	8-May-25 A	8-May-25 A	
600	DS-DD-ASD-210	HCAA Review - ASD 60% Subm. to HCAA	13.0d	9-May-25 A	28-May-25 A	
601	WBS - ASD 90% Construction Documents		86.0d	8-May-25 A	9-Sep-25 A	
602	WBS - ASD 90% NTP		1.0d	8-May-25 A	8-May-25 A	
603	DS-CD-ASD-40	ASD - 90% CD NTP	1.0d	8-May-25 A	8-May-25 A	
604	WBS - ASD 90% Design		86.0d	8-May-25 A	9-Sep-25 A	
605	WBS - ASD 90% Design Documents		70.0d	8-May-25 A	15-Aug-25 A	
606	WBS - Airside D Terminal		45.0d	8-May-25 A	11-Jul-25 A	
607	DS-CD-ASD-10	Architectural Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
608	DS-CD-ASD-20	Civil Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
609	DS-CD-ASD-30	Struct. Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
610	WBS - APN - Apron Site		47.0d	9-May-25 A	16-Jul-25 A	
611	DS-CD-ASD-50	Civil Design Docs. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
612	DS-CD-ASD-60	Architectural/Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
613	DS-CD-ASD-70	MEP/Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
614	DS-CD-ASD-80	Struct./Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
615	WBS - Preliminary Cost Estimate		22.0d	17-Jul-25 A	15-Aug-25 A	
616	DS-CD-ASD-90	Preliminary Print Set For Cost Estimate To HP - ASD 90% DD	22.0d	17-Jul-25 A	15-Aug-25 A	
617	WBS - ASD 90% Review QA/QC		24.0d	17-Jul-25 A	19-Aug-25 A	
618	DS-CD-ASD-100	CD Review - DQC - ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
619	DS-CD-ASD-110	Sr. Technical Review - ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
620	DS-CD-ASD-095	Start CD Review - ASD 90% Review QA/QC	0.0d	17-Jul-25 A		
621	DS-CD-ASD-120	Post to Bluebeam - ASD 90% Review QA/QC	0.0d	29-Jul-25 A	29-Jul-25 A	
622	DS-CD-ASD-130	IDR - ASD 90% Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
623	DS-CD-ASD-140	Visual Check - ASD 90% Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
624	DS-CD-ASD-150	QAR Check - ASD 90% Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
625	WBS - ASD 90% Submittal To HCAA		14.0d	20-Aug-25 A	9-Sep-25 A	
626	DS-CD-ASD-160	Complete Docs. & Assemble Pkg. - ASD 90% Subm.	1.0d	20-Aug-25 A	20-Aug-25 A	
627	DS-CD-ASD-170	Subm. Due to HCAA - ASD 90% Subm.	1.0d	21-Aug-25 A	21-Aug-25 A	
628	DS-CD-ASD-180	HCAA Review - ASD 90% Subm.	12.0d	22-Aug-25 A	9-Sep-25 A	
629	WBS - ASD 100% Construction Documents		50.0d	21-Aug-25 A	30-Oct-25 A	
630	WBS - ASD 100% NTP		1.0d	21-Aug-25 A	21-Aug-25 A	


	ID	Name	Dur	Start	Finish	TF
631	DS-CD-ASD-1000	ASD - 100% CD NTP	1.0d	21-Aug-25 A	21-Aug-25 A	
632	WBS - ASD 100% Design		49.0d	22-Aug-25 A	30-Oct-25 A	
633	WBS - ASD 100% Design Documents		36.0d	22-Aug-25 A	13-Oct-25 A	
634	WBS - Airside D Terminal		30.0d	22-Aug-25 A	3-Oct-25 A	
635	DS-CD-ASD-1010	Architectural Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
636	DS-CD-ASD-1030	Civil Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
637	DS-CD-ASD-1040	Struct. Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
638	WBS - Apron Site		30.0d	22-Aug-25 A	3-Oct-25 A	
639	DS-CD-ASD-1020	Civil Design Docs. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
640	DS-CD-ASD-1050	Architectural/Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
641	DS-CD-ASD-1060	MEP/Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
642	DS-CD-ASD-1070	Struct./Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
643	WBS - Preliminary Cost Estimate		12.0d	26-Sep-25 A	13-Oct-25 A	
644	DS-CD-ASD-1080	Preliminary Print Set for Cost Estimate to HP - ASD 100% DD Apron Site	12.0d	26-Sep-25 A	13-Oct-25 A	
645	WBS - ASD 100% Review QA/QC		17.0d	6-Oct-25 A	28-Oct-25 A	
646	DS-CD-ASD-1090	DQC - ASD 100% CD Review QA/QC	5.0d	6-Oct-25 A	10-Oct-25 A	
647	DS-CD-ASD-1100	Sr. Technical Review - ASD 100% CD Review QA/QC	5.0d	6-Oct-25 A	10-Oct-25 A	
648	DS-CD-ASD-1110	Post to Bluebeam - ASD 100% CD Review QA/QC	1.0d	13-Oct-25 A	13-Oct-25 A	
649	DS-CD-ASD-1120	IDR - ASD 100% CD Review QA/QC	8.0d	14-Oct-25 A	23-Oct-25 A	
650	DS-CD-ASD-1130	Visual Check - ASD 100% CD Review QA/QC	2.0d	24-Oct-25 A	27-Oct-25 A	
651	DS-CD-ASD-1140	QAR Check - ASD 100% CD Review QA/QC	1.0d	28-Oct-25 A	28-Oct-25 A	
652	WBS - ASD 100% Submittal To HCAA		2.0d	29-Oct-25 A	30-Oct-25 A	
653	DS-CD-ASD-1150	Complete Docs. & Assemble Pkg. - ASD 100% Subm. to HCAA	1.0d	29-Oct-25 A	29-Oct-25 A	
654	DS-CD-ASD-1160	Submittal Due to HP/HCAA - ASD 100% Subm. to HCAA	1.0d	30-Oct-25 A	30-Oct-25 A	
655	WBS - Airside E Optimization		369.0d	16-Sep-24 A	27-Feb-26	1,032.0d
656	WBS - ASE Optimization Proposal		168.0d	16-Sep-24 A	13-May-25 A	
657	DS-AE-10	Proposal Submitted (HNTB) - ASE Optimization	1.0d	16-Sep-24 A	16-Sep-24 A	
658	DS-AE-20	Owner Proposal Review - ASE Optimization	159.0d	17-Sep-24 A	1-May-25 A	
659	DS-AE-30	Anticipated NTP - ASE Optimization	1.0d	13-May-25 A	13-May-25 A	
660	WBS - ASE Optimization 15%		44.0d	14-May-25 A	16-Jul-25 A	
661	WBS - ASE Optimization 15% Documents		22.0d	14-May-25 A	13-Jun-25 A	
662	DS-AE-40	Exist. Conditions Investigation - ASE Optimization 15%	5.0d	14-May-25 A	20-May-25 A	
663	DS-AE-50	Concept Design - ASE Optimization 15%	12.0d	21-May-25 A	6-Jun-25 A	
664	DS-AE-60	Focus Team Mtg. With HCAA - ASE Optimization 15%	3.0d	9-Jun-25 A	11-Jun-25 A	
665	DS-AE-70	Incorporate Comments into Design - ASE Optimization 15%	2.0d	12-Jun-25 A	13-Jun-25 A	
666	WBS - ASE Optimization 15% QA/QC		10.0d	16-Jun-25 A	27-Jun-25 A	
667	DS-AE-90	DQC - ASE Optimization 15% QA/QC	4.0d	16-Jun-25 A	19-Jun-25 A	
668	DS-AE-80	Sr. Technical Review - ASE Optimization 15% QA/QC	4.0d	16-Jun-25 A	19-Jun-25 A	
669	DS-AE-100	Post Docs. - ASE Optimization 15% QA/QC	1.0d	19-Jun-25 A	19-Jun-25 A	
670	DS-AE-110	IDR - ASE Optimization 15% QA/QC	4.0d	20-Jun-25 A	25-Jun-25 A	
671	DS-AE-120	Visual Check - ASE Optimization 15% QA/QC	1.0d	26-Jun-25 A	26-Jun-25 A	
672	DS-AE-130	QAR - ASE Optimization 15% QA/QC	1.0d	27-Jun-25 A	27-Jun-25 A	

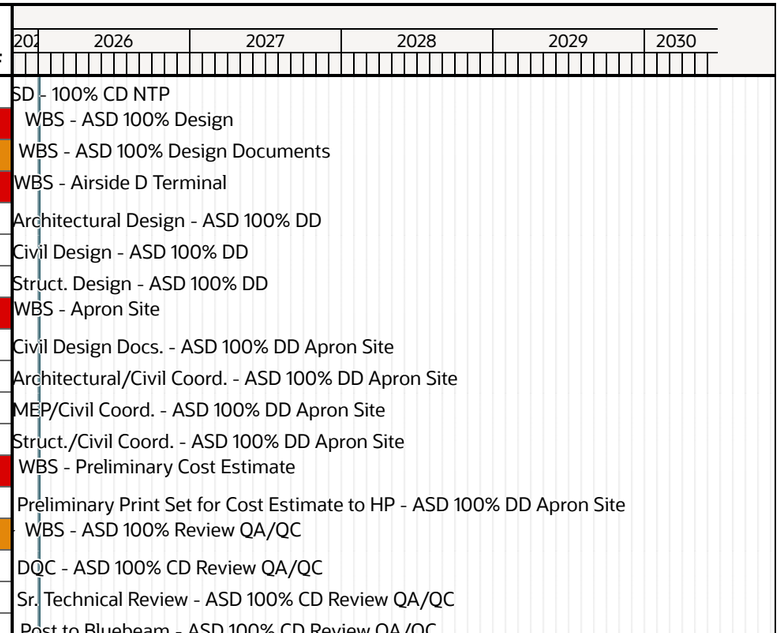


	ID	Name	Dur	Start	Finish	TF
673	WBS - ASE Optimization 15% Submittal To HCAA		12.0d	30-Jun-25 A	16-Jul-25 A	
674	DS-AE-140	Complete Docs. & Assemble Pkg. - ASE Optimization 15% Subm.	1.0d	30-Jun-25 A	30-Jun-25 A	
675	DS-AE-150	Subm. Due to HCAA - ASE Optimization 15% Subm.	1.0d	1-Jul-25 A	1-Jul-25 A	
676	DS-AE-160	Review (HCAA) - ASE Optimization 15% Subm.	10.0d	2-Jul-25 A	16-Jul-25 A	
677	WBS - ASE Optimization 50%		86.0d	3-Jul-25 A	3-Nov-25 A	
678	WBS - ASE Optimization 50% Documents		62.0d	3-Jul-25 A	30-Sep-25 A	
679	DS-AE-290	Design Docs. - ASE Optimization 50% Docs.	24.0d	3-Jul-25 A	6-Aug-25 A	
680	DS-AE-300	Focus Team Mtg. With HCAA - ASE Optimization 50% Docs.	5.0d	7-Aug-25 A	13-Aug-25 A	
681	DS-AE-310	Incorporate Comments into Design - ASE Optimization 50% Docs.	10.0d	14-Aug-25 A	27-Aug-25 A	
682	DS-AE-315	Decision Date for BHS Make-up System - ASE Optimization 50% Docs.	1.0d	28-Aug-25 A	28-Aug-25 A	
683	DS-AE-640	BNP Readiness for Coordination Update Documents - ASE Optimization 50% D...	4.0d	29-Aug-25 A	4-Sep-25 A	
684	DS-AE-650	Consultant Update Documents - ASE Optimization 50% Docs.	15.0d	5-Sep-25 A	25-Sep-25 A	
685	DS-AE-660	Finalize 50% Documents- ASE Optimization 50% Docs.	3.0d	26-Sep-25 A	30-Sep-25 A	
686	WBS - ASE Optimization 50% QA/QC		13.0d	1-Oct-25 A	17-Oct-25 A	
687	DS-AE-320	Sr. Technical Review - ASE Optimization 50% QA/QC	5.0d	1-Oct-25 A	7-Oct-25 A	
688	DS-AE-330	DQC - ASE Optimization 50% QA/QC	5.0d	1-Oct-25 A	7-Oct-25 A	
689	DS-AE-340	Post Docs. - ASE Optimization 50% QA/QC	1.0d	8-Oct-25 A	8-Oct-25 A	
690	DS-AE-350	IDR - ASE Optimization 50% QA/QC	5.0d	9-Oct-25 A	15-Oct-25 A	
691	DS-AE-360	Visual Check - ASE Optimization 50% QA/QC	1.0d	16-Oct-25 A	16-Oct-25 A	
692	DS-AE-370	QAR - ASE Optimization 50% QA/QC	1.0d	17-Oct-25 A	17-Oct-25 A	
693	WBS - ASE Optimization 50% Submittal To HCAA		12.0d	17-Oct-25 A	3-Nov-25 A	
694	DS-AE-380	Complete Docs. & Assemble Pkg. - ASE Optimization 50% Subm.	1.0d	17-Oct-25 A	17-Oct-25 A	
695	DS-AE-390	Subm. Due to HCAA - ASE Optimization 50% Subm.	1.0d	20-Oct-25 A	20-Oct-25 A	
696	DS-AE-400	Review by HCAA - ASE Optimization 50% Subm.	10.0d	21-Oct-25 A	3-Nov-25 A	
697	WBS - ASE Optimization 90%		54.0d	21-Oct-25 A	8-Jan-26	1,043.0d
698	WBS - ASE Optimization 90% Documents		32.0d	21-Oct-25 A	5-Dec-25 A	
699	DS-AE-410	Design Docs. - ASE Optimization 90% Docs.	25.0d	21-Oct-25 A	24-Nov-25 A	
700	DS-AE-420	Focus Team Mtg. With HCAA - ASE Optimization 90% Docs.	1.0d	25-Nov-25 A	25-Nov-25 A	
701	DS-AE-430	Incorporate Comments into Design - ASE Optimization 90% Docs.	6.0d	26-Nov-25 A	5-Dec-25 A	
702	WBS - ASE Optimization 90% QA/QC		9.0d	8-Dec-25 A	19-Dec-25 A	
703	DS-AE-440	Sr. Technical Review - ASE Optimization 90% QA/QC	3.0d	8-Dec-25 A	11-Dec-25 A	
704	DS-AE-450	DQC - ASE Optimization 90% QA/QC	3.0d	8-Dec-25 A	11-Dec-25 A	
705	DS-AE-460	Post Docs. - ASE Optimization 90% QA/QC	1.0d	12-Dec-25 A	12-Dec-25 A	
706	DS-AE-470	IDR - ASE Optimization 90% QA/QC	4.0d	15-Dec-25 A	18-Dec-25 A	
707	DS-AE-480	Visual Check / QA - ASE Optimization 90% QA/QC	1.0d	19-Dec-25 A	19-Dec-25 A	
708	WBS - ASE Optimization 90% Submittal To HCAA		12.0d	22-Dec-25 A	8-Jan-26	1,043.0d
709	DS-AE-500	Complete Docs. & Assemble Pkg. - ASE Optimization 90% Subm.	1.0d	22-Dec-25 A	22-Dec-25 A	
710	DS-AE-510	Subm. Due to HCAA - ASE Optimization 90% Subm.	1.0d	23-Dec-25 A	23-Dec-25 A	
711	DS-AE-520	Review by HCAA - ASE Optimization 90% Subm.	10.0d	24-Dec-25 A	8-Jan-26	1,042.0d
712	WBS - ASE Optimization 100%		46.0d	24-Dec-25 A	27-Feb-26	1,032.0d
713	WBS - ASE Optimization 100% Documents		26.0d	24-Dec-25 A	30-Jan-26	1,032.0d
714	DS-AE-530	Design Docs. - ASE Optimization 100%	21.0d	24-Dec-25 A	23-Jan-26	1,031.0d

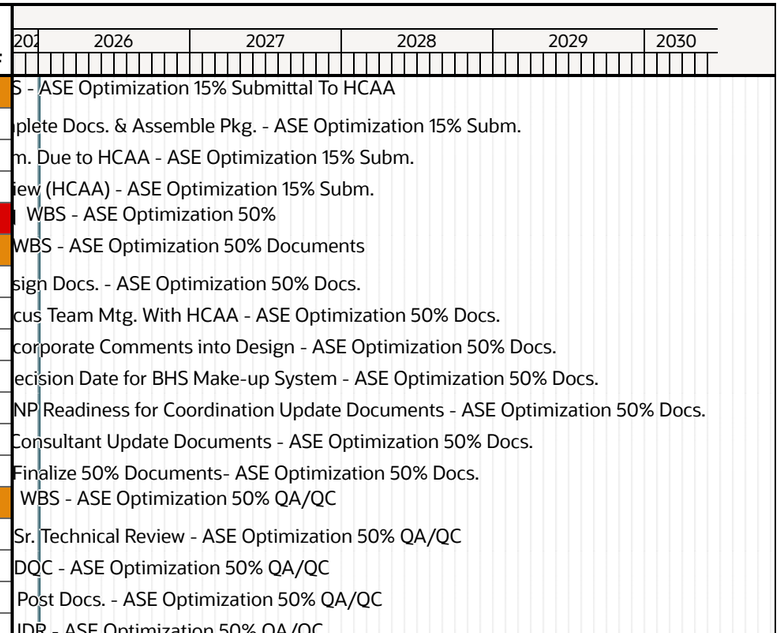

	ID	Name	Dur	Start	Finish	TF
715	DS-AE-550	Incorporate Comments into Design - ASE Optimization 100%	5.0d	26-Jan-26	30-Jan-26	1,031.0d
716	WBS - ASE Optimization 100% QA/QC		8.0d	2-Feb-26	11-Feb-26	1,032.0d
717	DS-AE-560	Sr. Technical Review - ASE Optimization 100% QA/QC	3.0d	2-Feb-26	4-Feb-26	1,031.0d
718	DS-AE-570	DQC - ASE Optimization 100% QA/QC	3.0d	2-Feb-26	4-Feb-26	1,031.0d
719	DS-AE-580	Post Docs. - ASE Optimization 100% QA/QC	1.0d	5-Feb-26	5-Feb-26	1,031.0d
720	DS-AE-590	IDR - ASE Optimization 100% QA/QC	3.0d	6-Feb-26	10-Feb-26	1,031.0d
721	DS-AE-600	Visual Check - ASE Optimization 100% QA/QC	1.0d	11-Feb-26	11-Feb-26	1,031.0d
722	WBS - ASE Optimization 100% Submittal To HCAA		12.0d	12-Feb-26	27-Feb-26	1,032.0d
723	DS-AE-620	Complete Docs. & Assemble Pkg. - ASE Optimization 100% Subm.	1.0d	12-Feb-26	12-Feb-26	1,031.0d
724	DS-AE-630	Subm. Due to HCAA - ASE Optimization 100% Subm.	1.0d	13-Feb-26	13-Feb-26	1,031.0d
725	DS-AE-670	100% Review by HCAA - ASE Optimization 100% Subm.	10.0d	16-Feb-26	27-Feb-26	1,031.0d
726	WBS - A-Sortation & Airside C Screening Integration		106.0d	8-Sep-25 A	6-Feb-26	947.0d
727	DS-AA-120	NTP - A-Sortation & Airside C Screening Integration (First $150k)	1.0d	8-Sep-25 A	8-Sep-25 A	
728	DS-AA-640	HNTB - Design Deliverables 15%, 30%, 60%, 90% & 100%	105.0d	9-Sep-25 A	6-Feb-26	946.0d
729	DS-AA-100	Proposal Submitted (HNTB) - A-Sortation & Airside C Screening Integration	1.0d	13-Oct-25 A	13-Oct-25 A	
730	DS-AA-110	Owner Proposal Review - A-Sortation & Airside C Screening Integration	52.0d	14-Oct-25 A	29-Dec-25	974.0d
731	DS-AA-630	NTP - A-Sortation & Airside C Screening Integration (Second $150k)	1.0d	29-Dec-25	29-Dec-25	807.0d
732	WBS - NST Application		95.0d	3-Apr-25 A	15-Aug-25 A	
733	DS-DD-NST-10	NST Mtg. - NST Appl.	1.0d	3-Apr-25 A	3-Apr-25 A	
734	DS-DD-NST-20	HNTB to Coordinate & Provide Information to NST - NST Appl.	3.0d	4-Apr-25 A	8-Apr-25 A	
735	DS-DD-NST-22	NST Draft Purchase Order - NST Appl.	5.0d	9-Apr-25 A	15-Apr-25 A	
736	DS-DD-NST-24	NST Reservation Letter - Email Received - NST Appl.	1.0d	28-Apr-25 A	28-Apr-25 A	
737	DS-DD-NST-30	HCAA Agreement Via Email - NST Appl.	5.0d	29-Apr-25 A	5-May-25 A	
738	DS-DD-NST-40	NST Reservation Letter - NST Appl.	5.0d	6-May-25 A	12-May-25 A	
739	DS-DD-NST-42	NST Revised Purchase Agreement HCAA Acceptance - NST Appl.	8.0d	13-May-25 A	22-May-25 A	
740	DS-DD-NST-43	NST & HCAA Agreement of Terms for Board Approval - NST Appl.	50.0d	23-May-25 A	4-Aug-25 A	
741	DS-DD-NST-44	NST HCAA Board Approval - NST Appl.	1.0d	7-Aug-25 A	7-Aug-25 A	
742	DS-DD-NST-46	NST Approval & Purchase Credit - NST Appl.	5.0d	8-Aug-25 A	14-Aug-25 A	
743	DS-DD-NST-50	NST Issuance & Completion of Credit Transfer - NST Appl.	1.0d	15-Aug-25 A	15-Aug-25 A	
744	WBS - SWFWMD Submittal Permit		137.0d	21-Mar-25 A	2-Oct-25 A	
745	PM-SW-ITB1-30	ITB 1 & Apron Docs. Complete - SWFWMD Sub. Permit	1.0d	21-Mar-25 A	21-Mar-25 A	
746	PM-SW-40	Prepare Docs. Complete 60% - SWFWMD Sub. Permit	34.0d	24-Mar-25 A	8-May-25 A	
747	PM-SW-45	Revise Model & Adjust Drainage Information - SWFWMD Sub. Permit	10.0d	9-May-25 A	22-May-25 A	
748	PM-SW-50	Prepare Application Docs. - SWFWMD Sub. Permit	15.0d	23-May-25 A	13-Jun-25 A	
749	PM-SW-ITB1-55	ASD/ITB 1 Subm. to AHJ - SWFWMD Sub. Permit	1.0d	16-Jun-25 A	16-Jun-25 A	
750	PM-SW-58	SWFWMD DQC - SWFWMD Sub. Permit	4.0d	17-Jun-25 A	20-Jun-25 A	
751	WBS - SWFWMD IDR		72.0d	23-Jun-25 A	2-Oct-25 A	
752	PM-SW-60	SWFWMD Initial Submittal to HCAA for Review - SWFWMD Sub. Permit	1.0d	23-Jun-25 A	23-Jun-25 A	
753	PM-SW-65	SWFWMD Submittal Review - SWFWMD Sub. Permit	1.0d	24-Jun-25 A	24-Jun-25 A	
754	PM-SW-80	Design Team Respond to Initial Comments - SWFWMD Sub. Permit	1.0d	25-Jun-25 A	25-Jun-25 A	
755	PM-SW-85	Visual Check - SWFWMD Sub. Permit	1.0d	26-Jun-25 A	26-Jun-25 A	
756	PM-SW-ITB1-90	Submit SWFWMD ASD/ITB1 Revision #1 to AHJ - SWFWMD Sub. Permit	1.0d	27-Jun-25 A	27-Jun-25 A	

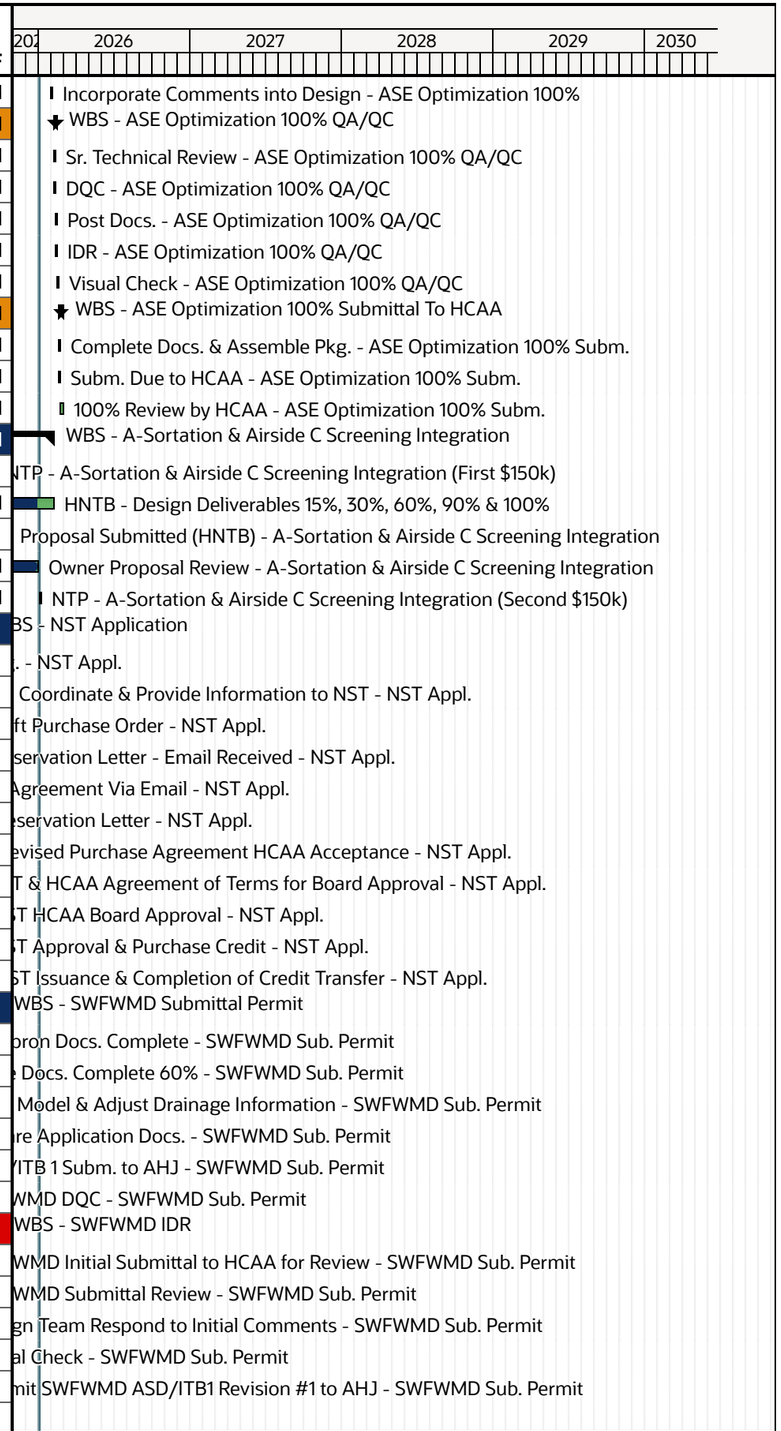

	ID	Name	Dur	Start	Finish	TF
757	PM-SW-70	AHJ Conducts SWFWMD Final Review - SWFWMD Sub. Permit	22.0d	30-Jun-25 A	30-Jul-25 A	
758	PM-SW-100	Design Team Update & Respond to Comments - SWFWMD Sub. Permit	9.0d	31-Jul-25 A	12-Aug-25 A	
759	PM-SW-110	Design Team Submit Revisions to AHJ - SWFWMD Sub. Permit	1.0d	13-Aug-25 A	13-Aug-25 A	
760	PM-SW-115	AHJ - RAI Review - SWFWMD Sub. Permit	22.0d	14-Aug-25 A	15-Sep-25 A	
761	PM-SW-120	SWFWMD Write up After Confirming no Comments - SWFWMD Sub. Permit	12.0d	16-Sep-25 A	1-Oct-25 A	
762	PM-SW-130	SWFWMD Permit Issuance - SWFWMD Sub. Permit	1.0d	2-Oct-25 A	2-Oct-25 A	
763	WBS - ASD - Site Plan		112.0d	27-Jan-25 A	2-Jul-25 A	
764	DS-DD-ASDSPR-10	Define Requirements - ASD Site Plan	10.0d	27-Jan-25 A	7-Feb-25 A	
765	DS-DD-ASDSPR-30	COT Informs ASD of SPR Requirement - ASD Site Plan	0.0d	27-Jan-25 A	27-Jan-25 A	
766	DS-DD-ASDSPR-20	COT Mtg. - ASD Site Plan	1.0d	10-Feb-25 A	10-Feb-25 A	
767	DS-DD-ASDSPR-40	Develop Site Plan - ASD Site Plan	10.0d	11-Feb-25 A	24-Feb-25 A	
768	DS-DD-ASDSPR-140	HCAA Approve rk Order Authorization - ASD Site Plan	10.0d	25-Feb-25 A	10-Mar-25 A	
769	DS-DD-ASDSPR-50	Complete SPR Document Pkg. - ASD Site Plan	1.0d	20-Mar-25 A	20-Mar-25 A	
770	DS-DD-ASDSPR-70	Prepare Docs. for HCAA Review - ASD Site Plan	5.0d	21-Mar-25 A	27-Mar-25 A	
771	DS-DD-ASDSPR-80	Submit SPR to COT for Review - ASD Site Plan	1.0d	28-Mar-25 A	28-Mar-25 A	
772	DS-DD-ASDSPR-90	COT SPR Review - ASD Site Plan	34.0d	1-Apr-25 A	16-May-25 A	
773	DS-DD-ASDSPR-100	COT SPR Comments Received - ASD Site Plan	1.0d	19-May-25 A	19-May-25 A	
774	DS-DD-ASDSPR-110	COT Design Team Respond to Comments - ASD Site Plan	13.0d	20-May-25 A	6-Jun-25 A	
775	DS-DD-ASDSPR-60	Submit SPR Revision #1 to COT - ASD Site Plan	1.0d	9-Jun-25 A	9-Jun-25 A	
776	DS-DD-ASDSPR-120	COT Review Responses - ASD Site Plan	14.0d	10-Jun-25 A	27-Jun-25 A	
777	DS-DD-ASDSPR-130	Anticipated SPR Permit Approval by COT - ASD Site Plan	1.0d	2-Jul-25 A	2-Jul-25 A	
778	WBS - ASD - Early Foundations		217.0d	22-Nov-24 A	1-Oct-25 A	
779	WBS - ASD - Early Foundations 60%		72.0d	22-Nov-24 A	7-Mar-25 A	
780	WBS - ASD - Early Foundations 60% Design Documents		41.0d	22-Nov-24 A	23-Jan-25 A	
781	DS-DD-ASDEF-10	Struct. Design Docs. - ASD Early Found. 60% DD	41.0d	22-Nov-24 A	23-Jan-25 A	
782	DS-DD-ASDEF-20	Architectural/Struct. Design Coord. - ASD Early Found. 60% DD	41.0d	22-Nov-24 A	23-Jan-25 A	
783	DS-DD-ASDEF-130	Update Found. Per Wind Study - ASD Early Found. 60% DD	10.0d	10-Jan-25 A	23-Jan-25 A	
784	WBS - ASD - Early Foundations 60% Review Progress Print		31.0d	24-Jan-25 A	7-Mar-25 A	
785	DS-DD-ASDEF-100	Progress Printed - ASD Early Found. 60% Review Progress Print	1.0d	24-Jan-25 A	24-Jan-25 A	
786	DS-DD-ASDEF-110	Bluebeam Review - ASD Early Found. 60% Review Progress Print	5.0d	27-Jan-25 A	31-Jan-25 A	
787	DS-DD-ASDEF-120	Address Comments Incorporate into Docs. - ASD Early Found. 60% Review Pro...	25.0d	3-Feb-25 A	7-Mar-25 A	
788	DS-DD-ASDEF-140	Focus Team Review With HCAA - ASD Early Found. 60% Review Progress Print	2.0d	10-Feb-25 A	11-Feb-25 A	
789	WBS - ASD - Early Foundations 100%		163.0d	12-Feb-25 A	1-Oct-25 A	
790	WBS - ASD - Early Foundations 100% Design Documents		21.0d	12-Feb-25 A	12-Mar-25 A	
791	DS-CD-ASDEF-10	Struct. Design Docs. - ASD Early Found. 100% DD	21.0d	12-Feb-25 A	12-Mar-25 A	
792	DS-CD-ASDEF-20	Architectural/Struct. Design Coord. - ASD Early Found. 100% DD	21.0d	12-Feb-25 A	12-Mar-25 A	
793	WBS - ASD - EF Preliminary Cost Estimate		20.0d	13-Mar-25 A	9-Apr-25 A	
794	DS-CD-ASDEF-30	ASD - Preliminary Set To HP For Cost Estimating	20.0d	13-Mar-25 A	9-Apr-25 A	
795	WBS - ASD - Early Foundations 100% Review QA/QC		18.0d	14-Mar-25 A	8-Apr-25 A	
796	DS-CD-ASDEF-40	DQC - ASD Early Found. 100% Review QA/QC	5.0d	14-Mar-25 A	20-Mar-25 A	
797	DS-CD-ASDEF-50	Sr. Technical Review - ASD Early Found. 100% Review QA/QC	5.0d	14-Mar-25 A	20-Mar-25 A	
798	DS-CD-ASDEF-60	Post to Bluebeam - ASD Early Found. 100% Review QA/QC	1.0d	21-Mar-25 A	21-Mar-25 A	

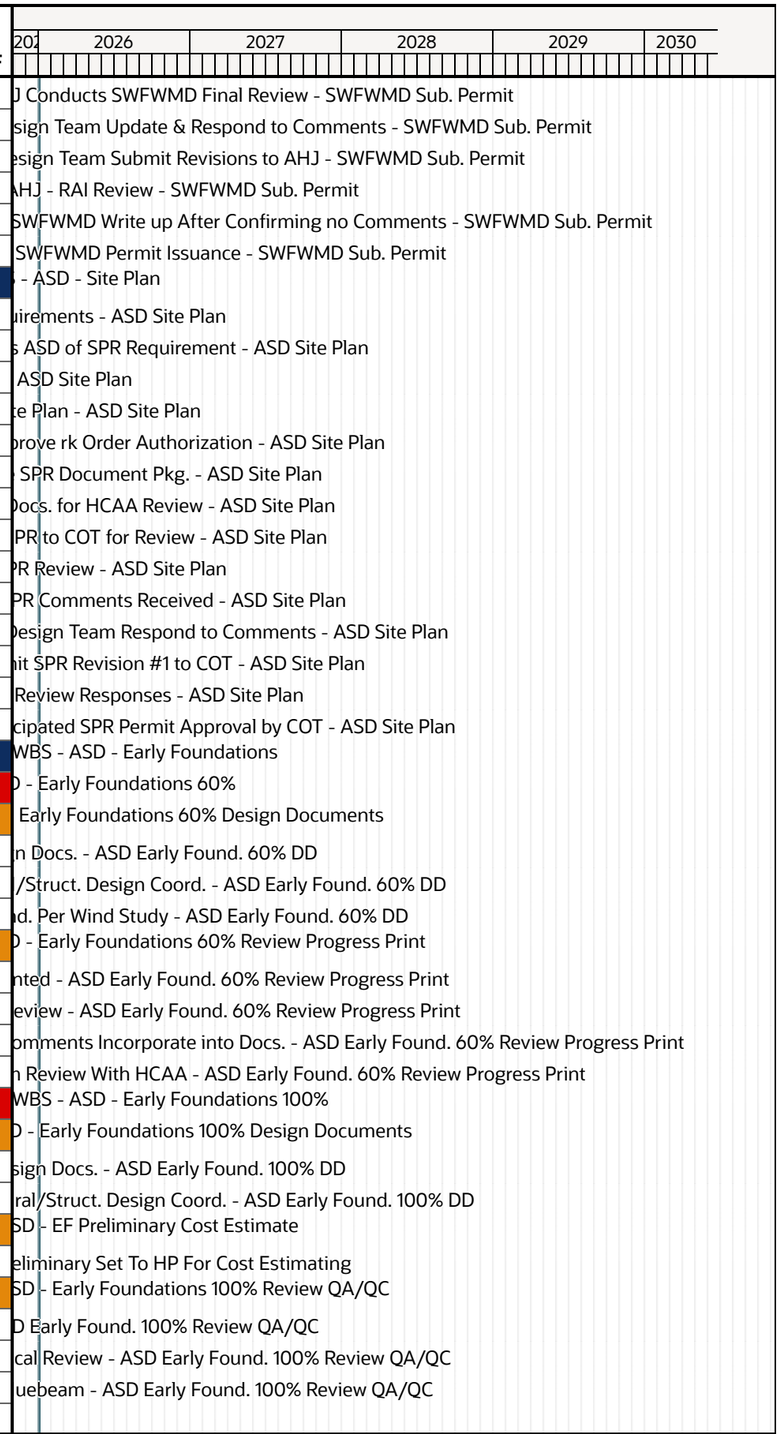


	ID	Name	Dur	Start	Finish	TF
799	DS-CD-ASDEF-70	IDR - ASD Early Found. 100% Review QA/QC	8.0d	24-Mar-25 A	2-Apr-25 A	
800	DS-CD-ASDEF-80	Visual Check - ASD Early Found. 100% Review QA/QC	2.0d	3-Apr-25 A	4-Apr-25 A	
801	DS-CD-ASDEF-90	QA Check - ASD Early Found. 100% Review QA/QC	2.0d	7-Apr-25 A	8-Apr-25 A	
802	WBS - ASD - Early Foundations 100% Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
803	DS-CD-ASDEF-100	Complete Docs. & Assemble Pkg. - ASD Early Found. 100% Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
804	DS-CD-ASDEF-110	Bid/Permit Set Subm. Due - ASD Early Found. 100% Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
805	DS-CD-ASDEF-120	HCAA Review - ASD Early Found. 100% Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
806	WBS - ASD - FND - Bidding and Negotiations		51.0d	11-Apr-25 A	23-Jun-25 A	
807	DS-FND-B&N-10	Update Plans with New Loads - ASD-FND-Bidding & Negotiations	24.0d	11-Apr-25 A	14-May-25 A	
808	DS-FND-B&N-20	Issued load impact to Base - ASD-FND-Bidding & Negotiations	1.0d	15-May-25 A	15-May-25 A	
809	DS-FND-B&N-30	Base to Update Found. Design /Details - ASD-FND-Bidding & Negotiations	14.0d	16-May-25 A	5-Jun-25 A	
810	DS-FND-B&N-40	Design Updates Finalized - ASD-FND-Bidding & Negotiations	0.0d		5-Jun-25 A	
811	DS-FND-B&N-50	Design Updates DQC Start - ASD-FND-Bidding & Negotiations	1.0d	6-Jun-25 A	6-Jun-25 A	
812	DS-FND-B&N-60	DQC - ASD-FND-Bidding & Negotiations	2.0d	6-Jun-25 A	9-Jun-25 A	
813	DS-FND-B&N-70	Post to IDR Bluebeam - ASD-FND-Bidding & Negotiations	0.0d		9-Jun-25 A	
814	DS-FND-B&N-80	IDR - ASD-FND-Bidding & Negotiations	2.0d	10-Jun-25 A	11-Jun-25 A	
815	DS-FND-B&N-90	VC / QA - ASD-FND-Bidding & Negotiations	1.0d	12-Jun-25 A	12-Jun-25 A	
816	DS-FND-B&N-100	Addendum Issued to HP - ASD-FND-Bidding & Negotiations	0.0d		12-Jun-25 A	
817	DS-FND-B&N-110	Bidding - ASD-FND-Bidding & Negotiations	4.0d	13-Jun-25 A	18-Jun-25 A	
818	DS-FND-B&N-120	Bids Due Date - ASD-FND-Bidding & Negotiations	1.0d	19-Jun-25 A	19-Jun-25 A	
819	DS-FND-B&N-130	Ready to submit to COT - ASD-FND-Bidding & Negotiations	1.0d	23-Jun-25 A	23-Jun-25 A	
820	WBS - ASD - FND Bulletin 1		48.0d	25-Jul-25 A	1-Oct-25 A	
821	DS-FND-B&N-140	ASD - FND Bulletin 1 - Update Drawings	35.0d	25-Jul-25 A	12-Sep-25 A	
822	DS-FND-B&N-150	ASD - FND Bulletin 1 - Finalize Documents	1.0d	15-Sep-25 A	15-Sep-25 A	
823	WBS - ASD FND Bulletin 1 QA/QC		9.0d	16-Sep-25 A	26-Sep-25 A	
824	DS-FND-B&N-160	ASD - FND Bulletin 1 - DQC	2.0d	16-Sep-25 A	17-Sep-25 A	
825	DS-FND-B&N-170	ASD - FND Bulletin 1 - IDR	6.0d	18-Sep-25 A	25-Sep-25 A	
826	DS-FND-B&N-180	ASD - FND Bulletin 1 - Visual Check / QAR	1.0d	26-Sep-25 A	26-Sep-25 A	
827	WBS - ASD FND Bulletin 1 - Submittal to HP		3.0d	29-Sep-25 A	1-Oct-25 A	
828	DS-FND-B&N-190	ASD - FND Bulletin 1 - Complete Documents & Assemble Package	1.0d	29-Sep-25 A	29-Sep-25 A	
829	DS-FND-B&N-200	ASD - FND Bulletin 1 - FND Addendum 2 Submittal to HP	1.0d	30-Sep-25 A	30-Sep-25 A	
830	DS-FND-B&N-210	ASD - FND Bulletin 1 - Submit to COT	1.0d	1-Oct-25 A	1-Oct-25 A	
831	WBS - ASD - Long Lead Package (Steel, Chillers, AHU, Switchgear, VT, etc)		30.0d	9-May-25 A	20-Jun-25 A	
832	WBS - ASD - Long Lead Package Design Documents		18.0d	9-May-25 A	4-Jun-25 A	
833	DS-DD-ASDLL-10	Struct. Design - Steel Pkg. Mill Order - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
834	DS-DD-ASDLL-20	Vertical Transportation - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
835	DS-DD-ASDLL-30	Mech. Design AHU - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
836	DS-DD-ASDLL-40	Elec. Power & Feeders - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
837	WBS - ASD - LLP Preliminary Cost Estimate		21.0d	9-May-25 A	9-Jun-25 A	
838	DS-DD-ASDLL-50	ASD - LLP Preliminary Set to HP For Cost Estimating	21.0d	9-May-25 A	9-Jun-25 A	
839	WBS - ASD - Long Lead Package Review QA/QC		5.0d	5-Jun-25 A	11-Jun-25 A	
840	DS-DD-ASDLL-60	DQC - ASD Long Lead Pckg. Review QA/QC	2.0d	5-Jun-25 A	6-Jun-25 A	

	ID	Name	Dur	Start	Finish	TF
841	DS-DD-ASDLL-70	Sr. Technical Review - ASD Long Lead Pckg. Review QA/QC	2.0d	5-Jun-25 A	6-Jun-25 A	
842	DS-DD-ASDLL-80	Post to Bluebeam - ASD Long Lead Pckg. Review QA/QC	0.0d		6-Jun-25 A	
843	DS-DD-ASDLL-90	IDR - ASD Long Lead Pckg. Review QA/QC	2.0d	9-Jun-25 A	10-Jun-25 A	
844	DS-DD-ASDLL-100	Visual Check - ASD Long Lead Pckg. Review QA/QC	1.0d	11-Jun-25 A	11-Jun-25 A	
845	DS-DD-ASDLL-110	QA Check - ASD Long Lead Pckg. Review QA/QC	1.0d	11-Jun-25 A	11-Jun-25 A	
846	WBS - ASD - Long Lead Package Submittal To HCAA		8.0d	11-Jun-25 A	20-Jun-25 A	
847	DS-DD-ASDLL-120	Complete & Assemble Docs. - ASD Long Lead Pckg. Subm. to HCAA	1.0d	11-Jun-25 A	11-Jun-25 A	
848	DS-DD-ASDLL-130	Submit Pkg. to HCAA - ASD Long Lead Pckg. Subm. to HCAA	1.0d	12-Jun-25 A	12-Jun-25 A	
849	DS-DD-ASDLL-140	HCAA Review - ASD Long Lead Pckg. Subm. to HCAA	6.0d	13-Jun-25 A	20-Jun-25 A	
850	WBS - ITB's - FAA Submittal Review		102.0d	1-Oct-24 A	25-Feb-25 A	
851	WBS - APN - ITB 1 - Paving - Hydrant Fueling - FAA Submittal		102.0d	1-Oct-24 A	25-Feb-25 A	
852	WBS - APN - ITB 1 - Design Documents		51.0d	1-Oct-24 A	12-Dec-24 A	
853	DS-DD-ITB1-AP-10	APN - ITB1 Hydrant Fueling - Civil - Paving Design	4.0d	1-Oct-24 A	4-Oct-24 A	
854	DS-DD-ITB1-AP-20	APN - ITB1 Hydrant Fueling - Civil - Paving Hydrant Fueling FAA	4.0d	1-Oct-24 A	4-Oct-24 A	
855	DS-DD-ITB1-AP-30	ATB1 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
856	DS-DD-ITB1-AP-40	ITB1 Hydrant Fueling - Civil - Civil - Docs.	30.0d	14-Oct-24 A	25-Nov-24 A	
857	DS-DD-ITB1-AP-50	ITB1 Hydrant Fueling - Civil - Preliminary Set to HP For Cost Estimating	16.0d	19-Nov-24 A	12-Dec-24 A	
858	WBS - APN - ITB 1 - Review QA/QC		16.0d	26-Nov-24 A	18-Dec-24 A	
859	DS-DD-ITB1-AP-170	Start QA/QC Review - APN - ITB1 Hydrant Fueling	1.0d	26-Nov-24 A	26-Nov-24 A	
860	DS-DD-ITB1-AP-60	Review - DQC - APN - ITB1 Hydrant Fueling	5.0d	27-Nov-24 A	4-Dec-24 A	
861	DS-DD-ITB1-AP-70	Sr. Technical Review - APN - ITB1 Hydrant Fueling	5.0d	27-Nov-24 A	4-Dec-24 A	
862	DS-DD-ITB1-AP-80	Post to Bluebeam - APN - ITB1 Hydrant Fueling	1.0d	5-Dec-24 A	5-Dec-24 A	
863	DS-DD-ITB1-AP-90	IDR - APN - ITB1 Hydrant Fueling	5.0d	6-Dec-24 A	12-Dec-24 A	
864	DS-DD-ITB1-AP-100	Visual Check - APN - ITB1 Hydrant Fueling	2.0d	16-Dec-24 A	17-Dec-24 A	
865	DS-DD-ITB1-AP-110	Review QA/QC Hydrant Fueling FAA - QA Check - APN - ITB1 Hydrant Fueling	1.0d	18-Dec-24 A	18-Dec-24 A	
866	WBS - APN - ITB 1 - Submittal To HCAA		47.0d	19-Dec-24 A	25-Feb-25 A	
867	DS-DD-ITB1-AP-120	Complete Docs. & Assemble Pkg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	19-Dec-24 A	19-Dec-24 A	
868	DS-DD-ITB1-AP-130	Subm. To HCAA - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	20-Dec-24 A	20-Dec-24 A	
869	DS-DD-ITB1-AP-140	FAA Review - APN - ITB1 Sub. to HCAA Hydrant Fueling	20.0d	23-Dec-24 A	21-Jan-25 A	
870	DS-DD-ITB1-AP-160	HCAA Review - APN - ITB1 Sub. to HCAA Hydrant Fueling	9.0d	23-Dec-24 A	6-Jan-25 A	
871	DS-DD-ITB1-AP-180	Respond to HCAA Comments - APN - ITB1 Sub. to HCAA Hydrant Fueling	7.0d	7-Jan-25 A	15-Jan-25 A	
872	DS-DD-ITB1-AP-150	HCAA Comment Resolution Mtg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	16-Jan-25 A	16-Jan-25 A	
873	DS-DD-ITB1-AP-200	Respond to FAA Comments - APN - ITB1 Sub. to HCAA Hydrant Fueling	3.0d	22-Jan-25 A	24-Jan-25 A	
874	DS-DD-ITB1-AP-190	FAA Comment Resolution Mtg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	25-Feb-25 A	25-Feb-25 A	
875	WBS - ASD - ITB 2 - PBB Design - FAA Submittal (60%)		95.0d	2-Oct-24 A	17-Feb-25 A	
876	WBS - ASD - ITB 2 - PBB Design Documents		68.0d	2-Oct-24 A	9-Jan-25 A	
877	DS-DD-ITB2-PB-10	Architectural Design Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
878	DS-DD-ITB2-PB-20	Civil Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
879	DS-DD-ITB2-PB-30	Utility Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
880	DS-DD-ITB2-PB-40	ATB2 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
881	DS-DD-ITB2-PB-50	Civil - Docs. - ASD ITB 2 PBB 60% DD	43.0d	14-Oct-24 A	13-Dec-24 A	
882	DS-DD-ITB2-PB-60	Preliminary Set to HP For Cost Estimating - ASD ITB 2 PBB 60% DD	22.0d	9-Dec-24 A	9-Jan-25 A	

	ID	Name	Dur	Start	Finish	TF
883	WBS - ASD - ITB 2 - PBB Review QA/QC		16.0d	16-Dec-24 A	8-Jan-25 A	
884	DS-DD-ITB2-PB-170	Start QA/QC - ASD ITB 2 PBB 60% Design Review QA/QC	1.0d	16-Dec-24 A	16-Dec-24 A	
885	DS-DD-ITB2-PB-70	DQC - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	17-Dec-24 A	23-Dec-24 A	
886	DS-DD-ITB2-PB-80	Sr. Technical Review - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	17-Dec-24 A	23-Dec-24 A	
887	DS-DD-ITB2-PB-90	Post to Bluebeam - ASD ITB 2 PBB 60% Design Review QA/QC	1.0d	24-Dec-24 A	24-Dec-24 A	
888	DS-DD-ITB2-PB-100	IDR - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	26-Dec-24 A	2-Jan-25 A	
889	DS-DD-ITB2-PB-110	Visual Check - ASD ITB 2 PBB 60% Design Review QA/QC	2.0d	3-Jan-25 A	6-Jan-25 A	
890	DS-DD-ITB2-PB-120	QA Check - ASD ITB 2 PBB 60% Design Review QA/QC	2.0d	7-Jan-25 A	8-Jan-25 A	
891	WBS - ASD - ITB 2 - PBB Submittal To HCAA		28.0d	9-Jan-25 A	17-Feb-25 A	
892	DS-DD-ITB2-PB-130	Complete Docs. & Assemble Pkg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	9-Jan-25 A	9-Jan-25 A	
893	DS-DD-ITB2-PB-140	Subm. to HCAA Due - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	10-Jan-25 A	10-Jan-25 A	
894	DS-DD-ITB2-PB-150	FAA Review - ASD ITB 2 PBB 60% Subm. to HCAA	21.0d	13-Jan-25 A	10-Feb-25 A	
895	DS-DD-ITB2-PB-180	HCAA Review - ASD ITB 2 PBB 60% Subm. to HCAA	10.0d	13-Jan-25 A	27-Jan-25 A	
896	DS-DD-ITB2-PB-160	HCAA Comment Resolution Mtg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	28-Jan-25 A	28-Jan-25 A	
897	DS-DD-ITB2-PB-190	FAA Comment Resolution Mtg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	17-Feb-25 A	17-Feb-25 A	
898	WBS - GDY - ITB 3 - Guideway Structure - FAA Submittal (60%)		80.0d	2-Oct-24 A	27-Jan-25 A	
899	WBS - GDY - ITB 3 - Guideway Design Documents		50.0d	2-Oct-24 A	12-Dec-24 A	
900	DS-DD-ITB3-GS-10	Architectural Coord. & Design - GDY ITB3 GDWY Structure 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
901	DS-DD-ITB3-GS-20	Struct. Design - GDY ITB3 GDWY Structure 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
902	DS-DD-ITB3-GS-30	ATB3 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
903	DS-DD-ITB3-GS-40	Civil - Docs. - GDY ITB3 GDWY Structure 60% DD	31.0d	14-Oct-24 A	26-Nov-24 A	
904	DS-DD-ITB3-GS-50	Preliminary Set to HP For Cost Estimating - GDY ITB3 GDWY Structure 60% DD	21.0d	12-Nov-24 A	12-Dec-24 A	
905	WBS - GDY - ITB 3 - Guideway Review QA/QC		15.0d	27-Nov-24 A	18-Dec-24 A	
906	DS-DD-ITB3-GS-160	Start QA/QC - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	27-Nov-24 A	27-Nov-24 A	
907	DS-DD-ITB3-GS-60	Review -DQC - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	29-Nov-24 A	5-Dec-24 A	
908	DS-DD-ITB3-GS-70	Sr. Technical Review - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	29-Nov-24 A	5-Dec-24 A	
909	DS-DD-ITB3-GS-80	Post to Bluebeam - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	6-Dec-24 A	6-Dec-24 A	
910	DS-DD-ITB3-GS-90	IDR - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	9-Dec-24 A	13-Dec-24 A	
911	DS-DD-ITB3-GS-100	Visual Check - GDY ITB3 GDWY Structure 60% QA/QC	2.0d	16-Dec-24 A	17-Dec-24 A	
912	DS-DD-ITB3-GS-110	QA Check - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	18-Dec-24 A	18-Dec-24 A	
913	WBS - GDY - ITB 3 - Guideway Submittal To HCAA		26.0d	19-Dec-24 A	27-Jan-25 A	
914	DS-DD-ITB3-GS-120	Complete Docs. & Assemble Pkg. - GDY ITB3 GDWY Structure 60% Subm. to H...	1.0d	19-Dec-24 A	19-Dec-24 A	
915	DS-DD-ITB3-GS-130	Subm. To HCAA - GDY ITB3 GDWY Structure 60% Subm. to HCAA	1.0d	20-Dec-24 A	20-Dec-24 A	
916	DS-DD-ITB3-GS-140	FAA Review - GDY ITB3 GDWY Structure 60% Subm. to HCAA	23.0d	23-Dec-24 A	24-Jan-25 A	
917	DS-DD-ITB3-GS-170	HCAA Review - GDY ITB3 GDWY Structure 60% Subm. to HCAA	24.0d	23-Dec-24 A	27-Jan-25 A	
918	DS-DD-ITB3-GS-150	Comment Resolution Mtg. - GDY ITB3 GDWY Structure 60% Subm. to HCAA	1.0d	27-Jan-25 A	27-Jan-25 A	
919	WBS - CCBS - 30% Design - TSA Submittals - Main Terminal		414.0d	13-Sep-23 A	28-Apr-25 A	
920	WBS - CCBS - 30% Design		238.0d	13-Sep-23 A	16-Aug-24 A	
921	WBS - CCBS - 30% - MT Study		77.0d	13-Sep-23 A	3-Jan-24 A	
922	DS-CC-SD-10	CCBS - 30% DD NTP - Main Terminal	1.0d	13-Sep-23 A	13-Sep-23 A	
923	DS-CC-SD-20	Site Visits - Analysis - CCBS 30% MT Study	25.0d	14-Sep-23 A	18-Oct-23 A	
924	DS-CC-SD-30	Site Walk - CCBS 30% MT Study	1.0d	19-Oct-23 A	19-Oct-23 A	




	ID	Name	Dur	Start	Finish	TF
925	DS-CC-SD-40	Document Study Completion - CCBS 30% MT Study	2.0d	20-Oct-23 A	23-Oct-23 A	
926	DS-CC-SD-50	VTC - Internal QA/QC - CCBS 30% MT Study	3.0d	24-Oct-23 A	26-Oct-23 A	
927	DS-CC-SD-60	VTC - Finalize Document - CCBS 30% MT Study	1.0d	27-Oct-23 A	27-Oct-23 A	
928	DS-CC-SD-70	Study QA/QC - CCBS 30% MT Study	5.0d	30-Oct-23 A	3-Nov-23 A	
929	DS-CC-SD-80	Compilation & Final Document - CCBS 30% MT Study	4.0d	6-Nov-23 A	9-Nov-23 A	
930	DS-CC-SD-90	Subm. To HCAA - CCBS 30% MT Study	1.0d	10-Nov-23 A	10-Nov-23 A	
931	DS-CC-SD-100	Review (HCAA) - CCBS 30% MT Study	19.0d	13-Nov-23 A	11-Dec-23 A	
932	DS-CC-SD-110	Final Presentation (HCAA) - CCBS 30% MT Study	1.0d	12-Dec-23 A	12-Dec-23 A	
933	DS-CC-SD-120	Owner Review & Determination - CCBS 30% MT Study	13.0d	13-Dec-23 A	2-Jan-24 A	
934	DS-CC-SD-130	HCAA Determination On CCBS 30% MT Study	1.0d	3-Jan-24 A	3-Jan-24 A	
935	WBS - CCBS - East End Sortation Study NTP		121.0d	11-Jan-24 A	27-Jun-24 A	
936	DS-CC-SD-140	East End Sortation ROM Subm. - East End Sortation Study	1.0d	11-Jan-24 A	11-Jan-24 A	
937	DS-CC-SD-150	NTP - East End Sortation Study	66.0d	16-Jan-24 A	16-Apr-24 A	
938	DS-CC-SD-160	Complete Study - East End Sortation Study	39.0d	17-Apr-24 A	11-Jun-24 A	
939	DS-CC-SD-170	Submit Docs. To HNTB - East End Sortation Study	1.0d	12-Jun-24 A	12-Jun-24 A	
940	DS-CC-SD-180	QA/QC - Start IDR - East End Sortation Study	5.0d	13-Jun-24 A	19-Jun-24 A	
941	DS-CC-SD-190	QA - East End Sortation Study	1.0d	20-Jun-24 A	20-Jun-24 A	
942	DS-CC-SD-200	Submit To HCAA - East End Sortation Study	1.0d	21-Jun-24 A	21-Jun-24 A	
943	DS-CC-SD-210	VTC Owner Presentation (Tentative) - East End Sortation Study	1.0d	27-Jun-24 A	27-Jun-24 A	
944	WBS - CCBS - Develop New BHS Concepts at Main Terminal		35.0d	28-Jun-24 A	16-Aug-24 A	
945	DS-CC-SD-220	Develop Updated Concept (No Single Point of Failure) - New Concept	7.0d	28-Jun-24 A	9-Jul-24 A	
946	DS-CC-SD-230	Conceptual Review Mtg. - HNTB/HP/VTC - New Concept	1.0d	10-Jul-24 A	10-Jul-24 A	
947	DS-CC-SD-240	Update Concepts & Validate Constructability - New Concept	4.0d	11-Jul-24 A	16-Jul-24 A	
948	DS-CC-SD-250	Develop Constraints & Limitations Based On Concepts - New Concept	4.0d	11-Jul-24 A	16-Jul-24 A	
949	DS-CC-SD-260	Mtg. to Review Updated Concepts - HNTB/HP/VTC - New Concept	1.0d	17-Jul-24 A	17-Jul-24 A	
950	DS-CC-SD-270	Develop Preliminary Docs. For Focus Team - New Concept	5.0d	18-Jul-24 A	24-Jul-24 A	
951	DS-CC-SD-280	Preliminary Review Constraints & Limitations with BHS Focus Team - New Conc...	1.0d	25-Jul-24 A	25-Jul-24 A	
952	DS-CC-SD-290	Incorporate New Concept Feedback From HCAA - New Concept	3.0d	26-Jul-24 A	30-Jul-24 A	
953	DS-CC-SD-300	Complete New Concept Study - New Concept	4.0d	26-Jul-24 A	31-Jul-24 A	
954	DS-CC-SD-310	Submit Docs. To HNTB - New Concept	1.0d	1-Aug-24 A	1-Aug-24 A	
955	DS-CC-SD-320	QA/QC - Start IDR - New Concept	3.0d	2-Aug-24 A	6-Aug-24 A	
956	DS-CC-SD-330	QA - New Concept	1.0d	7-Aug-24 A	7-Aug-24 A	
957	DS-CC-SD-340	Resubmit to HCAA - New Concept	1.0d	8-Aug-24 A	8-Aug-24 A	
958	DS-CC-SD-350	HCAA Review & Presentation - New Concept	5.0d	9-Aug-24 A	15-Aug-24 A	
959	DS-CC-SD-360	Decision on East End Sortation Study - New Concept	1.0d	16-Aug-24 A	16-Aug-24 A	
960	WBS - CCBS - Airside E Optimization		193.0d	24-May-24 A	26-Feb-25 A	
961	DS-AE-SD-10	Proposal Subm. - Airside E Optimization	1.0d	24-May-24 A	24-May-24 A	
962	DS-AE-SD-20	HCAA Proposal Comments Returned 6/17/24 - Airside E Optimization	14.0d	28-May-24 A	17-Jun-24 A	
963	DS-AE-SD-30	Revised Proposal - Airside E Optimization	10.0d	18-Jun-24 A	1-Jul-24 A	
964	DS-AE-SD-40	Submitted Revised Proposal To HP - Airside E Optimization	1.0d	2-Jul-24 A	2-Jul-24 A	
965	DS-AE-SD-50	Rev. 3 Submission To HCAA - Airside E Optimization	1.0d	3-Jul-24 A	3-Jul-24 A	
966	DS-AE-SD-60	HCAA Review Of Rev. 3 - Airside E Optimization	12.0d	8-Jul-24 A	23-Jul-24 A	

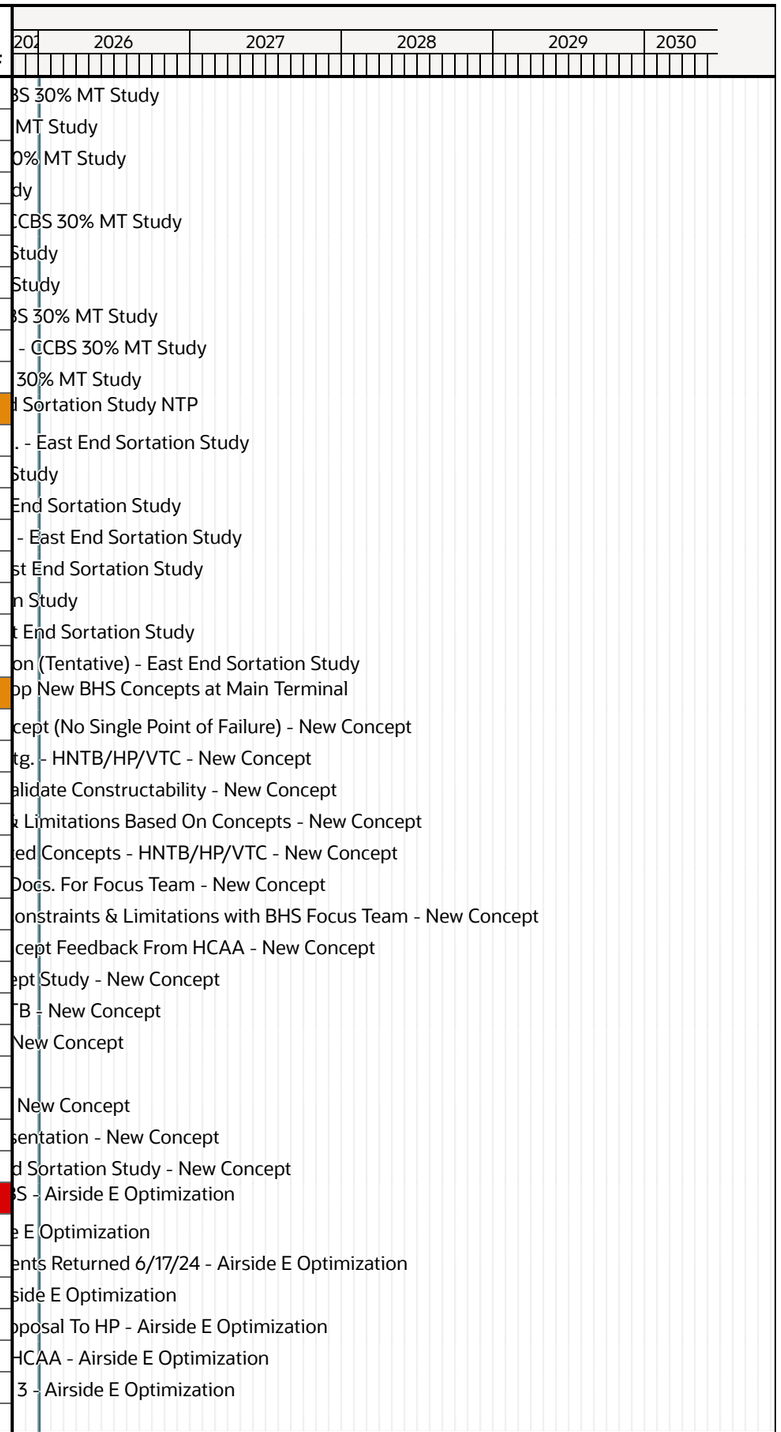


	ID	Name	Dur	Start	Finish	TF
967	DS-AE-SD-70	Rescinded to Rev. 3 From HCAA - Airside E Optimization	1.0d	23-Jul-24 A	23-Jul-24 A	
968	DS-AE-SD-80	HNTB Develop & Submit Rev. 4 (CE021) To HP - Airside E Optimization	38.0d	24-Jul-24 A	16-Sep-24 A	
969	DS-AE-SD-90	HP Review & Submit Rev. 4 (CE021) To HCAA - Airside E Optimization	7.0d	17-Sep-24 A	25-Sep-24 A	
970	DS-AE-SD-100	HCAA Review of Rev. 4 (CE021) - Airside E Optimization	105.0d	26-Sep-24 A	25-Feb-25 A	
971	DS-AE-SD-110	Airside E Optimization NTP - Airside E Optimization	1.0d	26-Feb-25 A	26-Feb-25 A	
972	WBS - CCBS - TSA Submittals - VTC		141.0d	4-Jan-24 A	19-Jul-24 A	
973	WBS - CCBS - TSA - Predesign CBIS		85.0d	4-Jan-24 A	1-May-24 A	
974	DS-CC-SD-1000	Develop Predesign CBIS - CCBS TSA	46.0d	4-Jan-24 A	7-Mar-24 A	
975	DS-CC-SD-1010	VTC DQC - CCBS TSA	6.0d	11-Mar-24 A	18-Mar-24 A	
976	DS-CC-SD-1020	HCAA Review - CCBS TSA	1.0d	19-Mar-24 A	19-Mar-24 A	
977	DS-CC-SD-1030	IDR/CCBS Predesign Document-Incorporated Comments - CCBS TSA	7.0d	20-Mar-24 A	28-Mar-24 A	
978	DS-CC-SD-1040	Predesign CBIS To TSA - CCBS TSA	4.0d	29-Mar-24 A	3-Apr-24 A	
979	DS-CC-SD-1050	Review by TSA - CCBS TSA	20.0d	4-Apr-24 A	1-May-24 A	
980	WBS - CCBS - TSA - Predesign Revision		56.0d	2-May-24 A	19-Jul-24 A	
981	DS-CC-SD-1070	VTC Resubmit to HNTB - CCBS TSA	11.0d	2-May-24 A	16-May-24 A	
982	DS-CC-SD-1080	HCAA Feedback - CCBS TSA	4.0d	17-May-24 A	22-May-24 A	
983	DS-CC-SD-1090	QA/QC Bluebeam Session - CCBS TSA	4.0d	17-May-24 A	22-May-24 A	
984	DS-CC-SD-1100	HNTB/HP VTC Review Of HCAA Comments - CCBS TSA	2.0d	23-May-24 A	24-May-24 A	
985	DS-CC-SD-1110	VTC to Respond to BB Session & HCAA Comments - CCBS TSA	5.0d	23-May-24 A	30-May-24 A	
986	DS-CC-SD-1120	Back Check Comments From HCAA & BB - CCBS TSA	1.0d	31-May-24 A	31-May-24 A	
987	DS-CC-SD-1130	QA HNTB On Process - CCBS TSA	1.0d	3-Jun-24 A	3-Jun-24 A	
988	DS-CC-SD-1140	Mtg. With HCAA - Validate Document - CCBS TSA	1.0d	4-Jun-24 A	4-Jun-24 A	
989	DS-CC-SD-1150	Final Corrections - CCBS TSA	1.0d	5-Jun-24 A	5-Jun-24 A	
990	DS-CC-SD-1160	ReSubm. to TSA - CCBS TSA	1.0d	6-Jun-24 A	6-Jun-24 A	
991	DS-CC-SD-1170	TSA Review - CCBS TSA	10.0d	7-Jun-24 A	20-Jun-24 A	
992	DS-CC-SD-1200	TSA Review Mtg. - CCBS TSA	9.0d	21-Jun-24 A	3-Jul-24 A	
993	DS-CC-SD-1210	TSA Predesign Approval - CCBS TSA	2.0d	5-Jul-24 A	8-Jul-24 A	
994	DS-CC-SD-1990	TSA (CLOSE GAP) - CCBS TSA	9.0d	9-Jul-24 A	19-Jul-24 A	
995	WBS - CCBS - Consultant Change - BNP		196.0d	22-Jul-24 A	28-Apr-25 A	
996	DS-CC-SD-1220	Notice To VTC - Stop work	1.0d	22-Jul-24 A	22-Jul-24 A	
997	DS-CC-SD-1230	BNP Engagement	5.0d	23-Jul-24 A	29-Jul-24 A	
998	DS-CC-SD-1300	BNP Contract Negotiations	30.0d	30-Jul-24 A	10-Sep-24 A	
999	DS-CC-SD-1400	BNP Executed Agreement	1.0d	11-Sep-24 A	11-Sep-24 A	
1000	WBS - CCBS - TSA Predesign BNP		29.0d	12-Sep-24 A	22-Oct-24 A	
1001	WBS - CCBS - TSA Predesign - BNP Documents		29.0d	12-Sep-24 A	22-Oct-24 A	
1002	DS-CC-SD-1410	CCBS Coord. & Review Exist. Docs. - CCBS TSA Predesign	10.0d	12-Sep-24 A	25-Sep-24 A	
1003	DS-CC-SD-1510	Concept Design & CCBS Model - CCBS TSA Predesign	8.0d	26-Sep-24 A	7-Oct-24 A	
1004	DS-CC-SD-1520	Mtg. With TSA - Question Predesign Subm. Requirements - CCBS TSA Predesign	1.0d	8-Oct-24 A	8-Oct-24 A	
1005	DS-CC-SD-1530	Submit Analysis of Predesign to TSA Per Mtg. - CCBS TSA Predesign	1.0d	8-Oct-24 A	8-Oct-24 A	
1006	DS-CC-SD-1540	TSA Comments Received - CCBS TSA Predesign	3.0d	9-Oct-24 A	11-Oct-24 A	
1007	DS-CC-SD-1550	BNP Response to Comments - CCBS TSA Predesign	3.0d	14-Oct-24 A	16-Oct-24 A	
1008	DS-CC-SD-1560	TSA Acceptance of Predesign Analysis - CCBS TSA Predesign	4.0d	17-Oct-24 A	22-Oct-24 A	

	ID	Name	Dur	Start	Finish	TF
1009	WBS - CCBS - TSA Schematic Design		64.0d	22-Oct-24 A	23-Jan-25 A	
1010	WBS - CCBS - TSA Schematic Design Documents		21.0d	22-Oct-24 A	19-Nov-24 A	
1011	DS-CC-SD-1570	TSA Acceptance of Predesign Analysis - CCBS TSA DD	1.0d	22-Oct-24 A	22-Oct-24 A	
1012	DS-CC-SD-1580	CCBS Schematic Design & Development - CCBS TSA DD	10.0d	23-Oct-24 A	5-Nov-24 A	
1013	DS-CC-SD-1590	Incorporate TSA Comments - CCBS TSA DD	7.0d	23-Oct-24 A	31-Oct-24 A	
1014	DS-CC-SD-1600	Complete Schematic Design - CCBS TSA DD	10.0d	6-Nov-24 A	19-Nov-24 A	
1015	WBS - CCBS - TSA Schematic Design QA/QC		20.0d	20-Nov-24 A	19-Dec-24 A	
1016	DS-CC-SD-1640	BNP Internal Review - DQC - CCBS TSA Schematic Design	4.0d	20-Nov-24 A	26-Nov-24 A	
1017	DS-CC-SD-1660	IDR - CCBS Predesign Document - Incorporate Comments - Include HCAA - CC...	5.0d	27-Nov-24 A	4-Dec-24 A	
1018	DS-CC-SD-1690	Prepare Docs. For HCAA Review - CCBS TSA Schematic Design	3.0d	9-Dec-24 A	11-Dec-24 A	
1019	DS-CC-SD-1710	HCAA Review - CCBS TSA Schematic Design	1.0d	12-Dec-24 A	12-Dec-24 A	
1020	DS-CC-SD-1720	HCAA Comment Resolution - CCBS TSA Schematic Design	1.0d	13-Dec-24 A	13-Dec-24 A	
1021	DS-CC-SD-1740	Pick Up Comments - CCBS TSA Schematic Design	2.0d	16-Dec-24 A	17-Dec-24 A	
1022	DS-CC-SD-1760	Visual Check - CCBS TSA Schematic Design	1.0d	18-Dec-24 A	18-Dec-24 A	
1023	DS-CC-SD-1780	QA - CCBS TSA Schematic Design	1.0d	19-Dec-24 A	19-Dec-24 A	
1024	WBS - CCBS - TSA Schematic Design Submittal		23.0d	20-Dec-24 A	23-Jan-25 A	
1025	DS-CC-SD-1800	Docs. Complete & Assemble Pkg. - TSA SD Subm.	1.0d	20-Dec-24 A	20-Dec-24 A	
1026	DS-CC-SD-1810	CBIS Schematic Design to TSA - TSA SD Subm.	1.0d	23-Dec-24 A	23-Dec-24 A	
1027	DS-CC-SD-1820	SD Review - TSA SD Subm.	21.0d	24-Dec-24 A	23-Jan-25 A	
1028	WBS - CCBS - TSA 30% Design - 3rd Submittal		88.0d	24-Dec-24 A	28-Apr-25 A	
1029	WBS - CCBS - TSA 30% Design - 3rd Submittal		33.0d	24-Dec-24 A	10-Feb-25 A	
1030	DS-CC-SD-1830	Design Development - TSA 30% Design	31.0d	24-Dec-24 A	6-Feb-25 A	
1031	DS-CC-SD-1840	MEP / FP Coord. & Docs. - TSA 30% Design	31.0d	24-Dec-24 A	6-Feb-25 A	
1032	DS-CC-SD-1850	Incorporate TSA Comments. - TSA 30% Design	10.0d	24-Jan-25 A	6-Feb-25 A	
1033	DS-CC-SD-1860	Complete Docs. - TSA 30% Design	2.0d	7-Feb-25 A	10-Feb-25 A	
1034	WBS - CCBS - TSA 30% Design QA/QC		23.0d	11-Feb-25 A	13-Mar-25 A	
1035	DS-CC-SD-1870	BNP Internal Review - DQC - TSA 30% Design	5.0d	11-Feb-25 A	17-Feb-25 A	
1036	DS-CC-SD-1880	IDR Predesign Document - Incorporate Comments - Include HCAA - TSA 30% ...	5.0d	18-Feb-25 A	24-Feb-25 A	
1037	DS-CC-SD-1890	Prepare Docs. for HCAA Review - TSA 30% Design	5.0d	25-Feb-25 A	3-Mar-25 A	
1038	DS-CC-SD-1900	HCAA Over the Shoulder Review - TSA 30% Design	1.0d	4-Mar-25 A	4-Mar-25 A	
1039	DS-CC-SD-1910	HCAA Comment Resolution - TSA 30% Design	1.0d	5-Mar-25 A	5-Mar-25 A	
1040	DS-CC-SD-1920	Pick Up Comments - TSA 30% Design	2.0d	6-Mar-25 A	7-Mar-25 A	
1041	DS-CC-SD-1930	Visual Check QA/QC - TSA 30% Design	2.0d	10-Mar-25 A	11-Mar-25 A	
1042	DS-CC-SD-1940	CCBS - TSA 30% Design	2.0d	12-Mar-25 A	13-Mar-25 A	
1043	WBS - CCBS - TSA 30% Design Submittal		32.0d	14-Mar-25 A	28-Apr-25 A	
1044	DS-CC-SD-1950	Sub. Complete & Assemble Docs. - TSA 30% Design	1.0d	14-Mar-25 A	14-Mar-25 A	
1045	DS-CC-SD-1960	CBIS Deliverable Due - TSA 30% Design	1.0d	17-Mar-25 A	17-Mar-25 A	
1046	DS-CC-SD-1970	Review - TSA 30% Design	30.0d	18-Mar-25 A	28-Apr-25 A	
1047	WBS - CCBS - 70% Design - Main Terminal		142.0d	17-Mar-25 A	3-Oct-25 A	
1048	DS-CC-DD-90	CCBS 70% DD NTP - Main Terminal	0.0d	17-Mar-25 A		
1049	WBS - CCBS - Main Terminal (70% BHS to TSA) Design Documents		86.0d	17-Mar-25 A	16-Jul-25 A	
1050	DS-CC-DD-150	Architectural Design - Coord. (70% Subm. to TSA)	52.0d	17-Mar-25 A	28-May-25 A	


	ID	Name	Dur	Start	Finish	TF
1051	DS-CC-DD-160	Struct. Design - Coord. (70% Subm. to TSA)	52.0d	17-Mar-25 A	28-May-25 A	
1052	DS-CC-DD-100	CCBS Coord. Assist with BNP & Contractor - Development to TSA 70%	57.0d	25-Apr-25 A	16-Jul-25 A	
1053	DS-CC-DD-220	Incorporate TSA Comments From 30%	20.0d	25-Apr-25 A	22-May-25 A	
1054	WBS - CCBS - Main Terminal (70% BHS to TSA) Review QA/QC		24.0d	17-Jul-25 A	19-Aug-25 A	
1055	DS-CC-DD-230	DQC 0 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
1056	DS-CC-DD-225	Start QA/QC 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	0.0d	17-Jul-25 A		
1057	DS-CC-DD-250	Post to Bluebeam 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	1.0d	29-Jul-25 A	29-Jul-25 A	
1058	DS-CC-DD-260	IDR 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
1059	DS-CC-DD-300	Visual Check 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
1060	DS-CC-DD-270	Prepare Docs. for Over the Shoulder Review 70% Subm. to TSA - CCBS (70% B...	1.0d	14-Aug-25 A	14-Aug-25 A	
1061	DS-CC-DD-280	HCAA Over the Shoulder Review 70% Subm. to TSA - CCBS (70% BHS to TSA) ...	1.0d	15-Aug-25 A	15-Aug-25 A	
1062	DS-CC-DD-310	QA Check 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
1063	WBS - CCBS - Main Terminal (70% BHS to TSA) Submittal		32.0d	20-Aug-25 A	3-Oct-25 A	
1064	DS-CC-DD-320	Complete Docs. & Assemble Package - CCBS 70% Subm. to TSA	1.0d	20-Aug-25 A	20-Aug-25 A	
1065	DS-CC-DD-340	TSA - CBIS 70% Subm. Due - CCBS 70% Subm. to TSA	1.0d	21-Aug-25 A	21-Aug-25 A	
1066	DS-CC-DD-360	TSA Review - CCBS 70% Subm. to TSA	20.0d	22-Aug-25 A	19-Sep-25 A	
1067	DS-CC-DD-370	Respond to Comments - CCBS 70% Subm. to TSA	5.0d	22-Sep-25 A	26-Sep-25 A	
1068	DS-CC-DD-380	Incorporate TSA & HCAA Comments - CCBS 70% Subm. to TSA	4.0d	29-Sep-25 A	3-Oct-25 A	
1069	DS-CC-DD-390	Submit HCAA 90% Pkg. (TSA 70%) - CCBS 70% Subm. to TSA	0.0d		3-Oct-25 A	
1070	WBS - CCBS - 100% Construction Documents - CCBS Main Terminal		73.0d	21-Aug-25 A	5-Dec-25 A	
1071	WBS - CCBS - 100% NTP		1.0d	21-Aug-25 A	21-Aug-25 A	
1072	DS-CC-CD-2200	NTP - CCBS Main Terminal CCBS 100% CD	0.0d	21-Aug-25 A	21-Aug-25 A	
1073	WBS - CCBS - 100% CCBS Docs to TSA/HCAA		30.0d	22-Aug-25 A	3-Oct-25 A	
1074	DS-CC-CD-90	TSA Review - 100% CCBS to TSA	20.0d	22-Aug-25 A	19-Sep-25 A	
1075	DS-CC-CD-100	Design - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
1076	DS-CC-CD-110	Architectural Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
1077	DS-CC-CD-120	MEP Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
1078	DS-CC-CD-130	Struct. Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
1079	WBS - CCBS - 100% Review QA/QC (100% CCBS To TSA/HCAA)		17.0d	6-Oct-25 A	28-Oct-25 A	
1080	DS-CC-CD-210	DQC - 100% Review QA/QC (100% CCBS To TSA)	5.0d	6-Oct-25 A	10-Oct-25 A	
1081	DS-CC-CD-220	3rd Party Review - 100% Review QA/QC (100% CCBS To TSA)	5.0d	6-Oct-25 A	10-Oct-25 A	
1082	DS-CC-CD-230	Post to Bluebeam - 100% Review QA/QC (100% CCBS To TSA)	1.0d	13-Oct-25 A	13-Oct-25 A	
1083	DS-CC-CD-240	IDR - 100% Review QA/QC (100% CCBS To TSA)	8.0d	14-Oct-25 A	23-Oct-25 A	
1084	DS-CC-CD-250	Visual Check - 100% Review QA/QC (100% CCBS To TSA)	2.0d	24-Oct-25 A	27-Oct-25 A	
1085	DS-CC-CD-260	QA Check - 100% Review QA/QC (100% CCBS To TSA)	1.0d	28-Oct-25 A	28-Oct-25 A	
1086	WBS - CCBS - 100% Submittal (100% CCBS To TSA/HCAA)		26.0d	29-Oct-25 A	5-Dec-25 A	
1087	DS-CC-CD-270	Complete Docs. & Assemble Pkg. - 100% Submittal (100% CCBS To TSA)	2.0d	29-Oct-25 A	30-Oct-25 A	
1088	DS-CC-CD-1240	HCAA - CBIS 100% Subm. Due - 100% Submittal (100% CCBS To TSA)	1.0d	30-Oct-25 A	30-Oct-25 A	
1089	DS-CC-CD-290	HCAA Review - 100% Submittal (100% CCBS To TSA)	19.0d	31-Oct-25 A	26-Nov-25 A	
1090	DS-CC-CD-285	HNTB to Submit to the City of Tampa (COT) - 100% Submittal (100% CCBS To T...	1.0d	7-Nov-25 A	7-Nov-25 A	
1091	DS-CC-CD-2320	Respond to Comments - 100% CCBS	5.0d	1-Dec-25 A	5-Dec-25 A	
1092	WBS - BHS - 30% Design Documents - ASD		181.0d	19-Apr-24 A	6-Jan-25 A	

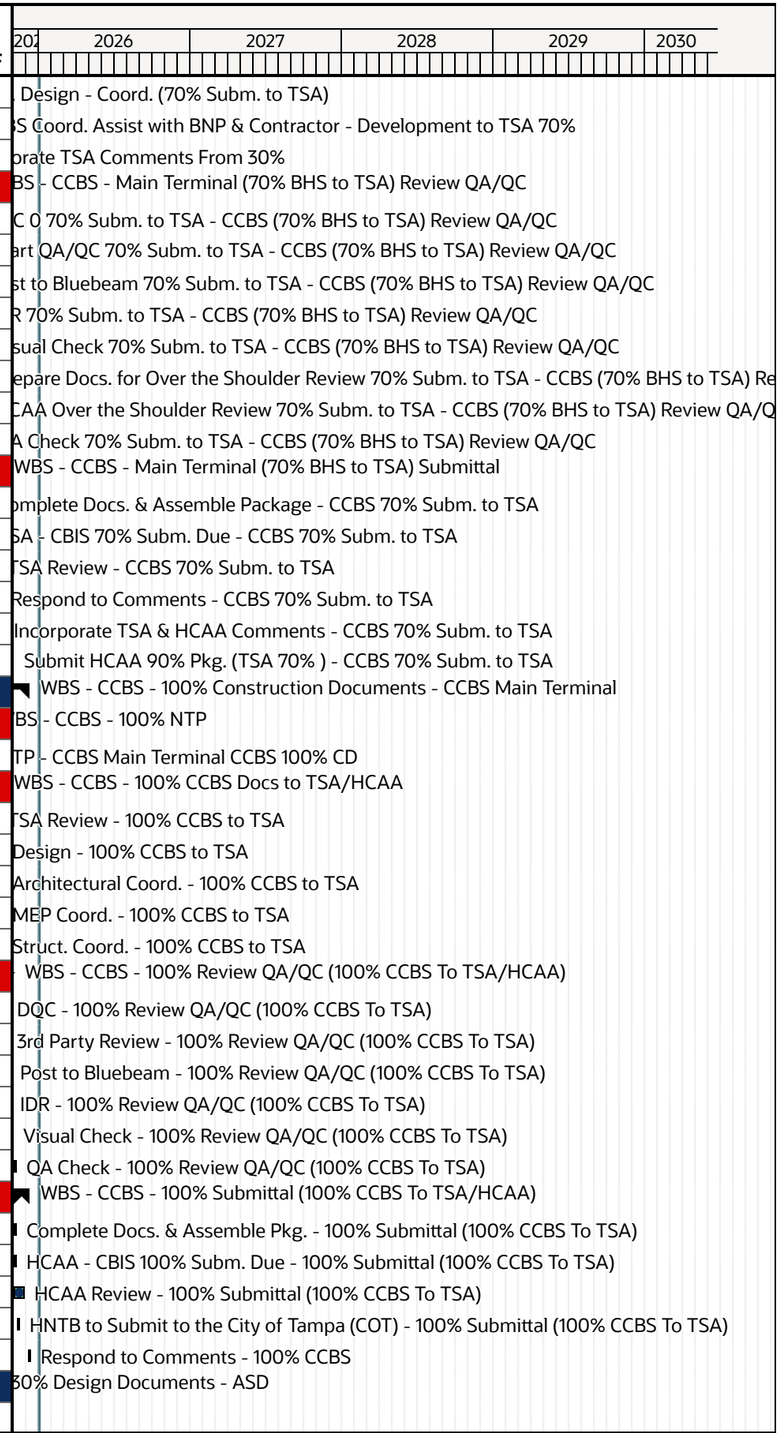


	ID	Name	Dur	Start	Finish	TF
1093	WBS - BHS - 30% Design Docs - ASD		92.0d	19-Apr-24 A	27-Aug-24 A	
1094	WBS - BHS - 30% Document Start - ASD		68.0d	19-Apr-24 A	24-Jul-24 A	
1095	DS-SD-BHS-1060	BHS Schematic Design At Airside D - Start 30%	1.0d	19-Apr-24 A	19-Apr-24 A	
1096	DS-SD-BHS-1180	BHS Restart On 30% Airside D Design	1.0d	10-Jun-24 A	10-Jun-24 A	
1097	DS-SD-BHS-1190	BHS Revise 30% BOD - ASD	31.0d	11-Jun-24 A	24-Jul-24 A	
1098	WBS - BHS Revised BOD Review QA/QC		12.0d	25-Jul-24 A	9-Aug-24 A	
1099	DS-SD-BHS-1250	Sr. Technical Review Discipline QC - BHS 30% BOD	3.0d	25-Jul-24 A	29-Jul-24 A	
1100	DS-SD-BHS-1260	DQC - Post Docs. - BHS 30% BOD	1.0d	25-Jul-24 A	25-Jul-24 A	
1101	DS-SD-BHS-1270	DQC - BHS 30% BOD	2.0d	26-Jul-24 A	29-Jul-24 A	
1102	DS-SD-BHS-1290	Post Docs. to Bluebeam Session/IDR Review - BHS 30% BOD	1.0d	30-Jul-24 A	30-Jul-24 A	
1103	DS-SD-BHS-1320	Basis of Design QA/QC - IDR - BHS 30% BOD	5.0d	31-Jul-24 A	6-Aug-24 A	
1104	DS-SD-BHS-1330	Docs. Complete - Visual Check - BHS 30% BOD	2.0d	7-Aug-24 A	8-Aug-24 A	
1105	DS-SD-BHS-1340	QAR Check - BHS 30% BOD	1.0d	9-Aug-24 A	9-Aug-24 A	
1106	WBS - BHS ASD - Revised BOD Submittal To HCAA		12.0d	12-Aug-24 A	27-Aug-24 A	
1107	DS-SD-BHS-1350	Assemble Pkg. - BHS 30% BOD	1.0d	12-Aug-24 A	12-Aug-24 A	
1108	DS-SD-BHS-1360	Submit Revised BOD Report Due To HCAA - BHS 30% BOD	1.0d	13-Aug-24 A	13-Aug-24 A	
1109	DS-SD-BHS-1370	HCAA Review - BHS 30% BOD	10.0d	14-Aug-24 A	27-Aug-24 A	
1110	WBS - BHS - 30% Design Documents Per Revised BOD - BNP		115.0d	23-Jul-24 A	6-Jan-25 A	
1111	WBS - BHS - 30% Design Documents - ASD - BNP		84.0d	23-Jul-24 A	18-Nov-24 A	
1112	DS-SD-BHS-1240	BNP Kickoff & Coord. - BHS 30% DD	4.0d	23-Jul-24 A	26-Jul-24 A	
1113	DS-SD-BHS-1280	BNP Concept Design Understanding Scope - BHS 30% DD	1.0d	29-Jul-24 A	29-Jul-24 A	
1114	DS-SD-BHS-1310	BNP Validation & Concept Study - BHS 30% DD	21.0d	30-Jul-24 A	27-Aug-24 A	
1115	DS-SD-BHS-1380	BHS Focus Team Mtg. 8/28/24 - BHS 30% DD	1.0d	28-Aug-24 A	28-Aug-24 A	
1116	DS-SD-BHS-1390	Program Docs. for Ricondo Mtg. - BHS 30% DD	9.0d	29-Aug-24 A	11-Sep-24 A	
1117	DS-SD-BHS-1420	BNP / Ricondo Centralized Baggage Mtg. 9/12/24 - BHS 30% DD	1.0d	12-Sep-24 A	12-Sep-24 A	
1118	DS-SD-BHS-1430	CBIS Design Update Mtg. 9/13/24 - BHS 30% DD	1.0d	13-Sep-24 A	13-Sep-24 A	
1119	DS-SD-BHS-1440	Architectural Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1120	DS-SD-BHS-1450	Struct. Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1121	DS-SD-BHS-1460	MEP Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1122	DS-SD-BHS-1470	Concept Plans & Model Development - BHS 30% DD	4.0d	16-Sep-24 A	19-Sep-24 A	
1123	DS-SD-BHS-1480	TSA Monthly Check in & BHS Focus Team Mtg. 9/20/24 - BHS 30% DD	1.0d	20-Sep-24 A	20-Sep-24 A	
1124	DS-SD-BHS-1500	Design Docs. - BHS 30% DD	41.0d	23-Sep-24 A	18-Nov-24 A	
1125	WBS - Preliminary Cost Estimate To HP For 30% Package		35.0d	20-Sep-24 A	7-Nov-24 A	
1126	DS-SD-BHS-1490	Basis Of Design & 30% Cost Estimate Document - BHS 30%	34.0d	20-Sep-24 A	6-Nov-24 A	
1127	DS-SD-BHS-1610	Cost Estimate Pkg. To HP - BHS 30%	1.0d	7-Nov-24 A	7-Nov-24 A	
1128	WBS - BHS - 30% Review QA/QC - ASD		19.0d	19-Nov-24 A	17-Dec-24 A	
1129	DS-SD-BHS-1620	DQC - BHS 30% Review QA/QC	4.0d	19-Nov-24 A	25-Nov-24 A	
1130	DS-SD-BHS-1630	Sr. Technical Review - BHS 30% Review QA/QC	4.0d	19-Nov-24 A	25-Nov-24 A	
1131	DS-SD-BHS-1650	Post to Bluebeam - BHS 30% Review QA/QC	1.0d	26-Nov-24 A	26-Nov-24 A	
1132	DS-SD-BHS-1680	IDR - BHS 30% Review QA/QC	10.0d	27-Nov-24 A	11-Dec-24 A	
1133	DS-SD-BHS-1700	Visual Check - BHS 30% Review QA/QC	2.0d	12-Dec-24 A	13-Dec-24 A	
1134	DS-SD-BHS-1730	QA Check - BHS 30% Review QA/QC	2.0d	16-Dec-24 A	17-Dec-24 A	

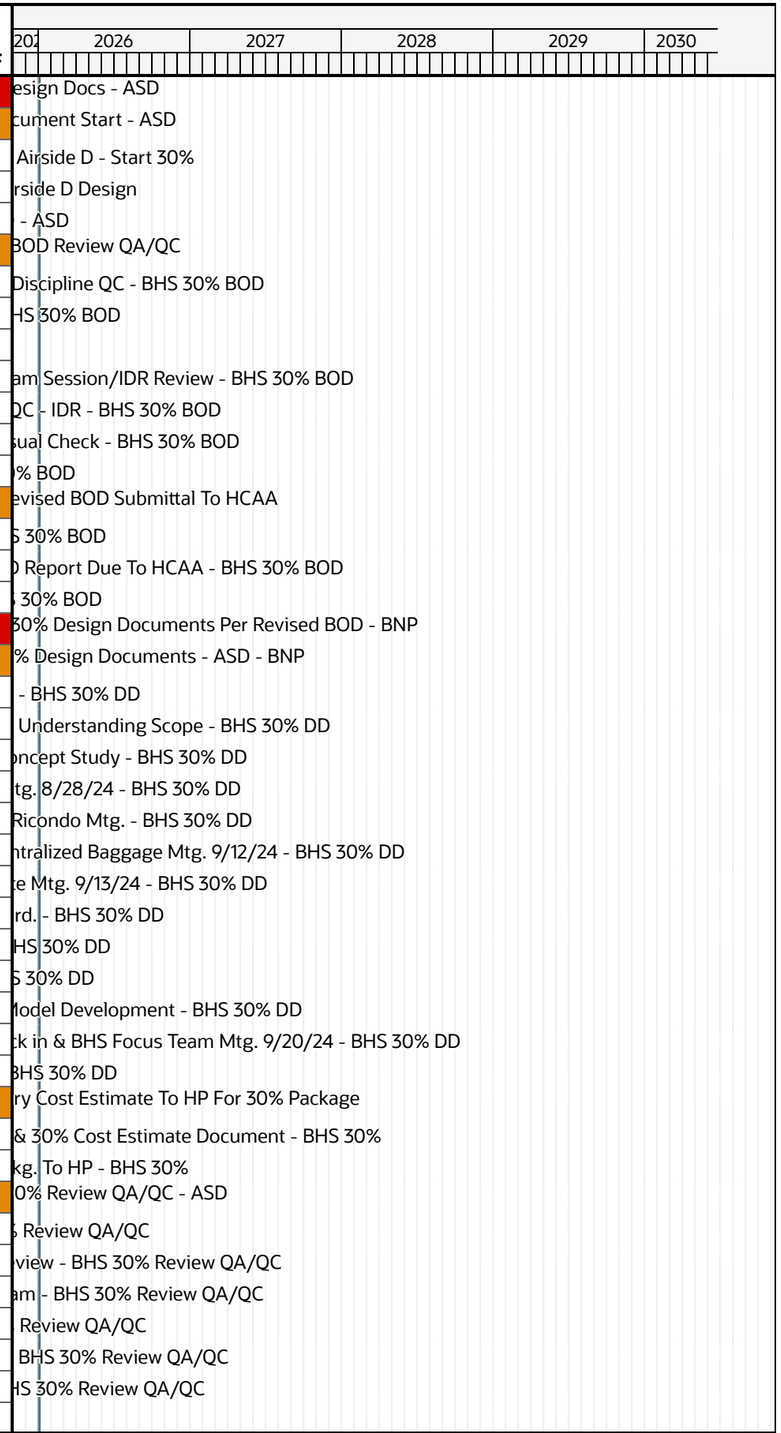

	ID	Name	Dur	Start	Finish	TF
1135	WBS - BHS - 30% Submittal To HCAA - ASD		12.0d	18-Dec-24 A	6-Jan-25 A	
1136	DS-SD-BHS-1750	Docs. Complete & Assemble Pkg. - BHS 30% Subm.	1.0d	18-Dec-24 A	18-Dec-24 A	
1137	DS-SD-BHS-1770	Airside D Subm. Due To HCAA - BHS 30% Subm.	1.0d	19-Dec-24 A	19-Dec-24 A	
1138	DS-SD-BHS-1790	HCAA Review - BHS 30% Subm.	10.0d	20-Dec-24 A	6-Jan-25 A	
1139	WBS - BHS - 60% Design Development - ASD		109.0d	19-Dec-24 A	22-May-25 A	
1140	DS-DD-BHS-10	BHS 60% DD ASD - NTP	1.0d	19-Dec-24 A	19-Dec-24 A	
1141	WBS - BHS - 60% Design Development - ASD Documents		77.0d	20-Dec-24 A	9-Apr-25 A	
1142	DS-DD-BHS-20	Develop ASD Docs. - BHS 60% Design Docs.	56.0d	20-Dec-24 A	11-Mar-25 A	
1143	DS-DD-BHS-25	Ascend Passenger Experience Extension - BHS 60% Design Docs.	20.0d	12-Mar-25 A	8-Apr-25 A	
1144	DS-DD-BHS-30	Complete & Assemble ASD Docs. - BHS 60% Design Docs.	1.0d	9-Apr-25 A	9-Apr-25 A	
1145	WBS - BHS - 60% Preliminary Cost Estimate To HP For 60% Package		2.0d	10-Apr-25 A	11-Apr-25 A	
1146	DS-DD-BHS-40	BHS 60% Basis of Design & 60% Cost Estimate Document	1.0d	10-Apr-25 A	10-Apr-25 A	
1147	DS-DD-BHS-50	BHS 60% Cost Estimate Pkg. to HP	1.0d	11-Apr-25 A	11-Apr-25 A	
1148	WBS - BHS - 60% Review QA/QC - ASD		19.0d	10-Apr-25 A	6-May-25 A	
1149	DS-DD-BHS-70	Sr. Technical Review - BHS 60% Review QA/QC ASD	5.0d	10-Apr-25 A	16-Apr-25 A	
1150	DS-DD-BHS-55	Start QA/QC - BHS 60% Review QA/QC ASD	0.0d	10-Apr-25 A		
1151	DS-DD-BHS-60	DQC - BHS 60% Review QA/QC ASD	3.0d	14-Apr-25 A	16-Apr-25 A	
1152	DS-DD-BHS-110	Post to Bluebeam Session - BHS 60% Review QA/QC ASD	1.0d	17-Apr-25 A	17-Apr-25 A	
1153	DS-DD-BHS-120	IDR - BHS 60% Review QA/QC ASD	9.0d	18-Apr-25 A	30-Apr-25 A	
1154	DS-DD-BHS-170	Visual Check - BHS 60% Review QA/QC ASD	2.0d	1-May-25 A	2-May-25 A	
1155	DS-DD-BHS-180	QA Check - BHS 60% Review QA/QC ASD	2.0d	5-May-25 A	6-May-25 A	
1156	WBS - BHS - 60% Submittal To Owner - ASD		12.0d	7-May-25 A	22-May-25 A	
1157	DS-DD-BHS-190	Docs. Complete & Assemble Pkg. - BHS 60% Subm.	1.0d	7-May-25 A	7-May-25 A	
1158	DS-DD-BHS-200	ASD - Subm. Due to HCAA - BHS 60% Subm.	1.0d	8-May-25 A	8-May-25 A	
1159	DS-DD-BHS-210	HCAA Review - BHS 60% Subm.	10.0d	9-May-25 A	22-May-25 A	
1160	WBS - BHS - 90% Design Development - ASD		84.0d	8-May-25 A	5-Sep-25 A	
1161	DS-CD-BHS-10	BHS 90% CD NTP - ASD	1.0d	8-May-25 A	8-May-25 A	
1162	WBS - BHS - 90% Design Development - ASD Documents		47.0d	9-May-25 A	16-Jul-25 A	
1163	DS-CD-BHS-20	ASD - Design Docs. - BHS 90% DD	46.0d	9-May-25 A	15-Jul-25 A	
1164	DS-CD-BHS-30	Complete & Assemble ASD Docs. - BHS 90% DD	1.0d	16-Jul-25 A	16-Jul-25 A	
1165	WBS - Preliminary Cost Estimate To HP For 90% Package		1.0d	17-Jul-25 A	17-Jul-25 A	
1166	DS-CD-BHS-40	BHS Basis Of Design & 90% Cost Estimate Document	1.0d	17-Jul-25 A	17-Jul-25 A	
1167	DS-CD-BHS-50	BHS 90% Cost Estimate Pkg. To HP	1.0d	17-Jul-25 A	17-Jul-25 A	
1168	WBS - BHS - 90% Review QA/QC - ASD		24.0d	17-Jul-25 A	19-Aug-25 A	
1169	DS-CD-BHS-60	DQC - BHS ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
1170	DS-CD-BHS-70	Sr. Technical Review - BHS ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
1171	DS-CD-BHS-140	Post to Bluebeam Session - BHS ASD 90% Review QA/QC	1.0d	29-Jul-25 A	29-Jul-25 A	
1172	DS-CD-BHS-150	IDR - BHS ASD 90% Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
1173	DS-CD-BHS-160	Visual Check - BHS ASD 90% Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
1174	DS-CD-BHS-170	QA Check - BHS ASD 90% Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
1175	WBS - BHS - 90% Submittal To HCAA - ASD		11.0d	20-Aug-25 A	5-Sep-25 A	
1176	DS-CD-BHS-180	Docs. Complete & Assemble Pkg. - BHS ASD 90% Subm.	0.0d	20-Aug-25 A	20-Aug-25 A	

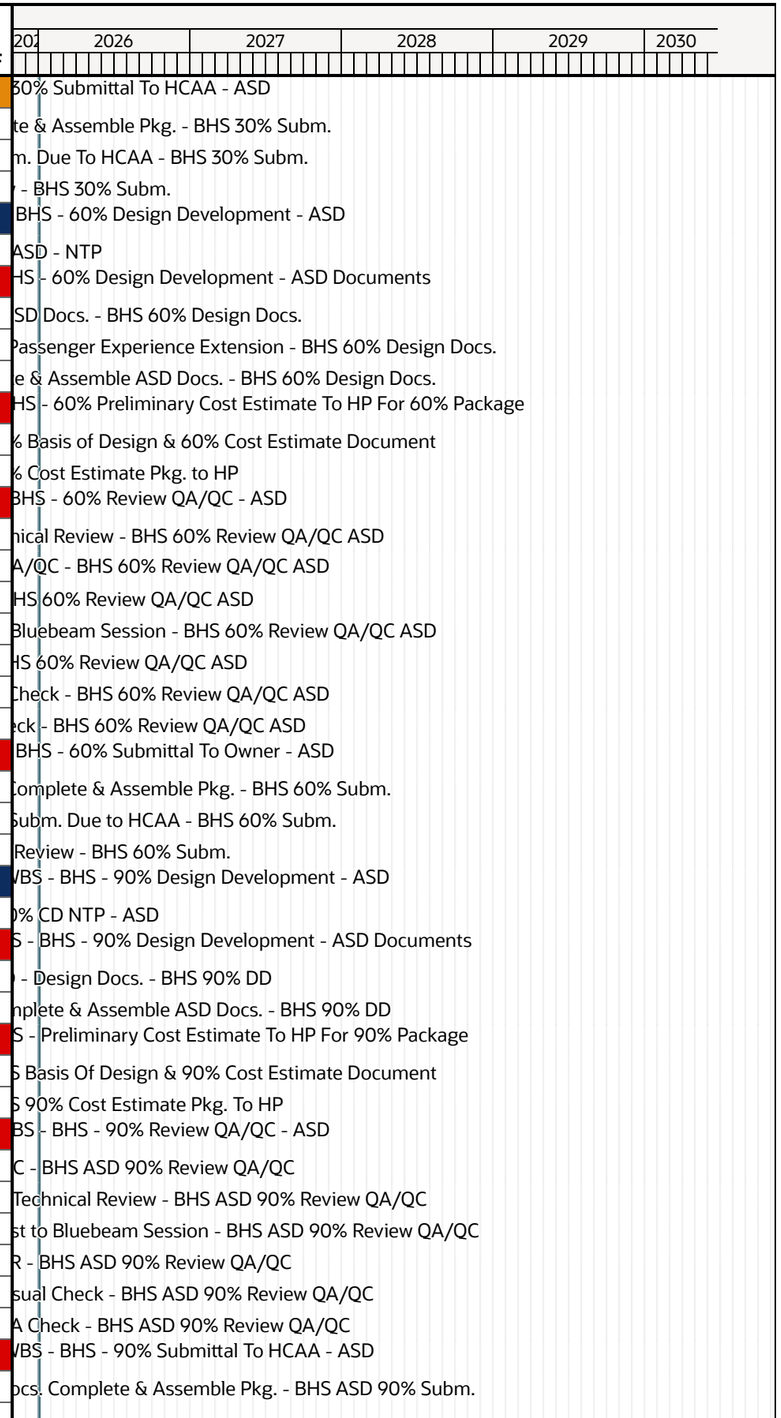

	ID	Name	Dur	Start	Finish	TF
1177	DS-CD-BHS-190	Due To HCAA - BHS ASD 90% Subm.	1.0d	21-Aug-25 A	21-Aug-25 A	
1178	DS-CD-BHS-200	HCAA Review - BHS ASD 90% Subm.	10.0d	22-Aug-25 A	5-Sep-25 A	
1179	WBS - BHS - 100% Design Development - ASD		78.0d	21-Aug-25 A	11-Dec-25 A	
1180	DS-CD-BHS-1100	BHS 100% CD NTP - ASD	0.0d	21-Aug-25 A		
1181	WBS - BHS - 100% Design Development - ASD Documents		31.0d	21-Aug-25 A	3-Oct-25 A	
1182	DS-CD-BHS-1110	ASD - Design Docs. - BHS 100% DD	30.0d	21-Aug-25 A	2-Oct-25 A	
1183	DS-CD-BHS-1130	ASD - Complete & Assemble Docs. - BHS 100% DD	1.0d	3-Oct-25 A	3-Oct-25 A	
1184	WBS - BHS - 100% Preliminary Cost Estimate to HP For 100% Package - ASD		30.0d	25-Aug-25 A	6-Oct-25 A	
1185	DS-CD-BHS-1120	BHS 100% Cost Estimate Pkg. To HP	29.0d	25-Aug-25 A	3-Oct-25 A	
1186	DS-CD-BHS-1140	Basis Of Design & BHS 100% Cost Estimate Document	1.0d	6-Oct-25 A	6-Oct-25 A	
1187	WBS - BHS - 100% Review QA/QC - ASD		17.0d	6-Oct-25 A	28-Oct-25 A	
1188	DS-CD-BHS-1150	DQC - BHS 100% Review QA/QC ASD	5.0d	6-Oct-25 A	10-Oct-25 A	
1189	DS-CD-BHS-1160	Technical Review - BHS 100% Review QA/QC ASD	5.0d	6-Oct-25 A	10-Oct-25 A	
1190	DS-CD-BHS-1170	Post to Bluebeam Session - BHS 100% Review QA/QC ASD	1.0d	13-Oct-25 A	13-Oct-25 A	
1191	DS-CD-BHS-1180	IDR - BHS 100% Review QA/QC ASD	8.0d	14-Oct-25 A	23-Oct-25 A	
1192	DS-CD-BHS-1190	Visual Check - BHS 100% Review QA/QC ASD	2.0d	24-Oct-25 A	27-Oct-25 A	
1193	DS-CD-BHS-1200	QA Check - BHS 100% Review QA/QC ASD	1.0d	28-Oct-25 A	28-Oct-25 A	
1194	WBS - BHS - 100% Submittal To HCAA - ASD		30.0d	29-Oct-25 A	11-Dec-25 A	
1195	DS-CD-BHS-1210	Docs. Complete & Assemble Pkg. - BHS 100% Subm. to HCAA	1.0d	29-Oct-25 A	29-Oct-25 A	
1196	DS-CD-BHS-1220	Subm. Due to HCAA - BHS 100% Subm. to HCAA	1.0d	30-Oct-25 A	30-Oct-25 A	
1197	DS-CD-BHS-1230	Owner Review - 100% BHS Submittal	10.0d	26-Nov-25 A	11-Dec-25 A	
1198	WBS - ITB's - 30%		77.0d	8-Jul-24 A	23-Oct-24 A	
1199	WBS - APN - ITB 1 - 30% Site Utilities, Paving, Fueling		69.0d	18-Jul-24 A	23-Oct-24 A	
1200	WBS - APN - ITB 1 - 30% Site Design Documents		52.0d	18-Jul-24 A	30-Sep-24 A	
1201	DS-SD-ITB1-AP-10	Site Civil Paving Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1202	DS-SD-ITB1-AP-20	Site Civil Airfield LTNG Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1203	DS-SD-ITB1-AP-30	Site Civil Drainage Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1204	DS-SD-ITB1-AP-40	Site Civil Hydrant Fueling Design ITB1 30% Site Utilities - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1205	DS-SD-ITB1-AP-50	Preliminary Set to HP For Cost Estimating - APN - ITB1 30% DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1206	WBS - APN - ITB 1 - 30% QA/QC		10.0d	16-Sep-24 A	27-Sep-24 A	
1207	DS-SD-ITB1-AP-60	DQC - APN - ITB1 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1208	DS-SD-ITB1-AP-70	Sr. Technical Review - APN - ITB1 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1209	DS-SD-ITB1-AP-80	IDR - APN - ITB1 30% QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1210	DS-SD-ITB1-AP-90	Site Utilities, Paving & Fueling Visual Check - APN - ITB1 30% QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1211	DS-SD-ITB1-AP-100	Site Utilities, Paving & Fueling QA Check - APN - ITB1 30% QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1212	WBS - APN - ITB 1 - 30% Submittal To HCAA		18.0d	30-Sep-24 A	23-Oct-24 A	
1213	DS-SD-ITB1-AP-110	Docs. Complete & Assemble Pkg. - APN - ITB1 30% Subm. QA/QC	1.0d	30-Sep-24 A	30-Sep-24 A	
1214	DS-SD-ITB1-AP-120	Due To HCAA - APN - ITB1 30% Subm. QA/QC	1.0d	1-Oct-24 A	1-Oct-24 A	
1215	DS-SD-ITB1-AP-130	HCAA Review - APN - ITB1 30% Subm. QA/QC	10.0d	2-Oct-24 A	15-Oct-24 A	
1216	DS-SD-ITB1-AP-140	Comment Resolution Mtg. - APN - ITB1 30% Subm. QA/QC	1.0d	23-Oct-24 A	23-Oct-24 A	
1217	WBS - ASD - ITB 2 - 30% PBB Design		69.0d	18-Jul-24 A	23-Oct-24 A	
1218	WBS - ASD - ITB 2 - 30% PBB Design Documents		52.0d	18-Jul-24 A	30-Sep-24 A	

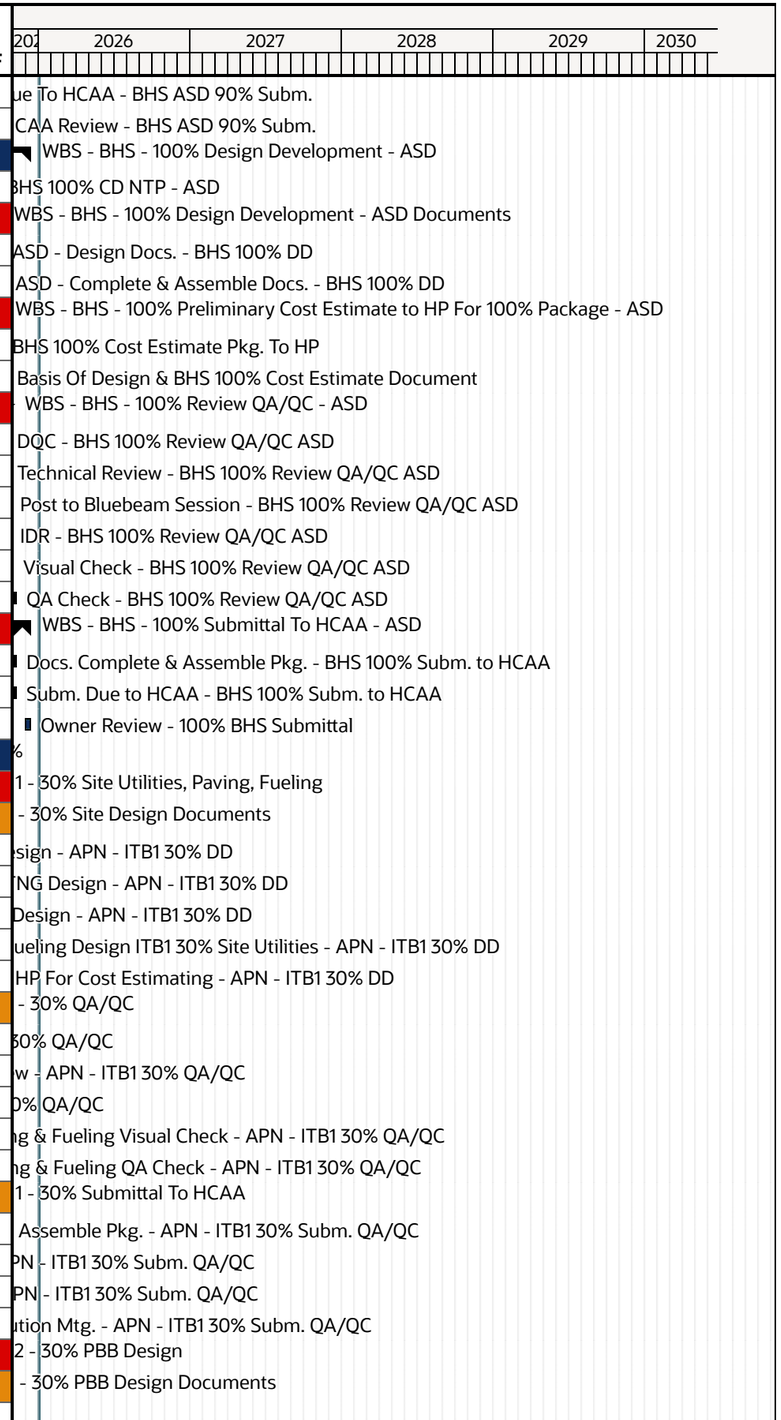


	ID	Name	Dur	Start	Finish	TF
1219	DS-SD-ITB2-PB-10	Architectural Design - ASD ITB 2 30% PBB DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1220	DS-SD-ITB2-PB-20	Struct. Design - ASD ITB 2 30% PBB DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1221	DS-SD-ITB2-PB-30	Preliminary Set To HP For Cost Estimating - ASD ITB 2 30% PBB DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1222	WBS - ASD - ITB 2 - 30% QA/QC		10.0d	16-Sep-24 A	27-Sep-24 A	
1223	DS-SD-ITB2-PB-40	DQC - ASD ITB 2 30% PBB QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1224	DS-SD-ITB2-PB-50	Sr. Technical Review - ASD ITB 2 30% PBB QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1225	DS-SD-ITB2-PB-60	IDR - ASD ITB 2 30% PBB QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1226	DS-SD-ITB2-PB-70	Visual Check - ASD ITB 2 30% PBB QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1227	DS-SD-ITB2-PB-80	QA Check - ASD ITB 2 30% PBB QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1228	WBS - ASD - ITB 2 - 30% Submittal To HCAA		18.0d	30-Sep-24 A	23-Oct-24 A	
1229	DS-SD-ITB2-PB-90	Docs. Complete & Assemble Pkg. - ASD ITB 2 30% Subm.	1.0d	30-Sep-24 A	30-Sep-24 A	
1230	DS-SD-ITB2-PB-100	Due To HCAA - ASD ITB 2 30% Subm.	1.0d	1-Oct-24 A	1-Oct-24 A	
1231	DS-SD-ITB2-PB-110	HCAA Review - ASD ITB 2 30% Subm.	10.0d	2-Oct-24 A	15-Oct-24 A	
1232	DS-SD-ITB2-PB-120	Comment Resolution Mtg. - ASD ITB 2 30% Subm.	1.0d	23-Oct-24 A	23-Oct-24 A	
1233	WBS - GDY - ITB 3 - 30% Guideway		77.0d	8-Jul-24 A	23-Oct-24 A	
1234	WBS - GDY - ITB 3 - 30% Guideway Design Documents		60.0d	8-Jul-24 A	30-Sep-24 A	
1235	DS-SD-ITB3-GS-10	Architectural Design - GDY ITB3 30% DD	49.0d	8-Jul-24 A	13-Sep-24 A	
1236	DS-SD-ITB3-GS-20	Struct. Design - GDY ITB3 30% DD	49.0d	8-Jul-24 A	13-Sep-24 A	
1237	DS-SD-ITB3-GS-30	Preliminary Set to HP For Cost Estimating - GDY ITB3 30% DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1238	WBS - GDY - ITB 3 - 30% QA/QC		10.0d	16-Sep-24 A	27-Sep-24 A	
1239	DS-SD-ITB3-GS-40	DQC - GDY ITB3 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1240	DS-SD-ITB3-GS-50	Sr. Technical Review - GDY ITB3 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1241	DS-SD-ITB3-GS-60	IDR - GDY ITB3 30% QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1242	DS-SD-ITB3-GS-70	Visual Check - GDY ITB3 30% QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1243	DS-SD-ITB3-GS-80	QA Check - GDY ITB3 30% QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1244	WBS - GDY - ITB 3 - 30% Submittal To HCAA		18.0d	30-Sep-24 A	23-Oct-24 A	
1245	DS-SD-ITB3-GS-90	Docs. Complete & Assemble Pkg. - GDY ITB3 30% Subm.	1.0d	30-Sep-24 A	30-Sep-24 A	
1246	DS-SD-ITB3-GS-100	Due To HCAA - GDY ITB3 30% Subm.	1.0d	1-Oct-24 A	1-Oct-24 A	
1247	DS-SD-ITB3-GS-110	HCAA Review - GDY ITB3 30% Subm.	10.0d	2-Oct-24 A	15-Oct-24 A	
1248	DS-SD-ITB3-GS-120	Comment Resolution Mtg. - GDY ITB3 30% Subm.	1.0d	23-Oct-24 A	23-Oct-24 A	
1249	WBS - ITB's - IFB/90% Submittal		87.0d	23-Dec-24 A	24-Apr-25 A	
1250	WBS - APN - ITB 1 - 90% - Paving - Hydrant Fueling		72.0d	23-Dec-24 A	3-Apr-25 A	
1251	WBS - APN - ITB 1 - 90% - Design Documents		61.0d	23-Dec-24 A	19-Mar-25 A	
1252	DS-CD-ITB1-AP-1120	Civil - Design Docs. - APN - ITB1 90% Paving /Hydrant Fueling	40.0d	23-Dec-24 A	18-Feb-25 A	
1253	DS-CD-ITB1-AP-10	Paving Design - Final Paving Decision ASD vs. ITB - APN - ITB1 90% Paving /H...	7.0d	17-Jan-25 A	27-Jan-25 A	
1254	DS-CD-ITB1-AP-20	Incorporate Comments ITB1 90% - APN - ITB1 90% Paving /Hydrant Fueling	16.0d	17-Jan-25 A	7-Feb-25 A	
1255	DS-CD-ITB1-AP-1130	Civil Focus Team Coord. Mtg. - No Comments After 2.12.25 - APN - ITB1 90% ...	3.0d	10-Feb-25 A	12-Feb-25 A	
1256	DS-CD-ITB1-AP-1160	Finalize Design Docs. - APN - ITB1 90% Paving /Hydrant Fueling	11.0d	13-Feb-25 A	27-Feb-25 A	
1257	DS-CD-ITB1-AP-40	Preliminary Set To HP For Cost Estimating - APN - ITB1 90% Paving /Hydrant F...	22.0d	18-Feb-25 A	19-Mar-25 A	
1258	DS-CD-ITB1-AP-30	P&D Provides Procurement with Front End Inf. - APN - ITB1 90% Paving /Hydra...	0.0d	25-Feb-25 A	25-Feb-25 A	
1259	DS-CD-ITB1-AP-1140	Solicitation Docs. (Front End) - APN - ITB1 90% Paving /Hydrant Fueling	15.0d	26-Feb-25 A	18-Mar-25 A	
1260	DS-CD-ITB1-AP-1150	Solicitation Docs. To Legal - APN - ITB1 90% Paving /Hydrant Fueling	1.0d	19-Mar-25 A	19-Mar-25 A	

	ID	Name	Dur	Start	Finish	TF
1261	WBS - APN - ITB 1 - 90% - Review QA/QC		13.0d	28-Feb-25 A	18-Mar-25 A	
1262	DS-CD-ITB1-AP-50	DQC - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	28-Feb-25 A	6-Mar-25 A	
1263	DS-CD-ITB1-AP-60	Sr. Technical Review - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	28-Feb-25 A	6-Mar-25 A	
1264	DS-CD-ITB1-AP-1170	Start QA/QC - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	0.0d	28-Feb-25 A		
1265	DS-CD-ITB1-AP-70	IDR - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	7-Mar-25 A	13-Mar-25 A	
1266	DS-CD-ITB1-AP-80	Visual Check - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	2.0d	14-Mar-25 A	17-Mar-25 A	
1267	DS-CD-ITB1-AP-90	QA Check - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	1.0d	18-Mar-25 A	18-Mar-25 A	
1268	WBS - APN - ITB 1 - 90% - Submittal To HCAA		12.0d	19-Mar-25 A	3-Apr-25 A	
1269	DS-CD-ITB1-AP-100	Complete Docs. & Assemble Pkg. - APN - ITB1 90% Paving /Hydrant Fueling S...	1.0d	19-Mar-25 A	19-Mar-25 A	
1270	DS-CD-ITB1-AP-110	Bid/Permit Subm. To HCAA - APN - ITB1 90% Paving /Hydrant Fueling Subm. t...	1.0d	20-Mar-25 A	20-Mar-25 A	
1271	DS-CD-ITB1-AP-120	HCAA Review - APN - ITB1 90% Paving /Hydrant Fueling Subm. to HCAA	10.0d	21-Mar-25 A	3-Apr-25 A	
1272	DS-CD-ITB1-AP-1180	Solicitation Docs. Posted for Bid - APN - ITB1 90% Paving /Hydrant Fueling Su...	1.0d	21-Mar-25 A	21-Mar-25 A	
1273	WBS - ASD - ITB 2 - 90% - PBB Design		74.0d	13-Jan-25 A	24-Apr-25 A	
1274	WBS - ASD - ITB 2 - 90% - PBB Design Documents		63.0d	13-Jan-25 A	9-Apr-25 A	
1275	DS-CD-ITB2-PB-10	Architectural Design Coord. - ASD ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1276	DS-CD-ITB2-PB-20	ASD - ITB 2 90% PBB Dsg. Docs. - Civil Coord. - ASD - ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1277	DS-CD-ITB2-PB-30	Utility Coord. - ASD ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1278	DS-CD-ITB2-PB-1150	Focus Team Coord. Mtg. - ASD ITB 2 90% PBB Dsg. Docs.	10.0d	20-Feb-25 A	5-Mar-25 A	
1279	DS-CD-ITB2-PB-1160	Front End Information & Project Description Development - ASD ITB 2 90% PB...	9.0d	6-Mar-25 A	18-Mar-25 A	
1280	DS-CD-ITB2-PB-1200	Finalize Design Docs. - ASD ITB 2 90% PBB Dsg. Docs.	10.0d	6-Mar-25 A	19-Mar-25 A	
1281	DS-CD-ITB2-PB-40	Preliminary Set to HP For Cost Estimating - ASD ITB 2 90% PBB Dsg. Docs.	22.0d	11-Mar-25 A	9-Apr-25 A	
1282	DS-CD-ITB2-PB-1170	P&D Provides Procurement with Front End Information - ASD ITB 2 90% PBB D...	1.0d	19-Mar-25 A	19-Mar-25 A	
1283	DS-CD-ITB2-PB-1180	Solicitation Docs. (Front End) - ASD ITB 2 90% PBB Dsg. Docs.	15.0d	19-Mar-25 A	8-Apr-25 A	
1284	DS-CD-ITB2-PB-1190	Solicitation Docs. to Legal - ASD ITB 2 90% PBB Dsg. Docs.	1.0d	9-Apr-25 A	9-Apr-25 A	
1285	WBS - ASD - ITB 2 - 90% - PBB Review QA/QC		14.0d	20-Mar-25 A	8-Apr-25 A	
1286	DS-CD-ITB2-PB-1140	Start QA/QC - ASD ITB 2 90% PBB Review QA/QC	1.0d	20-Mar-25 A	20-Mar-25 A	
1287	DS-CD-ITB2-PB-50	DQC - ASD ITB 2 90% PBB Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1288	DS-CD-ITB2-PB-60	Sr. Technical Review - ASD ITB 2 90% PBB Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1289	DS-CD-ITB2-PB-70	IDR - ASD ITB 2 90% PBB Review QA/QC	6.0d	28-Mar-25 A	4-Apr-25 A	
1290	DS-CD-ITB2-PB-80	Visual Check - ASD ITB 2 90% PBB Review QA/QC	1.0d	7-Apr-25 A	7-Apr-25 A	
1291	DS-CD-ITB2-PB-90	QA Check - ASD ITB 2 90% PBB Review QA/QC	1.0d	8-Apr-25 A	8-Apr-25 A	
1292	WBS - ASD - ITB 2 - 90% - PBB Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
1293	DS-CD-ITB2-PB-100	Complete Docs. & Assemble Pkg. - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
1294	DS-CD-ITB2-PB-110	Subm. to HCAA - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
1295	DS-CD-ITB2-PB-120	HCAA Review- ASD ITB 2 90% PBB Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
1296	DS-CD-ITB2-PB-1130	Solicitation Docs. Posted for Bid - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	16-Apr-25 A	16-Apr-25 A	
1297	WBS - GDY - ITB 3 - 90% - Guideway Structure		87.0d	23-Dec-24 A	24-Apr-25 A	
1298	WBS - GDY - ITB 3 - 90% - Guideway Design Documents		76.0d	23-Dec-24 A	9-Apr-25 A	
1299	DS-CD-ITB3-GS-10	Architectural Coord. & Design - GDY ITB3 90% GDWY Struct. DD	12.0d	23-Dec-24 A	9-Jan-25 A	
1300	DS-CD-ITB3-GS-20	Struct. Design - GDY ITB3 90% GDWY Struct. DD	12.0d	23-Dec-24 A	9-Jan-25 A	
1301	DS-CD-ITB3-GS-1140	Focus Team Coord. Mtg. - GDY ITB3 90% GDWY Struct. DD	13.0d	10-Jan-25 A	28-Jan-25 A	
1302	DS-CD-ITB3-GS-1190	Finalize Design Docs. - GDY ITB3 90% GDWY Struct. DD	36.0d	29-Jan-25 A	19-Mar-25 A	


	ID	Name	Dur	Start	Finish	TF
1303	DS-CD-ITB3-GS-1150	Front End Information & Project Description Development - GDY ITB3 90% GD...	4.0d	30-Jan-25 A	4-Feb-25 A	
1304	DS-CD-ITB3-GS-1160	P&D Provides Procurement with Front End Information - GDY ITB3 90% GDWY ...	1.0d	5-Feb-25 A	5-Feb-25 A	
1305	DS-CD-ITB3-GS-1170	Solicitation Docs. (Front End) - GDY ITB3 90% GDWY Struct. DD	9.0d	6-Feb-25 A	18-Feb-25 A	
1306	DS-CD-ITB3-GS-1180	Solicitation Docs. to Legal - GDY ITB3 90% GDWY Struct. DD	1.0d	19-Feb-25 A	19-Feb-25 A	
1307	DS-CD-ITB3-GS-30	Preliminary Set to HP For Cost Estimating - GDY ITB3 90% GDWY Struct. DD	22.0d	11-Mar-25 A	9-Apr-25 A	
1308	WBS - GDY - ITB 3 - 90% - Guideway Review QA/QC		14.0d	20-Mar-25 A	8-Apr-25 A	
1309	DS-CD-ITB3-GS-1130	Start QA/QC - GDY ITB3 90% GDWY Struct. Review QA/QC	0.0d	20-Mar-25 A		
1310	DS-CD-ITB3-GS-40	DQC - GDY ITB3 90% GDWY Struct. Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1311	DS-CD-ITB3-GS-50	Sr. Technical Review - GDY ITB3 90% GDWY Struct. Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1312	DS-CD-ITB3-GS-60	IDR - GDY ITB3 90% GDWY Struct. Review QA/QC	6.0d	28-Mar-25 A	4-Apr-25 A	
1313	DS-CD-ITB3-GS-70	Visual Check - GDY ITB3 90% GDWY Struct. Review QA/QC	1.0d	7-Apr-25 A	7-Apr-25 A	
1314	DS-CD-ITB3-GS-80	QA Check - GDY ITB3 90% GDWY Struct. Review QA/QC	1.0d	8-Apr-25 A	8-Apr-25 A	
1315	WBS - GDY - ITB 3 - 90% - Guideway Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
1316	DS-CD-ITB3-GS-90	Complete Docs. & Assemble Pkg. - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
1317	DS-CD-ITB3-GS-100	Bid/Permit Subm. To HCAA - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
1318	DS-CD-ITB3-GS-110	HCAA Review - GDY ITB3 90% GDWY Struct. Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
1319	DS-CD-ITB3-GS-1120	Solicitation Docs. Posted for Bid - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	16-Apr-25 A	16-Apr-25 A	
1320	WBS - ITB's - 100% (Addendum Set)		98.0d	21-Mar-25 A	7-Aug-25 A	
1321	WBS - APN - ITB 1 - 100% Paving - Hydrant Fueling (Addendum Set)		54.0d	21-Mar-25 A	5-Jun-25 A	
1322	WBS - APN - ITB 1 - 100% Paving - Design Documents		19.0d	21-Mar-25 A	16-Apr-25 A	
1323	DS-CD-ITB1-AP-1000	Civil - Paving Design - APN - ITB1 - 100% DD Paving (Addendum Set)	15.0d	21-Mar-25 A	10-Apr-25 A	
1324	DS-CD-ITB1-AP-1010	Civil - Hydrant Fueling Design Docs. - APN - ITB1 - 100% DD Paving (Addendu...	15.0d	21-Mar-25 A	10-Apr-25 A	
1325	DS-CD-ITB1-AP-1200	Bid Questions & RFI's - APN - ITB1 - 100% DD Paving (Addendum Set)	9.0d	24-Mar-25 A	3-Apr-25 A	
1326	DS-CD-ITB1-AP-1210	Pre-Bid Conference - APN - ITB1 - 100% DD Paving (Addendum Set)	1.0d	4-Apr-25 A	4-Apr-25 A	
1327	DS-CD-ITB1-AP-1220	Request for Clarification Deadline Complete - APN - ITB1 - 100% DD Paving (A...	0.0d		15-Apr-25 A	
1328	DS-CD-ITB1-AP-1230	Update Plans & Docs. - APN - ITB1 - 100% DD Paving (Addendum Set)	1.0d	16-Apr-25 A	16-Apr-25 A	
1329	DS-CD-ITB1-AP-1290	Final Addendum Posted - APN - ITB1 - 100% DD Paving (Addendum Set)	0.0d		16-Apr-25 A	
1330	WBS - APN - ITB 1 - 100% Paving - Review QA/QC		4.0d	15-Apr-25 A	18-Apr-25 A	
1331	DS-CD-ITB1-AP-1020	Hydrant Fueling - DQC - APN - ITB1 - 100% Paving (Addendum Set) Review QA...	1.0d	15-Apr-25 A	15-Apr-25 A	
1332	DS-CD-ITB1-AP-1030	Sr. Technical Review - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	16-Apr-25 A	16-Apr-25 A	
1333	DS-CD-ITB1-AP-1040	Post to Bluebeam - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	16-Apr-25 A	16-Apr-25 A	
1334	DS-CD-ITB1-AP-1015	Start QA/QC - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	0.0d	16-Apr-25 A		
1335	DS-CD-ITB1-AP-1050	IDR - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	17-Apr-25 A	17-Apr-25 A	
1336	DS-CD-ITB1-AP-1060	Visual Check - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	18-Apr-25 A	18-Apr-25 A	
1337	DS-CD-ITB1-AP-1070	QA Check - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	18-Apr-25 A	18-Apr-25 A	
1338	WBS - APN - ITB 1 - 100% Paving - Submittal To HCAA		33.0d	21-Apr-25 A	5-Jun-25 A	
1339	DS-CD-ITB1-AP-1080	Complete Docs. & Assemble Pkg. - APN - ITB1 - 100% Paving (Addendum Set) ...	1.0d	21-Apr-25 A	21-Apr-25 A	
1340	DS-CD-ITB1-AP-1090	Subm. To HCAA - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HCAA	1.0d	22-Apr-25 A	22-Apr-25 A	
1341	DS-CD-ITB1-AP-1100	ITB1 Addendum Posted for Solicitation - APN - ITB1 - 100% Paving (Addendu...	4.0d	23-Apr-25 A	28-Apr-25 A	
1342	DS-CD-ITB1-AP-1280	Contractors Bid Due - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HC...	1.0d	29-Apr-25 A	29-Apr-25 A	
1343	DS-CD-ITB1-AP-1110	HCAA Review - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HCAA	5.0d	30-Apr-25 A	6-May-25 A	
1344	DS-CD-ITB1-AP-1115	Notice of Intent to Award - APN - ITB1 - 100% Paving (Addendum Set) Subm. t...	1.0d	7-May-25 A	7-May-25 A	

	ID	Name	Dur	Start	Finish	TF
1345	DS-CD-ITB1-AP-1260	BIL Grant Application Process - APN - ITB1 - 100% Paving (Addendum Set) Sub...	10.0d	8-May-25 A	21-May-25 A	
1346	DS-CD-ITB1-AP-1265	BIL Grant Application Submitted - APN - ITB1 - 100% Paving (Addendum Set) S...	1.0d	22-May-25 A	22-May-25 A	
1347	DS-CD-ITB1-AP-1270	HCAA Board Approval - APN - ITB1 - 100% Paving (Addendum Set) Subm. to H...	1.0d	5-Jun-25 A	5-Jun-25 A	
1348	WBS - ASD - ITB 2 100% PBB Design (Addendum Set)		83.0d	11-Apr-25 A	7-Aug-25 A	
1349	WBS - ASD - ITB 2 100% - PBB Design Documents		22.0d	11-Apr-25 A	12-May-25 A	
1350	DS-CD-ITB2-PB-1000	Architectural Design Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1351	DS-CD-ITB2-PB-1010	Civil Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1352	DS-CD-ITB2-PB-1020	Utility Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1353	DS-CD-ITB2-PB-1210	Bid Questions & RFI's - ASD ITB 2 - 100% PBB DD	9.0d	17-Apr-25 A	29-Apr-25 A	
1354	DS-CD-ITB2-PB-1220	Pre-Bid Conference - ASD ITB 2 - 100% PBB DD	1.0d	30-Apr-25 A	30-Apr-25 A	
1355	DS-CD-ITB2-PB-1225	Contractor Bid Review / Submit Clarifications - ASD ITB 2 - 100% PBB DD	6.0d	1-May-25 A	8-May-25 A	
1356	DS-CD-ITB2-PB-1230	Request for Clarification Deadline - ASD ITB 2 - 100% PBB DD	1.0d	9-May-25 A	9-May-25 A	
1357	DS-CD-ITB2-PB-1240	Update Plans & Docs. - ASD ITB 2 - 100% PBB DD	1.0d	12-May-25 A	12-May-25 A	
1358	WBS - ASD - ITB 2 100% - PBB Review QA/QC		3.0d	13-May-25 A	15-May-25 A	
1359	DS-CD-ITB2-PB-1030	DQC - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1360	DS-CD-ITB2-PB-1040	Sr. Technical Review - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1361	DS-CD-ITB2-PB-1050	Post to Bluebeam - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1362	DS-CD-ITB2-PB-1025	Start QA/QC - ASD ITB 2 - 100% PBB Review QA/QC	0.0d	13-May-25 A		
1363	DS-CD-ITB2-PB-1060	IDR - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	14-May-25 A	14-May-25 A	
1364	DS-CD-ITB2-PB-1070	Visual Check - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	15-May-25 A	15-May-25 A	
1365	DS-CD-ITB2-PB-1080	QA Check - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	15-May-25 A	15-May-25 A	
1366	WBS - ASD - ITB 2 100% - PBB Submittal For Bid		58.0d	16-May-25 A	7-Aug-25 A	
1367	DS-CD-ITB2-PB-1090	Complete Docs. & Assemble Pkg. - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	16-May-25 A	16-May-25 A	
1368	DS-CD-ITB2-PB-1100	Addendum Subm. to HCAA Due - ASD ITB 2 - 100% PBB Subm. for Bid	0.0d	16-May-25 A	16-May-25 A	
1369	DS-CD-ITB2-PB-1110	ITB2 Addendum Posted for Solicitation - ASD ITB 2 - 100% PBB Subm. for Bid	4.0d	19-May-25 A	22-May-25 A	
1370	DS-CD-ITB2-PB-1120	HCAA Review - ASD ITB 2 - 100% PBB Subm. for Bid	10.0d	19-May-25 A	2-Jun-25 A	
1371	DS-CD-ITB2-PB-1260	Contractor Bids Due - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	28-May-25 A	28-May-25 A	
1372	DS-CD-ITB2-PB-1270	Notice of Intent to Award - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	3-Jun-25 A	3-Jun-25 A	
1373	DS-CD-ITB2-PB-1280	BIL Grant Application Submitted - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	4-Jun-25 A	4-Jun-25 A	
1374	DS-CD-ITB2-PB-1290	HCAA Board Approval - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	7-Aug-25 A	7-Aug-25 A	
1375	WBS - GDY - ITB 3 100% - Guideway Structure (Addendum Set)		83.0d	11-Apr-25 A	7-Aug-25 A	
1376	WBS - GDY - ITB 3 100% - Guideway Design Documents		22.0d	11-Apr-25 A	12-May-25 A	
1377	DS-CD-ITB3-GS-1000	Architectural Coord. & Design - ITB 3 100% DD	15.0d	11-Apr-25 A	1-May-25 A	
1378	DS-CD-ITB3-GS-1010	Structural Design - ITB 3 100% DD	15.0d	11-Apr-25 A	1-May-25 A	
1379	DS-CD-ITB3-GS-1200	Bid Questions & RFI's - ITB 3 100% DD	9.0d	17-Apr-25 A	29-Apr-25 A	
1380	DS-CD-ITB3-GS-1210	Pre-Bid Conference - ITB 3 100% DD	1.0d	30-Apr-25 A	30-Apr-25 A	
1381	DS-CD-ITB3-GS-1215	Contractor Bid Review/ Submit Clarifications - ITB 3 100% DD	6.0d	1-May-25 A	8-May-25 A	
1382	DS-CD-ITB3-GS-1220	Request for Clarification Deadline - ITB 3 100% DD	1.0d	9-May-25 A	9-May-25 A	
1383	DS-CD-ITB3-GS-1230	Update Plans & Docs. - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	
1384	WBS - GDY - ITB 3 100% - Guideway Review QA/QC		3.0d	12-May-25 A	14-May-25 A	
1385	DS-CD-ITB3-GS-1020	DQC - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	
1386	DS-CD-ITB3-GS-1030	Sr. Technical Review - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	


	ID	Name	Dur	Start	Finish	TF
1387	DS-CD-ITB3-GS-1015	Start QA/QC - ITB 3 100% DD	0.0d	12-May-25 A		
1388	DS-CD-ITB3-GS-1040	Post to Bluebeam - ITB 3 100% DD	0.0d		12-May-25 A	
1389	DS-CD-ITB3-GS-1050	IDR - ITB 3 100% DD	1.0d	13-May-25 A	13-May-25 A	
1390	DS-CD-ITB3-GS-1060	Visual Check - ITB 3 100% DD	1.0d	14-May-25 A	14-May-25 A	
1391	DS-CD-ITB3-GS-1070	QA Check - ITB 3 100% DD	1.0d	14-May-25 A	14-May-25 A	
1392	WBS - GDY - ITB 3 100% - Guideway Submittal For Bid		59.0d	15-May-25 A	7-Aug-25 A	
1393	DS-CD-ITB3-GS-1080	ITB 3 Complete Docs. & Assemble Pkg. - 100% Subm. for Bid	1.0d	15-May-25 A	15-May-25 A	
1394	DS-CD-ITB3-GS-1090	ITB 3 Addendum Subm. Due to HCAA - 100% Subm. for Bid	1.0d	16-May-25 A	16-May-25 A	
1395	DS-CD-ITB3-GS-1110	ITB 3 HCAA Review - 100% Subm. for Bid	9.0d	19-May-25 A	30-May-25 A	
1396	DS-CD-ITB3-GS-1095	ITB3 Resubmission of Addendum 3 - 100% Subm. for Bid	1.0d	19-May-25 A	19-May-25 A	
1397	DS-CD-ITB3-GS-1100	ITB3 Addendum Posted for Solicitation - 100% Subm. for Bid	5.0d	20-May-25 A	27-May-25 A	
1398	DS-CD-ITB3-GS-1250	ITB 3 Contractor Bids Due - 100% Subm. for Bid	1.0d	30-May-25 A	30-May-25 A	
1399	DS-CD-ITB3-GS-1260	ITB 3 Notice of Intent to Award - 100% Subm. for Bid	1.0d	2-Jun-25 A	2-Jun-25 A	
1400	DS-CD-ITB3-GS-1270	ITB 3 BIL Grant Application Submitted - 100% Subm. for Bid	1.0d	3-Jun-25 A	3-Jun-25 A	
1401	DS-CD-ITB3-GS-1280	ITB 3 HCAA Board Approval - 100% Subm. for Bid	1.0d	7-Aug-25 A	7-Aug-25 A	
1402	WBS - ASD Bulletin - LED Digital Technology Updates		583.0d	10-Nov-25 A	28-Feb-28	247.0d
1403	WBS - ASD - Bulletin - LED Digital Technology Updates - Design Development		583.0d	10-Nov-25 A	28-Feb-28	247.0d
1404	ASD-Bull-DT-290	HP/HNTB Prepare & Submit Proposal - ASD Bulletin - LED Dig. Tech. Upd.	9.0d	10-Nov-25 A	20-Nov-25 A	
1405	ASD-Bull-DT-310	HCAA Review & Approve Proposal - ASD Bulletin - LED Dig. Tech. Upd.	10.0d	26-Nov-25 A	11-Dec-25 A	
1406	ASD-Bull-DT-090	NTP - ASD - Bulletin - LED Dig. Tech. Upd.	1.0d	12-Dec-25 A	12-Dec-25 A	
1407	ASD-Bull-DT-100	Develop Design Documents - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	309.0d
1408	ASD-Bull-DT-330	HCAA RFQ Award Content Designers - ASD - Bulletin - LED Dig. Tech. Upd.	200.0d	15-Dec-25 A	25-Sep-26	247.0d
1409	ASD-Bull-DT-320	HCAA RFQ Purchase Gear, Panels, Equip. - ASD - Bulletin - LED Dig. Tech. Upd.	40.0d	28-Sep-26	20-Nov-26	309.0d
1410	ASD-Bull-DT-350	HCAA Design LED Content - ASD - Bulletin - LED Dig. Tech. Upd.	360.0d	28-Sep-26	28-Feb-28	247.0d
1411	ASD-Bull-DT-340	HCAA Fab. & Ship Panels LEDs - ASD - Bulletin - LED Dig. Tech. Upd.	224.0d	21-Nov-26	10-Jul-27	433.0d
1412	ASD-Bull-DT-370	HCAA Fab. & Ship Hardware LEDs - ASD - Bulletin - LED Dig. Tech. Upd.	55.0d	12-Jun-27	7-Aug-27	547.0d
1413	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades		258.0d	10-Nov-25 A	13-Nov-26	582.0d
1414	WBS - ASD Bulletin - FIS Elevator Tower Finish Upgrades Design Development		258.0d	10-Nov-25 A	13-Nov-26	582.0d
1415	ASD-Bull-ET-50	HP/HNTB Prepare & Submit Proposal - ASD Bulletin - FIS Elevator Tower Finish ...	131.0d	10-Nov-25 A	15-May-26	582.0d
1416	ASD-Bull-ET-60	HCAA Review & Approve Proposal - ASD Bulletin - FIS Elevator Tower Finish Up...	10.0d	18-May-26	1-Jun-26	582.0d
1417	ASD-Bull-ET-10	NTP - ASD Bulletin - FIS Elevator Tower Finish Upgrades	1.0d	2-Jun-26	2-Jun-26	582.0d
1418	ASD-Bull-ET-20	Develop Design Documents - ASD Bulletin - FIS Elevator Tower Finish Upgrades	116.0d	3-Jun-26	13-Nov-26	582.0d
1419	WBS - ASD - North Craft Parking Lot		48.0d	14-Oct-25 A	22-Dec-25 A	
1420	ASD-Bull-ET-70	Crisdel/HP Prepare & Submit 100% DD Proposal - ASD Bulletin - Craft Parking ...	14.0d	14-Oct-25 A	31-Oct-25 A	
1421	ASD-Bull-ET-90	HCAA Review & Approval Proposal - ASD Bulletin - Craft Parking Lot	4.0d	18-Nov-25 A	21-Nov-25 A	
1422	ASD-Bull-ET-110	Contract Development & Finalization - ASD Bulletin - Craft Parking Lot	5.0d	19-Nov-25 A	25-Nov-25 A	
1423	ASD-Bull-ET-100	Draft & Issue LOI - ASD Bulletin - Craft Parking Lot	3.0d	19-Nov-25 A	21-Nov-25 A	
1424	ASD-Bull-ET-120	Contract Negotiation - ASD Bulletin - Craft Parking Lot	4.0d	15-Dec-25 A	18-Dec-25 A	
1425	ASD-Bull-ET-130	Contract Execution - ASD Bulletin - Craft Parking Lot	1.0d	19-Dec-25 A	19-Dec-25 A	
1426	ASD-Bull-ET-80	NTP - ASD Bulletin - Craft Parking Lot	1.0d	22-Dec-25 A	22-Dec-25 A	
1427	WBS - ASD - PRECONSTRUCTION PHASE		1,316.0d	4-Aug-23 A	9-Oct-28	110.0d
1428	WBS - HCAA Board Approval Milestones		1,316.0d	4-Aug-23 A	9-Oct-28	110.0d

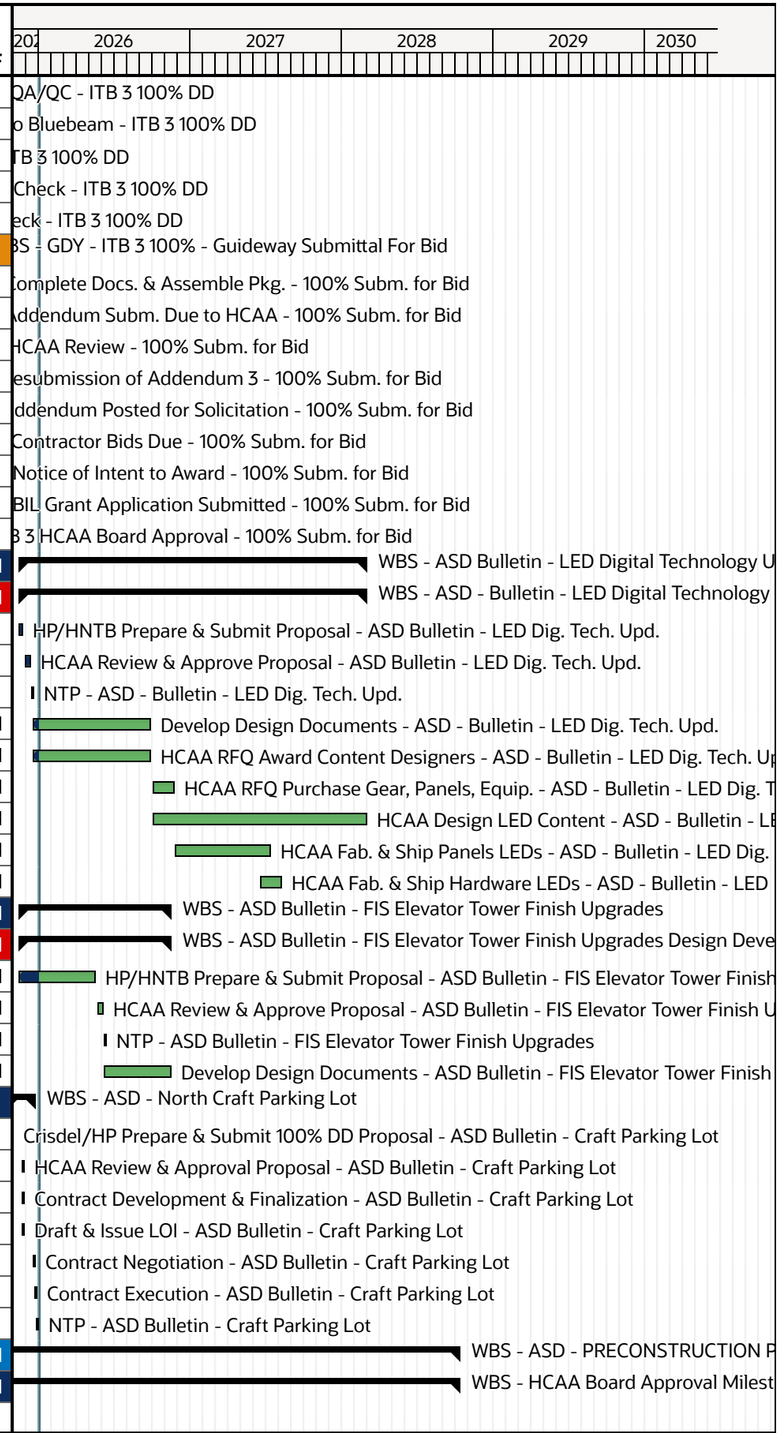

	ID	Name	Dur	Start	Finish	TF
1429	HA-BA-10	HCAA Board Award of Part 1.A Agreement (BHS) - HCAA Board Approval	1.0d	2-Oct-23 A	2-Oct-23 A	
1430	HA-BA-20	Enabling Pkg. 12.5.2024 - HCAA Board Approval	0.0d		5-Dec-24 A	
1431	HA-BA-ITB1-30	ITB 1 Pkg. 6.5.2025 - HCAA Board Approval	0.0d		5-Jun-25 A	
1432	HA-BA-50	Part 2 Supplemental A - Agreement Found. Pkg. 8.7.2025 - HCAA Board Appro...	0.0d		7-Aug-25 A	
1433	HA-BA-ITB2-3-70	ITB 2 & 3 Pkg.'s 8.7.2025 - HCAA Board Approval	0.0d		7-Aug-25 A	
1434	HA-BA-110	Part 2 Supplemental A - Agreement Found. Pkg. 8.7.2025 - Notice to Proceed	0.0d		15-Aug-25 A	
1435	HA-BA-90	Part 2 Supplemental B Agreement - Westside Checked Baggage - 10.2.25 - HC...	0.0d		2-Oct-25 A	
1436	HA-BA-95	Part 2 Supplemental B Agreement - ASD Structure (Precast & Steel) - 10.2.25 - ...	0.0d		2-Oct-25 A	
1437	HA-BA-60	Part 2 Supplemental C Agreement - HCAA Board Approval (2.5.2026)	0.0d		5-Feb-26	5.0d
1438	WBS - HCAA Board Award of Work Order 23-01		0.0d	4-Aug-23	4-Aug-23 A	
1439	HA-WO-10	Work Order 23-01 Executed	0.0d		4-Aug-23 A	
1440	WBS - HCAA Board Award of Work Order 23-01A		0.0d	2-Oct-23	2-Oct-23 A	
1441	HA-WO-20	Work Order 23-01 A Executed (Supp. B)	0.0d		2-Oct-23 A	
1442	WBS - HCAA Board Award of Part 2 Agreement - Enabling Package		85.0d	14-Aug-24 A	13-Dec-24 A	
1443	HA-2A-EN-10	Assemble Bid Pack - HCAA Board Award of P2 Agrmt Enabling Pckg.	6.0d	14-Aug-24 A	21-Aug-24 A	
1444	HA-2A-EN-20	Subcontractor Bid Phase - HCAA Board Award of P2 Agrmt Enabling Pckg.	20.0d	22-Aug-24 A	19-Sep-24 A	
1445	HA-2A-EN-30	Issue Subcontractor Bid Pkg.s - HCAA Board Award of P2 Agrmt Enabling Pckg.	1.0d	22-Aug-24 A	22-Aug-24 A	
1446	HA-2A-EN-40	Bid Day - HCAA Board Award of P2 Agrmt Enabling Pckg.	2.0d	18-Sep-24 A	19-Sep-24 A	
1447	HA-2A-EN-50	Reconcile Bids - HCAA Board Award of P2 Agrmt Enabling Pckg.	5.0d	20-Sep-24 A	26-Sep-24 A	
1448	HA-2A-EN-60	Commence Purchase Interviews - HCAA Board Award of P2 Agrmt Enabling Pckg.	0.0d	25-Sep-24 A		
1449	HA-2A-EN-70	Purchase Interview & Issue Doc U Sign Contracts - HCAA Board Award of P2 Ag...	8.0d	25-Sep-24 A	4-Oct-24 A	
1450	HA-2A-EN-190	GMP Pkg. Assembly - HCAA Board Award of P2 Agrmt Enabling Pckg.	4.0d	4-Oct-24 A	9-Oct-24 A	
1451	HA-2A-EN-220	Draft for Comment to HCAA Complete - HCAA Board Award of P2 Agrmt Enabli...	0.0d		9-Oct-24 A	
1452	HA-2A-EN-210	Negotiate / Address Comments w/ HCAA - HCAA Board Award of P2 Agrmt En...	13.0d	10-Oct-24 A	28-Oct-24 A	
1453	HA-2A-EN-230	Approval (5 Wks Prior to Board Mtng on 12.5.2024) Complete - HCAA Board A...	0.0d		12-Nov-24 A	
1454	HA-BA-80	HCAA NTP Submission - HCAA Board Approval	6.0d	6-Dec-24 A	13-Dec-24 A	
1455	WBS - Part 2 Agreement - Enabling Package Trade Partner Purchasing		8.0d	25-Sep-24 A	4-Oct-24 A	
1456	HA-2A-EN-80	Purchase Interview Elec. - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1457	HA-2A-EN-90	Purchase Interview Security - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1458	HA-2A-EN-100	Purchase Interview Civil - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1459	HA-2A-EN-110	Purchase Interview Low Voltage - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1460	HA-2A-EN-120	Purchase Interview Trailer - Part 2 Agreement Enabling Pckg.	1.0d	30-Sep-24 A	30-Sep-24 A	
1461	HA-2A-EN-130	Purchase Interview Fencing - Part 2 Agreement Enabling Pckg.	1.0d	30-Sep-24 A	30-Sep-24 A	
1462	HA-2A-EN-140	Purchase Interview Demolition - Part 2 Agreement Enabling Pckg.	1.0d	1-Oct-24 A	1-Oct-24 A	
1463	HA-2A-EN-150	Purchase Interview Material Testing & Pilot Holes - Part 2 Agreement Enabling ...	1.0d	1-Oct-24 A	1-Oct-24 A	
1464	HA-2A-EN-160	Purchase Interview Furniture - Part 2 Agreement Enabling Pckg.	1.0d	2-Oct-24 A	2-Oct-24 A	
1465	HA-2A-EN-170	Purchase Interview Site Logistics - Part 2 Agreement Enabling Pckg.	1.0d	3-Oct-24 A	3-Oct-24 A	
1466	HA-2A-EN-180	Purchase Interview Field Engineering - Part 2 Agreement Enabling Pckg.	1.0d	3-Oct-24 A	3-Oct-24 A	
1467	HA-2A-EN-200	Purchase Interview Dewatering - Part 2 Agreement Enabling Pckg.	1.0d	4-Oct-24 A	4-Oct-24 A	
1468	WBS - HCAA Board Award of Part 2 Supplement A - Ground Improvements & Foundations Package		134.0d	8-May-25 A	14-Nov-25 A	
1469	HA-2A-10	Bid Packaging - Ground Impr. & Found. Pckg	4.0d	8-May-25 A	13-May-25 A	
1470	HA-2A-20	Bidding Period - Ground Impr. & Found. Pckg	20.0d	14-May-25 A	11-Jun-25 A	

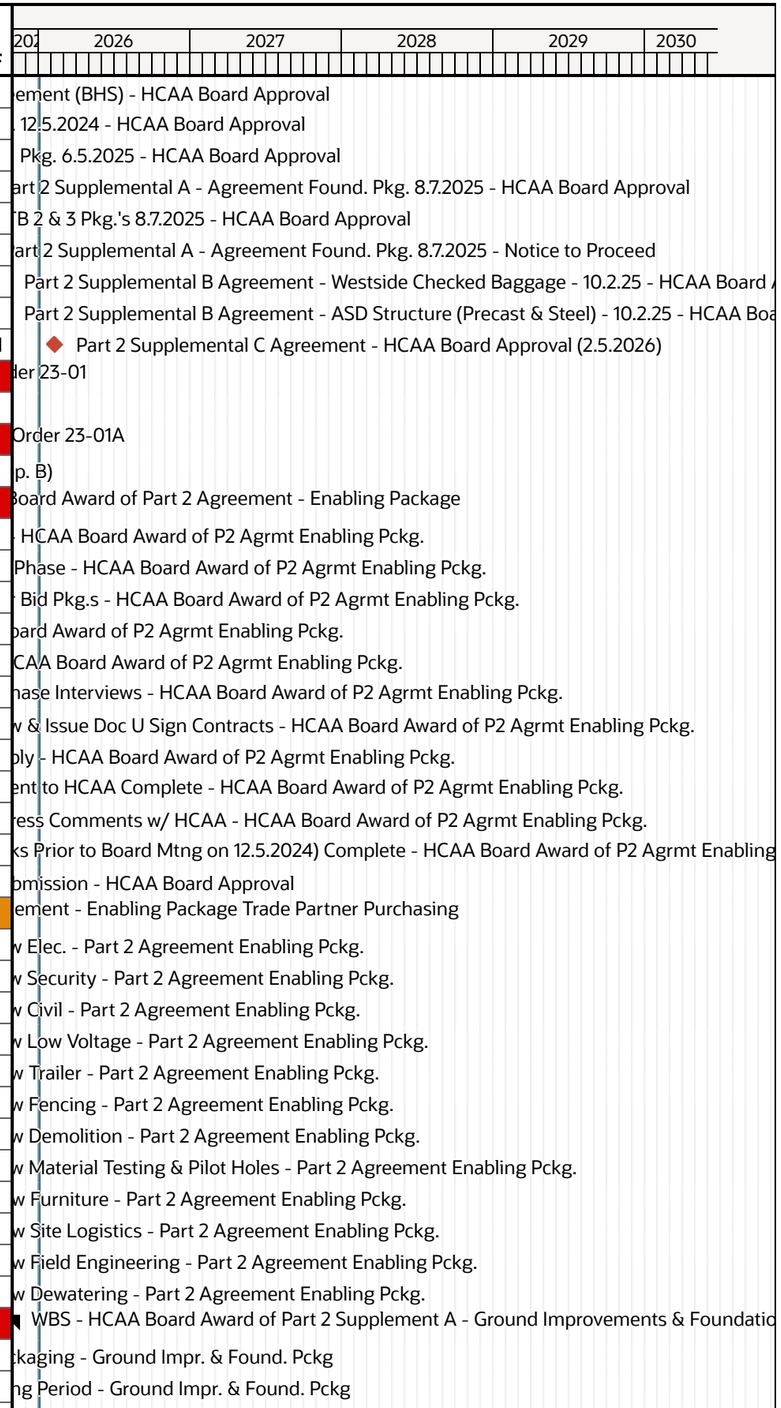

	ID	Name	Dur	Start	Finish	TF
1471	HA-2A-70	GMP Pkg. Assembly - Ground Impr. & Found. Pckg	5.0d	5-Jun-25 A	11-Jun-25 A	
1472	HA-2A-80	Draft for Comment to HCAA Complete - Ground Impr. & Found. Pckg	0.0d		11-Jun-25 A	
1473	HA-2A-90	Negotiate / Address Comments w/ HCAA - Ground Impr. & Found. Pckg	15.0d	12-Jun-25 A	2-Jul-25 A	
1474	HA-2A-130	Bid Addendum 6.12.2025 Found. - Ground Impr. & Found. Pckg	15.0d	12-Jun-25 A	2-Jul-25 A	
1475	HA-2A-100	Approval (5 Weeks Prior to Board Mtg. on 8.7.2025) - Ground Impr. & Found. P...	0.0d		2-Jul-25 A	
1476	HA-2A-30	Contracting Period - Ground Impr. & Found. Pckg	14.0d	3-Jul-25 A	23-Jul-25 A	
1477	WBS - Part 2 Supplement A - Ground Improvements Trade Partner Purchasing		92.0d	9-Jul-25 A	14-Nov-25 A	
1478	HA-2A-140	Purchase Interview - GMF - Anchor Bolts & Structural Steel Mill Order 7/9/25	1.0d	9-Jul-25 A	9-Jul-25 A	
1479	HA-2A-150	Purchase Interview - APG - Deep UG Electric & Long Lead 7/9/25	1.0d	9-Jul-25 A	9-Jul-25 A	
1480	HA-2A-160	Purchase Interview - MC Dean - Deep UG LV 7/10/25	1.0d	10-Jul-25 A	10-Jul-25 A	
1481	HA-2A-170	Purchase Interview - BCH - Deep UG Plumbing & HVAC Long Lead 7/11/25	1.0d	11-Jul-25 A	11-Jul-25 A	
1482	HA-2A-180	Purchase Interview - Menard DIP/LTP Ground Improvement 7/11/25	1.0d	11-Jul-25 A	11-Jul-25 A	
1483	HA-2A-190	Purchase Interview - Liberty - Found. Concrete 7/23/25	1.0d	23-Jul-25 A	23-Jul-25 A	
1484	HA-2A-240	Contracting Period - Menard DIP/LTP Ground Improvement	32.0d	18-Aug-25 A	1-Oct-25 A	
1485	HA-2A-200	Contracting Period - GMF - Anchor Bolts & Structural Steel Mill Order	52.0d	18-Aug-25 A	29-Oct-25 A	
1486	HA-2A-220	Contracting Period - MC Dean - QA/QC Deep UG	46.0d	18-Aug-25 A	21-Oct-25 A	
1487	HA-2A-210	Contracting Period - APG - Deep UG Elec. & Long Lead	45.0d	18-Aug-25 A	20-Oct-25 A	
1488	HA-2A-230	Contracting Period - BCH - Deep UG Plumbing & HVAC Long Lead	30.0d	18-Aug-25 A	29-Sep-25 A	
1489	HA-2A-250	Contracting Period - Liberty - Found. Concrete	18.0d	18-Aug-25 A	11-Sep-25 A	
1490	HA-2A-290	NTP - GMF - Anchor Bolts & Structural Steel Mill Order	0.0d	26-Aug-25 A		
1491	HA-2A-270	Subcontract Execution - Liberty - Found. Concrete	0.0d		11-Sep-25 A	
1492	HA-2A-280	Subcontract Execution - BCH - Deep UG Plumbing & HVAC Long Lead	0.0d		29-Sep-25 A	
1493	HA-2A-260	Subcontract Execution - Menard DIP/LTP Ground Improvement	0.0d		1-Oct-25 A	
1494	HA-2A-320	Subcontract Execution - MC Dean - QA/QC Deep UG	0.0d		21-Oct-25 A	
1495	HA-2A-310	Subcontract Execution - APG - Deep UG Elec. & Long Lead	0.0d		5-Nov-25 A	
1496	HA-2A-300	Subcontract Execution - GMF - Structural Steel	0.0d		14-Nov-25 A	
1497	WBS - HCAA Board Award of Part 2 Supplement B - Centralized Checked Baggage Enabling		87.0d	17-Jul-25 A	17-Nov-25 A	
1498	HA-2B-CC-10	Bid Packaging - CCBS Pckg.	2.0d	17-Jul-25 A	18-Jul-25 A	
1499	HA-2B-CC-20	Bidding Period - CCBS Pckg.	14.0d	21-Jul-25 A	7-Aug-25 A	
1500	HA-2B-CC-40	GMP Pkg. Assembly - CCBS Pckg.	4.0d	8-Aug-25 A	13-Aug-25 A	
1501	HA-2B-CC-70	Submit For Approval (8 Weeks Prior to Board Mtg. on 10.2.2025) - CCBS Pckg.	0.0d		14-Aug-25 A	
1502	HA-2B-CC-30	Contracting Period - CCBS Pckg.	29.0d	15-Aug-25 A	25-Sep-25 A	
1503	HA-2B-CC-60	Negotiate / Address Comments w/ HCAA - CCBS Pckg.	7.0d	17-Sep-25 A	25-Sep-25 A	
1504	HA-2B-CC-65	Board Meeting Agenda - CCBS Pckg.	4.0d	26-Sep-25 A	2-Oct-25 A	
1505	HA-2B-CC-75	Trade Partner Contract Negotiation - CCBS Pckg.	32.0d	3-Oct-25 A	17-Nov-25 A	
1506	HA-2B-CC-85	Trade Partner Contract Execution - CCBS Pckg.	0.0d		17-Nov-25 A	
1507	WBS - Part 2 Supplement B - ASD Structure (Precast & Steel)		100.0d	17-Jul-25 A	8-Dec-25 A	
1508	HA-2B-ASD-80	Bid Packaging - ASD Structure (Precast & Steel)	2.0d	17-Jul-25 A	18-Jul-25 A	
1509	HA-2B-ASD-90	Bidding Period - ASD Structure (Precast & Steel)	14.0d	21-Jul-25 A	7-Aug-25 A	
1510	HA-2B-ASD-110	GMP Pkg. Assembly - ASD Structure (Precast & Steel)	4.0d	8-Aug-25 A	13-Aug-25 A	
1511	HA-2B-ASD-140	Submit For Approval (8 Weeks Prior to Board Mtg. on 10.2.2025) - ASD Structu...	0.0d		14-Aug-25 A	
1512	HA-2B-ASD-100	Contracting Period - ASD Structure (Precast & Steel)	29.0d	15-Aug-25 A	25-Sep-25 A	

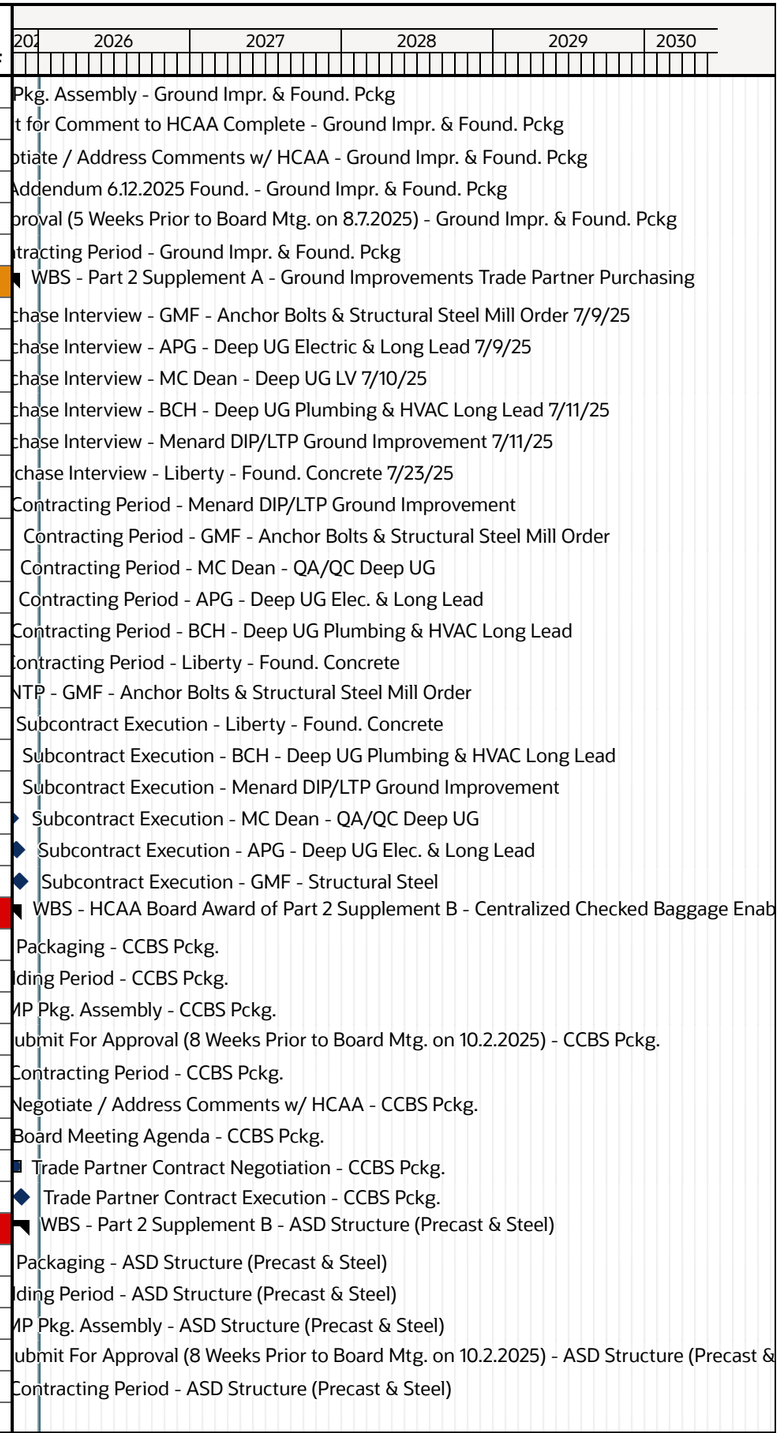


	ID	Name	Dur	Start	Finish	TF
1513	HA-2B-ASD-130	Negotiate/Address Comments w/ HCAA - ASD Structure (Precast & Steel)	7.0d	17-Sep-25 A	25-Sep-25 A	
1514	WBS - Architectural/Structural Precast		61.0d	11-Sep-25 A	8-Dec-25 A	
1515	HA-2B-ASD-160	Bidding Period - Precast	23.0d	11-Sep-25 A	13-Oct-25 A	
1516	HA-2B-ASD-170	Bid Review/Purchasing Meetings/Issue LOI - Precast	8.0d	24-Oct-25 A	4-Nov-25 A	
1517	HA-2B-ASD-180	Contracting Period - Precast	22.0d	5-Nov-25 A	8-Dec-25 A	
1518	HA-2B-ASD-190	Contract Execution Complete - Precast - Architectural/Structural	0.0d		8-Dec-25 A	
1519	WBS - HCAA Board Award of Part 2 Supplement C Wave 1 - Core & Shell Package		130.0d	22-Aug-25 A	26-Feb-26	410.0d
1520	HA-2C-W1-20	Bid Packaging - Part 2 Supp. C - Core & Shell Pkg.	10.0d	22-Aug-25 A	5-Sep-25 A	
1521	HA-2C-W1-30	Bidding Period - Part 2 Supp. C - Core & Shell Pkg.	37.0d	8-Sep-25 A	27-Oct-25 A	
1522	HA-2C-W1-35	Amendment 1 100% Drawings Pricing - Part 2 Supp. C - Core & Shell Pkg.	11.0d	28-Oct-25 A	11-Nov-25 A	
1523	HA-2C-W1-55	Contract Development/GMP Pkg. Assembly - Part 2 Supp. C - Core & Shell Pkg.	21.0d	12-Nov-25 A	12-Dec-25 A	
1524	HA-2C-W1-50	Bid Review/Bid Selection - Part 2 Supp. C - Core & Shell Pkg.	4.0d	12-Nov-25 A	17-Nov-25 A	
1525	HA-2C-W1-60	Submit For Approval (5 Weeks Prior to Board Mtg. on 2.5.2026 - Part 2 Supp. C ...	0.0d		12-Dec-25 A	
1526	HA-2C-W1-70	HCAA Review Supp. C for Board - Part 2 Supp. C - Core & Shell Pkg.	37.0d	15-Dec-25 A	5-Feb-26	0.0d
1527	HA-2C-W1-80	Board Date (NTP) - Part 2 Supp. C - Core & Shell Pkg. (2.5.26)	0.0d		5-Feb-26	0.0d
1528	HA-2C-W1-90	HCAA Contract Supp. C Execution - Part 2 Supp. C - Core & Shell Pkg.	15.0d	6-Feb-26	26-Feb-26	51.0d
1529	WBS - Part 2 Supplement C Wave 1 Purchasing & Contracting		64.0d	18-Nov-25 A	19-Feb-26	415.0d
1530	WBS - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		59.0d	18-Nov-25 A	12-Feb-26	95.0d
1531	2C-W1-PC-800	Purchasing Meeting - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purcha...	1.0d	18-Nov-25 A	18-Nov-25 A	
1532	2C-W1-PC-820	Contract Development, Review, & Issuance - Fire Protection Trade Partner - P2 ...	8.0d	24-Nov-25 A	5-Dec-25 A	
1533	2C-W1-PC-830	Contract Negoation - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purcha...	15.0d	8-Dec-25 A	29-Dec-25	122.0d
1534	2C-W1-PC-840	Contract Execution - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchas...	5.0d	6-Feb-26	12-Feb-26	95.0d
1535	2C-W1-PC-850	Contract Execution Complete - Fire Protection Trade Partner - P2 Supp. C Wave...	0.0d		12-Feb-26	95.0d
1536	WBS - Elevators/Escalators Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		59.0d	18-Nov-25 A	12-Feb-26	0.0d
1537	2C-W1-PC-740	Purchasing Meeting - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purch...	1.0d	18-Nov-25 A	18-Nov-25 A	
1538	2C-W1-PC-750	Draft & Issue LOI - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purchasi...	3.0d	2-Dec-25 A	4-Dec-25 A	
1539	2C-W1-PC-760	Contract Development, Review, & Issuance - Elev./Escalators Trade Partner - P...	4.0d	5-Dec-25 A	10-Dec-25 A	
1540	2C-W1-PC-770	Contract Negoation - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purch...	12.0d	11-Dec-25 A	29-Dec-25	27.0d
1541	2C-W1-PC-780	Contract Execution - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purcha...	5.0d	6-Feb-26	12-Feb-26	0.0d
1542	2C-W1-PC-790	Contract Execution Complete - Elev./Escalators Trade Partner - P2 Supp. C Wav...	0.0d		12-Feb-26	0.0d
1543	WBS - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		55.0d	24-Nov-25 A	12-Feb-26	386.0d
1544	2C-W1-PC-2060	Purchasing Meeting - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purcha...	0.0d	24-Nov-25 A	24-Nov-25 A	
1545	2C-W1-PC-2080	Contract Development, Review, & Issuance - Terrazzo Floor Trade Partner - P2 ...	5.0d	1-Dec-25 A	5-Dec-25 A	
1546	2C-W1-PC-2090	Contract Negoation - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchas...	15.0d	8-Dec-25 A	29-Dec-25	413.0d
1547	2C-W1-PC-2100	Contract Execution - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	6-Feb-26	12-Feb-26	386.0d
1548	2C-W1-PC-2110	Contract Execution Complete - Terrazzo Floor Trade Partner - P2 Supp. C Wave ...	0.0d		12-Feb-26	386.0d
1549	WBS - Roofing Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		51.0d	2-Dec-25 A	12-Feb-26	91.0d
1550	2C-W1-PC-70	Purchasing Meeting - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	1.0d	2-Dec-25 A	2-Dec-25 A	
1551	2C-W1-PC-80	Draft & Issue LOI - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & Co...	3.0d	3-Dec-25 A	5-Dec-25 A	
1552	2C-W1-PC-90	Contract Development, Review, & Issuance - Roofing Trade Partner - P2 Supp. ...	5.0d	10-Dec-25 A	16-Dec-25 A	
1553	2C-W1-PC-100	Contract Negoation - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	11.0d	17-Dec-25 A	2-Jan-26	115.0d
1554	2C-W1-PC-110	Contract Execution - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	91.0d



	ID	Name	Dur	Start	Finish	TF
1555	2C-W1-PC-120	Contract Execution Complete - Roofing Trade Partner - P2 Supp. C Wave 1 Purc...	0.0d		12-Feb-26	91.0d
1556	WBS - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		58.0d	19-Nov-25 A	12-Feb-26	26.0d
1557	2C-W1-PC-1220	Purchasing Meeting - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wav...	1.0d	19-Nov-25 A	19-Nov-25 A	
1558	2C-W1-PC-1240	Contract Development, Review, & Issuance - Acoustical Panel Ceilings Trade Pa...	8.0d	25-Nov-25 A	8-Dec-25 A	
1559	2C-W1-PC-1250	Contract Negoation - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wav...	14.0d	9-Dec-25 A	29-Dec-25	53.0d
1560	2C-W1-PC-1260	Contract Execution - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave...	5.0d	6-Feb-26	12-Feb-26	26.0d
1561	2C-W1-PC-1270	Contract Execution Complete - Acoustical Panel Ceilings Trade Partner - P2 Sup...	0.0d		12-Feb-26	26.0d
1562	WBS - Interior Wall Panels (Specialties/Decorative Glass) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contra...		51.0d	2-Dec-25 A	12-Feb-26	407.0d
1563	2C-W1-PC-370	Purchasing Meeting - Interior Wall Panels (Specialties/Decorative Glass) Trade ...	1.0d	2-Dec-25 A	2-Dec-25 A	
1564	2C-W1-PC-390	Contract Development, Review, & Issuance - Interior Wall Panels (Specialties/D...	2.0d	5-Dec-25 A	8-Dec-25 A	
1565	2C-W1-PC-400	Contract Negoation - Interior Wall Panels (Specialties/Decorative Glass) Trade P...	14.0d	9-Dec-25 A	29-Dec-25	434.0d
1566	2C-W1-PC-410	Contract Execution - Interior Wall Panels (Specialties/Decorative Glass) Trade P...	5.0d	6-Feb-26	12-Feb-26	407.0d
1567	2C-W1-PC-420	Contract Execution Complete - Interior Wall Panels (Specialties/Decorative Glas...	0.0d		12-Feb-26	407.0d
1568	WBS - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		51.0d	2-Dec-25 A	12-Feb-26	394.0d
1569	2C-W1-PC-2120	Purchasing Meeting - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 P...	1.0d	2-Dec-25 A	2-Dec-25 A	
1570	2C-W1-PC-2140	Contract Development, Review, & Issuance - Ornamental Metals Trade Partner ...	2.0d	5-Dec-25 A	8-Dec-25 A	
1571	2C-W1-PC-2150	Contract Negoation - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Pu...	14.0d	9-Dec-25 A	29-Dec-25	421.0d
1572	2C-W1-PC-2160	Contract Execution - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Pur...	5.0d	6-Feb-26	12-Feb-26	394.0d
1573	2C-W1-PC-2170	Contract Execution Complete - Ornamental Metals Trade Partner - P2 Supp. C ...	0.0d		12-Feb-26	394.0d
1574	WBS - Glass Handrail Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		50.0d	3-Dec-25 A	12-Feb-26	420.0d
1575	2C-W1-PC-440	Purchasing Meeting - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purcha...	1.0d	3-Dec-25 A	3-Dec-25 A	
1576	2C-W1-PC-460	Contract Development, Review, & Issuance - Glass Handrail Trade Partner - P2 ...	10.0d	29-Dec-25	12-Jan-26	428.0d
1577	2C-W1-PC-470	Contract Negoation - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purcha...	10.0d	13-Jan-26	26-Jan-26	428.0d
1578	2C-W1-PC-480	Contract Execution - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	6-Feb-26	12-Feb-26	420.0d
1579	2C-W1-PC-490	Contract Execution Complete - Glass Handrail Trade Partner - P2 Supp. C Wave ...	0.0d		12-Feb-26	420.0d
1580	WBS - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		50.0d	3-Dec-25 A	12-Feb-26	36.0d
1581	2C-W1-PC-1160	Purchasing Meeting - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	3-Dec-25 A	3-Dec-25 A	
1582	2C-W1-PC-1180	Contract Development, Review, & Issuance - Masonry Trade Partner - P2 Supp. ...	15.0d	8-Dec-25 A	29-Dec-25	53.0d
1583	2C-W1-PC-1190	Contract Negoation - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	53.0d
1584	2C-W1-PC-1200	Contract Execution - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	36.0d
1585	2C-W1-PC-1210	Contract Execution Complete - Masonry Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	36.0d
1586	WBS - Demolition Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		49.0d	4-Dec-25 A	12-Feb-26	61.0d
1587	2C-W1-PC-2420	Purchasing Meeting - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasin...	1.0d	4-Dec-25 A	4-Dec-25 A	
1588	2C-W1-PC-2440	Contract Development, Review, & Issuance - Demolition Trade Partner - P2 Sup...	8.0d	9-Dec-25 A	18-Dec-25 A	
1589	2C-W1-PC-2450	Contract Negoation - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasing...	12.0d	19-Dec-25 A	7-Jan-26	82.0d
1590	2C-W1-PC-2460	Contract Execution - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasing ...	5.0d	6-Feb-26	12-Feb-26	61.0d
1591	2C-W1-PC-2470	Contract Execution Complete - Demolition Trade Partner - P2 Supp. C Wave 1 P...	0.0d		12-Feb-26	61.0d
1592	WBS - Concrete SOG & SOMD Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		49.0d	4-Dec-25 A	12-Feb-26	101.0d
1593	2C-W1-PC-10	Purchasing Meeting - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	4-Dec-25 A	4-Dec-25 A	
1594	2C-W1-PC-30	Contract Development, Review, & Issuance - Concrete Trade Partner - P2 Supp. ...	14.0d	9-Dec-25 A	29-Dec-25	118.0d
1595	2C-W1-PC-40	Contract Negoation - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	30-Dec-25	13-Jan-26	118.0d
1596	2C-W1-PC-50	Contract Execution - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	101.0d



	ID	Name	Dur	Start	Finish	TF
1597	2C-W1-PC-60	Contract Execution Complete - Concrete Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	101.0d
1598	WBS - Interior/Exterior Metal Wall Panels Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		46.0d	9-Dec-25 A	12-Feb-26	91.0d
1599	2C-W1-PC-250	Purchasing Meeting - Interior/Exterior Metal Wall Panels Trade Partner - P2 Su...	1.0d	9-Dec-25 A	9-Dec-25 A	
1600	2C-W1-PC-270	Contract Development, Review, & Issuance - Interior/Exterior Metal Wall Panels...	7.0d	10-Dec-25 A	18-Dec-25 A	
1601	2C-W1-PC-280	Contract Negoation - Interior/Exterior Metal Wall Panels Trade Partner - P2 Sup...	11.0d	19-Dec-25 A	6-Jan-26	113.0d
1602	2C-W1-PC-290	Contract Execution - Interior/Exterior Metal Wall Panels Trade Partner - P2 Sup...	5.0d	6-Feb-26	12-Feb-26	91.0d
1603	2C-W1-PC-300	Contract Execution Complete - Interior/Exterior Metal Wall Panels Trade Partne...	0.0d		12-Feb-26	91.0d
1604	WBS - Spray Fireproofing & Insulation (K-13) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		46.0d	9-Dec-25 A	12-Feb-26	81.0d
1605	2C-W1-PC-130	Purchasing Meeting - Spray Fireproofing & Insulation (K-13) Trade Partner - P2...	1.0d	9-Dec-25 A	9-Dec-25 A	
1606	2C-W1-PC-150	Contract Development, Review, & Issuance - Spray Fireproofing & Insulation (K-...	5.0d	11-Dec-25 A	17-Dec-25 A	
1607	2C-W1-PC-160	Contract Negoation - Spray Fireproofing & Insulation (K-13) Trade Partner - P2 ...	11.0d	18-Dec-25 A	5-Jan-26	104.0d
1608	2C-W1-PC-170	Contract Execution - Spray Fireproofing & Insulation (K-13) Trade Partner - P2 ...	5.0d	6-Feb-26	12-Feb-26	81.0d
1609	2C-W1-PC-180	Contract Execution Complete - Spray Fireproofing & Insulation (K-13) Trade Par...	0.0d		12-Feb-26	81.0d
1610	WBS - Drywall & Related Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		45.0d	10-Dec-25 A	12-Feb-26	74.0d
1611	2C-W1-PC-500	Purchasing Meeting - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Pur...	1.0d	10-Dec-25 A	10-Dec-25 A	
1612	2C-W1-PC-520	Contract Development, Review, & Issuance - Drywall & Related Trade Partner - ...	5.0d	11-Dec-25 A	17-Dec-25 A	
1613	2C-W1-PC-530	Contract Negoation - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Purc...	11.0d	18-Dec-25 A	5-Jan-26	97.0d
1614	2C-W1-PC-540	Contract Execution - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Purc...	5.0d	6-Feb-26	12-Feb-26	74.0d
1615	2C-W1-PC-550	Contract Execution Complete - Drywall & Related Trade Partner - P2 Supp. C W...	0.0d		12-Feb-26	74.0d
1616	WBS - Glass & Glazing/Curtainwall Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		45.0d	10-Dec-25 A	12-Feb-26	81.0d
1617	2C-W1-PC-310	Purchasing Meeting - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C ...	1.0d	10-Dec-25 A	10-Dec-25 A	
1618	2C-W1-PC-330	Contract Development, Review, & Issuance - Glass & Glazing/Curtainwall Trade ...	6.0d	11-Dec-25 A	18-Dec-25 A	
1619	2C-W1-PC-340	Contract Negoation - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C W...	9.0d	19-Dec-25 A	2-Jan-26	105.0d
1620	2C-W1-PC-350	Contract Execution - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C W...	5.0d	6-Feb-26	12-Feb-26	81.0d
1621	2C-W1-PC-360	Contract Execution Complete - Glass & Glazing/Curtainwall Trade Partner - P2 ...	0.0d		12-Feb-26	81.0d
1622	WBS - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		44.0d	11-Dec-25 A	12-Feb-26	81.0d
1623	2C-W1-PC-1040	Purchasing Meeting - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	11-Dec-25 A	11-Dec-25 A	
1624	2C-W1-PC-1060	Contract Development, Review, & Issuance - Sitework Trade Partner - P2 Supp. ...	10.0d	29-Dec-25	12-Jan-26	89.0d
1625	2C-W1-PC-1070	Contract Negoation - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing &...	10.0d	13-Jan-26	26-Jan-26	89.0d
1626	2C-W1-PC-1080	Contract Execution - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	5.0d	6-Feb-26	12-Feb-26	81.0d
1627	2C-W1-PC-1090	Contract Execution Complete - Sitework Trade Partner - P2 Supp. C Wave 1 Pur...	0.0d		12-Feb-26	81.0d
1628	WBS - Waterproofing, Caulks, & Sealants Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		44.0d	11-Dec-25 A	12-Feb-26	101.0d
1629	2C-W1-PC-190	Purchasing Meeting - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	1.0d	11-Dec-25 A	11-Dec-25 A	
1630	2C-W1-PC-210	Contract Development, Review, & Issuance - Waterproofing, Caulks, & Sealants ...	10.0d	29-Dec-25	12-Jan-26	109.0d
1631	2C-W1-PC-220	Contract Negoation - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	10.0d	13-Jan-26	26-Jan-26	109.0d
1632	2C-W1-PC-230	Contract Execution - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	5.0d	6-Feb-26	12-Feb-26	101.0d
1633	2C-W1-PC-240	Contract Execution Complete - Waterproofing, Caulks, & Sealants Trade Partner...	0.0d		12-Feb-26	101.0d
1634	WBS - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partner - Part 2 Supp. B Purchasing & Contracting		3.0d	18-Dec-25 A	22-Dec-25 A	
1635	2C-W1-PC-2540	Purchasing Meeting - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partn...	1.0d	18-Dec-25 A	18-Dec-25 A	
1636	2C-W1-PC-2560	Contract Development, Review, & Issuance - Carbon Fiber Reinforcement Poly...	1.0d	19-Dec-25 A	19-Dec-25 A	
1637	2C-W1-PC-2580	Contract Execution - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partne...	1.0d	22-Dec-25 A	22-Dec-25 A	
1638	2C-W1-PC-2590	Contract Execution Complete - Carbon Fiber Reinforcement Polymer (CFRP) Tra...	0.0d		22-Dec-25 A	

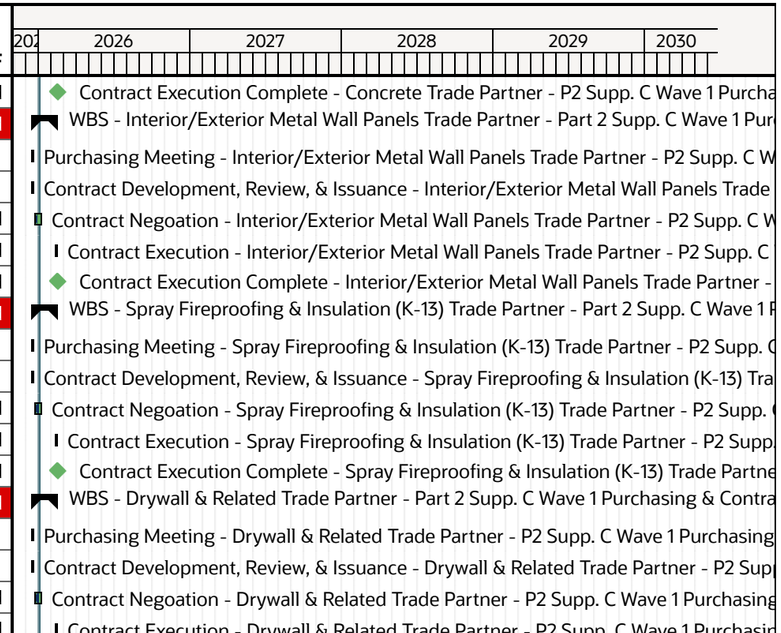

	ID	Name	Dur	Start	Finish	TF
1639	WBS - Electrical & Site Electrical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		29.0d	5-Jan-26	12-Feb-26	91.0d
1640	2C-W1-PC-860	Purchasing Meeting - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 Purc...	1.0d	5-Jan-26	5-Jan-26	9.0d
1641	2C-W1-PC-870	Draft, Review, & Issue Change Order - Elec. & Site Elec. Trade Partner - P2 Supp...	10.0d	6-Jan-26	19-Jan-26	94.0d
1642	2C-W1-PC-890	Change Order Negoation - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 ...	10.0d	20-Jan-26	2-Feb-26	94.0d
1643	2C-W1-PC-900	Change Order Execution - Elec. & Site Elec. Trade Partner - P2 Supp. C Wave 1 ...	5.0d	6-Feb-26	12-Feb-26	91.0d
1644	2C-W1-PC-910	Change Order Execution Complete - Elec. & Site Elec. Trade Partner - P2 Supp. ...	0.0d		12-Feb-26	91.0d
1645	WBS - Baggage Handling Contractor - Part 2 Supp. C Wave 1 Purchasing & Contracting		28.0d	6-Jan-26	12-Feb-26	0.0d
1646	2C-W1-PC-2480	Purchasing Meeting - Baggage Handling Contractor - P2 Supp. C Wave 1 Purch...	1.0d	6-Jan-26	6-Jan-26	9.0d
1647	2C-W1-PC-2490	Draft, Review, & Issue Change Order - Baggage Handling Contractor - P2 Supp. ...	3.0d	7-Jan-26	9-Jan-26	9.0d
1648	2C-W1-PC-2510	Change Order Negotiation - Baggage Handling Contractor - P2 Supp. C Wave 1 ...	10.0d	12-Jan-26	23-Jan-26	9.0d
1649	2C-W1-PC-2520	Change Order Execution - Baggage Handling Contractor - P2 Supp. C Wave 1 P...	5.0d	6-Feb-26	12-Feb-26	0.0d
1650	2C-W1-PC-2530	Change Order Execution Complete - Baggage Handling Contractor - P2 Supp. C...	0.0d		12-Feb-26	0.0d
1651	WBS - Low Voltage System Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		27.0d	7-Jan-26	12-Feb-26	9.0d
1652	2C-W1-PC-920	Purchasing Meeting - Low Voltage System Trade Partner - P2 Supp. C Wave 1 P...	1.0d	7-Jan-26	7-Jan-26	17.0d
1653	2C-W1-PC-930	Draft, Review, & Issue Change Order - Low Voltage System Trade Partner - P2 S...	3.0d	8-Jan-26	12-Jan-26	17.0d
1654	2C-W1-PC-950	Change Order Negoation - Low Voltage System Trade Partner - P2 Supp. C Wav...	10.0d	13-Jan-26	26-Jan-26	17.0d
1655	2C-W1-PC-960	Change Order Execution - Low Voltage System Trade Partner - P2 Supp. C Wav...	5.0d	6-Feb-26	12-Feb-26	9.0d
1656	2C-W1-PC-970	Change Order Execution Complete - Low Voltage System Trade Partner - P2 Su...	0.0d		12-Feb-26	9.0d
1657	WBS - Plumbing/Mechanical Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		29.0d	5-Jan-26	12-Feb-26	61.0d
1658	2C-W1-PC-1520	Purchasing Meeting - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1 Purc...	1.0d	5-Jan-26	5-Jan-26	55.0d
1659	2C-W1-PC-1530	Draft, Review, & Issue Change Order - Plumbing/Mech. Trade Partner - P2 Sup...	3.0d	6-Jan-26	8-Jan-26	71.0d
1660	2C-W1-PC-1550	Change Order Negoation - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1...	10.0d	9-Jan-26	22-Jan-26	71.0d
1661	2C-W1-PC-1560	Change Order Execution - Plumbing/Mech. Trade Partner - P2 Supp. C Wave 1 ...	5.0d	6-Feb-26	12-Feb-26	61.0d
1662	2C-W1-PC-1570	Change Order Execution Complete - Plumbing/Mech. Trade Partner - P2 Supp. ...	0.0d		12-Feb-26	61.0d
1663	WBS - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting-1		29.0d	8-Jan-26	17-Feb-26	359.0d
1664	2C-W1-PC-2600	Purchasing Meeting - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchas...	1.0d	8-Jan-26	8-Jan-26	352.0d
1665	2C-W1-PC-2610	Draft & Issue LOI - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasing...	3.0d	9-Jan-26	13-Jan-26	359.0d
1666	2C-W1-PC-2620	Contract Development, Review, & Issuance - Pipe Bursting Trade Partner - P2 S...	10.0d	14-Jan-26	27-Jan-26	359.0d
1667	2C-W1-PC-2630	Contract Negoation - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasi...	10.0d	28-Jan-26	10-Feb-26	359.0d
1668	2C-W1-PC-2640	Contract Execution - Pipe Bursting Trade Partner - P2 Supp. C Wave 1 Purchasi...	5.0d	11-Feb-26	17-Feb-26	359.0d
1669	2C-W1-PC-2650	Contract Execution Complete - Pipe Bursting Trade Partner - P2 Supp. C Wave ...	0.0d		17-Feb-26	359.0d
1670	WBS - Structural Steel Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		33.0d	6-Jan-26	19-Feb-26	58.0d
1671	2C-W1-PC-2660	Purchasing Meeting - Structural Steel Trade Partner - P2 Supp. C Wave 1 Purch...	1.0d	6-Jan-26	6-Jan-26	55.0d
1672	2C-W1-PC-2670	Draft, Review, & Issue Change Order - Structural Steel Trade Partner - P2 Supp. ...	3.0d	7-Jan-26	9-Jan-26	62.0d
1673	2C-W1-PC-2680	Change Order Negoation - Structural Steel Trade Partner - P2 Supp. C Wave 1 P...	10.0d	12-Jan-26	23-Jan-26	62.0d
1674	2C-W1-PC-2690	Change Order Execution - Structural Steel Trade Partner - P2 Supp. C Wave 1 P...	5.0d	26-Jan-26	30-Jan-26	62.0d
1675	A105770	Change Order Execution Complete - Structural Steel Trade Partner - P2 Supp. C...	10.0d	6-Feb-26	19-Feb-26	58.0d
1676	WBS - Part 2 Supplement C Wave 2- Finishes Package		95.0d	22-Dec-25 A	5-May-26	555.0d
1677	HA-2C-W2-90	Bid Packaging - Part 2 Supp. C Wave 2 - Finishes Pkg	9.0d	22-Dec-25 A	5-Jan-26	18.0d
1678	HA-2C-W2-100	Bidding Period - Part 2 Supp. C Wave 2 - Finishes Pkg	22.0d	6-Jan-26	4-Feb-26	18.0d
1679	HA-2C-W2-110	Bid Review/Bid Selection - Part 2 Supp. C Wave 2 - Finishes Pkg	12.0d	5-Feb-26	20-Feb-26	18.0d
1680	WBS - Part 2 Supplement C Wave 2 Purchasing and Contracting		51.0d	24-Feb-26	5-May-26	555.0d



	ID	Name	Dur	Start	Finish	TF
1681	WBS - Doors, Frames, & Hardware - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	24-Feb-26	3-Apr-26	19.0d
1682	2C-W2-PC-1270	Purchasing Meeting - Doors, Frames, & Hardware Trade Partner - P2 Supp. C W…	1.0d	24-Feb-26	24-Feb-26	14.0d
1683	2C-W2-PC-1280	Draft & Issue LOI - Doors, Frames, & Hardware Trade Partner - P2 Supp. C Wave…	3.0d	25-Feb-26	27-Feb-26	19.0d
1684	2C-W2-PC-1290	Contract Development, Review, & Issuance - Doors, Frames, & Hardware Trade …	10.0d	2-Mar-26	13-Mar-26	19.0d
1685	2C-W2-PC-1300	Contract Negoation - Doors, Frames, & Hardware Trade Partner - P2 Supp. C W…	10.0d	16-Mar-26	27-Mar-26	19.0d
1686	2C-W2-PC-1310	Contract Execution - Doors, Frames, & Hardware Trade Partner - P2 Supp. C Wa…	5.0d	30-Mar-26	3-Apr-26	19.0d
1687	2C-W2-PC-1320	Contract Execution Complete - Doors, Frames, & Hardware Trade Partner - P2 S…	0.0d		3-Apr-26	19.0d
1688	WBS - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	25-Feb-26	6-Apr-26	18.0d
1689	2C-W2-PC-370	Purchasing Meeting - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing &…	1.0d	25-Feb-26	25-Feb-26	14.0d
1690	2C-W2-PC-380	Draft & Issue LOI - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & Co…	3.0d	26-Feb-26	2-Mar-26	18.0d
1691	2C-W2-PC-390	Contract Development, Review, & Issuance - Flooring Trade Partner - P2 Supp. …	10.0d	3-Mar-26	16-Mar-26	18.0d
1692	2C-W2-PC-400	Contract Negoation - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & …	10.0d	17-Mar-26	30-Mar-26	18.0d
1693	2C-W2-PC-410	Contract Execution - Flooring Trade Partner - P2 Supp. C Wave 2 Purchasing & …	5.0d	31-Mar-26	6-Apr-26	18.0d
1694	2C-W2-PC-420	Contract Execution Complete - Flooring Trade Partner - P2 Supp. C Wave 2 Pur…	0.0d		6-Apr-26	18.0d
1695	WBS - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	26-Feb-26	7-Apr-26	355.0d
1696	2C-W2-PC-10	Purchasing Meeting - Architectural Millwork Trade Partner - P2 Supp. C Wave 2…	1.0d	26-Feb-26	26-Feb-26	19.0d
1697	2C-W2-PC-20	Draft & Issue LOI - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 Pu…	3.0d	27-Feb-26	3-Mar-26	355.0d
1698	2C-W2-PC-30	Contract Development, Review, & Issuance - Architectural Millwork Trade Partn…	10.0d	4-Mar-26	17-Mar-26	355.0d
1699	2C-W2-PC-40	Contract Negoation - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 …	10.0d	18-Mar-26	31-Mar-26	355.0d
1700	2C-W2-PC-50	Contract Execution - Architectural Millwork Trade Partner - P2 Supp. C Wave 2 …	5.0d	1-Apr-26	7-Apr-26	355.0d
1701	2C-W2-PC-60	Contract Execution Complete - Architectural Millwork Trade Partner - P2 Supp. …	0.0d		7-Apr-26	355.0d
1702	WBS - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	27-Feb-26	8-Apr-26	155.0d
1703	2C-W2-PC-250	Purchasing Meeting - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purc…	1.0d	27-Feb-26	27-Feb-26	19.0d
1704	2C-W2-PC-260	Draft & Issue LOI - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purchasi…	3.0d	2-Mar-26	4-Mar-26	155.0d
1705	2C-W2-PC-270	Contract Development, Review, & Issuance - Overhead Doors Trade Partner - P…	10.0d	5-Mar-26	18-Mar-26	155.0d
1706	2C-W2-PC-280	Contract Negoation - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purch…	10.0d	19-Mar-26	1-Apr-26	155.0d
1707	2C-W2-PC-290	Contract Execution - Overhead Doors Trade Partner - P2 Supp. C Wave 2 Purch…	5.0d	2-Apr-26	8-Apr-26	155.0d
1708	2C-W2-PC-300	Contract Execution Complete - Overhead Doors Trade Partner - P2 Supp. C Wav…	0.0d		8-Apr-26	155.0d
1709	WBS - Airport Access Controls Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	3-Mar-26	10-Apr-26	479.0d
1710	2C-W2-PC-70	Purchasing Meeting - Airport Access Controls Trade Partner - P2 Supp. C Wave …	1.0d	3-Mar-26	3-Mar-26	19.0d
1711	2C-W2-PC-80	Draft & Issue LOI - Airport Access Controls Trade Partner - P2 Supp. C Wave 2 P…	3.0d	4-Mar-26	6-Mar-26	479.0d
1712	2C-W2-PC-90	Contract Development, Review, & Issuance - Airport Access Controls Trade Part…	10.0d	9-Mar-26	20-Mar-26	479.0d
1713	2C-W2-PC-100	Contract Negoation - Airport Access Controls Trade Partner - P2 Supp. C Wave …	10.0d	23-Mar-26	3-Apr-26	479.0d
1714	2C-W2-PC-110	Contract Execution - Airport Access Controls Trade Partner - P2 Supp. C Wave 2…	5.0d	6-Apr-26	10-Apr-26	479.0d
1715	2C-W2-PC-120	Contract Execution Complete - Airport Access Controls Trade Partner - P2 Supp…	0.0d		10-Apr-26	479.0d
1716	WBS - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	4-Mar-26	13-Apr-26	380.0d
1717	2C-W2-PC-310	Purchasing Meeting - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasi…	1.0d	4-Mar-26	4-Mar-26	19.0d
1718	2C-W2-PC-320	Draft & Issue LOI - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasing …	3.0d	5-Mar-26	9-Mar-26	380.0d
1719	2C-W2-PC-330	Contract Development, Review, & Issuance - Tile & Stone Trade Partner - P2 Su…	10.0d	10-Mar-26	23-Mar-26	380.0d
1720	2C-W2-PC-340	Contract Negoation - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasin…	10.0d	24-Mar-26	6-Apr-26	380.0d
1721	2C-W2-PC-350	Contract Execution - Tile & Stone Trade Partner - P2 Supp. C Wave 2 Purchasin…	5.0d	7-Apr-26	13-Apr-26	380.0d
1722	2C-W2-PC-360	Contract Execution Complete - Tile & Stone Trade Partner - P2 Supp. C Wave 2 …	0.0d		13-Apr-26	380.0d




	ID	Name	Dur	Start	Finish	TF
1723	WBS - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	5-Mar-26	14-Apr-26	398.0d
1724	2C-W2-PC-610	Purchasing Meeting - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing &...	1.0d	5-Mar-26	5-Mar-26	19.0d
1725	2C-W2-PC-620	Draft & Issue LOI - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	3.0d	6-Mar-26	10-Mar-26	398.0d
1726	2C-W2-PC-630	Contract Development, Review, & Issuance - Signage Trade Partner - P2 Supp. ...	10.0d	11-Mar-26	24-Mar-26	398.0d
1727	2C-W2-PC-640	Contract Negoation - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	10.0d	25-Mar-26	7-Apr-26	398.0d
1728	2C-W2-PC-650	Contract Execution - Signage Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	5.0d	8-Apr-26	14-Apr-26	398.0d
1729	2C-W2-PC-660	Contract Execution Complete - Signage Trade Partner - P2 Supp. C Wave 2 Purc...	0.0d		14-Apr-26	398.0d
1730	WBS - Toilet Partitions & Accessories Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	6-Mar-26	15-Apr-26	367.0d
1731	2C-W2-PC-670	Purchasing Meeting - Toilet Partitions & Accessories Trade Partner - P2 Supp. C...	1.0d	6-Mar-26	6-Mar-26	19.0d
1732	2C-W2-PC-680	Draft & Issue LOI - Toilet Partitions & Accessories Trade Partner - P2 Supp. C W...	3.0d	9-Mar-26	11-Mar-26	367.0d
1733	2C-W2-PC-690	Contract Development, Review, & Issuance - Toilet Partitions & Accessories Tra...	10.0d	12-Mar-26	25-Mar-26	367.0d
1734	2C-W2-PC-700	Contract Negoation - Toilet Partitions & Accessories Trade Partner - P2 Supp. C...	10.0d	26-Mar-26	8-Apr-26	367.0d
1735	2C-W2-PC-710	Contract Execution - Toilet Partitions & Accessories Trade Partner - P2 Supp. C ...	5.0d	9-Apr-26	15-Apr-26	367.0d
1736	2C-W2-PC-720	Contract Execution Complete - Toilet Partitions & Accessories Trade Partner - P...	0.0d		15-Apr-26	367.0d
1737	WBS - Building Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	10-Mar-26	17-Apr-26	567.0d
1738	2C-W2-PC-730	Purchasing Meeting - Building Specialties Trade Partner - P2 Supp. C Wave 2 P...	1.0d	10-Mar-26	10-Mar-26	19.0d
1739	2C-W2-PC-740	Draft & Issue LOI - Building Specialties Trade Partner - P2 Supp. C Wave 2 Purc...	3.0d	11-Mar-26	13-Mar-26	567.0d
1740	2C-W2-PC-750	Contract Development, Review, & Issuance - Building Specialties Trade Partner ...	10.0d	16-Mar-26	27-Mar-26	567.0d
1741	2C-W2-PC-760	Contract Negoation - Building Specialties Trade Partner - P2 Supp. C Wave 2 Pu...	10.0d	30-Mar-26	10-Apr-26	567.0d
1742	2C-W2-PC-770	Contract Execution - Building Specialties Trade Partner - P2 Supp. C Wave 2 Pur...	5.0d	13-Apr-26	17-Apr-26	567.0d
1743	2C-W2-PC-780	Contract Execution Complete - Building Specialties Trade Partner - P2 Supp. C ...	0.0d		17-Apr-26	567.0d
1744	WBS - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	11-Mar-26	20-Apr-26	22.0d
1745	2C-W2-PC-190	Purchasing Meeting - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave ...	1.0d	11-Mar-26	11-Mar-26	19.0d
1746	2C-W2-PC-200	Draft & Issue LOI - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave 2 P...	3.0d	12-Mar-26	16-Mar-26	22.0d
1747	2C-W2-PC-210	Contract Development, Review, & Issuance - Paints & Wall Coverings Trade Part...	10.0d	17-Mar-26	30-Mar-26	22.0d
1748	2C-W2-PC-220	Contract Negoation - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave ...	10.0d	31-Mar-26	13-Apr-26	22.0d
1749	2C-W2-PC-230	Contract Execution - Paints & Wall Coverings Trade Partner - P2 Supp. C Wave ...	5.0d	14-Apr-26	20-Apr-26	22.0d
1750	2C-W2-PC-240	Contract Execution Complete - Paints & Wall Coverings Trade Partner - P2 Sup...	0.0d		20-Apr-26	22.0d
1751	WBS - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	12-Mar-26	21-Apr-26	456.0d
1752	2C-W2-PC-490	Purchasing Meeting - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchas...	1.0d	12-Mar-26	12-Mar-26	144.0d
1753	2C-W2-PC-500	Draft & Issue LOI - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasing...	3.0d	13-Mar-26	17-Mar-26	456.0d
1754	2C-W2-PC-510	Contract Development, Review, & Issuance - Access Floors Trade Partner - P2 S...	10.0d	18-Mar-26	31-Mar-26	456.0d
1755	2C-W2-PC-520	Contract Negoation - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasi...	10.0d	1-Apr-26	14-Apr-26	456.0d
1756	2C-W2-PC-530	Contract Execution - Access Floors Trade Partner - P2 Supp. C Wave 2 Purchasi...	5.0d	15-Apr-26	21-Apr-26	456.0d
1757	2C-W2-PC-540	Contract Execution Complete - Access Floors Trade Partner - P2 Supp. C Wave ...	0.0d		21-Apr-26	456.0d
1758	WBS - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	13-Mar-26	22-Apr-26	443.0d
1759	2C-W2-PC-1150	Purchasing Meeting - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	1.0d	13-Mar-26	13-Mar-26	144.0d
1760	2C-W2-PC-1160	Draft & Issue LOI - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	3.0d	16-Mar-26	18-Mar-26	443.0d
1761	2C-W2-PC-1170	Contract Development, Review, & Issuance - Fencing Trade Partner - P2 Supp. ...	10.0d	19-Mar-26	1-Apr-26	443.0d
1762	2C-W2-PC-1180	Contract Negoation - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	10.0d	2-Apr-26	15-Apr-26	443.0d
1763	2C-W2-PC-1190	Contract Execution - Fencing Trade Partner - P2 Supp. C Wave 2 Purchasing & ...	5.0d	16-Apr-26	22-Apr-26	443.0d
1764	2C-W2-PC-1200	Contract Execution Complete - Fencing Trade Partner - P2 Supp. C Wave 2 Purc...	0.0d		22-Apr-26	443.0d




	ID	Name	Dur	Start	Finish	TF
1765	WBS - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		31.0d	17-Mar-26	28-Apr-26	146.0d
1766	2C-W2-PC-790	Purchasing Meeting - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 ...	1.0d	17-Mar-26	17-Mar-26	144.0d
1767	2C-W2-PC-800	Draft & Issue LOI - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 Pur...	4.0d	18-Mar-26	23-Mar-26	146.0d
1768	2C-W2-PC-810	Contract Development, Review, & Issuance - Wire Mesh Partitions Trade Partne...	11.0d	24-Mar-26	7-Apr-26	146.0d
1769	2C-W2-PC-820	Contract Negoation - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 P...	10.0d	8-Apr-26	21-Apr-26	146.0d
1770	2C-W2-PC-830	Contract Execution - Wire Mesh Partitions Trade Partner - P2 Supp. C Wave 2 P...	5.0d	22-Apr-26	28-Apr-26	146.0d
1771	2C-W2-PC-840	Contract Execution Complete - Wire Mesh Partitions Trade Partner - P2 Supp. C...	0.0d		28-Apr-26	146.0d
1772	WBS - Window Coverings Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	18-Mar-26	27-Apr-26	497.0d
1773	2C-W2-PC-1030	Purchasing Meeting - Window Coverings Trade Partner - P2 Supp. C Wave 2 Pu...	1.0d	18-Mar-26	18-Mar-26	359.0d
1774	2C-W2-PC-1040	Draft & Issue LOI - Window Coverings Trade Partner - P2 Supp. C Wave 2 Purch...	3.0d	19-Mar-26	23-Mar-26	497.0d
1775	2C-W2-PC-1050	Contract Development, Review, & Issuance - Window Coverings Trade Partner -...	10.0d	24-Mar-26	6-Apr-26	497.0d
1776	2C-W2-PC-1060	Contract Negoation - Window Coverings Trade Partner - P2 Supp. C Wave 2 Pur...	10.0d	7-Apr-26	20-Apr-26	497.0d
1777	2C-W2-PC-1070	Contract Execution - Window Coverings Trade Partner - P2 Supp. C Wave 2 Pur...	5.0d	21-Apr-26	27-Apr-26	497.0d
1778	2C-W2-PC-1080	Contract Execution Complete - Window Coverings Trade Partner - P2 Supp. C ...	0.0d		27-Apr-26	497.0d
1779	WBS - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	19-Mar-26	28-Apr-26	361.0d
1780	2C-W2-PC-850	Purchasing Meeting - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & C...	1.0d	19-Mar-26	19-Mar-26	359.0d
1781	2C-W2-PC-860	Draft & Issue LOI - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Contr...	3.0d	20-Mar-26	24-Mar-26	361.0d
1782	2C-W2-PC-870	Contract Development, Review, & Issuance - FF&E Trade Partner - P2 Supp. C ...	10.0d	25-Mar-26	7-Apr-26	361.0d
1783	2C-W2-PC-880	Contract Negoation - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	10.0d	8-Apr-26	21-Apr-26	361.0d
1784	2C-W2-PC-890	Contract Execution - FF&E Trade Partner - P2 Supp. C Wave 2 Purchasing & Co...	5.0d	22-Apr-26	28-Apr-26	361.0d
1785	2C-W2-PC-900	Contract Execution Complete - FF&E Trade Partner - P2 Supp. C Wave 2 Purcha...	0.0d		28-Apr-26	361.0d
1786	WBS - Interior Plants & Planters Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	20-Mar-26	29-Apr-26	489.0d
1787	2C-W2-PC-1090	Purchasing Meeting - Interior Plants & Planters Trade Partner - P2 Supp. C Wav...	1.0d	20-Mar-26	20-Mar-26	439.0d
1788	2C-W2-PC-1100	Draft & Issue LOI - Interior Plants & Planters Trade Partner - P2 Supp. C Wave 2 ...	3.0d	23-Mar-26	25-Mar-26	489.0d
1789	2C-W2-PC-1110	Contract Development, Review, & Issuance - Interior Plants & Planters Trade Pa...	10.0d	26-Mar-26	8-Apr-26	489.0d
1790	2C-W2-PC-1120	Contract Negoation - Interior Plants & Planters Trade Partner - P2 Supp. C Wav...	10.0d	9-Apr-26	22-Apr-26	489.0d
1791	2C-W2-PC-1130	Contract Execution - Interior Plants & Planters Trade Partner - P2 Supp. C Wave...	5.0d	23-Apr-26	29-Apr-26	489.0d
1792	2C-W2-PC-1140	Contract Execution Complete - Interior Plants & Planters Trade Partner - P2 Sup...	0.0d		29-Apr-26	489.0d
1793	WBS - Bird Control Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	24-Mar-26	1-May-26	464.0d
1794	2C-W2-PC-1210	Purchasing Meeting - Bird Control Specialties Trade Partner - P2 Supp. C Wave ...	1.0d	24-Mar-26	24-Mar-26	439.0d
1795	2C-W2-PC-1220	Draft & Issue LOI - Bird Control Specialties Trade Partner - P2 Supp. C Wave 2 P...	3.0d	25-Mar-26	27-Mar-26	464.0d
1796	2C-W2-PC-1230	Contract Development, Review, & Issuance - Bird Control Specialties Trade Part...	10.0d	30-Mar-26	10-Apr-26	464.0d
1797	2C-W2-PC-1240	Contract Negoation - Bird Control Specialties Trade Partner - P2 Supp. C Wave ...	10.0d	13-Apr-26	24-Apr-26	464.0d
1798	2C-W2-PC-1250	Contract Execution - Bird Control Specialties Trade Partner - P2 Supp. C Wave 2...	5.0d	27-Apr-26	1-May-26	464.0d
1799	2C-W2-PC-1260	Contract Execution Complete - Bird Control Specialties Trade Partner - P2 Supp...	0.0d		1-May-26	464.0d
1800	WBS - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	25-Mar-26	4-May-26	440.0d
1801	2C-W2-PC-550	Purchasing Meeting - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purch...	1.0d	25-Mar-26	25-Mar-26	439.0d
1802	2C-W2-PC-560	Draft & Issue LOI - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purchasin...	3.0d	26-Mar-26	30-Mar-26	440.0d
1803	2C-W2-PC-570	Contract Development, Review, & Issuance - Site Specialties Trade Partner - P2 ...	10.0d	31-Mar-26	13-Apr-26	440.0d
1804	2C-W2-PC-580	Contract Negoation - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purcha...	10.0d	14-Apr-26	27-Apr-26	440.0d
1805	2C-W2-PC-590	Contract Execution - Site Specialties Trade Partner - P2 Supp. C Wave 2 Purcha...	5.0d	28-Apr-26	4-May-26	440.0d
1806	2C-W2-PC-600	Contract Execution Complete - Site Specialties Trade Partner - P2 Supp. C Wave...	0.0d		4-May-26	440.0d




	ID	Name	Dur	Start	Finish	TF
1807	WBS - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purchasing & Contracting		29.0d	26-Mar-26	5-May-26	467.0d
1808	2C-W2-PC-910	Purchasing Meeting - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purch...	1.0d	26-Mar-26	26-Mar-26	466.0d
1809	2C-W2-PC-920	Draft & Issue LOI - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purchasi...	3.0d	27-Mar-26	31-Mar-26	467.0d
1810	2C-W2-PC-930	Contract Development, Review, & Issuance - Metal Canopies Trade Partner - P2...	10.0d	1-Apr-26	14-Apr-26	467.0d
1811	2C-W2-PC-940	Contract Negoation - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purch...	10.0d	15-Apr-26	28-Apr-26	467.0d
1812	2C-W2-PC-950	Contract Execution - Metal Canopies Trade Partner - P2 Supp. C Wave 2 Purcha...	5.0d	29-Apr-26	5-May-26	467.0d
1813	2C-W2-PC-960	Contract Execution Complete - Metal Canopies Trade Partner - P2 Supp. C Wav...	0.0d		5-May-26	467.0d
1814	WBS - HCAA Alternative Procurement Preconstruction		975.0d	9-Dec-24 A	9-Oct-28	50.0d
1815	WBS - Concessions Program Preconstruction (by Others)		879.0d	9-Dec-24 A	23-May-28	4.0d
1816	HA-AL-CP-100	Concessions - Concessions Development	279.0d	9-Dec-24 A	14-Jan-26	4.0d
1817	HA-AL-CP-120	Concessions - Leasing Model/Business Structure (HCAA)	102.0d	15-Jan-26	8-Jun-26	4.0d
1818	HA-AL-CP-130	Concessions - RFP Development (HCAA)	132.0d	9-Jun-26	15-Dec-26	4.0d
1819	HA-AL-CP-150	Concessions - Concessionaires RFP Solicitation (HCAA)	177.0d	24-Dec-26	2-Sep-27	4.0d
1820	HA-AL-CP-160	Concessions - Concessionaires Design/Permitting Period (HCAA)	183.0d	3-Sep-27	23-May-28	4.0d
1821	WBS - Artwork Preconstruction (Coordination with DB Team)		855.0d	29-May-25 A	9-Oct-28	50.0d
1822	HA-AL-AW-10	Artwork - HCAA Requests for Proposals, Review & Selection of Artists	75.0d	29-May-25 A	12-Sep-25 A	
1823	HA-AL-AW-15	Artwork - Public Art Committee Orientation Meeting	1.0d	15-Sep-25 A	15-Sep-25 A	
1824	HA-AL-AW-20	Artwork - Issue Call for Artists (AS D Part 1 Awarded August 2023)	105.0d	16-Sep-25 A	13-Feb-26	50.0d
1825	HA-AL-AW-30	Artwork - Artist Outreach Conference (SkyCenter One)	5.0d	16-Feb-26	20-Feb-26	50.0d
1826	HA-AL-AW-40	Artwork - Deadline for Submissions	20.0d	23-Feb-26	20-Mar-26	50.0d
1827	HA-AL-AW-50	Artwork -Technical Evaluation Committee	3.0d	23-Mar-26	25-Mar-26	50.0d
1828	HA-AL-AW-60	Artwork - Present TEC recommendations to Art Committee	10.0d	26-Mar-26	8-Apr-26	50.0d
1829	HA-AL-AW-70	Artwork - Board Consideration | Artists Invited to Propose	46.0d	9-Apr-26	12-Jun-26	50.0d
1830	HA-AL-AW-80	Artwork - Pre-Solicitation Conference | Not Mandatory	2.0d	15-Jun-26	16-Jun-26	50.0d
1831	HA-AL-AW-90	Artwork - Question Deadline	20.0d	17-Jun-26	15-Jul-26	50.0d
1832	HA-AL-AW-100	Artwork - Final Addendum Posted	8.0d	16-Jul-26	27-Jul-26	50.0d
1833	HA-AL-AW-110	Artwork - Artist Presentations & Final Selections	35.0d	28-Jul-26	15-Sep-26	50.0d
1834	HA-AL-AW-120	Artwork - Board Consideration | Final Artist Selections	45.0d	16-Sep-26	17-Nov-26	50.0d
1835	HA-AL-AW-130	Artwork - Artist Design Period	100.0d	18-Nov-26	12-Apr-27	50.0d
1836	HA-AL-AW-140	Artwork - HP/HNTB Develop Artwork Infrastructure	60.0d	13-Apr-27	7-Jul-27	50.0d
1837	HA-AL-AW-150	Artwork - HP Build Artwork Infrastructure	80.0d	8-Jul-27	28-Oct-27	50.0d
1838	HA-AL-AW-160	Artwork - Artist Fab. & Ship Artwork	338.0d	29-Oct-27	9-Oct-28	70.0d
1839	WBS - Delta Airlines Preconstruction (Coordination with DB Team)		385.0d	15-Jan-26	20-Jul-27	200.0d
1840	HA-AL-DL-178	Delta Airlines - RFQ/RFP (HCAA)	90.0d	15-Jan-26	20-May-26	200.0d
1841	HA-AL-DL-188	Delta Airlines - Delta Airlines Selection (HCAA)	50.0d	21-May-26	31-Jul-26	200.0d
1842	HA-AL-DL-198	Delta Airlines - Delta Airlines Award Period (HCAA)	60.0d	3-Aug-26	26-Oct-26	200.0d
1843	HA-AL-DL-208	Delta Airlines - Delta Airlines Design Period (HCAA)	125.0d	27-Oct-26	23-Apr-27	200.0d
1844	HA-AL-DL-218	Delta Airlines - Delta Airlines Permitting Period (HCAA)	60.0d	26-Apr-27	20-Jul-27	200.0d
1845	WBS - Unassigned Airline Ops (Coordination with DB Team)		385.0d	15-Jan-26	20-Jul-27	311.0d
1846	HA-AL-AR-228	Unassigned Airline Ops - RFQ/RFP (HCAA)	90.0d	15-Jan-26	20-May-26	311.0d
1847	HA-AL-AR-238	Unassigned Airline Ops - Unassigned Airline Ops Selection (HCAA)	50.0d	21-May-26	31-Jul-26	311.0d
1848	HA-AL-AR-248	Unassigned Airline Ops - Unassigned Airline Ops Award Period (HCAA)	60.0d	3-Aug-26	26-Oct-26	311.0d

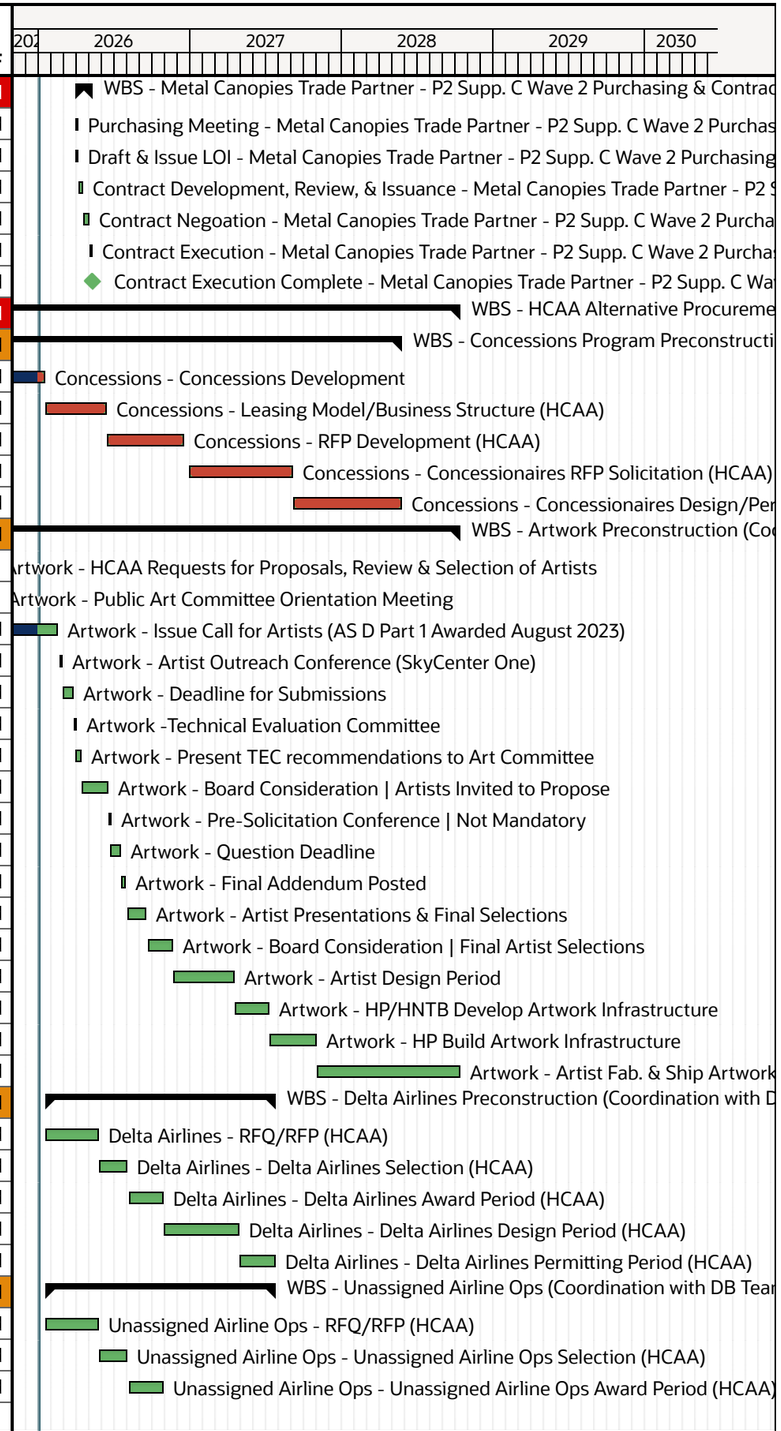


	ID	Name	Dur	Start	Finish	TF
1849	HA-AL-AR-258	Unassigned Airline Ops - Unassigned Airline Ops Design Period (HCAA)	125.0d	27-Oct-26	23-Apr-27	311.0d
1850	HA-AL-AR-268	Unassigned Airline Ops- Unassigned Airline Ops Permitting Period (HCAA)	60.0d	26-Apr-27	20-Jul-27	311.0d
1851	WBS - HCAA Common Club (Coordination with DB Team)		385.0d	15-Jan-26	20-Jul-27	221.0d
1852	HA-AL-CL-278	HCAA Common Club Tenant - RFQ/RFP (HCAA)	90.0d	15-Jan-26	20-May-26	221.0d
1853	HA-AL-CL-288	HCAA Common Club Tenant - HCAA Common Club Tenant Selection (HCAA)	50.0d	21-May-26	31-Jul-26	221.0d
1854	HA-AL-CL-298	HCAA Common Club Tenant - HCAA Common Club Tenant Award Period (HCAA)	60.0d	3-Aug-26	26-Oct-26	221.0d
1855	HA-AL-CL-308	HCAA Common Club Tenant - HCAA Common Club Tenant Design Period (HC...	125.0d	27-Oct-26	23-Apr-27	221.0d
1856	HA-AL-CL-318	HCAA Common Club Tenant - HCAA Common Club Tenant Permitting Period (...	60.0d	26-Apr-27	20-Jul-27	221.0d
1857	WBS - ASD - CITY OF TAMPA PERMITTING		266.0d	20-Mar-25 A	7-Apr-26	747.0d
1858	WBS - Early Foundations Permit		114.0d	10-Apr-25 A	22-Sep-25 A	
1859	ASDEF-PER-10	Docs. Complete - Early Found. Permit	0.0d		10-Apr-25 A	
1860	ASDEF-PER-20	Prepare Docs. / HCAA Review / Page Turn - Early Found. Permit	10.0d	11-Apr-25 A	24-Apr-25 A	
1861	ASDEF-PER-30	Submit Found. Docs. to COT - Early Found. Permit	1.0d	3-Jul-25 A	3-Jul-25 A	
1862	ASDEF-PER-135	Threshold Letter Completion & Received from HCAA - Early Found. Permit	30.0d	7-Jul-25 A	15-Aug-25 A	
1863	ASDEF-PER-40	COT Initial Subm. Review - Early Found. Permit	15.0d	18-Aug-25 A	8-Sep-25 A	
1864	ASDEF-PER-50	COT Initial Subm. Review Comments Received - Early Found. Permit	1.0d	9-Sep-25 A	9-Sep-25 A	
1865	ASDEF-PER-70	Submit Found. Revision # 1 to COT - Early Found. Permit	1.0d	10-Sep-25 A	10-Sep-25 A	
1866	ASDEF-PER-60	Design Team Respond to Initial Comments - Early Found. Permit	1.0d	10-Sep-25 A	10-Sep-25 A	
1867	ASDEF-PER-80	COT Revision #1 Review - Early Found. Permit	7.0d	11-Sep-25 A	19-Sep-25 A	
1868	ASDEF-PER-130	Anticipated Found. Permit Approval by COT - Early Found. Permit	1.0d	22-Sep-25 A	22-Sep-25 A	
1869	WBS - ITB1 - Apron, Site and Utilities Permit (comm. Misc)		62.0d	20-Mar-25 A	17-Jun-25 A	
1870	ASDEF-PER-ITB1-140	Docs. Complete - ITB1 Apron/Site & Util.	0.0d		20-Mar-25 A	
1871	ASDEF-PER-ITB1-150	Prepare Docs. / HCAA Review / Page Turn - ITB1 Apron/Site & Util.	11.0d	21-Mar-25 A	4-Apr-25 A	
1872	ASDEF-PER-ITB1-160	Submit ITB1 Docs. to COT - ITB1 Apron/Site & Util.	1.0d	7-Apr-25 A	7-Apr-25 A	
1873	ASDEF-PER-ITB1-170	COT Initial Subm. Review - ITB1 Apron/Site & Util.	22.0d	8-Apr-25 A	7-May-25 A	
1874	ASDEF-PER-ITB1-180	COT Initial Subm. Review Comments Received - ITB1 Apron/Site & Util.	1.0d	8-May-25 A	8-May-25 A	
1875	ASDEF-PER-ITB1-190	Design Team Respond to Initial Comments - ITB1 Apron/Site & Util.	10.0d	9-May-25 A	22-May-25 A	
1876	ASDEF-PER-ITB1-200	Submit ITB1 Revision # 1 to COT - ITB1 Apron/Site & Util.	1.0d	23-May-25 A	23-May-25 A	
1877	ASDEF-PER-ITB1-210	COT Revision # 1 Review - ITB1 Apron/Site & Util.	6.0d	27-May-25 A	3-Jun-25 A	
1878	ASDEF-PER-ITB1-260	Anticipated ITB1 Permit Approval by COT - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1879	ASDEF-PER-ITB1-220	ITB 1 Revision #1 Review Comments Received - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1880	ASDEF-PER-ITB1-212	ITB 1 Permit Approval by COT (6-4-25) - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1881	ASDEF-PER-ITB1-230	Design Team Respond to Revision #1 comments - ITB1 Apron/Site & Util.	9.0d	5-Jun-25 A	17-Jun-25 A	
1882	WBS - ITB2 - PBB Permit		107.0d	10-Apr-25 A	11-Sep-25 A	
1883	ASDEF-PER-ITB2-270	Docs. Complete - ITB2 PBB Permit	0.0d		10-Apr-25 A	
1884	ASDEF-PER-ITB2-280	Prepare Docs. / HCAA Review / Page Turn - ITB2 PBB Permit	10.0d	11-Apr-25 A	24-Apr-25 A	
1885	ASDEF-PER-ITB2-290	Submit ITB2 Docs. to COT - ITB2 PBB Permit	1.0d	15-Jul-25 A	15-Jul-25 A	
1886	ASDEF-PER-ITB2-300	COT Initial Subm. Review - ITB2 PBB Permit	17.0d	16-Jul-25 A	7-Aug-25 A	
1887	ASDEF-PER-ITB2-310	COT Initial Subm. Review Comments Received - ITB2 PBB Permit	1.0d	8-Aug-25 A	8-Aug-25 A	
1888	ASDEF-PER-ITB2-320	Design Team Respond to Initial Comments - ITB2 PBB Permit	14.0d	11-Aug-25 A	28-Aug-25 A	
1889	ASDEF-PER-ITB2-330	Submit ITB2 Revision # 1 to COT - ITB2 PBB Permit	1.0d	29-Aug-25 A	29-Aug-25 A	
1890	ASDEF-PER-ITB2-340	COT Revision #1 Review - ITB2 PBB Permit	7.0d	2-Sep-25 A	10-Sep-25 A	

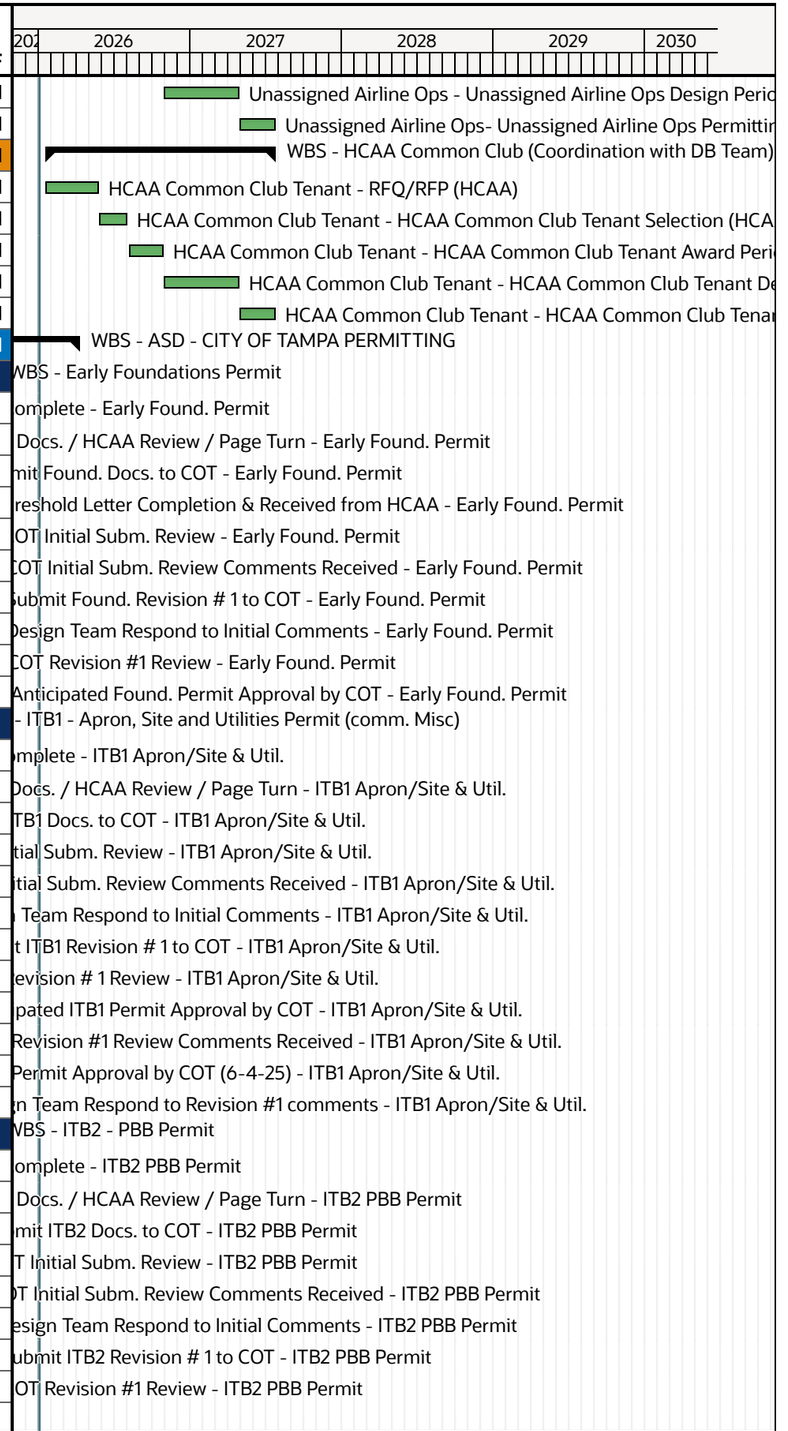


	ID	Name	Dur	Start	Finish	TF
1891	ASDEF-PER-ITB2-390	Anticipated ITB 2 Permit Approval by COT - ITB2 PBB Permit	1.0d	11-Sep-25 A	11-Sep-25 A	
1892	WBS - ITB3 - Structural Guideway Permit		137.0d	10-Apr-25 A	22-Oct-25 A	
1893	ASDEF-PER-ITB3-410	Prepare Docs. / HCAA Review / Page Turn - ITB3 Struct. Gdwy. Permit	1.0d	10-Apr-25 A	10-Apr-25 A	
1894	ASDEF-PER-ITB3-400	Docs. Complete - ITB3 Struct. Gdwy. Permit	0.0d		10-Apr-25 A	
1895	ASDEF-PER-ITB3-420	Submit ITB3 Docs. to COT (Submittal to HP) - ITB3 Struct. Gdwy. Permit	1.0d	3-Jul-25 A	3-Jul-25 A	
1896	ASDEF-PER-ITB3-525	Threshold Letter Completion & Received from HCAA - ITB3 Struct. Gdwy. Permit	50.0d	7-Jul-25 A	15-Sep-25 A	
1897	ASDEF-PER-ITB3-530	Submit ITB3 Docs. to COT - ITB3 Struct. Gdwy. Permit	1.0d	16-Sep-25 A	16-Sep-25 A	
1898	ASDEF-PER-ITB3-430	COT Initial Subm. Review - ITB3 Struct. Gdwy. Permit	1.0d	17-Sep-25 A	17-Sep-25 A	
1899	ASDEF-PER-ITB3-440	COT Initial Subm. Review Comments Received - ITB3 Struct. Gdwy. Permit	1.0d	1-Oct-25 A	1-Oct-25 A	
1900	ASDEF-PER-ITB3-450	Design Team Respond to Initial Comments - ITB3 Struct. Gdwy. Permit	9.0d	2-Oct-25 A	14-Oct-25 A	
1901	ASDEF-PER-ITB3-460	Submit ITB3 Initial Comment Responses to COT - ITB3 Struct. Gdwy. Permit	1.0d	15-Oct-25 A	15-Oct-25 A	
1902	ASDEF-PER-ITB3-520	ITB3 Permit Approval By COT - ITB3 Struct. Gdwy. Permit	1.0d	22-Oct-25 A	22-Oct-25 A	
1903	WBS - ASD Building Permit		143.0d	21-Aug-25 A	17-Mar-26	44.0d
1904	ASDEF-PER-ASD-530	Docs. Complete - ASD Building Permit	0.0d		21-Aug-25 A	
1905	ASDEF-PER-ASD-540	Prepare Docs. / HCAA Review / Page Turn - ASD Building Permit	10.0d	22-Aug-25 A	5-Sep-25 A	
1906	ASDEF-PER-ASD-550	Submit ASD Docs. to COT - ASD Building Permit	3.0d	15-Sep-25 A	17-Sep-25 A	
1907	ASDEF-PER-ASD-560	COT Initial Subm. Review - ASD Building Permit	36.0d	17-Sep-25 A	5-Nov-25 A	
1908	ASDEF-PER-ASD-570	COT Initial Subm. Review Comments Received - ASD Building Permit	1.0d	6-Nov-25 A	6-Nov-25 A	
1909	ASDEF-PER-ASD-580	Design Team Respond to Initial Comments - ASD Building Permit	9.0d	10-Nov-25 A	20-Nov-25 A	
1910	ASDEF-PER-ASD-590	Submit ASD Initial Comment Responses to COT - ASD Building Permit	2.0d	21-Nov-25 A	24-Nov-25 A	
1911	ASDEF-PER-ASD-640	COT Comment Response Subm. Review #1 - ASD Building Permit	29.0d	25-Nov-25 A	8-Jan-26	64.0d
1912	ASDEF-PER-ASD-645	ASD COT Revision #1 Comments Received - ASD Building Permit	1.0d	9-Jan-26	9-Jan-26	64.0d
1913	ASDEF-PER-ASD-646	Design Team Respond to Revision #1 Comments - ASD Building Permit	10.0d	12-Jan-26	23-Jan-26	64.0d
1914	ASDEF-PER-ASD-647	Submit ASD Revision #2 to COT - ASD Building Permit	1.0d	26-Jan-26	26-Jan-26	64.0d
1915	ASDEF-PER-ASD-648	ASD COT Review #2 - ASD Building Permit	15.0d	27-Jan-26	16-Feb-26	64.0d
1916	ASDEF-PER-ASD-650	Anticipated ASD Permit Approval By COT - ASD Building Permit	1.0d	17-Mar-26	17-Mar-26	44.0d
1917	WBS - CCBS Permit Main Terminal Building		71.0d	30-Oct-25 A	12-Feb-26	66.0d
1918	ASDEF-PER-MTB-660	Docs. Complete - Main Terminal Build. Permit / CCBS	0.0d		30-Oct-25 A	
1919	ASDEF-PER-MTB-670	Prepare Docs. / HCAA Review / Page Turn - Main Terminal Build. Permit / CCBS	3.0d	31-Oct-25 A	4-Nov-25 A	
1920	ASDEF-PER-MTB-680	Submit MT/BHS Document to HP/Beck for COT submission - Main Terminal Bui...	1.0d	5-Nov-25 A	5-Nov-25 A	
1921	ASDEF-PER-MTB-690	COT Initial Subm. Review - Main Terminal Build. Permit / CCBS	2.0d	6-Nov-25 A	7-Nov-25 A	
1922	ASDEF-PER-MTB-700	COT Initial Subm. Review Comments Received - Main Terminal Build. Permit / C...	16.0d	10-Nov-25 A	3-Dec-25 A	
1923	ASDEF-PER-MTB-705	MT BHS - COT initial comments Received - Main Terminal Build. Permit / CCBS	1.0d	4-Dec-25 A	4-Dec-25 A	
1924	ASDEF-PER-MTB-710	Design Team Respond to Initial Comments - Main Terminal Build. Permit / CCBS	9.0d	5-Dec-25 A	17-Dec-25 A	
1925	ASDEF-PER-MTB-720	Submit MT/BHS Revision #1 to COT - Main Terminal Build. Permit / CCBS	1.0d	18-Dec-25 A	18-Dec-25 A	
1926	ASDEF-PER-MTB-770	COT Revision #1 Review - Main Terminal Build. Permit / CCBS	15.0d	19-Dec-25 A	12-Jan-26	66.0d
1927	ASDEF-PER-MTB-772	MT BHS COT Revision #1 Comments Received - Main Terminal Build. Permit / ...	1.0d	13-Jan-26	13-Jan-26	66.0d
1928	ASDEF-PER-MTB-773	Design Team Respond to Revision #1 Comments - Main Terminal Build. Permit ...	10.0d	14-Jan-26	27-Jan-26	66.0d
1929	ASDEF-PER-MTB-774	Submit MT/BHS revision #2 to COT - Main Terminal Build. Permit / CCBS	1.0d	28-Jan-26	28-Jan-26	66.0d
1930	ASDEF-PER-MTB-775	Revision #2 COT Review - Main Terminal Build. Permit / CCBS	10.0d	29-Jan-26	11-Feb-26	66.0d
1931	ASDEF-PER-MTB-780	Anticipated MT/CCBS Permit Approval By COT - Main Terminal Build. Permit / ...	1.0d	12-Feb-26	12-Feb-26	66.0d
1932	WBS - Main Terminal Shuttle TI Permit		109.0d	30-Oct-25 A	7-Apr-26	359.0d

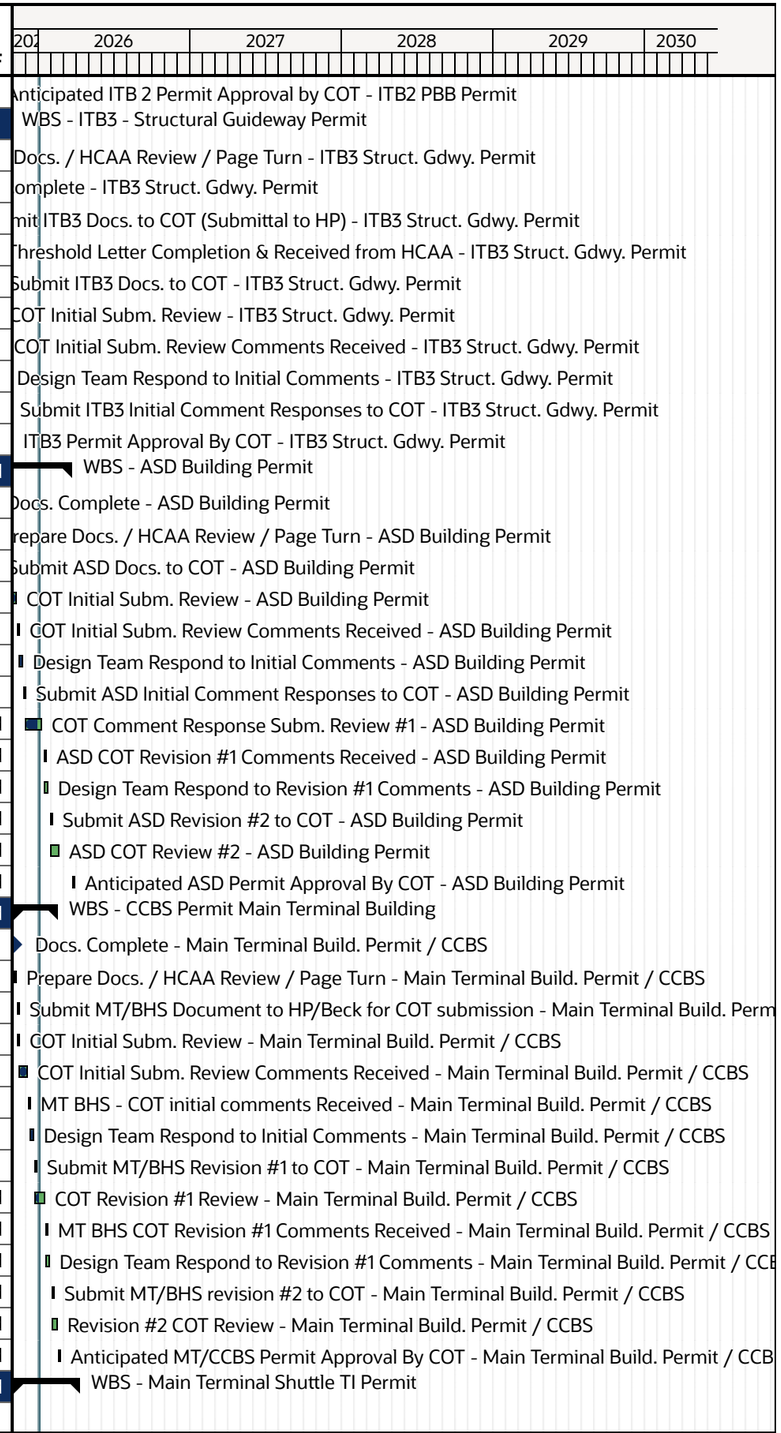


	ID	Name	Dur	Start	Finish	TF
1933	ASDEF-PER-MTS-790	Docs. Complete - Main Terminal Shuttle TI Permit	0.0d		30-Oct-25 A	
1934	ASDEF-PER-MTS-800	Prepare Docs. / HCAA Review / Page Turn - Main Terminal Shuttle TI Permit	5.0d	31-Oct-25 A	6-Nov-25 A	
1935	ASDEF-PER-MTS-810	Submit MT SP Docs. to COT - Main Terminal Shuttle TI Permit	1.0d	7-Nov-25 A	7-Nov-25 A	
1936	ASDEF-PER-MTS-815	Submit MT Shuttle TI Documents to COT - Main Terminal Shuttle TI Permit	24.0d	10-Nov-25 A	15-Dec-25 A	
1937	ASDEF-PER-MTS-820	COT Initial Subm. Review - Main Terminal Shuttle TI Permit	31.0d	16-Dec-25 A	29-Jan-26	359.0d
1938	ASDEF-PER-MTS-830	COT Initial Subm. Review Comments Received - Main Terminal Shuttle TI Permit	1.0d	30-Jan-26	30-Jan-26	359.0d
1939	ASDEF-PER-MTS-840	Design Team Respond to Initial Comments - Main Terminal Shuttle TI Permit	9.0d	2-Feb-26	12-Feb-26	359.0d
1940	ASDEF-PER-MTS-850	Submit MT Shuttle Comment Response to COT - Main Terminal Shuttle TI Permit	1.0d	13-Feb-26	13-Feb-26	359.0d
1941	ASDEF-PER-MTS-860	COT Revision #1 Review - Main Terminal Shuttle TI Permit	15.0d	16-Feb-26	6-Mar-26	359.0d
1942	ASDEF-PER-MTS-865	COT Revision #1 Review Comments - Main Terminal Shuttle TI Permit	1.0d	9-Mar-26	9-Mar-26	359.0d
1943	ASDEF-PER-MTS-867	Design Team Respond to Revision #1 Comments - Main Terminal Shuttle TI Per…	9.0d	10-Mar-26	20-Mar-26	359.0d
1944	ASDEF-PER-MTS-868	Submit MT Shuttle TI revision #2 to COT - Main Terminal Shuttle TI Permit	1.0d	23-Mar-26	23-Mar-26	359.0d
1945	ASDEF-PER-MTS-869	COT Review Comments Revision #2 - Main Terminal Shuttle TI Permit	10.0d	24-Mar-26	6-Apr-26	359.0d
1946	ASDEF-PER-MTS-910	Anticipated MT Shuttle Permit Approval By COT - Main Terminal Shuttle TI Permit	1.0d	7-Apr-26	7-Apr-26	359.0d
1947	WBS - ASD - GOVERNMENTAL/MUNICIPAL/FAA/SWFWMD/FDEP PERMITTING		433.0d	13-Aug-24 A	27-Apr-26	991.0d
1948	WBS - City of Tampa Utilities		415.0d	9-Sep-24 A	27-Apr-26	723.0d
1949	WBS - City of Tampa Water Department		415.0d	9-Sep-24 A	27-Apr-26	335.0d
1950	WBS - Part 2 Agreement - Enabling Package		221.0d	9-Sep-24 A	22-Jul-25 A	
1951	WBS - Enabling		221.0d	9-Sep-24 A	22-Jul-25 A	
1952	PM-P2-EN-200	Water Application Submission - Part 2 Agreement Enabling Pkg.	1.0d	9-Sep-24 A	9-Sep-24 A	
1953	PM-P2-EN-210	Water Commitment Letter - Part 2 Agreement Enabling Pkg.	151.0d	10-Sep-24 A	14-Apr-25 A	
1954	PM-P2-EN-220	Water Design Review Complete Part 2 Agreement Enabling Pkg.	68.0d	16-Apr-25 A	22-Jul-25 A	
1955	WBS - Part 1 Supplement C - Core & Shell Package		168.0d	28-Aug-25 A	27-Apr-26	335.0d
1956	PM-P2-2B-50	Water Application Submission - Part 2 Supp. C COT WD -Core, Shell & Finishes	1.0d	28-Aug-25 A	28-Aug-25 A	
1957	PM-P2-2B-40	Water Commitment Letter - Part 2 Supp. C COT WD -Core, Shell & Finishes	137.0d	29-Aug-25 A	16-Mar-26	44.0d
1958	PM-P2-2B-65	Water Design Review Complete - Part 2 Supp. C COT WD -Core, Shell & Finishes	30.0d	17-Mar-26	27-Apr-26	335.0d
1959	WBS - City of Tampa Waste Water Department		391.0d	9-Sep-24 A	24-Mar-26	359.0d
1960	WBS - Part 2 Agreement - Enabling Package		96.0d	9-Sep-24 A	24-Jan-25 A	
1961	WBS - Enabling		96.0d	9-Sep-24 A	24-Jan-25 A	
1962	PM-P2-EN-230	Wastewater Application Submission - Part 2 Enabling Pkg.	1.0d	9-Sep-24 A	9-Sep-24 A	
1963	PM-P2-EN-240	Wastewater Commitment Letter - Part 2 Enabling Pkg.	45.0d	10-Sep-24 A	11-Nov-24 A	
1964	PM-P2-EN-250	Wastewater Design Review Complete - Part 2 Enabling Pkg.	50.0d	12-Nov-24 A	24-Jan-25 A	
1965	WBS - Part 1 Supplement C- Core & Shell Package		81.0d	26-Nov-25 A	24-Mar-26	359.0d
1966	PM-P2-2B-70	Wastewater Application Submission - COT Core, Shell & Finishes	1.0d	26-Nov-25 A	26-Nov-25 A	
1967	PM-P2-2B-60	Wastewater Commitment Letter - COT Core, Shell & Finishes	31.0d	29-Dec-25	10-Feb-26	359.0d
1968	PM-P2-2B-90	Wastewater Design Review Complete - COT Core, Shell & Finishes	30.0d	11-Feb-26	24-Mar-26	359.0d
1969	WBS - City of Tampa Solid Waste		380.0d	9-Sep-24 A	9-Mar-26	758.0d
1970	WBS - Part 2 Agreement - Enabling Package		380.0d	9-Sep-24 A	9-Mar-26	758.0d
1971	WBS - Enabling		51.0d	9-Sep-24 A	18-Nov-24 A	
1972	PM-P2-2B-100	Solid Waste Application Submission - Part 2 Supp. B COT	1.0d	9-Sep-24 A	9-Sep-24 A	
1973	PM-P2-2B-110	Solid Waste Design Review Complete - Part 2 Supp. B COT	50.0d	10-Sep-24 A	18-Nov-24 A	
1974	WBS - Core & Shell		133.0d	28-Aug-25 A	9-Mar-26	758.0d

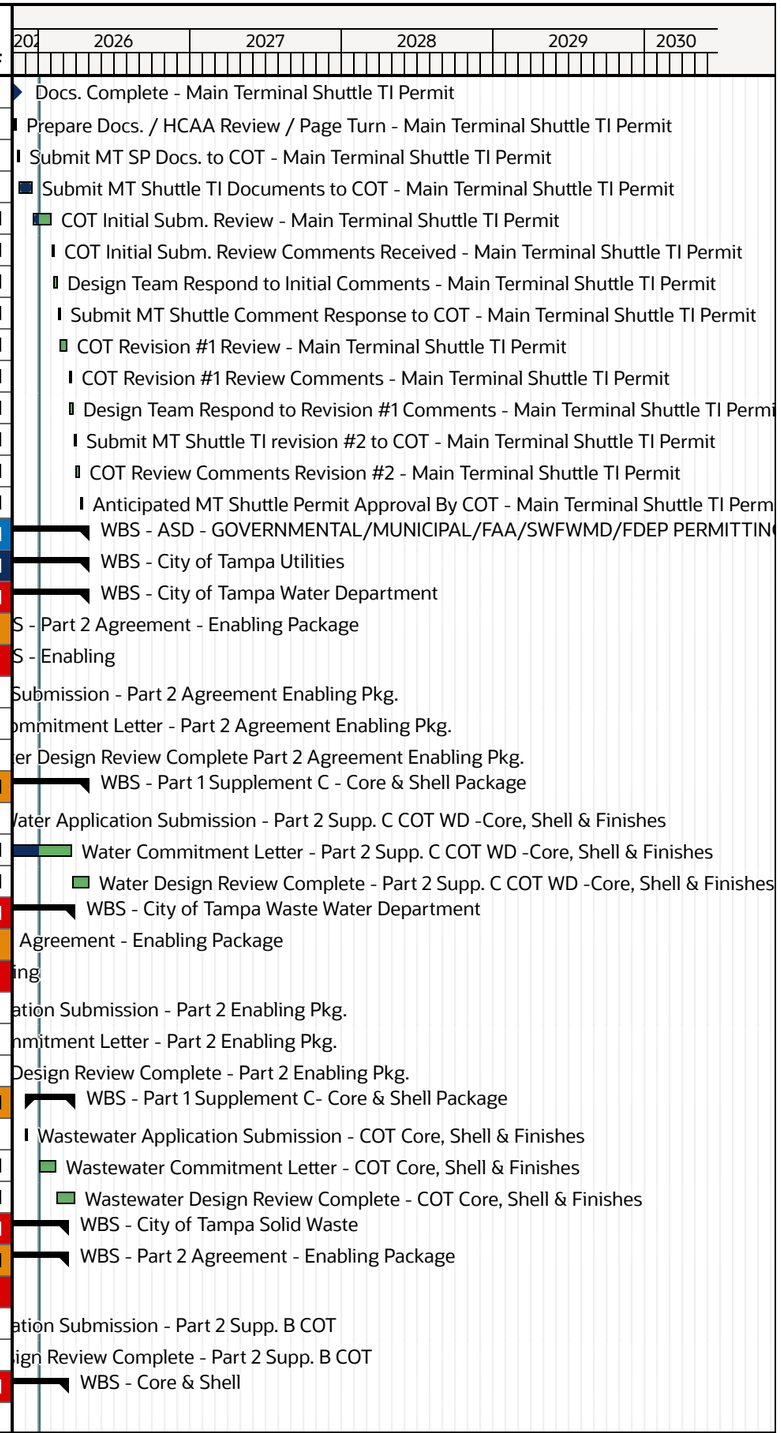

	ID	Name	Dur	Start	Finish	TF
1975	PM-P2-2B-120	Core & Shell Solid Waste Application Submission - Part 2 Supp. C COT	1.0d	28-Aug-25 A	28-Aug-25 A	
1976	PM-P2-2B-130	Core & Shell Solid Waste Design Review Complete - Part 2 Supp. C COT	132.0d	29-Aug-25 A	9-Mar-26	758.0d
1977	WBS - SWFWMD		59.0d	13-Aug-24 A	4-Nov-24 A	
1978	WBS - 8500 23 ASD - Site		59.0d	13-Aug-24 A	4-Nov-24 A	
1979	PM-SW-10	Site Drawing Set Pkg. Submission - 8500 23 ASD SWFWMD	1.0d	13-Aug-24 A	13-Aug-24 A	
1980	PM-SW-20	Site Drawing Set Pkg. Approval - 8500 23 ASD SWFWMD	58.0d	14-Aug-24 A	4-Nov-24 A	
1981	WBS - NPDES		62.0d	2-Sep-24 A	29-Nov-24 A	
1982	WBS - 8500 23 ASD - Site		62.0d	2-Sep-24 A	29-Nov-24 A	
1983	PM-EV-10	Site Drawing Set Pkg. Submission - 8500 23 ASD NPDES	0.0d	2-Sep-24 A	2-Sep-24 A	
1984	PM-EV-20	Site Drawing Set Pkg. Approval - 8500 23 ASD NPDES	62.0d	3-Sep-24 A	29-Nov-24 A	
1985	WBS - FDEP		290.0d	13-Dec-24 A	4-Feb-26	723.0d
1986	WBS - Part 2 Agreement - Enabling Package		1.0d	13-Dec-24 A	13-Dec-24 A	
1987	PM-FD-P2-EN-10	FDEP Part 2 - Enabling Drawing Pkg. Submission	1.0d	13-Dec-24 A	13-Dec-24 A	
1988	PM-FD-P2-EN-20	FDEP Part 2 - Enabling Drawing Pkg. Approval	1.0d	13-Dec-24 A	13-Dec-24 A	
1989	WBS - Part 1 Supplement C - Core & Shell Package		74.0d	20-Oct-25 A	4-Feb-26	723.0d
1990	PM-FD-P2-2B-20	Drawing Pkg. Submission - FDEP Part 2 Supp. C- Core, Shell & Finishes	1.0d	20-Oct-25 A	20-Oct-25 A	
1991	PM-FD-P2-2B-10	Drawing Pkg. Approval - FDEP Part 2 Supp. C- Core, Shell & Finishes	73.0d	21-Oct-25 A	4-Feb-26	723.0d
1992	WBS - FAA Permit		41.0d	29-Oct-24 A	27-Dec-24 A	
1993	PM-FA-10	FAA Permit - CSPP	41.0d	29-Oct-24 A	27-Dec-24 A	
1994	PM-FA-20	FAA Permit - 7460	24.0d	21-Nov-24 A	27-Dec-24 A	
1995	WBS - City of Tampa Construction Services		390.0d	28-Aug-24 A	12-Mar-26	765.0d
1996	WBS - Part 2 Agreement - Enabling Package		197.0d	28-Aug-24 A	6-Jun-25 A	
1997	WBS - Enabling - Master Permit		157.0d	28-Aug-24 A	10-Apr-25 A	
1998	PM-P2-EN-10	Part 2 Master Permit Enabling Pckg. Subm. Process	24.0d	28-Aug-24 A	1-Oct-24 A	
1999	PM-P2-EN-30	Part 2 Commence Master Permit Enabling Pckg. Submission	0.0d	1-Oct-24 A		
2000	PM-P2-EN-40	Part 2 Master Permit Enabling Pckg. Review & Approval	42.0d	2-Oct-24 A	2-Dec-24 A	
2001	PM-P2-EN-110	Part 2 State Administrator Paperwork Completed Prior To Removal Of Exist. Wells	4.0d	30-Dec-24 A	3-Jan-25 A	
2002	PM-P2-EN-130	Part 2 State Administrator Paperwork Completed at Conclusion to Removal of E...	5.0d	13-Jan-25 A	17-Jan-25 A	
2003	WBS - Enabling - Trade Permits		145.0d	16-Sep-24 A	10-Apr-25 A	
2004	PM-P2-EN-20	SWFWMD Permit - Enabling Trade Permits	36.0d	16-Sep-24 A	4-Nov-24 A	
2005	PM-P2-EN-60	Elec. Trade Permit - Enabling Trade Permits	1.0d	5-Feb-25 A	5-Feb-25 A	
2006	PM-P2-EN-100	Dewatering - Enabling Trade Permits	1.0d	10-Apr-25 A	10-Apr-25 A	
2007	WBS - Trailer Complex - Master Permit		49.0d	31-Mar-25 A	6-Jun-25 A	
2008	PM-P2-EN-120	Trailer Complex Master Permit Pkg. Approval	35.0d	31-Mar-25 A	16-May-25 A	
2009	WBS - Trailer Complex - Trade Permits		14.0d	19-May-25 A	6-Jun-25 A	
2010	PM-P2-EN-140	Trade Permits- Elec. - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
2011	PM-P2-EN-150	Trade Permits- Plumbing - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
2012	PM-P2-EN-160	Trade Permits- Low Voltage - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
2013	WBS - ITB Trades		77.0d	2-Jul-25 A	21-Oct-25 A	
2014	WBS - ITB 1 - Apron, Site & Hydrant Fueling		0.0d	2-Jul-25	2-Jul-25 A	
2015	PM-ITB1-10	ITB1 - Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
2016	WBS - ITB 2 - Passenger Boarding Bridges		48.0d	2-Jul-25 A	10-Sep-25 A	

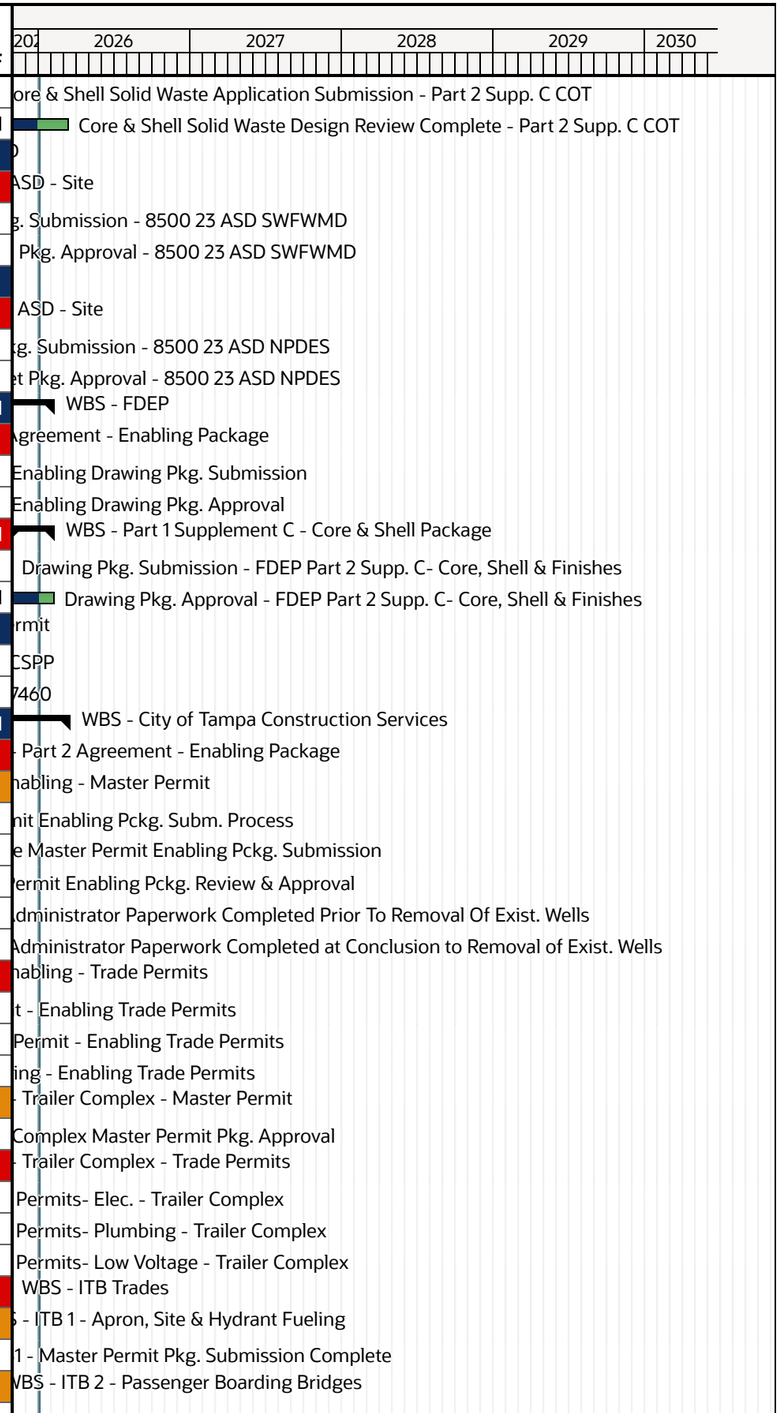


	ID	Name	Dur	Start	Finish	TF
2017	PM-ITB2 -1-20	ITB2 - PBB Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
2018	PM-ITB2 -1-40	ITB 2 - PBB Master Permit Pkg. Approval	32.0d	28-Jul-25 A	10-Sep-25 A	
2019	WBS - ITB 3 - Guideway		77.0d	2-Jul-25 A	21-Oct-25 A	
2020	PM-ITB3-1-30	ITB 3 - GDY Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
2021	PM-ITB3-1-40	ITB 3 - GDY Master Permit Pkg. Approval	77.0d	3-Jul-25 A	21-Oct-25 A	
2022	WBS - Part 2 Supplement A - Foundations		56.0d	3-Jul-25 A	22-Sep-25 A	
2023	WBS - Part 2 Supplement A - Foundations - Master Permit		56.0d	3-Jul-25 A	22-Sep-25 A	
2024	PM-P2-2A-10	Commence Master Permit Pkg. Submission - Part 2 Supp. A Found.	0.0d	3-Jul-25 A		
2025	PM-P2-2A-20	Master Permit Pkg. Approval - Part 2 Supp. A Found.	56.0d	3-Jul-25 A	22-Sep-25 A	
2026	WBS - Part 1 Supplement C - Core & Shell Package		122.0d	18-Sep-25 A	12-Mar-26	212.0d
2027	PM-P2-2B-10	Drawing Pkg. Submission - COT Const. Svs. -Part 1 Supp. C Core & Shell	1.0d	18-Sep-25 A	18-Sep-25 A	
2028	PM-P2-2B-20	Drawing Pkg. Approval - COT Const. Svs. -Part 1 Supp. C Core & Shell	76.0d	19-Sep-25 A	8-Jan-26	232.0d
2029	WBS - Part 1 Supplement C - Core, Shell Package Trade Permits		45.0d	6-Feb-26	12-Mar-26	212.0d
2030	PM-P2-2B-30	Trade Permit Place Holder - Fire Protection & Security - Part 1 Supp. C Core & S...	25.0d	6-Feb-26	12-Mar-26	212.0d
2031	WBS - ASD - PROCUREMENT PHASE		1,078.0d	13-Dec-24 A	13-Mar-29	261.0d
2032	WBS - Contractor Furnished & Install (CFCI)		1,078.0d	13-Dec-24 A	13-Mar-29	261.0d
2033	WBS - Part 2 Agreement - Enabling Procurement		202.0d	13-Dec-24 A	29-Sep-25 A	
2034	WBS - Enabling - Priority 1 Submittals		148.0d	13-Dec-24 A	14-Jul-25 A	
2035	WBS - Enabling - Civil Sanitary Lift Station		148.0d	13-Dec-24 A	14-Jul-25 A	
2036	PR-P2-EN-20	Prep & Submit Sanitary Lift Station Submittals - Part 2 Agreement	44.0d	13-Dec-24 A	14-Feb-25 A	
2037	PR-P2-EN-740	Approve Sanitary System Lift Station Submittals - Part 2 Agreement	28.0d	17-Feb-25 A	26-Mar-25 A	
2038	PR-P2-EN-1070	Fab. & Ship Sanitary Lift Station - Part 2 Agreement	108.0d	27-Mar-25 A	14-Jul-25 A	
2039	PR-P2-EN-1420	Deliver Sanitary Lift Station - Part 2 Agreement	0.0d		14-Jul-25 A	
2040	WBS - Enabling - Civil Storm System Material		114.0d	13-Dec-24 A	23-May-25 A	
2041	PR-P2-EN-10	Prep & Submit Storm RCP System Submittals - Part 2 Agreement Syst. Material	22.0d	13-Dec-24 A	15-Jan-25 A	
2042	PR-P2-EN-730	Approve Storm RCP System Submittals - Part 2 Agreement Syst. Material	50.0d	16-Jan-25 A	26-Mar-25 A	
2043	PR-P2-EN-1060	Fab. & Ship RCP Storm System - Part 2 Agreement Syst. Material	58.0d	27-Mar-25 A	23-May-25 A	
2044	PR-P2-EN-1390	Deliver RCP Storm System - Part 2 Agreement Syst. Material	0.0d		23-May-25 A	
2045	WBS - Enabling - Electrical Switch Gear		90.0d	19-Dec-24 A	25-Apr-25 A	
2046	PR-P2-EN-90	Prep & Submit Switch Gear Submittals - Part 2 Agreement	2.0d	19-Dec-24 A	20-Dec-24 A	
2047	PR-P2-EN-630	Approve Switch Gear Submittals - Part 2 Agreement	39.0d	23-Dec-24 A	17-Feb-25 A	
2048	PR-P2-EN-950	Fab. & Ship Switch Gear Submittals - Part 2 Agreement	58.0d	18-Feb-25 A	16-Apr-25 A	
2049	PR-P2-EN-1410	Deliver Switch Gear Submittals - Part 2 Agreement	0.0d		25-Apr-25 A	
2050	WBS - Enabling - Electrical Fiber Optic Material		39.0d	13-Dec-24 A	7-Feb-25 A	
2051	PR-P2-EN-80	Prep & Submit Fiber Optic Submittals - Part 2 Agreement	25.0d	13-Dec-24 A	20-Jan-25 A	
2052	PR-P2-EN-620	Approve Fiber Optic Submittals - Part 2 Agreement	9.0d	21-Jan-25 A	31-Jan-25 A	
2053	PR-P2-EN-940	Fiber Optic Fab. & Ship - Part 2 Agreement	5.0d	3-Feb-25 A	7-Feb-25 A	
2054	PR-P2-EN-1270	Deliver Fiber Optic - Part 2 Agreement	0.0d		7-Feb-25 A	
2055	WBS - Enabling - AOA Fence		60.0d	17-Dec-24 A	12-Mar-25 A	
2056	PR-P2-EN-120	Prep & Submit Fencing Pkg. - Part 2 Agreement AOA Fence	16.0d	17-Dec-24 A	9-Jan-25 A	
2057	PR-P2-EN-410	Approve Fencing Submittals - Part 2 Agreement AOA Fence	8.0d	10-Jan-25 A	21-Jan-25 A	
2058	PR-P2-EN-580	Fab. & Ship Fencing - Part 2 Agreement AOA Fence	49.0d	22-Jan-25 A	11-Mar-25 A	

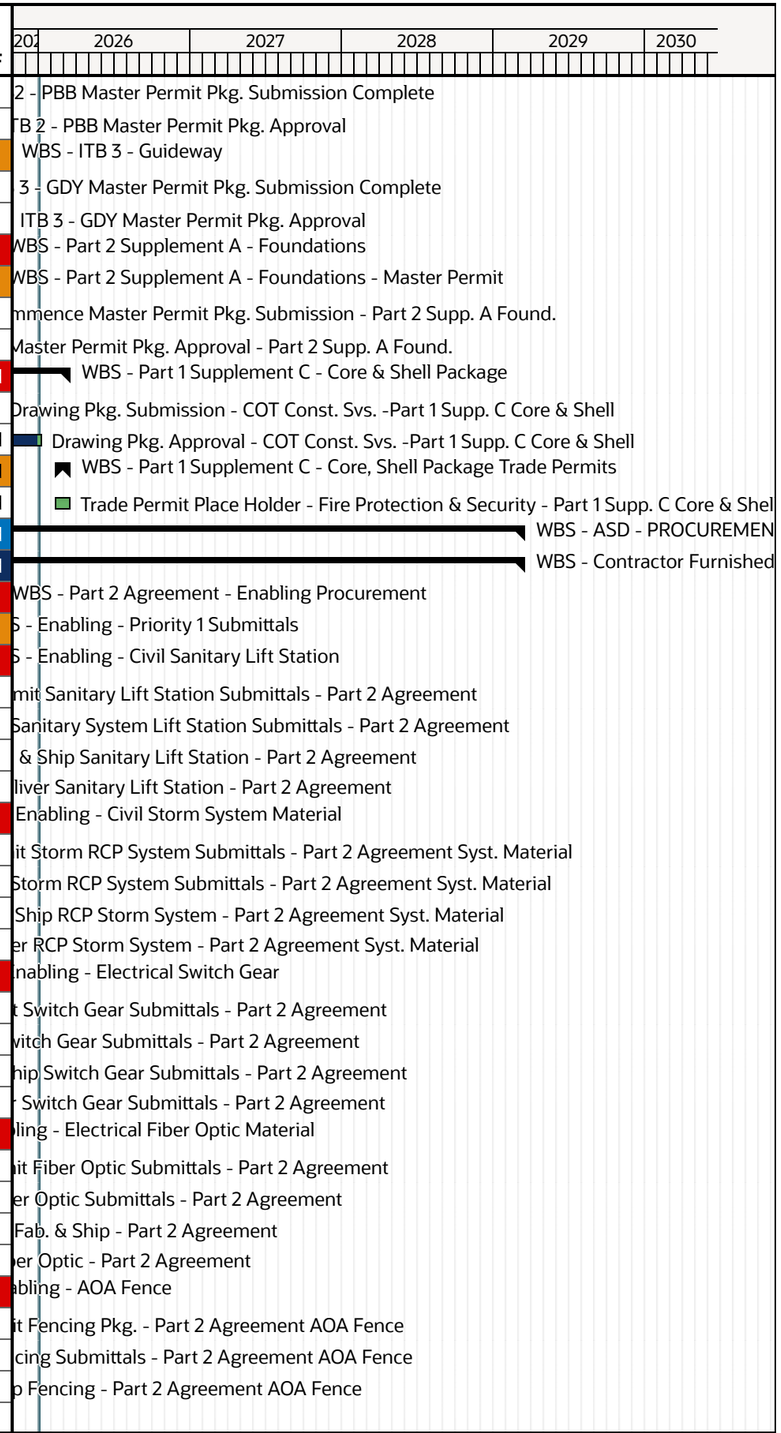


	ID	Name	Dur	Start	Finish	TF
2059	PR-P2-EN-590	Deliver Fencing - Part 2 Agreement AOA Fence	0.0d		12-Mar-25 A	
2060	WBS - Enabling - Trailers		117.0d	23-Dec-24 A	6-Jun-25 A	
2061	PR-P2-EN-140	Prep & Submit Shop Drawings For Trailer Pkg. - Part 2 Agreement	29.0d	23-Dec-24 A	3-Feb-25 A	
2062	PR-P2-EN-500	Approval Of Trailer Pkg. - Part 2 Agreement	8.0d	4-Feb-25 A	13-Feb-25 A	
2063	PR-P2-EN-1290	COT Permit Review for Trailers - Part 2 Agreement	25.0d	4-Feb-25 A	10-Mar-25 A	
2064	PR-P2-EN-1370	Fab. & Ship Trailers - Part 2 Agreement	87.0d	11-Mar-25 A	6-Jun-25 A	
2065	PR-P2-EN-1400	Delivery of Trailers - Part 2 Agreement	0.0d		6-Jun-25 A	
2066	WBS - Enabling - Furniture		103.0d	18-Feb-25 A	14-Jul-25 A	
2067	PR-P2-EN-130	Prep & Submit Trailer Furniture Pkg. - Part 2 Agreement	27.0d	18-Feb-25 A	26-Mar-25 A	
2068	PR-P2-EN-1160	Approve Trailer Furniture Pkg. - Part 2 Agreement	41.0d	27-Mar-25 A	22-May-25 A	
2069	PR-P2-EN-1300	Fab. & Ship Trailer Furniture Pkg. - Part 2 Agreement	44.0d	23-May-25 A	7-Jul-25 A	
2070	PR-P2-EN-1310	Deliver Trailer Furniture - Part 2 Agreement	0.0d		14-Jul-25 A	
2071	WBS - Enabling - Fuel Tank - Rebar		47.0d	13-Dec-24 A	19-Feb-25 A	
2072	PR-P2-EN-360	Prep & Submit Fuel Tank Rebar Pkg. - Part 2 Agreement	28.0d	13-Dec-24 A	23-Jan-25 A	
2073	PR-P2-EN-550	Approve Fuel Tank Rebar Submittals - Part 2 Agreement	11.0d	24-Jan-25 A	7-Feb-25 A	
2074	PR-P2-EN-850	Fab. & Ship Fuel Tank Rebar - Part 2 Agreement	10.0d	10-Feb-25 A	19-Feb-25 A	
2075	PR-P2-EN-1140	Deliver Fuel Tank Rebar - Part 2 Agreement	0.0d		19-Feb-25 A	
2076	WBS - Enabling - Fuel Tank - Concrete		39.0d	13-Dec-24 A	7-Feb-25 A	
2077	PR-P2-EN-370	Prep & Submit Fuel Tank Concrete Pkg. - Part 2 Agreement	24.0d	13-Dec-24 A	17-Jan-25 A	
2078	PR-P2-EN-560	Approve Fuel Tank Concrete Submittals - Part 2 Agreement	15.0d	20-Jan-25 A	7-Feb-25 A	
2079	WBS - Enabling - Fuel Tank - Electrical		49.0d	23-Dec-24 A	3-Mar-25 A	
2080	PR-P2-EN-380	Prep & Submit Fuel Tank Elec. Pkg. - Part 2 Agreement	18.0d	23-Dec-24 A	17-Jan-25 A	
2081	PR-P2-EN-570	Approve Fuel Tank Elec. Submittals - Part 2 Agreement	22.0d	20-Jan-25 A	18-Feb-25 A	
2082	PR-P2-EN-870	Fab. & Ship Fuel Tank Elec. - Part 2 Agreement	4.0d	25-Feb-25 A	28-Feb-25 A	
2083	PR-P2-EN-1260	Deliver Fuel Tank Elec. - Part 2 Agreement	0.0d		3-Mar-25 A	
2084	WBS - Enabling - Priority 2 Submittals		202.0d	13-Dec-24 A	29-Sep-25 A	
2085	WBS - Enabling - Civil Fire Line		176.0d	13-Dec-24 A	21-Aug-25 A	
2086	PR-P2-EN-60	Prep & Submit - Civil Fire Line Submittals - Priority 2	88.0d	13-Dec-24 A	17-Apr-25 A	
2087	PR-P2-EN-600	Approve Civil Fire Line Submittals - Priority 2	9.0d	18-Apr-25 A	30-Apr-25 A	
2088	PR-P2-EN-920	Fab. & Ship Civil Fire Line - Priority 2	32.0d	21-Jul-25 A	21-Aug-25 A	
2089	PR-P2-EN-1170	Deliver Civil Fire Line Complete - Priority 2	0.0d		21-Aug-25 A	
2090	WBS - Enabling - Civil Dewatering Equipment & Accessories		202.0d	13-Dec-24 A	29-Sep-25 A	
2091	PR-P2-EN-300	Prep & Submit - Civil Dewatering Equip. & Accessories Submittals - Priority 2	89.0d	13-Dec-24 A	18-Apr-25 A	
2092	PR-P2-EN-680	Approve Civil Dewatering Equip. & Accessories Submittals - Priority 2	8.0d	21-Apr-25 A	30-Apr-25 A	
2093	PR-P2-EN-1010	Fab. & Ship Civil Dewatering Equip. & Accessories - Priority 2	28.0d	1-May-25 A	29-May-25 A	
2094	PR-P2-EN-1230	Delivery Civil Dewatering Equip. & Accessories on Site - Priority 2	0.0d		29-Sep-25 A	
2095	WBS - Enabling - Civil MOT Bessie Coleman Cut Over		84.0d	13-Dec-24 A	11-Apr-25 A	
2096	PR-P2-EN-330	Prep & Submit - Civil MOT Bessie Coleman Cut Over Submittals - Priority 2	59.0d	13-Dec-24 A	7-Mar-25 A	
2097	PR-P2-EN-440	Approve Civil MOT Bessie Coleman Cut Over Submittals - Priority 2	2.0d	10-Mar-25 A	11-Mar-25 A	
2098	PR-P2-EN-710	Fab. & Ship - Civil MOT Bessie Coleman Cut Over - Priority 2	30.0d	12-Mar-25 A	10-Apr-25 A	
2099	PR-P2-EN-900	Delivery of Civil MOT Bessie Coleman Cut Over Complete - Priority 2	0.0d		11-Apr-25 A	
2100	WBS - Enabling - Lighting		123.0d	23-Dec-24 A	16-Jun-25 A	

	ID	Name	Dur	Start	Finish	TF
2101	PR-P2-EN-200	Prep & Submit LTNG Submittals - Priority 2	18.0d	23-Dec-24 A	17-Jan-25 A	
2102	PR-P2-EN-790	Approve LTNG Submittals - Priority 2	26.0d	20-Jan-25 A	24-Feb-25 A	
2103	PR-P2-EN-1090	LTNG Fab. & Ship - Priority 2	111.0d	25-Feb-25 A	16-Jun-25 A	
2104	PR-P2-EN-1380	Delivery of LTNG Complete - Priority 2	0.0d		16-Jun-25 A	
2105	WBS - Enabling - Electrical Raceways & Accessories		54.0d	23-Dec-24 A	10-Mar-25 A	
2106	PR-P2-EN-220	Prep & Submit Raceways/Wiring & Accessories Submittals - Priority 2	29.0d	23-Dec-24 A	3-Feb-25 A	
2107	PR-P2-EN-640	Approve Raceways/Wiring & Accessories Submittals - Priority 2	11.0d	4-Feb-25 A	18-Feb-25 A	
2108	PR-P2-EN-970	Raceways/Wiring & Accessories Fab. & Ship - Priority 2	1.0d	19-Feb-25 A	19-Feb-25 A	
2109	PR-P2-EN-1190	Delivery of Raceways/Wiring & Accessories on Site - Priority 2	0.0d		10-Mar-25 A	
2110	WBS - Enabling - Electrical Disconnect Devices		49.0d	23-Dec-24 A	3-Mar-25 A	
2111	PR-P2-EN-230	Prep & Submit Disconnect Devices Submittals - Priority 2	29.0d	23-Dec-24 A	3-Feb-25 A	
2112	PR-P2-EN-530	Approve Disconnect Devices Submittals - Priority 2	11.0d	4-Feb-25 A	18-Feb-25 A	
2113	PR-P2-EN-800	Disconnect Devices Fab. & Ship - Priority 2	10.0d	19-Feb-25 A	28-Feb-25 A	
2114	PR-P2-EN-1050	Delivery of Disconnect Devices Complete - Priority 2	0.0d		3-Mar-25 A	
2115	WBS - Enabling - Data & Power		43.0d	25-Feb-25 A	24-Apr-25 A	
2116	PR-P2-EN-150	Design Trailer Data & Power Plan - Priority 2	30.0d	25-Feb-25 A	7-Apr-25 A	
2117	PR-P2-EN-1080	Approve Trailer Data & Power Plan - Priority 2	13.0d	8-Apr-25 A	24-Apr-25 A	
2118	WBS - Enabling - Security System		74.0d	18-Feb-25 A	2-Jun-25 A	
2119	PR-P2-EN-160	Approve Trailer Security Systems Product Data - Priority 2	15.0d	18-Feb-25 A	10-Mar-25 A	
2120	PR-P2-EN-510	Deliver Trailer Security Systems - Priority 2	0.0d		2-Jun-25 A	
2121	WBS - Enabling - Guard Booths		131.0d	4-Feb-25 A	7-Aug-25 A	
2122	PR-P2-EN-240	Prep & Submit Guard Booths Pkg. - Priority 2	15.0d	4-Feb-25 A	24-Feb-25 A	
2123	PR-P2-EN-810	Approve Guard Booths Submittals - Priority 2	30.0d	19-Mar-25 A	29-Apr-25 A	
2124	PR-P2-EN-1100	Fab. & Ship Guard Booths - Priority 2	29.0d	30-Apr-25 A	29-May-25 A	
2125	PR-P2-EN-1340	Delivery of Guard Booths Complete - Priority 2	0.0d		7-Aug-25 A	
2126	WBS - Enabling - Cameras & Poles		153.0d	20-Jan-25 A	22-Aug-25 A	
2127	PR-P2-EN-820	Approve Cameras (HCAA) & Poles Submittals - Priority 2	26.0d	20-Jan-25 A	24-Feb-25 A	
2128	PR-P2-EN-250	Prep & Submit Cameras & Poles Pkg. - Priority 2	16.0d	21-Feb-25 A	14-Mar-25 A	
2129	PR-P2-EN-1110	Fab. & Ship Cameras (HCAA) & Poles - Priority 2	111.0d	25-Feb-25 A	16-Jun-25 A	
2130	PR-P2-EN-1350	Delivery of Cameras (HCAA) & Poles Complete - Priority 2	0.0d		22-Aug-25 A	
2131	WBS - Enabling - Priority 3 Submittals		163.0d	6-Jan-25 A	22-Aug-25 A	
2132	WBS - Enabling - Civil Domestic Water Material		99.0d	1-Apr-25 A	20-Aug-25 A	
2133	PR-P2-EN-30	Prep & Submit Civil Domestic Water Submittals Material - Priority 3	12.0d	1-Apr-25 A	17-Apr-25 A	
2134	PR-P2-EN-B002-10	Bulletin 002 Conditional Commitment for Water Service Letter Received	0.0d	14-Apr-25 A		
2135	PR-P2-EN-B002-20	Bulletin 002 Water Service Letter Transmitted to HCAA for Payment	14.0d	15-Apr-25 A	2-May-25 A	
2136	PR-P2-EN-470	Approve Civil Domestic Water Submittals Material - Priority 3	9.0d	18-Apr-25 A	30-Apr-25 A	
2137	PR-P2-EN-B002-30	Bulletin 002 Tampa Water Dept Plan Review	49.0d	5-May-25 A	14-Jul-25 A	
2138	PR-P2-EN-B002-40	Bulletin 002 Tampa Water Dept Plan Approval	0.0d		16-Jul-25 A	
2139	PR-P2-EN-750	Fab. & Ship Civil Domestic Water Material - Priority 3	14.0d	17-Jul-25 A	30-Jul-25 A	
2140	PR-P2-EN-1150	Delivery of Civil Domestic Water Material Complete - Priority 3	0.0d		20-Aug-25 A	
2141	WBS - Enabling - Civil Concrete Mix		16.0d	27-Jan-25 A	17-Feb-25 A	
2142	PR-P2-EN-40	Prep & Submit Civil Concrete Mix Submittals - Priority 3	10.0d	27-Jan-25 A	7-Feb-25 A	


	ID	Name	Dur	Start	Finish	TF
2143	PR-P2-EN-480	Approve Civil Concrete Mix Submittals - Priority 3	6.0d	10-Feb-25 A	17-Feb-25 A	
2144	WBS - Enabling - Civil Asphalt		8.0d	3-Mar-25 A	12-Mar-25 A	
2145	PR-P2-EN-50	Prep & Submit Civil Asphalt Submittals - Priority 3	4.0d	3-Mar-25 A	6-Mar-25 A	
2146	PR-P2-EN-490	Approve Civil Asphalt Submittals - Priority 3	5.0d	6-Mar-25 A	12-Mar-25 A	
2147	WBS - Enabling - Civil Sanitary Gravity Pipe & Accessories		56.0d	27-Jan-25 A	14-Apr-25 A	
2148	PR-P2-EN-270	Prep & Submit - Civil Sanitary Gravity Pipe & Accessories Submittals - Priority 3	21.0d	27-Jan-25 A	24-Feb-25 A	
2149	PR-P2-EN-650	Approve Civil Sanitary Gravity Pipe & Accessories Submittals - Priority 3	13.0d	25-Mar-25 A	10-Apr-25 A	
2150	PR-P2-EN-980	Fab. & Ship Civil Sanitary Gravity Pipe & Accessories - Priority 3	4.0d	11-Apr-25 A	14-Apr-25 A	
2151	PR-P2-EN-1200	Delivery of Civil Sanitary Gravity Pipe & Accessories Complete - Priority 3	0.0d		14-Apr-25 A	
2152	WBS - Enabling - Civil Underdrain Pipe & Accessories		114.0d	27-Jan-25 A	7-Jul-25 A	
2153	PR-P2-EN-290	Prep & Submit - Civil Underdrain Pipe & Accessories Submittals - Priority 3	21.0d	27-Jan-25 A	24-Feb-25 A	
2154	PR-P2-EN-670	Approve Civil Underdrain Pipe & Accessories Submittals - Priority 3	3.0d	18-Apr-25 A	22-Apr-25 A	
2155	PR-P2-EN-1000	Fab. & Ship Civil Underdrain Pipe & Accessories - Priority 3	54.0d	23-Apr-25 A	16-Jun-25 A	
2156	PR-P2-EN-1220	Delivery of Civil Underdrain Pipe & Accessories Complete - Priority 3	0.0d		7-Jul-25 A	
2157	WBS - Enabling - Electrical Low Voltage Material		40.0d	6-Jan-25 A	28-Feb-25 A	
2158	PR-P2-EN-70	Prep & Submit Low Voltage Material Submittals - Priority 3	9.0d	6-Jan-25 A	16-Jan-25 A	
2159	PR-P2-EN-610	Approve Low Voltage Material Submittals - Priority 3	11.0d	17-Jan-25 A	31-Jan-25 A	
2160	PR-P2-EN-930	Fab. & Ship Low Voltage Material - Priority 3	26.0d	3-Feb-25 A	28-Feb-25 A	
2161	PR-P2-EN-1180	Delivery of Low Voltage Material Complete - Priority 3	0.0d		28-Feb-25 A	
2162	WBS - Enabling - Break Shelter		51.0d	12-Jun-25 A	22-Aug-25 A	
2163	PR-P2-EN-260	Prep & Submit Break Shelter Pkg. - Priority 3	12.0d	12-Jun-25 A	27-Jun-25 A	
2164	PR-P2-EN-830	Approve Break Shelter Submittals - Priority 3	15.0d	30-Jun-25 A	21-Jul-25 A	
2165	PR-P2-EN-1120	Fab. & Ship Break Shelter - Priority 3	25.0d	22-Jul-25 A	15-Aug-25 A	
2166	PR-P2-EN-1360	Delivery of Break Shelter Complete - Priority 3	0.0d		22-Aug-25 A	
2167	WBS - Part 2 Supplement A - DIP / LTP, Foundations Package & Long Lead		546.0d	23-Jun-25 A	16-Aug-27	230.0d
2168	WBS - DIP / LTP Test Pile Program Materials		24.0d	23-Jun-25 A	25-Jul-25 A	
2169	PR-P2-1A-70	Prep & Submit Test Pile Program - Part 2 Supp. A DIP/LTP, Found. Package & Lo...	19.0d	23-Jun-25 A	21-Jul-25 A	
2170	PR-P2-1A-150	Approve Test Pile Program - Part 2 Supp. A DIP/LTP, Found. Package & Long Lead	13.0d	7-Jul-25 A	24-Jul-25 A	
2171	PR-P2-1A-280	Fab. & Ship Test Pile Program Materials - Part 2 Supp. A DIP/LTP, Found. Packa...	5.0d	21-Jul-25 A	25-Jul-25 A	
2172	PR-P2-1A-390	Deliver Test Pile Program Materials - Part 2 Supp. A DIP/LTP, Found. Package & ...	0.0d		25-Jul-25 A	
2173	WBS - DIP / LTP Test Pile Results		23.0d	21-Aug-25 A	23-Sep-25 A	
2174	PR-P2-1A-20	Prep & Submit DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP, Found. Packa...	11.0d	21-Aug-25 A	5-Sep-25 A	
2175	PR-P2-1A-140	Approve DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP, Found. Package & L...	7.0d	8-Sep-25 A	16-Sep-25 A	
2176	PR-P2-1A-145	Approve DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP (Rev 1) (returned as ...	5.0d	17-Sep-25 A	23-Sep-25 A	
2177	WBS - DIP / LTP Production Design		74.0d	8-Sep-25 A	22-Dec-25 A	
2178	PR-P2-1A-800	Prep & Submit DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, ...	20.0d	8-Sep-25 A	3-Oct-25 A	
2179	PR-P2-1A-810	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	14.0d	6-Oct-25 A	23-Oct-25 A	
2180	PR-P2-1A-860	Fab. & Ship DIP/LTP Production Piles - Part 2 Supp. A DIP/LTP, Found. Package ...	22.0d	6-Oct-25 A	27-Oct-25 A	
2181	PR-P2-1A-815	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	7.0d	24-Oct-25 A	3-Nov-25 A	
2182	PR-P2-1A-820	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	22.0d	19-Nov-25 A	22-Dec-25 A	
2183	PR-P2-1A-870	Delivery of DIP/LTP Production Piles - Part 2 Supp. A DIP/LTP, Found. Package ...	0.0d		22-Dec-25 A	
2184	WBS - DIP / LTP Area 6-1 Shop Drawings		39.0d	10-Nov-25 A	7-Jan-26	53.0d

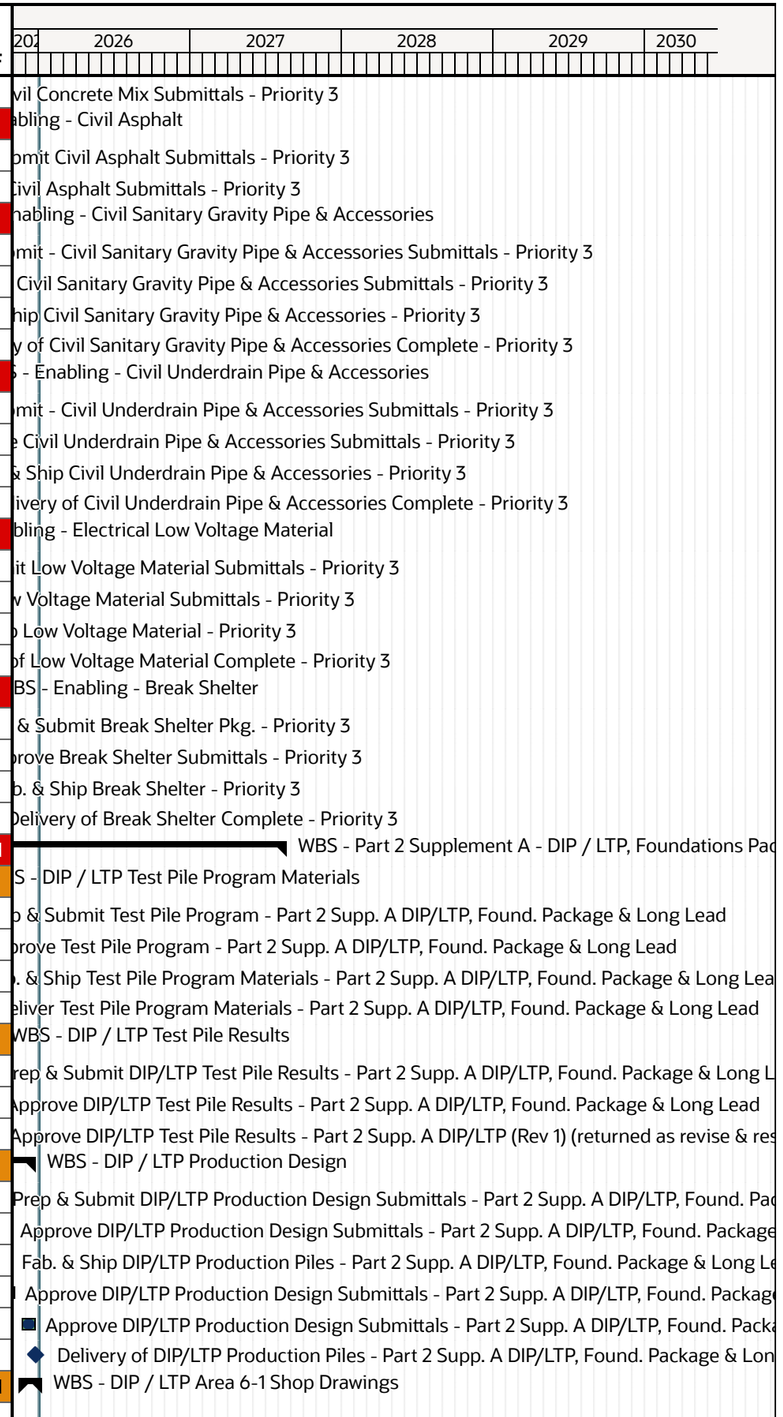


	ID	Name	Dur	Start	Finish	TF
2185	PR-P2-1A-1860	Prep & Submit DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DIP...	15.0d	10-Nov-25 A	2-Dec-25 A	
2186	PR-P2-1A-1890	HP Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DIP/L...	1.0d	3-Dec-25 A	3-Dec-25 A	
2187	PR-P2-1A-1870	HNTB Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DI...	0.0d	4-Dec-25 A	4-Dec-25 A	
2188	PR-P2-1A-1880	HCAA Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DI...	14.0d	17-Dec-25 A	7-Jan-26	53.0d
2189	WBS - DIP / LTP Production Shoes & Caps		13.0d	15-Oct-25 A	27-Oct-25 A	
2190	PR-P2-1A-900	Fab. & Ship DIP/LTP Production Shoes & Caps - Part 2 Supp. A DIP/LTP, Found. ...	13.0d	15-Oct-25 A	27-Oct-25 A	
2191	PR-P2-1A-910	Delivery of DIP/LTP Production Shoes & Caps - Part 2 Supp. A DIP/LTP, Found. ...	0.0d		27-Oct-25 A	
2192	WBS - DIP / LTP Production Grout		6.0d	15-Oct-25 A	22-Oct-25 A	
2193	PR-P2-1A-920	Prep & Submit DIP/LTP Production Grout Submittals - Part 2 Supp. A DIP/LTP, F...	3.0d	15-Oct-25 A	19-Oct-25 A	
2194	PR-P2-1A-930	Approve DIP/LTP Production Grout Submittals - Part 2 Supp. A DIP/LTP, Found. ...	3.0d	20-Oct-25 A	22-Oct-25 A	
2195	WBS - Foundations Package		126.0d	22-Sep-25 A	20-Mar-26	353.0d
2196	WBS - Rebar Foundations Area 2		54.0d	10-Oct-25 A	29-Dec-25	17.0d
2197	PR-P2-1A-80	Prep & Submit Rebar Found. Area 2 Submittals - Part 2 Supp. A	10.0d	10-Oct-25 A	23-Oct-25 A	
2198	PR-P2-1A-160	Approve Rebar Found. Area 2 Submittals - Part 2 Supp. A	12.0d	24-Oct-25 A	10-Nov-25 A	
2199	PR-P2-1A-1980	HCAA Approve Rebar Found. Area 2 Submittals - Part 2 Supp. A	16.0d	11-Nov-25 A	4-Dec-25 A	
2200	PR-P2-1A-290	Fab. & Ship Rebar Found. Area 2 - Part 2 Supp. A	29.0d	30-Nov-25 A	29-Dec-25	23.0d
2201	PR-P2-1A-430	Delivery of Rebar Found. Area 2 Complete - Part 2 Supp. A	0.0d		29-Dec-25	23.0d
2202	WBS - Rebar Foundations Area 6		59.0d	26-Sep-25 A	19-Dec-25 A	
2203	PR-P2-1A-90	Prep & Submit Rebar Found. Area 6 Submittals - Part 2 Supp. A	10.0d	26-Sep-25 A	9-Oct-25 A	
2204	PR-P2-1A-170	Approve Rebar Found. Area 6 Submittals - Part 2 Supp. A	11.0d	10-Oct-25 A	24-Oct-25 A	
2205	PR-P2-1A-410	Fab. & Ship Rebar Found. Area 6 - Part 2 Supp. A	45.0d	3-Nov-25 A	19-Dec-25 A	
2206	PR-P2-1A-420	Delivery of Rebar Found. Area 6 Complete - Part 2 Supp. A	0.0d		19-Dec-25 A	
2207	WBS - Rebar Foundations Area 1		85.0d	6-Nov-25 A	10-Mar-26	0.0d
2208	PR-P2-1A-1700	Prep & Submit Rebar Found. Area 1 Submittals - Part 2 Supp. A	22.0d	6-Nov-25 A	9-Dec-25 A	
2209	PR-P2-1A-1900	HP Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	9.0d	10-Dec-25 A	22-Dec-25 A	
2210	PR-P2-1A-1910	HNTB Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	11.0d	23-Dec-25 A	8-Jan-26	0.0d
2211	PR-P2-1A-1710	HCAA Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	15.0d	9-Jan-26	29-Jan-26	0.0d
2212	PR-P2-1A-1720	Fab. & Ship Rebar Found. Area 1 - Part 2 Supp. A	40.0d	30-Jan-26	10-Mar-26	0.0d
2213	PR-P2-1A-1730	Delivery of Rebar Found. Area 1 Complete - Part 2 Supp. A	0.0d		10-Mar-26	0.0d
2214	WBS - Rebar Foundations Area 3		80.0d	14-Nov-25 A	11-Mar-26	15.0d
2215	PR-P2-1A-1740	Prep & Submit Rebar Found. Area 3 Submittals - Part 2 Supp. A	1.0d	14-Nov-25 A	14-Nov-25 A	
2216	PR-P2-1A-1920	HP Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	24.0d	17-Nov-25 A	22-Dec-25 A	
2217	PR-P2-1A-1930	HNTB Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	12.0d	23-Dec-25 A	9-Jan-26	15.0d
2218	PR-P2-1A-1750	HCAA Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	15.0d	12-Jan-26	30-Jan-26	15.0d
2219	PR-P2-1A-1760	Fab. & Ship Rebar Found. Area 3 - Part 2 Supp. A	40.0d	31-Jan-26	11-Mar-26	21.0d
2220	PR-P2-1A-1770	Delivery of Rebar Found. Area 3 Complete - Part 2 Supp. A	0.0d		11-Mar-26	21.0d
2221	WBS - Rebar Foundations Area 5		86.0d	24-Oct-25 A	26-Feb-26	49.0d
2222	PR-P2-1A-1780	Prep & Submit Rebar Found. Area 5 Submittals - Part 2 Supp. A	11.0d	24-Oct-25 A	7-Nov-25 A	
2223	PR-P2-1A-1940	HP Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	29.0d	10-Nov-25 A	22-Dec-25 A	
2224	PR-P2-1A-1950	HNTB Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	49.0d
2225	PR-P2-1A-1790	HCAA Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	15.0d	7-Jan-26	27-Jan-26	49.0d
2226	PR-P2-1A-1800	Fab. & Ship Rebar Found. Area 5 - Part 2 Supp. A	30.0d	28-Jan-26	26-Feb-26	69.0d

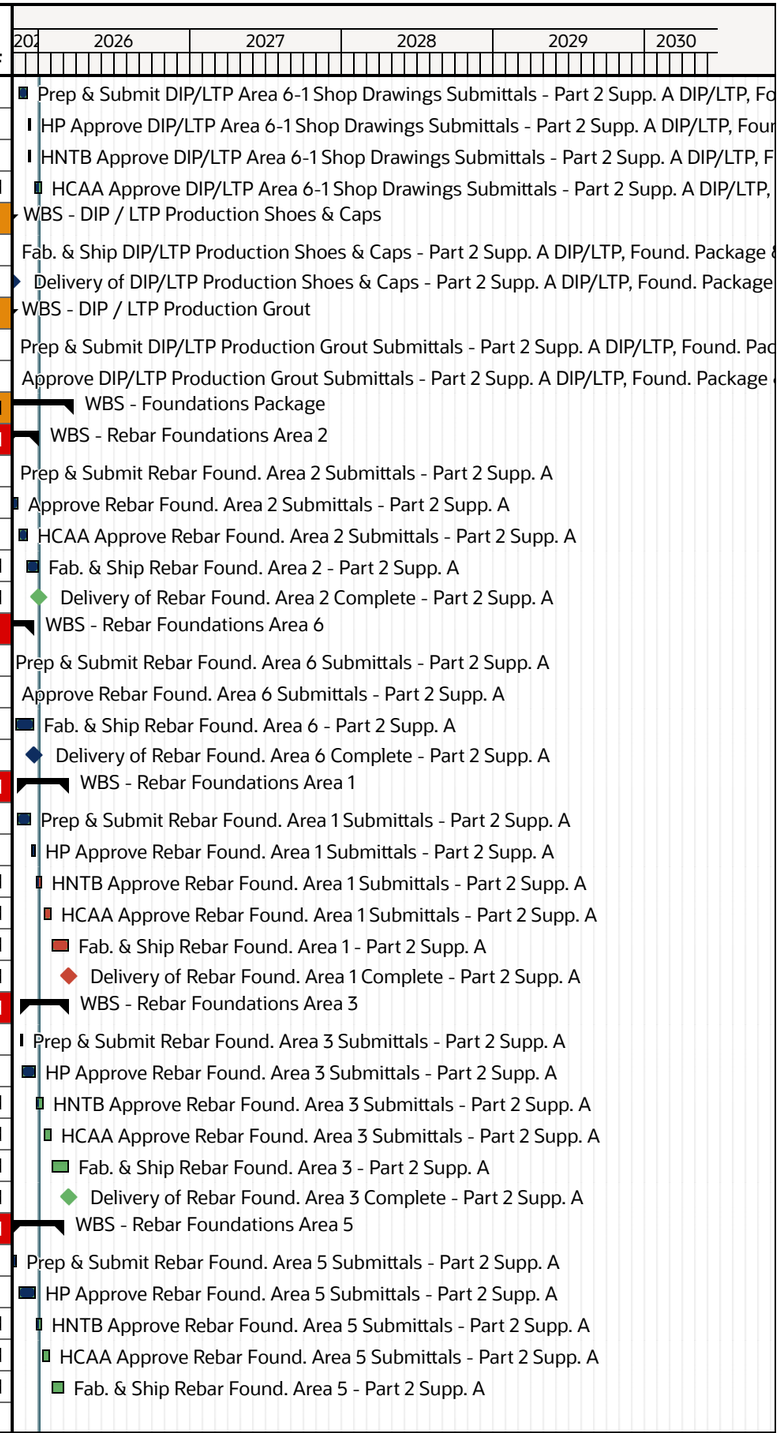


	ID	Name	Dur	Start	Finish	TF
2227	PR-P2-1A-1810	Delivery of Rebar Found. Area 5 Complete - Part 2 Supp. A	0.0d		26-Feb-26	69.0d
2228	WBS - Rebar Foundations Area 4		63.0d	26-Nov-25 A	26-Feb-26	69.0d
2229	PR-P2-1A-1820	Prep & Submit Rebar Found. Area 4 Submittals - Part 2 Supp. A	10.0d	26-Nov-25 A	11-Dec-25 A	
2230	PR-P2-1A-1960	HP Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	7.0d	12-Dec-25 A	22-Dec-25 A	
2231	PR-P2-1A-1970	HNTB Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	9.0d	23-Dec-25 A	6-Jan-26	69.0d
2232	PR-P2-1A-1830	HCAA Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	15.0d	7-Jan-26	27-Jan-26	69.0d
2233	PR-P2-1A-1840	Fab. & Ship Rebar Found. Area 4 - Part 2 Supp. A	30.0d	28-Jan-26	26-Feb-26	97.0d
2234	PR-P2-1A-1850	Delivery of Rebar Found. Area 4 Complete - Part 2 Supp. A	0.0d		26-Feb-26	97.0d
2235	WBS - Anchor Bolts		126.0d	22-Sep-25 A	20-Mar-26	353.0d
2236	WBS - Anchor Bolts Pkg #2 - Area 1		56.0d	22-Sep-25 A	10-Dec-25 A	
2237	PR-P2-1A-500	GMF Detailer Drawing Completion Window - Area 1 - Part 2 Supp. A - Anchor B...	34.0d	22-Sep-25 A	6-Nov-25 A	
2238	PR-P2-1A-510	GMF DM Drawing Review - Area 1 - Part 2 Supp. A - Anchor Bolts	1.0d	7-Nov-25 A	7-Nov-25 A	
2239	PR-P2-1A-520	HP & A/E Team Review of Detail Drawing - Area 1 - Part 2 Supp. A - Anchor Bolts	7.0d	10-Nov-25 A	18-Nov-25 A	
2240	PR-P2-1A-530	Return From Approval - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		18-Nov-25 A	
2241	PR-P2-1A-740	GMF Detailer Drawing Scrub & Clean up Window - Area 1 - Part 2 Supp. A - Anc...	6.0d	19-Nov-25 A	26-Nov-25 A	
2242	PR-P2-1A-1120	GMF DM RFF Review - Area 1 - Part 2 Supp. A - Anchor Bolts	5.0d	21-Nov-25 A	1-Dec-25 A	
2243	PR-P2-1A-1130	Release for Fab. - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		1-Dec-25 A	
2244	PR-P2-1A-1140	Procurement of Material - Area 1 - Part 2 Supp. A - Anchor Bolts	7.0d	2-Dec-25 A	10-Dec-25 A	
2245	PR-P2-1A-1150	Steel on site - Abs - Start Shipping - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	
2246	WBS - Anchor Bolts Pkg #1 Area 2		56.0d	22-Sep-25 A	10-Dec-25 A	
2247	PR-P2-1A-540	GMF Detailer Drawing Completion Window - Area 2 - Part 2 Supp. A - Anchor B...	22.0d	22-Sep-25 A	21-Oct-25 A	
2248	PR-P2-1A-550	GMF DM Drawing Review - Area 2 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Oct-25 A	21-Oct-25 A	
2249	PR-P2-1A-750	HP & A/E Team Review of Detail Drawing - Area 2 - Part 2 Supp. A - Anchor Bolts	15.0d	22-Oct-25 A	11-Nov-25 A	
2250	PR-P2-1A-570	GMF Detailer Drawing Scrub & Clean up Window - Area 2 - Part 2 Supp. A - Anc...	2.0d	7-Nov-25 A	10-Nov-25 A	
2251	PR-P2-1A-755	RFA'd 3 Days prior to 11/11 - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d	7-Nov-25 A	7-Nov-25 A	
2252	PR-P2-1A-560	Return From Approval - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		11-Nov-25 A	
2253	PR-P2-1A-940	GMF DM RFF Review - Area 2 - Part 2 Supp. A - Anchor Bolts	1.0d	12-Nov-25 A	12-Nov-25 A	
2254	PR-P2-1A-950	Release for Fab. - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		13-Nov-25 A	
2255	PR-P2-1A-960	Procurement of Material - Area 2 - Part 2 Supp. A - Anchor Bolts	17.0d	14-Nov-25 A	10-Dec-25 A	
2256	PR-P2-1A-970	Steel on site - Abs - Start Shipping - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	
2257	WBS - Anchor Bolts Pkg #2 Area 3		56.0d	22-Sep-25 A	10-Dec-25 A	
2258	PR-P2-1A-580	GMF Detailer Drawing Completion Window - Area 3 - Part 2 Supp. A - Anchor B...	34.0d	22-Sep-25 A	6-Nov-25 A	
2259	PR-P2-1A-590	GMF DM Drawing Review - Area 3 - Part 2 Supp. A - Anchor Bolts	1.0d	7-Nov-25 A	7-Nov-25 A	
2260	PR-P2-1A-600	HP & A/E Team Review of Detail Drawing - Area 3 - Part 2 Supp. A - Anchor Bolts	7.0d	10-Nov-25 A	18-Nov-25 A	
2261	PR-P2-1A-610	Return From Approval - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		18-Nov-25 A	
2262	PR-P2-1A-760	GMF Detailer Drawing Scrub & Clean up Window - Area 3 - Part 2 Supp. A - Anc...	6.0d	19-Nov-25 A	26-Nov-25 A	
2263	PR-P2-1A-1210	GMF DM RFF Review - Area 3 - Part 2 Supp. A - Anchor Bolts	5.0d	21-Nov-25 A	1-Dec-25 A	
2264	PR-P2-1A-1220	Release for Fab. - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		1-Dec-25 A	
2265	PR-P2-1A-1230	Procurement of Material - Area 3 - Part 2 Supp. A - Anchor Bolts	7.0d	2-Dec-25 A	10-Dec-25 A	
2266	PR-P2-1A-1240	Steel on site - Abs - Start Shipping - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	
2267	WBS - Anchor Bolts Pkg #3 Area 4		87.0d	22-Sep-25 A	26-Jan-26	92.0d
2268	PR-P2-1A-620	GMF Detailer Drawing Completion Window - Area 4 - Part 2 Supp. A - Anchor B...	44.0d	22-Sep-25 A	20-Nov-25 A	

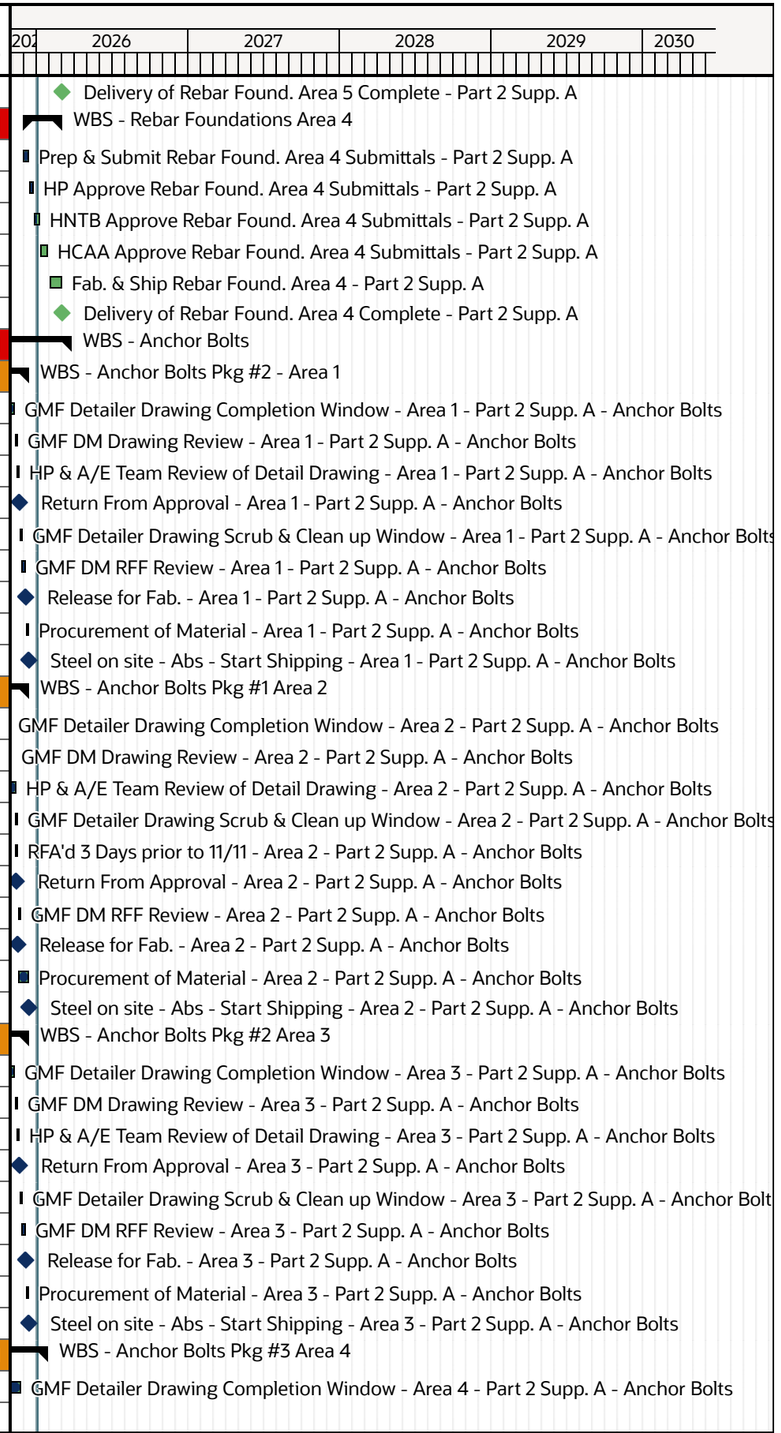


	ID	Name	Dur	Start	Finish	TF
2269	PR-P2-1A-630	GMF DM Drawing Review - Area 4 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Nov-25 A	21-Nov-25 A	
2270	PR-P2-1A-640	HP & A/E Team Review of Detail Drawing - Area 4 - Part 2 Supp. A - Anchor Bolts	14.0d	24-Nov-25 A	15-Dec-25 A	
2271	PR-P2-1A-650	Return From Approval - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		15-Dec-25 A	
2272	PR-P2-1A-780	GMF Detailer Drawing Scrub & Clean up Window - Area 4 - Part 2 Supp. A - Anc...	3.0d	16-Dec-25 A	18-Dec-25 A	
2273	PR-P2-1A-1300	GMF DM RFF Review - Area 4 - Part 2 Supp. A - Anchor Bolts	2.0d	19-Dec-25 A	22-Dec-25 A	
2274	PR-P2-1A-1310	Release for Fab. - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		22-Dec-25 A	
2275	PR-P2-1A-1320	Procurement of Material - Area 4 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	92.0d
2276	PR-P2-1A-1330	Steel on site - Abs - Start Shipping - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		26-Jan-26	92.0d
2277	WBS - Anchor Bolts Pkg #3 Area 5		87.0d	22-Sep-25 A	26-Jan-26	72.0d
2278	PR-P2-1A-1340	GMF Detailer Drawing Completion Window - Area 5 - Part 2 Supp. A - Anchor B...	44.0d	22-Sep-25 A	20-Nov-25 A	
2279	PR-P2-1A-1350	GMF DM Drawing Review - Area 5 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Nov-25 A	21-Nov-25 A	
2280	PR-P2-1A-1360	HP & A/E Team Review of Detail Drawing - Area 5 - Part 2 Supp. A - Anchor Bolts	14.0d	24-Nov-25 A	15-Dec-25 A	
2281	PR-P2-1A-1370	Return From Approval - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		15-Dec-25 A	
2282	PR-P2-1A-1380	GMF Detailer Drawing Scrub & Clean up Window - Area 5 - Part 2 Supp. A - Anc...	3.0d	16-Dec-25 A	18-Dec-25 A	
2283	PR-P2-1A-1390	GMF DM RFF Review - Area 5 - Part 2 Supp. A - Anchor Bolts	2.0d	19-Dec-25 A	22-Dec-25 A	
2284	PR-P2-1A-1400	Release for Fab. - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		22-Dec-25 A	
2285	PR-P2-1A-1410	Procurement of Material - Area 5 - Part 2 Supp. A - Anchor Bolts	23.0d	23-Dec-25 A	26-Jan-26	72.0d
2286	PR-P2-1A-1420	Steel on site - Abs - Start Shipping - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		26-Jan-26	72.0d
2287	WBS - Anchor Bolts Pkg #1 Area 6		56.0d	22-Sep-25 A	10-Dec-25 A	
2288	PR-P2-1A-700	GMF Detailer Drawing Completion Window - Area 6 - Part 2 Supp. A - Anchor B...	22.0d	22-Sep-25 A	21-Oct-25 A	
2289	PR-P2-1A-710	GMF DM Drawing Review - Area 6 - Part 2 Supp. A - Anchor Bolts	1.0d	22-Oct-25 A	22-Oct-25 A	
2290	PR-P2-1A-790	HP & A/E Team Review of Detail Drawing - Area 6 - Part 2 Supp. A - Anchor Bolts	15.0d	22-Oct-25 A	11-Nov-25 A	
2291	PR-P2-1A-730	GMF Detailer Drawing Scrub & Clean up Window - Area 6 - Part 2 Supp. A - Anc...	2.0d	7-Nov-25 A	10-Nov-25 A	
2292	PR-P2-1A-720	Return From Approval - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		11-Nov-25 A	
2293	PR-P2-1A-1030	GMF DM RFF Review - Area 6 - Part 2 Supp. A - Anchor Bolts	1.0d	12-Nov-25 A	12-Nov-25 A	
2294	PR-P2-1A-1040	Release for Fab. - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		13-Nov-25 A	
2295	PR-P2-1A-1050	Procurement of Material - Area 6 - Part 2 Supp. A - Anchor Bolts	17.0d	14-Nov-25 A	10-Dec-25 A	
2296	PR-P2-1A-1060	Steel on site - Abs - Start Shipping - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	
2297	WBS - Anchor Bolts Pkg #4 Area 6-1 Cooling Tower		79.0d	26-Nov-25 A	20-Mar-26	353.0d
2298	PR-P2-1A-1430	GMF Detailer Drawing Completion Window - Area 6-1 CT - Part 2 Supp. A - Anc...	38.0d	26-Nov-25 A	22-Jan-26	353.0d
2299	PR-P2-1A-1440	GMF DM Drawing Review - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	2.0d	23-Jan-26	26-Jan-26	353.0d
2300	PR-P2-1A-1450	HP & A/E Team Review of Detail Drawing - Area 6-1 CT - Part 2 Supp. A - Anch...	13.0d	27-Jan-26	12-Feb-26	353.0d
2301	PR-P2-1A-1460	Return From Approval - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		12-Feb-26	353.0d
2302	PR-P2-1A-1470	GMF Detailer Drawing Scrub & Clean up Window - Area 6-1 CT - Part 2 Supp. A ...	2.0d	13-Feb-26	16-Feb-26	353.0d
2303	PR-P2-1A-1480	GMF DM RFF Review - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	1.0d	17-Feb-26	17-Feb-26	353.0d
2304	PR-P2-1A-1490	Release for Fab. - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		17-Feb-26	353.0d
2305	PR-P2-1A-1500	Procurement of Material - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	23.0d	18-Feb-26	20-Mar-26	353.0d
2306	PR-P2-1A-1510	Steel on site - Abs - Start Shipping - Area 6-1 CT - Part 2 Supp. A - Anchor Bolts	0.0d		20-Mar-26	353.0d
2307	WBS - Embeds		122.0d	22-Sep-25 A	16-Mar-26	357.0d
2308	WBS - Embeds - Pkg #1 - Area 1-2-3-4-5-6		56.0d	22-Sep-25 A	10-Dec-25 A	
2309	PR-P2-1A-1530	Embeds Pkg #1 - GMF Detailer Drawing Completion Window - Area 1-2-3-4-5-...	28.0d	22-Sep-25 A	29-Oct-25 A	
2310	PR-P2-1A-1535	Embeds Pkg #1 - GMF DM Drawing Review - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		29-Oct-25 A	

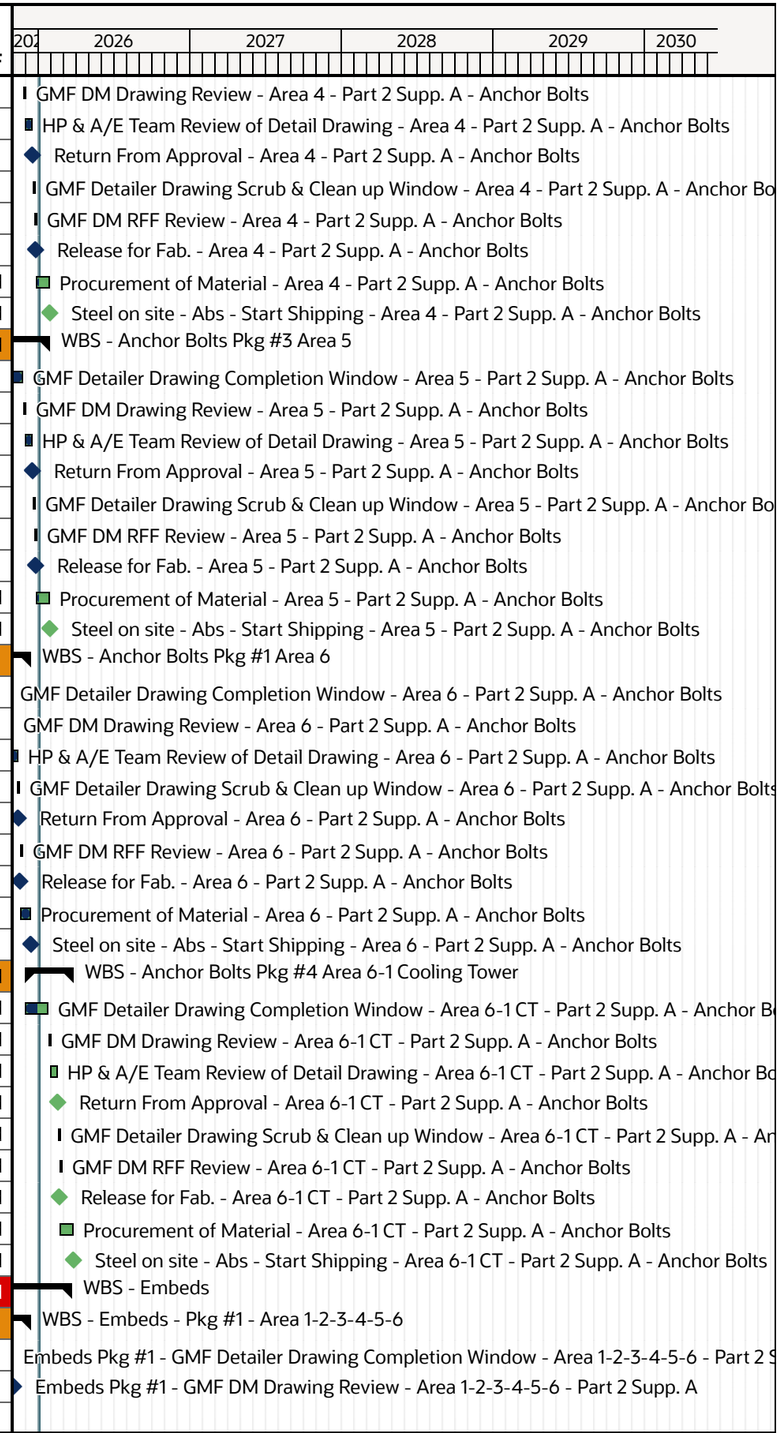


	ID	Name	Dur	Start	Finish	TF
2311	PR-P2-1A-1550	Embeds Pkg #1 - HP & A/E Team Review of Detail Drawing - Area 1-2-3-4-5-6 ...	9.0d	30-Oct-25 A	11-Nov-25 A	
2312	PR-P2-1A-1560	Embeds Pkg #1 - Return From Approval - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		11-Nov-25 A	
2313	PR-P2-1A-1570	Embeds Pkg #1 - GMF Detailer Drawing Scrub & Clean up Window - Area 1-2-3...	3.0d	12-Nov-25 A	14-Nov-25 A	
2314	PR-P2-1A-1572	Embeds Pkg #1 - GMF DM RFF Review - Area 1-2-3-4-5-6 - Part 2 Supp. A	5.0d	12-Nov-25 A	18-Nov-25 A	
2315	PR-P2-1A-1575	Embeds Pkg #1 - Release for Fab. - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		18-Nov-25 A	
2316	PR-P2-1A-1600	Embeds Pkg #1 - Fab. of Embeds - Area 1-2-3-4-5-6 - Part 2 Supp. A	14.0d	19-Nov-25 A	10-Dec-25 A	
2317	PR-P2-1A-1610	Embeds Pkg #1 - Embeds on Site - Start Shipping - Area 1-2-3-4-5-6 - Part 2 ...	0.0d		10-Dec-25 A	
2318	WBS - Embeds - Pkg. #2 - Area 6.1 - Cooling Tower (If needed)		94.0d	30-Oct-25 A	16-Mar-26	357.0d
2319	PR-P2-1A-1620	Embeds Pkg #2 - GMF Detailer Drawing Completion Window - Area 6.1 - Part 2...	39.0d	30-Oct-25 A	26-Dec-25 A	
2320	PR-P2-1A-1625	Embeds Pkg #2 - GMF DM Drawing Review - Area 6.1 - Part 2 Supp. A	2.0d	29-Dec-25	30-Dec-25	357.0d
2321	PR-P2-1A-1630	Embeds Pkg #2 - A/E Team Review of Detail Drawing - Area 6.1 - Part 2 Supp. A	15.0d	31-Dec-25	21-Jan-26	357.0d
2322	PR-P2-1A-1640	Embeds Pkg #2 - Return From Approval - Area 6.1 - Part 2 Supp. A	0.0d		21-Jan-26	357.0d
2323	PR-P2-1A-1650	Embeds Pkg #2 - GMF Detailer Drawing Scrub & Clean up Window - Area 6.1 - ...	2.0d	22-Jan-26	23-Jan-26	357.0d
2324	PR-P2-1A-1660	Embeds Pkg #2 - GMF DM RFF Review - Area 6.1 - Part 2 Supp. A	1.0d	26-Jan-26	26-Jan-26	357.0d
2325	PR-P2-1A-1670	Embeds Pkg #2 - Release for Fab. - Area 6.1 - Part 2 Supp. A	0.0d		26-Jan-26	357.0d
2326	PR-P2-1A-1680	Embeds Pkg #2 - Fab. of Embeds - Area 6.1 - Part 2 Supp. A	35.0d	27-Jan-26	16-Mar-26	357.0d
2327	PR-P2-1A-1690	Embeds Pkg #2 - Steel on Site - Start Shipping Embeds- Area 6.1 - Part 2 Supp. A	0.0d		16-Mar-26	357.0d
2328	WBS - Concrete Mix Designs		22.0d	10-Oct-25 A	10-Nov-25 A	
2329	PR-P2-1A-10	Prep & Submit Found. Concrete Mix Designs Submittals - Part 2 Supp. A Groun...	7.0d	10-Oct-25 A	20-Oct-25 A	
2330	PR-P2-1A-220	Approve Found. Concrete Mix Designs Submittals - Part 2 Supp. A Ground Impr...	15.0d	21-Oct-25 A	10-Nov-25 A	
2331	WBS - Underground Waterproofing		182.0d	8-Sep-25 A	26-May-26	10.0d
2332	PR-P2-1A-60	Prep Underground Waterproofing Submittals (Contractor) - Part 2 Supp. A	6.0d	8-Sep-25 A	15-Sep-25 A	
2333	PR-P2-1A-65	Review & Submit Underground Waterproofing Submittals (HP) - Part 2 Supp. A	11.0d	16-Sep-25 A	30-Sep-25 A	
2334	PR-P2-1A-270	Review & Approve Underground Waterproofing Submittals (HNTB) - Part 2 Sup...	10.0d	1-Oct-25 A	14-Oct-25 A	
2335	PR-P2-1A-275	Review & Approve Underground Waterproofing Submittals (HCAA) - Part 2 Sup...	35.0d	15-Oct-25 A	4-Dec-25 A	
2336	PR-P2-1A-310	Fab. & Ship Underground Waterproofing Products - Part 2 Supp. A	24.0d	5-Dec-25 A	29-Dec-25	14.0d
2337	PR-P2-1A-380	Delivery of Underground Waterproofing on Site - Part 2 Supp. A	146.0d	30-Dec-25	26-May-26	14.0d
2338	WBS - Underground Electrical Conduit		46.0d	15-Oct-25 A	19-Dec-25 A	
2339	PR-P2-1A-40	Prep Underground Elec. Conduit System Submittals (Contractor) - Part 2 Supp. A	5.0d	15-Oct-25 A	21-Oct-25 A	
2340	PR-P2-1A-42	Prep Underground Elec. Conduit System Submittals (Contractor) - Part 2 Supp. ...	4.0d	28-Oct-25 A	31-Oct-25 A	
2341	PR-P2-1A-250	Review & Approve Underground Elec. Conduit System Submittals (HNTB) - Part...	10.0d	3-Nov-25 A	14-Nov-25 A	
2342	PR-P2-1A-45	Review & Submit Underground Elec. Conduit System Submittals (HP) - Part 2 S...	1.0d	3-Nov-25 A	3-Nov-25 A	
2343	PR-P2-1A-255	Review & Approve Underground Elec. Conduit System Submittals (HCAA) - Part...	14.0d	14-Nov-25 A	5-Dec-25 A	
2344	PR-P2-1A-370	Fab. & Ship Underground Elec. Conduit System - Part 2 Supp. A	12.0d	8-Dec-25 A	19-Dec-25 A	
2345	PR-P2-1A-490	Delivery of Underground Elec. Conduit System on Site - Part 2 Supp. A	0.0d		19-Dec-25 A	
2346	WBS - Underground Chilled Water Piping & Sleeves		76.0d	8-Sep-25 A	24-Dec-25 A	
2347	PR-P2-1A-50	Prep Underground Chilled Water Sleeves Submittals (Contractor) - Part 2 Supp. A	21.0d	8-Sep-25 A	6-Oct-25 A	
2348	PR-P2-1A-55	Review & Submit Underground Chilled Water Sleeves Submittals (HP) - Part 2 S...	6.0d	20-Oct-25 A	27-Oct-25 A	
2349	PR-P2-1A-260	Review & Approve Underground Chilled Water Sleeves Submittals (HNTB) - Par...	10.0d	28-Oct-25 A	10-Nov-25 A	
2350	PR-P2-1A-265	Review & Approve Underground Chilled Water Sleeves Submittals (HCAA) - Par...	15.0d	11-Nov-25 A	3-Dec-25 A	
2351	PR-P2-1A-300	Fab. & Ship Underground Chilled Water Sleeves - Part 2 Supp. A	21.0d	4-Dec-25 A	24-Dec-25 A	
2352	PR-P2-1A-440	Delivery of Underground Chilled Water Sleeves on Site- Part 2 Supp. A	0.0d		24-Dec-25 A	

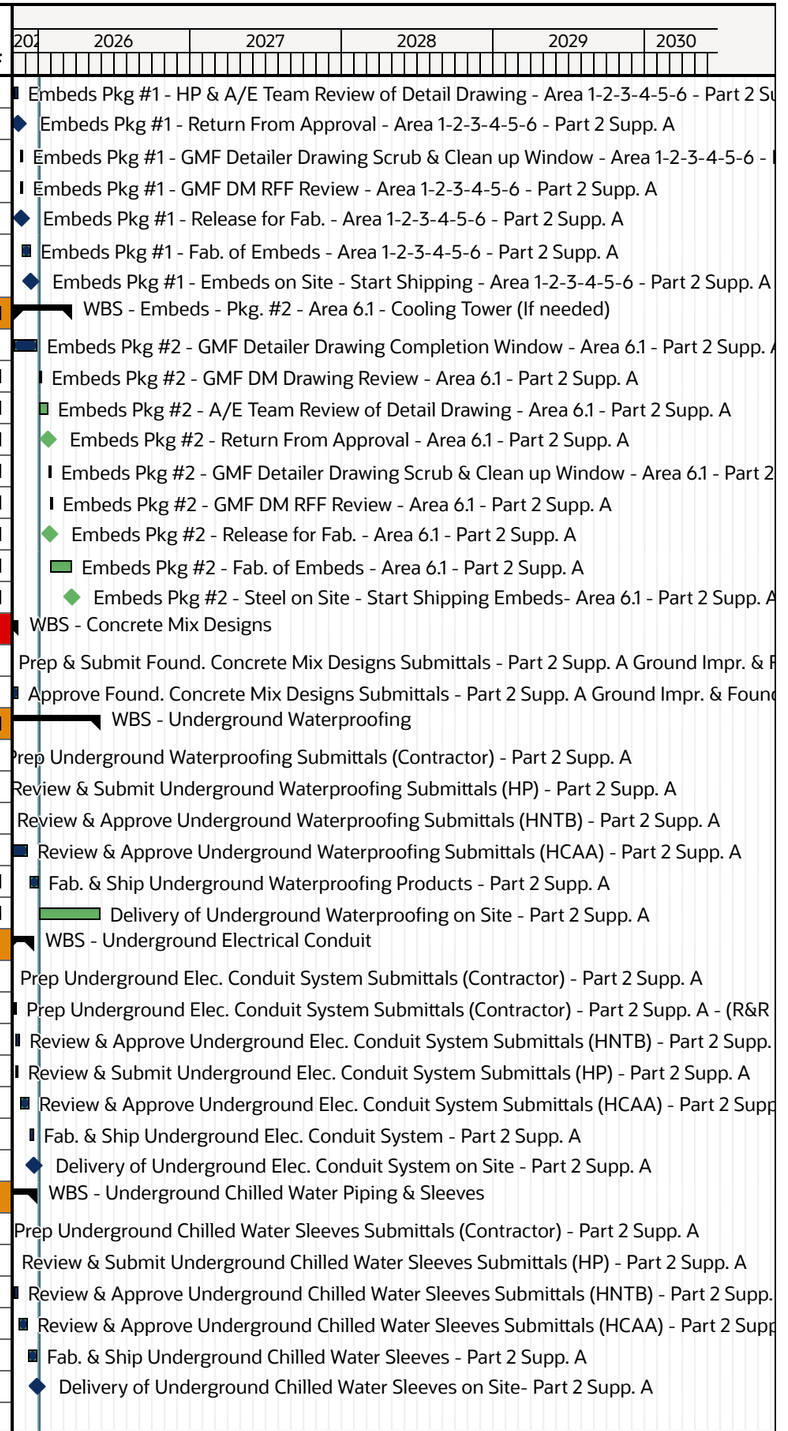


	ID	Name	Dur	Start	Finish	TF
2353	WBS - Underground Plumbing Submittals - ASD		54.0d	6-Oct-25 A	22-Dec-25 A	
2354	PR-P2-1A-61	Prep Underground Plumbing Submittals (Contractor) - Part 2 Supp. A	16.0d	6-Oct-25 A	27-Oct-25 A	
2355	PR-P2-1A-63	Review & Submit Underground Plumbing Submittals (HP) - Part 2 Supp. A	5.0d	28-Oct-25 A	3-Nov-25 A	
2356	PR-P2-1A-66	Review & Approve Underground Plumbing Submittals (HNTB) - Part 2 Supp. A	10.0d	4-Nov-25 A	17-Nov-25 A	
2357	PR-P2-1A-68	Review & Approve Underground Plumbing Submittals (HCAA) - Part 2 Supp. A	17.0d	18-Nov-25 A	12-Dec-25 A	
2358	PR-P2-1A-71	Fab. & Ship Underground Plumbing - Part 2 Supp. A	2.0d	15-Dec-25 A	16-Dec-25 A	
2359	PR-P2-1A-73	Delivery of Underground Plumbing on Site - Part 2 Supp. A	0.0d		22-Dec-25 A	
2360	WBS - Transformer Procurement - ASD		330.0d	13-Nov-25 A	4-Mar-27	271.0d
2361	PR-P1-1C1-70	Prep Transformer Submittals (Contractor) - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	270.0d
2362	PR-P1-1C1-75	Review & Submit Transformer Submittals (HP) - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	270.0d
2363	PR-P1-1C1-210	Review & Approve Transformer Submittals (HNTB) - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	270.0d
2364	PR-P1-1C1-215	Review & Approve Transformer Submittals (HCAA) - ASD	15.0d	4-Feb-26	24-Feb-26	270.0d
2365	PR-P1-1C1-250	Fab. & Ship Transformer - Part 2 Supp. A	365.0d	25-Feb-26	4-Mar-27	379.0d
2366	PR-P1-1C1-2410	Delivery of Transformer on Site - Part 2 Supp. A	0.0d		4-Mar-27	379.0d
2367	WBS - Long Lead Electrical		463.0d	20-Oct-25 A	16-Aug-27	230.0d
2368	WBS - Generator		445.0d	13-Nov-25 A	16-Aug-27	230.0d
2369	PR-P2-1B-180	Prep & Submit Generator Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	229.0d
2370	PR-P2-1B-7910	HP Approve Generator Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	229.0d
2371	PR-P2-1B-7920	HNTB Approve Generator Submittals - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	229.0d
2372	PR-P2-1B-200	HCAA Approve Generator Submittals - Part 2 Supp. A	15.0d	4-Feb-26	24-Feb-26	229.0d
2373	PR-P2-1B-220	Fab. & Ship Generator - Part 2 Supp. A	526.0d	25-Feb-26	16-Aug-27	322.0d
2374	PR-P2-1B-2430	Delivery of Generator on Site - Part 2 Supp. A	0.0d		16-Aug-27	322.0d
2375	WBS - Gear, Metering, SPD & Coordination Study		342.0d	20-Oct-25 A	24-Feb-27	166.0d
2376	PR-P2-1B-120	Prep & Submit Gear Submittals - Part 2 Supp. A	34.0d	13-Nov-25 A	5-Jan-26	166.0d
2377	PR-P2-1B-7930	HP Approve Gear Submittals - Part 2 Supp. A	5.0d	6-Jan-26	12-Jan-26	166.0d
2378	PR-P2-1B-7940	HNTB Approve Gear Submittals - Part 2 Supp. A	10.0d	13-Jan-26	26-Jan-26	166.0d
2379	PR-P2-1B-390	HCAA Approve Gear Submittals - Part 2 Supp. A	15.0d	27-Jan-26	16-Feb-26	166.0d
2380	PR-P2-1B-460	Fab. & Ship Gear - Part 2 Supp. A	365.0d	17-Feb-26	24-Feb-27	232.0d
2381	PR-P2-1B-2420	Delivery of Gear on Site - Part 2 Supp. A	0.0d		24-Feb-27	232.0d
2382	WBS - Gear Layout Package		39.0d	20-Oct-25 A	15-Dec-25 A	
2383	PR-P2-1B-7800	Prep & Submit Gear Layout Submittals - Part 2 Supp. A	25.0d	20-Oct-25 A	21-Nov-25 A	
2384	PR-P2-1B-7810	Approve Gear Layout Submittals - Part 2 Supp. A	14.0d	24-Nov-25 A	15-Dec-25 A	
2385	WBS - UPS Package		371.0d	13-Nov-25 A	30-Apr-27	169.0d
2386	PR-P2-1B-3000	Prep & Submit UPS Submittals - Part 2 Supp. A	40.0d	13-Nov-25 A	13-Jan-26	170.0d
2387	PR-P2-1B-7950	HP Approve UPS Submittals - Part 2 Supp. A	5.0d	14-Jan-26	20-Jan-26	170.0d
2388	PR-P2-1B-7960	HNTB Approve UPS Submittals - Part 2 Supp. A	10.0d	21-Jan-26	3-Feb-26	170.0d
2389	PR-P2-1B-3100	HCAA Approve UPS Submittals - Part 2 Supp. A	15.0d	4-Feb-26	24-Feb-26	170.0d
2390	PR-P2-1B-3200	Fab. & Ship UPS - Part 2 Supp. A	421.0d	25-Feb-26	29-Apr-27	237.0d
2391	PR-P2-1B-3300	Delivery of UPS on Site - Part 2 Supp. A	1.0d	30-Apr-27	30-Apr-27	237.0d
2392	WBS - Long Lead Mechanical		240.0d	12-Nov-25 A	22-Oct-26	362.0d
2393	WBS - Chillers Procurement		240.0d	12-Nov-25 A	22-Oct-26	362.0d
2394	PR-P2-1B-100	Prep & Submit Chillers Submittals - Part 2 Supp. A	30.0d	12-Nov-25 A	26-Dec-25 A	

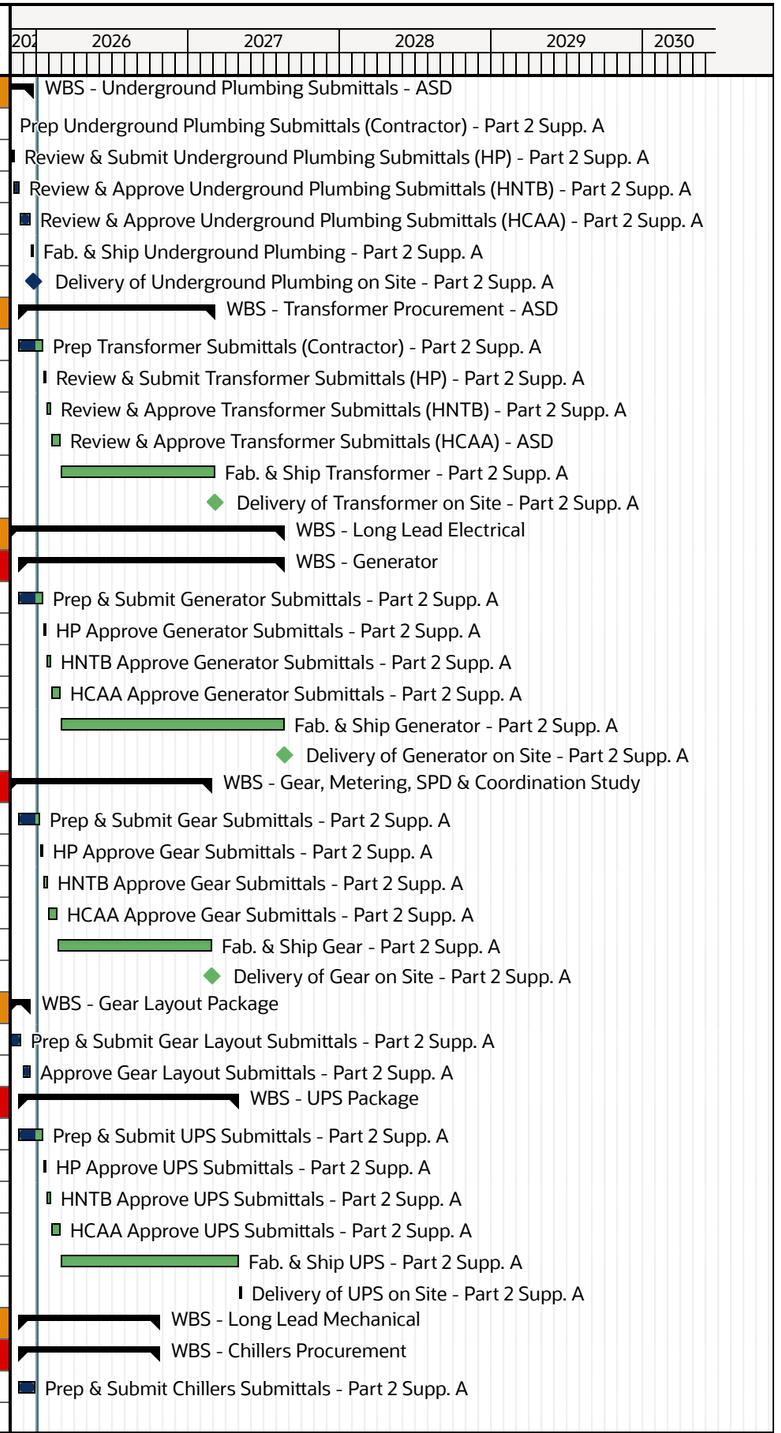


	ID	Name	Dur	Start	Finish	TF
2395	PR-P2-1B-7970	HP Approve Chillers Submittals - Part 2 Supp. A	5.0d	29-Dec-25	5-Jan-26	363.0d
2396	PR-P2-1B-7980	HNTB Approve Chillers Submittals - Part 2 Supp. A	10.0d	6-Jan-26	19-Jan-26	363.0d
2397	PR-P2-1B-280	HCAA Approve Chillers Submittals - Part 2 Supp. A	15.0d	20-Jan-26	9-Feb-26	363.0d
2398	PR-P2-1B-370	Fab. & Ship Chillers - Part 2 Supp. A	251.0d	10-Feb-26	22-Oct-26	508.0d
2399	PR-P2-1B-2330	Delivery of Chillers on Site - Part 2 Supp. A	0.0d		22-Oct-26	508.0d
2400	WBS - Long Lead Mill Order		100.0d	3-Nov-25 A	26-Mar-26	0.0d
2401	PR-P2-1B-3400	Prep & Submit Steel Mill Order Submittals - Part 2 Supp. A	20.0d	3-Nov-25 A	2-Dec-25 A	
2402	PR-P2-1B-7990	Issue / Process PO to Mill - Part 2 Supp. A	20.0d	3-Dec-25 A	31-Dec-25	0.0d
2403	PR-P2-1B-8000	Fab. & Ship Long Lead Mill Order - Part 2 Supp. A	84.0d	2-Jan-26	26-Mar-26	0.0d
2404	PR-P2-1B-3700	Delivery of Steel Mill Order to GMF Shop - Part 2 Supp. A	0.0d		26-Mar-26	0.0d
2405	WBS - Part 2 Supplement B - ASD Steel & Precast		267.0d	31-Oct-25 A	18-Nov-26	318.0d
2406	WBS - Structural Steel / Misc. Metals Procurement		267.0d	31-Oct-25 A	18-Nov-26	318.0d
2407	WBS - Structural Steel Seq 1		138.0d	31-Oct-25 A	18-May-26	0.0d
2408	PR-P2-1B-7600	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 1 - ...	28.0d	31-Oct-25 A	11-Dec-25 A	
2409	PR-P2-1B-7610	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 1 - Part 2 S...	5.0d	12-Dec-25 A	18-Dec-25 A	
2410	PR-P2-1B-7620	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	19-Dec-25 A	19-Jan-26	23.0d
2411	PR-P2-1B-7630	Return From Approval Struct. Steel/Misc. Metals SEQ 1 - Part 2 Supp. B	0.0d		19-Jan-26	23.0d
2412	PR-P2-1B-7640	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	20-Jan-26	2-Feb-26	23.0d
2413	PR-P2-1B-7650	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	8.0d	3-Feb-26	12-Feb-26	23.0d
2414	PR-P2-1B-7660	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	0.0d		12-Feb-26	23.0d
2415	PR-P2-1B-7670	Fab. of Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 Supp. B	37.0d	27-Mar-26	18-May-26	0.0d
2416	PR-P2-1B-7680	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 1 - Part 2 S...	0.0d		18-May-26	0.0d
2417	WBS - Structural Steel Seq 2		149.0d	31-Oct-25 A	3-Jun-26	5.0d
2418	PR-P2-1B-3710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 2 - ...	38.0d	31-Oct-25 A	26-Dec-25 A	
2419	PR-P2-1B-3720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 2 - Part 2 S...	5.0d	29-Dec-25	5-Jan-26	5.0d
2420	PR-P2-1B-3725	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 2...	20.0d	6-Jan-26	2-Feb-26	5.0d
2421	PR-P2-1B-3728	Return From Approval Struct. Steel/Misc. Metals SEQ 2 - Part 2 Supp. B	0.0d		2-Feb-26	5.0d
2422	PR-P2-1B-3730	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	3-Feb-26	16-Feb-26	5.0d
2423	PR-P2-1B-3740	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	5.0d	17-Feb-26	23-Feb-26	5.0d
2424	PR-P2-1B-3742	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	0.0d		23-Feb-26	5.0d
2425	PR-P2-1B-3744	Fab. of Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 Supp. B	71.0d	24-Feb-26	3-Jun-26	5.0d
2426	PR-P2-1B-3746	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 2 - Part 2 S...	0.0d		3-Jun-26	5.0d
2427	WBS - Structural Steel Seq 3		166.0d	31-Oct-25 A	26-Jun-26	3.0d
2428	PR-P2-1B-4810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 3 - ...	48.0d	31-Oct-25 A	12-Jan-26	3.0d
2429	PR-P2-1B-4820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 3 - Part 2 S...	5.0d	13-Jan-26	19-Jan-26	3.0d
2430	PR-P2-1B-4830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 3...	20.0d	20-Jan-26	16-Feb-26	3.0d
2431	PR-P2-1B-4840	Return From Approval Struct. Steel/Misc. Metals SEQ 3 - Part 2 Supp. B	0.0d		16-Feb-26	3.0d
2432	PR-P2-1B-4850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	17-Feb-26	2-Mar-26	3.0d
2433	PR-P2-1B-4870	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	5.0d	3-Mar-26	9-Mar-26	3.0d
2434	PR-P2-1B-4872	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	0.0d		9-Mar-26	3.0d
2435	PR-P2-1B-4874	Fab. of Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 Supp. B	76.0d	10-Mar-26	24-Jun-26	3.0d
2436	PR-P2-1B-4876	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 3 - Part 2 S...	0.0d		26-Jun-26	3.0d

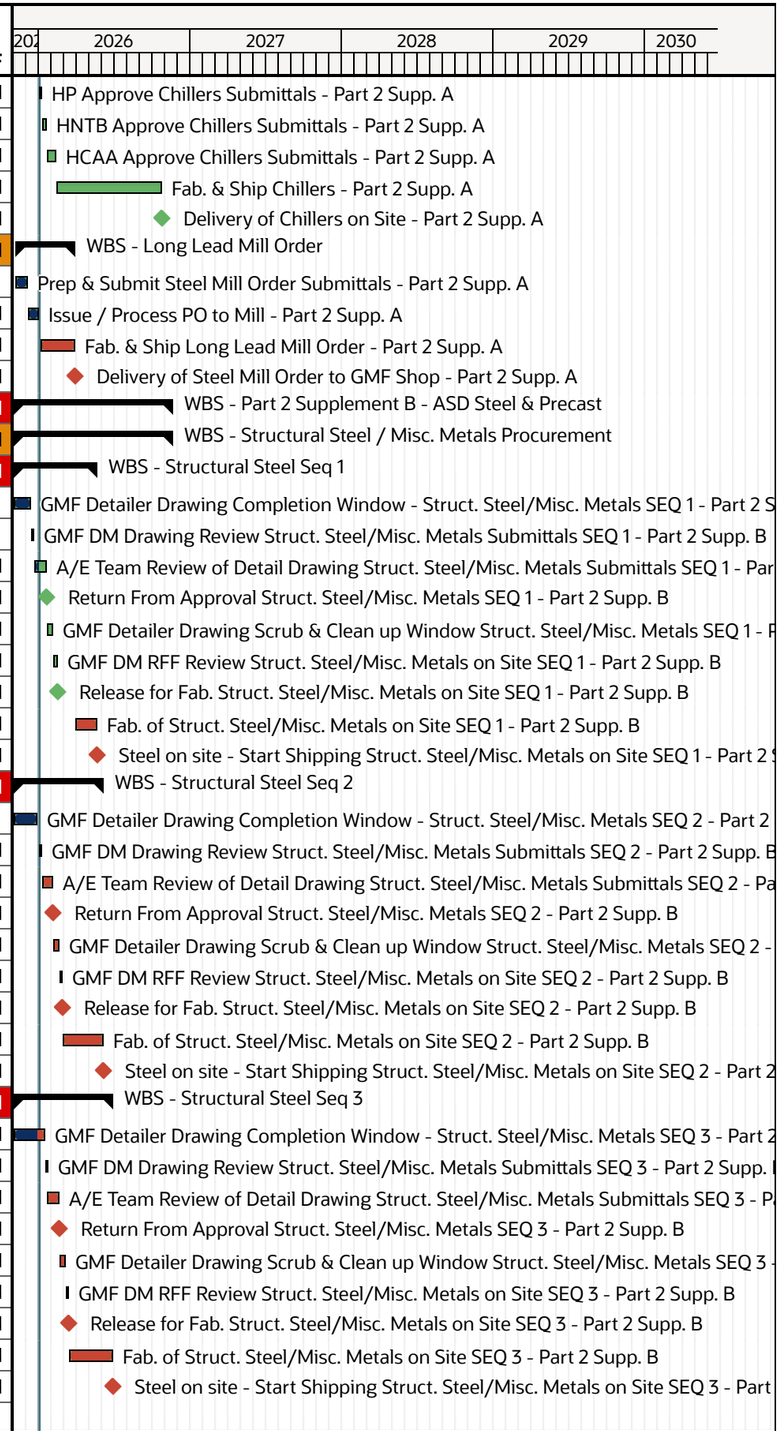


	ID	Name	Dur	Start	Finish	TF
2437	WBS - Structural Steel Seq 4		184.0d	31-Oct-25 A	23-Jul-26	3.0d
2438	PR-P2-1B-3760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 4 - ...	58.0d	31-Oct-25 A	26-Jan-26	3.0d
2439	PR-P2-1B-3770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 4 - Part 2 S...	5.0d	27-Jan-26	2-Feb-26	3.0d
2440	PR-P2-1B-3780	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 4...	20.0d	3-Feb-26	2-Mar-26	3.0d
2441	PR-P2-1B-3790	Return From Approval Struct. Steel/Misc. Metals SEQ 4 - Part 2 Supp. B	0.0d		2-Mar-26	3.0d
2442	PR-P2-1B-3800	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	3-Mar-26	16-Mar-26	3.0d
2443	PR-P2-1B-3802	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	5.0d	17-Mar-26	23-Mar-26	3.0d
2444	PR-P2-1B-3804	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	0.0d		23-Mar-26	3.0d
2445	PR-P2-1B-3806	Fab. of Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 Supp. B	76.0d	7-Apr-26	23-Jul-26	3.0d
2446	PR-P2-1B-3808	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 4 - Part 2 S...	0.0d		23-Jul-26	3.0d
2447	WBS - Structural Steel Seq 5		197.0d	31-Oct-25 A	11-Aug-26	9.0d
2448	PR-P2-1B-3810	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 5 - ...	63.0d	31-Oct-25 A	2-Feb-26	9.0d
2449	PR-P2-1B-3820	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 5 - Part 2 S...	5.0d	3-Feb-26	9-Feb-26	9.0d
2450	PR-P2-1B-3830	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 5...	20.0d	10-Feb-26	9-Mar-26	9.0d
2451	PR-P2-1B-3840	Return From Approval Struct. Steel/Misc. Metals SEQ 5 - Part 2 Supp. B	0.0d		9-Mar-26	9.0d
2452	PR-P2-1B-3850	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	10-Mar-26	23-Mar-26	9.0d
2453	PR-P2-1B-4880	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	5.0d	24-Mar-26	30-Mar-26	9.0d
2454	PR-P2-1B-4882	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	0.0d		30-Mar-26	9.0d
2455	PR-P2-1B-4284	Fab. of Struct. Steel/Misc. Metals on Site SEQ 5 - Part 2 Supp. B	76.0d	24-Apr-26	11-Aug-26	9.0d
2456	PR-P2-1B-4286	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 5- Part 2 Su...	0.0d		11-Aug-26	9.0d
2457	WBS - Structural Steel Seq 6		189.0d	31-Oct-25 A	30-Jul-26	36.0d
2458	PR-P2-1B-3860	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 6 - ...	73.0d	31-Oct-25 A	16-Feb-26	36.0d
2459	PR-P2-1B-3870	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 6 - Part 2 S...	5.0d	17-Feb-26	23-Feb-26	36.0d
2460	PR-P2-1B-3880	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 6...	20.0d	24-Feb-26	23-Mar-26	36.0d
2461	PR-P2-1B-3890	Return From Approval Struct. Steel/Misc. Metals SEQ 6 - Part 2 Supp. B	0.0d		23-Mar-26	36.0d
2462	PR-P2-1B-3900	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	24-Mar-26	6-Apr-26	36.0d
2463	PR-P2-1B-4900	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 6 - Part 2 Supp. B	5.0d	7-Apr-26	13-Apr-26	36.0d
2464	PR-P2-1B-4902	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 6 - Part 2 Supp. B	0.0d		13-Apr-26	36.0d
2465	PR-P2-1B-4904	Fab. of Struct. Steel/Misc. Metals on Site SEQ 6 - Part 2 Supp. B	76.0d	14-Apr-26	30-Jul-26	36.0d
2466	PR-P2-1B-4906	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 6 - Part 2 S...	0.0d		30-Jul-26	36.0d
2467	WBS - Structural Steel Seq 7		212.0d	31-Oct-25 A	1-Sep-26	29.0d
2468	PR-P2-1B-3910	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 7 - ...	68.0d	31-Oct-25 A	9-Feb-26	29.0d
2469	PR-P2-1B-3920	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 7 - Part 2 S...	5.0d	10-Feb-26	16-Feb-26	29.0d
2470	PR-P2-1B-3930	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 7...	20.0d	17-Feb-26	16-Mar-26	29.0d
2471	PR-P2-1B-3940	Return From Approval Struct. Steel/Misc. Metals SEQ 7 - Part 2 Supp. B	0.0d		16-Mar-26	29.0d
2472	PR-P2-1B-3950	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	17-Mar-26	30-Mar-26	29.0d
2473	PR-P2-1B-5040	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 7 - Part 2 Supp. B	5.0d	31-Mar-26	6-Apr-26	29.0d
2474	PR-P2-1B-5042	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 7 - Part 2 Supp. B	0.0d		6-Apr-26	29.0d
2475	PR-P2-1B-5044	Fab. of Struct. Steel/Misc. Metals on Site SEQ 7 - Part 2 Supp. B	75.0d	18-May-26	1-Sep-26	29.0d
2476	PR-P2-1B-5046	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 7 - Part 2 S...	0.0d		1-Sep-26	29.0d
2477	WBS - Structural Steel Seq 8		194.0d	31-Oct-25 A	6-Aug-26	45.0d
2478	PR-P2-1B-3960	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 8 - ...	78.0d	31-Oct-25 A	23-Feb-26	45.0d

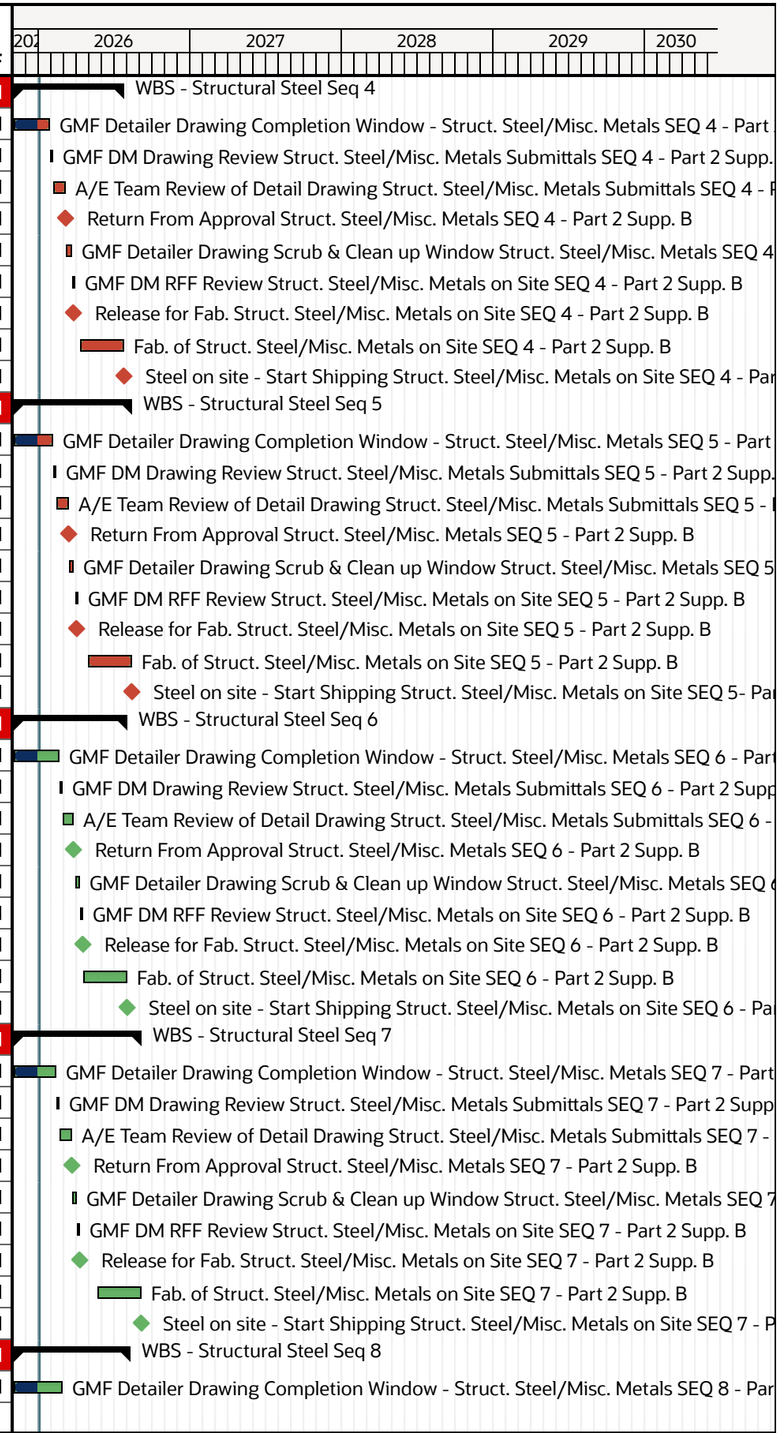


	ID	Name	Dur	Start	Finish	TF
2479	PR-P2-1B-3970	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 8 - Part 2 S...	5.0d	24-Feb-26	2-Mar-26	45.0d
2480	PR-P2-1B-3980	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 8...	20.0d	3-Mar-26	30-Mar-26	45.0d
2481	PR-P2-1B-3990	Return From Approval Struct. Steel/Misc. Metals SEQ 8 - Part 2 Supp. B	0.0d		30-Mar-26	45.0d
2482	PR-P2-1B-4000	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	31-Mar-26	13-Apr-26	45.0d
2483	PR-P2-1B-4002	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 8 - Part 2 Supp. B	6.0d	14-Apr-26	21-Apr-26	45.0d
2484	PR-P2-1B-4004	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 8 - Part 2 Supp. B	0.0d		21-Apr-26	45.0d
2485	PR-P2-1B-4006	Fab. of Struct. Steel/Misc. Metals on Site SEQ 8 - Part 2 Supp. B	75.0d	22-Apr-26	6-Aug-26	45.0d
2486	PR-P2-1B-4008	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 8 - Part 2 S...	0.0d		6-Aug-26	45.0d
2487	WBS - Structural Steel Seq 9		204.0d	31-Oct-25 A	20-Aug-26	43.0d
2488	PR-P2-1B-4710	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 9 - ...	88.0d	31-Oct-25 A	9-Mar-26	43.0d
2489	PR-P2-1B-4720	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 9 - Part 2 S...	5.0d	10-Mar-26	16-Mar-26	43.0d
2490	PR-P2-1B-4730	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 9...	20.0d	17-Mar-26	13-Apr-26	43.0d
2491	PR-P2-1B-4740	Return From Approval Struct. Steel/Misc. Metals SEQ 9 - Part 2 Supp. B	0.0d		13-Apr-26	43.0d
2492	PR-P2-1B-4750	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	11.0d	14-Apr-26	28-Apr-26	43.0d
2493	PR-P2-1B-4920	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 9 - Part 2 Supp. B	5.0d	29-Apr-26	5-May-26	43.0d
2494	PR-P2-1B-4922	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 9 - Part 2 Supp. B	0.0d		5-May-26	43.0d
2495	PR-P2-1B-4924	Fab. of Struct. Steel/Misc. Metals on Site SEQ 9 - Part 2 Supp. B	75.0d	6-May-26	20-Aug-26	43.0d
2496	PR-P2-1B-4926	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 9 - Part 2 S...	0.0d		20-Aug-26	43.0d
2497	WBS - Structural Steel Seq 10		219.0d	31-Oct-25 A	11-Sep-26	30.0d
2498	PR-P2-1B-4760	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 10 ...	93.0d	31-Oct-25 A	16-Mar-26	30.0d
2499	PR-P2-1B-4770	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 10 -Part 2 ...	5.0d	17-Mar-26	23-Mar-26	30.0d
2500	PR-P2-1B-4780	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	21.0d	24-Mar-26	21-Apr-26	30.0d
2501	PR-P2-1B-4790	Return From Approval Struct. Steel/Misc. Metals SEQ 10 - Part 2 Supp. B	0.0d		21-Apr-26	30.0d
2502	PR-P2-1B-4800	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	22-Apr-26	5-May-26	30.0d
2503	PR-P2-1B-4802	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 10 - Part 2 Supp. B	5.0d	6-May-26	12-May-26	30.0d
2504	PR-P2-1B-4804	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 10 - Part 2 Supp. B	0.0d		12-May-26	30.0d
2505	PR-P2-1B-4806	Fab. of Struct. Steel/Misc. Metals on Site SEQ 10 - Part 2 Supp. B	75.0d	28-May-26	11-Sep-26	30.0d
2506	PR-P2-1B-4808	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 10 - Part 2 ...	0.0d		11-Sep-26	30.0d
2507	WBS - Structural Steel Seq 11		214.0d	31-Oct-25 A	3-Sep-26	48.0d
2508	PR-P2-1B-4010	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 11 ...	98.0d	31-Oct-25 A	23-Mar-26	48.0d
2509	PR-P2-1B-4020	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 11 - Part 2 ...	5.0d	24-Mar-26	30-Mar-26	48.0d
2510	PR-P2-1B-4030	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	21.0d	31-Mar-26	28-Apr-26	48.0d
2511	PR-P2-1B-4040	Return From Approval Struct. Steel/Misc. Metals SEQ 11 - Part 2 Supp. B	0.0d		28-Apr-26	48.0d
2512	PR-P2-1B-4050	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	29-Apr-26	12-May-26	48.0d
2513	PR-P2-1B-4940	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 11 - Part 2 Supp. B	5.0d	13-May-26	19-May-26	48.0d
2514	PR-P2-1B-4942	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 11 - Part 2 Supp. B	0.0d		19-May-26	48.0d
2515	PR-P2-1B-4944	Fab. of Struct. Steel/Misc. Metals on Site SEQ 11 - Part 2 Supp. B	75.0d	20-May-26	3-Sep-26	48.0d
2516	PR-P2-1B-4946	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 11- Part 2 S...	0.0d		3-Sep-26	48.0d
2517	WBS - Structural Steel Seq 12		231.0d	31-Oct-25 A	29-Sep-26	35.0d
2518	PR-P2-1B-6970	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 12 ...	103.0d	31-Oct-25 A	30-Mar-26	35.0d
2519	PR-P2-1B-6980	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 12 - Part 2 ...	5.0d	31-Mar-26	6-Apr-26	35.0d
2520	PR-P2-1B-6990	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	21.0d	7-Apr-26	5-May-26	35.0d

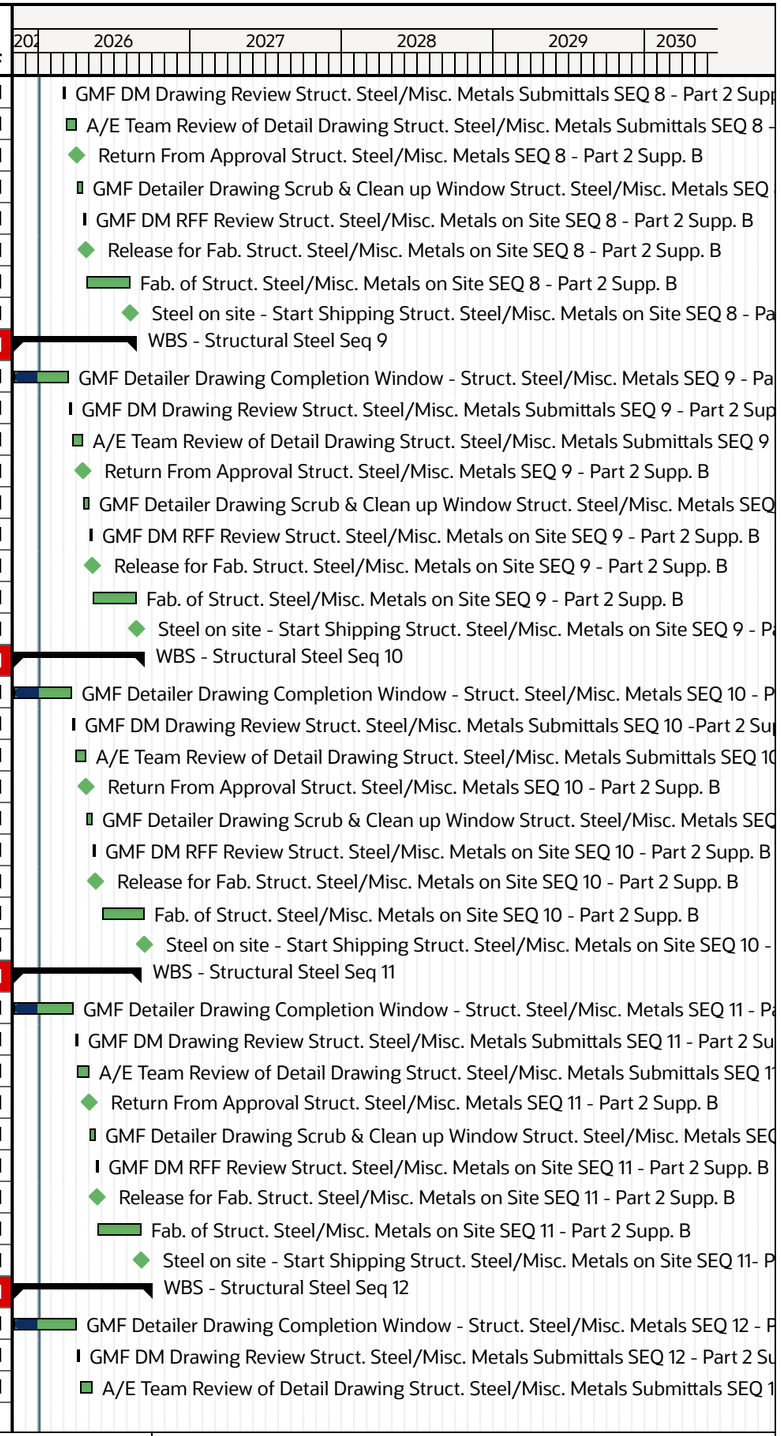


	ID	Name	Dur	Start	Finish	TF
2521	PR-P2-1B-7000	Return From Approval Struct. Steel/Misc. Metals SEQ 12 - Part 2 Supp. B	0.0d		5-May-26	35.0d
2522	PR-P2-1B-7010	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	6-May-26	19-May-26	35.0d
2523	PR-P2-1B-7020	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 12 - Part 2 Supp. B	5.0d	20-May-26	27-May-26	35.0d
2524	PR-P2-1B-7030	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 12 - Part 2 Supp. B	0.0d		27-May-26	35.0d
2525	PR-P2-1B-7040	Fab. of Struct. Steel/Misc. Metals on Site SEQ 12 - Part 2 Supp. B	75.0d	15-Jun-26	29-Sep-26	35.0d
2526	PR-P2-1B-7050	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 12 - Part 2 ...	0.0d		29-Sep-26	35.0d
2527	WBS - Structural Steel Seq 13		231.0d	31-Oct-25 A	29-Sep-26	45.0d
2528	PR-P2-1B-7060	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 13 ...	108.0d	31-Oct-25 A	6-Apr-26	45.0d
2529	PR-P2-1B-7070	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 13 - Part 2 ...	5.0d	7-Apr-26	13-Apr-26	45.0d
2530	PR-P2-1B-7080	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	21.0d	14-Apr-26	12-May-26	45.0d
2531	PR-P2-1B-7090	Return From Approval Struct. Steel/Misc. Metals SEQ 13 - Part 2 Supp. B	0.0d		12-May-26	45.0d
2532	PR-P2-1B-7100	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	13-May-26	27-May-26	45.0d
2533	PR-P2-1B-7110	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 13 - Part 2 Supp. B	5.0d	28-May-26	3-Jun-26	45.0d
2534	PR-P2-1B-7120	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 13 - Part 2 Supp. B	0.0d		3-Jun-26	45.0d
2535	PR-P2-1B-7130	Fab. of Struct. Steel/Misc. Metals on Site SEQ 13 - Part 2 Supp. B	75.0d	15-Jun-26	29-Sep-26	45.0d
2536	PR-P2-1B-7140	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 13 - Part 2 ...	0.0d		29-Sep-26	45.0d
2537	WBS - Structural Steel Seq 14		237.0d	31-Oct-25 A	7-Oct-26	43.0d
2538	PR-P2-1B-7150	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 14 ...	113.0d	31-Oct-25 A	13-Apr-26	43.0d
2539	PR-P2-1B-7160	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 14 - Part 2 ...	6.0d	14-Apr-26	21-Apr-26	43.0d
2540	PR-P2-1B-7170	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	22-Apr-26	19-May-26	43.0d
2541	PR-P2-1B-7180	Return From Approval Struct. Steel/Misc. Metals SEQ 14- Part 2 Supp. B	0.0d		19-May-26	43.0d
2542	PR-P2-1B-7190	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	20-May-26	3-Jun-26	43.0d
2543	PR-P2-1B-7200	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 14 - Part 2 Supp. B	5.0d	4-Jun-26	10-Jun-26	43.0d
2544	PR-P2-1B-7210	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 14 - Part 2 Supp. B	0.0d		10-Jun-26	43.0d
2545	PR-P2-1B-7220	Fab. of Struct. Steel/Misc. Metals on Site SEQ 14 - Part 2 Supp. B	75.0d	23-Jun-26	7-Oct-26	43.0d
2546	PR-P2-1B-7230	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 14 - Part 2 ...	0.0d		7-Oct-26	43.0d
2547	WBS - Structural Steel Seq 15		242.0d	31-Oct-25 A	14-Oct-26	42.0d
2548	PR-P2-1B-7240	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 15 ...	119.0d	31-Oct-25 A	21-Apr-26	42.0d
2549	PR-P2-1B-7250	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 15 - Part 2 ...	5.0d	22-Apr-26	28-Apr-26	42.0d
2550	PR-P2-1B-7260	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	29-Apr-26	27-May-26	42.0d
2551	PR-P2-1B-7270	Return From Approval Struct. Steel/Misc. Metals SEQ 15 - Part 2 Supp. B	0.0d		27-May-26	42.0d
2552	PR-P2-1B-7280	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	28-May-26	10-Jun-26	42.0d
2553	PR-P2-1B-7290	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 15 - Part 2 Supp. B	5.0d	11-Jun-26	17-Jun-26	42.0d
2554	PR-P2-1B-7300	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 15 - Part 2 Supp. B	0.0d		17-Jun-26	42.0d
2555	PR-P2-1B-7310	Fab. of Struct. Steel/Misc. Metals on Site SEQ 15 - Part 2 Supp. B	75.0d	30-Jun-26	14-Oct-26	42.0d
2556	PR-P2-1B-7320	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 15 - Part 2 ...	0.0d		14-Oct-26	42.0d
2557	WBS - Structural Steel Seq 16		249.0d	31-Oct-25 A	23-Oct-26	49.0d
2558	PR-P2-1B-7330	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 16 ...	124.0d	31-Oct-25 A	28-Apr-26	49.0d
2559	PR-P2-1B-7340	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 16 - Part 2 ...	5.0d	29-Apr-26	5-May-26	49.0d
2560	PR-P2-1B-7350	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	6-May-26	3-Jun-26	49.0d
2561	PR-P2-1B-7360	Return From Approval Struct. Steel/Misc. Metals SEQ 16 - Part 2 Supp. B	0.0d		3-Jun-26	49.0d
2562	PR-P2-1B-7370	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	4-Jun-26	17-Jun-26	49.0d

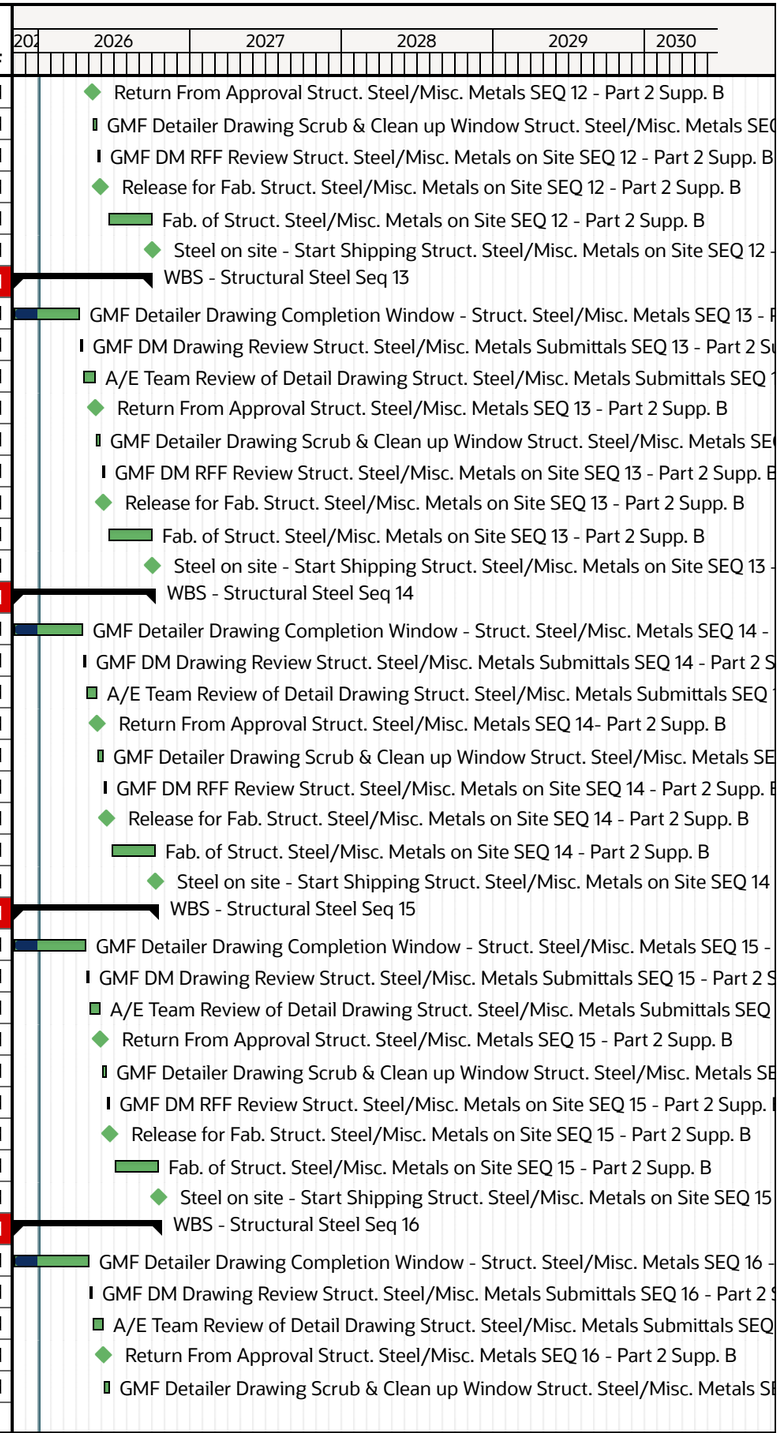


	ID	Name	Dur	Start	Finish	TF
2563	PR-P2-1B-7380	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 16 - Part 2 Supp. B	5.0d	18-Jun-26	24-Jun-26	49.0d
2564	PR-P2-1B-7390	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 16 - Part 2 Supp. B	0.0d		24-Jun-26	49.0d
2565	PR-P2-1B-7400	Fab. of Struct. Steel/Misc. Metals on Site SEQ 16 - Part 2 Supp. B	75.0d	10-Jul-26	23-Oct-26	49.0d
2566	PR-P2-1B-7410	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 16 - Part 2 ...	0.0d		23-Oct-26	49.0d
2567	WBS - Structural Steel Seq 17		257.0d	31-Oct-25 A	4-Nov-26	48.0d
2568	PR-P2-1B-7420	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 17 ...	129.0d	31-Oct-25 A	5-May-26	48.0d
2569	PR-P2-1B-7430	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 17 - Part 2 ...	5.0d	6-May-26	12-May-26	48.0d
2570	PR-P2-1B-7440	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	13-May-26	10-Jun-26	48.0d
2571	PR-P2-1B-7450	Return From Approval Struct. Steel/Misc. Metals SEQ 17 - Part 2 Supp. B	0.0d		10-Jun-26	48.0d
2572	PR-P2-1B-7460	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	11-Jun-26	24-Jun-26	48.0d
2573	PR-P2-1B-7470	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 17 - Part 2 Supp. B	5.0d	25-Jun-26	1-Jul-26	48.0d
2574	PR-P2-1B-7480	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 17 - Part 2 Supp. B	0.0d		1-Jul-26	48.0d
2575	PR-P2-1B-7490	Fab. of Struct. Steel/Misc. Metals on Site SEQ 17 - Part 2 Supp. B	75.0d	22-Jul-26	4-Nov-26	48.0d
2576	PR-P2-1B-7500	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 17 - Part 2 ...	0.0d		4-Nov-26	48.0d
2577	WBS - Structural Steel Seq 18		258.0d	31-Oct-25 A	5-Nov-26	49.0d
2578	PR-P2-1B-7510	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 18 ...	134.0d	31-Oct-25 A	12-May-26	49.0d
2579	PR-P2-1B-7520	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 18 - Part 2 ...	5.0d	13-May-26	19-May-26	49.0d
2580	PR-P2-1B-7530	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	20-May-26	17-Jun-26	49.0d
2581	PR-P2-1B-7540	Return From Approval Struct. Steel/Misc. Metals SEQ 18 - Part 2 Supp. B	0.0d		17-Jun-26	49.0d
2582	PR-P2-1B-7550	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	18-Jun-26	1-Jul-26	49.0d
2583	PR-P2-1B-7560	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 18 - Part 2 Supp. B	5.0d	2-Jul-26	9-Jul-26	49.0d
2584	PR-P2-1B-7570	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 18 - Part 2 Supp. B	0.0d		9-Jul-26	49.0d
2585	PR-P2-1B-7580	Fab. of Struct. Steel/Misc. Metals on Site SEQ 18 - Part 2 Supp. B	75.0d	23-Jul-26	5-Nov-26	49.0d
2586	PR-P2-1B-7590	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 18 - Part 2 ...	0.0d		5-Nov-26	49.0d
2587	WBS - Structural Steel Seq 19		267.0d	31-Oct-25 A	18-Nov-26	57.0d
2588	PR-P2-1B-7690	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 19 ...	139.0d	31-Oct-25 A	19-May-26	57.0d
2589	PR-P2-1B-7700	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 19 - Part 2 ...	5.0d	20-May-26	27-May-26	57.0d
2590	PR-P2-1B-7710	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals SEQ 1...	20.0d	28-May-26	24-Jun-26	57.0d
2591	PR-P2-1B-7720	Return From Approval Struct. Steel/Misc. Metals SEQ 19 - Part 2 Supp. B	0.0d		24-Jun-26	57.0d
2592	PR-P2-1B-7730	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals SEQ...	10.0d	25-Jun-26	9-Jul-26	57.0d
2593	PR-P2-1B-7740	GMF DM RFF Review Struct. Steel/Misc. Metals on Site SEQ 19 - Part 2 Supp. B	5.0d	10-Jul-26	16-Jul-26	57.0d
2594	PR-P2-1B-7750	Release for Fab. Struct. Steel/Misc. Metals on Site SEQ 19 - Part 2 Supp. B	0.0d		16-Jul-26	57.0d
2595	PR-P2-1B-7760	Fab. of Struct. Steel/Misc. Metals on Site SEQ 19 - Part 2 Supp. B	75.0d	5-Aug-26	18-Nov-26	57.0d
2596	PR-P2-1B-7770	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site SEQ 19 - Part 2 ...	0.0d		18-Nov-26	57.0d
2597	WBS - Structural Steel Seq 20 (Cooling Tower)		262.0d	31-Oct-25 A	11-Nov-26	323.0d
2598	PR-P2-1B-7820	GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals (Cooling...	124.0d	31-Oct-25 A	28-Apr-26	323.0d
2599	PR-P2-1B-7830	GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals (Cooling Tower) ...	5.0d	29-Apr-26	5-May-26	323.0d
2600	PR-P2-1B-7840	A/E Team Review of Detail Drawing Struct. Steel/Misc. Metals Submittals (Cooli...	20.0d	6-May-26	3-Jun-26	323.0d
2601	PR-P2-1B-7850	Return From Approval Struct. Steel/Misc. Metals (Cooling Tower) - Part 2 Supp. B	0.0d		3-Jun-26	323.0d
2602	PR-P2-1B-7860	GMF Detailer Drawing Scrub & Clean up Window Struct. Steel/Misc. Metals (Co...	10.0d	4-Jun-26	17-Jun-26	323.0d
2603	PR-P2-1B-7870	GMF DM RFF Review Struct. Steel/Misc. Metals on Site (Cooling Tower) - Part 2 ...	5.0d	18-Jun-26	24-Jun-26	323.0d
2604	PR-P2-1B-7880	Release for Fab. Struct. Steel/Misc. Metals on Site (Cooling Tower) - Part 2 Supp...	0.0d		24-Jun-26	323.0d

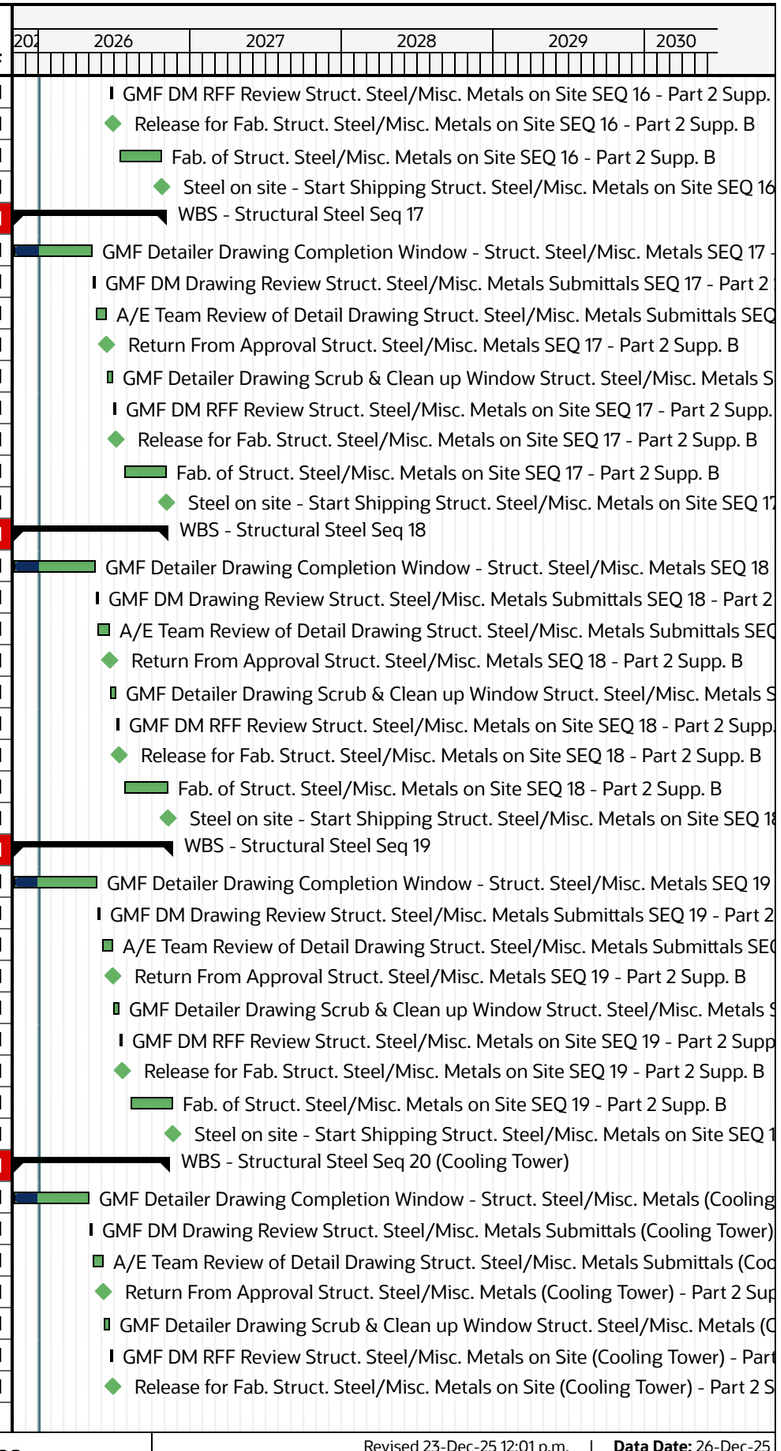


	ID	Name	Dur	Start	Finish	TF
2605	PR-P2-1B-7890	Fab. of Struct. Steel/Misc. Metals on Site (Cooling Tower) - Part 2 Supp. B	75.0d	1-Jul-26	15-Oct-26	323.0d
2606	PR-P2-1B-7900	Steel on site - Start Shipping Struct. Steel/Misc. Metals on Site (Cooling Tower) ...	0.0d		11-Nov-26	323.0d
2607	WBS - Precast Procurement		151.0d	11-Nov-25 A	16-Jun-26	174.0d
2608	WBS - Elevator Cores		90.0d	11-Nov-25 A	20-Mar-26	21.0d
2609	PR-P2-1B-6700	Prep & Submit Elevator Cores Submittals - Part 2 Supp. B	14.0d	11-Nov-25 A	2-Dec-25 A	
2610	PR-P2-1B-6710	HP Review & Submit Elevator Cores Submittals - Part 2 Supp. B	10.0d	3-Dec-25 A	16-Dec-25 A	
2611	PR-P2-1B-7780	HNTB Review & Approve Elevator Cores Submittals - Part 2 Supp. B	11.0d	17-Dec-25 A	2-Jan-26	21.0d
2612	PR-P2-1B-6720	HCAA Review & Approve Elevator Cores - Part 2 Supp. B	15.0d	5-Jan-26	23-Jan-26	21.0d
2613	PR-P2-1B-6730	Fab. & Ship Elevator Cores - Part 2 Supp. B	56.0d	24-Jan-26	20-Mar-26	31.0d
2614	PR-P2-1B-6780	Delivery of Elevator Cores on Site- Part 2 Supp. B	0.0d		20-Mar-26	31.0d
2615	WBS - Exterior Arch Precast Panels		120.0d	29-Dec-25	16-Jun-26	174.0d
2616	PR-P2-1B-6740	Prep & Submit Exterior Arch Precast Panel Submittals - Part 2 Supp. B	30.0d	29-Dec-25	9-Feb-26	174.0d
2617	PR-P2-1B-6750	HP Review & Submit Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	10-Feb-26	23-Feb-26	174.0d
2618	PR-P2-1B-7790	HNTB Review & Approve Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	24-Feb-26	9-Mar-26	174.0d
2619	PR-P2-1B-6760	HCAA Review & Approve Exterior Arch Precast Panel Submittals - Part 2 Supp. B	10.0d	10-Mar-26	23-Mar-26	174.0d
2620	PR-P2-1B-6790	Fab. & Ship Exterior Arch Precast Panel - Part 2 Supp. B	84.0d	24-Mar-26	16-Jun-26	245.0d
2621	PR-P2-1B-6770	Delivery of Exterior Arch Precast Panel on Site - Part 2 Supp. B	0.0d		16-Jun-26	245.0d
2622	WBS - Part 1 Supplement C Wave 1 - Core & Shell Procurement		862.0d	20-Oct-25 A	13-Mar-29	261.0d
2623	WBS - Concrete Procurement SOG & SOMD - ASD		55.0d	13-Feb-26	30-Apr-26	109.0d
2624	PR-P1-1C1-450	Prep Concrete Submittal (Contractor)- SOG & SOMD - ASD	20.0d	13-Feb-26	12-Mar-26	101.0d
2625	PR-P1-1C1-455	Review & Submit Concrete Submittal (HP) - SOG & SOMD - ASD	10.0d	13-Mar-26	26-Mar-26	101.0d
2626	PR-P1-1C1-500	Review & Approve Concrete Submittal (HNTB) - SOG & SOMD - ASD	10.0d	27-Mar-26	9-Apr-26	101.0d
2627	PR-P1-1C1-505	Review & Approve Concrete Submittal (HCAA) - SOG & SOMD - ASD	15.0d	10-Apr-26	30-Apr-26	101.0d
2628	PR-P1-1C1-520	Concrete Mix Design Approved - SOG & SOMD - ASD	0.0d		30-Apr-26	109.0d
2629	WBS - Masonry Procurement - ASD		145.0d	13-Feb-26	8-Sep-26	37.0d
2630	PR-P2-1C1-6850	Prep Masonry Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	36.0d
2631	PR-P2-1C1-6860	Review & Submit Masonry Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	36.0d
2632	PR-P2-1C1-6870	Review & Approve Masonry Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	36.0d
2633	PR-P2-1C1-6880	Review & Approve Masonry Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	36.0d
2634	PR-P2-1C1-6890	Fab. & Ship Masonry - ASD	113.0d	15-May-26	8-Sep-26	51.0d
2635	PR-P2-1C1-6900	Delivery of Masonry on Site - ASD	0.0d		8-Sep-26	51.0d
2636	WBS - Column Covers Procurement - ASD		145.0d	13-Feb-26	8-Sep-26	396.0d
2637	PR-P2-1C1-700	Prep Column Covers Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	394.0d
2638	PR-P2-1C1-705	Review & Submit Column Covers Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	394.0d
2639	PR-P2-1C1-1210	Review & Approve Column Covers Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	394.0d
2640	PR-P2-1C1-1215	Review & Approve Column Covers Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	394.0d
2641	PR-P2-1C1-1600	Fab. & Ship Column Covers - ASD	113.0d	15-May-26	8-Sep-26	554.0d
2642	PR-P2-1C1-2270	Delivery of Column Covers on Site - ASD	0.0d		8-Sep-26	554.0d
2643	WBS - Interior Metal Specialties Procurement - ASD		105.0d	13-Feb-26	13-Jul-26	538.0d
2644	PR-P2-1C1-6910	Prep Interior Metal Specialties Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	537.0d
2645	PR-P2-1C1-6920	Review & Submit Interior Metal Specialties Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	537.0d
2646	PR-P2-1C1-6930	Review & Approve Interior Metal Specialties Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	537.0d

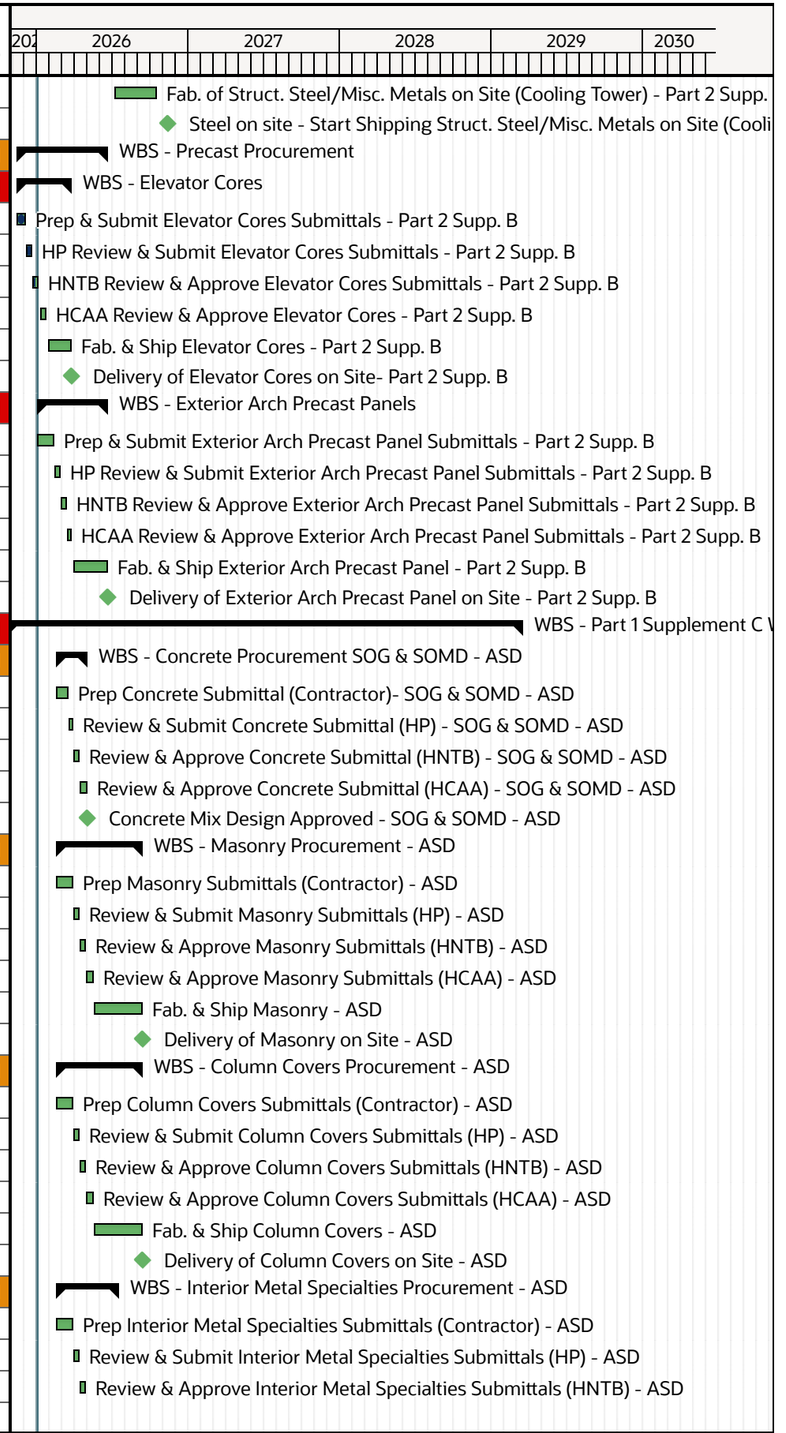


	ID	Name	Dur	Start	Finish	TF
2647	PR-P2-1C1-6940	Review & Approve Interior Metal Specialties Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	537.0d
2648	PR-P2-1C1-6950	Fab. & Ship Interior Metal Specialties - ASD	57.0d	15-May-26	13-Jul-26	754.0d
2649	PR-P2-1C1-6960	Delivery of Interior Metal Specialties on Site - ASD	0.0d		13-Jul-26	754.0d
2650	WBS - Wall & Door Protection Procurement - ASD		105.0d	13-Feb-26	13-Jul-26	568.0d
2651	PR-P2-1C1-7850	Prep Wall & Door Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	567.0d
2652	PR-P2-1C1-7860	Review & Submit Wall & Door Protection Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	567.0d
2653	PR-P2-1C1-7870	Review & Approve Wall & Door Protection Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	567.0d
2654	PR-P2-1C1-7880	Review & Approve Wall & Door Protection Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	567.0d
2655	PR-P2-1C1-7890	Fab. & Ship Wall & Door Protection - ASD	57.0d	15-May-26	13-Jul-26	796.0d
2656	PR-P2-1C1-7900	Delivery of Wall & Door Protection on Site - ASD	0.0d		13-Jul-26	796.0d
2657	WBS - Glass Handrail Procurement - ASD		153.0d	13-Feb-26	20-Sep-26	421.0d
2658	PR-P1-1C1-650	Prep Glass Handrail Submittals (Contractor) - ASD	40.0d	13-Feb-26	9-Apr-26	420.0d
2659	PR-P1-1C1-655	Review & Submit Glass Handrail Submittals (HP) - ASD	10.0d	10-Apr-26	23-Apr-26	420.0d
2660	PR-P1-1C1-1550	Review & Approve Glass Handrail Submittals (HNTB) - ASD	10.0d	24-Apr-26	7-May-26	420.0d
2661	PR-P1-1C1-1555	Review & Approve Glass Handrail Submittals (HCAA) - ASD	15.0d	8-May-26	29-May-26	420.0d
2662	PR-P1-1C1-1900	Fab. & Ship Glass Handrail - ASD	111.0d	30-May-26	20-Sep-26	589.0d
2663	PR-P1-1C1-2290	Delivery of Glass Handrail on Site - ASD	0.0d		20-Sep-26	589.0d
2664	WBS - Waterproofing, Caulks & Sealants Procurement - ASD		75.0d	13-Feb-26	29-May-26	302.0d
2665	PR-P1-1C1-600	Prep Water Proofing, Caulks & Sealants Submittals (Contractor) - ASD	20.0d	13-Feb-26	12-Mar-26	101.0d
2666	PR-P1-1C1-605	Review & Submit Water Proofing, Caulks & Sealants Submittals (HP)- ASD	10.0d	13-Mar-26	26-Mar-26	101.0d
2667	PR-P1-1C1-1020	Review & Approve Water Proofing, Caulks & Sealants Submittals (HNTB) - ASD	10.0d	27-Mar-26	9-Apr-26	101.0d
2668	PR-P1-1C1-1025	Review & Approve Water Proofing, Caulks & Sealants Submittals (HCAA) - ASD	15.0d	10-Apr-26	30-Apr-26	101.0d
2669	PR-P1-1C1-1140	Fab. & Ship Water Proofing, Caulks & Sealants - ASD	28.0d	1-May-26	29-May-26	425.0d
2670	PR-P1-1C1-1870	Delivery of Water Proofing, Caulks & Sealants on Site - ASD	0.0d		29-May-26	425.0d
2671	WBS - Interior/Exterior Metal Wall Panels Procurement - ASD		119.0d	13-Feb-26	31-Jul-26	260.0d
2672	PR-P1-1C1-610	Interior/Exterior Metal Wall Panels Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2673	PR-P1-1C1-615	Review & Submit Interior/Exterior Metal Wall Panels Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2674	PR-P1-1C1-1150	Review & Approve Interior/Exterior Metal Wall Panels Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2675	PR-P1-1C1-1155	Review & Approve Interior/Exterior Metal Wall Panels Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2676	PR-P1-1C1-1520	Fab. & Ship Interior/Exterior Metal Wall Panels - ASD	75.0d	15-May-26	31-Jul-26	366.0d
2677	PR-P1-1C1-2210	Delivery of Interior Interior/Exterior Metal Wall Panels on Site - ASD	0.0d		31-Jul-26	366.0d
2678	WBS - Roofing Procurement - ASD		125.0d	13-Feb-26	10-Aug-26	153.0d
2679	PR-P1-1C1-580	Prep Roofing Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2680	PR-P1-1C1-585	Review & Submit Roofing Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2681	PR-P1-1C1-1120	Review & Approve Roofing Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2682	PR-P1-1C1-1125	Review & Approve Roofing Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2683	PR-P1-1C1-1510	Fab. & Ship Roofing - ASD	85.0d	15-May-26	10-Aug-26	215.0d
2684	PR-P1-1C1-2170	Delivery of Roofing on Site - ASD	0.0d		10-Aug-26	215.0d
2685	WBS - Fall Protection (Roofing Contractor) Procurement - ASD		144.0d	13-Feb-26	6-Sep-26	134.0d
2686	PR-P2-1C1-7480	Prep Fall Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
2687	PR-P2-1C1-7490	Review & Submit Fall Protection Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	133.0d
2688	PR-P2-1C1-7500	Review & Approve Fall Protection Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	133.0d

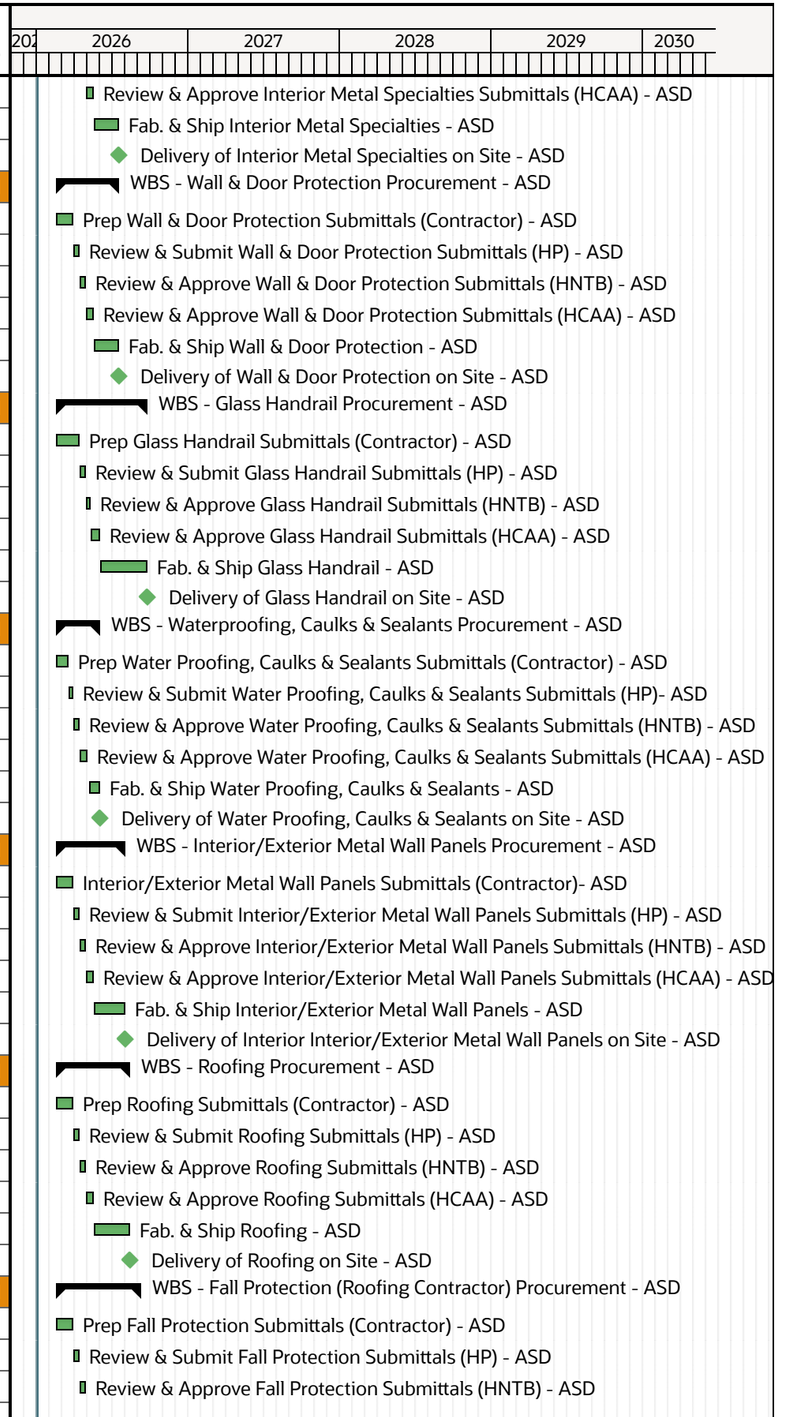

	ID	Name	Dur	Start	Finish	TF
2689	PR-P2-1C1-7510	Review & Approve Fall Protection Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	133.0d
2690	PR-P2-1C1-7520	Fab. & Ship Fall Protection - ASD	112.0d	15-May-26	6-Sep-26	188.0d
2691	PR-P2-1C1-7530	Delivery of Fall Protection on Site - ASD	0.0d		6-Sep-26	188.0d
2692	WBS - Spray Fireproofing & Insulation (K-13) Procurement - ASD		160.0d	13-Feb-26	29-Sep-26	80.0d
2693	PR-P1-1C1-590	Prep Spray Fireproofing & Insulation Submittals (Contractor) - ASD	20.0d	13-Feb-26	12-Mar-26	81.0d
2694	PR-P1-1C1-595	Review & Submit Spray Fireproofing & Insulation Submittals (HP)- ASD	10.0d	13-Mar-26	26-Mar-26	81.0d
2695	PR-P1-1C1-1010	Review & Approve Spray Fireproofing & Insulation Submittals (HNTB) - ASD	10.0d	27-Mar-26	9-Apr-26	81.0d
2696	PR-P1-1C1-1015	Review & Approve Spray Fireproofing & Insulation Submittals (HCAA) - ASD	15.0d	10-Apr-26	30-Apr-26	81.0d
2697	PR-P1-1C1-1130	Fab. & Ship Spray Fireproofing & Insulation - ASD	148.0d	1-May-26	29-Sep-26	114.0d
2698	PR-P1-1C1-2350	Delivery of Spray Fireproofing & Insulation on Site - ASD	0.0d		29-Sep-26	114.0d
2699	WBS - Glass & Glazing/Curtainwall Procurement - ASD		183.0d	13-Feb-26	1-Nov-26	96.0d
2700	PR-P1-1C1-630	Prep Glass & Glazing/Curtainwall Submittals (Contractor) - ASD	40.0d	13-Feb-26	9-Apr-26	81.0d
2701	PR-P1-1C1-635	Review & Submit Glass & Glazing/Curtainwall Submittals (HP) - ASD	10.0d	10-Apr-26	23-Apr-26	81.0d
2702	PR-P1-1C1-1530	Review & Approve Glass & Glazing/Curtainwall Submittals (HNTB) - ASD	10.0d	24-Apr-26	7-May-26	81.0d
2703	PR-P1-1C1-1535	Review & Approve Glass & Glazing/Curtainwall Submittals (HCAA) - ASD	15.0d	8-May-26	29-May-26	81.0d
2704	PR-P1-1C1-1880	Fab. & Ship Glass & Glazing/Curtainwall - ASD	153.0d	30-May-26	1-Nov-26	136.0d
2705	PR-P1-1C1-2360	Delivery of Glass & Glazing/Curtainwall on Site - ASD	0.0d		1-Nov-26	136.0d
2706	WBS - Louvers Procurement (Mechanical) - ASD		109.0d	13-Feb-26	19-Jul-26	275.0d
2707	PR-P2-1C1-940	Prep Louvers Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	273.0d
2708	PR-P2-1C1-945	Review & Submit Louvers Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	273.0d
2709	PR-P2-1C1-1430	Review & Approve Louvers Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	273.0d
2710	PR-P2-1C1-1435	Review & Approve Louvers Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	273.0d
2711	PR-P2-1C1-1810	Fab. & Ship Louvers - ASD	63.0d	15-May-26	19-Jul-26	385.0d
2712	PR-P2-1C1-2120	Delivery of Louvers on Site - ASD	0.0d		19-Jul-26	385.0d
2713	WBS - Automatic/Glass Door, Frames, & Hardware Procurement - ASD		124.0d	13-Feb-26	8-Aug-26	293.0d
2714	PR-P2-1C1-660	Prep Automatic/Glass Door & Hardware Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	175.0d
2715	PR-P2-1C1-665	Review & Submit Automatic/Glass Door & Hardware Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	175.0d
2716	PR-P2-1C1-1170	Review & Approve Automatic/Glass Door, Frames, & Hardware Submittals (HNT…	10.0d	10-Apr-26	23-Apr-26	175.0d
2717	PR-P2-1C1-1175	Review & Approve Automatic/Glass Door & Hardware Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	175.0d
2718	PR-P2-1C1-1560	Fab. & Ship Automatic/Glass Doors & Hardware - ASD	83.0d	15-May-26	8-Aug-26	412.0d
2719	PR-P2-1C1-7390	Fab. & Ship Automatic/Glass Door Frames - ASD	48.0d	15-May-26	2-Jul-26	248.0d
2720	PR-P2-1C1-2220	Delivery of Automatic/Glass Door Frames on Site - ASD	0.0d		2-Jul-26	248.0d
2721	PR-P2-1C1-7410	Delivery of Automatic/Glass Door & Hardware on Site - ASD	0.0d		8-Aug-26	412.0d
2722	WBS - Interior Wall Panels (Specialties/Decorative Glass) Procurement - ASD		183.0d	13-Feb-26	1-Nov-26	408.0d
2723	PR-P1-1C1-640	Prep Interior Wall Panels (Specialties/Decorative Glass) Submittals (Contractor)-…	40.0d	13-Feb-26	9-Apr-26	407.0d
2724	PR-P1-1C1-645	Review & Submit Interior Wall Panels (Specialties/Decorative Glass) Submittals …	10.0d	10-Apr-26	23-Apr-26	407.0d
2725	PR-P1-1C1-1540	Review & Approve Interior Wall Panels (Specialties/Decorative Glass) Submittal…	10.0d	24-Apr-26	7-May-26	407.0d
2726	PR-P1-1C1-1545	Review & Approve Interior Wall Panels (Specialties/Decorative Glass) Submittal…	15.0d	8-May-26	29-May-26	407.0d
2727	PR-P1-1C1-1890	Fab. & Ship Interior Wall Panels (Specialties/Decorative Glass) - ASD	153.0d	30-May-26	1-Nov-26	572.0d
2728	PR-P1-1C1-2370	Delivery of Interior Wall Panels (Specialties/Decorative Glass) on Site - ASD	0.0d		1-Nov-26	572.0d
2729	WBS - Drywall & Related Procurement - ASD		100.0d	13-Feb-26	6-Jul-26	73.0d
2730	PR-P1-1C1-670	Prep Drywall & Related Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	74.0d

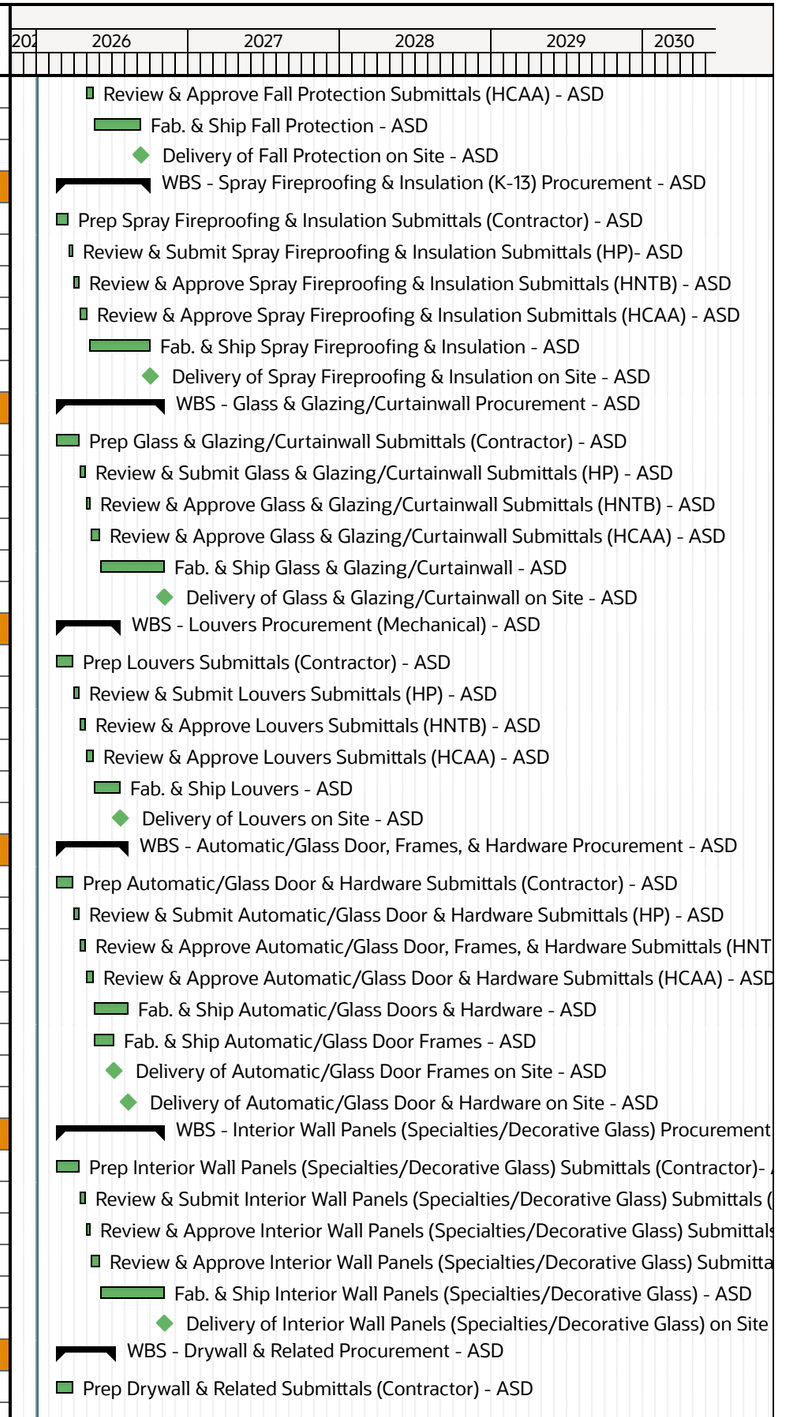


	ID	Name	Dur	Start	Finish	TF
2731	PR-P1-1C1-675	Review & Submit Drywall & Related Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	74.0d
2732	PR-P1-1C1-1180	Review & Approve Drywall & Related Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	74.0d
2733	PR-P1-1C1-1185	Review & Approve Drywall & Related Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	74.0d
2734	PR-P1-1C1-1570	Fab. & Ship Drywall & Related - ASD	50.0d	15-May-26	6-Jul-26	103.0d
2735	PR-P1-1C1-2010	Delivery of Drywall & Related on Site - ASD	0.0d		6-Jul-26	103.0d
2736	WBS - Acoustical Metal Panel Ceilings Procurement - ASD		130.0d	13-Feb-26	17-Aug-26	431.0d
2737	PR-P2-1C1-720	Prep Acoustical Metal Panel Ceilings Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	430.0d
2738	PR-P2-1C1-725	Review & Submit Acoustical Metal Panel Ceilings Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	430.0d
2739	PR-P2-1C1-1230	Review & Approve Acoustical Metal Panel Ceilings Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	430.0d
2740	PR-P2-1C1-1235	Review & Approve Acoustical Metal Panel Ceilings Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	430.0d
2741	PR-P2-1C1-1620	Fab. & Ship Acoustical Metal Panel Ceilings - ASD	92.0d	15-May-26	17-Aug-26	603.0d
2742	PR-P2-1C1-2200	Delivery of Acoustical Metal Panel Ceilings on Site - ASD	0.0d		17-Aug-26	603.0d
2743	WBS - Acoustical Panel Ceilings Procurement - ASD		130.0d	13-Feb-26	17-Aug-26	245.0d
2744	PR-P2-1C1-7970	Prep Acoustical Panel Ceilings Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	244.0d
2745	PR-P2-1C1-7980	Review & Submit Acoustical Panel Ceilings Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	244.0d
2746	PR-P2-1C1-7990	Review & Approve Acoustical Panel Ceilings Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	244.0d
2747	PR-P2-1C1-8000	Review & Approve Acoustical Panel Ceilings Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	244.0d
2748	PR-P2-1C1-8010	Fab. & Ship Acoustical Panel Ceilings - ASD	92.0d	15-May-26	17-Aug-26	343.0d
2749	PR-P2-1C1-8020	Delivery of Acoustical Panel Ceilings on Site - ASD	0.0d		17-Aug-26	343.0d
2750	WBS - Suspended Wood Ceiling Procurement - ASD		130.0d	13-Feb-26	17-Aug-26	436.0d
2751	PR-P2-1C1-7910	Prep Suspended Wood Ceiling Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	435.0d
2752	PR-P2-1C1-7920	Review & Submit Suspended Wood Ceiling Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	435.0d
2753	PR-P2-1C1-7930	Review & Approve Suspended Wood Ceiling Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	435.0d
2754	PR-P2-1C1-7940	Review & Approve Suspended Wood Ceiling Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	435.0d
2755	PR-P2-1C1-7950	Fab. & Ship Suspended Wood Ceiling - ASD	92.0d	15-May-26	17-Aug-26	610.0d
2756	PR-P2-1C1-7960	Delivery of Suspended Wood Ceiling on Site - ASD	0.0d		17-Aug-26	610.0d
2757	WBS - Escalators - ES-01 & ES-03 Procurement - ASD		175.0d	13-Feb-26	20-Oct-26	133.0d
2758	PR-P1-1C1-790	Prep Escalators 1 & 3 Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
2759	PR-P1-1C1-795	Review & Submit Escalators 1 & 3 Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	133.0d
2760	PR-P1-1C1-1290	Review & Approve Escalators 1 & 3 Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	133.0d
2761	PR-P1-1C1-1295	Review & Approve Escalators 1 & 3 Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	133.0d
2762	PR-P1-1C1-1670	Fab. & Ship Escalators 1 & 3 - ASD	155.0d	15-May-26	20-Oct-26	187.0d
2763	PR-P1-1C1-2380	Delivery of Escalators 1 & 3 on Site - ASD	0.0d		20-Oct-26	187.0d
2764	WBS - Escalators - ES-02 & ES-04 Procurement - ASD		175.0d	13-Feb-26	20-Oct-26	133.0d
2765	PR-P1-1C1-800	Prep Escalators 2 & 4 Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	133.0d
2766	PR-P1-1C1-805	Review & Submit Escalators 2 & 4 Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	133.0d
2767	PR-P1-1C1-1300	Review & Approve Escalators 2 & 4 Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	133.0d
2768	PR-P1-1C1-1305	Review & Approve Escalators 2 & 4 Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	133.0d
2769	PR-P1-1C1-1680	Fab. & Ship Escalators 2 & 4 - ASD	155.0d	15-May-26	20-Oct-26	187.0d
2770	PR-P1-1C1-2390	Delivery of Escalators 2 & 4 on Site - ASD	0.0d		20-Oct-26	187.0d
2771	WBS - Elevators EL-01 - EL-11 Procurement - ASD		617.0d	13-Feb-26	18-Jul-28	62.0d
2772	PR-P1-1C1-810	Prep Elev. 01-11 Submittals - ASD	50.0d	13-Feb-26	23-Apr-26	0.0d

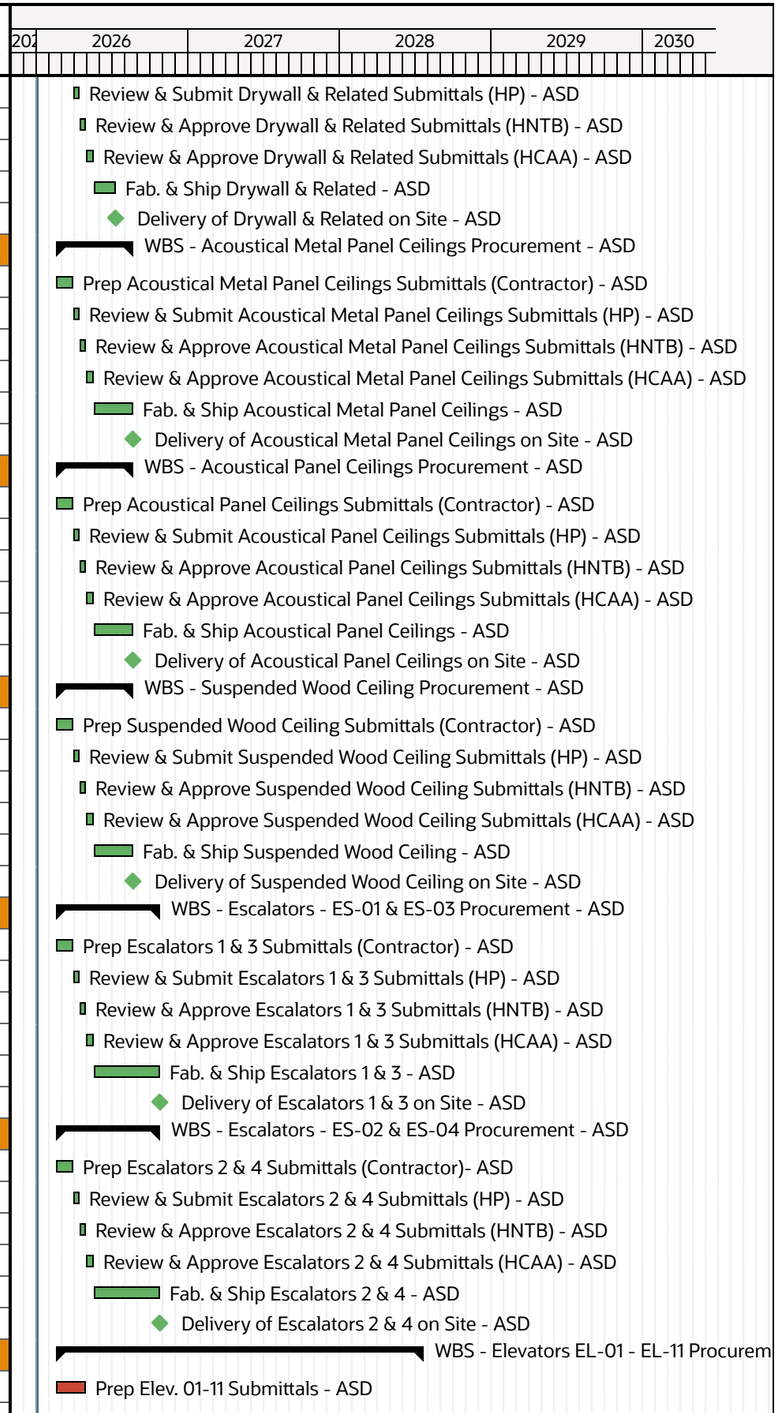


	ID	Name	Dur	Start	Finish	TF
2773	PR-P1-1C1-815	Review & Submit Elev. 01-11 Submittals (HP) - ASD	10.0d	24-Apr-26	7-May-26	0.0d
2774	PR-P1-1C1-1310	Review & Approve Elev. 01-11 Submittals (HNTB) - ASD	10.0d	8-May-26	21-May-26	0.0d
2775	PR-P1-1C1-1315	Review & Approve Elev. 01-11 Submittals (HCAA) - ASD	15.0d	22-May-26	12-Jun-26	0.0d
2776	PR-P1-1C1-1690	Fab. & Ship Elev. 01-02 - ASD	153.0d	13-Jun-26	15-Nov-26	469.0d
2777	PR-P1-1C1-3890	Fab. & Ship Elev. 08 - ASD	154.0d	13-Jun-26	16-Nov-26	88.0d
2778	PR-P1-1C1-3900	Fab. & Ship Elev. 09-10-11 - ASD	155.0d	13-Jun-26	17-Nov-26	143.0d
2779	PR-P1-1C1-3800	Fab. & Ship Elev. 03-04 - ASD	156.0d	13-Jun-26	18-Nov-26	472.0d
2780	PR-P1-1C1-3830	Fab. & Ship Elev. 06-07 - ASD	154.0d	13-Jun-26	16-Nov-26	2.0d
2781	PR-P1-1C1-3860	Fab. & Ship Elev. 05 - ASD	155.0d	13-Jun-26	17-Nov-26	143.0d
2782	PR-P1-1C1-2400	Delivery of Elev. 01-02 on Site - ASD	0.0d		15-Nov-26	469.0d
2783	PR-P1-1C1-3790	Off Site Staging of Elev. 01-02 - ASD	117.0d	16-Nov-26	16-Mar-27	469.0d
2784	PR-P1-1C1-3970	Delivery of Elev. 08 on Site - ASD	0.0d		16-Nov-26	88.0d
2785	PR-P1-1C1-3850	Delivery of Elev. 06-07 on Site - ASD	0.0d		16-Nov-26	2.0d
2786	PR-P1-1C1-3930	Off Site Staging of Elev. 08 - ASD	593.0d	17-Nov-26	18-Jul-28	88.0d
2787	PR-P1-1C1-3840	Off Site Staging of Elev. 06-07 - ASD	497.0d	17-Nov-26	11-Apr-28	2.0d
2788	PR-P1-1C1-3980	Delivery of Elev. 09-10-11 on Site - ASD	0.0d		17-Nov-26	143.0d
2789	PR-P1-1C1-3880	Delivery of Elev. 05 on Site - ASD	0.0d		17-Nov-26	143.0d
2790	PR-P1-1C1-3940	Off Site Staging of Elev. 09-10-11 - ASD	441.0d	18-Nov-26	16-Feb-28	143.0d
2791	PR-P1-1C1-3870	Off Site Staging of Elev. 05 - ASD	441.0d	18-Nov-26	16-Feb-28	143.0d
2792	PR-P1-1C1-3820	Delivery of Elev. 03-04 on Site - ASD	0.0d		18-Nov-26	472.0d
2793	PR-P1-1C1-3810	Off Site Staging of Elev. 03-04 - ASD	113.0d	19-Nov-26	15-Mar-27	472.0d
2794	WBS - Elevators EL-12 - EL-15 5500 MRLs Submittals Procurement - ASD		215.0d	13-Feb-26	17-Dec-26	216.0d
2795	PR-P1-1C1-3730	Prep Elev. 12-15 5500 MRLs Submittals - ASD	40.0d	13-Feb-26	9-Apr-26	215.0d
2796	PR-P1-1C1-3770	Review & Submit Elev. 12-15 5500 MRLs Submittals (HP) - ASD	10.0d	10-Apr-26	23-Apr-26	215.0d
2797	PR-P1-1C1-3760	Review & Approve Elev. 12-15 5500 MRLs Submittals (HNTB) - ASD	10.0d	24-Apr-26	7-May-26	215.0d
2798	PR-P1-1C1-3780	Review & Approve Elev. 12-15 5500 MRLs Submittals (HCAA) - ASD	15.0d	8-May-26	29-May-26	215.0d
2799	PR-P1-1C1-3740	Fab. & Ship Elev. 12-15 5500 MRLs - ASD	197.0d	30-May-26	17-Dec-26	304.0d
2800	PR-P1-1C1-3750	Delivery of Elev. 12-15 5500 MRLs on Site - ASD	0.0d		17-Dec-26	304.0d
2801	WBS - Fire Suppression Procurement - ASD		138.0d	13-Feb-26	27-Aug-26	94.0d
2802	PR-P1-1C1-820	Prep Fire Suppression Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	95.0d
2803	PR-P1-1C1-825	Review & Submit Fire Suppression Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	95.0d
2804	PR-P1-1C1-1320	Review & Approve Fire Suppression Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	95.0d
2805	PR-P1-1C1-1325	Review & Approve Fire Suppression Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	95.0d
2806	PR-P1-1C1-1700	Fab. & Ship Fire Suppression - ASD	102.0d	15-May-26	27-Aug-26	134.0d
2807	PR-P1-1C1-2160	Delivery of Fire Suppression on Site - ASD	0.0d		27-Aug-26	134.0d
2808	WBS - Landscaping & Irrigation (Sitework) Procurement - ASD		105.0d	13-Feb-26	13-Jul-26	387.0d
2809	PR-P1-1C1-850	Prep Landscaping & Irrigation Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
2810	PR-P1-1C1-855	Review & Submit Landscaping & Irrigation Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	386.0d
2811	PR-P1-1C1-1350	Review & Approve Landscaping & Irrigation Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	386.0d
2812	PR-P1-1C1-1355	Review & Approve Landscaping & Irrigation Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	386.0d
2813	PR-P1-1C1-1730	Fab. & Ship Landscaping & Irrigation - ASD	57.0d	15-May-26	13-Jul-26	543.0d
2814	PR-P1-1C1-2080	Delivery of Landscaping & Irrigation on Site - ASD	0.0d		13-Jul-26	543.0d




	ID	Name	Dur	Start	Finish	TF
2815	WBS - Roadway Work (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	415.0d
2816	PR-P1-1C1-10	Prep Roadway Work (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	415.0d
2817	PR-P1-1C1-15	Review & Submit Roadway Work (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	415.0d
2818	PR-P1-1C1-20	Review & Approve Roadway Work (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	415.0d
2819	PR-P1-1C1-25	Review & Approve Roadway Work (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	415.0d
2820	PR-P1-1C1-30	Fab. & Ship Roadway Work (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	582.0d
2821	PR-P1-1C1-40	Delivery of Roadway Work (Sitework) on Site - ASD	0.0d		12-Jun-26	582.0d
2822	WBS - UG Sanitary (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	96.0d
2823	PR-P1-1C1-3070	Prep UG Sanitary (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	96.0d
2824	PR-P1-1C1-3110	Review & Submit UG Sanitary (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	96.0d
2825	PR-P1-1C1-3100	Review & Approve UG Sanitary (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	96.0d
2826	PR-P1-1C1-3120	Review & Approve UG Sanitary (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	96.0d
2827	PR-P1-1C1-3080	Fab. & Ship UG Sanitary (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	135.0d
2828	PR-P1-1C1-3090	Delivery of UG Sanitary (Sitework) on Site - ASD	0.0d		12-Jun-26	135.0d
2829	WBS - Concrete Mix Design Curbs & Sidewalks (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	510.0d
2830	PR-P1-1C1-3130	Prep Concrete Mix Design (Curbs & Sidewalks Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	510.0d
2831	PR-P1-1C1-3170	Review & Submit Concrete Mix Design (Curbs & Sidewalks Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	510.0d
2832	PR-P1-1C1-3160	Review & Approve Concrete Mix Design (Curbs & Sidewalks Sitework) (HNTB) - ...	10.0d	10-Apr-26	23-Apr-26	510.0d
2833	PR-P1-1C1-3180	Review & Approve Concrete Mix Design (Curbs & Sidewalks Sitework) (HCAA) - ...	15.0d	24-Apr-26	14-May-26	510.0d
2834	PR-P1-1C1-3140	Fab. & Ship Concrete Mix Design (Curbs & Sidewalks Sitework) - ASD	28.0d	15-May-26	12-Jun-26	715.0d
2835	PR-P1-1C1-3150	Delivery of Concrete Mix Design (Curbs & Sidewalks Sitework) on Site - ASD	0.0d		12-Jun-26	715.0d
2836	WBS - UG Fire Suppression (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	166.0d
2837	PR-P1-1C1-3190	Prep UG Fire Suppression (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	166.0d
2838	PR-P1-1C1-3230	Review & Submit UG Fire Suppression (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	166.0d
2839	PR-P1-1C1-3220	Review & Approve UG Fire Suppression (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	166.0d
2840	PR-P1-1C1-3240	Review & Approve UG Fire Suppression (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	166.0d
2841	PR-P1-1C1-3200	Fab. & Ship UG Fire Suppression (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	235.0d
2842	PR-P1-1C1-3210	Delivery of UG Fire Suppression (Sitework) on Site - ASD	0.0d		12-Jun-26	235.0d
2843	WBS - Grease Traps (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	307.0d
2844	PR-P1-1C1-3250	Prep Grease Traps (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	307.0d
2845	PR-P1-1C1-3290	Review & Submit Grease Traps (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	307.0d
2846	PR-P1-1C1-3280	Review & Approve Grease Traps (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	307.0d
2847	PR-P1-1C1-3300	Review & Approve Grease Traps (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	307.0d
2848	PR-P1-1C1-3260	Fab. & Ship Grease Traps (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	432.0d
2849	PR-P1-1C1-3270	Delivery of Grease Traps (Sitework) on Site - ASD	0.0d		12-Jun-26	432.0d
2850	WBS - Oil/Water Separator (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	307.0d
2851	PR-P1-1C1-3310	Prep Oil/Water Separator (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	307.0d
2852	PR-P1-1C1-3350	Review & Submit Oil/Water Separator (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	307.0d
2853	PR-P1-1C1-3340	Review & Approve Oil/Water Separator (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	307.0d
2854	PR-P1-1C1-3360	Review & Approve Oil/Water Separator (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	307.0d
2855	PR-P1-1C1-3320	Fab. & Ship Oil/Water Separator (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	432.0d
2856	PR-P1-1C1-3330	Delivery of Oil/Water Separator (Sitework) on Site - ASD	0.0d		12-Jun-26	432.0d

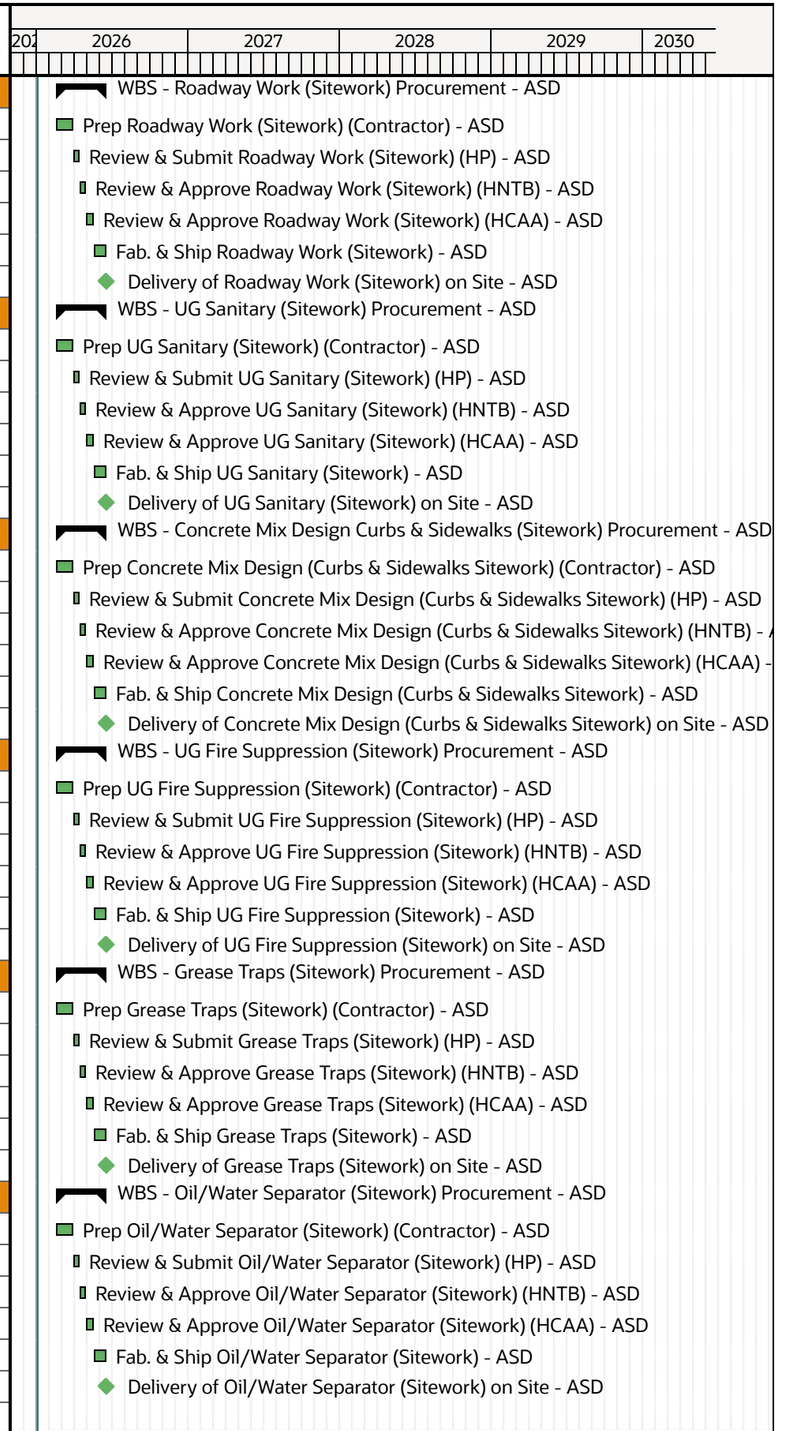


	ID	Name	Dur	Start	Finish	TF
2857	WBS - Concrete Mix Design Paving (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	432.0d
2858	PR-P1-1C1-3370	Prep Concrete Mix Design (Paving Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	432.0d
2859	PR-P1-1C1-3410	Review & Submit Concrete Mix Design (Paving Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	432.0d
2860	PR-P1-1C1-3400	Review & Approve Concrete Mix Design (Paving Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	432.0d
2861	PR-P1-1C1-3420	Review & Approve Concrete Mix Design (Paving Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	432.0d
2862	PR-P1-1C1-3380	Fab. & Ship Concrete Mix Design (Paving Sitework) - ASD	28.0d	15-May-26	12-Jun-26	607.0d
2863	PR-P1-1C1-3390	Delivery of Concrete Mix Design (Paving Sitework) on Site - ASD	0.0d		12-Jun-26	607.0d
2864	WBS - Asphalt Paving (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	606.0d
2865	PR-P1-1C1-3430	Prep Asphalt Paving (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	606.0d
2866	PR-P1-1C1-3470	Review & Submit Asphalt Paving (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	606.0d
2867	PR-P1-1C1-3460	Review & Approve Asphalt Paving (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	606.0d
2868	PR-P1-1C1-3480	Review & Approve Asphalt Paving (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	606.0d
2869	PR-P1-1C1-3440	Fab. & Ship Asphalt Paving (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	851.0d
2870	PR-P1-1C1-3450	Delivery of Asphalt Paving (Sitework) on Site - ASD	0.0d		12-Jun-26	851.0d
2871	WBS - Pavement Striping (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	611.0d
2872	PR-P1-1C1-3490	Prep Pavement Striping (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	611.0d
2873	PR-P1-1C1-3530	Review & Submit Pavement Striping (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	611.0d
2874	PR-P1-1C1-3520	Review & Approve Pavement Striping (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	611.0d
2875	PR-P1-1C1-3540	Review & Approve Pavement Striping (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	611.0d
2876	PR-P1-1C1-3500	Fab. & Ship Pavement Striping (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	858.0d
2877	PR-P1-1C1-3510	Delivery of Pavement Striping (Sitework) on Site - ASD	0.0d		12-Jun-26	858.0d
2878	WBS - Potable Water Systems (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	166.0d
2879	PR-P1-1C1-3550	Prep Potable Water Systems (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	166.0d
2880	PR-P1-1C1-3590	Review & Submit Potable Water Systems (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	166.0d
2881	PR-P1-1C1-3580	Review & Approve Potable Water Systems (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	166.0d
2882	PR-P1-1C1-3600	Review & Approve Potable Water Systems (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	166.0d
2883	PR-P1-1C1-3560	Fab. & Ship Potable Water Systems (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	235.0d
2884	PR-P1-1C1-3570	Delivery of Potable Water Systems (Sitework) on Site - ASD	0.0d		12-Jun-26	235.0d
2885	WBS - Storm Structures (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	81.0d
2886	PR-P1-1C1-3010	Prep Storm Structures (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	81.0d
2887	PR-P1-1C1-3050	Review & Submit Storm Structures (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	81.0d
2888	PR-P1-1C1-3040	Review & Approve Storm Structures (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	81.0d
2889	PR-P1-1C1-3060	Review & Approve Storm Structures (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	81.0d
2890	PR-P1-1C1-3020	Fab. & Ship Storm Structures (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	114.0d
2891	PR-P1-1C1-3030	Delivery of Storm Structures (Sitework) on Site - ASD	0.0d		12-Jun-26	114.0d
2892	WBS - Exterior Metal Framing - ASD		108.0d	13-Feb-26	16-Jul-26	108.0d
2893	PR-P2-1C1-880	Prep Exterior Metal Framing Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2894	PR-P2-1C1-885	Review & Submit Exterior Metal Framing Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2895	PR-P2-1C1-1380	Review & Approve Exterior Metal Framing Submittals (HNTB)- ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2896	PR-P2-1C1-1385	Review & Approve Exterior Metal Framing Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2897	PR-P2-1C1-1760	Fab. & Ship Exterior Metal Framing - ASD	60.0d	15-May-26	16-Jul-26	154.0d
2898	PR-P2-1C1-2190	Delivery of Exterior Metal Framing on Site - ASD	0.0d		16-Jul-26	154.0d

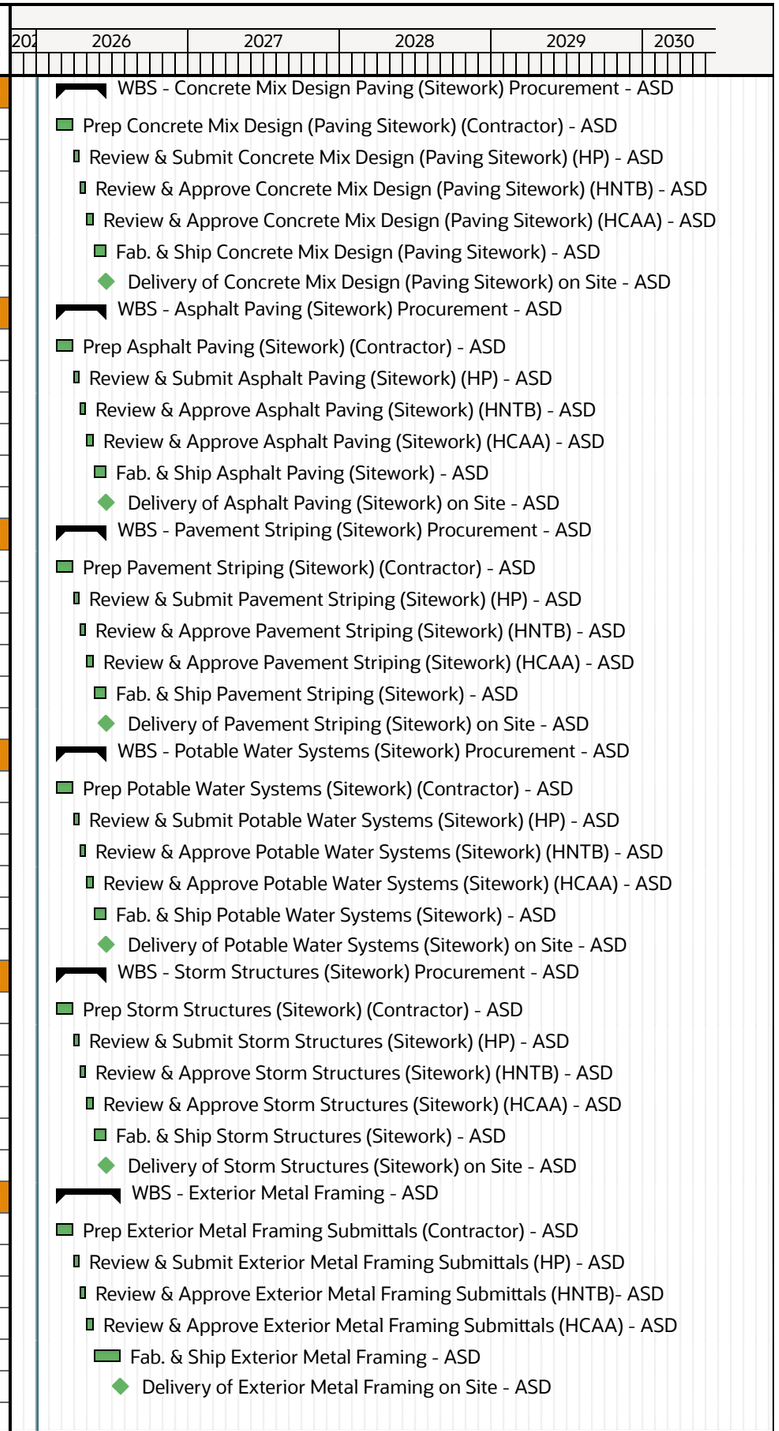


	ID	Name	Dur	Start	Finish	TF
2899	WBS - Structural Steel Dumpster Procurement - ASD		61.0d	13-Feb-26	8-May-26	173.0d
2900	PR-P2-1C1-870	Prep Struct. Steel Dumpster Submittals (Contractor) - ASD	15.0d	13-Feb-26	5-Mar-26	174.0d
2901	PR-P2-1C1-875	Review & Submit Struct. Steel Dumpster Submittals (HP) - ASD	10.0d	6-Mar-26	19-Mar-26	174.0d
2902	PR-P2-1C1-1370	Review & Approve Struct. Steel Dumpster Submittals (HNTB) - ASD	10.0d	20-Mar-26	2-Apr-26	174.0d
2903	PR-P2-1C1-1375	Review & Approve Struct. Steel Dumpster Submittals (HCAA) - ASD	15.0d	3-Apr-26	23-Apr-26	174.0d
2904	PR-P2-1C1-1750	Fab. & Ship Struct. Steel Dumpster (HCAA) - ASD	15.0d	24-Apr-26	8-May-26	246.0d
2905	PR-P2-1C1-2090	Delivery of Struct. Steel Dumpster - ASD	0.0d		8-May-26	246.0d
2906	WBS - Boilers Procurement - ASD		124.0d	13-Feb-26	9-Aug-26	425.0d
2907	PR-P2-1C1-90	Prep Boilers Submittals (Contractor) - Part 2 Supp. ASD	30.0d	13-Feb-26	26-Mar-26	424.0d
2908	PR-P2-1C1-95	Review & Submit Boilers Submittals (HP) - Part 2 Supp. ASD	10.0d	27-Mar-26	9-Apr-26	424.0d
2909	PR-P2-1C1-270	Review & Approve Boilers Submittals (HNTB) - Part 2 Supp. ASD	10.0d	10-Apr-26	23-Apr-26	424.0d
2910	PR-P2-1C1-275	Review & Approve Boilers Submittals (HCAA) - Part 2 Supp. ASD	15.0d	24-Apr-26	14-May-26	424.0d
2911	PR-P2-1C1-360	Fab. & Ship Boilers - Part 2 Supp. ASD	84.0d	15-May-26	9-Aug-26	595.0d
2912	PR-P2-1C1-2320	Delivery of Boilers on Site - Part 2 Supp. ASD	0.0d		9-Aug-26	595.0d
2913	WBS - HVAC System Procurement - ASD		88.0d	13-Feb-26	17-Jun-26	198.0d
2914	PR-P1-1C1-3670	Prep HVAC System Submittals (Contractor) - Part 2 Supp. A	30.0d	13-Feb-26	26-Mar-26	198.0d
2915	PR-P1-1C1-3710	Review & Submit HVAC System Submittals (HP) - Part 2 Supp. A	5.0d	27-Mar-26	2-Apr-26	198.0d
2916	PR-P1-1C1-3700	Review & Approve HVAC System Submittals (HNTB) - Part 2 Supp. A	10.0d	3-Apr-26	16-Apr-26	198.0d
2917	PR-P1-1C1-3720	Review & Approve HVAC System Submittals (HCAA) - Part 2 Supp. A	15.0d	17-Apr-26	7-May-26	198.0d
2918	PR-P1-1C1-3680	Fab. & Ship HVAC System - Part 2 Supp. A	40.0d	8-May-26	17-Jun-26	279.0d
2919	PR-P1-1C1-3690	Delivery of HVAC System on Site - Part 2 Supp. A	0.0d		17-Jun-26	279.0d
2920	WBS - Air Handling Unit Procurement - ASD		159.0d	13-Feb-26	28-Sep-26	246.0d
2921	PR-P1-1C1-50	Prep Air Handling Units Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	244.0d
2922	PR-P1-1C1-55	Review & Submit Air Handling Units Submittals (HP) - ASD	5.0d	27-Mar-26	2-Apr-26	244.0d
2923	PR-P1-1C1-230	Review & Approve Air Handling Units Submittals (HNTB) - ASD	10.0d	3-Apr-26	16-Apr-26	244.0d
2924	PR-P1-1C1-235	Review & Approve Air Handling Units Submittals (HCAA) - ASD	15.0d	17-Apr-26	7-May-26	244.0d
2925	PR-P1-1C1-330	Fab. & Ship Air Handling Units - ASD	140.0d	8-May-26	28-Sep-26	344.0d
2926	PR-P1-1C1-2300	Delivery of Air Handling Units on Site - ASD	0.0d		28-Sep-26	344.0d
2927	WBS - Materials & Equip for Cooling Tower Fans Procurement - ASD		224.0d	13-Feb-26	31-Dec-26	290.0d
2928	PR-P2-1C1-80	Prep Cooling Tower Fans Submittals (Contractor) - ASD	21.0d	13-Feb-26	13-Mar-26	290.0d
2929	PR-P2-1C1-85	Review & Submit Cooling Tower Fans Submittals (HP) - ASD	10.0d	16-Mar-26	27-Mar-26	290.0d
2930	PR-P2-1C1-260	Review & Approve Cooling Tower Fans Submittals (HNTB) - ASD	10.0d	30-Mar-26	10-Apr-26	290.0d
2931	PR-P2-1C1-265	Review & Approve Cooling Tower Fans Submittals (HCAA) - ASD	15.0d	13-Apr-26	1-May-26	290.0d
2932	PR-P2-1C1-350	Fab. Long Lead Items for Cooling Tower Fans - ASD	65.0d	4-May-26	4-Aug-26	290.0d
2933	PR-P2-1C1-355	Ship Materials & Equip. for Cooling Tower Fans - ASD	103.0d	5-Aug-26	31-Dec-26	290.0d
2934	PR-P2-1C1-2310	Delivery of Materials & Equip. for Cooling Tower Fans to Site on Site - ASD	0.0d		31-Dec-26	406.0d
2935	WBS - Natural Gas Equip. Procurement - ASD		108.0d	13-Feb-26	16-Jul-26	431.0d
2936	PR-P2-1C1-160	Prep Natural Gas Equip. Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	432.0d
2937	PR-P2-1C1-165	Review & Submit Natural Gas Equip. Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	432.0d
2938	PR-P2-1C1-310	Review & Approve Natural Gas Equip. Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	432.0d
2939	PR-P2-1C1-315	Review & Approve Natural Gas Equip. Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	432.0d
2940	PR-P2-1C1-410	Fab. & Ship Natural Gas Equip. - ASD	60.0d	15-May-26	16-Jul-26	605.0d

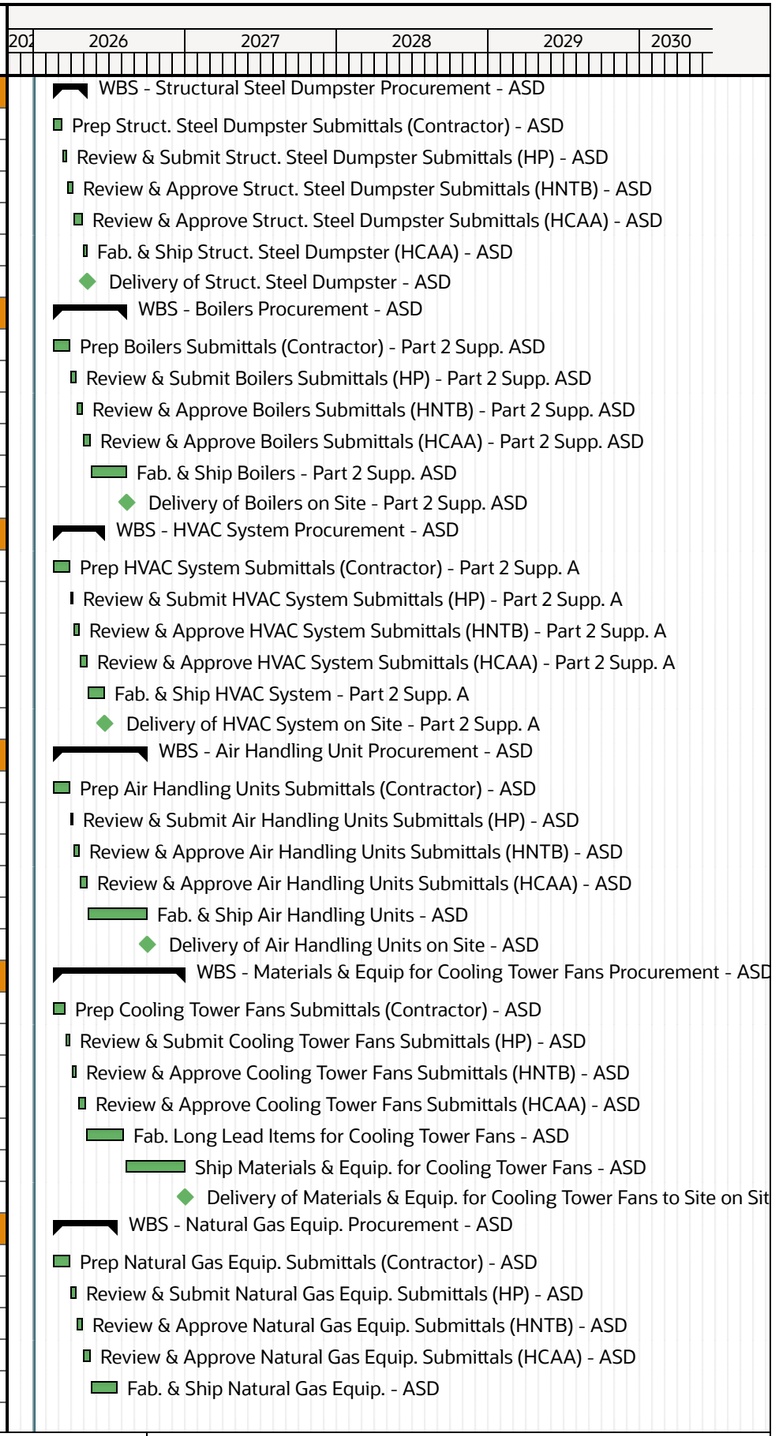


	ID	Name	Dur	Start	Finish	TF
2941	PR-P2-1C1-1000	Delivery of Natural Gas Equip. on Site - ASD	0.0d		16-Jul-26	605.0d
2942	WBS - Water Softening System Procurement - ASD		150.0d	13-Feb-26	15-Sep-26	389.0d
2943	PR-P2-1C1-170	Prep Water Softening System Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	388.0d
2944	PR-P2-1C1-175	Review & Submit Water Softening System Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	388.0d
2945	PR-P2-1C1-320	Review & Approve Water Softening System Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	388.0d
2946	PR-P2-1C1-325	Review & Approve Water Softening System Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	388.0d
2947	PR-P2-1C1-420	Fab. & Ship Water Softening System - ASD	120.0d	15-May-26	15-Sep-26	545.0d
2948	PR-P2-1C1-2000	Delivery of Water Softening System on Site - ASD	0.0d		15-Sep-26	545.0d
2949	WBS - Pumps Procurement - ASD		136.0d	13-Feb-26	25-Aug-26	398.0d
2950	PR-P2-1C1-110	Prep Pumps Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	397.0d
2951	PR-P2-1C1-115	Review & Submit Pumps Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	397.0d
2952	PR-P2-1C1-290	Review & Approve Pumps Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	397.0d
2953	PR-P2-1C1-295	Review & Approve Pumps Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	397.0d
2954	PR-P2-1C1-380	Fab. & Ship Pumps - ASD	100.0d	15-May-26	25-Aug-26	558.0d
2955	PR-P2-1C1-1910	Delivery of Pumps on Site - ASD	0.0d		25-Aug-26	558.0d
2956	WBS - Electrical & Site Electrical Procurement - ASD		93.0d	13-Feb-26	24-Jun-26	145.0d
2957	PR-P1-1C1-830	Prep Elec. & Site Elec. Submittals (Contractor)- ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2958	PR-P1-1C1-835	Review & Submit Elec. & Site Elec. Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2959	PR-P1-1C1-1330	Review & Approve Elec. & Site Elec. Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2960	PR-P1-1C1-1335	Review & Approve Elec. & Site Elec. Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2961	PR-P1-1C1-1710	Fab. & Ship Elec. & Site Elec. - ASD	40.0d	15-May-26	24-Jun-26	204.0d
2962	PR-P1-1C1-2060	Delivery of Elec. & Site Elec. on Site - ASD	0.0d		24-Jun-26	204.0d
2963	WBS - Special Exterior Lighting Procurement - ASD		150.0d	13-Feb-26	15-Sep-26	394.0d
2964	PR-P2-1C1-140	Prep Special Exterior LTNG Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	393.0d
2965	PR-P2-1C1-145	Review & Submit Special Exterior LTNG Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	393.0d
2966	PR-P2-1C1-150	Review & Approve Special Exterior LTNG Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	393.0d
2967	PR-P2-1C1-155	Review & Approve Special Exterior LTNG Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	393.0d
2968	PR-P2-1C1-190	Fab. & Ship Special Exterior LTNG - ASD	120.0d	15-May-26	15-Sep-26	552.0d
2969	PR-P2-1C1-1850	Delivery of Special Exterior LTNG on Site - ASD	0.0d		15-Sep-26	552.0d
2970	WBS - Lightning Protection Procurement - ASD		93.0d	13-Feb-26	24-Jun-26	451.0d
2971	PR-P2-1C1-130	Prep Lightning Protection Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2972	PR-P2-1C1-135	Review & Submit Lightning Protection Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2973	PR-P2-1C1-300	Review & Approve Lightning Protection Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2974	PR-P2-1C1-305	Review & Approve Lightning Protection Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2975	PR-P2-1C1-400	Fab. & Ship Lightning Protection - ASD	40.0d	15-May-26	24-Jun-26	632.0d
2976	PR-P2-1C1-510	Delivery of Lightning Protection on Site - ASD	0.0d		24-Jun-26	632.0d
2977	WBS - Low Voltage System Procurement - ASD		93.0d	13-Feb-26	24-Jun-26	239.0d
2978	PR-P1-1C1-840	Prep Low Voltage System Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
2979	PR-P1-1C1-845	Review & Submit Low Voltage System Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
2980	PR-P1-1C1-1340	Review & Approve Low Voltage System Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
2981	PR-P1-1C1-1345	Review & Approve Low Voltage System Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
2982	PR-P1-1C1-1720	Fab. & Ship Low Voltage System - ASD	40.0d	15-May-26	24-Jun-26	335.0d

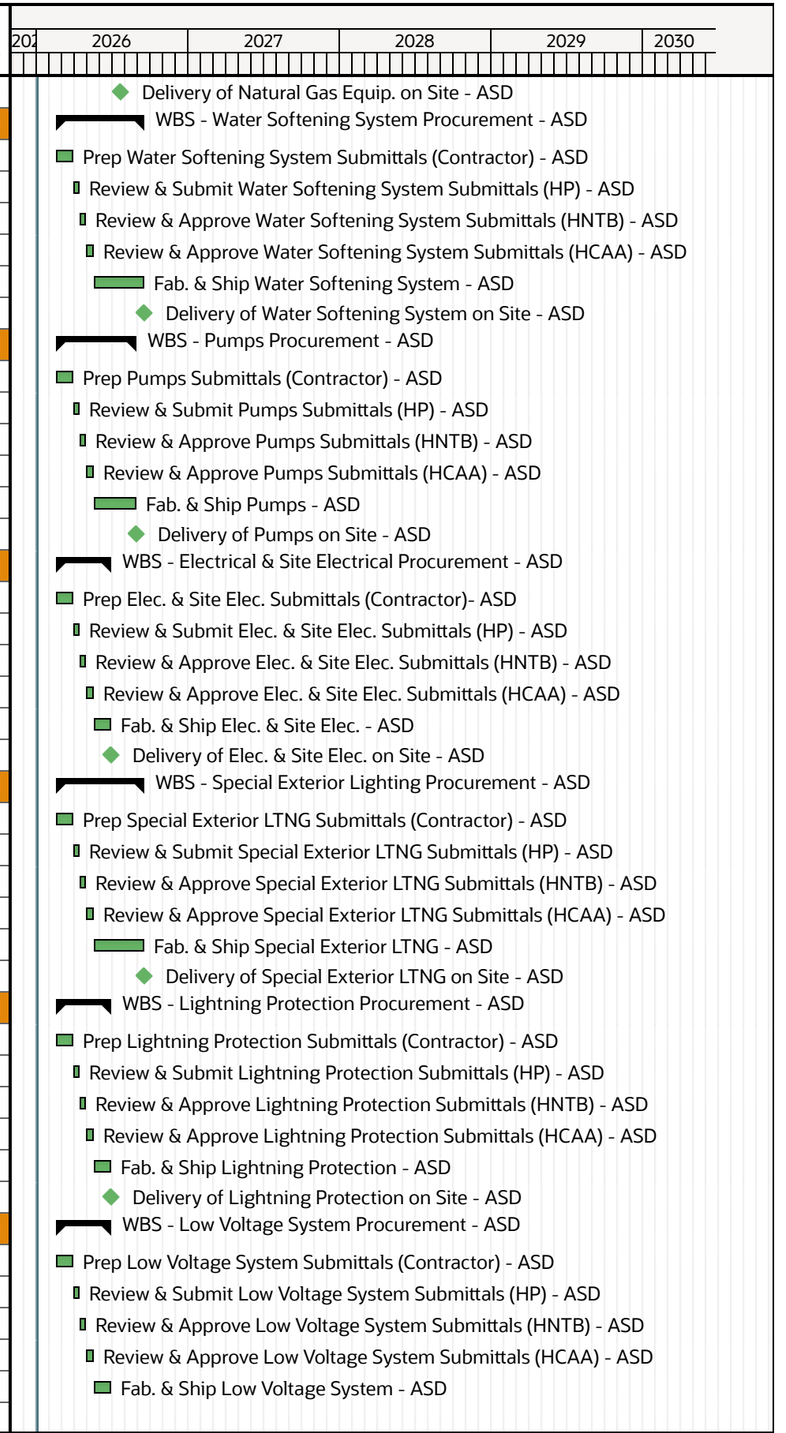


	ID	Name	Dur	Start	Finish	TF
2983	PR-P1-1C1-2070	Delivery of Low Voltage System on Site - ASD	0.0d		24-Jun-26	335.0d
2984	WBS - Terrazzo Floor Procurement - ASD		122.0d	13-Feb-26	5-Aug-26	385.0d
2985	PR-P2-1C1-680	Prep Terrazzo Floor Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
2986	PR-P2-1C1-685	Review & Submit Terrazzo Floor Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	386.0d
2987	PR-P2-1C1-1190	Review & Approve Terrazzo Floor Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	386.0d
2988	PR-P2-1C1-1195	Review & Approve Terrazzo Floor Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	386.0d
2989	PR-P2-1C1-1580	Fab. & Ship Terrazzo Floor Materials - ASD	80.0d	15-May-26	5-Aug-26	541.0d
2990	PR-P2-1C1-2250	Delivery of Terrazzo Floor Materials on Site - ASD	0.0d		5-Aug-26	541.0d
2991	WBS - Terrazzo Monumental Stair Treads Procurement - ASD		144.0d	13-Feb-26	6-Sep-26	387.0d
2992	PR-P2-1C1-440	Prep Terrazzo Monumental Stair Treads Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	386.0d
2993	PR-P2-1C1-445	Review & Submit Terrazzo Monumental Stair Treads Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	386.0d
2994	PR-P2-1C1-490	Review & Approve Terrazzo Monumental Stair Treads Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	386.0d
2995	PR-P2-1C1-495	Review & Approve Terrazzo Monumental Stair Treads Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	386.0d
2996	PR-P2-1C1-540	Fab. & Ship Terrazzo Monumental Stair Treads - ASD	112.0d	15-May-26	6-Sep-26	541.0d
2997	PR-P2-1C1-2040	Delivery of Terrazzo Monumental Stair Treads on Site - ASD	0.0d		6-Sep-26	541.0d
2998	WBS - Interior Handrail - ASD		82.0d	6-Feb-26	2-Jun-26	118.0d
2999	PR-P2-1C1-910	Prep Interior Handrail Submittals (Contractor) - ASD	30.0d	6-Feb-26	19-Mar-26	118.0d
3000	PR-P2-1C1-915	Review & Submit Interior Handrail Submittals (HP) - ASD	10.0d	20-Mar-26	2-Apr-26	118.0d
3001	PR-P2-1C1-990	Review & Approve Interior Handrail Submittals (HNTB) - ASD	10.0d	3-Apr-26	16-Apr-26	118.0d
3002	PR-P2-1C1-995	Review & Approve Interior Handrail Submittals (HCAA) - ASD	15.0d	17-Apr-26	7-May-26	118.0d
3003	PR-P2-1C1-1060	Fab. & Ship Interior Handrail (HNTB) - ASD	25.0d	8-May-26	2-Jun-26	165.0d
3004	PR-P2-1C1-1860	Delivery of Interior Handrail on Site - ASD	0.0d		2-Jun-26	165.0d
3005	WBS - Exterior Insulation - ASD		85.0d	13-Feb-26	14-Jun-26	161.0d
3006	PR-P2-1C1-890	Prep Exterior Insulation Submittals (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	91.0d
3007	PR-P2-1C1-895	Review & Submit Exterior Insulation Submittals (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	91.0d
3008	PR-P2-1C1-1390	Review & Approve Exterior Insulation Submittals (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	91.0d
3009	PR-P2-1C1-1395	Review & Approve Exterior Insulation Submittals (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	91.0d
3010	PR-P2-1C1-1770	Fab. & Ship Exterior Insulation - ASD	30.0d	15-May-26	14-Jun-26	226.0d
3011	PR-P2-1C1-1990	Delivery of Exterior Insulation on Site - ASD	0.0d		14-Jun-26	226.0d
3012	WBS - Expansion Joint Procurement - ASD		88.0d	13-Feb-26	17-Jun-26	289.0d
3013	PR-P2-1C1-960	Prep Expansion Joint Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	288.0d
3014	PR-P2-1C1-965	Review & Submit Expansion Joint Submittals (HP) - ASD	10.0d	20-Mar-26	2-Apr-26	288.0d
3015	PR-P2-1C1-1080	Review & Approve Expansion Joint Submittals (HNTB) - ASD	10.0d	3-Apr-26	16-Apr-26	288.0d
3016	PR-P2-1C1-1085	Review & Approve Expansion Joint Submittals (HCAA) - ASD	15.0d	17-Apr-26	7-May-26	288.0d
3017	PR-P2-1C1-1470	Fab. & Ship Expansion Joint - ASD	40.0d	8-May-26	17-Jun-26	406.0d
3018	PR-P2-1C1-2030	Delivery of Expansion Joint on Site - ASD	0.0d		17-Jun-26	406.0d
3019	WBS - Demolition Safety Plan Submittal - ASD		25.0d	13-Feb-26	19-Mar-26	61.0d
3020	PR-P2-1C1-7840	Submit Demolition Safety Plan (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	61.0d
3021	WBS - Ductwork/Mechanical Systems - ASD		80.0d	13-Feb-26	7-Jun-26	152.0d
3022	PR-P2-1C1-8280	Prep Ductwork/Mech. Systems Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	151.0d
3023	PR-P2-1C1-8290	Review & Submit Ductwork/Mech. Systems Submittals (HP) - ASD	10.0d	20-Mar-26	2-Apr-26	151.0d
3024	PR-P2-1C1-8300	Review & Approve Ductwork/Mech. Systems Submittals (HNTB) - ASD	10.0d	3-Apr-26	16-Apr-26	151.0d

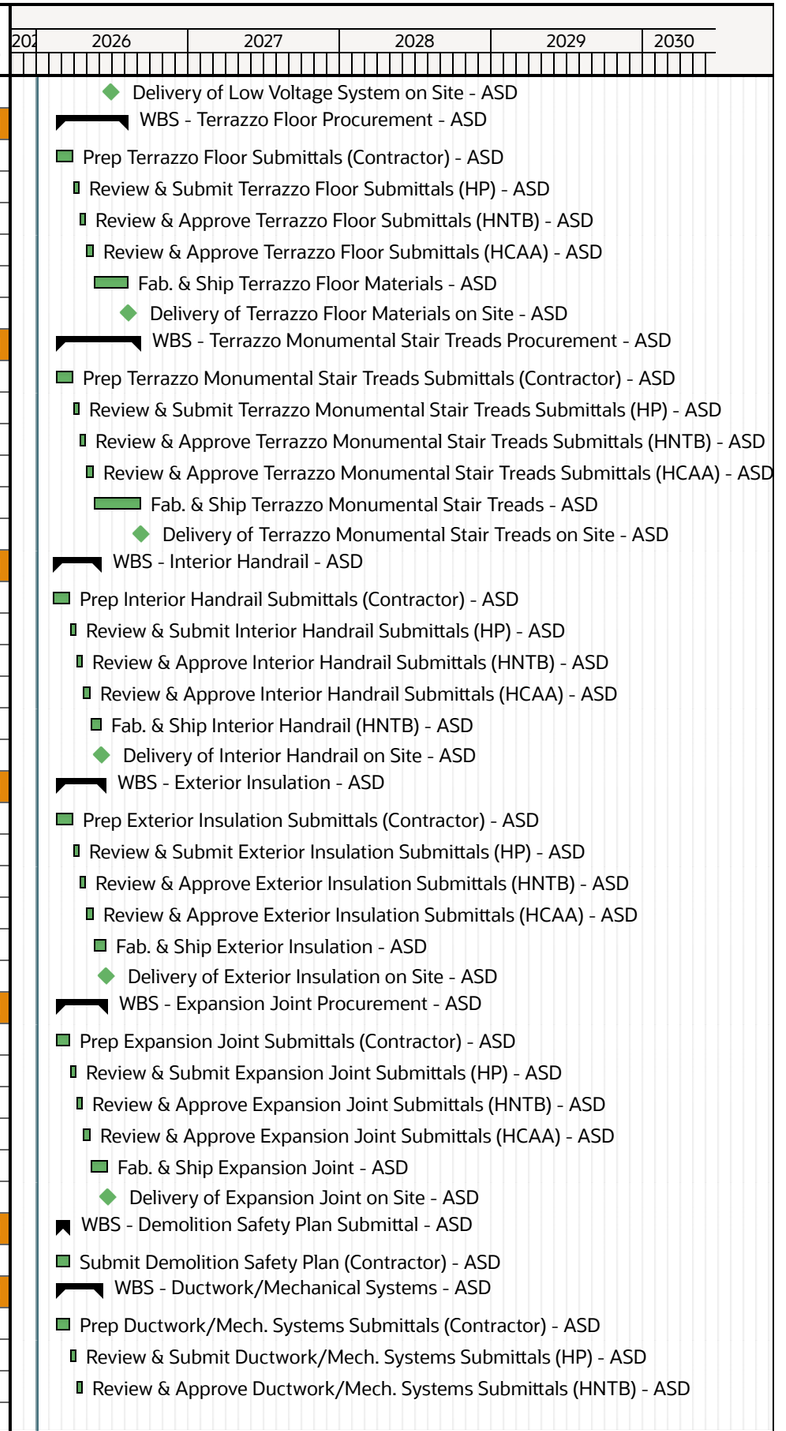


	ID	Name	Dur	Start	Finish	TF
3025	PR-P2-1C1-8310	Review & Approve Ductwork/Mech. Systems Submittals (HCAA) - ASD	15.0d	17-Apr-26	7-May-26	151.0d
3026	PR-P2-1C1-8320	Fab. & Ship Ductwork/Mech. Systems - ASD	30.0d	8-May-26	7-Jun-26	213.0d
3027	PR-P2-1C1-8330	Delivery of Ductwork/Mech. Systems on Site - ASD	0.0d		7-Jun-26	213.0d
3028	WBS - Plumbing Systems - ASD		88.0d	13-Feb-26	17-Jun-26	149.0d
3029	PR-P2-1C1-8400	Prep Plumbing Systems Submittals (Contractor) - ASD	25.0d	13-Feb-26	19-Mar-26	149.0d
3030	PR-P2-1C1-8410	Review & Submit Plumbing Systems Submittals (HP) - ASD	10.0d	20-Mar-26	2-Apr-26	149.0d
3031	PR-P2-1C1-8420	Review & Approve Plumbing Systems Submittals (HNTB) - ASD	10.0d	3-Apr-26	16-Apr-26	149.0d
3032	PR-P2-1C1-8430	Review & Approve Plumbing Systems Submittals (HCAA) - ASD	15.0d	17-Apr-26	7-May-26	149.0d
3033	PR-P2-1C1-8440	Fab. & Ship Plumbing Systems - ASD	40.0d	8-May-26	17-Jun-26	210.0d
3034	PR-P2-1C1-8450	Delivery of Plumbing Systems on Site - ASD	0.0d		17-Jun-26	210.0d
3035	WBS - Pedestrian Control Signage (Sitework) Procurement - ASD		85.0d	13-Feb-26	12-Jun-26	548.0d
3036	PR-P1-1C1-3610	Prep Pedestrian Control Signage (Sitework) (Contractor) - ASD	30.0d	13-Feb-26	26-Mar-26	548.0d
3037	PR-P1-1C1-3650	Review & Submit Pedestrian Control Signage (Sitework) (HP) - ASD	10.0d	27-Mar-26	9-Apr-26	548.0d
3038	PR-P1-1C1-3640	Review & Approve Pedestrian Control Signage (Sitework) (HNTB) - ASD	10.0d	10-Apr-26	23-Apr-26	548.0d
3039	PR-P1-1C1-3660	Review & Approve Pedestrian Control Signage (Sitework) (HCAA) - ASD	15.0d	24-Apr-26	14-May-26	548.0d
3040	PR-P1-1C1-3620	Fab. & Ship Pedestrian Control Signage (Sitework) - ASD	28.0d	15-May-26	12-Jun-26	769.0d
3041	PR-P1-1C1-3630	Delivery of Pedestrian Control Signage (Sitework) on Site - ASD	0.0d		12-Jun-26	769.0d
3042	WBS - Baggage Handling System Procurement - ASD		862.0d	20-Oct-25 A	13-Mar-29	261.0d
3043	WBS - General BHS Submittals & Procurement - ASD		862.0d	20-Oct-25 A	13-Mar-29	261.0d
3044	WBS - Site Specific Safety Plans Submittals - ASD		40.0d	20-Oct-25 A	16-Dec-25 A	
3045	A109210	Prep & Submit Site Specific Safety Plans - ASD	13.0d	20-Oct-25 A	5-Nov-25 A	
3046	A109220	Review & Approve (HP) Site Specific Safety Plans - ASD	2.0d	6-Nov-25 A	7-Nov-25 A	
3047	A109230	Review & Approve (HNTB) Site Specific Safety Plans - ASD	11.0d	10-Nov-25 A	24-Nov-25 A	
3048	A109240	Review & Approve (HCAA) Site Specific Safety Plans - ASD	14.0d	25-Nov-25 A	16-Dec-25 A	
3049	WBS - Quality Control Manual Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
3050	A109250	Prep & Submit Quality Control Manual - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
3051	A109260	Review & Approve (HP) Quality Control Manual - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
3052	A109270	Review & Approve (HNTB) Quality Control Manual - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
3053	A109280	Review & Approve (HCAA) Quality Control Manual - ASD	15.0d	21-Jan-26	10-Feb-26	263.0d
3054	WBS - Environmental Requirements Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	1,045.0d
3055	A109310	Prep & Submit Environmental Requirements - ASD	48.0d	20-Oct-25 A	29-Dec-25	1,044.0d
3056	A109340	Review & Approve (HP) Environmental Requirements - ASD	5.0d	30-Dec-25	6-Jan-26	1,044.0d
3057	A109380	Review & Approve (HNTB) Environmental Requirements - ASD	10.0d	7-Jan-26	20-Jan-26	1,044.0d
3058	A109390	Review & Approve (HCAA) Environmental Requirements - ASD	15.0d	21-Jan-26	10-Feb-26	1,044.0d
3059	WBS - Project Organizational Chart & Management Team Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
3060	A109300	Prep & Submit Project Organizational Chart & Management Team - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
3061	A109320	Review & Approve (HP) Project Organizational Chart & Management Team - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d
3062	A109400	Review & Approve (HNTB) Project Organizational Chart & Management Team - ...	10.0d	7-Jan-26	20-Jan-26	263.0d
3063	A109410	Review & Approve (HCAA) Project Organizational Chart & Management Team - ...	15.0d	21-Jan-26	10-Feb-26	263.0d
3064	WBS - Detailed Master Schedule Submittals - ASD		78.0d	20-Oct-25 A	10-Feb-26	263.0d
3065	A109290	Prep & Submit Detailed Master Schedule - ASD	48.0d	20-Oct-25 A	29-Dec-25	263.0d
3066	A109330	Review & Approve (HP) Detailed Master Schedule - ASD	5.0d	30-Dec-25	6-Jan-26	263.0d

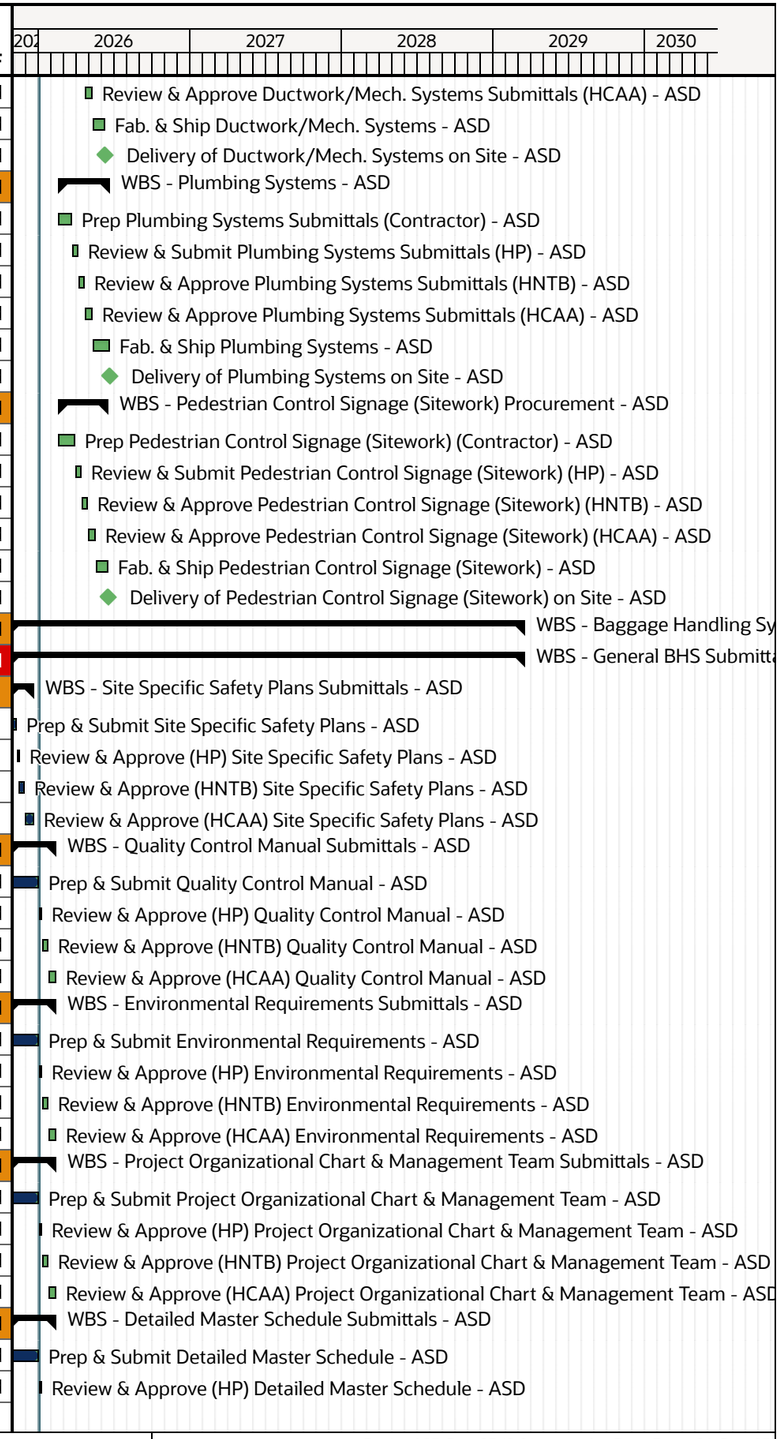


	ID	Name	Dur	Start	Finish	TF
3067	A109420	Review & Approve (HNTB) Detailed Master Schedule - ASD	10.0d	7-Jan-26	20-Jan-26	263.0d
3068	A109430	Review & Approve (HCAA) Detailed Master Schedule - ASD	15.0d	21-Jan-26	10-Feb-26	263.0d
3069	WBS - O&M Manual Submittals - ASD		86.0d	18-Nov-25 A	23-Mar-26	653.0d
3070	A109350	Prep & Submit O&M Manual - Draft - ASD	31.0d	18-Nov-25 A	5-Jan-26	653.0d
3071	A109440	Review & Approve (HP) O&M Manual - Draft - ASD	5.0d	6-Jan-26	12-Jan-26	653.0d
3072	A109450	Review & Approve (HNTB) O&M Manual - Draft - ASD	10.0d	13-Jan-26	26-Jan-26	653.0d
3073	A109360	Review & Approve (HCAA) O&M Manual - Draft - ASD	15.0d	27-Jan-26	16-Feb-26	653.0d
3074	A109370	Submit O&M Manual - Final - ASD	25.0d	17-Feb-26	23-Mar-26	653.0d
3075	WBS - Baggage Tag Verification Report Submittals - ASD		40.0d	13-Feb-26	9-Apr-26	906.0d
3076	D2916	Prep & Submit Baggage Tag Verification Report - ASD	10.0d	13-Feb-26	26-Feb-26	905.0d
3077	A109460	Review & Approve (HP) Baggage Tag Verification Report - ASD	5.0d	27-Feb-26	5-Mar-26	905.0d
3078	A109470	Review & Approve (HNTB) Baggage Tag Verification Report - ASD	10.0d	6-Mar-26	19-Mar-26	905.0d
3079	D2926	Review & Approve (HCAA) Baggage Tag Verification Report - ASD	15.0d	20-Mar-26	9-Apr-26	905.0d
3080	WBS - List of Lubricants Submittals - ASD		60.0d	7-Sep-28	1-Dec-28	53.0d
3081	D2936	Prep & Submit List of Lubricants - ASD	30.0d	7-Sep-28	18-Oct-28	53.0d
3082	A109480	Review & Approve (HP) List of Lubricants - ASD	5.0d	19-Oct-28	25-Oct-28	53.0d
3083	A109490	Review & Approve (HNTB) List of Lubricants - ASD	10.0d	26-Oct-28	8-Nov-28	53.0d
3084	D2946	Review & Approve (HCAA) List of Lubricants - ASD	15.0d	9-Nov-28	1-Dec-28	53.0d
3085	WBS - Periodic Maintenance Inspection & Lubrication Chart - ASD		90.0d	13-Feb-26	19-Jun-26	590.0d
3086	D2976	Prep & Submit Periodic Maintenance Inspection & Lubrication Chart - ASD	60.0d	13-Feb-26	7-May-26	590.0d
3087	D3006	Review & Approve (HP) Periodic Maintenance Inspection & Lubrication Chart - ...	5.0d	8-May-26	14-May-26	590.0d
3088	D2996	Review & Approve (HNTB) Periodic Maintenance Inspection & Lubrication Char...	10.0d	15-May-26	29-May-26	590.0d
3089	D2986	Review & Approve (HCAA) Periodic Maintenance Inspection & Lubrication Char...	15.0d	1-Jun-26	19-Jun-26	590.0d
3090	WBS - Configuration Management Plan Submittals - ASD		60.0d	13-Feb-26	7-May-26	886.0d
3091	A109500	Prep & Submit Configuration Management Plan - ASD	30.0d	13-Feb-26	26-Mar-26	885.0d
3092	A109510	Review & Approve (HP) Configuration Management Plan - ASD	5.0d	27-Mar-26	2-Apr-26	885.0d
3093	A109520	Review & Approve (HNTB) Configuration Management Plan - ASD	10.0d	3-Apr-26	16-Apr-26	885.0d
3094	A109530	Review & Approve (HCAA) Configuration Management Plan - ASD	15.0d	17-Apr-26	7-May-26	885.0d
3095	WBS - BHS Equipment Combined Heat Output Figures Submittals - ASD		120.0d	13-Feb-26	3-Aug-26	281.0d
3096	A109540	Prep & Submit BHS Equip. Combined Heat Output Figures - ASD	90.0d	13-Feb-26	19-Jun-26	281.0d
3097	A109550	Review & Approve (HP) BHS Equip. Combined Heat Output Figures - ASD	5.0d	22-Jun-26	26-Jun-26	281.0d
3098	A109560	Review & Approve (HNTB) BHS Equip. Combined Heat Output Figures - ASD	10.0d	29-Jun-26	13-Jul-26	281.0d
3099	A109570	Review & Approve (HCAA) BHS Equip. Combined Heat Output Figures - ASD	15.0d	14-Jul-26	3-Aug-26	281.0d
3100	WBS - System Inspection, Functional Specification, and Test Plan Submittals - ASD		60.0d	10-Jun-26	2-Sep-26	535.0d
3101	D3016	Prep & Submit System Inspection, Functional Specification, & Test Plan - ASD	30.0d	10-Jun-26	22-Jul-26	535.0d
3102	A109580	Review & Approve (HP) System Inspection, Functional Specification, & Test Pla...	5.0d	23-Jul-26	29-Jul-26	535.0d
3103	A109590	Review & Approve (HNTB) System Inspection, Functional Specification, & Test ...	10.0d	30-Jul-26	12-Aug-26	535.0d
3104	D3026	Review & Approve (HCAA) System Inspection, Functional Specification, & Test ...	15.0d	13-Aug-26	2-Sep-26	535.0d
3105	WBS - Estimated Parts List - ASD		60.0d	7-Sep-28	1-Dec-28	53.0d
3106	D3056	Prep & Submit Estimated Parts List - ASD	30.0d	7-Sep-28	18-Oct-28	53.0d
3107	D3076	Review & Approve (HP) Estimated Parts List - ASD	5.0d	19-Oct-28	25-Oct-28	53.0d
3108	D3086	Review & Approve (HNTB) Estimated Parts List - ASD	10.0d	26-Oct-28	8-Nov-28	53.0d

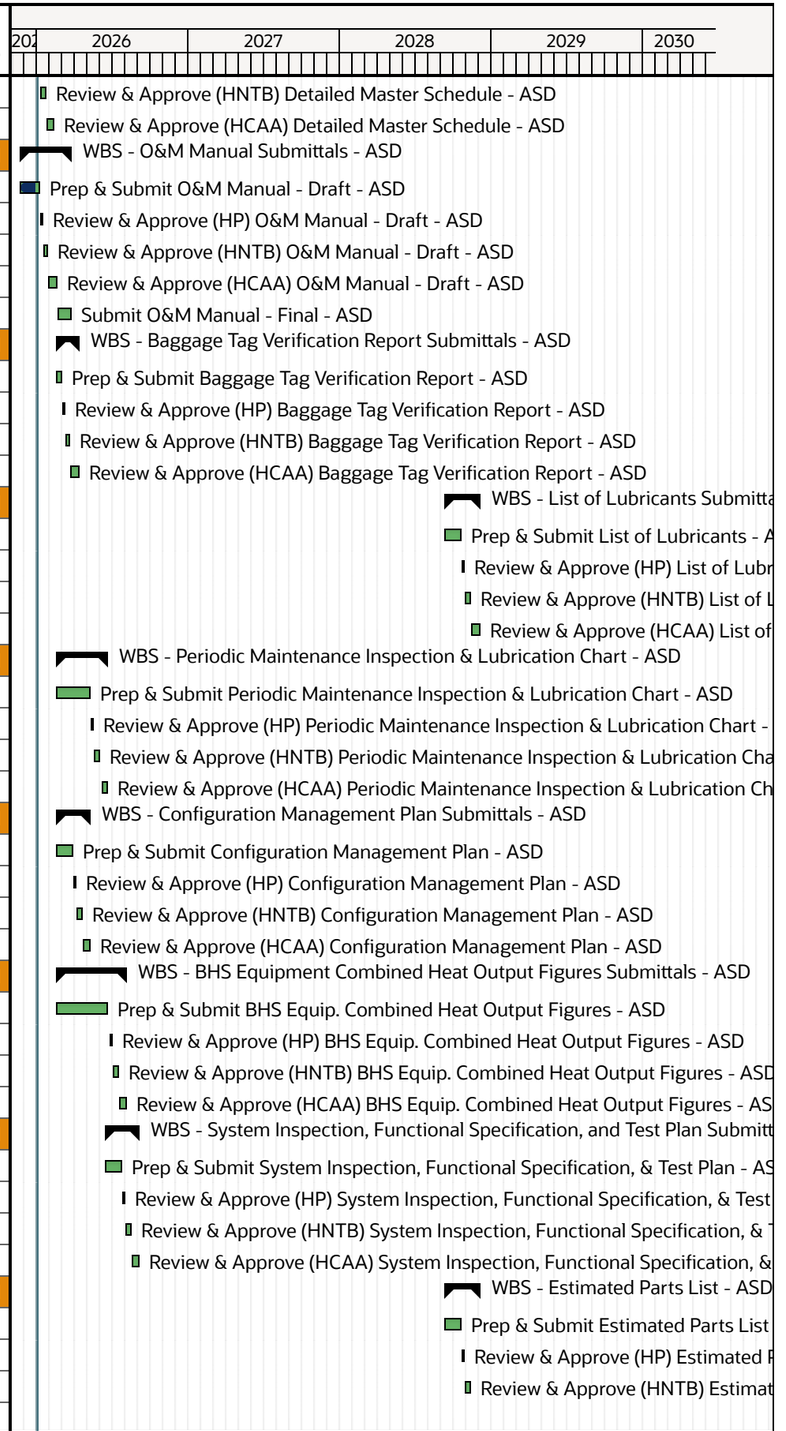


	ID	Name	Dur	Start	Finish	TF
3109	D3066	Review & Approve (HCAA) Estimated Parts List - ASD	15.0d	9-Nov-28	1-Dec-28	53.0d
3110	WBS - O&M Training Plan & Proposed Agenda Submittals		45.0d	13-Feb-26	16-Apr-26	632.0d
3111	D3096	Prep & Submit O&M Training Plan & Proposed Agenda	15.0d	13-Feb-26	5-Mar-26	632.0d
3112	A109600	Review & Approve (HP) O&M Training Plan & Proposed Agenda	5.0d	6-Mar-26	12-Mar-26	632.0d
3113	A109610	Review & Approve (HNTB) O&M Training Plan & Proposed Agenda	10.0d	13-Mar-26	26-Mar-26	632.0d
3114	D3106	Review & Approve (HCAA) O&M Training Plan & Proposed Agenda	15.0d	27-Mar-26	16-Apr-26	632.0d
3115	WBS - Final Parts List		60.0d	7-Sep-28	1-Dec-28	331.0d
3116	D3136	Prep & Submit Final Parts List	30.0d	7-Sep-28	18-Oct-28	330.0d
3117	D3156	Review & Approve (HP) Final Parts List	5.0d	19-Oct-28	25-Oct-28	330.0d
3118	D3166	Review & Approve (HNTB) Final Parts List	10.0d	26-Oct-28	8-Nov-28	330.0d
3119	D3146	Review & Approve (HCAA) Final Parts List	15.0d	9-Nov-28	1-Dec-28	330.0d
3120	WBS - Computer/Software/Hardware Inventory		45.0d	7-Sep-28	8-Nov-28	346.0d
3121	D3196	Prep & Submit Computer/Software/Hardware Inventory	15.0d	7-Sep-28	27-Sep-28	345.0d
3122	D3216	Review & Approve (HP) Computer/Software/Hardware Inventory	5.0d	28-Sep-28	4-Oct-28	345.0d
3123	D3226	Review & Approve (HNTB) Computer/Software/Hardware Inventory	10.0d	5-Oct-28	18-Oct-28	345.0d
3124	D3206	Review & Approve (HCAA) Computer/Software/Hardware Inventory	15.0d	19-Oct-28	8-Nov-28	345.0d
3125	WBS - Computer Log Submittals		45.0d	11-Dec-28	13-Feb-29	281.0d
3126	D3236	Prep & Submit Computer Log	15.0d	11-Dec-28	2-Jan-29	280.0d
3127	A109620	Review & Approve (HP) Computer Log	5.0d	3-Jan-29	9-Jan-29	280.0d
3128	A109630	Review & Approve (HNTB) Computer Log	10.0d	10-Jan-29	23-Jan-29	280.0d
3129	D3246	Review & Approve (HCAA) Computer Log	15.0d	24-Jan-29	13-Feb-29	280.0d
3130	WBS - Operational Run-In and Closeout Data Documentation		45.0d	10-Jan-29	13-Mar-29	261.0d
3131	D3276	Prep & Submit Operational Run-in & Closeout Data Documentation	15.0d	10-Jan-29	30-Jan-29	260.0d
3132	D3296	Review & Approve (HP) Operational Run-in & Closeout Data Documentation	5.0d	31-Jan-29	6-Feb-29	260.0d
3133	D3306	Review & Approve (HNTB) Operational Run-in & Closeout Data Documentation	10.0d	7-Feb-29	20-Feb-29	260.0d
3134	D3286	Review & Approve (HCAA) Operational Run-in & Closeout Data Documentation	15.0d	21-Feb-29	13-Mar-29	260.0d
3135	WBS - Certificate of Installation Compliance		45.0d	7-Sep-28	8-Nov-28	346.0d
3136	D3336	Prep & Submit Certificate of Install Compliance	15.0d	7-Sep-28	27-Sep-28	345.0d
3137	D3356	Review & Approve (HP) Certificate of Install Compliance	5.0d	28-Sep-28	4-Oct-28	345.0d
3138	D3366	Review & Approve (HNTB) Certificate of Install Compliance	10.0d	5-Oct-28	18-Oct-28	345.0d
3139	D3346	Review & Approve (HCAA) Certificate of Install Compliance	15.0d	19-Oct-28	8-Nov-28	345.0d
3140	WBS - Certificate of Testing Compliance		30.0d	11-Jan-29	21-Feb-29	275.0d
3141	D3396	Prep & Submit Certificate of Testing Compliance	5.0d	11-Jan-29	17-Jan-29	274.0d
3142	D3416	Review & Approve (HP) Certificate of Testing Compliance	5.0d	18-Jan-29	24-Jan-29	274.0d
3143	D3426	Review & Approve (HNTB) Certificate of Testing Compliance	5.0d	25-Jan-29	31-Jan-29	274.0d
3144	D3406	Review & Approve (HCAA) Certificate of Testing Compliance	15.0d	1-Feb-29	21-Feb-29	274.0d
3145	WBS - Mechanical BHS Submittals & Procurement - ASD		710.0d	3-Feb-26	15-Nov-28	341.0d
3146	WBS - General Mechanical BHS Submittals & Procurement - ASD		710.0d	3-Feb-26	15-Nov-28	341.0d
3147	WBS - Sector M - General Mechanical BHS Submittals & Procurement - ASD		190.0d	13-Feb-26	10-Nov-26	853.0d
3148	WBS - Mechanical Submittals - Sector M		50.0d	13-Feb-26	23-Apr-26	362.0d
3149	D1495	Prep & Submit Mech. Plan & Elev Dwg Set - Sector M	20.0d	13-Feb-26	12-Mar-26	362.0d
3150	D5476	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector M	5.0d	13-Mar-26	19-Mar-26	362.0d

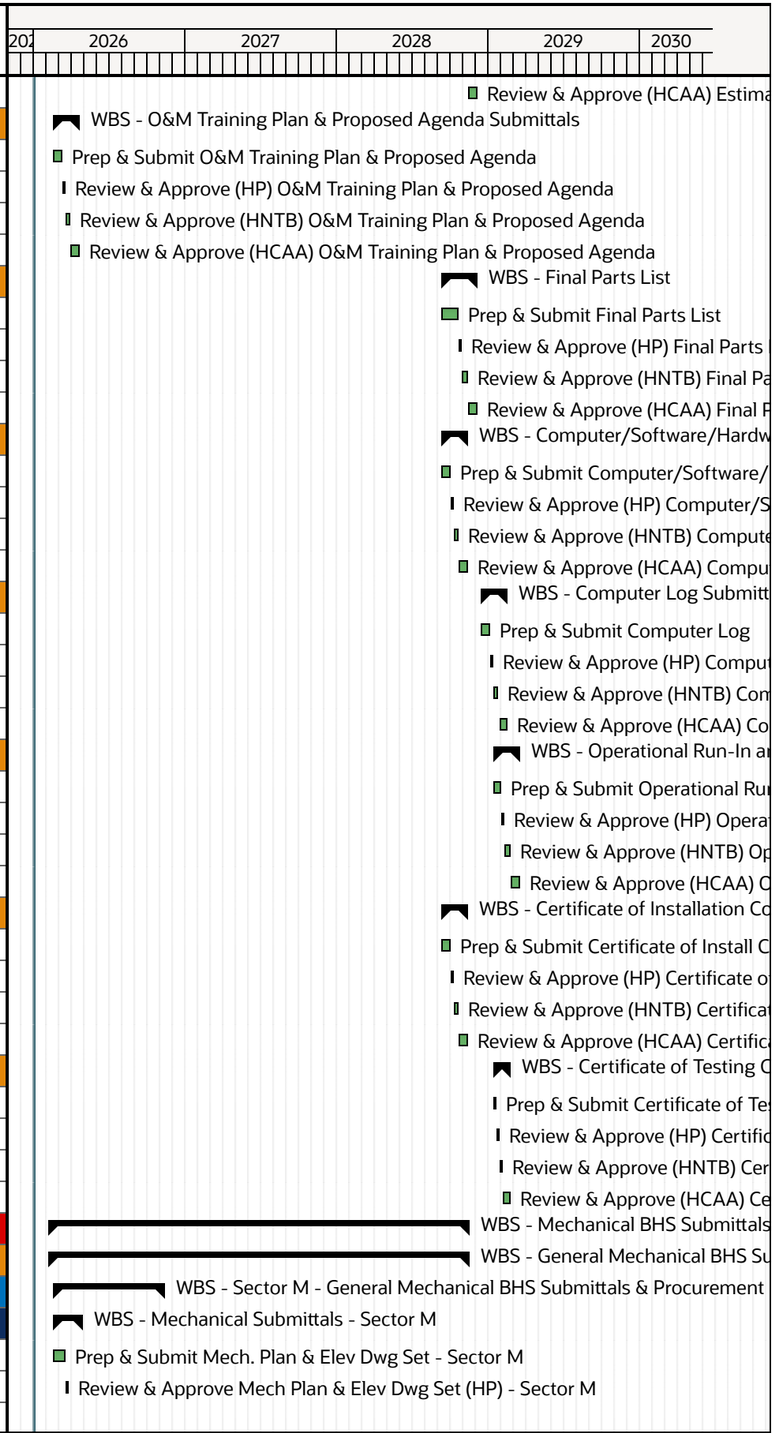


	ID	Name	Dur	Start	Finish	TF
3151	D5486	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector M	10.0d	20-Mar-26	2-Apr-26	362.0d
3152	D1496	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector M	15.0d	3-Apr-26	23-Apr-26	362.0d
3153	WBS - Mechanical Fabrication - Sector M		140.0d	24-Apr-26	10-Nov-26	853.0d
3154	D1497	Fab. & Deliver Conveyor TD1 34/36 - Sector M	120.0d	24-Apr-26	13-Oct-26	362.0d
3155	D1498	Fab. & Deliver Conveyor TD2 32/34 - Sector M	120.0d	24-Apr-26	13-Oct-26	432.0d
3156	D1499	Prep TD1 34/36 Matl for Install - Sector M	20.0d	14-Oct-26	10-Nov-26	852.0d
3157	D1500	Prep TD2 32/34 Matl for Install - Sector M	20.0d	14-Oct-26	10-Nov-26	432.0d
3158	WBS - Sector L		195.0d	13-Feb-26	17-Nov-26	848.0d
3159	WBS - Mechanical Submittals - Sector L		50.0d	13-Feb-26	23-Apr-26	367.0d
3160	D1501	Prep & Submit Mech. Plan & Elev Dwg Set - Sector L	20.0d	13-Feb-26	12-Mar-26	367.0d
3161	D5496	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector L	5.0d	13-Mar-26	19-Mar-26	367.0d
3162	D5506	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector L	10.0d	20-Mar-26	2-Apr-26	367.0d
3163	D1502	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector L	15.0d	3-Apr-26	23-Apr-26	367.0d
3164	WBS - Mechanical Fabrication - Sector L		140.0d	1-May-26	17-Nov-26	848.0d
3165	D1503	Fab. & Deliver Conveyor TD1 37/41 - Sector L	120.0d	1-May-26	20-Oct-26	362.0d
3166	D1504	Fab. & Deliver Conveyor TD2 35/39 - Sector L	120.0d	1-May-26	20-Oct-26	362.0d
3167	D1505	Prep TD1 37/41 Matl for Install - Sector L	20.0d	21-Oct-26	17-Nov-26	847.0d
3168	D1506	Prep TD2 35/39 Matl for Install - Sector L	20.0d	21-Oct-26	17-Nov-26	407.0d
3169	WBS - Sector K		200.0d	13-Feb-26	24-Nov-26	383.0d
3170	WBS - Mechanical Submittals - Sector K		50.0d	13-Feb-26	23-Apr-26	372.0d
3171	D1507	Prep & Submit Mech. Plan & Elev Dwg Set - Sector K	20.0d	13-Feb-26	12-Mar-26	0.0d
3172	D5516	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector K	5.0d	13-Mar-26	19-Mar-26	372.0d
3173	D5526	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector K	10.0d	20-Mar-26	2-Apr-26	372.0d
3174	D1508	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector K	15.0d	3-Apr-26	23-Apr-26	372.0d
3175	WBS - Mechanical Fabrication - Sector K		140.0d	8-May-26	24-Nov-26	383.0d
3176	D1509	Fab. & Deliver Conveyor TD1 42/47 - Sector K	120.0d	8-May-26	27-Oct-26	383.0d
3177	D1510	Fab. & Deliver Conveyor TD2 40/45 - Sector K	120.0d	8-May-26	27-Oct-26	362.0d
3178	D1511	Prep Mech. Matl for Install - Sector K	20.0d	28-Oct-26	24-Nov-26	383.0d
3179	WBS - Sector J - Apron 2		199.0d	13-Mar-26	23-Dec-26	442.0d
3180	WBS - Mechanical Submittals - Sector J		95.0d	13-Mar-26	27-Jul-26	66.0d
3181	D1512	Prep & Submit Mech. Plan & Elev Dwg Set - Sector J	20.0d	13-Mar-26	9-Apr-26	0.0d
3182	D5536	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector J	5.0d	10-Apr-26	16-Apr-26	66.0d
3183	D5546	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector J	10.0d	17-Apr-26	30-Apr-26	66.0d
3184	D1513	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector J	15.0d	1-May-26	21-May-26	66.0d
3185	D1515	Prep & Submit Header Steel Dwg Set - Sector J	15.0d	22-May-26	12-Jun-26	66.0d
3186	D5556	Review & Approve Header Steel Dwg Set (HP) - Sector J	5.0d	15-Jun-26	19-Jun-26	66.0d
3187	D5566	Review & Approve Header Steel Dwg Set (HNTB) - Sector J	10.0d	22-Jun-26	6-Jul-26	66.0d
3188	D1518	Review & Approve Header Steel Dwg Set (HCAA) - Sector J	15.0d	7-Jul-26	27-Jul-26	66.0d
3189	WBS - Mechanical Fabrication - Sector J		149.0d	22-May-26	23-Dec-26	442.0d
3190	D1514	Fab. & Deliver Conveyor TD1 48/57 - Sector J	120.0d	22-May-26	10-Nov-26	357.0d
3191	D1516	Fab. & Deliver Conveyor TD2 46/54 - Sector J	120.0d	1-Jun-26	17-Nov-26	385.0d
3192	D1517	Fab. & Deliver Conveyor RID1 11/16 - Sector J	120.0d	8-Jun-26	24-Nov-26	442.0d

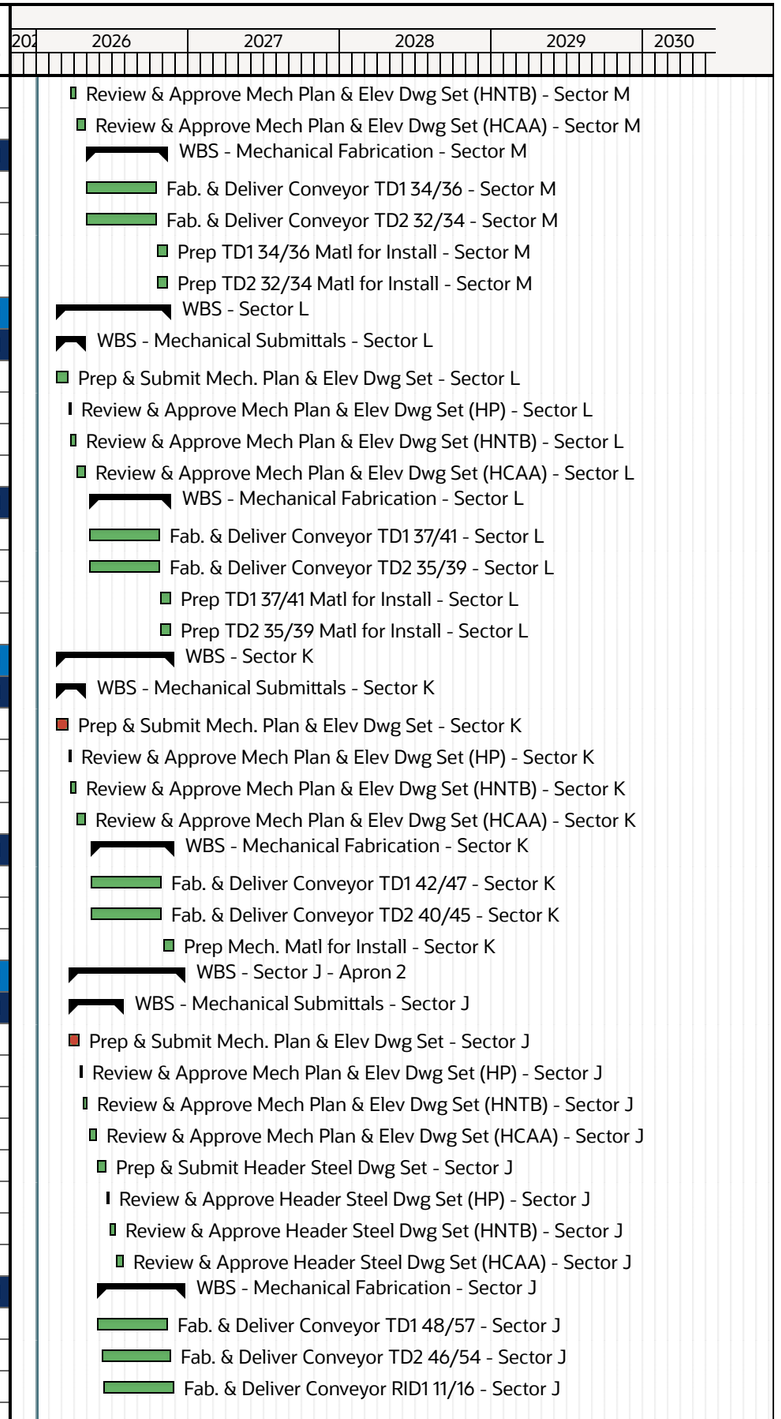


	ID	Name	Dur	Start	Finish	TF
3193	D1519	Fab. & Deliver Header Steel / Platform / Sills - Sector J	80.0d	28-Jul-26	17-Nov-26	66.0d
3194	D1520	Prep TD1 48/57 Matl for Install - Sector J	20.0d	11-Nov-26	10-Dec-26	357.0d
3195	D1521	Prep TD2 46/54 Matl for Install - Sector J	20.0d	18-Nov-26	17-Dec-26	385.0d
3196	D1522	Prep RID1 11/16 Matl for Install - Sector J	19.0d	25-Nov-26	23-Dec-26	442.0d
3197	WBS - Sector F - Apron 4		252.0d	3-Feb-26	29-Jan-27	420.0d
3198	WBS - Mechanical Submittals - Sector F		115.0d	10-Apr-26	22-Sep-26	45.0d
3199	D1531	Prep & Submit Mech. Plan & Elev Dwg Set - Sector F	35.0d	10-Apr-26	29-May-26	0.0d
3200	D5576	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector F	5.0d	1-Jun-26	5-Jun-26	45.0d
3201	D5586	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector F	10.0d	8-Jun-26	19-Jun-26	45.0d
3202	D1532	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector F	15.0d	22-Jun-26	13-Jul-26	45.0d
3203	D1535	Prep & Submit Header Steel Dwg Set - Sector F	20.0d	14-Jul-26	10-Aug-26	45.0d
3204	D5596	Review & Approve Header Steel Dwg Set (HP) - Sector F	5.0d	11-Aug-26	17-Aug-26	45.0d
3205	D5606	Review & Approve Header Steel Dwg Set (HNTB) - Sector F	10.0d	18-Aug-26	31-Aug-26	45.0d
3206	D1548	Review & Approve Header Steel Dwg Set (HCAA) - Sector F	15.0d	1-Sep-26	22-Sep-26	45.0d
3207	WBS - Mechanical Fabrication - Sector F		252.0d	3-Feb-26	29-Jan-27	420.0d
3208	D1523	Fab. & Deliver HSD MED1 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3209	D1524	Fab. & Deliver HSD MED2 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3210	D1525	Fab. & Deliver HSD MFD1A 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3211	D1526	Fab. & Deliver HSD MFD1B 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3212	D1527	Fab. & Deliver HSD MFD2A 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3213	D1528	Fab. & Deliver HSD MFD2B 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3214	D1529	Fab. & Deliver HSD MFD3A 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3215	D1530	Fab. & Deliver HSD MFD3B 1 - Sector F	140.0d	3-Feb-26	19-Aug-26	419.0d
3216	D1533	Fab. & Deliver Conveyor TD1 58/68 - Sector F	119.0d	14-Jul-26	31-Dec-26	327.0d
3217	D1534	Fab. & Deliver Conveyor MFD2A 01/04 - Sector F	119.0d	14-Jul-26	31-Dec-26	368.0d
3218	D1536	Fab. & Deliver Conveyor TD2 55/63 - Sector F	119.0d	14-Jul-26	31-Dec-26	360.0d
3219	D1537	Fab. & Deliver Conveyor MFD2B 01/05 - Sector F	119.0d	14-Jul-26	31-Dec-26	371.0d
3220	D1538	Fab. & Deliver Conveyor RID1 07/10 - Sector F	119.0d	14-Jul-26	31-Dec-26	402.0d
3221	D1539	Fab. & Deliver Conveyor MUD2 - Sector F	119.0d	14-Jul-26	31-Dec-26	379.0d
3222	D1540	Fab. & Deliver Conveyor MED1 01/12 - Sector F	119.0d	14-Jul-26	31-Dec-26	410.0d
3223	D1541	Fab. & Deliver Conveyor MFD3A 01/05 - Sector F	119.0d	14-Jul-26	31-Dec-26	391.0d
3224	D1542	Fab. & Deliver Conveyor MED2 01/12 - Sector F	119.0d	14-Jul-26	31-Dec-26	410.0d
3225	D1543	Fab. & Deliver Conveyor MFD3B 01/05 - Sector F	119.0d	14-Jul-26	31-Dec-26	400.0d
3226	D1544	Fab. & Deliver Conveyor MFD1A 01/09 - Sector F	119.0d	14-Jul-26	31-Dec-26	346.0d
3227	D1545	Fab. & Deliver Conveyor MUD3 - Sector F	119.0d	14-Jul-26	31-Dec-26	403.0d
3228	D1546	Fab. & Deliver Conveyor MFD1B 01/05 - Sector F	119.0d	14-Jul-26	31-Dec-26	420.0d
3229	D1547	Fab. & Deliver Conveyor MUD1 - Sector F	119.0d	14-Jul-26	31-Dec-26	358.0d
3230	D1549	Fab. & Deliver Header Steel / Platform / Sills - Sector F	79.0d	23-Sep-26	15-Jan-27	45.0d
3231	D1550	Prep TD1 58/68 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	327.0d
3232	D1551	Prep MFD2A 01/04 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	368.0d
3233	D1552	Prep TD2 55/63 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	360.0d
3234	D1553	Prep MFD3A 01/05 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	391.0d

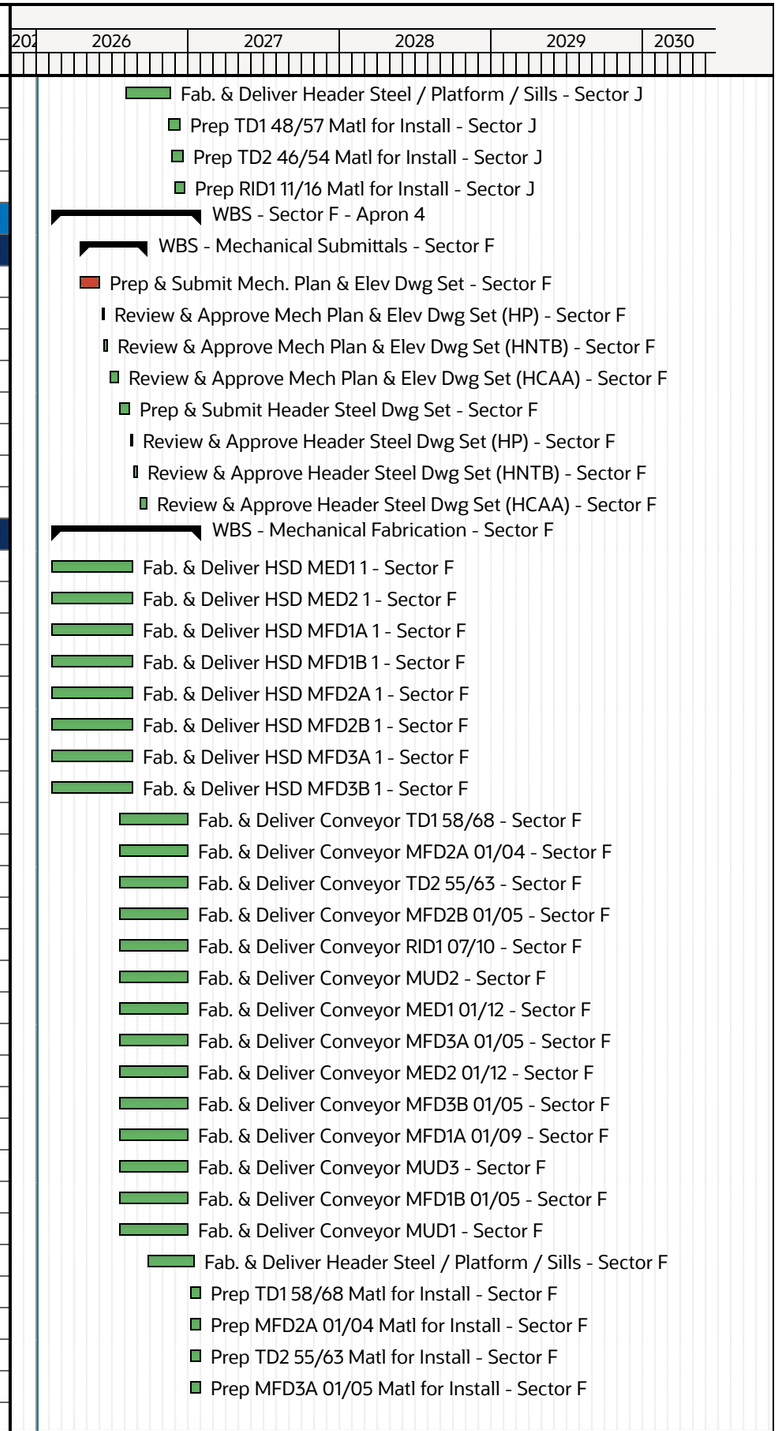


	ID	Name	Dur	Start	Finish	TF
3235	D1554	Prep MFD1B 01/05 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	420.0d
3236	D1555	Prep MED2 01/12 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	410.0d
3237	D1556	Prep RID1 07/10 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	402.0d
3238	D1557	Prep MFD3B 01/05 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	400.0d
3239	D1558	Prep MFD2B 01/05 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	371.0d
3240	D1559	Prep MED1 01/12 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	410.0d
3241	D1560	Prep MUD1 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	358.0d
3242	D1561	Prep MUD2 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	379.0d
3243	D1562	Prep MFD1A 01/09 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	346.0d
3244	D1563	Prep MUD3 Matl for Install - Sector F	20.0d	4-Jan-27	29-Jan-27	403.0d
3245	WBS - Sector E - Apron 5		199.0d	1-Jun-26	12-Mar-27	769.0d
3246	WBS - Mechanical Submittals - Sector E - Apron 5		110.0d	1-Jun-26	3-Nov-26	85.0d
3247	D1564	Prep & Submit Mech. Plan & Elev Dwg Set - Sector E	30.0d	1-Jun-26	13-Jul-26	0.0d
3248	D5616	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector E	5.0d	14-Jul-26	20-Jul-26	85.0d
3249	D5626	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector E	10.0d	21-Jul-26	3-Aug-26	85.0d
3250	D1565	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector E	15.0d	4-Aug-26	24-Aug-26	85.0d
3251	D1568	Prep & Submit Header Steel Dwg Set - Sector E	20.0d	25-Aug-26	22-Sep-26	85.0d
3252	D5636	Review & Approve Header Steel Dwg Set (HP) - Sector E	5.0d	23-Sep-26	29-Sep-26	85.0d
3253	D5646	Review & Approve Header Steel Dwg Set (HNTB) - Sector E	10.0d	30-Sep-26	13-Oct-26	85.0d
3254	D1592	Review & Approve Header Steel Dwg Set (HCAA) - Sector E	15.0d	14-Oct-26	3-Nov-26	85.0d
3255	WBS - Mechanical Fabrication - Sector E - Apron 5		139.0d	25-Aug-26	12-Mar-27	769.0d
3256	D1566	Fab. & Deliver Conveyor CFD2A 04/07 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3257	D1567	Fab. & Deliver Conveyor CFD4A 01/03 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3258	D1569	Fab. & Deliver Conveyor CFD2B 04/12 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3259	D1570	Fab. & Deliver Conveyor CFD4B 01/03 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3260	D1571	Fab. & Deliver Conveyor CFD3A 04/06 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3261	D1572	Fab. & Deliver Conveyor CDD2 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3262	D1573	Fab. & Deliver Conveyor CFD3B 04/12 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3263	D1574	Fab. & Deliver Conveyor CFD2A 08/09 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3264	D1575	Fab. & Deliver Conveyor CFD4A 04/07 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3265	D1576	Fab. & Deliver Conveyor CFD2B 13/14 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3266	D1577	Fab. & Deliver Conveyor CFD4B 04/11 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3267	D1578	Fab. & Deliver Conveyor CFD3A 01/03 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3268	D1579	Fab. & Deliver Conveyor CFD3B 01/03 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3269	D1580	Fab. & Deliver Conveyor CDD3 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3270	D1581	Fab. & Deliver Conveyor CFD3A 07/08 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3271	D1582	Fab. & Deliver Conveyor CFD3B 13/14 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3272	D1583	Fab. & Deliver Conveyor CDD4 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3273	D1584	Fab. & Deliver Conveyor CFD4A 08/09 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3274	D1585	Fab. & Deliver Conveyor CFD4B 12/13 - Sector E	119.0d	25-Aug-26	12-Feb-27	290.0d
3275	D1586	Fab. & Deliver CFD2A 07 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d
3276	D1587	Fab. & Deliver CFD2B 12 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d

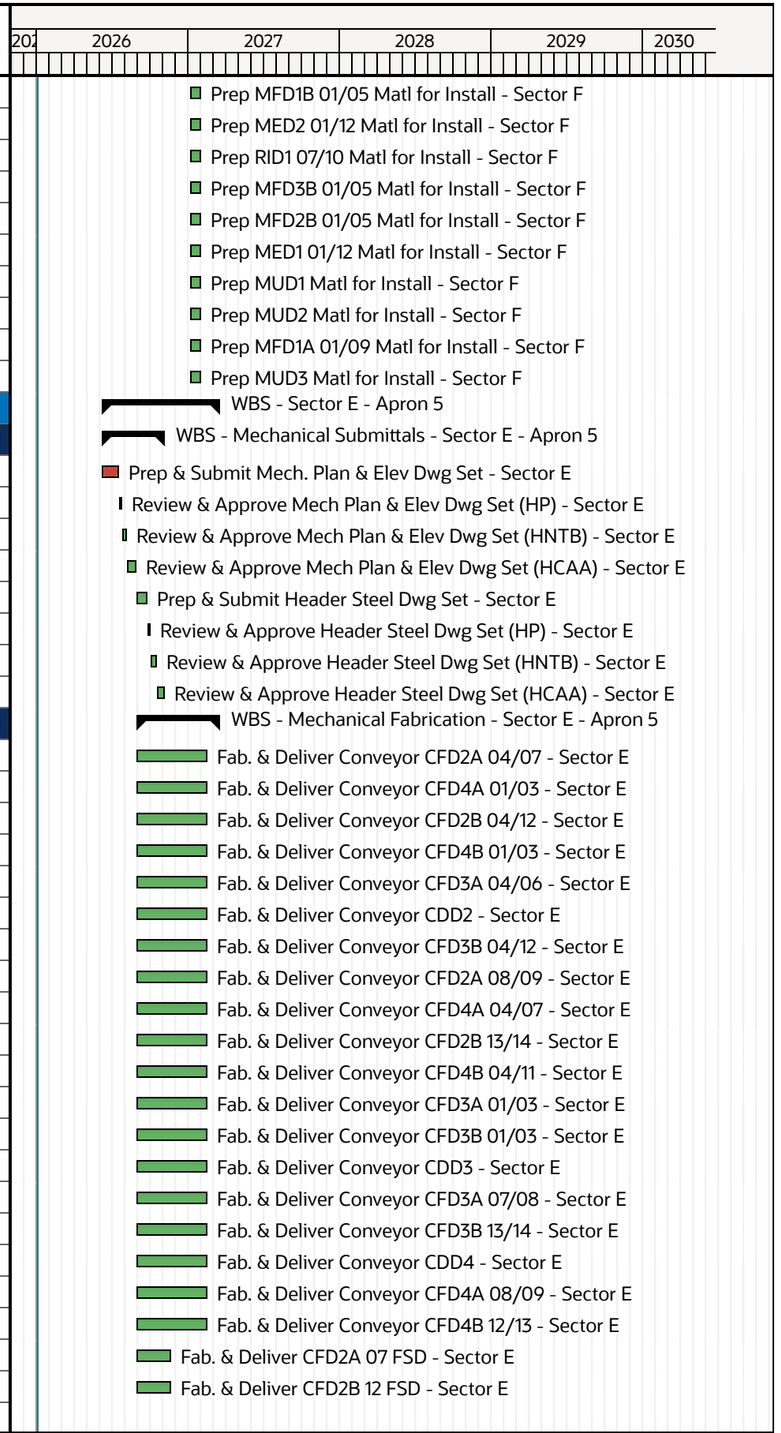


	ID	Name	Dur	Start	Finish	TF
3277	D1588	Fab. & Deliver CFD3A 06 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d
3278	D1589	Fab. & Deliver CFD3B 12 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d
3279	D1590	Fab. & Deliver CFD4A 07 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d
3280	D1591	Fab. & Deliver CFD4B 12 FSD - Sector E	60.0d	25-Aug-26	17-Nov-26	847.0d
3281	D1593	Fab. & Deliver Header Steel / Platform / Sills - Sector E	79.0d	4-Nov-26	26-Feb-27	85.0d
3282	D1594	Prep Mech. Matl for Install - Sector E	20.0d	15-Feb-27	12-Mar-27	290.0d
3283	WBS - Sector B - Apron 8		189.0d	14-Jul-26	9-Apr-27	749.0d
3284	WBS - Mechanical Submittals - Sector B - Apron 8		95.0d	14-Jul-26	24-Nov-26	108.0d
3285	D1595	Prep & Submit Mech. Plan & Elev Dwg Set - Sector B	20.0d	14-Jul-26	10-Aug-26	0.0d
3286	D5656	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector B	5.0d	11-Aug-26	17-Aug-26	108.0d
3287	D5666	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector B	10.0d	18-Aug-26	31-Aug-26	108.0d
3288	D1596	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector B	15.0d	1-Sep-26	22-Sep-26	108.0d
3289	D1599	Prep & Submit Header Steel Dwg Set - Sector B	15.0d	23-Sep-26	13-Oct-26	108.0d
3290	D5676	Review & Approve Header Steel Dwg Set (HP) - Sector B	5.0d	14-Oct-26	20-Oct-26	108.0d
3291	D5686	Review & Approve Header Steel Dwg Set (HNTB) - Sector B	10.0d	21-Oct-26	3-Nov-26	108.0d
3292	D1609	Review & Approve Header Steel Dwg Set (HCAA) - Sector B	15.0d	4-Nov-26	24-Nov-26	108.0d
3293	WBS - Mechanical Fabrication - Sector B - Apron 8		139.0d	23-Sep-26	9-Apr-27	749.0d
3294	D1597	Fab. & Deliver Conveyor CFD1B 04/12 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3295	D1598	Fab. & Deliver Conveyor CFD2B 01/03 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3296	D1600	Fab. & Deliver Conveyor CFD1A 01/03 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3297	D1601	Fab. & Deliver Conveyor CDD1 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3298	D1602	Fab. & Deliver Conveyor CFD1B 01/03 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3299	D1603	Fab. & Deliver Conveyor CFD1A 08/09 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3300	D1604	Fab. & Deliver Conveyor CFD2A 01/03 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3301	D1605	Fab. & Deliver Conveyor CFD1B 13/14 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3302	D1606	Fab. & Deliver Conveyor CFD1A 04/07 - Sector B	119.0d	23-Sep-26	12-Mar-27	326.0d
3303	D1607	Fab. & Deliver CFD1A 07 FSD - Sector B	60.0d	23-Sep-26	17-Dec-26	827.0d
3304	D1608	Fab. & Deliver CFD1B 12 FSD - Sector B	60.0d	23-Sep-26	17-Dec-26	827.0d
3305	D1610	Fab. & Deliver Header Steel / Platform / Sills - Sector B	79.0d	25-Nov-26	19-Mar-27	108.0d
3306	D1611	Prep Mech. Matl for Install - Sector B	20.0d	15-Mar-27	9-Apr-27	326.0d
3307	WBS - Sector C -Apron 9		332.0d	3-Feb-26	21-May-27	304.0d
3308	WBS - Mechanical Submittals - Sector C - Apron 9		110.0d	11-Aug-26	18-Jan-27	0.0d
3309	D1618	Prep & Submit Mech. Plan & Elev Dwg Set - Sector C	30.0d	11-Aug-26	22-Sep-26	0.0d
3310	D5696	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector C	5.0d	23-Sep-26	29-Sep-26	0.0d
3311	D5706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector C	10.0d	30-Sep-26	13-Oct-26	0.0d
3312	D1619	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector C	15.0d	14-Oct-26	3-Nov-26	0.0d
3313	D1622	Prep & Submit Header Steel Dwg Set - Sector C	20.0d	4-Nov-26	3-Dec-26	0.0d
3314	D5716	Review & Approve Header Steel Dwg Set (HP) - Sector C	5.0d	4-Dec-26	10-Dec-26	0.0d
3315	D5726	Review & Approve Header Steel Dwg Set (HNTB) - Sector C	10.0d	11-Dec-26	24-Dec-26	0.0d
3316	D1633	Review & Approve Header Steel Dwg Set (HCAA) - Sector C	15.0d	28-Dec-26	18-Jan-27	0.0d
3317	WBS - Mechanical Fabrication - Sector C - Apron 9		332.0d	3-Feb-26	21-May-27	304.0d
3318	D1612	Fab. & Deliver HSD MFD4A 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d

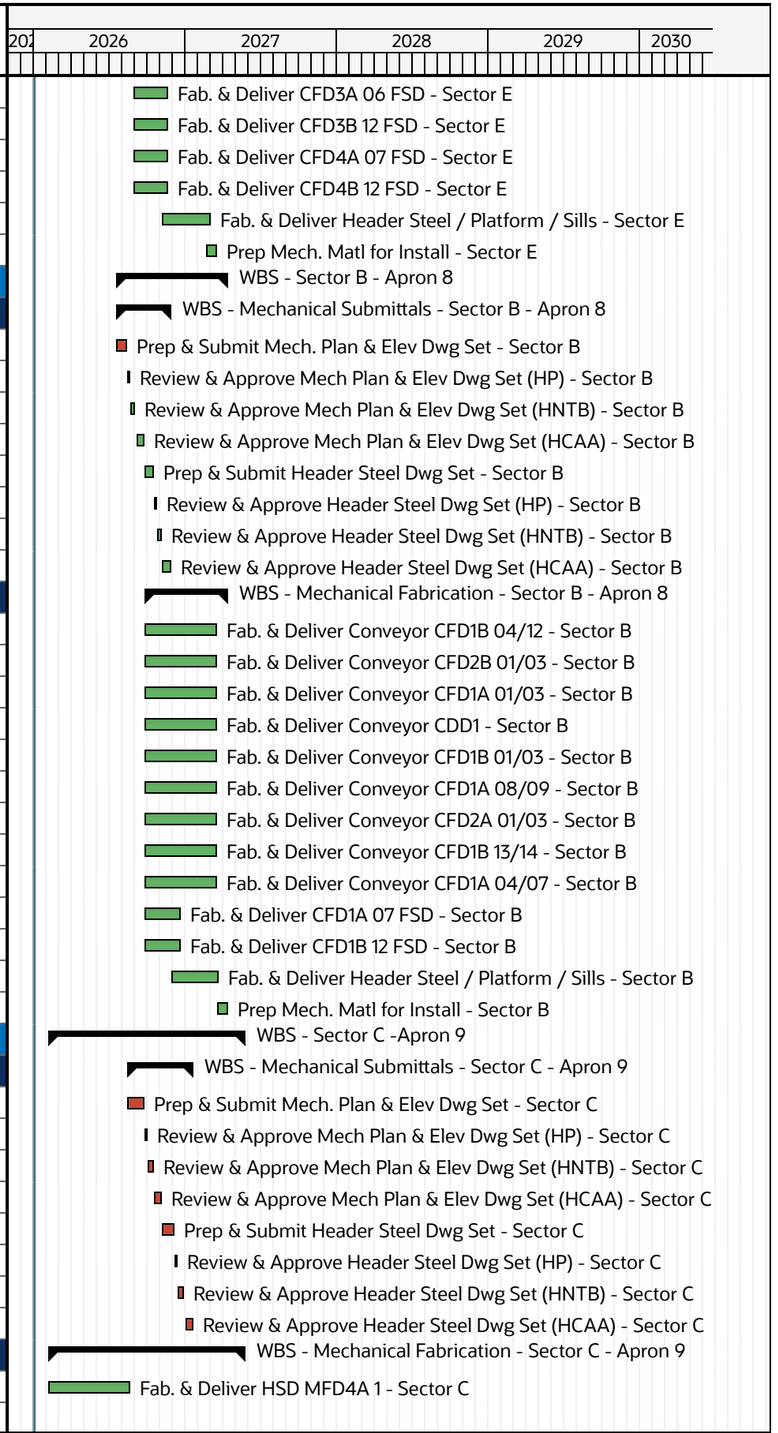


	ID	Name	Dur	Start	Finish	TF
3319	D1613	Fab. & Deliver HSD MFD4B 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d
3320	D1614	Fab. & Deliver HSD MFD5A 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d
3321	D1615	Fab. & Deliver HSD MFD5B 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d
3322	D1616	Fab. & Deliver HSD MFD6A 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d
3323	D1617	Fab. & Deliver HSD MFD6B 1 - Sector C	140.0d	3-Feb-26	19-Aug-26	419.0d
3324	D1620	Fab. & Deliver Conveyor TD1 69/75 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3325	D1621	Fab. & Deliver Conveyor MFD5A 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3326	D1623	Fab. & Deliver Conveyor TD2 64/74 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3327	D1624	Fab. & Deliver Conveyor MFD5B 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3328	D1625	Fab. & Deliver Conveyor RID1 01/06 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3329	D1626	Fab. & Deliver Conveyor MUD5 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3330	D1627	Fab. & Deliver Conveyor MFD4A 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3331	D1628	Fab. & Deliver Conveyor MFD6A 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3332	D1629	Fab. & Deliver Conveyor MFD4B 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3333	D1630	Fab. & Deliver Conveyor MFD6B 01/05 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3334	D1631	Fab. & Deliver Conveyor MUD4 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3335	D1632	Fab. & Deliver Conveyor MUD6 - Sector C	119.0d	4-Nov-26	23-Apr-27	304.0d
3336	D1634	Fab. & Deliver Header Steel / Platform / Sills - Sector C	80.0d	19-Jan-27	10-May-27	0.0d
3337	D1635	Prep Mech. Matl for Install - Sector C	20.0d	26-Apr-27	21-May-27	304.0d
3338	WBS - Sector H - Apron 5		179.0d	23-Sep-26	7-Jun-27	709.0d
3339	WBS - Mechanical Submittals - Sector H - Apron 5		40.0d	23-Sep-26	17-Nov-26	320.0d
3340	D1636	Prep & Submit Mech. Plan & Elev Dwg Set - Sector H	10.0d	23-Sep-26	6-Oct-26	320.0d
3341	D5736	Review & Approve Mech Plan & Elev Dwg Set (HP) - Sector H	5.0d	7-Oct-26	13-Oct-26	320.0d
3342	D5746	Review & Approve Mech Plan & Elev Dwg Set (HNTB) - Sector H	10.0d	14-Oct-26	27-Oct-26	320.0d
3343	D1637	Review & Approve Mech Plan & Elev Dwg Set (HCAA) - Sector H	15.0d	28-Oct-26	17-Nov-26	320.0d
3344	WBS - Mechanical Fabrication - Sector H - Apron 5		139.0d	18-Nov-26	7-Jun-27	709.0d
3345	D1638	Fab. & Deliver Conveyor OSD1 01/03 - Sector H	119.0d	18-Nov-26	7-May-27	320.0d
3346	D1639	Fab. & Deliver Conveyor IRD1 01/06 - Sector H	119.0d	18-Nov-26	7-May-27	320.0d
3347	D1640	Fab. & Deliver OSD1 02 FSD - Sector H	59.0d	18-Nov-26	12-Feb-27	788.0d
3348	D1641	Fab. & Deliver IRD1 02 FSD - Sector H	59.0d	18-Nov-26	12-Feb-27	788.0d
3349	D1642	Prep Mech. Matl for Install - Sector H	20.0d	10-May-27	7-Jun-27	320.0d
3350	WBS - Mechanical As-Built Drawings		50.0d	7-Sep-28	15-Nov-28	341.0d
3351	D3496	Prep & Submit Mech. As-Built Drawings	20.0d	7-Sep-28	4-Oct-28	340.0d
3352	D3516	Review & Approve (HP) Mech. As-Built Drawings	5.0d	5-Oct-28	11-Oct-28	340.0d
3353	D3526	Review & Approve (HNTB) Mech. As-Built Drawings	10.0d	12-Oct-28	25-Oct-28	340.0d
3354	D3506	Review & Approve (HCAA) Mech. As-Built Drawings	15.0d	26-Oct-28	15-Nov-28	340.0d
3355	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - ASD		766.0d	18-Nov-25 A	22-Nov-28	336.0d
3356	WBS - Sector M		115.0d	13-Mar-26	24-Aug-26	880.0d
3357	D1731	Prep & Submit Elect Drawings MPP-A20, CSC-A20, MPP-B20, CSC-B20 - Secto…	45.0d	13-Mar-26	14-May-26	879.0d
3358	D5756	Review & Approve Elec. Drawings (HP) MPP-A20, CSC-A20, MPP-B20, CSC-B2…	5.0d	15-May-26	21-May-26	879.0d
3359	D5766	Review & Approve Elec. Drawings (HNTB) MPP-A20, CSC-A20, MPP-B20, CSC-…	10.0d	22-May-26	5-Jun-26	879.0d
3360	D1732	Review & Approve Elec. Drawings (HCAA) MPP-A20, CSC-A20, MPP-B20, CSC-…	15.0d	8-Jun-26	26-Jun-26	879.0d

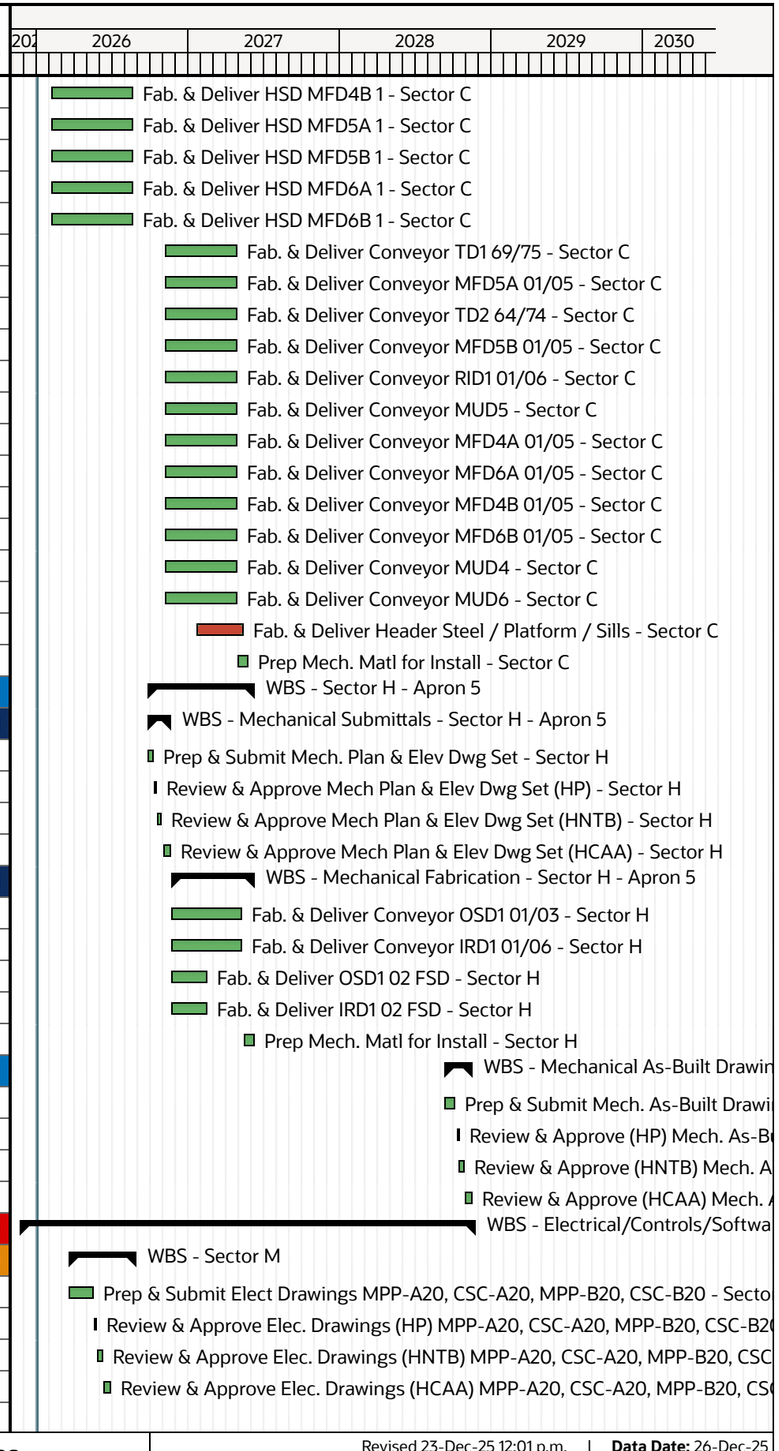


	ID	Name	Dur	Start	Finish	TF
3361	D1733	Fab. & Deliver MPP-A20, CSC-A20, MPP-B20, CSC-B20, Elect Field Devices, Ca...	40.0d	29-Jun-26	24-Aug-26	879.0d
3362	WBS - Sector J - Apron 2		115.0d	10-Apr-26	22-Sep-26	513.0d
3363	D1734	Prep & Submit Elect Drawings MPP-A30, CSC-A30, MPP-B30, CSC-B30 - Sector J	45.0d	10-Apr-26	12-Jun-26	513.0d
3364	D5776	Review & Approve Elec. Drawings (HP) MPP-A30, CSC-A30, MPP-B30, CSC-B3...	5.0d	15-Jun-26	19-Jun-26	513.0d
3365	D5786	Review & Approve Elec. Drawings (HNTB) MPP-A30, CSC-A30, MPP-B30, CSC-...	10.0d	22-Jun-26	6-Jul-26	513.0d
3366	D1735	Review & Approve Elec. Drawings (HCAA) MPP-A30, CSC-A30, MPP-B30, CSC-...	15.0d	7-Jul-26	27-Jul-26	513.0d
3367	D1736	Fab. & Deliver MPP-A30, CSC-A30, MPP-B30, CSC-B30, Elect Field Devices, Ca...	40.0d	28-Jul-26	22-Sep-26	513.0d
3368	WBS - Sector F - Apron 4		130.0d	1-Jun-26	3-Dec-26	772.0d
3369	D1737	Prep & Submit Elect Drawings MPP-B31, CSD-B31, MPP-A35, CSC-A35, MPP-...	45.0d	1-Jun-26	3-Aug-26	771.0d
3370	D5796	Review & Approve Elec. Drawings (HP) MPP-B31, CSD-B31, MPP-A35, CSC-A3...	15.0d	4-Aug-26	24-Aug-26	771.0d
3371	D5806	Review & Approve Elec. Drawings (HNTB) MPP-B31, CSD-B31, MPP-A35, CSC-...	15.0d	25-Aug-26	15-Sep-26	771.0d
3372	D1738	Review & Approve Elec. Drawings (HCAA) MPP-B31, CSD-B31, MPP-A35, CSC-...	15.0d	16-Sep-26	6-Oct-26	771.0d
3373	D1739	Fab. & Deliver MPP-B31, CSD-B31, MPP-A35, CSC-A35, MPP-B35, CSC-B35, M...	40.0d	7-Oct-26	3-Dec-26	771.0d
3374	WBS - Sector E - Apron 5		114.0d	14-Jul-26	23-Dec-26	452.0d
3375	D1740	Prep & Submit Elect Drawings MPP-A33, CSC-A33, MPP-B33, CSC-B33, MPP-...	45.0d	14-Jul-26	15-Sep-26	452.0d
3376	D5816	Review & Approve Elec. Drawings (HP) MPP-A33, CSC-A33, MPP-B33, CSC-B3...	5.0d	16-Sep-26	22-Sep-26	452.0d
3377	D5826	Review & Approve Elec. Drawings (HNTB) MPP-A33, CSC-A33, MPP-B33, CSC-...	10.0d	23-Sep-26	6-Oct-26	452.0d
3378	D1741	Review & Approve Elec. Drawings (HCAA) MPP-A33, CSC-A33, MPP-B33, CSC-...	15.0d	7-Oct-26	27-Oct-26	452.0d
3379	D1742	Fab. & Deliver MPP-A33, CSC-A33, MPP-B33, CSC-B33, MPP-A34, CSC-A34, M...	39.0d	28-Oct-26	23-Dec-26	452.0d
3380	WBS - Sector C - Apron 9		115.0d	23-Sep-26	8-Mar-27	351.0d
3381	D1743	Prep & Submit Elect Dwg Sets MPPs & CSCs A31, B32, B36, A37 & B37 - Sector C	45.0d	23-Sep-26	24-Nov-26	351.0d
3382	D5836	Review & Approve Elec. Dwg Sets (HP) MPPs & CSCs A31, B32, B36, A37 & B37...	5.0d	25-Nov-26	3-Dec-26	351.0d
3383	D5846	Review & Approve Elec. Dwg Sets (HNTB) MPPs & CSCs A31, B32, B36, A37 & ...	10.0d	4-Dec-26	17-Dec-26	351.0d
3384	D1744	Review & Approve Elec. Dwg Sets (HCAA) MPPs & CSCs A31, B32, B36, A37 & ...	15.0d	18-Dec-26	11-Jan-27	351.0d
3385	D1745	Fab. & Deliver MPPs & CSCs A31, B32, B36, A37 & B37, Elect Field Devices, Ca...	40.0d	12-Jan-27	8-Mar-27	351.0d
3386	WBS - General Electrical/Controls/Software Engineering Submittals - ASD		766.0d	18-Nov-25 A	22-Nov-28	336.0d
3387	WBS - Factory Acceptance Test Plan & Agenda		45.0d	13-Feb-26	16-Apr-26	901.0d
3388	D5986	Prep & Submit Factory Acceptance Test Plan & Agenda	15.0d	13-Feb-26	5-Mar-26	900.0d
3389	D6006	HP Review & Approve Factory Acceptance Test Plan & Agenda	5.0d	6-Mar-26	12-Mar-26	900.0d
3390	D6016	HNTB Review & Approve Factory Acceptance Test Plan & Agenda	10.0d	13-Mar-26	26-Mar-26	900.0d
3391	D5996	HCAA Review & Approve Factory Acceptance Test Plan & Agenda	15.0d	27-Mar-26	16-Apr-26	900.0d
3392	WBS - Power Requirements and MCP/MPP/CSC/FCP Sizes Submittals		75.0d	13-Feb-26	29-May-26	961.0d
3393	A109840	Prep & Submit Power Requirements & MCP/MPP/CSC/FCP Sizes	45.0d	13-Feb-26	16-Apr-26	531.0d
3394	A109860	Review & Approve (HP) Power Requirements & MCP/MPP/CSC/FCP Sizes	5.0d	17-Apr-26	23-Apr-26	960.0d
3395	A109870	Review & Approve (HNTB) Power Requirements & MCP/MPP/CSC/FCP Sizes	10.0d	24-Apr-26	7-May-26	960.0d
3396	A109850	Review & Approve (HCAA) Power Requirements & MCP/MPP/CSC/FCP Sizes	15.0d	8-May-26	29-May-26	960.0d
3397	WBS - E-Stop Zone Drawings Submittals		90.0d	17-Apr-26	24-Aug-26	531.0d
3398	A109880	Prep & Submit E-Stop Zone Drawings	60.0d	17-Apr-26	13-Jul-26	531.0d
3399	A109890	Review & Approve (HP) E-Stop Zone Drawings	5.0d	14-Jul-26	20-Jul-26	531.0d
3400	A109900	Review & Approve (HNTB) E-Stop Zone Drawings	10.0d	21-Jul-26	3-Aug-26	531.0d
3401	A109910	Review & Approve (HCAA) E-Stop Zone Drawings	15.0d	4-Aug-26	24-Aug-26	531.0d
3402	WBS - Final Electrical As-Built Drawings		55.0d	7-Sep-28	22-Nov-28	336.0d

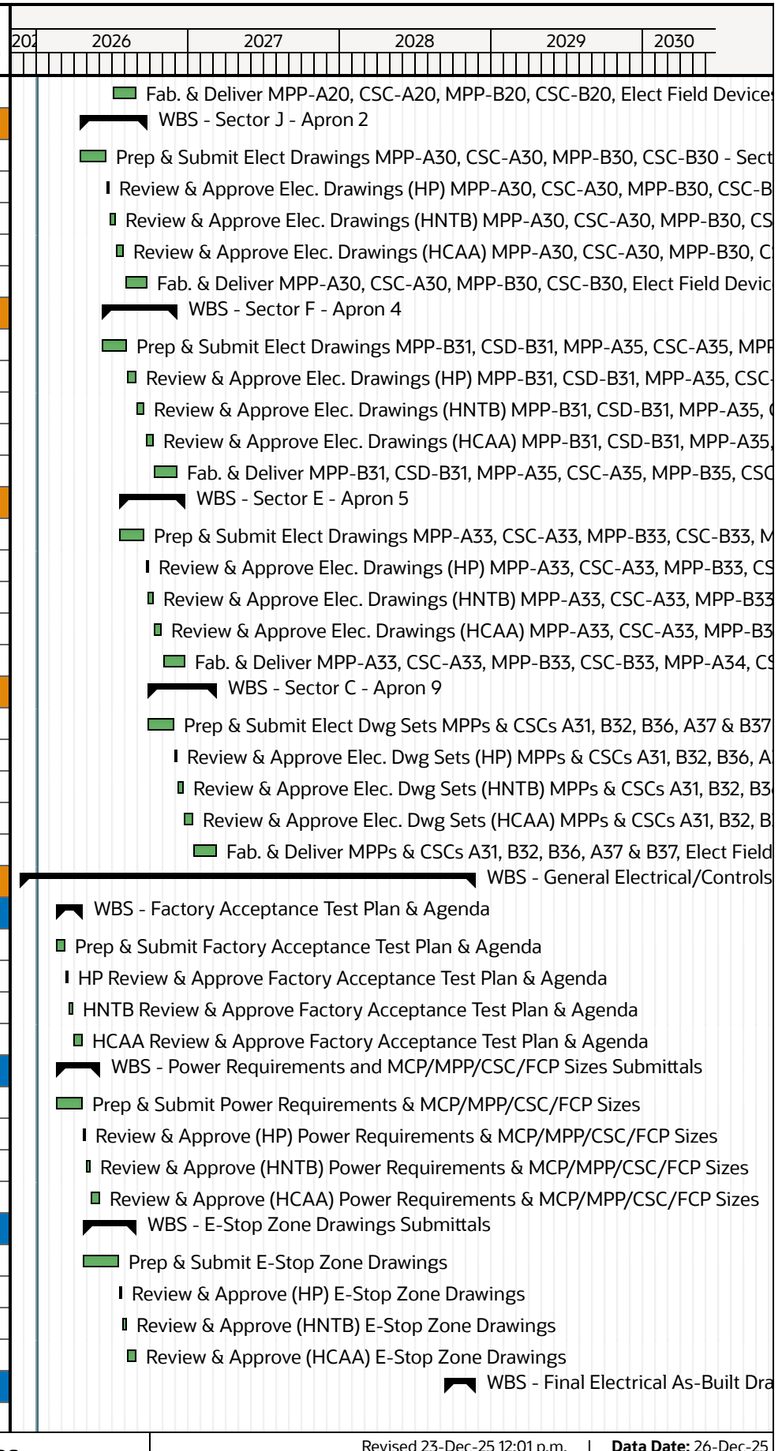


	ID	Name	Dur	Start	Finish	TF
3403	D6026	Prep & Submit Final Electrical As-Built Drawings	25.0d	7-Sep-28	11-Oct-28	335.0d
3404	D6126	HP Review & Approve Final Elec. As-Built Drawings	5.0d	12-Oct-28	18-Oct-28	335.0d
3405	D6136	HNTB Review & Approve Final Elec. As-Built Drawings	10.0d	19-Oct-28	1-Nov-28	335.0d
3406	D6036	HCAA Review & Approve Final Elec. As-Built Drawings	15.0d	2-Nov-28	22-Nov-28	335.0d
3407	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		57.0d	18-Nov-25 A	10-Feb-26	373.0d
3408	A110050	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	27.0d	18-Nov-25 A	29-Dec-25	373.0d
3409	A110070	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
3410	A110160	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
3411	A110170	Review & Approve (HCAA) Elec. / Controls / Computer Catalog Cuts & Equip. S...	15.0d	21-Jan-26	10-Feb-26	373.0d
3412	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		103.0d	30-Dec-25	22-May-26	962.0d
3413	A110020	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	30-Dec-25	20-Jan-26	929.0d
3414	A110090	Review & Approve (HP) ATR / BMA Catalog Cuts & Equip. Specs	5.0d	21-Jan-26	27-Jan-26	929.0d
3415	A110180	Review & Approve (HNTB) ATR / BMA Catalog Cuts & Equip. Specs	10.0d	28-Jan-26	10-Feb-26	929.0d
3416	A110190	Review & Approve (HCAA) ATR / BMA Catalog Cuts & Equip. Specs	15.0d	11-Feb-26	3-Mar-26	929.0d
3417	A109990	Fab. & Ship ATR Equip.- ASD Conveyors	80.0d	4-Mar-26	22-May-26	1,352.0d
3418	A110290	Deliver ATR Equip.- ASD Conveyors	0.0d		22-May-26	961.0d
3419	WBS - Lower-Level Network Architecture Drawings Submittals		60.0d	30-Dec-25	24-Mar-26	383.0d
3420	A110040	Prep & Submit Lower-Level Network Architecture Drawings	30.0d	30-Dec-25	10-Feb-26	383.0d
3421	A110210	Review & Approve (HP) Lower-Level Network Architecture Drawings	5.0d	11-Feb-26	17-Feb-26	383.0d
3422	A110200	Review & Approve (HNTB) Lower-Level Network Architecture Drawings	10.0d	18-Feb-26	3-Mar-26	383.0d
3423	A110110	Review & Approve (HCAA) Lower-Level Network Architecture Drawings	15.0d	4-Mar-26	24-Mar-26	383.0d
3424	WBS - Upper-Level Network Architecture Drawings Submittals		60.0d	11-Feb-26	5-May-26	808.0d
3425	A110010	Prep & Submit Upper-Level Network Architecture Drawings	30.0d	11-Feb-26	24-Mar-26	807.0d
3426	A110100	Review & Approve (HP) Upper-Level Network Architecture Drawings	5.0d	25-Mar-26	31-Mar-26	807.0d
3427	A110240	Review & Approve (HNTB) Upper-Level Network Architecture Drawings	10.0d	1-Apr-26	14-Apr-26	807.0d
3428	A110250	Review & Approve (HCAA) Upper-Level Network Architecture Drawings	15.0d	15-Apr-26	5-May-26	807.0d
3429	WBS - Functional Specification Submittals		141.0d	18-Nov-25 A	9-Jun-26	535.0d
3430	A110060	Prep & Submit Functional Specification [180 days prior to pre-TRR]	111.0d	18-Nov-25 A	27-Apr-26	535.0d
3431	A110130	Review & Approve (HP) Functional Specification	5.0d	28-Apr-26	4-May-26	535.0d
3432	A110260	Review & Approve (HNTB) Functional Specification	10.0d	5-May-26	18-May-26	535.0d
3433	A110270	Review & Approve (HCAA) Functional Specification	15.0d	19-May-26	9-Jun-26	535.0d
3434	WBS - Electrical & Controls Equipment Procurement		95.0d	11-Feb-26	24-Jun-26	930.0d
3435	D6046	Procure BHS Control Room Equip.	40.0d	11-Feb-26	7-Apr-26	827.0d
3436	D6056	Procure BHS Server Room Equip.	40.0d	11-Feb-26	7-Apr-26	827.0d
3437	D6066	Procure PLC Enclosure(s) Equip.	40.0d	11-Feb-26	7-Apr-26	827.0d
3438	D6106	Procure Manual Encode Consoles	40.0d	11-Feb-26	7-Apr-26	373.0d
3439	D6116	Procure ATR Equip. (Airside D)	80.0d	4-Mar-26	24-Jun-26	929.0d
3440	WBS - Cybersecurity Plan Submittals		50.0d	13-Feb-26	23-Apr-26	211.0d
3441	A110370	Prep & Submit Cybersecurity Plan [5 days prior to beneficial use by phase]	20.0d	13-Feb-26	12-Mar-26	211.0d
3442	A110390	Review & Approve (HP) Cybersecurity Plan	5.0d	13-Mar-26	19-Mar-26	211.0d
3443	A110420	Review & Approve (HNTB) Cybersecurity Plan	10.0d	20-Mar-26	2-Apr-26	211.0d
3444	A110430	Review & Approve (HCAA) Cybersecurity Plan	15.0d	3-Apr-26	23-Apr-26	211.0d

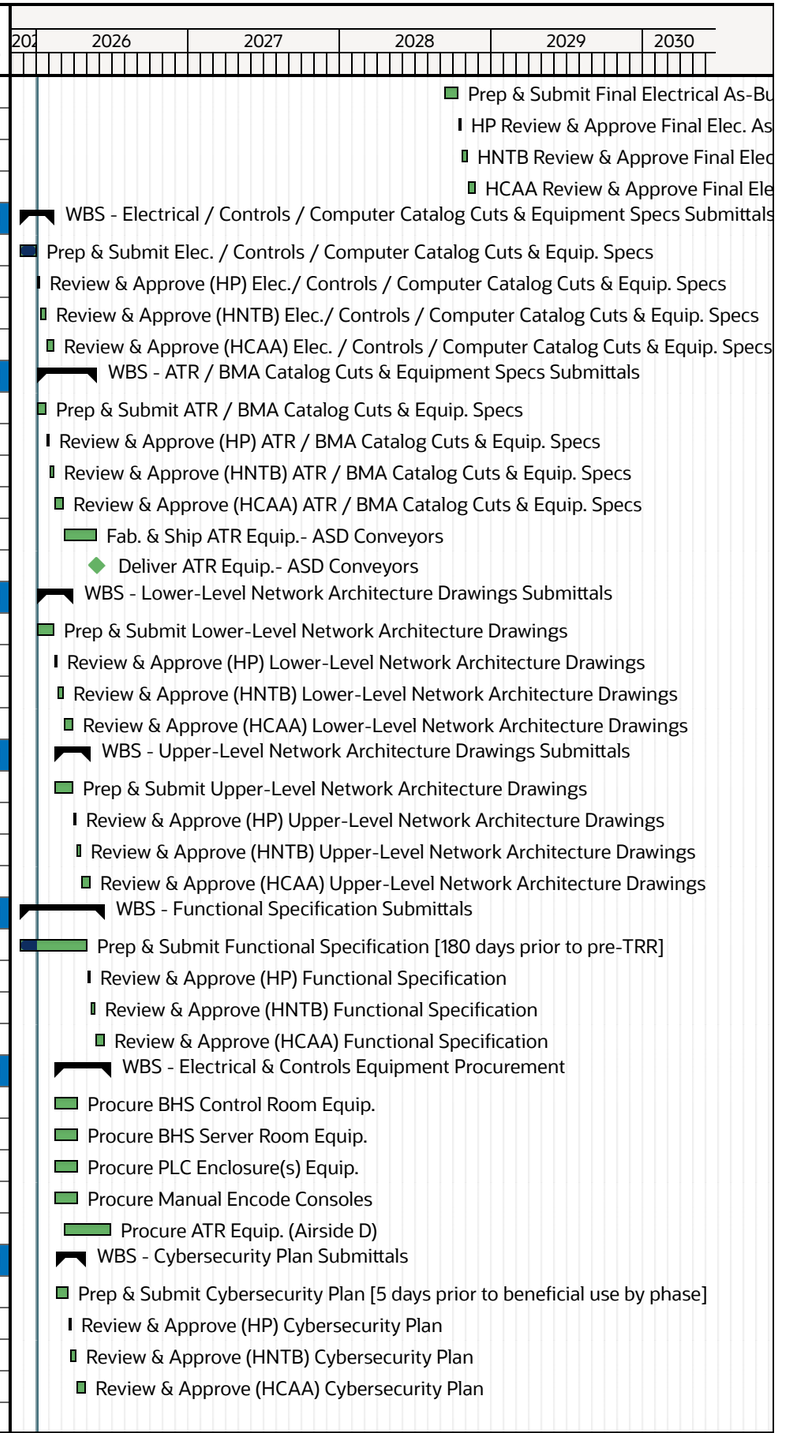


	ID	Name	Dur	Start	Finish	TF
3445	WBS - Software Development/Testing & Factory Acceptance Testing - ASD		218.0d	6-May-26	16-Mar-27	709.0d
3446	D1756	Software Development / Testing - Airside D FAT	60.0d	6-May-26	30-Jul-26	827.0d
3447	D1755	PLC Code Development - Airside D FAT	80.0d	6-May-26	27-Aug-26	807.0d
3448	D1757	Internal FAT - Airside D FAT	9.0d	28-Aug-26	10-Sep-26	807.0d
3449	D1758	Customer FAT - Airside D FAT	5.0d	11-Sep-26	17-Sep-26	807.0d
3450	D1759	FAT Remediation - Airside D FAT	10.0d	18-Sep-26	1-Oct-26	807.0d
3451	D1760	FAT Remediation / Customer Demonstration - Airside D FAT	5.0d	2-Oct-26	8-Oct-26	807.0d
3452	D1761	FAT Clean Up / Ship to Site - Airside D FAT	10.0d	3-Mar-27	16-Mar-27	708.0d
3453	WBS - Wave 2 Supplement C - Finishes Procurement		223.0d	6-Apr-26	20-Feb-27	461.0d
3454	WBS - Metal Doors, Frames, Hardware Procurement - ASD		90.0d	6-Apr-26	11-Aug-26	139.0d
3455	PR-P1-1C1-2420	Prep Metal Doors, Frames, Hardware Submittals (Contractor) - ASD	30.0d	6-Apr-26	15-May-26	139.0d
3456	PR-P1-1C1-2430	Review & Submit Metal Doors, Frames, Hardware Submittals (HP) - ASD	10.0d	18-May-26	1-Jun-26	139.0d
3457	PR-P1-1C1-2440	Review & Approve Metal Doors, Frames, Hardware Submittals (HNTB) - ASD	10.0d	2-Jun-26	15-Jun-26	139.0d
3458	PR-P1-1C1-2450	Review & Approve Metal Doors, Frames, Hardware Submittals (HCAA) - ASD	15.0d	16-Jun-26	7-Jul-26	139.0d
3459	PR-P1-1C1-2460	Fab. & Ship Metal Doors, Frames, Hardware - ASD	35.0d	8-Jul-26	11-Aug-26	197.0d
3460	PR-P1-1C1-2470	Delivery of Metal Doors, Frames, Hardware on Site - ASD	0.0d		11-Aug-26	197.0d
3461	WBS - Airport Access Controls Procurement - ASD		122.0d	13-Apr-26	3-Oct-26	478.0d
3462	PR-P2-1C2-6970	Prep Airport Access Controls Submittals (Contractor) - ASD	30.0d	13-Apr-26	22-May-26	479.0d
3463	PR-P2-1C2-6980	Review & Submit Airport Access Controls Submittals (HP) - ASD	10.0d	26-May-26	8-Jun-26	479.0d
3464	PR-P2-1C2-6990	Review & Approve Airport Access Controls Submittals (HNTB) - ASD	10.0d	9-Jun-26	22-Jun-26	479.0d
3465	PR-P2-1C2-7000	Review & Approve Airport Access Controls Submittals (HCAA) - ASD	15.0d	23-Jun-26	14-Jul-26	479.0d
3466	PR-P2-1C2-7010	Fab. & Ship Airport Access Controls - ASD	80.0d	15-Jul-26	3-Oct-26	671.0d
3467	PR-P2-1C2-7020	Delivery of Airport Access Controls on Site - ASD	0.0d		3-Oct-26	671.0d
3468	WBS - Site Specialties Procurement - ASD		107.0d	5-May-26	5-Oct-26	441.0d
3469	PR-P2-1C2-770	Prep Site Specialties Submittals (Contractor) - ASD	30.0d	5-May-26	16-Jun-26	440.0d
3470	PR-P2-1C2-775	Review & Submit Site Specialties Submittals (HP) - ASD	10.0d	17-Jun-26	30-Jun-26	440.0d
3471	PR-P2-1C2-1270	Review & Approve Site Specialties Submittals (HNTB) - ASD	10.0d	1-Jul-26	15-Jul-26	440.0d
3472	PR-P2-1C2-1275	Review & Approve Site Specialties Submittals (HCAA) - ASD	15.0d	16-Jul-26	5-Aug-26	440.0d
3473	PR-P2-1C2-1650	Fab. & Ship Site Specialties Fab. - ASD	60.0d	6-Aug-26	5-Oct-26	617.0d
3474	PR-P2-1C2-2180	Delivery of Site Specialties on Site - ASD	0.0d		5-Oct-26	617.0d
3475	WBS - Architectural Millwork Procurement - ASD		164.0d	8-Apr-26	30-Nov-26	357.0d
3476	PR-P2-1C2-550	Prep Architectural Millwork Submittals (Contractor) - ASD	30.0d	8-Apr-26	19-May-26	355.0d
3477	PR-P2-1C2-555	Review & Submit Architectural Millwork Submittals (HP) - ASD	10.0d	20-May-26	3-Jun-26	355.0d
3478	PR-P2-1C2-1090	Review & Approve Architectural Millwork Submittals (HNTB)- ASD	10.0d	4-Jun-26	17-Jun-26	355.0d
3479	PR-P2-1C2-1095	Review & Approve Architectural Millwork Submittals (HCAA) - ASD	15.0d	18-Jun-26	9-Jul-26	355.0d
3480	PR-P2-1C2-1480	Fab. & Ship Architectural Millwork - ASD	141.0d	10-Jul-26	30-Nov-26	499.0d
3481	PR-P2-1C2-2340	Delivery of Architectural Millwork on Site - ASD	0.0d		30-Nov-26	499.0d
3482	WBS - Overhead Doors Procurement - ASD		84.0d	9-Apr-26	6-Aug-26	492.0d
3483	PR-P2-1C2-7030	Prep Overhead Doors Submittals (Contractor) - ASD	20.0d	9-Apr-26	6-May-26	493.0d
3484	PR-P2-1C2-7040	Review & Submit Overhead Doors Submittals (HP) - ASD	10.0d	7-May-26	20-May-26	493.0d
3485	PR-P2-1C2-7050	Review & Approve Overhead Doors Submittals (HNTB) - ASD	10.0d	21-May-26	4-Jun-26	493.0d
3486	PR-P2-1C2-7060	Review & Approve Overhead Doors Submittals (HCAA) - ASD	15.0d	5-Jun-26	25-Jun-26	493.0d

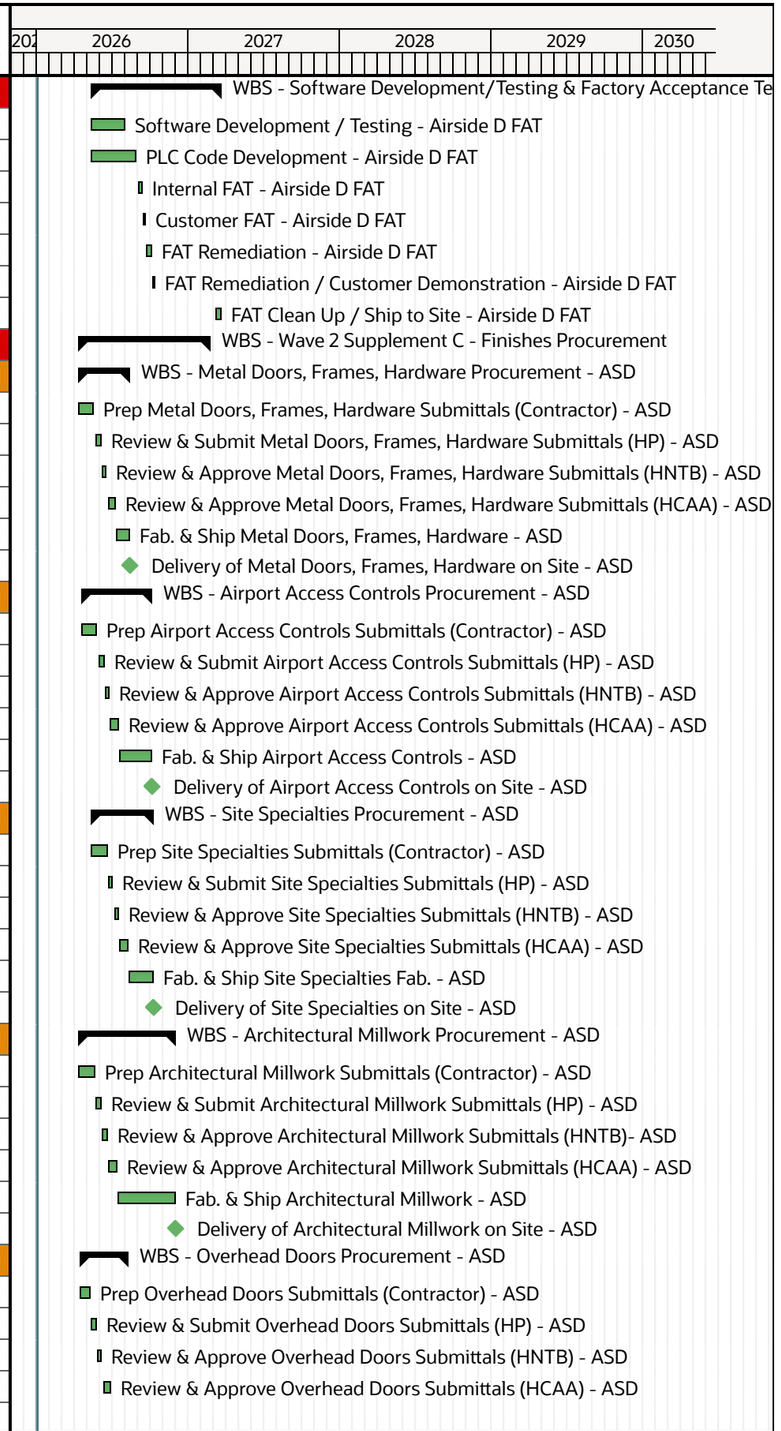


	ID	Name	Dur	Start	Finish	TF
3487	PR-P2-1C2-7070	Fab. & Ship Overhead Doors - ASD	40.0d	26-Jun-26	6-Aug-26	692.0d
3488	PR-P2-1C2-7080	Delivery of Overhead Doors on Site - ASD	0.0d		6-Aug-26	692.0d
3489	WBS - Overhead Coiling Doors Procurement - ASD		93.0d	9-Apr-26	19-Aug-26	156.0d
3490	PR-P2-1C2-950	Prep Overhead Coiling Doors Submittals (Contractor) - ASD	30.0d	9-Apr-26	20-May-26	155.0d
3491	PR-P2-1C2-955	Review & Submit Overhead Coiling Doors Submittals (HP) - ASD	10.0d	21-May-26	4-Jun-26	155.0d
3492	PR-P2-1C2-1440	Review & Approve Overhead Coiling Doors Submittals (HNTB) - ASD	10.0d	5-Jun-26	18-Jun-26	155.0d
3493	PR-P2-1C2-1445	Review & Approve Overhead Coiling Doors Submittals (HCAA) - ASD	15.0d	19-Jun-26	10-Jul-26	155.0d
3494	PR-P2-1C2-1820	Fab. & Ship Overhead Coiling Doors - ASD	40.0d	11-Jul-26	19-Aug-26	220.0d
3495	PR-P2-1C2-2110	Delivery of Overhead Coiling Doors on Site - ASD	0.0d		19-Aug-26	220.0d
3496	WBS - Tile & Stone Procurement - ASD		107.0d	14-Apr-26	14-Sep-26	396.0d
3497	PR-P2-1C2-7330	Prep Tile & Stone Submittals (Contractor) - ASD	30.0d	14-Apr-26	26-May-26	395.0d
3498	PR-P2-1C2-7340	Review & Submit Tile & Stone Submittals (HP) - ASD	10.0d	27-May-26	9-Jun-26	395.0d
3499	PR-P2-1C2-7350	Review & Approve Tile & Stone Submittals (HNTB) - ASD	10.0d	10-Jun-26	23-Jun-26	395.0d
3500	PR-P2-1C2-7360	Review & Approve Tile & Stone Submittals (HCAA) - ASD	15.0d	24-Jun-26	15-Jul-26	395.0d
3501	PR-P2-1C2-7370	Fab. & Ship Tile & Stone - ASD	60.0d	16-Jul-26	14-Sep-26	554.0d
3502	PR-P2-1C2-7380	Delivery of Tile & Stone on Site - ASD	0.0d		14-Sep-26	554.0d
3503	WBS - Flooring Procurement - ASD		107.0d	7-Apr-26	6-Sep-26	389.0d
3504	PR-P2-1C2-7150	Prep Flooring Submittals (Contractor) - ASD	30.0d	7-Apr-26	18-May-26	389.0d
3505	PR-P2-1C2-7160	Review & Submit Flooring Submittals (HP) - ASD	10.0d	19-May-26	2-Jun-26	389.0d
3506	PR-P2-1C2-7170	Review & Approve Flooring Submittals (HNTB) - ASD	10.0d	3-Jun-26	16-Jun-26	389.0d
3507	PR-P2-1C2-7180	Review & Approve Flooring Submittals (HCAA) - ASD	15.0d	17-Jun-26	8-Jul-26	389.0d
3508	PR-P2-1C2-7190	Fab. & Ship Flooring - ASD	60.0d	9-Jul-26	6-Sep-26	545.0d
3509	PR-P2-1C2-7200	Delivery of Flooring on Site - ASD	0.0d		6-Sep-26	545.0d
3510	WBS - Specialty Flooring Procurement - ASD		107.0d	7-Apr-26	6-Sep-26	487.0d
3511	PR-P2-1C2-7420	Prep Specialty Flooring Submittals (Contractor) - ASD	30.0d	7-Apr-26	18-May-26	487.0d
3512	PR-P2-1C2-7430	Review & Submit Specialty Flooring Submittals (HP) - ASD	10.0d	19-May-26	2-Jun-26	487.0d
3513	PR-P2-1C2-7440	Review & Approve Specialty Flooring Submittals (HNTB) - ASD	10.0d	3-Jun-26	16-Jun-26	487.0d
3514	PR-P2-1C2-7450	Review & Approve Specialty Flooring Submittals (HCAA) - ASD	15.0d	17-Jun-26	8-Jul-26	487.0d
3515	PR-P2-1C2-7460	Fab. & Ship Specialty Flooring - ASD	60.0d	9-Jul-26	6-Sep-26	683.0d
3516	PR-P2-1C2-7470	Delivery of Specialty Flooring on Site - ASD	0.0d		6-Sep-26	683.0d
3517	WBS - Access Floors Procurement - ASD		107.0d	22-Apr-26	22-Sep-26	456.0d
3518	PR-P2-1C2-7210	Prep Access Floors Submittals (Contractor) - ASD	30.0d	22-Apr-26	3-Jun-26	456.0d
3519	PR-P2-1C2-7220	Review & Submit Access Floors Submittals (HP) - ASD	10.0d	4-Jun-26	17-Jun-26	456.0d
3520	PR-P2-1C2-7230	Review & Approve Access Floors Submittals (HNTB) - ASD	10.0d	18-Jun-26	1-Jul-26	456.0d
3521	PR-P2-1C2-7240	Review & Approve Access Floors Submittals (HCAA) - ASD	15.0d	2-Jul-26	23-Jul-26	456.0d
3522	PR-P2-1C2-7250	Fab. & Ship Access Floors - ASD	60.0d	24-Jul-26	22-Sep-26	640.0d
3523	PR-P2-1C2-7260	Delivery of Access Floors on Site - ASD	0.0d		22-Sep-26	640.0d
3524	WBS - Paints & Wall Coverings Procurement - ASD		82.0d	21-Apr-26	16-Aug-26	319.0d
3525	PR-P2-1C2-710	Prep Paints & Wall Coverings Submittals (Contractor) - ASD	30.0d	21-Apr-26	2-Jun-26	319.0d
3526	PR-P2-1C2-715	Review & Submit Paints & Wall Coverings Submittals (HP) - ASD	10.0d	3-Jun-26	16-Jun-26	319.0d
3527	PR-P2-1C2-1610	Review & Approve Paints & Wall Coverings (HNTB) - ASD	10.0d	17-Jun-26	30-Jun-26	319.0d
3528	PR-P2-1C2-1615	Review & Approve Paints & Wall Coverings (HCAA) - ASD	15.0d	1-Jul-26	22-Jul-26	319.0d

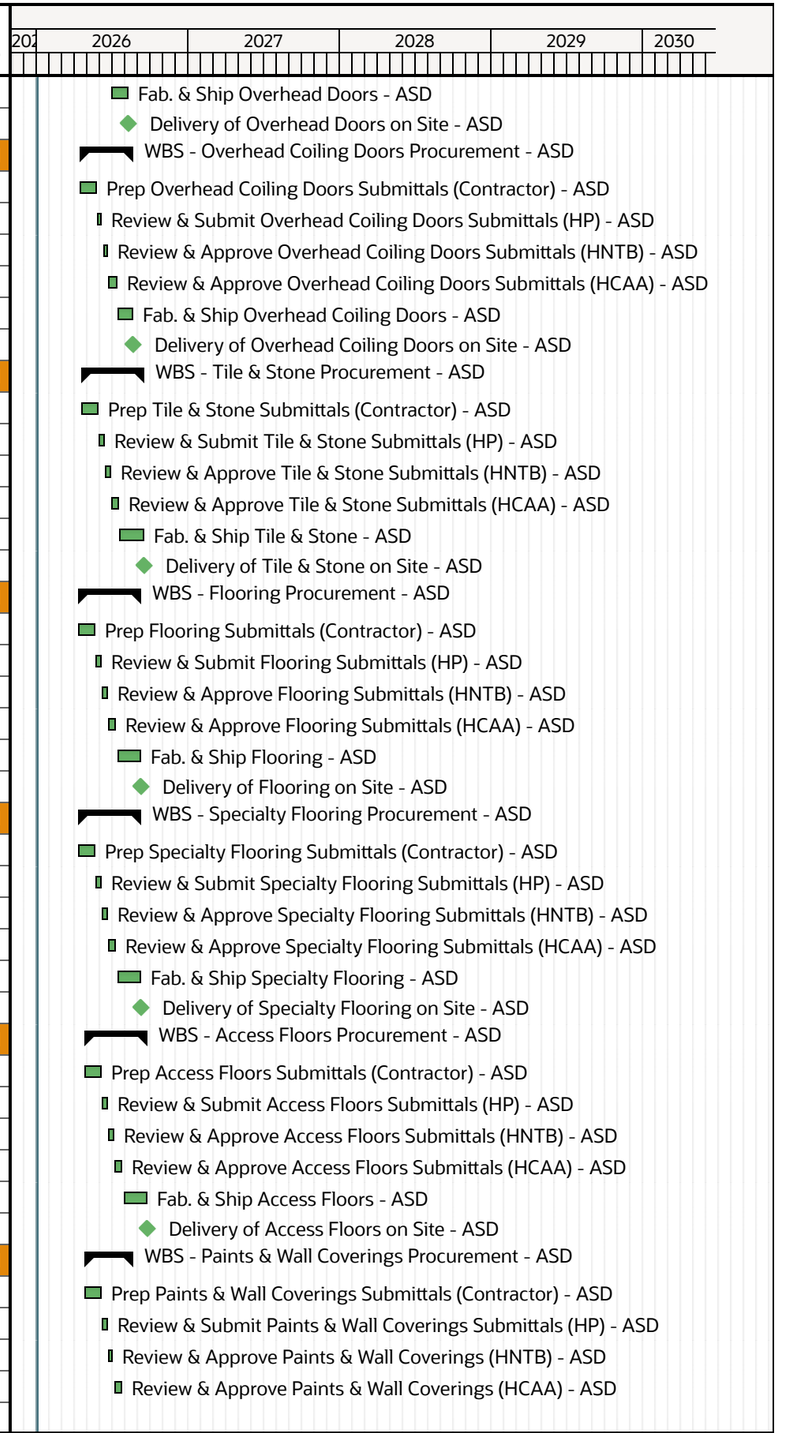


	ID	Name	Dur	Start	Finish	TF
3529	PR-P2-1C2-1935	Fab. & Ship Paints & Wall Coverings - ASD	25.0d	23-Jul-26	16-Aug-26	447.0d
3530	PR-P2-1C2-1940	Delivery of Paints & Wall Coverings on Site - ASD	0.0d		16-Aug-26	447.0d
3531	WBS - Signage Procurement - ASD		82.0d	15-Apr-26	10-Aug-26	541.0d
3532	PR-P2-1C2-970	Prep Signage Submittals (Contractor) - ASD	30.0d	15-Apr-26	27-May-26	541.0d
3533	PR-P2-1C2-975	Review & Submit Signage Submittals - ASD	10.0d	28-May-26	10-Jun-26	541.0d
3534	PR-P2-1C2-1450	Review & Approve Signage Submittals (HNTB) - ASD	10.0d	11-Jun-26	24-Jun-26	541.0d
3535	PR-P2-1C2-1046	Review & Approve Signage Submittals (HCAA) - ASD	15.0d	25-Jun-26	16-Jul-26	541.0d
3536	PR-P2-1C2-1830	Fab. & Ship Signage - ASD	25.0d	17-Jul-26	10-Aug-26	759.0d
3537	PR-P2-1C2-1970	Delivery of Signage on Site - ASD	0.0d		10-Aug-26	759.0d
3538	WBS - Toilet Partition & Accessories Procurement - ASD		93.0d	16-Apr-26	26-Aug-26	368.0d
3539	PR-P2-1C2-730	Prep Toilet Partition & Accessories Submittals (Contractor) - ASD	30.0d	16-Apr-26	28-May-26	367.0d
3540	PR-P2-1C2-735	Review & Submit Toilet Partition & Accessories Submittals (HP) - ASD	10.0d	29-May-26	11-Jun-26	367.0d
3541	PR-P2-1C2-1240	Review & Approve Toilet Partition & Accessories Submittals (HNTB) - ASD	10.0d	12-Jun-26	25-Jun-26	367.0d
3542	PR-P2-1C2-1245	Review & Approve Toilet Partition & Accessories Submittals (HCAA) - ASD	15.0d	26-Jun-26	17-Jul-26	367.0d
3543	PR-P2-1C2-1630	Fab. & Ship Toilet Partition & Accessories Fab. - ASD	40.0d	18-Jul-26	26-Aug-26	516.0d
3544	PR-P2-1C2-2050	Delivery of Toilet Partition & Accessories on Site - ASD	0.0d		26-Aug-26	516.0d
3545	WBS - Building Specialties Procurement - ASD		107.0d	20-Apr-26	20-Sep-26	567.0d
3546	PR-P2-1C2-7090	Prep Building Specialties Submittals (Contractor) - ASD	30.0d	20-Apr-26	1-Jun-26	567.0d
3547	PR-P2-1C2-7100	Review & Submit Building Specialties Submittals (HP) - ASD	10.0d	2-Jun-26	15-Jun-26	567.0d
3548	PR-P2-1C2-7110	Review & Approve Building Specialties Submittals (HNTB) - ASD	10.0d	16-Jun-26	29-Jun-26	567.0d
3549	PR-P2-1C2-7120	Review & Approve Building Specialties Submittals (HCAA) - ASD	15.0d	30-Jun-26	21-Jul-26	567.0d
3550	PR-P2-1C2-7130	Fab. & Ship Building Specialties Fab. - ASD	60.0d	22-Jul-26	20-Sep-26	795.0d
3551	PR-P2-1C2-7140	Delivery of Building Specialties on Site - ASD	0.0d		20-Sep-26	795.0d
3552	WBS - Wire Mesh Partitions Procurement - ASD		83.0d	29-Apr-26	25-Aug-26	147.0d
3553	PR-P2-1C2-760	Prep Wire Mesh Partitions Submittals (Contractor) - ASD	20.0d	29-Apr-26	27-May-26	146.0d
3554	PR-P2-1C2-765	Review & Submit Wire Mesh Partitions Submittals (HP) - ASD	10.0d	28-May-26	10-Jun-26	146.0d
3555	PR-P2-1C2-1050	Review & Approve Wire Mesh Partitions Submittals (HNTB) - ASD	10.0d	11-Jun-26	24-Jun-26	146.0d
3556	PR-P2-1C2-1055	Review & Approve Wire Mesh Partitions Submittals (HCAA) - ASD	15.0d	25-Jun-26	16-Jul-26	146.0d
3557	PR-P2-1C2-1070	Fab. & Ship Wire Mesh Partitions - ASD	40.0d	17-Jul-26	25-Aug-26	207.0d
3558	PR-P2-1C2-1950	Delivery of Wire Mesh Partitions on Site - ASD	0.0d		25-Aug-26	207.0d
3559	WBS - FF&E Procurement - ASD		206.0d	29-Apr-26	20-Feb-27	362.0d
3560	PR-P2-1C2-7270	Prep FF&E Submittals (Contractor) - ASD	30.0d	29-Apr-26	10-Jun-26	361.0d
3561	PR-P2-1C2-7280	Review & Submit FF&E Submittals (HP) - ASD	10.0d	11-Jun-26	24-Jun-26	361.0d
3562	PR-P2-1C2-7290	Review & Approve FF&E Submittals (HNTB) - ASD	10.0d	25-Jun-26	9-Jul-26	361.0d
3563	PR-P2-1C2-7300	Review & Approve FF&E Submittals (HCAA) - ASD	15.0d	10-Jul-26	30-Jul-26	361.0d
3564	PR-P2-1C2-7310	Fab. & Ship FF&E - ASD	200.0d	31-Jul-26	20-Feb-27	507.0d
3565	PR-P2-1C2-7320	Delivery of FF&E on Site - ASD	0.0d		20-Feb-27	507.0d
3566	WBS - Metal Canopies Procurement - ASD		97.0d	6-May-26	22-Sep-26	467.0d
3567	PR-P2-1C2-620	Prep Submit Metal Canopies Submittals (Contractor) - ASD	20.0d	6-May-26	3-Jun-26	467.0d
3568	PR-P2-1C2-625	Review & Submit Metal Canopies Submittals (HP) - ASD	10.0d	4-Jun-26	17-Jun-26	467.0d
3569	PR-P2-1C2-1030	Review & Approve Metal Canopies Submittals (HNTB) - ASD	10.0d	18-Jun-26	1-Jul-26	467.0d
3570	PR-P2-1C2-1035	Review & Approve Metal Canopies Submittals (HCAA) - ASD	15.0d	2-Jul-26	23-Jul-26	467.0d

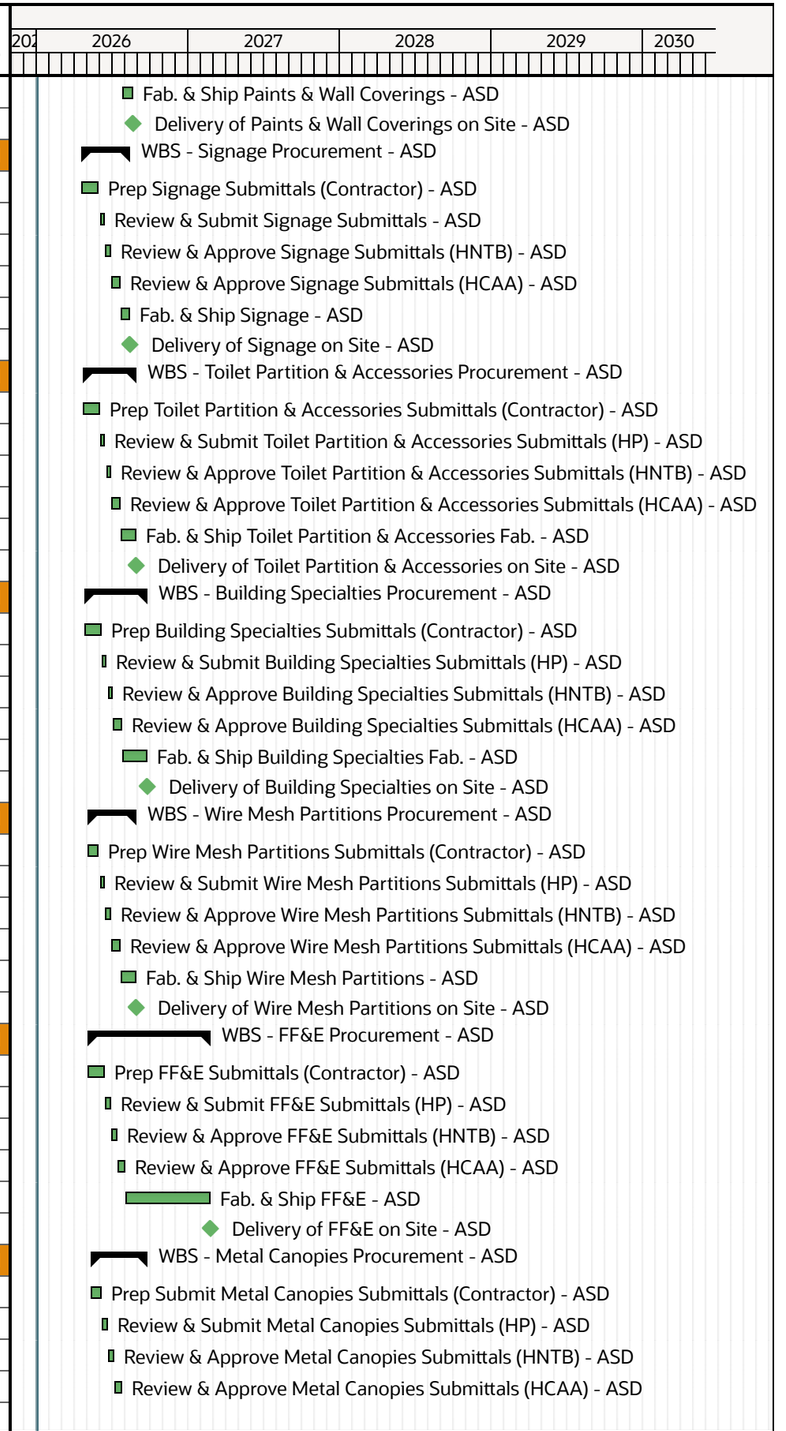


	ID	Name	Dur	Start	Finish	TF
3571	PR-P2-1C2-1160	Fab. & Ship Metal Canopies - ASD	60.0d	24-Jul-26	22-Sep-26	655.0d
3572	PR-P2-1C2-2140	Delivery of Metal Canopies on Site - ASD	0.0d		22-Sep-26	655.0d
3573	WBS - Window Coverings Procurement - ASD		121.0d	28-Apr-26	18-Oct-26	497.0d
3574	PR-P2-1C2-780	Prep Window Coverings Submittals (Contractor) - ASD	30.0d	28-Apr-26	9-Jun-26	497.0d
3575	PR-P2-1C2-785	Review & Submit Window Coverings Submittals (HP) - ASD	10.0d	10-Jun-26	23-Jun-26	497.0d
3576	PR-P2-1C2-1280	Review & Approve Window Coverings Submittals (HNTB) - ASD	10.0d	24-Jun-26	8-Jul-26	497.0d
3577	PR-P2-1C2-1285	Review & Approve Window Coverings Submittals (HCAA) - ASD	15.0d	9-Jul-26	29-Jul-26	497.0d
3578	PR-P2-1C2-1660	Fab. & Ship Window Coverings - ASD	80.0d	30-Jul-26	18-Oct-26	697.0d
3579	PR-P2-1C2-2280	Delivery of Window Coverings on Site - ASD	0.0d		18-Oct-26	697.0d
3580	WBS - Interior Plants & Planters Procurement - ASD		83.0d	30-Apr-26	26-Aug-26	489.0d
3581	PR-P2-1C2-740	Interior Plants & Planters Submittals (Contractor) - ASD	20.0d	30-Apr-26	28-May-26	489.0d
3582	PR-P2-1C2-745	Review & Submit Interior Plants & Planters Submittals (HP) - ASD	10.0d	29-May-26	11-Jun-26	489.0d
3583	PR-P2-1C2-1040	Review & Approve Interior Plants & Planters Submittals (HNTB) - ASD	10.0d	12-Jun-26	25-Jun-26	489.0d
3584	PR-P2-1C2-1045	Review & Approve Interior Plants & Planters Submittals (HCAA) - ASD	15.0d	26-Jun-26	17-Jul-26	489.0d
3585	PR-P2-1C2-1250	Fab. & Ship Interior Plants & Planters - ASD	40.0d	18-Jul-26	26-Aug-26	687.0d
3586	PR-P2-1C2-1980	Delivery of Interior Plants & Planters on Site - ASD	0.0d		26-Aug-26	687.0d
3587	WBS - Fencing Procurement - ASD		121.0d	23-Apr-26	13-Oct-26	443.0d
3588	PR-P2-1C2-560	Prep Fencing Submittals (Contractor) - ASD	30.0d	23-Apr-26	4-Jun-26	443.0d
3589	PR-P2-1C2-565	Review & Submit Fencing Submittals (HP) - ASD	10.0d	5-Jun-26	18-Jun-26	443.0d
3590	PR-P2-1C2-1100	Review & Approve Fencing Submittals (HNTB) - ASD	10.0d	19-Jun-26	2-Jul-26	443.0d
3591	PR-P2-1C2-1105	Review & Approve Fencing Submittals (HCAA) - ASD	15.0d	6-Jul-26	24-Jul-26	443.0d
3592	PR-P2-1C2-1490	Fab. & Ship Fencing - ASD	80.0d	25-Jul-26	13-Oct-26	621.0d
3593	PR-P2-1C2-2240	Delivery of Fencing on Site - ASD	0.0d		13-Oct-26	621.0d
3594	WBS - Bird Control Specialties Procurement - ASD		97.0d	4-May-26	20-Sep-26	466.0d
3595	PR-P2-1C2-7840	Prep Bird Control Specialties Submittals (Contractor) - ASD	31.0d	4-May-26	16-Jun-26	464.0d
3596	PR-P2-1C2-7850	Review & Submit Bird Control Specialties Submittals (HP) - ASD	10.0d	17-Jun-26	30-Jun-26	464.0d
3597	PR-P2-1C2-7860	Review & Approve Bird Control Specialties Submittals (HNTB) - ASD	10.0d	1-Jul-26	15-Jul-26	464.0d
3598	PR-P2-1C2-7870	Review & Approve Bird Control Specialties Submittals (HCAA) - ASD	15.0d	16-Jul-26	5-Aug-26	464.0d
3599	PR-P2-1C2-7880	Fab. & Ship Bird Control Specialties - ASD	45.0d	6-Aug-26	20-Sep-26	652.0d
3600	PR-P2-1C2-7890	Delivery of Bird Control Specialties on Site - ASD	0.0d		20-Sep-26	652.0d
3601	WBS - VDC Coordination		354.0d	7-Oct-25 A	1-Mar-27	162.0d
3602	PR-VDC-10	Kickoff Meeting - VDC Coordination	0.0d	7-Oct-25 A		
3603	WBS - Deep Underground - VDC Coordination		100.0d	7-Oct-25 A	28-Feb-26	184.0d
3604	PR-VDC-DU-300	Model, Coordinate & Sign-off Deep UG East - VDC Coordination	29.0d	7-Oct-25 A	14-Nov-25 A	
3605	PR-VDC-DU-310	Model, Coordinate & Sign-off Deep UG West - VDC Coordination	42.0d	21-Oct-25 A	19-Dec-25 A	
3606	WBS - Deep UG East VDC Coordination		28.0d	17-Nov-25 A	29-Dec-25	120.0d
3607	WBS - Mechanical Shop Drawings - Deep UG East VDC Coordination		27.0d	18-Nov-25 A	29-Dec-25	120.0d
3608	PR-VDC-DU-4080	Prep & Submit Deep UG East Mech. Shop Drawings	2.0d	18-Nov-25 A	19-Nov-25 A	
3609	PR-VDC-DU-4090	Review & Approve (HP) Deep UG East Mech. Shop Drawings	2.0d	20-Nov-25 A	21-Nov-25 A	
3610	PR-VDC-DU-4060	Review & Approve (HNTB) Deep UG East Mech. Shop Drawings	3.0d	21-Nov-25 A	25-Nov-25 A	
3611	PR-VDC-DU-4070	Review & Approve (HCAA) Deep UG East Mech. Shop Drawings	6.0d	26-Nov-25 A	5-Dec-25 A	
3612	PR-VDC-DU-4100	Fab. & Ship Deep UG East Mech. Shop Drawings	21.0d	8-Dec-25 A	29-Dec-25	168.0d

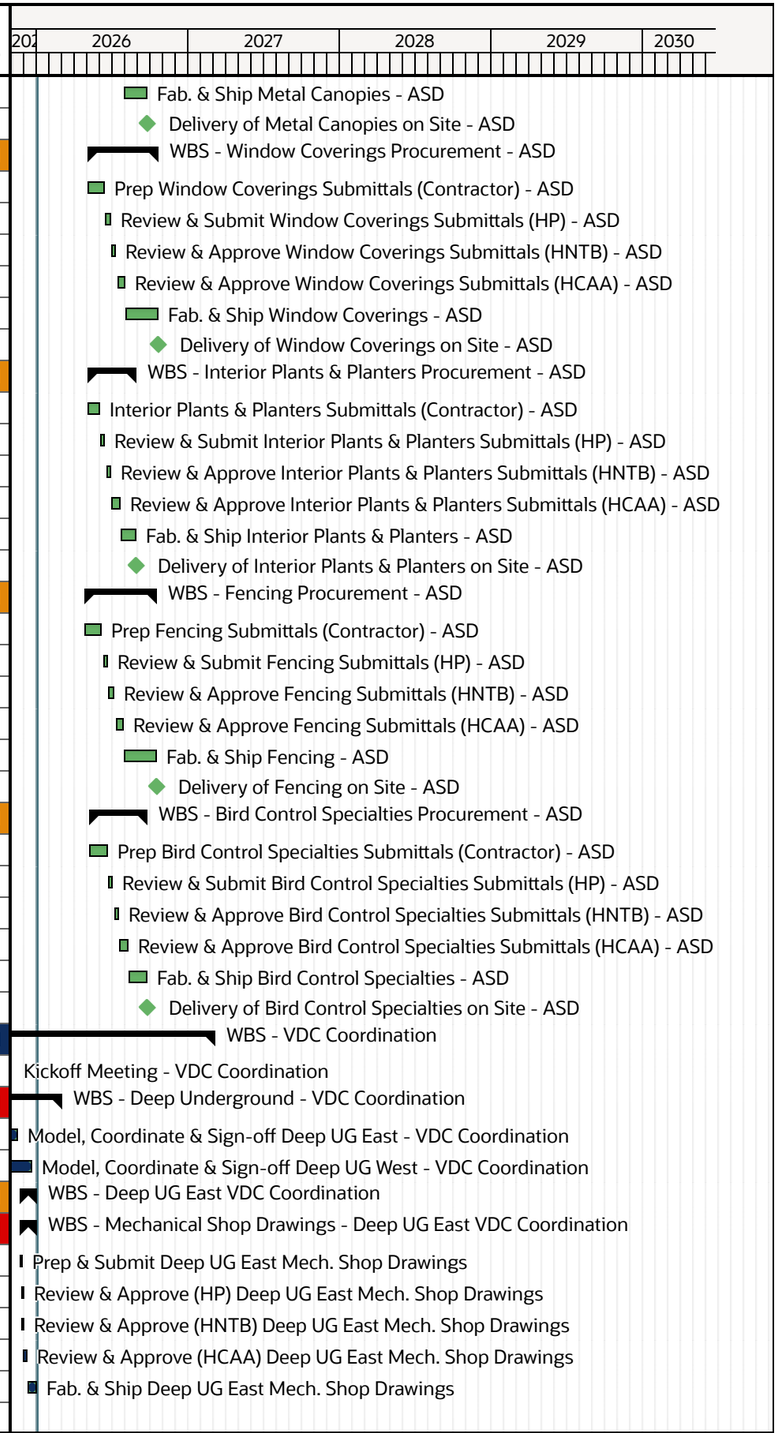


	ID	Name	Dur	Start	Finish	TF
3613	WBS - Electrical & Low Voltage Shop Drawings - Deep UG East VDC Coordination		15.0d	17-Nov-25 A	9-Dec-25 A	
3614	PR-VDC-DU-4160	Prep & Submit Deep UG East Elec. Shop Drawings	5.0d	17-Nov-25 A	21-Nov-25 A	
3615	PR-VDC-DU-4170	Review & Approve (HP) Deep UG East Elec.Shop Drawings	5.0d	24-Nov-25 A	2-Dec-25 A	
3616	PR-VDC-DU-4180	Review & Approve (HNTB) Deep UG East Elec. Shop Drawings	5.0d	24-Nov-25 A	2-Dec-25 A	
3617	PR-VDC-DU-4190	Review & Approve (HCAA) Deep UG East Elec. Shop Drawings	2.0d	3-Dec-25 A	4-Dec-25 A	
3618	PR-VDC-DU-4200	Fab. & Ship Deep UG East Elec. Shop Drawings	6.0d	4-Dec-25 A	9-Dec-25 A	
3619	WBS - Plumbing Shop Drawings - Deep UG East VDC Coordination		23.0d	18-Nov-25 A	22-Dec-25 A	
3620	PR-VDC-DU-4110	Prep & Submit Deep UG East Plumbing Shop Drawings	2.0d	18-Nov-25 A	19-Nov-25 A	
3621	PR-VDC-DU-4120	Review & Approve (HP) Deep UG East Plumbing Shop Drawings	2.0d	20-Nov-25 A	21-Nov-25 A	
3622	PR-VDC-DU-4130	Review & Approve (HNTB) Deep UG East Plumbing Shop Drawings	3.0d	21-Nov-25 A	25-Nov-25 A	
3623	PR-VDC-DU-4140	Review & Approve (HCAA) Deep UG East Plumbing Shop Drawings	6.0d	26-Nov-25 A	5-Dec-25 A	
3624	PR-VDC-DU-4150	Fab. & Ship Deep UG East Plumbing Shop Drawings	17.0d	6-Dec-25 A	22-Dec-25 A	
3625	WBS - Deep UG West VDC Coordination		44.0d	29-Dec-25	28-Feb-26	184.0d
3626	WBS - Plumbing Shop Drawings - Deep UG West VDC Coordination		44.0d	29-Dec-25	28-Feb-26	73.0d
3627	PR-VDC-DU-4360	Prep & Submit Deep UG West Plumbing Shop Drawings	10.0d	29-Dec-25	12-Jan-26	73.0d
3628	PR-VDC-DU-4370	Review & Approve (HP) Deep UG West Plumbing Shop Drawings	5.0d	13-Jan-26	19-Jan-26	73.0d
3629	PR-VDC-DU-4380	Review & Approve (HNTB) Deep UG West Plumbing Shop Drawings	10.0d	20-Jan-26	2-Feb-26	73.0d
3630	PR-VDC-DU-4390	Review & Approve (HCAA) Deep UG West Plumbing Shop Drawings	15.0d	3-Feb-26	23-Feb-26	73.0d
3631	PR-VDC-DU-4400	Fab. & Ship Deep UG West Plumbing Shop Drawings	5.0d	24-Feb-26	28-Feb-26	102.0d
3632	WBS - Electrical & Low Voltage Shop Drawings - Deep UG West VDC Coordination		40.0d	29-Dec-25	23-Feb-26	188.0d
3633	PR-VDC-DU-4410	Prep & Submit Deep UG West Elec. Shop Drawings	10.0d	29-Dec-25	12-Jan-26	91.0d
3634	PR-VDC-DU-4420	Review & Approve (HP) Deep UG West Elec.Shop Drawings	5.0d	13-Jan-26	19-Jan-26	188.0d
3635	PR-VDC-DU-4430	Review & Approve (HNTB) Deep UG West Elec.Shop Drawings	10.0d	20-Jan-26	2-Feb-26	188.0d
3636	PR-VDC-DU-4440	Review & Approve (HCAA) Deep UG West Elec. Shop Drawings	15.0d	3-Feb-26	23-Feb-26	188.0d
3637	PR-VDC-DU-4450	Deep UG West Elec. Shop Drawings Approved	0.0d		23-Feb-26	263.0d
3638	WBS - Shallow Underground - VDC Coordination		60.0d	29-Dec-25	23-Mar-26	239.0d
3639	PR-VDC-ST-400	Model, Coordinate & Sign-off Shallow UG East - VDC Coordination	21.0d	29-Dec-25	27-Jan-26	147.0d
3640	PR-VDC-ST-410	Model, Coordinate & Sign-off Shallow UG West - VDC Coordination	21.0d	20-Jan-26	17-Feb-26	239.0d
3641	WBS - Shallow UG East - VDC Coordination		24.0d	28-Jan-26	2-Mar-26	147.0d
3642	WBS - Mechanical Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d
3643	PR-VDC-SU-4580	Prep & Submit Shallow UG East Mech. Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
3644	PR-VDC-SU-4590	Review & Approve (HP) Shallow UG East Mech. Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
3645	PR-VDC-SU-4560	Review & Approve (HNTB) Shallow UG East Mech. Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
3646	PR-VDC-SU-4570	Review & Approve (HCAA) Shallow UG East Mech. Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
3647	PR-VDC-SU-4600	Shallow UG East Mech. Shop Drawings Approved	0.0d		25-Feb-26	211.0d
3648	WBS - Electrical Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d
3649	PR-VDC-SU-4660	Prep & Submit Shallow UG East Elec. Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
3650	PR-VDC-SU-4670	Review & Approve (HP) Shallow UG East Elec.Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
3651	PR-VDC-SU-4680	Review & Approve (HNTB) Shallow UG East Elec. Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
3652	PR-VDC-SU-4690	Review & Approve (HCAA) Shallow UG East Elec. Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
3653	PR-VDC-SU-4700	Shallow UG East Elec. Shop Drawings Approved	0.0d		25-Feb-26	211.0d
3654	WBS - Low Voltage Shop Drawings - Shallow UG East - VDC Coordination		21.0d	28-Jan-26	25-Feb-26	150.0d

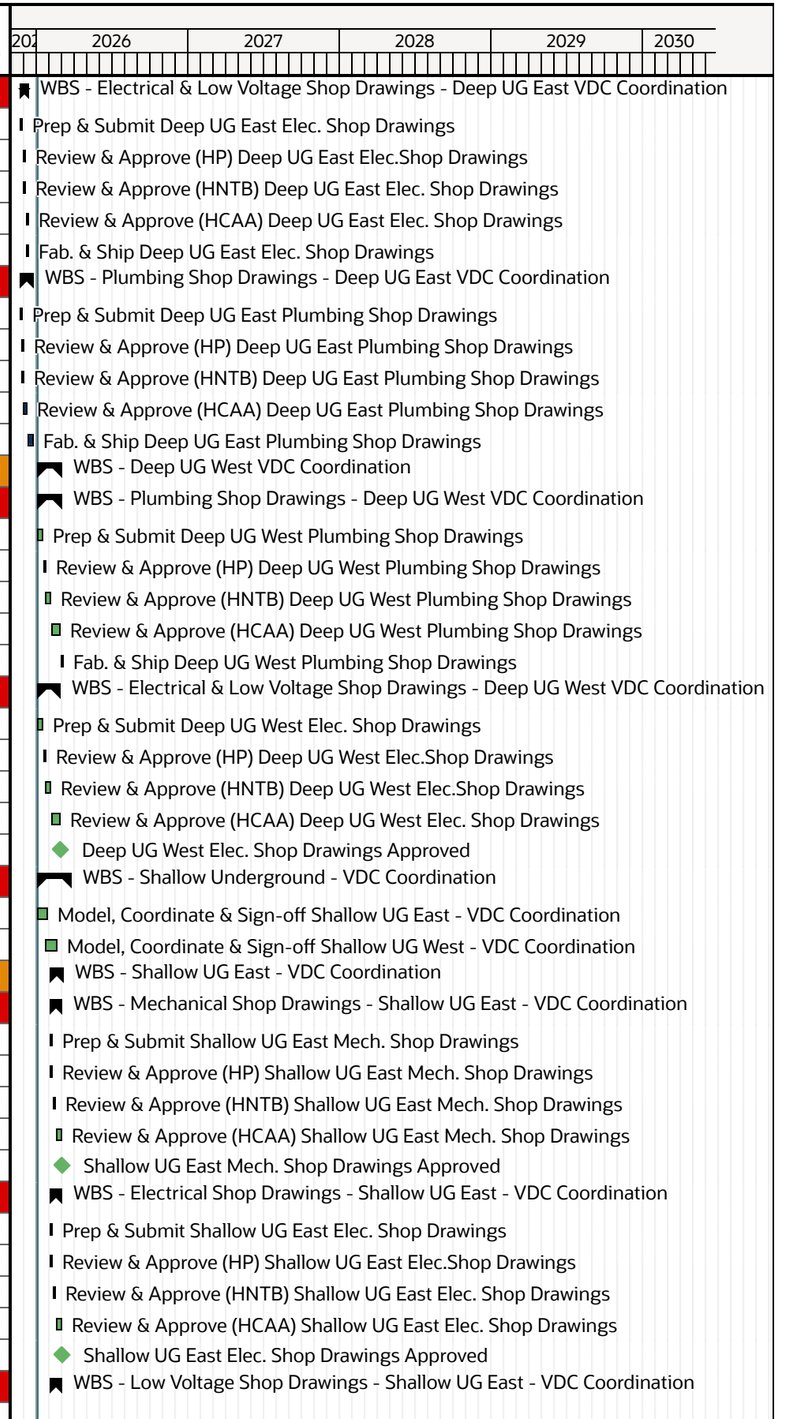

	ID	Name	Dur	Start	Finish	TF
3655	PR-VDC-SU-4710	Prep & Submit Shallow UG East Low Voltage Shop Drawings	1.0d	28-Jan-26	28-Jan-26	150.0d
3656	PR-VDC-SU-4720	Review & Approve (HP) Shallow UG East Low Voltage Shop Drawings	5.0d	29-Jan-26	4-Feb-26	150.0d
3657	PR-VDC-SU-4730	Review & Approve (HNTB) Shallow UG East Low Voltage Shop Drawings	5.0d	5-Feb-26	11-Feb-26	150.0d
3658	PR-VDC-SU-4740	Review & Approve (HCAA) Shallow UG East Low Voltage Shop Drawings	10.0d	12-Feb-26	25-Feb-26	150.0d
3659	PR-VDC-SU-4750	Shallow UG East Low Voltage Shop Drawings Approved	0.0d		25-Feb-26	211.0d
3660	WBS - Plumbing Shop Drawings - Shallow UG East - VDC Coordination		24.0d	28-Jan-26	2-Mar-26	147.0d
3661	PR-VDC-SU-4610	Prep & Submit Shallow UG East Plumbing Shop Drawings	1.0d	28-Jan-26	28-Jan-26	147.0d
3662	PR-VDC-SU-4620	Review & Approve (HP) Shallow UG East Plumbing Shop Drawings	5.0d	29-Jan-26	4-Feb-26	147.0d
3663	PR-VDC-SU-4630	Review & Approve (HNTB) Shallow UG East Plumbing Shop Drawings	5.0d	5-Feb-26	11-Feb-26	147.0d
3664	PR-VDC-SU-4640	Review & Approve (HCAA) Shallow UG East Plumbing Shop Drawings	10.0d	12-Feb-26	25-Feb-26	147.0d
3665	PR-VDC-SU-4650	Shallow UG East Plumbing Shop Drawings Approved	5.0d	26-Feb-26	2-Mar-26	206.0d
3666	WBS - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
3667	WBS - Mechanical Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
3668	PR-VDC-SU-4830	Prep & Submit Shallow UG West Mech. Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
3669	PR-VDC-SU-4840	Review & Approve (HP) Shallow UG West Mech. Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
3670	PR-VDC-SU-4810	Review & Approve (HNTB) Shallow UG West Mech. Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
3671	PR-VDC-SU-4820	Review & Approve (HCAA) Shallow UG West Mech. Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
3672	PR-VDC-SU-4850	Fab. & Ship Shallow UG West Mech. Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
3673	WBS - Electrical Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
3674	PR-VDC-SU-4910	Prep & Submit Shallow UG West Elec. Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
3675	PR-VDC-SU-4920	Review & Approve (HP) Shallow UG West Elec.Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
3676	PR-VDC-SU-4930	Review & Approve (HNTB) Shallow UG West Elec. Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
3677	PR-VDC-SU-4940	Review & Approve (HCAA) Shallow UG West Elec. Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
3678	PR-VDC-SU-4950	Fab. & Ship Shallow UG West Elec. Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
3679	WBS - Low Voltage Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
3680	PR-VDC-SU-4960	Prep & Submit Shallow UG West Low Voltage Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
3681	PR-VDC-SU-4970	Review & Approve (HP) Shallow UG West Low Voltage Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
3682	PR-VDC-SU-4980	Review & Approve (HNTB) Shallow UG West Low Voltage Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
3683	PR-VDC-SU-4990	Review & Approve (HCAA) Shallow UG West Low Voltage Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
3684	PR-VDC-SU-5000	Fab. & Ship Shallow UG West Low Voltage Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
3685	WBS - Plumbing Shop Drawings - Shallow UG West - VDC Coordination		24.0d	18-Feb-26	23-Mar-26	239.0d
3686	PR-VDC-SU-4860	Prep & Submit Shallow UG West Plumbing Shop Drawings	1.0d	18-Feb-26	18-Feb-26	239.0d
3687	PR-VDC-SU-4870	Review & Approve (HP) Shallow UG West Plumbing Shop Drawings	5.0d	19-Feb-26	25-Feb-26	239.0d
3688	PR-VDC-SU-4880	Review & Approve (HNTB) Shallow UG West Plumbing Shop Drawings	5.0d	26-Feb-26	4-Mar-26	239.0d
3689	PR-VDC-SU-4890	Review & Approve (HCAA) Shallow UG West Plumbing Shop Drawings	10.0d	5-Mar-26	18-Mar-26	239.0d
3690	PR-VDC-SU-4900	Fab. & Ship Shallow UG West Plumbing Shop Drawings	5.0d	19-Mar-26	23-Mar-26	336.0d
3691	WBS - Overhead - VDC Coordination		298.0d	29-Dec-25	1-Mar-27	162.0d
3692	PR-VDC-ST-10	Model, Coordinate & Sign-off Level 1, Area 1 - OH VDC Coordination	35.0d	29-Dec-25	16-Feb-26	23.0d
3693	PR-VDC-ST-20	Model, Coordinate & Sign-off Level 1, Area 2 - OH VDC Coordination	40.0d	5-Jan-26	27-Feb-26	23.0d
3694	PR-VDC-ST-70	Model, Coordinate & Sign-off Level 2, Area 8 - OH VDC Coordination	45.0d	2-Feb-26	3-Apr-26	23.0d
3695	PR-VDC-ST-150	Model, Coordinate & Sign-off Level 3, Club/Nov. Steel Area - OH VDC Coordina...	25.0d	9-Mar-26	10-Apr-26	23.0d
3696	PR-VDC-ST-80	Model, Coordinate & Sign-off Level 2&3, Area 9 - OH VDC Coordination	30.0d	30-Mar-26	8-May-26	23.0d

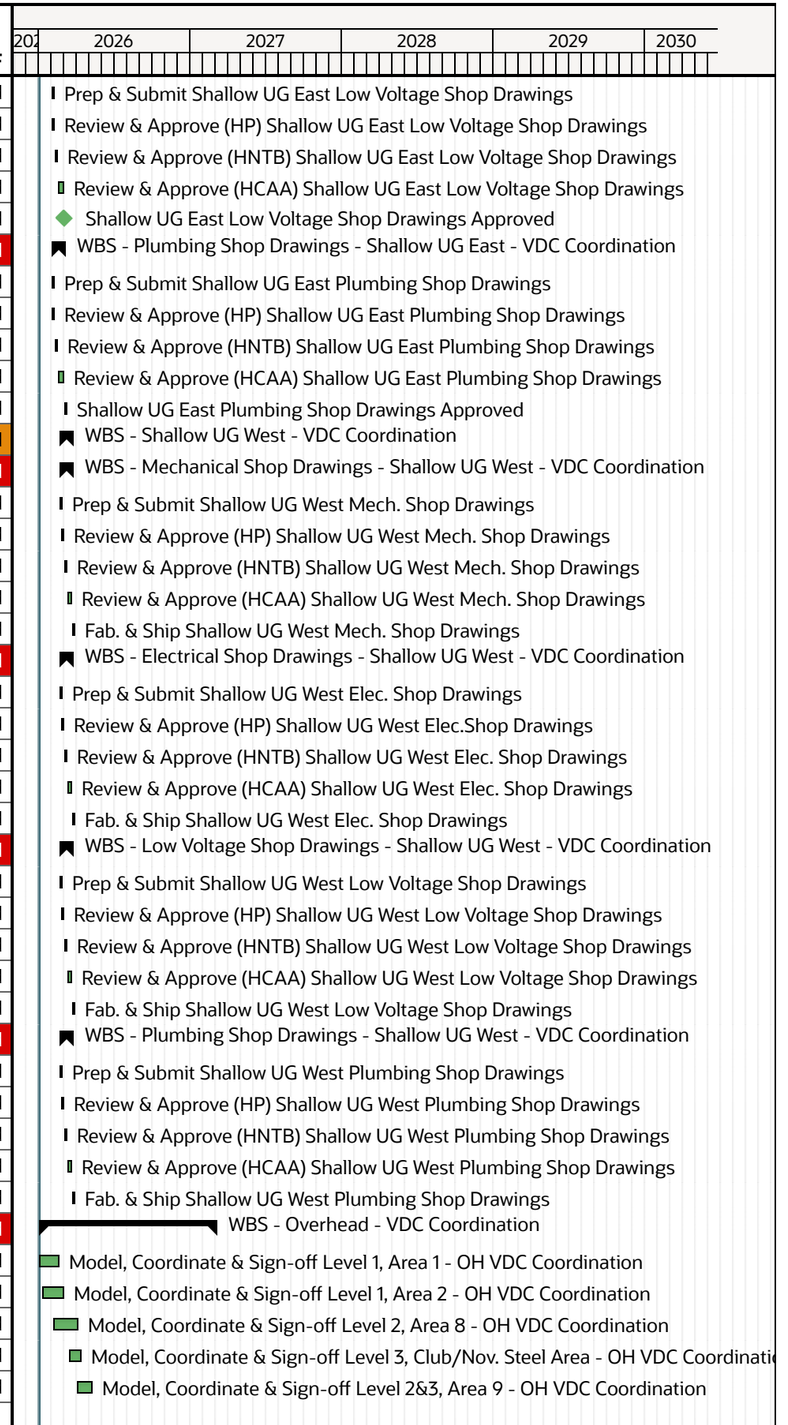

	ID	Name	Dur	Start	Finish	TF
3697	PR-VDC-ST-160	Model, Coordinate & Sign-off Level 3, Club 1&2 Area - OH VDC Coordination	15.0d	6-Apr-26	24-Apr-26	36.0d
3698	PR-VDC-ST-30	Model, Coordinate & Sign-off Level 1, Area 3 - OH VDC Coordination	40.0d	13-Apr-26	8-Jun-26	36.0d
3699	PR-VDC-ST-40	Model, Coordinate & Sign-off Level 1, Area 4 - OH VDC Coordination	40.0d	11-May-26	7-Jul-26	36.0d
3700	PR-VDC-ST-50	Model, Coordinate & Sign-off Level 1, Area 5 - OH VDC Coordination	30.0d	9-Jun-26	21-Jul-26	36.0d
3701	PR-VDC-ST-90	Model, Coordinate & Sign-off Level 2, Concessions - OH VDC Coordination	35.0d	23-Jun-26	11-Aug-26	36.0d
3702	PR-VDC-ST-100	Model, Coordinate & Sign-off Level 3, Area 10 - OH VDC Coordination	25.0d	15-Jul-26	18-Aug-26	36.0d
3703	PR-VDC-ST-110	Model, Coordinate & Sign-off Level 3, Area 11 - OH VDC Coordination	40.0d	22-Jul-26	16-Sep-26	36.0d
3704	PR-VDC-ST-60	Model, Coordinate & Sign-off Level 1, Areas 6&7 - OH VDC Coordination	40.0d	19-Aug-26	14-Oct-26	36.0d
3705	PR-VDC-ST-120	Model, Coordinate & Sign-off Level 3, Area 12 - OH VDC Coordination	30.0d	17-Sep-26	28-Oct-26	79.0d
3706	PR-VDC-ST-130	Model, Coordinate & Sign-off Level 3, Area 13 - OH VDC Coordination	35.0d	1-Oct-26	18-Nov-26	88.0d
3707	PR-VDC-ST-140	Model, Coordinate & Sign-off Level 3, Area 14 - OH VDC Coordination	35.0d	22-Oct-26	11-Dec-26	88.0d
3708	WBS - Level 1, Area 1 - OH VDC Coordination		48.0d	17-Feb-26	23-Apr-26	103.0d
3709	WBS - Mechanical Shop Drawings - Level 1, Area 1		43.0d	17-Feb-26	16-Apr-26	108.0d
3710	PR-VDC-L1A1-10	Prep & Submit Level 1, Area 1 Mech. Shop Drawings	10.0d	17-Feb-26	2-Mar-26	108.0d
3711	PR-VDC-L1A1-20	Review & Approve (HP) Level 1, Area 1 Mech. Shop Drawings	5.0d	3-Mar-26	9-Mar-26	108.0d
3712	PR-VDC-L1A1-30	Review & Approve (HNTB) Level 1, Area 1 Mech. Shop Drawings	10.0d	10-Mar-26	23-Mar-26	108.0d
3713	PR-VDC-L1A1-40	Review & Approve (HCAA) Level 1, Area 1 Mech. Shop Drawings	10.0d	24-Mar-26	6-Apr-26	108.0d
3714	PR-VDC-L1A1-50	Fab. & Ship Level 1, Area 1 Mech. Shop Drawings	10.0d	7-Apr-26	16-Apr-26	151.0d
3715	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 1		48.0d	17-Feb-26	23-Apr-26	103.0d
3716	PR-VDC-L1A1-60	Prep & Submit Level 1, Area 1 Fire Sprinkler Shop Drawings	10.0d	17-Feb-26	2-Mar-26	103.0d
3717	PR-VDC-L1A1-70	Review & Approve (HP) Level 1, Area 1 Fire Sprinkler Shop Drawings	5.0d	3-Mar-26	9-Mar-26	103.0d
3718	PR-VDC-L1A1-80	Review & Approve (HNTB) Level 1, Area 1 Fire Sprinkler Shop Drawings	10.0d	10-Mar-26	23-Mar-26	103.0d
3719	PR-VDC-L1A1-90	Review & Approve (HCAA) Level 1, Area 1 Fire Sprinkler Shop Drawings	15.0d	24-Mar-26	13-Apr-26	103.0d
3720	PR-VDC-L1A1-100	Fab. & Ship Level 1, Area 1 Fire Sprinkler Shop Drawings	10.0d	14-Apr-26	23-Apr-26	144.0d
3721	WBS - Electrical Shop Drawings - Level 1, Area 1		40.0d	17-Feb-26	13-Apr-26	111.0d
3722	PR-VDC-L1A1-160	Prep & Submit Level 1, Area 1 Elec. Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
3723	PR-VDC-L1A1-170	Review & Approve (HP) Level 1, Area 1 Elec.Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
3724	PR-VDC-L1A1-180	Review & Approve (HNTB) Level 1, Area 1 Elec. Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
3725	PR-VDC-L1A1-190	Review & Approve (HCAA) Level 1, Area 1 Elec. Shop Drawings	15.0d	24-Mar-26	13-Apr-26	111.0d
3726	PR-VDC-L1A1-200	Level 1, Area 1 Elec. Shop Drawings Approved	0.0d		13-Apr-26	154.0d
3727	WBS - Low Voltage Shop Drawings - Level 1, Area 1		40.0d	17-Feb-26	13-Apr-26	111.0d
3728	PR-VDC-L1A1-210	Prep & Submit Level 1, Area 1 Low Voltage Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
3729	PR-VDC-L1A1-220	Review & Approve (HP) Level 1, Area 1 Low Voltage Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
3730	PR-VDC-L1A1-230	Review & Approve (HNTB) Level 1, Area 1 Low Voltage Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
3731	PR-VDC-L1A1-240	Review & Approve (HCAA) Level 1, Area 1 Low Voltage Shop Drawings	15.0d	24-Mar-26	13-Apr-26	111.0d
3732	PR-VDC-L1A1-250	Level 1, Area 1 Low Voltage Shop Drawings Approved	0.0d		13-Apr-26	154.0d
3733	WBS - Plumbing Shop Drawings - Level 1, Area 1		40.0d	17-Feb-26	13-Apr-26	111.0d
3734	PR-VDC-L1A1-110	Prep & Submit Level 1, Area 1 Plumbing Shop Drawings	10.0d	17-Feb-26	2-Mar-26	111.0d
3735	PR-VDC-L1A1-120	Review & Approve (HP) Level 1, Area 1 Plumbing Shop Drawings	5.0d	3-Mar-26	9-Mar-26	111.0d
3736	PR-VDC-L1A1-130	Review & Approve (HNTB) Level 1, Area 1 Plumbing Shop Drawings	10.0d	10-Mar-26	23-Mar-26	111.0d
3737	PR-VDC-L1A1-140	Review & Approve (HCAA) Level 1, Area 1 Plumbing Shop Drawings	15.0d	24-Mar-26	13-Apr-26	111.0d
3738	PR-VDC-L1A1-150	Level 1, Area 1 Plumbing Shop Drawings Approved	0.0d		13-Apr-26	154.0d

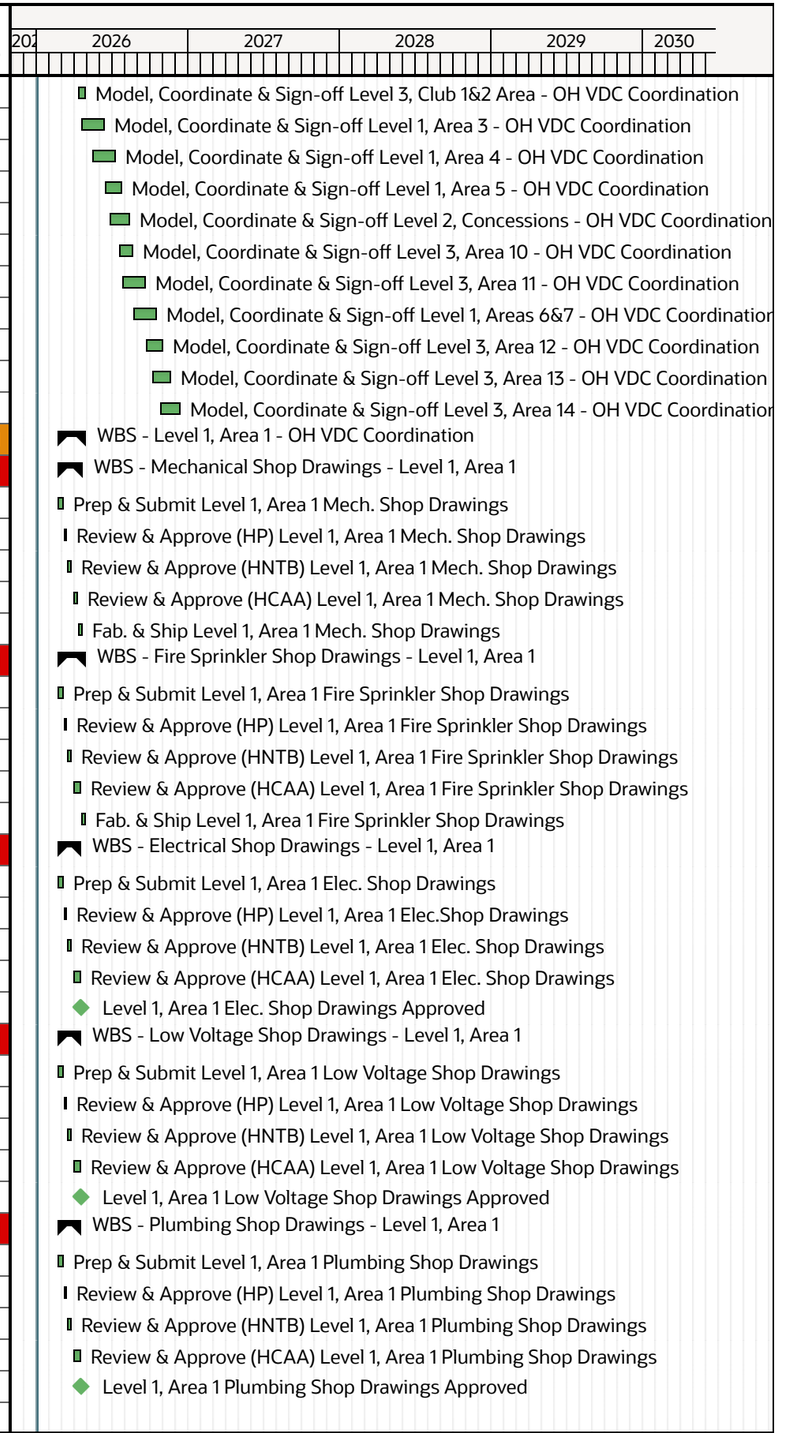

ID	Name	Dur	Start	Finish	TF
3739	WBS - Level 1, Area 2 - OH VDC Coordination	46.0d	2-Mar-26	4-May-26	96.0d
3740	WBS - Mechanical Shop Drawings - Level 1, Area 2	46.0d	2-Mar-26	4-May-26	96.0d
3741	PR-VDC-L1A2-330	Prep & Submit Level 1, Area 2 Mech. Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
3742	PR-VDC-L1A2-340	Review & Approve (HP) Level 1, Area 2 Mech. Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
3743	PR-VDC-L1A2-310	Review & Approve (HNTB) Level 1, Area 2 Mech. Shop Drawings	10.0d	23-Mar-26	3-Apr-26	94.0d
3744	PR-VDC-L1A2-320	Review & Approve (HCAA) Level 1, Area 2 Mech. Shop Drawings	15.0d	6-Apr-26	24-Apr-26	94.0d
3745	PR-VDC-L1A2-350	Fab. & Ship Level 1, Area 2 Mech. Shop Drawings	10.0d	25-Apr-26	4-May-26	133.0d
3746	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 2	46.0d	2-Mar-26	4-May-26	96.0d
3747	PR-VDC-L1A2-260	Prep & Submit Level 1, Area 2 Fire Sprinkler Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
3748	PR-VDC-L1A2-270	Review & Approve (HP) Level 1, Area 2 Fire Sprinkler Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
3749	PR-VDC-L1A2-280	Review & Approve (HNTB) Level 1, Area 2 Fire Sprinkler Shop Drawings	10.0d	23-Mar-26	3-Apr-26	94.0d
3750	PR-VDC-L1A2-290	Review & Approve (HCAA) Level 1, Area 2 Fire Sprinkler Shop Drawings	15.0d	6-Apr-26	24-Apr-26	94.0d
3751	PR-VDC-L1A2-300	Fab. & Ship Level 1, Area 2 Fire Sprinkler Shop Drawings	10.0d	25-Apr-26	4-May-26	133.0d
3752	WBS - Plumbing Shop Drawings - Level 1, Area 2	46.0d	2-Mar-26	4-May-26	96.0d
3753	PR-VDC-L1A2-360	Prep & Submit Level 1, Area 2 Plumbing Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
3754	PR-VDC-L1A2-370	Review & Approve (HP) Level 1, Area 2 Plumbing Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
3755	PR-VDC-L1A2-380	Review & Approve (HNTB) Level 1, Area 2 Plumbing Shop Drawings	10.0d	23-Mar-26	3-Apr-26	94.0d
3756	PR-VDC-L1A2-390	Review & Approve (HCAA) Level 1, Area 2 Plumbing Shop Drawings	15.0d	6-Apr-26	24-Apr-26	94.0d
3757	PR-VDC-L1A2-400	Fab. & Ship Level 1, Area 2 Plumbing Shop Drawings	10.0d	25-Apr-26	4-May-26	133.0d
3758	WBS - Electrical Shop Drawings - Level 1, Area 2	46.0d	2-Mar-26	4-May-26	96.0d
3759	PR-VDC-L1A2-410	Prep & Submit Level 1, Area 2 Elec. Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
3760	PR-VDC-L1A2-420	Review & Approve (HP) Level 1, Area 2 Elec.Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
3761	PR-VDC-L1A2-430	Review & Approve (HNTB) Level 1, Area 2 Elec. Shop Drawings	10.0d	23-Mar-26	3-Apr-26	94.0d
3762	PR-VDC-L1A2-440	Review & Approve (HCAA) Level 1, Area 2 Elec. Shop Drawings	15.0d	6-Apr-26	24-Apr-26	94.0d
3763	PR-VDC-L1A2-450	Fab. & Ship Level 1, Area 2 Elec. Shop Drawings	10.0d	25-Apr-26	4-May-26	133.0d
3764	WBS - Low Voltage Shop Drawings - Level 1, Area 2	46.0d	2-Mar-26	4-May-26	96.0d
3765	PR-VDC-L1A2-460	Prep & Submit Level 1, Area 2 Low Voltage Shop Drawings	10.0d	2-Mar-26	13-Mar-26	94.0d
3766	PR-VDC-L1A2-470	Review & Approve (HP) Level 1, Area 2 Low Voltage Shop Drawings	5.0d	16-Mar-26	20-Mar-26	94.0d
3767	PR-VDC-L1A2-480	Review & Approve (HNTB) Level 1, Area 2 Low Voltage Shop Drawings	10.0d	23-Mar-26	3-Apr-26	94.0d
3768	PR-VDC-L1A2-490	Review & Approve (HCAA) Level 1, Area 2 Low Voltage Shop Drawings	15.0d	6-Apr-26	24-Apr-26	94.0d
3769	PR-VDC-L1A2-500	Fab. & Ship Level 1, Area 2 Low Voltage Shop Drawings	10.0d	25-Apr-26	4-May-26	133.0d
3770	WBS - Level 1, Area 3 - OH VDC Coordination	38.0d	9-Jun-26	2-Aug-26	81.0d
3771	WBS - Mechanical Shop Drawings - Level 1, Area 3	38.0d	9-Jun-26	2-Aug-26	81.0d
3772	PR-VDC-L1A3-580	Prep & Submit Level 1, Area 3 Mech. Shop Drawings	10.0d	9-Jun-26	22-Jun-26	81.0d
3773	PR-VDC-L1A3-590	Review & Approve (HP) Level 1, Area 3 Mech. Shop Drawings	5.0d	23-Jun-26	29-Jun-26	81.0d
3774	PR-VDC-L1A3-560	Review & Approve (HNTB) Level 1, Area 3 Mech. Shop Drawings	5.0d	30-Jun-26	7-Jul-26	81.0d
3775	PR-VDC-L1A3-570	Review & Approve (HCAA) Level 1, Area 3 Mech. Shop Drawings	15.0d	8-Jul-26	28-Jul-26	81.0d
3776	PR-VDC-L1A3-600	Fab. & Ship Level 1, Area 3 Mech. Shop Drawings	5.0d	29-Jul-26	2-Aug-26	113.0d
3777	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 3	38.0d	9-Jun-26	2-Aug-26	81.0d
3778	PR-VDC-L1A3-510	Prep & Submit Level 1, Area 3 Fire Sprinkler Shop Drawings	10.0d	9-Jun-26	22-Jun-26	81.0d
3779	PR-VDC-L1A3-520	Review & Approve (HP) Level 1, Area 3 Fire Sprinkler Shop Drawings	5.0d	23-Jun-26	29-Jun-26	81.0d
3780	PR-VDC-L1A3-530	Review & Approve (HNTB) Level 1, Area 3 Fire Sprinkler Shop Drawings	5.0d	30-Jun-26	7-Jul-26	81.0d




	ID	Name	Dur	Start	Finish	TF
3781	PR-VDC-L1A3-540	Review & Approve (HCAA) Level 1, Area 3 Fire Sprinkler Shop Drawings	15.0d	8-Jul-26	28-Jul-26	81.0d
3782	PR-VDC-L1A3-550	Fab. & Ship Level 1, Area 3 Fire Sprinkler Shop Drawings	5.0d	29-Jul-26	2-Aug-26	113.0d
3783	WBS - Plumbing Shop Drawings - Level 1, Area 3		38.0d	9-Jun-26	2-Aug-26	81.0d
3784	PR-VDC-L1A3-610	Prep & Submit Level 1, Area 3 Plumbing Shop Drawings	10.0d	9-Jun-26	22-Jun-26	81.0d
3785	PR-VDC-L1A3-620	Review & Approve (HP) Level 1, Area 3 Plumbing Shop Drawings	5.0d	23-Jun-26	29-Jun-26	81.0d
3786	PR-VDC-L1A3-630	Review & Approve (HNTB) Level 1, Area 3 Plumbing Shop Drawings	5.0d	30-Jun-26	7-Jul-26	81.0d
3787	PR-VDC-L1A3-640	Review & Approve (HCAA) Level 1, Area 3 Plumbing Shop Drawings	15.0d	8-Jul-26	28-Jul-26	81.0d
3788	PR-VDC-L1A3-650	Fab. & Ship Level 1, Area 3 Plumbing Shop Drawings	5.0d	29-Jul-26	2-Aug-26	113.0d
3789	WBS - Electrical Shop Drawings - Level 1, Area 3		38.0d	9-Jun-26	2-Aug-26	81.0d
3790	PR-VDC-L1A3-660	Prep & Submit Level 1, Area 3 Elec. Shop Drawings	10.0d	9-Jun-26	22-Jun-26	81.0d
3791	PR-VDC-L1A3-670	Review & Approve (HP) Level 1, Area 3 Elec.Shop Drawings	5.0d	23-Jun-26	29-Jun-26	81.0d
3792	PR-VDC-L1A3-680	Review & Approve (HNTB) Level 1, Area 3 Elec. Shop Drawings	5.0d	30-Jun-26	7-Jul-26	81.0d
3793	PR-VDC-L1A3-690	Review & Approve (HCAA) Level 1, Area 3 Elec. Shop Drawings	15.0d	8-Jul-26	28-Jul-26	81.0d
3794	PR-VDC-L1A3-700	Fab. & Ship Level 1, Area 3 Elec. Shop Drawings	5.0d	29-Jul-26	2-Aug-26	113.0d
3795	WBS - Low Voltage Shop Drawings - Level 1, Area 3		38.0d	9-Jun-26	2-Aug-26	81.0d
3796	PR-VDC-L1A3-710	Prep & Submit Level 1, Area 3 Low Voltage Shop Drawings	10.0d	9-Jun-26	22-Jun-26	81.0d
3797	PR-VDC-L1A3-720	Review & Approve (HP) Level 1, Area 3 Low Voltage Shop Drawings	5.0d	23-Jun-26	29-Jun-26	81.0d
3798	PR-VDC-L1A3-730	Review & Approve (HNTB) Level 1, Area 3 Low Voltage Shop Drawings	5.0d	30-Jun-26	7-Jul-26	81.0d
3799	PR-VDC-L1A3-740	Review & Approve (HCAA) Level 1, Area 3 Low Voltage Shop Drawings	15.0d	8-Jul-26	28-Jul-26	81.0d
3800	PR-VDC-L1A3-750	Fab. & Ship Level 1, Area 3 Low Voltage Shop Drawings	5.0d	29-Jul-26	2-Aug-26	113.0d
3801	WBS - Level 1, Area 4 - OH VDC Coordination		54.0d	8-Jul-26	22-Sep-26	68.0d
3802	WBS - Mechanical Shop Drawings - Level 1, Area 4		54.0d	8-Jul-26	22-Sep-26	68.0d
3803	PR-VDC-L1A4-830	Prep & Submit Level 1, Area 4 Mech. Shop Drawings	10.0d	8-Jul-26	21-Jul-26	68.0d
3804	PR-VDC-L1A4-840	Review & Approve (HP) Level 1, Area 4 Mech. Shop Drawings	5.0d	22-Jul-26	28-Jul-26	68.0d
3805	PR-VDC-L1A4-810	Review & Approve (HNTB) Level 1, Area 4 Mech. Shop Drawings	10.0d	29-Jul-26	11-Aug-26	68.0d
3806	PR-VDC-L1A4-820	Review & Approve (HCAA) Level 1, Area 4 Mech. Shop Drawings	15.0d	12-Aug-26	1-Sep-26	68.0d
3807	PR-VDC-L1A4-850	Fab. & Ship Level 1, Area 4 Mech. Shop Drawings	20.0d	2-Sep-26	22-Sep-26	96.0d
3808	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 4		54.0d	8-Jul-26	22-Sep-26	68.0d
3809	PR-VDC-L1A4-760	Prep & Submit Level 1, Area 4 Fire Sprinkler Shop Drawings	10.0d	8-Jul-26	21-Jul-26	68.0d
3810	PR-VDC-L1A4-770	Review & Approve (HP) Level 1, Area 4 Fire Sprinkler Shop Drawings	5.0d	22-Jul-26	28-Jul-26	68.0d
3811	PR-VDC-L1A4-780	Review & Approve (HNTB) Level 1, Area 4 Fire Sprinkler Shop Drawings	10.0d	29-Jul-26	11-Aug-26	68.0d
3812	PR-VDC-L1A4-790	Review & Approve (HCAA) Level 1, Area 4 Fire Sprinkler Shop Drawings	15.0d	12-Aug-26	1-Sep-26	68.0d
3813	PR-VDC-L1A4-800	Fab. & Ship Level 1, Area 4 Fire Sprinkler Shop Drawings	20.0d	2-Sep-26	22-Sep-26	96.0d
3814	WBS - Plumbing Shop Drawings - Level 1, Area 4		54.0d	8-Jul-26	22-Sep-26	68.0d
3815	PR-VDC-L1A4-860	Prep & Submit Level 1, Area 4 Plumbing Shop Drawings	10.0d	8-Jul-26	21-Jul-26	68.0d
3816	PR-VDC-L1A4-870	Review & Approve (HP) Level 1, Area 4 Plumbing Shop Drawings	5.0d	22-Jul-26	28-Jul-26	68.0d
3817	PR-VDC-L1A4-880	Review & Approve (HNTB) Level 1, Area 4 Plumbing Shop Drawings	10.0d	29-Jul-26	11-Aug-26	68.0d
3818	PR-VDC-L1A4-890	Review & Approve (HCAA) Level 1, Area 4 Plumbing Shop Drawings	15.0d	12-Aug-26	1-Sep-26	68.0d
3819	PR-VDC-L1A4-900	Fab. & Ship Level 1, Area 4 Plumbing Shop Drawings	20.0d	2-Sep-26	22-Sep-26	96.0d
3820	WBS - Electrical Shop Drawings - Level 1, Area 4		54.0d	8-Jul-26	22-Sep-26	68.0d
3821	PR-VDC-L1A4-910	Prep & Submit Level 1, Area 4 Elec. Shop Drawings	10.0d	8-Jul-26	21-Jul-26	68.0d
3822	PR-VDC-L1A4-920	Review & Approve (HP) Level 1, Area 4 Elec.Shop Drawings	5.0d	22-Jul-26	28-Jul-26	68.0d



	ID	Name	Dur	Start	Finish	TF
3823	PR-VDC-L1A4-930	Review & Approve (HNTB) Level 1, Area 4 Elec. Shop Drawings	10.0d	29-Jul-26	11-Aug-26	68.0d
3824	PR-VDC-L1A4-940	Review & Approve (HCAA) Level 1, Area 4 Elec. Shop Drawings	15.0d	12-Aug-26	1-Sep-26	68.0d
3825	PR-VDC-L1A4-950	Fab. & Ship Level 1, Area 4 Elec. Shop Drawings	20.0d	2-Sep-26	22-Sep-26	96.0d
3826	WBS - Low Voltage Shop Drawings - Level 1, Area 4		54.0d	8-Jul-26	22-Sep-26	68.0d
3827	PR-VDC-L1A4-960	Prep & Submit Level 1, Area 4 Low Voltage Shop Drawings	10.0d	8-Jul-26	21-Jul-26	68.0d
3828	PR-VDC-L1A4-970	Review & Approve (HP) Level 1, Area 4 Low Voltage Shop Drawings	5.0d	22-Jul-26	28-Jul-26	68.0d
3829	PR-VDC-L1A4-980	Review & Approve (HNTB) Level 1, Area 4 Low Voltage Shop Drawings	10.0d	29-Jul-26	11-Aug-26	68.0d
3830	PR-VDC-L1A4-990	Review & Approve (HCAA) Level 1, Area 4 Low Voltage Shop Drawings	15.0d	12-Aug-26	1-Sep-26	68.0d
3831	PR-VDC-L1A4-1000	Fab. & Ship Level 1, Area 4 Low Voltage Shop Drawings	20.0d	2-Sep-26	22-Sep-26	96.0d
3832	WBS - Level 1, Area 5 - OH VDC Coordination		54.0d	22-Jul-26	6-Oct-26	68.0d
3833	WBS - Mechanical Shop Drawings - Level 1, Area 5		54.0d	22-Jul-26	6-Oct-26	68.0d
3834	PR-VDC-L1A5-1080	Prep & Submit Level 1, Area 5 Mech. Shop Drawings	10.0d	22-Jul-26	4-Aug-26	68.0d
3835	PR-VDC-L1A5-1090	Review & Approve (HP) Level 1, Area 5 Mech. Shop Drawings	5.0d	5-Aug-26	11-Aug-26	68.0d
3836	PR-VDC-L1A5-1060	Review & Approve (HNTB) Level 1, Area 5 Mech. Shop Drawings	10.0d	12-Aug-26	25-Aug-26	68.0d
3837	PR-VDC-L1A5-1070	Review & Approve (HCAA) Level 1, Area 5 Mech. Shop Drawings	15.0d	26-Aug-26	16-Sep-26	68.0d
3838	PR-VDC-L1A5-1100	Fab. & Ship Level 1, Area 5 Mech. Shop Drawings	20.0d	17-Sep-26	6-Oct-26	96.0d
3839	WBS - Fire Sprinkler Shop Drawings - Level 1, Area 5		54.0d	22-Jul-26	6-Oct-26	68.0d
3840	PR-VDC-L1A5-1010	Prep & Submit Level 1, Area 5 Fire Sprinkler Shop Drawings	10.0d	22-Jul-26	4-Aug-26	68.0d
3841	PR-VDC-L1A5-1020	Review & Approve (HP) Level 1, Area 5 Fire Sprinkler Shop Drawings	5.0d	5-Aug-26	11-Aug-26	68.0d
3842	PR-VDC-L1A5-1030	Review & Approve (HNTB) Level 1, Area 5 Fire Sprinkler Shop Drawings	10.0d	12-Aug-26	25-Aug-26	68.0d
3843	PR-VDC-L1A5-1040	Review & Approve (HCAA) Level 1, Area 5 Fire Sprinkler Shop Drawings	15.0d	26-Aug-26	16-Sep-26	68.0d
3844	PR-VDC-L1A5-1050	Fab. & Ship Level 1, Area 5 Fire Sprinkler Shop Drawings	20.0d	17-Sep-26	6-Oct-26	96.0d
3845	WBS - Electrical Shop Drawings - Level 1, Area 5		54.0d	22-Jul-26	6-Oct-26	68.0d
3846	PR-VDC-L1A5-1160	Prep & Submit Level 1, Area 5 Elec. Shop Drawings	10.0d	22-Jul-26	4-Aug-26	68.0d
3847	PR-VDC-L1A5-1170	Review & Approve (HP) Level 1, Area 5 Elec.Shop Drawings	5.0d	5-Aug-26	11-Aug-26	68.0d
3848	PR-VDC-L1A5-1180	Review & Approve (HNTB) Level 1, Area 5 Elec. Shop Drawings	10.0d	12-Aug-26	25-Aug-26	68.0d
3849	PR-VDC-L1A5-1190	Review & Approve (HCAA) Level 1, Area 5 Elec. Shop Drawings	15.0d	26-Aug-26	16-Sep-26	68.0d
3850	PR-VDC-L1A5-1200	Fab. & Ship Level 1, Area 5 Elec. Shop Drawings	20.0d	17-Sep-26	6-Oct-26	96.0d
3851	WBS - Low Voltage Shop Drawings - Level 1, Area 5		54.0d	22-Jul-26	6-Oct-26	68.0d
3852	PR-VDC-L1A5-1210	Prep & Submit Level 1, Area 5 Low Voltage Shop Drawings	10.0d	22-Jul-26	4-Aug-26	68.0d
3853	PR-VDC-L1A5-1220	Review & Approve (HP) Level 1, Area 5 Low Voltage Shop Drawings	5.0d	5-Aug-26	11-Aug-26	68.0d
3854	PR-VDC-L1A5-1230	Review & Approve (HNTB) Level 1, Area 5 Low Voltage Shop Drawings	10.0d	12-Aug-26	25-Aug-26	68.0d
3855	PR-VDC-L1A5-1240	Review & Approve (HCAA) Level 1, Area 5 Low Voltage Shop Drawings	15.0d	26-Aug-26	16-Sep-26	68.0d
3856	PR-VDC-L1A5-1250	Fab. & Ship Level 1, Area 5 Low Voltage Shop Drawings	20.0d	17-Sep-26	6-Oct-26	96.0d
3857	WBS - Plumbing Shop Drawings - Level 1, Area 5		54.0d	22-Jul-26	6-Oct-26	68.0d
3858	PR-VDC-L1A5-1110	Prep & Submit Level 1, Area 5 Plumbing Shop Drawings	10.0d	22-Jul-26	4-Aug-26	68.0d
3859	PR-VDC-L1A5-1120	Review & Approve (HP) Level 1, Area 5 Plumbing Shop Drawings	5.0d	5-Aug-26	11-Aug-26	68.0d
3860	PR-VDC-L1A5-1130	Review & Approve (HNTB) Level 1, Area 5 Plumbing Shop Drawings	10.0d	12-Aug-26	25-Aug-26	68.0d
3861	PR-VDC-L1A5-1140	Review & Approve (HCAA) Level 1, Area 5 Plumbing Shop Drawings	15.0d	26-Aug-26	16-Sep-26	68.0d
3862	PR-VDC-L1A5-1150	Fab. & Ship Level 1, Area 5 Plumbing Shop Drawings	20.0d	17-Sep-26	6-Oct-26	96.0d
3863	WBS - Level 1, Areas 6&7 - OH VDC Coordination		58.0d	15-Oct-26	9-Jan-27	37.0d
3864	WBS - Mechanical Shop Drawings - Level 1, Areas 6&7		58.0d	15-Oct-26	9-Jan-27	37.0d




	ID	Name	Dur	Start	Finish	TF
3865	PR-VDC-L1A6-1330	Prep & Submit Level 1, Areas 6&7 Mech. Shop Drawings	10.0d	15-Oct-26	28-Oct-26	36.0d
3866	PR-VDC-L1A6-1340	Review & Approve (HP) Level 1, Areas 6&7 Mech. Shop Drawings	5.0d	29-Oct-26	4-Nov-26	36.0d
3867	PR-VDC-L1A6-1310	Review & Approve (HNTB) Level 1, Areas 6&7 Mech. Shop Drawings	15.0d	5-Nov-26	25-Nov-26	36.0d
3868	PR-VDC-L1A6-1320	Review & Approve (HCAA) Level 1, Areas 6&7 Mech. Shop Drawings	15.0d	30-Nov-26	18-Dec-26	36.0d
3869	PR-VDC-L1A6-1350	Fab. & Ship Level 1, Areas 6&7 Mech. Shop Drawings	20.0d	19-Dec-26	9-Jan-27	52.0d
3870	WBS - Fire Sprinkler Shop Drawings - Level 1, Areas 6&7		53.0d	15-Oct-26	2-Jan-27	42.0d
3871	PR-VDC-L1A6-1260	Prep & Submit Level 1, Areas 6&7 Fire Sprinkler Shop Drawings	10.0d	15-Oct-26	28-Oct-26	41.0d
3872	PR-VDC-L1A6-1270	Review & Approve (HP) Level 1, Areas 6&7 Fire Sprinkler Shop Drawings	5.0d	29-Oct-26	4-Nov-26	41.0d
3873	PR-VDC-L1A6-1280	Review & Approve (HNTB) Level 1, Areas 6&7 Fire Sprinkler Shop Drawings	10.0d	5-Nov-26	18-Nov-26	41.0d
3874	PR-VDC-L1A6-1290	Review & Approve (HCAA) Level 1, Areas 6&7 Fire Sprinkler Shop Drawings	15.0d	19-Nov-26	11-Dec-26	41.0d
3875	PR-VDC-L1A6-1300	Fab. & Ship Level 1, Areas 6&7 Fire Sprinkler Shop Drawings	20.0d	12-Dec-26	2-Jan-27	59.0d
3876	WBS - Plumbing Shop Drawings - Level 1, Areas 6&7		53.0d	15-Oct-26	2-Jan-27	42.0d
3877	PR-VDC-L1A6-1360	Prep & Submit Level 1, Areas 6&7 Plumbing Shop Drawings	10.0d	15-Oct-26	28-Oct-26	41.0d
3878	PR-VDC-L1A6-1370	Review & Approve (HP) Level 1, Areas 6&7 Plumbing Shop Drawings	5.0d	29-Oct-26	4-Nov-26	41.0d
3879	PR-VDC-L1A6-1380	Review & Approve (HNTB) Level 1, Areas 6&7 Plumbing Shop Drawings	10.0d	5-Nov-26	18-Nov-26	41.0d
3880	PR-VDC-L1A6-1390	Review & Approve (HCAA) Level 1, Areas 6&7 Plumbing Shop Drawings	15.0d	19-Nov-26	11-Dec-26	41.0d
3881	PR-VDC-L1A6-1400	Fab. & Ship Level 1, Areas 6&7 Plumbing Shop Drawings	20.0d	12-Dec-26	2-Jan-27	59.0d
3882	WBS - Electrical Shop Drawings - Level 1, Areas 6&7		53.0d	15-Oct-26	2-Jan-27	42.0d
3883	PR-VDC-L1A6-1410	Prep & Submit Level 1, Areas 6&7 Elec. Shop Drawings	10.0d	15-Oct-26	28-Oct-26	41.0d
3884	PR-VDC-L1A6-1420	Review & Approve (HP) Level 1, Areas 6&7 Elec.Shop Drawings	5.0d	29-Oct-26	4-Nov-26	41.0d
3885	PR-VDC-L1A6-1430	Review & Approve (HNTB) Level 1, Areas 6&7 Elec. Shop Drawings	10.0d	5-Nov-26	18-Nov-26	41.0d
3886	PR-VDC-L1A6-1440	Review & Approve (HCAA) Level 1, Areas 6&7 Elec. Shop Drawings	15.0d	19-Nov-26	11-Dec-26	41.0d
3887	PR-VDC-L1A6-1450	Fab. & Ship Level 1, Areas 6&7 Elec. Shop Drawings	20.0d	12-Dec-26	2-Jan-27	59.0d
3888	WBS - Low Voltage Shop Drawings - Level 1, Areas 6&7		53.0d	15-Oct-26	2-Jan-27	42.0d
3889	PR-VDC-L1A6-1460	Prep & Submit Level 1, Areas 6&7 Low Voltage Shop Drawings	10.0d	15-Oct-26	28-Oct-26	41.0d
3890	PR-VDC-L1A6-1470	Review & Approve (HP) Level 1, Areas 6&7 Low Voltage Shop Drawings	5.0d	29-Oct-26	4-Nov-26	41.0d
3891	PR-VDC-L1A6-1480	Review & Approve (HNTB) Level 1, Areas 6&7 Low Voltage Shop Drawings	10.0d	5-Nov-26	18-Nov-26	41.0d
3892	PR-VDC-L1A6-1490	Review & Approve (HCAA) Level 1, Areas 6&7 Low Voltage Shop Drawings	15.0d	19-Nov-26	11-Dec-26	41.0d
3893	PR-VDC-L1A6-1500	Fab. & Ship Level 1, Areas 6&7 Low Voltage Shop Drawings	20.0d	12-Dec-26	2-Jan-27	59.0d
3894	WBS - Level 2, Area 8 - OH VDC Coordination		33.0d	6-Apr-26	20-May-26	84.0d
3895	WBS - Mechanical Shop Drawings - Level 2, Area 8		33.0d	6-Apr-26	20-May-26	84.0d
3896	PR-VDC-L2A8-1580	Prep & Submit Level 2, Area 8 Mech. Shop Drawings	10.0d	6-Apr-26	17-Apr-26	82.0d
3897	PR-VDC-L2A8-1590	Review & Approve (HP) Level 2, Area 8 Mech. Shop Drawings	5.0d	20-Apr-26	24-Apr-26	82.0d
3898	PR-VDC-L2A8-1560	Review & Approve (HNTB) Level 2, Area 8 Mech. Shop Drawings	5.0d	27-Apr-26	1-May-26	82.0d
3899	PR-VDC-L2A8-1570	Review & Approve (HCAA) Level 2, Area 8 Mech. Shop Drawings	10.0d	4-May-26	15-May-26	82.0d
3900	PR-VDC-L2A8-1600	Fab. & Ship Level 2, Area 8 Mech. Shop Drawings	5.0d	16-May-26	20-May-26	117.0d
3901	WBS - Fire Sprinkler Shop Drawings - Level 2, Area 8		33.0d	6-Apr-26	20-May-26	84.0d
3902	PR-VDC-L2A8-1510	Prep & Submit Level 2, Area 8 Fire Sprinkler Shop Drawings	10.0d	6-Apr-26	17-Apr-26	82.0d
3903	PR-VDC-L2A8-1520	Review & Approve (HP) Level 2, Area 8 Fire Sprinkler Shop Drawings	5.0d	20-Apr-26	24-Apr-26	82.0d
3904	PR-VDC-L2A8-1530	Review & Approve (HNTB) Level 2, Area 8 Fire Sprinkler Shop Drawings	5.0d	27-Apr-26	1-May-26	82.0d
3905	PR-VDC-L2A8-1540	Review & Approve (HCAA) Level 2, Area 8 Fire Sprinkler Shop Drawings	10.0d	4-May-26	15-May-26	82.0d
3906	PR-VDC-L2A8-1550	Fab. & Ship Level 2, Area 8 Fire Sprinkler Shop Drawings	5.0d	16-May-26	20-May-26	117.0d

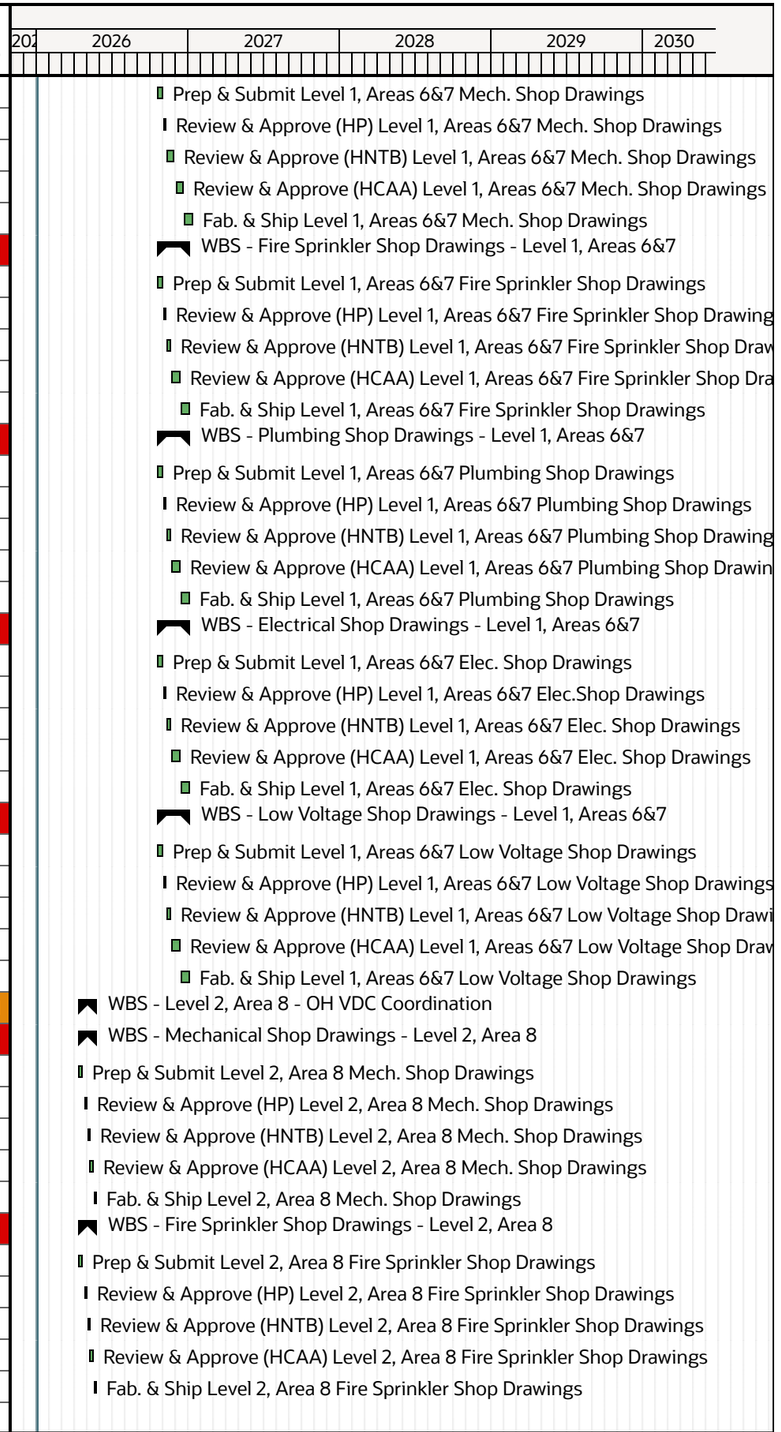

	ID	Name	Dur	Start	Finish	TF
3907	WBS - Plumbing Shop Drawings - Level 2, Area 8		33.0d	6-Apr-26	20-May-26	84.0d
3908	PR-VDC-L2A8-1610	Prep & Submit Level 2, Area 8 Plumbing Shop Drawings	10.0d	6-Apr-26	17-Apr-26	82.0d
3909	PR-VDC-L2A8-1620	Review & Approve (HP) Level 2, Area 8 Plumbing Shop Drawings	5.0d	20-Apr-26	24-Apr-26	82.0d
3910	PR-VDC-L2A8-1630	Review & Approve (HNTB) Level 2, Area 8 Plumbing Shop Drawings	5.0d	27-Apr-26	1-May-26	82.0d
3911	PR-VDC-L2A8-1640	Review & Approve (HCAA) Level 2, Area 8 Plumbing Shop Drawings	10.0d	4-May-26	15-May-26	82.0d
3912	PR-VDC-L2A8-1650	Fab. & Ship Level 2, Area 8 Plumbing Shop Drawings	5.0d	16-May-26	20-May-26	117.0d
3913	WBS - Electrical Shop Drawings - Level 2, Area 8		33.0d	6-Apr-26	20-May-26	84.0d
3914	PR-VDC-L2A8-1660	Prep & Submit Level 2, Area 8 Elec. Shop Drawings	10.0d	6-Apr-26	17-Apr-26	82.0d
3915	PR-VDC-L2A8-1670	Review & Approve (HP) Level 2, Area 8 Elec.Shop Drawings	5.0d	20-Apr-26	24-Apr-26	82.0d
3916	PR-VDC-L2A8-1680	Review & Approve (HNTB) Level 2, Area 8 Elec. Shop Drawings	5.0d	27-Apr-26	1-May-26	82.0d
3917	PR-VDC-L2A8-1690	Review & Approve (HCAA) Level 2, Area 8 Elec. Shop Drawings	10.0d	4-May-26	15-May-26	82.0d
3918	PR-VDC-L2A8-1700	Fab. & Ship Level 2, Area 8 Elec. Shop Drawings	5.0d	16-May-26	20-May-26	117.0d
3919	WBS - Low Voltage Shop Drawings - Level 2, Area 8		33.0d	6-Apr-26	20-May-26	84.0d
3920	PR-VDC-L2A8-1710	Prep & Submit Level 2, Area 8 Low Voltage Shop Drawings	10.0d	6-Apr-26	17-Apr-26	82.0d
3921	PR-VDC-L2A8-1720	Review & Approve (HP) Level 2, Area 8 Low Voltage Shop Drawings	5.0d	20-Apr-26	24-Apr-26	82.0d
3922	PR-VDC-L2A8-1730	Review & Approve (HNTB) Level 2, Area 8 Low Voltage Shop Drawings	5.0d	27-Apr-26	1-May-26	82.0d
3923	PR-VDC-L2A8-1740	Review & Approve (HCAA) Level 2, Area 8 Low Voltage Shop Drawings	10.0d	4-May-26	15-May-26	82.0d
3924	PR-VDC-L2A8-1750	Fab. & Ship Level 2, Area 8 Low Voltage Shop Drawings	5.0d	16-May-26	20-May-26	117.0d
3925	WBS - Level 2&3, Area 9 - OH VDC Coordination		43.0d	11-May-26	12-Jul-26	25.0d
3926	WBS - Mechanical Shop Drawings - Level 2&3, Area 9		43.0d	11-May-26	12-Jul-26	25.0d
3927	PR-VDC-L2A9-1830	Prep & Submit Level 2&3, Area 9 Mech. Shop Drawings	10.0d	11-May-26	22-May-26	23.0d
3928	PR-VDC-L2A9-1840	Review & Approve (HP) Level 2&3, Area 9 Mech. Shop Drawings	5.0d	26-May-26	1-Jun-26	23.0d
3929	PR-VDC-L2A9-1810	Review & Approve (HNTB) Level 2&3, Area 9 Mech. Shop Drawings	10.0d	2-Jun-26	15-Jun-26	23.0d
3930	PR-VDC-L2A9-1820	Review & Approve (HCAA) Level 2&3, Area 9 Mech. Shop Drawings	15.0d	16-Jun-26	7-Jul-26	23.0d
3931	PR-VDC-L2A9-1850	Fab. & Ship Level 2&3, Area 9 Mech. Shop Drawings	5.0d	8-Jul-26	12-Jul-26	33.0d
3932	WBS - Fire Sprinkler Shop Drawings - Level 2&3, Area 9		43.0d	11-May-26	12-Jul-26	25.0d
3933	PR-VDC-L2A9-1760	Prep & Submit Level 2&3, Area 9 Fire Sprinkler Shop Drawings	10.0d	11-May-26	22-May-26	23.0d
3934	PR-VDC-L2A9-1770	Review & Approve (HP) Level 2&3, Area 9 Fire Sprinkler Shop Drawings	5.0d	26-May-26	1-Jun-26	23.0d
3935	PR-VDC-L2A9-1780	Review & Approve (HNTB) Level 2&3, Area 9 Fire Sprinkler Shop Drawings	10.0d	2-Jun-26	15-Jun-26	23.0d
3936	PR-VDC-L2A9-1790	Review & Approve (HCAA) Level 2&3, Area 9 Fire Sprinkler Shop Drawings	15.0d	16-Jun-26	7-Jul-26	23.0d
3937	PR-VDC-L2A9-1800	Fab. & Ship Level 2&3, Area 9 Fire Sprinkler Shop Drawings	5.0d	8-Jul-26	12-Jul-26	33.0d
3938	WBS - Electrical Shop Drawings - Level 2&3, Area 9		43.0d	11-May-26	12-Jul-26	25.0d
3939	PR-VDC-L2A9-1910	Prep & Submit Level 2&3, Area 9 Elec. Shop Drawings	10.0d	11-May-26	22-May-26	23.0d
3940	PR-VDC-L2A9-1920	Review & Approve (HP) Level 2&3, Area 9 Elec.Shop Drawings	5.0d	26-May-26	1-Jun-26	23.0d
3941	PR-VDC-L2A9-1930	Review & Approve (HNTB) Level 2&3, Area 9 Elec. Shop Drawings	10.0d	2-Jun-26	15-Jun-26	23.0d
3942	PR-VDC-L2A9-1940	Review & Approve (HCAA) Level 2&3, Area 9 Elec. Shop Drawings	15.0d	16-Jun-26	7-Jul-26	23.0d
3943	PR-VDC-L2A9-1950	Fab. & Ship Level 2&3, Area 9 Elec. Shop Drawings	5.0d	8-Jul-26	12-Jul-26	33.0d
3944	WBS - Low Voltage Shop Drawings - Level 2&3, Area 9		43.0d	11-May-26	12-Jul-26	25.0d
3945	PR-VDC-L2A9-1960	Prep & Submit Level 2&3, Area 9 Low Voltage Shop Drawings	10.0d	11-May-26	22-May-26	23.0d
3946	PR-VDC-L2A9-1970	Review & Approve (HP) Level 2&3, Area 9 Low Voltage Shop Drawings	5.0d	26-May-26	1-Jun-26	23.0d
3947	PR-VDC-L2A9-1980	Review & Approve (HNTB) Level 2&3, Area 9 Low Voltage Shop Drawings	10.0d	2-Jun-26	15-Jun-26	23.0d
3948	PR-VDC-L2A9-1990	Review & Approve (HCAA) Level 2&3, Area 9 Low Voltage Shop Drawings	15.0d	16-Jun-26	7-Jul-26	23.0d




	ID	Name	Dur	Start	Finish	TF
3949	PR-VDC-L2A9-2000	Fab. & Ship Level 2&3, Area 9 Low Voltage Shop Drawings	5.0d	8-Jul-26	12-Jul-26	33.0d
3950	WBS - Plumbing Shop Drawings - Level 2&3, Area 9		43.0d	11-May-26	12-Jul-26	25.0d
3951	PR-VDC-L2A9-1860	Prep & Submit Level 2&3, Area 9 Plumbing Shop Drawings	10.0d	11-May-26	22-May-26	23.0d
3952	PR-VDC-L2A9-1870	Review & Approve (HP) Level 2&3, Area 9 Plumbing Shop Drawings	5.0d	26-May-26	1-Jun-26	23.0d
3953	PR-VDC-L2A9-1880	Review & Approve (HNTB) Level 2&3, Area 9 Plumbing Shop Drawings	10.0d	2-Jun-26	15-Jun-26	23.0d
3954	PR-VDC-L2A9-1890	Review & Approve (HCAA) Level 2&3, Area 9 Plumbing Shop Drawings	15.0d	16-Jun-26	7-Jul-26	23.0d
3955	PR-VDC-L2A9-1900	Fab. & Ship Level 2&3, Area 9 Plumbing Shop Drawings	5.0d	8-Jul-26	12-Jul-26	33.0d
3956	WBS - Level 2, Concessions - OH VDC Coordination		47.0d	12-Aug-26	17-Oct-26	37.0d
3957	WBS - Mechanical Shop Drawings - Level 2, Concessions		47.0d	12-Aug-26	17-Oct-26	37.0d
3958	PR-VDC-L2AC-2080	Prep & Submit Level 2, Concessions Mech. Shop Drawings	10.0d	12-Aug-26	25-Aug-26	36.0d
3959	PR-VDC-L2AC-2090	Review & Approve (HP) Level 2, Concessions Mech. Shop Drawings	5.0d	26-Aug-26	1-Sep-26	36.0d
3960	PR-VDC-L2AC-2060	Review & Approve (HNTB) Level 2, Concessions Mech. Shop Drawings	10.0d	2-Sep-26	16-Sep-26	36.0d
3961	PR-VDC-L2AC-2070	Review & Approve (HCAA) Level 2, Concessions Mech. Shop Drawings	15.0d	17-Sep-26	7-Oct-26	36.0d
3962	PR-VDC-L2AC-2100	Fab. & Ship Level 2, Concessions Mech. Shop Drawings	10.0d	8-Oct-26	17-Oct-26	52.0d
3963	WBS - Fire Sprinkler Shop Drawings - Level 2, Concessions		47.0d	12-Aug-26	17-Oct-26	37.0d
3964	PR-VDC-L2AC-2010	Prep & Submit Level 2, Concessions Fire Sprinkler Shop Drawings	10.0d	12-Aug-26	25-Aug-26	36.0d
3965	PR-VDC-L2AC-2020	Review & Approve (HP) Level 2, Concessions Fire Sprinkler Shop Drawings	5.0d	26-Aug-26	1-Sep-26	36.0d
3966	PR-VDC-L2AC-2030	Review & Approve (HNTB) Level 2, Concessions Fire Sprinkler Shop Drawings	10.0d	2-Sep-26	16-Sep-26	36.0d
3967	PR-VDC-L2AC-2040	Review & Approve (HCAA) Level 2, Concessions Fire Sprinkler Shop Drawings	15.0d	17-Sep-26	7-Oct-26	36.0d
3968	PR-VDC-L2AC-2050	Fab. & Ship Level 2, Concessions Fire Sprinkler Shop Drawings	10.0d	8-Oct-26	17-Oct-26	52.0d
3969	WBS - Plumbing Shop Drawings - Level 2, Concessions		47.0d	12-Aug-26	17-Oct-26	37.0d
3970	PR-VDC-L2AC-2110	Prep & Submit Level 2, Concessions Plumbing Shop Drawings	10.0d	12-Aug-26	25-Aug-26	36.0d
3971	PR-VDC-L2AC-2120	Review & Approve (HP) Level 2, Concessions Plumbing Shop Drawings	5.0d	26-Aug-26	1-Sep-26	36.0d
3972	PR-VDC-L2AC-2130	Review & Approve (HNTB) Level 2, Concessions Plumbing Shop Drawings	10.0d	2-Sep-26	16-Sep-26	36.0d
3973	PR-VDC-L2AC-2140	Review & Approve (HCAA) Level 2, Concessions Plumbing Shop Drawings	15.0d	17-Sep-26	7-Oct-26	36.0d
3974	PR-VDC-L2AC-2150	Fab. & Ship Level 2, Concessions Plumbing Shop Drawings	10.0d	8-Oct-26	17-Oct-26	52.0d
3975	WBS - Electrical Shop Drawings - Level 2, Concessions		47.0d	12-Aug-26	17-Oct-26	37.0d
3976	PR-VDC-L2AC-2160	Prep & Submit Level 2, Concessions Elec. Shop Drawings	10.0d	12-Aug-26	25-Aug-26	36.0d
3977	PR-VDC-L2AC-2170	Review & Approve (HP) Level 2, Concessions Elec.Shop Drawings	5.0d	26-Aug-26	1-Sep-26	36.0d
3978	PR-VDC-L2AC-2180	Review & Approve (HNTB) Level 2, Concessions Elec. Shop Drawings	10.0d	2-Sep-26	16-Sep-26	36.0d
3979	PR-VDC-L2AC-2190	Review & Approve (HCAA) Level 2, Concessions Elec. Shop Drawings	15.0d	17-Sep-26	7-Oct-26	36.0d
3980	PR-VDC-L2AC-2200	Fab. & Ship Level 2, Concessions Elec. Shop Drawings	10.0d	8-Oct-26	17-Oct-26	52.0d
3981	WBS - Low Voltage Shop Drawings - Level 2, Concessions		47.0d	12-Aug-26	17-Oct-26	37.0d
3982	PR-VDC-L2AC-2210	Prep & Submit Level 2, Concessions Low Voltage Shop Drawings	10.0d	12-Aug-26	25-Aug-26	36.0d
3983	PR-VDC-L2AC-2220	Review & Approve (HP) Level 2, Concessions Low Voltage Shop Drawings	5.0d	26-Aug-26	1-Sep-26	36.0d
3984	PR-VDC-L2AC-2230	Review & Approve (HNTB) Level 2, Concessions Low Voltage Shop Drawings	10.0d	2-Sep-26	16-Sep-26	36.0d
3985	PR-VDC-L2AC-2240	Review & Approve (HCAA) Level 2, Concessions Low Voltage Shop Drawings	15.0d	17-Sep-26	7-Oct-26	36.0d
3986	PR-VDC-L2AC-2250	Fab. & Ship Level 2, Concessions Low Voltage Shop Drawings	10.0d	8-Oct-26	17-Oct-26	52.0d
3987	WBS - Level 3, Area 10 - OH VDC Coordination		54.0d	19-Aug-26	3-Nov-26	182.0d
3988	WBS - Mechanical Shop Drawings - Level 3, Area 10		54.0d	19-Aug-26	3-Nov-26	132.0d
3989	PR-VDC-L3A10-2330	Prep & Submit Level 3, Area 10 Mech. Shop Drawings	10.0d	19-Aug-26	1-Sep-26	132.0d
3990	PR-VDC-L3A10-2340	Review & Approve (HP) Level 3, Area 10 Mech. Shop Drawings	5.0d	2-Sep-26	9-Sep-26	132.0d

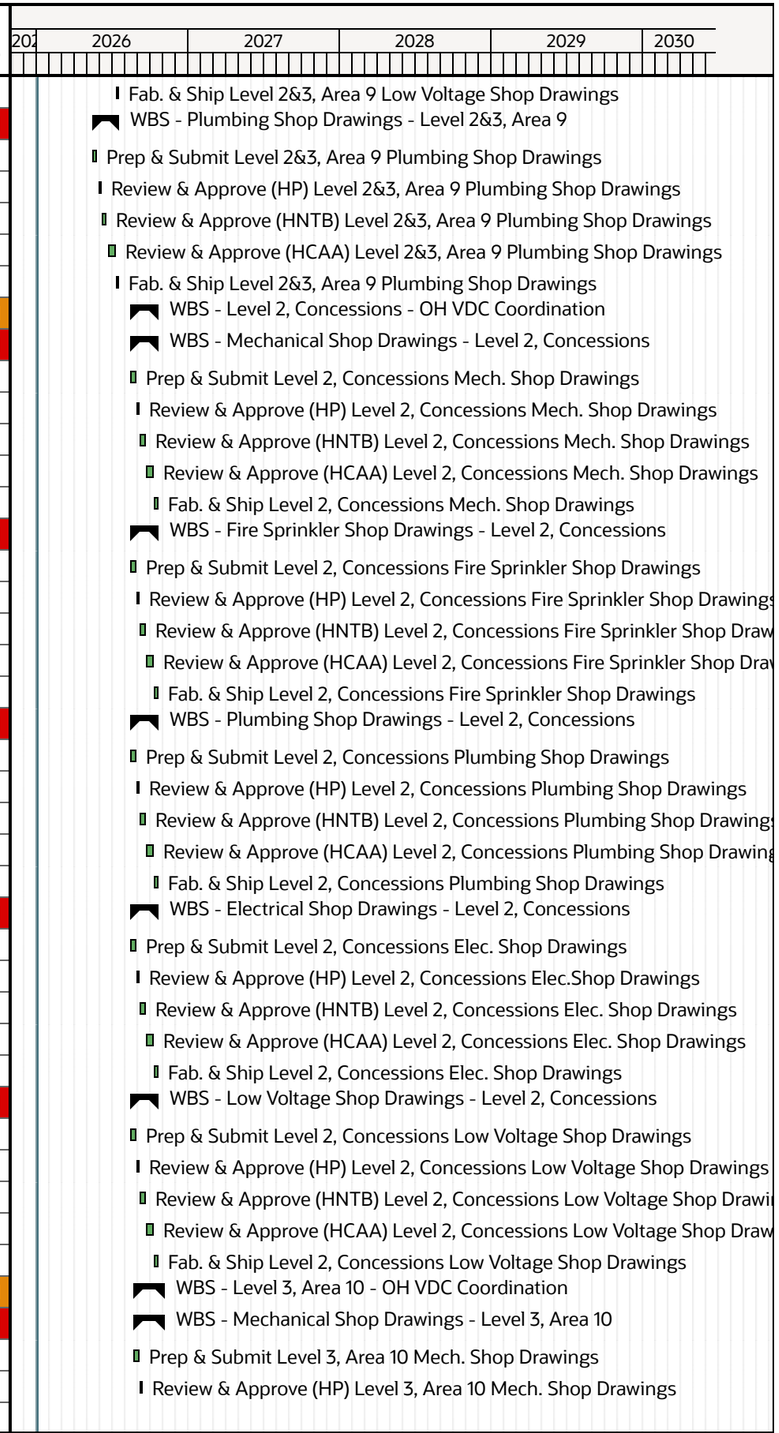

	ID	Name	Dur	Start	Finish	TF
3991	PR-VDC-L3A10-2310	Review & Approve (HNTB) Level 3, Area 10 Mech. Shop Drawings	10.0d	10-Sep-26	23-Sep-26	132.0d
3992	PR-VDC-L3A10-2320	Review & Approve (HCAA) Level 3, Area 10 Mech. Shop Drawings	15.0d	24-Sep-26	14-Oct-26	132.0d
3993	PR-VDC-L3A10-2350	Fab. & Ship Level 3, Area 10 Mech. Shop Drawings	20.0d	15-Oct-26	3-Nov-26	186.0d
3994	WBS - Fire Sprinkler Shop Drawings - Level 3, Area 10		54.0d	19-Aug-26	3-Nov-26	117.0d
3995	PR-VDC-L3A10-2260	Prep & Submit Level 3, Area 10 Fire Sprinkler Shop Drawings	10.0d	19-Aug-26	1-Sep-26	117.0d
3996	PR-VDC-L3A10-2270	Review & Approve (HP) Level 3, Area 10 Fire Sprinkler Shop Drawings	5.0d	2-Sep-26	9-Sep-26	117.0d
3997	PR-VDC-L3A10-2280	Review & Approve (HNTB) Level 3, Area 10 Fire Sprinkler Shop Drawings	10.0d	10-Sep-26	23-Sep-26	117.0d
3998	PR-VDC-L3A10-2290	Review & Approve (HCAA) Level 3, Area 10 Fire Sprinkler Shop Drawings	15.0d	24-Sep-26	14-Oct-26	117.0d
3999	PR-VDC-L3A10-2300	Fab. & Ship Level 3, Area 10 Fire Sprinkler Shop Drawings	20.0d	15-Oct-26	3-Nov-26	165.0d
4000	WBS - Plumbing Shop Drawings - Level 3, Area 10		54.0d	19-Aug-26	3-Nov-26	64.0d
4001	PR-VDC-L3A10-2360	Prep & Submit Level 3, Area 10 Plumbing Shop Drawings	10.0d	19-Aug-26	1-Sep-26	64.0d
4002	PR-VDC-L3A10-2370	Review & Approve (HP) Level 3, Area 10 Plumbing Shop Drawings	5.0d	2-Sep-26	9-Sep-26	64.0d
4003	PR-VDC-L3A10-2380	Review & Approve (HNTB) Level 3, Area 10 Plumbing Shop Drawings	10.0d	10-Sep-26	23-Sep-26	64.0d
4004	PR-VDC-L3A10-2390	Review & Approve (HCAA) Level 3, Area 10 Plumbing Shop Drawings	15.0d	24-Sep-26	14-Oct-26	64.0d
4005	PR-VDC-L3A10-2400	Fab. & Ship Level 3, Area 10 Plumbing Shop Drawings	20.0d	15-Oct-26	3-Nov-26	92.0d
4006	WBS - Electrical Shop Drawings - Level 3, Area 10		54.0d	19-Aug-26	3-Nov-26	122.0d
4007	PR-VDC-L3A10-2410	Prep & Submit Level 3, Area 10 Elec. Shop Drawings	10.0d	19-Aug-26	1-Sep-26	122.0d
4008	PR-VDC-L3A10-2420	Review & Approve (HP) Level 3, Area 10 Elec.Shop Drawings	5.0d	2-Sep-26	9-Sep-26	122.0d
4009	PR-VDC-L3A10-2430	Review & Approve (HNTB) Level 3, Area 10 Elec. Shop Drawings	10.0d	10-Sep-26	23-Sep-26	122.0d
4010	PR-VDC-L3A10-2440	Review & Approve (HCAA) Level 3, Area 10 Elec. Shop Drawings	15.0d	24-Sep-26	14-Oct-26	122.0d
4011	PR-VDC-L3A10-2450	Fab. & Ship Level 3, Area 10 Elec. Shop Drawings	20.0d	15-Oct-26	3-Nov-26	172.0d
4012	WBS - Low Voltage Shop Drawings - Level 3, Area 10		54.0d	19-Aug-26	3-Nov-26	182.0d
4013	PR-VDC-L3A10-2460	Prep & Submit Level 3, Area 10 Low Voltage Shop Drawings	10.0d	19-Aug-26	1-Sep-26	182.0d
4014	PR-VDC-L3A10-2470	Review & Approve (HP) Level 3, Area 10 Low Voltage Shop Drawings	5.0d	2-Sep-26	9-Sep-26	182.0d
4015	PR-VDC-L3A10-2480	Review & Approve (HNTB) Level 3, Area 10 Low Voltage Shop Drawings	10.0d	10-Sep-26	23-Sep-26	182.0d
4016	PR-VDC-L3A10-2490	Review & Approve (HCAA) Level 3, Area 10 Low Voltage Shop Drawings	15.0d	24-Sep-26	14-Oct-26	182.0d
4017	PR-VDC-L3A10-2500	Fab. & Ship Level 3, Area 10 Low Voltage Shop Drawings	20.0d	15-Oct-26	3-Nov-26	256.0d
4018	WBS - Level 3, Area 11 - OH VDC Coordination		54.0d	17-Sep-26	3-Dec-26	165.0d
4019	WBS - Fire Sprinkler Shop Drawings - Level 3, Area 11		54.0d	17-Sep-26	3-Dec-26	163.0d
4020	PR-VDC-L3A11-2510	Prep & Submit Level 3, Area 11 Fire Sprinkler Shop Drawings	10.0d	17-Sep-26	30-Sep-26	163.0d
4021	PR-VDC-L3A11-2520	Review & Approve (HP) Level 3, Area 11 Fire Sprinkler Shop Drawings	5.0d	1-Oct-26	7-Oct-26	163.0d
4022	PR-VDC-L3A11-2530	Review & Approve (HNTB) Level 3, Area 11 Fire Sprinkler Shop Drawings	15.0d	8-Oct-26	28-Oct-26	163.0d
4023	PR-VDC-L3A11-2540	Review & Approve (HCAA) Level 3, Area 11 Fire Sprinkler Shop Drawings	10.0d	29-Oct-26	11-Nov-26	163.0d
4024	PR-VDC-L3A11-2550	Fab. & Ship Level 3, Area 11 Fire Sprinkler Shop Drawings	20.0d	12-Nov-26	3-Dec-26	229.0d
4025	WBS - Electrical Shop Drawings - Level 3, Area 11		49.0d	17-Sep-26	24-Nov-26	168.0d
4026	PR-VDC-L3A11-2660	Prep & Submit Level 3, Area 11 Elec. Shop Drawings	10.0d	17-Sep-26	30-Sep-26	168.0d
4027	PR-VDC-L3A11-2670	Review & Approve (HP) Level 3, Area 11 Elec.Shop Drawings	5.0d	1-Oct-26	7-Oct-26	168.0d
4028	PR-VDC-L3A11-2680	Review & Approve (HNTB) Level 3, Area 11 Elec. Shop Drawings	10.0d	8-Oct-26	21-Oct-26	168.0d
4029	PR-VDC-L3A11-2690	Review & Approve (HCAA) Level 3, Area 11 Elec. Shop Drawings	10.0d	22-Oct-26	4-Nov-26	168.0d
4030	PR-VDC-L3A11-2700	Fab. & Ship Level 3, Area 11 Elec. Shop Drawings	20.0d	5-Nov-26	24-Nov-26	236.0d
4031	WBS - Low Voltage Shop Drawings - Level 3, Area 11		54.0d	17-Sep-26	3-Dec-26	165.0d
4032	PR-VDC-L3A11-2710	Prep & Submit Level 3, Area 11 Low Voltage Shop Drawings	10.0d	17-Sep-26	30-Sep-26	165.0d



	ID	Name	Dur	Start	Finish	TF
4033	PR-VDC-L3A11-2720	Review & Approve (HP) Level 3, Area 11 Low Voltage Shop Drawings	5.0d	1-Oct-26	7-Oct-26	165.0d
4034	PR-VDC-L3A11-2730	Review & Approve (HNTB) Level 3, Area 11 Low Voltage Shop Drawings	10.0d	8-Oct-26	21-Oct-26	165.0d
4035	PR-VDC-L3A11-2740	Review & Approve (HCAA) Level 3, Area 11 Low Voltage Shop Drawings	15.0d	22-Oct-26	11-Nov-26	165.0d
4036	PR-VDC-L3A11-2750	Fab. & Ship Level 3, Area 11 Low Voltage Shop Drawings	20.0d	12-Nov-26	3-Dec-26	231.0d
4037	WBS - Level 3, Area 12 - OH VDC Coordination		54.0d	29-Oct-26	18-Jan-27	142.0d
4038	WBS - Mechanical Shop Drawings - Level 3, Area 12		54.0d	29-Oct-26	18-Jan-27	97.0d
4039	PR-VDC-L3A12-2830	Prep & Submit Level 3, Area 12 Mech. Shop Drawings	10.0d	29-Oct-26	11-Nov-26	96.0d
4040	PR-VDC-L3A12-2840	Review & Approve (HP) Level 3, Area 12 Mech. Shop Drawings	5.0d	12-Nov-26	18-Nov-26	96.0d
4041	PR-VDC-L3A12-2810	Review & Approve (HNTB) Level 3, Area 12 Mech. Shop Drawings	10.0d	19-Nov-26	4-Dec-26	96.0d
4042	PR-VDC-L3A12-2820	Review & Approve (HCAA) Level 3, Area 12 Mech. Shop Drawings	15.0d	7-Dec-26	28-Dec-26	96.0d
4043	PR-VDC-L3A12-2850	Fab. & Ship Level 3, Area 12 Mech. Shop Drawings	20.0d	29-Dec-26	18-Jan-27	134.0d
4044	WBS - Fire Sprinkler Shop Drawings - Level 3, Area 12		54.0d	29-Oct-26	18-Jan-27	79.0d
4045	PR-VDC-L3A12-2760	Prep & Submit Level 3, Area 12 Fire Sprinkler Shop Drawings	10.0d	29-Oct-26	11-Nov-26	79.0d
4046	PR-VDC-L3A12-2770	Review & Approve (HP) Level 3, Area 12 Fire Sprinkler Shop Drawings	5.0d	12-Nov-26	18-Nov-26	79.0d
4047	PR-VDC-L3A12-2780	Review & Approve (HNTB) Level 3, Area 12 Fire Sprinkler Shop Drawings	10.0d	19-Nov-26	4-Dec-26	79.0d
4048	PR-VDC-L3A12-2790	Review & Approve (HCAA) Level 3, Area 12 Fire Sprinkler Shop Drawings	15.0d	7-Dec-26	28-Dec-26	79.0d
4049	PR-VDC-L3A12-2800	Fab. & Ship Level 3, Area 12 Fire Sprinkler Shop Drawings	20.0d	29-Dec-26	18-Jan-27	111.0d
4050	WBS - Electrical Shop Drawings - Level 3, Area 12		54.0d	29-Oct-26	18-Jan-27	84.0d
4051	PR-VDC-L3A12-2910	Prep & Submit Level 3, Area 12 Elec. Shop Drawings	10.0d	29-Oct-26	11-Nov-26	84.0d
4052	PR-VDC-L3A12-2920	Review & Approve (HP) Level 3, Area 12 Elec.Shop Drawings	5.0d	12-Nov-26	18-Nov-26	84.0d
4053	PR-VDC-L3A12-2930	Review & Approve (HNTB) Level 3, Area 12 Elec. Shop Drawings	10.0d	19-Nov-26	4-Dec-26	84.0d
4054	PR-VDC-L3A12-2940	Review & Approve (HCAA) Level 3, Area 12 Elec. Shop Drawings	15.0d	7-Dec-26	28-Dec-26	84.0d
4055	PR-VDC-L3A12-2950	Fab. & Ship Level 3, Area 12 Elec. Shop Drawings	20.0d	29-Dec-26	18-Jan-27	118.0d
4056	WBS - Low Voltage Shop Drawings - Level 3, Area 12		54.0d	29-Oct-26	18-Jan-27	142.0d
4057	PR-VDC-L3A12-2960	Prep & Submit Level 3, Area 12 Low Voltage Shop Drawings	10.0d	29-Oct-26	11-Nov-26	142.0d
4058	PR-VDC-L3A12-2970	Review & Approve (HP) Level 3, Area 12 Low Voltage Shop Drawings	5.0d	12-Nov-26	18-Nov-26	142.0d
4059	PR-VDC-L3A12-2980	Review & Approve (HNTB) Level 3, Area 12 Low Voltage Shop Drawings	10.0d	19-Nov-26	4-Dec-26	142.0d
4060	PR-VDC-L3A12-2990	Review & Approve (HCAA) Level 3, Area 12 Low Voltage Shop Drawings	15.0d	7-Dec-26	28-Dec-26	142.0d
4061	PR-VDC-L3A12-3000	Fab. & Ship Level 3, Area 12 Low Voltage Shop Drawings	20.0d	29-Dec-26	18-Jan-27	198.0d
4062	WBS - Plumbing Shop Drawings - Level 3, Area 12		54.0d	29-Oct-26	18-Jan-27	89.0d
4063	PR-VDC-L3A12-2860	Prep & Submit Level 3, Area 12 Plumbing Shop Drawings	10.0d	29-Oct-26	11-Nov-26	89.0d
4064	PR-VDC-L3A12-2870	Review & Approve (HP) Level 3, Area 12 Plumbing Shop Drawings	5.0d	12-Nov-26	18-Nov-26	89.0d
4065	PR-VDC-L3A12-2880	Review & Approve (HNTB) Level 3, Area 12 Plumbing Shop Drawings	10.0d	19-Nov-26	4-Dec-26	89.0d
4066	PR-VDC-L3A12-2890	Review & Approve (HCAA) Level 3, Area 12 Plumbing Shop Drawings	15.0d	7-Dec-26	28-Dec-26	89.0d
4067	PR-VDC-L3A12-2900	Fab. & Ship Level 3, Area 12 Plumbing Shop Drawings	20.0d	29-Dec-26	18-Jan-27	125.0d
4068	WBS - Level 3, Area 13 - OH VDC Coordination		54.0d	19-Nov-26	8-Feb-27	163.0d
4069	WBS - Mechanical Shop Drawings - Level 3, Area 13		54.0d	19-Nov-26	8-Feb-27	107.0d
4070	PR-VDC-L3A13-3080	Prep & Submit Level 3, Area 13 Mech. Shop Drawings	10.0d	19-Nov-26	4-Dec-26	107.0d
4071	PR-VDC-L3A13-3090	Review & Approve (HP) Level 3, Area 13 Mech. Shop Drawings	5.0d	7-Dec-26	11-Dec-26	107.0d
4072	PR-VDC-L3A13-3060	Review & Approve (HNTB) Level 3, Area 13 Mech. Shop Drawings	10.0d	14-Dec-26	28-Dec-26	107.0d
4073	PR-VDC-L3A13-3070	Review & Approve (HCAA) Level 3, Area 13 Mech. Shop Drawings	15.0d	29-Dec-26	19-Jan-27	107.0d
4074	PR-VDC-L3A13-3100	Fab. & Ship Level 3, Area 13 Mech. Shop Drawings	20.0d	20-Jan-27	8-Feb-27	149.0d

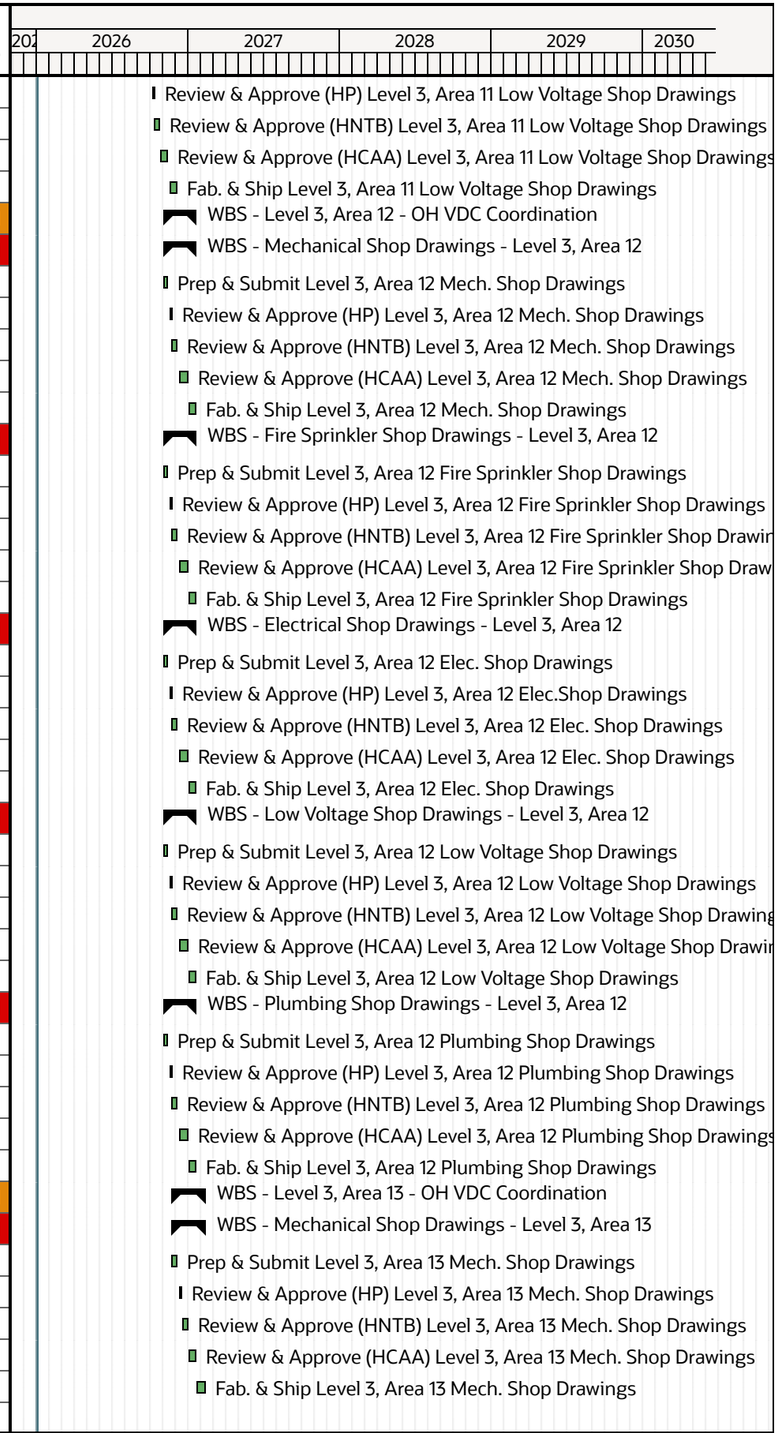

	ID	Name	Dur	Start	Finish	TF
4075	WBS - Fire Sprinkler Shop Drawings - Level 3, Area 13		54.0d	19-Nov-26	8-Feb-27	90.0d
4076	PR-VDC-L3A13-3010	Prep & Submit Level 3, Area 13 Fire Sprinkler Shop Drawings	10.0d	19-Nov-26	4-Dec-26	90.0d
4077	PR-VDC-L3A13-3020	Review & Approve (HP) Level 3, Area 13 Fire Sprinkler Shop Drawings	5.0d	7-Dec-26	11-Dec-26	90.0d
4078	PR-VDC-L3A13-3030	Review & Approve (HNTB) Level 3, Area 13 Fire Sprinkler Shop Drawings	10.0d	14-Dec-26	28-Dec-26	90.0d
4079	PR-VDC-L3A13-3040	Review & Approve (HCAA) Level 3, Area 13 Fire Sprinkler Shop Drawings	15.0d	29-Dec-26	19-Jan-27	90.0d
4080	PR-VDC-L3A13-3050	Fab. & Ship Level 3, Area 13 Fire Sprinkler Shop Drawings	20.0d	20-Jan-27	8-Feb-27	125.0d
4081	WBS - Plumbing Shop Drawings - Level 3, Area 13		54.0d	19-Nov-26	8-Feb-27	100.0d
4082	PR-VDC-L3A13-3110	Prep & Submit Level 3, Area 13 Plumbing Shop Drawings	10.0d	19-Nov-26	4-Dec-26	100.0d
4083	PR-VDC-L3A13-3120	Review & Approve (HP) Level 3, Area 13 Plumbing Shop Drawings	5.0d	7-Dec-26	11-Dec-26	100.0d
4084	PR-VDC-L3A13-3130	Review & Approve (HNTB) Level 3, Area 13 Plumbing Shop Drawings	10.0d	14-Dec-26	28-Dec-26	100.0d
4085	PR-VDC-L3A13-3140	Review & Approve (HCAA) Level 3, Area 13 Plumbing Shop Drawings	15.0d	29-Dec-26	19-Jan-27	100.0d
4086	PR-VDC-L3A13-3150	Fab. & Ship Level 3, Area 13 Plumbing Shop Drawings	20.0d	20-Jan-27	8-Feb-27	139.0d
4087	WBS - Electrical Shop Drawings - Level 3, Area 13		54.0d	19-Nov-26	8-Feb-27	95.0d
4088	PR-VDC-L3A13-3160	Prep & Submit Level 3, Area 13 Elec. Shop Drawings	10.0d	19-Nov-26	4-Dec-26	95.0d
4089	PR-VDC-L3A13-3170	Review & Approve (HP) Level 3, Area 13 Elec.Shop Drawings	5.0d	7-Dec-26	11-Dec-26	95.0d
4090	PR-VDC-L3A13-3180	Review & Approve (HNTB) Level 3, Area 13 Elec. Shop Drawings	10.0d	14-Dec-26	28-Dec-26	95.0d
4091	PR-VDC-L3A13-3190	Review & Approve (HCAA) Level 3, Area 13 Elec. Shop Drawings	15.0d	29-Dec-26	19-Jan-27	95.0d
4092	PR-VDC-L3A13-3200	Fab. & Ship Level 3, Area 13 Elec. Shop Drawings	20.0d	20-Jan-27	8-Feb-27	132.0d
4093	WBS - Low Voltage Shop Drawings - Level 3, Area 13		54.0d	19-Nov-26	8-Feb-27	163.0d
4094	PR-VDC-L3A13-3210	Prep & Submit Level 3, Area 13 Low Voltage Shop Drawings	10.0d	19-Nov-26	4-Dec-26	163.0d
4095	PR-VDC-L3A13-3220	Review & Approve (HP) Level 3, Area 13 Low Voltage Shop Drawings	5.0d	7-Dec-26	11-Dec-26	163.0d
4096	PR-VDC-L3A13-3230	Review & Approve (HNTB) Level 3, Area 13 Low Voltage Shop Drawings	10.0d	14-Dec-26	28-Dec-26	163.0d
4097	PR-VDC-L3A13-3240	Review & Approve (HCAA) Level 3, Area 13 Low Voltage Shop Drawings	15.0d	29-Dec-26	19-Jan-27	163.0d
4098	PR-VDC-L3A13-3250	Fab. & Ship Level 3, Area 13 Low Voltage Shop Drawings	20.0d	20-Jan-27	8-Feb-27	227.0d
4099	WBS - Level 3, Area 14 - OH VDC Coordination		54.0d	14-Dec-26	1-Mar-27	162.0d
4100	WBS - Mechanical Shop Drawings - Level 3, Area 14		54.0d	14-Dec-26	1-Mar-27	107.0d
4101	PR-VDC-L3A14-3330	Prep & Submit Level 3, Area 14 Mech. Shop Drawings	10.0d	14-Dec-26	28-Dec-26	107.0d
4102	PR-VDC-L3A14-3340	Review & Approve (HP) Level 3, Area 14 Mech. Shop Drawings	5.0d	29-Dec-26	5-Jan-27	107.0d
4103	PR-VDC-L3A14-3310	Review & Approve (HNTB) Level 3, Area 14 Mech. Shop Drawings	10.0d	6-Jan-27	19-Jan-27	107.0d
4104	PR-VDC-L3A14-3320	Review & Approve (HCAA) Level 3, Area 14 Mech. Shop Drawings	15.0d	20-Jan-27	9-Feb-27	107.0d
4105	PR-VDC-L3A14-3350	Fab. & Ship Level 3, Area 14 Mech. Shop Drawings	20.0d	10-Feb-27	1-Mar-27	149.0d
4106	WBS - Fire Sprinkler Shop Drawings - Level 3, Area 14		54.0d	14-Dec-26	1-Mar-27	89.0d
4107	PR-VDC-L3A14-3260	Prep & Submit Level 3, Area 14 Fire Sprinkler Shop Drawings	10.0d	14-Dec-26	28-Dec-26	88.0d
4108	PR-VDC-L3A14-3270	Review & Approve (HP) Level 3, Area 14 Fire Sprinkler Shop Drawings	5.0d	29-Dec-26	5-Jan-27	88.0d
4109	PR-VDC-L3A14-3280	Review & Approve (HNTB) Level 3, Area 14 Fire Sprinkler Shop Drawings	10.0d	6-Jan-27	19-Jan-27	88.0d
4110	PR-VDC-L3A14-3290	Review & Approve (HCAA) Level 3, Area 14 Fire Sprinkler Shop Drawings	15.0d	20-Jan-27	9-Feb-27	88.0d
4111	PR-VDC-L3A14-3300	Fab. & Ship Level 3, Area 14 Fire Sprinkler Shop Drawings	20.0d	10-Feb-27	1-Mar-27	123.0d
4112	WBS - Electrical Shop Drawings - Level 3, Area 14		54.0d	14-Dec-26	1-Mar-27	94.0d
4113	PR-VDC-L3A14-3410	Prep & Submit Level 3, Area 14 Elec. Shop Drawings	10.0d	14-Dec-26	28-Dec-26	93.0d
4114	PR-VDC-L3A14-3420	Review & Approve (HP) Level 3, Area 14 Elec.Shop Drawings	5.0d	29-Dec-26	5-Jan-27	93.0d
4115	PR-VDC-L3A14-3430	Review & Approve (HNTB) Level 3, Area 14 Elec. Shop Drawings	10.0d	6-Jan-27	19-Jan-27	93.0d
4116	PR-VDC-L3A14-3440	Review & Approve (HCAA) Level 3, Area 14 Elec. Shop Drawings	15.0d	20-Jan-27	9-Feb-27	93.0d




	ID	Name	Dur	Start	Finish	TF
4117	PR-VDC-L3A14-3450	Fab. & Ship Level 3, Area 14 Elec. Shop Drawings	20.0d	10-Feb-27	1-Mar-27	130.0d
4118	WBS - Low Voltage Shop Drawings - Level 3, Area 14		54.0d	14-Dec-26	1-Mar-27	162.0d
4119	PR-VDC-L3A14-3460	Prep & Submit Level 3, Area 14 Low Voltage Shop Drawings	10.0d	14-Dec-26	28-Dec-26	162.0d
4120	PR-VDC-L3A14-3470	Review & Approve (HP) Level 3, Area 14 Low Voltage Shop Drawings	5.0d	29-Dec-26	5-Jan-27	162.0d
4121	PR-VDC-L3A14-3480	Review & Approve (HNTB) Level 3, Area 14 Low Voltage Shop Drawings	10.0d	6-Jan-27	19-Jan-27	162.0d
4122	PR-VDC-L3A14-3490	Review & Approve (HCAA) Level 3, Area 14 Low Voltage Shop Drawings	15.0d	20-Jan-27	9-Feb-27	162.0d
4123	PR-VDC-L3A14-3500	Fab. & Ship Level 3, Area 14 Low Voltage Shop Drawings	20.0d	10-Feb-27	1-Mar-27	226.0d
4124	WBS - Plumbing Shop Drawings - Level 3, Area 14		54.0d	14-Dec-26	1-Mar-27	99.0d
4125	PR-VDC-L3A14-3360	Prep & Submit Level 3, Area 14 Plumbing Shop Drawings	10.0d	14-Dec-26	28-Dec-26	98.0d
4126	PR-VDC-L3A14-3370	Review & Approve (HP) Level 3, Area 14 Plumbing Shop Drawings	5.0d	29-Dec-26	5-Jan-27	98.0d
4127	PR-VDC-L3A14-3380	Review & Approve (HNTB) Level 3, Area 14 Plumbing Shop Drawings	10.0d	6-Jan-27	19-Jan-27	98.0d
4128	PR-VDC-L3A14-3390	Review & Approve (HCAA) Level 3, Area 14 Plumbing Shop Drawings	15.0d	20-Jan-27	9-Feb-27	98.0d
4129	PR-VDC-L3A14-3400	Fab. & Ship Level 3, Area 14 Plumbing Shop Drawings	20.0d	10-Feb-27	1-Mar-27	137.0d
4130	WBS - Level 3, Club/Nov. Steel Area - OH VDC Coordination		39.0d	13-Apr-26	6-Jun-26	73.0d
4131	WBS - Mechanical Shop Drawings - Level 3, Club/Nov. Steel Area		39.0d	13-Apr-26	6-Jun-26	73.0d
4132	PR-VDC-L3CL-3580	Prep & Submit Level 3, Club/Nov. Steel Area Mech. Shop Drawings	10.0d	13-Apr-26	24-Apr-26	72.0d
4133	PR-VDC-L3CL-3590	Review & Approve (HP) Level 3, Club/Nov. Steel Area Mech. Shop Drawings	5.0d	27-Apr-26	1-May-26	72.0d
4134	PR-VDC-L3CL-3560	Review & Approve (HNTB) Level 3, Club/Nov. Steel Area Mech. Shop Drawings	5.0d	4-May-26	8-May-26	72.0d
4135	PR-VDC-L3CL-3570	Review & Approve (HCAA) Level 3, Club/Nov. Steel Area Mech. Shop Drawings	15.0d	11-May-26	1-Jun-26	72.0d
4136	PR-VDC-L3CL-3600	Fab. & Ship Level 3, Club/Nov. Steel Area Mech. Shop Drawings	5.0d	2-Jun-26	6-Jun-26	101.0d
4137	WBS - Fire Sprinkler Shop Drawings - Level 3, Club/Nov. Steel Area		39.0d	13-Apr-26	6-Jun-26	73.0d
4138	PR-VDC-L3CL-3510	Prep & Submit Level 3, Club/Nov. Steel Area Fire Sprinkler Shop Drawings	10.0d	13-Apr-26	24-Apr-26	72.0d
4139	PR-VDC-L3CL-3520	Review & Approve (HP) Level 3, Club/Nov. Steel Area Fire Sprinkler Shop Drawi...	5.0d	27-Apr-26	1-May-26	72.0d
4140	PR-VDC-L3CL-3530	Review & Approve (HNTB) Level 3, Club/Nov. Steel Area Fire Sprinkler Shop Dra...	5.0d	4-May-26	8-May-26	72.0d
4141	PR-VDC-L3CL-3540	Review & Approve (HCAA) Level 3, Club/Nov. Steel Area Fire Sprinkler Shop Dr...	15.0d	11-May-26	1-Jun-26	72.0d
4142	PR-VDC-L3CL-3550	Fab. & Ship Level 3, Club/Nov. Steel Area Fire Sprinkler Shop Drawings	5.0d	2-Jun-26	6-Jun-26	101.0d
4143	WBS - Plumbing Shop Drawings - Level 3, Club/Nov. Steel Area		39.0d	13-Apr-26	6-Jun-26	73.0d
4144	PR-VDC-L3CL-3610	Prep & Submit Level 3, Club/Nov. Steel Area Plumbing Shop Drawings	10.0d	13-Apr-26	24-Apr-26	72.0d
4145	PR-VDC-L3CL-3620	Review & Approve (HP) Level 3, Club/Nov. Steel Area Plumbing Shop Drawings	5.0d	27-Apr-26	1-May-26	72.0d
4146	PR-VDC-L3CL-3630	Review & Approve (HNTB) Level 3, Club/Nov. Steel Area Plumbing Shop Drawings	5.0d	4-May-26	8-May-26	72.0d
4147	PR-VDC-L3CL-3640	Review & Approve (HCAA) Level 3, Club/Nov. Steel Area Plumbing Shop Drawin...	15.0d	11-May-26	1-Jun-26	72.0d
4148	PR-VDC-L3CL-3650	Fab. & Ship Level 3, Club/Nov. Steel Area Plumbing Shop Drawings	5.0d	2-Jun-26	6-Jun-26	101.0d
4149	WBS - Electrical Shop Drawings - Level 3, Club/Nov. Steel Area		39.0d	13-Apr-26	6-Jun-26	73.0d
4150	PR-VDC-L3CL-3660	Prep & Submit Level 3, Club/Nov. Steel Area Elec. Shop Drawings	10.0d	13-Apr-26	24-Apr-26	72.0d
4151	PR-VDC-L3CL-3670	Review & Approve (HP) Level 3, Club/Nov. Steel Area Elec.Shop Drawings	5.0d	27-Apr-26	1-May-26	72.0d
4152	PR-VDC-L3CL-3680	Review & Approve (HNTB) Level 3, Club/Nov. Steel Area Elec. Shop Drawings	5.0d	4-May-26	8-May-26	72.0d
4153	PR-VDC-L3CL-3690	Review & Approve (HCAA) Level 3, Club/Nov. Steel Area Elec. Shop Drawings	15.0d	11-May-26	1-Jun-26	72.0d
4154	PR-VDC-L3CL-3700	Fab. & Ship Level 3, Club/Nov. Steel Area Elec. Shop Drawings	5.0d	2-Jun-26	6-Jun-26	101.0d
4155	WBS - Low Voltage Shop Drawings - Level 3, Club/Nov. Steel Area		39.0d	13-Apr-26	6-Jun-26	73.0d
4156	PR-VDC-L3CL-3710	Prep & Submit Level 3, Club/Nov. Steel Area Low Voltage Shop Drawings	10.0d	13-Apr-26	24-Apr-26	72.0d
4157	PR-VDC-L3CL-3720	Review & Approve (HP) Level 3, Club/Nov. Steel Area Low Voltage Shop Drawings	5.0d	27-Apr-26	1-May-26	72.0d
4158	PR-VDC-L3CL-3730	Review & Approve (HNTB) Level 3, Club/Nov. Steel Area Low Voltage Shop Dra...	5.0d	4-May-26	8-May-26	72.0d



	ID	Name	Dur	Start	Finish	TF
4159	PR-VDC-L3CL-3740	Review & Approve (HCAA) Level 3, Club/Nov. Steel Area Low Voltage Shop Dra...	15.0d	11-May-26	1-Jun-26	72.0d
4160	PR-VDC-L3CL-3750	Fab. & Ship Level 3, Club/Nov. Steel Area Low Voltage Shop Drawings	5.0d	2-Jun-26	6-Jun-26	101.0d
4161	WBS - Level 3, Club 1&2 - OH VDC Coordination		44.0d	27-Apr-26	27-Jun-26	266.0d
4162	WBS - Mechanical Shop Drawings - Level 3, Club 1&2		44.0d	27-Apr-26	27-Jun-26	189.0d
4163	PR-VDC-L3CL1-3830	Prep & Submit Level 3, Club 1&2 Area Mech. Shop Drawings	10.0d	27-Apr-26	8-May-26	190.0d
4164	PR-VDC-L3CL1-3840	Review & Approve (HP) Level 3, Club 1&2 Area Mech. Shop Drawings	5.0d	11-May-26	15-May-26	190.0d
4165	PR-VDC-L3CL1-3810	Review & Approve (HNTB) Level 3, Club 1&2 Area Mech. Shop Drawings	10.0d	18-May-26	1-Jun-26	190.0d
4166	PR-VDC-L3CL1-3820	Review & Approve (HCAA) Level 3, Club 1&2 Area Mech. Shop Drawings	15.0d	2-Jun-26	22-Jun-26	190.0d
4167	PR-VDC-L3CL1-3850	Fab. & Ship Level 3, Club 1&2 Area Mech. Shop Drawings	5.0d	23-Jun-26	27-Jun-26	267.0d
4168	WBS - Fire Sprinkler Shop Drawings - Level 3, Club 1&2		44.0d	27-Apr-26	27-Jun-26	187.0d
4169	PR-VDC-L3CL1-3760	Prep & Submit Level 3, Club 1&2 Area Fire Sprinkler Shop Drawings	10.0d	27-Apr-26	8-May-26	188.0d
4170	PR-VDC-L3CL1-3770	Review & Approve (HP) Level 3, Club 1&2 Area Fire Sprinkler Shop Drawings	5.0d	11-May-26	15-May-26	188.0d
4171	PR-VDC-L3CL1-3780	Review & Approve (HNTB) Level 3, Club 1&2 Area Fire Sprinkler Shop Drawings	10.0d	18-May-26	1-Jun-26	188.0d
4172	PR-VDC-L3CL1-3790	Review & Approve (HCAA) Level 3, Club 1&2 Area Fire Sprinkler Shop Drawings	15.0d	2-Jun-26	22-Jun-26	188.0d
4173	PR-VDC-L3CL1-3800	Fab. & Ship Level 3, Club 1&2 Area Fire Sprinkler Shop Drawings	5.0d	23-Jun-26	27-Jun-26	263.0d
4174	WBS - Plumbing Shop Drawings - Level 3, Club 1&2		44.0d	27-Apr-26	27-Jun-26	191.0d
4175	PR-VDC-L3CL1-3860	Prep & Submit Level 3, Club 1&2 Area Plumbing Shop Drawings	10.0d	27-Apr-26	8-May-26	192.0d
4176	PR-VDC-L3CL1-3870	Review & Approve (HP) Level 3, Club 1&2 Area Plumbing Shop Drawings	5.0d	11-May-26	15-May-26	192.0d
4177	PR-VDC-L3CL1-3880	Review & Approve (HNTB) Level 3, Club 1&2 Area Plumbing Shop Drawings	10.0d	18-May-26	1-Jun-26	192.0d
4178	PR-VDC-L3CL1-3890	Review & Approve (HCAA) Level 3, Club 1&2 Area Plumbing Shop Drawings	15.0d	2-Jun-26	22-Jun-26	192.0d
4179	PR-VDC-L3CL1-3900	Fab. & Ship Level 3, Club 1&2 Area Plumbing Shop Drawings	5.0d	23-Jun-26	27-Jun-26	269.0d
4180	WBS - Electrical Shop Drawings - Level 3, Club 1&2		44.0d	27-Apr-26	27-Jun-26	177.0d
4181	PR-VDC-L3CL1-3910	Prep & Submit Level 3, Club 1&2 Area Elec. Shop Drawings	10.0d	27-Apr-26	8-May-26	178.0d
4182	PR-VDC-L3CL1-3920	Review & Approve (HP) Level 3, Club 1&2 Area Elec.Shop Drawings	5.0d	11-May-26	15-May-26	178.0d
4183	PR-VDC-L3CL1-3930	Review & Approve (HNTB) Level 3, Club 1&2 Area Elec. Shop Drawings	10.0d	18-May-26	1-Jun-26	178.0d
4184	PR-VDC-L3CL1-3940	Review & Approve (HCAA) Level 3, Club 1&2 Area Elec. Shop Drawings	15.0d	2-Jun-26	22-Jun-26	178.0d
4185	PR-VDC-L3CL1-3950	Fab. & Ship Level 3, Club 1&2 Area Elec. Shop Drawings	5.0d	23-Jun-26	27-Jun-26	249.0d
4186	WBS - Low Voltage Shop Drawings - Level 3, Club 1&2		44.0d	27-Apr-26	27-Jun-26	266.0d
4187	PR-VDC-L3CL1-3960	Prep & Submit Level 3, Club 1&2 Area Low Voltage Shop Drawings	10.0d	27-Apr-26	8-May-26	266.0d
4188	PR-VDC-L3CL1-3970	Review & Approve (HP) Level 3, Club 1&2 Area Low Voltage Shop Drawings	5.0d	11-May-26	15-May-26	266.0d
4189	PR-VDC-L3CL1-3980	Review & Approve (HNTB) Level 3, Club 1&2 Area Low Voltage Shop Drawings	10.0d	18-May-26	1-Jun-26	266.0d
4190	PR-VDC-L3CL1-3990	Review & Approve (HCAA) Level 3, Club 1&2 Area Low Voltage Shop Drawings	15.0d	2-Jun-26	22-Jun-26	266.0d
4191	PR-VDC-L3CL1-4000	Fab. & Ship Level 3, Club 1&2 Area Low Voltage Shop Drawings	5.0d	23-Jun-26	27-Jun-26	372.0d
4192	WBS - ASD - CONSTRUCTION PHASE		1,081.0d	13-Dec-24 A	16-Mar-29	258.0d
4193	WBS - ASD Mock Up's		190.0d	6-Feb-26	3-Nov-26	352.0d
4194	WBS - ASD Restroom Mock Up		190.0d	6-Feb-26	3-Nov-26	352.0d
4195	ASD-MU-600	ASD Restroom Submittal's Approval	120.0d	6-Feb-26	27-Jul-26	352.0d
4196	ASD-MU-580	Complete ASD Restroom Mock Up	60.0d	28-Jul-26	20-Oct-26	352.0d
4197	ASD-MU-590	Owner Restroom Mock Up Approval - ASD Mock Up	10.0d	21-Oct-26	3-Nov-26	352.0d
4198	WBS - ASD Exterior Assemblies Mock Up		60.0d	1-Jun-26	24-Aug-26	81.0d
4199	ASD-MU-300	Grade MU Pad - ASD Mock Up	5.0d	1-Jun-26	5-Jun-26	81.0d
4200	ASD-MU-430	Excavate Found. - ASD Mock Up	3.0d	8-Jun-26	10-Jun-26	81.0d




	ID	Name	Dur	Start	Finish	TF
4201	ASD-MU-400	FRP Found. - ASD Mock Up	5.0d	11-Jun-26	17-Jun-26	81.0d
4202	ASD-MU-440	Install Waterproofing On Found. - ASD Mock Up	5.0d	18-Jun-26	24-Jun-26	81.0d
4203	ASD-MU-450	Backfill Found. - ASD Mock Up	5.0d	25-Jun-26	1-Jul-26	81.0d
4204	ASD-MU-470	Install Flashing/Compressible Filler - ASD Mock Up	5.0d	25-Jun-26	1-Jul-26	91.0d
4205	ASD-MU-460	FRP MU SOG - ASD Mock Up	5.0d	2-Jul-26	9-Jul-26	81.0d
4206	ASD-MU-480	Install MU Steel Support/Bracing - ASD Mock Up	5.0d	10-Jul-26	16-Jul-26	81.0d
4207	ASD-MU-410	Install Pre-Cast System (WA-10) - ASD Mock Up	5.0d	17-Jul-26	23-Jul-26	81.0d
4208	ASD-MU-500	Install Door Frames & Hardware Apron - ASD Mock Up	2.0d	24-Jul-26	27-Jul-26	86.0d
4209	ASD-MU-490	Install Metal Wall Panel System - ASD Mock Up	5.0d	24-Jul-26	30-Jul-26	83.0d
4210	ASD-MU-540	Install Framing for Eave & Roofing System- ASD Mock Up	5.0d	24-Jul-26	30-Jul-26	81.0d
4211	ASD-MU-420	Install Louver System - ASD Mock Up	2.0d	31-Jul-26	3-Aug-26	81.0d
4212	ASD-MU-510	Install Door Frames & Hardware PBB - ASD Mock Up	2.0d	31-Jul-26	3-Aug-26	83.0d
4213	ASD-MU-560	Install Spray Foam Insulation - ASD Mock Up	2.0d	31-Jul-26	3-Aug-26	81.0d
4214	ASD-MU-100	Install Curtain Wall System - ASD Mock Up	5.0d	4-Aug-26	10-Aug-26	81.0d
4215	ASD-MU-520	Install Utility Stub Outs PPB Wall - ASD Mock Up	3.0d	4-Aug-26	6-Aug-26	83.0d
4216	ASD-MU-550	Install Roofing & Gutter System - ASD Mock Up	5.0d	4-Aug-26	10-Aug-26	81.0d
4217	ASD-MU-200	Install Roof Fascia System - ASD Mock Up	5.0d	11-Aug-26	17-Aug-26	81.0d
4218	ASD-MU-530	Install Downspout - ASD Mock Up	3.0d	18-Aug-26	20-Aug-26	81.0d
4219	ASD-MU-570	Owner Mock Up Approval - ASD Mock Up	2.0d	21-Aug-26	24-Aug-26	81.0d
4220	WBS - Enabling		296.0d	13-Dec-24 A	12-Feb-26	785.0d
4221	WBS - Milestones		236.0d	13-Dec-24 A	14-Nov-25 A	
4222	EN-MLS-10	Notice to Proceed / Enabling Scope Construction Start	0.0d	13-Dec-24 A		
4223	EN-MLS-20	Personnel Transition to Trailers Complete	0.0d		3-Oct-25 A	
4224	EN-MLS-40	ASD - Enabling Water Line Complete	0.0d		14-Nov-25 A	
4225	WBS - Hammocks		296.0d	13-Dec-24 A	12-Feb-26	785.0d
4226	EN-HAM-10	Enabling Scope (GCs/Markups) - (LOE)	296.0d	13-Dec-24 A	12-Feb-26	785.0d
4227	EN-HAM-30	Fuel Tank Relocation Scope - (LOE)	25.0d	19-Feb-25 A	25-Mar-25 A	
4228	EN-HAM-20	Bessie Coleman Closure Detour Scope - (LOE)	83.0d	21-Apr-25 A	15-Aug-25 A	
4229	WBS - Phase A Work Area		200.0d	7-Jan-25 A	16-Oct-25 A	
4230	EN-DM-PHA-10	Install Low Profile Barricades North Of VSR & SW Of VSR at TOFA Boundaries - ...	4.0d	7-Jan-25 A	10-Jan-25 A	
4231	EN-DM-PHA-20	Demo Exist. Taxiway B Markings - Phase A	2.0d	30-Jan-25 A	31-Jan-25 A	
4232	EN-DM-PHA-50	Demo Exist. Taxiway V Markings - Phase A	2.0d	31-Jan-25 A	3-Feb-25 A	
4233	EN-DM-PHA-110	Paint Edge Markings At Taxiway - Phase A	1.0d	5-Feb-25 A	5-Feb-25 A	
4234	EN-DM-PHA-80	De-Energize Exist. Taxiway Apron LTNG - Phase A	3.0d	27-Feb-25 A	3-Mar-25 A	
4235	EN-DM-PHA-40	Demo Exist. Taxiway Apron LTNG, Wiring & Conduit (Store Fixtures Safely) - Ph...	1.0d	4-Mar-25 A	4-Mar-25 A	
4236	EN-DM-PHA-30	Demo Exist. Taxiway U Markings At NE On VSR - Phase A	1.0d	14-Mar-25 A	14-Mar-25 A	
4237	EN-DM-PHA-90	Paint Directional Markings In Area At New VSR (Centerline, Edge, Stop Marking...	2.0d	18-Mar-25 A	19-Mar-25 A	
4238	EN-DM-PHA-120	Install White, Semi-Flushed Roadway Reflectors - Phase A	2.0d	18-Mar-25 A	19-Mar-25 A	
4239	EN-DM-PHA-60	Demo Exist. Taxi Lane Z/Stop Bar Markings on SW Of VSR - Phase A	1.0d	25-Apr-25 A	25-Apr-25 A	
4240	EN-DM-PHA-100	Paint Edge Markings At Zipper Roadway - Phase A	1.0d	25-Apr-25 A	25-Apr-25 A	
4241	EN-DM-PHA-130	Install Signage - Phase A	5.0d	28-Jul-25 A	1-Aug-25 A	
4242	EN-DM-PHA-70	Obscure & Demo Exist. Airfield Guidance Signage - Phase A	1.0d	16-Oct-25 A	16-Oct-25 A	

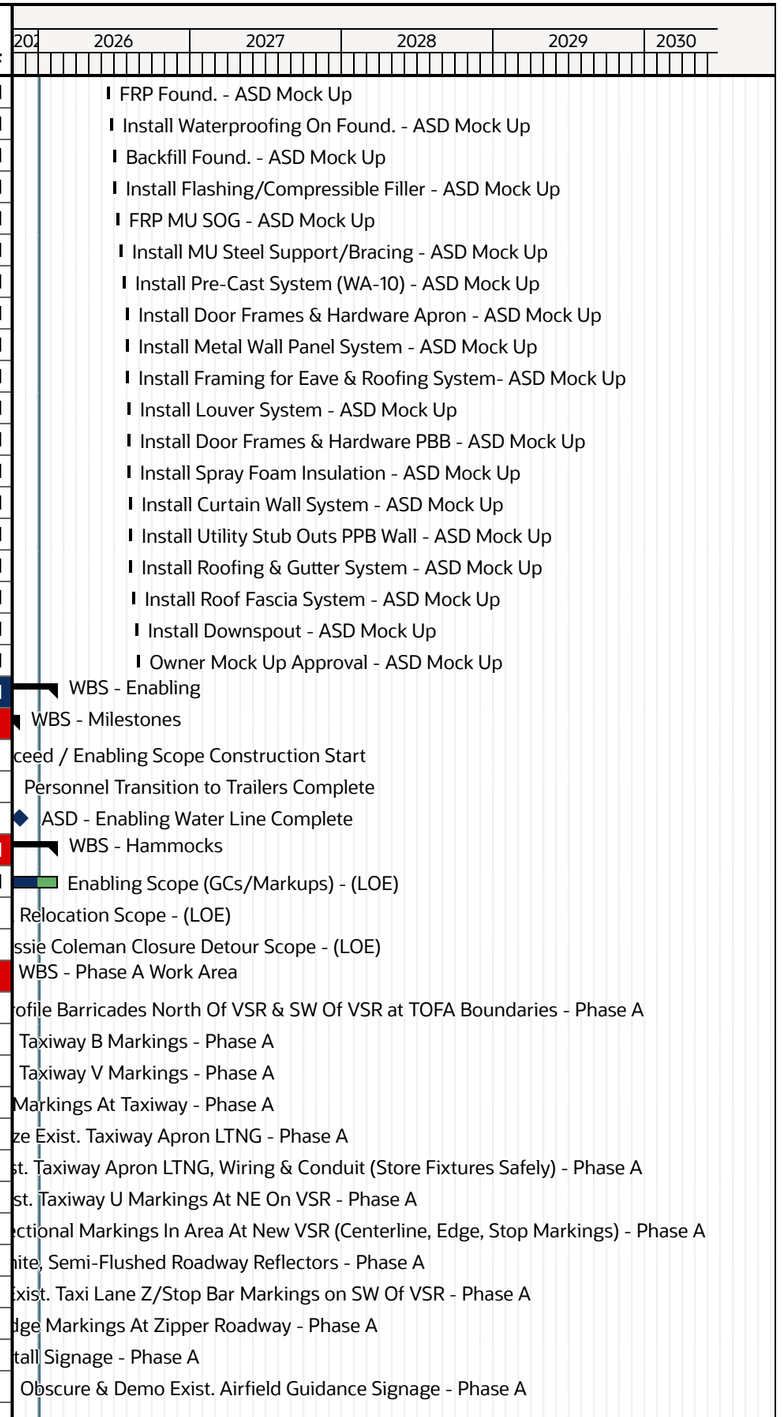


	ID	Name	Dur	Start	Finish	TF
4243	WBS - Phase B Work Area		230.0d	27-Jan-25 A	19-Dec-25 A	
4244	WBS - Trailer Complex		230.0d	27-Jan-25 A	19-Dec-25 A	
4245	WBS - Parking Lot		207.0d	27-Jan-25 A	14-Nov-25 A	
4246	EN-AT-PL-10	Construct Sediment Barrier/Staked Turbidity Barrier Erosion Control - Phase B ...	10.0d	27-Jan-25 A	7-Feb-25 A	
4247	EN-AT-PL-340	Demo Exist. AOA Fence - Phase B Parking Lot	4.0d	18-Feb-25 A	21-Feb-25 A	
4248	EN-AT-PL-20	Clear & Grub - Phase B Parking Lot	8.0d	24-Feb-25 A	5-Mar-25 A	
4249	EN-AT-PL-70	Install / Shape Ditch at Parking Perimeter - Phase B Parking Lot	15.0d	24-Feb-25 A	14-Mar-25 A	
4250	EN-AT-PL-130	Cut Exist. Grade & Lvl. To Base Elevation - Phase B Parking Lot	3.0d	6-Mar-25 A	10-Mar-25 A	
4251	EN-AT-PL-160	Fill & Compact Subgrade Layer - Phase B Parking Lot	3.0d	6-Mar-25 A	10-Mar-25 A	
4252	EN-AT-PL-180	Fill & Compact 6" Base Layers - Phase B Parking Lot	3.0d	11-Mar-25 A	14-Mar-25 A	
4253	EN-AT-PL-150	Install Underg. Utilities In Parking Lot for Lights, EV Stations & Cameras - Phase...	19.0d	18-Mar-25 A	11-Apr-25 A	
4254	EN-AT-PL-30	Install Elec. Infrastructure Main to Complex - (For TECO Main) - Phase B Parkin...	42.0d	14-Apr-25 A	11-Jun-25 A	
4255	EN-AT-PL-140	Install UG Utilities/Data For New Guard Booth - Phase B Parking Lot	37.0d	23-Apr-25 A	13-Jun-25 A	
4256	EN-AT-PL-50	Install Data Infrastructure to Complex - (For Frontier Main) - Phase B Parking Lot	15.0d	27-May-25 A	16-Jun-25 A	
4257	EN-AT-PL-60	Install 66' OF 14" x 23" ERCP (S-210, S-211) - Phase B Parking Lot	9.0d	27-May-25 A	6-Jun-25 A	
4258	EN-AT-PL-200	FRP Elec. Equip. Pads - Phase B Parking Lot	15.0d	3-Jun-25 A	23-Jun-25 A	
4259	EN-AT-PL-210	Set Elec. Equip. - Phase B Parking Lot	15.0d	4-Jun-25 A	24-Jun-25 A	
4260	EN-AT-PL-90	Install 6' x 2' Sumps (2 each) - Phase B Parking Lot	2.0d	9-Jun-25 A	10-Jun-25 A	
4261	EN-AT-PL-220	Install Paving - Phase B Parking Lot	4.0d	11-Jun-25 A	16-Jun-25 A	
4262	EN-AT-PL-120	Trailer Complex TECO Transformer Live - Phase B Parking Lot	0.0d		11-Jun-25 A	
4263	EN-AT-PL-80	Install 3" FM To Lift Station Location - Phase B Parking Lot	25.0d	14-Jul-25 A	15-Aug-25 A	
4264	EN-AT-PL-280	Install LTNG Poles/ Fixtures - Phase B Parking Lot	20.0d	28-Jul-25 A	22-Aug-25 A	
4265	EN-AT-PL-170	Provide Power & Disconnect to the Lift Station - Phase B Parking Lot	5.0d	28-Jul-25 A	1-Aug-25 A	
4266	EN-AT-PL-360	Precon Meeting with COT - Phase B Parking Lot	0.0d	5-Aug-25 A		
4267	EN-AT-PL-370	Perform Layout & Locates- Phase B Parking Lot	5.0d	6-Aug-25 A	12-Aug-25 A	
4268	EN-AT-PL-270	Set Guard Shack & Connect Utilities - Phase B Parking Lot	10.0d	8-Aug-25 A	21-Aug-25 A	
4269	EN-AT-PL-250	Install Sanitary Lift Station at Trailers - Phase B Parking Lot	48.0d	18-Aug-25 A	23-Oct-25 A	
4270	EN-AT-PL-40	Install 12", 10" & 6" Water Main to Complex - Phase B Parking Lot	40.0d	25-Aug-25 A	10-Oct-25 A	
4271	EN-AT-PL-240	Install Temporary Striping - Phase B Parking Lot	3.0d	26-Aug-25 A	28-Aug-25 A	
4272	EN-AT-PL-330	Install Signage - Phase B Parking Lot	46.0d	12-Sep-25 A	14-Nov-25 A	
4273	EN-AT-PL-350	Install Paving - Phase B Parking Lot - West Entrance & Tie-in to Excellence Dr.	2.0d	17-Sep-25 A	18-Sep-25 A	
4274	EN-AT-PL-310	Install EV Station Pedestals - Phase B Parking Lot	3.0d	18-Sep-25 A	22-Sep-25 A	
4275	EN-AT-PL-320	Install Permanent Striping - Phase B Parking Lot	4.0d	23-Sep-25 A	26-Sep-25 A	
4276	EN-AT-PL-300	Install Break Area Structure - Phase B Parking Lot	9.0d	7-Oct-25 A	17-Oct-25 A	
4277	EN-AT-PL-110	Lay Sod at Perimeter - Phase B Parking Lot	5.0d	21-Oct-25 A	27-Oct-25 A	
4278	EN-AT-PL-380	DEP Approval	2.0d	6-Nov-25 A	7-Nov-25 A	
4279	EN-AT-PL-190	FRP For Submeter & Backflow Preventer Assembly - Phase B Parking Lot	3.0d	10-Nov-25 A	12-Nov-25 A	
4280	EN-AT-PL-100	Install 1" Water Service to Hose Bibb at Lift Station Location From 8" Water Sup...	3.0d	12-Nov-25 A	14-Nov-25 A	
4281	WBS - Office Trailers		168.0d	23-Apr-25 A	19-Dec-25 A	
4282	EN-AT-TC-90	Install Elec. Mains to All Office Trailers - Phase B	32.0d	23-Apr-25 A	6-Jun-25 A	
4283	EN-AT-TC-20	Install 2" Fiber Conduit from North Parking Lot to Office Trailers - Phase B	56.0d	23-Apr-25 A	11-Jul-25 A	
4284	EN-AT-TC-10	Install Office Trailers - Phase B	40.0d	19-May-25 A	15-Jul-25 A	




	ID	Name	Dur	Start	Finish	TF
4285	EN-AT-TC-60	Trim Out Trailer Seams & Roofing for Office Trailers - Phase B	39.0d	27-May-25 A	21-Jul-25 A	
4286	EN-AT-TC-180	Install 8" & 6" Sanitary Supply Lines to All Office Trailers - Phase B	20.0d	10-Jul-25 A	6-Aug-25 A	
4287	EN-AT-TC-100	Install Data Infrastructure to All Office Trailers - Phase B	11.0d	18-Jul-25 A	1-Aug-25 A	
4288	EN-AT-TC-80	Install Horizontal Data Cabling to Office Trailers - Phase B	15.0d	21-Jul-25 A	8-Aug-25 A	
4289	EN-AT-TC-220	Install Office Trailers' Furniture - Phase B	59.0d	21-Jul-25 A	10-Oct-25 A	
4290	EN-AT-TC-40	Install Ramp, Steps & Decks for Office Trailers - Phase B	19.0d	11-Aug-25 A	5-Sep-25 A	
4291	EN-AT-TC-110	Install 12" x 4"W Telecom Main Grounding Bar at 18" AFF To Bond All Office Tr...	5.0d	11-Aug-25 A	15-Aug-25 A	
4292	EN-AT-TC-190	Install Canopies to Office Trailers - Phase B	40.0d	18-Aug-25 A	13-Oct-25 A	
4293	EN-AT-TC-120	Terminate Data in Office Trailers IT Closet - Phase B	5.0d	18-Aug-25 A	22-Aug-25 A	
4294	EN-AT-TC-200	Install Gutters & Downspouts to Office Trailers - Phase B	21.0d	28-Aug-25 A	26-Sep-25 A	
4295	EN-AT-TC-130	IT Closet Server Install & Commission Office Trailers - Phase B	8.0d	29-Aug-25 A	10-Sep-25 A	
4296	EN-AT-TC-70	Install 8", 6", 2" & 1" Water Supply Lines w/All Associated Devices to All Office T...	29.0d	15-Sep-25 A	17-Oct-25 A	
4297	EN-AT-TC-150	Install Fire Hydrant (Office Trailers) - Phase B	1.0d	15-Sep-25 A	15-Sep-25 A	
4298	EN-AT-TC-170	Final Cleaning (Office Trailers) - Phase B	11.0d	1-Oct-25 A	15-Oct-25 A	
4299	EN-AT-TC-230	Personnel Trans. to Office Trailers Complete - Phase B	0.0d		3-Oct-25 A	
4300	EN-AT-TC-160	Install (4) 6" Steel Fire Hydrant Protection Pipe Bollards (Office Trailers) - Phase B	4.0d	4-Nov-25 A	7-Nov-25 A	
4301	EN-AT-TC-240	Install 1" Water Service to Hose Bibb from 2" Water Supply Main for Office Trail...	4.0d	11-Nov-25 A	14-Nov-25 A	
4302	EN-AT-TC-30	Install Above Ground Submeter Assembly on Slab for Office Trailers - Phase B	2.0d	12-Nov-25 A	13-Nov-25 A	
4303	EN-AT-TC-50	Install Backflow Preventer Assembly on Slab for Office Trailers - Phase B	2.0d	13-Nov-25 A	14-Nov-25 A	
4304	EN-AT-TC-210	Office Trailers City Insp. for CO - Phase B	4.0d	17-Nov-25 A	20-Nov-25 A	
4305	EN-AT-TC-235	Construct FDOT Asphaltic Concrete Curb & a FDOT Type II Trench Drain (RFI - E...	22.0d	24-Nov-25 A	19-Dec-25 A	
4306	WBS - Road to ASD Site From Trailer Complex		202.0d	19-Feb-25 A	4-Dec-25 A	
4307	EN-AT-RD-10	TSA / CBP / HCAA / HP Walk New AOA Fence & Trans. VSR Final Configuration	1.0d	9-Sep-25 A	9-Sep-25 A	
4308	EN-AT-RD-20	TSA / CBP / HCAA Comment Correction	2.0d	10-Sep-25 A	11-Sep-25 A	
4309	EN-AT-RD-30	Final TSA/CBP/HCAA/HP AOA Fence Walk	1.0d	12-Sep-25 A	12-Sep-25 A	
4310	EN-AT-RD-40	Trans. Access Road to Final Configuration	0.0d		12-Sep-25 A	
4311	WBS - North Gate		202.0d	19-Feb-25 A	4-Dec-25 A	
4312	EN-AT-RDNG-20	Remove/ Relocate Exist. Fence as Needed - Phase B North Gate	3.0d	19-Feb-25 A	21-Feb-25 A	
4313	EN-AT-RDNG-10	Layout Road & Sidewalk Perimeters - Phase B North Gate	5.0d	25-Feb-25 A	3-Mar-25 A	
4314	EN-AT-RDNG-40	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Phase ...	3.0d	25-Feb-25 A	27-Feb-25 A	
4315	EN-AT-RDNG-80	Install 52' Of 14"x23" ERCP (S-207, S-208, S-209) - Phase B North Gate	11.0d	27-May-25 A	10-Jun-25 A	
4316	EN-AT-RDNG-30	Remove Exist. Guard Shack - Phase B North Gate	1.0d	6-Jun-25 A	6-Jun-25 A	
4317	EN-AT-RDNG-50	Clear & Grub at Roadway - Phase B North Gate	3.0d	9-Jun-25 A	11-Jun-25 A	
4318	EN-AT-RDNG-70	Install UG Utilities/Data for New Guard Booth - (Approx. 450' +/-) - Phase B No...	24.0d	12-Jun-25 A	16-Jul-25 A	
4319	EN-AT-RDNG-110	Fill & Compact Subgrade Layer - Phase B North Gate	10.0d	12-Jun-25 A	25-Jun-25 A	
4320	EN-AT-RDNG-120	Fill & Compact 6" Base Layers - Phase B North Gate	23.0d	13-Jun-25 A	16-Jul-25 A	
4321	EN-AT-RDNG-60	Connect To Exist. AOA Fence w/Sliding Gates - Phase B North GSE	34.0d	18-Jun-25 A	5-Aug-25 A	
4322	EN-AT-RDNG-90	Install (2) 6' x 2' Sumps - Phase B North Gate	2.0d	28-Jul-25 A	29-Jul-25 A	
4323	EN-AT-RDNG-160	FRP Guard Shack Concrete Pad - Phase B North Gate	1.0d	4-Aug-25 A	4-Aug-25 A	
4324	EN-AT-RDNG-220	Connect To Exist. AOA Fence w/Sliding Gates - Phase B South GSE	2.0d	4-Aug-25 A	5-Aug-25 A	
4325	EN-AT-RDNG-180	Set Guard Shack & Connect Utilities - Phase B North Gate	10.0d	8-Aug-25 A	21-Aug-25 A	
4326	EN-AT-RDNG-170	Install Light Poles - Phase B North Gate	5.0d	18-Aug-25 A	22-Aug-25 A	

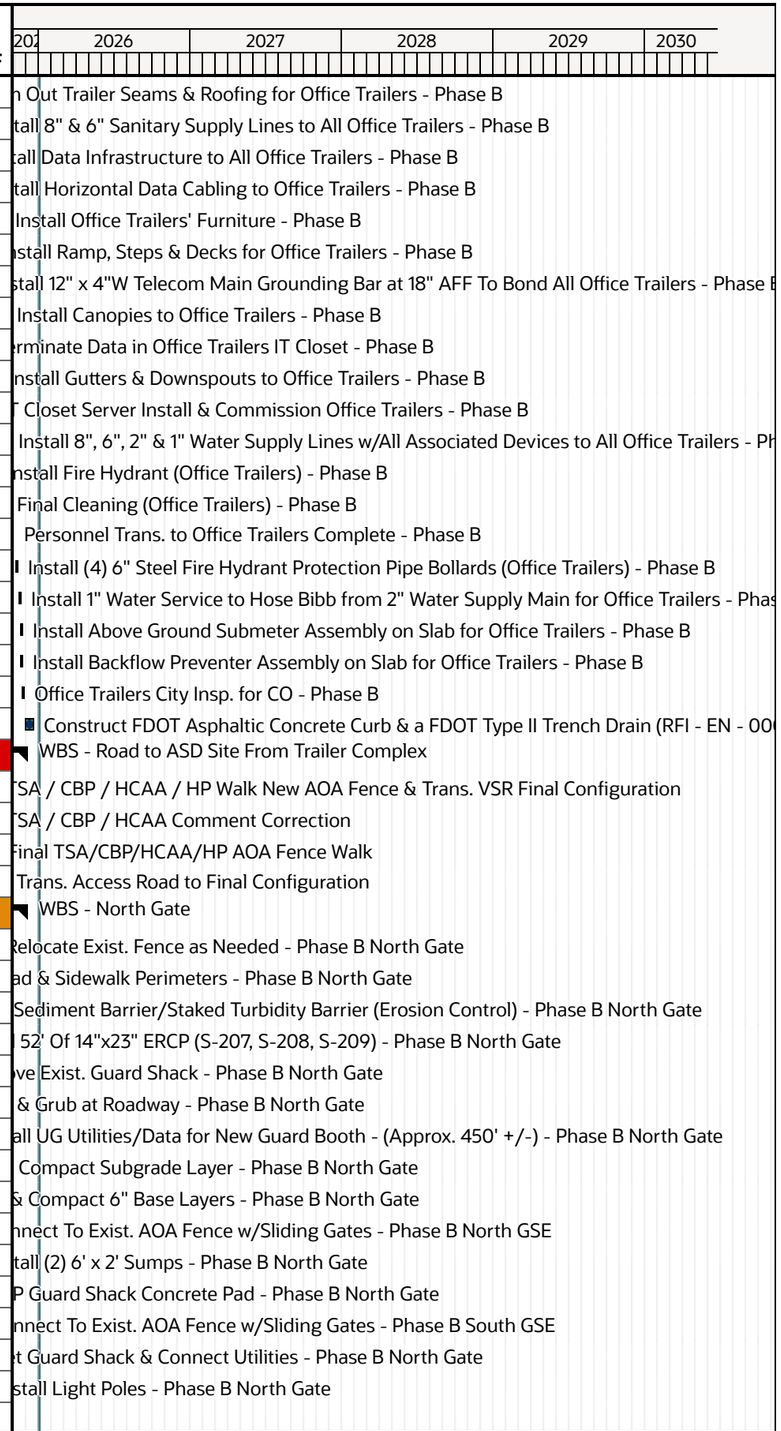


	ID	Name	Dur	Start	Finish	TF
4327	EN-AT-RDNG-190	Connect Guard Shack to Data/Power - Phase B North Gate	2.0d	21-Aug-25 A	22-Aug-25 A	
4328	EN-AT-RDNG-200	Install Cameras at Guard Gate - Phase B North Gate	3.0d	26-Aug-25 A	28-Aug-25 A	
4329	EN-AT-RDNG-130	Install Paving - 1st - 2" Lift - Phase B North Gate	1.0d	15-Sep-25 A	15-Sep-25 A	
4330	EN-AT-RDNG-210	Install Permanent Striping - Phase B North Gate	5.0d	15-Sep-25 A	19-Sep-25 A	
4331	EN-AT-RDNG-140	Install Paving - 2nd - 2" Lift - Phase B North Gate	1.0d	17-Sep-25 A	17-Sep-25 A	
4332	EN-AT-RDNG-150	Install Temporary Striping - Phase B North Gate	0.0d	19-Sep-25 A	19-Sep-25 A	
4333	EN-AT-RDNG-100	Lay Sod at Perimeter - Phase B North Gate	5.0d	26-Nov-25 A	4-Dec-25 A	
4334	WBS - South Gate		155.0d	20-Feb-25 A	29-Sep-25 A	
4335	EN-AT-RDSG-20	Remove AOA Exist. Fence - Phase B South Gate	5.0d	20-Feb-25 A	26-Feb-25 A	
4336	EN-AT-RDSG-10	Layout Road & Sidewalk Perimeters - Phase B South Gate	5.0d	4-Mar-25 A	10-Mar-25 A	
4337	EN-AT-RDSG-100	Fill & Compact Subgrade Layer - Phase B South Gate	4.0d	11-Mar-25 A	14-Mar-25 A	
4338	EN-AT-RDSG-30	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Phase ...	3.0d	11-Mar-25 A	13-Mar-25 A	
4339	EN-AT-RDSG-50	Install UG Utilities/Data For New Guard Booth - (Approx. 450' +/-) - Phase B So...	33.0d	27-May-25 A	11-Jul-25 A	
4340	EN-AT-RDSG-80	Install 52' Of 18" RCP To (2) 4' Of 30" RCP w/Concrete Jackets & S-200, S-201 ...	27.0d	2-Jun-25 A	9-Jul-25 A	
4341	EN-AT-RDSG-60	Install 73' At 12"x18" ERCP & S-206 - Phase B South Gate	5.0d	1-Jul-25 A	8-Jul-25 A	
4342	EN-AT-RDSG-70	Install 43' Of 18" RCP & 4' Of 24" RCP To 4' Of 30" & 42" RCP w/Concrete Jack...	12.0d	10-Jul-25 A	25-Jul-25 A	
4343	EN-AT-RDSG-150	FRP Guard Shack Pad - Phase B South Gate	2.0d	28-Jul-25 A	29-Jul-25 A	
4344	EN-AT-RDSG-40	Connect To Exist. AOA Fence w/Sliding Gates - Phase B South Gate	4.0d	28-Jul-25 A	31-Jul-25 A	
4345	EN-AT-RDSG-110	Fill & Compact 6" Base Layers - Phase B South Gate	7.0d	28-Jul-25 A	5-Aug-25 A	
4346	EN-AT-RDSG-170	Set Guard Shack & Connect Utilities - Phase B South Gate	11.0d	8-Aug-25 A	22-Aug-25 A	
4347	EN-AT-RDSG-180	Connect Guard Shack to Data/Power - Phase B South Gate	2.0d	18-Aug-25 A	19-Aug-25 A	
4348	EN-AT-RDSG-160	Install Light Poles - Phase B South Gate	5.0d	18-Aug-25 A	22-Aug-25 A	
4349	EN-AT-RDSG-190	Install Cameras at Guard Shack - Phase B South Gate	3.0d	26-Aug-25 A	28-Aug-25 A	
4350	EN-AT-RDSG-120	Install Paving - 1st - 2" Lift - Phase B South Gate	1.0d	15-Sep-25 A	15-Sep-25 A	
4351	EN-AT-RDSG-130	Install Paving - 2nd - 2" Lift - Phase B South Gate	1.0d	17-Sep-25 A	17-Sep-25 A	
4352	EN-AT-RDSG-140	Install Temporary Striping - Phase B South Gate	1.0d	19-Sep-25 A	19-Sep-25 A	
4353	EN-AT-RDSG-200	Install Permanent Striping - Phase B South Gate	1.0d	26-Sep-25 A	26-Sep-25 A	
4354	EN-AT-RDSG-90	Construct Concrete Gutter Trans. Between Exist. Edge of Pavement & S-203 - P...	2.0d	26-Sep-25 A	29-Sep-25 A	
4355	WBS - Phase C Work Area		282.0d	6-Jan-25 A	12-Feb-26	785.0d
4356	EN-DM-PHC-40	Install Temporary Lighted Channelizing Cones for Active VSR - Phase C	5.0d	6-Jan-25 A	10-Jan-25 A	
4357	EN-DM-PHC-50	Decommission Exist. Monitor Wells - Phase C	2.0d	9-Jan-25 A	10-Jan-25 A	
4358	EN-DM-PHC-60	Layout for Fence/Sliding Guard Gate Install - Phase C	3.0d	22-Jan-25 A	24-Jan-25 A	
4359	EN-DM-PHC-30	Mobilize Site Safety & SWPPP BMPs - Phase C	5.0d	27-Jan-25 A	31-Jan-25 A	
4360	EN-DM-PHC-80	Install Signage - Phase C	5.0d	27-Jan-25 A	31-Jan-25 A	
4361	EN-DM-PHC-90	Install AOA Fencing/Sliding Guard Gate - Phase C	145.0d	29-Jan-25 A	23-Jun-25 A	
4362	EN-DM-PHC-120	De-Energize All Airfield LTNG - Phase C	1.0d	3-Feb-25 A	3-Feb-25 A	
4363	EN-DM-PHC-150	Remove Exist. Airfield LTNG Poles & Bases - Phase C	1.0d	26-Feb-25 A	26-Feb-25 A	
4364	EN-DM-PHC-70	Camera & Laser Profile Exist. Utilities Prior to Demolition - Phase C	4.0d	3-Mar-25 A	6-Mar-25 A	
4365	EN-DM-PHC-200	Trans. VSR to Perimeter of ASD AOA Fence - Phase C	1.0d	25-Apr-25 A	25-Apr-25 A	
4366	EN-DM-PHC-110	TECO - De-Energize Exist. 300kva Transformer - Phase C	1.0d	19-May-25 A	19-May-25 A	
4367	EN-DM-PHC-140	Relocate Exist. Elec. Equip. to be Reused - Phase C	1.0d	19-May-25 A	19-May-25 A	
4368	EN-DM-PHC-180	Install Non-AOA Fencing - Phase C	39.0d	2-Jun-25 A	25-Jul-25 A	

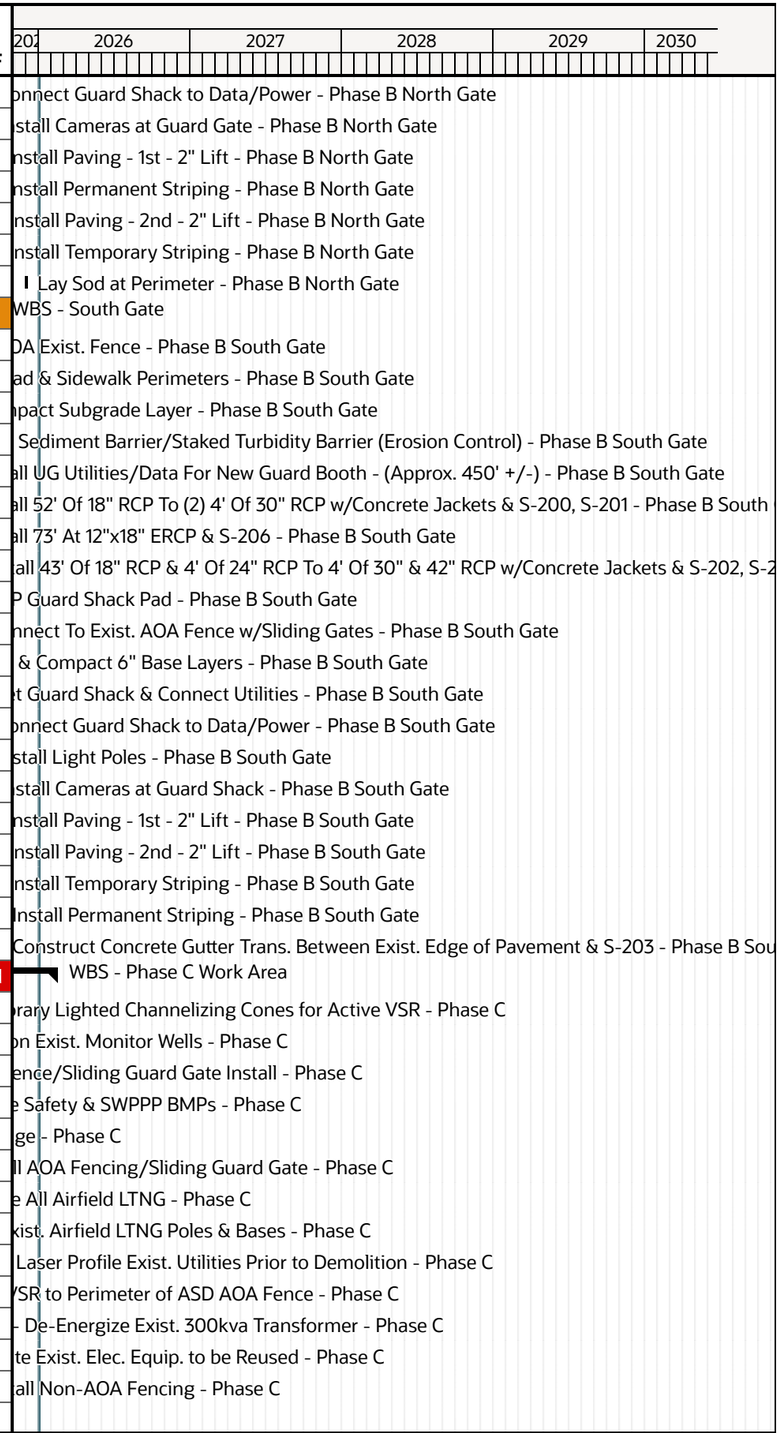


	ID	Name	Dur	Start	Finish	TF
4369	EN-DM-PHC-130	Intercept Sanitary Upstream of Triturator & Cut / Cap - Phase C	3.0d	11-Jun-25 A	13-Jun-25 A	
4370	EN-DM-PHC-250	Apron Exist. Fuel Line & Utilities Removal - Phase C	18.0d	11-Jun-25 A	7-Jul-25 A	
4371	EN-DM-PHC-160	TSA / CBP / HCAA / HP Walk New AOA Fence & Trans. VSR Initial Insp. - Phase C	1.0d	8-Aug-25 A	8-Aug-25 A	
4372	EN-DM-PHC-170	TSA / CBP / HCAA Comment Correction - Phase C	5.0d	11-Aug-25 A	15-Aug-25 A	
4373	EN-DM-PHC-190	Final TSA/CBP/HCAA/HP AOA Fence Walk Insp. - Phase C	1.0d	15-Aug-25 A	15-Aug-25 A	
4374	EN-DM-PHC-210	Demo Exist. AOA Fence - Phase C	5.0d	18-Aug-25 A	22-Aug-25 A	
4375	EN-DM-PHC-100	Exist. 12" Water Main Intercept & Install Above Ground Manifold - Phase C	5.0d	17-Nov-25 A	21-Nov-25 A	
4376	WBS - Area 4		30.0d	10-Feb-25 A	21-Mar-25 A	
4377	EN-DM-A4-10	Remove Apron Concrete - Phase C Area 4	30.0d	10-Feb-25 A	21-Mar-25 A	
4378	WBS - Area 3		68.0d	27-Jan-25 A	30-Apr-25 A	
4379	EN-DM-A3-10	Remove Apron Concrete - Phase C Area 3	68.0d	27-Jan-25 A	30-Apr-25 A	
4380	WBS - Area 2		189.0d	26-Feb-25 A	20-Nov-25 A	
4381	EN-DM-A2-10	Remove Apron Concrete - Phase C Area 2	58.0d	26-Feb-25 A	16-May-25 A	
4382	EN-DM-A2-30	Commence Crushed Concrete Install at Apron Perimeter Edge - Phase C Area 2	0.0d	8-Jul-25 A		
4383	EN-DM-A2-20	Install 2" Non-Potable HDPE Water Service to Truck Wash Locations - Phase C ...	8.0d	11-Nov-25 A	20-Nov-25 A	
4384	WBS - Area 1		257.0d	10-Feb-25 A	12-Feb-26	785.0d
4385	EN-DM-A1-10	Saw Cut Limits of Apron Demolition - Phase C Area 1	4.0d	10-Feb-25 A	13-Feb-25 A	
4386	EN-DM-A1-70	Remove Apron Concrete - Phase C Area 1	34.0d	21-Apr-25 A	6-Jun-25 A	
4387	EN-DM-A1-100	Crushed Concrete Ready for Paving Contractor - Phase C Area 1	0.0d		6-Jun-25 A	
4388	EN-DM-A1-40	Remove Exist. Drainage Structure, Partial Drainage Pipe & Plug Pipe - Phase C ...	2.0d	11-Jun-25 A	12-Jun-25 A	
4389	EN-DM-A1-50	Demo Exist. Light Poles (Keep J-Box Active) - Phase C Area 1	2.0d	14-Jul-25 A	15-Jul-25 A	
4390	EN-DM-A1-60	All Exist. Wall Pack LTNG Inside Tunnel to Be Demolished w/Conduit & Wire - P...	5.0d	11-Aug-25 A	15-Aug-25 A	
4391	EN-DM-A1-30	Final Utility Cut & Caps & SIDA Fence Sign Offs Complete - Phase C Area 1	0.0d		15-Aug-25 A	
4392	EN-DM-A1-80	Close Bessie Coleman Service Road - Phase C Area 1	0.0d		15-Aug-25 A	
4393	EN-DM-A1-110	Demo First Half of Tunnel Structure - Phase C Area 1	34.0d	18-Aug-25 A	3-Oct-25 A	
4394	EN-DM-A1-90	Install Temporary Strut Support System at Tunnel - Phase C Area 1	29.0d	29-Aug-25 A	9-Oct-25 A	
4395	EN-DM-A1-120	Remove Exist. GDWY Pile Caps (3) - Phase C Area 1	5.0d	22-Sep-25 A	26-Sep-25 A	
4396	EN-DM-A1-130	Demo Second Half of Tunnel Structure - Phase C Area 1	10.0d	30-Jan-26	12-Feb-26	0.0d
4397	WBS - Soil Cut & Grade		39.0d	1-Sep-25 A	24-Oct-25 A	
4398	EN-DM-10	Cut FIS Low Area	39.0d	1-Sep-25 A	24-Oct-25 A	
4399	EN-DM-20	Cut Apron High Area	30.0d	8-Sep-25 A	17-Oct-25 A	
4400	WBS - Dewatering		35.0d	30-Sep-25 A	17-Nov-25 A	
4401	EN-DM-30	Install Underdrain Low Area - Phase C Dewatering	11.0d	30-Sep-25 A	14-Oct-25 A	
4402	EN-DM-40	Install Sump Structure - Phase C Dewatering	2.0d	30-Sep-25 A	1-Oct-25 A	
4403	EN-DM-100	Install Underdrain High Area - Phase C Dewatering	10.0d	3-Oct-25 A	16-Oct-25 A	
4404	EN-DM-50	Install Settlement Tanks - Phase C Dewatering	1.0d	6-Oct-25 A	6-Oct-25 A	
4405	EN-DM-80	Install Piping from Sump to Discharge - Phase C Dewatering	22.0d	17-Oct-25 A	17-Nov-25 A	
4406	EN-DM-70	Install Pumps - Phase C Dewatering	5.0d	31-Oct-25 A	6-Nov-25 A	
4407	EN-DM-90	Dewatering System Active - Phase C Dewatering	0.0d		17-Nov-25 A	
4408	WBS - Fuel Tank Relocation		24.0d	20-Feb-25 A	25-Mar-25 A	
4409	EN-UR-FT-100	Remove & Replace Exist. Curb/Gutter to Maintain Drainage - Phase C Tank Relo	1.0d	20-Feb-25 A	20-Feb-25 A	
4410	EN-UR-FT-110	Demo & Replace Pavement To Provide Lvl. Ground for Fuel Tank - Phase C Tank...	1.0d	20-Feb-25 A	20-Feb-25 A	

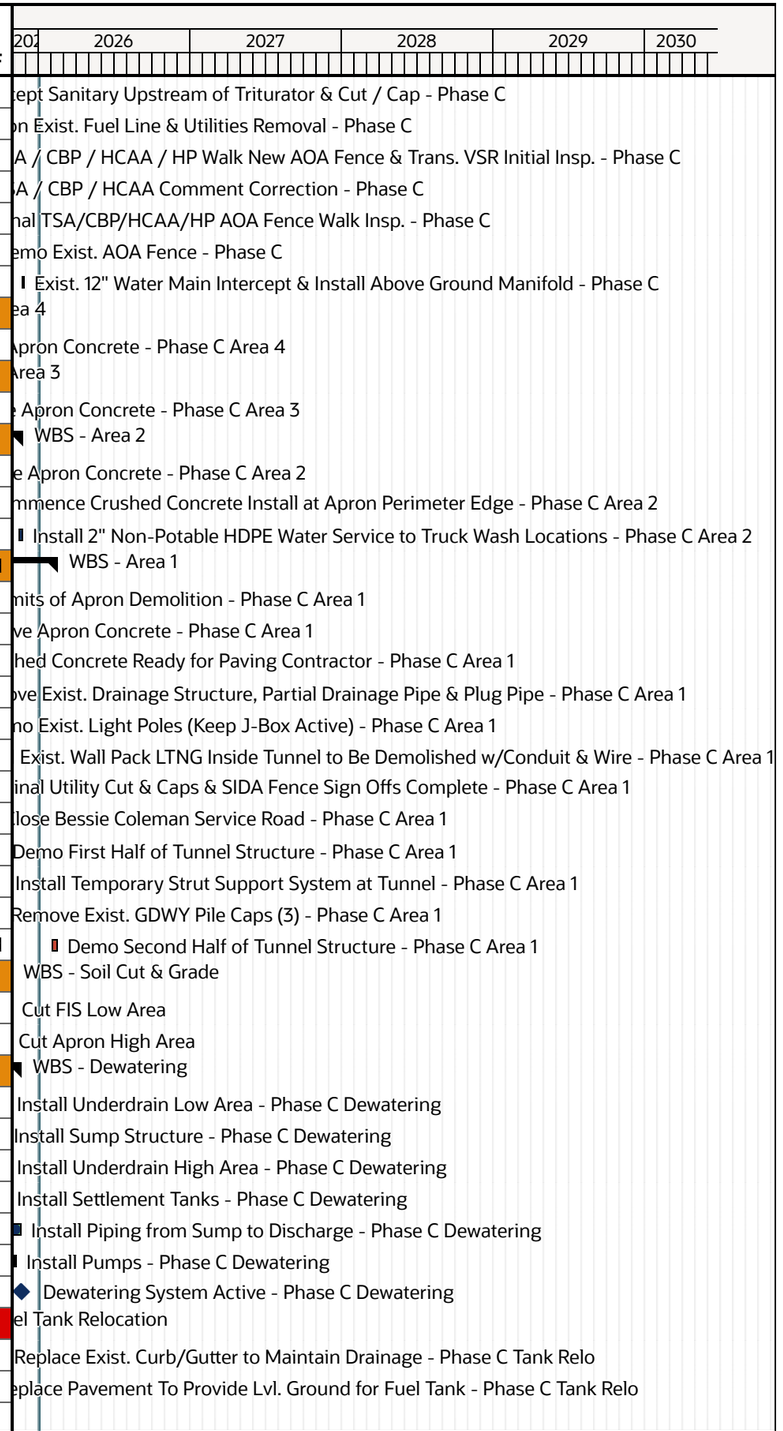


	ID	Name	Dur	Start	Finish	TF
4411	EN-UR-FT-20	FRP New Pad - Phase C Tank Relo	14.0d	21-Feb-25 A	12-Mar-25 A	
4412	EN-UR-FT-90	Install Elec. Service Feed to Tank - Phase C Tank Relo	6.0d	3-Mar-25 A	10-Mar-25 A	
4413	EN-UR-FT-50	Demo Exist. MBLC Panel - Phase C Tank Relo	1.0d	3-Mar-25 A	3-Mar-25 A	
4414	EN-UR-FT-120	Install NEMA 3R 240v/60A MCB 1PH Panel w/(4) 20A Breakers to Serve Reloca...	1.0d	10-Mar-25 A	10-Mar-25 A	
4415	EN-UR-FT-40	7 Day Cure on Concrete - Phase C Tank Relo	4.0d	12-Mar-25 A	15-Mar-25 A	
4416	EN-UR-FT-80	Decommission Exist. Tank - Phase C Tank Relo	1.0d	14-Mar-25 A	14-Mar-25 A	
4417	EN-UR-FT-30	Pressure Test Prior to Move - Phase C Tank Relo	1.0d	17-Mar-25 A	17-Mar-25 A	
4418	EN-UR-FT-60	Demo Exist. Shut Off Switch & Conduit - Phase C Tank Relo	2.0d	17-Mar-25 A	18-Mar-25 A	
4419	EN-UR-FT-70	Exist. Timer Removal (Salvage for Relocation to New Panel) - Phase C Tank Relo	1.0d	17-Mar-25 A	17-Mar-25 A	
4420	EN-UR-FT-150	Relocate Fuel Tank - Phase C Tank Relo	1.0d	18-Mar-25 A	18-Mar-25 A	
4421	EN-UR-FT-140	Relocate/Install Exist. Timer - Phase C Tank Relo	1.0d	20-Mar-25 A	20-Mar-25 A	
4422	EN-UR-FT-160	Pressure Test Post Relocation - Phase C Tank Relo	1.0d	24-Mar-25 A	24-Mar-25 A	
4423	EN-UR-FT-130	Install Conduit & Emergency Shut Off Switch - Phase C Tank Relo	1.0d	24-Mar-25 A	24-Mar-25 A	
4424	EN-UR-FT-170	Refill Fuel Tank - Phase C Tank Relo	0.0d		25-Mar-25 A	
4425	WBS - Bessie Coleman Closure Detour		132.0d	21-Apr-25 A	24-Oct-25 A	
4426	EN-BC-20	Remove Exist. Oak Tree - Bessie Coleman Closure	5.0d	21-Apr-25 A	25-Apr-25 A	
4427	EN-BC-30	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Bessie ...	1.0d	21-Apr-25 A	21-Apr-25 A	
4428	EN-BC-40	Cut & Clear for Curb/Asphalt - Vacuum Excavate - Bessie Coleman Closure	11.0d	25-Apr-25 A	9-May-25 A	
4429	EN-BC-50	Reclaim Water Valves to Be Adjusted - Bessie Coleman Closure	4.0d	30-Apr-25 A	5-May-25 A	
4430	EN-BC-10	Install MOT & Temp Fence - Bessie Coleman Closure	7.0d	1-May-25 A	9-May-25 A	
4431	EN-BC-60	Fill & Compact Subgrade Layer - Bessie Coleman Closure	5.0d	6-May-25 A	12-May-25 A	
4432	EN-BC-80	Form & Pour Curbs - Bessie Coleman Closure	4.0d	14-May-25 A	19-May-25 A	
4433	EN-BC-70	Fill & Compact 6" Base Layers - Bessie Coleman Closure	6.0d	21-May-25 A	29-May-25 A	
4434	EN-BC-RFI056-10	Procure Revised Signage per RFI 00056 - Bessie Coleman Closure	31.0d	23-May-25 A	8-Jul-25 A	
4435	EN-BC-90	Install Asphalt 1st - 2" Lift - Bessie Coleman Closure	1.0d	9-Jun-25 A	9-Jun-25 A	
4436	EN-BC-120	Install Asphalt 2nd - 2" Lift - Bessie Coleman Closure	1.0d	9-Jun-25 A	9-Jun-25 A	
4437	EN-BC-110	Install All Detour/Road Closure/Directional Signage (Area 1) - Bessie Coleman ...	5.0d	10-Jul-25 A	16-Jul-25 A	
4438	EN-BC-130	Install Temporary Striping (Area 1) - Bessie Coleman Closure	1.0d	14-Jul-25 A	14-Jul-25 A	
4439	EN-BC-100	Install FDOT Type 3 Barricades (Signs Mounted on Barricade) - Bessie Coleman ...	1.0d	15-Aug-25 A	15-Aug-25 A	
4440	EN-BC-140	Install Permanent Striping (Area 1) - Bessie Coleman Closure	2.0d	26-Aug-25 A	27-Aug-25 A	
4441	EN-BC-150	Stabilize Soil Post Grade Cut & Dewatering Install	5.0d	20-Oct-25 A	24-Oct-25 A	
4442	WBS - Weather Calendar Enabling		18.0d	28-Oct-25 A	14-Nov-25 A	
4443	EN-WE-10	Weather Days for Enabling Scope Dec 2024 thru Dec 2025	10.0d	28-Oct-25 A	6-Nov-25 A	
4444	EN-WE-20	Weather Surplus Days for Enabling Scope Dec 2024 thru Dec 2025	8.0d	7-Nov-25 A	14-Nov-25 A	
4445	WBS - Enabling Scope Substantial Completion		26.0d	21-Oct-25 A	25-Nov-25 A	
4446	EN-BC-160	QC Punch Walk for Demo Completion	4.0d	21-Oct-25 A	24-Oct-25 A	
4447	EN-PLA-10	Prep & Submit Pre-SC Documentation - Enabling Scope	1.0d	17-Nov-25 A	17-Nov-25 A	
4448	EN-PLA-40	HP/HCAA Substantial Completion Walk - Enabling Scope	1.0d	17-Nov-25 A	17-Nov-25 A	
4449	EN-PLA-30	HCAA Review & Approve Documentation - Enabling Scope	6.0d	18-Nov-25 A	25-Nov-25 A	
4450	WBS - Ground Improvements		128.0d	25-Jul-25 A	27-Jan-26	82.0d
4451	WBS - Milestones		71.0d	25-Jul-25 A	3-Nov-25 A	
4452	GI-HAM-20	Test Pile Program LOE - DIP/LTP	19.0d	25-Jul-25 A	20-Aug-25 A	

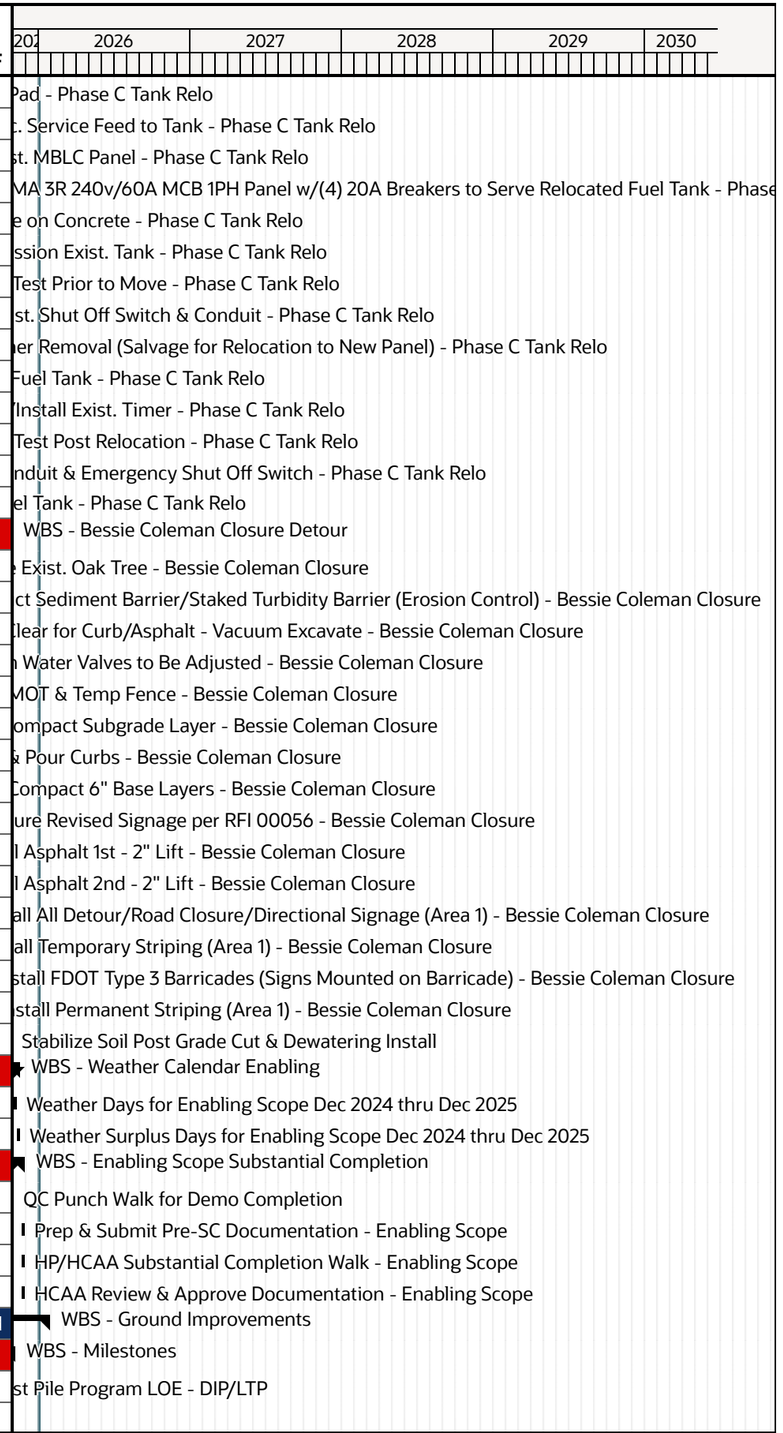


	ID	Name	Dur	Start	Finish	TF
4453	GI-100	Test Pile Program Complete - DIP/LTP	0.0d		20-Aug-25 A	
4454	GI-30	Mobilize For Production Install - DIP/LTP	6.0d	27-Oct-25 A	3-Nov-25 A	
4455	WBS - Test Pile Program		18.0d	28-Jul-25 A	20-Aug-25 A	
4456	GI-40	Mobilize Equip. & Materials for Test Pile - DIP/LTP	5.0d	28-Jul-25 A	1-Aug-25 A	
4457	GI-70	Drill Reaction Piles - DIP/LTP	5.0d	4-Aug-25 A	8-Aug-25 A	
4458	GI-90	Test (4) Single Element DIPs - DIP/LTP	5.0d	11-Aug-25 A	15-Aug-25 A	
4459	GI-80	Install LTP on F6 & F8 Test Area - DIP/LTP	5.0d	11-Aug-25 A	15-Aug-25 A	
4460	GI-50	Test F8 Footing - DIP/LTP	2.0d	18-Aug-25 A	19-Aug-25 A	
4461	GI-60	Test F6 Footing - DIP/LTP	1.0d	20-Aug-25 A	20-Aug-25 A	
4462	WBS - Rigid Inclusions - Area 6		21.0d	3-Nov-25 A	3-Dec-25 A	
4463	GI-A6-20	DIP Install - RI DIPS Area 6	12.0d	3-Nov-25 A	18-Nov-25 A	
4464	GI-A6-30	Excavate - RI DIPS Area 6	8.0d	7-Nov-25 A	18-Nov-25 A	
4465	GI-A6-40	Cut Dip & Install Grout - RI DIPS Area 6	15.0d	11-Nov-25 A	3-Dec-25 A	
4466	GI-A6-50	Install Steel Caps - RI DIPS Area 6	15.0d	11-Nov-25 A	3-Dec-25 A	
4467	WBS - Rigid Inclusions - Area 2		38.0d	7-Nov-25 A	5-Jan-26	98.0d
4468	GI-A2-100	DIP Install - RI DIPS Area 2	24.0d	7-Nov-25 A	12-Dec-25 A	
4469	GI-A2-110	Excavate - RI DIPS Area 2	11.0d	1-Dec-25 A	15-Dec-25 A	
4470	GI-A2-120	Cut Dip RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
4471	GI-A2-130	Install Grout & Install Steel Caps - RI DIPS Area 2	5.0d	29-Dec-25	5-Jan-26	98.0d
4472	WBS - Rigid Inclusions - Area 1		18.0d	15-Dec-25 A	9-Jan-26	41.0d
4473	GI-A1-30	Excavate - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
4474	GI-A1-20	DIP Install - RI DIPS Area 1 - 12/13 Line	14.0d	15-Dec-25 A	5-Jan-26	41.0d
4475	GI-A1-40	Cut Dip & Install Grout - RI DIPS Area 1 - 12/13 Line	2.0d	6-Jan-26	7-Jan-26	41.0d
4476	GI-A1-50	Install Steel Caps - RI DIPS Area 1 - 12/13 Line	2.0d	8-Jan-26	9-Jan-26	41.0d
4477	WBS - Rigid Inclusions - Area 3		24.0d	15-Dec-25 A	19-Jan-26	51.0d
4478	GI-A3-140	DIP Install - RI DIPS Area 3	20.0d	15-Dec-25 A	13-Jan-26	46.0d
4479	GI-A3-100	Excavate - RI DIPS Area 3	14.0d	15-Dec-25 A	5-Jan-26	51.0d
4480	GI-A3-110	Cut Dip & Install Grout - RI DIPS Area 3	5.0d	6-Jan-26	12-Jan-26	51.0d
4481	GI-A3-120	Install Steel Caps - RI DIPS Area 3	5.0d	13-Jan-26	19-Jan-26	51.0d
4482	WBS - Rigid Inclusions - Area 5		19.0d	15-Dec-25 A	12-Jan-26	81.0d
4483	GI-A5-110	Excavate - RI DIPS Area 5	14.0d	15-Dec-25 A	5-Jan-26	82.0d
4484	GI-A5-100	DIP Install - RI DIPS Area 5	19.0d	15-Dec-25 A	12-Jan-26	47.0d
4485	GI-A5-120	Cut Dip & Install Grout - RI DIPS Area 5	2.0d	6-Jan-26	7-Jan-26	82.0d
4486	GI-A5-130	Install Steel Caps - RI DIPS Area 5	2.0d	8-Jan-26	9-Jan-26	82.0d
4487	WBS - Rigid Inclusions - Area 4		9.0d	14-Jan-26	26-Jan-26	46.0d
4488	GI-A4-80	DIP Install - RI DIPS Area 4	9.0d	14-Jan-26	26-Jan-26	46.0d
4489	GI-A4-90	Excavate - RI DIPS Area 4	5.0d	14-Jan-26	20-Jan-26	46.0d
4490	GI-A4-100	Cut Dip & Install Grout - RI DIPS Area 4	2.0d	21-Jan-26	22-Jan-26	46.0d
4491	GI-A4-110	Install Steel Caps - RI DIPS Area 4	2.0d	23-Jan-26	26-Jan-26	46.0d
4492	WBS - Rigid Inclusions - Area 6-1 Cooling Tower		10.0d	14-Jan-26	27-Jan-26	46.0d
4493	GI-A6-1-110	Excavate - RI DIPS Area 6 - 1	3.0d	14-Jan-26	16-Jan-26	49.0d
4494	GI-A6-1-100	DIP Install - RI DIPS Area 6 - 1	4.0d	14-Jan-26	19-Jan-26	49.0d

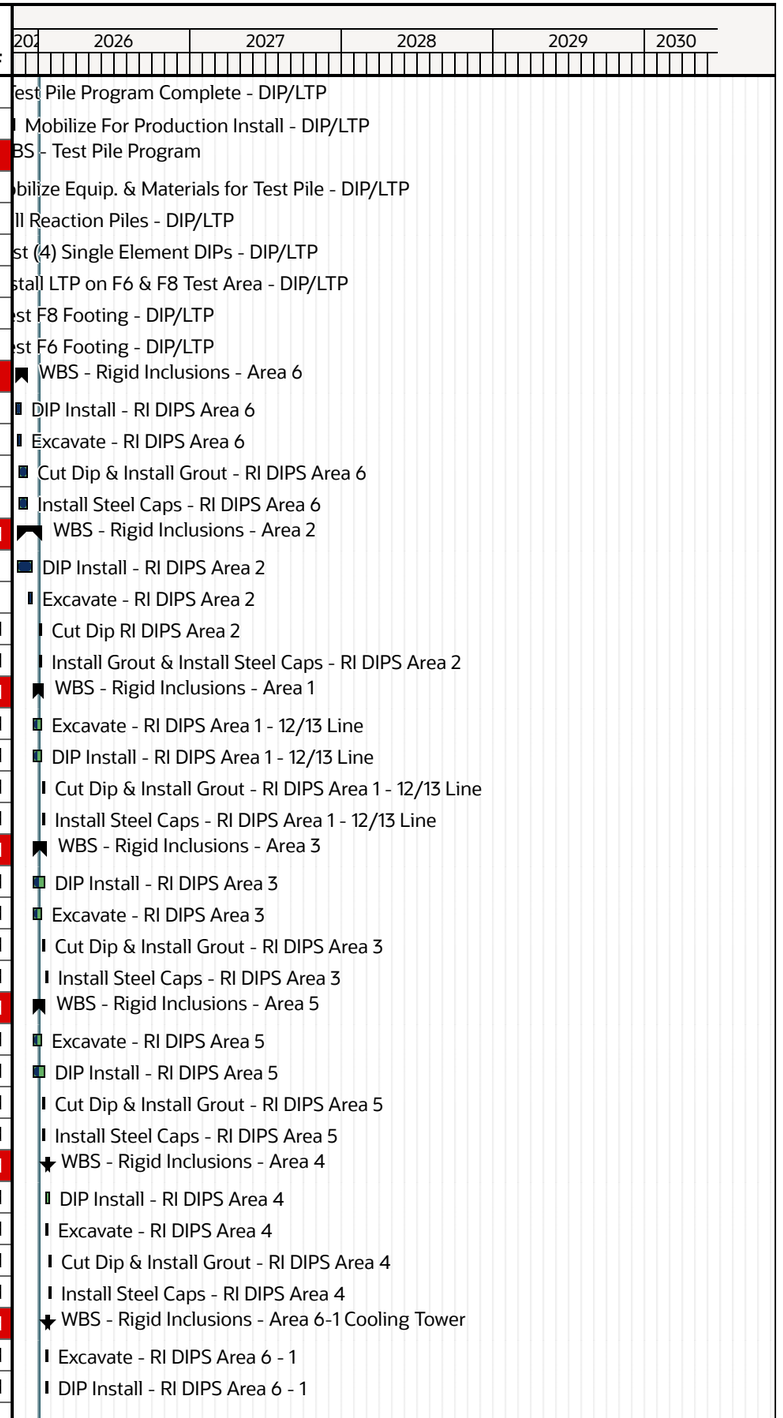


	ID	Name	Dur	Start	Finish	TF
4495	GI-A6-1-120	Cut Dip & Install Grout - RI DIPS Area 6 - 1	2.0d	19-Jan-26	20-Jan-26	49.0d
4496	GI-A6-1-130	Install Steel Caps - RI DIPS Area 6 - 1	2.0d	26-Jan-26	27-Jan-26	46.0d
4497	WBS - Foundations & Deep Underground		231.0d	24-Nov-25 A	21-Oct-26	60.0d
4498	WBS - Milestones		169.0d	24-Nov-25 A	27-Jul-26	95.0d
4499	GI-FS1000	Found. - Mobilize	3.0d	24-Nov-25 A	28-Nov-25 A	
4500	GI-FS-A5-6390	28 Day Cure on All Concrete for Steel - Area 6	28.0d	7-Jan-26	3-Feb-26	199.0d
4501	MLS-GI-FS1040	Found. Area 6 - Ready for Steel	0.0d		3-Feb-26	142.0d
4502	GI-FS-A2-4470	28 Day Cure on All Concrete for Steel - Area 2.A	28.0d	14-Feb-26	13-Mar-26	88.0d
4503	GI-FS-A1-6960	28 Day Cure on All Concrete for Steel - Elevator & Escalator Pits	28.0d	27-Feb-26	26-Mar-26	25.0d
4504	GI-FS-A2-7180	28 Day Cure on All Concrete for Steel - Area 2.2	28.0d	3-Mar-26	30-Mar-26	71.0d
4505	GI-FS-A1-4440	28 Day Cure on All Concrete for Steel - Area 1	28.0d	18-Mar-26	14-Apr-26	34.0d
4506	MLS-GI-FS6950	Elevator Pits - Ready for Precast	0.0d		26-Mar-26	17.0d
4507	MLS-GI-FS1030	Found. Area 2 - Ready For Steel	0.0d		30-Mar-26	51.0d
4508	MLS-GI-FS-1010	Found. Area 1 - Ready for Steel	0.0d		14-Apr-26	24.0d
4509	GI-FS-A3-4500	28 Day Cure on All Concrete for Steel - Area 3	28.0d	30-Apr-26	28-May-26	164.0d
4510	MLS-GI-FS1020	Found. Area 3 - Ready For Steel	0.0d		28-May-26	117.0d
4511	GI-FS-A5-4560	28 Day Cure on All Concrete for Steel - Area 5	28.0d	29-May-26	25-Jun-26	115.0d
4512	MLS-GI-FS1060	Found. Area 5 - Ready for Steel	0.0d		25-Jun-26	82.0d
4513	GI-FS-A3-6810	28 Day Cure on All Concrete for Steel - Area 4	28.0d	26-Jun-26	25-Jul-26	134.0d
4514	MLS-GI-FS1050	Found. Area 4 - Ready for Steel	0.0d		27-Jul-26	95.0d
4515	WBS - Elevator / Escalator Pits		31.0d	23-Jan-26	6-Mar-26	31.0d
4516	GI-FS-A1-6910	Excavate Area For Found. - Elevator & Escalator Pits	5.0d	23-Jan-26	29-Jan-26	17.0d
4517	GI-FS-A1-6920	FRP Found. - Elevator & Escalator Pits	20.0d	30-Jan-26	26-Feb-26	17.0d
4518	GI-FS-A1-6930	Install Waterproofing On Found. - Elevator & Escalator Pits	20.0d	2-Feb-26	27-Feb-26	31.0d
4519	GI-FS-A1-6940	MEPF In-Wall R/I - Elevator & Escalator Pits	15.0d	2-Feb-26	20-Feb-26	31.0d
4520	GI-FS-A1-6950	Backfill Found. - Elevator & Escalator Pits	10.0d	23-Feb-26	6-Mar-26	31.0d
4521	WBS - Foundations - Area 6		32.0d	1-Dec-25 A	15-Jan-26	4.0d
4522	GI-FS-A1-6810	Excavate Area For Found. - Area 6	11.0d	1-Dec-25 A	15-Dec-25 A	
4523	GI-FS-A1-6820	FRP Found. - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
4524	GI-FS-A1-6840	MEPF In-Wall R/I - Area 6	14.0d	16-Dec-25 A	6-Jan-26	4.0d
4525	GI-FS-A1-6830	Install Waterproofing On Found. - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
4526	GI-FS-A1-6850	Backfill Found. - Area 6	7.0d	7-Jan-26	15-Jan-26	4.0d
4527	GI-FS-A1-6825	FRP Turndown - Area 6	5.0d	7-Jan-26	13-Jan-26	5.0d
4528	WBS - Foundations - Area 2		35.0d	16-Jan-26	5-Mar-26	2.0d
4529	GI-FS-A1-6610	Excavate Area For Found. - Area 2.A	5.0d	16-Jan-26	22-Jan-26	4.0d
4530	GI-FS-A1-6620	FRP Found. - Area 2.A	20.0d	19-Jan-26	13-Feb-26	4.0d
4531	GI-FS-A1-6640	MEPF In-Wall R/I - Area 2.A	15.0d	19-Jan-26	6-Feb-26	6.0d
4532	GI-FS-A1-6630	Install Waterproofing On Found. - Area 2.A	20.0d	20-Jan-26	16-Feb-26	4.0d
4533	GI-FS-A1-6650	Backfill Found. - Area 2.A	7.0d	11-Feb-26	19-Feb-26	4.0d
4534	GI-FS-A1-6970	Excavate Area For Found. - Area 2.B	3.0d	13-Feb-26	17-Feb-26	2.0d
4535	GI-FS-A1-6980	FRP Found. - Area 2.B	11.0d	16-Feb-26	2-Mar-26	2.0d
4536	GI-FS-A1-6990	Install Waterproofing On Found. - Area 2.B	10.0d	17-Feb-26	2-Mar-26	2.0d

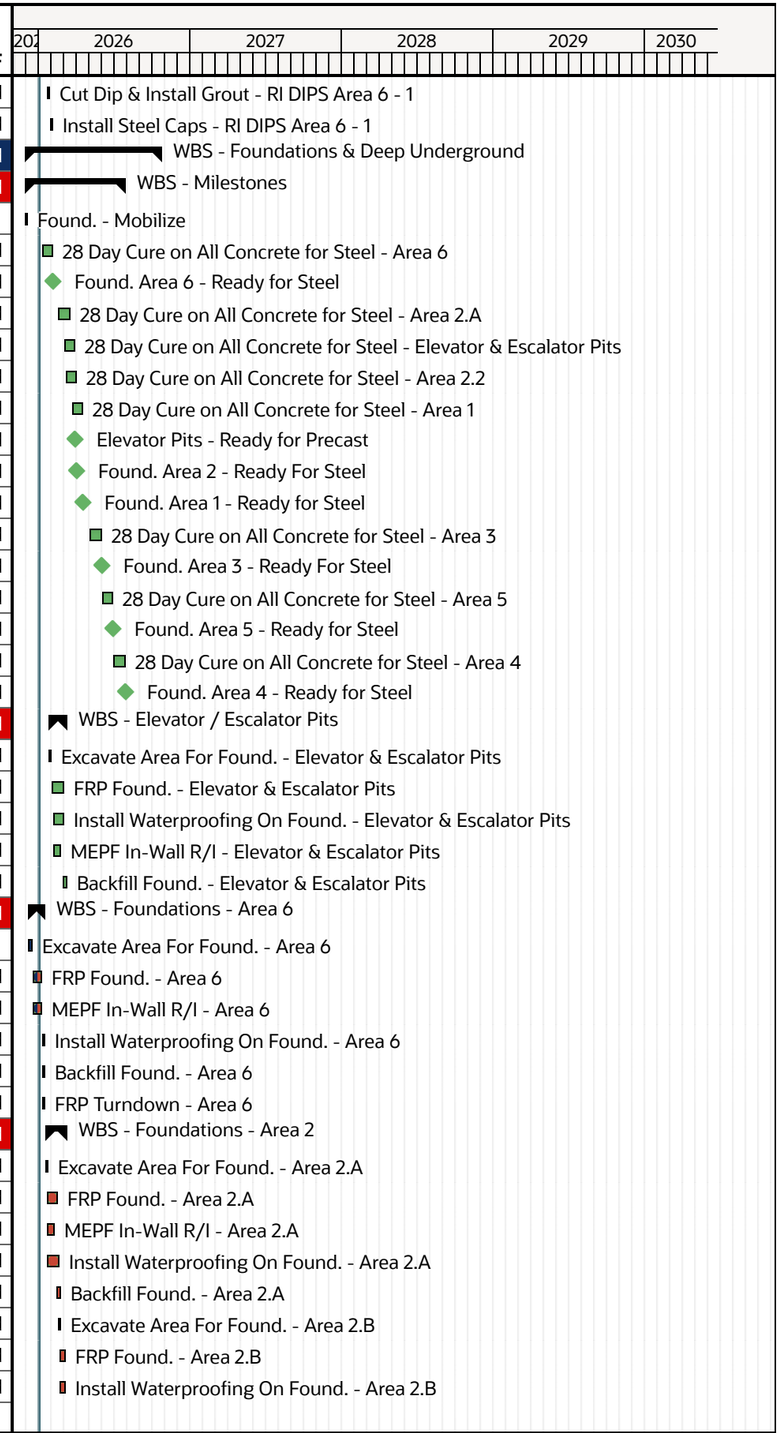


	ID	Name	Dur	Start	Finish	TF
4537	GI-FS-A1-7000	MEPF In-Wall R/I - Area 2.B	7.0d	18-Feb-26	26-Feb-26	3.0d
4538	GI-FS-A1-7010	Backfill Found. - Area 2.B	4.0d	2-Mar-26	5-Mar-26	2.0d
4539	WBS - Foundations - Area 1		18.0d	6-Mar-26	31-Mar-26	0.0d
4540	GI-FS-A1-1070	Excavate Area For Found. - Area 1.A	2.0d	6-Mar-26	9-Mar-26	2.0d
4541	GI-FS-A1-1250	FRP Found. - Area 1.A	5.0d	11-Mar-26	17-Mar-26	0.0d
4542	GI-FS-A1-1410	MEPF In-Wall R/I - Area 1.A	2.0d	11-Mar-26	12-Mar-26	2.0d
4543	GI-FS-A1-1260	Install Waterproofing On Found. - Area 1.A	3.0d	12-Mar-26	16-Mar-26	0.0d
4544	GI-FS-A1-1270	Backfill Found. - Area 1.A	3.0d	17-Mar-26	19-Mar-26	0.0d
4545	GI-FS-A1-7020	Excavate Area For Found. - Area 1.B	3.0d	17-Mar-26	19-Mar-26	0.0d
4546	GI-FS-A1-7030	FRP Found. - Area 1.B	7.0d	18-Mar-26	26-Mar-26	0.0d
4547	GI-FS-A1-7040	MEPF In-Wall R/I - Area 1.B	3.0d	19-Mar-26	23-Mar-26	3.0d
4548	GI-FS-A1-7050	Install Waterproofing On Found. - Area 1.B	4.0d	23-Mar-26	26-Mar-26	0.0d
4549	GI-FS-A1-7060	Backfill Found. - Area 1.B	3.0d	27-Mar-26	31-Mar-26	0.0d
4550	WBS - Foundations - Patch / Finish / Protect		15.0d	18-Mar-26	7-Apr-26	29.0d
4551	GI-FS-A1-4260	Found. Areas - Patch / Finish / Protect Found.	15.0d	18-Mar-26	7-Apr-26	29.0d
4552	WBS - Foundations - Area 3		25.0d	1-Apr-26	5-May-26	0.0d
4553	GI-FS-A1-6660	Excavate Area For Found. - Area 3	5.0d	1-Apr-26	7-Apr-26	0.0d
4554	GI-FS-A1-6670	FRP Found. - Area 3	20.0d	2-Apr-26	29-Apr-26	0.0d
4555	GI-FS-A1-6680	Install Waterproofing On Found. - Area 3	20.0d	3-Apr-26	30-Apr-26	0.0d
4556	GI-FS-A1-6690	MEPF In-Wall R/I - Area 3	15.0d	3-Apr-26	23-Apr-26	1.0d
4557	GI-FS-A1-6700	Backfill Found. - Area 3	10.0d	22-Apr-26	5-May-26	0.0d
4558	WBS - Foundations - Area 5		20.0d	6-May-26	3-Jun-26	0.0d
4559	GI-FS-A1-6710	Excavate Area For Found. - Area 5	5.0d	6-May-26	12-May-26	0.0d
4560	GI-FS-A1-6720	FRP Found. - Area 5	15.0d	7-May-26	28-May-26	0.0d
4561	GI-FS-A1-6730	Install Waterproofing On Found. - Area 5	15.0d	8-May-26	29-May-26	0.0d
4562	GI-FS-A1-6740	MEPF In-Wall R/I - Area 5	10.0d	8-May-26	21-May-26	1.0d
4563	GI-FS-A1-6750	Backfill Found. - Area 5	7.0d	26-May-26	3-Jun-26	0.0d
4564	WBS - Foundations - Area 4		20.0d	4-Jun-26	1-Jul-26	0.0d
4565	GI-FS-A1-6760	Excavate Area For Found. - Area 4	5.0d	4-Jun-26	10-Jun-26	0.0d
4566	GI-FS-A1-6770	FRP Found. - Area 4	15.0d	5-Jun-26	25-Jun-26	0.0d
4567	GI-FS-A1-6780	Install Waterproofing On Found. - Area 4	15.0d	8-Jun-26	26-Jun-26	0.0d
4568	GI-FS-A1-6790	MEPF In-Wall R/I - Area 4	10.0d	9-Jun-26	22-Jun-26	0.0d
4569	GI-FS-A1-6800	Backfill Found. - Area 4	7.0d	23-Jun-26	1-Jul-26	0.0d
4570	WBS - Deep Underground MEP - All Areas		185.0d	16-Dec-25 A	4-Sep-26	92.0d
4571	WBS - Deep Underground MEP - Area 2		73.0d	16-Dec-25 A	30-Mar-26	84.0d
4572	GI-FS-A2-5410	Excavate - Deep UG Sanitary- Plumber - Area 2.B.1	5.0d	16-Dec-25 A	22-Dec-25 A	
4573	GI-FS-A2-5470	Excavate - Deep UG Conduit - Elec. - Area 2.B.1	5.0d	16-Dec-25 A	22-Dec-25 A	
4574	GI-FS-A2-5550	Excavate - Deep UG Sanitary - Plumbing - Area 2.B.2	4.0d	17-Dec-25 A	22-Dec-25 A	
4575	GI-FS-A2-5570	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.2	6.0d	22-Dec-25 A	30-Dec-25	30.0d
4576	GI-FS-A2-5500	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.1	21.0d	23-Dec-25 A	22-Jan-26	10.0d
4577	GI-FS-A2-5610	Inspect - Deep UG Sanitary - Plumber - Area 2.B.2	2.0d	29-Dec-25	30-Dec-25	30.0d
4578	GI-FS-A2-6980	Excavate - Deep UG Piping - Mech. - Area 2.B	4.0d	30-Dec-25	5-Jan-26	120.0d

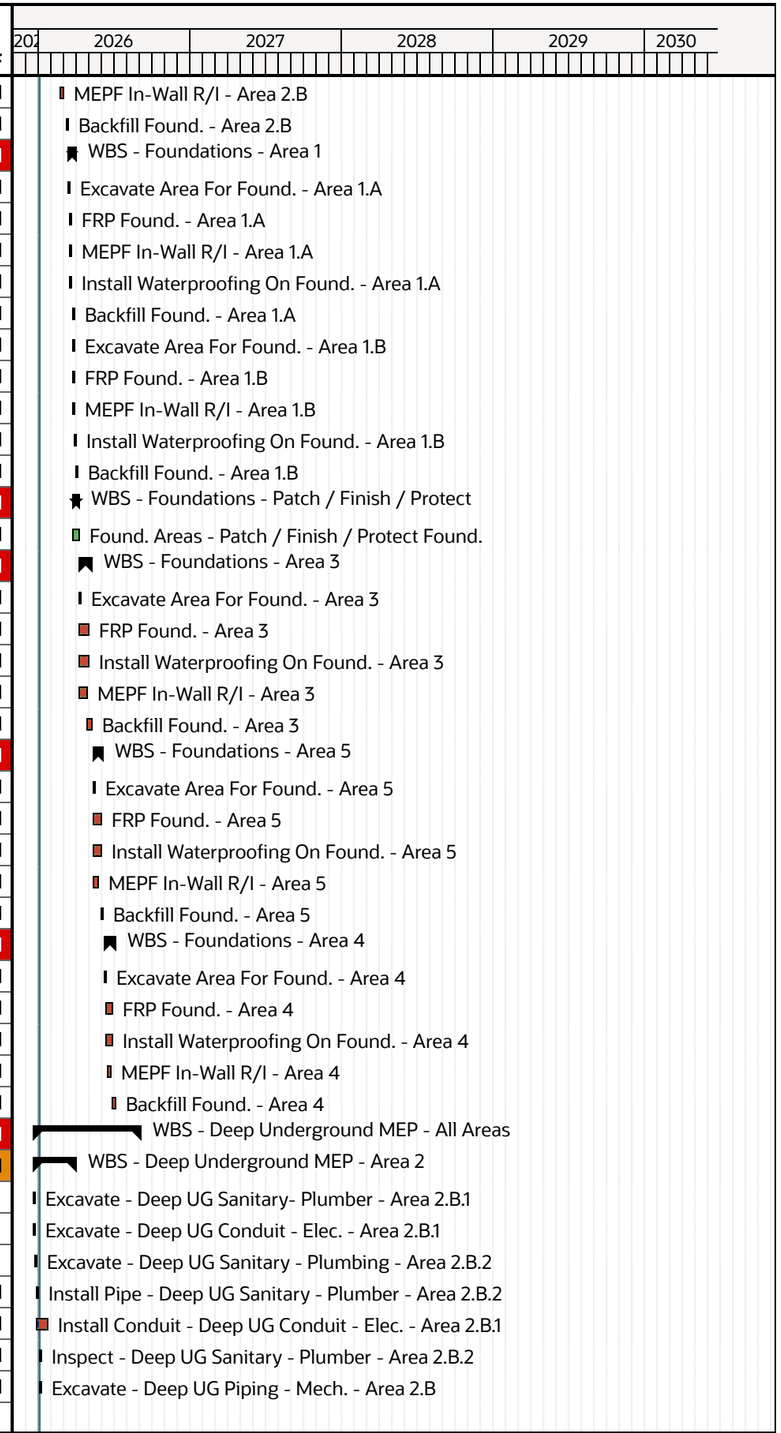


	ID	Name	Dur	Start	Finish	TF
4579	GI-FS-A2-5630	Backfill - Deep UG Sanitary - Plumber - Area 2.B.2	3.0d	31-Dec-25	5-Jan-26	30.0d
4580	GI-FS-A2-6990	Install - Deep UG Piping - Mech. - Area 2.B	4.0d	6-Jan-26	9-Jan-26	120.0d
4581	GI-FS-A2-7120	Excavate - Deep UG Water Main - Plumbing - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
4582	GI-FS-A2-7080	Excavate - Deep UG Fire Main - Fire - Area 2.B	5.0d	6-Jan-26	12-Jan-26	98.0d
4583	GI-FS-A2-5420	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.1	5.0d	8-Jan-26	14-Jan-26	102.0d
4584	GI-FS-A2-7000	Inspect - Deep UG Piping - Mech. - Area 2.B	2.0d	12-Jan-26	13-Jan-26	120.0d
4585	GI-FS-A2-5440	Inspect - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	13-Jan-26	14-Jan-26	102.0d
4586	GI-FS-A2-7130	Install Pipe - Deep UG Water Main - Plumbing - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
4587	GI-FS-A2-7090	Install Pipe - Deep UG Fire Main - Fire - Area 2.B	5.0d	13-Jan-26	19-Jan-26	98.0d
4588	GI-FS-A2-7010	Backfill - Deep UG Piping - Mech. - Area 2.B	3.0d	14-Jan-26	16-Jan-26	120.0d
4589	GI-FS-A2-5450	Backfill - Deep UG Sanitary - Plumber - Area 2.B.1	2.0d	15-Jan-26	16-Jan-26	102.0d
4590	GI-FS-A2-7140	Inspect - Deep UG Water Main - Plumbing - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
4591	GI-FS-A2-7100	Inspect - Deep UG Fire Main - Fire - Area 2.B	2.0d	16-Jan-26	19-Jan-26	98.0d
4592	GI-FS-A2-7150	Backfill - Deep UG Water Main - Plumbing - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
4593	GI-FS-A2-7110	Backfill - Deep UG Fire Main - Fire - Area 2.B	3.0d	20-Jan-26	22-Jan-26	98.0d
4594	GI-FS-A2-5580	Inspect - Deep UG Conduit - Elec. - Area 2.B.1	2.0d	23-Jan-26	26-Jan-26	10.0d
4595	GI-FS-A2-5590	Backfill - Deep UG Conduit - Elec. - Area 2.B.1	5.0d	27-Jan-26	2-Feb-26	10.0d
4596	GI-FS-A2-5780	Excavate - Deep UG Conduit - Elec. - Area 2.A.2	5.0d	3-Feb-26	9-Feb-26	71.0d
4597	GI-FS-A2-7160	TECO 30 Day Advanced Notice to Schedule Conduit Pathways Install for PDS R...	1.0d	3-Feb-26	3-Feb-26	82.0d
4598	GI-FS-A2-5840	Install Conduit - Deep UG Conduit - Elec. - Area 2.A.2	10.0d	10-Feb-26	23-Feb-26	79.0d
4599	GI-FS-A2-5460	Excavate - Deep UG Sanitary - Plumber - Area 2.A.1	5.0d	20-Feb-26	26-Feb-26	99.0d
4600	GI-FS-A2-5620	Excavate - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	20-Feb-26	26-Feb-26	96.0d
4601	GI-FS-A2-5890	Inspect - Deep UG Conduit - Elec. - Area 2.A.2	2.0d	20-Feb-26	23-Feb-26	79.0d
4602	GI-FS-A2-5790	Excavate - Deep UG Sanitary - Plumber - Area 2.A.2	3.0d	20-Feb-26	24-Feb-26	103.0d
4603	GI-FS-A2-5900	Backfill - Deep UG Conduit - Elec. - Area 2.A.2	7.0d	24-Feb-26	4-Mar-26	79.0d
4604	GI-FS-A2-5820	Install Pipe - Deep UG Sanitary - Plumber - Area 2.A.2	3.0d	25-Feb-26	27-Feb-26	103.0d
4605	GI-FS-A2-5850	Inspect - Deep UG Sanitary - Plumber - Area 2.A.2	2.0d	26-Feb-26	27-Feb-26	103.0d
4606	GI-FS-A2-5490	Install Pipe - Deep UG Sanitary - Plumber - Area 2.A.1	5.0d	27-Feb-26	5-Mar-26	99.0d
4607	GI-FS-A2-5670	Install Conduit - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	27-Feb-26	5-Mar-26	96.0d
4608	GI-FS-A2-5860	Backfill - Deep UG Sanitary - Plumber - Area 2.A.2	2.0d	2-Mar-26	3-Mar-26	103.0d
4609	GI-FS-A2-7210	Excavate - Deep UG Sanitary- Plumber - Area 2.B.3	6.0d	3-Mar-26	10-Mar-26	58.0d
4610	GI-FS-A2-7240	Excavate - Deep UG Sanitary- Plumber - Area 2.B.4	6.0d	3-Mar-26	10-Mar-26	58.0d
4611	GI-FS-A2-5510	Inspect - Deep UG Sanitary - Plumber - Area 2.A.1	2.0d	4-Mar-26	5-Mar-26	99.0d
4612	GI-FS-A2-5680	Inspect - Deep UG Conduit - Elec. - Area 2.A.1	2.0d	4-Mar-26	5-Mar-26	96.0d
4613	GI-FS-A2-5530	Backfill - Deep UG Sanitary - Plumber - Area 2.A.1	2.0d	6-Mar-26	9-Mar-26	99.0d
4614	GI-FS-A2-5700	Backfill - Deep UG Conduit - Elec. - Area 2.A.1	5.0d	6-Mar-26	12-Mar-26	96.0d
4615	GI-FS-A2-6610	Excavate - Deep UG LV Conduit - Low Voltage - Area 2.B	6.0d	6-Mar-26	13-Mar-26	21.0d
4616	GI-FS-A2-6730	Excavate - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	6-Mar-26	10-Mar-26	21.0d
4617	GI-FS-A2-7170	TECO Install Conduit pathways for PDS Room 6097	10.0d	6-Mar-26	19-Mar-26	58.0d
4618	GI-FS-A2-6740	Install Conduit - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	11-Mar-26	13-Mar-26	21.0d
4619	GI-FS-A2-7190	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.3	5.0d	11-Mar-26	17-Mar-26	58.0d
4620	GI-FS-A2-7200	Install Pipe - Deep UG Sanitary - Plumber - Area 2.B.4	5.0d	11-Mar-26	17-Mar-26	58.0d

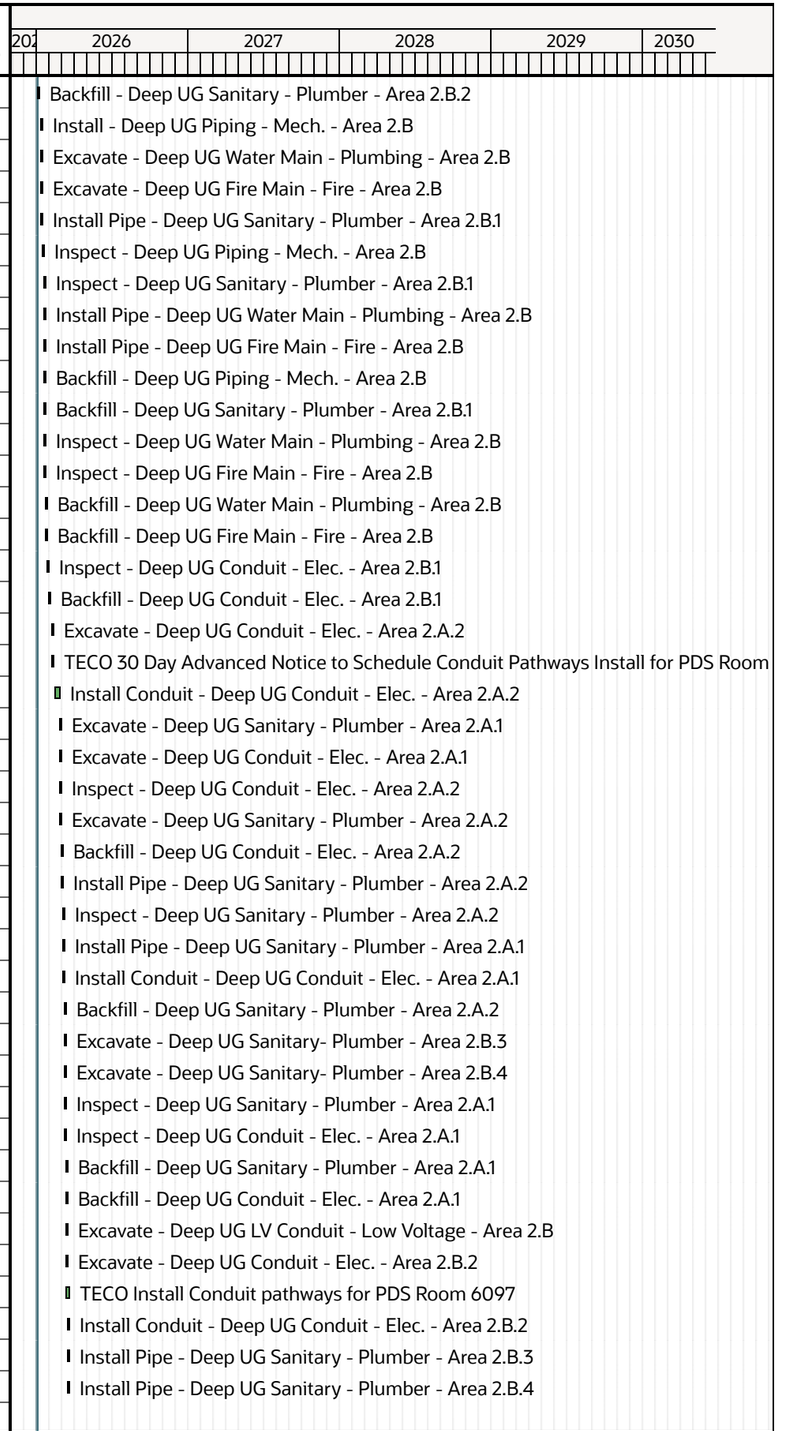

	ID	Name	Dur	Start	Finish	TF
4621	GI-FS-A2-6630	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 2.B	5.0d	16-Mar-26	20-Mar-26	21.0d
4622	GI-FS-A2-6750	Inspect - Deep UG Conduit - Elec. - Area 2.B.2	2.0d	16-Mar-26	17-Mar-26	21.0d
4623	GI-FS-A2-7220	Inspect - Deep UG Sanitary - Plumber - Area 2.B.3	2.0d	16-Mar-26	17-Mar-26	58.0d
4624	GI-FS-A2-7250	Inspect - Deep UG Sanitary - Plumber - Area 2.B.4	2.0d	16-Mar-26	17-Mar-26	58.0d
4625	GI-FS-A2-6760	Backfill - Deep UG Conduit - Elec. - Area 2.B.2	3.0d	18-Mar-26	20-Mar-26	21.0d
4626	GI-FS-A2-7230	Backfill - Deep UG Sanitary - Plumber - Area 2.B.3	2.0d	18-Mar-26	19-Mar-26	58.0d
4627	GI-FS-A2-7260	Backfill - Deep UG Sanitary - Plumber - Area 2.B.4	2.0d	18-Mar-26	19-Mar-26	58.0d
4628	GI-FS-A2-6640	Inspect - Deep UG LV Conduit - Low Voltage - Area 2.B	2.0d	19-Mar-26	20-Mar-26	21.0d
4629	GI-FS-A2-6650	Backfill - Deep UG LV Conduit - Low Voltage - Area 2.B	6.0d	23-Mar-26	30-Mar-26	21.0d
4630	WBS - Deep Underground MEP - Area 1		82.0d	6-Jan-26	29-Apr-26	46.0d
4631	GI-FS-A1-5650	Excavate - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	6-Jan-26	14-Jan-26	65.0d
4632	GI-FS-A1-7070	Excavate - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	6-Jan-26	14-Jan-26	30.0d
4633	GI-FS-A1-5710	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1A	7.0d	15-Jan-26	23-Jan-26	65.0d
4634	GI-FS-A1-7080	Install Pipe - Deep UG Sanitary - Plumber - Area 1.1B	7.0d	15-Jan-26	23-Jan-26	30.0d
4635	GI-FS-A1-5750	Inspect - Deep UG Sanitary - Plumber - Area 1.1A	2.0d	22-Jan-26	23-Jan-26	65.0d
4636	GI-FS-A1-7090	Inspect - Deep UG Sanitary - Plumber - Area 1.1B	2.0d	22-Jan-26	23-Jan-26	30.0d
4637	GI-FS-A1-5770	Backfill - Deep UG Sanitary - Plumber - Area 1.1A	2.0d	26-Jan-26	27-Jan-26	65.0d
4638	GI-FS-A1-7100	Backfill - Deep UG Sanitary - Plumber - Area 1.1B	2.0d	26-Jan-26	27-Jan-26	30.0d
4639	GI-FS-A1-6540	Excavate - Deep UG LV Conduit - Low Voltage - Area 1.1	5.0d	31-Mar-26	6-Apr-26	21.0d
4640	GI-FS-A1-6560	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 1.1	4.0d	7-Apr-26	10-Apr-26	21.0d
4641	GI-FS-A1-6590	Inspect - Deep UG LV Conduit - Low Voltage - Area 1.1	2.0d	9-Apr-26	10-Apr-26	21.0d
4642	GI-FS-A1-6600	Backfill - Deep UG LV Conduit - Low Voltage - Area 1.1	5.0d	13-Apr-26	17-Apr-26	21.0d
4643	GI-FS-A1-6450	Excavate - Deep UG LV Conduit - Low Voltage - Area 1.2	3.0d	20-Apr-26	22-Apr-26	46.0d
4644	GI-FS-A1-6470	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 1.2	2.0d	23-Apr-26	24-Apr-26	46.0d
4645	GI-FS-A1-6500	Inspect - Deep UG LV Conduit - Low Voltage - Area 1.2	2.0d	23-Apr-26	24-Apr-26	46.0d
4646	GI-FS-A1-6520	Backfill - Deep UG LV Conduit - Low Voltage - Area 1.2	3.0d	27-Apr-26	29-Apr-26	46.0d
4647	WBS - Deep Underground MEP - Area 6		68.0d	16-Jan-26	21-Apr-26	122.0d
4648	GI-FS-A6-5690	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.4	6.0d	16-Jan-26	23-Jan-26	129.0d
4649	GI-FS-A6-5720	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.4	4.0d	26-Jan-26	29-Jan-26	129.0d
4650	GI-FS-A6-5730	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.4	2.0d	28-Jan-26	29-Jan-26	129.0d
4651	GI-FS-A6-5740	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.4	5.0d	30-Jan-26	5-Feb-26	129.0d
4652	GI-FS-A6-6080	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.1	4.0d	6-Feb-26	11-Feb-26	129.0d
4653	GI-FS-A6-5870	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.2	6.0d	6-Feb-26	13-Feb-26	150.0d
4654	GI-FS-A6-6100	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.1	3.0d	12-Feb-26	16-Feb-26	129.0d
4655	GI-FS-A6-6150	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.1	2.0d	13-Feb-26	16-Feb-26	129.0d
4656	GI-FS-A6-5910	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.2	6.0d	16-Feb-26	23-Feb-26	150.0d
4657	GI-FS-A6-6160	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.1	4.0d	17-Feb-26	20-Feb-26	129.0d
4658	GI-FS-A6-5950	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.2	2.0d	20-Feb-26	23-Feb-26	150.0d
4659	GI-FS-A6-5960	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.2	7.0d	24-Feb-26	4-Mar-26	150.0d
4660	GI-FS-A6-5920	Excavate - Deep UG Conduit - Elec. - Area 6.2	5.0d	5-Mar-26	11-Mar-26	106.0d
4661	GI-FS-A6-5990	Excavate - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	5-Mar-26	6-Mar-26	150.0d
4662	GI-FS-A6-6030	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	9-Mar-26	10-Mar-26	150.0d

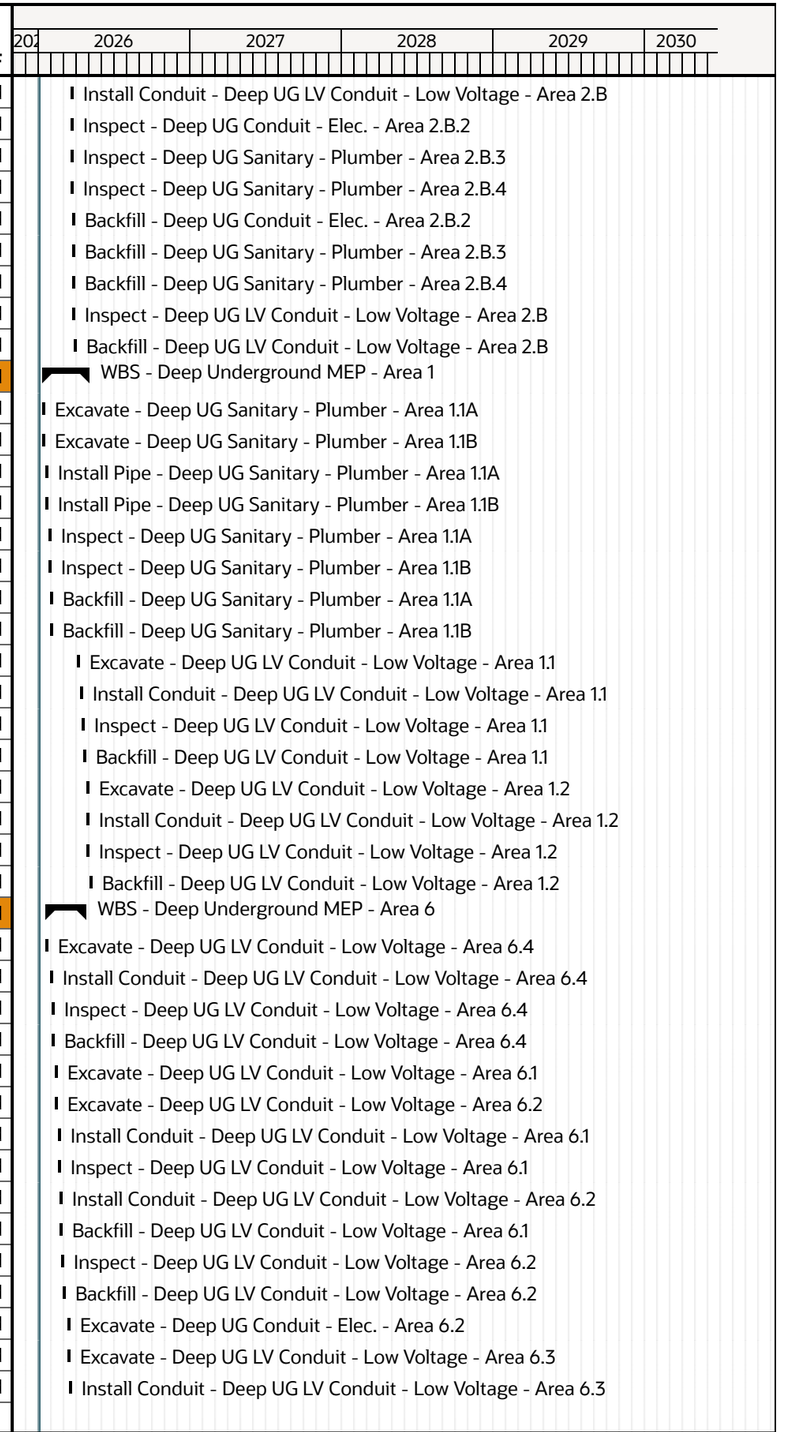


	ID	Name	Dur	Start	Finish	TF
4663	GI-FS-A6-6040	Inspect - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	9-Mar-26	10-Mar-26	150.0d
4664	GI-FS-A6-6530	Excavate - Deep UG Sanitary - Plumber - Area 6.1	4.0d	10-Mar-26	13-Mar-26	108.0d
4665	GI-FS-A6-6050	Backfill - Deep UG LV Conduit - Low Voltage - Area 6.3	2.0d	11-Mar-26	12-Mar-26	150.0d
4666	GI-FS-A6-5940	Install Conduit - Deep UG Conduit - Elec. - Area 6.2	5.0d	12-Mar-26	18-Mar-26	106.0d
4667	GI-FS-A6-6400	Excavate - Deep UG Conduit - Elec. - Area 6.1	5.0d	13-Mar-26	19-Mar-26	100.0d
4668	GI-FS-A6-6550	Install Pipe - Deep UG Sanitary - Plumber - Area 6.1	4.0d	16-Mar-26	19-Mar-26	108.0d
4669	GI-FS-A6-5970	Inspect - Deep UG Conduit - Elec. - Area 6.2	2.0d	17-Mar-26	18-Mar-26	106.0d
4670	GI-FS-A6-6570	Inspect - Deep UG Sanitary - Plumber - Area 6.1	2.0d	18-Mar-26	19-Mar-26	108.0d
4671	GI-FS-A6-5980	Backfill - Deep UG Conduit - Elec. - Area 6.2	5.0d	19-Mar-26	25-Mar-26	106.0d
4672	GI-FS-A6-6580	Backfill - Deep UG Sanitary - Plumber - Area 6.1	2.0d	20-Mar-26	23-Mar-26	108.0d
4673	GI-FS-A6-6430	Install Conduit - Deep UG Conduit - Elec. - Area 6.1	5.0d	20-Mar-26	26-Mar-26	100.0d
4674	GI-FS-A6-6460	Inspect - Deep UG Conduit - Elec. - Area 6.1	2.0d	25-Mar-26	26-Mar-26	100.0d
4675	GI-FS-A6-6480	Backfill - Deep UG Conduit - Elec. - Area 6.1	5.0d	27-Mar-26	2-Apr-26	100.0d
4676	GI-FS-A6-6890	Excavate - Deep UG Conduit - Elec. - Area 6.3	5.0d	3-Apr-26	9-Apr-26	122.0d
4677	GI-FS-A6-6900	Install Conduit - Deep UG Conduit - Elec. - Area 6.3	5.0d	10-Apr-26	16-Apr-26	122.0d
4678	GI-FS-A6-6910	Inspect - Deep UG Conduit - Elec. - Area 6.3	2.0d	15-Apr-26	16-Apr-26	122.0d
4679	GI-FS-A6-6920	Backfill - Deep UG Conduit - Elec. - Area 6.3	3.0d	17-Apr-26	21-Apr-26	122.0d
4680	WBS - Deep Underground MEP - Area 3		88.0d	10-Feb-26	12-Jun-26	59.0d
4681	GI-FS-A3-6840	Directional Bore to Anchor Tenant Operations Area for Temp Power	5.0d	10-Feb-26	16-Feb-26	71.0d
4682	GI-FS-A3-6830	Pull Feeders/Set Transformers/Temp Panels Power On	10.0d	17-Feb-26	2-Mar-26	71.0d
4683	GI-FS-A3-6060	Excavate - Deep UG Conduit - Elec. - Area 3.1	5.0d	6-May-26	12-May-26	35.0d
4684	GI-FS-A3-6350	Excavate - Deep UG LV Conduit - Low Voltage - Area 3.1	5.0d	6-May-26	12-May-26	36.0d
4685	GI-FS-A3-5880	Excavate - Deep UG Sanitary - Plumber - Area 3.1	7.0d	6-May-26	14-May-26	26.0d
4686	GI-FS-A3-6120	Install Conduit - Deep UG Conduit - Elec. - Area 3.1	5.0d	13-May-26	19-May-26	59.0d
4687	GI-FS-A3-6370	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 3.1	4.0d	13-May-26	18-May-26	36.0d
4688	GI-FS-A3-6410	Inspect - Deep UG LV Conduit - Low Voltage - Area 3.1	2.0d	15-May-26	18-May-26	36.0d
4689	GI-FS-A3-5930	Install Pipe - Deep UG Sanitary - Plumber - Area 3.1	13.0d	15-May-26	3-Jun-26	26.0d
4690	GI-FS-A3-6200	Inspect - Deep UG Conduit - Elec. - Area 3.1	2.0d	18-May-26	19-May-26	59.0d
4691	GI-FS-A3-6420	Backfill - Deep UG LV Conduit - Low Voltage - Area 3.1	5.0d	19-May-26	26-May-26	36.0d
4692	GI-FS-A3-6210	Backfill - Deep UG Conduit - Elec. - Area 3.1	3.0d	20-May-26	22-May-26	59.0d
4693	GI-FS-A3-6770	Excavate - Deep UG Conduit - Elec. - Area 3.2	5.0d	26-May-26	1-Jun-26	59.0d
4694	GI-FS-A3-6010	Inspect - Deep UG Sanitary - Plumber - Area 3.1	2.0d	2-Jun-26	3-Jun-26	26.0d
4695	GI-FS-A3-6780	Install Conduit - Deep UG Conduit - Elec. - Area 3.2	5.0d	2-Jun-26	8-Jun-26	59.0d
4696	GI-FS-A3-6020	Backfill - Deep UG Sanitary - Plumber - Area 3.1	4.0d	4-Jun-26	9-Jun-26	26.0d
4697	GI-FS-A3-6790	Inspect - Deep UG Conduit - Elec. - Area 3.2	2.0d	8-Jun-26	9-Jun-26	59.0d
4698	GI-FS-A3-6800	Backfill - Deep UG Conduit - Elec. - Area 3.2	3.0d	10-Jun-26	12-Jun-26	59.0d
4699	WBS - Deep Underground MEP - Area 5		51.0d	4-Jun-26	14-Aug-26	80.0d
4700	GI-FS-A5-6000	Excavate - Deep UG Conduit - Elec. - Area 5.1	5.0d	4-Jun-26	10-Jun-26	117.0d
4701	GI-FS-A5-5560	Excavate - Deep UG LV Conduit - Low Voltage - Area 5.1	5.0d	4-Jun-26	10-Jun-26	15.0d
4702	GI-FS-A5-5600	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 5.1	4.0d	9-Jun-26	12-Jun-26	15.0d
4703	GI-FS-A5-6070	Install Conduit - Deep UG Conduit - Elec. - Area 5.1	5.0d	11-Jun-26	17-Jun-26	117.0d
4704	GI-FS-A5-5640	Inspect - Deep UG LV Conduit - Low Voltage - Area 5.1	2.0d	11-Jun-26	12-Jun-26	15.0d

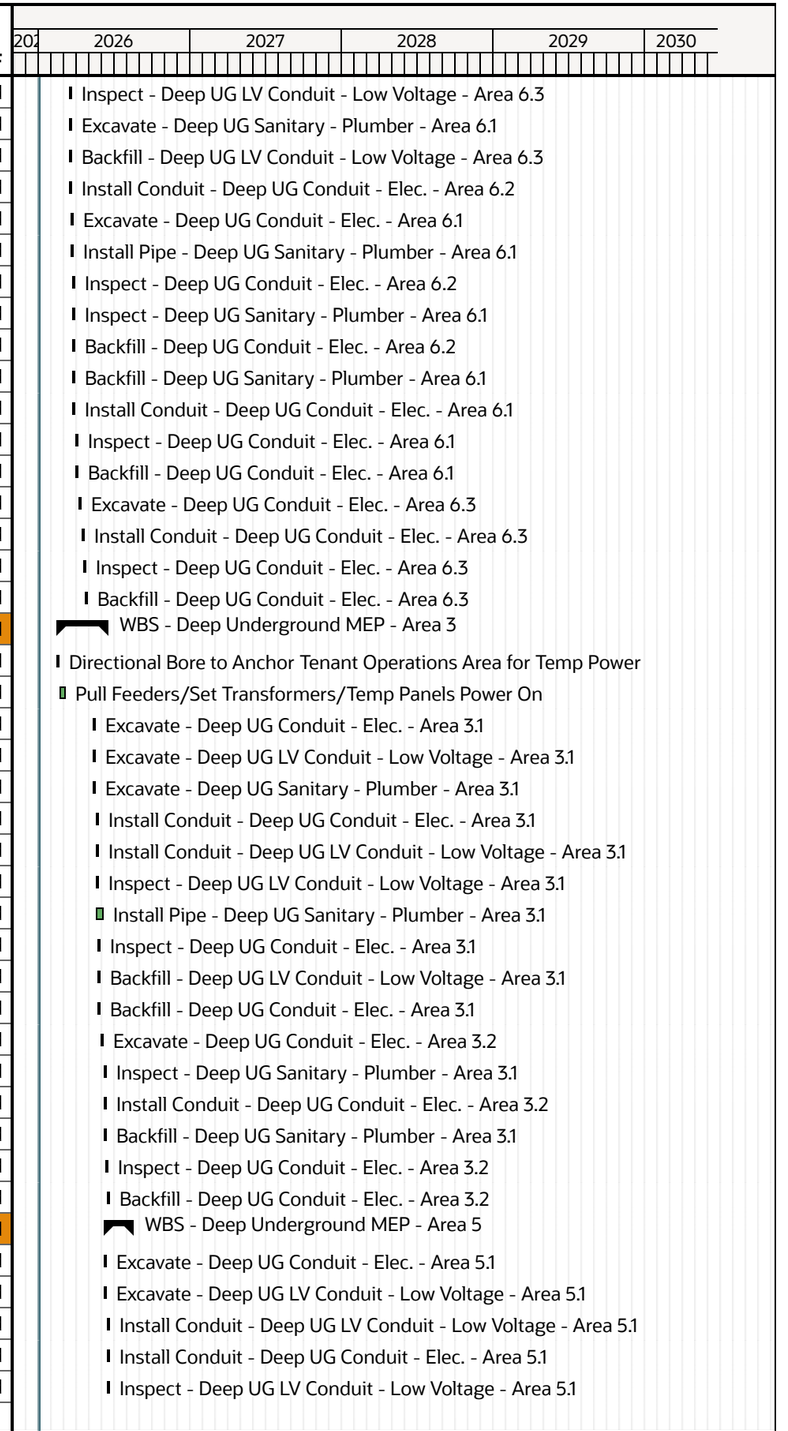

	ID	Name	Dur	Start	Finish	TF
4705	GI-FS-A5-5660	Backfill - Deep UG LV Conduit - Low Voltage - Area 5.1	4.0d	15-Jun-26	18-Jun-26	15.0d
4706	GI-FS-A5-6180	Excavate - Deep UG Sanitary - Plumber - Area 5.1	10.0d	15-Jun-26	26-Jun-26	15.0d
4707	GI-FS-A5-6130	Inspect - Deep UG Conduit - Elec. - Area 5.1	2.0d	17-Jun-26	18-Jun-26	117.0d
4708	GI-FS-A5-6140	Backfill - Deep UG Conduit - Elec. - Area 5.1	3.0d	19-Jun-26	23-Jun-26	117.0d
4709	GI-FS-A5-6230	Install Pipe - Deep UG Sanitary - Plumber - Area 5.1	10.0d	29-Jun-26	13-Jul-26	15.0d
4710	GI-FS-A5-6270	Inspect - Deep UG Sanitary - Plumber - Area 5.1	2.0d	10-Jul-26	13-Jul-26	15.0d
4711	GI-FS-A5-6280	Backfill - Deep UG Sanitary - Plumber - Area 5.1	5.0d	14-Jul-26	20-Jul-26	15.0d
4712	GI-FS-A5-6300	Excavate - Deep UG Sanitary - Plumber - Area 5.2	10.0d	14-Jul-26	27-Jul-26	15.0d
4713	GI-FS-A5-6340	Install Pipe - Deep UG Sanitary - Plumber - Area 5.2	6.0d	28-Jul-26	4-Aug-26	15.0d
4714	GI-FS-A5-6360	Inspect - Deep UG Sanitary - Plumber - Area 5.2	2.0d	3-Aug-26	4-Aug-26	15.0d
4715	GI-FS-A5-6380	Backfill - Deep UG Sanitary - Plumber - Area 5.2	8.0d	5-Aug-26	14-Aug-26	15.0d
4716	WBS - Deep Underground MEP - Area 4		46.0d	2-Jul-26	4-Sep-26	92.0d
4717	GI-FS-A4-6290	Excavate - Deep UG LV Conduit - Low Voltage - Area 4.1	3.0d	2-Jul-26	7-Jul-26	0.0d
4718	GI-FS-A4-6810	Excavate - Deep UG Conduit - Elec. - Area 4.1	5.0d	2-Jul-26	9-Jul-26	112.0d
4719	GI-FS-A4-6310	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 4.1	2.0d	8-Jul-26	9-Jul-26	0.0d
4720	GI-FS-A4-6320	Inspect - Deep UG LV Conduit - Low Voltage - Area 4.1	2.0d	10-Jul-26	13-Jul-26	0.0d
4721	GI-FS-A4-6820	Install Conduit - Deep UG Conduit - Elec. - Area 4.1	5.0d	10-Jul-26	16-Jul-26	112.0d
4722	GI-FS-A4-6330	Backfill - Deep UG LV Conduit - Low Voltage - Area 4.1	3.0d	14-Jul-26	16-Jul-26	0.0d
4723	GI-FS-A4-6830	Inspect - Deep UG Conduit - Elec. - Area 4.1	2.0d	15-Jul-26	16-Jul-26	112.0d
4724	GI-FS-A4-5430	Excavate - Deep UG LV Conduit - Low Voltage - Area 4.2	7.0d	17-Jul-26	27-Jul-26	65.0d
4725	GI-FS-A4-6690	Excavate - Deep UG Sanitary - Plumber - Area 4.1	4.0d	17-Jul-26	22-Jul-26	0.0d
4726	GI-FS-A4-6840	Backfill - Deep UG Conduit - Elec. - Area 4.1	3.0d	17-Jul-26	21-Jul-26	112.0d
4727	GI-FS-A4-6850	Excavate - Deep UG Conduit - Elec. - Area 4.2	5.0d	22-Jul-26	28-Jul-26	112.0d
4728	GI-FS-A4-6700	Install Pipe - Deep UG Sanitary - Plumber - Area 4.1	4.0d	23-Jul-26	28-Jul-26	0.0d
4729	GI-FS-A4-6710	Inspect - Deep UG Sanitary - Plumber - Area 4.1	2.0d	27-Jul-26	28-Jul-26	0.0d
4730	GI-FS-A4-5480	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 4.2	7.0d	28-Jul-26	5-Aug-26	65.0d
4731	GI-FS-A4-6720	Backfill - Deep UG Sanitary - Plumber - Area 4.1	3.0d	29-Jul-26	31-Jul-26	0.0d
4732	GI-FS-A4-6860	Install Conduit - Deep UG Conduit - Elec. - Area 4.2	5.0d	29-Jul-26	4-Aug-26	112.0d
4733	GI-FS-A4-6090	Excavate - Deep UG Sanitary - Plumber - Area 4.2	4.0d	3-Aug-26	6-Aug-26	0.0d
4734	GI-FS-A4-6870	Inspect - Deep UG Conduit - Elec. - Area 4.2	2.0d	3-Aug-26	4-Aug-26	112.0d
4735	GI-FS-A4-5520	Inspect - Deep UG LV Conduit - Low Voltage - Area 4.2	2.0d	4-Aug-26	5-Aug-26	65.0d
4736	GI-FS-A4-6880	Backfill - Deep UG Conduit - Elec. - Area 4.2	3.0d	5-Aug-26	7-Aug-26	112.0d
4737	GI-FS-A4-5540	Backfill - Deep UG LV Conduit - Low Voltage - Area 4.2	8.0d	6-Aug-26	17-Aug-26	65.0d
4738	GI-FS-A4-6110	Install Pipe - Deep UG Sanitary - Plumber - Area 4.2	4.0d	7-Aug-26	12-Aug-26	0.0d
4739	GI-FS-A4-6170	Inspect - Deep UG Sanitary - Plumber - Area 4.2	2.0d	11-Aug-26	12-Aug-26	0.0d
4740	GI-FS-A4-6190	Backfill - Deep UG Sanitary - Plumber - Area 4.2	3.0d	13-Aug-26	17-Aug-26	0.0d
4741	GI-FS-A4-6220	Excavate - Deep UG LV Conduit - Low Voltage - Area 4.3	5.0d	18-Aug-26	24-Aug-26	65.0d
4742	GI-FS-A4-6390	Excavate - Deep UG Sanitary - Plumber - Area 4.3	6.0d	18-Aug-26	25-Aug-26	0.0d
4743	GI-FS-A4-6240	Install Conduit - Deep UG LV Conduit - Low Voltage - Area 4.3	4.0d	25-Aug-26	28-Aug-26	65.0d
4744	GI-FS-A4-6440	Install Pipe - Deep UG Sanitary - Plumber - Area 4.3	6.0d	26-Aug-26	2-Sep-26	0.0d
4745	GI-FS-A4-6250	Inspect - Deep UG LV Conduit - Low Voltage - Area 4.3	2.0d	27-Aug-26	28-Aug-26	65.0d
4746	GI-FS-A4-6260	Backfill - Deep UG LV Conduit - Low Voltage - Area 4.3	5.0d	31-Aug-26	4-Sep-26	65.0d




	ID	Name	Dur	Start	Finish	TF
4747	GI-FS-A4-6490	Inspect - Deep UG Sanitary - Plumber - Area 4.3	2.0d	1-Sep-26	2-Sep-26	0.0d
4748	GI-FS-A4-6510	Backfill - Deep UG Sanitary - Plumber - Area 4.3	2.0d	3-Sep-26	4-Sep-26	0.0d
4749	WBS - Foundations - Substantial Completion		32.0d	8-Sep-26	21-Oct-26	0.0d
4750	GI-FS-4350	Prep & Submit Pre-Substantial Completion Documentation - Found. Scope	20.0d	8-Sep-26	5-Oct-26	0.0d
4751	GI-FS-4360	Substantial Completion Final Clean - Found. Scope	5.0d	6-Oct-26	12-Oct-26	0.0d
4752	GI-FS-4370	Final Insp. - Found. Scope	5.0d	13-Oct-26	19-Oct-26	0.0d
4753	GI-FS-4380	HP Pre Substantial Completion QC Insp. - Found. Scope	2.0d	16-Oct-26	19-Oct-26	0.0d
4754	GI-FS-4390	Substantial Completion Insp. - Found. Scope	2.0d	20-Oct-26	21-Oct-26	0.0d
4755	WBS - Structure & Elevated Slabs		311.0d	27-Mar-26	16-Jun-27	542.0d
4756	GI-FS-200	Stand Precast Elevator Shafts - Structure & Slabs	20.0d	27-Mar-26	23-Apr-26	17.0d
4757	GI-FS-4400	Structural & Misc Steel ASD Steel Fab. (LOE)	274.0d	19-May-26	16-Jun-27	66.0d
4758	GI-FS-140	Steel Deck & Detailed Metal Decks - Structure & Slabs (LOE)	193.0d	1-Jun-26	4-Mar-27	16.0d
4759	GI-FS-360	Slabs on Metal Deck (SOMD) Hangers Through Concrete - Structure & Slabs (L...	218.0d	22-Jun-26	29-Apr-27	202.0d
4760	GI-FS-MLS-180	Structure Complete - Structure & Slabs	0.0d		29-Apr-27	202.0d
4761	GI-FS-MLS-190	Miscellaneous Metals Complete - Structure	0.0d		16-Jun-27	541.0d
4762	WBS - Structure Area - November - Seq 1		80.0d	19-May-26	10-Sep-26	63.0d
4763	GI-FS-SQN-130	Erect & Bolt/Weld - NOVEMBER - Steel Seq. S1	8.0d	19-May-26	29-May-26	0.0d
4764	GI-FS-SQN-140	Deck & Detail - NOVEMBER - Steel Seq. S1	15.0d	1-Jun-26	19-Jun-26	63.0d
4765	GI-FS-SQN-150	Install Stairs - NOVEMBER - Steel Seq. S1	5.0d	1-Jun-26	5-Jun-26	0.0d
4766	GI-FS-SQN-170	Elevator Steel - NOVEMBER - Steel Seq. S1	3.0d	8-Jun-26	10-Jun-26	0.0d
4767	GI-FS-SQN-160	Turn Over to MEPF Contractors - NOVEMBER - Steel Seq. S1	0.0d		19-Jun-26	63.0d
4768	GI-FS-SQF-80	Monumental Stairs - NOVEMBER - Steel	12.0d	4-Aug-26	19-Aug-26	63.0d
4769	GI-FS-SQN-180	Misc Metal (Handrails & etc) - NOVEMBER - Steel	15.0d	20-Aug-26	10-Sep-26	63.0d
4770	WBS - Steel Sequence November -SOMD		28.0d	22-Jun-26	30-Jul-26	77.0d
4771	GI-FS-SQN-SOMD-90	MEPF Hangers & Block Outs Concourse - SEQ NOVEMBER - SOMD	6.0d	22-Jun-26	29-Jun-26	63.0d
4772	GI-FS-SQN-SOMD-100	MEPF Hangers & Block Outs Roof - SEQ NOVEMBER - SOMD	6.0d	22-Jun-26	29-Jun-26	76.0d
4773	GI-FS-SQN-SOMD-110	FRP Pour 1 Concourse - SEQ NOVEMBER - SOMD	6.0d	30-Jun-26	8-Jul-26	76.0d
4774	GI-FS-SQN-SOMD-160	7 Day Concrete Cure - Concourse - SEQ NOVEMBER - SOMD	7.0d	9-Jul-26	15-Jul-26	108.0d
4775	GI-FS-SQN-SOMD-140	FRP Pour 1 Club - SEQ NOVEMBER - SOMD	6.0d	16-Jul-26	23-Jul-26	77.0d
4776	GI-FS-SQN-SOMD-150	7 Day Concrete Cure - Club - SEQ NOVEMBER - SOMD	7.0d	24-Jul-26	30-Jul-26	109.0d
4777	WBS - Structure Area - November -SOG		24.0d	30-Jun-26	3-Aug-26	63.0d
4778	GI-FS-SQN-SOG-110	Underground MEPF - Pour 1 - SEQ NOVEMBER - SOG	5.0d	30-Jun-26	7-Jul-26	63.0d
4779	GI-FS-SQN-SOG-130	FRP Pour 1 - SEQ NOVEMBER - SOG	7.0d	8-Jul-26	16-Jul-26	63.0d
4780	GI-FS-SQN-SOG-170	Underground MEPF - Pour 2 - SEQ NOVEMBER - SOG	5.0d	8-Jul-26	14-Jul-26	65.0d
4781	GI-FS-SQN-SOG-150	FRP Pour 2 - SEQ NOVEMBER - SOG	7.0d	17-Jul-26	27-Jul-26	63.0d
4782	GI-FS-SQN-SOG-160	7 Day Concrete Cure - SEQ NOVEMBER - SOG	7.0d	28-Jul-26	3-Aug-26	89.0d
4783	WBS - Structure Area - Alpha - Seq 2 & 3		122.0d	11-Jun-26	3-Dec-26	74.0d
4784	GI-FS-SQA-10	Erect & Bolt/Weld Lower Steel - SEQ ALPHA - Steel (S2)	15.0d	11-Jun-26	1-Jul-26	0.0d
4785	GI-FS-SQA-120	Erect & Bolt/Weld Upper Steel - SEQ ALPHA - Steel (S3)	11.0d	2-Jul-26	17-Jul-26	0.0d
4786	GI-FS-SQA-20	Deck & Detail - SEQ ALPHA - Steel (S2 & S3)	20.0d	20-Jul-26	14-Aug-26	0.0d
4787	GI-FS-SQA-30	Install Stairs - SEQ ALPHA - Steel	4.0d	20-Jul-26	23-Jul-26	0.0d
4788	GI-FS-SQA-50	Elevator Steel - SEQ ALPHA - Steel	3.0d	24-Jul-26	28-Jul-26	0.0d

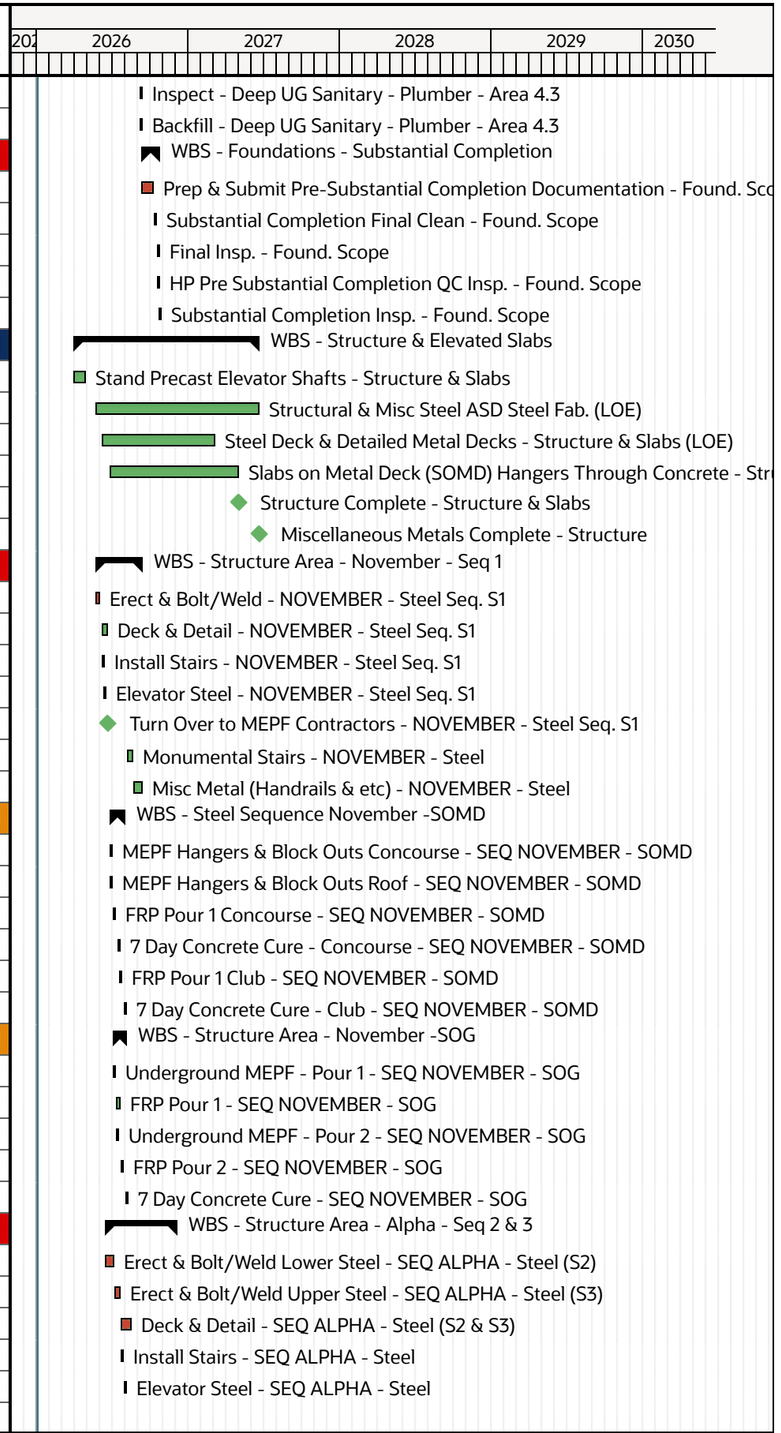


ID	Name	Dur	Start	Finish	TF
4789	GI-FS-SQA-40	Turn Over to MEPF Contractors - SEQ ALPHA - Steel (S2 & S3)	0.0d		14-Aug-26	0.0d
4790	GI-FS-SQA-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ ALPHA - Steel	20.0d	13-Oct-26	9-Nov-26	41.0d
4791	WBS - Steel Sequence Alpha - SOMD		40.0d	17-Aug-26	12-Oct-26	97.0d
4792	GI-FS-SQA-SOMD-20	MEPF Hangers & Block Outs Club - SEQ ALPHA - SOMD	6.0d	17-Aug-26	24-Aug-26	0.0d
4793	GI-FS-SQA-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ ALPHA - SOMD	6.0d	17-Aug-26	24-Aug-26	0.0d
4794	GI-FS-SQA-SOMD-30	FRP Pour 1 Concourse - SEQ ALPHA - SOMD	6.0d	25-Aug-26	1-Sep-26	0.0d
4795	GI-FS-SQA-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ ALPHA - SOMD	6.0d	25-Aug-26	1-Sep-26	125.0d
4796	GI-FS-SQA-SOMD-50	FRP Pour 2 Concourse - SEQ ALPHA - SOMD	6.0d	2-Sep-26	10-Sep-26	0.0d
4797	GI-FS-SQA-SOMD-60	FRP Pour 3 Concourse - SEQ ALPHA - SOMD	6.0d	11-Sep-26	18-Sep-26	0.0d
4798	GI-FS-SQA-SOMD-90	7 Day Concrete Cure - Concourse - SEQ ALPHA - SOMD	7.0d	19-Sep-26	25-Sep-26	59.0d
4799	GI-FS-SQA-SOMD-70	FRP Pour 1 Club - SEQ ALPHA - SOMD	6.0d	28-Sep-26	5-Oct-26	41.0d
4800	GI-FS-SQA-SOMD-80	7 Day Concrete Cure - Club - SEQ ALPHA - SOMD	7.0d	6-Oct-26	12-Oct-26	57.0d
4801	WBS - Structure Area - Alpha - SOG		38.0d	25-Aug-26	16-Oct-26	88.0d
4802	GI-FS-SQA-SOG-90	Underground MEPF - Pour 2 - SEQ ALPHA - SOG	5.0d	25-Aug-26	31-Aug-26	12.0d
4803	GI-FS-SQA-SOG-40	FRP Pour 2 - SEQ ALPHA - SOG	7.0d	1-Sep-26	10-Sep-26	114.0d
4804	GI-FS-SQA-SOG-100	Underground MEPF - Pour 3 - SEQ ALPHA - SOG	5.0d	1-Sep-26	8-Sep-26	12.0d
4805	GI-FS-SQA-SOG-60	FRP Pour 3 - SEQ ALPHA - SOG	7.0d	9-Sep-26	17-Sep-26	30.0d
4806	GI-FS-SQA-SOG-110	Underground MEPF - Pour 4 - SEQ ALPHA - SOG	5.0d	9-Sep-26	15-Sep-26	12.0d
4807	GI-FS-SQA-SOG-70	FRP Pour 4 - SEQ ALPHA - SOG	5.0d	18-Sep-26	24-Sep-26	30.0d
4808	GI-FS-SQA-SOG-80	7 Day Concrete Cure - SEQ ALPHA - SOG	7.0d	25-Sep-26	1-Oct-26	42.0d
4809	GI-FS-SQA-SOG-120	FRP Pour 5 BHS Mezzanine Deck - SEQ ALPHA - SOMD	5.0d	25-Sep-26	1-Oct-26	93.0d
4810	GI-FS-SQA-SOG-10	Underground MEPF - Pour 1 - SEQ ALPHA - SOG	5.0d	1-Oct-26	7-Oct-26	1.0d
4811	GI-FS-SQA-SOG-30	FRP Pour 1 - SEQ ALPHA - SOG	7.0d	8-Oct-26	16-Oct-26	1.0d
4812	WBS - Structure Area - Alpha - Guideway Structure		76.0d	17-Aug-26	3-Dec-26	74.0d
4813	GI-FS-SQA-SOG-130	FRP Guideway Structure Column	10.0d	17-Aug-26	28-Aug-26	1.0d
4814	GI-FS-SQA-SOG-150	Install Guideway Structure Deck Shoring	5.0d	31-Aug-26	4-Sep-26	1.0d
4815	GI-FS-SQA-SOG-200	FRP Guideway Structure Deck	5.0d	8-Sep-26	14-Sep-26	1.0d
4816	GI-FS-SQA-SOG-210	Guideway Structure Deck Cure	7.0d	15-Sep-26	23-Sep-26	1.0d
4817	GI-FS-SQA-SOG-250	Guideway Structure Shoring Removal	5.0d	24-Sep-26	30-Sep-26	1.0d
4818	GI-FS-SQA-SOG-160	FRP Guideway Structure Plinths	10.0d	1-Oct-26	14-Oct-26	74.0d
4819	GI-FS-SQA-SOG-170	FRP Guideway Structure Guidebeam Support	5.0d	15-Oct-26	21-Oct-26	74.0d
4820	GI-FS-SQA-SOG-190	Install Guideway Structure Running Surface Shoring	5.0d	22-Oct-26	28-Oct-26	74.0d
4821	GI-FS-SQA-SOG-220	FRP Guideway Structure Running Surface	10.0d	29-Oct-26	11-Nov-26	74.0d
4822	GI-FS-SQA-SOG-230	Guideway Structure Running Surface Cure	7.0d	12-Nov-26	20-Nov-26	74.0d
4823	GI-FS-SQA-SOG-240	Guideway Structure Running Surface Shoring Form Strip	7.0d	23-Nov-26	3-Dec-26	74.0d
4824	WBS - Structure Area - Bravo - Seq 4		93.0d	29-Jul-26	9-Dec-26	57.0d
4825	GI-FS-SQB-10	Erect & Bolt/Weld - SEQ BRAVO - Steel (S4)	12.0d	29-Jul-26	13-Aug-26	0.0d
4826	GI-FS-SQB-30	Deck & Detail - SEQ BRAVO - Steel (S4)	20.0d	14-Aug-26	11-Sep-26	52.0d
4827	GI-FS-SQB-20	Install Stairs - SEQ BRAVO - Steel	4.0d	14-Aug-26	19-Aug-26	0.0d
4828	GI-FS-SQB-50	Elevator Steel - SEQ BRAVO - Steel	3.0d	20-Aug-26	24-Aug-26	0.0d
4829	GI-FS-SQB-40	Turn Over to MEPF Contractors - SEQ BRAVO - Steel (S4)	0.0d		11-Sep-26	52.0d
4830	GI-FS-SQB-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ BRAVO - Steel	20.0d	10-Nov-26	9-Dec-26	41.0d




ID	Name	Dur	Start	Finish	TF
4831	WBS - Structure Area - Bravo - SOMD	29.0d	14-Sep-26	22-Oct-26	89.0d
4832	GI-FS-SQB-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ BRAVO - SOMD	6.0d	14-Sep-26	21-Sep-26	52.0d
4833	GI-FS-SQB-SOMD-10	MEPF Hangers & Block Outs Club - SEQ BRAVO - SOMD	6.0d	14-Sep-26	21-Sep-26	52.0d
4834	GI-FS-SQB-SOMD-30	FRP Pour 1 Concourse - SEQ BRAVO - SOMD	6.0d	22-Sep-26	29-Sep-26	54.0d
4835	GI-FS-SQB-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ BRAVO - SOMD	6.0d	22-Sep-26	29-Sep-26	106.0d
4836	GI-FS-SQB-SOMD-50	FRP Pour 2 Concourse - SEQ BRAVO - SOMD	6.0d	30-Sep-26	7-Oct-26	54.0d
4837	GI-FS-SQB-SOMD-80	7 Day Concrete Cure - Concourse- SEQ BRAVO - SOMD	7.0d	8-Oct-26	14-Oct-26	77.0d
4838	GI-FS-SQB-SOMD-70	FRP Pour 1 Club - SEQ BRAVO - SOMD	6.0d	15-Oct-26	22-Oct-26	53.0d
4839	WBS - Structure Area - Bravo - SOG	24.0d	22-Sep-26	23-Oct-26	52.0d
4840	GI-FS-SQB-SOG-10	Underground MEPF - Pour 1 - SEQ BRAVO - SOG	5.0d	22-Sep-26	28-Sep-26	52.0d
4841	GI-FS-SQB-SOG-30	FRP Pour 1 - SEQ BRAVO - SOG	7.0d	29-Sep-26	7-Oct-26	52.0d
4842	GI-FS-SQB-SOG-70	Underground MEPF - Pour 2 - SEQ BRAVO - SOG	5.0d	29-Sep-26	5-Oct-26	54.0d
4843	GI-FS-SQB-SOG-50	FRP Pour 2 - SEQ BRAVO - SOG	7.0d	8-Oct-26	16-Oct-26	52.0d
4844	GI-FS-SQB-SOG-60	7 Day Concrete Cure - Apron- SEQ BRAVO - SOG	7.0d	17-Oct-26	23-Oct-26	76.0d
4845	WBS - Structure Area - Charlie - Seq 5	94.0d	25-Aug-26	8-Jan-27	41.0d
4846	GI-FS-SQC-10	Erect & Bolt/Weld - SEQ CHARLIE - Steel (S5)	12.0d	25-Aug-26	10-Sep-26	0.0d
4847	GI-FS-SQC-20	Deck & Detail - SEQ CHARLIE - Steel (S5)	20.0d	11-Sep-26	8-Oct-26	42.0d
4848	GI-FS-SQC-30	Install Stairs - SEQ CHARLIE - Steel	4.0d	11-Sep-26	16-Sep-26	0.0d
4849	GI-FS-SQC-50	Elevator Steel - SEQ CHARLIE - Steel	3.0d	17-Sep-26	21-Sep-26	0.0d
4850	GI-FS-SQC-40	Turn Over to MEPF Contractors - SEQ CHARLIE - Steel (S5)	0.0d		8-Oct-26	42.0d
4851	GI-FS-SQC-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ CHARLIE - Steel	20.0d	10-Dec-26	8-Jan-27	41.0d
4852	WBS - Structure Area - Charlie - SOMD	34.0d	9-Oct-26	25-Nov-26	65.0d
4853	GI-FS-SQC-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ CHARLIE - SOMD	6.0d	9-Oct-26	16-Oct-26	42.0d
4854	GI-FS-SQC-SOMD-20	MEPF Hangers & Block Outs Club- SEQ CHARLIE - SOMD	6.0d	9-Oct-26	16-Oct-26	42.0d
4855	GI-FS-SQC-SOMD-30	FRP Pour 1 Concourse- SEQ CHARLIE - SOMD	6.0d	19-Oct-26	26-Oct-26	43.0d
4856	GI-FS-SQC-SOMD-40	MEPF Hangers & Block Outs Roof- SEQ CHARLIE - SOMD	6.0d	19-Oct-26	26-Oct-26	87.0d
4857	GI-FS-SQC-SOMD-50	FRP Pour 2 Concourse- SEQ CHARLIE - SOMD	6.0d	27-Oct-26	3-Nov-26	43.0d
4858	GI-FS-SQC-SOMD-80	7 Day Concrete Cure - Concourse - SEQ CHARLIE - SOMD	7.0d	4-Nov-26	10-Nov-26	61.0d
4859	GI-FS-SQC-SOMD-60	FRP Pour 1 Club- SEQ CHARLIE - SOMD	6.0d	11-Nov-26	18-Nov-26	49.0d
4860	GI-FS-SQC-SOMD-70	7 Day Concrete Cure - Club - SEQ CHARLIE - SOMD	7.0d	19-Nov-26	25-Nov-26	71.0d
4861	WBS - Structure Area - Charlie - SOG	24.0d	19-Oct-26	19-Nov-26	42.0d
4862	GI-FS-SQC-SOG-10	Underground MEPF - Pour 1 - SEQ CHARLIE - SOG	5.0d	19-Oct-26	23-Oct-26	42.0d
4863	GI-FS-SQC-SOG-30	FRP Pour 1 - SEQ CHARLIE - SOG	7.0d	26-Oct-26	3-Nov-26	42.0d
4864	GI-FS-SQC-SOG-70	Underground MEPF - Pour 2 - SEQ CHARLIE - SOG	5.0d	26-Oct-26	30-Oct-26	44.0d
4865	GI-FS-SQC-SOG-50	FRP Pour 2 - SEQ CHARLIE - SOG	7.0d	4-Nov-26	12-Nov-26	42.0d
4866	GI-FS-SQC-SOG-60	7 Day Concrete Cure - SEQ CHARLIE - SOG	7.0d	13-Nov-26	19-Nov-26	62.0d
4867	WBS - Structure Area - India - Seq 6	95.0d	22-Sep-26	5-Feb-27	78.0d
4868	GI-FS-SQI-10	Erect & Bolt/Weld - SEQ INDIA - Steel (S6)	6.0d	22-Sep-26	29-Sep-26	0.0d
4869	GI-FS-SQI-20	Deck & Detail - SEQ INDIA - Steel (S6)	20.0d	30-Sep-26	27-Oct-26	35.0d
4870	GI-FS-SQI-30	Install Stairs - SEQ INDIA - Steel	5.0d	30-Sep-26	6-Oct-26	0.0d
4871	GI-FS-SQI-50	Elevator Steel - SEQ INDIA - Steel	3.0d	7-Oct-26	9-Oct-26	0.0d
4872	GI-FS-SQI-40	Turn Over to MEPF Contractors - SEQ INDIA - Steel (S6)	0.0d		27-Oct-26	35.0d

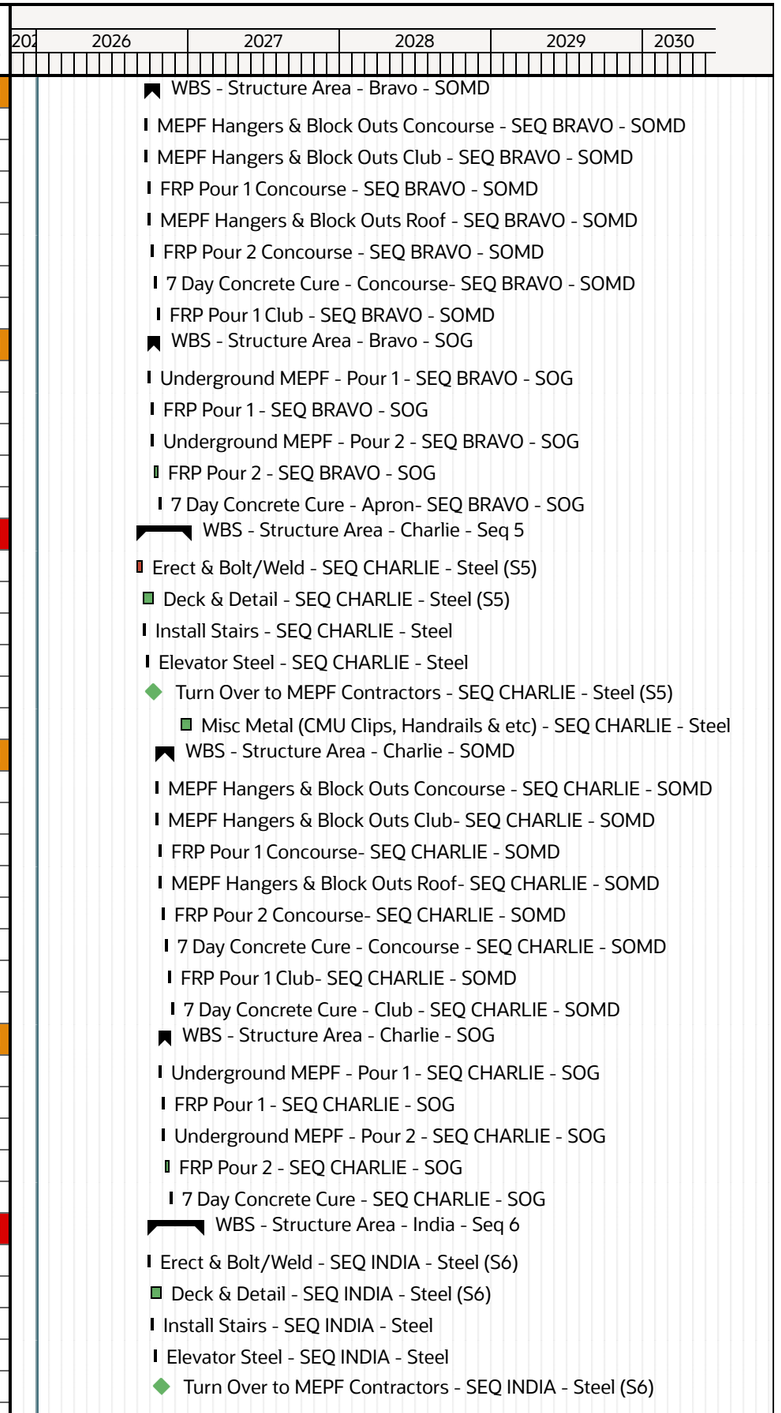


	ID	Name	Dur	Start	Finish	TF
4873	GI-FS-SQI-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ INDIA - Steel	20.0d	11-Jan-27	5-Feb-27	78.0d
4874	WBS - Structure Area - India - SOMD		32.0d	28-Oct-26	14-Dec-26	37.0d
4875	GI-FS-SQI-SOMD-10	MEPF Hangers & Block Outs Club - SEQ INDIA - SOMD	6.0d	28-Oct-26	4-Nov-26	35.0d
4876	GI-FS-SQI-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ INDIA - SOMD	6.0d	28-Oct-26	4-Nov-26	35.0d
4877	GI-FS-SQI-SOMD-30	FRP Pour 1 Concourse - SEQ INDIA - SOMD	6.0d	5-Nov-26	12-Nov-26	35.0d
4878	GI-FS-SQI-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ INDIA - SOMD	6.0d	5-Nov-26	12-Nov-26	35.0d
4879	GI-FS-SQI-SOMD-50	FRP Pour 2 Concourse - SEQ INDIA - SOMD	6.0d	13-Nov-26	20-Nov-26	35.0d
4880	GI-FS-SQI-SOMD-70	7 Day Concrete Cure - Concourse - SEQ INDIA - SOMD	7.0d	21-Nov-26	29-Nov-26	51.0d
4881	GI-FS-SQI-SOMD-60	FRP Pour 1 Club - SEQ INDIA - SOMD	6.0d	30-Nov-26	7-Dec-26	37.0d
4882	GI-FS-SQI-SOMD-80	7 Day Concrete Cure - Club - SEQ INDIA - SOMD	7.0d	8-Dec-26	14-Dec-26	53.0d
4883	WBS - Structure Area - India - SOG		24.0d	5-Nov-26	10-Dec-26	56.0d
4884	GI-FS-SQI-SOG-10	Underground MEPF - Pour 1 - SEQ INDIA - SOG	5.0d	5-Nov-26	11-Nov-26	56.0d
4885	GI-FS-SQI-SOG-30	FRP Pour 1 - SEQ INDIA - SOG	7.0d	12-Nov-26	20-Nov-26	56.0d
4886	GI-FS-SQI-SOG-60	Underground MEPF - Pour 2 - SEQ INDIA - SOG	5.0d	12-Nov-26	18-Nov-26	58.0d
4887	GI-FS-SQI-SOG-40	FRP Pour 2 - SEQ INDIA - SOG	7.0d	23-Nov-26	3-Dec-26	56.0d
4888	GI-FS-SQI-SOG-50	7 Day Concrete Cure - SEQ INDIA - SOG	7.0d	4-Dec-26	10-Dec-26	80.0d
4889	WBS - Structure Area - Delta - Seq 7 & 10		97.0d	22-Sep-26	9-Feb-27	55.0d
4890	GI-FS-SQD-10	Erect & Bolt/Weld Lower Steel - SEQ DELTA - Steel (S7)	8.0d	22-Sep-26	1-Oct-26	16.0d
4891	GI-FS-SQD-70	Erect & Bolt/Weld Upper Steel - SEQ DELTA - Steel (10)	9.0d	2-Oct-26	14-Oct-26	16.0d
4892	GI-FS-SQD-20	Deck & Detail - SEQ DELTA - Steel (S7 & S10)	20.0d	15-Oct-26	11-Nov-26	32.0d
4893	GI-FS-SQD-30	Install Stairs - SEQ DELTA - Steel	5.0d	15-Oct-26	21-Oct-26	16.0d
4894	GI-FS-SQD-50	Elevator Steel - SEQ DELTA - Steel	3.0d	22-Oct-26	26-Oct-26	16.0d
4895	GI-FS-SQD-40	Turn Over to MEPF Contractors - SEQ DELTA - Steel (S7 & S10)	0.0d		11-Nov-26	32.0d
4896	GI-FS-SQD-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ DELTA - Steel	20.0d	13-Jan-27	9-Feb-27	39.0d
4897	WBS - Structure Area - Delta - SOMD		40.0d	12-Nov-26	12-Jan-27	75.0d
4898	GI-FS-SQD-SOMD-10	MEPF & BHS Hangers & Block Outs Concourse - SEQ DELTA - SOMD	6.0d	12-Nov-26	19-Nov-26	32.0d
4899	GI-FS-SQD-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ DELTA - SOMD	6.0d	12-Nov-26	19-Nov-26	109.0d
4900	GI-FS-SQD-SOMD-30	FRP Pour 1 Concourse - SEQ DELTA - SOMD	6.0d	20-Nov-26	1-Dec-26	32.0d
4901	GI-FS-SQD-SOMD-40	FRP Pour 2 Concourse - SEQ DELTA - SOMD	6.0d	2-Dec-26	9-Dec-26	32.0d
4902	GI-FS-SQD-SOMD-70	7 Day Concrete Cure - Concourse - SEQ DELTA - SOMD	7.0d	10-Dec-26	16-Dec-26	46.0d
4903	GI-FS-SQD-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ DELTA - SOMD	6.0d	17-Dec-26	24-Dec-26	32.0d
4904	GI-FS-SQD-SOMD-50	FRP Pour 2 Ster. Corr. - SEQ DELTA - SOMD	6.0d	28-Dec-26	5-Jan-27	32.0d
4905	GI-FS-SQD-SOMD-80	7 Day Concrete Cure - Sterile - SEQ DELTA - SOMD	7.0d	6-Jan-27	12-Jan-27	44.0d
4906	WBS - Structure Area - Delta - SOG		23.0d	20-Nov-26	26-Dec-26	38.0d
4907	GI-FS-SQD-SOG-10	Underground MEPF - Pour 1 - SEQ DELTA - SOG	5.0d	20-Nov-26	30-Nov-26	37.0d
4908	GI-FS-SQD-SOG-30	FRP Pour 1 - SEQ DELTA - SOG	7.0d	1-Dec-26	9-Dec-26	37.0d
4909	GI-FS-SQD-SOG-70	Underground MEPF - Pour 2 - SEQ DELTA - SOG	5.0d	1-Dec-26	7-Dec-26	39.0d
4910	GI-FS-SQD-SOG-60	FRP Pour 2 - SEQ DELTA - SOG	7.0d	10-Dec-26	18-Dec-26	37.0d
4911	GI-FS-SQD-SOMD-90	7 Day Concrete Cure - SEQ DELTA - SOG	7.0d	19-Dec-26	26-Dec-26	53.0d
4912	WBS - Structure Area - Juliett - Seq 8 & 9		101.0d	12-Oct-26	5-Mar-27	78.0d
4913	GI-FS-SQJ-70	Erect & Bolt/Weld Lower Steel - SEQ JULIET - Steel (S8)	8.0d	12-Oct-26	21-Oct-26	0.0d
4914	GI-FS-SQJ-10	Erect & Bolt/Weld Upper Steel - SEQ JULIET - Steel (S9)	7.0d	22-Oct-26	30-Oct-26	0.0d

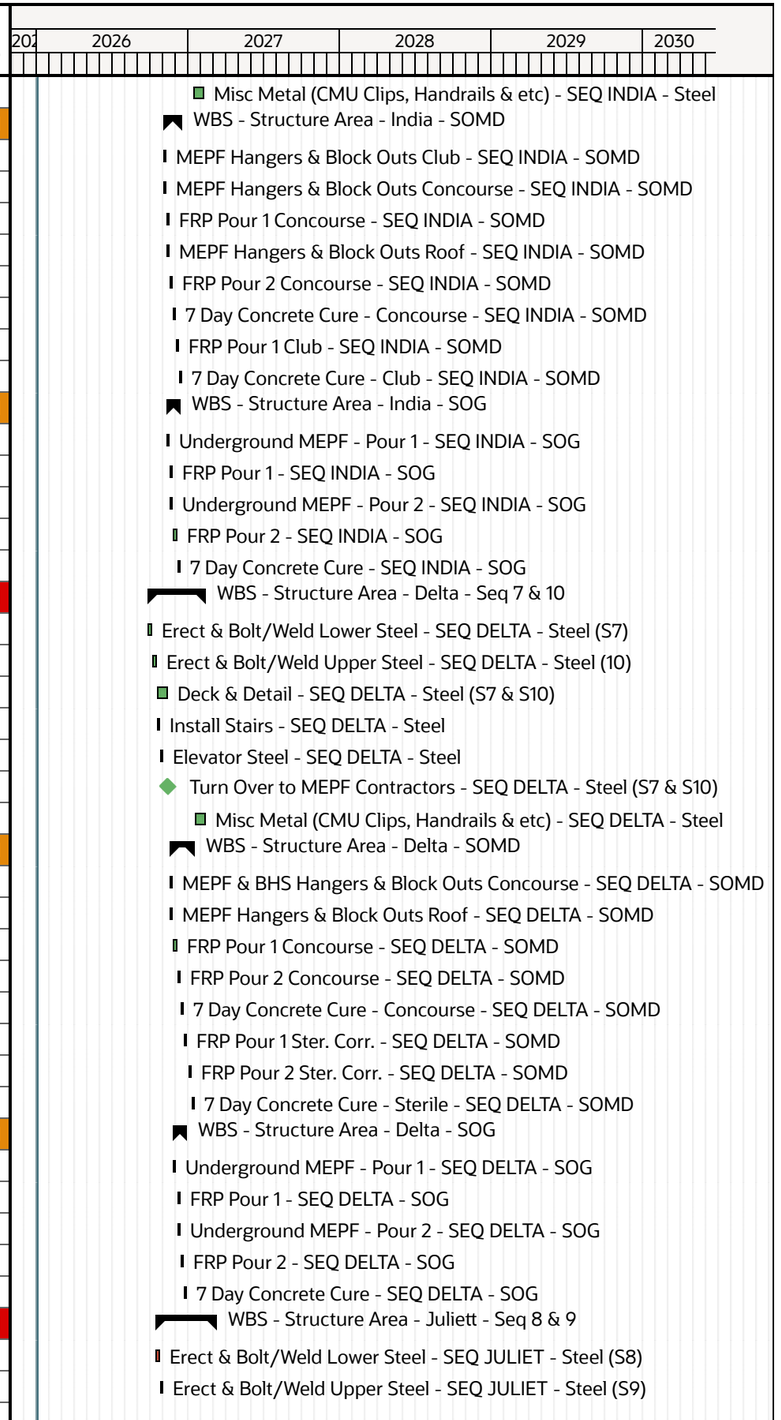


	ID	Name	Dur	Start	Finish	TF
4915	GI-FS-SQJ-20	Deck & Detail - SEQ JULIET - Steel (S8 & S9)	20.0d	2-Nov-26	1-Dec-26	7.0d
4916	GI-FS-SQJ-30	Install Stairs - SEQ JULIET - Steel	5.0d	2-Nov-26	6-Nov-26	0.0d
4917	GI-FS-SQJ-50	Elevator Steel - SEQ JULIET - Steel	3.0d	9-Nov-26	11-Nov-26	0.0d
4918	GI-FS-SQJ-40	Turn Over to MEPF Contractors - SEQ JULIET - Steel (S8 & S9)	0.0d		1-Dec-26	7.0d
4919	GI-FS-SQJ-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ JULIET - Steel	20.0d	8-Feb-27	5-Mar-27	78.0d
4920	WBS - Structure Area - Juliet - SOMD		34.0d	2-Dec-26	20-Jan-27	58.0d
4921	GI-FS-SQJ-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ JULIET - SOMD	6.0d	2-Dec-26	9-Dec-26	7.0d
4922	GI-FS-SQJ-SOMD-10	MEPF Hangers & Block Outs Club - SEQ JULIET - SOMD	6.0d	2-Dec-26	9-Dec-26	7.0d
4923	GI-FS-SQJ-SOMD-30	FRP Pour 1 Concourse - SEQ JULIET - SOMD	6.0d	10-Dec-26	17-Dec-26	7.0d
4924	GI-FS-SQJ-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ JULIET - SOMD	6.0d	10-Dec-26	17-Dec-26	7.0d
4925	GI-FS-SQJ-SOMD-50	FRP Pour 2 Concourse - SEQ JULIET - SOMD	6.0d	18-Dec-26	28-Dec-26	7.0d
4926	GI-FS-SQJ-SOMD-70	7 Day Concrete Cure - Concourse - SEQ JULIET - SOMD	7.0d	29-Dec-26	5-Jan-27	9.0d
4927	GI-FS-SQJ-SOMD-60	FRP Pour 1 Club - SEQ JULIET - SOMD	6.0d	6-Jan-27	13-Jan-27	58.0d
4928	GI-FS-SQJ-SOMD-80	7 Day Concrete Cure - Club - SEQ JULIET - SOMD	7.0d	14-Jan-27	20-Jan-27	82.0d
4929	WBS - Structure Area - Juliet - SOG		31.0d	10-Dec-26	25-Jan-27	39.0d
4930	GI-FS-SQJ-SOG-10	Underground MEPF - Pour 1 - SEQ JULIET - SOG	5.0d	10-Dec-26	16-Dec-26	39.0d
4931	GI-FS-SQJ-SOG-30	FRP Pour 1 - SEQ JULIET - SOG	7.0d	17-Dec-26	28-Dec-26	39.0d
4932	GI-FS-SQJ-SOG-80	Underground MEPF - Pour 2 - SEQ JULIET - SOG	5.0d	17-Dec-26	23-Dec-26	41.0d
4933	GI-FS-SQJ-SOG-90	Underground MEPF - Pour 3 - SEQ JULIET - SOG	5.0d	24-Dec-26	31-Dec-26	43.0d
4934	GI-FS-SQJ-SOG-50	FRP Pour 2 - SEQ JULIET - SOG	7.0d	29-Dec-26	7-Jan-27	39.0d
4935	GI-FS-SQJ-SOG-60	FRP Pour 3 - SEQ JULIET - SOG	7.0d	8-Jan-27	18-Jan-27	39.0d
4936	GI-FS-SQJ-SOG-70	7 Day Concrete Cure - SEQ JULIET - SOG	7.0d	19-Jan-27	25-Jan-27	55.0d
4937	WBS - Structure Area - Echo - Seq 12		92.0d	27-Oct-26	9-Mar-27	39.0d
4938	GI-FS-SQE-10	Erect & Bolt/Weld - SEQ ECHO - Steel (S12)	6.0d	27-Oct-26	3-Nov-26	16.0d
4939	GI-FS-SQE-20	Deck & Detail - SEQ ECHO - Steel (S12)	20.0d	4-Nov-26	3-Dec-26	30.0d
4940	GI-FS-SQE-30	Install Stairs - SEQ ECHO - Steel	5.0d	4-Nov-26	10-Nov-26	16.0d
4941	GI-FS-SQE-50	Elevator Steel - SEQ ECHO - Steel	3.0d	11-Nov-26	13-Nov-26	16.0d
4942	GI-FS-SQE-40	Turn Over to MEPF Contractors - SEQ ECHO - Steel (S12)	0.0d		3-Dec-26	30.0d
4943	GI-FS-SQE-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ ECHO - Steel	20.0d	10-Feb-27	9-Mar-27	39.0d
4944	WBS - Structure Area - Echo - SOMD		17.0d	4-Dec-26	29-Dec-26	68.0d
4945	GI-FS-SQE-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ ECHO - SOMD	6.0d	4-Dec-26	11-Dec-26	32.0d
4946	GI-FS-SQE-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ ECHO - SOMD	6.0d	4-Dec-26	11-Dec-26	30.0d
4947	GI-FS-SQE-SOMD-30	FRP Pour 1 Concourse - SEQ ECHO - SOMD	6.0d	14-Dec-26	21-Dec-26	68.0d
4948	GI-FS-SQE-SOMD-40	7 Day Concrete Cure - SEQ ECHO - SOMD	7.0d	22-Dec-26	29-Dec-26	96.0d
4949	WBS - Structure Area - Echo - SOG		24.0d	14-Dec-26	18-Jan-27	32.0d
4950	GI-FS-SQE-SOG-10	Underground MEPF - Pour 1 - SEQ ECHO - SOG	5.0d	14-Dec-26	18-Dec-26	32.0d
4951	GI-FS-SQE-SOG-30	FRP Pour 1 - SEQ ECHO - SOG	7.0d	21-Dec-26	30-Dec-26	32.0d
4952	GI-FS-SQE-SOG-80	Underground MEPF - Pour 2 - SEQ ECHO - SOG	5.0d	21-Dec-26	28-Dec-26	34.0d
4953	GI-FS-SQE-SOG-60	FRP Pour 2 - SEQ ECHO - SOG	7.0d	31-Dec-26	11-Jan-27	32.0d
4954	GI-FS-SQE-SOG-70	7 Day Concrete Cure - SEQ ECHO - SOG	7.0d	12-Jan-27	18-Jan-27	44.0d
4955	WBS - Structure Area - Kilo - Seq 11 & 13		110.0d	12-Nov-26	20-Apr-27	66.0d
4956	GI-FS-SQK-10	Erect & Bolt/Weld Lower Steel - SEQ KILO - Steel (S11)	14.0d	12-Nov-26	3-Dec-26	0.0d

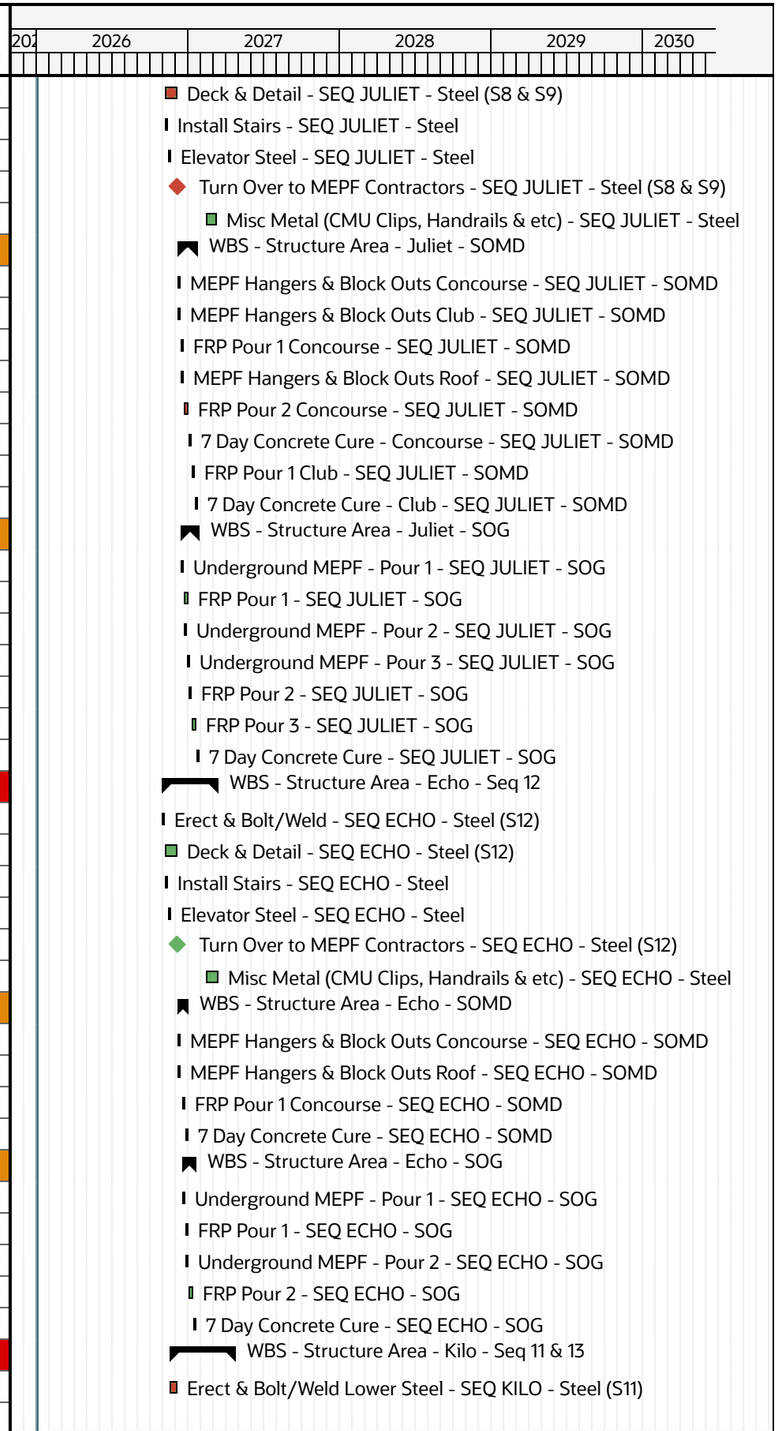


	ID	Name	Dur	Start	Finish	TF
4957	GI-FS-SQK-70	Erect & Bolt/Weld Upper Steel - SEQ KILO - Steel (S13)	8.0d	4-Dec-26	15-Dec-26	0.0d
4958	GI-FS-SQK-20	Deck & Detail - SEQ KILO - Steel (S11 & S13)	20.0d	16-Dec-26	14-Jan-27	0.0d
4959	GI-FS-SQK-50	Elevator Steel - SEQ KILO - Steel	3.0d	16-Dec-26	18-Dec-26	0.0d
4960	GI-FS-SQK-40	Turn Over to MEPF Contractors - SEQ KILO - Steel (S11 & S13)	0.0d		14-Jan-27	0.0d
4961	GI-FS-SQK-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ KILO - Steel	20.0d	24-Mar-27	20-Apr-27	66.0d
4962	WBS - Structure Area - Kilo - SOMD		48.0d	15-Jan-27	23-Mar-27	23.0d
4963	GI-FS-SQK-SOMD-10	MEPF & BHS Hangers & Block Outs Concourse - SEQ KILO - SOMD	6.0d	15-Jan-27	22-Jan-27	0.0d
4964	GI-FS-SQK-SOMD-20	FRP Pour 1 Concourse - SEQ KILO - SOMD	6.0d	25-Jan-27	1-Feb-27	0.0d
4965	GI-FS-SQK-SOMD-30	MEPF Hangers & Block Outs Roof - SEQ KILO - SOMD	6.0d	25-Jan-27	1-Feb-27	44.0d
4966	GI-FS-SQK-SOMD-40	FRP Pour 2 Concourse - SEQ KILO - SOMD	6.0d	2-Feb-27	9-Feb-27	0.0d
4967	GI-FS-SQK-SOMD-50	FRP Pour 3 Concourse - SEQ KILO - SOMD	6.0d	10-Feb-27	17-Feb-27	0.0d
4968	GI-FS-SQK-SOMD-60	FRP Pour 4 Concourse - SEQ KILO - SOMD	6.0d	18-Feb-27	25-Feb-27	0.0d
4969	GI-FS-SQK-SOMD-80	7 Day Concrete Cure - Concourse - SEQ KILO - SOMD	7.0d	26-Feb-27	4-Mar-27	0.0d
4970	GI-FS-SQK-SOMD-70	FRP Pour 1 Club - SEQ KILO - SOMD	6.0d	5-Mar-27	12-Mar-27	23.0d
4971	GI-FS-SQK-SOMD-90	7 Day Concrete Cure - Club - SEQ KILO - SOMD	7.0d	15-Mar-27	23-Mar-27	23.0d
4972	WBS - Structure Area - Kilo - SOG		38.0d	25-Jan-27	17-Mar-27	27.0d
4973	GI-FS-SQK-SOG-10	Underground MEPF - Pour 1 - SEQ KILO - SOG	5.0d	25-Jan-27	29-Jan-27	27.0d
4974	GI-FS-SQK-SOG-30	FRP Pour 1 - SEQ KILO - SOG	7.0d	1-Feb-27	9-Feb-27	27.0d
4975	GI-FS-SQK-SOG-80	Underground MEPF - Pour 2 - SEQ KILO - SOG	5.0d	1-Feb-27	5-Feb-27	29.0d
4976	GI-FS-SQK-SOG-90	Underground MEPF - Pour 3 - SEQ KILO - SOG	5.0d	8-Feb-27	12-Feb-27	31.0d
4977	GI-FS-SQK-SOG-40	FRP Pour 2 - SEQ KILO - SOG	7.0d	10-Feb-27	18-Feb-27	27.0d
4978	GI-FS-SQK-SOG-100	Underground MEPF - Pour 4 - SEQ KILO - SOG	5.0d	15-Feb-27	19-Feb-27	33.0d
4979	GI-FS-SQK-SOG-50	FRP Pour 3 - SEQ KILO - SOG	7.0d	19-Feb-27	1-Mar-27	27.0d
4980	GI-FS-SQK-SOG-60	FRP Pour 4 - SEQ KILO - SOG	7.0d	2-Mar-27	10-Mar-27	27.0d
4981	GI-FS-SQK-SOG-70	7 Day Concrete Cure - SEQ KILO - SOG	7.0d	11-Mar-27	17-Mar-27	39.0d
4982	WBS - Structure Area - Hotel - Seq 19		100.0d	21-Jan-27	10-Jun-27	546.0d
4983	GI-FS-SQH-10	Erect & Bolt/Weld - SEQ HOTEL - Steel (S19)	11.0d	21-Jan-27	4-Feb-27	16.0d
4984	GI-FS-SQH-30	Deck & Detail - SEQ HOTEL - Steel (S19)	20.0d	5-Feb-27	4-Mar-27	16.0d
4985	GI-FS-SQH-20	Install Stairs - SEQ HOTEL - Steel	5.0d	5-Feb-27	11-Feb-27	28.0d
4986	GI-FS-SQH-50	Elevator Steel - SEQ HOTEL - Steel	3.0d	12-Feb-27	16-Feb-27	28.0d
4987	GI-FS-SQH-40	Turn Over to MEPF Contractors - SEQ HOTEL - Steel (S19)	0.0d		4-Mar-27	16.0d
4988	GI-FS-SQH-60	Misc Metal (Handrails & etc) - SEQ HOTEL - Steel	20.0d	13-May-27	10-Jun-27	545.0d
4989	WBS - Structure Area - Hotel - SOMD		40.0d	5-Mar-27	29-Apr-27	25.0d
4990	GI-FS-SQH-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ HOTEL - SOMD	6.0d	5-Mar-27	12-Mar-27	48.0d
4991	GI-FS-SQH-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ HOTEL - SOMD	6.0d	5-Mar-27	12-Mar-27	26.0d
4992	GI-FS-SQH-SOMD-30	FRP Pour 1 Concourse - SEQ HOTEL - SOMD	6.0d	15-Mar-27	22-Mar-27	26.0d
4993	GI-FS-SQH-SOMD-40	FRP Pour 2 Concourse - SEQ HOTEL - SOMD	6.0d	23-Mar-27	30-Mar-27	26.0d
4994	GI-FS-SQH-SOMD-70	7 Day Concrete Cure - Concourse - SEQ HOTEL - SOMD	7.0d	31-Mar-27	6-Apr-27	36.0d
4995	GI-FS-SQH-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ HOTEL - SOMD	6.0d	7-Apr-27	14-Apr-27	26.0d
4996	GI-FS-SQH-SOMD-50	FRP Pour 2 Ster. Corr. - SEQ HOTEL - SOMD	6.0d	15-Apr-27	22-Apr-27	26.0d
4997	GI-FS-SQH-SOMD-80	7 Day Concrete Cure - Sterile - SEQ HOTEL - SOMD	7.0d	23-Apr-27	29-Apr-27	36.0d
4998	WBS - Structure Area - Hotel - SOG		24.0d	15-Mar-27	15-Apr-27	35.0d

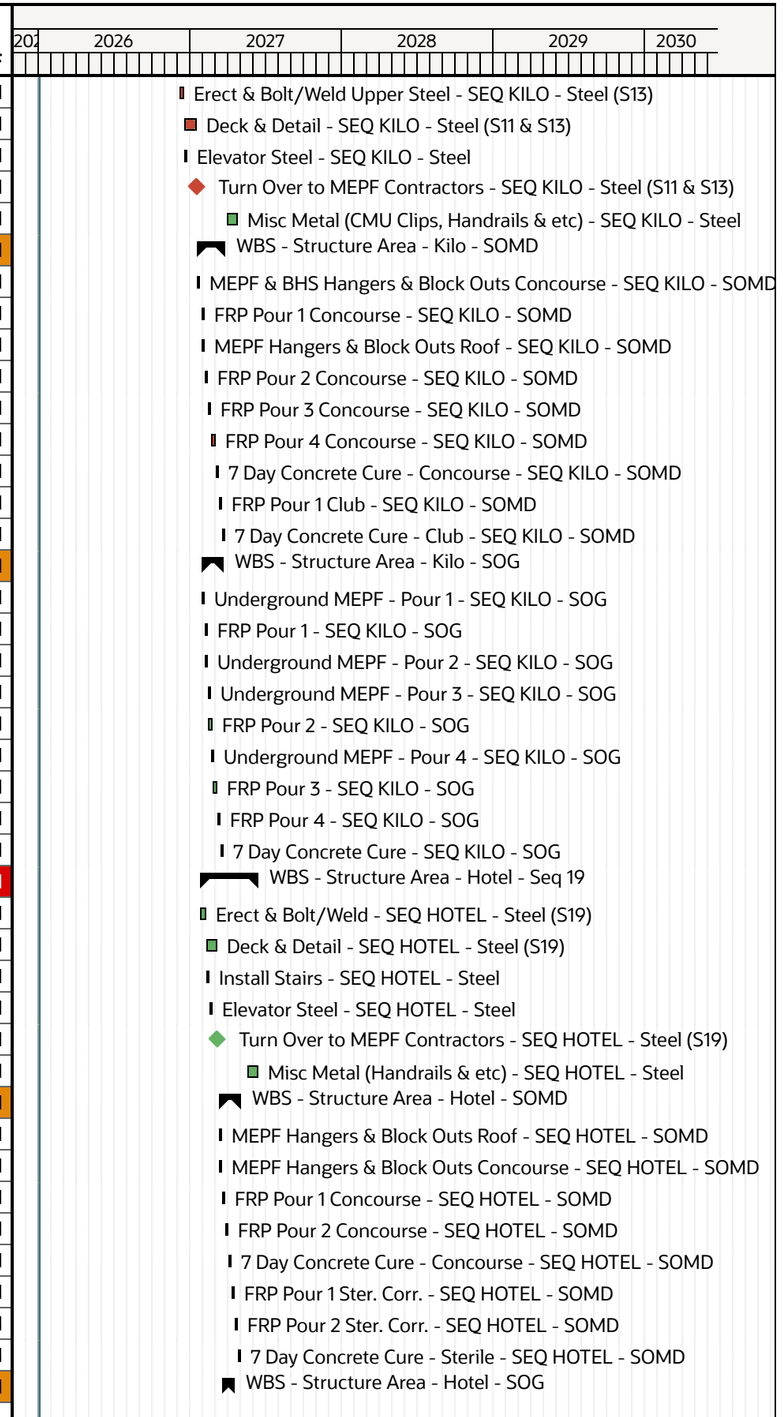


	ID	Name	Dur	Start	Finish	TF
4999	GI-FS-SQH-SOG-10	Underground MEPF - Pour 1 - SEQ HOTEL - SOG	5.0d	15-Mar-27	19-Mar-27	36.0d
5000	GI-FS-SQH-SOG-30	FRP Pour 1 - SEQ HOTEL - SOG	7.0d	22-Mar-27	30-Mar-27	36.0d
5001	GI-FS-SQH-SOG-70	Underground MEPF - Pour 2 - SEQ HOTEL - SOG	5.0d	22-Mar-27	26-Mar-27	38.0d
5002	GI-FS-SQH-SOG-50	FRP Pour 2 - SEQ HOTEL - SOG	7.0d	31-Mar-27	8-Apr-27	36.0d
5003	GI-FS-SQH-SOG-60	7 Day Concrete Cure - SEQ HOTEL - SOG	7.0d	9-Apr-27	15-Apr-27	50.0d
5004	WBS - Structure Area - Foxtrot - Seq 14		104.0d	16-Nov-26	14-Apr-27	33.0d
5005	GI-FS-SQF-10	Erect & Bolt/Weld - SEQ FOXTROT - Steel (S14)	11.0d	16-Nov-26	2-Dec-26	16.0d
5006	GI-FS-SQF-30	Install Stairs - SEQ FOXTROT - Steel	4.0d	3-Dec-26	8-Dec-26	16.0d
5007	GI-FS-SQF-20	Deck & Detail - SEQ FOXTROT - Steel (S14)	20.0d	3-Dec-26	31-Dec-26	35.0d
5008	GI-FS-SQF-50	Elevator Steel - SEQ FOXTROT - Steel	3.0d	9-Dec-26	11-Dec-26	16.0d
5009	GI-FS-SQF-40	Turn Over to MEPF Contractors - SEQ FOXTROT - Steel (S14)	0.0d		31-Dec-26	35.0d
5010	GI-FS-SQF-70	Monumental Stairs - SEQ FOXTROT - Steel	12.0d	15-Feb-27	2-Mar-27	44.0d
5011	GI-FS-SQF-60	Misc Metal (CMU Clips, Handrails & etc) - SEQ FOXTROT - Steel	20.0d	18-Mar-27	14-Apr-27	33.0d
5012	WBS - Structure Area - Foxtrot - SOMD		53.0d	4-Jan-27	17-Mar-27	29.0d
5013	GI-FS-SQF-SOMD-30	MEPF Hangers & Block Outs Concourse - SEQ FOXTROT - SOMD	6.0d	4-Jan-27	11-Jan-27	35.0d
5014	GI-FS-SQF-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ FOXTROT - SOMD	6.0d	4-Jan-27	11-Jan-27	76.0d
5015	GI-FS-SQF-SOMD-40	FRP Pour 1 Concourse - SEQ FOXTROT - SOMD	6.0d	12-Jan-27	19-Jan-27	35.0d
5016	GI-FS-SQF-SOMD-50	FRP Pour 2 Concourse - SEQ FOXTROT - SOMD	6.0d	20-Jan-27	27-Jan-27	35.0d
5017	GI-FS-SQF-SOMD-80	7 Day Concrete Cure - Concourse - SEQ FOXTROT - SOMD	7.0d	28-Jan-27	3-Feb-27	49.0d
5018	GI-FS-SQF-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ FOXTROT - SOMD	6.0d	4-Feb-27	11-Feb-27	35.0d
5019	GI-FS-SQF-SOMD-70	FRP Pour 2 Ster. Corr. - SEQ FOXTROT - SOMD	6.0d	12-Feb-27	19-Feb-27	35.0d
5020	GI-FS-SQF-SOMD-90	7 Day Concrete Cure -Sterile - SEQ FOXTROT - SOMD	7.0d	11-Mar-27	17-Mar-27	32.0d
5021	WBS - Structure Area - Foxtrot - SOG		24.0d	12-Jan-27	12-Feb-27	44.0d
5022	GI-FS-SQF-SOG-10	Underground MEPF - Pour 1 - SEQ FOXTROT - SOG	5.0d	12-Jan-27	18-Jan-27	44.0d
5023	GI-FS-SQF-SOG-30	FRP Pour 1 - SEQ FOXTROT - SOG	7.0d	19-Jan-27	27-Jan-27	44.0d
5024	GI-FS-SQF-SOG-60	Underground MEPF - Pour 2 - SEQ FOXTROT - SOG	5.0d	19-Jan-27	25-Jan-27	46.0d
5025	GI-FS-SQF-SOG-40	FRP Pour 2 - SEQ FOXTROT - SOG	7.0d	28-Jan-27	5-Feb-27	44.0d
5026	GI-FS-SQF-SOG-50	7 Day Concrete Cure - SEQ FOXTROT - SOG	7.0d	6-Feb-27	12-Feb-27	62.0d
5027	WBS - Structure Area - Golf - Seq 16 & 18		106.0d	14-Dec-26	12-May-27	33.0d
5028	GI-FS-SQG-70	Erect & Bolt/Weld Lower Steel - SEQ GOLF - Steel (S16)	9.0d	14-Dec-26	24-Dec-26	16.0d
5029	GI-FS-SQG-10	Erect & Bolt/Weld Upper Steel - SEQ GOLF - Steel (S18)	9.0d	28-Dec-26	8-Jan-27	16.0d
5030	GI-FS-SQG-20	Install Stairs - SEQ GOLF - Steel	5.0d	11-Jan-27	15-Jan-27	16.0d
5031	GI-FS-SQG-30	Deck & Detail - SEQ GOLF - Steel (S16 & S18)	20.0d	11-Jan-27	5-Feb-27	17.0d
5032	GI-FS-SQG-50	Elevator Steel - SEQ GOLF - Steel	3.0d	18-Jan-27	20-Jan-27	16.0d
5033	GI-FS-SQG-40	Turn Over to MEPF Contractors - SEQ GOLF - Steel (S16 & S18)	0.0d		5-Feb-27	17.0d
5034	GI-FS-SQG-60	Misc Metal (Handrails & etc) - SEQ GOLF - Steel	20.0d	15-Apr-27	12-May-27	33.0d
5035	WBS - Structure Area - Golf - SOMD		38.0d	8-Feb-27	31-Mar-27	17.0d
5036	GI-FS-SQG-SOMD-20	MEPF Hangers & Block Outs Concourse - SEQ GOLF - SOMD	6.0d	8-Feb-27	15-Feb-27	17.0d
5037	GI-FS-SQG-SOMD-40	MEPF Hangers & Block Outs Roof - SEQ GOLF - SOMD	6.0d	8-Feb-27	15-Feb-27	23.0d
5038	GI-FS-SQG-SOMD-30	FRP Pour 1 Concourse - SEQ GOLF - SOMD	6.0d	16-Feb-27	23-Feb-27	17.0d
5039	GI-FS-SQG-SOMD-50	FRP Pour 2 Concourse - SEQ GOLF - SOMD	6.0d	24-Feb-27	3-Mar-27	17.0d
5040	GI-FS-SQG-SOMD-80	7 Day Concrete Cure - Concourse - SEQ GOLF - SOMD	7.0d	4-Mar-27	10-Mar-27	25.0d

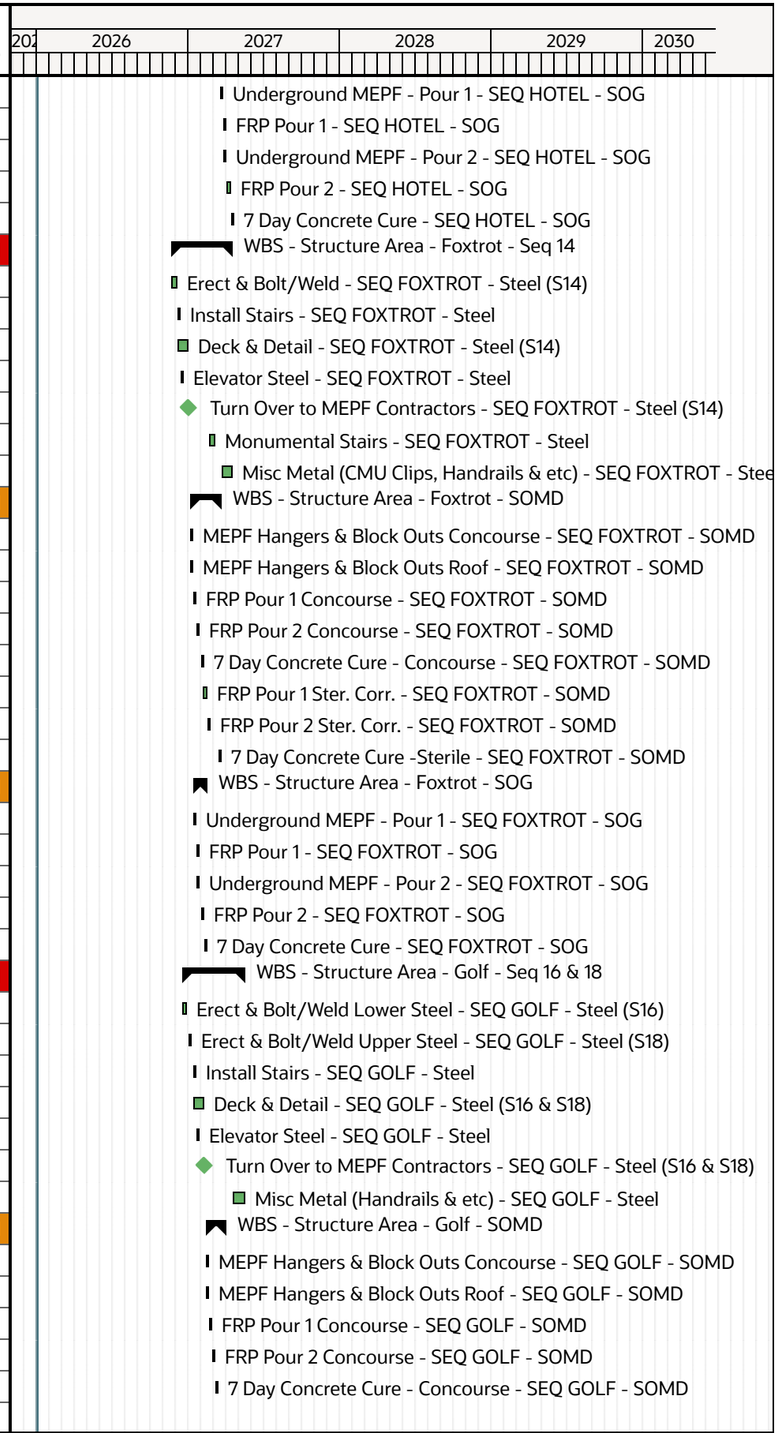

ID	Name	Dur	Start	Finish	TF
5041	GI-FS-SQG-SOMD-60	FRP Pour 1 Ster. Corr. - SEQ GOLF - SOMD	5.0d	11-Mar-27	17-Mar-27	17.0d
5042	GI-FS-SQG-SOMD-70	FRP Pour 2 Ster. Corr. - SEQ GOLF - SOMD	5.0d	18-Mar-27	24-Mar-27	17.0d
5043	GI-FS-SQG-SOMD-90	7 Day Concrete Cure - Sterile - SEQ GOLF - SOMD	7.0d	25-Mar-27	31-Mar-27	25.0d
5044	WBS - Structure Area - Golf - SOG		31.0d	16-Feb-27	30-Mar-27	18.0d
5045	GI-FS-SQG-SOG-10	Underground MEPF - Pour 1 - SEQ GOLF - SOG	5.0d	16-Feb-27	22-Feb-27	18.0d
5046	GI-FS-SQG-SOG-30	FRP Pour 1 - SEQ GOLF - SOG	7.0d	23-Feb-27	3-Mar-27	18.0d
5047	GI-FS-SQG-SOG-80	Underground MEPF - Pour 2 - SEQ GOLF - SOG	5.0d	23-Feb-27	1-Mar-27	20.0d
5048	GI-FS-SQG-SOG-90	Underground MEPF - Pour 3 - SEQ GOLF - SOG	5.0d	2-Mar-27	8-Mar-27	22.0d
5049	GI-FS-SQG-SOG-50	FRP Pour 2 - SEQ GOLF - SOG	7.0d	4-Mar-27	12-Mar-27	18.0d
5050	GI-FS-SQG-SOG-60	FRP Pour 3 - SEQ GOLF - SOG	7.0d	15-Mar-27	23-Mar-27	18.0d
5051	GI-FS-SQG-SOG-70	7 Day Concrete Cure - SEQ GOLF - SOG	7.0d	24-Mar-27	30-Mar-27	26.0d
5052	WBS - Structure Area - Lima - Seq 15		108.0d	16-Dec-26	18-May-27	66.0d
5053	GI-FS-SQL-10	Erect & Bolt/Weld - SEQ LIMA - Steel (S15)	13.0d	16-Dec-26	5-Jan-27	0.0d
5054	GI-FS-SQL-20	Deck & Detail - SEQ LIMA - Steel (S15)	20.0d	6-Jan-27	2-Feb-27	0.0d
5055	GI-FS-SQL-30	Install Stairs - SEQ LIMA - Steel	5.0d	6-Jan-27	12-Jan-27	0.0d
5056	GI-FS-SQL-50	Elevator Steel - SEQ LIMA - Steel	3.0d	13-Jan-27	15-Jan-27	0.0d
5057	GI-FS-SQL-40	Turn Over to MEPF Contractors - SEQ LIMA - Steel (S15)	0.0d		5-Feb-27	0.0d
5058	GI-FS-SQL-60	Misc Metal (Handrails & etc) - SEQ LIMA - Steel	20.0d	21-Apr-27	18-May-27	66.0d
5059	WBS - Structure Area - Lima - SOMD		29.0d	8-Feb-27	18-Mar-27	0.0d
5060	GI-FS-SQL-SOMD-10	MEPF Hangers & Block Outs Concourse - SEQ LIMA - SOMD	6.0d	8-Feb-27	15-Feb-27	0.0d
5061	GI-FS-SQL-SOMD-30	FRP Pour 1 Concourse - SEQ LIMA - SOMD	6.0d	16-Feb-27	23-Feb-27	0.0d
5062	GI-FS-SQL-SOMD-40	FRP Pour 2 Concourse - SEQ LIMA - SOMD	6.0d	24-Feb-27	3-Mar-27	0.0d
5063	GI-FS-SQL-SOMD-50	7 Day Concrete Cure - SEQ LIMA - SOMD	7.0d	4-Mar-27	10-Mar-27	0.0d
5064	GI-FS-SQL-SOMD-20	MEPF Hangers & Block Outs Roof - SEQ LIMA - SOMD	6.0d	11-Mar-27	18-Mar-27	0.0d
5065	WBS - Structure Area - Lima - SOG		24.0d	8-Feb-27	11-Mar-27	31.0d
5066	GI-FS-SQL-SOG-10	Underground MEPF - Pour 1 - SEQ LIMA - SOG	5.0d	8-Feb-27	12-Feb-27	31.0d
5067	GI-FS-SQL-SOG-30	FRP Pour 1 - SEQ LIMA - SOG	7.0d	15-Feb-27	23-Feb-27	31.0d
5068	GI-FS-SQL-SOG-70	Underground MEPF - Pour 2 - SEQ LIMA - SOG	5.0d	15-Feb-27	19-Feb-27	33.0d
5069	GI-FS-SQL-SOG-50	FRP Pour 2 - SEQ LIMA - SOG	7.0d	24-Feb-27	4-Mar-27	31.0d
5070	GI-FS-SQL-SOG-60	7 Day Concrete Cure - SEQ LIMA - SOG	7.0d	5-Mar-27	11-Mar-27	45.0d
5071	WBS - Structure Area - Mike - Seq 17		107.0d	18-Jan-27	16-Jun-27	66.0d
5072	GI-FS-SQM-70	Erect & Bolt/Weld - SEQ MIKE - Steel (S17)	6.0d	18-Jan-27	25-Jan-27	0.0d
5073	GI-FS-SQM-80	Deck & Detail - SEQ MIKE - Steel (S17)	20.0d	26-Jan-27	22-Feb-27	0.0d
5074	GI-FS-SQM-90	Install Stairs - SEQ MIKE - Steel	5.0d	26-Jan-27	1-Feb-27	12.0d
5075	GI-FS-SQM-110	Elevator Steel - SEQ MIKE - Steel	3.0d	2-Feb-27	4-Feb-27	12.0d
5076	GI-FS-SQM-100	Turn Over to MEPF Contractors - SEQ MIKE - Steel (S17)	0.0d		22-Feb-27	0.0d
5077	GI-FS-SQM-120	Misc Metal (CMU Clips, Handrails & etc) - SEQ MIKE - Steel	20.0d	19-May-27	16-Jun-27	66.0d
5078	WBS - Structure Area - Mike -SOMD		29.0d	23-Feb-27	2-Apr-27	44.0d
5079	GI-FS-SQM-SOMD-50	MEPF Hangers & Block Outs Concourse - SEQ MIKE - SOMD	6.0d	23-Feb-27	2-Mar-27	0.0d
5080	GI-FS-SQM-SOMD-70	FRP Pour 1 Concourse - SEQ MIKE - SOMD	6.0d	3-Mar-27	10-Mar-27	0.0d
5081	GI-FS-SQM-SOMD-80	FRP Pour 2 Concourse - SEQ MIKE - SOMD	6.0d	11-Mar-27	18-Mar-27	0.0d
5082	GI-FS-SQM-SOMD-130	FRP Pour 1 Club - SEQ MIKE - SOMD	6.0d	19-Mar-27	26-Mar-27	49.0d

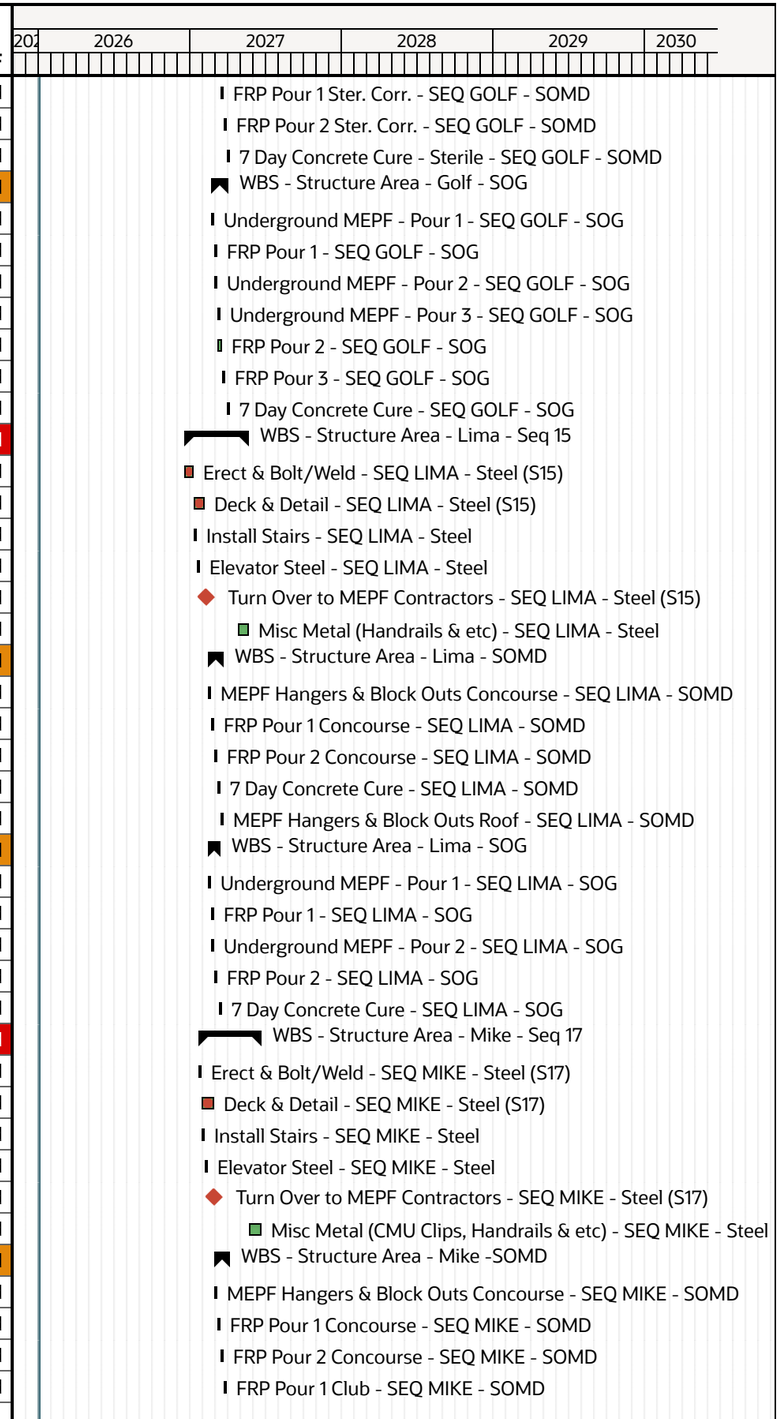


	ID	Name	Dur	Start	Finish	TF
5083	GI-FS-SQM-SOMD-90	7 Day Concrete Cure - SEQ MIKE - SOMD	7.0d	19-Mar-27	25-Mar-27	0.0d
5084	GI-FS-SQM-SOMD-60	MEPF Hangers & Block Outs Roof - SEQ MIKE - SOMD	6.0d	26-Mar-27	2-Apr-27	0.0d
5085	WBS - Structure Area - Mike -SOG		24.0d	3-Mar-27	5-Apr-27	43.0d
5086	GI-FS-SQM-SOG-60	Underground MEPF - Pour 1 - SEQ MIKE - SOG	5.0d	3-Mar-27	9-Mar-27	43.0d
5087	GI-FS-SQM-SOG-80	FRP Pour 1 - SEQ MIKE - SOG	7.0d	10-Mar-27	18-Mar-27	43.0d
5088	GI-FS-SQM-SOG-120	Underground MEPF - Pour 2 - SEQ MIKE - SOG	5.0d	10-Mar-27	16-Mar-27	45.0d
5089	GI-FS-SQM-SOG-100	FRP Pour 2 - SEQ MIKE - SOG	7.0d	19-Mar-27	29-Mar-27	43.0d
5090	GI-FS-SQM-SOG-110	7 Day Concrete Cure - SEQ MIKE - SOG	7.0d	30-Mar-27	5-Apr-27	60.0d
5091	GI-FS-SQM-SOG-130	FRP Pour 3 Mezzanine Deck - SEQ MIKE - SOG	5.0d	30-Mar-27	5-Apr-27	43.0d
5092	WBS - Superstructure		695.0d	22-Jun-26	16-Mar-29	0.0d
5093	WBS - Infrastructure, MEPTFP Rough-in & Equipment		547.0d	8-Sep-26	31-Oct-28	62.0d
5094	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron Level		538.0d	21-Sep-26	31-Oct-28	62.0d
5095	FN-AP8-MDF-2550	Hang, Tape & Finish Drywall - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	6-Dec-27	10-Dec-27	85.0d
5096	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 1		450.0d	21-Sep-26	27-Jun-28	150.0d
5097	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Electrical - Apron 1		450.0d	21-Sep-26	27-Jun-28	150.0d
5098	WBS - Main & Emergency Electrical Rooms - INTR - Apron 1		88.0d	21-Sep-26	26-Jan-27	192.0d
5099	RI-AP1-ER-7570	Layout Walls - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	21-Sep-26	25-Sep-26	232.0d
5100	RI-AP1-ER-260	Install HM Door Frames - Main & Emergency Elec. Rooms - INTR - AP 1	3.0d	19-Oct-26	21-Oct-26	231.0d
5101	RI-AP1-ER-7460	Elec. Rough-in Walls CMU Walls - Main & Emergency Elec. Rooms - INTR - AP 1	15.0d	19-Oct-26	6-Nov-26	217.0d
5102	RI-AP1-ER-7510	Install Block Walls/Masonry Door Frames - Main & Emergency Elec. Rooms - IN...	15.0d	19-Oct-26	6-Nov-26	217.0d
5103	RI-AP1-ER-7480	Elec. Layout for Housekeeping/Equip. Pads - Main & Emergency Elec Rooms - I...	2.0d	9-Nov-26	10-Nov-26	217.0d
5104	RI-AP1-ER-7600	Install CMU Clips at All Walls - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	9-Nov-26	13-Nov-26	224.0d
5105	RI-AP1-ER-7520	FRP Equip. Pads - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	11-Nov-26	17-Nov-26	217.0d
5106	RI-AP1-ER-180	Install Elec. Hangers - Main & Emergency Elec. Rooms - INTR - AP 1	2.0d	16-Nov-26	17-Nov-26	217.0d
5107	RI-AP1-ER-7540	Install Mech. Hangers - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	18-Nov-26	24-Nov-26	217.0d
5108	RI-AP1-ER-200	Install Fire Sprinkler Hangers - Main & Emergency Elec. Rooms - INTR - AP 1	2.0d	23-Nov-26	24-Nov-26	217.0d
5109	RI-AP1-ER-210	Install Fireproofing - Main & Emergency Elec. Rooms - INTR - AP 1	3.0d	25-Nov-26	1-Dec-26	217.0d
5110	RI-AP1-ER-7530	Seal Equip. Pads - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	2-Dec-26	8-Dec-26	220.0d
5111	RI-AP1-ER-7550	Install OH Duct/Equip. - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	2-Dec-26	8-Dec-26	217.0d
5112	RI-AP1-ER-7580	Install CHW OH Rough-in - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	2-Dec-26	8-Dec-26	217.0d
5113	RI-AP1-ER-7610	Install CHW/Duct Insulation - Main & Emergency Elec. Rooms - INTR - AP 1	5.0d	15-Jan-27	21-Jan-27	192.0d
5114	RI-AP1-ER-220	Fire Sprinkler Mains & Branch Line Rough-in - Main & Emergency Elec. Rooms ...	3.0d	22-Jan-27	26-Jan-27	192.0d
5115	WBS - Infrastructure, Elect. Rough-in & Equipment - Truck Court Generator		79.0d	17-Aug-27	8-Dec-27	291.0d
5116	TC-GE-RI-AP-130	Install Generator - Infrastructure, Elec. Rough-in & Equip. Truck Court	5.0d	17-Aug-27	23-Aug-27	230.0d
5117	TC-GE-RI-AP-220	Generator Tank Registration & Certification with FDEP - Infrastructure, Elec. Ro...	30.0d	17-Aug-27	28-Sep-27	232.0d
5118	TC-GE-RI-AP-140	Install Elec. Connections to Generator - Infrastructure, Elec. Rough-in & Equip. ...	5.0d	24-Aug-27	30-Aug-27	230.0d
5119	TC-GE-RI-AP-150	Elec. Feeder Wire Measurements & Procurement - Infrastructure, Elec. Rough-i...	12.0d	31-Aug-27	16-Sep-27	230.0d
5120	TC-GE-RI-AP-160	Elec. Pull & Terminate Wire - Infrastructure, Elec. Rough-in & Equip. Truck Court	20.0d	17-Sep-27	14-Oct-27	230.0d
5121	TC-GE-RI-AP-170	APG QC of generator & ATS System (Third Party Elec. Testing) - Infrastructure, ...	5.0d	15-Oct-27	21-Oct-27	230.0d
5122	TC-GE-RI-AP-190	Manufacturers Start-up Checklist Provided/Manufacturer Schedules Technicia...	10.0d	22-Oct-27	4-Nov-27	291.0d
5123	TC-GE-RI-AP-200	Manufacturer Preliminary Install Scope - Infrastructure, Elec. Rough-in & Equip....	10.0d	5-Nov-27	18-Nov-27	291.0d
5124	TC-GE-RI-AP-210	Manufacturer QC Prior to Start-up - Infrastructure, Elec. Rough-in & Equip. Tru...	3.0d	19-Nov-27	23-Nov-27	291.0d

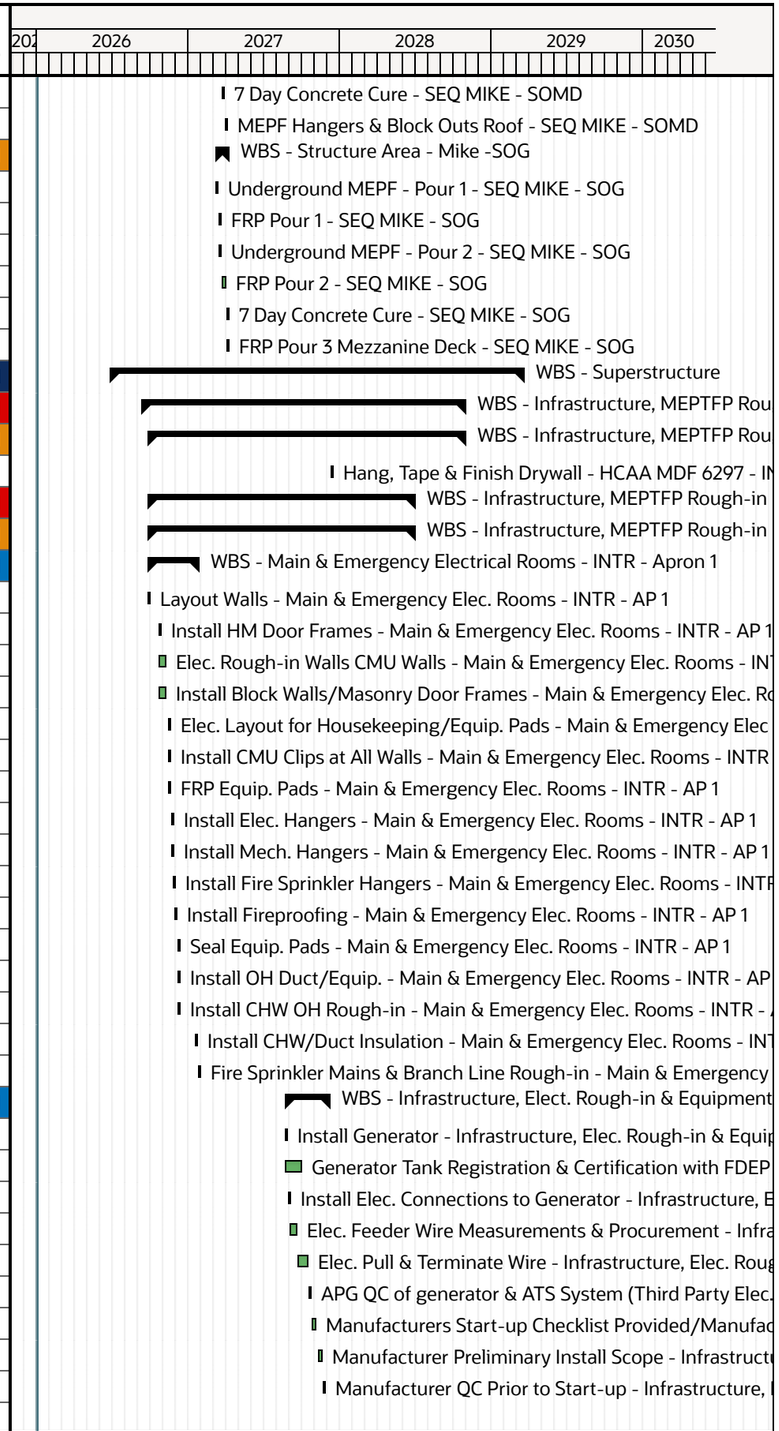


	ID	Name	Dur	Start	Finish	TF
5125	TC-GE-RI-AP-230	City of Tampa Final Inspection - Infrastructure, Elec. Rough-in & Equip. Truck C...	2.0d	24-Nov-27	29-Nov-27	291.0d
5126	TC-GE-RI-AP-240	Fire Marshall Final Inspection - Infrastructure, Elec. Rough-in & Equip. Truck Co...	2.0d	30-Nov-27	1-Dec-27	291.0d
5127	TC-GE-RI-AP-180	Generator Start-up & Load Bank Testing - Infrastructure, Elec. Rough-in & Equi...	5.0d	2-Dec-27	8-Dec-27	291.0d
5128	WBS - Service (#4) & Freight (#3) Elevator Cabs/Shaft - INTR - Apron 1		415.0d	9-Nov-26	27-Jun-28	82.0d
5129	VC-EL-AP1-1723	Install Elev. Safety Rail/Net - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	9-Nov-26	13-Nov-26	397.0d
5130	VC-EL-AP1-1720	Install Temp Sump Pit Cover - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	12-Nov-26	13-Nov-26	397.0d
5131	VC-EL-AP1-1733	Install Scaffold in Hoistway - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	16-Nov-26	20-Nov-26	397.0d
5132	VC-EL-AP1-1743	Rough-in Elec. In Shaft - Service(#4)/Freight Elevator(#3) - INTR - AP 1	8.0d	23-Nov-26	4-Dec-26	397.0d
5133	VC-EL-AP1-1600	Install Elev. Pit LTNG/Outlets - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	7-Dec-26	11-Dec-26	397.0d
5134	VC-EL-AP1-1610	Install Temp Power for Elevator Release - Service(#4)/Freight Elevator(#3) - IN...	5.0d	7-Dec-26	11-Dec-26	402.0d
5135	VC-EL-AP1-1730	Install Fire Sprinkler at Bottom of Freight(#3) - Service(#4)/Freight Elevator(#3...	2.0d	10-Dec-26	11-Dec-26	402.0d
5136	VC-EL-AP1-1710	Remove Scaffold in Hoistway - Service(#4)/Freight(#3) - INTR - AP 1	5.0d	14-Dec-26	18-Dec-26	397.0d
5137	VC-EL-AP1-1620	Install Elev. Rails - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	27-Oct-27	2-Nov-27	180.0d
5138	VC-EL-AP1-2080	Set Elev. Equip. in Shaft - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	3-Nov-27	4-Nov-27	180.0d
5139	VC-EL-AP1-2090	Install Platform & Weights - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	5-Nov-27	11-Nov-27	180.0d
5140	VC-EL-AP1-2100	Install Hoistway & Cabling - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	5-Nov-27	11-Nov-27	180.0d
5141	VC-EL-AP1-2110	Install Elev. Doors - Service(#4)/Freight Elevator(#3) - INTR - AP 1	3.0d	12-Nov-27	16-Nov-27	180.0d
5142	VC-EL-AP1-2120	Install Elev. Equip in Pit - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	12-Nov-27	18-Nov-27	180.0d
5143	VC-EL-AP1-2130	Install Elev. Cab - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	17-Nov-27	23-Nov-27	180.0d
5144	VC-EL-AP1-2140	Connect Elevator Elec. Equip. - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	24-Nov-27	2-Dec-27	180.0d
5145	VC-EL-AP1-1740	Grout Elevator Door Frames - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	3-Dec-27	9-Dec-27	180.0d
5146	VC-EL-AP1-2000	Install Elev. Flooring - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	3-Dec-27	6-Dec-27	183.0d
5147	VC-EL-AP1-2030	Grout Elevator Sills - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	10-Dec-27	16-Dec-27	180.0d
5148	VC-EL-AP1-2070	Set Elev. Fronts & Call Boxes - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	17-Dec-27	23-Dec-27	180.0d
5149	VC-EL-AP1-1750	Remove Elevator Safety Rail/Net - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	27-Dec-27	28-Dec-27	180.0d
5150	VC-EL-AP1-1630	Elec. Run Time for Final Connections - Service(#4)/Freight Elevator(#3) - INTR ...	5.0d	29-Dec-27	5-Jan-28	180.0d
5151	VC-EL-AP1-1650	Install Fire Alarm Trim - Service(#4)/Freight Elevator(#3) - INTR - AP 1	3.0d	6-Jan-28	10-Jan-28	180.0d
5152	VC-EL-AP1-2020	Install Cameras - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	6-Jan-28	12-Jan-28	180.0d
5153	VC-EL-AP1-1770	Install Pit Ladder - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	7-Jan-28	10-Jan-28	180.0d
5154	VC-EL-AP1-1760	Install Sump Pump & Final Grate Cover - Service(#4)/Freight Elevator(#3) - INT...	2.0d	11-Jan-28	12-Jan-28	180.0d
5155	VC-EL-AP1-1660	Adjust/Test Elev. - Service(#4)/Freight Elevator(#3) - INTR - AP 1	10.0d	13-Jan-28	26-Jan-28	180.0d
5156	VC-EL-AP1-1980	Liftnet/Phone Service Configuration - Service(#4)/Freight Elevator(#3) - INTR ...	5.0d	14-Jun-28	20-Jun-28	82.0d
5157	VC-EL-AP1-2060	Prepare Elev. Punchlist - Service(#4)/Freight Elevator(#3) - INTR - AP 1	5.0d	21-Jun-28	27-Jun-28	82.0d
5158	WBS - Service (#4) & Freight (#3) Elevator Machine Room - INTR - Apron 1		370.0d	9-Nov-26	24-Apr-28	195.0d
5159	VC-EL-AP1-1780	Frame North 2 Hr Rated Wall - Service(#4)/Freight Elevator(#3) Machine Room...	2.0d	9-Nov-26	10-Nov-26	344.0d
5160	VC-EL-AP1-1790	Hang Machine Room Side 1st Layer - Service(#4)/Freight Elevator(#3) Machin...	2.0d	27-Aug-27	30-Aug-27	143.0d
5161	VC-EL-AP1-1800	Inspect 1st Layer - Service(#4)/Freight Elevator(#3) Machine Room - INTR - AP 1	2.0d	31-Aug-27	1-Sep-27	143.0d
5162	VC-EL-AP1-1810	Hang Machine Room Side 2nd Layer - Service(#4)/Freight Elevator(#3) Machin...	2.0d	2-Sep-27	3-Sep-27	143.0d
5163	VC-EL-AP1-1820	Tape/Finish 2 Hr Rated Wall - Service(#4)/Freight Elevator(#3) Machine Room ...	5.0d	7-Sep-27	13-Sep-27	143.0d
5164	VC-EL-AP1-1830	Frame 2 Hr Rated Lid with Shaft Liner - Service(#4)/Freight Elevator(#3) Machi...	2.0d	14-Sep-27	15-Sep-27	143.0d
5165	VC-EL-AP1-1840	Insulate Ceiling - Service(#4)/Freight Elevator(#3) Machine Room - INTR - AP 1	2.0d	16-Sep-27	17-Sep-27	143.0d
5166	VC-EL-AP1-1850	Inspect Ceiling Insulation - Service(#4)/Freight Elevator(#3) Machine Room - I...	2.0d	20-Sep-27	21-Sep-27	143.0d




	ID	Name	Dur	Start	Finish	TF
5167	VC-EL-AP1-1880	Hang 1st Layer Ceiling - Service(#4)/Freight Elevator(#3) Machine Room - INT...	2.0d	22-Sep-27	23-Sep-27	143.0d
5168	VC-EL-AP1-1870	Inspect 1st Layer Ceiling - Service(#4)/Freight Elevator(#3) Machine Room - IN...	2.0d	24-Sep-27	27-Sep-27	143.0d
5169	VC-EL-AP1-1860	Hang 2nd Layer Ceiling - Service(#4)/Freight Elevator(#3) Machine Room - IN...	2.0d	28-Sep-27	29-Sep-27	143.0d
5170	VC-EL-AP1-1910	Tape/Finish Ceiling - Service(#4)/Freight Elevator(#3) Machine Room - INTR - ...	5.0d	30-Sep-27	6-Oct-27	143.0d
5171	VC-EL-AP1-1900	1st Coat Paint Machine Room - Service(#4)/Freight Elevator(#3) Machine Roo...	2.0d	7-Oct-27	8-Oct-27	143.0d
5172	VC-EL-AP1-1580	Elec. Wall Rough Elev. Equip. Room - Service(#4)/Freight Elevator(#3) Machine...	3.0d	11-Oct-27	13-Oct-27	152.0d
5173	VC-EL-AP1-1930	Install Door & Hardware - Service (#4)/Freight Elevator (#3) Machine Room - I...	2.0d	11-Oct-27	12-Oct-27	143.0d
5174	VC-EL-AP1-1890	Set Elev. Controllers - Service(#4)/Freight Elevator(#3) Machine Room - INTR - ...	5.0d	13-Oct-27	19-Oct-27	143.0d
5175	VC-EL-AP1-1590	Elec. OH Elev. Equip. Room - Service(#4)/Freight Elevator(#3) Machine Room -...	5.0d	14-Oct-27	20-Oct-27	152.0d
5176	VC-EL-AP1-1920	Install Elev. Pathways/Wire Elev. - Service(#4)/Freight Elevator(#3) Machine Ro...	10.0d	20-Oct-27	2-Nov-27	143.0d
5177	VC-EL-AP1-1950	Apply Final Paint - Service(#4)/Freight Elevator(#3) Machine Room - INTR - AP 1	5.0d	3-Nov-27	9-Nov-27	143.0d
5178	VC-EL-AP1-2040	Install Fire Alarm Trim - Service(#4)/Freight Elevator(#3) Machine Room - INT...	5.0d	10-Nov-27	16-Nov-27	181.0d
5179	VC-EL-AP1-1960	Seal Concrete Floor - Service(#4)/Freight Elevator(#3) Machine Room - INTR - ...	5.0d	10-Nov-27	16-Nov-27	143.0d
5180	VC-EL-AP1-1990	Install Fire Extinguisher & Cabinet - Service(#4)/Freight Elevator(#3) Machine ...	5.0d	10-Nov-27	16-Nov-27	143.0d
5181	VC-EL-AP1-2050	Low Voltage Trim Out - Service(#4)/Freight Elevator(#3) Machine Room - INTR...	5.0d	10-Nov-27	16-Nov-27	181.0d
5182	VC-EL-AP1-1940	Install FCUs-1-6080 - Service(#4)/Freight Elevator(#3) Machine Room - INTR -...	5.0d	17-Nov-27	23-Nov-27	181.0d
5183	VC-EL-AP1-1970	Install Rubber Base - Service(#4)/Freight Elevator(#3) Machine Room - INTR - ...	5.0d	17-Nov-27	23-Nov-27	143.0d
5184	VC-EL-AP1-2150	FCU Start Up - Service(#4)/Freight Elevator(#3) Machine Room - INTR - AP 1	2.0d	21-Apr-28	24-Apr-28	195.0d
5185	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 2		115.0d	22-Oct-26	6-Apr-27	200.0d
5186	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 2 - Overall		115.0d	22-Oct-26	6-Apr-27	200.0d
5187	WBS - Overall Rough-in - INTR - Apron 2		115.0d	22-Oct-26	6-Apr-27	200.0d
5188	RI-AP2-300	Layout Walls/Top Track - Overall Rough-in - INTR - AP 2	5.0d	22-Oct-26	28-Oct-26	1.0d
5189	RI-AP2-5720	Install Block Walls/Masonry Door Frames - INTR - AP 2	15.0d	29-Oct-26	18-Nov-26	1.0d
5190	RI-AP2-5730	Elec. Rough-in Block Walls - Overall Rough-in - INTR - AP 2	15.0d	29-Oct-26	18-Nov-26	16.0d
5191	RI-AP2-5740	Install Plumbing Rough-in Block Walls - Overall Rough-in - INTR - AP 2	3.0d	4-Nov-26	6-Nov-26	52.0d
5192	RI-AP2-320	Install Duct Hangers - Overall Rough-in - INTR - AP 2	2.0d	19-Nov-26	20-Nov-26	36.0d
5193	RI-AP2-310	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 2	2.0d	19-Nov-26	20-Nov-26	36.0d
5194	RI-AP2-325	Install CHW Hangers - Overall Rough-in - INTR - AP 2	2.0d	23-Nov-26	24-Nov-26	36.0d
5195	RI-AP2-330	Install Plumbing Hangers - Overall Rough-in - INTR - AP 2	2.0d	25-Nov-26	30-Nov-26	36.0d
5196	RI-AP2-340	Install Elec. Hangers - Overall Rough-in - INTR - AP 2	2.0d	1-Dec-26	2-Dec-26	36.0d
5197	RI-AP2-350	Install Fireproofing - Overall Rough-in - INTR - AP 2	5.0d	3-Dec-26	9-Dec-26	36.0d
5198	RI-AP2-355	Install Under-Slab on Deck Insulation - INTR - AP 2	5.0d	10-Dec-26	16-Dec-26	36.0d
5199	RI-AP2-360	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 2	10.0d	17-Dec-26	31-Dec-26	36.0d
5200	RI-AP2-5810	Install CHW OH Rough-in - Overall Rough-in - INTR - AP 2	5.0d	17-Dec-26	23-Dec-26	78.0d
5201	RI-AP2-370	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 2	10.0d	4-Jan-27	15-Jan-27	73.0d
5202	RI-AP2-5850	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 2	5.0d	4-Jan-27	8-Jan-27	36.0d
5203	RI-AP2-5860	Install HM Door Frames - Overall Rough-in - INTR - AP 2	5.0d	4-Jan-27	8-Jan-27	41.0d
5204	RI-AP2-5750	Install Plumbing Rough-in Walls - Overall Rough INTR - AP 2	5.0d	11-Jan-27	15-Jan-27	36.0d
5205	RI-AP2-440	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 2	10.0d	18-Jan-27	29-Jan-27	36.0d
5206	RI-AP2-5800	Install Duct Insulation - Overall Rough-in - INTR - AP 2	5.0d	18-Jan-27	22-Jan-27	73.0d
5207	RI-AP2-5820	Install CHW Insulation - Overall Rough-in - INTR - AP 2	5.0d	18-Jan-27	22-Jan-27	73.0d
5208	RI-AP2-5830	Install Plumbing Insulation - Overall Rough-in - INTR - AP 2	5.0d	18-Jan-27	22-Jan-27	73.0d

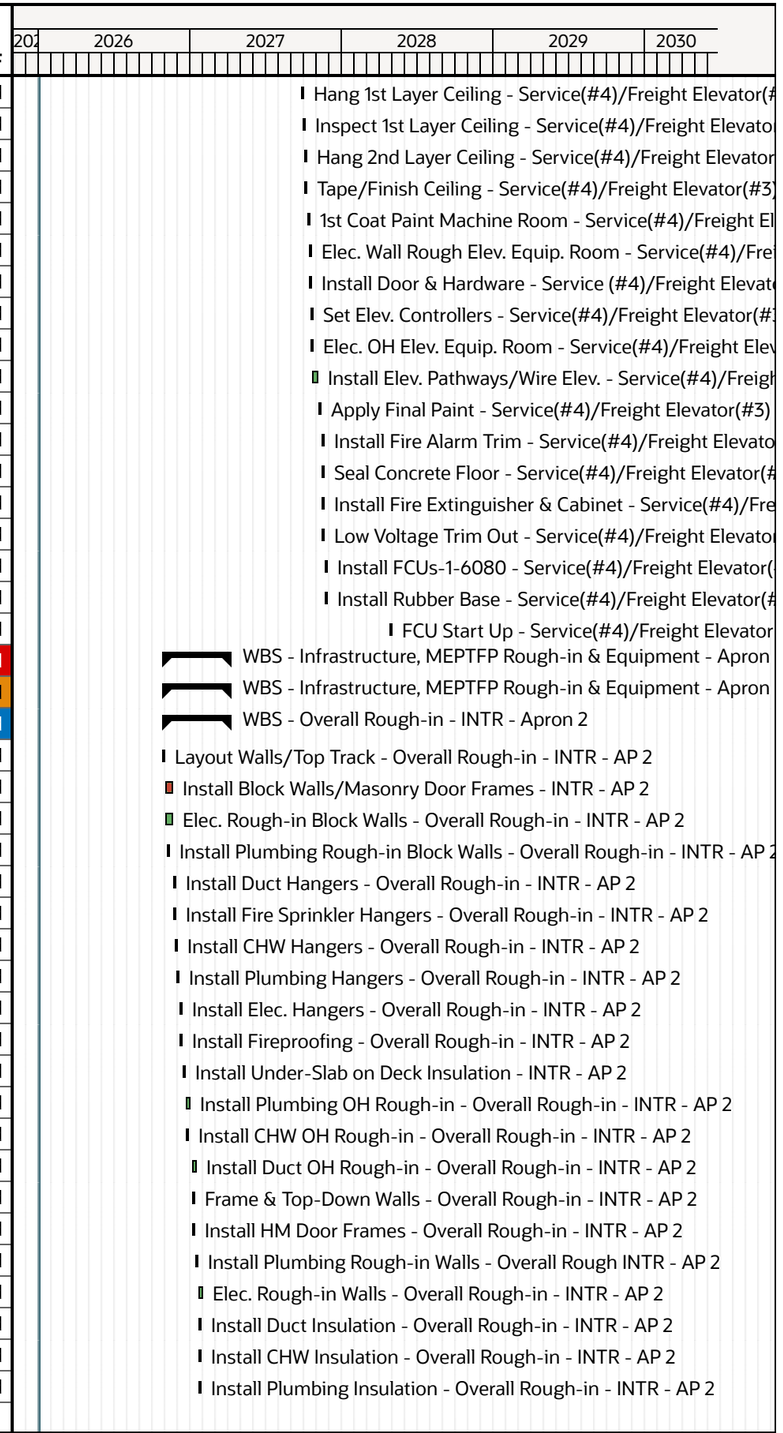


	ID	Name	Dur	Start	Finish	TF
5209	RI-AP2-5840	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 2	15.0d	25-Jan-27	12-Feb-27	73.0d
5210	RI-AP2-430	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 2	6.0d	1-Feb-27	8-Feb-27	36.0d
5211	RI-AP2-390	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 2	10.0d	15-Feb-27	26-Feb-27	78.0d
5212	RI-AP2-5890	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 2	10.0d	15-Feb-27	26-Feb-27	93.0d
5213	RI-AP2-380	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 2	10.0d	1-Mar-27	12-Mar-27	78.0d
5214	RI-AP2-5870	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 2	5.0d	1-Mar-27	5-Mar-27	181.0d
5215	RI-AP2-5900	Pull BAS Cable - Overall Rough-in - INTR - AP 2	10.0d	1-Mar-27	12-Mar-27	217.0d
5216	RI-AP2-5880	Low Volt Pull & Terminate - Overall Rough-in - INTR - AP 2	12.0d	15-Mar-27	30-Mar-27	159.0d
5217	RI-AP2-450	Patch Fireproofing - Overall Rough-in - INTR - AP 2	5.0d	31-Mar-27	6-Apr-27	159.0d
5218	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Support Restrooms - Apron 2		27.0d	15-Jan-27	22-Feb-27	200.0d
5219	RI-AP2-SRR-5880	Insulate 2 Hr Rated Wall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	15-Jan-27	18-Jan-27	200.0d
5220	RI-AP2-SRR-5890	Inspect Insulation - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	19-Jan-27	20-Jan-27	200.0d
5221	RI-AP2-SRR-5910	Hang 1st Layer Drywall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	21-Jan-27	22-Jan-27	200.0d
5222	RI-AP2-SRR-5900	Inspect 1st Layer Drywall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	25-Jan-27	26-Jan-27	200.0d
5223	RI-AP2-SRR-5920	Hang 2nd Layer Drywall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	27-Jan-27	28-Jan-27	200.0d
5224	RI-AP2-SRR-5930	Mud/Tape Drywall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	5.0d	29-Jan-27	4-Feb-27	200.0d
5225	RI-AP2-SRR-5970	Frame Front Partition Wall - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	5-Feb-27	8-Feb-27	200.0d
5226	RI-AP2-SRR-5940	Install Plumbing in Chase - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	9-Feb-27	10-Feb-27	200.0d
5227	RI-AP2-SRR-5950	Install Elec. in Chase - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	11-Feb-27	12-Feb-27	200.0d
5228	RI-AP2-SRR-5960	Install Blocking - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	15-Feb-27	16-Feb-27	200.0d
5229	RI-AP2-SRR-5980	Inspect MEP in chase - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	17-Feb-27	18-Feb-27	200.0d
5230	RI-AP2-SRR-5990	Inspect Wall Framing - Supp. Restrms 6009/6010/6092 - INTR - AP 2	2.0d	19-Feb-27	22-Feb-27	200.0d
5231	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 3		396.0d	2-Oct-26	24-Apr-28	195.0d
5232	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 3		396.0d	2-Oct-26	24-Apr-28	195.0d
5233	WBS - Overall Rough-in - INTR- Apron 3		203.0d	2-Oct-26	21-Jul-27	320.0d
5234	RI-AP3-1230	Layout Walls/Top Track - Overall Rough-in - INTR - AP 3	5.0d	2-Oct-26	8-Oct-26	30.0d
5235	RI-AP3-5760	Install Block Walls/Masonry Door Frames - Overall Rough-in - INTR - AP 3	15.0d	19-Nov-26	11-Dec-26	1.0d
5236	RI-AP3-5770	Elec. Rough-in Block Walls - Overall Rough-in - INTR - AP 3	15.0d	14-Dec-26	5-Jan-27	1.0d
5237	RI-AP3-5820	Install Steel Support for Baggage Deck - Overall Rough-in - INTR - AP 3	5.0d	14-Dec-26	18-Dec-26	464.0d
5238	RI-AP3-5840	Metal Panel System Scan - Overall Rough-in - INTR - AP 3	5.0d	14-Dec-26	18-Dec-26	419.0d
5239	RI-AP3-5830	FRP Baggage Deck - Overall Rough-in - INTR - AP 3	5.0d	21-Dec-26	28-Dec-26	464.0d
5240	RI-AP3-1404	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 3	5.0d	6-Jan-27	12-Jan-27	1.0d
5241	RI-AP3-1240	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 3	2.0d	13-Jan-27	14-Jan-27	1.0d
5242	RI-AP3-1255	Install CHW Hangers - Overall Rough-in - INTR - AP 3	2.0d	15-Jan-27	18-Jan-27	69.0d
5243	RI-AP3-1260	Install Plumbing Hangers - Overall Rough-in - INTR - AP 3	3.0d	19-Jan-27	21-Jan-27	69.0d
5244	RI-AP3-1270	Install Elec. Hangers - Overall Rough-in - INTR - AP 3	2.0d	22-Jan-27	25-Jan-27	69.0d
5245	RI-AP3-1284	Install Fireproofing - Overall Rough-in - INTR - AP 3	10.0d	26-Jan-27	8-Feb-27	69.0d
5246	RI-AP3-1304	Install Expansion Joint - Overall Rough-in - INTR - AP 3	10.0d	9-Feb-27	22-Feb-27	127.0d
5247	RI-AP3-1414	Install CHW OH Rough-in - Overall Rough-in - INTR - AP 3	5.0d	9-Feb-27	15-Feb-27	77.0d
5248	RI-AP3-1424	Install CHW/Duct Insulation - Overall Rough-in INTR - AP 3	10.0d	16-Feb-27	1-Mar-27	122.0d
5249	RI-AP3-1294	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 3	10.0d	26-Feb-27	11-Mar-27	56.0d
5250	RI-AP3-1324	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 3	15.0d	5-Mar-27	25-Mar-27	64.0d

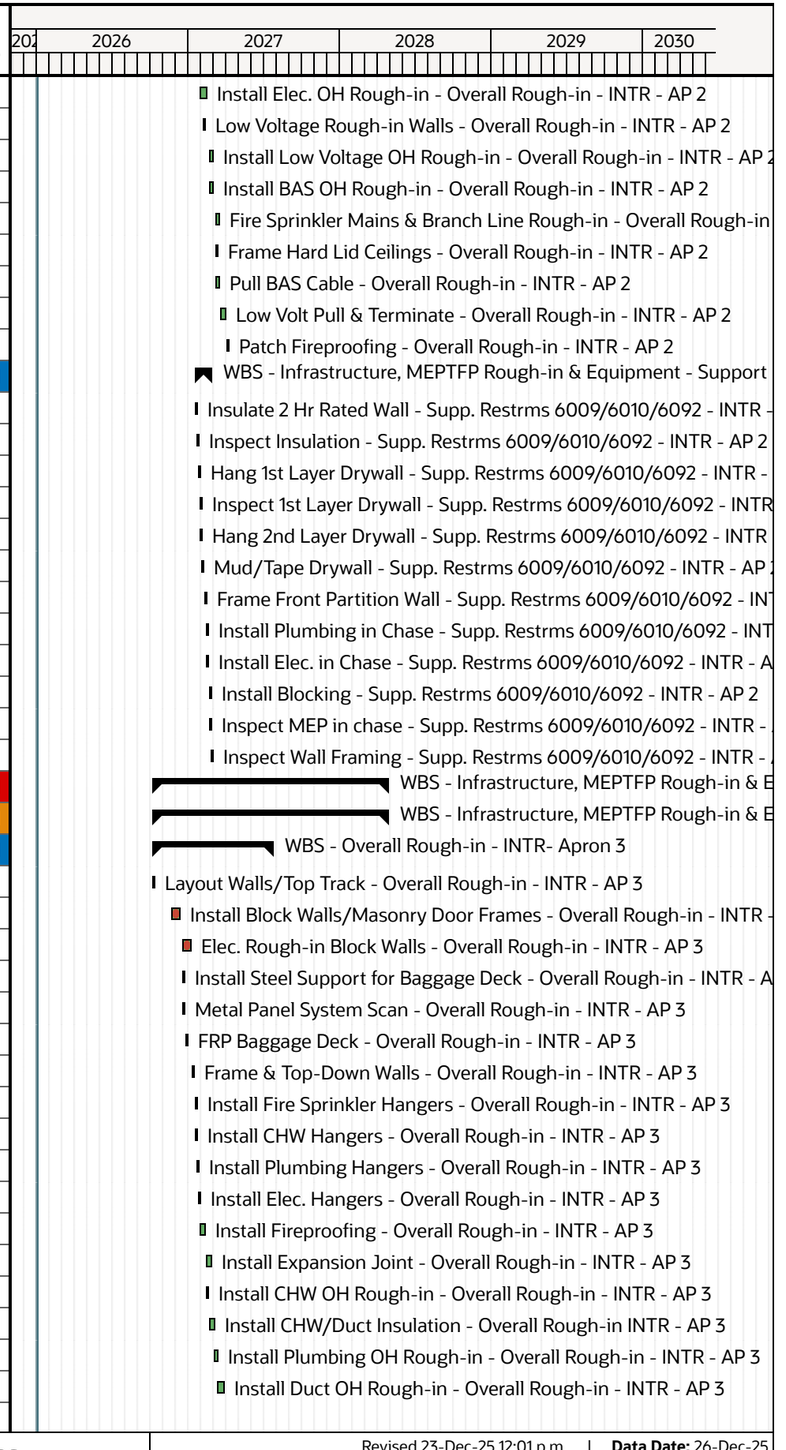


ID	Name	Dur	Start	Finish	TF
5251	RI-AP3-1334	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 3	10.0d	2-Apr-27	15-Apr-27	64.0d
5252	RI-AP3-1344	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 3	20.0d	9-Apr-27	6-May-27	64.0d
5253	RI-AP3-1354	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 3	10.0d	7-May-27	20-May-27	64.0d
5254	RI-AP3-5780	FRP Alstom PDS Elec. Pads - Overall Rough-in - INTR - AP 3	5.0d	7-May-27	13-May-27	69.0d
5255	RI-AP3-5800	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 3	10.0d	21-May-27	4-Jun-27	54.0d
5256	RI-AP3-1364	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 3	10.0d	7-Jun-27	18-Jun-27	54.0d
5257	RI-AP3-1374	Install HM Door Frames - Overall Rough-in - INTR - AP 3	3.0d	7-Jun-27	9-Jun-27	78.0d
5258	RI-AP3-5810	Pull BAS Cable - Overall Rough-in - INTR - AP 3	10.0d	7-Jun-27	18-Jun-27	136.0d
5259	RI-AP3-1384	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 3	10.0d	21-Jun-27	2-Jul-27	54.0d
5260	RI-AP3-1394	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 3	2.0d	6-Jul-27	7-Jul-27	54.0d
5261	RI-AP3-5790	Low Volt Pull & Terminate - Overall Rough-in - INTR - AP 3	5.0d	8-Jul-27	14-Jul-27	54.0d
5262	RI-AP3-1450	Patch Fireproofing - Overall Rough-in - INTR - AP 3	5.0d	15-Jul-27	21-Jul-27	54.0d
5263	WBS - Service (#1) & Freight (#2) Elevator Cabs/Shaft - INTR - Apron 3		277.0d	15-Jan-27	16-Feb-28	175.0d
5264	VC-EL-AP3-2160	Install Elev. Safety Rail/Net - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	15-Jan-27	21-Jan-27	348.0d
5265	VC-EL-AP3-2190	Install Temp Sump Pit Cover - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	22-Jan-27	25-Jan-27	348.0d
5266	VC-EL-AP3-2170	Install Scaffold in Hoistway - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	26-Jan-27	1-Feb-27	348.0d
5267	VC-EL-AP3-2180	Rough-in Elec. In Shaft - Service(#1)/Freight Elevator(#2) - INTR - AP 3	8.0d	2-Feb-27	11-Feb-27	348.0d
5268	VC-EL-AP3-2080	Install Elev. Pit LTNG/Outlets - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	12-Feb-27	18-Feb-27	348.0d
5269	VC-EL-AP3-2090	Install Temp Power for Elevator Release - Service(#1)/Freight Elevator(#2) - IN...	5.0d	12-Feb-27	18-Feb-27	353.0d
5270	VC-EL-AP3-2280	Remove Scaffold in Hoistway - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	19-Feb-27	25-Feb-27	348.0d
5271	VC-EL-AP3-2200	Install Fire Sprinkler at Bottom of Freight(#3) - Service(#1)/Freight Elevator(#2...	2.0d	19-Feb-27	22-Feb-27	351.0d
5272	VC-EL-AP3-2100	Install Elev. Rails - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	1-Nov-27	5-Nov-27	175.0d
5273	VC-EL-AP3-2550	Set Elev. Equip in Shaft - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	8-Nov-27	9-Nov-27	175.0d
5274	VC-EL-AP3-2560	Install Platform & Weights - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	10-Nov-27	16-Nov-27	175.0d
5275	VC-EL-AP3-2570	Install Hoistway Elec. Cabling - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	10-Nov-27	16-Nov-27	175.0d
5276	VC-EL-AP3-2590	INstall Elev. Doors - Service(#1)/Freight Elevator(#2) - INTR - AP 3	3.0d	17-Nov-27	19-Nov-27	175.0d
5277	VC-EL-AP3-2580	Install Elev. Equip in Pit - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	17-Nov-27	23-Nov-27	175.0d
5278	VC-EL-AP3-2600	Install Elev. Cab - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	22-Nov-27	30-Nov-27	175.0d
5279	VC-EL-AP3-2610	Connect Elevator Elec. Equip. - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	1-Dec-27	7-Dec-27	175.0d
5280	VC-EL-AP3-2210	Grout Elevator Door Frames - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	8-Dec-27	14-Dec-27	175.0d
5281	VC-EL-AP3-2470	Install Elev. Flooring - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	8-Dec-27	9-Dec-27	178.0d
5282	VC-EL-AP3-2500	Grout Elevator Sills - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	15-Dec-27	21-Dec-27	175.0d
5283	VC-EL-AP3-2540	Set Elev. Fronts & Call Boxes - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	22-Dec-27	29-Dec-27	175.0d
5284	VC-EL-AP3-2220	Remove Elevator Safety Rail/Net - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	30-Dec-27	3-Jan-28	175.0d
5285	VC-EL-AP3-2110	Elec. Run Time for Final Connections - Service(#1)/Freight Elevator(#2) - INTR ...	5.0d	4-Jan-28	10-Jan-28	175.0d
5286	VC-EL-AP3-2120	Install Fire Alarm Trim - Service(#1)/Freight Elevator(#2) - INTR - AP 3	3.0d	11-Jan-28	13-Jan-28	175.0d
5287	VC-EL-AP3-2490	Install Cameras - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	11-Jan-28	17-Jan-28	177.0d
5288	VC-EL-AP3-2240	Install Pit Ladder - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	14-Jan-28	17-Jan-28	175.0d
5289	VC-EL-AP3-2230	Install Sump Pump & Final Grate Cover - Service(#1)/Freight Elevator(#2) - INT...	2.0d	18-Jan-28	19-Jan-28	175.0d
5290	VC-EL-AP3-2130	Adjust/Test Elev. - Service(#1)/Freight Elevator(#2) - INTR - AP 3	10.0d	20-Jan-28	2-Feb-28	175.0d
5291	VC-EL-AP3-2450	Liftnet/Phone Service Configuration - Service(#1)/Freight Elevator(#2) - INTR ...	5.0d	3-Feb-28	9-Feb-28	175.0d
5292	VC-EL-AP3-2530	Prepare Elevator Punchlist - Service(#1)/Freight Elevator(#2) - INTR - AP 3	5.0d	10-Feb-28	16-Feb-28	175.0d

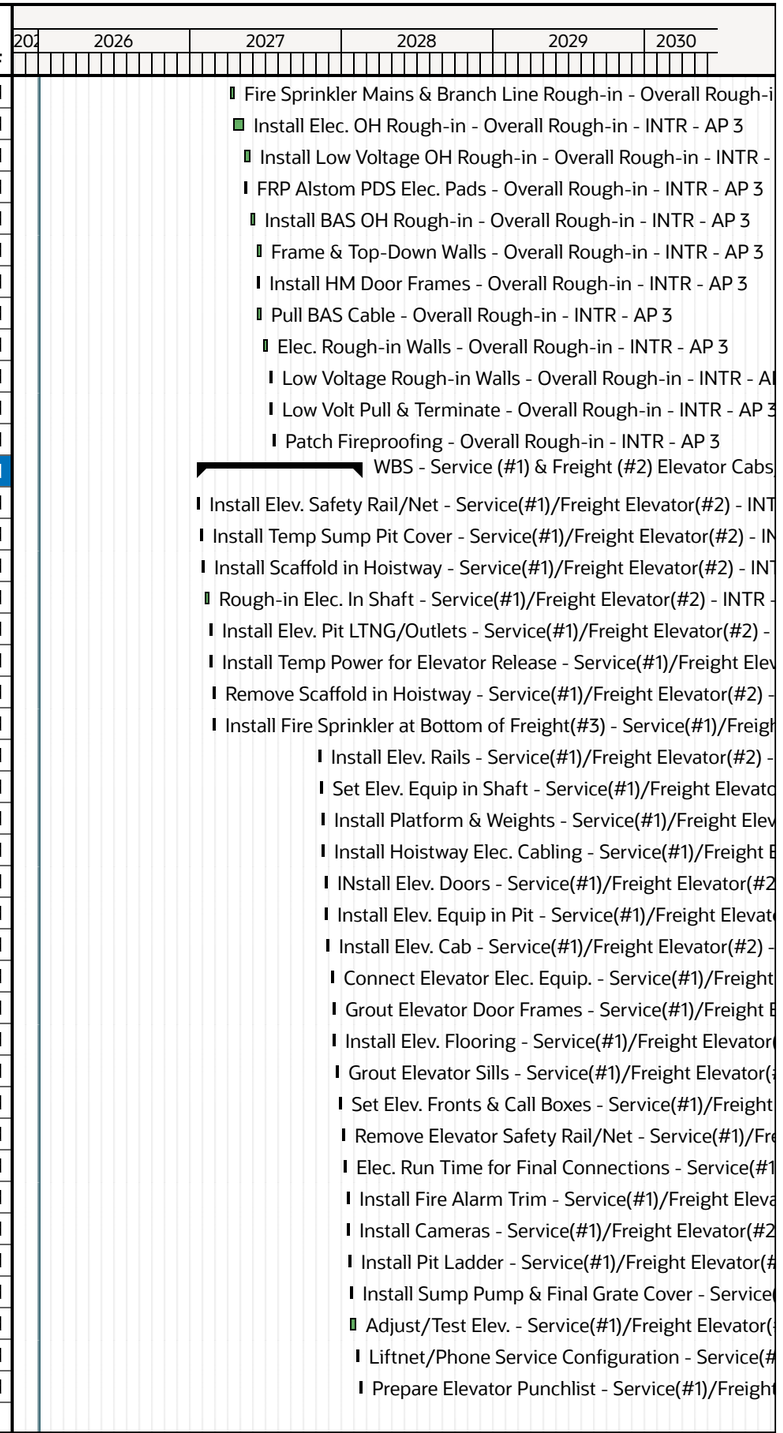


	ID	Name	Dur	Start	Finish	TF
5293	WBS - Service (#1) & Freight (#2) Elevator Machine/Controller Room - INTR - Apron 3		165.0d	31-Aug-27	24-Apr-28	195.0d
5294	VC-EL-AP3-2290	Hang Machine Room Side 1st Layer - Service (#1) & Freight (#2) Elevator Contr...	2.0d	31-Aug-27	1-Sep-27	172.0d
5295	VC-EL-AP3-2193	Inspect 1st Layer - Service (#1) & Freight (#2) Elevator Control Room 6105 - IN...	2.0d	2-Sep-27	3-Sep-27	172.0d
5296	VC-EL-AP3-2183	Hang Machine Room Side 2nd Layer - Service (#1) & Freight (#2) Elevator Cont...	2.0d	7-Sep-27	8-Sep-27	172.0d
5297	VC-EL-AP3-2196	Tape/Finish 2 Hr Rated Wall - Service (#1) & Freight (#2) Elevator Control Roo...	5.0d	9-Sep-27	15-Sep-27	172.0d
5298	VC-EL-AP3-2300	Frame 2 Hr Rated Lid with Shaft Liner - Service (#1) & Freight (#2) Elevator Co...	2.0d	16-Sep-27	17-Sep-27	172.0d
5299	VC-EL-AP3-2310	Insulate Ceiling - Service (#1) & Freight (#2) Elevator Control Room 6105 - INT...	2.0d	20-Sep-27	21-Sep-27	172.0d
5300	VC-EL-AP3-2320	Inspect Ceiling Insulation - Service (#1) & Freight (#2) Elevator Control Room 6...	2.0d	22-Sep-27	23-Sep-27	172.0d
5301	VC-EL-AP3-2350	Hang 1st Layer Ceiling - Service (#1) & Freight (#2) Elevator Control Room 610...	2.0d	24-Sep-27	27-Sep-27	172.0d
5302	VC-EL-AP3-2340	Inspect 1st Layer Ceiling - Service (#1) & Freight (#2) Elevator Control Room 6...	2.0d	28-Sep-27	29-Sep-27	172.0d
5303	VC-EL-AP3-2330	Hang 2nd Layer Ceiling - Service (#1) & Freight (#2) Elevator Control Room 61...	2.0d	30-Sep-27	1-Oct-27	172.0d
5304	VC-EL-AP3-2380	Tape/Finish Ceiling - Service (#1) & Freight (#2) Elevator Control Room 6105 - ...	5.0d	4-Oct-27	8-Oct-27	172.0d
5305	VC-EL-AP3-2370	1st Coat Paint Machine Room - Service (#1) & Freight (#2) Elevator Machine/C...	2.0d	11-Oct-27	12-Oct-27	172.0d
5306	VC-EL-AP3-2060	Elec. Wall Rough Elev. Equip. Room - Service (#1) & Freight (#2) Elevator Machi...	3.0d	13-Oct-27	15-Oct-27	172.0d
5307	VC-EL-AP3-2400	Install Door & Hardware - Service (#1) & Freight (#2) Elevator Machine/Control...	2.0d	13-Oct-27	14-Oct-27	173.0d
5308	VC-EL-AP3-2360	Set Elev. Controllers & Equip. - Service (#1) & Freight (#2) Elevator Machine/Co...	5.0d	15-Oct-27	21-Oct-27	173.0d
5309	VC-EL-AP3-2070	Install Elec. OH Elev. Equip. Room - Service (#1) & Freight (#2) Elevator Machin...	5.0d	18-Oct-27	22-Oct-27	172.0d
5310	VC-EL-AP3-2390	Install Elev. Pathways/Wire Elev. - Service (#1) & Freight (#2) Elevator Machine...	10.0d	25-Oct-27	5-Nov-27	172.0d
5311	VC-EL-AP3-2420	Apply Final Paint - Service (#1) & Freight (#2) Elevator Machine/Control Room ...	5.0d	8-Nov-27	12-Nov-27	172.0d
5312	VC-EL-AP3-2460	Install Fire Extinguisher & Cabinet - Service (#1) & Freight (#2) Elevator Machin...	2.0d	15-Nov-27	16-Nov-27	247.0d
5313	VC-EL-AP3-2510	Install Fire Alarm Trim - Service (#1) & Freight (#2) Elevator Machine/Control R...	5.0d	15-Nov-27	19-Nov-27	172.0d
5314	VC-EL-AP3-2430	Seal Concrete Floor - Service (#1) & Freight (#2) Elevator Machine/Control Roo...	5.0d	17-Nov-27	23-Nov-27	247.0d
5315	VC-EL-AP3-2520	Low Voltage Trim Out - Service (#1) & Freight (#2) Elevator Machine/Control R...	5.0d	22-Nov-27	30-Nov-27	172.0d
5316	VC-EL-AP3-2440	Install Rubber Base - Service (#1) & Freight (#2) Elevator Machine/Control Roo...	5.0d	24-Nov-27	2-Dec-27	247.0d
5317	VC-EL-AP3-2410	Install FCUs-1-6090 - Service (#1) & Freight (#2) Elevator Machine/Control Ro...	5.0d	1-Dec-27	7-Dec-27	172.0d
5318	VC-EL-AP3-2620	FCU Start Up - Service (#1) & Freight (#2) Elevator Machine/Control Room - IN...	2.0d	21-Apr-28	24-Apr-28	195.0d
5319	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 4		205.0d	26-Jan-27	11-Nov-27	149.0d
5320	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 4		205.0d	26-Jan-27	11-Nov-27	149.0d
5321	WBS - Overall Rough-in - INTR - Apron 4		205.0d	26-Jan-27	11-Nov-27	149.0d
5322	RI-AP4-1360	Layout Walls/Top Track - Overall Rough-in - INTR - AP 4	5.0d	26-Jan-27	1-Feb-27	76.0d
5323	RI-AP4-5780	Install Block Walls/Masonry Door Frames - Overall Rough-in - INTR - AP 4	15.0d	2-Feb-27	22-Feb-27	80.0d
5324	RI-AP4-5790	Elec. Rough-in Block Walls - Overall Rough-in - INTR - AP 4	15.0d	2-Feb-27	22-Feb-27	90.0d
5325	RI-AP4-1385	Install Mech Hangers - Overall Rough-in - INTR - AP 4	3.0d	2-Feb-27	4-Feb-27	76.0d
5326	RI-AP4-5850	FRP Baggage Housekeeping Pads - Overall Rough-in - INTR - AP 4	10.0d	2-Feb-27	15-Feb-27	324.0d
5327	RI-AP4-5880	Install HM Door Frames - Overall Rough-in - INTR - AP 4	5.0d	2-Feb-27	8-Feb-27	288.0d
5328	RI-AP4-1370	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 4	3.0d	5-Feb-27	9-Feb-27	76.0d
5329	RI-AP4-1390	Install Plumbing Hangers - Overall Rough-in - INTR - AP 4	4.0d	10-Feb-27	15-Feb-27	76.0d
5330	RI-AP4-1400	Install Elec. Hangers - Overall Rough-in - INTR - AP 4	2.0d	16-Feb-27	17-Feb-27	76.0d
5331	RI-AP4-5860	Install Signage Supports - Overall Rough-in - INTR - AP 4	7.0d	18-Feb-27	26-Feb-27	76.0d
5332	RI-AP4-1510	Low Voltage Rough-in Block Walls - Overall Rough-in - INTR - AP 4	3.0d	23-Feb-27	25-Feb-27	275.0d
5333	RI-AP4-1410	Install Fireproofing - Overall Rough-in - INTR - AP 4	10.0d	12-Mar-27	25-Mar-27	67.0d
5334	RI-AP4-5840	Install Under-Slab on Deck Insulation - Overall Rough-in - INTR - AP 4	10.0d	26-Mar-27	8-Apr-27	67.0d

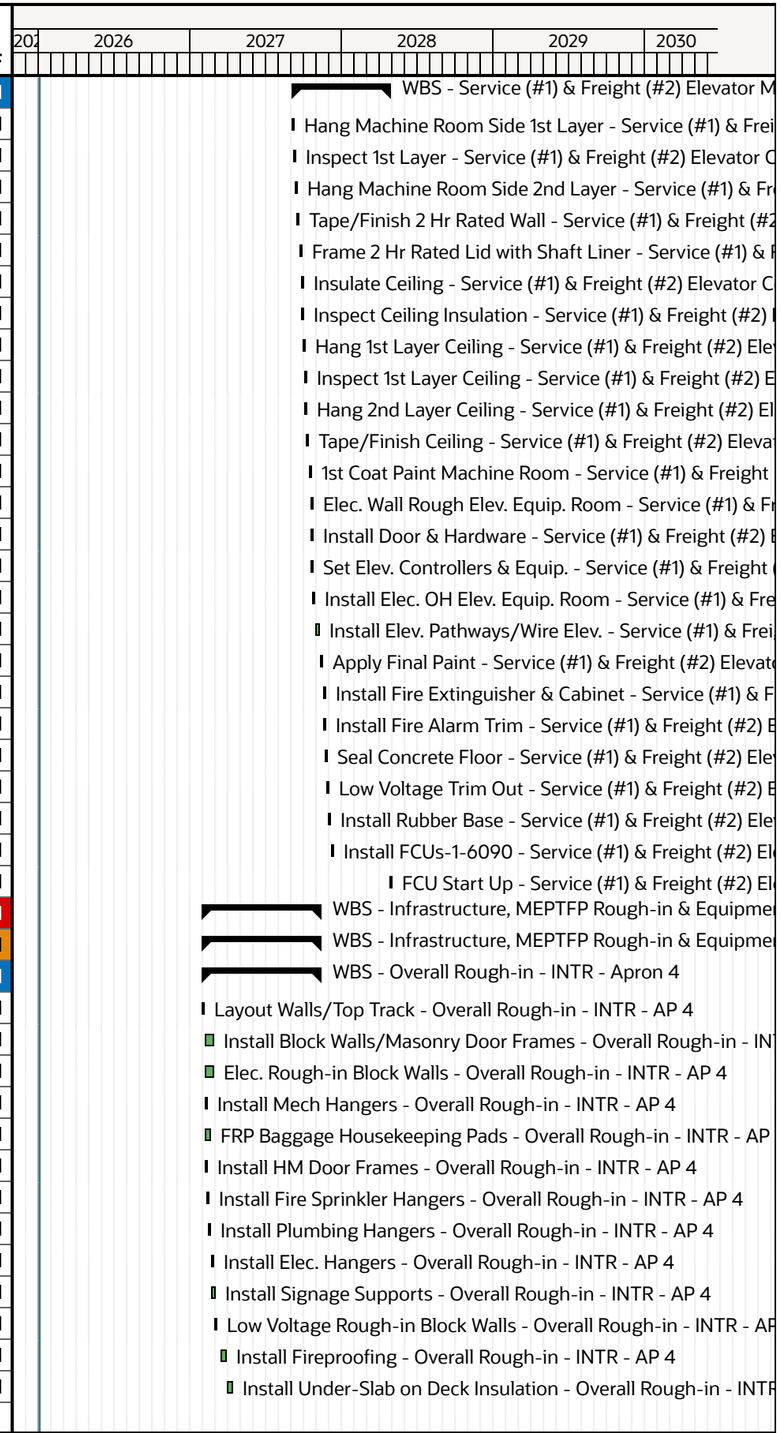


	ID	Name	Dur	Start	Finish	TF
5335	RI-AP4-5910	Install Sheathing/Vapor Barrier (WA22) - Overall Rough-in - INTR - AP 4	6.0d	21-Jun-27	28-Jun-27	190.0d
5336	RI-AP4-5920	Install 7/8" Hat Channel (WA22) - Overall Rough-in - INTR - AP 4	5.0d	29-Jun-27	6-Jul-27	240.0d
5337	RI-AP4-1420	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 4	15.0d	8-Jul-27	28-Jul-27	5.0d
5338	RI-AP4-1430	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 4	10.0d	29-Jul-27	11-Aug-27	5.0d
5339	RI-AP4-5820	Install CHW/Glycol OH Rough-in - Overall Rough-in - INTR - AP 4	5.0d	12-Aug-27	18-Aug-27	5.0d
5340	RI-AP4-1440	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 4	10.0d	19-Aug-27	1-Sep-27	5.0d
5341	RI-AP4-5830	Insulate CHW Insulation - Overall Rough-in INTR - AP 4	5.0d	2-Sep-27	9-Sep-27	138.0d
5342	RI-AP4-5800	Install Duct Insulation - Overall Rough-in - INTR - AP 4	5.0d	2-Sep-27	9-Sep-27	138.0d
5343	RI-AP4-5810	Install Plumbing Insulation - Overall Rough-in - INTR - AP 4	5.0d	2-Sep-27	9-Sep-27	138.0d
5344	RI-AP4-1450	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 4	20.0d	10-Sep-27	7-Oct-27	0.0d
5345	RI-AP4-1460	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 4	10.0d	8-Oct-27	21-Oct-27	98.0d
5346	RI-AP4-5890	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 4	10.0d	8-Oct-27	21-Oct-27	20.0d
5347	RI-AP4-5870	Low Volt Pull & Terminate - Overall Rough-in - INTR - AP 4	10.0d	22-Oct-27	4-Nov-27	98.0d
5348	RI-AP4-5900	Pull BAS Cable - Overall Rough-in - INTR - AP 4	10.0d	22-Oct-27	4-Nov-27	69.0d
5349	RI-AP4-1520	Patch Fireproofing - Overall Rough-in - INTR - AP 4	5.0d	5-Nov-27	11-Nov-27	98.0d
5350	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 5		359.0d	6-Apr-27	31-Aug-28	104.0d
5351	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 5		205.0d	6-Apr-27	26-Jan-28	151.0d
5352	WBS - Overall Rough-in - INTR - Apron 5		205.0d	6-Apr-27	26-Jan-28	151.0d
5353	RI-AP5-200	Layout Walls/Top Track - Overall Rough-in - INTR - AP 5	10.0d	6-Apr-27	19-Apr-27	49.0d
5354	RI-AP5-210	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 5	2.0d	20-Apr-27	21-Apr-27	68.0d
5355	RI-AP5-220	Install Duct Hangers - Overall Rough-in - INTR - AP 5	2.0d	22-Apr-27	23-Apr-27	68.0d
5356	RI-AP5-225	Install CHW Hangers - Overall Rough-in - INTR - AP 5	2.0d	22-Apr-27	23-Apr-27	68.0d
5357	RI-AP5-230	Install Plumbing Hangers - Overall Rough-in - INTR - AP 5	2.0d	26-Apr-27	27-Apr-27	68.0d
5358	RI-AP5-240	Install Elec. Hangers - Overall Rough-in - INTR - AP 5	2.0d	28-Apr-27	29-Apr-27	68.0d
5359	RI-AP5-4720	Install Signage Supports- Overall Rough-in - INTR - AP 5	3.0d	30-Apr-27	4-May-27	68.0d
5360	RI-AP5-250	Install Fireproofing - Overall Rough-in - INTR - AP 5	10.0d	2-Jun-27	15-Jun-27	49.0d
5361	RI-AP5-4670	Install CHW OH Rough-in - Overall - INTR - AP 5	5.0d	16-Jun-27	22-Jun-27	50.0d
5362	RI-AP5-4680	Insulate CHW Insulation - Overall Rough-in INTR - AP 5	5.0d	23-Jun-27	29-Jun-27	113.0d
5363	RI-AP5-260	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 5	6.0d	29-Jul-27	5-Aug-27	19.0d
5364	RI-AP5-270	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 5	10.0d	6-Aug-27	19-Aug-27	19.0d
5365	RI-AP5-4650	Install Plumbing Insulation - Overall Rough-in - INTR - AP 5	5.0d	6-Aug-27	12-Aug-27	29.0d
5366	RI-AP5-4660	Install Duct Insulation - Overall Rough-in - INTR - AP 5	5.0d	20-Aug-27	26-Aug-27	19.0d
5367	RI-AP5-280	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 5	10.0d	27-Aug-27	10-Sep-27	19.0d
5368	RI-AP5-320	Install HM Door Frames - Overall Rough-in - INTR - AP 5	5.0d	27-Aug-27	2-Sep-27	77.0d
5369	RI-AP5-4690	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 5	15.0d	27-Aug-27	17-Sep-27	52.0d
5370	RI-AP5-4710	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 5	5.0d	20-Sep-27	24-Sep-27	112.0d
5371	RI-AP5-4700	Install Plumbing Rough-in Walls - Overall Rough-in - INTR - AP 5	5.0d	20-Sep-27	24-Sep-27	52.0d
5372	RI-AP5-350	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 5	3.0d	27-Sep-27	29-Sep-27	59.0d
5373	RI-AP5-290	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 5	20.0d	8-Oct-27	4-Nov-27	0.0d
5374	RI-AP5-300	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 5	10.0d	5-Nov-27	18-Nov-27	13.0d
5375	RI-AP5-4760	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 5	10.0d	5-Nov-27	18-Nov-27	10.0d
5376	RI-AP5-310	Elec. Rough-in Walls & Columns - Overall Rough-in - INTR - AP 5	10.0d	19-Nov-27	6-Dec-27	13.0d

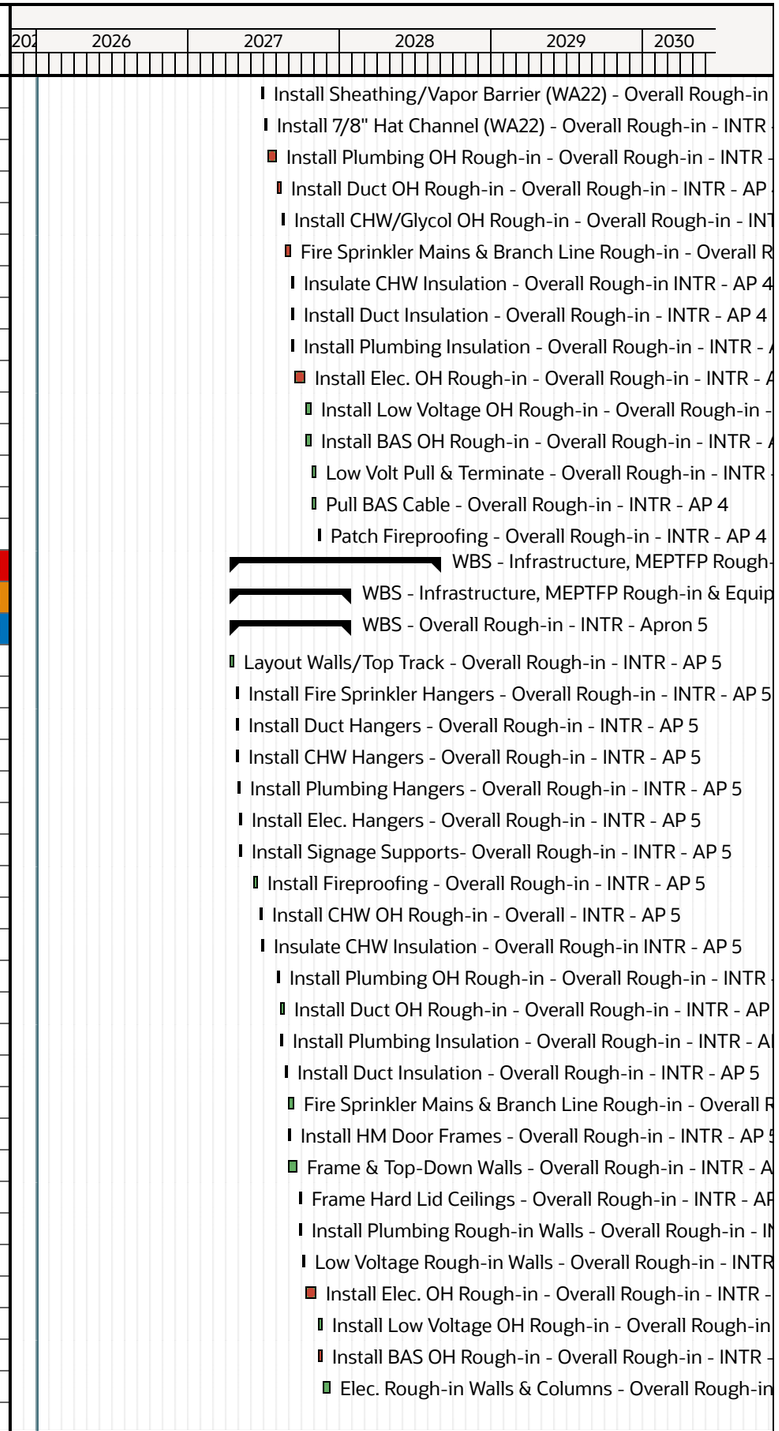

	ID	Name	Dur	Start	Finish	TF
5377	RI-AP5-340	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 5	5.0d	19-Nov-27	29-Nov-27	181.0d
5378	RI-AP5-4770	Pull BAS Cable - Overall Rough-in - INTR - AP 5	10.0d	19-Nov-27	6-Dec-27	59.0d
5379	RI-AP5-330	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 5	3.0d	7-Dec-27	9-Dec-27	63.0d
5380	RI-AP5-4740	Low Volt Pull Cabling - Overall Rough-in - INTR - AP 5	17.0d	10-Dec-27	5-Jan-28	63.0d
5381	RI-AP5-4750	Low Volt Terminate - Overall Rough-in - INTR - AP 5	5.0d	6-Jan-28	12-Jan-28	63.0d
5382	RI-AP5-360	Patch Fireproofing - Overall Rough-in - INTR - AP 5	5.0d	13-Jan-28	19-Jan-28	151.0d
5383	RI-AP5-4730	Install Structural Steel Tubing for Declaration Lanes - Overall Rough-in - INTR - ...	5.0d	20-Jan-28	26-Jan-28	151.0d
5384	WBS - Infrastructure, MEPTFP Rough-in & Equipment - IDF - Apron 5		359.0d	6-Apr-27	31-Aug-28	38.0d
5385	WBS - Tenant IDF 6152 - INTRF - Alias ASD 01181 - Apron 5		359.0d	6-Apr-27	31-Aug-28	38.0d
5386	RI-AP5-IDF-4170	Layout Walls/Top Track - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	6-Apr-27	12-Apr-27	198.0d
5387	RI-AP5-IDF-4180	Install Fire Sprinkler Hangers - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	13-Apr-27	14-Apr-27	198.0d
5388	RI-AP5-IDF-4210	Install Elec. Hangers - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	15-Apr-27	16-Apr-27	198.0d
5389	RI-AP5-IDF-4220	Install Fireproofing - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	26-Apr-27	27-Apr-27	193.0d
5390	RI-AP5-IDF-4240	Install Expansion Joint - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	28-Apr-27	30-Apr-27	283.0d
5391	RI-AP5-IDF-4260	Fire Sprinkler Mains & Branch Line Rough-in - Tenant IDF 6152 - INTRF - Alias ...	4.0d	12-May-27	17-May-27	259.0d
5392	RI-AP5-IDF-4270	Install Elec. OH Rough-in - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	10.0d	18-May-27	1-Jun-27	259.0d
5393	RI-AP5-IDF-4280	Install Low Voltage OH Rough-in - Tenant IDF 6152 - INTRF - Alias ASD 01181 ...	3.0d	2-Jun-27	4-Jun-27	259.0d
5394	RI-AP5-IDF-4290	Frame & Top-Down Walls - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	4.0d	7-Jun-27	10-Jun-27	259.0d
5395	RI-AP5-IDF-4300	Install HM Door Frames - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	7-Jun-27	9-Jun-27	260.0d
5396	RI-AP5-IDF-4310	Elec. Rough-in Walls - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	11-Jun-27	15-Jun-27	259.0d
5397	RI-AP5-IDF-4320	Low Voltage Rough-in Walls - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	4.0d	16-Jun-27	21-Jun-27	259.0d
5398	RI-AP5-IDF-4330	Low Voltage/Elec. in Wall Inspection (COT) - Tenant IDF 6152 - INTRF - Alias A...	2.0d	22-Jun-27	23-Jun-27	259.0d
5399	RI-AP5-IDF-4495	Patch Fireproofing - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	24-Jun-27	30-Jun-27	259.0d
5400	FN-AP5-IDF-4500	Hang, Tape & Finish Drywall - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	2-Feb-28	8-Feb-28	111.0d
5401	FN-AP5-IDF-4510	Prime & First Coat - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	9-Feb-28	10-Feb-28	111.0d
5402	FN-AP5-IDF-4520	Firestopping - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	11-Feb-28	15-Feb-28	111.0d
5403	FN-AP5-IDF-4790	Install FCUs -1-6152 - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	11-Feb-28	17-Feb-28	132.0d
5404	FN-AP5-IDF-4530	Install Tech Room Backerboard - Tenant IDF 6152 - INTRF - Alias ASD 01181 - ...	2.0d	16-Feb-28	17-Feb-28	111.0d
5405	FN-AP5-IDF-4540	Set Racks - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	10.0d	18-Feb-28	2-Mar-28	111.0d
5406	FN-AP5-IDF-4550	Install Ladder Rack - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	3-Mar-28	7-Mar-28	111.0d
5407	FN-AP5-IDF-4560	Pull & Terminate Fiber - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	10.0d	8-Mar-28	21-Mar-28	111.0d
5408	FN-AP5-IDF-4570	Trim-Out Low Voltage - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	22-Mar-28	28-Mar-28	111.0d
5409	FN-AP5-IDF-4580	Apply Final Paint - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	29-Mar-28	4-Apr-28	111.0d
5410	FN-AP5-IDF-4590	Install Door & Hardware - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	5-Apr-28	6-Apr-28	111.0d
5411	FN-AP5-IDF-4600	Install Flooring - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	7-Apr-28	13-Apr-28	111.0d
5412	FN-AP5-IDF-4810	Install Rubber Base - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	5.0d	14-Apr-28	20-Apr-28	111.0d
5413	FN-AP5-IDF-4610	Low Voltage Testing - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	3.0d	21-Apr-28	25-Apr-28	111.0d
5414	FN-AP5-IDF-4830	FCU Start Up - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	2.0d	7-Aug-28	8-Aug-28	38.0d
5415	FN-AP5-IDF-4620	Owner's Acceptance Walkthrough - Tenant IDF 6152 - INTRF - Alias ASD 0118...	2.0d	9-Aug-28	10-Aug-28	38.0d
5416	FN-AP5-IDF-4630	Owner Equip. Install - Tenant IDF 6152 - INTRF - Alias ASD 01181 - AP 5	15.0d	11-Aug-28	31-Aug-28	38.0d
5417	WBS - HCAA IDF 6153 - INTRF - Alias ASD 01180 - Apron 5		359.0d	6-Apr-27	31-Aug-28	38.0d
5418	RI-AP5-IDF-4340	Layout Walls/Top Track - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	6-Apr-27	12-Apr-27	198.0d

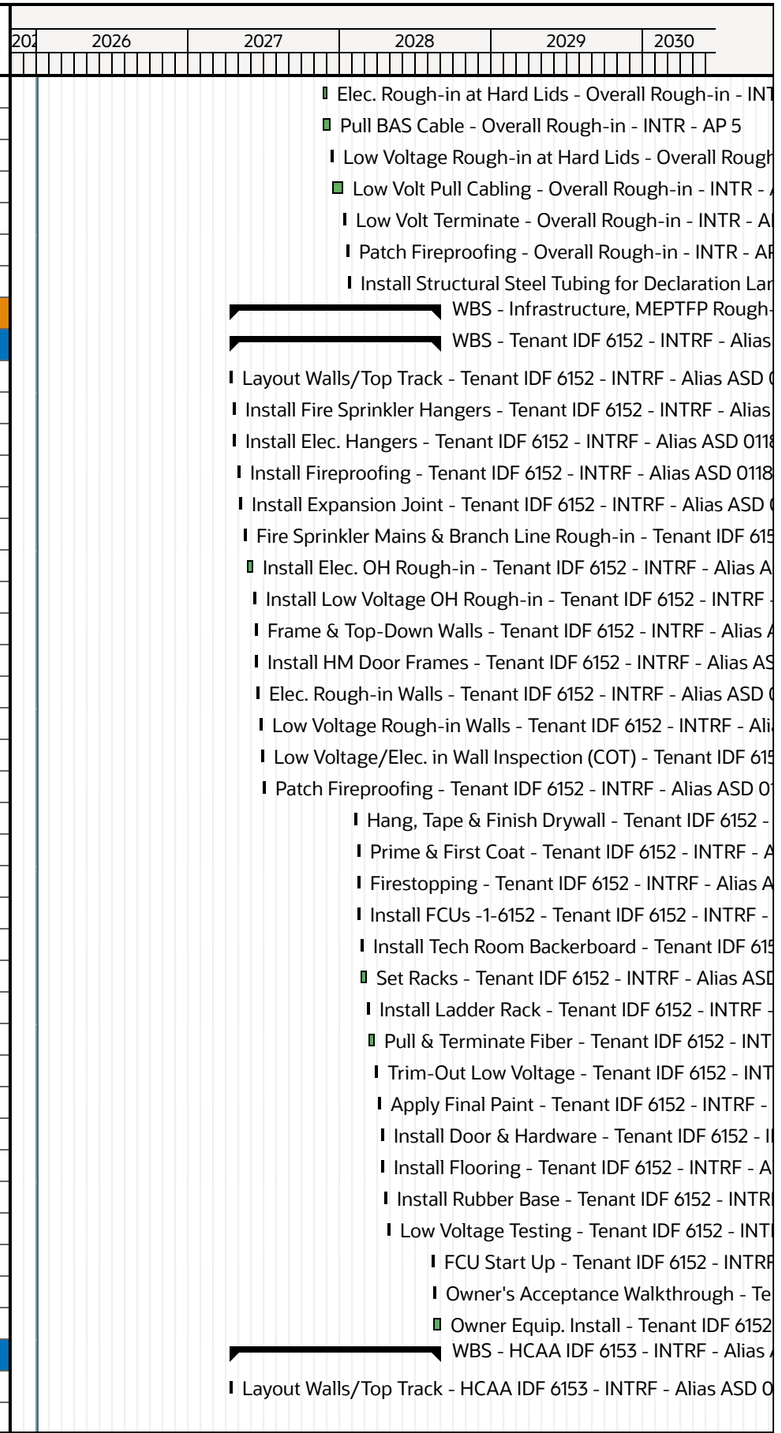


	ID	Name	Dur	Start	Finish	TF
5419	RI-AP5-IDF-4350	Install Fire Sprinkler Hangers - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	13-Apr-27	14-Apr-27	198.0d
5420	RI-AP5-IDF-4380	Install Elec. Hangers - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	15-Apr-27	16-Apr-27	198.0d
5421	RI-AP5-IDF-4390	Install Fireproofing - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	26-Apr-27	27-Apr-27	193.0d
5422	RI-AP5-IDF-4430	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6153 - INTRF - Alias ...	4.0d	28-Apr-27	3-May-27	269.0d
5423	RI-AP5-IDF-4440	Install Elec. OH Rough-in - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	10.0d	5-May-27	18-May-27	268.0d
5424	RI-AP5-IDF-4450	Install Low Voltage OH Rough-in - HCAA IDF 6153 - INTRF - Alias ASD 01180 -...	3.0d	19-May-27	21-May-27	268.0d
5425	RI-AP5-IDF-4460	Frame & Top-Down Walls - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	4.0d	24-May-27	27-May-27	268.0d
5426	RI-AP5-IDF-4470	Install HM Door Frames - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	3.0d	24-May-27	26-May-27	269.0d
5427	RI-AP5-IDF-4480	Elec. Rough-in Walls - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	4.0d	28-May-27	3-Jun-27	268.0d
5428	RI-AP5-IDF-4490	Low Voltage Rough-in Walls - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	3.0d	4-Jun-27	8-Jun-27	268.0d
5429	RI-AP5-IDF-4500	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6153 - INTRF - Alias AS...	2.0d	9-Jun-27	10-Jun-27	268.0d
5430	RI-AP5-IDF-4640	Patch Fireproofing - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	11-Jun-27	17-Jun-27	268.0d
5431	FN-AP5-IDF-4650	Hang, Tape & Finish Drywall - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	2-Feb-28	8-Feb-28	111.0d
5432	FN-AP5-IDF-4660	Prime & First Coat - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	9-Feb-28	10-Feb-28	111.0d
5433	FN-AP5-IDF-4670	Firestopping - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	3.0d	11-Feb-28	15-Feb-28	111.0d
5434	FN-AP5-IDF-4800	Install FCUs -1-6153 - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	11-Feb-28	17-Feb-28	132.0d
5435	FN-AP5-IDF-4680	Install Tech Room Backerboard - HCAA IDF 6153 - INTRF - Alias ASD 01180 - A...	2.0d	16-Feb-28	17-Feb-28	111.0d
5436	FN-AP5-IDF-4690	Set Racks - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	10.0d	18-Feb-28	2-Mar-28	111.0d
5437	FN-AP5-IDF-4700	Install Ladder Rack - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	3.0d	3-Mar-28	7-Mar-28	111.0d
5438	FN-AP5-IDF-4710	Pull & Terminate Fiber - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	10.0d	8-Mar-28	21-Mar-28	111.0d
5439	FN-AP5-IDF-4850	Pull & Terminate Fiber for PBB D61 - HCAA IDF 6153 - INTRF - Alias ASD 0118...	10.0d	8-Mar-28	21-Mar-28	111.0d
5440	FN-AP5-IDF-4720	Trim-Out Low Voltage - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	22-Mar-28	28-Mar-28	111.0d
5441	FN-AP5-IDF-4730	Apply Final Paint - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	29-Mar-28	4-Apr-28	111.0d
5442	FN-AP5-IDF-4740	Install Door & Hardware - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	5-Apr-28	6-Apr-28	111.0d
5443	FN-AP5-IDF-4750	Install Flooring - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	7-Apr-28	13-Apr-28	111.0d
5444	FN-AP5-IDF-4820	Install Rubber Base - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	5.0d	14-Apr-28	20-Apr-28	111.0d
5445	FN-AP5-IDF-4760	Low Voltage Testing - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	3.0d	21-Apr-28	25-Apr-28	111.0d
5446	FN-AP5-IDF-4840	FCU Start Up - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	2.0d	7-Aug-28	8-Aug-28	38.0d
5447	FN-AP5-IDF-4770	Owner's Acceptance Walkthrough - HCAA IDF 6153 - INTRF - Alias ASD 01180 ...	2.0d	9-Aug-28	10-Aug-28	38.0d
5448	FN-AP5-IDF-4780	Owner Equip. Install - HCAA IDF 6153 - INTRF - Alias ASD 01180 - AP 5	15.0d	11-Aug-28	31-Aug-28	38.0d
5449	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mechanical - Apron 5		82.0d	6-Apr-27	30-Jul-27	223.0d
5450	RI-AP5-MR-1170	Layout Walls/Top Track - Mech. Room - INTR - AP 5	5.0d	6-Apr-27	12-Apr-27	225.0d
5451	RI-AP5-MR-1180	Install Fire Sprinkler Hangers - Mech. Room - INTR - AP 5	2.0d	13-Apr-27	14-Apr-27	225.0d
5452	RI-AP5-MR-1210	FRP Equip. Pads - Mech. Room - INTR - AP 5	5.0d	13-Apr-27	19-Apr-27	280.0d
5453	RI-AP5-MR-1200	Install Duct/CHW Hangers - Mech. Room - INTR - AP 5	2.0d	16-Apr-27	19-Apr-27	225.0d
5454	RI-AP5-MR-1230	Set Mech. Equip. - Mech. Room - INTR - AP 5	5.0d	20-Apr-27	26-Apr-27	280.0d
5455	RI-AP5-MR-1240	Install Elec. Hangers - Mech. Room - INTR - AP 5	2.0d	20-Apr-27	21-Apr-27	225.0d
5456	RI-AP5-MR-1250	Install Fireproofing - Mech. Room - INTR - AP 5	2.0d	26-Apr-27	27-Apr-27	223.0d
5457	RI-AP5-MR-1270	Install Duct OH Rough-in - Mech. Room - INTR - AP 5	10.0d	28-Apr-27	11-May-27	223.0d
5458	RI-AP5-MR-1280	Install CHW OH Rough-in - Mech. Room - INTR - AP 5	10.0d	12-May-27	25-May-27	223.0d
5459	RI-AP5-MR-1290	Fire Sprinkler Mains & Branch Line Rough-in - Mech. Room - INTR - AP 5	10.0d	26-May-27	9-Jun-27	223.0d
5460	RI-AP5-MR-1370	Install CHW Insulation - Mech. Room - INTR - AP 5	5.0d	26-May-27	2-Jun-27	254.0d

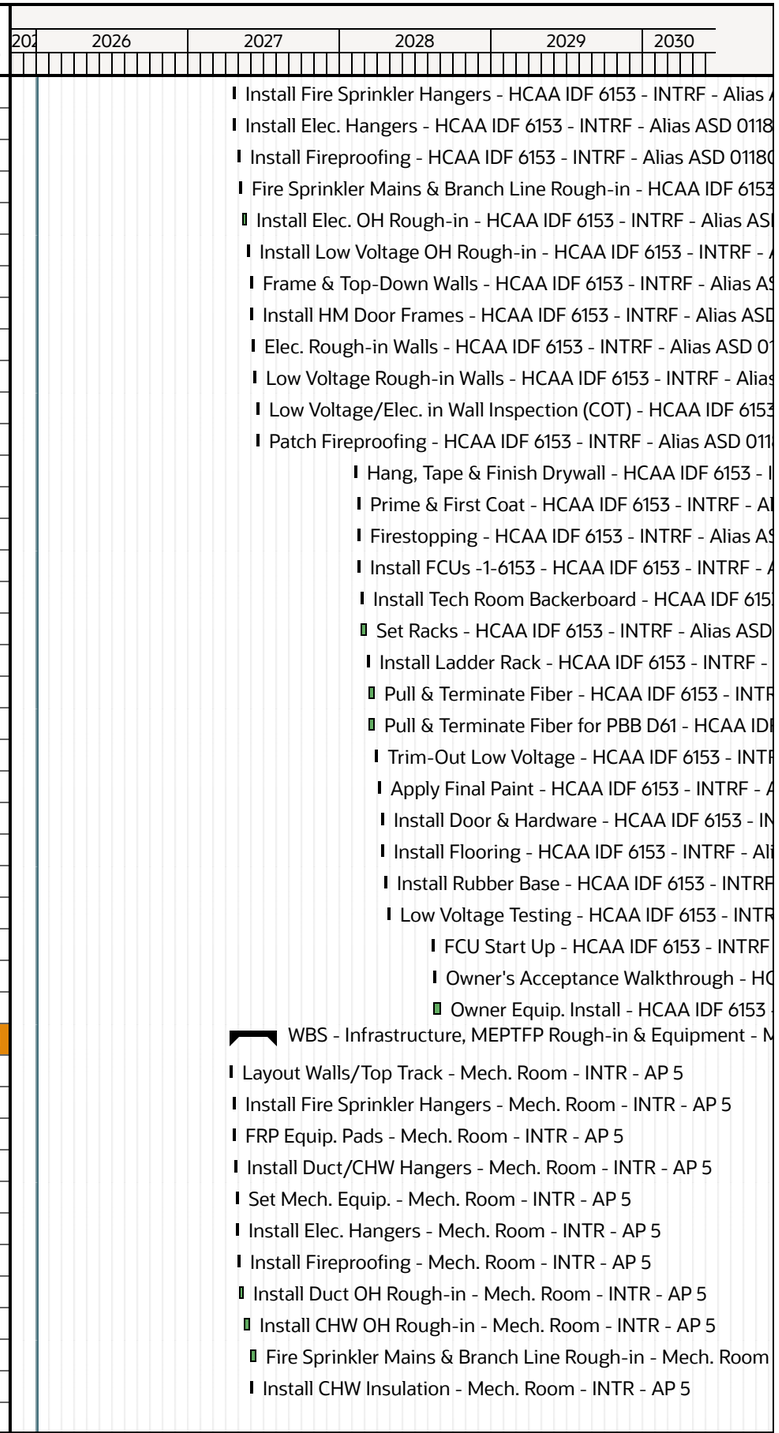

	ID	Name	Dur	Start	Finish	TF
5461	RI-AP5-MR-1380	Install Duct Insulation - Mech. Room - INTR - AP 5	5.0d	26-May-27	2-Jun-27	254.0d
5462	RI-AP5-MR-1300	Install Elec. OH Rough-in - Mech. Room - INTR - AP 5	10.0d	10-Jun-27	23-Jun-27	223.0d
5463	RI-AP5-MR-1310	Low Voltage Rough-in Ceilings - Mech. Room - INTR - AP 5	3.0d	24-Jun-27	28-Jun-27	223.0d
5464	RI-AP5-MR-1320	Frame & Top-Down Walls - Mech. Room - INTR - AP 5	10.0d	29-Jun-27	13-Jul-27	223.0d
5465	RI-AP5-MR-1330	Install HM Door Frames - Mech. Room - INTR - AP 5	3.0d	29-Jun-27	1-Jul-27	230.0d
5466	RI-AP5-MR-1340	Elec. Rough-in Walls - Mech. Room - INTR - AP 5	3.0d	14-Jul-27	16-Jul-27	223.0d
5467	RI-AP5-MR-1350	Low Voltage Rough-in Walls - Mech. Room - INTR - AP 5	3.0d	19-Jul-27	21-Jul-27	225.0d
5468	RI-AP5-MR-1390	Pull & Terminate to Mech. Equip. - Mech. Room. - INTR - AP 5	5.0d	19-Jul-27	23-Jul-27	223.0d
5469	RI-AP5-MR-1400	Patch Fireproofing - Mech. Room - INTR - AP 5	5.0d	26-Jul-27	30-Jul-27	223.0d
5470	WBS - Service (#5) Elevator Cabs/Shaft - INTR - Apron 5		102.0d	12-Jan-28	2-Jun-28	99.0d
5471	VC-EL-AP5-2060	Install Elev. Safety Rail/Net - Service(#5) - INTR - AP 5	5.0d	12-Jan-28	18-Jan-28	99.0d
5472	VC-EL-AP5-2180	Install Scaffold in Hoistway - Service(#5) - INTR - AP 5	5.0d	19-Jan-28	25-Jan-28	99.0d
5473	VC-EL-AP5-2070	Rough-in Elec. In Shaft - Service(#5) - INTR - AP 5	8.0d	26-Jan-28	4-Feb-28	99.0d
5474	VC-EL-AP5-2200	Install Temp Sump Pit Cover - Service(#5) - INTR - AP 5	2.0d	26-Jan-28	27-Jan-28	105.0d
5475	VC-EL-AP5-2080	Install Elev. Pit LTNG/Outlets - Service(#5) - INTR - AP 5	5.0d	7-Feb-28	11-Feb-28	99.0d
5476	VC-EL-AP5-2090	Install Temp Power for Elevator Release - Service(#5) - INTR - AP 5	5.0d	7-Feb-28	11-Feb-28	104.0d
5477	VC-EL-AP5-2190	Remove Scaffold in Hoistway - Service(#5) - INTR - AP 5	5.0d	14-Feb-28	18-Feb-28	99.0d
5478	VC-EL-AP5-2100	Install Elev. Rails - Service(#5) - INTR - AP 5	5.0d	21-Feb-28	25-Feb-28	99.0d
5479	VC-EL-AP5-4290	Set Elev. Equip. in Shaft - Service(#5) - INTR - AP 5	2.0d	28-Feb-28	29-Feb-28	99.0d
5480	VC-EL-AP5-4310	Install Hoistway Elec. Cabling - Service(#5) - INTR - AP 5	5.0d	1-Mar-28	7-Mar-28	99.0d
5481	VC-EL-AP5-4300	Install Platform & Weights - Service(#5) - INTR - AP 5	5.0d	1-Mar-28	7-Mar-28	99.0d
5482	VC-EL-AP5-4320	Install Elev. Equip. in Pit - Service(#5) - INTR - AP 5	5.0d	8-Mar-28	14-Mar-28	99.0d
5483	VC-EL-AP5-4330	Install Elev. Doors - Service(#5) - INTR - AP 5	3.0d	8-Mar-28	10-Mar-28	99.0d
5484	VC-EL-AP5-4340	Install Elev. Cab - Service(#5) - INTR - AP 5	5.0d	13-Mar-28	17-Mar-28	99.0d
5485	VC-EL-AP5-4350	Connect Elev. Equip. - Service(#5) - INTR - AP 5	5.0d	20-Mar-28	24-Mar-28	99.0d
5486	VC-EL-AP5-2220	Grout Elevator Door Frames - Service(#5) - INTR - AP 5	5.0d	27-Mar-28	31-Mar-28	99.0d
5487	VC-EL-AP5-2270	Install Elev. Flooring - Service(#5) - INTR - AP 5	2.0d	27-Mar-28	28-Mar-28	102.0d
5488	VC-EL-AP5-2300	Grout Elevator Sills - Service(#5) - INTR - AP 5	5.0d	3-Apr-28	7-Apr-28	99.0d
5489	VC-EL-AP5-4280	Set Elev. Fronts & Call Boxes - Service(#5) - INTR - AP 5	5.0d	10-Apr-28	14-Apr-28	99.0d
5490	VC-EL-AP5-2230	Remove Elevator Safety Rail/Net - Service(#5) - INTR - AP 5	2.0d	17-Apr-28	18-Apr-28	99.0d
5491	VC-EL-AP5-2110	Elec. Run Time for Final Connections - Service(#5) - INTR - AP 5	5.0d	19-Apr-28	25-Apr-28	99.0d
5492	VC-EL-AP5-2120	Install Fire Alarm Trim - Service(#5) - INTR - AP 5	3.0d	26-Apr-28	28-Apr-28	99.0d
5493	VC-EL-AP5-2290	Install Cameras - Service(#5) - INTR - AP 5	5.0d	26-Apr-28	2-May-28	101.0d
5494	VC-EL-AP5-2250	Install Pit Ladder - Service(#5) - INTR - AP 5	2.0d	1-May-28	2-May-28	99.0d
5495	VC-EL-AP5-2240	Install Sump Pump & Final Grate Cover - Service(#5) - INTR - AP 5	2.0d	3-May-28	4-May-28	99.0d
5496	VC-EL-AP5-2130	Adjust/Test Elev. - Service(#5) - INTR - AP 5	10.0d	5-May-28	18-May-28	99.0d
5497	VC-EL-AP5-2260	Liftnet/Phone Service Configuration - Service(#5) - INTR - AP 5	5.0d	19-May-28	25-May-28	99.0d
5498	VC-EL-AP5-4270	Prepare Elev. Punchlist - Service(#5) - INTR - AP 5	5.0d	26-May-28	2-Jun-28	99.0d
5499	WBS - Escalator (#3 & #4) - INTR - Apron 5		123.0d	30-Apr-27	22-Oct-27	217.0d
5500	VC-ESC-AP5-2280	Set Escalator Trusses - Escalator (#3 & #4) - INTR - AP 5	5.0d	30-Apr-27	6-May-27	0.0d
5501	VC-ESC-AP5-2290	Build out Escalators - Escalator (#3 & #4) - INTR - Apron 5	20.0d	25-Aug-27	22-Sep-27	217.0d
5502	VC-ESC-AP5-2300	Install Escalator Covers - Escalator (#3 & #4) - INTR - Apron 5	5.0d	23-Sep-27	29-Sep-27	217.0d



	ID	Name	Dur	Start	Finish	TF
5503	VC-ESC-AP5-2310	Install Sump Pump & Final Grate Cover - Escalator (#3 & #4) - INTR - Apron 5	2.0d	30-Sep-27	1-Oct-27	217.0d
5504	VC-ESC-AP5-2320	Adjust Esc/Elev. - Service (#5) - Escalator (#3 & #4) - INTR - AP 5	10.0d	4-Oct-27	15-Oct-27	217.0d
5505	VC-ESC-AP5-2330	Liftnet/Phone Service Configuration - Escalator (#3 & #4) - INTR - Apron 5	5.0d	18-Oct-27	22-Oct-27	217.0d
5506	WBS - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - Apron 5		158.0d	12-Jan-28	22-Aug-28	111.0d
5507	VC-EL-AP5-3940	Install Elev. Safety Rail/Net - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR...	5.0d	12-Jan-28	18-Jan-28	99.0d
5508	VC-EL-AP5-4060	Install Scaffold in Hoistway - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR...	5.0d	19-Jan-28	25-Jan-28	99.0d
5509	VC-EL-AP5-3950	Rough-in Elec. In Shaft - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - A...	8.0d	26-Jan-28	4-Feb-28	99.0d
5510	VC-EL-AP5-4080	Install Temp Sump Pit Cover - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INT...	2.0d	26-Jan-28	27-Jan-28	105.0d
5511	VC-EL-AP5-3960	Install Elev. Pit LTNG/Outlets - Passenger (#9, 10, 11) Elevator Cabs/Shaft - IN...	5.0d	7-Feb-28	11-Feb-28	99.0d
5512	VC-EL-AP5-3970	Install Temp Power for Elevator Release - Passenger (#9, 10, 11) Elevator Cabs/...	5.0d	7-Feb-28	11-Feb-28	104.0d
5513	VC-EL-AP5-4070	Remove Scaffold in Hoistway - Passenger (#9, 10, 11) Elevator Cabs/Shaft - IN...	5.0d	14-Feb-28	18-Feb-28	99.0d
5514	VC-EL-AP5-3980	Install Elev. Rails - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	5.0d	21-Feb-28	25-Feb-28	99.0d
5515	VC-EL-AP5-4180	Set Elev. Equip in Shaft - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - A...	2.0d	28-Feb-28	29-Feb-28	99.0d
5516	VC-EL-AP5-4190	Install Platform & Weights - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR ...	5.0d	1-Mar-28	7-Mar-28	99.0d
5517	VC-EL-AP5-4200	Install Hoistway Elec. Cabling - Passenger (#9, 10, 11) Elevator Cabs/Shaft - IN...	5.0d	1-Mar-28	7-Mar-28	99.0d
5518	VC-EL-AP5-4210	Install Elev Equip in Pit - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - A...	5.0d	8-Mar-28	14-Mar-28	99.0d
5519	VC-EL-AP5-4220	Install Elev. Doors - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	3.0d	10-Mar-28	14-Mar-28	99.0d
5520	VC-EL-AP5-4230	Install Elev. Cab - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	5.0d	15-Mar-28	21-Mar-28	99.0d
5521	VC-EL-AP5-4250	Connect Elevator Elec. Equip. - Passenger (#9, 10, 11) Elevator Cabs/Shaft - IN...	5.0d	22-Mar-28	28-Mar-28	99.0d
5522	VC-EL-AP5-4370	Field Measure & Fab. Decorative Glass Panels (GL04) - Passenger (#9, 10, 11) E...	70.0d	22-Mar-28	28-Jun-28	111.0d
5523	VC-EL-AP5-4090	Grout Elevator Door Frames - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INT...	5.0d	29-Mar-28	4-Apr-28	99.0d
5524	VC-EL-AP5-4140	Install Terrazzo Flooring at (TR02) - Passenger (#9, 10, 11) Elevator Cabs/Shaft...	4.0d	29-Mar-28	3-Apr-28	100.0d
5525	VC-EL-AP5-4170	Grout Elevator Sills - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	5.0d	5-Apr-28	11-Apr-28	99.0d
5526	VC-EL-AP5-4240	Set Elev. Fronts & Call Boxes - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INT...	5.0d	12-Apr-28	18-Apr-28	165.0d
5527	VC-EL-AP5-4100	Remove Elevator Safety Rail/Net - Passenger (#9, 10, 11) Elevator Cabs/Shaft ...	2.0d	19-Apr-28	20-Apr-28	165.0d
5528	VC-EL-AP5-3990	Elec. Run Time for Final Connections - Passenger (#9, 10, 11) Elevator Cabs/S...	5.0d	21-Apr-28	27-Apr-28	165.0d
5529	VC-EL-AP5-4160	Install Cameras - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	5.0d	28-Apr-28	4-May-28	167.0d
5530	VC-EL-AP5-4380	Install Decorative Glass Glazing (GL04) - Passenger (#9, 10, 11) Elevator Cabs/...	7.0d	29-Jun-28	10-Jul-28	111.0d
5531	VC-EL-AP5-4390	Install Metal Base - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	3.0d	11-Jul-28	13-Jul-28	112.0d
5532	VC-EL-AP5-4400	Install Architectural Woodwork (WA01) - Passenger (#9, 10, 11) Elevator Cabs/...	4.0d	11-Jul-28	14-Jul-28	111.0d
5533	VC-EL-AP5-4000	Install Fire Alarm Trim - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	3.0d	17-Jul-28	19-Jul-28	111.0d
5534	VC-EL-AP5-4120	Install Pit Ladder - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	2.0d	20-Jul-28	21-Jul-28	111.0d
5535	VC-EL-AP5-4110	Install Sump Pump & Final Grate Cover - Passenger (#9, 10, 11) Elevator Cabs/...	2.0d	24-Jul-28	25-Jul-28	111.0d
5536	VC-EL-AP5-4010	Adjust/Test Elev. - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	10.0d	26-Jul-28	8-Aug-28	111.0d
5537	VC-EL-AP5-4130	Liftnet/Phone Service Configuration - Passenger (#9, 10, 11) Elevator Cabs/Sh...	5.0d	9-Aug-28	15-Aug-28	111.0d
5538	VC-EL-AP5-4260	Prepare Elev. Punchlist - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - A...	5.0d	16-Aug-28	22-Aug-28	111.0d
5539	WBS - Passenger (#9, 10, 11) Elevator Machine/Controller Room - INTR - Apron 5		148.0d	12-Jan-28	8-Aug-28	73.0d
5540	VC-EL-AP5-2560	Hang Machine Room Side 1st Layer - Passenger (#9, 10, 11) Elevator Machine/...	2.0d	12-Jan-28	13-Jan-28	97.0d
5541	VC-EL-AP5-2570	Inspect 1st Layer - Passenger (#9, 10, 11) Elevator Machine/Controller Room - ...	2.0d	14-Jan-28	17-Jan-28	97.0d
5542	VC-EL-AP5-2580	Hang Machine Room Side 2nd Layer - Passenger (#9, 10, 11) Elevator Machine...	2.0d	18-Jan-28	19-Jan-28	97.0d
5543	VC-EL-AP5-2590	Tape/Finish 2 Hr Rated Wall - Passenger (#9, 10, 11) Elevator Machine/Control...	5.0d	20-Jan-28	26-Jan-28	97.0d
5544	VC-EL-AP5-2600	Frame 2 Hr Rated Lid with Shaft Liner - Passenger (#9, 10, 11) Elevator Machin...	2.0d	27-Jan-28	28-Jan-28	97.0d

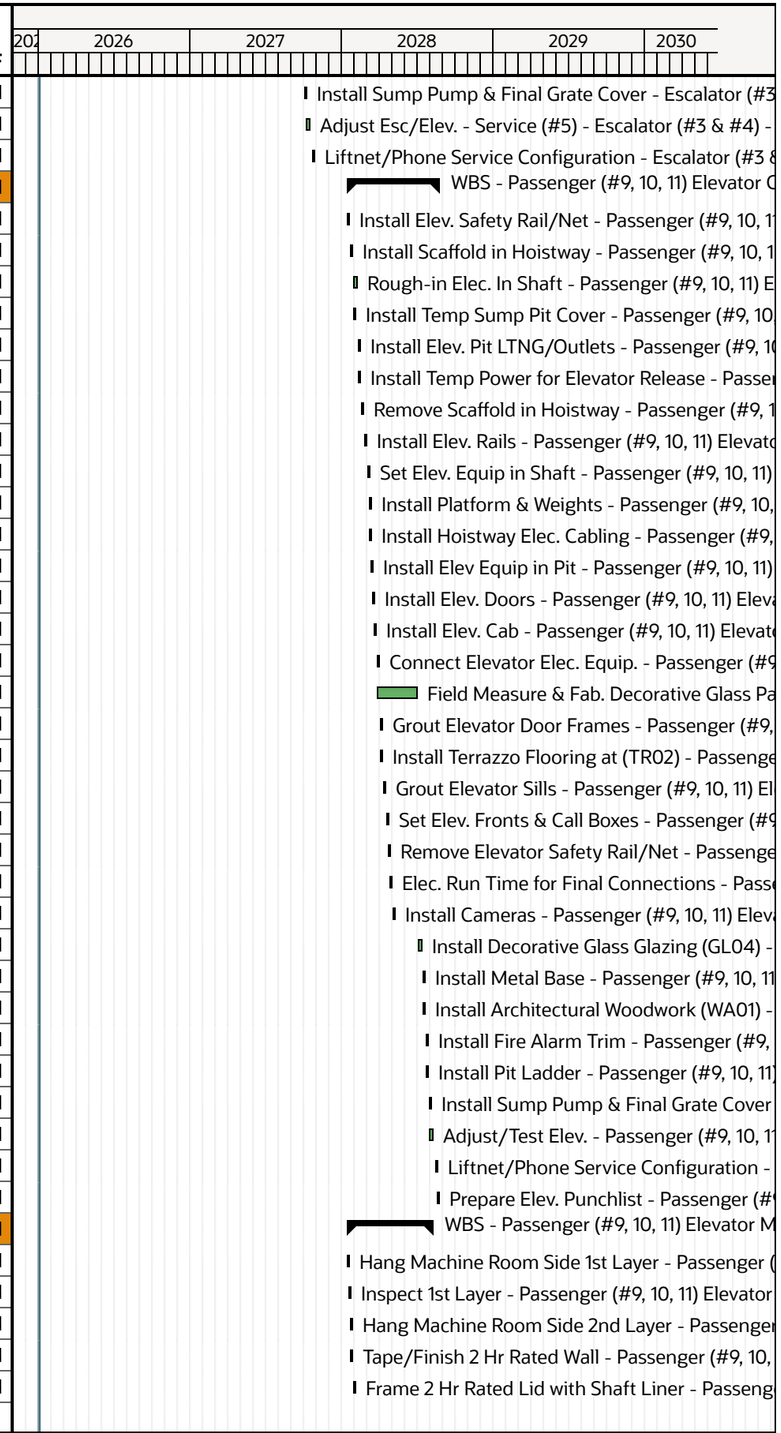


	ID	Name	Dur	Start	Finish	TF
5545	VC-EL-AP5-2610	Insulate Ceiling - Passenger (#9, 10, 11) Elevator Machine/Controller Room - I...	2.0d	31-Jan-28	1-Feb-28	97.0d
5546	VC-EL-AP5-2620	Inspect Ceiling Insulation - Passenger (#9, 10, 11) Elevator Machine/Controller ...	2.0d	2-Feb-28	3-Feb-28	97.0d
5547	VC-EL-AP5-2650	Hang 1st Layer Ceiling - Passenger (#9, 10, 11) Elevator Machine/Controller Ro...	2.0d	4-Feb-28	7-Feb-28	97.0d
5548	VC-EL-AP5-2640	Inspect 1st Layer Ceiling - Passenger (#9, 10, 11) Elevator Machine/Controller ...	2.0d	8-Feb-28	9-Feb-28	97.0d
5549	VC-EL-AP5-2630	Hang 2nd Layer Ceiling - Passenger (#9, 10, 11) Elevator Machine/Controller R...	2.0d	10-Feb-28	11-Feb-28	97.0d
5550	VC-EL-AP5-2680	Tape/Finish Ceiling - Passenger (#9, 10, 11) Elevator Machine/Controller Roo...	5.0d	14-Feb-28	18-Feb-28	97.0d
5551	VC-EL-AP5-2670	1st Coat Paint Machine Room - Passenger (#9, 10, 11) Elevator Machine/Contr...	2.0d	21-Feb-28	22-Feb-28	97.0d
5552	VC-EL-AP5-2530	Elec. Wall Rough Elev. Equip. Room - Passenger (#9, 10, 11) Elevator Machine/...	3.0d	23-Feb-28	25-Feb-28	97.0d
5553	VC-EL-AP5-2700	Install Door & Hardware - Passenger (#9, 10, 11) Elevator Machine/Controller R...	2.0d	23-Feb-28	24-Feb-28	98.0d
5554	VC-EL-AP5-2660	Set Elev. Controllers & Equip. - Passenger (#9, 10, 11) Elevator Machine/Contro...	5.0d	25-Feb-28	2-Mar-28	98.0d
5555	VC-EL-AP5-2540	Install Elec. OH Elev. Equip. Room - Passenger (#9, 10, 11) Elevator Machine/C...	15.0d	28-Feb-28	17-Mar-28	97.0d
5556	VC-EL-AP5-2690	Install Elev. Pathways/Wire Elev. - Passenger (#9, 10, 11) Elevator Machine/Co...	10.0d	3-Mar-28	16-Mar-28	98.0d
5557	VC-EL-AP5-2720	Apply Final Paint - Passenger (#9, 10, 11) Elevator Machine/Controller Room - ...	5.0d	20-Mar-28	24-Mar-28	97.0d
5558	VC-EL-AP5-2750	Install Fire Extinguisher & Cabinet - Passenger (#9, 10, 11) Elevator Machine/C...	2.0d	27-Mar-28	28-Mar-28	161.0d
5559	VC-EL-AP5-2760	Install Fire Alarm Trim - Passenger (#9, 10, 11) Elevator Machine/Controller Ro...	2.0d	27-Mar-28	28-Mar-28	97.0d
5560	VC-EL-AP5-2730	Seal Concrete Floor - Passenger (#9, 10, 11) Elevator Machine/Controller Roo...	3.0d	29-Mar-28	31-Mar-28	161.0d
5561	VC-EL-AP5-2770	Low Voltage Trim Out - Passenger (#9, 10, 11) Elevator Machine/Controller Ro...	2.0d	29-Mar-28	30-Mar-28	97.0d
5562	VC-EL-AP5-2710	Install FCUs-1-6155 - Passenger (#9, 10, 11) Elevator Machine/Controller Roo...	5.0d	31-Mar-28	6-Apr-28	97.0d
5563	VC-EL-AP5-2740	Install Rubber Base - Passenger (#9, 10, 11) Elevator Machine/Controller Room...	2.0d	3-Apr-28	4-Apr-28	161.0d
5564	VC-EL-AP5-4360	FCU Start Up - Passenger (#9, 10, 11) Elevator Machine/Controller Room - INT...	2.0d	7-Aug-28	8-Aug-28	16.0d
5565	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 6		395.0d	14-Apr-27	31-Oct-28	62.0d
5566	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 6		262.0d	14-Apr-27	24-Apr-28	90.0d
5567	WBS - Overall Rough-in - INTRF - Apron 6		262.0d	14-Apr-27	24-Apr-28	90.0d
5568	RI-AP6-10	Layout Walls/Top Track - Overall Rough-in - INTR - AP 6	10.0d	14-Apr-27	27-Apr-27	86.0d
5569	RI-AP6-4090	Install CMU Walls/Masonry Frames - Overall Rough-in - INTR - AP 6	5.0d	28-Apr-27	4-May-27	86.0d
5570	RI-AP6-20	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 6	2.0d	5-May-27	6-May-27	86.0d
5571	RI-AP6-30	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 6	4.0d	7-May-27	12-May-27	86.0d
5572	RI-AP6-40	Install Plumbing Hangers - Overall Rough-in - INTR - AP 6	2.0d	13-May-27	14-May-27	86.0d
5573	RI-AP6-50	Install Elec. Hangers - Overall Rough-in - INTR - AP 6	2.0d	17-May-27	18-May-27	86.0d
5574	RI-AP6-60	Install Fireproofing - Overall Rough-in - INTR - AP 6	10.0d	30-Jun-27	14-Jul-27	57.0d
5575	RI-AP6-4050	Install Duct Insulation - Overall Rough-in - INTR - AP 6	10.0d	11-Aug-27	24-Aug-27	133.0d
5576	RI-AP6-80	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 6	10.0d	30-Sep-27	13-Oct-27	58.0d
5577	RI-AP6-90	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 6	20.0d	7-Oct-27	3-Nov-27	58.0d
5578	RI-AP6-4060	Install Plumbing Insulation - Overall Rough-in - INTR - AP 6	5.0d	14-Oct-27	20-Oct-27	93.0d
5579	RI-AP6-100	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 6	10.0d	21-Oct-27	3-Nov-27	58.0d
5580	RI-AP6-4070	Install CHW OH Rough-in - Overall - INTR - AP 6	10.0d	4-Nov-27	17-Nov-27	65.0d
5581	RI-AP6-4080	Install CHW Insulation - Overall Rough-in INTR - AP 6	8.0d	18-Nov-27	1-Dec-27	65.0d
5582	RI-AP6-110	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 6	20.0d	6-Jan-28	2-Feb-28	12.0d
5583	RI-AP6-120	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 6	10.0d	3-Feb-28	16-Feb-28	12.0d
5584	RI-AP6-4130	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 6	10.0d	3-Feb-28	16-Feb-28	12.0d
5585	RI-AP6-130	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 6	10.0d	17-Feb-28	1-Mar-28	12.0d
5586	RI-AP6-140	Install HM Door Frames - Overall Rough-in - INTR - AP 6	3.0d	17-Feb-28	21-Feb-28	29.0d




	ID	Name	Dur	Start	Finish	TF
5587	RI-AP6-4140	Pull BAS Cable - Overall Rough-in - INTR - AP 6	10.0d	2-Mar-28	15-Mar-28	69.0d
5588	RI-AP6-150	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 6	10.0d	6-Mar-28	17-Mar-28	10.0d
5589	RI-AP6-160	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 6	3.0d	20-Mar-28	22-Mar-28	90.0d
5590	RI-AP6-4100	Install LTNG for Anchor Tenant Ops - Overall Rough-in - INTR - AP 6	10.0d	20-Mar-28	31-Mar-28	40.0d
5591	RI-AP6-4110	Low Volt Pull Cabling - Overall Rough-in - INTR - AP 6	18.0d	23-Mar-28	17-Apr-28	90.0d
5592	RI-AP6-4120	Low Volt Terminate Cabling - Overall Rough-in - INTR - AP 6	5.0d	18-Apr-28	24-Apr-28	90.0d
5593	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Restroom - Apron 6		80.0d	21-Apr-27	12-Aug-27	164.0d
5594	WBS - Gang Bathroom #1 - INTR - Apron 6		80.0d	21-Apr-27	12-Aug-27	164.0d
5595	RI-AP6-R1-1470	Frame & Top-Down Walls - Gang Bathroom #1 - INTR - AP 6	2.0d	21-Apr-27	22-Apr-27	204.0d
5596	RI-AP6-R1-1480	Set Restrooms Carriers - Gang Bathroom #1 - INTR - AP 6	5.0d	22-Apr-27	28-Apr-27	204.0d
5597	RI-AP6-R1-1490	Install Blocking & Backing for Specialties - Gang Bathroom #1 - INTR - AP 6	3.0d	23-Apr-27	27-Apr-27	217.0d
5598	RI-AP6-R1-1500	Fire Sprinkler Mains & Branch Line Rough-in - Gang Bathroom #1 - INTR - AP 6	10.0d	23-Apr-27	6-May-27	212.0d
5599	RI-AP6-R1-1620	Install 1/2" Plywood Backing - Gang Bathroom #1 - INTR - AP 6	2.0d	28-Apr-27	29-Apr-27	237.0d
5600	RI-AP6-R1-1550	Install Plumbing Rough-in Walls - Gang Bathroom #1 - INTR - AP 6	10.0d	29-Apr-27	12-May-27	204.0d
5601	RI-AP6-R1-1590	Frame Ceiling - Gang Bathroom #1 - INTR - AP 6	2.0d	29-Apr-27	30-Apr-27	213.0d
5602	RI-AP6-R1-1600	Install Recessed Can RI/Speaker RI Frames - Gang Bathroom #1 - INTR - AP 6	2.0d	30-Apr-27	3-May-27	215.0d
5603	RI-AP6-R1-1530	Low Voltage Rough-in Ceilings - Gang Bathroom #1 - INTR - AP 6	3.0d	3-May-27	5-May-27	213.0d
5604	RI-AP6-R1-1560	Elec. Rough-in Walls - Gang Bathroom #1 - INTR - AP 6	3.0d	5-May-27	7-May-27	204.0d
5605	RI-AP6-R1-1570	Low Voltage Rough-in Walls - Gang Bathroom #1 - INTR - AP 6	3.0d	10-May-27	12-May-27	204.0d
5606	RI-AP6-R1-1580	Install Vanities Steel Support - Gang Bathroom #1 - INTR - AP 6	2.0d	13-May-27	14-May-27	204.0d
5607	RI-AP6-R1-1610	Install Wall Insulation - Gang Bathroom #1 - INTR - AP 6	2.0d	11-Aug-27	12-Aug-27	144.0d
5608	WBS - Infrastructure, MEPTFP Rough-in & Equipment - MDF/IDF - Apron 6		346.0d	28-Apr-27	6-Sep-28	35.0d
5609	WBS - LAN/CBP MDF 6185 - INTRF - CBP IDF Alias 101 - Apron 6		346.0d	28-Apr-27	6-Sep-28	24.0d
5610	RI-AP6-MDF-3660	Layout Walls/Top Track - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	28-Apr-27	4-May-27	180.0d
5611	RI-AP6-MDF-3670	Install Fire Sprinkler Hangers - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	5-May-27	6-May-27	180.0d
5612	RI-AP6-MDF-3680	Install Duct/CHW Hangers - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	7-May-27	10-May-27	180.0d
5613	RI-AP6-MDF-3700	Install Elec. Hangers - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	11-May-27	12-May-27	180.0d
5614	RI-AP6-MDF-3710	Install Fireproofing - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	13-May-27	14-May-27	180.0d
5615	RI-AP6-MDF-3750	Fire Sprinkler Mains & Branch Line Rough-in - MDF 6185 - INTRF - CBP IDF Ali...	4.0d	17-May-27	20-May-27	248.0d
5616	RI-AP6-MDF-3760	Install Elec. OH Rough-in - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	24-May-27	7-Jun-27	247.0d
5617	RI-AP6-MDF-3770	Install Low Voltage OH Rough-in - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	8-Jun-27	10-Jun-27	247.0d
5618	RI-AP6-MDF-3780	Frame & Top-Down Walls - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	4.0d	11-Jun-27	16-Jun-27	247.0d
5619	RI-AP6-MDF-3790	Install HM Door Frames - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	11-Jun-27	15-Jun-27	248.0d
5620	RI-AP6-MDF-3800	Elec. Rough-in Walls - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	17-Jun-27	21-Jun-27	247.0d
5621	RI-AP6-MDF-3810	Low Voltage Rough-in Walls - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	22-Jun-27	24-Jun-27	247.0d
5622	RI-AP6-MDF-3820	Low Voltage/Elec. in Wall Inspection (COT) - MDF 6185 - INTRF - CBP IDF Alias ...	2.0d	25-Jun-27	28-Jun-27	247.0d
5623	RI-AP6-MDF-4040	Patch Fireproofing - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	29-Jun-27	6-Jul-27	247.0d
5624	FN-AP6-MDF-4050	Hang, Tape & Finish Drywall - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	12-Jan-28	18-Jan-28	117.0d
5625	FN-AP6-MDF-4060	Prime and First Coat - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	19-Jan-28	20-Jan-28	117.0d
5626	FN-AP6-MDF-4070	Firestopping - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	21-Jan-28	25-Jan-28	117.0d
5627	FN-AP6-MDF-4190	Install FCU-1-6185 - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	21-Jan-28	27-Jan-28	137.0d
5628	FN-AP6-MDF-4080	Install Tech Room Backerboard - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	26-Jan-28	27-Jan-28	117.0d




	ID	Name	Dur	Start	Finish	TF
5629	FN-AP6-MDF-4090	Set Racks - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	28-Jan-28	10-Feb-28	117.0d
5630	FN-AP6-MDF-4100	Install Ladder Rack - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	11-Feb-28	15-Feb-28	117.0d
5631	FN-AP6-MDF-4110	Pull & Terminate Fiber - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	16-Feb-28	29-Feb-28	117.0d
5632	FN-AP6-MDF-4120	Trim-Out Low Voltage - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	1-Mar-28	7-Mar-28	117.0d
5633	FN-AP6-MDF-4140	Install Door & Hardware - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	8-Mar-28	9-Mar-28	118.0d
5634	FN-AP6-MDF-4160	Low Voltage Testing - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	8-Mar-28	10-Mar-28	117.0d
5635	FN-AP6-MDF-4150	Install Flooring - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	13-Mar-28	17-Mar-28	117.0d
5636	FN-AP6-MDF-4210	Install Rubber Base - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	20-Mar-28	24-Mar-28	117.0d
5637	FN-AP6-MDF-4130	Apply Final Paint - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	27-Mar-28	31-Mar-28	117.0d
5638	FN-AP6-MDF-4200	FCU Start-Up - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	7-Aug-28	11-Aug-28	24.0d
5639	FN-AP6-MDF-4170	Owner's Acceptance Walkthrough - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	14-Aug-28	15-Aug-28	24.0d
5640	FN-AP6-MDF-4180	Owner Equip. Install - MDF 6185 - INTRF - CBP IDF Alias 101 - AP 6	15.0d	16-Aug-28	6-Sep-28	24.0d
5641	WBS - HCAA IDF 6199 - INTRF- Alias ASD 01280 - Apron 6		343.0d	28-Apr-27	31-Aug-28	38.0d
5642	RI-AP6-IDF-3490	Layout Walls/Top Track - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	28-Apr-27	4-May-27	182.0d
5643	RI-AP6-IDF-3500	Install Fire Sprinkler Hangers - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	5-May-27	6-May-27	182.0d
5644	RI-AP6-IDF-3530	Install Elec. Hangers - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	7-May-27	10-May-27	182.0d
5645	RI-AP6-IDF-3540	Install Fireproofing - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	11-May-27	12-May-27	182.0d
5646	RI-AP6-IDF-3580	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6199 - INTRF - Alias ...	4.0d	13-May-27	18-May-27	259.0d
5647	RI-AP6-IDF-3590	Install Elec. OH Rough-in - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	10.0d	20-May-27	3-Jun-27	258.0d
5648	RI-AP6-IDF-3600	Install Low Voltage OH Rough-in - HCAA IDF 6199 - INTRF - Alias ASD 01280 -...	3.0d	4-Jun-27	8-Jun-27	258.0d
5649	RI-AP6-IDF-3610	Frame & Top-Down Walls - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	4.0d	9-Jun-27	14-Jun-27	258.0d
5650	RI-AP6-IDF-3620	Install HM Door Frames - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	9-Jun-27	11-Jun-27	259.0d
5651	RI-AP6-IDF-3630	Elec. Rough-in Walls - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	15-Jun-27	17-Jun-27	258.0d
5652	RI-AP6-IDF-3640	Low Voltage Rough-in Walls - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	18-Jun-27	22-Jun-27	258.0d
5653	RI-AP6-IDF-3650	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6199 - INTRF - Alias AS...	2.0d	23-Jun-27	24-Jun-27	258.0d
5654	RI-AP6-IDF-3895	Patch Fireproofing - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	25-Jun-27	1-Jul-27	258.0d
5655	FN-AP6-IDF-3900	Hang, Tape & Finish Drywall - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	12-Jan-28	18-Jan-28	126.0d
5656	FN-AP6-IDF-3910	Prime & First Coat - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	19-Jan-28	20-Jan-28	129.0d
5657	FN-AP6-IDF-3920	Firestopping - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	21-Jan-28	25-Jan-28	129.0d
5658	FN-AP6-IDF-4040	Install FCUs-1-6199 - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	21-Jan-28	27-Jan-28	137.0d
5659	FN-AP6-IDF-3930	Install Tech Room Backerboard - HCAA IDF 6199 - INTRF - Alias ASD 01280 - A...	2.0d	26-Jan-28	27-Jan-28	129.0d
5660	FN-AP6-IDF-3940	Set Racks - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	10.0d	28-Jan-28	10-Feb-28	129.0d
5661	FN-AP6-IDF-3950	Install Ladder Rack - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	11-Feb-28	15-Feb-28	129.0d
5662	FN-AP6-IDF-3960	Pull & Terminate Fiber - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	10.0d	16-Feb-28	29-Feb-28	129.0d
5663	FN-AP6-IDF-4080	Pull & Terminate Fiber for PBB D56, D57, D58, D59, D60 - HCAA IDF 6199 - IN...	10.0d	16-Feb-28	29-Feb-28	129.0d
5664	FN-AP6-IDF-3970	Trim-Out Low Voltage - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	1-Mar-28	7-Mar-28	129.0d
5665	FN-AP6-IDF-3990	Install Door & Hardware - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	8-Mar-28	9-Mar-28	129.0d
5666	FN-AP6-IDF-4010	Low Voltage Testing - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	3.0d	8-Mar-28	10-Mar-28	143.0d
5667	FN-AP6-IDF-4000	Install Flooring - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	10-Mar-28	16-Mar-28	129.0d
5668	FN-AP6-IDF-4090	Install Rubber Base - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	17-Mar-28	23-Mar-28	129.0d
5669	FN-AP6-IDF-3980	Apply Final Paint - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	5.0d	24-Mar-28	30-Mar-28	129.0d
5670	FN-AP6-IDF-4060	FCU Start Up - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	2.0d	7-Aug-28	8-Aug-28	38.0d

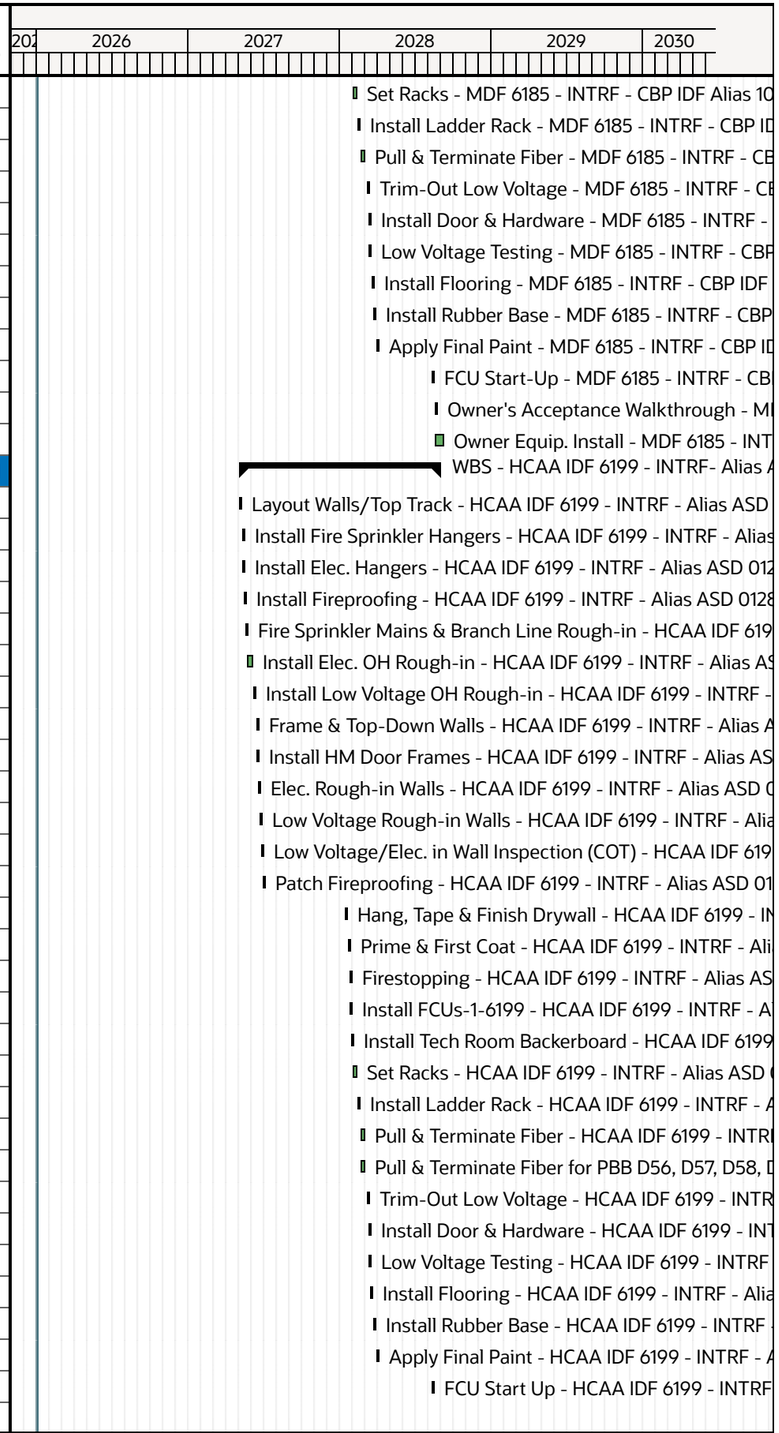


	ID	Name	Dur	Start	Finish	TF
5671	FN-AP6-IDF-4020	Owner's Acceptance Walkthrough - HCAA IDF 6199 - INTRF - Alias ASD 01280 ...	2.0d	9-Aug-28	10-Aug-28	38.0d
5672	FN-AP6-IDF-4030	Owner Equip. Install - HCAA IDF 6199 - INTRF - Alias ASD 01280 - AP 6	15.0d	11-Aug-28	31-Aug-28	38.0d
5673	WBS - Tenant IDF 6201 - INTRF - Alias ASD 01281 - Apron 6		343.0d	28-Apr-27	31-Aug-28	38.0d
5674	RI-AP6-IDF-3320	Layout Walls/Top Track - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	28-Apr-27	4-May-27	182.0d
5675	RI-AP6-IDF-3330	Install Fire Sprinkler Hangers - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	5-May-27	6-May-27	182.0d
5676	RI-AP6-IDF-3360	Install Elec. Hangers - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	7-May-27	10-May-27	182.0d
5677	RI-AP6-IDF-3370	Install Fireproofing - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	11-May-27	12-May-27	182.0d
5678	RI-AP6-IDF-3410	Fire Sprinkler Mains & Branch Line Rough-in - Tenant IDF 6201 - INTRF - Alias ...	4.0d	13-May-27	18-May-27	249.0d
5679	RI-AP6-IDF-3420	Install Elec. OH Rough-in - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	10.0d	20-May-27	3-Jun-27	248.0d
5680	RI-AP6-IDF-3430	Install Low Voltage OH Rough-in - Tenant IDF 6201 - INTRF - Alias ASD 01281 ...	3.0d	4-Jun-27	8-Jun-27	248.0d
5681	RI-AP6-IDF-3440	Frame & Top-Down Walls - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	4.0d	9-Jun-27	14-Jun-27	248.0d
5682	RI-AP6-IDF-3450	Install HM Door Frames - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	3.0d	9-Jun-27	11-Jun-27	249.0d
5683	RI-AP6-IDF-3460	Elec. Rough-in Walls - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	3.0d	15-Jun-27	17-Jun-27	248.0d
5684	RI-AP6-IDF-3470	Low Voltage Rough-in Walls - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	4.0d	18-Jun-27	23-Jun-27	248.0d
5685	RI-AP6-IDF-3480	Low Voltage/Elec. in Wall Inspection (COT) - Tenant IDF 6201 - INTRF - Alias A...	2.0d	24-Jun-27	25-Jun-27	248.0d
5686	RI -AP6-IDF-3746	Patch Fireproofing - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	28-Jun-27	2-Jul-27	248.0d
5687	FN-AP6-IDF-3750	Hang, Tape & Finish Drywall - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	12-Jan-28	18-Jan-28	117.0d
5688	FN-AP6-IDF-3760	Prime & First Coat - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	19-Jan-28	20-Jan-28	129.0d
5689	FN-AP6-IDF-3770	Firestopping - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	3.0d	21-Jan-28	25-Jan-28	129.0d
5690	FN-AP6-IDF-4050	Install FCUs-1-6201 - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	21-Jan-28	27-Jan-28	137.0d
5691	FN-AP6-IDF-3780	Install Tech Room Backerboard - Tenant IDF 6201 - INTRF - Alias ASD 01281 - ...	2.0d	26-Jan-28	27-Jan-28	129.0d
5692	FN-AP6-IDF-3790	Set Racks - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	10.0d	28-Jan-28	10-Feb-28	129.0d
5693	FN-AP6-IDF-3800	Install Ladder Rack - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	3.0d	11-Feb-28	15-Feb-28	129.0d
5694	FN-AP6-IDF-3810	Pull & Terminate Fiber - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	10.0d	16-Feb-28	29-Feb-28	129.0d
5695	FN-AP6-IDF-3820	Trim-Out Low Voltage - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	1-Mar-28	7-Mar-28	129.0d
5696	FN-AP6-IDF-3840	Install Door & Hardware - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	8-Mar-28	9-Mar-28	129.0d
5697	FN-AP6-IDF-3850	Install Flooring - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	10-Mar-28	16-Mar-28	129.0d
5698	FN-AP6-IDF-3860	Low Voltage Testing - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	3.0d	17-Mar-28	21-Mar-28	131.0d
5699	FN-AP6-IDF-4100	Install Rubber Base - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	17-Mar-28	23-Mar-28	129.0d
5700	FN-AP6-IDF-3830	Apply Final Paint - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	5.0d	24-Mar-28	30-Mar-28	129.0d
5701	FN-AP6-IDF-4070	FCU Start Up - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	2.0d	7-Aug-28	8-Aug-28	38.0d
5702	FN-AP6-IDF-3870	Owner's Acceptance Walkthrough - Tenant IDF 6201 - INTRF - Alias ASD 0128...	2.0d	9-Aug-28	10-Aug-28	38.0d
5703	FN-AP6-IDF-3880	Owner Equip. Install - Tenant IDF 6201 - INTRF - Alias ASD 01281 - AP 6	15.0d	11-Aug-28	31-Aug-28	38.0d
5704	WBS - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - Apron 6		344.0d	28-Apr-27	1-Sep-28	37.0d
5705	RI-AP6-LN-3830	Layout Walls/Top Track - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	28-Apr-27	4-May-27	182.0d
5706	RI-AP6-LN-3840	Install Fire Sprinkler Hangers - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	5-May-27	6-May-27	182.0d
5707	RI-AP6-LN-3870	Install Elec. Hangers - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	7-May-27	10-May-27	182.0d
5708	RI-AP6-LN-3880	Install Fireproofing - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	11-May-27	12-May-27	182.0d
5709	RI-AP6-LN-3920	Fire Sprinkler Mains & Branch Line Rough-in - SLAN IDF 6180 - INTRF - CBP ID...	4.0d	13-May-27	18-May-27	259.0d
5710	RI-AP6-LN-3930	Install Elec. OH Rough-in - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	20-May-27	3-Jun-27	258.0d
5711	RI-AP6-LN-3940	Install Low Voltage OH Rough-in - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 ...	3.0d	4-Jun-27	8-Jun-27	258.0d
5712	RI-AP6-LN-3950	Frame & Top-Down Walls - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	4.0d	9-Jun-27	14-Jun-27	258.0d

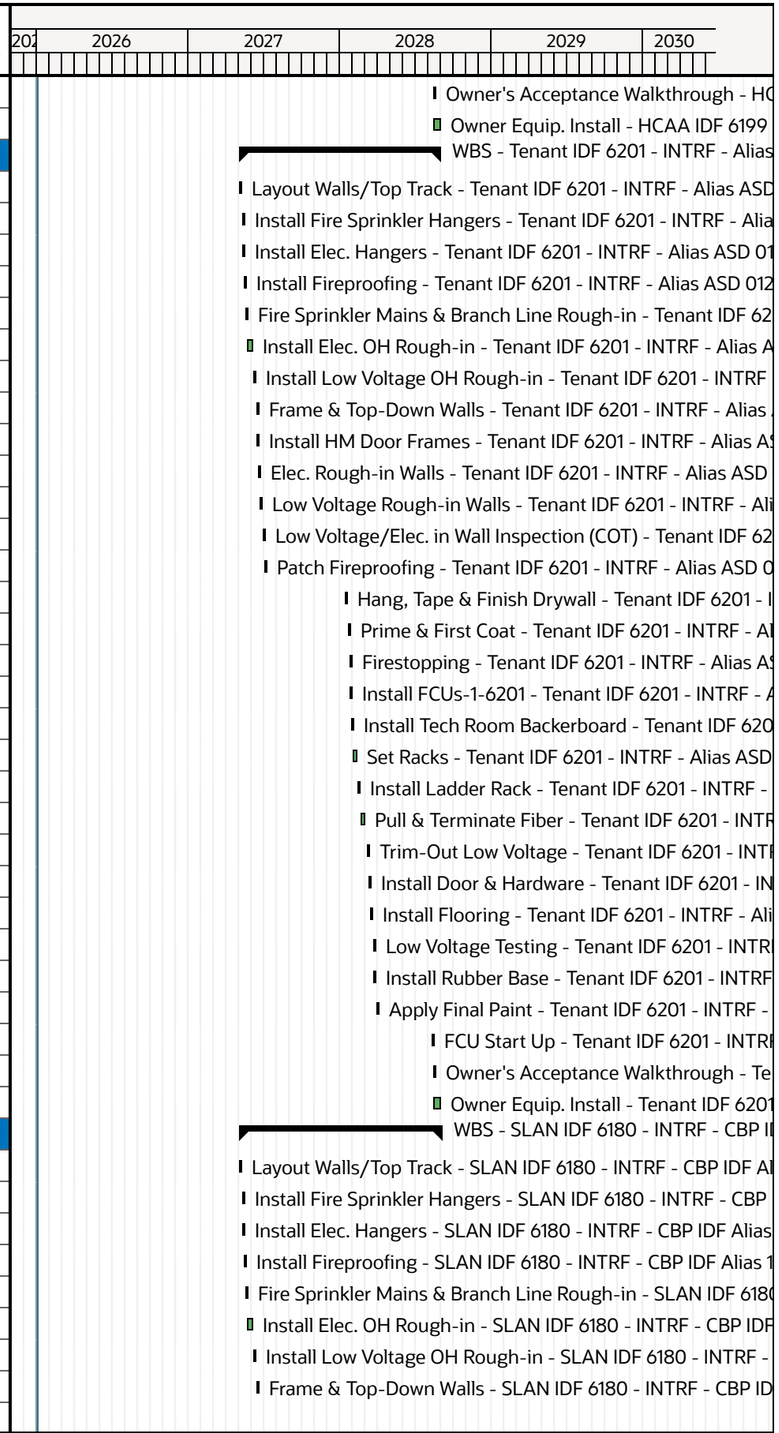

	ID	Name	Dur	Start	Finish	TF
5713	RI-AP6-LN-3960	Install HM Door Frames - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	9-Jun-27	11-Jun-27	259.0d
5714	RI-AP6-LN-3970	Elec. Rough-in Walls - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	15-Jun-27	17-Jun-27	258.0d
5715	RI-AP6-LN-3980	Low Voltage Rough-in Walls - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	18-Jun-27	22-Jun-27	258.0d
5716	RI-AP6-LN-3990	Low Voltage/Elec. in Wall Inspection (COT) - SLAN IDF 6180 - INTRF - CBP IDF ...	2.0d	23-Jun-27	24-Jun-27	258.0d
5717	RI-AP6-LN-4190	Patch Fireproofing - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	25-Jun-27	1-Jul-27	258.0d
5718	FN-AP6-LN-4200	Hang, Tape & Finish Drywall - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	12-Jan-28	18-Jan-28	126.0d
5719	FN-AP6-LN-4210	Prime & First Coat - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	19-Jan-28	20-Jan-28	129.0d
5720	FN-AP6-LN-4220	Firestopping - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	21-Jan-28	25-Jan-28	129.0d
5721	FN-AP6-LN-4340	Install FCU-1-6180 - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	21-Jan-28	27-Jan-28	137.0d
5722	FN-AP6-LN-4230	Install Tech Room Backerboard - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - ...	2.0d	26-Jan-28	27-Jan-28	129.0d
5723	FN-AP6-LN-4240	Set Racks - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	28-Jan-28	10-Feb-28	129.0d
5724	FN-AP6-LN-4250	Install Ladder Rack - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	11-Feb-28	15-Feb-28	129.0d
5725	FN-AP6-LN-4260	Pull & Terminate Fiber - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	10.0d	16-Feb-28	29-Feb-28	129.0d
5726	FN-AP6-LN-4270	Trim-Out Low Voltage - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	1-Mar-28	7-Mar-28	129.0d
5727	FN-AP6-LN-4290	Install Door & Hardware - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	8-Mar-28	9-Mar-28	129.0d
5728	FN-AP6-LN-4310	Low Voltage Testing - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	3.0d	8-Mar-28	10-Mar-28	143.0d
5729	FN-AP6-LN-4300	Install Flooring - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	10-Mar-28	16-Mar-28	129.0d
5730	FN-AP6-LN-4360	Install Rubber Base - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	17-Mar-28	23-Mar-28	129.0d
5731	FN-AP6-LN-4280	Apply Final Paint - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	5.0d	24-Mar-28	30-Mar-28	129.0d
5732	FN-AP6-LN-4350	FCU Start Up - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	2.0d	7-Aug-28	8-Aug-28	38.0d
5733	FN-AP6-LN-4320	Owner's Acceptance Walkthrough - SLAN IDF 6180 - INTRF - CBP IDF Alias 10...	2.0d	10-Aug-28	11-Aug-28	37.0d
5734	FN-AP6-LN-4330	Owner Equip. Install - SLAN IDF 6180 - INTRF - CBP IDF Alias 101 - AP 6	15.0d	14-Aug-28	1-Sep-28	37.0d
5735	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Electrical - Apron 6		68.0d	21-Apr-27	27-Jul-27	171.0d
5736	WBS - Electrical Room - Apron 6 - Room 6200		68.0d	21-Apr-27	27-Jul-27	120.0d
5737	RI-AP6-ER-2460	Layout Walls/Top Track - Elec. Room 6200 - INTRF - AP 6	5.0d	21-Apr-27	27-Apr-27	120.0d
5738	RI-AP6-ER-2470	Elec. Layout for Conduit Windows (Pre Framing) - Elec. Room 6200 - INTRF - A...	2.0d	28-Apr-27	29-Apr-27	120.0d
5739	RI-AP6-ER-2480	Install Fire Sprinkler Hangers - Elec. Room 6200 - INTRF - AP 6	2.0d	30-Apr-27	3-May-27	120.0d
5740	RI-AP6-ER-2490	Install Elec. Hangers - Elec. Room 6200 - INTRF - AP 6	5.0d	4-May-27	10-May-27	120.0d
5741	RI-AP6-ER-2500	Install Fireproofing - Elec. Room 6200 - INTRF - AP 6	2.0d	11-May-27	12-May-27	120.0d
5742	RI-AP6-ER-2510	Fire Sprinkler Mains & Branch Line Rough-in - Elec. Room 6200 - INTRF - AP 6	10.0d	13-May-27	26-May-27	120.0d
5743	RI-AP6-ER-2520	Low Voltage Rough-in Ceilings - Elec. Room 6200 - INTRF - AP 6	10.0d	27-May-27	10-Jun-27	120.0d
5744	RI-AP6-ER-2530	Frame & Top-Down Walls - Elec. Room 6200 - INTRF - AP 6	10.0d	11-Jun-27	24-Jun-27	120.0d
5745	RI-AP6-ER-2560	Install HM Door Frames - Elec. Room 6200 - INTRF - AP 6	3.0d	11-Jun-27	15-Jun-27	134.0d
5746	RI-AP6-ER-2540	Elec. Layout-Panel Backing & Housekeeping Pads (Post Framing) - Elec. Room ...	5.0d	25-Jun-27	1-Jul-27	120.0d
5747	RI-AP6-ER-2550	Pour Equip. Pads - Elec. Room 6200 - INTRF - AP 6	2.0d	2-Jul-27	6-Jul-27	120.0d
5748	RI-AP6-ER-2570	Elec. Rough-in Walls - Elec. Room 6200 - INTRF - AP 6	5.0d	7-Jul-27	13-Jul-27	120.0d
5749	RI-AP6-ER-2580	Low Voltage Rough-in Walls - Elec. Room 6200 - INTRF - AP 6	5.0d	14-Jul-27	20-Jul-27	120.0d
5750	RI-AP6-ER-2590	Patch Fireproofing - Elec. Room 6200 - INTRF - AP 6	5.0d	21-Jul-27	27-Jul-27	120.0d
5751	WBS - Electrical Room - Apron 6 - CBP 6175		54.0d	28-Apr-27	14-Jul-27	180.0d
5752	RI-AP6-ER-2610	Layout Walls/Top Track - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	28-Apr-27	4-May-27	160.0d
5753	RI-AP6-ER-2620	Elec. Layout for Conduit Windows (Pre Framing) - Elec. Room CBP 6175 - INTR...	2.0d	5-May-27	6-May-27	160.0d
5754	RI-AP6-ER-2630	Install Fire Sprinkler Hangers - Elec. Room CBP 6175 - INTRF - AP 6	2.0d	7-May-27	10-May-27	160.0d

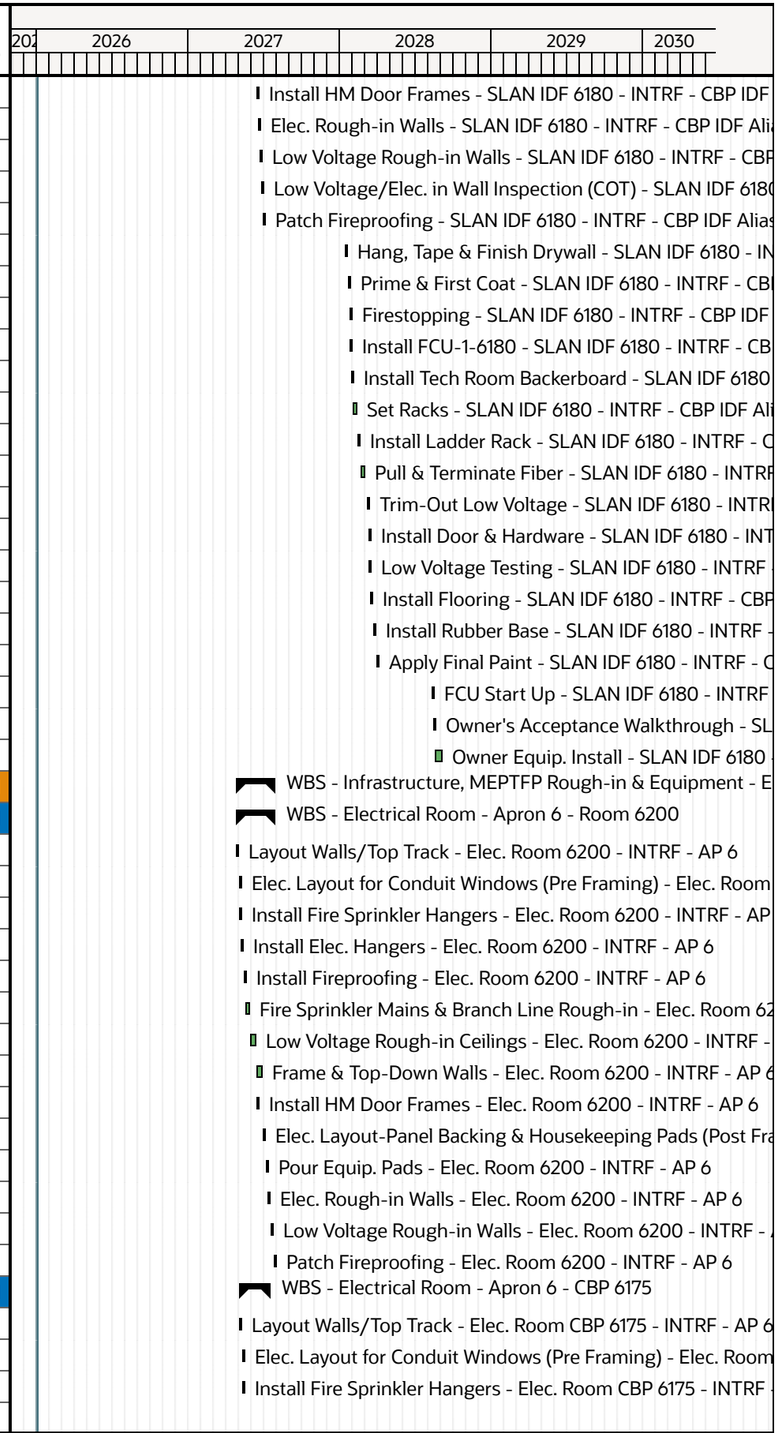


	ID	Name	Dur	Start	Finish	TF
5755	RI-AP6-ER-2640	Install Elec. Hangers - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	11-May-27	17-May-27	160.0d
5756	RI-AP6-ER-2650	Install Fireproofing - Elec. Room CBP 6175 - INTRF - AP 6	2.0d	18-May-27	19-May-27	160.0d
5757	RI-AP6-ER-2660	Fire Sprinkler Mains & Branch Line Rough-in - Elec. Room CBP 6175 - INTRF - ...	10.0d	20-May-27	3-Jun-27	160.0d
5758	RI-AP6-ER-2670	Low Voltage Rough-in Ceilings - Elec. Room CBP 6175 - INTRF - AP 6	10.0d	4-Jun-27	17-Jun-27	160.0d
5759	RI-AP6-ER-2680	Frame & Top-Down Walls - Elec. Room CBP 6175 - INTRF - AP 6	10.0d	18-Jun-27	1-Jul-27	160.0d
5760	RI-AP6-ER-2710	Install HM Door Frames - Elec. Room CBP 6175 - INTRF - AP 6	3.0d	18-Jun-27	22-Jun-27	160.0d
5761	RI-AP6-ER-2720	Elec. Rough-in Walls - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	23-Jun-27	29-Jun-27	160.0d
5762	RI-AP6-ER-2730	Low Voltage Rough-in Walls - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	30-Jun-27	7-Jul-27	160.0d
5763	RI-AP6-ER-2690	Elec. Layout-Panel Backing & Housekeeping Pads (Post Framing) - Elec. Room ...	5.0d	2-Jul-27	9-Jul-27	181.0d
5764	RI-AP6-ER-2740	Patch Fireproofing - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	8-Jul-27	14-Jul-27	160.0d
5765	RI-AP6-ER-2700	Pour Equip. Pads - Elec. Room CBP 6175 - INTRF - AP 6	2.0d	12-Jul-27	13-Jul-27	181.0d
5766	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mechanical Room - Apron 6		268.0d	28-Apr-27	16-May-28	81.0d
5767	RI-AP6-MR-1180	Layout Walls/Top Track - Mech. Room - INTR - AP 6	5.0d	28-Apr-27	4-May-27	158.0d
5768	RI-AP6-MR-1190	Pour Equip. Pads - Mech. Room - INTR - AP 6	2.0d	5-May-27	6-May-27	251.0d
5769	RI-AP6-MR-1200	Install Fire Sprinkler Hangers - Mech. Room - INTR - AP 6	2.0d	5-May-27	6-May-27	158.0d
5770	RI-AP6-MR-1210	Set Mech. Equip./AHU - Mech. Room - INTR - AP 6	5.0d	7-May-27	13-May-27	251.0d
5771	RI-AP6-MR-1220	Install Duct/CHW Hangers - Mech. Room - INTR - AP 6	3.0d	10-May-27	12-May-27	158.0d
5772	RI-AP6-MR-1230	Install Plumbing Hangers - Mech. Room - INTR - AP 6	5.0d	13-May-27	19-May-27	158.0d
5773	RI-AP6-MR-1240	Install Elec. Hangers - Mech. Room - INTR - AP 6	2.0d	20-May-27	21-May-27	158.0d
5774	RI-AP6-MR-1250	Install Fireproofing - Mech. Room - INTR - AP 6	2.0d	24-May-27	25-May-27	158.0d
5775	RI-AP6-MR-1260	Install Plumbing OH Rough-in - Mech. Room - INTR - AP 6	5.0d	26-May-27	2-Jun-27	158.0d
5776	RI-AP6-MR-1270	Install Duct OH Rough-in - Mech. Room - INTR - AP 6	15.0d	3-Jun-27	23-Jun-27	158.0d
5777	RI-AP6-MR-1290	Install CHW OH Rough-in - Mech. Room - INTR - AP 6	15.0d	24-Jun-27	15-Jul-27	182.0d
5778	RI-AP6-MR-1300	Fire Sprinkler Mains & Branch Line Rough-in - Mech. Room - INTR - AP 6	10.0d	16-Jul-27	29-Jul-27	182.0d
5779	RI-AP6-MR-1330	Install Elec. OH Rough-in - Mech. Room - INTR - AP 6	10.0d	30-Jul-27	12-Aug-27	182.0d
5780	RI-AP6-MR-1340	Install Mech. Equip. - Mech. Room - INTR - AP 6	10.0d	13-Aug-27	26-Aug-27	188.0d
5781	RI-AP6-MR-1350	Low Voltage Rough-in Ceilings - Mech. Room - INTR - AP 6	3.0d	13-Aug-27	17-Aug-27	182.0d
5782	RI-AP6-MR-1360	Frame & Top-Down Walls - Mech. Room - INTR - AP 6	10.0d	18-Aug-27	31-Aug-27	182.0d
5783	RI-AP6-MR-1380	Install HM Door Frames - Mech. Room - INTR - AP 6	3.0d	18-Aug-27	20-Aug-27	189.0d
5784	RI-AP6-MR-1320	Install Duct Insulation - Mech. Room - INTR - AP 6	5.0d	25-Aug-27	31-Aug-27	180.0d
5785	RI-AP6-MR-1400	Elec. Rough-in Walls - Mech. Room - INTR - AP 6	3.0d	1-Sep-27	3-Sep-27	182.0d
5786	RI-AP6-MR-1420	Low Voltage Rough-in Walls - Mech. Room - INTR - AP 6	3.0d	7-Sep-27	9-Sep-27	250.0d
5787	RI-AP6-MR-1280	Install Plumbing Insulation - Mech. Room - INTR - AP 6	5.0d	21-Oct-27	27-Oct-27	145.0d
5788	RI-AP6-MR-1310	Install CHW Insulation - Mech. Room - INTR - AP 6	5.0d	2-Dec-27	8-Dec-27	117.0d
5789	RI-AP6-MR-1440	Pull & Terminate to Mech. Equip. - Mech. Room. - INTR - AP 6	5.0d	3-May-28	9-May-28	15.0d
5790	RI-AP6-MR-1450	Patch Fireproofing - Mech. Room - INTR - AP 6	5.0d	10-May-28	16-May-28	81.0d
5791	WBS - Service (#8) Elevator Cabs/Shaft - INTR - Apron 6		119.0d	15-May-28	31-Oct-28	62.0d
5792	VC-EL-AP6-2390	Install Elev. Safety Rail/Net - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	15-May-28	19-May-28	79.0d
5793	VC-EL-AP6-2510	Install Scaffold in Hoistway - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	22-May-28	26-May-28	79.0d
5794	VC-EL-AP6-2400	Rough-in Elec. In Shaft - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	8.0d	30-May-28	8-Jun-28	79.0d
5795	VC-EL-AP6-2530	Install Temp Sump Pit Cover - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	30-May-28	31-May-28	85.0d
5796	VC-EL-AP6-2410	Install Elev. Pit LTNG/Outlets - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	9-Jun-28	15-Jun-28	79.0d

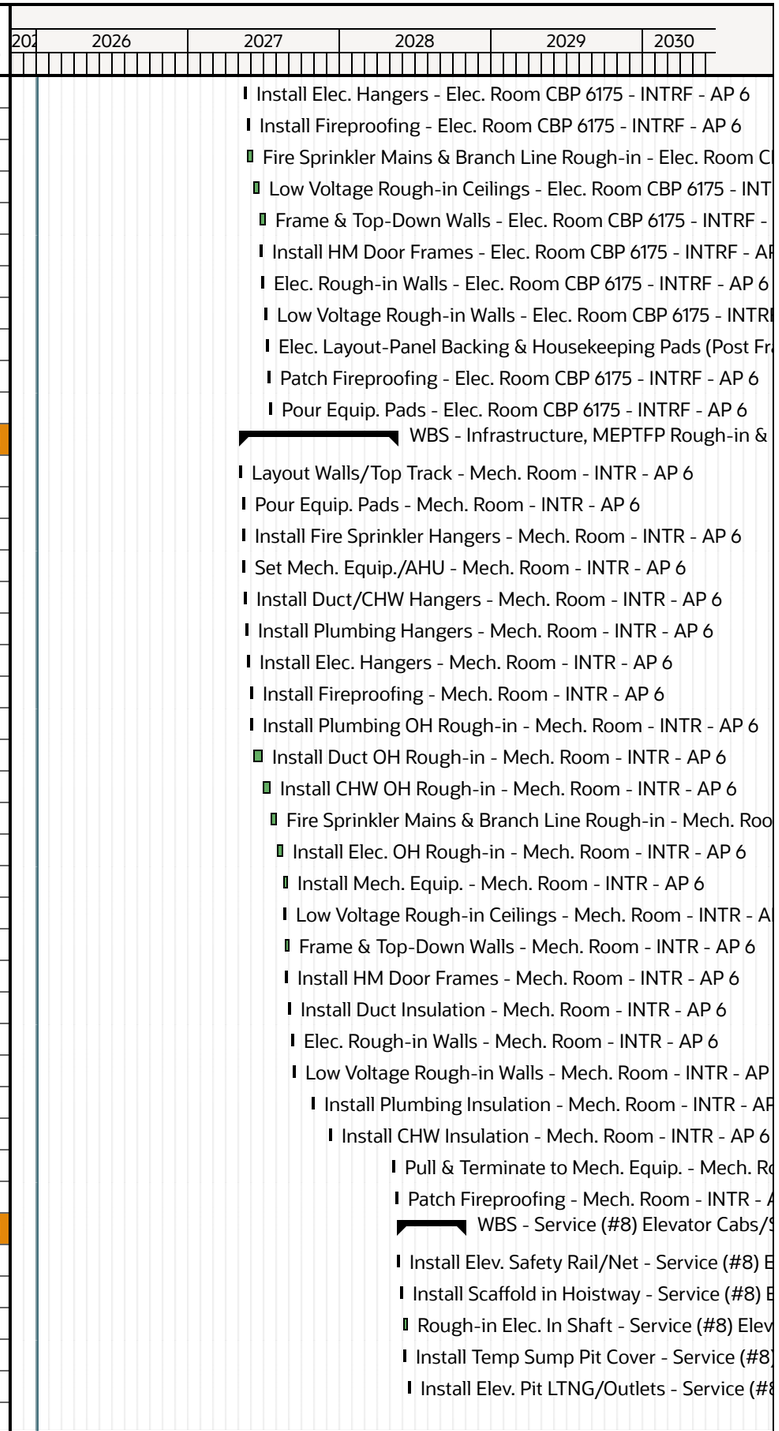


	ID	Name	Dur	Start	Finish	TF
5797	VC-EL-AP6-2420	Install Temp Power for Elevator Release - Service (#8) Elevator Cabs/Shaft - IN...	5.0d	9-Jun-28	15-Jun-28	84.0d
5798	VC-EL-AP6-2520	Remove Scaffold in Hoistway - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	16-Jun-28	22-Jun-28	79.0d
5799	VC-EL-AP6-2430	Install Elev. Rails - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	19-Jul-28	25-Jul-28	62.0d
5800	VC-EL-AP6-2880	Set Elev. Equip in Shaft - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	26-Jul-28	27-Jul-28	62.0d
5801	VC-EL-AP6-2890	Install Platform & Weights - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	28-Jul-28	3-Aug-28	62.0d
5802	VC-EL-AP6-2900	Install Hoistway Elec. Cabling - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	28-Jul-28	3-Aug-28	62.0d
5803	VC-EL-AP6-2920	Install Elev. Doors - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	3.0d	4-Aug-28	8-Aug-28	62.0d
5804	VC-EL-AP6-2910	Install Elev. Equip. in Pit - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	4-Aug-28	7-Aug-28	62.0d
5805	VC-EL-AP6-2930	Install Elev. Cab - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	9-Aug-28	15-Aug-28	62.0d
5806	VC-EL-AP6-2940	Connect Elevator Elec. Equip - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	16-Aug-28	22-Aug-28	62.0d
5807	VC-EL-AP6-2540	Grout Elevator Door Frames - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	23-Aug-28	29-Aug-28	62.0d
5808	VC-EL-AP6-2590	Install Elev. Flooring - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	23-Aug-28	24-Aug-28	65.0d
5809	VC-EL-AP6-2620	Grout Elevator Sills - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	30-Aug-28	6-Sep-28	62.0d
5810	VC-EL-AP6-2950	Set Elev. Fronts & Call Boxes - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	7-Sep-28	13-Sep-28	62.0d
5811	VC-EL-AP6-2550	Remove Elevator Safety Rail/Net - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	14-Sep-28	15-Sep-28	62.0d
5812	VC-EL-AP6-2440	Elec. Run Time for Final Connections - Service (#8) Elevator Cabs/Shaft - INTR ...	5.0d	18-Sep-28	22-Sep-28	62.0d
5813	VC-EL-AP6-2450	Install Fire Alarm Trim - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	3.0d	25-Sep-28	27-Sep-28	62.0d
5814	VC-EL-AP6-2610	Install Cameras - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	25-Sep-28	29-Sep-28	64.0d
5815	VC-EL-AP6-2570	Install Pit Ladder - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	28-Sep-28	29-Sep-28	62.0d
5816	VC-EL-AP6-2560	Install Sump Pump & Final Grate Cover - Service (#8) Elevator Cabs/Shaft - INT...	2.0d	2-Oct-28	3-Oct-28	62.0d
5817	VC-EL-AP6-2460	Adjust/Test Elev. - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	10.0d	4-Oct-28	17-Oct-28	62.0d
5818	VC-EL-AP6-2580	Liftnet/Phone Service Configuration - Service (#8) Elevator Cabs/Shaft - INTR ...	5.0d	18-Oct-28	24-Oct-28	62.0d
5819	VC-EL-AP6-2960	Prepare Elev. Punchlist - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	5.0d	25-Oct-28	31-Oct-28	62.0d
5820	WBS - Service (#8) Elevator Machine Room - INTR - Apron 6		85.0d	10-Apr-28	8-Aug-28	73.0d
5821	VC-EL-AP6-2660	Hang Machine Room Side 1st Layer - Service (#8) Elevator Machine Room - IN...	2.0d	10-Apr-28	11-Apr-28	58.0d
5822	VC-EL-AP6-2670	Inspect 1st Layer - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	12-Apr-28	13-Apr-28	58.0d
5823	VC-EL-AP6-2680	Hang Machine Room Side 2nd Layer - Service (#8) Elevator Machine Room - IN...	2.0d	14-Apr-28	17-Apr-28	58.0d
5824	VC-EL-AP6-2690	Tape/Finish 2 Hr Rated Wall - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	18-Apr-28	24-Apr-28	58.0d
5825	VC-EL-AP6-2700	Frame 2 Hr Rated Lid with Shaft Liner - Service (#8) Elevator Machine Room - I...	2.0d	25-Apr-28	26-Apr-28	58.0d
5826	VC-EL-AP6-2710	Insulate Ceiling - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	27-Apr-28	28-Apr-28	58.0d
5827	VC-EL-AP6-2720	Inspect Ceiling Insulation - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	1-May-28	2-May-28	58.0d
5828	VC-EL-AP6-2750	Hang 1st Layer Ceiling - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	3-May-28	4-May-28	58.0d
5829	VC-EL-AP6-2740	Inspect 1st Layer Ceiling - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	5-May-28	8-May-28	58.0d
5830	VC-EL-AP6-2730	Hang 2nd Layer Ceiling - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	9-May-28	10-May-28	58.0d
5831	VC-EL-AP6-2780	Tape/Finish Ceiling - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	11-May-28	17-May-28	58.0d
5832	VC-EL-AP6-2770	1st Coat Paint Machine Room - Service (#8) Elevator Machine Room - INTR - A...	2.0d	18-May-28	19-May-28	58.0d
5833	VC-EL-AP6-2630	Elec. Wall Rough Elev. Equip. Room - Service (#8) Elevator Machine Room - INT...	3.0d	22-May-28	24-May-28	58.0d
5834	VC-EL-AP6-2800	Install Door & Hardware - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	22-May-28	23-May-28	59.0d
5835	VC-EL-AP6-2760	Set Elev. Controllers - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	24-May-28	31-May-28	59.0d
5836	VC-EL-AP6-2640	Install Elec. OH Elev. Equip. Room - Service (#8) Elevator Machine Room - INTR...	5.0d	25-May-28	1-Jun-28	58.0d
5837	VC-EL-AP6-2790	Install Elev. Pathways/Wire Elev. - Service (#8) Elevator Machine Room - INTR -...	10.0d	2-Jun-28	15-Jun-28	58.0d
5838	VC-EL-AP6-2820	Apply Final Paint - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	16-Jun-28	22-Jun-28	58.0d




	ID	Name	Dur	Start	Finish	TF
5839	VC-EL-AP6-2850	Install Fire Extinguisher & Cabinet - Service (#8) Elevator Machine Room - INTR...	5.0d	23-Jun-28	29-Jun-28	90.0d
5840	VC-EL-AP6-2860	Install Fire Alarm Trim - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	23-Jun-28	29-Jun-28	58.0d
5841	VC-EL-AP6-2870	Low Voltage Trim Out - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	23-Jun-28	29-Jun-28	58.0d
5842	VC-EL-AP6-2810	Install FCUs-1-6210 - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	30-Jun-28	7-Jul-28	58.0d
5843	VC-EL-AP6-2830	Seal Concrete Floor - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	30-Jun-28	7-Jul-28	90.0d
5844	VC-EL-AP6-2840	Install Rubber Base - Service (#8) Elevator Machine Room - INTR - AP 6	5.0d	10-Jul-28	14-Jul-28	90.0d
5845	VC-EL-AP6-2970	FCU Start Up - Service (#8) Elevator Machine Room - INTR - AP 6	2.0d	7-Aug-28	8-Aug-28	38.0d
5846	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 7		276.0d	13-May-27	13-Jun-28	94.0d
5847	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 7		252.0d	13-May-27	9-May-28	64.0d
5848	WBS - Overall Rough-in - INTR - Apron 7		252.0d	13-May-27	9-May-28	64.0d
5849	RI-AP7-1280	Layout Walls/Top Track - Overall Rough-in - INTR - AP 7	10.0d	13-May-27	26-May-27	33.0d
5850	RI-AP7-1290	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 7	2.0d	27-May-27	28-May-27	78.0d
5851	RI-AP7-1300	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 7	3.0d	1-Jun-27	3-Jun-27	78.0d
5852	RI-AP7-1310	Install Plumbing Hangers - Overall Rough-in - INTR - AP 7	5.0d	4-Jun-27	10-Jun-27	78.0d
5853	RI-AP7-1320	Install Elec. Hangers - Overall Rough-in - INTR - AP 7	2.0d	11-Jun-27	14-Jun-27	78.0d
5854	RI-AP7-1330	Install Fireproofing - Overall Rough-in - INTR - AP 7	10.0d	15-Jul-27	28-Jul-27	57.0d
5855	RI-AP7-1340	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 7	18.0d	3-Sep-27	29-Sep-27	31.0d
5856	RI-AP7-1360	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 7	20.0d	13-Sep-27	8-Oct-27	31.0d
5857	RI-AP7-2470	Install Plumbing Insulation - Overall Rough-in - INTR - AP 7	6.0d	30-Sep-27	7-Oct-27	102.0d
5858	RI-AP7-2460	Install Duct Insulation - Overall Rough-in - INTR - AP 7	10.0d	11-Oct-27	22-Oct-27	86.0d
5859	RI-AP7-2480	Install CHW OH Rough-in - Overall - INTR - AP 7	8.0d	11-Oct-27	20-Oct-27	31.0d
5860	RI-AP7-2490	Install CHW Insulation - Overall Rough-in INTR - AP 7	5.0d	25-Oct-27	29-Oct-27	86.0d
5861	RI-AP7-1380	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 7	20.0d	7-Dec-27	5-Jan-28	0.0d
5862	RI-AP7-1390	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 7	10.0d	6-Jan-28	19-Jan-28	0.0d
5863	RI-AP7-2520	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 7	20.0d	6-Jan-28	2-Feb-28	0.0d
5864	RI-AP7-1370	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 7	10.0d	20-Jan-28	2-Feb-28	0.0d
5865	RI-AP7-1400	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 7	10.0d	3-Feb-28	16-Feb-28	2.0d
5866	RI-AP7-1440	Install HM Door Frames - Overall Rough-in - INTR - AP 7	3.0d	3-Feb-28	7-Feb-28	9.0d
5867	RI-AP7-1410	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 7	5.0d	3-Feb-28	9-Feb-28	0.0d
5868	RI-AP7-2530	Pull BAS Cable - Overall Rough-in - INTR - AP 7	20.0d	3-Feb-28	1-Mar-28	39.0d
5869	RI-AP7-1430	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7.0d	10-Feb-28	18-Feb-28	0.0d
5870	RI-AP7-1450	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 7	10.0d	21-Feb-28	3-Mar-28	0.0d
5871	RI-AP7-2500	Install LTNG for Future Tenant Spaces - Overall Rough-in - INTR - AP 7	15.0d	6-Mar-28	24-Mar-28	1.0d
5872	RI-AP7-1420	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 7	7.0d	27-Mar-28	4-Apr-28	1.0d
5873	RI-AP7-1460	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 7	5.0d	5-Apr-28	11-Apr-28	36.0d
5874	RI-AP7-2510	Pull & Terminate Low Volt- Overall Rough-in - INTR - AP 7	20.0d	12-Apr-28	9-May-28	64.0d
5875	WBS - Infrastructure, MEPTFP Rough-in & Equipment - IDF - Apron 7		266.0d	27-May-27	13-Jun-28	94.0d
5876	WBS - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - Apron 7		217.0d	27-May-27	4-Apr-28	132.0d
5877	RI-AP7-IDF-1590	Layout Walls/Top Track - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	27-May-27	3-Jun-27	158.0d
5878	RI-AP7-IDF-1600	Install Fire Sprinkler Hangers - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	4-Jun-27	7-Jun-27	161.0d
5879	RI-AP7-IDF-1630	Install Elec. Hangers - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	8-Jun-27	9-Jun-27	161.0d
5880	RI-AP7-IDF-1640	Install Fireproofing - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	10-Jun-27	11-Jun-27	161.0d

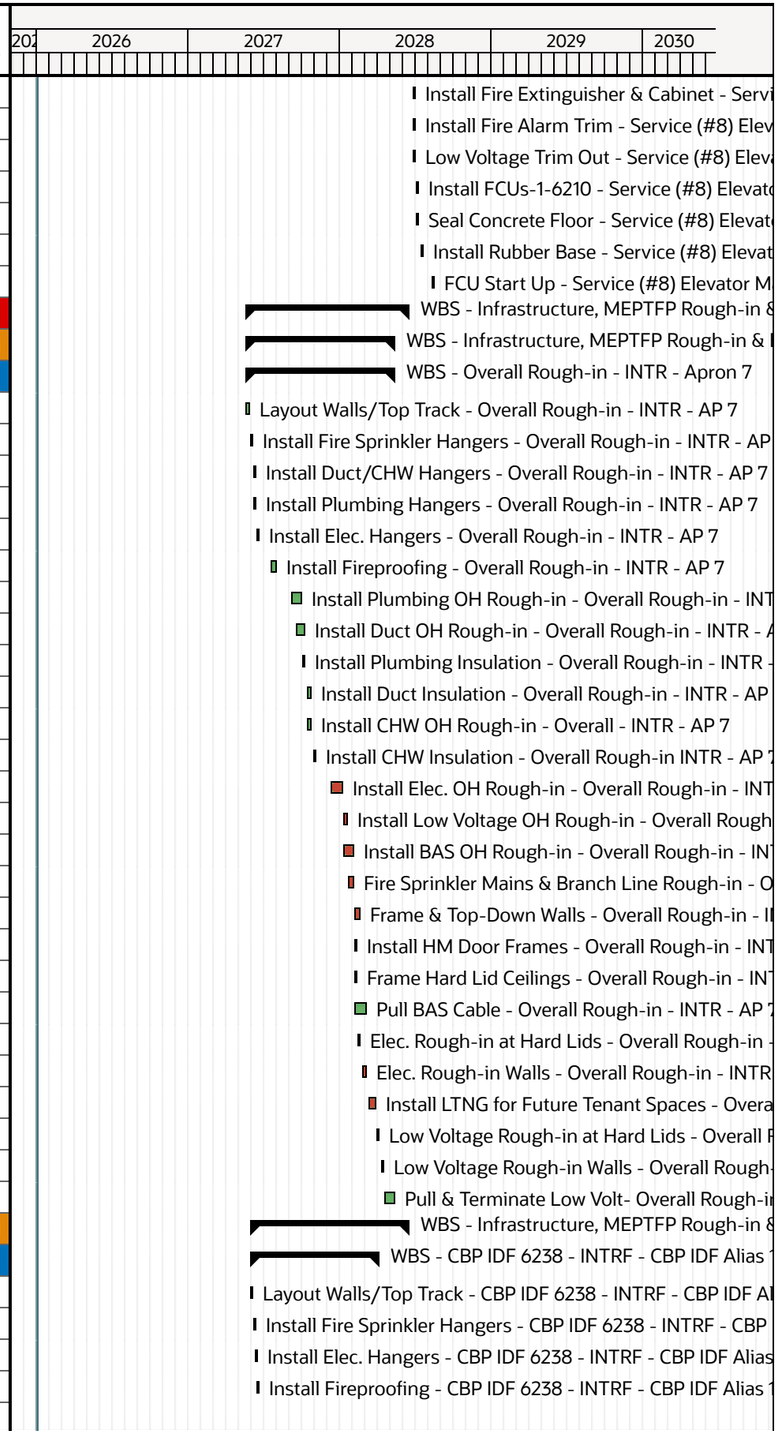


	ID	Name	Dur	Start	Finish	TF
5881	RI-AP7-IDF-1680	Fire Sprinkler Mains & Branch Line Rough-in - CBP IDF 6238 - INTRF - CBP IDF ...	4.0d	14-Jun-27	17-Jun-27	217.0d
5882	RI-AP7-IDF-1700	Install Elec. OH Rough-in - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	7.0d	21-Jun-27	29-Jun-27	216.0d
5883	RI-AP7-IDF-1690	Install Low Voltage OH Rough-in - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - ...	7.0d	30-Jun-27	9-Jul-27	216.0d
5884	RI-AP7-IDF-1710	Frame & Top-Down Walls - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	4.0d	12-Jul-27	15-Jul-27	216.0d
5885	RI-AP7-IDF-1720	Install HM Door Frames - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	12-Jul-27	14-Jul-27	216.0d
5886	RI-AP7-IDF-1740	Elec. Rough-in Walls - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	12-Jul-27	14-Jul-27	219.0d
5887	RI-AP7-IDF-1730	Low Voltage Rough-in Walls - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	15-Jul-27	19-Jul-27	216.0d
5888	FN-AP7-IDF-1630	Install Door & Hardware - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	16-Jul-27	19-Jul-27	284.0d
5889	RI-AP7-IDF-1735	Low Voltage/Elec. in Wall Inspection (COT) - CBP IDF 6238 - INTRF - CBP IDF Al...	2.0d	20-Jul-27	21-Jul-27	216.0d
5890	RI-AP7-IDF-1560	Patch Fireproofing - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	22-Jul-27	28-Jul-27	216.0d
5891	FN-AP7-IDF-1570	Hang, Tape & Finish Drywall - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	20-Dec-27	27-Dec-27	117.0d
5892	FN-AP7-IDF-1580	Prime & First Coat - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	28-Dec-27	29-Dec-27	135.0d
5893	FN-AP7-IDF-1585	Firestopping - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	30-Dec-27	4-Jan-28	135.0d
5894	FN-AP7-IDF-2540	Install FCUs-1-6238 - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	30-Dec-27	6-Jan-28	154.0d
5895	FN-AP7-IDF-1587	Install Tech Room Backerboard - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - A...	2.0d	5-Jan-28	6-Jan-28	135.0d
5896	FN-AP7-IDF-1590	Set Racks - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	10.0d	7-Jan-28	20-Jan-28	135.0d
5897	FN-AP7-IDF-1600	Install Ladder Rack - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	21-Jan-28	25-Jan-28	135.0d
5898	FN-AP7-IDF-1610	Pull & Terminate Fiber - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	10.0d	26-Jan-28	8-Feb-28	135.0d
5899	FN-AP7-IDF-1615	Trim-Out Low Voltage - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	9-Feb-28	15-Feb-28	135.0d
5900	FN-AP7-IDF-1645	Low Voltage Testing - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	3.0d	16-Feb-28	18-Feb-28	135.0d
5901	FN-AP7-IDF-1640	Install Flooring - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	21-Feb-28	22-Feb-28	135.0d
5902	FN-AP7-IDF-2630	Install Rubber Base - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	23-Feb-28	29-Feb-28	135.0d
5903	FN-AP7-IDF-1620	Apply Final Paint - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	5.0d	1-Mar-28	7-Mar-28	135.0d
5904	FN-AP7-IDF-2570	FCU Start Up - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	2.0d	9-Mar-28	10-Mar-28	132.0d
5905	FN-AP7-IDF-2220	Owner's Acceptance Walkthrough - CBP IDF 6238 - INTRF - CBP IDF Alias 103 -...	2.0d	13-Mar-28	14-Mar-28	132.0d
5906	FN-AP7-IDF-2230	Owner Equip. Install - CBP IDF 6238 - INTRF - CBP IDF Alias 103 - AP 7	15.0d	15-Mar-28	4-Apr-28	132.0d
5907	WBS - HCAA IDF 6194 - INTRF - Alias ASD 01380 - Apron 7		263.0d	2-Jun-27	13-Jun-28	94.0d
5908	RI-AP7-IDF-2120	Layout Walls/Top Track - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	2-Jun-27	8-Jun-27	158.0d
5909	RI-AP7-IDF-2220	Install Fire Sprinkler Hangers - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	9-Jun-27	10-Jun-27	158.0d
5910	RI-AP7-IDF-2240	Install Elec. Hangers - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	11-Jun-27	14-Jun-27	158.0d
5911	RI-AP7-IDF-2200	Install Fireproofing - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	15-Jun-27	16-Jun-27	158.0d
5912	RI-AP7-IDF-2160	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6194 - INTRF - Alias ...	4.0d	17-Jun-27	22-Jun-27	216.0d
5913	RI-AP7-IDF-2140	Install Elec. OH Rough-in - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	10.0d	24-Jun-27	8-Jul-27	215.0d
5914	RI-AP7-IDF-2180	Install Low Voltage OH Rough-in - HCAA IDF 6194 - INTRF - Alias ASD 01380 -...	3.0d	9-Jul-27	13-Jul-27	215.0d
5915	RI-AP7-IDF-2130	Frame & Top-Down Walls - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	4.0d	14-Jul-27	19-Jul-27	215.0d
5916	RI-AP7-IDF-2190	Install HM Door Frames - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	14-Jul-27	16-Jul-27	216.0d
5917	FN-AP7-IDF-2310	Install Door & Hardware - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	19-Jul-27	20-Jul-27	294.0d
5918	RI-AP7-IDF-2250	Elec. Rough-in Walls - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	20-Jul-27	22-Jul-27	215.0d
5919	RI-AP7-IDF-2260	Low Voltage Rough-in Walls - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	23-Jul-27	27-Jul-27	215.0d
5920	RI-AP7-IDF-2280	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6194 - INTRF - Alias AS...	2.0d	28-Jul-27	29-Jul-27	215.0d
5921	RI-AP7-IDF-2275	Patch Fireproofing - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	30-Jul-27	5-Aug-27	215.0d
5922	FN-AP7-IDF-2280	Hang, Tape & Finish Drywall - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	28-Dec-27	4-Jan-28	117.0d

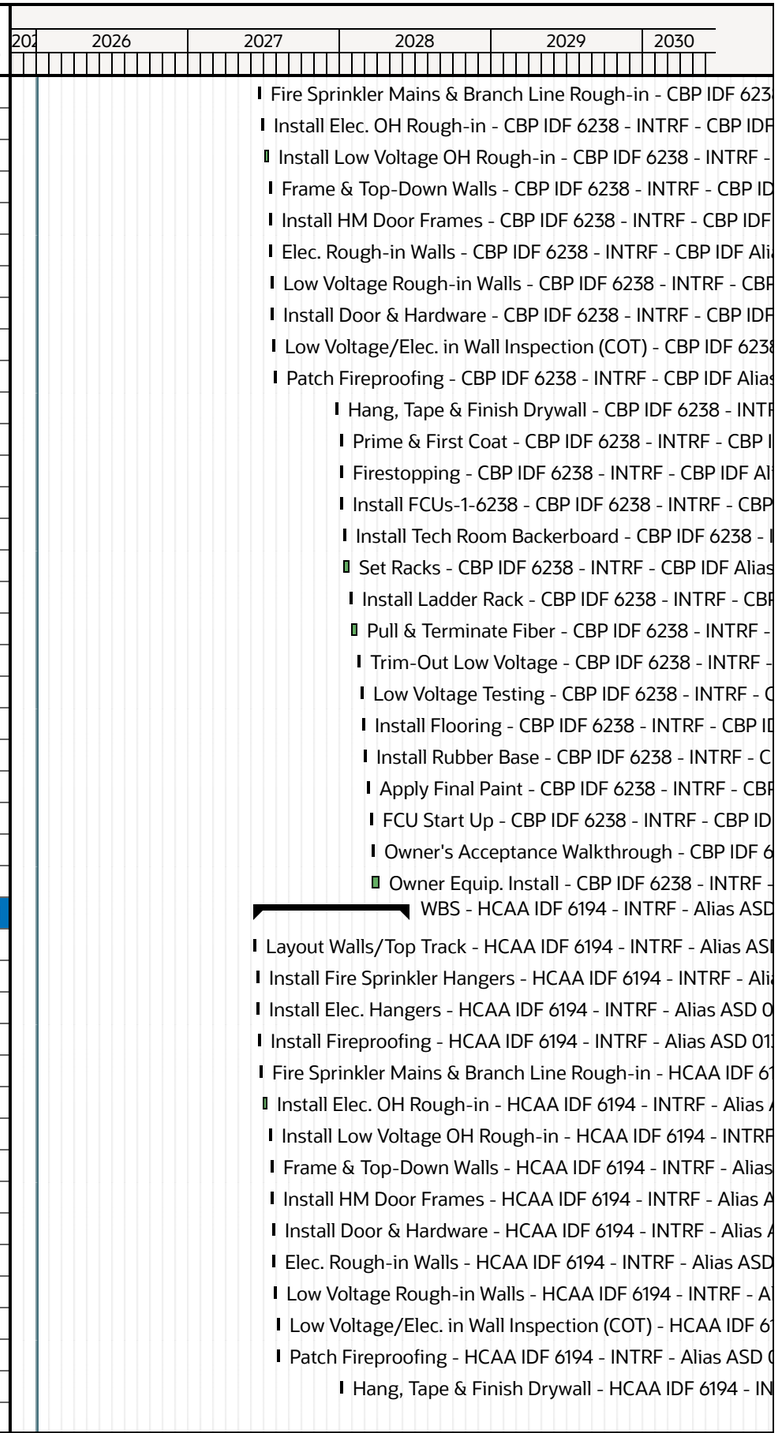


	ID	Name	Dur	Start	Finish	TF
5923	FN-AP7-IDF-2290	Prime & First Coat - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	5-Jan-28	6-Jan-28	141.0d
5924	FN-AP7-IDF-2330	Firestopping - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	7-Jan-28	11-Jan-28	141.0d
5925	FN-AP7-IDF-2550	Install FCUs-1-6194 - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	7-Jan-28	13-Jan-28	147.0d
5926	FN-AP7-IDF-2340	Install Tech Room Backerboard - HCAA IDF 6194 - INTRF - Alias ASD 01380 - A...	2.0d	12-Jan-28	13-Jan-28	141.0d
5927	FN-AP7-IDF-2260	Set Racks - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	10.0d	14-Jan-28	27-Jan-28	141.0d
5928	FN-AP7-IDF-2250	Install Ladder Rack - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	28-Jan-28	1-Feb-28	141.0d
5929	FN-AP7-IDF-2240	Pull & Terminate Fiber - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	10.0d	2-Feb-28	15-Feb-28	141.0d
5930	FN-AP7-IDF-2600	Pull & Terminate Fiber for PBB D53, D54, D55 - HCAA IDF 6194 - INTRF - Alias ...	10.0d	2-Feb-28	15-Feb-28	141.0d
5931	FN-AP7-IDF-2350	Trim-Out Low Voltage - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	16-Feb-28	22-Feb-28	141.0d
5932	FN-AP7-IDF-2360	Low Voltage Testing - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	3.0d	23-Feb-28	25-Feb-28	141.0d
5933	FN-AP7-IDF-2320	Install Flooring - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	2.0d	28-Feb-28	29-Feb-28	141.0d
5934	FN-AP7-IDF-2620	Install Rubber Base - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	1-Mar-28	7-Mar-28	141.0d
5935	FN-AP7-IDF-2300	Apply Final Paint - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	8-Mar-28	14-Mar-28	141.0d
5936	FN-AP7-IDF-2580	FCU Start Up - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	5.0d	9-Mar-28	15-Mar-28	140.0d
5937	FN-AP7-IDF-2370	Owner's Acceptance Walkthrough - HCAA IDF 6194 - INTRF - Alias ASD 01380 ...	2.0d	16-Mar-28	17-Mar-28	140.0d
5938	FN-AP7-IDF-2380	Owner Equipment Install - HCAA IDF 6194 - INTRF - Alias ASD 01380 - AP 7	15.0d	23-May-28	13-Jun-28	94.0d
5939	WBS - Tenant IDF 6193 - INTRF - Alias ASD 01381 - Apron 7		220.0d	7-Jun-27	17-Apr-28	134.0d
5940	RI-AP7-IDF-2290	Layout Walls/Top Track - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	7-Jun-27	11-Jun-27	164.0d
5941	RI-AP7-IDF-2300	Install Fire Sprinkler Hangers - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	14-Jun-27	15-Jun-27	164.0d
5942	RI-AP7-IDF-2330	Install Elec. Hangers - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	16-Jun-27	17-Jun-27	217.0d
5943	RI-AP7-IDF-2340	Install Fireproofing - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	18-Jun-27	21-Jun-27	217.0d
5944	RI-AP7-IDF-2380	Fire Sprinkler Mains & Branch Line Rough-in - Tenant IDF 6193 - INTRF - Alias ...	4.0d	22-Jun-27	25-Jun-27	218.0d
5945	RI-AP7-IDF-2390	Install Elec. OH Rough-in - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	10.0d	29-Jun-27	13-Jul-27	217.0d
5946	RI-AP7-IDF-2400	Install Low Voltage OH Rough-in - Tenant IDF 6193 - INTRF - Alias ASD 01381 ...	3.0d	14-Jul-27	16-Jul-27	217.0d
5947	RI-AP7-IDF-2410	Frame & Top-Down Walls - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	4.0d	19-Jul-27	22-Jul-27	217.0d
5948	RI-AP7-IDF-2420	Install HM Door Frames - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	19-Jul-27	21-Jul-27	218.0d
5949	RI-AP7-IDF-2430	Elec. Rough-in Walls - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	23-Jul-27	27-Jul-27	217.0d
5950	RI-AP7-IDF-2440	Low Voltage Rough-in Walls - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	28-Jul-27	30-Jul-27	217.0d
5951	RI-AP7-IDF-2450	Low Voltage/Elec. in Wall Inspection (COT) - Tenant IDF 6193 - INTRF - Alias A...	2.0d	2-Aug-27	3-Aug-27	217.0d
5952	RI-AP7-IDF-2395	Patch Fireproofing - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	4-Aug-27	10-Aug-27	217.0d
5953	FN-AP7-IDF-2400	Hang, Tape & Finish Drywall - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	5-Jan-28	11-Jan-28	117.0d
5954	FN-AP7-IDF-2410	Prime & First Coat - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	12-Jan-28	13-Jan-28	134.0d
5955	FN-AP7-IDF-2420	Firestopping - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	14-Jan-28	18-Jan-28	134.0d
5956	FN-AP7-IDF-2560	Install FCUs-1-6193 - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	14-Jan-28	20-Jan-28	142.0d
5957	FN-AP7-IDF-2430	Install Tech Room Backerboard - Tenant IDF 6193 - INTRF - Alias ASD 01381 - ...	2.0d	19-Jan-28	20-Jan-28	134.0d
5958	FN-AP7-IDF-2490	Install Door & Hardware - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	21-Jan-28	24-Jan-28	134.0d
5959	FN-AP7-IDF-2440	Set Racks - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	10.0d	25-Jan-28	7-Feb-28	134.0d
5960	FN-AP7-IDF-2450	Install Ladder Rack - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	8-Feb-28	10-Feb-28	134.0d
5961	FN-AP7-IDF-2460	Pull & Terminate Fiber - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	10.0d	11-Feb-28	24-Feb-28	134.0d
5962	FN-AP7-IDF-2470	Trim-Out Low Voltage - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	25-Feb-28	2-Mar-28	134.0d
5963	FN-AP7-IDF-2510	Low Voltage Testing - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	3.0d	3-Mar-28	7-Mar-28	134.0d
5964	FN-AP7-IDF-2500	Install Flooring - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	8-Mar-28	9-Mar-28	134.0d

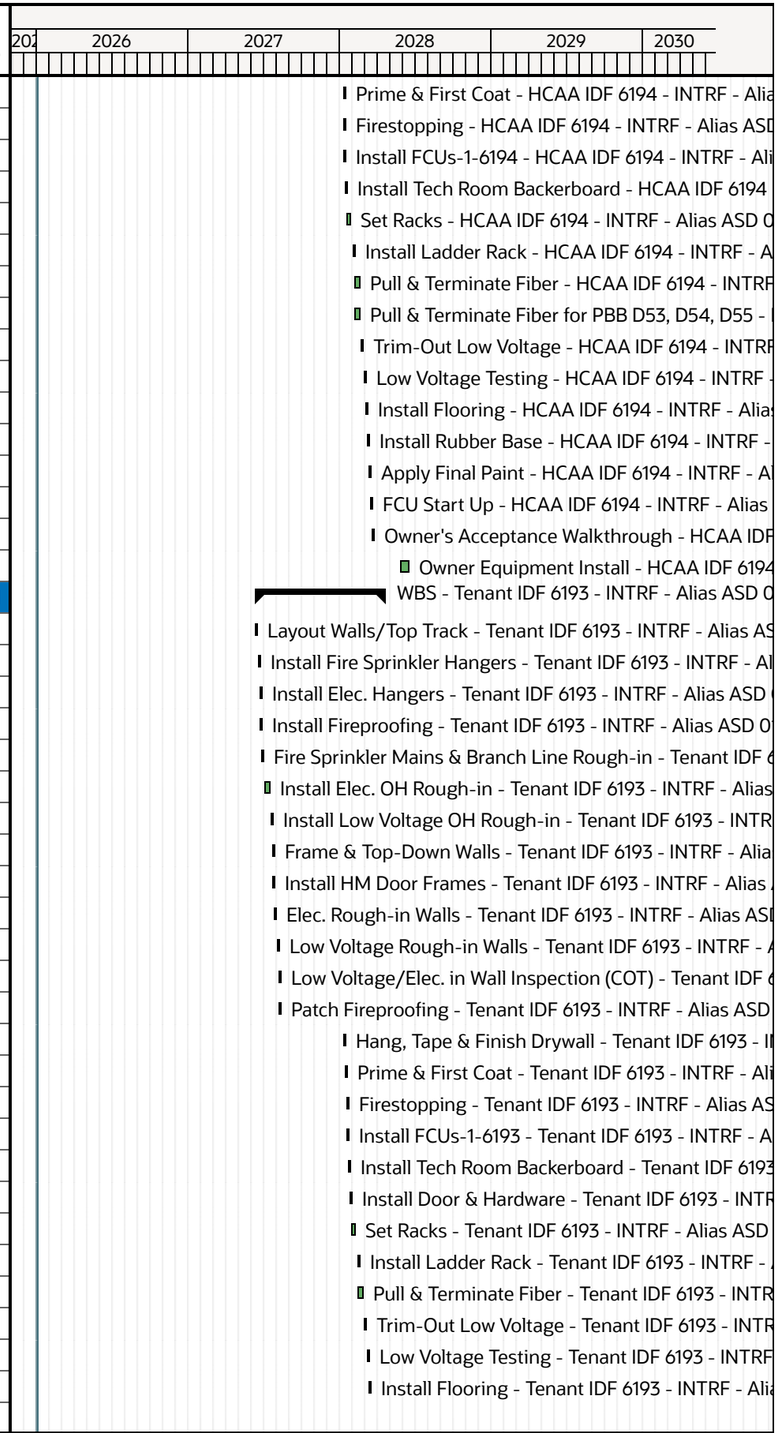

	ID	Name	Dur	Start	Finish	TF
5965	FN-AP7-IDF-2590	FCU Start Up - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	2.0d	9-Mar-28	10-Mar-28	143.0d
5966	FN-AP7-IDF-2610	Install Rubber Base - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	10-Mar-28	16-Mar-28	134.0d
5967	FN-AP7-IDF-2480	Apply Final Paint - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	5.0d	17-Mar-28	23-Mar-28	134.0d
5968	FN-AP7-IDF-2520	Owner's Acceptance Walkthrough - Tenant IDF 6193 - INTRF - Alias ASD 0138...	2.0d	24-Mar-28	27-Mar-28	134.0d
5969	FN-AP7-IDF-2530	Owner Equipment Install - Tenant IDF 6193 - INTRF - Alias ASD 01381 - AP 7	15.0d	28-Mar-28	17-Apr-28	134.0d
5970	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Electrical - Apron 7		29.0d	27-May-27	8-Jul-27	53.0d
5971	WBS - Distribution/Electrical Room #6197 - INTRF - Apron 7		29.0d	27-May-27	8-Jul-27	53.0d
5972	RI-AP7-ER-810	Layout Walls/Top Track - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	27-May-27	3-Jun-27	33.0d
5973	RI-AP7-ER-812	Elec. Layout for Conduit Windows (Pre Framing) - Dist. Elec. Room 6197 - INTR...	2.0d	2-Jun-27	3-Jun-27	33.0d
5974	RI-AP7-ER-820	Install Fire Sprinkler Hangers - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	4-Jun-27	7-Jun-27	33.0d
5975	RI-AP7-ER-840	Install Elec. Hangers - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	8-Jun-27	9-Jun-27	33.0d
5976	RI-AP7-ER-850	Install Fireproofing - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	10-Jun-27	11-Jun-27	33.0d
5977	RI-AP7-ER-860	Fire Sprinkler Mains & Branch Line Rough-in - Dist. Elec. Room 6197 - INTRF - ...	5.0d	14-Jun-27	18-Jun-27	33.0d
5978	RI-AP7-ER-890	Frame & Top-Down Walls - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	21-Jun-27	22-Jun-27	33.0d
5979	RI-AP7-ER-910	Install HM Door Frames - Dist. Elec. Room 6197 - INTRF - AP 7	3.0d	21-Jun-27	23-Jun-27	33.0d
5980	RI-AP7-ER-814	Elec. Layout-Panel Backing & Housekeeping Pads (Post Framing) - Dist. Elec. R...	5.0d	23-Jun-27	29-Jun-27	57.0d
5981	RI-AP7-ER-920	Elec. Rough-in Walls - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	24-Jun-27	30-Jun-27	33.0d
5982	RI-AP7-ER-830	Pour Equip. Pads - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	30-Jun-27	1-Jul-27	57.0d
5983	RI-AP7-ER-940	Patch Fireproofing - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	1-Jul-27	8-Jul-27	33.0d
5984	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mechanical - Apron 7		154.0d	18-May-27	27-Dec-27	144.0d
5985	WBS - Mechanical Room - INTR - Apron 7		154.0d	18-May-27	27-Dec-27	144.0d
5986	RI-AP7-MR-370	Layout Walls/Top Track - Mech. Room - INTR - AP 7	5.0d	18-May-27	24-May-27	54.0d
5987	RI-AP7-MR-385	Pour Equip. Pads - Mech. Room - INTR - AP 7	2.0d	25-May-27	26-May-27	286.0d
5988	RI-AP7-MR-395	Install Fire Sprinkler Hangers - Mech. Room - INTR - AP 7	2.0d	25-May-27	26-May-27	54.0d
5989	RI-AP7-MR-580	Set Mech. Equip. - Mech. Room - INTR - AP 7	5.0d	27-May-27	3-Jun-27	286.0d
5990	RI-AP7-MR-400	Install Duct/CHW Hangers - Mech. Room - INTR - AP 7	4.0d	27-May-27	2-Jun-27	54.0d
5991	RI-AP7-MR-410	Install Plumbing Hangers - Mech. Room - INTR - AP 7	2.0d	3-Jun-27	4-Jun-27	54.0d
5992	RI-AP7-MR-420	Install Elec. Hangers - Mech. Room - INTR - AP 7	2.0d	7-Jun-27	8-Jun-27	54.0d
5993	RI-AP7-MR-430	Install Fireproofing - Mech. Room - INTR - AP 7	2.0d	9-Jun-27	10-Jun-27	54.0d
5994	RI-AP7-MR-440	Install Plumbing OH Rough-in - Mech. Room - INTR - AP 7	5.0d	11-Jun-27	17-Jun-27	54.0d
5995	RI-AP7-MR-460	Install Duct OH Rough-in - Mech. Room - INTR - AP 7	15.0d	18-Jun-27	9-Jul-27	54.0d
5996	RI-AP7-MR-1170	Install Plumbing Insulation - Mech. Room - INTR - AP 7	2.0d	18-Jun-27	21-Jun-27	115.0d
5997	RI-AP7-MR-1120	Install CHW OH Rough-in - Mech. Room - INTR - AP 7	15.0d	12-Jul-27	30-Jul-27	54.0d
5998	RI-AP7-MR-1160	Install Duct Insulation - Mech. Room - INTR - AP 7	5.0d	12-Jul-27	16-Jul-27	97.0d
5999	RI-AP7-MR-470	Fire Sprinkler Mains & Branch Line Rough-in - Mech. Room - INTR - AP 7	10.0d	2-Aug-27	13-Aug-27	54.0d
6000	RI-AP7-MR-1130	Install CHW Insulation - Mech. Room - INTR - AP 7	5.0d	2-Aug-27	6-Aug-27	82.0d
6001	RI-AP7-MR-490	Install Elec. OH Rough-in - Mech. Room - INTR - AP 7	10.0d	16-Aug-27	27-Aug-27	54.0d
6002	RI-AP7-MR-500	Frame & Top-Down Walls - Mech. Room - INTR - AP 7	10.0d	30-Aug-27	13-Sep-27	54.0d
6003	RI-AP7-MR-520	Install HM Door Frames - Mech. Room - INTR - AP 7	3.0d	30-Aug-27	1-Sep-27	61.0d
6004	RI-AP7-MR-450	Install Mech. Equip. - Mech. Room - INTR - AP 7	10.0d	30-Aug-27	13-Sep-27	57.0d
6005	RI-AP7-MR-550	Elec. Rough-in Walls - Mech. Room - INTR - AP 7	3.0d	14-Sep-27	16-Sep-27	54.0d
6006	RI-AP7-MR-458	Pull & Terminate to Mech. Equip. - Mech. Room - INTR - AP 7	10.0d	6-Dec-27	17-Dec-27	0.0d

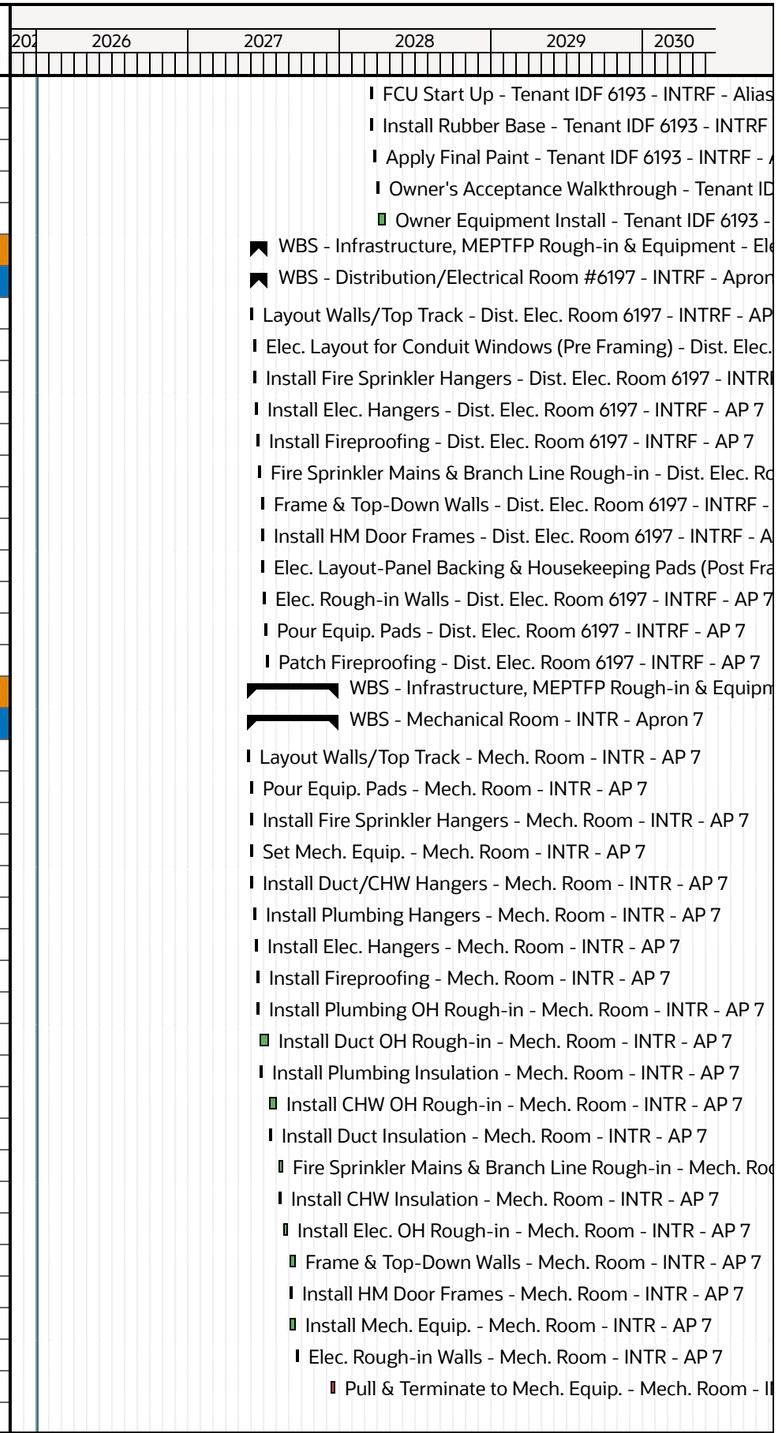


	ID	Name	Dur	Start	Finish	TF
6007	RI-AP7-MR-570	Patch Fireproofing - Mech. Room - INTR - AP 7	5.0d	20-Dec-27	27-Dec-27	0.0d
6008	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 8		392.0d	29-Mar-27	10-Oct-28	77.0d
6009	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 8		237.0d	29-Mar-27	2-Mar-28	57.0d
6010	WBS - Overall Rough-in - INTR - Apron 8		237.0d	29-Mar-27	2-Mar-28	57.0d
6011	RI-AP8-1790	Layout Walls/Top Track - Overall Rough-in - INTR - AP 8	10.0d	29-Mar-27	9-Apr-27	91.0d
6012	RI-AP8-1800	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 8	2.0d	12-Apr-27	13-Apr-27	91.0d
6013	RI-AP8-1810	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 8	2.0d	14-Apr-27	15-Apr-27	91.0d
6014	RI-AP8-1820	Install Plumbing Hangers - Overall Rough-in - INTR - AP 8	3.0d	16-Apr-27	20-Apr-27	91.0d
6015	RI-AP8-1830	Install Elec. Hangers - Overall Rough-in - INTR - AP 8	2.0d	21-Apr-27	22-Apr-27	91.0d
6016	RI-AP8-3030	Install Signage Supports - Overall Rough-in - INTR - AP 8	3.0d	23-Apr-27	27-Apr-27	91.0d
6017	RI-AP8-1840	Install Fireproofing - Overall Rough-in - INTR - AP 8	10.0d	16-Jun-27	29-Jun-27	57.0d
6018	RI-AP8-1860	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 8	20.0d	6-Aug-27	2-Sep-27	31.0d
6019	RI-AP8-1870	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 8	15.0d	13-Aug-27	2-Sep-27	34.0d
6020	RI-AP8-2970	Install Plumbing Insulation - Overall Rough-in - INTR - AP 8	5.0d	3-Sep-27	10-Sep-27	91.0d
6021	RI-AP8-3020	Install Duct Insulation - Overall Rough-in INTR - AP 8	10.0d	3-Sep-27	17-Sep-27	86.0d
6022	RI-AP8-3010	Install CHW OH Rough-in - Overall Rough-in - INTR - AP8	5.0d	3-Sep-27	10-Sep-27	76.0d
6023	RI-AP8-1880	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 8	10.0d	13-Sep-27	24-Sep-27	34.0d
6024	RI-AP8-3000	Install CHW Insulation - Overall Rough-in INTR - AP 8	3.0d	13-Sep-27	15-Sep-27	76.0d
6025	RI-AP8-1900	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 8	20.0d	5-Nov-27	6-Dec-27	0.0d
6026	RI-AP8-1890	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 8	10.0d	7-Dec-27	20-Dec-27	10.0d
6027	RI-AP8-3060	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 8	20.0d	7-Dec-27	5-Jan-28	0.0d
6028	RI-AP8-1910	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 8	10.0d	6-Jan-28	19-Jan-28	12.0d
6029	RI-AP8-1950	Install HM Door Frames - Overall Rough-in - INTR - AP 8	3.0d	6-Jan-28	10-Jan-28	12.0d
6030	RI-AP8-1920	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 8	5.0d	6-Jan-28	12-Jan-28	0.0d
6031	RI-AP8-3070	Pull BAS Cable - Overall Rough-in - INTR - AP 8	20.0d	6-Jan-28	2-Feb-28	39.0d
6032	RI-AP8-1970	Elec. Rough-in Walls & Columns - Overall Rough-in - INTR - AP 8	10.0d	13-Jan-28	26-Jan-28	3.0d
6033	RI-AP8-1930	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	10.0d	13-Jan-28	26-Jan-28	0.0d
6034	RI-AP8-1960	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 8	3.0d	27-Jan-28	31-Jan-28	0.0d
6035	RI-AP8-1940	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 8	3.0d	27-Jan-28	31-Jan-28	0.0d
6036	RI-AP8-3040	Pull Low Voltage Cabling - Overall Rough-in - INTR - AP 8	15.0d	1-Feb-28	21-Feb-28	57.0d
6037	RI-AP8-3050	Terminate Low Voltage Cabling - Overall Rough-in - INTR - AP 8	8.0d	22-Feb-28	2-Mar-28	57.0d
6038	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - MDF/IDF - Apron 8		284.0d	12-Apr-27	22-May-28	98.0d
6039	WBS - HCAA MDF 6297 - INTRF - Alias ASD 01480 - Apron 8		284.0d	12-Apr-27	22-May-28	82.0d
6040	RI-AP8-MDF-2460	Layout Walls/Top Track - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	12-Apr-27	16-Apr-27	188.0d
6041	RI-AP8-MDF-2470	Install Fire Sprinkler Hangers - HCAA MDF 6297 - INTRF - Alias ASD 01480 - A...	2.0d	19-Apr-27	20-Apr-27	194.0d
6042	RI-AP8-MDF-2500	Install Elec. Hangers - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	21-Apr-27	22-Apr-27	194.0d
6043	RI-AP8-MDF-2510	Install Fireproofing - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	23-Apr-27	26-Apr-27	194.0d
6044	RI-AP8-MDF-2550	Fire Sprinkler Mains & Branch Line Rough-in - HCAA MDF 6297 - INTRF - Alias ...	4.0d	27-Apr-27	30-Apr-27	199.0d
6045	RI-AP8-MDF-2560	Install Elec. OH Rough-in - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	15.0d	4-May-27	24-May-27	198.0d
6046	RI-AP8-MDF-2570	Install Low Voltage OH Rough-in - HCAA MDF 6297 - INTRF - Alias ASD 01480...	3.0d	25-May-27	27-May-27	198.0d
6047	RI-AP8-MDF-2580	Frame & Top-Down Walls - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	4.0d	28-May-27	3-Jun-27	198.0d
6048	RI-AP8-MDF-2590	Install HM Door Frames - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	3.0d	28-May-27	2-Jun-27	199.0d

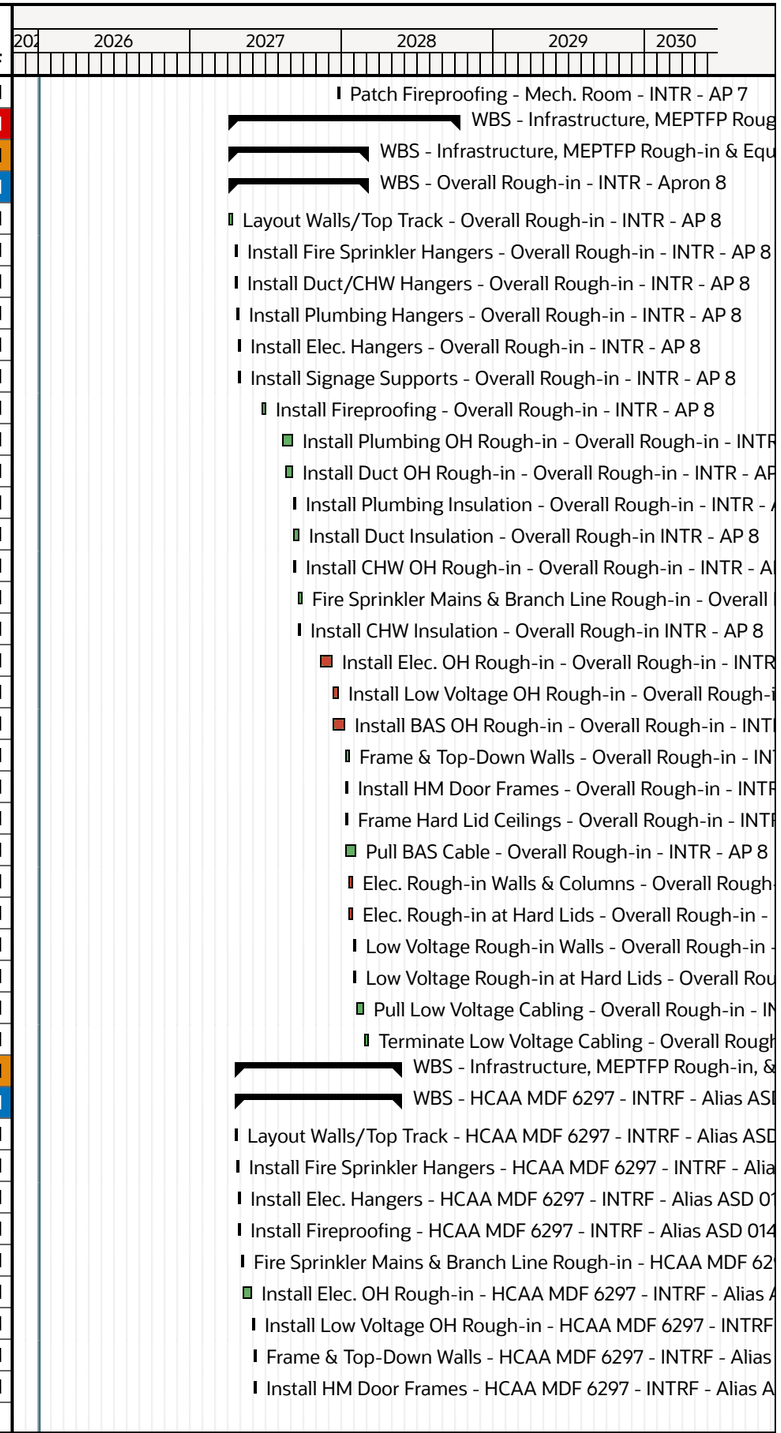


	ID	Name	Dur	Start	Finish	TF
6049	RI-AP8-MDF-2600	Elec. Rough-in Walls - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	3.0d	4-Jun-27	8-Jun-27	198.0d
6050	RI-AP8-MDF-2610	Low Voltage Rough-in Walls - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	4.0d	9-Jun-27	14-Jun-27	198.0d
6051	RI-AP8-MDF-2620	Low Voltage/Elec. in Wall Inspection (COT) - HCAA MDF 6297 - INTRF - Alias A...	2.0d	15-Jun-27	16-Jun-27	198.0d
6052	RI-AP8-MDF-2548	Patch Fireproofing - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	17-Jun-27	23-Jun-27	198.0d
6053	FN-AP8-MDF-2560	Prime & First Coat - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	13-Dec-27	14-Dec-27	85.0d
6054	FN-AP8-MDF-2570	Firestopping - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	3.0d	15-Dec-27	17-Dec-27	85.0d
6055	FN-AP8-MDF-2640	Install Door & Hardware - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	15-Dec-27	16-Dec-27	170.0d
6056	FN-AP8-MDF-2840	Install FCUs-1-6297 - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	15-Dec-27	21-Dec-27	170.0d
6057	FN-AP8-MDF-2580	Install Tech Room Backerboard - HCAA MDF 6297 - INTRF - Alias ASD 01480 - ...	2.0d	20-Dec-27	21-Dec-27	85.0d
6058	FN-AP8-MDF-2590	Set Racks - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	10.0d	22-Dec-27	6-Jan-28	85.0d
6059	FN-AP8-MDF-2600	Install Ladder Rack - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	3.0d	7-Jan-28	11-Jan-28	85.0d
6060	FN-AP8-MDF-2610	Pull & Terminate Fiber - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	10.0d	12-Jan-28	25-Jan-28	85.0d
6061	FN-AP8-MDF-2880	Pull & Terminate Fiber for PBB D52 - HCAA MDF 6297 - INTRF - Alias ASD 014...	4.0d	12-Jan-28	17-Jan-28	135.0d
6062	FN-AP8-MDF-2620	Trim-Out Low Voltage - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	26-Jan-28	1-Feb-28	129.0d
6063	FN-AP8-MDF-2660	Low Voltage Testing - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	3.0d	2-Feb-28	4-Feb-28	129.0d
6064	FN-AP8-MDF-2650	Install Flooring - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	7-Feb-28	8-Feb-28	129.0d
6065	FN-AP8-MDF-2890	Install Rubber Base - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	9-Feb-28	15-Feb-28	129.0d
6066	FN-AP8-MDF-2630	Apply Final Paint - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	5.0d	16-Feb-28	22-Feb-28	129.0d
6067	FN-AP8-MDF-2860	FCU Start Up - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	2.0d	26-Apr-28	27-Apr-28	82.0d
6068	FN-AP8-MDF-2670	Owner's Acceptance Walkthrough - HCAA MDF 6297 - INTRF - Alias ASD 0148...	2.0d	28-Apr-28	1-May-28	82.0d
6069	FN-AP8-MDF-2680	Owner Equip. Install - HCAA MDF 6297 - INTRF - Alias ASD 01480 - AP 8	15.0d	2-May-28	22-May-28	82.0d
6070	WBS - Tenant MDF 6296 - INTRF- Alias ASD 01481 - Apron 8		281.0d	15-Apr-27	22-May-28	94.0d
6071	RI-AP8-MDF-2630	Layout Walls/Top Track - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	15-Apr-27	21-Apr-27	188.0d
6072	RI-AP8-MDF-2640	Install Fire Sprinkler Hangers - Tenant MDF 6296 - INTRF - Alias ASD 01481 - ...	2.0d	22-Apr-27	23-Apr-27	236.0d
6073	RI-AP8-MDF-2670	Install Elec. Hangers - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	26-Apr-27	27-Apr-27	236.0d
6074	RI-AP8-MDF-2680	Install Fireproofing - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	28-Apr-27	29-Apr-27	236.0d
6075	RI-AP8-MDF-2720	Fire Sprinkler Mains & Branch Line Rough-in - Tenant MDF 6296 - INTRF - Alia...	4.0d	30-Apr-27	5-May-27	237.0d
6076	RI-AP8-MDF-2730	Install Elec. OH Rough-in - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	7.0d	7-May-27	17-May-27	236.0d
6077	RI-AP8-MDF-2740	Install Low Voltage OH Rough-in - Tenant MDF 6296 - INTRF - Alias ASD 0148...	3.0d	18-May-27	20-May-27	236.0d
6078	RI-AP8-MDF-2750	Frame & Top-Down Walls - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	4.0d	21-May-27	26-May-27	236.0d
6079	RI-AP8-MDF-2760	Install HM Door Frames - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	3.0d	21-May-27	25-May-27	237.0d
6080	RI-AP8-MDF-2770	Elec. Rough-in Walls - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	3.0d	27-May-27	1-Jun-27	236.0d
6081	RI-AP8-MDF-2780	Low Voltage Rough-in Walls - Tenant MDF 6296 - INTRF - Alias ASD 01481 - A...	3.0d	2-Jun-27	4-Jun-27	236.0d
6082	RI-AP8-MDF-2790	Low Voltage/Elec. in Wall Inspection (COT) - Tenant MDF 6296 - INTRF - Alias ...	2.0d	7-Jun-27	8-Jun-27	236.0d
6083	RI-AP8-MDF-2695	Patch Fireproofing - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	9-Jun-27	15-Jun-27	236.0d
6084	FN-AP8-MDF-2700	Hang, Tape & Finish Drywall - Tenant MDF 6296 - INTRF - Alias ASD 01481 - A...	5.0d	6-Dec-27	10-Dec-27	117.0d
6085	FN-AP8-MDF-2710	Prime & First Coat - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	13-Dec-27	14-Dec-27	141.0d
6086	FN-AP8-MDF-2720	Firestopping - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	3.0d	15-Dec-27	17-Dec-27	141.0d
6087	FN-AP8-MDF-2790	Install Door & Hardware - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	15-Dec-27	16-Dec-27	182.0d
6088	FN-AP8-MDF-2850	Install FCUs-1-6296 - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	15-Dec-27	21-Dec-27	172.0d
6089	FN-AP8-MDF-2730	Install Tech Room Backerboard - Tenant MDF 6296 - INTRF - Alias ASD 01481 ...	2.0d	20-Dec-27	21-Dec-27	141.0d
6090	FN-AP8-MDF-2740	Set Racks - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	10.0d	22-Dec-27	6-Jan-28	141.0d



	ID	Name	Dur	Start	Finish	TF
6091	FN-AP8-MDF-2750	Install Ladder Rack - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	3.0d	7-Jan-28	11-Jan-28	141.0d
6092	FN-AP8-MDF-2760	Pull & Terminate Fiber - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	10.0d	12-Jan-28	25-Jan-28	141.0d
6093	FN-AP8-MDF-2770	Trim-Out Low Voltage - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	26-Jan-28	1-Feb-28	141.0d
6094	FN-AP8-MDF-2810	Low Voltage Testing - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	3.0d	2-Feb-28	4-Feb-28	141.0d
6095	FN-AP8-MDF-2800	Install Flooring - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	7-Feb-28	8-Feb-28	141.0d
6096	FN-AP8-MDF-2900	Install Rubber Base - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	9-Feb-28	15-Feb-28	141.0d
6097	FN-AP8-MDF-2780	Apply Final Paint - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	5.0d	16-Feb-28	22-Feb-28	141.0d
6098	FN-AP8-MDF-2870	FCU Start Up - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	2.0d	26-Apr-28	27-Apr-28	94.0d
6099	FN-AP8-MDF-2820	Owner's Acceptance Walkthrough - Tenant MDF 6296 - INTRF - Alias ASD 014...	2.0d	28-Apr-28	1-May-28	94.0d
6100	FN-AP8-MDF-2830	Owner Equip. Install - Tenant MDF 6296 - INTRF - Alias ASD 01481 - AP 8	15.0d	2-May-28	22-May-28	94.0d
6101	WBS - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - Apron 8		278.0d	20-Apr-27	22-May-28	98.0d
6102	RI-AP8-IDF-2800	Layout Walls/Top Track - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	20-Apr-27	26-Apr-27	188.0d
6103	RI-AP8-IDF-2810	Install Fire Sprinkler Hangers - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	27-Apr-27	28-Apr-27	188.0d
6104	RI-AP8-IDF-2840	Install Elec. Hangers - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	29-Apr-27	30-Apr-27	188.0d
6105	RI-AP8-IDF-2850	Install Fireproofing - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	3-May-27	4-May-27	188.0d
6106	RI-AP8-IDF-2890	Fire Sprinkler Mains & Branch Line Rough-in - CBP IDF 6287 - INTRF - CBP IDF ...	4.0d	5-May-27	10-May-27	236.0d
6107	RI-AP8-IDF-2900	Install Elec. OH Rough-in - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	10.0d	12-May-27	25-May-27	235.0d
6108	RI-AP8-IDF-2910	Install Low Voltage OH Rough-in - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - ...	3.0d	26-May-27	28-May-27	235.0d
6109	RI-AP8-IDF-2920	Frame & Top-Down Walls - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	4.0d	1-Jun-27	4-Jun-27	235.0d
6110	RI-AP8-IDF-2930	Install HM Door Frames - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	1-Jun-27	3-Jun-27	236.0d
6111	RI-AP8-IDF-2940	Elec. Rough-in Walls - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	7-Jun-27	9-Jun-27	235.0d
6112	RI-AP8-IDF-2950	Low Voltage Rough-in Walls - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	10-Jun-27	14-Jun-27	235.0d
6113	RI-AP8-IDF-2960	Low Voltage/Elec. in Wall Inspection (COT) - CBP IDF 6287 - INTRF - CBP IDF Al...	2.0d	15-Jun-27	16-Jun-27	235.0d
6114	RI-AP8-IDF-2845	Patch Fireproofing - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	17-Jun-27	23-Jun-27	235.0d
6115	FN-AP8-IDF-2850	Hang, Tape & Finish Drywall - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	13-Dec-27	17-Dec-27	117.0d
6116	FN-AP8-IDF-2860	Prime & First Coat - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	20-Dec-27	21-Dec-27	140.0d
6117	FN-AP8-IDF-2870	Firestopping - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	22-Dec-27	27-Dec-27	140.0d
6118	FN-AP8-IDF-2940	Install Door & Hardware - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	22-Dec-27	23-Dec-27	181.0d
6119	FN-AP8-IDF-2990	Install FCUs-1-6287 - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	22-Dec-27	29-Dec-27	157.0d
6120	FN-AP8-IDF-2880	Install Tech Room Backerboard - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - A...	2.0d	28-Dec-27	29-Dec-27	140.0d
6121	FN-AP8-IDF-2890	Set Racks - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	10.0d	30-Dec-27	13-Jan-28	140.0d
6122	FN-AP8-IDF-2900	Install Ladder Rack - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	14-Jan-28	18-Jan-28	140.0d
6123	FN-AP8-IDF-2910	Pull & Terminate Fiber - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	10.0d	19-Jan-28	1-Feb-28	140.0d
6124	FN-AP8-IDF-2920	Trim-Out Low Voltage - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	2-Feb-28	8-Feb-28	140.0d
6125	FN-AP8-IDF-2960	Low Voltage Testing - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	3.0d	9-Feb-28	11-Feb-28	140.0d
6126	FN-AP8-IDF-2950	Install Flooring - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	14-Feb-28	15-Feb-28	140.0d
6127	FN-AP8-IDF-3010	Install Rubber Base - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	16-Feb-28	22-Feb-28	140.0d
6128	FN-AP8-IDF-2930	Apply Final Paint - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	5.0d	23-Feb-28	29-Feb-28	140.0d
6129	FN-AP8-IDF-3000	FCU Start Up - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	2.0d	26-Apr-28	27-Apr-28	98.0d
6130	FN-AP8-IDF-2970	Owner's Acceptance Walkthrough - CBP IDF 6287 - INTRF - CBP IDF Alias 102 -...	2.0d	28-Apr-28	1-May-28	98.0d
6131	FN-AP8-IDF-2980	Owner Equipment Install - CBP IDF 6287 - INTRF - CBP IDF Alias 102 - AP 8	15.0d	2-May-28	22-May-28	98.0d
6132	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Electrical - Apron 8		54.0d	12-Apr-27	25-Jun-27	181.0d

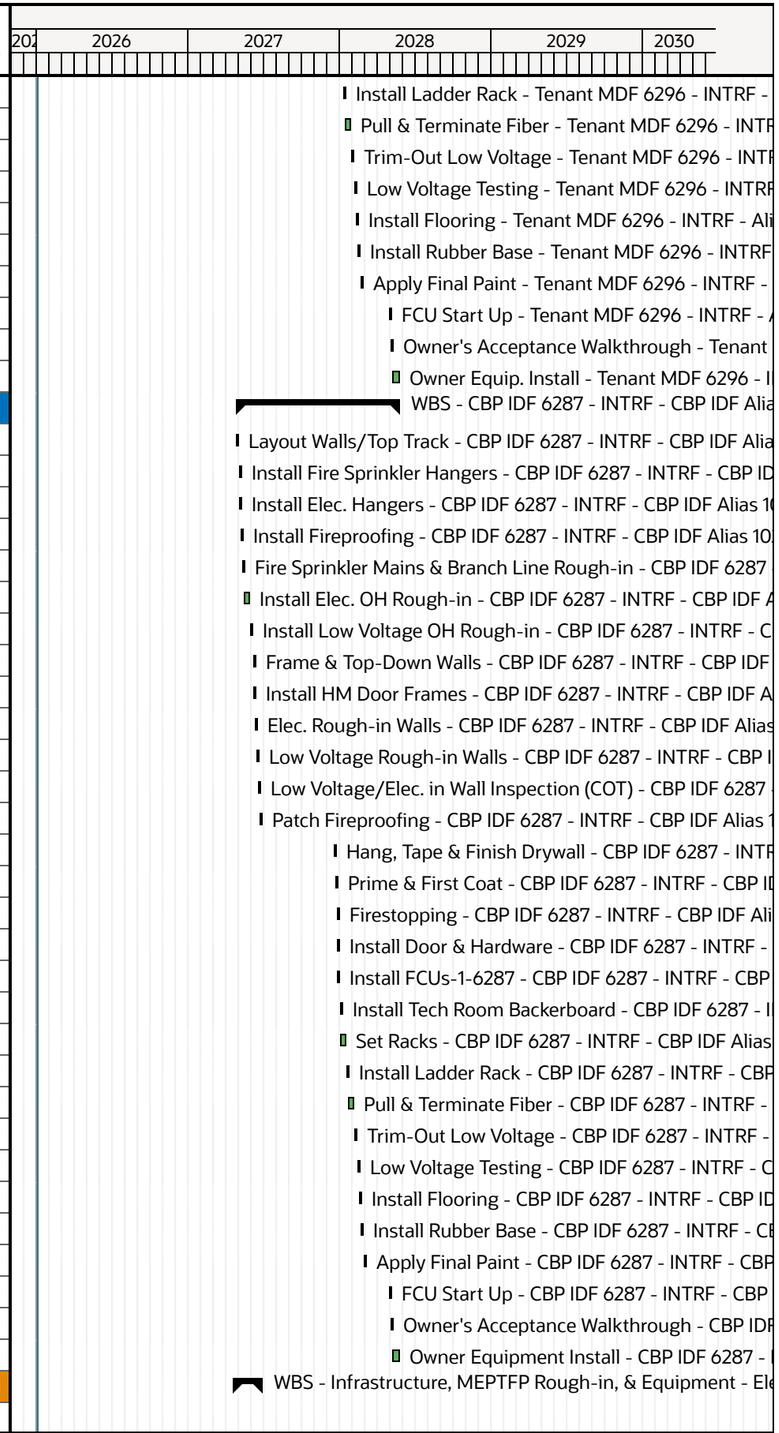


	ID	Name	Dur	Start	Finish	TF
6133	WBS - Distribution/Electrical Room #6290 - INTRF - Apron 8		54.0d	12-Apr-27	25-Jun-27	181.0d
6134	RI-AP8-ER-2475	Layout Walls/Top Track - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	12-Apr-27	16-Apr-27	111.0d
6135	RI-AP8-ER-2485	Elec. Layout for Conduit Windows (Pre Framing) - Dist. Elec. Room 6290 - INTR...	2.0d	19-Apr-27	20-Apr-27	111.0d
6136	RI-AP8-ER-2495	Install Fire Sprinkler Hangers - Dist. Elec. Room 6290 - INTRF - AP 8	2.0d	21-Apr-27	22-Apr-27	111.0d
6137	RI-AP8-ER-2505	Install Elec. Hangers - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	23-Apr-27	29-Apr-27	111.0d
6138	RI-AP8-ER-2515	Install Fireproofing - Dist. Elec. Room 6290 - INTRF - AP 8	2.0d	30-Apr-27	3-May-27	111.0d
6139	RI-AP8-ER-2525	Fire Sprinkler Mains & Branch Line Rough-in - Dist. Elec. Room 6290 - INTRF - ...	10.0d	4-May-27	17-May-27	111.0d
6140	RI-AP8-ER-2535	Low Voltage Rough-in Ceilings - Dist. Elec. Room 6290 - INTRF - AP 8	10.0d	18-May-27	1-Jun-27	111.0d
6141	RI-AP8-ER-2545	Frame & Top-Down Walls - Dist. Elec. Room 6290 - INTRF - AP 8	10.0d	2-Jun-27	15-Jun-27	111.0d
6142	RI-AP8-ER-2575	Install HM Door Frames - Dist. Elec. Room 6290 - INTRF - AP 8	3.0d	2-Jun-27	4-Jun-27	111.0d
6143	RI-AP8-ER-2585	Elec. Rough-in Walls - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	7-Jun-27	11-Jun-27	111.0d
6144	RI-AP8-ER-2595	Low Voltage Rough-in Walls - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	14-Jun-27	18-Jun-27	111.0d
6145	RI-AP8-ER-2555	Elec. Layout-Panel Backing & Housekeeping Pads (Post Framing) - Dist. Elec. R...	5.0d	16-Jun-27	22-Jun-27	182.0d
6146	RI-AP8-ER-2605	Patch Fireproofing - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	21-Jun-27	25-Jun-27	111.0d
6147	RI-AP8-ER-2565	Pour Equip. Pads - Dist. Elec. Room 6290 - INTRF - AP 8	2.0d	23-Jun-27	24-Jun-27	182.0d
6148	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Restrooms - Apron 8		48.0d	1-Apr-27	8-Jun-27	283.0d
6149	WBS - Gang Bathroom #2 - INTR - Apron 8		48.0d	1-Apr-27	8-Jun-27	283.0d
6150	RI-AP8-R2-1980	Frame & Top-Down Walls - Gang B/room #2 - INTR - AP 8	5.0d	1-Apr-27	7-Apr-27	218.0d
6151	RI-AP8-R2-1990	Set Restrooms Carriers - Gang Bathroom #2 - INTR - AP 8	4.0d	2-Apr-27	7-Apr-27	218.0d
6152	RI-AP8-R2-2060	Install Plumbing Rough-in Walls - Gang B/room #2 - INTR - AP 8	10.0d	8-Apr-27	21-Apr-27	218.0d
6153	RI-AP8-R2-2000	Install Blocking & Backing for Specialties - Gang B/room #2 - INTR - AP 8	3.0d	8-Apr-27	12-Apr-27	233.0d
6154	RI-AP8-R2-2010	Fire Sprinkler Mains & Branch Line Rough-in - Gang B/room #2 - INTR - AP 8	10.0d	8-Apr-27	21-Apr-27	228.0d
6155	RI-AP8-R2-2300	Install 1/2" Plywood Backing - Gang B/room #2 - INTR - AP 8	5.0d	8-Apr-27	14-Apr-27	321.0d
6156	RI-AP8-R2-2070	Elec. Rough-in Walls - Gang B/room #2 - INTR - AP 8	8.0d	14-Apr-27	23-Apr-27	218.0d
6157	RI-AP8-R2-2080	Low Voltage Rough-in Walls - Gang B/room #2 - INTR - AP 8	3.0d	26-Apr-27	28-Apr-27	218.0d
6158	RI-AP8-R2-2090	Install Vanities Steel Support - Gang B/room #2 - INTR - AP 8	2.0d	29-Apr-27	30-Apr-27	219.0d
6159	RI-AP8-R2-2100	Frame Ceiling - Gang B/room #2 - INTR - AP 8	2.0d	29-Apr-27	30-Apr-27	218.0d
6160	RI-AP8-R2-2110	Install Recessed Can RI/Speaker RI Frames - Gang B/room #2 - INTR - AP 8	2.0d	30-Apr-27	3-May-27	220.0d
6161	RI-AP8-R2-2040	Low Voltage Rough-in Ceilings - Gang B/room #2 - INTR - AP 8	3.0d	3-May-27	5-May-27	218.0d
6162	RI-AP8-R2-2120	Install Wall Insulation - Gang B/room #2 - INTR - AP 8	2.0d	7-Jun-27	8-Jun-27	195.0d
6163	WBS - Service (#6 & #7) Elevator Cabs/Shaft - INTR - Apron 8		158.0d	29-Feb-28	10-Oct-28	77.0d
6164	VC-EL-AP8-2880	Install Elev. Safety Rail/Net - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	29-Feb-28	6-Mar-28	5.0d
6165	VC-EL-AP8-3020	Install Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	7-Mar-28	13-Mar-28	5.0d
6166	VC-EL-AP8-2890	Rough-in Elec. In Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	8.0d	14-Mar-28	23-Mar-28	5.0d
6167	VC-EL-AP8-3040	Install Temp Sump Pit Cover - Service (#6 & #7) Elevator Cabs/Shaft - INTR - A...	2.0d	14-Mar-28	15-Mar-28	11.0d
6168	VC-EL-AP8-2920	Install Elev. Pit LTNG/Outlets - Service (#6 & #7) Elevator Cabs/Shaft - INTR - ...	5.0d	24-Mar-28	30-Mar-28	5.0d
6169	VC-EL-AP8-2930	Install Temp Power for Elevator Release - Service (#6 & #7) Elevator Cabs/Shaf...	5.0d	24-Mar-28	30-Mar-28	10.0d
6170	VC-EL-AP8-3030	Remove Scaffold in Hoistway - Service (#6 & #7) Elevator Cabs/Shaft - INTR - ...	5.0d	31-Mar-28	6-Apr-28	5.0d
6171	VC-EL-AP8-2940	Install Elev. Rails - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	14-Apr-28	20-Apr-28	0.0d
6172	VC-EL-AP8-3400	Set Elev. Equip. in Shaft - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	2.0d	21-Apr-28	24-Apr-28	0.0d
6173	VC-EL-AP8-3420	Install Hoistway Elec. Cabling - Service (#6 & #7) Elevator Cabs/Shaft - INTR - ...	5.0d	25-Apr-28	1-May-28	0.0d
6174	VC-EL-AP8-3410	Install Platform & Weights - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	25-Apr-28	1-May-28	0.0d

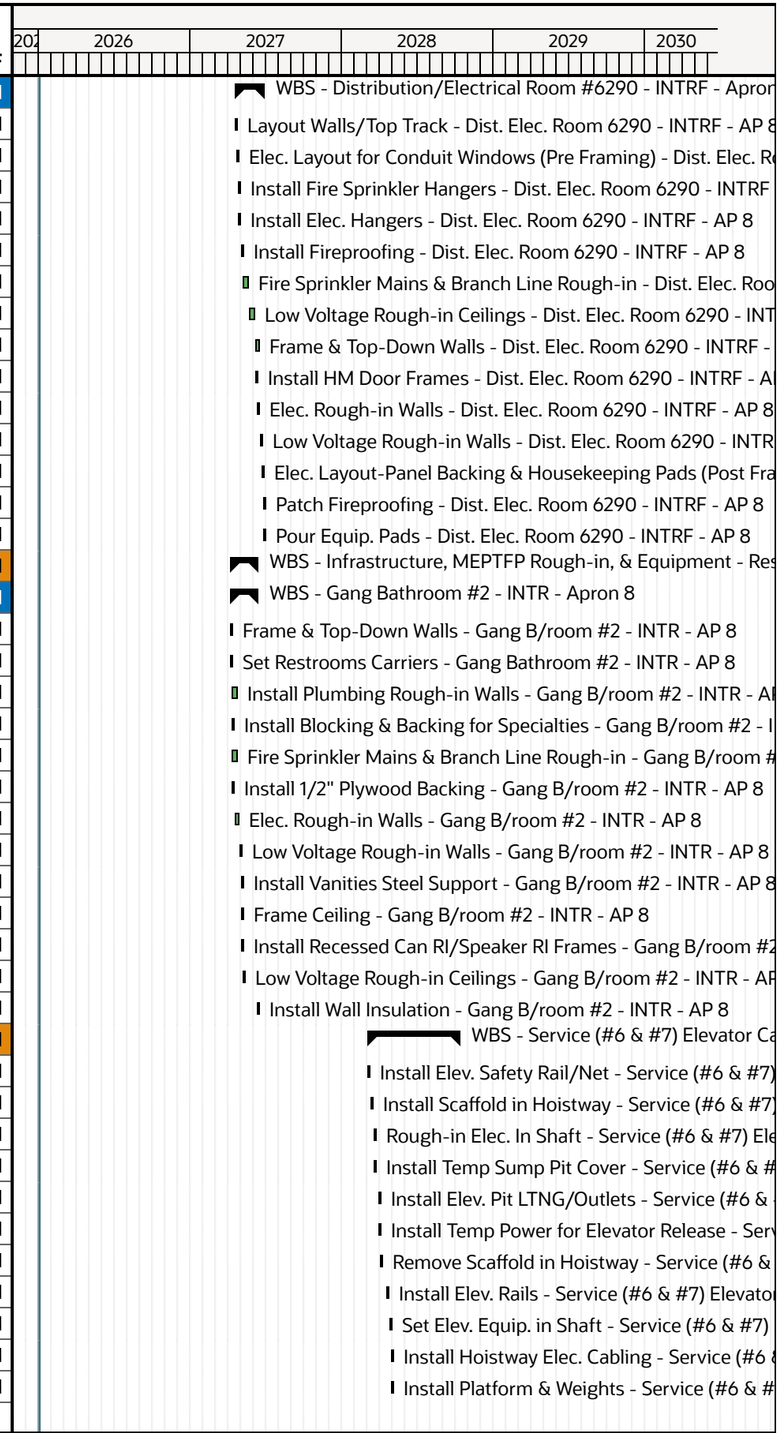


	ID	Name	Dur	Start	Finish	TF
6175	VC-EL-AP8-3430	Install Elev. Equip in Pit - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	2-May-28	8-May-28	0.0d
6176	VC-EL-AP8-3440	Install Elev. Doors - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3.0d	2-May-28	4-May-28	0.0d
6177	VC-EL-AP8-3450	Install Elev. Cab - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	5-May-28	11-May-28	13.0d
6178	VC-EL-AP8-3460	Connect Elev. Elec. Equip. - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	12-May-28	18-May-28	13.0d
6179	VC-EL-AP8-3480	Field Measure & Fab. Decorative Glass Panels (GL04) - Service (#6 & #7) Elevat...	70.0d	12-May-28	21-Aug-28	77.0d
6180	VC-EL-AP8-3060	Grout Elevator Door Frames - Service (#6 & #7) Elevator Cabs/Shaft - INTR - A...	5.0d	19-May-28	25-May-28	13.0d
6181	VC-EL-AP8-3320	Install Terrazzo Flooring at (TR02) - Service (#6 & #7) Elevator Cabs/Shaft - IN...	2.0d	19-May-28	22-May-28	16.0d
6182	VC-EL-AP8-3350	Grout Elevator Sills - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	26-May-28	2-Jun-28	13.0d
6183	VC-EL-AP8-3390	Set Elev. Fronts & Call Boxes - Service (#6 & #7) Elevator Cabs/Shaft - INTR - A...	5.0d	5-Jun-28	9-Jun-28	13.0d
6184	VC-EL-AP8-3070	Remove Elevator Safety Rail/Net - Service (#6 & #7) Elevator Cabs/Shaft - INT...	2.0d	12-Jun-28	13-Jun-28	13.0d
6185	VC-EL-AP8-2950	Elec. Run Time for Final Connections - Service (#6 & #7) Elevator Cabs/Shaft - ...	5.0d	14-Jun-28	20-Jun-28	13.0d
6186	VC-EL-AP8-3340	Install Cameras - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	21-Jun-28	27-Jun-28	130.0d
6187	VC-EL-AP8-3490	Install Decorative Glass Glazing (GL04) - Service (#6 & #7) Elevator Cabs/Shaft...	5.0d	22-Aug-28	28-Aug-28	77.0d
6188	VC-EL-AP8-3500	Install Metal Base - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	2.0d	29-Aug-28	30-Aug-28	78.0d
6189	VC-EL-AP8-3510	Install Architectural Woodwork (WA01) - Service (#6 & #7) Elevator Cabs/Shaft...	3.0d	29-Aug-28	31-Aug-28	77.0d
6190	VC-EL-AP8-2960	Install Fire Alarm Trim - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3.0d	1-Sep-28	6-Sep-28	77.0d
6191	VC-EL-AP8-3090	Install Pit Ladder - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	2.0d	7-Sep-28	8-Sep-28	77.0d
6192	VC-EL-AP8-3080	Install Sump Pump & Final Grate Cover - Service (#6 & #7) Elevator Cabs/Shaft...	2.0d	11-Sep-28	12-Sep-28	77.0d
6193	VC-EL-AP8-2970	Adjust/Test Elev. - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	10.0d	13-Sep-28	26-Sep-28	77.0d
6194	VC-EL-AP8-3300	Liftnet/Phone Service Configuration - Service (#6 & #7) Elevator Cabs/Shaft - ...	5.0d	27-Sep-28	3-Oct-28	77.0d
6195	VC-EL-AP8-3380	Prepare Elev. Punchlist - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	5.0d	4-Oct-28	10-Oct-28	77.0d
6196	WBS - Service (#6 & #7) Elevator Machine Room - INTR - Apron 8		67.0d	15-Feb-28	17-May-28	130.0d
6197	VC-EL-AP8-3110	Hang Machine Room Side 1st Layer - Service (#6 & #7) Elevator Machine Roo...	2.0d	15-Feb-28	16-Feb-28	0.0d
6198	VC-EL-AP8-3120	Inspect 1st Layer - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	17-Feb-28	18-Feb-28	0.0d
6199	VC-EL-AP8-3130	Hang Machine Room Side 2nd Layer - Service (#6 & #7) Elevator Machine Roo...	2.0d	21-Feb-28	22-Feb-28	0.0d
6200	VC-EL-AP8-3140	Tape/Finish 2 Hr Rated Wall - Service (#6 & #7) Elevator Machine Room - INTR...	5.0d	23-Feb-28	29-Feb-28	0.0d
6201	VC-EL-AP8-3150	Frame 2 Hr Rated Lid with Shaft Liner - Service (#6 & #7) Elevator Machine Ro...	2.0d	1-Mar-28	2-Mar-28	0.0d
6202	VC-EL-AP8-3160	Insulate Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	3-Mar-28	6-Mar-28	0.0d
6203	VC-EL-AP8-3170	Inspect Ceiling Insulation - Service (#6 & #7) Elevator Machine Room - INTR - ...	2.0d	7-Mar-28	8-Mar-28	0.0d
6204	VC-EL-AP8-3200	Hang 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	9-Mar-28	10-Mar-28	0.0d
6205	VC-EL-AP8-3190	Inspect 1st Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - A...	2.0d	13-Mar-28	14-Mar-28	0.0d
6206	VC-EL-AP8-3180	Hang 2nd Layer Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	15-Mar-28	16-Mar-28	0.0d
6207	VC-EL-AP8-3230	Tape/Finish Ceiling - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	17-Mar-28	23-Mar-28	0.0d
6208	VC-EL-AP8-3220	1st Coat Paint Machine Room - Service (#6 & #7) Elevator Machine Room - INT...	2.0d	24-Mar-28	27-Mar-28	0.0d
6209	VC-EL-AP8-2900	Elec. Wall Rough Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room...	3.0d	28-Mar-28	30-Mar-28	0.0d
6210	VC-EL-AP8-3250	Install Door & Hardware - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	28-Mar-28	29-Mar-28	1.0d
6211	VC-EL-AP8-3210	Set Elev. Controllers - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	30-Mar-28	5-Apr-28	1.0d
6212	VC-EL-AP8-2910	Install Elec. OH Elev. Equip. Room - Service (#6 & #7) Elevator Machine Room -...	5.0d	31-Mar-28	6-Apr-28	0.0d
6213	VC-EL-AP8-3240	Install Elev. Pathways/Wire Elev. - Service (#6 & #7) Elevator Machine Room - I...	10.0d	7-Apr-28	20-Apr-28	0.0d
6214	VC-EL-AP8-3270	Apply Final Paint - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	21-Apr-28	27-Apr-28	76.0d
6215	VC-EL-AP8-3280	Seal Concrete Floor - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	28-Apr-28	4-May-28	134.0d
6216	VC-EL-AP8-3310	Install Fire Extinguisher & Cabinet - Service (#6 & #7) Elevator Machine Room ...	2.0d	28-Apr-28	1-May-28	76.0d




	ID	Name	Dur	Start	Finish	TF
6217	VC-EL-AP8-3360	Install Fire Alarm Trim - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	2-May-28	8-May-28	76.0d
6218	VC-EL-AP8-3370	Low Voltage Trim Out - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	2-May-28	8-May-28	76.0d
6219	VC-EL-AP8-3290	Install Rubber Base - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	5-May-28	11-May-28	134.0d
6220	VC-EL-AP8-3260	Install FCUs-1-6294 - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	5.0d	9-May-28	15-May-28	76.0d
6221	VC-EL-AP8-3470	FCU Start Up - Service (#6 & #7) Elevator Machine Room - INTR - AP 8	2.0d	16-May-28	17-May-28	76.0d
6222	WBS - Escalator (#1 & #2) - INTR - Apron 8		47.0d	30-Apr-27	7-Jul-27	256.0d
6223	VC-ESC-AP8-3350	Set Escalator Trusses - Escalator (#1 & #2) - INTR - AP 8	5.0d	30-Apr-27	6-May-27	66.0d
6224	VC-ESC-AP8-3360	Build out Escalators - Escalator (#1 & #2) - INTR - AP 8	20.0d	7-May-27	4-Jun-27	256.0d
6225	VC-ESC-AP8-3370	Install Escalator Covers - Escalator (#1 & #2) - INTR - AP 8	5.0d	7-Jun-27	11-Jun-27	256.0d
6226	VC-ESC-AP8-3380	Install Sump Pump & Final Grate Cover - 4) - Escalator (#1 & #2) - INTR - AP 8	2.0d	14-Jun-27	15-Jun-27	256.0d
6227	VC-ESC-AP8-3390	Adjust Esc/Elev. - Service (#5) - Escalator (#1 & #2) - INTR - AP 8	10.0d	16-Jun-27	29-Jun-27	256.0d
6228	VC-ESC-AP8-3400	Liftnet/Phone Service Configuration - Escalator (#1 & #2) - INTR - AP 8	5.0d	30-Jun-27	7-Jul-27	256.0d
6229	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 9		193.0d	26-Jan-27	26-Oct-27	188.0d
6230	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - Apron 9		193.0d	26-Jan-27	26-Oct-27	188.0d
6231	WBS - Overall Rough-in - INTR - Apron 9		193.0d	26-Jan-27	26-Oct-27	188.0d
6232	RI-AP9-3310	Layout Walls/Top Track - Overall Rough-in - INTR - AP 9	10.0d	26-Jan-27	8-Feb-27	65.0d
6233	RI-AP9-3550	FRP Baggage Housekeeping Pads - Overall Rough-in - INTR - AP 9	10.0d	26-Jan-27	8-Feb-27	371.0d
6234	RI-AP9-3320	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 9	2.0d	9-Feb-27	10-Feb-27	67.0d
6235	RI-AP9-3440	Install Block Walls/Masonry Door Frames - INTR - AP 9	10.0d	9-Feb-27	22-Feb-27	82.0d
6236	RI-AP9-3460	Install HM Door Frames - Overall Rough-in - INTR - AP 9	3.0d	9-Feb-27	11-Feb-27	267.0d
6237	RI-AP9-3330	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 9	2.0d	11-Feb-27	12-Feb-27	67.0d
6238	RI-AP9-3340	Install Plumbing Hangers - Overall Rough-in - INTR - AP 9	2.0d	15-Feb-27	16-Feb-27	67.0d
6239	RI-AP9-3350	Install Elec. Hangers - Overall Rough-in - INTR - AP 9	2.0d	17-Feb-27	18-Feb-27	67.0d
6240	RI-AP9-3660	Install Signage Supports - Overall Rough-in - INTR - AP 9	5.0d	19-Feb-27	25-Feb-27	67.0d
6241	RI-AP9-3360	Install Fireproofing - Overall Rough-in - INTR - AP 9	10.0d	26-Feb-27	11-Mar-27	67.0d
6242	RI-AP9-3540	Install Under-Slab on Deck Insulation - INTR - AP 9	10.0d	12-Mar-27	25-Mar-27	69.0d
6243	RI-AP9-3700	Patch Fireproofing - Overall Rough-in - INTR - AP 9	5.0d	25-Jun-27	1-Jul-27	0.0d
6244	RI-AP9-3380	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 9	3.0d	2-Jul-27	7-Jul-27	0.0d
6245	RI-AP9-3510	Install Plumbing Insulation - Overall Rough-in - INTR - AP 9	2.0d	8-Jul-27	9-Jul-27	160.0d
6246	RI-AP9-3390	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 9	10.0d	15-Jul-27	28-Jul-27	0.0d
6247	RI-AP9-3400	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 9	10.0d	29-Jul-27	11-Aug-27	0.0d
6248	RI-AP9-3530	Install Duct Insulation - Overall Rough-in - INTR - AP 9	5.0d	29-Jul-27	4-Aug-27	142.0d
6249	RI-AP9-3410	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 9	20.0d	12-Aug-27	9-Sep-27	0.0d
6250	RI-AP9-3500	Install CHW OH Rough-in - Overall Rough-in - INTR - AP 9	5.0d	12-Aug-27	18-Aug-27	132.0d
6251	RI-AP9-3680	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 9	20.0d	12-Aug-27	9-Sep-27	40.0d
6252	RI-AP9-3520	Install CHW Insulation - Overall Rough-in - INTR - AP 9	3.0d	19-Aug-27	23-Aug-27	132.0d
6253	RI-AP9-3420	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 9	10.0d	10-Sep-27	23-Sep-27	110.0d
6254	RI-AP9-3690	Pull BAS Cable - Overall Rough-in - INTR - AP 9	20.0d	10-Sep-27	7-Oct-27	79.0d
6255	RI-AP9-3470	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 9	10.0d	24-Sep-27	7-Oct-27	110.0d
6256	RI-AP9-3490	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 9	3.0d	8-Oct-27	12-Oct-27	110.0d
6257	RI-AP9-3670	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - AP 9	10.0d	13-Oct-27	26-Oct-27	110.0d
6258	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 10		286.0d	8-Jan-27	22-Feb-28	96.0d

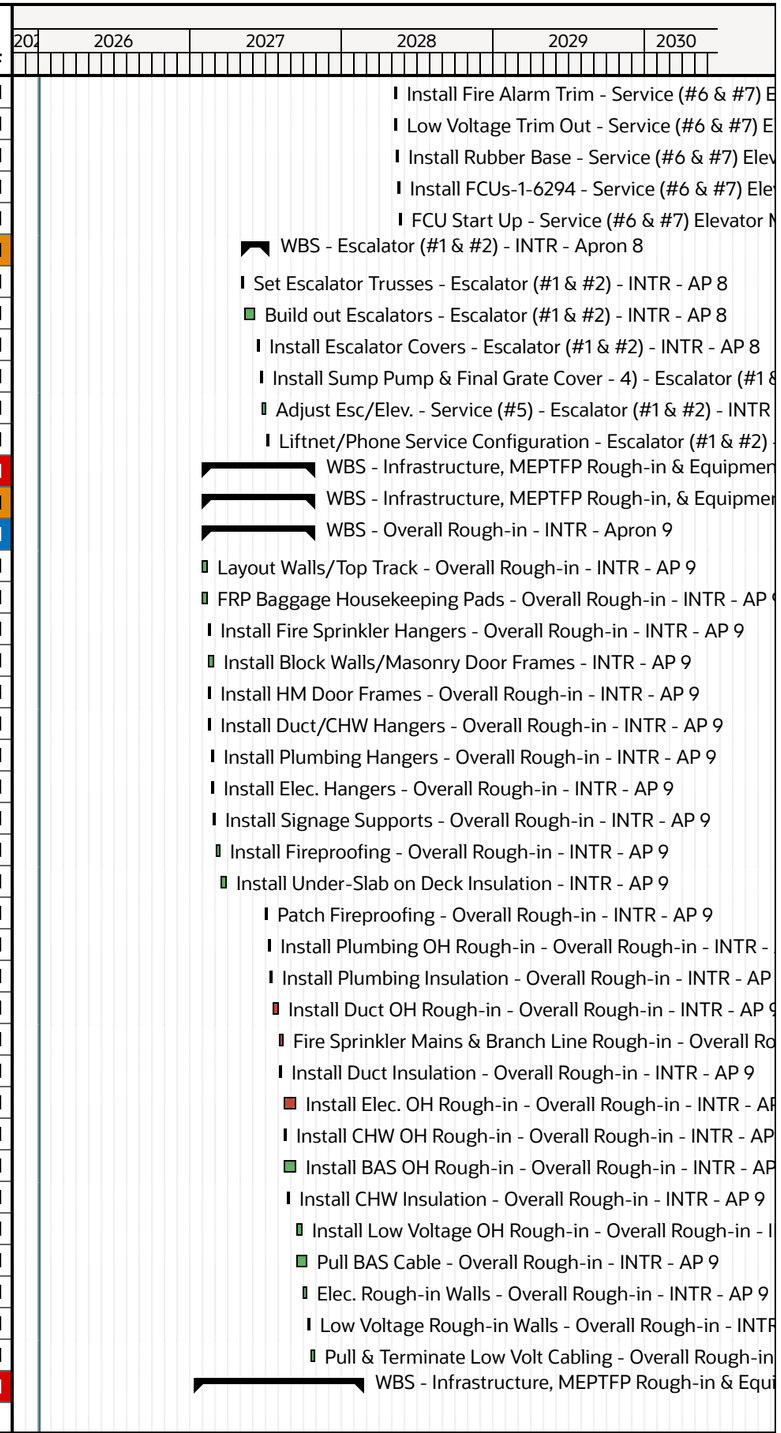

	ID	Name	Dur	Start	Finish	TF
6259	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mechanical - Apron 10		286.0d	8-Jan-27	22-Feb-28	96.0d
6260	WBS - Mechanical Room - INTR - Apron 10		286.0d	8-Jan-27	22-Feb-28	96.0d
6261	RI-AP10-MR-840	Layout Walls/Top Track - Overall Mech. Room - INTR - AP 10	8.0d	8-Jan-27	19-Jan-27	69.0d
6262	RI-AP10-MR-860	Install Fire Sprinkler Hangers - Overall Mech. Room - INTR - AP 10	2.0d	20-Jan-27	21-Jan-27	75.0d
6263	RI-AP10-MR-1160	Install Block Walls/Masonry Door Frames - Overall Mech. Room - INTR - AP 10	5.0d	20-Jan-27	26-Jan-27	91.0d
6264	RI-AP10-MR-870	Install Duct/CHW Hangers - Overall Mech. Room - INTR - AP 10	4.0d	25-Jan-27	28-Jan-27	75.0d
6265	RI-AP10-MR-850	Pour Equip. Pads - Overall Mech. Room - INTR - AP 10	2.0d	27-Jan-27	28-Jan-27	341.0d
6266	RI-AP10-MR-1050	Set Mech. Equip. - Overall Mech. Room - INTR - AP 10	5.0d	29-Jan-27	4-Feb-27	341.0d
6267	RI-AP10-MR-880	Install Plumbing Hangers - Overall Mech. Room - INTR - AP 10	2.0d	29-Jan-27	1-Feb-27	75.0d
6268	RI-AP10-MR-890	Install Elec. Hangers - Overall Mech. Room - INTR - AP 10	2.0d	2-Feb-27	3-Feb-27	75.0d
6269	RI-AP10-MR-900	Install Fireproofing - Overall Mech. Room - INTR - AP 10	2.0d	4-Feb-27	5-Feb-27	75.0d
6270	RI-AP10-MR-910	Install Plumbing OH Rough-in - Overall Mech. Room - INTR - AP 10	5.0d	8-Feb-27	12-Feb-27	230.0d
6271	RI-AP10-MR-930	Install Duct OH Rough-in - Overall Mech. Room - INTR - AP 10	20.0d	15-Feb-27	12-Mar-27	230.0d
6272	RI-AP10-MR-1060	Install Plumbing Insulation - Overall Mech. Room - INTR - AP 10	2.0d	18-Feb-27	19-Feb-27	330.0d
6273	RI-AP10-MR-1070	Install CHW OH Rough-in - Overall Mech. Room - INTR - AP 10	20.0d	15-Mar-27	9-Apr-27	255.0d
6274	RI-AP10-MR-940	Fire Sprinkler Mains & Branch Line Rough-in - Overall Mech. Room - INTR - AP ...	10.0d	12-Apr-27	23-Apr-27	259.0d
6275	RI-AP10-MR-1090	Install CHW Insulation - Overall Mech. Room - INTR - AP 10	10.0d	12-Apr-27	23-Apr-27	275.0d
6276	RI-AP10-MR-1080	Install Duct Insulation - Overall Mech. Room - INTR - AP 10	10.0d	12-Apr-27	23-Apr-27	270.0d
6277	RI-AP10-MR-950	Install Elec. OH Rough-in - Overall Mech. Room - INTR - AP 10	10.0d	26-Apr-27	7-May-27	259.0d
6278	RI-AP10-MR-960	Low Voltage Rough-in Ceilings - Overall Mech. Room - INTR - AP 10	3.0d	10-May-27	12-May-27	259.0d
6279	RI-AP10-MR-980	Frame & Top-Down Walls - Overall Mech. Room - INTR - AP 10	10.0d	20-Sep-27	1-Oct-27	170.0d
6280	RI-AP10-MR-990	Install HM Door Frames - Overall Mech. Room - INTR - AP 10	3.0d	20-Sep-27	22-Sep-27	177.0d
6281	RI-AP10-MR-1000	Elec. Rough-in Walls - Overall Mech. Room - INTR - AP 10	3.0d	8-Oct-27	12-Oct-27	166.0d
6282	RI-AP10-MR-1010	Low Voltage Rough-in Walls - Overall Mech. Room - INTR - AP 10	3.0d	13-Oct-27	15-Oct-27	174.0d
6283	RI-AP10-MR-1170	Pull & Terminate Low Volt Cabling - Overall Mech. Room - INTR - AP 10	5.0d	18-Oct-27	22-Oct-27	174.0d
6284	RI-AP10-MR-1150	Pull & Terminate to Mech. Equip. - Overall Mech. Room - INTR - AP 10	5.0d	9-Feb-28	15-Feb-28	85.0d
6285	RI-AP10-MR-1040	Patch Fireproofing - Overall Mech. Room - INTR - AP 10	5.0d	16-Feb-28	22-Feb-28	96.0d
6286	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 11		373.0d	28-Dec-26	13-Jun-28	94.0d
6287	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 11		146.0d	28-Dec-26	22-Jul-27	145.0d
6288	WBS - Overall Rough-in - INTR - Apron 11		146.0d	28-Dec-26	22-Jul-27	145.0d
6289	RI-AP11-10	Layout Walls/Top Track - Overall Rough-in - INTR - AP 11	8.0d	28-Dec-26	7-Jan-27	69.0d
6290	RI-AP11-3360	Install Block Walls/Masonry Door Frames INTR - AP 11	5.0d	8-Jan-27	14-Jan-27	83.0d
6291	RI-AP11-20	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - AP 11	2.0d	15-Jan-27	18-Jan-27	83.0d
6292	RI-AP11-30	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 11	2.0d	19-Jan-27	20-Jan-27	83.0d
6293	RI-AP11-40	Install Plumbing Hangers - Overall Rough-in - INTR - AP 11	2.0d	21-Jan-27	22-Jan-27	83.0d
6294	RI-AP11-50	Install Elec. Hangers - Overall Rough-in - INTR - AP 11	2.0d	25-Jan-27	26-Jan-27	83.0d
6295	RI-AP11-60	Install Fireproofing - Overall Rough-in - INTR - AP 11	5.0d	8-Feb-27	12-Feb-27	75.0d
6296	RI-AP11-80	Install Plumbing OH Rough-in - Overall Rough-in - INTR - AP 11	8.0d	12-Mar-27	23-Mar-27	56.0d
6297	RI-AP11-90	Install Duct OH Rough-in - Overall Rough-in - INTR - AP 11	8.0d	19-Mar-27	30-Mar-27	56.0d
6298	RI-AP11-3320	Install Plumbing Insulation - Overall Rough-in - INTR - AP 11	4.0d	24-Mar-27	29-Mar-27	148.0d
6299	RI-AP11-3330	Install Duct Insulation - Overall Rough-in - INTR - AP 11	5.0d	31-Mar-27	6-Apr-27	142.0d
6300	RI-AP11-3350	Install CHW OH Rough-In - Overall Rough-in - INTR - AP 11	5.0d	31-Mar-27	6-Apr-27	56.0d

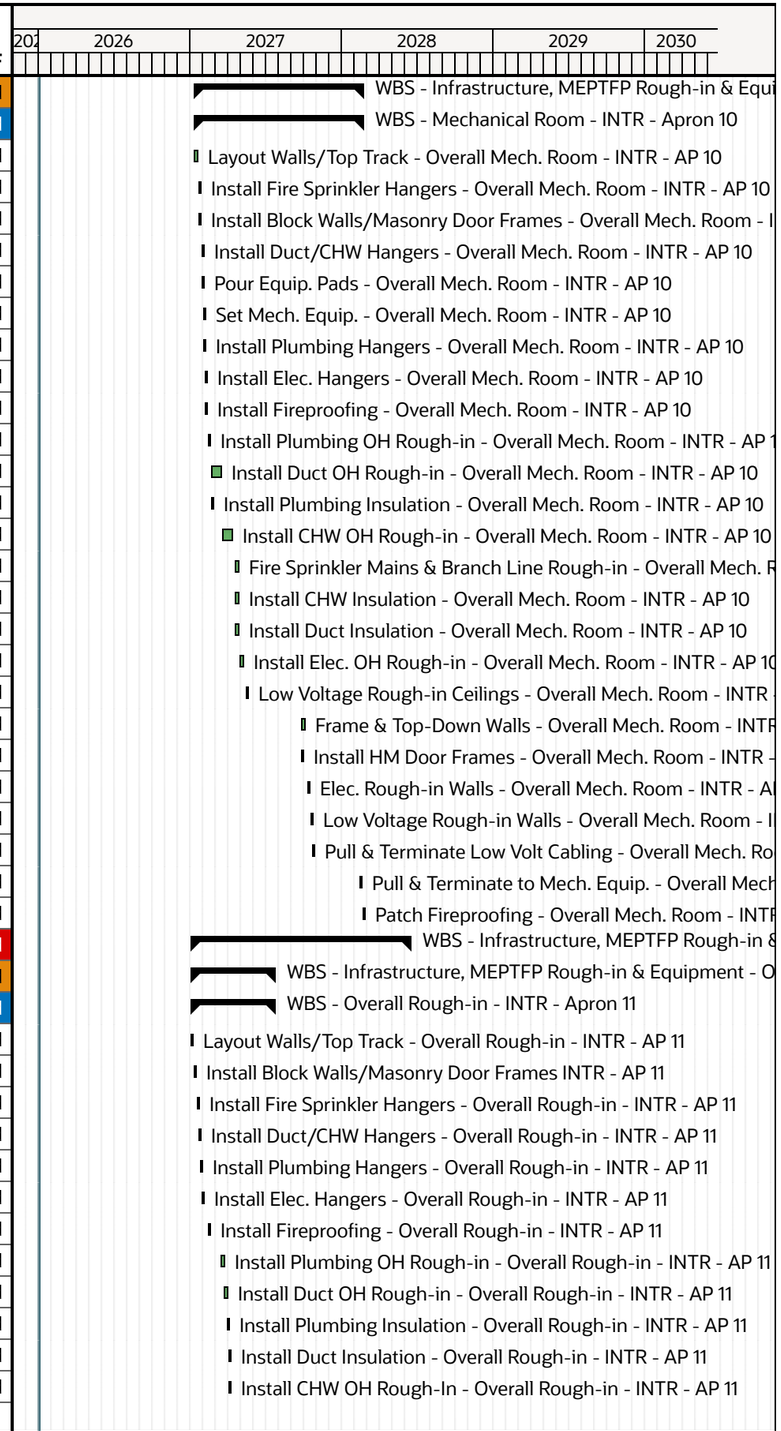


	ID	Name	Dur	Start	Finish	TF
6301	RI-AP11-3340	Install CHW Insulation - Overall Rough-in - INTR - AP 11	4.0d	7-Apr-27	12-Apr-27	138.0d
6302	RI-AP11-110	Install Elec. OH Rough-in - Overall Rough-in - INTR - AP 11	20.0d	9-Apr-27	6-May-27	54.0d
6303	RI-AP11-120	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - AP 11	10.0d	7-May-27	20-May-27	100.0d
6304	RI-AP11-3380	Install BAS OH Rough-in - Overall Rough-in - INTR - AP 11	10.0d	7-May-27	20-May-27	54.0d
6305	RI-AP11-100	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - AP 11	10.0d	21-May-27	4-Jun-27	100.0d
6306	RI-AP11-130	Frame Hard Lid Ceilings - Overall Rough-in - INTR - AP 11	5.0d	21-May-27	27-May-27	128.0d
6307	RI-AP11-3390	Pull BAS Cable - Overall Rough-in - INTR - AP 11	10.0d	21-May-27	4-Jun-27	178.0d
6308	RI-AP11-160	Elec. Rough-in at Hard Lids - Overall Rough-in - INTR - AP 11	5.0d	28-May-27	4-Jun-27	128.0d
6309	RI-AP11-140	Frame & Top-Down Walls - Overall Rough-in - INTR - AP 11	10.0d	7-Jun-27	18-Jun-27	100.0d
6310	RI-AP11-170	Install HM Door Frames - Overall Rough-in - INTR - AP 11	3.0d	7-Jun-27	9-Jun-27	125.0d
6311	RI-AP11-190	Elec. Rough-in Walls - Overall Rough-in - INTR - AP 11	10.0d	21-Jun-27	2-Jul-27	118.0d
6312	RI-AP11-150	Low Voltage Rough-in at Hard Lids - Overall Rough-in - INTR - AP 11	3.0d	6-Jul-27	8-Jul-27	118.0d
6313	RI-AP11-180	Low Voltage Rough-in Walls - Overall Rough-in - INTR - AP 11	3.0d	9-Jul-27	13-Jul-27	118.0d
6314	RI-AP11-3370	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - AP 11	7.0d	14-Jul-27	22-Jul-27	118.0d
6315	WBS - Infrastructure, MEPTFP Rough-in & Equipment - IDF - Apron 11		365.0d	8-Jan-27	13-Jun-28	94.0d
6316	WBS - HCAA IDF 6006 - INTRF- Alias ASD 01580 - Apron 11		365.0d	8-Jan-27	13-Jun-28	94.0d
6317	RI-AP11-IDF-3140	Layout Walls/Top Track - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	8-Jan-27	11-Jan-27	253.0d
6318	RI-AP11-IDF-3150	Install Fire Sprinkler Hangers - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP ...	2.0d	12-Jan-27	13-Jan-27	253.0d
6319	RI-AP11-IDF-3180	Install Elec. Hangers - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	14-Jan-27	15-Jan-27	253.0d
6320	RI-AP11-IDF-3190	Install Fireproofing - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	26-Jan-27	27-Jan-27	247.0d
6321	RI-AP11-IDF-3230	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6006 - INTRF - Alias ...	4.0d	28-Jan-27	2-Feb-27	248.0d
6322	RI-AP11-IDF-3240	Install Elec. OH Rough-in - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	10.0d	4-Feb-27	17-Feb-27	247.0d
6323	RI-AP11-IDF-3250	Install Low Voltage OH Rough-in - HCAA IDF 6006 - INTRF - Alias ASD 01580 -...	3.0d	18-Feb-27	22-Feb-27	247.0d
6324	RI-AP11-IDF-3260	Frame & Top-Down Walls - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	4.0d	23-Feb-27	26-Feb-27	247.0d
6325	RI-AP11-IDF-3270	Install HM Door Frames - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	23-Feb-27	25-Feb-27	248.0d
6326	FN-AP11-IDF-3240	Install Door & Hardware - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	26-Feb-27	1-Mar-27	393.0d
6327	RI-AP11-IDF-3280	Elec. Rough-in Walls - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	1-Mar-27	3-Mar-27	247.0d
6328	RI-AP11-IDF-3290	Low Voltage Rough-in Walls - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	4-Mar-27	8-Mar-27	247.0d
6329	RI-AP11-IDF-3300	Low Voltage/Elect. in Wall Inspection (COT) - HCAA IDF 6006 - INTRF - Alias A...	2.0d	9-Mar-27	10-Mar-27	247.0d
6330	RI-AP11-IDF-3145	Patch Fireproofing - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	11-Mar-27	17-Mar-27	247.0d
6331	FN-AP11-IDF-3150	Hang, Tape & Finish Drywall - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	4-Nov-27	10-Nov-27	85.0d
6332	FN-AP11-IDF-3160	Prime & First Coat - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	11-Nov-27	12-Nov-27	176.0d
6333	FN-AP11-IDF-3170	Firestopping - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	15-Nov-27	17-Nov-27	176.0d
6334	FN-AP11-IDF-3310	Install FCUs-1-6006 - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	15-Nov-27	19-Nov-27	183.0d
6335	FN-AP11-IDF-3180	Install Tech Room Backerboard - HCAA IDF 6006 - INTRF - Alias ASD 01580 - A...	2.0d	18-Nov-27	19-Nov-27	176.0d
6336	FN-AP11-IDF-3190	Set Racks - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	10.0d	22-Nov-27	7-Dec-27	176.0d
6337	FN-AP11-IDF-3200	Install Ladder Rack - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	8-Dec-27	10-Dec-27	176.0d
6338	FN-AP11-IDF-3210	Pull & Terminate Fiber - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	10.0d	13-Dec-27	27-Dec-27	176.0d
6339	FN-AP11-IDF-3350	Pull & Terminate Fiber for PBB D48, D49, D50, D51 - HCAA IDF 6006 - INTRF - ...	10.0d	13-Dec-27	27-Dec-27	176.0d
6340	FN-AP11-IDF-3220	Trim-Out Low Voltage - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	28-Dec-27	4-Jan-28	176.0d
6341	FN-AP11-IDF-3260	Low Voltage Testing - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	3.0d	5-Jan-28	7-Jan-28	176.0d
6342	FN-AP11-IDF-3250	Install Flooring - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	10-Jan-28	11-Jan-28	176.0d

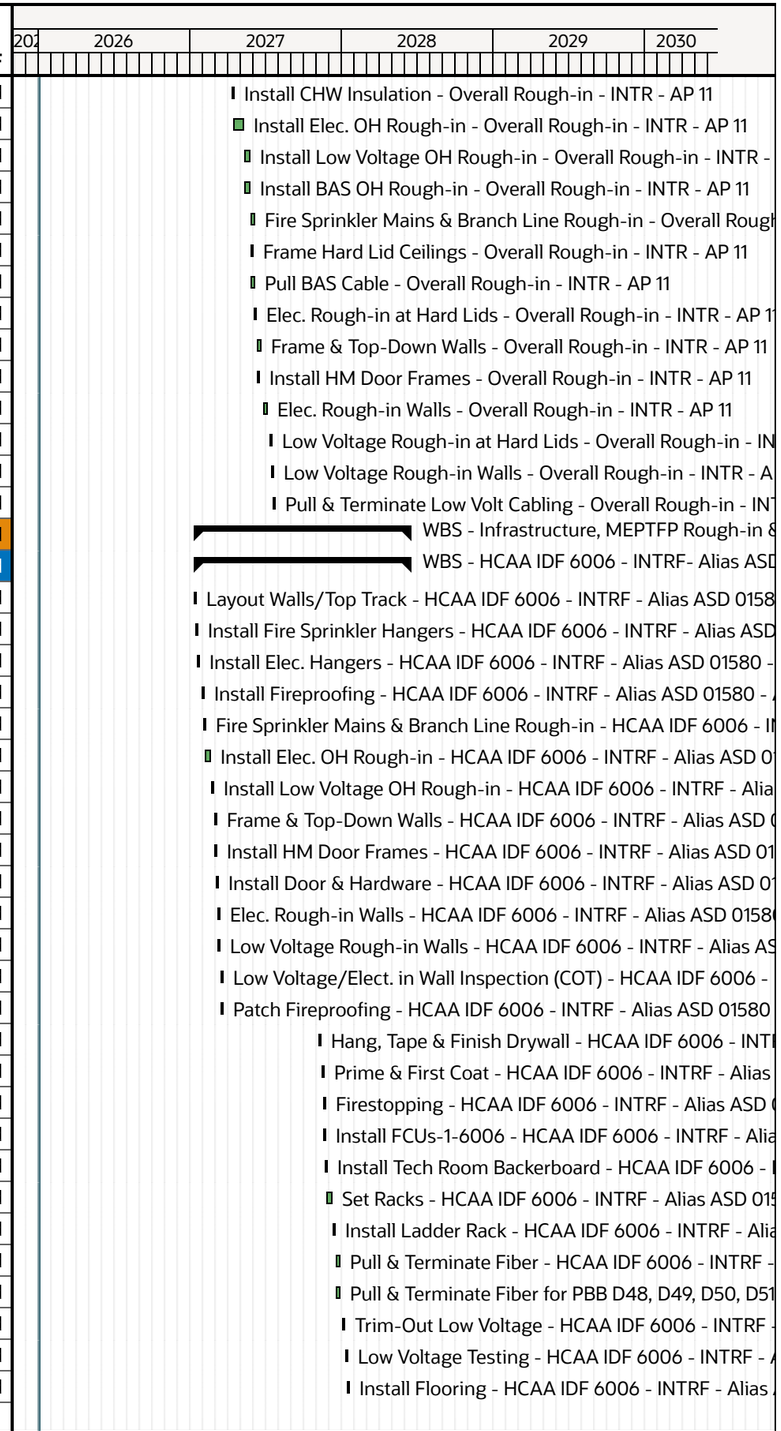


	ID	Name	Dur	Start	Finish	TF
6343	FN-AP11-IDF-3360	Install Rubber Base - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	12-Jan-28	18-Jan-28	176.0d
6344	FN-AP11-IDF-3230	Apply Final Paint - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	5.0d	19-Jan-28	25-Jan-28	176.0d
6345	FN-AP11-IDF-3330	FCU Start Up - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	2.0d	21-Apr-28	24-Apr-28	112.0d
6346	FN-AP11-IDF-3270	Owner's Acceptance Walkthrough - HCAA IDF 6006 - INTRF - Alias ASD 01580 ...	2.0d	25-Apr-28	26-Apr-28	112.0d
6347	FN-AP11-IDF-3280	Owner Equipment Install - HCAA IDF 6006 - INTRF - Alias ASD 01580 - AP 11	15.0d	23-May-28	13-Jun-28	94.0d
6348	WBS - Tenant IDF 6004 - INTRF- Alias ASD 01581 - Apron 11		365.0d	8-Jan-27	13-Jun-28	94.0d
6349	RI-AP11-IDF-2970	Layout Walls/Top Track - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	8-Jan-27	11-Jan-27	263.0d
6350	RI-AP11-IDF-2980	Install Fire Sprinkler Hangers - Tenant IDF 6004 - INTRF - Alias ASD 01581 - A...	2.0d	12-Jan-27	13-Jan-27	263.0d
6351	RI-AP11-IDF-3010	Install Elec. Hangers - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	14-Jan-27	15-Jan-27	263.0d
6352	RI-AP11-IDF-3020	Install Fireproofing - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	26-Jan-27	27-Jan-27	257.0d
6353	RI-AP11-IDF-3060	Fire Sprinkler Mains & Branch Line Rough-in - Tenant IDF 6004 - INTRF - Alias ...	4.0d	28-Jan-27	2-Feb-27	268.0d
6354	RI-AP11-IDF-3070	Install Elec. OH Rough-in - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	10.0d	4-Feb-27	17-Feb-27	267.0d
6355	RI-AP11-IDF-3080	Install Low Voltage OH Rough-in - Tenant IDF 6004 - INTRF - Alias ASD 01581 ...	3.0d	18-Feb-27	22-Feb-27	267.0d
6356	RI-AP11-IDF-3090	Frame & Top-Down Walls - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	4.0d	23-Feb-27	26-Feb-27	267.0d
6357	RI-AP11-IDF-3100	Install HM Door Frames - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	3.0d	23-Feb-27	25-Feb-27	268.0d
6358	RI-AP11-IDF-3110	Elec. Rough-in Walls - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	3.0d	1-Mar-27	3-Mar-27	267.0d
6359	RI-AP11-IDF-3120	Low Voltage Rough-in Walls - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP ...	3.0d	4-Mar-27	8-Mar-27	267.0d
6360	RI-AP11-IDF-3130	Low Voltage/Elect. in Wall Inspection (COT) - Tenant IDF 6004 - INTRF - Alias A...	2.0d	9-Mar-27	10-Mar-27	267.0d
6361	RI-AP11-IDF-2995	Patch Fireproofing - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	5.0d	11-Mar-27	17-Mar-27	267.0d
6362	FN-AP11-IDF-3000	Hang, Tape & Finish Drywall - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP ...	5.0d	6-Dec-27	10-Dec-27	85.0d
6363	FN-AP11-IDF-3010	Prime & First Coat - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	13-Dec-27	14-Dec-27	163.0d
6364	FN-AP11-IDF-3020	Firestopping - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	3.0d	15-Dec-27	17-Dec-27	163.0d
6365	FN-AP11-IDF-3090	Install Door & Hardware - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	15-Dec-27	16-Dec-27	190.0d
6366	FN-AP11-IDF-3320	Install FCUs-1-6004 - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	5.0d	15-Dec-27	21-Dec-27	163.0d
6367	FN-AP11-IDF-3030	Install Tech Room Backerboard - Tenant IDF 6004 - INTRF - Alias ASD 01581 - ...	2.0d	20-Dec-27	21-Dec-27	163.0d
6368	FN-AP11-IDF-3040	Set Racks - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	10.0d	22-Dec-27	6-Jan-28	163.0d
6369	FN-AP11-IDF-3050	Install Ladder Rack - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	3.0d	7-Jan-28	11-Jan-28	163.0d
6370	FN-AP11-IDF-3060	Pull & Terminate Fiber - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	10.0d	12-Jan-28	25-Jan-28	163.0d
6371	FN-AP11-IDF-3070	Trim-Out Low Voltage - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	5.0d	26-Jan-28	1-Feb-28	163.0d
6372	FN-AP11-IDF-3100	Install Flooring - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	26-Jan-28	27-Jan-28	164.0d
6373	FN-AP11-IDF-3300	Install Rubber Base - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	5.0d	28-Jan-28	3-Feb-28	164.0d
6374	FN-AP11-IDF-3110	Low Voltage Testing - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	3.0d	2-Feb-28	4-Feb-28	163.0d
6375	FN-AP11-IDF-3080	Apply Final Paint - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	5.0d	7-Feb-28	11-Feb-28	163.0d
6376	FN-AP11-IDF-3340	FCU Start Up - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	2.0d	21-Apr-28	24-Apr-28	112.0d
6377	FN-AP11-IDF-3120	Owner's Acceptance Walkthrough - Tenant IDF 6004 - INTRF - Alias ASD 0158...	2.0d	25-Apr-28	26-Apr-28	112.0d
6378	FN-AP11-IDF-3130	Owner Equipment Install - Tenant IDF 6004 - INTRF - Alias ASD 01581 - AP 11	15.0d	23-May-28	13-Jun-28	94.0d
6379	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Electrical - Apron 11		52.0d	8-Jan-27	22-Mar-27	249.0d
6380	WBS - Distribution/Electrical Room #6003 - INTRF - Apron 11		52.0d	8-Jan-27	22-Mar-27	249.0d
6381	RI-AP11-ER-2620	Layout Walls/Top Track - Dist. Elec. Room #6003 - INTR - AP 11	2.0d	8-Jan-27	11-Jan-27	165.0d
6382	RI-AP11-ER-2630	Elec. Layout for Conduit Windows (Pre Framing) - Dist. Elec. Room #6003 - INT...	2.0d	12-Jan-27	13-Jan-27	165.0d
6383	RI-AP11-ER-2640	Install Fire Sprinkler Hangers - Dist. Elec. Room #6003 - INTR - AP 11	2.0d	14-Jan-27	15-Jan-27	165.0d
6384	RI-AP11-ER-2650	Install Elec. Hangers - Dist. Elec. Room #6003 - INTR - AP 11	5.0d	18-Jan-27	22-Jan-27	165.0d




	ID	Name	Dur	Start	Finish	TF
6385	RI-AP11-ER-2660	Install Fireproofing - Dist. Elec. Room #6003 - INTR - AP 11	2.0d	26-Jan-27	27-Jan-27	164.0d
6386	RI-AP11-ER-2670	Fire Sprinkler Mains & Branch Line Rough-in - Dist. Elec. Room #6003 - INTR - ...	10.0d	28-Jan-27	10-Feb-27	164.0d
6387	RI-AP11-ER-2680	Low Voltage Rough-in Ceilings - Dist. Elec. Room #6003 - INTR - AP 11	10.0d	11-Feb-27	24-Feb-27	164.0d
6388	RI-AP11-ER-2690	Frame & Top-Down Walls - Dist. Elec. Room #6003 - INTR - AP 11	10.0d	25-Feb-27	10-Mar-27	164.0d
6389	RI-AP11-ER-2720	Install HM Door Frames - Dist. Elec. Room #6003 - INTR - AP 11	3.0d	25-Feb-27	1-Mar-27	164.0d
6390	RI-AP11-ER-2730	Elec. Rough-in Walls - Dist. Elec. Room #6003 - INTR - AP 11	5.0d	2-Mar-27	8-Mar-27	164.0d
6391	RI-AP11-ER-2740	Low Voltage Rough-in Walls - Dist. Elec. Room #6003 - INTR - AP 11	5.0d	9-Mar-27	15-Mar-27	164.0d
6392	RI-AP11-ER-2700	Elec. Layout-Panel Backing & Housekeeping Pads (Post Framing) - Dist. Elec. R...	5.0d	11-Mar-27	17-Mar-27	250.0d
6393	RI-AP11-ER-2750	Patch Fireproofing - Dist. Elec. Room #6003 - INTR - AP 11	5.0d	16-Mar-27	22-Mar-27	164.0d
6394	RI-AP11-ER-2710	Pour Equip. Pads - Dist. Elec. Room #6003 - INTR - AP 11	2.0d	18-Mar-27	19-Mar-27	250.0d
6395	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Apron 12		396.0d	20-Nov-26	13-Jun-28	112.0d
6396	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Apron 12		129.0d	20-Nov-26	25-May-27	175.0d
6397	WBS - Overall Rough-in - INTR - Apron 12		129.0d	20-Nov-26	25-May-27	175.0d
6398	RI-AP12-10	Layout Walls/Top Track - Overall Rough-in- INTR - AP 12	3.0d	20-Nov-26	24-Nov-26	66.0d
6399	RI-AP12-5420	Install Block Walls/Masonry Door Frames INTR - AP 12	5.0d	14-Dec-26	18-Dec-26	55.0d
6400	RI-AP12-20	Install Fire Sprinkler Hangers - Overall Rough-in- INTR - AP 12	2.0d	21-Dec-26	22-Dec-26	55.0d
6401	RI-AP12-30	Install Duct/CHW Hangers - Overall Rough-in - INTR - AP 12	2.0d	23-Dec-26	24-Dec-26	55.0d
6402	RI-AP12-40	Install Plumbing Hangers - Overall Rough-in- INTR - AP 12	10.0d	28-Dec-26	11-Jan-27	55.0d
6403	RI-AP12-50	Install Elec. Hangers - Overall Rough-in- INTR - AP 12	2.0d	12-Jan-27	13-Jan-27	55.0d
6404	RI-AP12-60	Install Fireproofing - Overall Rough-in- INTR - AP 12	10.0d	15-Jan-27	28-Jan-27	54.0d
6405	RI-AP12-70	Install Plumbing OH Rough-in - Overall Rough-in- INTR - AP 12	20.0d	29-Jan-27	25-Feb-27	54.0d
6406	RI-AP12-90	Install Duct OH Rough-in - Overall Rough-in- INTR - AP 12	15.0d	5-Feb-27	25-Feb-27	54.0d
6407	RI-AP12-5380	Install Plumbing Insulation - Overall Rough-in - INTR - AP 12	10.0d	26-Feb-27	11-Mar-27	138.0d
6408	RI-AP12-5400	Install CHW OH Rough-in - Overall Rough-in - INTR - AP 12	5.0d	26-Feb-27	4-Mar-27	54.0d
6409	RI-AP12-5410	Install Duct Insulation - Overall Rough-in - INTR - AP 12	5.0d	26-Feb-27	4-Mar-27	143.0d
6410	RI-AP12-100	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in- INTR - AP 12	10.0d	5-Mar-27	18-Mar-27	54.0d
6411	RI-AP12-5390	Install CHW Insulation - Overall Rough-in - INTR - AP 12	5.0d	5-Mar-27	11-Mar-27	138.0d
6412	RI-AP12-110	Install Elec. OH Rough-in - Overall Rough-in- INTR - AP 12	20.0d	12-Mar-27	8-Apr-27	54.0d
6413	RI-AP12-120	Install Low Voltage OH Rough-in - Overall Rough-in- INTR - AP 12	10.0d	9-Apr-27	22-Apr-27	108.0d
6414	RI-AP12-5440	Install BAS OH Rough-in - Overall Rough-in- INTR - AP 12	10.0d	9-Apr-27	22-Apr-27	64.0d
6415	RI-AP12-130	Frame & Top-Down Walls - Overall Rough-in- INTR - AP 12	10.0d	23-Apr-27	6-May-27	108.0d
6416	RI-AP12-140	Install HM Door Frames - Overall Rough-in- INTR - AP 12	3.0d	23-Apr-27	27-Apr-27	108.0d
6417	RI-AP12-5450	Pull BAS Cable - Overall Rough-in- INTR - AP 12	10.0d	23-Apr-27	6-May-27	188.0d
6418	RI-AP12-160	Elec. Rough-in Walls - Overall Rough-in- INTR - AP 12	10.0d	28-Apr-27	11-May-27	108.0d
6419	RI-AP12-150	Low Voltage Rough-in Walls - Overall Rough-in- INTR - AP 12	3.0d	12-May-27	14-May-27	108.0d
6420	RI-AP12-5430	Pull & Terminate Low Volt Cabling - Overall Rough-in- INTR - AP 12	7.0d	17-May-27	25-May-27	153.0d
6421	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mechanical (CUP) - Apron 12		320.0d	20-Nov-26	25-Feb-28	188.0d
6422	WBS - CUP - INTRF - CUP Room 6079 - Apron 12		320.0d	20-Nov-26	25-Feb-28	188.0d
6423	WBS - Infrastructure, Buildout - INTRF - CUP Room 6079 - AP12		320.0d	20-Nov-26	25-Feb-28	188.0d
6424	RI-AP12-CP-5090	Layout Walls/Top Track - INTRF - CUP Room 6079 - AP12	5.0d	20-Nov-26	30-Nov-26	243.0d
6425	RI-AP12-CP-5230	Install HM Door Frames - INTRF - CUP Room 6079 - AP12	3.0d	1-Dec-26	3-Dec-26	245.0d
6426	RI-AP12-CP-5380	Install CMU Walls - INTRF - CUP Room 6079 - AP12	10.0d	1-Dec-26	14-Dec-26	243.0d

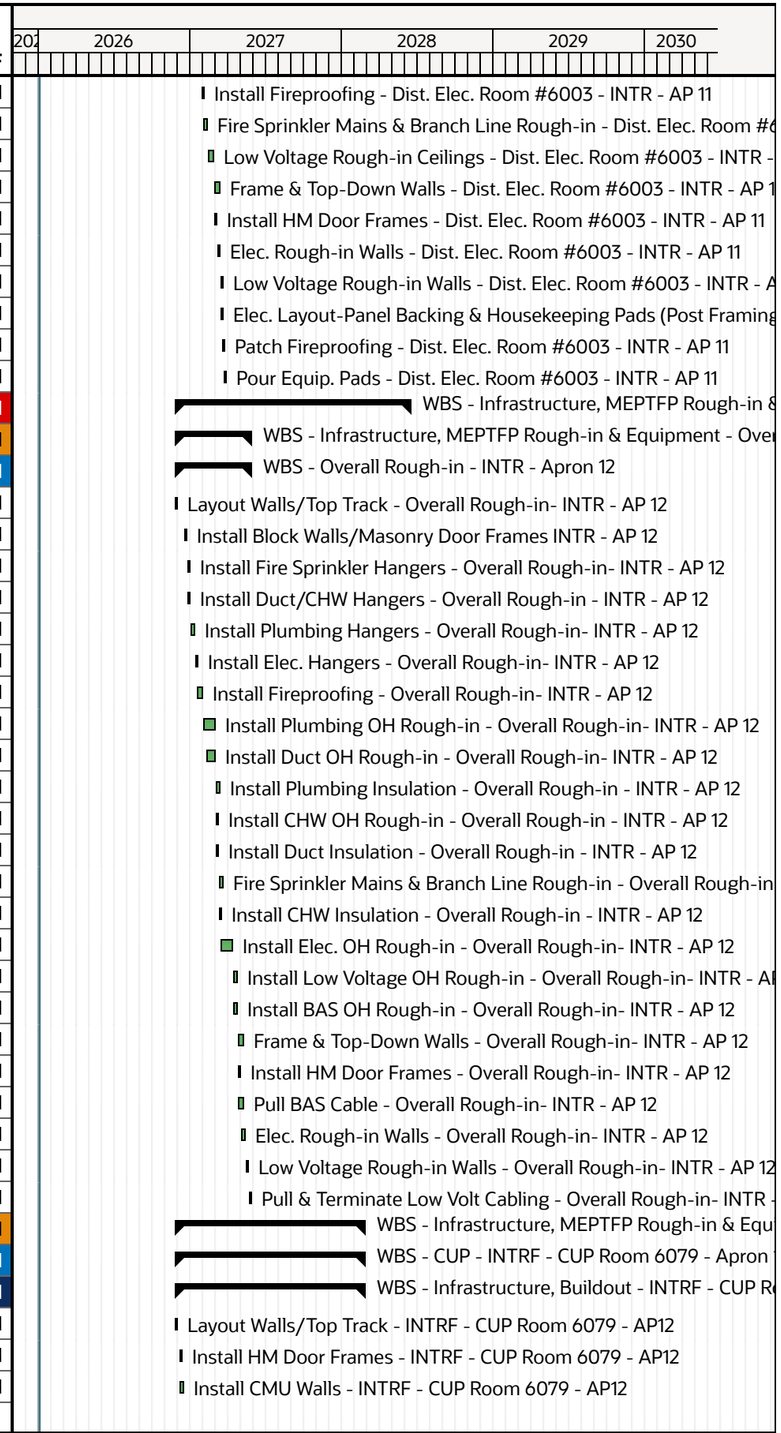

	ID	Name	Dur	Start	Finish	TF
6427	RI-AP12-CP-5240	Elec. Rough-in Walls - INTRF - CUP Room 6079 - AP12	3.0d	4-Dec-26	8-Dec-26	245.0d
6428	RI-AP12-CP-5250	Low Voltage Rough-in Walls - INTRF - CUP Room 6079 - AP12	3.0d	4-Dec-26	8-Dec-26	245.0d
6429	RI-AP12-CP-5100	Install Fire Sprinkler Hangers - INTRF - CUP Room 6079 - AP12	2.0d	11-Dec-26	14-Dec-26	243.0d
6430	RI-AP12-CP-5110	Install Duct/CHW Hangers - INTRF - CUP Room 6079 - AP12	2.0d	11-Dec-26	14-Dec-26	243.0d
6431	RI-AP12-CP-5120	Install Plumbing Hangers - INTRF - CUP Room 6079 - AP12	2.0d	15-Dec-26	16-Dec-26	243.0d
6432	RI-AP12-CP-5130	Install Elec. Hangers - INTRF - CUP Room 6079 - AP12	2.0d	17-Dec-26	18-Dec-26	243.0d
6433	RI-AP12-CP-5140	Install Fireproofing - INTRF - CUP Room 6079 - AP12	5.0d	15-Jan-27	21-Jan-27	226.0d
6434	RI-AP12-CP-5190	Fire Sprinkler Mains & Branch Line Rough-in - INTRF - CUP Room 6079 - AP12	10.0d	22-Jan-27	4-Feb-27	226.0d
6435	RI-AP12-CP-5180	Install Duct & CHW OH Rough-in - INTRF - CUP Room 6079 - AP12	15.0d	5-Feb-27	25-Feb-27	226.0d
6436	RI-AP12-CP-5150	Install Plumbing OH Rough-in - INTRF - CUP Room 6079 - AP12	5.0d	26-Feb-27	4-Mar-27	226.0d
6437	RI-AP12-CP-5160	Insulate OH Duct - Infrastructure, MEPTFP Rough-in & Equip. - CUP	5.0d	26-Feb-27	4-Mar-27	249.0d
6438	RI-AP12-CP-5170	Insulate OH CHW - Infrastructure, MEPTFP Rough-in & Equip. - CUP	5.0d	26-Feb-27	4-Mar-27	249.0d
6439	RI-AP12-CP-5200	Install Elec. OH Rough-in - INTRF - CUP Room 6079 - AP12	20.0d	5-Mar-27	1-Apr-27	226.0d
6440	RI-AP12-CP-5205	Insulate OH Plumbing - Infrastructure, MEPTFP Rough-in & Equip. - CUP	5.0d	12-Mar-27	18-Mar-27	239.0d
6441	RI-AP12-CP-5210	Install Low Voltage OH Rough-in - INTRF - CUP Room 6079 - AP12	3.0d	2-Apr-27	6-Apr-27	226.0d
6442	RI-AP12-CP-5290	Firestopping - INTRF - CUP Room 6079 - AP12	2.0d	7-Apr-27	8-Apr-27	410.0d
6443	RI-AP12-CP-5295	Pour Pads (Pump, Boiler, Chiller, Condenser) - Infrastructure, MEPTFP Rough-in...	10.0d	7-Apr-27	20-Apr-27	226.0d
6444	RI-AP12-CP-5350	Cure & Epoxy Pads - Infrastructure, MEPTFP Rough-in & Equip. - CUP Room 60...	7.0d	21-Apr-27	29-Apr-27	226.0d
6445	RI-AP12-CP-5340	Seal Concrete - INTRF - CUP Room 6079 - AP12	2.0d	27-Apr-27	28-Apr-27	398.0d
6446	RI-AP12-CP-5360	Set Pumps - Infrastructure, MEPTFP Rough-in & Equip. - CUP Room 6079 - AP12	5.0d	30-Apr-27	6-May-27	226.0d
6447	RI-AP12-CP-5370	Set Chillers - Infrastructure, MEPTFP Rough-in & Equip. - CUP Room 6079 - AP12	10.0d	7-May-27	20-May-27	226.0d
6448	RI-AP12-CP-5390	Install (Boilers, Condensers) - Infrastructure, MEPTFP Rough-in & Equip. - CUP ...	20.0d	21-May-27	18-Jun-27	226.0d
6449	RI-AP12-CP-5400	Chilled Water Avail - Fill & Flush - Infrastructure, MEPTFP Rough-in & Equip. - C...	20.0d	18-Nov-27	17-Dec-27	100.0d
6450	RI-AP12-CP-5410	Condenser Avail - Fill & Flush - Infrastructure, MEPTFP Rough-in & Equip. - CU...	15.0d	20-Dec-27	11-Jan-28	100.0d
6451	RI-AP12-CP-5420	HHW Avail - Fill & Flush - Infrastructure, MEPTFP Rough-in & Equip. - CUP Roo...	15.0d	12-Jan-28	1-Feb-28	100.0d
6452	RI-AP12-CP-5430	Final Tie in & Install Meters & Gauges - Infrastructure, MEPTFP Rough-in & Equ...	15.0d	2-Feb-28	22-Feb-28	108.0d
6453	RI-AP12-CP-5440	Glycol Available - Fill & Flush - Infrastructure, MEPTFP Rough-in & Equip. - CUP...	15.0d	2-Feb-28	22-Feb-28	100.0d
6454	RI-AP12-CP-5450	Start-up AHU - Mech. Room - INTF - CUP Room 6079 - AP12	3.0d	23-Feb-28	25-Feb-28	108.0d
6455	WBS - Infrastructure, MEPTFP Rough-in & Equipment - IDF - Apron 12		393.0d	25-Nov-26	13-Jun-28	94.0d
6456	WBS - Tenant IDF 6046 - INTRF - Alias ASD 01681 - Apron 12		375.0d	2-Dec-26	22-May-28	109.0d
6457	RI-AP12-IDF-4510	Layout Walls/Top Track - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	2-Dec-26	8-Dec-26	137.0d
6458	RI-AP12-IDF-4520	Install Fire Sprinkler Hangers - Tenant IDF 6046 - INTRF - Alias ASD 01681 - A...	2.0d	9-Dec-26	10-Dec-26	137.0d
6459	RI-AP12-IDF-4530	Install Duct/CHW Hangers - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	11-Dec-26	14-Dec-26	137.0d
6460	RI-AP12-IDF-4540	Install Plumbing Hangers - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	20.0d	15-Dec-26	13-Jan-27	137.0d
6461	RI-AP12-IDF-4550	Install Elec. Hangers - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	14-Jan-27	15-Jan-27	137.0d
6462	RI-AP12-IDF-4560	Install Fireproofing - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	18-Jan-27	19-Jan-27	137.0d
6463	RI-AP12-IDF-4570	Install Plumbing OH Rough-in - Tenant IDF 6046 - INTRF - Alias ASD 01681 - A...	20.0d	20-Jan-27	16-Feb-27	137.0d
6464	RI-AP12-IDF-4590	Install Duct & CHW OH Rough-in - Tenant IDF 6046 - INTRF - Alias ASD 01681 ...	15.0d	27-Jan-27	16-Feb-27	137.0d
6465	RI-AP12-IDF-4600	Install Mech. Equipment - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	15.0d	27-Jan-27	16-Feb-27	137.0d
6466	RI-AP12-IDF-4610	Fire Sprinkler Mains & Branch Line Rough-in - Tenant IDF 6046 - INTRF - Alias ...	10.0d	3-Feb-27	16-Feb-27	137.0d
6467	RI-AP12-IDF-4620	Install Elec. OH Rough-in - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	20.0d	10-Feb-27	9-Mar-27	137.0d
6468	RI-AP12-IDF-4630	Install Low Voltage OH Rough-in - Tenant IDF 6046 - INTRF - Alias ASD 01681 ...	3.0d	10-Mar-27	12-Mar-27	137.0d

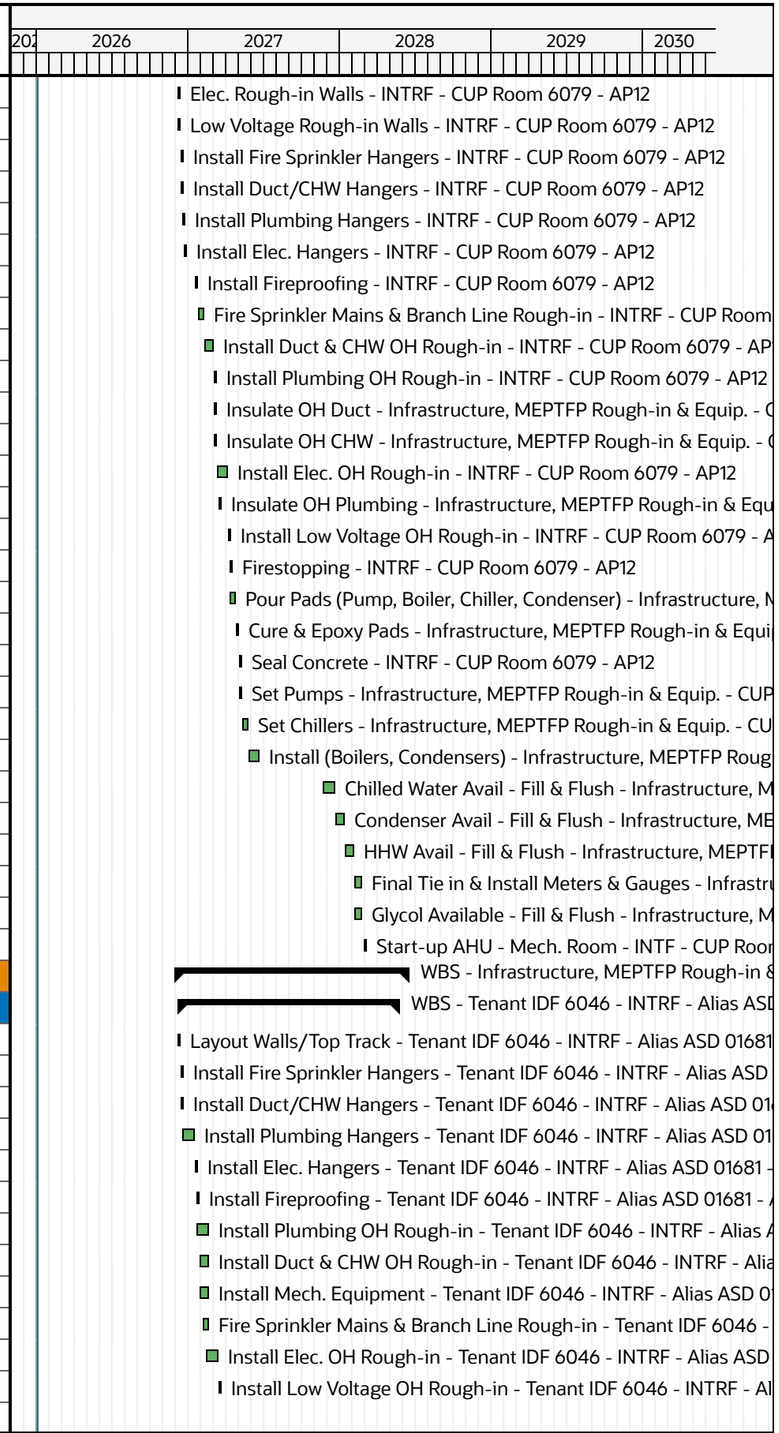


	ID	Name	Dur	Start	Finish	TF
6469	RI-AP12-IDF-4646	Frame & Top-Down Walls - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	10.0d	15-Mar-27	26-Mar-27	137.0d
6470	RI-AP12-IDF-4650	Install HM Door Frames - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	3.0d	15-Mar-27	17-Mar-27	144.0d
6471	RI-AP12-IDF-4660	Elec. Rough-in Walls - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	3.0d	29-Mar-27	31-Mar-27	137.0d
6472	RI-AP12-IDF-4670	Low Voltage Rough-in Walls - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP ...	3.0d	1-Apr-27	5-Apr-27	137.0d
6473	RI-AP12-IDF-4680	Low Voltage/Elect. in Wall Inspection (COT) - Tenant IDF 6046 - INTRF - Alias A...	2.0d	6-Apr-27	7-Apr-27	137.0d
6474	RI-AP12-IDF-4690	Hang, Tape & Finish Drywall - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP ...	5.0d	25-Aug-27	31-Aug-27	40.0d
6475	RI-AP12-IDF-4700	Prime & First Coat - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	1-Sep-27	2-Sep-27	215.0d
6476	RI-AP12-IDF-4710	Firestopping - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	3-Sep-27	7-Sep-27	215.0d
6477	RI-AP12-IDF-5090	Install FCUs-1-6046 - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	3-Sep-27	10-Sep-27	233.0d
6478	RI-AP12-IDF-5200	Install Door & Hardware - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	3.0d	3-Sep-27	8-Sep-27	254.0d
6479	RI-AP12-IDF-4720	Install Tech Room Backerboard - Tenant IDF 6046 - INTRF - Alias ASD 01681 - ...	2.0d	8-Sep-27	9-Sep-27	215.0d
6480	RI-AP12-IDF-4730	Set Racks - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	10.0d	10-Sep-27	23-Sep-27	215.0d
6481	RI-AP12-IDF-5150	Install Ladder Rack - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	3.0d	24-Sep-27	28-Sep-27	215.0d
6482	RI-AP12-IDF-4740	Pull & Terminate Fiber - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	20.0d	29-Sep-27	26-Oct-27	215.0d
6483	RI-AP12-IDF-4750	Trim-Out Low Voltage - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	27-Oct-27	2-Nov-27	215.0d
6484	RI-AP12-IDF-4760	Install Flooring - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	2.0d	3-Nov-27	4-Nov-27	215.0d
6485	RI-AP12-IDF-4770	Low Voltage Testing - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	10.0d	5-Nov-27	18-Nov-27	220.0d
6486	RI-AP12-IDF-5130	Install Rubber Base - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	5-Nov-27	11-Nov-27	215.0d
6487	RI-AP12-IDF-5160	Apply Final Paint - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	12-Nov-27	18-Nov-27	215.0d
6488	RI-AP12-IDF-5100	FCU Start Up - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	5.0d	21-Apr-28	27-Apr-28	109.0d
6489	RI-AP12-IDF-4780	Owner's Acceptance Walkthrough - Tenant IDF 6046 - INTRF - Alias ASD 0168...	2.0d	28-Apr-28	1-May-28	109.0d
6490	RI-AP12-IDF-4790	Owner Equipment Install - Tenant IDF 6046 - INTRF - Alias ASD 01681 - AP 12	15.0d	2-May-28	22-May-28	109.0d
6491	WBS - HCAA IDF 6047 - INTRF - Alias ASD 01680 - Apron 12		393.0d	25-Nov-26	13-Jun-28	82.0d
6492	RI-AP12-IDF-4800	Layout Walls/Top Track - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	25-Nov-26	3-Dec-26	137.0d
6493	RI-AP12-IDF-4810	Install Fire Sprinkler Hangers - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP ...	2.0d	4-Dec-26	7-Dec-26	158.0d
6494	RI-AP12-IDF-4820	Install Duct/CHW Hangers - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	8-Dec-26	9-Dec-26	158.0d
6495	RI-AP12-IDF-4830	Install Plumbing Hangers - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	10-Dec-26	11-Dec-26	158.0d
6496	RI-AP12-IDF-4840	Install Elec. Hangers - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	14-Dec-26	15-Dec-26	158.0d
6497	RI-AP12-IDF-4850	Install Fireproofing - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	15-Jan-27	18-Jan-27	138.0d
6498	RI-AP12-IDF-4860	Install Plumbing OH Rough-in - HCAA IDF 6047 - INTRF - Alias ASD 01680 - A...	10.0d	19-Jan-27	1-Feb-27	138.0d
6499	RI-AP12-IDF-4880	Install Duct & CHW OH Rough-in - HCAA IDF 6047 - INTRF - Alias ASD 01680 -...	15.0d	26-Jan-27	15-Feb-27	138.0d
6500	RI-AP12-IDF-4890	Install Mech. Equip. - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	15.0d	26-Jan-27	15-Feb-27	138.0d
6501	RI-AP12-IDF-4900	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6047 - INTRF - Alias ...	10.0d	2-Feb-27	15-Feb-27	138.0d
6502	RI-AP12-IDF-4910	Install Elec. OH Rough-in - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	20.0d	9-Feb-27	8-Mar-27	138.0d
6503	RI-AP12-IDF-4920	Install Low Voltage OH Rough-in - HCAA IDF 6047 - INTRF - Alias ASD 01680 -...	3.0d	9-Mar-27	11-Mar-27	138.0d
6504	RI-AP12-IDF-4930	Frame & Top-Down Walls - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	10.0d	12-Mar-27	25-Mar-27	138.0d
6505	RI-AP12-IDF-4940	Install HM Door Frames - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	3.0d	12-Mar-27	16-Mar-27	145.0d
6506	RI-AP12-IDF-4950	Elec. Rough-in Walls - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	3.0d	26-Mar-27	30-Mar-27	138.0d
6507	RI-AP12-IDF-4960	Low Voltage Rough-in Walls - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	3.0d	31-Mar-27	2-Apr-27	138.0d
6508	RI-AP12-IDF-4970	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6047 - INTRF - Alias AS...	2.0d	5-Apr-27	6-Apr-27	138.0d
6509	RI-AP12-IDF-4980	Hang, Tape & Finish Drywall - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	14-Oct-27	20-Oct-27	5.0d
6510	RI-AP12-IDF-4990	Prime & First Coat - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	21-Oct-27	22-Oct-27	172.0d

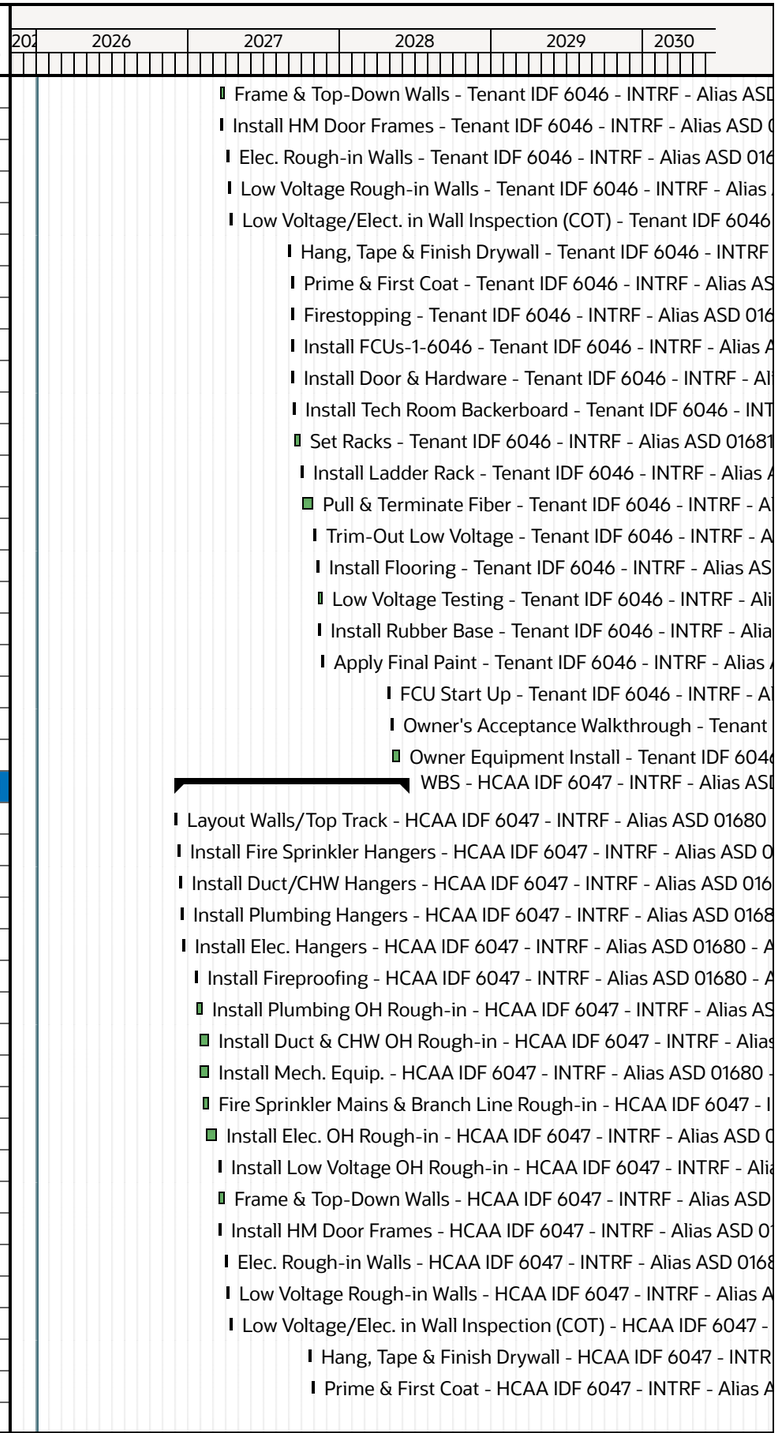


	ID	Name	Dur	Start	Finish	TF
6511	RI-AP12-IDF-5000	Firestopping - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	25-Oct-27	26-Oct-27	172.0d
6512	RI-AP12-IDF-5110	Install FCUs-1-6047 - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	25-Oct-27	29-Oct-27	220.0d
6513	RI-AP12-IDF-5210	Install Door & Hardware - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	3.0d	25-Oct-27	27-Oct-27	210.0d
6514	RI-AP12-IDF-5010	Install Tech Room Backerboard - HCAA IDF 6047 - INTRF - Alias ASD 01680 - A...	2.0d	27-Oct-27	28-Oct-27	172.0d
6515	RI-AP12-IDF-5020	Set Racks - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	10.0d	29-Oct-27	11-Nov-27	172.0d
6516	RI-AP12-IDF-5170	Install Ladder Rack - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	12-Nov-27	15-Nov-27	172.0d
6517	RI-AP12-IDF-5030	Pull & Terminate Fiber - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	20.0d	16-Nov-27	15-Dec-27	172.0d
6518	RI-AP12-IDF-5190	Pull & Terminate Fiber for PBB D46, D47 - HCAA IDF 6047 - INTRF - Alias ASD ...	20.0d	16-Nov-27	15-Dec-27	172.0d
6519	RI-AP12-IDF-5040	Trim-Out Low Voltage - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	16-Dec-27	22-Dec-27	172.0d
6520	RI-AP12-IDF-5050	Install Flooring - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	23-Dec-27	27-Dec-27	172.0d
6521	RI-AP12-IDF-5060	Low Voltage Testing - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	10.0d	28-Dec-27	11-Jan-28	174.0d
6522	RI-AP12-IDF-5140	Install Rubber Base - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	28-Dec-27	4-Jan-28	172.0d
6523	RI-AP12-IDF-5180	Apply Final Paint - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	5.0d	5-Jan-28	11-Jan-28	172.0d
6524	RI-AP12-IDF-5120	FCU Start Up - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	2.0d	21-Apr-28	24-Apr-28	100.0d
6525	RI-AP12-IDF-5070	Owner's Acceptance Walkthrough - HCAA IDF 6047 - INTRF - Alias ASD 01680 ...	2.0d	25-Apr-28	26-Apr-28	100.0d
6526	RI-AP12-IDF-5080	Owner Equip. Install - HCAA IDF 6047 - INTRF - Alias ASD 01680 - AP 12	15.0d	23-May-28	13-Jun-28	82.0d
6527	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Level		181.0d	13-Jan-27	27-Sep-27	198.0d
6528	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Corridor 6		96.0d	12-May-27	27-Sep-27	198.0d
6529	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Sterile Corridor 6		96.0d	12-May-27	27-Sep-27	198.0d
6530	RI-SC6-4090	Layout Walls/Top Track - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	12-May-27	25-May-27	194.0d
6531	RI-SC6-4100	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Sterile Corr. 6	2.0d	26-May-27	27-May-27	194.0d
6532	RI-SC6-4110	Install Elec. Hangers - Overall Rough-in - INTR - Sterile Corr. 6	2.0d	26-May-27	27-May-27	194.0d
6533	RI-SC6-4120	Install Fireproofing - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	28-May-27	11-Jun-27	194.0d
6534	RI-SC6-4140	Install Elec. OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 6	20.0d	14-Jul-27	10-Aug-27	173.0d
6535	RI-SC6-4130	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Sterile ...	10.0d	11-Aug-27	24-Aug-27	173.0d
6536	RI-SC6-4150	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 6	3.0d	11-Aug-27	13-Aug-27	180.0d
6537	RI-SC6-4210	Install BAS OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	11-Aug-27	24-Aug-27	173.0d
6538	RI-SC6-4160	Frame & Top-Down Walls - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	25-Aug-27	8-Sep-27	173.0d
6539	RI-SC6-4170	Install HM Door Frames - Overall Rough-in - INTR - Sterile Corr. 6	3.0d	25-Aug-27	27-Aug-27	180.0d
6540	RI-SC6-4220	Pull BAS Cable - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	25-Aug-27	8-Sep-27	211.0d
6541	RI-SC6-4180	Elec. Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 6	10.0d	9-Sep-27	22-Sep-27	173.0d
6542	RI-SC6-4200	Install Signage Blocking/Backing - Overall Rough-in - INTR - Sterile Corr. 6	3.0d	9-Sep-27	13-Sep-27	183.0d
6543	RI-SC6-4190	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 6	3.0d	23-Sep-27	27-Sep-27	173.0d
6544	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Corridor 7		86.0d	28-Apr-27	27-Aug-27	164.0d
6545	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Sterile Corridor 7		86.0d	28-Apr-27	27-Aug-27	164.0d
6546	RI-SC7-4200	Layout Walls/Top Track - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	28-Apr-27	11-May-27	145.0d
6547	RI-SC7-4210	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Sterile Corr. 7	2.0d	12-May-27	13-May-27	145.0d
6548	RI-SC7-4220	Install Elec. Hangers - Overall Rough-in - INTR - Sterile Corr. 7	2.0d	12-May-27	13-May-27	145.0d
6549	RI-SC7-4230	Install Fireproofing - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	14-May-27	27-May-27	145.0d
6550	RI-SC7-4250	Install Elec. OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 7	20.0d	15-Jun-27	13-Jul-27	134.0d
6551	RI-SC7-4240	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Sterile ...	10.0d	14-Jul-27	27-Jul-27	134.0d
6552	RI-SC7-4260	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 7	3.0d	14-Jul-27	16-Jul-27	141.0d




	ID	Name	Dur	Start	Finish	TF
6553	RI-SC7-4340	Install BAS OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	14-Jul-27	27-Jul-27	134.0d
6554	RI-SC7-4270	Frame & Top-Down Walls - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	28-Jul-27	10-Aug-27	134.0d
6555	RI-SC7-4280	Install HM Door Frames - Overall Rough-in - INTR - Sterile Corr. 7	3.0d	28-Jul-27	30-Jul-27	141.0d
6556	RI-SC7-4350	Pull BAS Cable - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	28-Jul-27	10-Aug-27	177.0d
6557	RI-SC7-4290	Elec. Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 7	10.0d	11-Aug-27	24-Aug-27	134.0d
6558	RI-SC7-4330	Install Signage Blocking/Backing - Overall Rough-in - INTR - Sterile Corr. 7	3.0d	11-Aug-27	13-Aug-27	144.0d
6559	RI-SC7-4300	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 7	3.0d	25-Aug-27	27-Aug-27	134.0d
6560	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Corridor 8		85.0d	1-Apr-27	30-Jul-27	163.0d
6561	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Sterile Corridor 8		85.0d	1-Apr-27	30-Jul-27	163.0d
6562	RI-SC8-4310	Layout Walls/Top Track - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	1-Apr-27	14-Apr-27	144.0d
6563	RI-SC8-4320	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Sterile Corr. 8	2.0d	15-Apr-27	16-Apr-27	144.0d
6564	RI-SC8-4330	Install Elec. Hangers - Overall Rough-in - INTR - Sterile Corr. 8	2.0d	15-Apr-27	16-Apr-27	144.0d
6565	RI-SC8-4340	Install Fireproofing - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	19-Apr-27	30-Apr-27	144.0d
6566	RI-SC8-4360	Install Elec. OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 8	20.0d	17-May-27	14-Jun-27	134.0d
6567	RI-SC8-4350	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Sterile ...	10.0d	15-Jun-27	28-Jun-27	135.0d
6568	RI-SC8-4370	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 8	3.0d	15-Jun-27	17-Jun-27	142.0d
6569	RI-SC8-4430	Install BAS OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	15-Jun-27	28-Jun-27	135.0d
6570	RI-SC8-4380	Frame & Top-Down Walls - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	29-Jun-27	13-Jul-27	135.0d
6571	RI-SC8-4390	Install HM Door Frames - Overall Rough-in - INTR - Sterile Corr. 8	3.0d	29-Jun-27	1-Jul-27	142.0d
6572	RI-SC8-4440	Pull BAS Cable - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	29-Jun-27	13-Jul-27	176.0d
6573	RI-SC8-4400	Elec. Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 8	10.0d	14-Jul-27	27-Jul-27	135.0d
6574	RI-SC8-4420	Install Signage Blocking/Backing - Overall Rough-in - INTR - Sterile Corr. 8	3.0d	14-Jul-27	16-Jul-27	145.0d
6575	RI-SC8-4450	Install 1/2" Plywood Backing for GL07E/GLOZD - Overall Rough-in - INTR - Ste...	10.0d	14-Jul-27	27-Jul-27	135.0d
6576	RI-SC8-4410	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 8	3.0d	28-Jul-27	30-Jul-27	135.0d
6577	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Corridor 9		75.0d	18-Mar-27	1-Jul-27	162.0d
6578	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Sterile Corridor 9		75.0d	18-Mar-27	1-Jul-27	162.0d
6579	RI-SC9-4420	Layout Walls/Top Track - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	18-Mar-27	31-Mar-27	134.0d
6580	RI-SC9-4430	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Sterile Corr. 9	2.0d	1-Apr-27	2-Apr-27	134.0d
6581	RI-SC9-4440	Install Elec. Hangers - Overall Rough-in - INTR - Sterile Corr. 9	2.0d	1-Apr-27	2-Apr-27	134.0d
6582	RI-SC9-4450	Install Fireproofing - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	5-Apr-27	16-Apr-27	134.0d
6583	RI-SC9-4470	Install Elec. OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 9	20.0d	19-Apr-27	14-May-27	134.0d
6584	RI-SC9-4460	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Sterile ...	10.0d	17-May-27	28-May-27	135.0d
6585	RI-SC9-4480	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 9	3.0d	17-May-27	19-May-27	142.0d
6586	RI-SC9-4540	Install BAS OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	17-May-27	28-May-27	135.0d
6587	RI-SC9-4490	Frame & Top-Down Walls - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	1-Jun-27	14-Jun-27	135.0d
6588	RI-SC9-4500	Install HM Door Frames - Overall Rough-in - INTR - Sterile Corr. 9	3.0d	1-Jun-27	3-Jun-27	159.0d
6589	RI-SC9-4550	Pull BAS Cable - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	1-Jun-27	14-Jun-27	175.0d
6590	RI-SC9-4510	Elec. Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 9	10.0d	15-Jun-27	28-Jun-27	135.0d
6591	RI-SC9-4530	Install Signage Blocking/Backing - Overall Rough-in - INTR - Sterile Corr. 9	3.0d	15-Jun-27	17-Jun-27	145.0d
6592	RI-SC9-4520	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 9	3.0d	29-Jun-27	1-Jul-27	135.0d
6593	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Sterile Corridor 11		75.0d	13-Jan-27	27-Apr-27	182.0d
6594	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Overall - Sterile Corridor 11		75.0d	13-Jan-27	27-Apr-27	182.0d

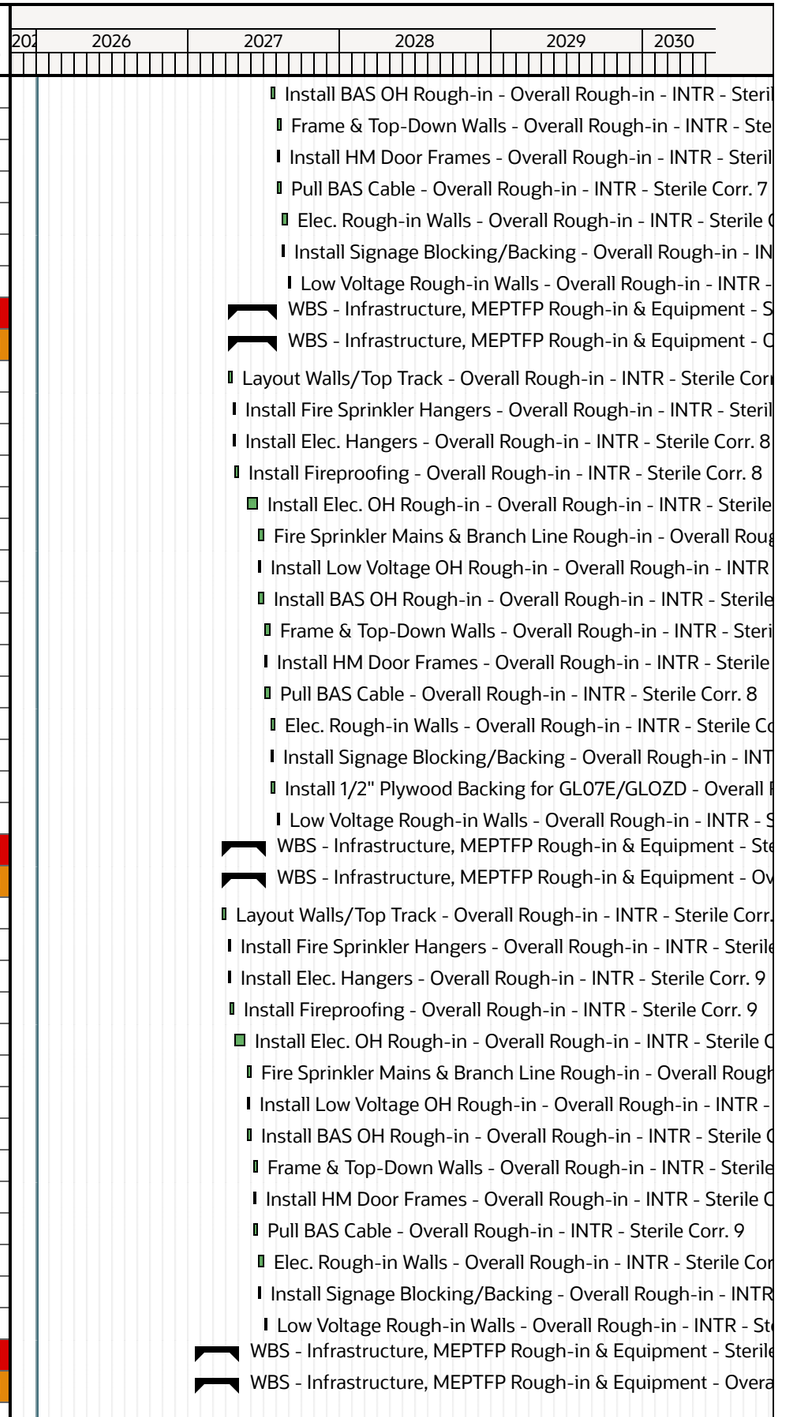


	ID	Name	Dur	Start	Finish	TF
6595	RI-SC11-4530	Layout Walls/Top Track - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	13-Jan-27	26-Jan-27	156.0d
6596	RI-SC11-4540	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Sterile Corr. 11	2.0d	27-Jan-27	28-Jan-27	156.0d
6597	RI-SC11-4550	Install Elec. Hangers - Overall Rough-in - INTR - Sterile Corr. 11	2.0d	27-Jan-27	28-Jan-27	156.0d
6598	RI-SC11-4560	Install Fireproofing - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	29-Jan-27	11-Feb-27	156.0d
6599	RI-SC11-4580	Install Elec. OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 11	20.0d	12-Feb-27	11-Mar-27	156.0d
6600	RI-SC11-4670	Install BAS OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	12-Feb-27	25-Feb-27	176.0d
6601	RI-SC11-4680	Pull BAS Cable - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	26-Feb-27	11-Mar-27	215.0d
6602	RI-SC11-4570	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Sterile ...	10.0d	12-Mar-27	25-Mar-27	156.0d
6603	RI-SC11-4590	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Sterile Corr. 11	3.0d	12-Mar-27	16-Mar-27	163.0d
6604	RI-SC11-4600	Frame & Top-Down Walls - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	26-Mar-27	8-Apr-27	156.0d
6605	RI-SC11-4610	Install HM Door Frames - Overall Rough-in - INTR - Sterile Corr. 11	3.0d	26-Mar-27	30-Mar-27	202.0d
6606	RI-SC11-4620	Elec. Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 11	10.0d	9-Apr-27	22-Apr-27	156.0d
6607	RI-SC11-4660	Install Signage Blocking/Backing - Overall Rough-in - INTR - Sterile Corr. 11	3.0d	9-Apr-27	13-Apr-27	166.0d
6608	RI-SC11-4630	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Sterile Corr. 11	3.0d	23-Apr-27	27-Apr-27	156.0d
6609	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Concourse Level		431.0d	8-Sep-26	17-May-28	112.0d
6610	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Concourse 1		387.0d	9-Nov-26	17-May-28	86.0d
6611	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 1		184.0d	9-Nov-26	30-Jul-27	188.0d
6612	WBS - Overall Rough-in - INTR - Conc. 1		184.0d	9-Nov-26	30-Jul-27	188.0d
6613	RI-C1-1220	Layout Walls/Top Track - Overall Rough-in - INTR - C1	10.0d	9-Nov-26	20-Nov-26	71.0d
6614	RI-C1-1230	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C1	5.0d	23-Nov-26	1-Dec-26	71.0d
6615	RI-C1-1460	Install Mech. Hangers - Overall Rough-in - INTR - C1	5.0d	2-Dec-26	8-Dec-26	71.0d
6616	RI-C1-1240	Install Elec. Hangers - Overall Rough-in - INTR - C1	5.0d	9-Dec-26	15-Dec-26	71.0d
6617	RI-C1-1250	Install Plumbing Hangers - Overall Rough-in - INTR - C1	2.0d	16-Dec-26	17-Dec-26	71.0d
6618	RI-C1-1260	Install Fireproofing - Overall Rough-in - INTR - C1	5.0d	19-Jan-27	25-Jan-27	51.0d
6619	RI-C1-1270	Install Duct OH Rough-in - Overall Rough-in - INTR - C1	15.0d	2-Feb-27	22-Feb-27	46.0d
6620	RI-C1-1290	Install Plumbing OH Rough-in - Overall Rough-in - INTR - C1	5.0d	23-Feb-27	1-Mar-27	46.0d
6621	RI-C1-1450	Install CHW OH Rough-in - Overall Rough-in - INTR - C1	15.0d	2-Mar-27	22-Mar-27	46.0d
6622	RI-C1-1320	Install Elec. OH Rough-in - Overall Rough-in - INTR - C1	20.0d	23-Mar-27	19-Apr-27	46.0d
6623	RI-C1-1350	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C1	10.0d	20-Apr-27	3-May-27	46.0d
6624	RI-C1-1480	Install BAS OH Rough-in - Overall Rough-in - INTR - C1	10.0d	20-Apr-27	3-May-27	46.0d
6625	RI-C1-1360	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C1	10.0d	4-May-27	17-May-27	46.0d
6626	RI-C1-1490	Pull BAS Cable - Overall Rough-in - INTR - C1	10.0d	4-May-27	17-May-27	240.0d
6627	RI-C1-1330	Install Plumbing Insulation - Overall Rough-in - INTR - C1	5.0d	18-May-27	24-May-27	61.0d
6628	RI-C1-1340	Install Duct Insulation - Overall Rough-in - INTR - C1	5.0d	18-May-27	24-May-27	61.0d
6629	RI-C1-1370	Frame & Top-Down Walls - Overall Rough-in - INTR - C1	10.0d	18-May-27	1-Jun-27	46.0d
6630	RI-C1-1400	Install HM Door Frames - Overall Rough-in - INTR - C1	5.0d	18-May-27	24-May-27	61.0d
6631	RI-C1-1380	Frame Ceiling(Stairs) - Overall Rough-in - INTR - C1	10.0d	2-Jun-27	15-Jun-27	46.0d
6632	RI-C1-1390	Install Plumbing Rough-in Walls Overall Rough-in - INTR - C1	5.0d	16-Jun-27	22-Jun-27	46.0d
6633	RI-C1-1410	Elec. Rough-in Walls - Overall Rough-in - INTR - C1	5.0d	23-Jun-27	29-Jun-27	46.0d
6634	RI-C1-1420	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C1	5.0d	30-Jun-27	7-Jul-27	46.0d
6635	RI-C1-1470	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - C1	5.0d	8-Jul-27	14-Jul-27	46.0d
6636	RI-C1-1430	Patch Fireproofing - Overall Rough-in - INTR - C1	2.0d	15-Jul-27	16-Jul-27	46.0d

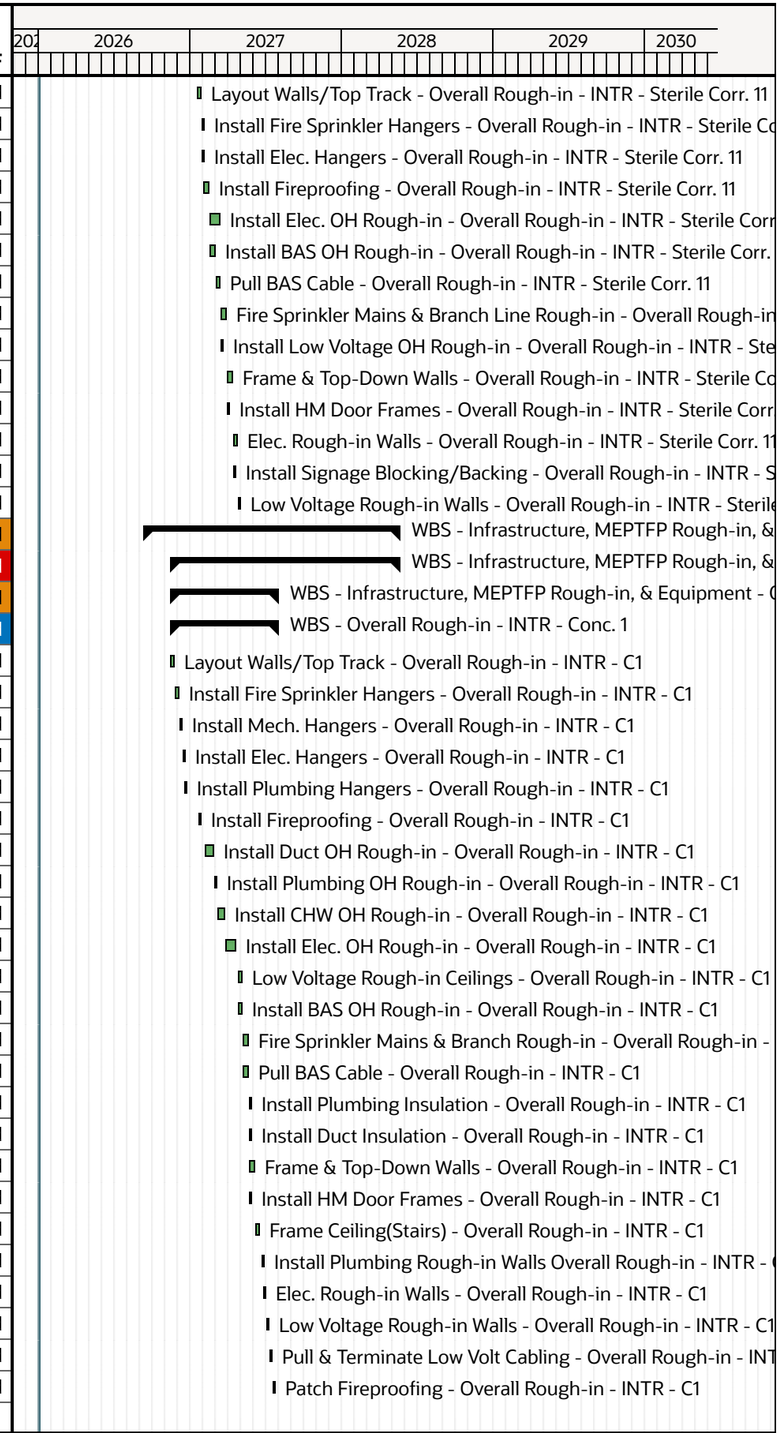


	ID	Name	Dur	Start	Finish	TF
6637	RI-C1-1440	Install Wall Insulation - Overall Rough-in - INTR - C1	3.0d	28-Jul-27	30-Jul-27	39.0d
6638	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - MDF - INTRF - Conc. 1		377.0d	23-Nov-26	17-May-28	86.0d
6639	WBS - HCAA MDF 6454 - INTRF - Alias ASD 02180 - Conc. 1		377.0d	23-Nov-26	17-May-28	85.0d
6640	RI-C1-MDF-6300	Layout Walls/Top Track - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	23-Nov-26	1-Dec-26	161.0d
6641	RI-C1-MDF-7350	Install Fire Sprinkler Hangers - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	2-Dec-26	8-Dec-26	167.0d
6642	RI-C1-MDF-7360	Install Elec. Hangers - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	9-Dec-26	15-Dec-26	167.0d
6643	RI-C1-MDF-7250	Install Fireproofing - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	15-Jan-27	18-Jan-27	147.0d
6644	RI-C1-MDF-6310	Fire Sprinkler Mains & Branch Line Rough-in - HCAA MDF 6454 - INTRF - Alias ...	5.0d	19-Jan-27	25-Jan-27	147.0d
6645	RI-C1-MDF-7230	Install Elec. OH Rough-in - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	10.0d	26-Jan-27	8-Feb-27	147.0d
6646	RI-C1-MDF-7240	Install Low Voltage OH Rough-in - HCAA MDF 6454 - INTRF - Alias ASD 02180...	5.0d	9-Feb-27	15-Feb-27	147.0d
6647	RI-C1-MDF-7190	Install HM Door Frames - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	16-Feb-27	17-Feb-27	376.0d
6648	RI-C1-MDF-7170	Frame & Top-Down Walls - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	16-Feb-27	22-Feb-27	147.0d
6649	RI-C1-MDF-7180	Elec. Rough-in Walls - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	23-Feb-27	1-Mar-27	147.0d
6650	RI-C1-MDF-7300	Low Voltage Rough-in Walls - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	2-Mar-27	8-Mar-27	147.0d
6651	RI-C1-MDF-7310	Low Voltage/Elec. in Wall Inspection (COT) - HCAA MDF 6454 - INTRF - Alias A...	2.0d	9-Mar-27	10-Mar-27	147.0d
6652	RI-C1-MDF-7370	Patch Fireproofing - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	11-Mar-27	17-Mar-27	147.0d
6653	RI-C1-MDF-6480	Hang, Tape & Finish Drywall - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	7-Oct-27	13-Oct-27	5.0d
6654	RI-C1-MDF-6490	Prime & First Coat - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	14-Oct-27	15-Oct-27	164.0d
6655	RI-C1-MDF-6500	Firestopping - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	18-Oct-27	19-Oct-27	164.0d
6656	RI-C1-MDF-6510	Install FCUs-2-6454 - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	18-Oct-27	22-Oct-27	210.0d
6657	RI-C1-MDF-7270	Install Door & Hardware - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	3.0d	18-Oct-27	20-Oct-27	207.0d
6658	RI-C1-MDF-7320	Install Tech Room Backerboard - HCAA MDF 6454 - INTRF - Alias ASD 02180 - ...	2.0d	20-Oct-27	21-Oct-27	164.0d
6659	RI-C1-MDF-7330	Set Racks - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	10.0d	22-Oct-27	4-Nov-27	164.0d
6660	RI-C1-MDF-7340	Install Ladder Rack - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	3.0d	5-Nov-27	9-Nov-27	164.0d
6661	RI-C1-MDF-6530	Pull & Terminate Fiber - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	20.0d	10-Nov-27	9-Dec-27	164.0d
6662	RI-C1-MDF-6540	Trim-Out Low Voltage - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	10-Dec-27	16-Dec-27	164.0d
6663	RI-C1-MDF-6550	Install Flooring - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	17-Dec-27	20-Dec-27	164.0d
6664	RI-C1-MDF-6560	Low Voltage Testing - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	3.0d	17-Dec-27	21-Dec-27	174.0d
6665	RI-C1-MDF-7260	Install Rubber Base - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	21-Dec-27	22-Dec-27	164.0d
6666	RI-C1-MDF-7380	Apply Final Paint - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	5.0d	23-Dec-27	30-Dec-27	164.0d
6667	RI-C1-MDF-7280	FCU Start Up - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	2.0d	21-Apr-28	24-Apr-28	85.0d
6668	RI-C1-MDF-6570	Owner's Acceptance Walkthrough - HCAA MDF 6454 - INTRF - Alias ASD 0218...	2.0d	25-Apr-28	26-Apr-28	85.0d
6669	RI-C1-MDF-6580	Owner Equip. Install - HCAA MDF 6454 - INTRF - Alias ASD 02180 - C1	15.0d	27-Apr-28	17-May-28	85.0d
6670	WBS - Tenant MDF 6447 - INTRF - Alias ASD 02181 - Conc. 1		374.0d	30-Nov-26	17-May-28	86.0d
6671	RI-C1-MDF-6880	Layout Walls/Top Track - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	30-Nov-26	4-Dec-26	161.0d
6672	RI-C1-MDF-7390	Install Fire Sprinkler Hangers - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	7-Dec-26	11-Dec-26	161.0d
6673	RI-C1-MDF-7400	Install Elec. Hangers - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	14-Dec-26	18-Dec-26	161.0d
6674	RI-C1-MDF-6960	Install Fireproofing - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	15-Jan-27	18-Jan-27	144.0d
6675	RI-C1-MDF-6920	Fire Sprinkler Mains & Branch Line Rough-in - Tenant MDF 6447 - INTRF - Alia...	5.0d	19-Jan-27	25-Jan-27	144.0d
6676	RI-C1-MDF-6940	Install Elec. OH Rough-in - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	10.0d	26-Jan-27	8-Feb-27	144.0d
6677	RI-C1-MDF-6950	Install Low Voltage OH Rough-in - Tenant MDF 6447 - INTRF - Alias ASD 0218...	5.0d	9-Feb-27	15-Feb-27	144.0d
6678	RI-C1-MDF-6890	Frame & Top-Down Walls - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	16-Feb-27	22-Feb-27	144.0d

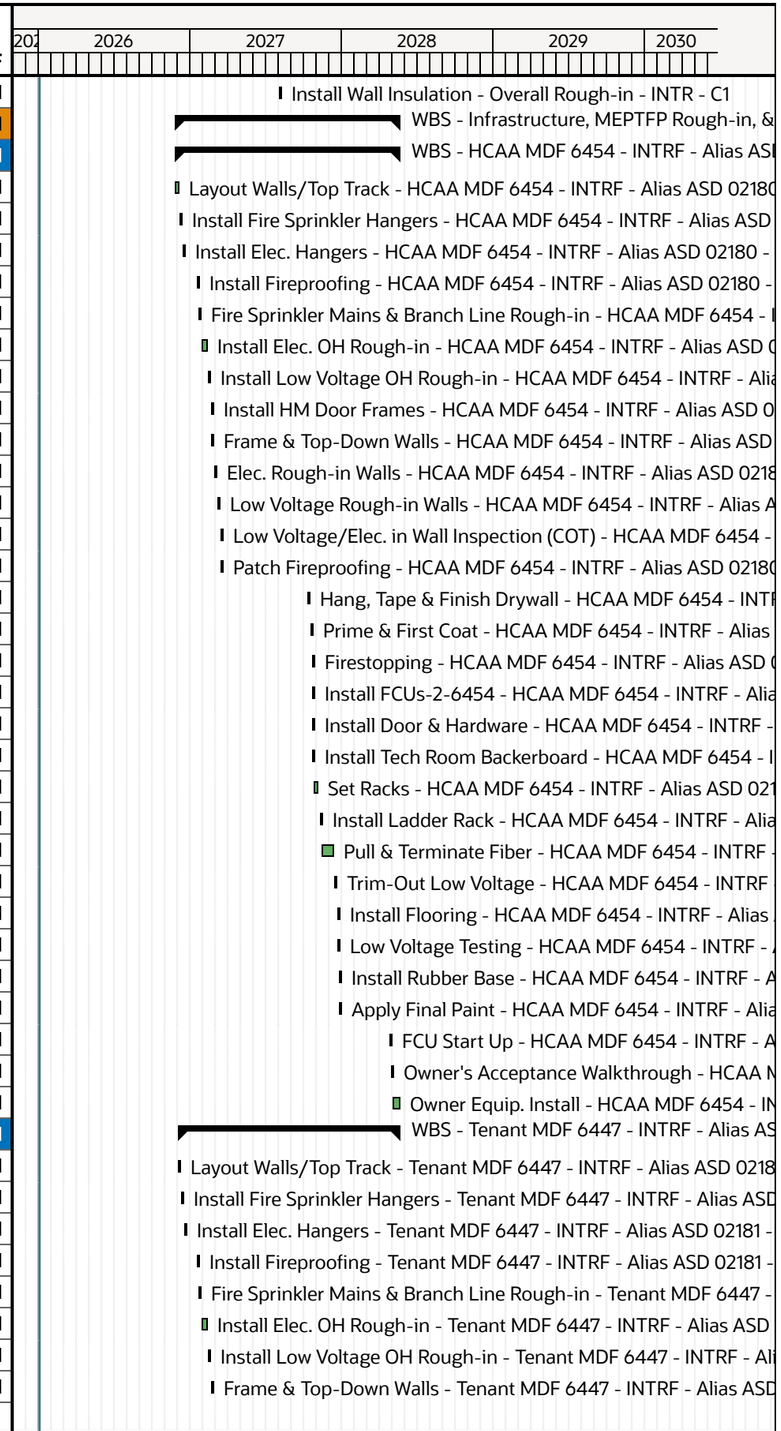


	ID	Name	Dur	Start	Finish	TF
6679	RI-C1-MDF-6910	Install HM Door Frames - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	16-Feb-27	17-Feb-27	377.0d
6680	RI-C1-MDF-6900	Elec. Rough-in Walls - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	23-Feb-27	1-Mar-27	144.0d
6681	RI-C1-MDF-7410	Low Voltage Rough-in Walls - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	2-Mar-27	8-Mar-27	144.0d
6682	RI-C1-MDF-7420	Low Voltage/Elec. in Wall Inspection (COT) - Tenant MDF 6447 - INTRF - Alias ...	5.0d	9-Mar-27	15-Mar-27	144.0d
6683	RI-C1-MDF-7430	Patch Fireproofing - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	16-Mar-27	22-Mar-27	144.0d
6684	RI-C1-MDF-6970	Hang, Tape & Finish Drywall - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	7-Oct-27	13-Oct-27	5.0d
6685	RI-C1-MDF-6980	Prime & First Coat - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	14-Oct-27	15-Oct-27	167.0d
6686	RI-C1-MDF-6990	Firestopping - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	18-Oct-27	19-Oct-27	167.0d
6687	RI-C1-MDF-7000	Install FCUs-2-6447 - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	18-Oct-27	22-Oct-27	211.0d
6688	RI-C1-MDF-7040	Install Door & Hardware - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	3.0d	18-Oct-27	20-Oct-27	208.0d
6689	RI-C1-MDF-7440	Install Tech Room Backerboard - Tenant MDF 6447 - INTRF - Alias ASD 02181 ...	2.0d	20-Oct-27	21-Oct-27	167.0d
6690	RI-C1-MDF-7470	Apply Final Paint - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	21-Oct-27	27-Oct-27	208.0d
6691	RI-C1-MDF-7450	Set Racks - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	10.0d	22-Oct-27	4-Nov-27	167.0d
6692	RI-C1-MDF-7460	Install Ladder Rack - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	5-Nov-27	8-Nov-27	167.0d
6693	RI-C1-MDF-7050	Pull & Terminate Fiber - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	20.0d	9-Nov-27	8-Dec-27	167.0d
6694	RI-C1-MDF-7010	Trim-Out Low Voltage - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	9-Dec-27	15-Dec-27	167.0d
6695	RI-C1-MDF-7070	Low Voltage Testing - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	3.0d	16-Dec-27	20-Dec-27	167.0d
6696	RI-C1-MDF-7020	Install Flooring - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	5.0d	21-Dec-27	28-Dec-27	167.0d
6697	RI-C1-MDF-7030	Install Rubber Base - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	29-Dec-27	30-Dec-27	167.0d
6698	RI-C1-MDF-7290	FCU Start Up - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	2.0d	21-Apr-28	24-Apr-28	86.0d
6699	RI-C1-MDF-7150	Owner's Acceptance Walkthrough - Tenant MDF 6447 - INTRF - Alias ASD 021...	2.0d	25-Apr-28	26-Apr-28	86.0d
6700	RI-C1-MDF-7160	Owner Equip. Install - Tenant MDF 6447 - INTRF - Alias ASD 02181 - C1	15.0d	27-Apr-28	17-May-28	86.0d
6701	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Concourse 2		398.0d	21-Sep-26	13-Apr-28	94.0d
6702	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 2		239.0d	21-Sep-26	27-Aug-27	5.0d
6703	WBS - Overall Rough-in (Non-APM) - INTR - Conc. 2		206.0d	26-Oct-26	17-Aug-27	13.0d
6704	RI-C2-670	Layout Walls/Top Track - Overall Rough-in - INTR - C2	10.0d	26-Oct-26	6-Nov-26	68.0d
6705	RI-C2-1160	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C2	5.0d	9-Nov-26	13-Nov-26	68.0d
6706	RI-C2-1170	Install Elec. Hangers - Overall Rough-in - INTR - C2	5.0d	16-Nov-26	20-Nov-26	68.0d
6707	RI-C2-1230	Install Duct Hangers - Overall Rough-in - INTR - C2	5.0d	23-Nov-26	1-Dec-26	68.0d
6708	RI-C2-1180	Install Plumbing Hangers - Overall Rough-in - INTR - C2	5.0d	2-Dec-26	8-Dec-26	68.0d
6709	RI-C2-1200	Install Fireproofing - Overall Rough-in - INTR - C2	5.0d	12-Jan-27	18-Jan-27	46.0d
6710	RI-C2-730	Frame Ceiling - Overall Rough-in - INTR - C2	5.0d	19-Jan-27	25-Jan-27	111.0d
6711	RI-C2-740	Install Duct OH Rough-in - Overall Rough-in - INTR - C2	10.0d	19-Jan-27	1-Feb-27	46.0d
6712	RI-C2-1120	Install CHW OH Rough-in - Overall Rough-in - INTR - C2	5.0d	2-Feb-27	8-Feb-27	47.0d
6713	RI-C2-700	Install Plumbing OH Rough-in - Overall Rough-in - INTR - C2	10.0d	9-Feb-27	22-Feb-27	47.0d
6714	RI-C2-1130	Install CHW Insulation - Overall Rough-in - INTR - C2	8.0d	9-Feb-27	18-Feb-27	93.0d
6715	RI-C2-710	Install Elec. OH Rough-in - Overall Rough-in - INTR - C2	20.0d	23-Feb-27	22-Mar-27	47.0d
6716	RI-C2-1140	Install Plumbing Insulation - Overall Rough-in - INTR - C2	3.0d	23-Feb-27	25-Feb-27	88.0d
6717	RI-C2-1150	Install Duct Insulation - Overall Rough-in - INTR - C2	5.0d	23-Feb-27	1-Mar-27	86.0d
6718	RI-C2-720	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C2	10.0d	23-Mar-27	5-Apr-27	53.0d
6719	RI-C2-1510	Install BAS OH Rough-in - Overall Rough-in - INTR - C2	10.0d	23-Mar-27	5-Apr-27	47.0d
6720	RI-C2-680	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C2	8.0d	6-Apr-27	15-Apr-27	53.0d

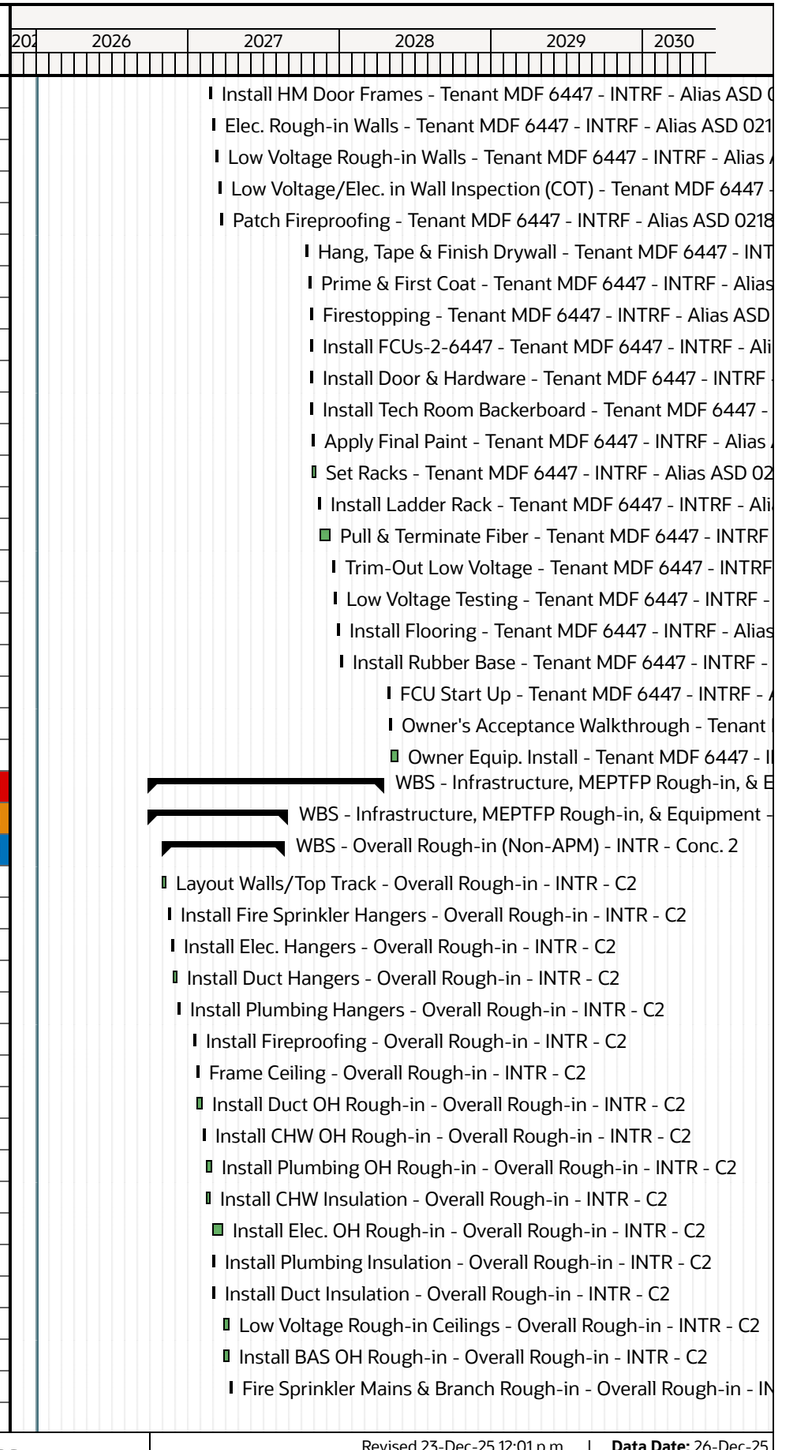


	ID	Name	Dur	Start	Finish	TF
6721	RI-C2-870	Install HM Door Frames - Overall Rough-in - INTR - C2	2.0d	16-Apr-27	19-Apr-27	82.0d
6722	RI-C2-840	Frame & Top-Down Walls - Overall Rough-in - INTR - C2	5.0d	16-Apr-27	22-Apr-27	53.0d
6723	RI-C2-1220	Install Sign Supports & Backing - Overall Rough-in - INTR - C2	5.0d	23-Apr-27	29-Apr-27	53.0d
6724	RI-C2-750	Install Plumbing Rough-in Walls Overall Rough-in - INTR - C2	3.0d	30-Apr-27	4-May-27	53.0d
6725	RI-C2-770	Elec. Rough-in Walls - Overall Rough-in - INTR - C2	5.0d	5-May-27	11-May-27	53.0d
6726	RI-C2-760	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C2	5.0d	12-May-27	18-May-27	53.0d
6727	RI-C2-1500	Pull & Terminate Low Volt Cabling- Overall Rough-in - INTR - C2	8.0d	19-May-27	28-May-27	53.0d
6728	RI-C2-830	Patch Fireproofing - Overall Rough-in - INTR - C2	2.0d	1-Jun-27	2-Jun-27	53.0d
6729	RI-C2-1540	Pull BAS Cable - Overall Rough-in - INTR - C2	10.0d	19-Jul-27	30-Jul-27	25.0d
6730	RI-C2-1210	Install Wall Insulation - Overall Rough-in - INTR - C2	5.0d	11-Aug-27	17-Aug-27	5.0d
6731	WBS - Shuttle Train Tube - INTR - Concourse 2		115.0d	21-Sep-26	4-Mar-27	0.0d
6732	RI-C2-SP-1370	Install Train Tube Metal Deck - SMP/Train Tube - INTR - C2	5.0d	21-Sep-26	25-Sep-26	0.0d
6733	RI-C2-SP-1420	Install Temp Tunnel Peel & Stick - SMP/Train Tube - INTR - C2	10.0d	28-Sep-26	9-Oct-26	0.0d
6734	RI-C2-SP-1230	Layout Walls/Top Track - SMP/Train Tube - INTR - C2	5.0d	12-Oct-26	16-Oct-26	0.0d
6735	RI-C2-SP-1320	Frame Walls Train Tube A - SMP/Train Tube - INTR - C2	15.0d	19-Oct-26	6-Nov-26	0.0d
6736	RI-C2-SP-1390	Frame Walls Train Tube B - SMP/Train Tube - INTR - C2	15.0d	9-Nov-26	1-Dec-26	0.0d
6737	RI-C2-SP-1430	Install Fall Protection Anchors Train A & Train B - SMP/Train Tube - INTR - C2	5.0d	2-Dec-26	8-Dec-26	0.0d
6738	RI-C2-SP-1260	Install Fireproofing - SMP/Train Tube - INTR - C2	5.0d	9-Dec-26	15-Dec-26	0.0d
6739	RI-C2-SP-1280	Install Elec. OH Rough-in - SMP/Train Tube - INTR - C2	10.0d	16-Dec-26	30-Dec-26	0.0d
6740	RI-C2-SP-1290	Low Voltage Rough-in Ceilings - SMP/Train Tube - INTR - C2	10.0d	16-Dec-26	30-Dec-26	0.0d
6741	RI-C2-SP-1350	Install Sheathing - SMP/Train Tube - INTR - C2	6.0d	31-Dec-26	8-Jan-27	0.0d
6742	RI-C2-SP-1380	Insulate Inner Train Tube Wall - SMP/Train Tube - INTR - C2	4.0d	31-Dec-26	6-Jan-27	12.0d
6743	RI-C2-SP-1340	Install Vapor Barrier System - SMP/Train Tube - INTR - C2	10.0d	11-Jan-27	22-Jan-27	0.0d
6744	RI-C2-SP-1360	Install Metal Panel Support Hat Channel- SMP/Train Tube - INTR - C2	4.0d	25-Jan-27	28-Jan-27	0.0d
6745	RI-C2-SP-1400	Metal Panel Wall System Scan - SMP/Train Tube - INTR - C2	5.0d	29-Jan-27	4-Feb-27	0.0d
6746	RI-C2-SP-1410	Metal Panel Wall System Fab. - SMP/Train Tube - INTR - C2	20.0d	5-Feb-27	4-Mar-27	0.0d
6747	WBS - Shuttle Platform High Ceiling - INTR - Conc. 2-1		219.0d	19-Oct-26	27-Aug-27	0.0d
6748	RI-C2-1250	Layout Walls/Top Track - Shuttle Platform High Ceiling - INTR - C2-1	5.0d	19-Oct-26	23-Oct-26	68.0d
6749	RI-C2-1270	Frame High/Low Ceiling - Shuttle Platform High Ceiling - INTR - C2-1	20.0d	26-Oct-26	20-Nov-26	92.0d
6750	RI-C2-1420	Install High/Low Fire Sprinkler Hangers - Shuttle Platform High Ceiling - INTR - ...	7.0d	23-Nov-26	3-Dec-26	92.0d
6751	RI-C2-1430	Install High/Low Elec. Hangers - Shuttle Platform High Ceiling - INTR - C2-1	7.0d	4-Dec-26	14-Dec-26	92.0d
6752	RI-C2-1450	Install Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1-1	7.0d	26-Apr-27	4-May-27	0.0d
6753	RI-C2-1560	Install Dancefloor - Shuttle Platform High Ceiling - INTR - C2-1	11.0d	5-May-27	19-May-27	0.0d
6754	RI-C2-1340	Install Elec. OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15.0d	20-May-27	10-Jun-27	0.0d
6755	RI-C2-1310	Low Voltage Rough-in Ceilings - Shuttle Platform High Ceiling - INTR - C2-1	15.0d	11-Jun-27	1-Jul-27	0.0d
6756	RI-C2-1520	Install BAS OH Rough-in - Shuttle Platform High Ceiling - INTR - C2-1	15.0d	11-Jun-27	1-Jul-27	0.0d
6757	RI-C2-1320	Fire Sprinkler Mains & Branch Rough-in - Shuttle Platform High Ceiling - INTR -...	8.0d	2-Jul-27	14-Jul-27	0.0d
6758	RI-C2-1530	Pull BAS Cable - Shuttle Platform High Ceiling - INTR - C2-1	10.0d	2-Jul-27	16-Jul-27	25.0d
6759	RI-C2-1360	Frame & Top-Down High Walls - Shuttle Platform High Ceiling - INTR - C2-1	10.0d	15-Jul-27	28-Jul-27	0.0d
6760	RI-C2-1470	Install Sign Supports & Backing - Shuttle Platform High Ceiling - INTR - C2-1	5.0d	29-Jul-27	4-Aug-27	0.0d
6761	RI-C2-1260	Elec. Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5.0d	5-Aug-27	11-Aug-27	0.0d
6762	RI-C2-1300	Low Voltage Rough-in High Walls - Shuttle Platform High Ceiling - INTR - C2-1	5.0d	12-Aug-27	18-Aug-27	0.0d

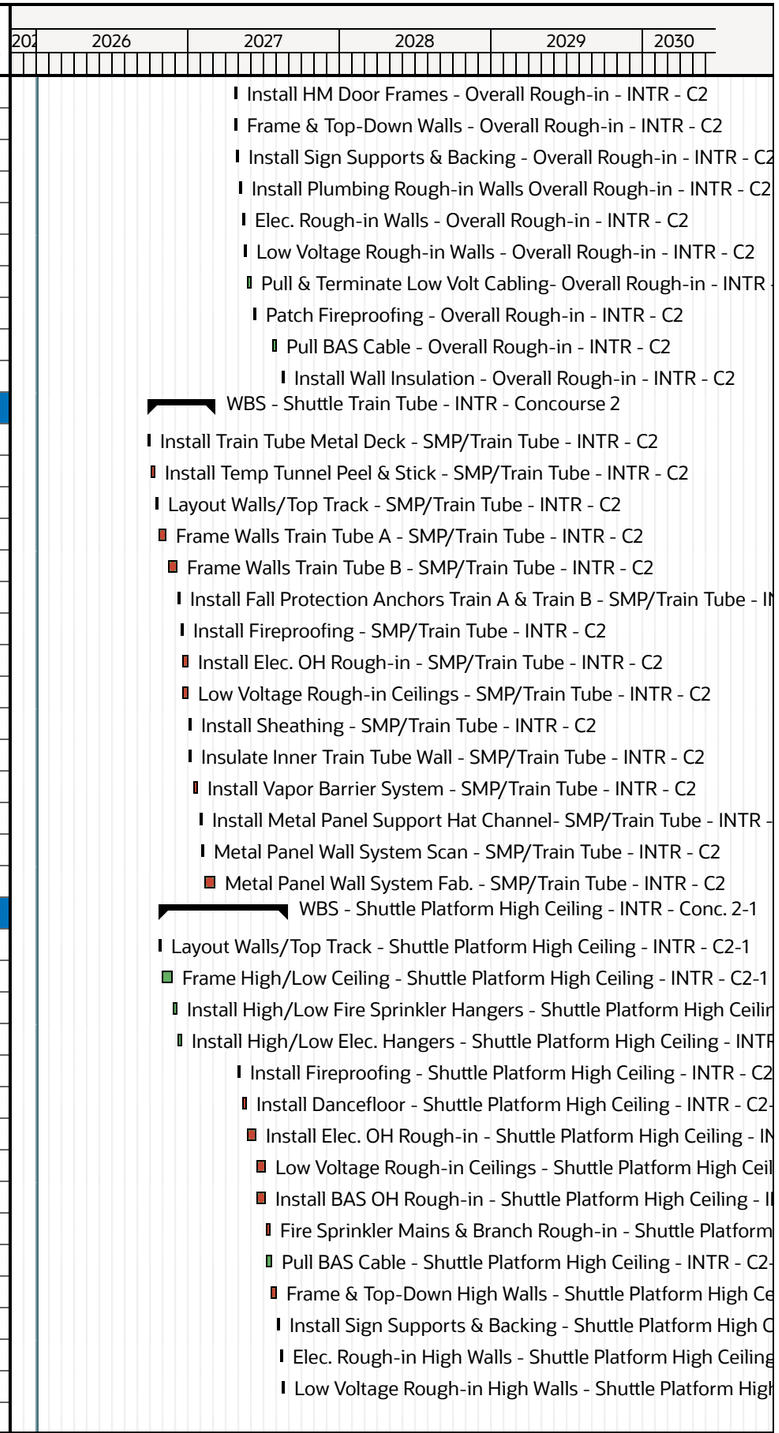

	ID	Name	Dur	Start	Finish	TF
6763	RI-C2-1350	Patch Fireproofing - Shuttle Platform High Ceiling - INTR - C2-1	2.0d	19-Aug-27	20-Aug-27	0.0d
6764	RI-C2-1460	Install Wall Insulation - Shuttle Platform High Ceiling - INTR - C2-1	5.0d	23-Aug-27	27-Aug-27	0.0d
6765	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Mechanical - INTR - Conc. 2		142.0d	9-Nov-26	1-Jun-27	315.0d
6766	WBS - Mechanical Room - INTR - Conc. 2		142.0d	9-Nov-26	1-Jun-27	315.0d
6767	RI-C2-MR-900	Layout Walls/ Top Track - Mech. Room - INTR - C2	5.0d	9-Nov-26	13-Nov-26	240.0d
6768	RI-C2-MR-910	Layout AHU Equip. Pads - Mech. Room - INTR - C2	2.0d	16-Nov-26	17-Nov-26	240.0d
6769	RI-C2-MR-920	FRP AHU Equip. Pads - Mech. Room - INTR - C2	5.0d	18-Nov-26	24-Nov-26	240.0d
6770	RI-C2-MR-930	Set AHUs on Equip. Pad - Mech. Room - INTR - C2	5.0d	25-Nov-26	3-Dec-26	240.0d
6771	RI-C2-MR-1130	Install Plumbing Equip. - Mech. Room - INTR - C2	5.0d	4-Dec-26	10-Dec-26	240.0d
6772	RI-C2-MR-940	Frame & Top-Down Walls - Mech. Room - INTR - C2	10.0d	11-Dec-26	24-Dec-26	240.0d
6773	RI-C2-MR-950	Install HM Door Frames - Mech. Room - INTR - C2	5.0d	11-Dec-26	17-Dec-26	240.0d
6774	RI-C2-MR-980	Install Plumbing OH Rough-in - Mech. Room - INTR - C2	15.0d	18-Dec-26	11-Jan-27	240.0d
6775	RI-C2-MR-970	Install Duct OH Rough- in - Mech. Room - INTR - C2	15.0d	12-Jan-27	1-Feb-27	304.0d
6776	RI-C2-MR-1090	Install CHW/Vent OH Rough- in - Mech. Room - INTR - C2	15.0d	9-Feb-27	1-Mar-27	375.0d
6777	RI-C2-MR-1100	Install Plumbing Insulation - Mech. Room - INTR - C2	7.0d	26-Feb-27	8-Mar-27	207.0d
6778	RI-C2-MR-1120	Install Duct Insulation - Mech. Room - INTR - C2	10.0d	2-Mar-27	15-Mar-27	202.0d
6779	RI-C2-MR-1110	Install CHW Insulation - Mech. Room - INTR - Mech Room - C2	5.0d	2-Mar-27	8-Mar-27	375.0d
6780	RI-C2-MR-960	Fire Sprinkler Mains & Branch Line Rough-in - Mech. Room - INTR - C2	10.0d	16-Mar-27	29-Mar-27	202.0d
6781	RI-C2-MR-990	Install Elec. OH Rough-in - Mech. Room - INTR - C2	15.0d	30-Mar-27	19-Apr-27	202.0d
6782	RI-C2-MR-1050	Install Fireproofing - Mech. Room - INTR - C2	5.0d	20-Apr-27	26-Apr-27	202.0d
6783	RI-C2-MR-1140	Install BAS Rough-in - Mech. Room - INTR - C2	15.0d	20-Apr-27	10-May-27	312.0d
6784	RI-C2-MR-1020	Install Plumbing Rough-in Walls - Mech. Room - INTR - C2	5.0d	27-Apr-27	3-May-27	202.0d
6785	RI-C2-MR-1010	Elec. Rough-in Walls - Mech. Room - INTR - C2	3.0d	4-May-27	6-May-27	202.0d
6786	RI-C2-MR-1000	Low Voltage Rough-in Wall - Mech. Room - INTR - C2	5.0d	7-May-27	13-May-27	202.0d
6787	RI-C2-MR-1150	Pull BAS Cable - Mech. Room - INTR - C2	15.0d	11-May-27	1-Jun-27	312.0d
6788	RI-C2-MR-1060	Firestopping - Mech. Room - INTR - C2	2.0d	14-May-27	17-May-27	202.0d
6789	RI-C2-MR-1080	Pull & Terminate Elec. to Mech. Equip. - Mech. Room - INTR - C2	7.0d	18-May-27	26-May-27	202.0d
6790	WBS - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - Concourse 2		102.0d	18-Nov-27	13-Apr-28	48.0d
6791	VC-EL-C2-3700	Install Elev. Safety Rail/Net - Passenger (#12 & #13) Elevator Cabs/Shaft - INT...	5.0d	18-Nov-27	24-Nov-27	48.0d
6792	VC-EL-C2-3820	Install Scaffold in Hoistway - Passenger (#12 & #13) Elevator Cabs/Shaft - INT...	5.0d	29-Nov-27	3-Dec-27	48.0d
6793	VC-EL-C2-3710	Rough-in Elec. In Shaft - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	8.0d	6-Dec-27	15-Dec-27	48.0d
6794	VC-EL-C2-3840	Install Temp Sump Pit Cover - Passenger (#12 & #13) Elevator Cabs/Shaft - IN...	2.0d	6-Dec-27	7-Dec-27	54.0d
6795	VC-EL-C2-3720	Install Elev. Pit LTNG/Outlets - Passenger (#12 & #13) Elevator Cabs/Shaft - IN...	5.0d	16-Dec-27	22-Dec-27	48.0d
6796	VC-EL-C2-3730	Install Temp Power for Elevator Release - Passenger (#12 & #13) Elevator Cabs...	5.0d	16-Dec-27	22-Dec-27	53.0d
6797	VC-EL-C2-3830	Remove Scaffold in Hoistway - Passenger (#12 & #13) Elevator Cabs/Shaft - IN...	5.0d	23-Dec-27	30-Dec-27	48.0d
6798	VC-EL-C2-3740	Install Elev. Rails - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	3-Jan-28	7-Jan-28	48.0d
6799	VC-EL-C2-3940	Set Elev. Equip in Shaft - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	2.0d	10-Jan-28	11-Jan-28	48.0d
6800	VC-EL-C2-3960	Install Hoistway Elec. Cabling - Passenger (#12 & #13) Elevator Cabs/Shaft - I...	5.0d	12-Jan-28	18-Jan-28	48.0d
6801	VC-EL-C2-3950	Install Platform & Weights - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR...	5.0d	12-Jan-28	18-Jan-28	48.0d
6802	VC-EL-C2-3970	Install Elev. Equip. in Pit - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	19-Jan-28	25-Jan-28	48.0d
6803	VC-EL-C2-3980	Install Elev. Doors - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	3.0d	19-Jan-28	21-Jan-28	48.0d
6804	VC-EL-C2-3990	Install Elev. Cab - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	24-Jan-28	28-Jan-28	48.0d

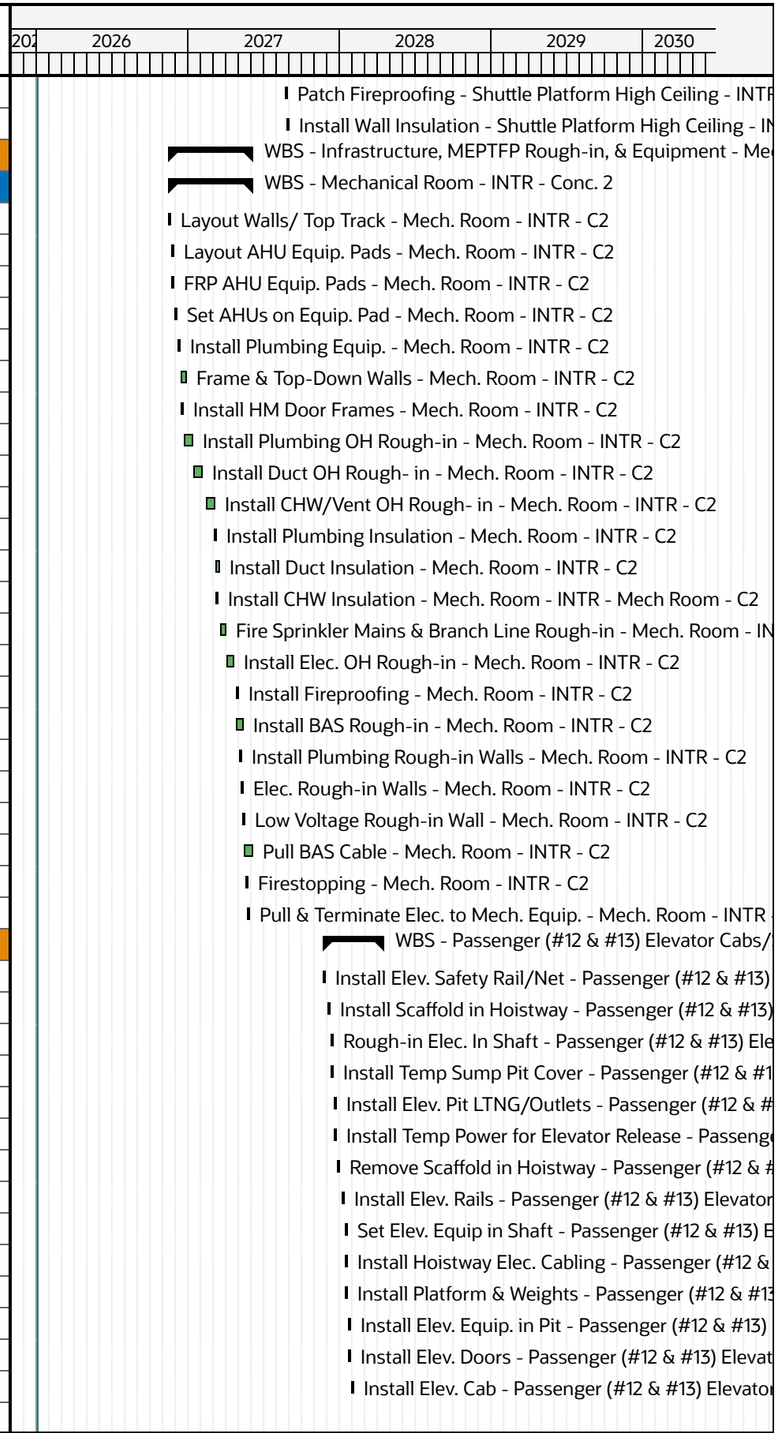


	ID	Name	Dur	Start	Finish	TF
6805	VC-EL-C2-4000	Connect Elev. Equip - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	31-Jan-28	4-Feb-28	48.0d
6806	VC-EL-C2-3850	Grout Elevator Door Frames - Passenger (#12 & #13) Elevator Cabs/Shaft - IN...	5.0d	7-Feb-28	11-Feb-28	48.0d
6807	VC-EL-C2-3900	Install Elev. Flooring - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	2.0d	7-Feb-28	8-Feb-28	51.0d
6808	VC-EL-C2-3930	Grout Elevator Sills - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	14-Feb-28	18-Feb-28	48.0d
6809	VC-EL-C2-4020	Set Elev. Fronts & Call Boxes - Passenger (#12 & #13) Elevator Cabs/Shaft - IN...	5.0d	21-Feb-28	25-Feb-28	48.0d
6810	VC-EL-C2-3860	Remove Elevator Safety Rail/Net - Passenger (#12 & #13) Elevator Cabs/Shaft ...	2.0d	28-Feb-28	29-Feb-28	48.0d
6811	VC-EL-C2-3750	Elec. Run Time for Final Connections - Passenger (#12 & #13) Elevator Cabs/S...	5.0d	1-Mar-28	7-Mar-28	48.0d
6812	VC-EL-C2-3760	Install Fire Alarm Trim - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	3.0d	8-Mar-28	10-Mar-28	48.0d
6813	VC-EL-C2-3920	Install Cameras - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	8-Mar-28	14-Mar-28	50.0d
6814	VC-EL-C2-3880	Install Pit Ladder - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	2.0d	13-Mar-28	14-Mar-28	48.0d
6815	VC-EL-C2-3870	Install Sump Pump & Final Grate Cover - Passenger (#12 & #13) Elevator Cabs...	2.0d	15-Mar-28	16-Mar-28	48.0d
6816	VC-EL-C2-3770	Adjust/Test Elev. - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	10.0d	17-Mar-28	30-Mar-28	48.0d
6817	VC-EL-C2-3890	Liftnet/Phone Service Configuration - Passenger (#12 & #13) Elevator Cabs/S...	5.0d	31-Mar-28	6-Apr-28	48.0d
6818	VC-EL-C2-4010	Prepare Elev. Punchlist - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	5.0d	7-Apr-28	13-Apr-28	48.0d
6819	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 3		431.0d	8-Sep-26	17-May-28	112.0d
6820	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 3		148.0d	30-Nov-26	28-Jun-27	269.0d
6821	WBS - SSCP - TSA Checkpoints - INTR - Conc. 3		148.0d	30-Nov-26	28-Jun-27	269.0d
6822	RI-C3-SS-10	Layout Walls/Top Track - SSCP Check Points - INTR - C3	10.0d	30-Nov-26	11-Dec-26	125.0d
6823	RI-C3-SS-20	Install Fire Sprinkler Hangers - SSCP Check Points - INTR - C3	2.0d	14-Dec-26	15-Dec-26	125.0d
6824	RI-C3-SS-30	Install Duct/CHW Hangers - SSCP Check Points - INTR - C3	2.0d	16-Dec-26	17-Dec-26	125.0d
6825	RI-C3-SS-40	Install Plumbing Hangers - SSCP Check Points - INTR - C3	3.0d	18-Dec-26	22-Dec-26	125.0d
6826	RI-C3-SS-50	Install Elec. Hangers - SSCP Check Points - INTR - C3	2.0d	23-Dec-26	24-Dec-26	125.0d
6827	RI-C3-SS-60	Install Fireproofing - SSCP Check Points - INTR - C3	5.0d	26-Jan-27	1-Feb-27	105.0d
6828	RI-C3-SS-70	Install Plumbing OH Rough-in - SSCP Check Points - INTR - C3	10.0d	2-Feb-27	15-Feb-27	105.0d
6829	RI-C3-SS-90	Install Mech. Equip. - SSCP Check Points - INTR - C3	5.0d	9-Feb-27	15-Feb-27	105.0d
6830	RI-C3-SS-80	Install Duct & CHW OH Rough-in - SSCP Check Points - INTR - C3	10.0d	23-Feb-27	8-Mar-27	95.0d
6831	RI-C3-SS-100	Fire Sprinkler Mains & Branch Line Rough-in - SSCP Check Points - INTR - C3	10.0d	2-Mar-27	15-Mar-27	95.0d
6832	RI-C3-SS-110	Install Elec. OH Rough-in - SSCP Check Points - INTR - C3	15.0d	9-Mar-27	29-Mar-27	95.0d
6833	RI-C3-SS-120	Low Voltage Rough-in Ceilings - SSCP Check Points - INTR - C3	10.0d	9-Mar-27	22-Mar-27	110.0d
6834	RI-C3-SS-260	Install BAS OH Rough-in - SSCP Check Points - INTR - C3	10.0d	30-Mar-27	12-Apr-27	95.0d
6835	RI-C3-SS-140	Frame Hard Lid Ceilings - SSCP Check Points - INTR - C3	7.0d	13-Apr-27	21-Apr-27	255.0d
6836	RI-C3-SS-270	Pull BAS Cable - SSCP Check Points - INTR - C3	10.0d	13-Apr-27	26-Apr-27	313.0d
6837	RI-C3-SS-180	Elec. Rough-in at Hard Lids - SSCP Check Points - INTR - C3	7.0d	22-Apr-27	30-Apr-27	255.0d
6838	RI-C3-SS-220	Install Duct Insulation - SSCP Check Points - INTR - C3	5.0d	26-Apr-27	30-Apr-27	81.0d
6839	RI-C3-SS-210	Install Plumbing Insulation - SSCP Check Points - INTR - C3	5.0d	26-Apr-27	30-Apr-27	81.0d
6840	RI-C3-SS-190	Low Voltage Rough-in at Hard Lids - SSCP Check Points - INTR - C3	5.0d	3-May-27	7-May-27	255.0d
6841	RI-C3-SS-130	Frame & Top-Down Walls - SSCP Check Points - INTR - C3	5.0d	2-Jun-27	8-Jun-27	60.0d
6842	RI-C3-SS-150	Install HM Door Frames - SSCP Check Points - INTR - C3	3.0d	2-Jun-27	4-Jun-27	73.0d
6843	FN-C3-SS-110	Install Wood Ceiling Track - SSCP Check Points - INTF - C3	10.0d	9-Jun-27	22-Jun-27	216.0d
6844	RI-C3-SS-160	Elec. Rough-in Walls - SSCP Check Points - INTR - C3	3.0d	9-Jun-27	11-Jun-27	71.0d
6845	RI-C3-SS-170	Low Voltage Rough-in Walls - SSCP Check Points - INTR - C3	3.0d	9-Jun-27	11-Jun-27	60.0d
6846	RI-C3-SS-230	Frame Security Glazing System - SSCP Check Points - INTR - C3	5.0d	9-Jun-27	15-Jun-27	69.0d

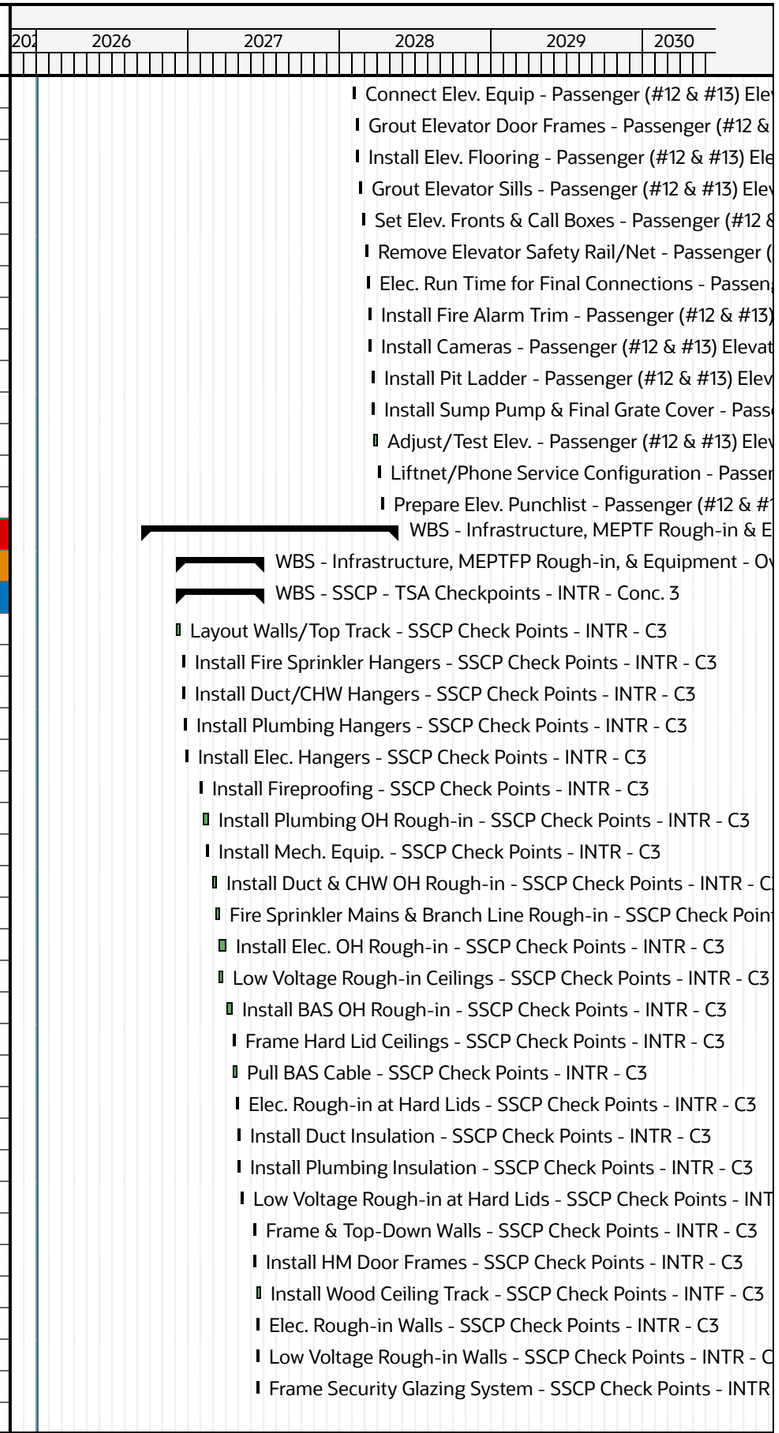


	ID	Name	Dur	Start	Finish	TF
6847	RI-C3-SS-250	Frame Interior Glazed Curtain Wall - West Wall (GW04) - SSCP Check Points - IN...	5.0d	9-Jun-27	15-Jun-27	211.0d
6848	RI-C3-SS-240	Pull & Terminate Low Volt Cabling - SSCP Check Points - INTR - C3	11.0d	14-Jun-27	28-Jun-27	60.0d
6849	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - IDF - Concourse 3		431.0d	8-Sep-26	17-May-28	112.0d
6850	WBS - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - Conc. 3		431.0d	8-Sep-26	17-May-28	112.0d
6851	RI-C3-IDF-6900	Install Flooring - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	3.0d	8-Sep-26	10-Sep-26	514.0d
6852	RI-C3-IDF-6910	Install Rubber Base - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	11-Sep-26	14-Sep-26	514.0d
6853	RI-C3-IDF-6760	Low Voltage Testing - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	15-Sep-26	21-Sep-26	514.0d
6854	RI-C3-IDF-6590	Layout Walls/Top Track - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	30-Nov-26	4-Dec-26	160.0d
6855	RI-C3-IDF-7070	Install Fire Sprinkler Hangers - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	7-Dec-26	8-Dec-26	160.0d
6856	RI-C3-IDF-7080	Install Elec. Hangers - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	9-Dec-26	10-Dec-26	160.0d
6857	RI-C3-IDF-6670	Install Fireproofing - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	5-Jan-27	6-Jan-27	145.0d
6858	RI-C3-IDF-6630	Fire Sprinkler Mains & Branch Line Rough-in- TSA IDF 6504 - INTRF - TSA IDF ...	5.0d	7-Jan-27	13-Jan-27	145.0d
6859	RI-C3-IDF-6650	Install Elec. OH Rough-in - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	10.0d	14-Jan-27	27-Jan-27	145.0d
6860	RI-C3-IDF-6660	Install Low Voltage OH Rough-in - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	10.0d	28-Jan-27	10-Feb-27	145.0d
6861	RI-C3-IDF-6600	Frame & Top-Down Walls - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	11-Feb-27	17-Feb-27	145.0d
6862	RI-C3-IDF-6620	Install HM Door Frames - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	11-Feb-27	12-Feb-27	409.0d
6863	RI-C3-IDF-6610	Elec. Rough-in Walls - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	18-Feb-27	24-Feb-27	145.0d
6864	RI-C3-IDF-7060	Low Voltage Rough-in Walls - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	25-Feb-27	3-Mar-27	145.0d
6865	RI-C3-IDF-7090	Low Voltage/Elec. in Wall Inspection (COT) - TSA IDF 6504 - INTRF - TSA IDF Al...	2.0d	4-Mar-27	5-Mar-27	145.0d
6866	RI-C3-IDF-7100	Patch Fireproofing - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	8-Mar-27	12-Mar-27	145.0d
6867	RI-C3-IDF-6680	Hang, Tape & Finish Drywall - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	30-Sep-27	6-Oct-27	5.0d
6868	RI-C3-IDF-6690	Prime & First Coat - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	7-Oct-27	8-Oct-27	199.0d
6869	RI-C3-IDF-6700	Firestopping - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	11-Oct-27	12-Oct-27	199.0d
6870	RI-C3-IDF-6890	Install Door & Hardware - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	11-Oct-27	12-Oct-27	242.0d
6871	RI-C3-IDF-7040	Install FCUs-2-6504 - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	11-Oct-27	15-Oct-27	216.0d
6872	RI-C3-IDF-6710	Install Tech Room Backerboard - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	3.0d	13-Oct-27	15-Oct-27	199.0d
6873	RI-C3-IDF-6720	Set Racks - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	10.0d	18-Oct-27	29-Oct-27	199.0d
6874	RI-C3-IDF-6730	Install Ladder Rack - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	3.0d	1-Nov-27	3-Nov-27	199.0d
6875	RI-C3-IDF-6740	Pull & Terminate Fiber - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	10.0d	4-Nov-27	17-Nov-27	199.0d
6876	RI-C3-IDF-7000	Trim-Out Low Voltage- TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	18-Nov-27	24-Nov-27	199.0d
6877	RI-C3-IDF-7150	Low Voltage Testing - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	29-Nov-27	3-Dec-27	199.0d
6878	RI-C3-IDF-7160	Install Flooring - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	6-Dec-27	7-Dec-27	199.0d
6879	RI-C3-IDF-7170	Install Rubber Base - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	8-Dec-27	14-Dec-27	199.0d
6880	RI-C3-IDF-6880	Apply Final Paint - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	5.0d	15-Dec-27	21-Dec-27	199.0d
6881	RI-C3-IDF-7050	FCU Start Up - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	2.0d	21-Apr-28	24-Apr-28	112.0d
6882	RI-C3-IDF-6770	Owner's Acceptance Walkthrough - TSA IDF 6504 - INTRF - TSA IDF Alias 201 -...	2.0d	25-Apr-28	26-Apr-28	112.0d
6883	RI-C3-IDF-6780	Owner Equipment Install - TSA IDF 6504 - INTRF - TSA IDF Alias 201 - C3	15.0d	27-Apr-28	17-May-28	112.0d
6884	WBS - HCAA IDF 6503 - INTRF - Alias ASD 02280 - Conc. 3		374.0d	30-Nov-26	17-May-28	112.0d
6885	RI-C3-IDF-6010	Layout Walls/Top Track - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	30-Nov-26	4-Dec-26	350.0d
6886	RI-C3-IDF-7120	Install Fire Sprinkler Hangers - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	7-Dec-26	11-Dec-26	350.0d
6887	RI-C3-IDF-7130	Install Elec. Hangers - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	14-Dec-26	18-Dec-26	350.0d
6888	RI-C3-IDF-6090	Install Fireproofing - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	2.0d	5-Jan-27	6-Jan-27	341.0d




	ID	Name	Dur	Start	Finish	TF
6889	RI-C3-IDF-6050	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6503 - INTRF - Alias ...	5.0d	7-Jan-27	13-Jan-27	341.0d
6890	RI-C3-IDF-6070	Install Elec. OH Rough-in -in - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	10.0d	14-Jan-27	27-Jan-27	341.0d
6891	RI-C3-IDF-6080	Install Low Voltage OH Rough-in - HCAA IDF 6503 - INTRF - Alias ASD 02280 -...	10.0d	28-Jan-27	10-Feb-27	341.0d
6892	RI-C3-IDF-6020	Frame & Top-Down Walls - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	4.0d	11-Feb-27	16-Feb-27	341.0d
6893	RI-C3-IDF-6040	Install HM Door Frames - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	2.0d	11-Feb-27	12-Feb-27	396.0d
6894	RI-C3-IDF-6030	Elec. Rough-in Walls - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	17-Feb-27	23-Feb-27	341.0d
6895	RI-C3-IDF-6980	Low Voltage Rough-in Walls - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	24-Feb-27	2-Mar-27	341.0d
6896	RI-C3-IDF-7110	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6503 - INTRF - Alias AS...	5.0d	3-Mar-27	9-Mar-27	341.0d
6897	RI-C3-IDF-7140	Patch Fireproofing - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	10-Mar-27	16-Mar-27	341.0d
6898	RI-C3-IDF-6110	Hang, Tape & Finish Drywall - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	30-Sep-27	6-Oct-27	203.0d
6899	RI-C3-IDF-6120	Prime & First Coat - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	2.0d	7-Oct-27	8-Oct-27	203.0d
6900	RI-C3-IDF-6130	Firestopping - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	2.0d	11-Oct-27	12-Oct-27	203.0d
6901	RI-C3-IDF-6150	Install FCUs-2-6503 - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	11-Oct-27	15-Oct-27	216.0d
6902	RI-C3-IDF-7210	Install Door & Hardware - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	11-Oct-27	15-Oct-27	229.0d
6903	RI-C3-IDF-6140	Install Tech Room Backerboard - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	3.0d	13-Oct-27	15-Oct-27	203.0d
6904	RI-C3-IDF-6160	Set Racks- HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	18-Oct-27	22-Oct-27	203.0d
6905	RI-C3-IDF-6170	Install Ladder Rack - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	3.0d	25-Oct-27	27-Oct-27	203.0d
6906	RI-C3-IDF-6190	Pull & Terminate Fiber - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	10.0d	28-Oct-27	10-Nov-27	203.0d
6907	RI-C3-IDF-6180	Trim-Out Low Voltage - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	3.0d	11-Nov-27	15-Nov-27	203.0d
6908	RI-C3-IDF-7030	Low Voltage Testing - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	16-Nov-27	22-Nov-27	203.0d
6909	RI-C3-IDF-7180	Install Flooring - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	23-Nov-27	1-Dec-27	203.0d
6910	RI-C3-IDF-7190	Install Rubber Base - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	2-Dec-27	8-Dec-27	203.0d
6911	RI-C3-IDF-7200	Apply Final Paint - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	5.0d	9-Dec-27	15-Dec-27	203.0d
6912	RI-C3-IDF-7010	FCU Start Up - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	2.0d	21-Apr-28	24-Apr-28	112.0d
6913	RI-C3-IDF-6280	Owner's Acceptance Walkthrough - HCAA IDF 6503 - INTRF - Alias ASD 02280 ...	2.0d	25-Apr-28	26-Apr-28	112.0d
6914	RI-C3-IDF-6290	Owner Equip. Install - HCAA IDF 6503 - INTRF - Alias ASD 02280 - C3	15.0d	27-Apr-28	17-May-28	112.0d
6915	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 4		170.0d	30-Apr-27	3-Jan-28	56.0d
6916	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 4		170.0d	30-Apr-27	3-Jan-28	56.0d
6917	WBS - Overall Rough-in - INTR - Conc. 4		170.0d	30-Apr-27	3-Jan-28	56.0d
6918	RI-CN-C4-1460	Layout Walls/Top Track - Overall Rough-in - INTR - C4	10.0d	30-Apr-27	13-May-27	36.0d
6919	RI-CN-C4-1470	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C4	5.0d	14-May-27	20-May-27	36.0d
6920	RI-CN-C4-1480	Install Elec. Hangers - Overall Rough-in - INTR - C4	5.0d	21-May-27	27-May-27	36.0d
6921	RI-CN-C4-1490	Install Plumbing Hangers - Overall Rough-in - INTR - C4	3.0d	28-May-27	2-Jun-27	36.0d
6922	RI-CN-C4-1500	Install Fireproofing - Overall Rough-in - INTR - C4	5.0d	3-Jun-27	9-Jun-27	36.0d
6923	RI-CN-C4-1510	Install Duct OH Rough-in - Overall Rough-in - INTR - C4	20.0d	10-Jun-27	8-Jul-27	36.0d
6924	RI-CN-C4-1520	Install Plumbing OH Rough-in - Overall Rough-in - INTR - C4	15.0d	9-Jul-27	29-Jul-27	36.0d
6925	RI-CN-C4-1540	Install Elec. OH Rough-in - Overall Rough-in - INTR - C4	20.0d	30-Jul-27	26-Aug-27	36.0d
6926	RI-CN-C4-1590	Install Plumbing Insulation - Overall Rough-in - INTR - C4	3.0d	11-Aug-27	13-Aug-27	95.0d
6927	RI-CN-C4-1600	Install Duct Insulation - Overall Rough-in - INTR - C4	10.0d	11-Aug-27	24-Aug-27	122.0d
6928	RI-CN-C4-1550	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C4	10.0d	27-Aug-27	10-Sep-27	36.0d
6929	RI-CN-C4-1700	Install BAS OH Rough-in - Overall Rough-in - INTR - C4	10.0d	27-Aug-27	10-Sep-27	36.0d
6930	RI-CN-C4-1560	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C4	10.0d	13-Sep-27	24-Sep-27	36.0d

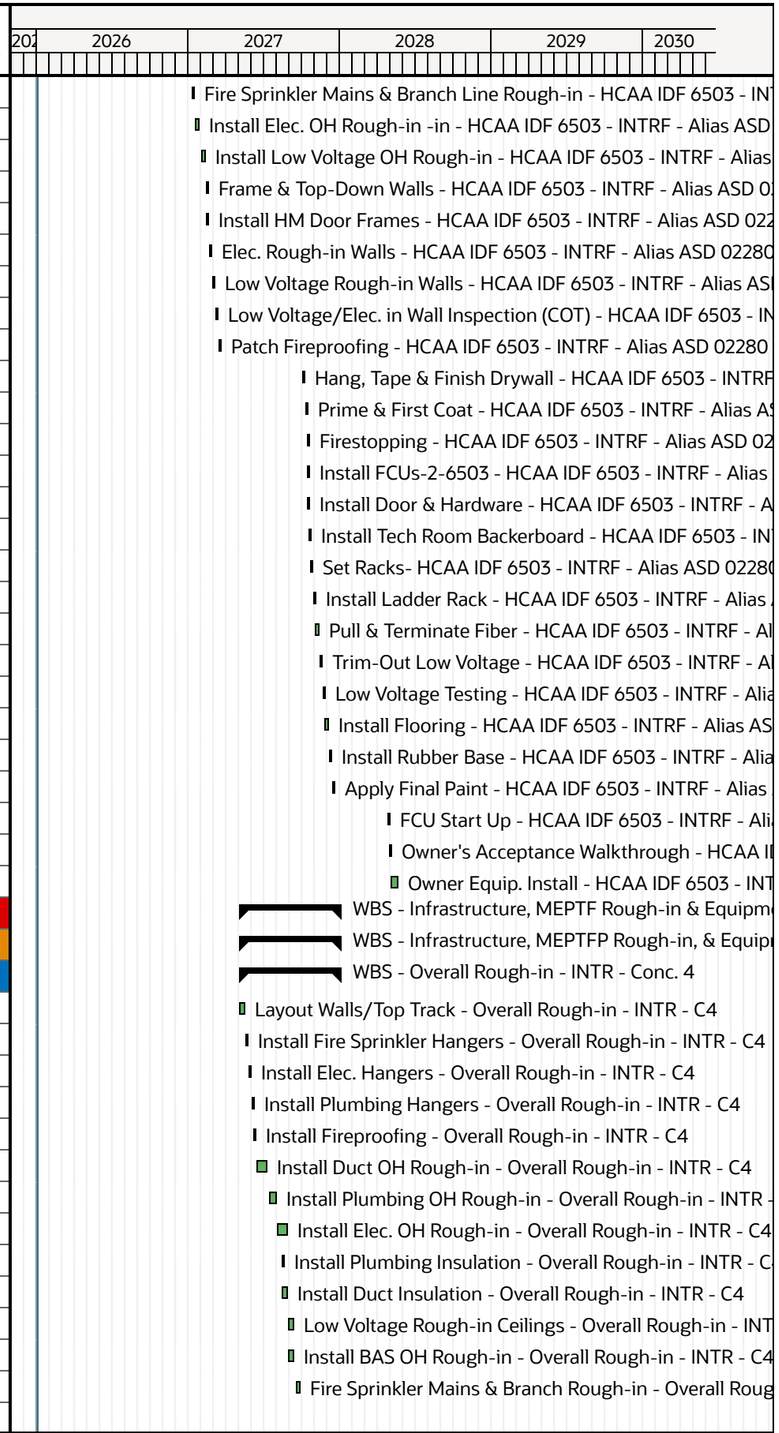

	ID	Name	Dur	Start	Finish	TF
6931	RI-CN-C4-1710	Pull BAS Cable - Overall Rough-in - INTR - C4	10.0d	13-Sep-27	24-Sep-27	123.0d
6932	RI-CN-C4-1570	Frame & Top-Down Walls - Overall Rough-in - INTR - C4	10.0d	27-Sep-27	8-Oct-27	36.0d
6933	RI-CN-C4-1670	Glazing Framing - Overall Rough-in - INTR - C4	5.0d	11-Oct-27	15-Oct-27	36.0d
6934	RI-CN-C4-1580	Frame Ceiling - Overall Rough-in - INTR - C4	10.0d	18-Oct-27	29-Oct-27	36.0d
6935	RI-CN-C4-1610	Install HM Door Frames - Overall Rough-in - INTR - C4	5.0d	1-Nov-27	5-Nov-27	36.0d
6936	RI-CN-C4-1620	Install Plumbing Rough-in Walls Overall Rough-in - INTR - C4	7.0d	8-Nov-27	16-Nov-27	36.0d
6937	RI-CN-C4-1630	Elec. Rough-in Walls & Holdroom Columns - Overall Rough-in - INTR - C4	7.0d	17-Nov-27	29-Nov-27	36.0d
6938	RI-CN-C4-1640	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C4	5.0d	30-Nov-27	6-Dec-27	36.0d
6939	RI-CN-C4-1690	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - C4	13.0d	7-Dec-27	23-Dec-27	36.0d
6940	RI-CN-C4-1650	Patch Fireproofing - Overall Rough-in - INTR - C4	2.0d	27-Dec-27	28-Dec-27	36.0d
6941	RI-CN-C4-1660	Install Wall Insulation - Overall Rough-in - INTR - C4	3.0d	29-Dec-27	3-Jan-28	36.0d
6942	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 5		141.0d	1-Apr-27	19-Oct-27	109.0d
6943	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 5		141.0d	1-Apr-27	19-Oct-27	109.0d
6944	WBS - Overall Rough-in - INTR - Conc. 5		141.0d	1-Apr-27	19-Oct-27	109.0d
6945	RI-CN-C5-1670	Layout Walls/Top Track - Overall Rough-in - INTR - C5	10.0d	1-Apr-27	14-Apr-27	43.0d
6946	RI-CN-C5-1680	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C5	5.0d	15-Apr-27	21-Apr-27	43.0d
6947	RI-CN-C5-1690	Install Elec. Hangers - Overall Rough-in - INTR - C5	5.0d	22-Apr-27	28-Apr-27	43.0d
6948	RI-CN-C5-1700	Install Plumbing Hangers - Overall Rough-in - INTR - C5	2.0d	29-Apr-27	30-Apr-27	43.0d
6949	RI-CN-C5-1710	Install Fireproofing - Overall Rough-in - INTR - C5	5.0d	3-May-27	7-May-27	43.0d
6950	RI-CN-C5-1720	Install Duct OH Rough-in - Overall Rough-in - INTR - C5	15.0d	10-May-27	28-May-27	43.0d
6951	RI-CN-C5-1730	Install Plumbing OH Rough-in - Overall Rough-in - INTR - C5	3.0d	1-Jun-27	3-Jun-27	66.0d
6952	RI-CN-C5-1740	Install Elec. OH Rough-in - Overall Rough-in - INTR - C5	15.0d	4-Jun-27	24-Jun-27	66.0d
6953	RI-CN-C5-1790	Install Plumbing Insulation - Overall Rough-in - INTR - C5	3.0d	7-Jun-27	9-Jun-27	132.0d
6954	RI-CN-C5-1800	Install Duct Insulation - Overall Rough-in - INTR - C5	5.0d	7-Jun-27	11-Jun-27	130.0d
6955	RI-CN-C5-1750	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C5	10.0d	25-Jun-27	9-Jul-27	66.0d
6956	RI-CN-C5-1880	Install BAS OH Rough-in - Overall Rough-in - INTR - C5	10.0d	25-Jun-27	9-Jul-27	66.0d
6957	RI-CN-C5-1760	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C5	10.0d	12-Jul-27	23-Jul-27	66.0d
6958	RI-CN-C5-1890	Pull BAS Cable - Overall Rough-in - INTR - C5	10.0d	12-Jul-27	23-Jul-27	170.0d
6959	RI-CN-C5-1770	Frame & Top-Down Walls - Overall Rough-in - INTR - C5	10.0d	26-Jul-27	6-Aug-27	66.0d
6960	RI-CN-C4-1680	Glazing Framing - Overall Rough-in - INTR - C5	10.0d	9-Aug-27	20-Aug-27	66.0d
6961	RI-CN-C5-1780	Frame Ceiling - Overall Rough-in - INTR - C5	10.0d	23-Aug-27	3-Sep-27	66.0d
6962	RI-CN-C5-1810	Install HM Door Frames - Overall Rough-in - INTR - C5	5.0d	7-Sep-27	13-Sep-27	66.0d
6963	RI-CN-C5-1820	Install Plumbing Rough-in Walls Overall Rough-in - INTR - C5	3.0d	14-Sep-27	16-Sep-27	66.0d
6964	RI-CN-C5-1830	Elec. Rough-in Walls & Holdroom Columns - Overall Rough-in - INTR - C5	7.0d	17-Sep-27	27-Sep-27	66.0d
6965	RI-CN-C5-1840	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C5	5.0d	28-Sep-27	4-Oct-27	66.0d
6966	RI-CN-C5-1870	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - C5	6.0d	5-Oct-27	12-Oct-27	66.0d
6967	RI-CN-C5-1850	Patch Fireproofing - Overall Rough-in - INTR - C5	2.0d	13-Oct-27	14-Oct-27	66.0d
6968	RI-CN-C5-1860	Install Wall Insulation - Overall Rough-in - INTR - C5	3.0d	15-Oct-27	19-Oct-27	66.0d
6969	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 6		175.0d	4-Feb-27	11-Oct-27	95.0d
6970	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 6		175.0d	4-Feb-27	11-Oct-27	95.0d
6971	WBS - Overall Rough-in - INTR - Conc. 6		175.0d	4-Feb-27	11-Oct-27	95.0d
6972	RI-CN-C6-1870	Layout Walls/Top Track - Overall Rough-in - INTR - C6	10.0d	4-Feb-27	17-Feb-27	57.0d

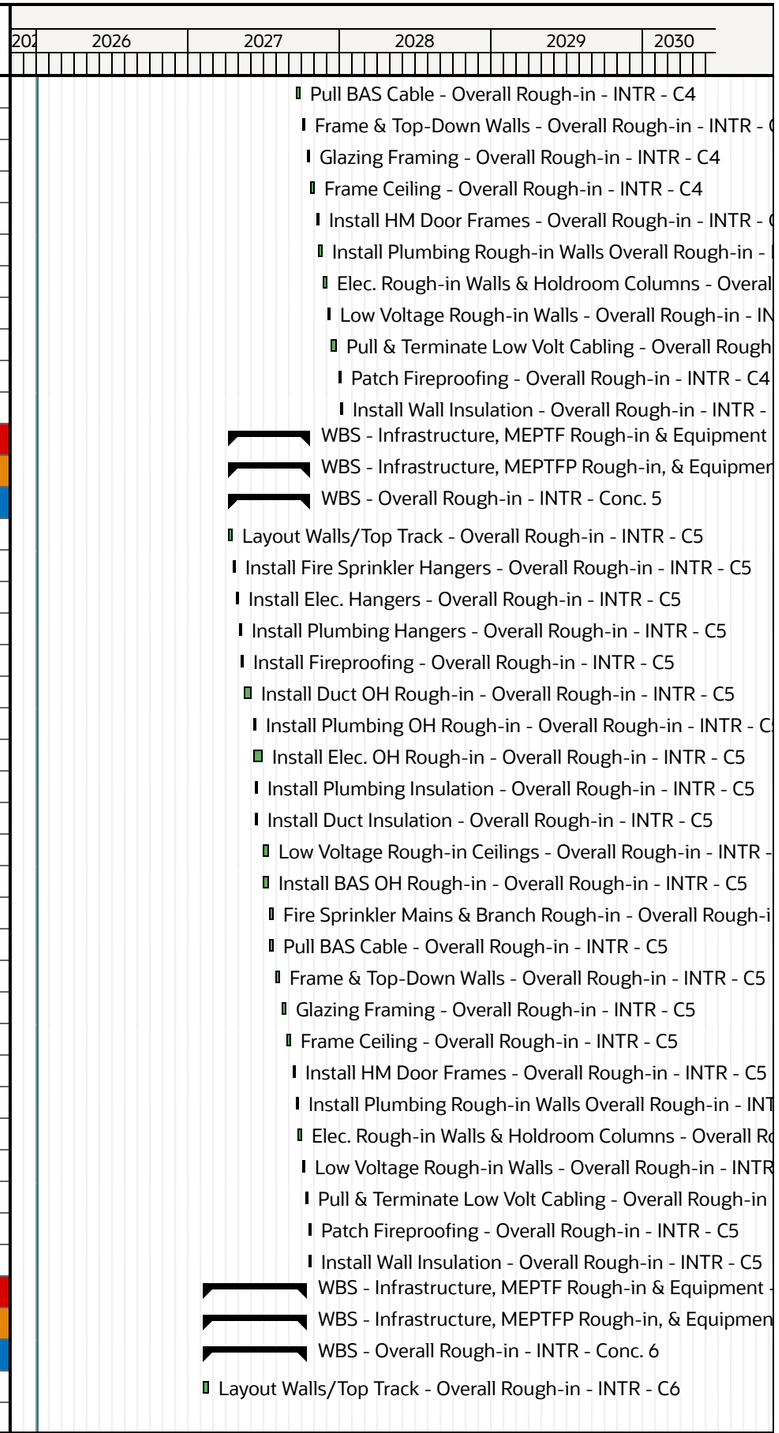


	ID	Name	Dur	Start	Finish	TF
6973	RI-CN-C6-1880	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C6	5.0d	18-Feb-27	24-Feb-27	57.0d
6974	RI-CN-C6-1890	Install Elec. Hangers - Overall Rough-in - INTR - C6	5.0d	25-Feb-27	3-Mar-27	57.0d
6975	RI-CN-C6-1900	Install Plumbing Hangers - Overall Rough-in - INTR - C6	3.0d	4-Mar-27	8-Mar-27	57.0d
6976	RI-CN-C6-1910	Install Fireproofing - Overall Rough-in - INTR - C6	5.0d	9-Mar-27	15-Mar-27	57.0d
6977	RI-CN-C6-1920	Install Duct OH Rough-in - Overall Rough-in - INTR - C6	15.0d	16-Mar-27	5-Apr-27	57.0d
6978	RI-CN-C6-1930	Install Plumbing OH Rough-in - Overall Rough-in - INTR - C6	15.0d	6-Apr-27	26-Apr-27	57.0d
6979	RI-CN-C6-1940	Install Elec. OH Rough-in - Overall Rough-in - INTR - C6	15.0d	27-Apr-27	17-May-27	57.0d
6980	RI-CN-C6-1950	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C6	10.0d	18-May-27	1-Jun-27	57.0d
6981	RI-CN-C6-2090	Install BAS OH Rough-in - Overall Rough-in - INTR - C6	10.0d	18-May-27	1-Jun-27	57.0d
6982	RI-CN-C6-1960	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C6	10.0d	2-Jun-27	15-Jun-27	57.0d
6983	RI-CN-C6-2100	Pull BAS Cable - Overall Rough-in - INTR - C6	10.0d	2-Jun-27	15-Jun-27	177.0d
6984	RI-CN-C6-1970	Frame & Top-Down Walls - Overall Rough-in - INTR - C6	10.0d	16-Jun-27	29-Jun-27	57.0d
6985	RI-CN-C6-2070	Frame Glass Glazing - Overall Rough-in - INTR - C6	10.0d	30-Jun-27	14-Jul-27	57.0d
6986	RI-CN-C6-1980	Frame Ceiling - Overall Rough-in - INTR - C6	10.0d	15-Jul-27	28-Jul-27	57.0d
6987	RI-CN-C6-1990	Install Plumbing Insulation - Overall Rough-in - INTR - C6	5.0d	29-Jul-27	4-Aug-27	57.0d
6988	RI-CN-C6-2000	Install Duct Insulation - Overall Rough-in - INTR - C6	5.0d	29-Jul-27	4-Aug-27	57.0d
6989	RI-CN-C6-2010	Install HM Door Frames - Overall Rough-in - INTR - C6	5.0d	29-Jul-27	4-Aug-27	57.0d
6990	RI-CN-C6-2020	Install Plumbing Rough-in Walls Overall Rough-in - INTR - C6	20.0d	5-Aug-27	1-Sep-27	57.0d
6991	RI-CN-C6-2030	Elec. Rough-in Walls & Holdroom Columns - Overall Rough-in - INTR - C6	7.0d	2-Sep-27	13-Sep-27	57.0d
6992	RI-CN-C6-2040	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C6	5.0d	14-Sep-27	20-Sep-27	57.0d
6993	RI-CN-C6-2080	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - C6	10.0d	21-Sep-27	4-Oct-27	57.0d
6994	RI-CN-C6-2050	Patch Fireproofing - Overall Rough-in - INTR - C6	2.0d	5-Oct-27	6-Oct-27	57.0d
6995	RI-CN-C6-2060	Install Wall Insulation - Overall Rough-in - INTR - C6	3.0d	7-Oct-27	11-Oct-27	57.0d
6996	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 7		133.0d	17-Dec-26	24-Jun-27	163.0d
6997	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 7		133.0d	17-Dec-26	24-Jun-27	163.0d
6998	WBS - Overall Rough-in - INTR - Conc. 7		133.0d	17-Dec-26	24-Jun-27	163.0d
6999	RI-CN-C7-2070	Layout Walls/Top Track - Overall Rough-in - INTR - C7	10.0d	17-Dec-26	31-Dec-26	78.0d
7000	RI-CN-C7-2080	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - C7	5.0d	4-Jan-27	8-Jan-27	78.0d
7001	RI-CN-C7-2090	Install Elec. Hangers - Overall Rough-in - INTR - C7	5.0d	11-Jan-27	15-Jan-27	78.0d
7002	RI-CN-C7-2110	Install Fireproofing - Overall Rough-in - INTR - C7	5.0d	18-Jan-27	22-Jan-27	78.0d
7003	RI-CN-C7-2120	Install Duct OH Rough-in - Overall Rough-in - INTR - C7	15.0d	25-Jan-27	12-Feb-27	78.0d
7004	RI-CN-C7-2140	Install Elec. OH Rough-in - Overall Rough-in - INTR - C7	15.0d	15-Feb-27	5-Mar-27	98.0d
7005	RI-CN-C7-2200	Install Duct Insulation - Overall Rough-in - INTR - C7	5.0d	15-Feb-27	19-Feb-27	179.0d
7006	RI-CN-C7-2150	Low Voltage Rough-in Ceilings - Overall Rough-in - INTR - C7	10.0d	8-Mar-27	19-Mar-27	98.0d
7007	RI-CN-C7-2290	Install BAS OH Rough-in - Overall Rough-in - INTR - C7	10.0d	8-Mar-27	19-Mar-27	98.0d
7008	RI-CN-C7-2160	Fire Sprinkler Mains & Branch Rough-in - Overall Rough-in - INTR - C7	10.0d	22-Mar-27	2-Apr-27	98.0d
7009	RI-CN-C7-2300	Pull BAS Cable - Overall Rough-in - INTR - C7	10.0d	22-Mar-27	2-Apr-27	221.0d
7010	RI-CN-C7-2170	Frame & Top-Down Walls - Overall Rough-in - INTR - C7	10.0d	5-Apr-27	16-Apr-27	98.0d
7011	RI-CN-C7-2270	Frame Glass Glazing - Overall Rough-in - INTR - C7	7.0d	19-Apr-27	27-Apr-27	117.0d
7012	RI-CN-C7-2180	Frame Ceiling - Overall Rough-in - INTR - C7	10.0d	28-Apr-27	11-May-27	117.0d
7013	RI-CN-C7-2210	Install HM Door Frames - Overall Rough-in - INTR - C7	5.0d	12-May-27	18-May-27	117.0d
7014	RI-CN-C7-2230	Elec. Rough-in Walls & Holdroom Columns - Overall Rough-in - INTR - C7	7.0d	19-May-27	27-May-27	117.0d

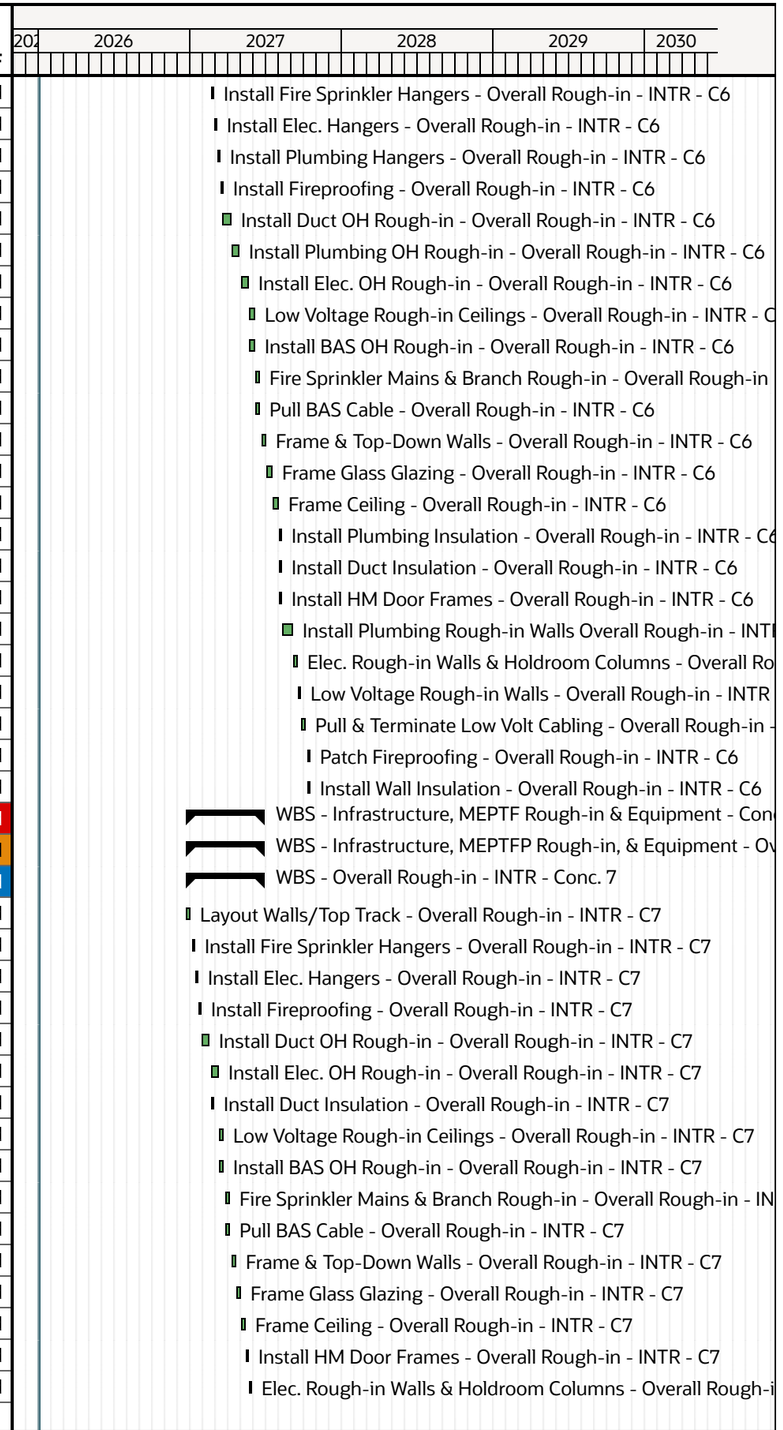


	ID	Name	Dur	Start	Finish	TF
7015	RI-CN-C7-2240	Low Voltage Rough-in Walls - Overall Rough-in - INTR - C7	5.0d	28-May-27	4-Jun-27	117.0d
7016	RI-CN-C7-2280	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - C7	9.0d	7-Jun-27	17-Jun-27	117.0d
7017	RI-CN-C7-2250	Patch Fireproofing - Overall Rough-in - INTR - C7	2.0d	18-Jun-27	21-Jun-27	117.0d
7018	RI-CN-C7-2260	Install Wall Insulation - Overall Rough-in - INTR - C7	3.0d	22-Jun-27	24-Jun-27	117.0d
7019	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 8		245.0d	5-Mar-27	21-Feb-28	13.0d
7020	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Conc. 8		245.0d	5-Mar-27	21-Feb-28	13.0d
7021	WBS - Overall Rough-in - INTR - Conc. 8		245.0d	5-Mar-27	21-Feb-28	13.0d
7022	WBS - Phase 1 High Ceiling - Conc. 8		176.0d	11-Jun-27	21-Feb-28	0.0d
7023	RI-C8-2470	Dancefloor Install Phase 1 - Overall - INTR - C8 Ph1	31.0d	11-Jun-27	26-Jul-27	0.0d
7024	RI-C8-2560	Install Fire Sprinkler Hangers - Phase 1 - C8 Ph1	5.0d	27-Jul-27	2-Aug-27	0.0d
7025	RI-C8-2570	Install Elec. Hangers - Phase 1 - C8 Ph1	5.0d	27-Jul-27	2-Aug-27	0.0d
7026	RI-C8-2690	Architectural Form Ceiling Framing - Overall - INTR - C8 Ph1	15.0d	27-Jul-27	16-Aug-27	34.0d
7027	RI-C8-2580	Install Low Voltage Hangers - Phase 1 - C8 Ph1	5.0d	29-Jul-27	4-Aug-27	0.0d
7028	RI-C8-2610	Fire Sprinkler Mains & Branch Rough-in - Overall - INTR - C8 Ph1	20.0d	3-Aug-27	30-Aug-27	2.0d
7029	RI-C8-2590	Install Elec. OH Rough-in - Overall Rough-in - INTR - C8 Ph1 Ph1	20.0d	3-Aug-27	30-Aug-27	2.0d
7030	RI-C8-2600	Low Voltage Rough-in Ceilings - Overall - INTR - C8 Ph1	15.0d	5-Aug-27	25-Aug-27	5.0d
7031	RI-C8-3080	Frame Drywall Ceiling - Inner Soffit - Phase 1 - C8 Ph1	20.0d	5-Aug-27	1-Sep-27	0.0d
7032	RI-C8-3090	Install ACT Ceiling Grid Supports - Phase 1 - C8 Ph1	20.0d	5-Aug-27	1-Sep-27	0.0d
7033	RI-C8-3150	Architectural Form Transition/Bottom Edge Framing - Overall - INTR - C8 Ph1	15.0d	17-Aug-27	7-Sep-27	34.0d
7034	RI-C8-2540	Frame Drywall Ceiling - Outter Soffit - Phase 1 - C8 Ph1	20.0d	2-Sep-27	30-Sep-27	0.0d
7035	RI-C8-3160	Rough- In Architectural Form/LED Screen - Overall - INTR - C8 Ph1	20.0d	8-Sep-27	5-Oct-27	34.0d
7036	RI-C8-1760	Install ACT Ceiling Grid - Phase 1 - C8 Ph1	20.0d	17-Sep-27	14-Oct-27	0.0d
7037	RI-C8-3140	Install GFRG - Architectural Form - Overall - INTR - C8 Ph1	20.0d	6-Oct-27	2-Nov-27	34.0d
7038	RI-C8-2620	Complete Fire Sprinkler OH Rough-in - Phase 1 - C8 Ph1	10.0d	8-Oct-27	21-Oct-27	0.0d
7039	RI-C8-2630	Complete Elec. OH Rough-in - Phase 1 - C8 Ph1	10.0d	12-Oct-27	25-Oct-27	0.0d
7040	RI-C8-2640	Complete Low Voltage OH Rough-in - Phase 1 - C8 Ph1	5.0d	15-Oct-27	21-Oct-27	2.0d
7041	RI-C8-2670	Install GFRP High Area - Overall - INTR - C8 Ph1	20.0d	15-Oct-27	11-Nov-27	27.0d
7042	RI-C8-2550	Hang, Tape & Finish Drywall Ceiling - Phase 1 - C8 Ph1	20.0d	26-Oct-27	22-Nov-27	0.0d
7043	RI-C8-2700	Install GFRP Low Area - Overall - INTR - C8 Ph1	20.0d	12-Nov-27	13-Dec-27	27.0d
7044	RI-C8-1770	Install ACT Ceiling Device Tiles (Close-in) - Phase 1- C8 Ph1	10.0d	23-Nov-27	8-Dec-27	0.0d
7045	FN-CN-2410	Finish/Trim-Out High Ceiling Install - Overall - INTF - C8 Ph 1	20.0d	2-Dec-27	30-Dec-27	0.0d
7046	RI-C8-3100	Install ACT Remaining Tiles (Close-in) - Phase 1- C8 Ph1	20.0d	16-Dec-27	14-Jan-28	0.0d
7047	FN-CN-2500	Apply Final Paint High Ceiling - Overall - INTF - C8 Ph 1	8.0d	12-Jan-28	21-Jan-28	0.0d
7048	RI-C8-2650	Dancefloor Removal Phase 1 - Overall - INTR - C8 Ph1	21.0d	24-Jan-28	21-Feb-28	0.0d
7049	WBS - Phase 2 High Ceiling- Conc. 8		206.0d	5-Mar-27	27-Dec-27	52.0d
7050	RI-C8-2520	Dancefloor Install Phase 2 - Overall - INTR - C8 Ph2	33.0d	5-Mar-27	20-Apr-27	0.0d
7051	RI-C8-2720	Install Fire Sprinkler Hangers - Phase 2 - C8 Ph2	5.0d	21-Apr-27	27-Apr-27	69.0d
7052	RI-C8-3170	Architectural Form Ceiling Framing - Overall - INTR - C8 Ph2	15.0d	21-Apr-27	11-May-27	113.0d
7053	RI-C8-2730	Install Elec. Hangers - Phase 2 - C8 Ph2	10.0d	23-Apr-27	6-May-27	69.0d
7054	RI-C8-2740	Install Low Voltage Hangers - Phase 2 - C8 Ph2	5.0d	27-Apr-27	3-May-27	74.0d
7055	RI-C8-2750	Fire Sprinkler Mains & Branch Rough-in - Overall - INTR - C8 Ph2	20.0d	28-Apr-27	25-May-27	76.0d
7056	RI-C8-2770	Low Voltage Rough-in Ceilings - Overall - INTR - C8 Ph2	15.0d	4-May-27	24-May-27	77.0d




	ID	Name	Dur	Start	Finish	TF
7057	RI-C8-2760	Install Elec. OH Rough-in - Overall Rough-in - INTR - C8 Ph2 Ph2	20.0d	7-May-27	4-Jun-27	69.0d
7058	RI-C8-3130	Frame Drywall Ceiling - Inner Soffit - Phase 2 - C8 Ph2	20.0d	11-May-27	8-Jun-27	69.0d
7059	RI-C8-3120	Install ACT Ceiling Grid Supports - Phase 2 - C8 Ph2	18.0d	11-May-27	4-Jun-27	69.0d
7060	RI-C8-3180	Architectural Form Transition/Bottom Edge Framing - Overall - INTR - C8 Ph2	15.0d	12-May-27	2-Jun-27	113.0d
7061	RI-C8-3190	Rough- In Architectural Form/LED Screen - Overall - INTR - C8 Ph2	20.0d	3-Jun-27	30-Jun-27	113.0d
7062	RI-C8-2780	Frame Drywall Ceiling - Outter Soffit - Phase 2 - C8 Ph2	20.0d	9-Jun-27	7-Jul-27	69.0d
7063	RI-C8-2790	Install ACT Ceiling Grid - Phase 2 - C8 Ph2	20.0d	23-Jun-27	21-Jul-27	69.0d
7064	RI-C8-3200	Install GFRG - Architectural Form - Overall - INTR - C8 Ph2	20.0d	1-Jul-27	29-Jul-27	113.0d
7065	RI-C8-2800	Complete Fire Sprinkler OH Rough-in - Phase 2 - C8 Ph2	10.0d	15-Jul-27	28-Jul-27	69.0d
7066	RI-C8-2810	Complete Elec. OH Rough-in - Phase 2 - C8 Ph2	10.0d	19-Jul-27	30-Jul-27	69.0d
7067	RI-C8-2820	Complete Low Voltage OH Rough-in - Phase 2 - C8 Ph2	5.0d	22-Jul-27	28-Jul-27	71.0d
7068	RI-C8-2850	Install GFRP High Area - Overall - INTR - C8 Ph2	20.0d	22-Jul-27	18-Aug-27	99.0d
7069	RI-C8-2880	Install GFRP Low Area - Overall - INTR - C8 Ph2	20.0d	19-Aug-27	16-Sep-27	99.0d
7070	RI-C8-2830	Hang, Tape & Finish Drywall Ceiling - Phase 2 - C8 Ph2	20.0d	25-Aug-27	22-Sep-27	52.0d
7071	RI-C8-3110	Install ACT Ceiling Device Tiles (Close-in) - Phase 2- C8 Ph2	15.0d	23-Sep-27	13-Oct-27	52.0d
7072	RI-C8-2840	Install ACT Remaining Tiles (Close-in) - Phase 2- C8 Ph2	20.0d	14-Oct-27	10-Nov-27	52.0d
7073	FN-CN-2420	Finish/Trim-Out High Ceiling Install - Overall - INTF - C8 Ph2 Ph2	20.0d	14-Oct-27	10-Nov-27	60.0d
7074	FN-CN-2510	Apply Final Paint High Ceiling - Overall - INTF - C8 Ph 2	8.0d	11-Nov-27	22-Nov-27	52.0d
7075	RI-C8-2890	Dancefloor Removal Phase 2 - Overall - INTR - C8 Ph2	22.0d	23-Nov-27	27-Dec-27	52.0d
7076	WBS - Phase 3 High Ceiling - Conc. 8		187.0d	21-Apr-27	17-Jan-28	32.0d
7077	RI-C8-2530	Dancefloor Install Phase 3 - Overall - INTR - C8 Ph3	36.0d	21-Apr-27	10-Jun-27	0.0d
7078	RI-C8-2900	Install Fire Sprinkler Hangers - Phase 3 - C8 Ph3	5.0d	11-Jun-27	17-Jun-27	32.0d
7079	RI-C8-3210	Architectural Form Ceiling Framing - Overall - INTR - C8 Ph3	15.0d	11-Jun-27	1-Jul-27	70.0d
7080	RI-C8-2910	Install Elec. Hangers - Phase 3 - C8 Ph3	10.0d	15-Jun-27	28-Jun-27	32.0d
7081	RI-C8-2920	Install Low Voltage Hangers - Phase 3 - C8 Ph3	5.0d	17-Jun-27	23-Jun-27	35.0d
7082	RI-C8-2930	Fire Sprinkler Mains & Branch Rough-in - Overall - INTR - C8 Ph3	20.0d	18-Jun-27	16-Jul-27	39.0d
7083	RI-C8-2950	Low Voltage Rough-in Ceilings - Overall - INTR - C8 Ph3	15.0d	24-Jun-27	15-Jul-27	40.0d
7084	RI-C8-2940	Install Elec. OH Rough-in - Overall Rough-in - INTR - C8 Ph3 Ph3	20.0d	29-Jun-27	27-Jul-27	32.0d
7085	RI-C8-3250	Install ACT Ceiling Grid Supports - Phase 2 - C8 Ph3	20.0d	29-Jun-27	27-Jul-27	32.0d
7086	RI-C8-3270	Frame Drywall Ceiling - Inner Soffit - Phase 3 - C8 Ph3	20.0d	29-Jun-27	27-Jul-27	32.0d
7087	RI-C8-3220	Architectural Form Transition/Bottom Edge Framing - Overall - INTR - C8 Ph3	15.0d	2-Jul-27	23-Jul-27	70.0d
7088	RI-C8-3230	Rough- In Architectural Form/LED Screen - Overall - INTR - C8 Ph3	20.0d	26-Jul-27	20-Aug-27	70.0d
7089	RI-C8-3260	Frame Drywall Ceiling - Outter Soffit - Phase 3 - C8 Ph3	20.0d	28-Jul-27	24-Aug-27	32.0d
7090	RI-C8-2970	Install ACT Ceiling Grid - Phase 3- C8 Ph3	20.0d	11-Aug-27	8-Sep-27	32.0d
7091	RI-C8-3240	Install GFRG - Architectural Form - Overall - INTR - C8 Ph3	20.0d	23-Aug-27	20-Sep-27	70.0d
7092	RI-C8-2980	Complete Fire Sprinkler OH Rough-in - Phase 3 - C8 Ph3	10.0d	1-Sep-27	15-Sep-27	32.0d
7093	RI-C8-2990	Complete Elec. OH Rough-in - Phase 3 - C8 Ph3	7.0d	7-Sep-27	15-Sep-27	32.0d
7094	RI-C8-3000	Complete Low Voltage OH Rough-in - Phase 3 - C8 Ph3	5.0d	9-Sep-27	15-Sep-27	32.0d
7095	RI-C8-3030	Install GFRP High Area - Overall - INTR - C8 Ph3	20.0d	9-Sep-27	6-Oct-27	58.0d
7096	RI-C8-3010	Hang, Tape & Finish Drywall Ceiling - Phase 3 - C8 Ph3	20.0d	16-Sep-27	13-Oct-27	32.0d
7097	RI-C8-3060	Install GFRP Low Area - Overall - INTR - C8 Ph3	20.0d	7-Oct-27	3-Nov-27	58.0d
7098	RI-C8-3280	Install ACT Ceiling Device Tiles (Close-in) - Phase 3- C8 Ph3	18.0d	14-Oct-27	8-Nov-27	32.0d

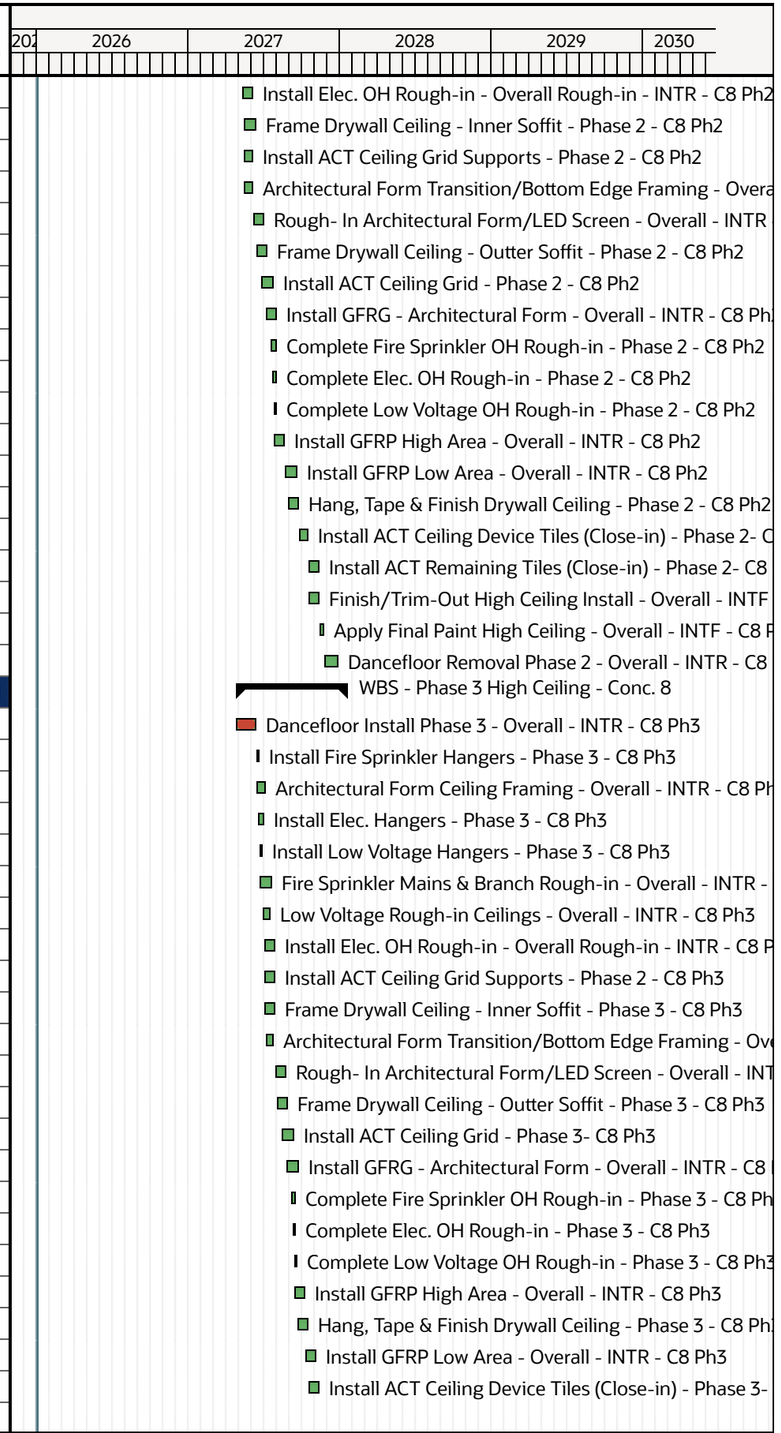


	ID	Name	Dur	Start	Finish	TF
7099	RI-C8-3020	Install ACT Ceiling Tiles (Close-in) - Phase 3A - C8 Ph3	10.0d	9-Nov-27	22-Nov-27	32.0d
7100	FN-CN-2430	Finish/Trim-Out High Ceiling Install - Overall - INTF - C8 Ph3	20.0d	9-Nov-27	8-Dec-27	35.0d
7101	RI-C8-3290	Install ACT Ceiling Tiles (Close-in) - Phase 3B- C8 Ph3	15.0d	9-Nov-27	1-Dec-27	32.0d
7102	FN-CN-2520	Apply Final Paint High Ceiling - Overall - INTF - C8 Ph 3	8.0d	2-Dec-27	13-Dec-27	32.0d
7103	RI-C8-3070	Dancefloor Removal Phase 3 - Overall - INTR - C8 Ph3	23.0d	14-Dec-27	17-Jan-28	32.0d
7104	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 9		155.0d	11-Mar-27	18-Oct-27	228.0d
7105	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall/Restrooms/Concessions - Conc.9		155.0d	11-Mar-27	18-Oct-27	228.0d
7106	WBS - Overall/Gang Bathrooms #3/Concessions - INTR - Concourse 9		155.0d	11-Mar-27	18-Oct-27	228.0d
7107	RI-C9-R3-1630	Layout Walls/Top Track - Overall/Restrooms - INTR - C9	10.0d	11-Mar-27	24-Mar-27	153.0d
7108	RI-C9-R3-5840	Install Fire Sprinkler Hangers - Overall/Restrooms - INTR - C9	2.0d	25-Mar-27	26-Mar-27	153.0d
7109	RI-C9-R3-5850	Install Duct Hangers - Overall/Restrooms - INTR - C9	2.0d	29-Mar-27	30-Mar-27	153.0d
7110	RI-C9-R3-5860	Install CHW Hangers - Overall/Restrooms - INTR - C9	2.0d	31-Mar-27	1-Apr-27	153.0d
7111	RI-C9-R3-5870	Install Plumbing Hangers - Overall/Restrooms - INTR - C9	5.0d	2-Apr-27	8-Apr-27	153.0d
7112	RI-C9-R3-5880	Install Elec. Hangers - Overall/Restrooms - INTR - C9	2.0d	9-Apr-27	12-Apr-27	153.0d
7113	RI-C9-R3-5890	Install Fireproofing - Overall/Restrooms - INTR - C9	3.0d	30-Apr-27	4-May-27	140.0d
7114	RI-C9-R3-5950	Fire Sprinkler Mains & Branch Line Rough-in - Overall/Restrooms - INTR - C9	10.0d	5-May-27	18-May-27	140.0d
7115	RI-C9-R3-5900	Install Plumbing/Gas OH Rough-in - Overall/Restrooms - INTR - C9	10.0d	19-May-27	2-Jun-27	140.0d
7116	RI-C9-R3-5910	Install CHW OH Rough-in - Overall/Restrooms - INTR - C9	12.0d	24-May-27	9-Jun-27	140.0d
7117	RI-C9-R3-5920	Install Duct OH Rough-in - Overall/Restrooms - INTR - C9	12.0d	1-Jun-27	16-Jun-27	140.0d
7118	RI-C9-R3-5930	Install Elec. OH Rough-in - Overall Rough-in - INTR - C9	15.0d	17-Jun-27	8-Jul-27	140.0d
7119	RI-C9-R3-5940	Install Low Voltage OH Rough-in - Overall/Restrooms - INTR - C9	6.0d	8-Jul-27	15-Jul-27	145.0d
7120	RI-C9-R3-6010	Install BAS OH Rough-in - Overall/Restrooms - INTR - C9	10.0d	9-Jul-27	22-Jul-27	140.0d
7121	RI-C9-R3-5960	Install Duct Insulation - Overall/Restrooms - INTR - C9	5.0d	23-Jul-27	29-Jul-27	140.0d
7122	RI-C9-R3-5970	Install CHW Insulation - Overall/Restrooms - INTR - C9	5.0d	23-Jul-27	29-Jul-27	148.0d
7123	RI-C9-R3-6020	Pull BAS Cable - Overall/Restrooms - INTR - C9	10.0d	23-Jul-27	5-Aug-27	199.0d
7124	RI-C9-R3-5980	Install Plumbing Insulation - Overall/Restrooms - INTR - C9	4.0d	30-Jul-27	4-Aug-27	148.0d
7125	RI-C9-R3-1740	Install HM Door Frames - Overall/Restrooms - INTR - C9	2.0d	5-Aug-27	6-Aug-27	161.0d
7126	RI-C9-R3-1890	Frame & Top-Down Walls - Overall/Restrooms - INTR - C9	10.0d	5-Aug-27	18-Aug-27	148.0d
7127	RI-C9-R3-1620	Set Restroom Carriers - Overall/Restrooms - INTR - C9	5.0d	19-Aug-27	25-Aug-27	148.0d
7128	RI-C9-R3-6000	Install 1/2" Plywood Backing - Overall/Restrooms - INTR - C9	2.0d	19-Aug-27	20-Aug-27	268.0d
7129	RI-C9-R3-1650	Install Plumbing Rough-in Walls - Overall/Restrooms - INTR - C9	17.0d	26-Aug-27	20-Sep-27	148.0d
7130	RI-C9-R3-1690	Install Blocking & Backing/Verify Recess Specialties & Signage - Overall/Restro...	6.0d	26-Aug-27	2-Sep-27	179.0d
7131	RI-C9-R3-1640	Elec. Rough-in Walls - Overall/Restrooms - INTR - C9	8.0d	21-Sep-27	30-Sep-27	148.0d
7132	RI-C9-R3-1700	Low Voltage Rough-in Walls - Overall/Restrooms - INTR - C9	3.0d	1-Oct-27	5-Oct-27	148.0d
7133	RI-C9-R3-1670	Install Vanities Steel Support - Overall/Restrooms - INTR - C9	4.0d	6-Oct-27	11-Oct-27	151.0d
7134	RI-C9-R3-1790	Install Recessed Can RI/Speaker RI Frames - Overall/Restrooms - INTR - C9	2.0d	6-Oct-27	7-Oct-27	155.0d
7135	RI-C9-R3-5990	Pull & Terminate Low Volt Cabling - Overall/Restrooms - INTR - C9	7.0d	6-Oct-27	14-Oct-27	148.0d
7136	RI-C9-R3-1910	Install Wall Insulation - Overall/Restrooms - INTR - C9	2.0d	15-Oct-27	18-Oct-27	148.0d
7137	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 10		109.0d	5-Mar-27	6-Aug-27	205.0d
7138	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall/Restrooms/Concessions - Concourse 10		109.0d	5-Mar-27	6-Aug-27	205.0d
7139	RI-C10-R2-120	Layout Walls/Top Track - Overall/Restrooms/Concess. - INTR - C10	5.0d	5-Mar-27	11-Mar-27	160.0d
7140	RI-C10-R2-5990	Install Fire Sprinkler Hangers - Overall/Restrooms/Concess. - INTR - C10	2.0d	12-Mar-27	15-Mar-27	160.0d

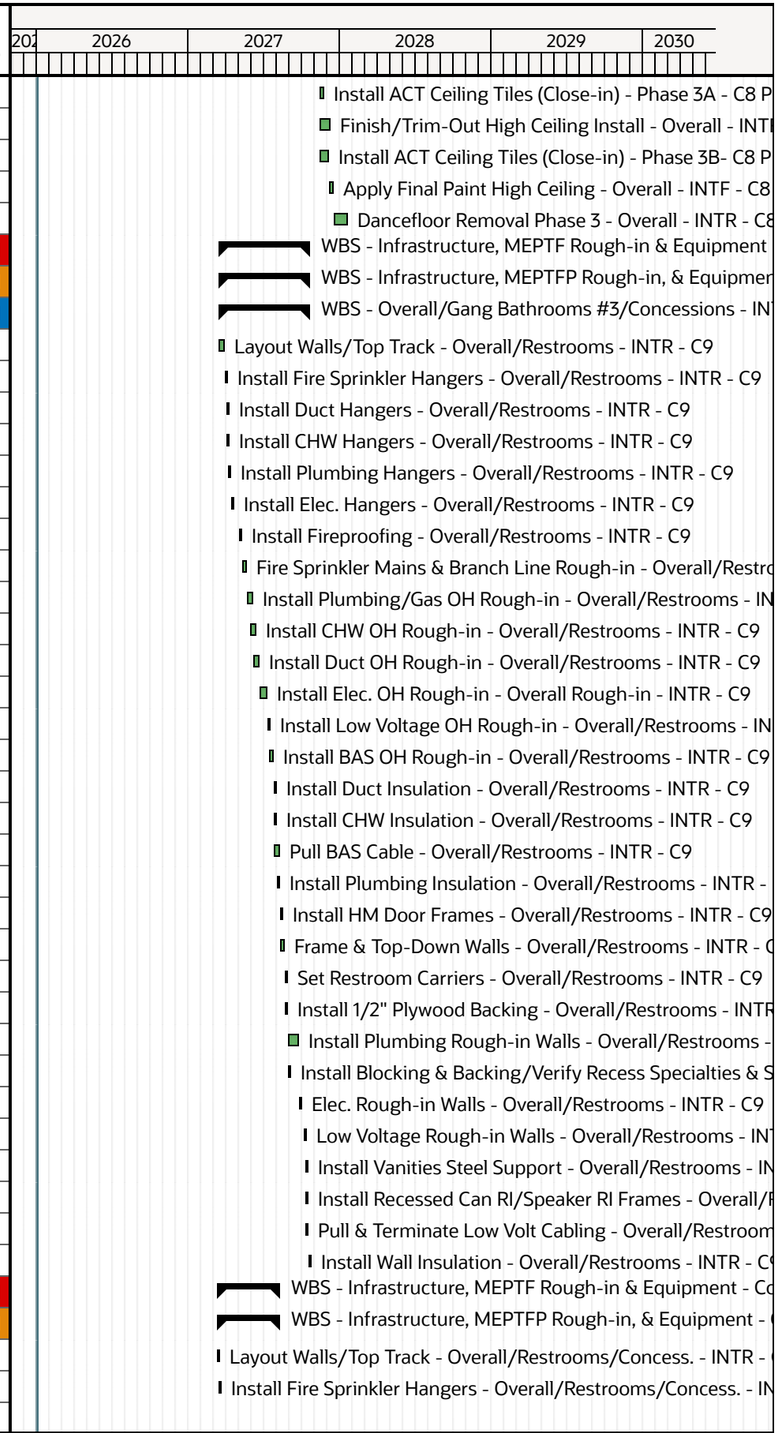


	ID	Name	Dur	Start	Finish	TF
7141	RI-C10-R2-6000	Install Duct Hangers - Overall/Restrooms/Concess. - INTR - C10	2.0d	16-Mar-27	17-Mar-27	160.0d
7142	RI-C10-R2-6010	Install CHW Hangers - Overall/Restrooms/Concess. - INTR - C10	2.0d	18-Mar-27	19-Mar-27	160.0d
7143	RI-C10-R2-6020	Install Plumbing Hangers - Overall/Restrooms/Concess. - INTR - C10	4.0d	22-Mar-27	25-Mar-27	160.0d
7144	RI-C10-R2-6030	Install Elec. Hangers - Overall/Restrooms/Concess. - INTR - C10	2.0d	26-Mar-27	29-Mar-27	160.0d
7145	RI-C10-R2-6040	Install Fireproofing - Overall/Restrooms/Concess. - INTR - C10	3.0d	9-Apr-27	13-Apr-27	152.0d
7146	RI-C10-R2-6100	Fire Sprinkler Mains & Branch Line Rough-in - Overall/Restrooms/Concess. - I...	10.0d	14-Apr-27	27-Apr-27	152.0d
7147	RI-C10-R2-6050	Install Plumbing/Gas OH Rough-in - Overall/Restrooms/Concess. - INTR - C10	6.0d	19-Apr-27	26-Apr-27	152.0d
7148	RI-C10-R2-6060	CHW OH Rough-in - Overall/Restrooms/Concess. - INTR - C10	8.0d	19-Apr-27	28-Apr-27	152.0d
7149	RI-C10-R2-6070	Install Duct OH Rough-in - Overall/Restrooms/Concess. - INTR - C10	10.0d	29-Apr-27	12-May-27	152.0d
7150	RI-C10-R2-6130	Install Plumbing Insulation - Overall/Restrooms/Concess. - INTR - C10	5.0d	30-Apr-27	6-May-27	200.0d
7151	RI-C10-R2-6080	Install Elec. OH Rough-in - Overall Rough-in - INTR - C10	15.0d	13-May-27	3-Jun-27	164.0d
7152	RI-C10-R2-6090	Low Voltage OH Rough-in - Overall/Restrooms/Concess. - INTR - C10	6.0d	4-Jun-27	11-Jun-27	168.0d
7153	RI-C10-R2-6160	Install BAS OH Rough-in - Overall/Restrooms/Concess. - INTR - C10	10.0d	4-Jun-27	17-Jun-27	164.0d
7154	RI-C10-R2-6110	Install Duct Insulation - Overall/Restrooms/Concess. - INTR - C10	5.0d	18-Jun-27	24-Jun-27	164.0d
7155	RI-C10-R2-6120	Install CHW Insulation - Overall/Restrooms/Concess. - INTR - C10	5.0d	18-Jun-27	24-Jun-27	166.0d
7156	RI-C10-R2-6170	Pull BAS Cable - Overall/Restrooms/Concess. - INTR - C10	10.0d	18-Jun-27	1-Jul-27	230.0d
7157	RI-C10-R2-330	Install HM Door Frames - Overall/Restrooms/Concess. - INTR - C10	2.0d	25-Jun-27	28-Jun-27	218.0d
7158	RI-C10-R2-1920	Frame & Top-Down Walls - Overall/Restrooms/Concess. - INTR - C10	10.0d	25-Jun-27	9-Jul-27	166.0d
7159	RI-C10-R2-160	Set Restroom Carriers - Overall/Restrooms/Concess. - INTR - C10	5.0d	12-Jul-27	16-Jul-27	205.0d
7160	RI-C10-R2-480	Install Plumbing Rough-in Walls - Overall/Restrooms/Concess. - INTR - C10	10.0d	19-Jul-27	30-Jul-27	205.0d
7161	RI-C10-R2-290	Install Blocking & Backing/Verify Recess Specialties & Signage - Overall/Restro...	3.0d	19-Jul-27	21-Jul-27	213.0d
7162	RI-C10-R2-510	Elec. Rough-in Walls - Overall/Restrooms/Concess. - INTR - C10	5.0d	23-Jul-27	29-Jul-27	205.0d
7163	RI-C10-R2-520	Low Voltage Rough-in Walls - Overall/Restrooms/Concess. - INTR - C10	3.0d	23-Jul-27	27-Jul-27	206.0d
7164	RI-C10-R2-6140	Pull & Terminate Low Volt Cabling - Overall/Restrooms/Concess. - INTR - C10	5.0d	28-Jul-27	3-Aug-27	206.0d
7165	RI-C10-R2-540	Install Vanities Steel Support - Overall/Restrooms/Concess. - INTR - C10	2.0d	30-Jul-27	2-Aug-27	205.0d
7166	RI-C10-R2-590	Install Recessed Can RI/Speaker RI Frames - Overall/Restrooms/Concess. - INT...	2.0d	3-Aug-27	4-Aug-27	205.0d
7167	RI-C10-R2-550	Install Wall Insulation - Overall/Restrooms/Concess. - INTR - C10	2.0d	5-Aug-27	6-Aug-27	205.0d
7168	WBS - Infrastructure, MEPTF Rough-in & Equipment - Concourse 11		157.0d	6-Jan-27	16-Aug-27	262.0d
7169	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall/Restrooms - Conc. 11		138.0d	6-Jan-27	20-Jul-27	281.0d
7170	WBS - Overall/Gang Bathrooms #1 - INTR - Concourse 11		138.0d	6-Jan-27	20-Jul-27	281.0d
7171	RI-C11-R1-10	Layout Walls/Top Track - Overall/Restrooms - INTR - C11	10.0d	6-Jan-27	19-Jan-27	7.0d
7172	RI-C11-R1-6140	Install Fire Sprinkler Hangers - Overall/Restrooms - INTR - C11	2.0d	20-Jan-27	21-Jan-27	7.0d
7173	RI-C11-R1-6150	Install Duct Hangers - Overall/Restrooms - INTR - C11	2.0d	22-Jan-27	25-Jan-27	7.0d
7174	RI-C11-R1-6160	Install CHW Hangers - Overall/Restrooms - INTR - C11	2.0d	26-Jan-27	27-Jan-27	7.0d
7175	RI-C11-R1-6170	Install Plumbing Hangers - Overall/Restrooms - INTR - C11	5.0d	28-Jan-27	3-Feb-27	7.0d
7176	RI-C11-R1-6180	Install Elec. Hangers - Overall/Restrooms - INTR - C11	2.0d	4-Feb-27	5-Feb-27	7.0d
7177	RI-C11-R1-6190	Install Fireproofing - Overall/Restrooms - INTR - C11	3.0d	8-Feb-27	10-Feb-27	7.0d
7178	RI-C11-R1-6250	Fire Sprinkler Mains & Branch Line Rough-in - Overall/Restrooms - INTR - C11	10.0d	11-Feb-27	24-Feb-27	7.0d
7179	RI-C11-R1-6200	Install Plumbing OH Rough-in - Overall/Restrooms - INTR - C11	10.0d	25-Feb-27	10-Mar-27	7.0d
7180	RI-C11-R1-6210	Install CHW OH Rough-in - Overall/Restrooms - INTR - C11	8.0d	25-Feb-27	8-Mar-27	9.0d
7181	RI-C11-R1-6220	Install Duct OH Rough-in - Overall/Restrooms - INTR - C11	8.0d	11-Mar-27	22-Mar-27	7.0d
7182	RI-C11-R1-6230	Install Elec. OH Rough-in - Overall Rough-in - INTR - C11	15.0d	23-Mar-27	12-Apr-27	7.0d

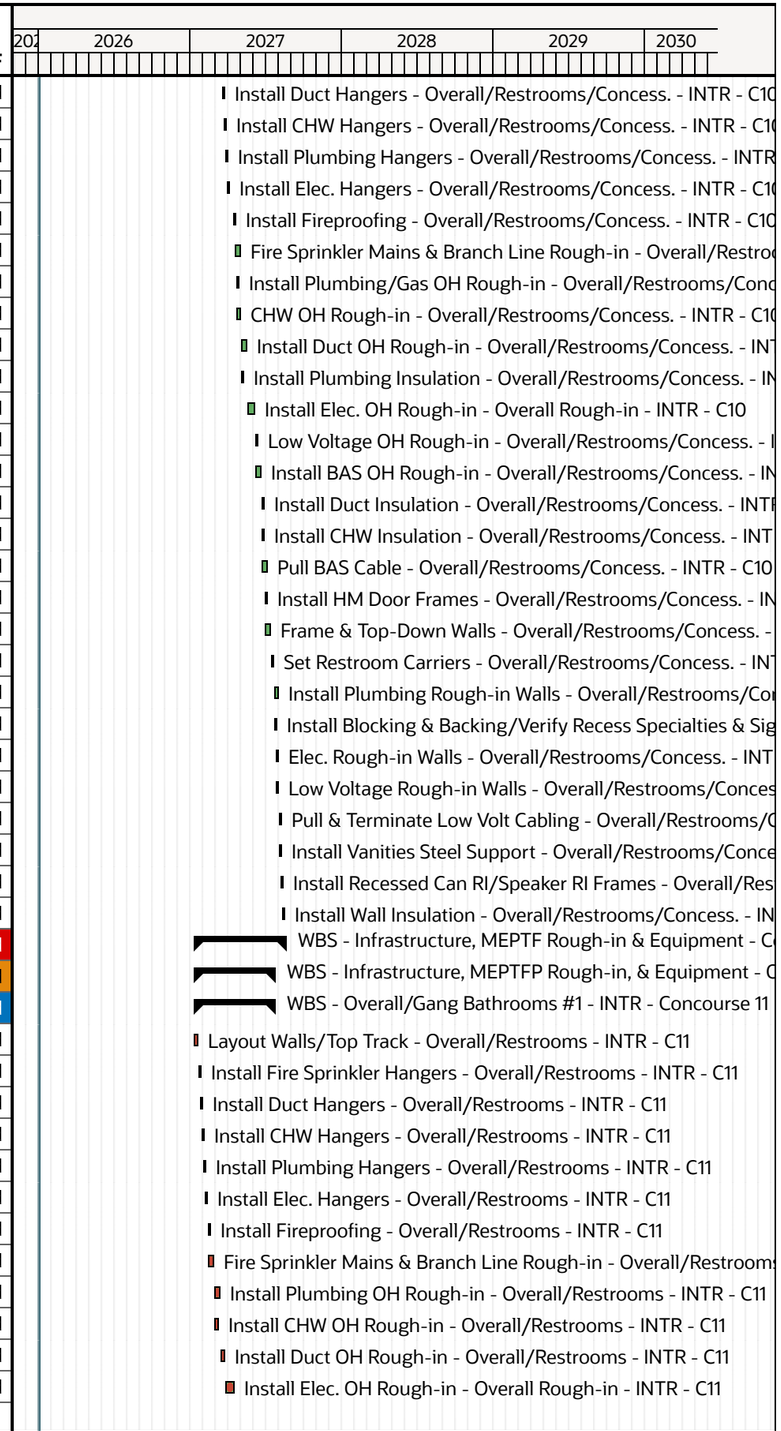


	ID	Name	Dur	Start	Finish	TF
7183	RI-C11-R1-6240	Install Low Voltage OH Rough-in - Overall/Restrooms - INTR - C11	6.0d	13-Apr-27	20-Apr-27	11.0d
7184	RI-C11-R1-6300	Install BAS OH Rough-in - Overall Rough-in - INTR - C11	10.0d	13-Apr-27	26-Apr-27	7.0d
7185	RI-C11-R1-6260	Install Duct Insulation - Overall/Restrooms - INTR - C11	4.0d	27-Apr-27	30-Apr-27	13.0d
7186	RI-C11-R1-6270	Install CHW Insulation - Overall/Restrooms - INTR - C11	5.0d	27-Apr-27	3-May-27	7.0d
7187	RI-C11-R1-6310	Pull BAS Cable - Overall Rough-in - INTR - C11	10.0d	27-Apr-27	10-May-27	197.0d
7188	RI-C11-R1-6280	Install Plumbing Insulation - Overall/Restrooms - INTR - C11	5.0d	4-May-27	10-May-27	7.0d
7189	RI-C11-R1-70	Install HM Door Frames - Overall/Restrooms - INTR - C11	2.0d	11-May-27	12-May-27	191.0d
7190	RI-C11-R1-1930	Frame & Top-Down Walls - Overall/Restrooms - INTR - C11	15.0d	11-May-27	1-Jun-27	7.0d
7191	RI-C11-R1-20	Set Restroom Carriers - Overall/Restrooms - INTR - C11	9.0d	2-Jun-27	14-Jun-27	148.0d
7192	RI-C11-R1-6320	Install 1/2" Plywood Backing - Overall/Restrooms - INTR - C11	4.0d	2-Jun-27	7-Jun-27	311.0d
7193	RI-C11-R1-40	Install Blocking & Backing/Verify Recess Specialties & Signage - Overall/Restro...	3.0d	15-Jun-27	17-Jun-27	148.0d
7194	RI-C11-R1-150	Install Plumbing Rough-in Walls - Overall/Restrooms - INTR - C11	20.0d	18-Jun-27	16-Jul-27	148.0d
7195	RI-C11-R1-190	Elec. Rough-in Walls - Overall/Restrooms - INTR - C11	5.0d	24-Jun-27	30-Jun-27	151.0d
7196	RI-C11-R1-200	Low Voltage Rough-in Walls - Overall/Restrooms - INTR - C11	3.0d	1-Jul-27	6-Jul-27	151.0d
7197	RI-C11-R1-220	Install Vanities Steel Support - Overall/Restrooms - INTR - C11	2.0d	7-Jul-27	8-Jul-27	156.0d
7198	RI-C11-R1-260	Install Recessed Can RI/Speaker RI Frames - Overall/Restrooms - INTR - C11	2.0d	7-Jul-27	8-Jul-27	154.0d
7199	RI-C11-R1-6290	Pull & Terminate Low Volt Cabling - Overall/Restrooms - INTR - C11	5.0d	7-Jul-27	13-Jul-27	151.0d
7200	RI-C11-R1-230	Install Wall Insulation - Overall/Restrooms - INTR - C11	2.0d	19-Jul-27	20-Jul-27	148.0d
7201	WBS - Service (#14 & #15) Elevator Cabs/Shaft - INTR - Concourse 11		153.0d	12-Jan-27	16-Aug-27	201.0d
7202	VC-EL-C11-3460	Install Elev. Safety Rail/Net - Service (#14 & #15) Elevator Cabs/Shaft - INTR - ...	5.0d	12-Jan-27	18-Jan-27	201.0d
7203	VC-EL-C11-3580	Install Scaffold in Hoistway - Service (#14 & #15) Elevator Cabs/Shaft - INTR - ...	5.0d	19-Jan-27	25-Jan-27	201.0d
7204	VC-EL-C11-3470	Rough-in Elec. In Shaft - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	8.0d	26-Jan-27	4-Feb-27	201.0d
7205	VC-EL-C11-3600	Install Temp Sump Pit Cover - Service (#14 & #15) Elevator Cabs/Shaft - INTR ...	2.0d	26-Jan-27	27-Jan-27	207.0d
7206	VC-EL-C11-3480	Install Elev. Pit LTNG/Outlets - Service (#14 & #15) Elevator Cabs/Shaft - INTR ...	5.0d	5-Feb-27	11-Feb-27	201.0d
7207	VC-EL-C11-3490	Install Temp Power for Elevator Release - Service (#14 & #15) Elevator Cabs/S...	5.0d	5-Feb-27	11-Feb-27	206.0d
7208	VC-EL-C11-3590	Remove Scaffold in Hoistway - Service (#14 & #15) Elevator Cabs/Shaft - INTR...	5.0d	12-Feb-27	18-Feb-27	201.0d
7209	VC-EL-C11-3500	Install Elev. Rails - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	19-Feb-27	25-Feb-27	201.0d
7210	VC-EL-C11-3700	Set Elev. Equip. in Shaft - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	2.0d	26-Feb-27	1-Mar-27	201.0d
7211	VC-EL-C11-3720	Install Hoistway Elec. Cabling - Service (#14 & #15) Elevator Cabs/Shaft - INTR...	5.0d	2-Mar-27	8-Mar-27	201.0d
7212	VC-EL-C11-3710	Install Platform & Weights - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C...	5.0d	2-Mar-27	8-Mar-27	201.0d
7213	VC-EL-C11-3730	install Elev. Equip in Pit - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	9-Mar-27	15-Mar-27	201.0d
7214	VC-EL-C11-3740	Install Elev. Doors - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	3.0d	11-Mar-27	15-Mar-27	201.0d
7215	VC-EL-C11-3750	Install Elev. Cab - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	16-Mar-27	22-Mar-27	201.0d
7216	VC-EL-C11-3760	Connect Elev. Elec. Equip - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	23-Mar-27	29-Mar-27	252.0d
7217	VC-EL-C11-3790	Field Measure & Fab. Decorative Glass Panels (GL04) - Service (#14 & #15) Ele...	70.0d	23-Mar-27	29-Jun-27	201.0d
7218	VC-EL-C11-3610	Grout Elevator Door Frames - Service (#14 & #15) Elevator Cabs/Shaft - INTR -...	5.0d	30-Mar-27	5-Apr-27	252.0d
7219	VC-EL-C11-3660	Install Terrazzo Flooring at (TR02)- Service (#14 & #15) Elevator Cabs/Shaft - I...	2.0d	30-Mar-27	31-Mar-27	255.0d
7220	VC-EL-C11-3690	Grout Elevator Sills - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	6-Apr-27	12-Apr-27	252.0d
7221	VC-EL-C11-3780	Set Elev. Fronts & Call Boxes - Service (#14 & #15) Elevator Cabs/Shaft - INTR ...	5.0d	13-Apr-27	19-Apr-27	252.0d
7222	VC-EL-C11-3620	Remove Elevator Safety Rail/Net - Service (#14 & #15) Elevator Cabs/Shaft - I...	2.0d	20-Apr-27	21-Apr-27	252.0d
7223	VC-EL-C11-3510	Elec. Run Time for Final Connections - Service (#6 & #7) Elevator Cabs/Shaft - ...	5.0d	22-Apr-27	28-Apr-27	252.0d
7224	VC-EL-C11-3680	Install Cameras - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	29-Apr-27	5-May-27	252.0d

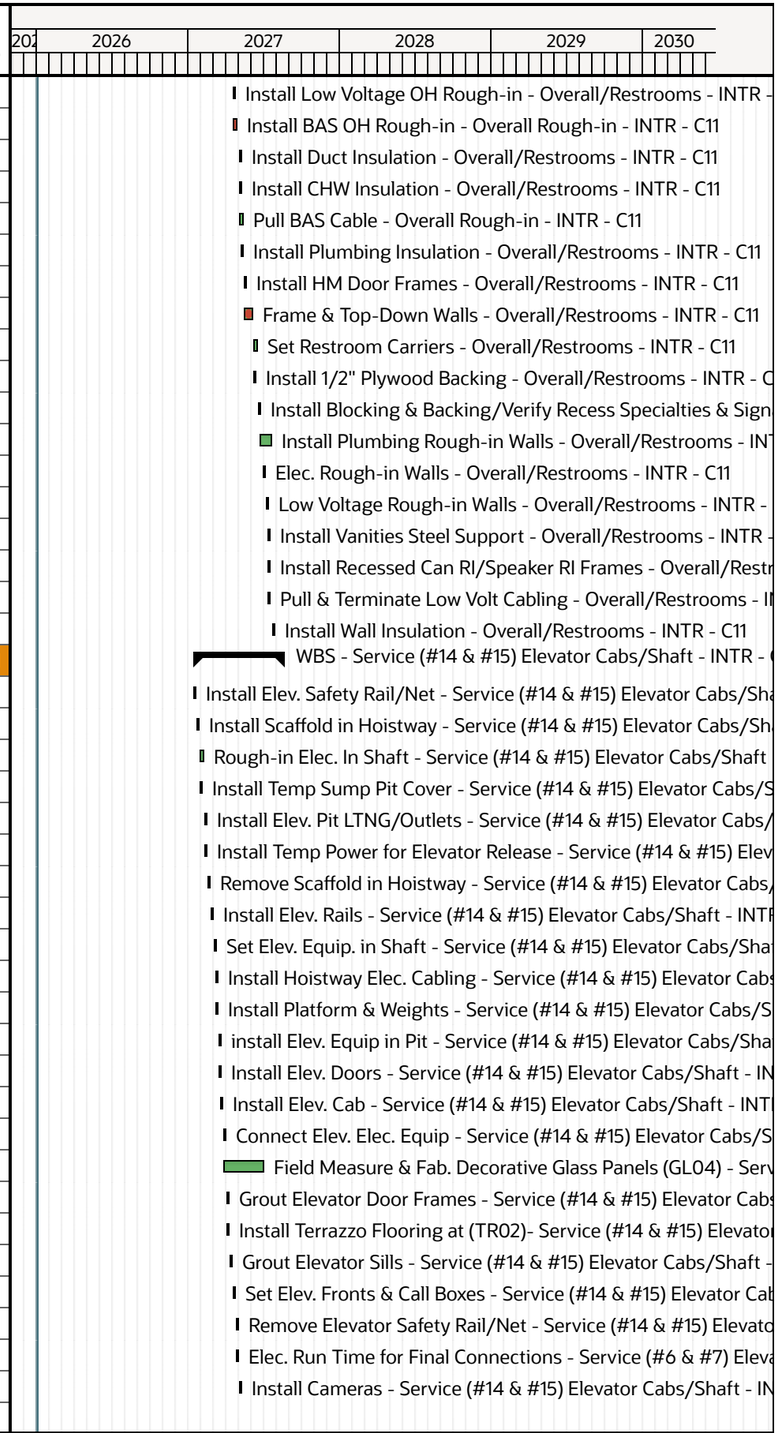


	ID	Name	Dur	Start	Finish	TF
7225	VC-EL-C11-3800	Install Decorative Glass Glazing (GL04) - Service (#14 & #15) Elevator Cabs/Sh...	5.0d	30-Jun-27	7-Jul-27	201.0d
7226	VC-EL-C11-3810	Install Metal Base - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	2.0d	8-Jul-27	9-Jul-27	202.0d
7227	VC-EL-C11-3820	Install Architectural Woodwork (WA01) - Service (#14 & #15) Elevator Cabs/Sh...	3.0d	8-Jul-27	12-Jul-27	201.0d
7228	VC-EL-C11-3520	Install Fire Alarm Trim - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	3.0d	13-Jul-27	15-Jul-27	201.0d
7229	VC-EL-C11-3630	Install Sump Pump & Final Grate Cover - Service (#14 & #15) Elevator Cabs/Sh...	2.0d	16-Jul-27	19-Jul-27	201.0d
7230	VC-EL-C11-3640	Install Pit Ladder - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	2.0d	16-Jul-27	19-Jul-27	201.0d
7231	VC-EL-C11-3530	Adjust/Test Elev. - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	10.0d	20-Jul-27	2-Aug-27	201.0d
7232	VC-EL-C11-3650	Liftnet/Phone Service Configuration - Service (#14 & #15) Elevator Cabs/Shaf...	5.0d	3-Aug-27	9-Aug-27	201.0d
7233	VC-EL-C11-3770	Prepare Elev. Punchlist - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	5.0d	10-Aug-27	16-Aug-27	201.0d
7234	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Mezzanine/Club Level		380.0d	15-Dec-26	12-Jun-28	95.0d
7235	WBS - Infrastructure, MEPTFP Rough-in & Equipment - Club 1		380.0d	15-Dec-26	12-Jun-28	95.0d
7236	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Club 1		162.0d	15-Dec-26	3-Aug-27	88.0d
7237	RI-MC1-5840	Layout Walls/Top Track - Overall Rough-in - INTR - Club 1	10.0d	15-Dec-26	29-Dec-26	37.0d
7238	RI-MC1-6040	Install HM Door Frames - Overall Rough-in - INTR - Club 1	3.0d	15-Dec-26	17-Dec-26	242.0d
7239	RI-MC1-5850	Frame & Top-Down Walls - Overall Rough-in - INTR - Club 1	15.0d	30-Dec-26	20-Jan-27	88.0d
7240	RI-MC1-5890	Install Duct Hangers - Overall Rough-in - INTR - Club 1	4.0d	30-Dec-26	5-Jan-27	99.0d
7241	RI-MC1-5900	Install CHW Hangers - Overall Rough-in - INTR - Club 1	2.0d	6-Jan-27	7-Jan-27	99.0d
7242	RI-MC1-5880	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Club 1	2.0d	21-Jan-27	22-Jan-27	88.0d
7243	RI-MC1-5910	Install Plumbing Hangers - Overall Rough-in - INTR - Club 1	3.0d	25-Jan-27	27-Jan-27	88.0d
7244	RI-MC1-5920	Install Elec. Hangers - Overall Rough-in - INTR - Club 1	2.0d	28-Jan-27	29-Jan-27	88.0d
7245	RI-MC1-5930	Install Fireproofing - Overall Rough-in - INTR - Club 1	3.0d	1-Feb-27	3-Feb-27	88.0d
7246	RI-MC1-5960	Install Duct OH Rough-in - Overall Rough-in - INTR - Club 1	20.0d	4-Feb-27	3-Mar-27	88.0d
7247	RI-MC1-6000	Install Duct Insulation - Overall Rough-in - INTR - Club 1	20.0d	11-Feb-27	10-Mar-27	143.0d
7248	RI-MC1-5940	Install Plumbing OH Rough-in - Overall Rough-in - INTR - Club 1	10.0d	4-Mar-27	17-Mar-27	88.0d
7249	RI-MC1-5950	Install CHW OH Rough-in Mains - Overall Rough-in - INTR - Club 1	20.0d	4-Mar-27	31-Mar-27	88.0d
7250	RI-MC1-5970	Install Elec. OH Rough-in - Overall Rough-in - INTR - Club 1	15.0d	18-Mar-27	7-Apr-27	102.0d
7251	RI-MC1-5954	Install CHW OH Rough-in AHU Connections - Overall Rough-in - INTR - Club 1	20.0d	1-Apr-27	28-Apr-27	88.0d
7252	RI-MC1-6100	Install BAS OH Rough-in - Overall Rough-in - INTR - Club 1	10.0d	8-Apr-27	21-Apr-27	102.0d
7253	RI-MC1-6110	Pull BAS Cable - Overall Rough-in - INTR - Club 1	10.0d	22-Apr-27	5-May-27	102.0d
7254	RI-MC1-6010	Install CHW Insulation - Overall Rough-in - INTR - Club 1	20.0d	29-Apr-27	26-May-27	88.0d
7255	RI-MC1-5980	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Club 1	6.0d	27-May-27	4-Jun-27	88.0d
7256	RI-MC1-5990	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Club 1	10.0d	7-Jun-27	18-Jun-27	88.0d
7257	RI-MC1-6020	Install Plumbing Insulation - Overall Rough-in - INTR - Club 1	5.0d	21-Jun-27	25-Jun-27	88.0d
7258	RI-MC1-6060	Elec. Rough-in Walls - Overall Rough-in - INTR - Club 1	10.0d	28-Jun-27	12-Jul-27	88.0d
7259	RI-MC1-6070	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Club 1	6.0d	13-Jul-27	20-Jul-27	88.0d
7260	RI-MC1-6090	Pull & Terminate Low Volt Cabling - Overall Rough-in - INTR - Club 1	5.0d	21-Jul-27	27-Jul-27	88.0d
7261	RI-MC1-6080	Patch Fireproofing - Overall Rough-in - INTR - Club 1	5.0d	28-Jul-27	3-Aug-27	88.0d
7262	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - IDF - INTR - Club 1		370.0d	30-Dec-26	12-Jun-28	95.0d
7263	WBS - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1		370.0d	30-Dec-26	12-Jun-28	95.0d
7264	RI-MC1-IDF-7170	Layout Walls/Top Track - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	30-Dec-26	6-Jan-27	37.0d
7265	RI-MC1-IDF-7420	Install Fire Sprinkler Hangers -HCAA IDF 6677 - INTRF - Alias ASD 03180 - Clu...	5.0d	7-Jan-27	13-Jan-27	131.0d
7266	RI-MC1-IDF-7430	Install Elec. Hangers - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	14-Jan-27	20-Jan-27	131.0d

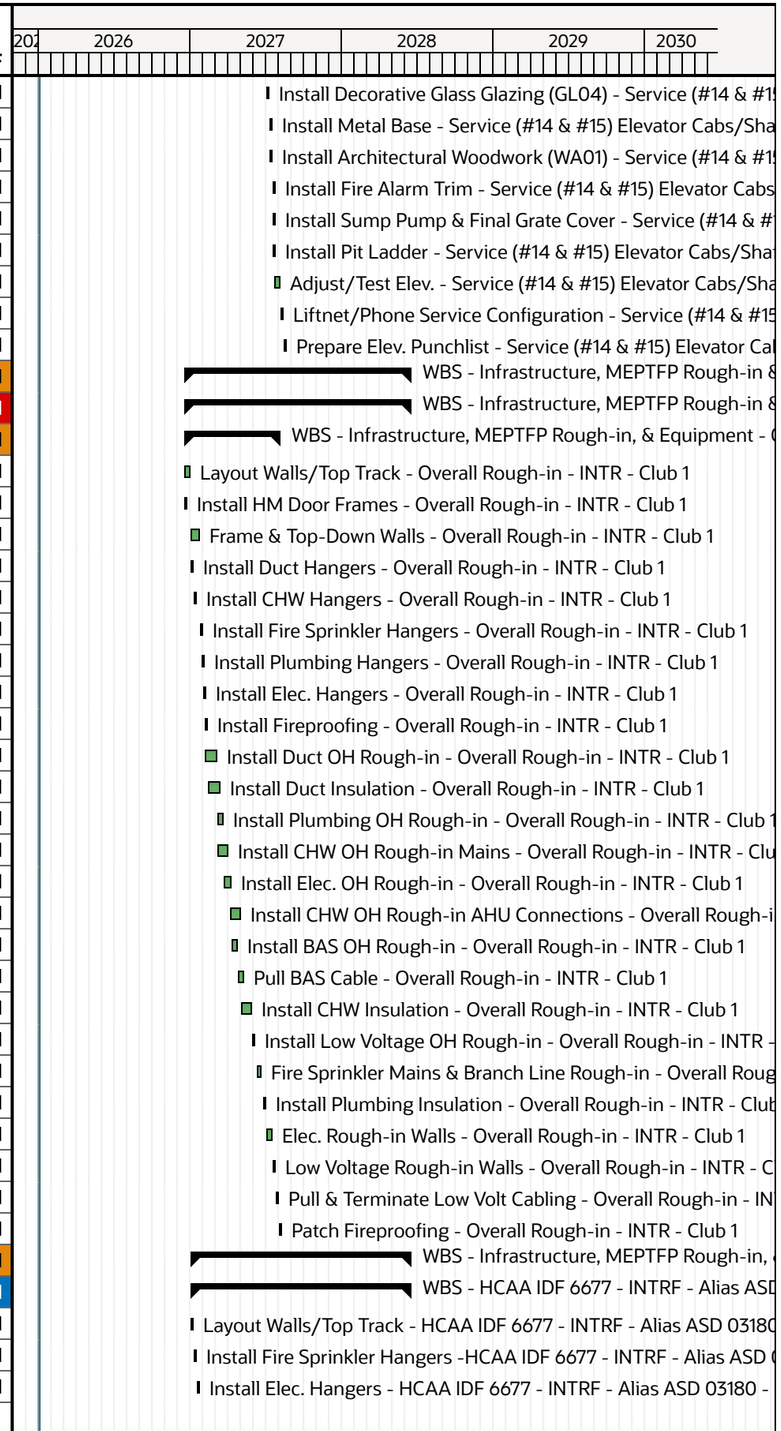


	ID	Name	Dur	Start	Finish	TF
7267	RI-MC1-IDF-7220	Install Fireproofing - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	21-Jan-27	22-Jan-27	131.0d
7268	RI-MC1-IDF-7180	Fire Sprinkler Mains & Branch Line Rough-in - HCAA IDF 6677 - INTRF - Alias ...	2.0d	25-Jan-27	26-Jan-27	131.0d
7269	RI-MC1-IDF-7200	Install Elec. OH Rough- in - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	10.0d	27-Jan-27	9-Feb-27	131.0d
7270	RI-MC1-IDF-7210	Install Low Voltage OH Rough-in-HCAA IDF 6677 - INTRF - Alias ASD 03180 - ...	10.0d	10-Feb-27	23-Feb-27	131.0d
7271	RI-MC1-IDF-7360	Frame & Top-Down Walls - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	24-Feb-27	25-Feb-27	131.0d
7272	RI-MC1-IDF-7370	Install HM Door Frames - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	24-Feb-27	25-Feb-27	399.0d
7273	RI-MC1-IDF-7350	Elec. Rough-in Walls - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	26-Feb-27	4-Mar-27	131.0d
7274	RI-MC1-IDF-7440	Low Voltage Rough-in Walls - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	5-Mar-27	11-Mar-27	131.0d
7275	RI-MC1-IDF-7450	Low Voltage/Elec. in Wall Inspection (COT) - HCAA IDF 6677 - INTRF - Alias AS...	5.0d	12-Mar-27	18-Mar-27	131.0d
7276	RI-MC1-IDF-7460	Patch Fireproofing - Low Voltage/Elec. in Wall Inspection (COT)	5.0d	19-Mar-27	25-Mar-27	131.0d
7277	RI-MC1-IDF-7250	Hang, Tape & Finish Drywall - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	16-Sep-27	22-Sep-27	10.0d
7278	RI-MC1-IDF-7260	Prime & First Coat - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	3.0d	23-Sep-27	27-Sep-27	216.0d
7279	FN-MC1-IDF-7370	Firestopping - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	28-Sep-27	29-Sep-27	216.0d
7280	FN-MC1-IDF-7390	Install FCUs-3-6677 - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	28-Sep-27	4-Oct-27	229.0d
7281	RI-MC1-IDF-7410	Install Door & Hardware - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	28-Sep-27	4-Oct-27	250.0d
7282	FN-MC1-IDF-7380	Install Tech Room Backerboard - HCAA IDF 6677 - INTRF - Alias ASD 03180 - C...	2.0d	30-Sep-27	1-Oct-27	216.0d
7283	FN-MC1-IDF-7580	Set Racks - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	4-Oct-27	8-Oct-27	216.0d
7284	FN-MC1-IDF-7590	Install Ladder Rack - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	3.0d	11-Oct-27	13-Oct-27	216.0d
7285	FN-MC1-IDF-7400	Pull & Terminate Fiber - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	10.0d	14-Oct-27	27-Oct-27	216.0d
7286	FN-MC1-IDF-7410	Trim-Out Low Voltage - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	28-Oct-27	3-Nov-27	216.0d
7287	FN-MC1-IDF-7430	Low Voltage Testing - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	4-Nov-27	10-Nov-27	216.0d
7288	FN-MC1-IDF-7420	Install Flooring - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	11-Nov-27	12-Nov-27	216.0d
7289	FN-MC1-IDF-7660	Install Rubber Base - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	5.0d	15-Nov-27	19-Nov-27	216.0d
7290	FN-MC1-IDF-7425	Apply Final Paint - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	3.0d	22-Nov-27	24-Nov-27	216.0d
7291	FN-MC1-IDF-7640	FCU Start Up - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	2.0d	16-May-28	17-May-28	95.0d
7292	FN-MC1-IDF-7440	Owner's Acceptance Walkthrough - HCAA IDF 6677 - INTRF - Alias ASD 03180 ...	2.0d	18-May-28	19-May-28	95.0d
7293	FN-MC1-IDF-7450	Owner Equipment Install - HCAA IDF 6677 - INTRF - Alias ASD 03180 - Club 1	15.0d	22-May-28	12-Jun-28	95.0d
7294	WBS - Tenant IDF 6678 - INTR - Alias ASD 03181 - Club 1		367.0d	5-Jan-27	12-Jun-28	95.0d
7295	RI-MC1-IDF-1000	Layout Walls/Top Track - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	5-Jan-27	11-Jan-27	37.0d
7296	RI-MC1-IDF-7470	Install Fire Sprinkler Hangers - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Cl...	5.0d	12-Jan-27	18-Jan-27	138.0d
7297	RI-MC1-IDF-7480	Install Elec. Hangers - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	19-Jan-27	25-Jan-27	138.0d
7298	RI-MC1-IDF-1050	Install Fireproofing - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	26-Jan-27	27-Jan-27	138.0d
7299	RI-MC1-IDF-1040	Fire Sprinkler Mains & Branch Rough-in - Tenant IDF 6678 - INTRF - Alias ASD ...	2.0d	28-Jan-27	29-Jan-27	138.0d
7300	RI-MC1-IDF-7390	Install Elec. OH Rough- in - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	10.0d	1-Feb-27	12-Feb-27	138.0d
7301	RI-MC1-IDF-7400	Install Low Voltage OH Rough-in- Tenant IDF 6678 - INTRF - Alias ASD 03181 -...	10.0d	15-Feb-27	26-Feb-27	138.0d
7302	RI-MC1-IDF-1010	Frame & Top-Down Walls - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	1-Mar-27	2-Mar-27	138.0d
7303	RI-MC1-IDF-1030	Install HM Door Frames - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	1-Mar-27	2-Mar-27	389.0d
7304	RI-MC1-IDF-1020	Elec. Rough-in Walls - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	3-Mar-27	9-Mar-27	138.0d
7305	RI-MC1-IDF-7490	Low Voltage Rough-in Walls - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Clu...	5.0d	10-Mar-27	16-Mar-27	138.0d
7306	RI-MC1-IDF-7500	Low Voltage/Elec. in Wall Inspection (COT) - Tenant IDF 6678 - INTRF - Alias A...	5.0d	17-Mar-27	23-Mar-27	138.0d
7307	RI-MC1-IDF-7510	Patch Fireproofing - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	24-Mar-27	30-Mar-27	138.0d
7308	RI-MC1-IDF-1060	Hang, Tape & Finish Drywall - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Clu...	5.0d	7-Oct-27	13-Oct-27	5.0d

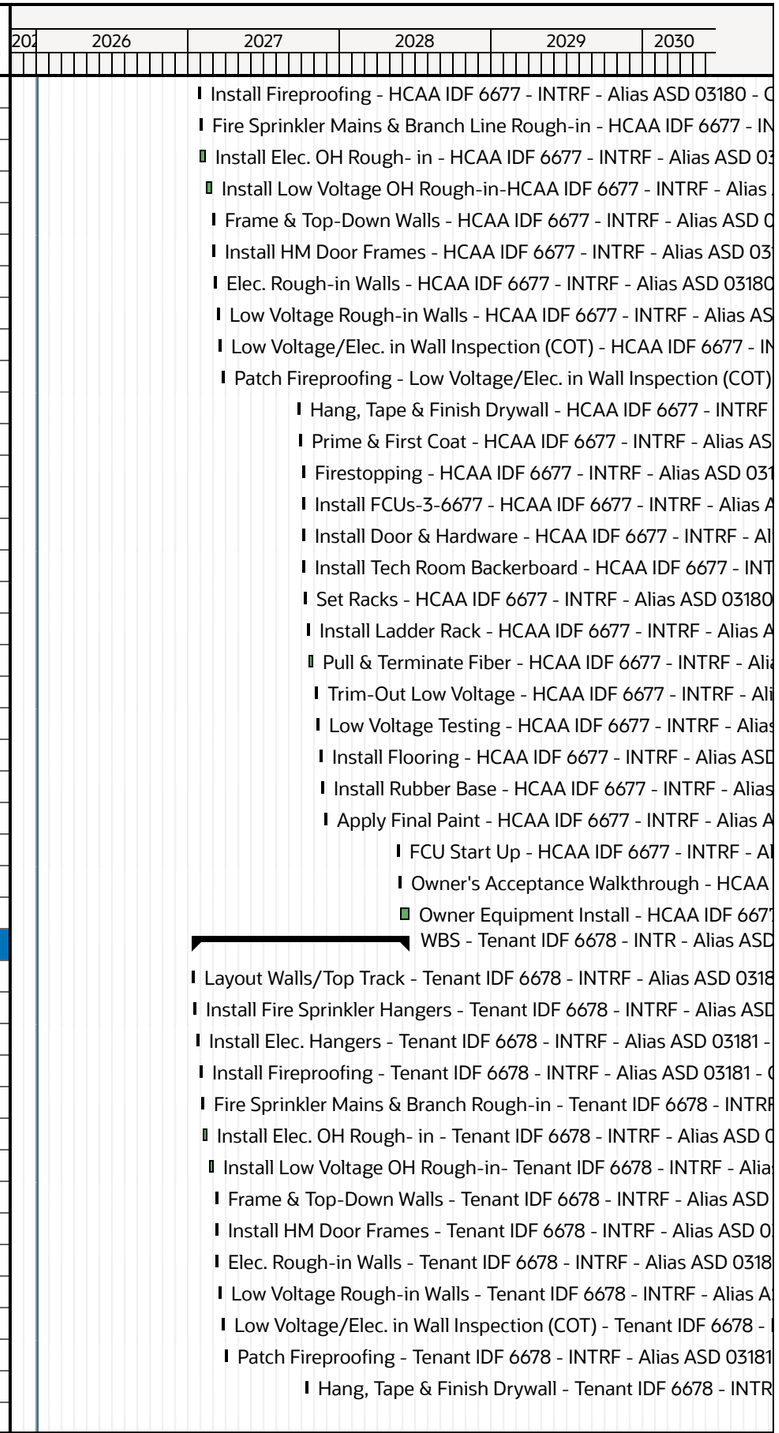

	ID	Name	Dur	Start	Finish	TF
7309	RI-MC1-IDF-1080	Prime & First Coat - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	3.0d	14-Oct-27	18-Oct-27	199.0d
7310	RI-MC1-IDF-7520	Install Door & Hardware - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	19-Oct-27	25-Oct-27	228.0d
7311	RI-MC1-IDF-1090	Firestopping - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	21-Oct-27	22-Oct-27	199.0d
7312	FN-MC1-IDF-7500	Install Tech Room Backerboard - Tenant IDF 6678 - INTRF - Alias ASD 03181 - ...	2.0d	25-Oct-27	26-Oct-27	199.0d
7313	FN-MC1-IDF-7610	Install FCUs-3-6678 - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	27-Oct-27	2-Nov-27	208.0d
7314	FN-MC1-IDF-7620	Set Racks - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	29-Dec-27	5-Jan-28	157.0d
7315	FN-MC1-IDF-7510	Install Ladder Rack - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	3.0d	6-Jan-28	10-Jan-28	157.0d
7316	FN-MC1-IDF-7520	Pull & Terminate Fiber - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	10.0d	11-Jan-28	24-Jan-28	157.0d
7317	FN-MC1-IDF-7530	Trim-Out Low Voltage - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	25-Jan-28	31-Jan-28	157.0d
7318	FN-MC1-IDF-7550	Low Voltage Testing - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	1-Feb-28	7-Feb-28	157.0d
7319	FN-MC1-IDF-7540	Install Flooring - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	8-Feb-28	9-Feb-28	157.0d
7320	FN-MC1-IDF-7670	Install Rubber Base - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	5.0d	10-Feb-28	16-Feb-28	157.0d
7321	FN-MC1-IDF-7545	Apply Final Paint - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	3.0d	17-Feb-28	21-Feb-28	157.0d
7322	FN-MC1-IDF-7650	FCU Start Up - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	2.0d	16-May-28	17-May-28	95.0d
7323	FN-MC1-IDF-7560	Owner's Acceptance Walkthrough - Tenant IDF 6678 - INTRF - Alias ASD 0318...	2.0d	18-May-28	19-May-28	95.0d
7324	FN-MC1-IDF-7570	Owner Equip. Install - Tenant IDF 6678 - INTRF - Alias ASD 03181 - Club 1	15.0d	22-May-28	12-Jun-28	95.0d
7325	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Elect. Room 6676- INTRF - Club 1		33.0d	12-Jan-27	25-Feb-27	302.0d
7326	RI-MC1-ER-3310	Layout Walls/Top Track - Elec. Room 6676 - INTRF - Club 1	5.0d	12-Jan-27	18-Jan-27	37.0d
7327	RI-MC1-ER-3320	Elec. Layout for Conduit Windows (Pre Framing) - Elec. Room 6676 - INTRF - Cl...	2.0d	19-Jan-27	20-Jan-27	37.0d
7328	RI-MC1-ER-3380	Frame & Top-Down Walls - Elec. Room 6676 - INTRF - Club 1	2.0d	21-Jan-27	22-Jan-27	37.0d
7329	RI-MC1-ER-3410	Install HM Door Frames - Elec. Room 6676 - INTRF - Club 1	2.0d	21-Jan-27	22-Jan-27	37.0d
7330	RI-MC1-ER-3390	Elec. Layout- Housekeeping Pads (Post Framing) - Elec. Room 6676 - INTRF - C...	2.0d	25-Jan-27	26-Jan-27	305.0d
7331	RI-MC1-ER-3420	Elec. Rough-in Walls - Elec. Room 6676 - INTRF - Club 1	5.0d	25-Jan-27	29-Jan-27	165.0d
7332	RI-MC1-ER-3400	FRP Equip. Pads - Elec. Room 6676 - INTRF - Club 1	5.0d	1-Feb-27	5-Feb-27	302.0d
7333	RI-MC1-ER-3430	Low Voltage Rough-in Walls - Elec. Room 6676 - INTRF - Club 1	5.0d	1-Feb-27	5-Feb-27	165.0d
7334	RI-MC1-ER-3340	Install Elec. Hangers - Elec. Room 6676 - INTRF - Club 1	5.0d	8-Feb-27	12-Feb-27	302.0d
7335	RI-MC1-ER-3330	Install Fire Sprinkler Hangers - Elec. Room 6676 - INTRF - Club 1	2.0d	15-Feb-27	16-Feb-27	302.0d
7336	RI-MC1-ER-3350	Install Fireproofing - Elec. Room 6676 - INTRF - Club 1	2.0d	17-Feb-27	18-Feb-27	302.0d
7337	RI-MC1-ER-3360	Fire Sprinkler Mains & Branch Line Rough-in - Elec. Room 6676 - INTRF - Club 1	5.0d	19-Feb-27	25-Feb-27	302.0d
7338	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Mechanical - INTR - Club 1		123.0d	25-Jan-27	16-Jul-27	37.0d
7339	RI-MC1-MR-170	Layout Walls/Top Track - Mech. Room - INTR - Club 1	5.0d	25-Jan-27	29-Jan-27	37.0d
7340	RI-MC1-MR-180	FRP Equip. Pads - Mech. Room - INTR - Club 1	5.0d	1-Feb-27	5-Feb-27	37.0d
7341	RI-MC1-MR-190	Install Fire Sprinkler Hangers - Mech. Room - INTR - Club 1	2.0d	1-Feb-27	2-Feb-27	38.0d
7342	RI-MC1-MR-200	Install Duct/CHW Hangers - Mech. Room - INTR - Club 1	2.0d	3-Feb-27	4-Feb-27	38.0d
7343	RI-MC1-MR-210	Install Plumbing Hangers - Mech. Room - INTR - Club 1	5.0d	5-Feb-27	11-Feb-27	38.0d
7344	RI-MC1-MR-380	Set AHU's - Mech. Room - INTR - Club 1	10.0d	8-Feb-27	19-Feb-27	37.0d
7345	RI-MC1-MR-220	Install Elec. Hangers - Mech. Room - INTR - Club 1	2.0d	12-Feb-27	15-Feb-27	38.0d
7346	RI-MC1-MR-230	Install Fireproofing - Mech. Room - INTR - Club 1	3.0d	16-Feb-27	18-Feb-27	38.0d
7347	RI-MC1-MR-260	Install Duct OH Rough-in - Mech. Room - INTR - Club 1	20.0d	22-Feb-27	19-Mar-27	37.0d
7348	RI-MC1-MR-240	Install Plumbing OH Rough-in - Mech. Room - INTR - Club 1	15.0d	22-Mar-27	9-Apr-27	62.0d
7349	RI-MC1-MR-7410	Install CHW OH Rough-in - Mech. Room - INTR - Club 1	20.0d	22-Mar-27	16-Apr-27	37.0d
7350	RI-MC1-MR-7430	Install Duct Insulation - Mech. Room - INTR - Club 1	5.0d	22-Mar-27	26-Mar-27	97.0d

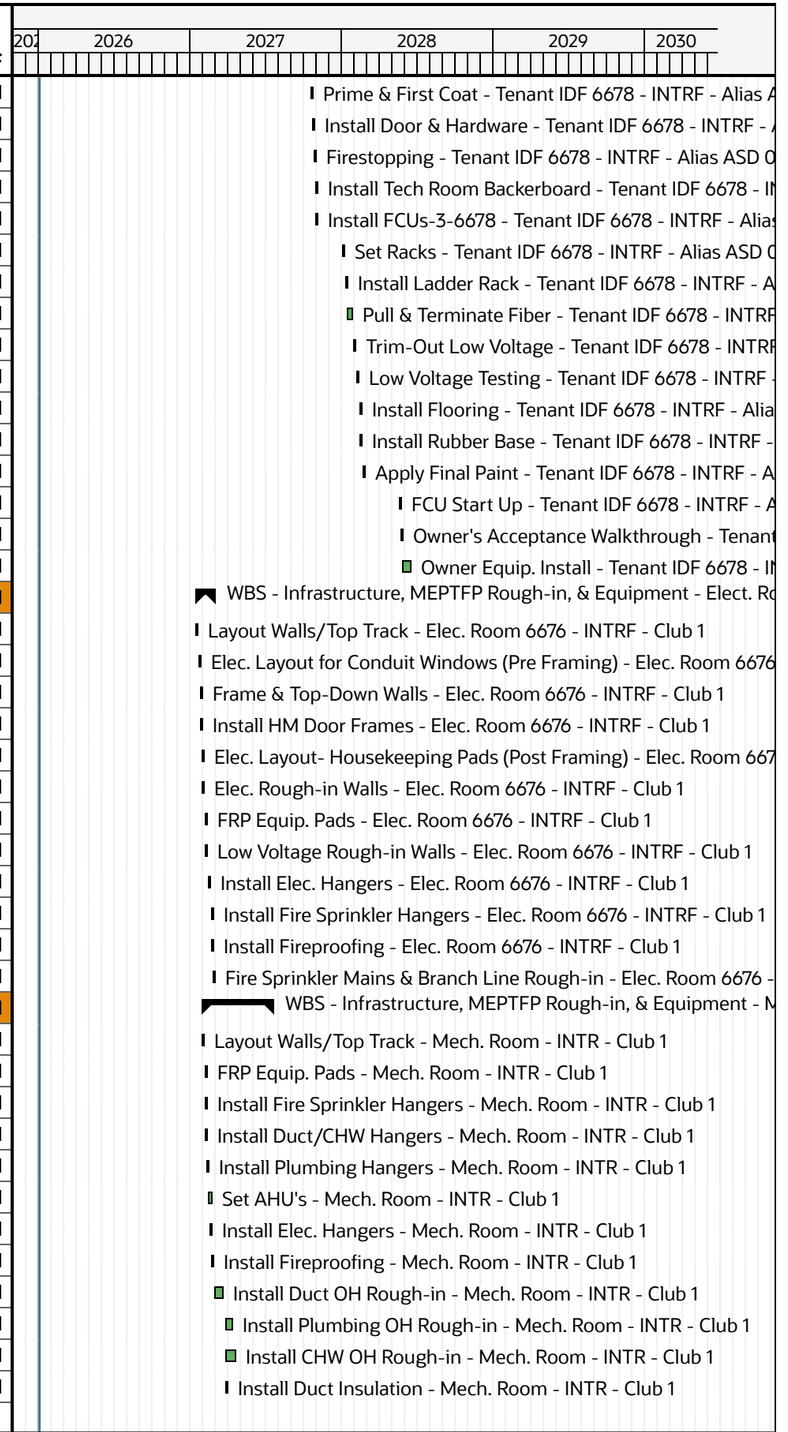

	ID	Name	Dur	Start	Finish	TF
7351	RI-MC1-MR-7420	Install Plumbing Insulation - Mech. Room - INTR - Club 1	15.0d	12-Apr-27	30-Apr-27	72.0d
7352	RI-MC1-MR-270	Fire Sprinkler Mains & Branch Line Rough-in - Mech. Room - INTR - Club 1	10.0d	19-Apr-27	30-Apr-27	37.0d
7353	RI-MC1-MR-7440	Install CHW Insulation - Mech. Room - INTR - Club 1	5.0d	19-Apr-27	23-Apr-27	77.0d
7354	RI-MC1-MR-280	Install Elec. OH Rough-in - Mech. Room - INTR - Club 1	15.0d	3-May-27	21-May-27	37.0d
7355	RI-MC1-MR-290	Low Voltage Rough-in Ceilings - Mech. Room - INTR - Club 1	10.0d	24-May-27	7-Jun-27	37.0d
7356	RI-MC1-MR-250	Install Remaining Mech. Equip. - Mech. Room - INTR - Club 1	10.0d	24-May-27	7-Jun-27	52.0d
7357	RI-MC1-MR-310	Frame & Top-Down Walls - Mech. Room - INTR - Club 1	2.0d	8-Jun-27	9-Jun-27	37.0d
7358	RI-MC1-MR-350	Elec. Rough-in Walls - Mech. Room - INTR - Club 1	5.0d	10-Jun-27	16-Jun-27	37.0d
7359	RI-MC1-MR-320	Install HM Door Frames - Mech. Room - INTR - Club 1	2.0d	15-Jun-27	16-Jun-27	53.0d
7360	RI-MC1-MR-330	Low Voltage Rough-in Walls - Mech. Room - INTR - Club 1	3.0d	17-Jun-27	21-Jun-27	37.0d
7361	RI-MC1-MR-360	Elec. Rough-in at Hard Lids - Mech. Room - INTR - Club 1	5.0d	22-Jun-27	28-Jun-27	37.0d
7362	RI-MC1-MR-340	Low Voltage Rough-in at Hard Lids - Mech. Room - INTR - Club 1	3.0d	29-Jun-27	1-Jul-27	42.0d
7363	RI-MC1-MR-258	Pull & Terminate to Mech. Equip. - Mech. Room - INTR - Club 1	8.0d	29-Jun-27	9-Jul-27	37.0d
7364	RI-MC1-MR-370	Patch Fireproofing - Mech. Room - INTR - Club 1	5.0d	12-Jul-27	16-Jul-27	37.0d
7365	WBS - Infrastructure, MEPT Rough-in & Equipment - Club 2		99.0d	29-Mar-27	16-Aug-27	265.0d
7366	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Club 2		99.0d	29-Mar-27	16-Aug-27	265.0d
7367	RI-CL-MC2-10	Layout Walls/Top Track - Overall Rough-in - INTR - Club 2	10.0d	29-Mar-27	9-Apr-27	99.0d
7368	RI-CL-MC2-20	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Club 2	2.0d	12-Apr-27	13-Apr-27	99.0d
7369	RI-CL-MC2-50	Install Elec. Hangers - Overall Rough-in - INTR - Club 2	2.0d	14-Apr-27	15-Apr-27	99.0d
7370	RI-CL-MC2-60	Install Fireproofing - Overall Rough-in - INTR - Club 2	10.0d	26-Apr-27	7-May-27	93.0d
7371	RI-CL-MC2-100	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Club 2	10.0d	10-May-27	21-May-27	93.0d
7372	RI-CL-MC2-80	Install Expansion Joint - Overall Rough-in - INTR - Club 2	10.0d	10-May-27	21-May-27	128.0d
7373	RI-CL-MC2-380	Install VAV/Duct Rough-in - Overall Rough-in - INTR - Club 2	5.0d	10-May-27	14-May-27	133.0d
7374	RI-CL-MC2-110	Install Elec. OH Rough-in - Overall Rough-in - INTR - Club 2	20.0d	1-Jun-27	28-Jun-27	93.0d
7375	RI-CL-MC2-120	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Club 2	5.0d	29-Jun-27	6-Jul-27	98.0d
7376	RI-CL-MC2-390	Install BAS OH Rough-in - Overall Rough-in - INTR - Club 2	10.0d	29-Jun-27	13-Jul-27	93.0d
7377	RI-CL-MC2-130	Frame & Top-Down Walls - Overall Rough-in - INTR - Club 2	10.0d	14-Jul-27	27-Jul-27	93.0d
7378	RI-CL-MC2-140	Install HM Door Frames - Overall Rough-in - INTR - Club 2	3.0d	14-Jul-27	16-Jul-27	100.0d
7379	RI-CL-MC2-400	Pull BAS Cable - Overall Rough-in - INTR - Club 2	10.0d	14-Jul-27	27-Jul-27	108.0d
7380	RI-CL-MC2-150	Elec. Rough-in Walls - Overall Rough-in - INTR - Club 2	5.0d	28-Jul-27	3-Aug-27	93.0d
7381	RI-CL-MC2-160	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Club 2	5.0d	4-Aug-27	10-Aug-27	93.0d
7382	RI-CL-MC2-370	Install Plumbing Insulation - Overall Rough-in - INTR - Club 2	4.0d	11-Aug-27	16-Aug-27	265.0d
7383	WBS - Infrastructure, MEPT Rough-in & Equipment - Club 3		166.0d	21-Jan-27	14-Sep-27	246.0d
7384	WBS - Infrastructure, MEPTFP Rough-in, & Equipment - Overall - INTR - Club 3		166.0d	21-Jan-27	14-Sep-27	246.0d
7385	RI-CL-MC3-330	Layout Walls/Top Track - Overall Rough-in - INTR - Club 3	10.0d	21-Jan-27	3-Feb-27	134.0d
7386	RI-CL-MC3-340	Install Fire Sprinkler Hangers - Overall Rough-in - INTR - Club 3	2.0d	4-Feb-27	5-Feb-27	134.0d
7387	RI-CL-MC3-360	Install Plumbing Hangers - Overall Rough-in - INTR - Club 3	2.0d	8-Feb-27	9-Feb-27	134.0d
7388	RI-CL-MC3-370	Install Elec. Hangers - Overall Rough-in - INTR - Club 3	2.0d	10-Feb-27	11-Feb-27	134.0d
7389	RI-CL-MC3-380	Install Fireproofing - Overall Rough-in - INTR - Club 3	10.0d	12-Feb-27	25-Feb-27	134.0d
7390	RI-CL-MC3-390	Install Plumbing OH Rough-in - Overall Rough-in - INTR - Club 3	5.0d	26-Feb-27	4-Mar-27	207.0d
7391	RI-CL-MC3-420	Fire Sprinkler Mains & Branch Line Rough-in - Overall Rough-in - INTR - Club 3	10.0d	12-Mar-27	25-Mar-27	207.0d
7392	RI-CL-MC3-440	Install Elec. OH Rough-in - Overall Rough-in - INTR - Club 3	20.0d	19-Mar-27	15-Apr-27	207.0d

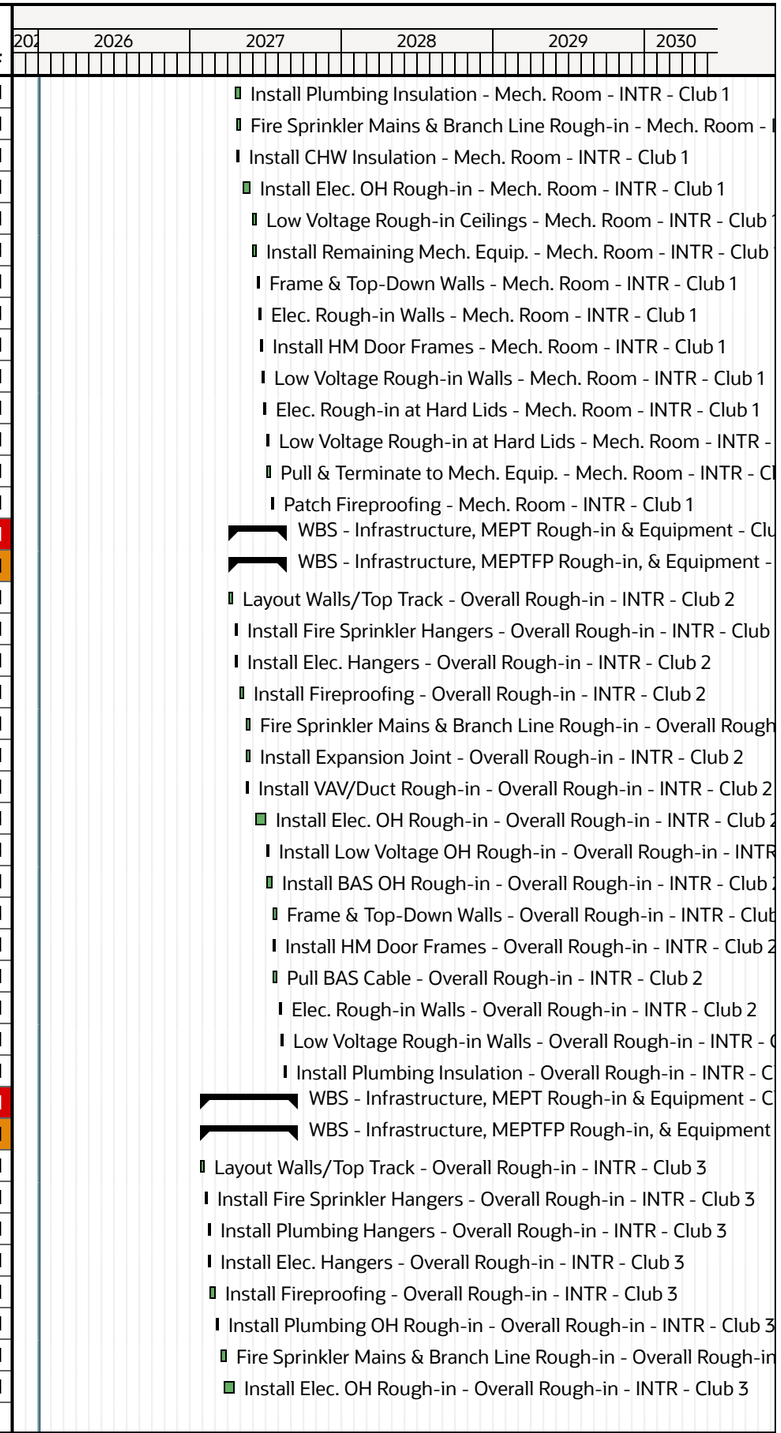


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:01 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski

	ID	Name	Dur	Start	Finish	TF
7393	RI-CL-MC3-430	Install Low Voltage OH Rough-in - Overall Rough-in - INTR - Club 3	3.0d	16-Apr-27	20-Apr-27	214.0d
7394	RI-CL-MC3-530	Install BAS OH Rough-in - Overall Rough-in - INTR - Club 3	10.0d	16-Apr-27	29-Apr-27	207.0d
7395	RI-CL-MC3-450	Frame & Top-Down Walls - Overall Rough-in - INTR - Club 3	10.0d	30-Apr-27	13-May-27	207.0d
7396	RI-CL-MC3-460	Install HM Door Frames - Overall Rough-in - INTR - Club 3	3.0d	30-Apr-27	4-May-27	214.0d
7397	RI-CL-MC3-540	Pull BAS Cable - Overall Rough-in - INTR - Club 3	10.0d	30-Apr-27	13-May-27	225.0d
7398	RI-CL-MC3-470	Elec. Rough-in Walls - Overall Rough-in - INTR - Club 3	10.0d	14-May-27	27-May-27	207.0d
7399	RI-CL-MC3-480	Low Voltage Rough-in Walls - Overall Rough-in - INTR - Club 3	3.0d	28-May-27	2-Jun-27	207.0d
7400	RI-CL-MC3-510	Install Plumbing Insulation - Overall Rough-in - INTR - Club 3	5.0d	11-Aug-27	17-Aug-27	265.0d
7401	RI-CL-MC3-520	Install Interior Curtain Wall Supports - Overall Rough-in - INTR - Club 3	20.0d	17-Aug-27	14-Sep-27	150.0d
7402	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out		572.0d	16-Dec-26	16-Mar-29	0.0d
7403	WBS - Interior Partitions, Finishes & MEPTFP Trim - Apron Level		493.0d	21-Dec-26	28-Nov-28	56.0d
7404	WBS - Apron Level Milestones		112.0d	19-Jun-28	28-Nov-28	16.0d
7405	FN-MLS-AP-290	Apron Level Plumbing Trim Out Complete	0.0d		19-Jun-28	63.0d
7406	FN-MLS-AP-90	Apron Level Mech. Trim Out Complete	0.0d		12-Jul-28	72.0d
7407	FN-MLS-AP-120	Apron Level Fire Alarm Trim Out Complete	0.0d		19-Jul-28	67.0d
7408	FN-MLS-AP-130	Apron Level Fire Protection Trim Out Complete	0.0d		24-Jul-28	64.0d
7409	FN-MLS-AP-310	Apron Level Doors & Hardware Complete	0.0d		18-Aug-28	45.0d
7410	FN-MLS-AP-100	Apron Level Elec. Trim Out Complete	0.0d		1-Sep-28	35.0d
7411	FN-MLS-AP-110	Apron Level Low Voltage Trim Out Complete	0.0d		18-Sep-28	25.0d
7412	FN-MLS-AP-320	Apron Level Internal Punchlist	20.0d	30-Oct-28	28-Nov-28	16.0d
7413	FN-MLS-AP-300	Apron Level Finishes Complete	0.0d		28-Nov-28	16.0d
7414	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 1		232.0d	27-Jan-27	23-Dec-27	212.0d
7415	WBS - Main 6082 & Emergency Electrical Rooms 6081 - INTF - Apron 1		232.0d	27-Jan-27	23-Dec-27	212.0d
7416	FN-AP1-ER-180	Prime & First Coat - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	27-Jan-27	2-Feb-27	207.0d
7417	RI-AP1-ER-7470	Elec. Switchgear Brought into Building & Protected - Main & Emerg. Elec. Room...	5.0d	25-Feb-27	3-Mar-27	166.0d
7418	RI-AP1-ER-1920	Install Elec. Switchgear on Equip. Pad - Main & Emerg. Elec. Rooms - INTR - AP 1	20.0d	4-Mar-27	31-Mar-27	166.0d
7419	FN-AP1-ER-210	Install Elec. Transformers - Main & Emerg. Elec. Rooms - INTF - AP 1	10.0d	1-Apr-27	14-Apr-27	166.0d
7420	RI-AP1-ER-7490	Install Elec. Panelboards - Main & Emerg. Elec. Rooms - INTR - AP 1	10.0d	1-Apr-27	14-Apr-27	206.0d
7421	RI-AP1-ER-1940	Surface Mount Wall Rough - Main & Emerg. Elec. Rooms - INTR - AP 1	15.0d	15-Apr-27	5-May-27	221.0d
7422	FN-AP1-ER-5120	Install Door - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	15-Apr-27	21-Apr-27	246.0d
7423	FN-AP1-ER-5090	Elec. Feeder Wire Measure & Procure - Main & Emerg. Elec. Rooms - INTF - AP 1	20.0d	15-Apr-27	12-May-27	166.0d
7424	FN-AP1-ER-5160	Install Door Hardware - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	22-Apr-27	28-Apr-27	246.0d
7425	FN-AP1-ER-5200	UPS System Install - Main & Emerg. Elec. Rooms - INTR - AP 1	5.0d	3-May-27	7-May-27	169.0d
7426	RI-AP1-ER-7500	Elec. Equip Connections & O/H R/I - Main & Emerg. Elec. Rooms - INTR - AP 1	15.0d	6-May-27	26-May-27	221.0d
7427	RI-AP1-ER-7630	Pull & Terminate Elec. Switchgear - Main & Emerg. Elec. Rooms - INTR - AP 1	20.0d	13-May-27	10-Jun-27	166.0d
7428	RI-AP1-ER-1990	Final Patch Fireproofing - Main & Emerg. Elec. Rooms - INTR - AP 1	3.0d	27-May-27	1-Jun-27	223.0d
7429	FN-AP1-ER-5140	Install Fire Alarm Trim - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	27-May-27	3-Jun-27	353.0d
7430	FN-AP1-ER-5130	Install Low Voltage Trim - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	27-May-27	3-Jun-27	221.0d
7431	FN-AP1-ER-5170	Install Fire Protection Trim - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	2-Jun-27	8-Jun-27	223.0d
7432	FN-AP1-ER-220	Pull & Terminate Elec. Panels & XMRF - Main & Emerg. Elec. Rooms - INTF - AP 1	20.0d	11-Jun-27	9-Jul-27	166.0d
7433	FN-AP1-ER-224	3rd Party Testing/Feeder Wire & Elec. Equip. - Main & Emerg. Elec. Rooms - IN...	20.0d	12-Jul-27	6-Aug-27	166.0d
7434	FN-AP1-ER-230	Install Light Fixtures & Trim - Main & Emerg. Elec. Rooms - INTF - AP 1	10.0d	9-Aug-27	20-Aug-27	166.0d

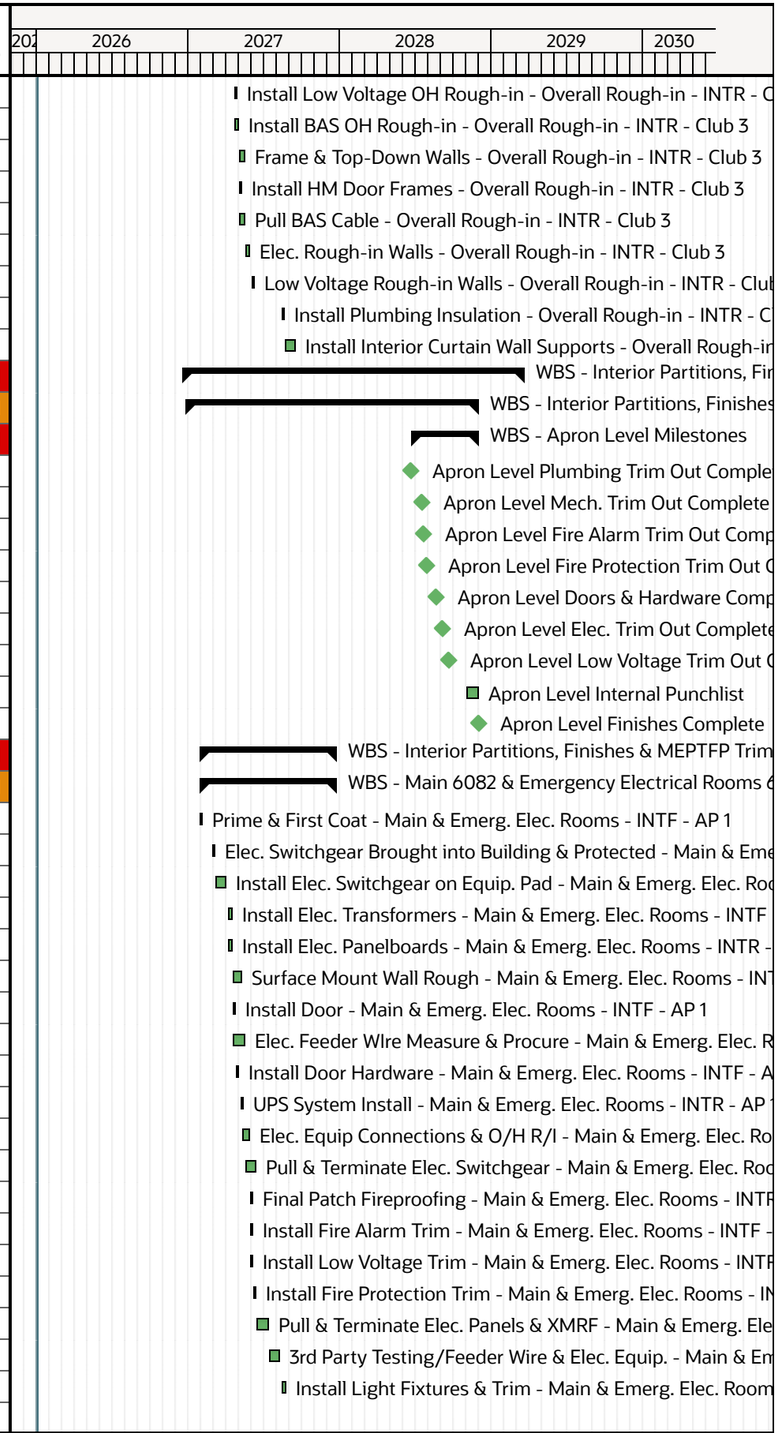


	ID	Name	Dur	Start	Finish	TF
7435	FN-AP1-ER-250	Apply Final Paint - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	23-Aug-27	27-Aug-27	177.0d
7436	FN-AP1-ER-280	Seal Concrete - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	23-Aug-27	27-Aug-27	166.0d
7437	FN-AP1-ER-5099	Energize Panels - Main & Emerg. Elec. Rooms - INTF - AP 1	2.0d	30-Aug-27	31-Aug-27	166.0d
7438	FN-AP1-ER-5100	Elec. Insp for Perm Power for Test - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	1-Sep-27	8-Sep-27	166.0d
7439	FN-AP1-ER-5110	APG QC Procedure for Perm Power Available for Dist. - Main & Emerg. Elec. Roo…	9.0d	9-Sep-27	21-Sep-27	166.0d
7440	FN-AP1-ER-240	Final Checkout & Panel Startup - Main & Emerg. Elec. Rooms - INTF - AP 1	10.0d	22-Sep-27	5-Oct-27	166.0d
7441	FN-AP1-ER-260	Start-up Elec. Equip. - Main & Emerg. Elec. Rooms - INTF - AP 1	15.0d	6-Oct-27	26-Oct-27	166.0d
7442	FN-AP1-ER-5180	Install Rubber Base - Main & Emerg. Elec. Rooms - INTF - AP 1	5.0d	24-Nov-27	2-Dec-27	143.0d
7443	FN-AP1-ER-5190	Install Signage - Main & Emerg. Elec. Rooms - INTF - AP 1	3.0d	3-Dec-27	7-Dec-27	143.0d
7444	FN-AP1-ER-5150	Install HVAC/Make Final Piping Connections CH Trim - Main & Emerg. Elec. Ro…	4.0d	20-Dec-27	23-Dec-27	149.0d
7445	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 2		300.0d	23-Feb-27	26-Apr-28	205.0d
7446	WBS - Fire Alarm Control Panel Room 6084 - INTF - Apron 2		171.0d	25-Aug-27	26-Apr-28	125.0d
7447	FN-AP2-FA-4960	Prime & First Coat - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	25-Aug-27	26-Aug-27	170.0d
7448	FN-AP2-FA-5040	Install Doors & Hardware - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	27-Aug-27	30-Aug-27	193.0d
7449	FN-AP2-FA-5110	Install Diffusers - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	27-Aug-27	2-Sep-27	170.0d
7450	FN-AP2-FA-5120	Install FCU's - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	27-Aug-27	2-Sep-27	238.0d
7451	FN-AP2-FA-4970	Install LTNG/Elec. Trim - Fire Alarm Control Rm 6084 - INTF - AP 2	3.0d	3-Sep-27	8-Sep-27	170.0d
7452	FN-AP2-FA-5090	Install Fire Protection Trim - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	9-Sep-27	15-Sep-27	170.0d
7453	FN-AP2-FA-4990	Mount FA Panels - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	16-Sep-27	22-Sep-27	170.0d
7454	FN-AP2-FA-5010	Pull & Terminate Fiber - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	26-Jan-28	1-Feb-28	85.0d
7455	FN-AP2-FA-5070	Install Fire Alarm Trim - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	2-Feb-28	3-Feb-28	85.0d
7456	FN-AP2-FA-5050	Seal Concrete - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	4-Feb-28	10-Feb-28	85.0d
7457	FN-AP2-FA-5130	Install Rubber Base - Fire Alarm Control Rm 6084 - INTF - AP 2	3.0d	11-Feb-28	15-Feb-28	85.0d
7458	FN-AP2-FA-5030	Apply Final Paint - Fire Alarm Control Rm 6084 - INTF - AP 2	5.0d	16-Feb-28	22-Feb-28	165.0d
7459	FN-AP2-FA-5080	Equip. Install - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	23-Feb-28	24-Feb-28	165.0d
7460	FN-AP2-FA-5140	FCU Start Up - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	21-Apr-28	24-Apr-28	125.0d
7461	FN-AP2-FA-5160	Fire Alarm Panel Startup - Fire Alarm Control Rm 6084 - INTF - AP 2	2.0d	25-Apr-28	26-Apr-28	125.0d
7462	WBS - FP Room 6093 - INTF - Apron 2		125.0d	15-Mar-27	8-Sep-27	301.0d
7463	FN-AP2-FP-470	Install Fire & Jockey Pump FP Room - INTF - AP 2	5.0d	15-Mar-27	19-Mar-27	358.0d
7464	FN-AP2-FP-480	Connect All Piping & Valves - FP Room - INTF - AP 2	5.0d	22-Mar-27	26-Mar-27	358.0d
7465	FN-AP2-FP-500	Install Fire Pump Controllers - FP Room - INTF - AP 2	5.0d	22-Mar-27	26-Mar-27	391.0d
7466	FN-AP2-FP-350	Install Ceiling Light Fixtures & Trim - FP Room - INTF - AP 2	5.0d	7-Apr-27	13-Apr-27	351.0d
7467	FN-AP2-FP-370	Install Fire Alarm Trim - FP Room - INTF - AP 2	3.0d	19-Apr-27	21-Apr-27	345.0d
7468	FN-AP2-FP-330	Install Low Voltage Trim - FP Room - INTF - AP 2	5.0d	19-Apr-27	23-Apr-27	343.0d
7469	FN-AP2-FP-340	Install Doors - FP Room - INTF - AP 2	5.0d	19-Apr-27	23-Apr-27	376.0d
7470	FN-AP2-FP-380	Seal Concrete Floor - FP Room - INTF - AP 2	10.0d	26-Apr-27	7-May-27	343.0d
7471	FN-AP2-FP-360	Install Diffusers - FP Room - INTF - AP 2	4.0d	26-Apr-27	29-Apr-27	360.0d
7472	FN-AP2-FP-390	Install Fire Protection Trim - FP Room - INTF - AP 2	7.0d	7-May-27	17-May-27	360.0d
7473	FN-AP2-FP-430	Install Low Voltage Trim Walls - FP Room - INTF - AP 2	5.0d	10-May-27	14-May-27	366.0d
7474	FN-AP2-FP-400	Plumbing Fixtures & Trim - FP Room - INTF - AP 2	3.0d	10-May-27	12-May-27	343.0d
7475	FN-AP2-FP-490	Install WH-2(hose bib) - FP Room - INTF - AP 2	5.0d	10-May-27	14-May-27	361.0d
7476	FN-AP2-FP-540	Install BAS Trim Walls - FP Room - INTF - AP 2	5.0d	10-May-27	14-May-27	366.0d

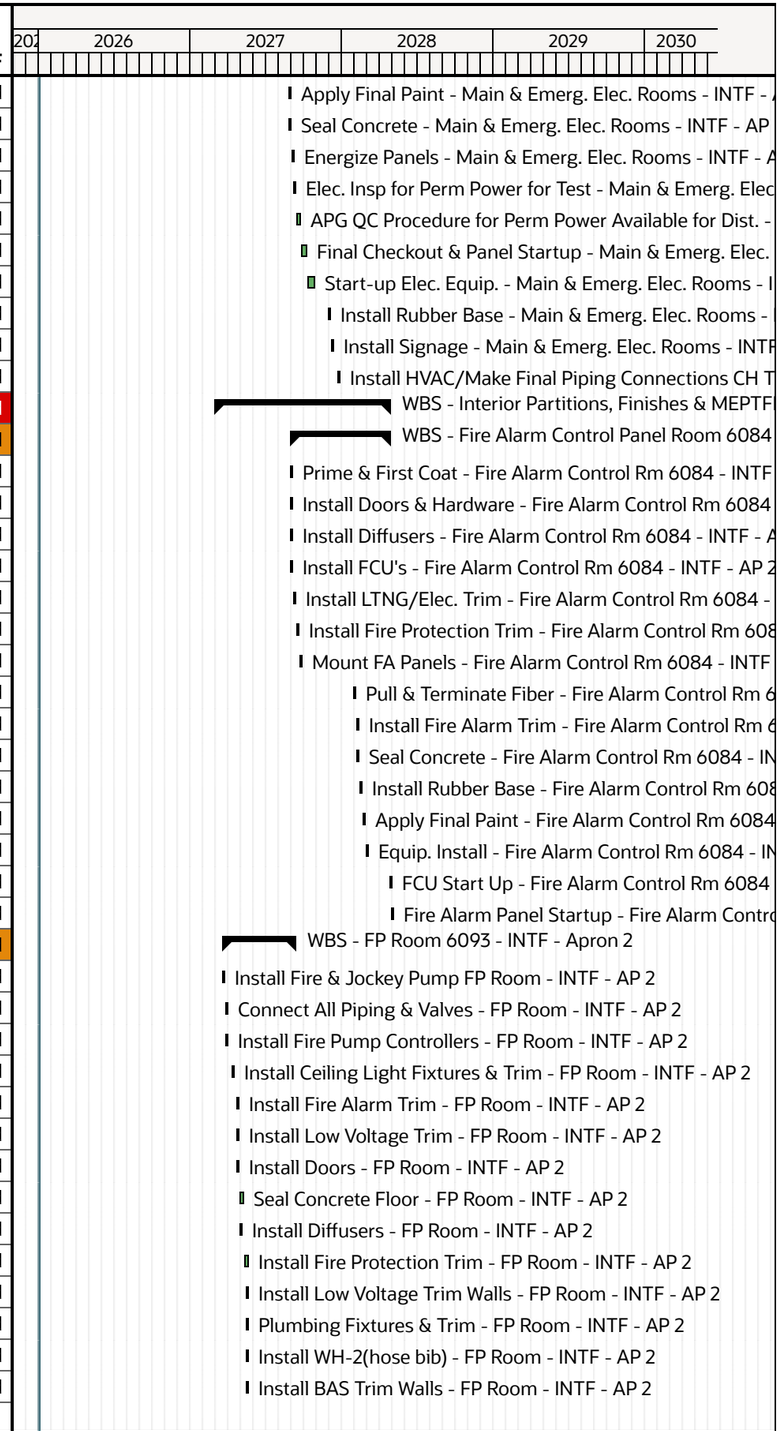


	ID	Name	Dur	Start	Finish	TF
7477	FN-AP2-FP-440	Install Door Hardware - FP Room - INTF - AP 2	5.0d	13-May-27	19-May-27	363.0d
7478	FN-AP2-FP-410	Install Light Fixtures & Trim Walls - FP Room - INTF - AP 2	5.0d	18-May-27	24-May-27	360.0d
7479	FN-AP2-FP-450	Install Signage - FP Room - INTF - AP 2	5.0d	2-Jun-27	8-Jun-27	365.0d
7480	FN-AP2-FP-510	Test Fire Pump - FP Room - INTF - AP 2	5.0d	1-Sep-27	8-Sep-27	286.0d
7481	WBS - Shuttle Maintenance 6087- INTF - Apron 2		48.0d	12-May-27	20-Jul-27	341.0d
7482	FN-AP2-SM-1065	Prime & First Coat Walls - Shuttle Maint. - INTF - AP 2	5.0d	12-May-27	18-May-27	206.0d
7483	FN-AP2-SM-1035	Install Coil Roll Up Door 6087B Shuttle Maint. - INTF - AP 2	5.0d	19-May-27	25-May-27	206.0d
7484	FN-AP2-SM-1085	Install Stair J5(x2) & J2(1) & J7 (1) - Shuttle Maint. - INTF - AP 2	5.0d	26-May-27	2-Jun-27	206.0d
7485	FN-AP2-SM-710	Install Doors & Hardware - Shuttle Maint. - INTF - AP 2	5.0d	3-Jun-27	9-Jun-27	344.0d
7486	FN-AP2-SM-1045	Install Plumbing Fixutres & Eye Wash Station - Shuttle Maint. - INTF - AP 2	5.0d	3-Jun-27	9-Jun-27	206.0d
7487	FN-AP2-SM-770	Install Light Fixtures & Trim Walls - Shuttle Maint. - INTF - AP 2	5.0d	10-Jun-27	16-Jun-27	206.0d
7488	FN-AP2-SM-800	Install Fire Protection Trim - Shuttle Maint. - INTF - AP 2	5.0d	10-Jun-27	16-Jun-27	206.0d
7489	FN-AP2-SM-750	Install Fire Alarm Trim - Shuttle Maint. - INTF - AP 2	3.0d	17-Jun-27	21-Jun-27	339.0d
7490	FN-AP2-SM-780	Install Low Voltage Trim Walls - Shuttle Maint. - INTF - AP 2	5.0d	17-Jun-27	23-Jun-27	339.0d
7491	FN-AP2-SM-1095	Install Clearance Floor Striping - Shuttle Maint. - INTF - AP 2	5.0d	17-Jun-27	23-Jun-27	206.0d
7492	FN-AP2-SM-1115	Install BAS Trim Walls - Shuttle Maint. - INTF - AP 2	5.0d	17-Jun-27	23-Jun-27	339.0d
7493	FN-AP2-SM-1055	Seal Concrete - Shuttle Maint. - INTF - AP 2	5.0d	24-Jun-27	30-Jun-27	206.0d
7494	FN-AP2-SM-1075	Apply Final Paint - Shuttle Maint. - INTF - AP 2	5.0d	2-Jul-27	9-Jul-27	205.0d
7495	FN-AP2-SM-1105	Install FECs - Shuttle Maint. - INTF - AP 2	2.0d	12-Jul-27	13-Jul-27	341.0d
7496	FN-AP2-SM-810	Install Signage at Shuttle Maintenance & BOH - Shuttle Maint. - INTF - AP 2	5.0d	14-Jul-27	20-Jul-27	341.0d
7497	WBS - APM Parts Storage 6089- INTF - Apron 2		267.0d	7-Apr-27	24-Apr-28	207.0d
7498	FN-AP2-SM-830	Hang Drywall Walls - APM Parts Storage - INTF - AP 2	5.0d	7-Apr-27	13-Apr-27	159.0d
7499	FN-AP2-SM-840	Tape & Finish Walls - APM Parts Storage - INTF - AP 2	10.0d	14-Apr-27	27-Apr-27	210.0d
7500	FN-AP2-SM-850	Prime & One Coat Walls - APM Parts Storage - INTF - AP 2	7.0d	28-Apr-27	6-May-27	210.0d
7501	FN-AP2-SM-870	Install Doors - APM Parts Storage - INTF - AP 2	5.0d	7-May-27	13-May-27	362.0d
7502	FN-AP2-SM-1015	Install ACT Ceiling Grid - APM Parts Storage - INTF - AP 2	2.0d	7-May-27	10-May-27	213.0d
7503	FN-AP2-SM-880	Install Flooring & Base - APM Parts Storage - INTF - AP 2	3.0d	11-May-27	13-May-27	218.0d
7504	FN-AP2-SM-890	Install Diffusers - APM Parts Storage - INTF - AP 2	4.0d	14-May-27	19-May-27	210.0d
7505	FN-AP2-SM-970	Install Door Hardware - APM Parts Storage - INTF - AP 2	5.0d	14-May-27	20-May-27	362.0d
7506	FN-AP2-SM-910	Install Fire Protection Trim - APM Parts Storage - INTF - AP 2	10.0d	20-May-27	3-Jun-27	210.0d
7507	FN-AP2-SM-900	Install Fire Alarm Trim - APM Parts Storage - INTF - AP 2	3.0d	20-May-27	24-May-27	212.0d
7508	FN-AP2-SM-860	Install Low Voltage Trim - APM Parts Storage - INTF - AP 2	7.0d	20-May-27	28-May-27	212.0d
7509	FN-AP2-FP-520	Install FCU -1-6089 - APM Parts Storage - INTF - AP 2	5.0d	20-May-27	26-May-27	307.0d
7510	FN-AP2-SM-920	Install Interior Specialties/Mounting Brackets/OFOI - APM Parts Storage - INTF...	5.0d	25-May-27	1-Jun-27	212.0d
7511	FN-AP2-SM-930	Install Light Fixtures & Trim Walls - APM Parts Storage - INTF - AP 2	5.0d	1-Jun-27	7-Jun-27	351.0d
7512	FN-AP2-SM-960	Install Low Voltage Trim Walls - APM Parts Storage - INTF - AP 2	5.0d	2-Jun-27	8-Jun-27	212.0d
7513	FN-AP2-SM-1125	Install BAS Trim Walls - APM Parts Storage - INTF - AP 2	5.0d	2-Jun-27	8-Jun-27	212.0d
7514	FN-AP2-SM-1025	Install ACT Ceiling Tiles - APM Parts Storage - INTF - AP 2	5.0d	4-Jun-27	10-Jun-27	210.0d
7515	FN-AP2-SM-940	Apply Final Paint - APM Parts Storage - INTF - AP 2	5.0d	15-Jun-27	21-Jun-27	208.0d
7516	FN-AP2-SM-950	Install FF&E - APM Parts Storage - INTF - AP 2	10.0d	22-Jun-27	6-Jul-27	346.0d
7517	FN-AP2-SM-980	Install Signage - APM Parts Storage - INTF - AP 2	5.0d	7-Jul-27	13-Jul-27	346.0d
7518	FN-AP2-FP-530	FCU Start Up - APM Parts Storage - INTF - AP 2	2.0d	21-Apr-28	24-Apr-28	207.0d




	ID	Name	Dur	Start	Finish	TF
7519	WBS - Fleet Manager 6086/Maintenance Work Room 6098/Utility Closet 6091 - INTF - Apron 2		267.0d	7-Apr-27	24-Apr-28	207.0d
7520	FN-AP2-SR-990	Install Wall Insulation - Fleet Mgmt. - INTF - AP 2	5.0d	7-Apr-27	13-Apr-27	164.0d
7521	FN-AP2-SR-1000	Hang Drywall Walls - Fleet Mgmt. - INTF - AP 2	5.0d	21-Apr-27	27-Apr-27	159.0d
7522	FN-AP2-SR-1010	Tape & Finish Walls - Fleet Mgmt. - INTF - AP 2	10.0d	28-Apr-27	11-May-27	205.0d
7523	FN-AP2-SR-1020	Prime & One Coat Walls - Fleet Mgmt. - INTF - AP 2	7.0d	12-May-27	20-May-27	205.0d
7524	FN-AP2-SR-1190	Install FCU - 1-6098 - Fleet Mgmt. - INTF - AP 2	5.0d	12-May-27	18-May-27	313.0d
7525	FN-AP2-SR-1170	Install ACT Ceiling Grid - Fleet Mgmt. - INTF - AP 2	2.0d	21-May-27	24-May-27	205.0d
7526	FN-AP2-SR-1100	Install Light Fixtures & Trim Walls - Fleet Mgmt. - INTF - AP 2	5.0d	25-May-27	1-Jun-27	205.0d
7527	FN-AP2-SR-1030	Install Flooring & Base - Fleet Mgmt. - INTF - AP 2	3.0d	25-May-27	27-May-27	211.0d
7528	FN-AP2-SR-1200	Install Fan (EF-09) - Fleet Mgmt. - INTF - AP 2	5.0d	25-May-27	1-Jun-27	217.0d
7529	FN-AP2-SR-1050	Install Doors - Fleet Mgmt. - INTF - AP 2	5.0d	28-May-27	4-Jun-27	214.0d
7530	FN-AP2-SR-1060	Install Diffusers - Fleet Mgmt. - INTF - AP 2	4.0d	2-Jun-27	7-Jun-27	205.0d
7531	FN-AP2-SR-1130	Install Door Hardware - Fleet Mgmt. - INTF - AP 2	5.0d	7-Jun-27	11-Jun-27	214.0d
7532	FN-AP2-SR-1040	Install Low Voltage Trim - Fleet Mgmt. - INTF - AP 2	5.0d	8-Jun-27	14-Jun-27	205.0d
7533	FN-AP2-SR-1160	Install Fire Alarm Trim - Fleet Mgmt. - INTF - AP 2	5.0d	8-Jun-27	14-Jun-27	205.0d
7534	FN-AP2-SR-1080	Install Fire Protection Trim - Fleet Mgmt. - INTF - AP 2	3.0d	15-Jun-27	17-Jun-27	205.0d
7535	FN-AP2-SR-1140	Install Low Voltage Trim Walls - Fleet Mgmt. - INTF - AP 2	5.0d	15-Jun-27	21-Jun-27	341.0d
7536	FN-AP2-SR-1220	Install BAS Trim Walls - Fleet Mgmt. - INTF - AP 2	5.0d	15-Jun-27	21-Jun-27	341.0d
7537	FN-AP2-SR-1090	Install Interior Specialties/Mounting Brackets/OFOI - Fleet Mgmt. - INTF - AP 2	5.0d	18-Jun-27	24-Jun-27	205.0d
7538	FN-AP2-SR-1180	Install ACT Ceiling Tiles - Fleet Mgmt. - INTF - AP 2	5.0d	18-Jun-27	24-Jun-27	205.0d
7539	FN-AP2-SR-1110	Apply Final Paint - Fleet Mgmt. - INTF - AP 2	5.0d	25-Jun-27	1-Jul-27	205.0d
7540	FN-AP2-SR-1120	Install FF&E - Fleet Mgmt. - INTF - AP 2	5.0d	2-Jul-27	9-Jul-27	343.0d
7541	FN-AP2-SR-1150	Install Signage - Fleet Mgmt. - INTF - AP 2	5.0d	12-Jul-27	16-Jul-27	343.0d
7542	FN-AP2-SR-1210	FCU Start Up - 1-6098 - Fleet Mgmt. - INTF - AP 2	2.0d	21-Apr-28	24-Apr-28	207.0d
7543	WBS - Electrical & Electronics RM/DOC Control/Tech Office 6102 - INTF - Apron 2		262.0d	14-Apr-27	24-Apr-28	207.0d
7544	FN-AP2-IT-1340	Hang Drywall Walls - Elec. & Electronics RM/DOC Control/Tech Office - INTF - ...	5.0d	14-Apr-27	20-Apr-27	159.0d
7545	FN-AP2-IT-1350	Prime & First Coat - Elec. & Electronics RM/DOC Control/Tech Office - INTF - A...	5.0d	21-Apr-27	27-Apr-27	204.0d
7546	FN-AP2-IT-1430	Install Door & Hardware - Elec. & Electronics RM/DOC Control/Tech Office - IN...	2.0d	28-Apr-27	29-Apr-27	231.0d
7547	FN-AP2-IT-1500	Install ACT Ceiling Grid - Elec. & Electronics RM/DOC Control/Tech Office - INT...	5.0d	28-Apr-27	4-May-27	204.0d
7548	FN-AP2-IT-1450	Install LTNG/Elec. Trim - Elec. & Electronics RM/DOC Control/Tech Office - INT...	5.0d	5-May-27	11-May-27	208.0d
7549	FN-AP2-IT-1460	Install Low Volt Trim - Elec. & Electronics RM/DOC Control/Tech Office - INTF - ...	5.0d	12-May-27	18-May-27	208.0d
7550	FN-AP2-IT-1470	Install Fire Alarm Trim - Elec. & Electronics RM/DOC Control/Tech Office - INTF...	5.0d	12-May-27	18-May-27	208.0d
7551	FN-AP2-IT-1490	Install FCU - Elec. & Electronics RM/DOC Control/Tech Office - INTF - AP 2	5.0d	12-May-27	18-May-27	313.0d
7552	FN-AP2-IT-1480	Install Fire Protection Trim - Elec. & Electronics RM/DOC Control/Tech Office - I...	5.0d	19-May-27	25-May-27	208.0d
7553	FN-AP2-IT-1510	Install ACT Ceiling Tiles- Elec. & Electronics RM/DOC Control/Tech Office - INT...	5.0d	26-May-27	2-Jun-27	208.0d
7554	FN-AP2-IT-1440	Install Flooring & Base - Elec. & Electronics RM/DOC Control/Tech Office - INTF...	3.0d	3-Jun-27	7-Jun-27	208.0d
7555	FN-AP2-IT-1410	Apply Final Paint - Elec. & Electronics RM/DOC Control/Tech Office - INTF - AP 2	5.0d	8-Jun-27	14-Jun-27	208.0d
7556	FN-AP2-IT-1520	FCU Start Up - Elec. & Electronics RM/DOC Control/Tech Office - INTF - AP 2	2.0d	21-Apr-28	24-Apr-28	207.0d
7557	WBS - Support Restroom 6092/Restrooms 6009 & 6010 - INTF - Apron 2		100.0d	23-Feb-27	14-Jul-27	204.0d
7558	FN-AP2-SRR-100	Install Wall Insulation - Support Restroom - INTF - AP 2	5.0d	23-Feb-27	1-Mar-27	200.0d
7559	FN-AP2-SRR-110	Hang Drywall Walls - Support Restroom - INTF - AP 2	5.0d	28-Apr-27	4-May-27	159.0d
7560	FN-AP2-SRR-120	Install ACT Ceiling Grid - Support Restroom - INTF - AP 2	2.0d	5-May-27	6-May-27	204.0d

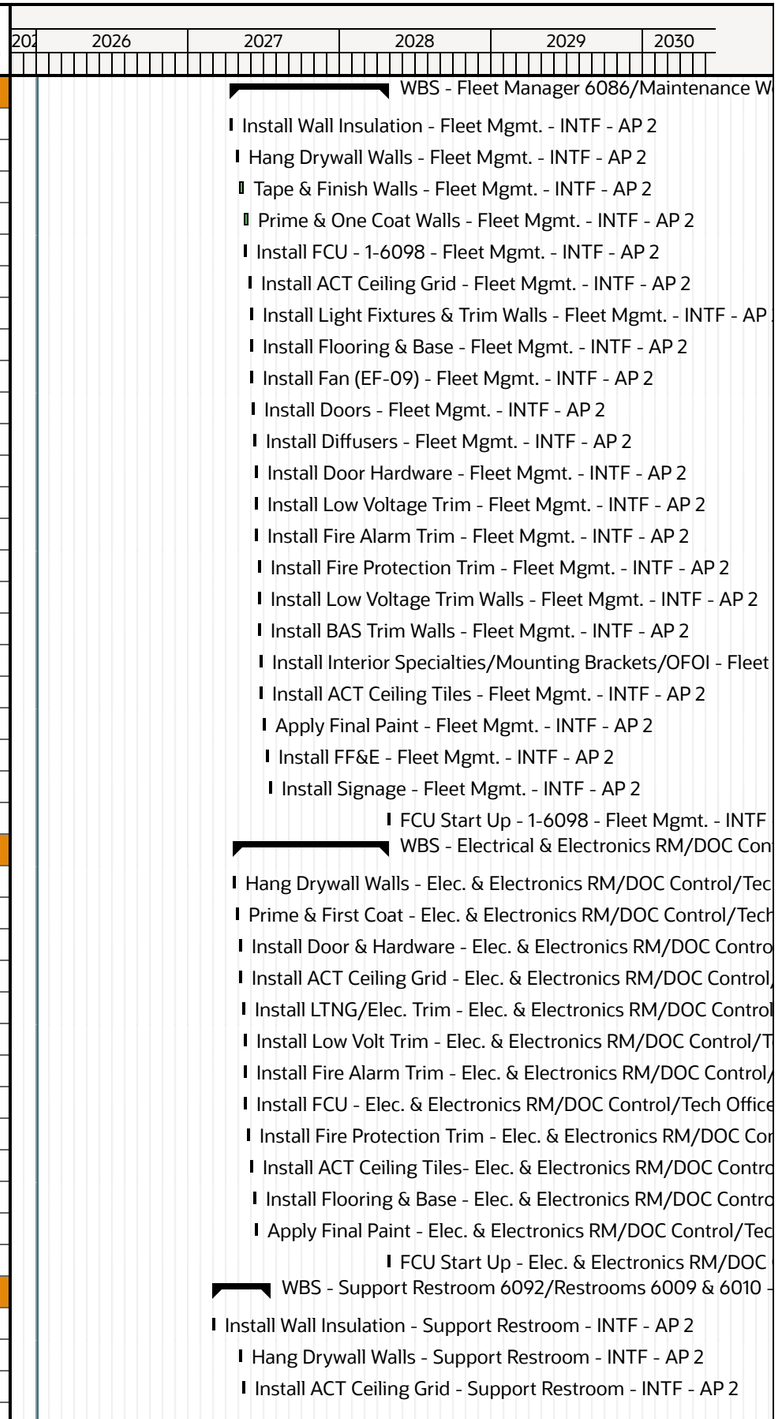


	ID	Name	Dur	Start	Finish	TF
7561	FN-AP2-SRR-130	Install Elec. Trim - Support Restroom - INTF - AP 2	5.0d	7-May-27	13-May-27	204.0d
7562	FN-AP2-SRR-230	Install Exhaust Fans & Trim - Support Restroom - INTF - AP 2	5.0d	7-May-27	13-May-27	239.0d
7563	FN-AP2-SRR-140	Install Mech. Trim - Support Restroom - INTF - AP 2	5.0d	14-May-27	20-May-27	204.0d
7564	FN-AP2-SRR-150	Install Fire Protection Trim - Support Restroom - INTF - AP 2	5.0d	21-May-27	27-May-27	204.0d
7565	FN-AP2-SRR-160	Install Door & Hardware - Support Restroom - INTF - AP 2	5.0d	28-May-27	4-Jun-27	204.0d
7566	FN-AP2-SRR-170	Install Wall/Floor Tile & Grout - Support Restroom - INTF - AP 2	5.0d	7-Jun-27	11-Jun-27	204.0d
7567	FN-AP2-SRR-180	Install Plumbing Fixtures - Support Restroom - INTF - AP 2	5.0d	14-Jun-27	18-Jun-27	204.0d
7568	FN-AP2-SRR-190	Install Toilet Accessories - Support Restroom - INTF - AP 2	5.0d	21-Jun-27	25-Jun-27	204.0d
7569	FN-AP2-SRR-200	Install Elec. Trim - Support Restroom - INTF - AP 2	5.0d	28-Jun-27	2-Jul-27	204.0d
7570	FN-AP2-SRR-210	Install ACT Ceiling Tiles - Support Restroom - INTF - AP 2	5.0d	6-Jul-27	12-Jul-27	204.0d
7571	FN-AP2-SRR-220	Install Fire Alarm Trim- Support Restroom - INTF - AP 2	5.0d	6-Jul-27	12-Jul-27	204.0d
7572	FN-AP2-SRR-240	Apply Final Paint - Support Restroom - INTF - AP 2	2.0d	13-Jul-27	14-Jul-27	204.0d
7573	WBS - Domestic Water Pump Room 6095 - INTF - Apron 2		25.0d	7-Apr-27	11-May-27	369.0d
7574	FN-AP2-WP-10	Prime & First Coat - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	7-Apr-27	13-Apr-27	354.0d
7575	FN-AP2-WP-20	Install Booster Pump & Associated Piping - Domestic Water Pump Room 6095 ...	5.0d	14-Apr-27	20-Apr-27	354.0d
7576	FN-AP2-WP-30	Install Door Hardware - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	14-Apr-27	20-Apr-27	368.0d
7577	FN-AP2-WP-40	Install Lights - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	14-Apr-27	20-Apr-27	379.0d
7578	FN-AP2-WP-50	Install Mech. Trim - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	14-Apr-27	20-Apr-27	384.0d
7579	FN-AP2-WP-60	Install Water Heater & Expansion Tank - Domestic Water Pump Room 6095 - IN...	5.0d	21-Apr-27	27-Apr-27	354.0d
7580	FN-AP2-WP-90	Seal Concrete Floor - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	28-Apr-27	4-May-27	358.0d
7581	FN-AP2-WP-80	Install Fire Alarm Trim - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	28-Apr-27	4-May-27	374.0d
7582	FN-AP2-WP-70	Apply Final Paint - Domestic Water Pump Room 6095 - INTF - AP 2	5.0d	5-May-27	11-May-27	358.0d
7583	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 3		407.0d	21-Dec-26	26-Jul-28	142.0d
7584	WBS - Marshalling 6099 Rm - INTF - AP 3		98.0d	22-Jul-27	9-Dec-27	143.0d
7585	FN-AP3-ELR-1460	Hang, Tape & Finish Drywall - Marshalling Rm/Elev Machine Rm 6099 - INTF - ...	10.0d	22-Jul-27	4-Aug-27	166.0d
7586	FN-AP3-ELR-1470	Prime & First Coat - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	5.0d	5-Aug-27	11-Aug-27	166.0d
7587	FN-AP3-ELR-1500	Install Light Fixtures & Trim - Marshalling Rm/Elev Machine Rm 6099 - INTF - ...	10.0d	19-Aug-27	1-Sep-27	166.0d
7588	FN-AP3-ELR-1560	Install Fire Alarm Trim - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	5.0d	2-Sep-27	9-Sep-27	166.0d
7589	FN-AP3-ELR-1570	Install Fire Protection Trim - Marshalling Rm/Elev Machine Rm 6099 - INTF - A...	5.0d	10-Sep-27	16-Sep-27	166.0d
7590	FN-AP3-ELR-1600	Install Mech. Trim - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	5.0d	17-Sep-27	23-Sep-27	166.0d
7591	FN-AP3-ELR-1540	Install Door - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	2.0d	24-Sep-27	27-Sep-27	166.0d
7592	FN-AP3-ELR-1580	Install Door Hardware - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	2.0d	28-Sep-27	29-Sep-27	166.0d
7593	FN-AP3-ELR-1550	Install RT Flooring & Base - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	3.0d	30-Sep-27	4-Oct-27	166.0d
7594	FN-AP3-ELR-1530	Apply Final Paint - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	5.0d	5-Oct-27	11-Oct-27	167.0d
7595	FN-AP3-ELR-1590	Install Signage - Marshalling Rm/Elev Machine Rm 6099 - INTF - AP 3	2.0d	8-Dec-27	9-Dec-27	143.0d
7596	WBS - Shipping & Receiving Area 6101- INTF- Apron 3		169.0d	25-Aug-27	24-Apr-28	207.0d
7597	FN-AP3-SH-1160	Install Wall Insulation - Ship & Receiving Area 6101- INTF - AP 3	5.0d	25-Aug-27	31-Aug-27	81.0d
7598	FN-AP3-SH-1180	Hang Drywall Walls - Ship & Receiving Area 6101- INTF - AP 3	5.0d	1-Sep-27	8-Sep-27	81.0d
7599	FN-AP3-SH-1370	Hang Hard Lid Ceilings - Ship & Receiving Area 6101- INTF - AP 3	5.0d	9-Sep-27	15-Sep-27	81.0d
7600	FN-AP3-SH-1190	Tape & Finish Walls - Ship & Receiving Area 6101- INTF - AP 3	10.0d	16-Sep-27	29-Sep-27	150.0d
7601	FN-AP3-SH-1200	Prime & One Coat Walls - Ship & Receiving Area 6101- INTF - AP 3	8.0d	30-Sep-27	11-Oct-27	150.0d
7602	FN-AP3-SH-1220	Install Doors - Ship & Receiving Area 6101- INTF - AP 3	5.0d	12-Oct-27	18-Oct-27	162.0d

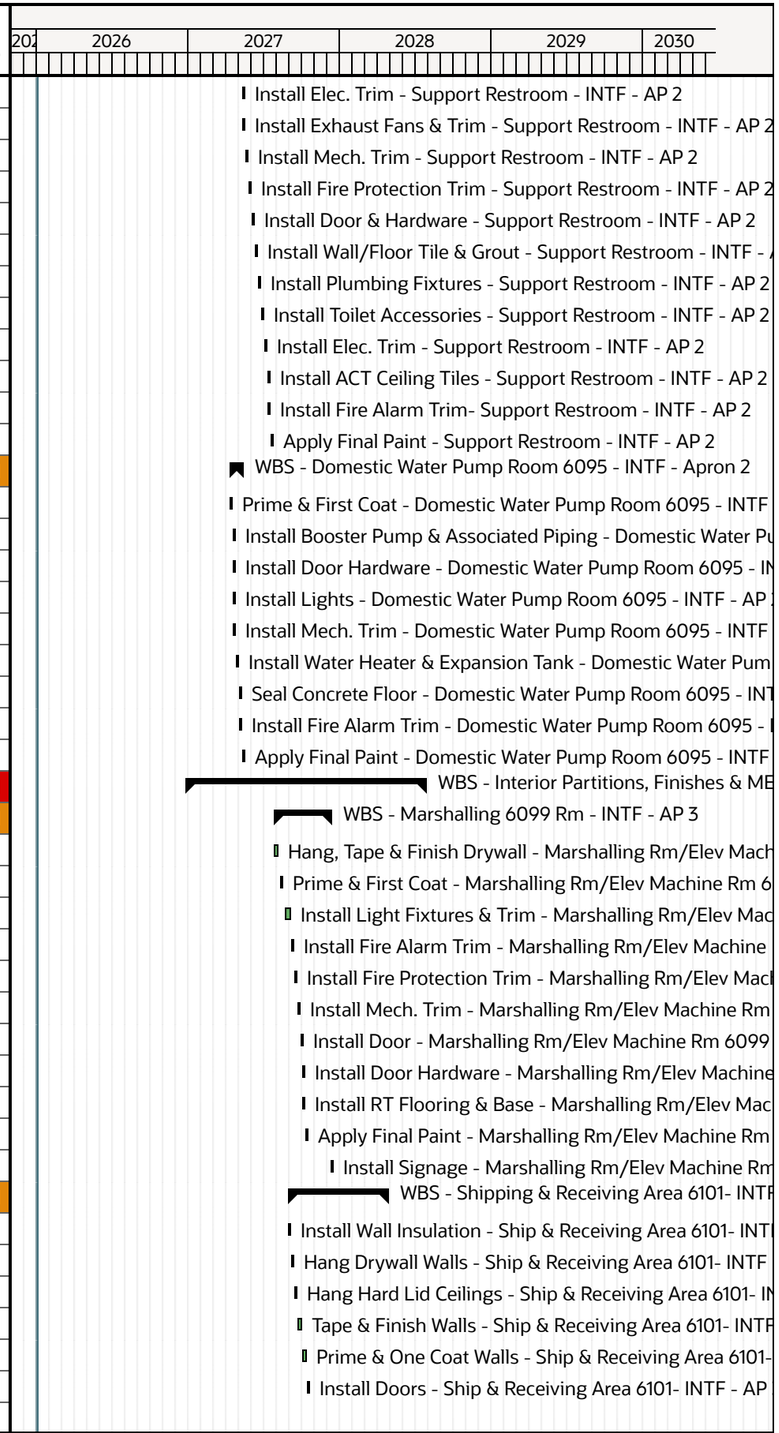


	ID	Name	Dur	Start	Finish	TF
7603	FN-AP3-SH-1230	Install RT Flooring & Base - Ship & Receiving Area 6101- INTF - AP 3	3.0d	12-Oct-27	14-Oct-27	164.0d
7604	FN-AP3-SH-1350	Install ACT Ceiling Grid - Ship & Receiving Area 6101- INTF - AP 3	3.0d	12-Oct-27	14-Oct-27	150.0d
7605	FN-AP3-SH-1260	Install Fire Alarm Trim - Ship & Receiving Area 6101- INTF - AP 3	9.0d	15-Oct-27	27-Oct-27	150.0d
7606	FN-AP3-SH-1210	Install Low Voltage Trim - Ship & Receiving Area 6101- INTF - AP 3	9.0d	15-Oct-27	27-Oct-27	150.0d
7607	FN-AP3-SH-1240	Install Diffusers - Ship & Receiving Area 6101- INTF - AP 3	5.0d	19-Oct-27	25-Oct-27	152.0d
7608	FN-AP3-SH-1300	Install Door Hardware - Ship & Receiving Area 6101- INTF - AP 3	5.0d	19-Oct-27	25-Oct-27	162.0d
7609	FN-AP3-SH-1250	Install Fire Protection Trim - Ship & Receiving Area 6101- INTF - AP 3	5.0d	26-Oct-27	1-Nov-27	152.0d
7610	FN-AP3-SH-1400	Install FCU -1-6101- Ship & Receiving Area 6101- INTF - AP 3	2.0d	26-Oct-27	27-Oct-27	199.0d
7611	FN-AP3-SH-1280	Install Light Fixtures & Trim Walls - Ship & Receiving Area 6101- INTF - AP 3	5.0d	28-Oct-27	3-Nov-27	150.0d
7612	FN-AP3-SH-1270	Install Interior Specialties/Mounting Brackets/OFOI - Ship & Receiving Area 61...	5.0d	2-Nov-27	8-Nov-27	152.0d
7613	FN-AP3-SH-1310	Install Low Voltage Trim Walls - Ship & Receiving Area 6101- INTF - AP 3	5.0d	2-Nov-27	8-Nov-27	152.0d
7614	FN-AP3-SH-1420	Install BAS Trim Walls - Ship & Receiving Area 6101- INTF - AP 3	5.0d	2-Nov-27	8-Nov-27	152.0d
7615	FN-AP3-SH-1360	Install ACT Tiles - Ship & Receiving Area 6101- INTF - AP 3	5.0d	4-Nov-27	10-Nov-27	150.0d
7616	FN-AP3-SH-1290	Apply Final Paint - Ship & Receiving Area 6101- INTF - AP 3	5.0d	16-Feb-28	22-Feb-28	85.0d
7617	FN-AP3-SH-1380	Install Roll up Door 6101B - Ship & Receiving Area 6101- INTF - AP 3	2.0d	23-Feb-28	24-Feb-28	85.0d
7618	FN-AP3-SH-1320	Install FF&E- Ship & Receiving Area 6101- INTF - AP 3	5.0d	25-Feb-28	2-Mar-28	85.0d
7619	FN-AP3-SH-1330	Install Signage - Ship & Receiving Area 6101- INTF - AP 3	7.0d	3-Mar-28	13-Mar-28	85.0d
7620	FN-AP3-SH-1410	FCU Start Up - Ship & Receiving Area 6101- INTF - AP 3	2.0d	21-Apr-28	24-Apr-28	207.0d
7621	WBS - UPS 6094/ATC 6096 Room - INTF - Apron 3		327.0d	13-Jan-27	24-Apr-28	207.0d
7622	RI-AP3-UPS-6000	Install Fire Sprinkler Hangers - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	13-Jan-27	14-Jan-27	14.0d
7623	RI-AP3-UPS-6010	Install CHW Hangers - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	15-Jan-27	18-Jan-27	14.0d
7624	RI-AP3-UPS-6020	Install Plumbing Hangers - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	19-Jan-27	20-Jan-27	14.0d
7625	RI-AP3-UPS-6030	Install Elec. Hangers - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	21-Jan-27	22-Jan-27	14.0d
7626	RI-AP3-UPS-6040	Install Fireproofing - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	25-Jan-27	26-Jan-27	14.0d
7627	RI-AP3-UPS-6050	Install CHW OH Rough-in - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	27-Jan-27	28-Jan-27	17.0d
7628	RI-AP3-UPS-6060	Install Plumbing OH Rough-in - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	27-Jan-27	28-Jan-27	14.0d
7629	RI-AP3-UPS-6080	Install CHW/Duct Insulation - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	29-Jan-27	1-Feb-27	32.0d
7630	RI-AP3-UPS-6070	Install Duct OH Rough-in - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	3-Feb-27	4-Feb-27	14.0d
7631	RI-AP3-UPS-6090	Fire Sprinkler Mains & Branch Line Rough-in - UPS 6094/ATC 6096 Room - INT...	3.0d	5-Feb-27	9-Feb-27	14.0d
7632	RI-AP3-UPS-6100	Install Elec. OH Rough-in - UPS 6094/ATC 6096 Room - INTF - AP 3	5.0d	12-Feb-27	18-Feb-27	14.0d
7633	RI-AP3-UPS-6110	Install Low Voltage OH Rough-in - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	19-Feb-27	22-Feb-27	14.0d
7634	RI-AP3-UPS-6120	FRP Alstom UPS Elec. Pad - UPS 6094/ATC 6096 Room - INTF - AP 3	5.0d	19-Feb-27	25-Feb-27	14.0d
7635	RI-AP3-UPS-6130	Patch Fireproofing - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	26-Feb-27	1-Mar-27	14.0d
7636	FN-AP3-UPS-480	Prime & One Coat Paint - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	2-Mar-27	3-Mar-27	14.0d
7637	FN-AP3-UPS-620	Install Doors & Hardware - UPS 6094/ATC 6096 Room - INTF - AP 3	3.0d	4-Mar-27	8-Mar-27	14.0d
7638	FN-AP3-UPS-500	Install Light Fixtures & Trim - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	9-Mar-27	10-Mar-27	14.0d
7639	FN-AP3-UPS-530	Install Fire Protection Trim - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	11-Mar-27	12-Mar-27	14.0d
7640	FN-AP3-UPS-540	Install Fire Alarm Trim - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	11-Mar-27	12-Mar-27	14.0d
7641	FN-AP3-UPS-560	Install Low Volt Trim - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	11-Mar-27	12-Mar-27	14.0d
7642	FN-AP3-UPS-590	Install Mech. Trim - UPS Room 6094 - INTF - AP 3	2.0d	15-Mar-27	16-Mar-27	14.0d
7643	FN-AP3-UPS-520	Install RT Flooring & Base - UPS 6094/ATC 6096 Room - INTF - AP 3	3.0d	17-Mar-27	19-Mar-27	14.0d
7644	FN-AP3-UPS-600	Install FCU-1-6096 - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	17-Mar-27	18-Mar-27	355.0d

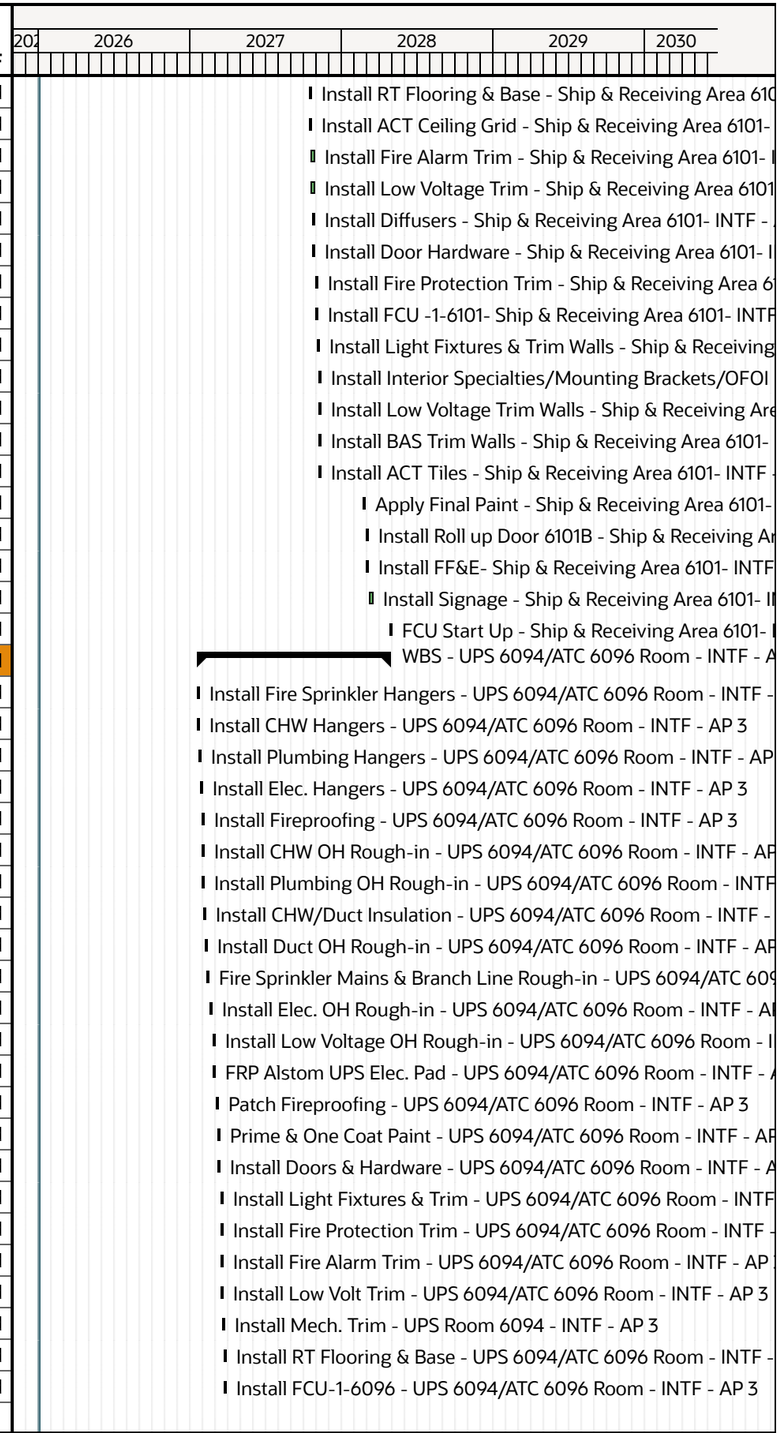


	ID	Name	Dur	Start	Finish	TF
7645	FN-AP3-UPS-1430	Hang Drywall (Post Alstom Turnover) - UPS 6094/ATC 6096 Room - INTF - AP 3	5.0d	25-Aug-27	31-Aug-27	170.0d
7646	FN-AP3-UPS-1440	Tape & Finish Drywall (Post Alstom Turnover) - UPS 6094/ATC 6096 Room - IN...	5.0d	1-Sep-27	8-Sep-27	170.0d
7647	FN-AP3-UPS-510	Apply Final Paint - (Post Alstom Turnover) - UPS 6094/ATC 6096 Room - INTF ...	5.0d	9-Sep-27	15-Sep-27	170.0d
7648	FN-AP3-UPS-630	Install FECs - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	16-Sep-27	17-Sep-27	299.0d
7649	FN-AP3-UPS-1450	FCU Start Up - UPS 6094/ATC 6096 Room - INTF - AP 3	2.0d	21-Apr-28	24-Apr-28	207.0d
7650	WBS - PDS Room 6097 - INTF - AP 3		180.0d	13-Jan-27	24-Sep-27	294.0d
7651	RI-AP3-PDS-5800	Install Fire Sprinkler Hangers - PDS Room 6097 - INTF - AP 3	2.0d	13-Jan-27	14-Jan-27	1.0d
7652	RI-AP3-PDS-5810	Install CHW Hangers - PDS Room 6097 - INTF - AP 3	2.0d	15-Jan-27	18-Jan-27	1.0d
7653	RI-AP3-PDS-5820	Install Plumbing Hangers - PDS Room 6097 - INTF - AP 3	2.0d	19-Jan-27	20-Jan-27	1.0d
7654	RI-AP3-PDS-5830	Install Elec. Hangers - PDS Room 6097 - INTF - AP 3	2.0d	21-Jan-27	22-Jan-27	1.0d
7655	RI-AP3-PDS-5840	Install Fireproofing - PDS Room 6097 - INTF - AP 3	5.0d	25-Jan-27	29-Jan-27	1.0d
7656	RI-AP3-PDS-5860	Install CHW OH Rough-in - PDS Room 6097 - INTF - AP 3	5.0d	1-Feb-27	5-Feb-27	1.0d
7657	RI-AP3-PDS-5870	Install Plumbing OH Rough-in - PDS Room 6097 - INTF - AP 3	2.0d	1-Feb-27	2-Feb-27	1.0d
7658	RI-AP3-PDS-5880	Install Duct OH Rough-in - PDS Room 6097 - INTF - AP 3	5.0d	8-Feb-27	12-Feb-27	1.0d
7659	RI-AP3-PDS-5900	Install CHW/Duct Insulation - PDS Room 6097 - INTF - AP 3	5.0d	8-Feb-27	12-Feb-27	16.0d
7660	RI-AP3-PDS-5890	Fire Sprinkler Mains & Branch Line Rough-in - PDS Room 6097 - INTF - AP 3	5.0d	15-Feb-27	19-Feb-27	1.0d
7661	RI-AP3-PDS-5910	Install Elec. OH Rough-in - PDS Room 6097 - INTF - AP 3	5.0d	22-Feb-27	26-Feb-27	1.0d
7662	RI-AP3-PDS-5920	Install Low Voltage OH Rough-in - PDS Room 6097 - INTF - AP 3	2.0d	1-Mar-27	2-Mar-27	4.0d
7663	RI-AP3-PDS-5930	FRP Alstom PDS Elec. Pads - PDS Room 6097 - INTF - AP 3	5.0d	1-Mar-27	5-Mar-27	1.0d
7664	RI-AP3-PDS-5990	Patch Fireproofing - PDS Room 6097 - INTF - AP 3	2.0d	8-Mar-27	9-Mar-27	1.0d
7665	FN-AP3-PDS-660	Prime & One Coat Paint - PDS Room 6097 - INTF - AP 3	5.0d	10-Mar-27	16-Mar-27	1.0d
7666	FN-AP3-PDS-680	Install Doors & Hardware - PDS Room 6097 - INTF - AP 3	2.0d	17-Mar-27	18-Mar-27	1.0d
7667	FN-AP3-PDS-690	Install Light Fixtures & Trim - PDS Room 6097 - INTF - AP 3	5.0d	19-Mar-27	25-Mar-27	1.0d
7668	FN-AP3-PDS-800	Install Coil Roll-Up Doors (6097E & 6097C) - PDS Room 6097 - INTF - AP 3	5.0d	19-Mar-27	25-Mar-27	10.0d
7669	FN-AP3-PDS-710	Install Fire Alarm Trim - PDS Room 6097 - INTF - AP 3	2.0d	26-Mar-27	29-Mar-27	5.0d
7670	FN-AP3-PDS-720	Install Low Volt Trim - PDS Room 6097 - INTF - AP 3	2.0d	26-Mar-27	29-Mar-27	1.0d
7671	FN-AP3-PDS-730	Install Mech. Trim - PDS Room 6097 - INTF - AP 3	2.0d	30-Mar-27	31-Mar-27	1.0d
7672	FN-AP3-PDS-700	Install Fire Protection Trim - PDS Room 6097 - INTF - AP 3	2.0d	1-Apr-27	2-Apr-27	1.0d
7673	FN-AP3-PDS-750	Install BCU -1-6097 - PDS Room 6097 - INTF - AP 3	2.0d	1-Apr-27	2-Apr-27	1.0d
7674	FN-AP3-PDS-760	Install RF Flooring & Base - PDS Room 6097 - INTF - AP 3	3.0d	5-Apr-27	7-Apr-27	1.0d
7675	FN-AP3-PDS-1410	Hang Drywall (Post Alstom Turnover) - PDS Room 6097 - INTF - AP 3	5.0d	25-Aug-27	31-Aug-27	175.0d
7676	FN-AP3-PDS-1420	Tape & Finish Drywall (Post Alstom Turnover) - PDS Room 6097 - INTF - AP 3	5.0d	1-Sep-27	8-Sep-27	175.0d
7677	FN-AP3-PDS-770	Apply Final Paint - (Post Alstom Turnover) PDS Room 6097 - INTF - AP 3	5.0d	16-Sep-27	22-Sep-27	170.0d
7678	FN-AP3-PDS-780	Install FECs - PDS Room 6097 - INTF - AP 3	2.0d	23-Sep-27	24-Sep-27	294.0d
7679	WBS - BHS Control Room 6107 - INTF - AP 3		91.0d	10-Jun-27	18-Oct-27	278.0d
7680	FN-AP3-BHS-1020	Install Windows & Trim - BHS Control Room 6107 - INTF - AP 3	5.0d	10-Jun-27	16-Jun-27	78.0d
7681	FN-AP3-BHS-820	Hang, Tape & Finish Drywall - BHS Control Room 6107 - INTF - AP 3	10.0d	22-Jul-27	4-Aug-27	54.0d
7682	FN-AP3-BHS-830	Install Fire Rated Backboards - BHS Control Room 6107 - INTF - AP 3	3.0d	5-Aug-27	9-Aug-27	113.0d
7683	FN-AP3-BHS-840	Prime & One Coat Paint - BHS Control Room 6107 - INTF - AP 3	5.0d	10-Aug-27	16-Aug-27	113.0d
7684	FN-AP3-BHS-850	Install ACT Ceiling Grid - BHS Control Room 6107 - INTF - AP 3	2.0d	17-Aug-27	18-Aug-27	113.0d
7685	FN-AP3-BHS-860	Install Doors & Hardware - BHS Control Room 6107 - INTF - AP 3	3.0d	17-Aug-27	19-Aug-27	167.0d
7686	FN-AP3-BHS-870	Install Light Fixtures & Trim - BHS Control Room 6107 - INTF - AP 3	3.0d	20-Aug-27	24-Aug-27	167.0d

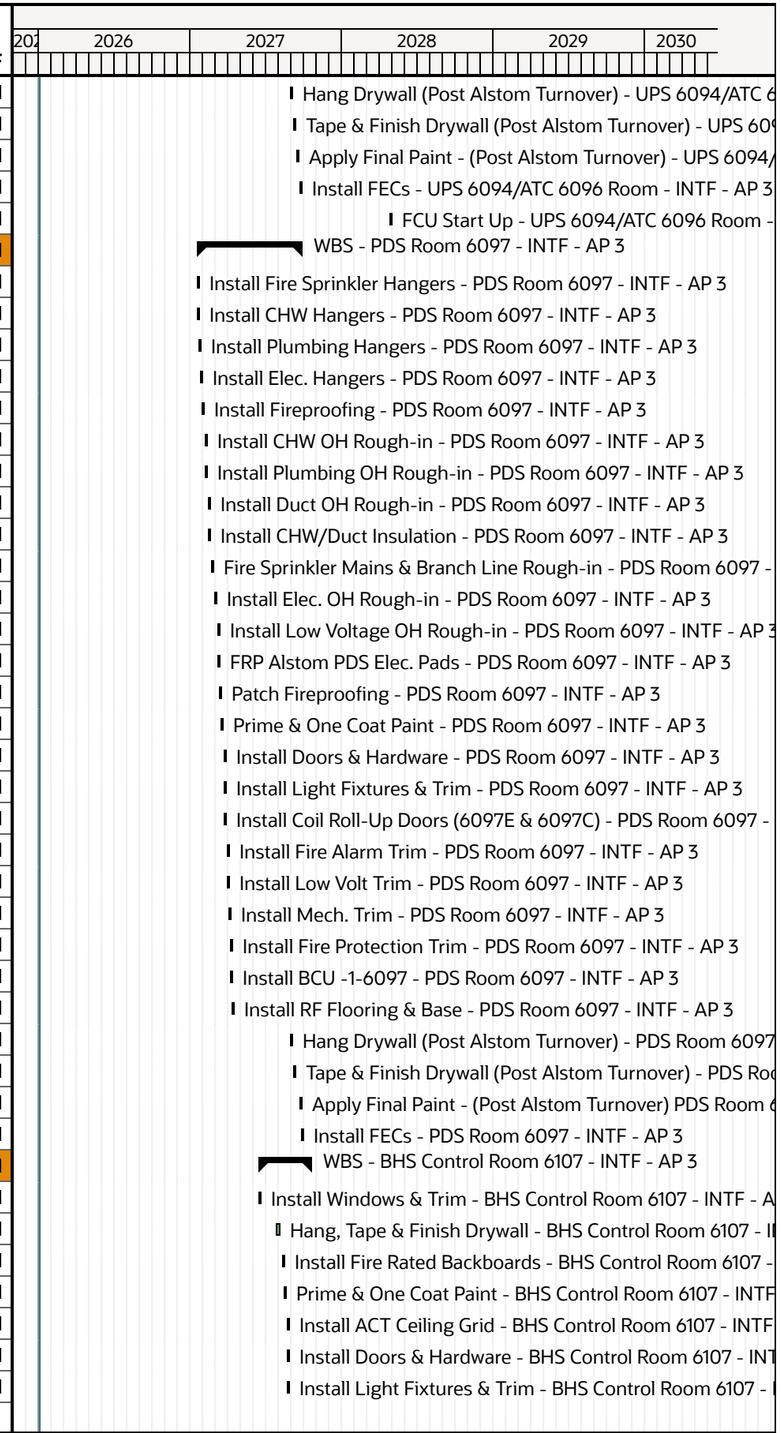


	ID	Name	Dur	Start	Finish	TF
7687	FN-AP3-BHS-880	Install Fire Protection Trim - BHS Control Room 6107 - INTF - AP 3	2.0d	25-Aug-27	26-Aug-27	180.0d
7688	FN-AP3-BHS-890	Install Fire Alarm Trim - BHS Control Room 6107 - INTF - AP 3	5.0d	25-Aug-27	31-Aug-27	167.0d
7689	FN-AP3-BHS-900	Install Low Volt Trim - BHS Control Room 6107 - INTF - AP 3	5.0d	25-Aug-27	31-Aug-27	167.0d
7690	FN-AP3-BHS-910	Install Plumbing Trim - BHS Control Room 6107 - INTF - AP 3	5.0d	1-Sep-27	8-Sep-27	167.0d
7691	FN-AP3-BHS-920	Install Mech. Trim - BHS Control Room 6107 - INTF - AP 3	5.0d	9-Sep-27	15-Sep-27	167.0d
7692	FN-AP3-BHS-930	Install ACT Tiles - BHS Control Room 6107 - INTF - AP 3	5.0d	16-Sep-27	22-Sep-27	167.0d
7693	FN-AP3-BHS-950	Install RT Flooring & Base - BHS Control Room 6107 - INTF - AP 3	3.0d	23-Sep-27	27-Sep-27	167.0d
7694	FN-AP3-BHS-960	Apply Final Paint - BHS Control Room 6107 - INTF - AP 3	5.0d	28-Sep-27	4-Oct-27	167.0d
7695	FN-AP3-BHS-1000	Install Millwork - BHS Control Room 6107 - INTF - AP 3	5.0d	5-Oct-27	11-Oct-27	278.0d
7696	FN-AP3-BHS-1010	Install FF&E - BHS Control Room 6107 - INTF - AP 3	5.0d	12-Oct-27	18-Oct-27	278.0d
7697	WBS - Employee Portal 6104 - INTF - AP 3		62.0d	22-Jul-27	18-Oct-27	258.0d
7698	FN-AP3-SR-1040	Hang Drywall Walls - Employee Portal 6104 - INTF - AP 3	5.0d	22-Jul-27	28-Jul-27	105.0d
7699	FN-AP3-SR-1060	Prime & One Coat Paint - Employee Portal 6104 - INTF - AP 3	5.0d	29-Jul-27	4-Aug-27	123.0d
7700	FN-AP3-SR-1080	Install Doors & Hardware - Employee Portal 6104 - INTF - AP 3	3.0d	5-Aug-27	9-Aug-27	187.0d
7701	FN-AP3-SR-1070	Install ACT Ceiling Grid - Employee Portal 6104 - INTF - AP 3	3.0d	19-Aug-27	23-Aug-27	113.0d
7702	FN-AP3-SR-1090	Install Light Fixtures & Trim - Employee Portal 6104 - INTF - AP 3	3.0d	24-Aug-27	26-Aug-27	177.0d
7703	FN-AP3-SR-1100	Install Fire Protection Trim - Employee Portal 6104 - INTF - AP 3	2.0d	27-Aug-27	30-Aug-27	292.0d
7704	FN-AP3-SR-1110	Install Fire Alarm Trim - Employee Portal 6104 - INTF - AP 3	5.0d	27-Aug-27	2-Sep-27	289.0d
7705	FN-AP3-SR-1120	Install Low Volt Trim - Employee Portal 6104 - INTF - AP 3	5.0d	27-Aug-27	2-Sep-27	177.0d
7706	FN-AP3-SR-1140	Install Mech. Trim - Employee Portal 6104 - INTF - AP 3	5.0d	3-Sep-27	10-Sep-27	177.0d
7707	FN-AP3-SR-1150	Install ACT Tiles - Employee Portal 6104 - INTF - AP 3	5.0d	13-Sep-27	17-Sep-27	177.0d
7708	FN-AP3-SR-1160	Install RT Flooring & Base - Employee Portal 6104 - INTF - AP 3	3.0d	5-Oct-27	7-Oct-27	166.0d
7709	FN-AP3-SR-1170	Apply Final Paint - Employee Portal 6104 - INTF - AP 3	5.0d	12-Oct-27	18-Oct-27	167.0d
7710	WBS - Support Corridor 6008 - INTF - AP 3		407.0d	21-Dec-26	26-Jul-28	82.0d
7711	FN-AP3-SR-1500	Insulated Metal Panel System Fab - Support Corridor 6008 - INTF - AP 3	50.0d	21-Dec-26	2-Mar-27	419.0d
7712	FN-AP3-SR-1510	Install Insulated Metal Panel System for Bagge Tunnel - Support Corridor 6008 ...	10.0d	3-Mar-27	16-Mar-27	419.0d
7713	FN-AP3-SR-1300	Install Elec. Trim - Support Corridor 6008 - INTF - AP 3	5.0d	4-Nov-27	10-Nov-27	156.0d
7714	FN-AP3-SR-1310	Install Mech. Trim - Support Corridor 6008 - INTF - AP 3	5.0d	11-Nov-27	17-Nov-27	226.0d
7715	FN-AP3-SR-1320	Install Fire Protection Trim - Support Corridor 6008 - INTF - AP 3	5.0d	18-Nov-27	24-Nov-27	226.0d
7716	FN-AP3-SR-1340	Install Fire Alarm Trim - Support Corridor 6008 - INTF - AP 3	5.0d	29-Nov-27	3-Dec-27	226.0d
7717	FN-AP3-SR-1330	Install Doors & Hardware - Support Corridor 6008 - INTF - AP 3	5.0d	29-Nov-27	3-Dec-27	226.0d
7718	FN-AP3-SR-1350	install Low Voltage & Security Trim - Support Corridor 6008 - INTF - AP 3	5.0d	29-Nov-27	3-Dec-27	226.0d
7719	FN-AP3-SR-1370	Seal Concrete Floor - Support Corridor 6008 - INTF - AP 3	5.0d	28-Jun-28	5-Jul-28	82.0d
7720	FN-AP3-SR-1360	Install Rubber Base - Support Corridor 6008 - INTF - AP 3	5.0d	6-Jul-28	12-Jul-28	82.0d
7721	FN-AP3-SR-1390	Apply Final Paint - Support Corridor 6008 - INTF - AP 3	5.0d	13-Jul-28	19-Jul-28	82.0d
7722	FN-AP3-SR-1380	Install FEC Cabinets & Accessories - Support Corridor 6008 - INTF - AP 3	5.0d	20-Jul-28	26-Jul-28	82.0d
7723	WBS - Loading Dock Exterior - INTF - AP 3		127.0d	4-Nov-27	4-May-28	85.0d
7724	FN-AP3-LD-1220	Install Elec. Trim - Loading Dock Exterior - INTF - AP 3	5.0d	4-Nov-27	10-Nov-27	156.0d
7725	FN-AP3-LD-1230	Install Mech. Trim - Loading Dock Exterior - INTF - AP 3	5.0d	11-Nov-27	17-Nov-27	156.0d
7726	FN-AP3-LD-1240	Install Protection Trim - Loading Dock Exterior - INTF - AP 3	5.0d	18-Nov-27	24-Nov-27	156.0d
7727	FN-AP3-LD-1250	Install Dock Levelers - Loading Dock Exterior - INTF - AP 3	5.0d	29-Nov-27	3-Dec-27	156.0d
7728	FN-AP3-LD-1260	Install Dock Bumpers/Column Bumpers - Loading Dock Exterior - INTF - AP 3	3.0d	6-Dec-27	8-Dec-27	156.0d

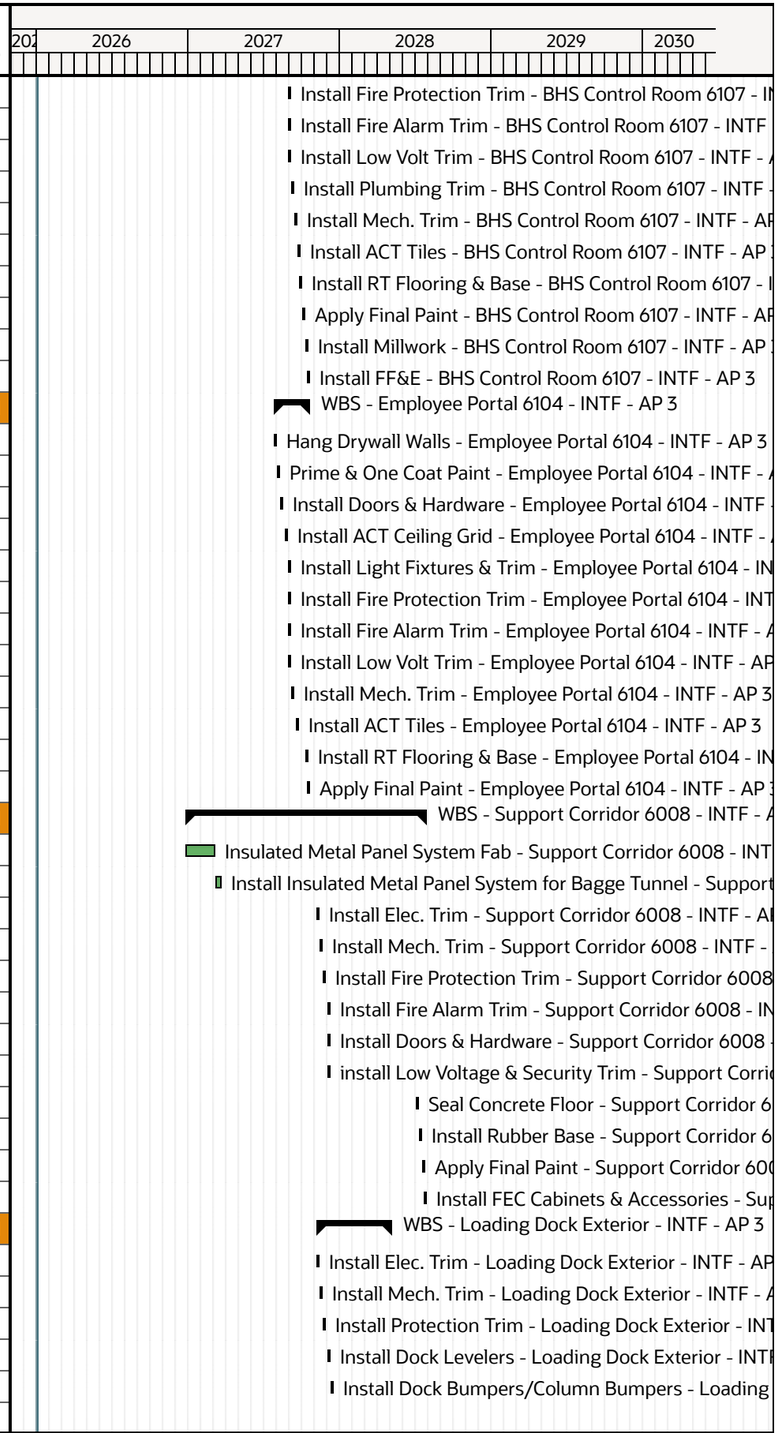


	ID	Name	Dur	Start	Finish	TF
7729	FN-AP3-LD-1270	Install Roll Up Doors (6097E/6097C/6008F)- Loading Dock Exterior - INTF - A...	5.0d	9-Dec-27	15-Dec-27	156.0d
7730	FN-AP3-LD-1280	Install Doors & Hardware - Loading Dock Exterior - INTF - AP 3	5.0d	16-Dec-27	22-Dec-27	156.0d
7731	FN-AP3-LD-1210	Install Handrail & Gate - Loading Dock Exterior - INTF - AP 3	10.0d	23-Dec-27	7-Jan-28	156.0d
7732	FN-AP3-LD-1290	Install Trash Compactors - Loading Dock Exterior - INTF - AP 3	10.0d	10-Jan-28	21-Jan-28	156.0d
7733	FN-AP3-LD-1400	Install Signage - Loading Dock Exterior - INTF - AP 3	3.0d	2-May-28	4-May-28	85.0d
7734	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 4		253.0d	1-Apr-27	29-Mar-28	150.0d
7735	WBS - Outbound Baggage Makeup/Oversize Bagge Drop Off - INTF - Apron 4		191.0d	29-Jun-27	29-Mar-28	85.0d
7736	FN-AP4-BM-2190	Metal Panel System Scan - O/Bound BHS Makeup - INTF - AP 4	5.0d	29-Jun-27	6-Jul-27	190.0d
7737	FN-AP4-BM-2200	Insulated Metal Panel Wall System Fab - O/Bound BHS Makeup - INTF - AP 4	50.0d	7-Jul-27	15-Sep-27	190.0d
7738	FN-AP4-BM-2180	Install Insulated Metal Wall Panel (WA22) - O/Bound BHS Makeup - INTF - AP 4	6.0d	16-Sep-27	23-Sep-27	190.0d
7739	FN-AP4-BM-2050	Insulate Ceilings & Soffits - O/Bound BHS Makeup - INTF - AP 4	7.0d	12-Nov-27	22-Nov-27	98.0d
7740	FN-AP4-BM-2060	Apply Prime, First, Paint Ceilings - O/Bound BHS Makeup - INTF - AP 4	7.0d	23-Nov-27	3-Dec-27	98.0d
7741	FN-AP4-BM-1880	Install Ceiling Light Fixtures & Trim - O/Bound BHS Makeup - INTF - AP 4	10.0d	6-Dec-27	17-Dec-27	98.0d
7742	FN-AP4-BM-2000	Install Doors - O/Bound BHS Makeup - INTF - AP 4	5.0d	6-Dec-27	10-Dec-27	151.0d
7743	FN-AP4-BM-1910	Install Door Hardware - O/Bound BHS Makeup - INTF - AP 4	5.0d	13-Dec-27	17-Dec-27	151.0d
7744	FN-AP4-BM-1900	Install Diffusers - O/Bound BHS Makeup - INTF - AP 4	5.0d	20-Dec-27	27-Dec-27	98.0d
7745	FN-AP4-BM-1990	Install Low Voltage Trim - O/Bound BHS Makeup - INTF - AP 4	7.0d	28-Dec-27	6-Jan-28	98.0d
7746	FN-AP4-BM-2120	Install Fire Alarm Trim - O/Bound BHS Makeup - INTF - AP 4	5.0d	28-Dec-27	4-Jan-28	98.0d
7747	FN-AP4-BM-1930	Install Fire Protection Trim - O/Bound BHS Makeup - INTF - AP 4	3.0d	5-Jan-28	7-Jan-28	98.0d
7748	FN-AP4-BM-2030	Install Light Fixtures & Trim Walls - O/Bound BHS Makeup - INTF - AP 4	5.0d	10-Jan-28	14-Jan-28	123.0d
7749	FN-AP4-BM-2080	Seal Concrete Floor - O/Bound BHS Makeup - INTF - AP 4	20.0d	10-Jan-28	4-Feb-28	98.0d
7750	FN-AP4-BM-2150	Install 6" Tug Lane Striping/Cross Walk Striping - O/Bound BHS Makeup - INTF...	5.0d	7-Feb-28	11-Feb-28	98.0d
7751	FN-AP4-BM-2170	Install FECs - O/Bound BHS Makeup - INTF - AP 4	3.0d	7-Feb-28	9-Feb-28	105.0d
7752	FN-AP4-BM-2160	Install Galvanized Bollards - O/Bound BHS Makeup - INTF - AP 4	5.0d	14-Feb-28	18-Feb-28	98.0d
7753	FN-AP4-BM-2040	Install Low Voltage Trim Walls - O/Bound BHS Makeup - INTF - AP 4	5.0d	21-Feb-28	25-Feb-28	98.0d
7754	FN-AP4-BM-2140	Install Roll-Up Doors (6001A,6002A, 6002B & 6002C) - O/Bound BHS Makeup...	5.0d	28-Feb-28	3-Mar-28	98.0d
7755	FN-AP4-BM-2020	Install/Hang Signage - O/Bound BHS Makeup - INTF - AP 4	5.0d	23-Mar-28	29-Mar-28	85.0d
7756	WBS - Outbound Baggage Electrical - Apron 4		165.0d	1-Apr-27	22-Nov-27	238.0d
7757	FN-AP4-ER-2685	Set Elec. Switchgear & Equip. - Outbound Baggage Electrical - INTRF - AP 4	10.0d	1-Apr-27	14-Apr-27	314.0d
7758	FN-AP4-ER-2625	Install Elec. OH Rough-in - Outbound Baggage Electrical - INTRF - AP 4	15.0d	15-Apr-27	5-May-27	314.0d
7759	FN-AP4-ER-2695	Install Elec. Panels & Transformers - Outbound Baggage Electrical - INTRF - AP 4	10.0d	6-May-27	19-May-27	314.0d
7760	FN-AP4-ER-2705	Elec. Feeder Wire Measurements & Procurement - Outbound Baggage Electrica...	10.0d	20-May-27	3-Jun-27	314.0d
7761	FN-AP4-ER-2715	Pull & Terminate Elec. - Outbound Baggage Electrical - INTRF - AP 4	20.0d	12-Jul-27	6-Aug-27	289.0d
7762	FN-AP4-ER-2725	Third Party Elec. Testing - Outbound Baggage Electrical - INTRF - AP 4	3.0d	9-Aug-27	11-Aug-27	289.0d
7763	FN-AP4-ER-2735	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Outbound B...	2.0d	12-Aug-27	13-Aug-27	289.0d
7764	FN-AP4-ER-2745	APG QC Procedure for Perm Power Available for Dist. - Outbound Baggage Elec...	15.0d	27-Oct-27	16-Nov-27	238.0d
7765	FN-AP4-ER-2755	Final Checkout & Panel Startup - Outbound Baggage Electrical - INTRF - AP 4	2.0d	17-Nov-27	18-Nov-27	238.0d
7766	FN-AP4-ER-2765	Energize Baggage Equip. - Outbound Baggage Electrical - INTRF - AP 4	2.0d	19-Nov-27	22-Nov-27	238.0d
7767	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 5		229.0d	7-Dec-27	27-Oct-28	16.0d
7768	WBS - Baggage Claim 2, 3 & 4/Oversize Baggage - INTF - Apron 5		167.0d	21-Dec-27	15-Aug-28	68.0d
7769	FN-AP5-IB-1130	Install Wall Insulation- Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	21-Dec-27	28-Dec-27	13.0d
7770	FN-AP5-IB-1120	Insulate Ceilings & Soffits - Baggage Claim 2, 3, & 4 - INTF - AP 5	7.0d	21-Dec-27	30-Dec-27	34.0d

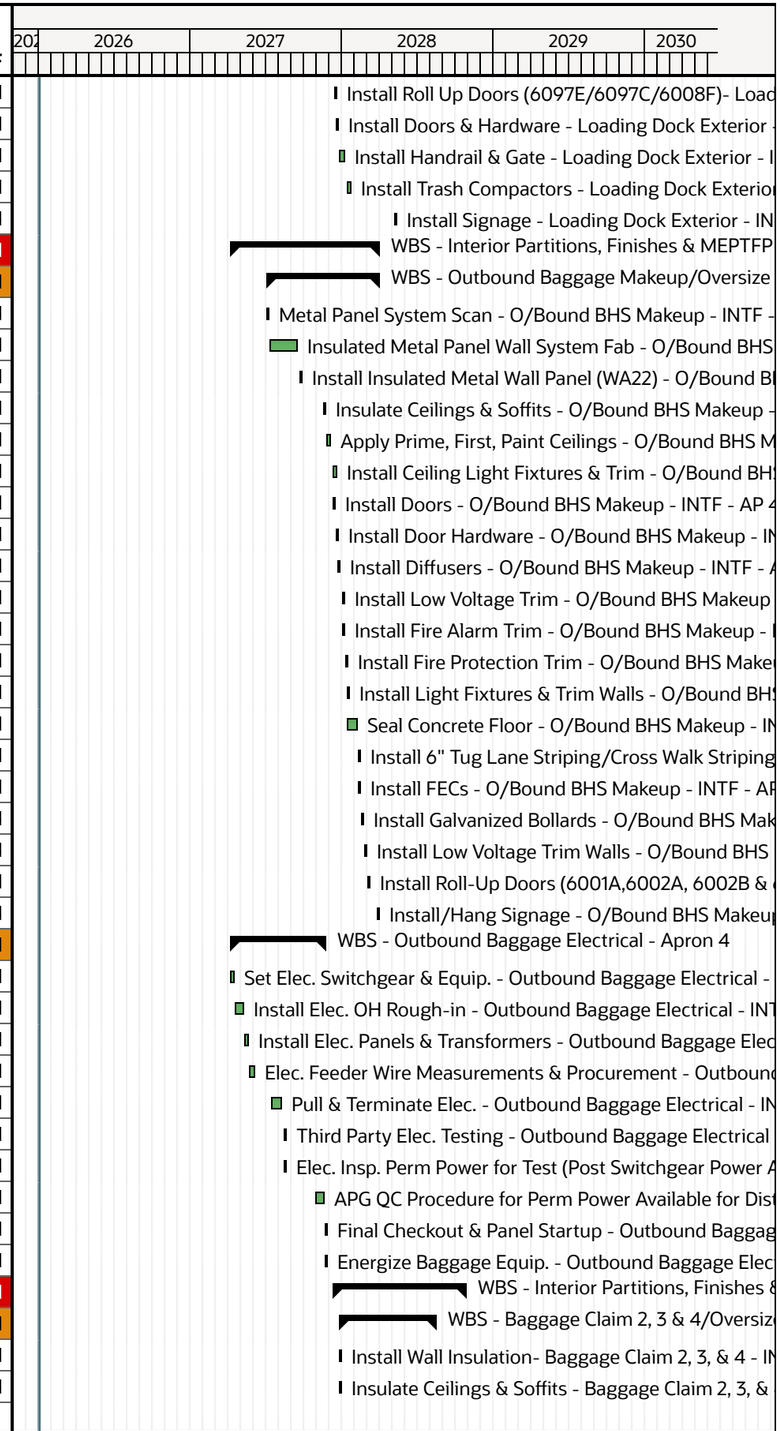


	ID	Name	Dur	Start	Finish	TF
7771	FN-AP5-IB-1140	Hang Hard Lid Ceilings - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	3-Jan-28	14-Jan-28	34.0d
7772	FN-AP5-IB-1150	Hang Drywall Walls - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	5-Jan-28	11-Jan-28	18.0d
7773	FN-AP5-IB-1170	Tape & Finish Walls - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	12-Jan-28	25-Jan-28	37.0d
7774	FN-AP5-IB-1420	Install Curtain Wall At South End - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	12-Jan-28	18-Jan-28	42.0d
7775	FN-AP5-IB-1160	Tape & Finish Ceilings - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	17-Jan-28	28-Jan-28	34.0d
7776	FN-AP5-IB-1190	Prime & One Coat Walls - Baggage Claim 2, 3, & 4 - INTF - AP 5	7.0d	26-Jan-28	3-Feb-28	37.0d
7777	FN-AP5-IB-1180	Apply Prime, First, Paint Ceilings - Baggage Claim 2, 3, & 4 - INTF - AP 5	7.0d	31-Jan-28	8-Feb-28	34.0d
7778	FN-AP5-IB-1230	Install Ceiling Light Fixtures & Trim - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	9-Feb-28	22-Feb-28	42.0d
7779	FN-AP5-IB-1220	Install Metal Ceiling Perimeter - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	9-Feb-28	22-Feb-28	34.0d
7780	FN-AP5-IB-1200	Install Doors - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	9-Feb-28	15-Feb-28	34.0d
7781	FN-AP5-IB-1210	Install ACT Ceiling Grid - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	9-Feb-28	22-Feb-28	34.0d
7782	FN-AP5-IB-1370	Install Door Hardware - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	16-Feb-28	22-Feb-28	34.0d
7783	FN-AP5-IB-1240	Install Diffusers - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	23-Feb-28	29-Feb-28	34.0d
7784	FN-AP5-IB-1250	Install Low Voltage Trim - Baggage Claim 2, 3, & 4 - INTF - AP 5	7.0d	23-Feb-28	2-Mar-28	34.0d
7785	FN-AP5-IB-1390	Install Fire Alarm Trim - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	23-Feb-28	29-Feb-28	34.0d
7786	FN-AP5-IB-1260	Install Fire Protection Trim - Baggage Claim 2, 3, & 4 - INTF - AP 5	3.0d	1-Mar-28	3-Mar-28	34.0d
7787	FN-AP5-IB-1280	Install Ceiling Tile - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	3-Mar-28	16-Mar-28	35.0d
7788	FN-AP5-IB-1410	Polish Exposed Concrete - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	6-Mar-28	10-Mar-28	34.0d
7789	FN-AP5-IB-1270	Install Metal Ceiling Panels - Baggage Claim 2, 3, & 4 - INTF - AP 5	15.0d	13-Mar-28	31-Mar-28	34.0d
7790	FN-AP5-IB-1290	Install Metal Base - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	20-Mar-28	31-Mar-28	34.0d
7791	FN-AP5-IB-1300	Install Carpet Flooring - Baggage Claim 2, 3, & 4 - INTF - AP 5	20.0d	3-Apr-28	28-Apr-28	34.0d
7792	FN-AP5-IB-1310	Install Column Covers - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	1-May-28	12-May-28	49.0d
7793	FN-AP5-IB-1330	Install Light Fixtures & Trim Walls/Columns - Baggage Claim 2, 3, & 4 - INTF - ...	5.0d	15-May-28	19-May-28	49.0d
7794	FN-AP5-IB-1340	Install Low Voltage Trim Walls/Columns - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	15-May-28	19-May-28	49.0d
7795	FN-AP5-IB-1450	Install Terrazzo Flooring at Baggage Claim 1, 2, 3, & 4 - INTF - AP 5	20.0d	15-May-28	12-Jun-28	28.0d
7796	FN-AP5-IB-1460	Install BAS Trim Walls/Columns - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	15-May-28	19-May-28	49.0d
7797	FN-AP5-IB-1350	Install Interior Specialties/Mounting Brackets/OFOI - Baggage Claim 2, 3, & 4 - ...	10.0d	22-May-28	5-Jun-28	49.0d
7798	FN-AP5-IB-1320	Apply Final Paint - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	6-Jun-28	19-Jun-28	49.0d
7799	FN-AP5-IB-1430	Finish Declaration Lanes - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	20-Jun-28	26-Jun-28	49.0d
7800	FN-AP5-IB-1360	Install FF&E - Baggage Claim 2, 3, & 4 - INTF - AP 5	10.0d	27-Jun-28	11-Jul-28	49.0d
7801	FN-AP5-IB-1380	Install Signage & Dimensional Text - Baggage Claim 2, 3, & 4 - INTF - AP 5	5.0d	12-Jul-28	18-Jul-28	49.0d
7802	FN-AP5-IB-1440	Terrazzo Final Polish - Baggage Claim 1, 2, 3, & 4 - INTF - AP 5	20.0d	19-Jul-28	15-Aug-28	68.0d
7803	WBS - HCAA Maintenance Room/Custodial Storage - INTF - Apron 5		114.0d	6-Jan-28	14-Jun-28	111.0d
7804	FN-AP5-SR-270	Install Wall Insulation - HCAA Maint. - INTF - AP 5	5.0d	6-Jan-28	12-Jan-28	13.0d
7805	FN-AP5-SR-280	Insulate Ceilings & Soffits - HCAA Maint. - INTF - AP 5	5.0d	6-Jan-28	12-Jan-28	21.0d
7806	FN-AP5-SR-300	Hang Drywall Walls - HCAA Maint. - INTF - AP 5	2.0d	14-Jan-28	17-Jan-28	18.0d
7807	FN-AP5-SR-290	Hang Hard Lid Ceilings - HCAA Maint. - INTF - AP 5	2.0d	18-Jan-28	19-Jan-28	18.0d
7808	FN-AP5-SR-320	Tape & Finish Walls - HCAA Maint. - INTF - AP 5	10.0d	18-Jan-28	31-Jan-28	91.0d
7809	FN-AP5-SR-310	Tape & Finish Ceilings - HCAA Maint. - INTF - AP 5	10.0d	20-Jan-28	2-Feb-28	89.0d
7810	FN-AP5-SR-340	Prime & One Coat Walls - HCAA Maint. - INTF - AP 5	7.0d	1-Feb-28	9-Feb-28	91.0d
7811	FN-AP5-SR-330	Apply Prime, First, Paint Ceilings - HCAA Maint. - INTF - AP 5	7.0d	3-Feb-28	11-Feb-28	89.0d
7812	FN-AP5-SR-360	Install Ceiling Light Fixtures & Trim - HCAA Maint. - INTF - AP 5	10.0d	14-Feb-28	25-Feb-28	89.0d

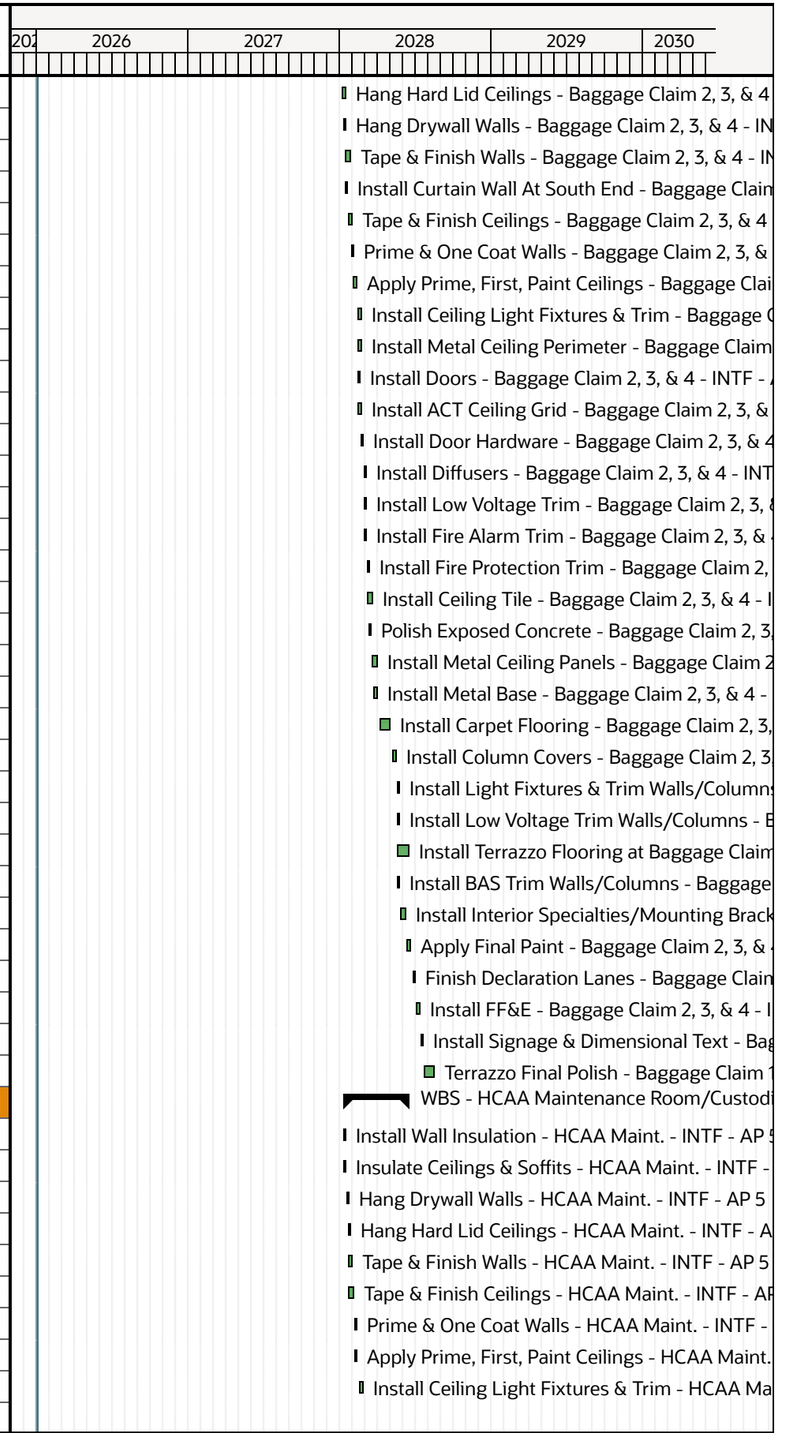


	ID	Name	Dur	Start	Finish	TF
7813	FN-AP5-SR-400	Install Fire Protection Trim - HCAA Maint. - INTF - AP 5	3.0d	14-Feb-28	16-Feb-28	96.0d
7814	FN-AP5-SR-390	Install Low Voltage Trim - HCAA Maint. - INTF - AP 5	5.0d	14-Feb-28	18-Feb-28	94.0d
7815	FN-AP5-SR-350	Install Doors - HCAA Maint. - INTF - AP 5	5.0d	14-Feb-28	18-Feb-28	170.0d
7816	FN-AP5-SR-520	Install Fire Alarm Trim - HCAA Maint. - INTF - AP 5	5.0d	14-Feb-28	18-Feb-28	94.0d
7817	FN-AP5-SR-480	Install Door Hardware - HCAA Maint. - INTF - AP 5	3.0d	21-Feb-28	23-Feb-28	170.0d
7818	FN-AP5-SR-420	Install Resinous Flooring - HCAA Maint. - INTF - AP 5	10.0d	15-May-28	26-May-28	34.0d
7819	FN-AP5-SR-540	Polish Concrete - HCAA Maint. - INTF - AP 5	5.0d	15-May-28	19-May-28	116.0d
7820	FN-AP5-SR-560	Install Rubber Base - HCAA Maint. - INTF - AP 5	5.0d	22-May-28	26-May-28	116.0d
7821	FN-AP5-SR-470	Install Light Fixtures & Trim Walls - HCAA Maint. - INTF - AP 5	5.0d	30-May-28	5-Jun-28	98.0d
7822	FN-AP5-SR-500	Install Low Voltage Trim Walls - HCAA Maint. - INTF - AP 5	5.0d	30-May-28	5-Jun-28	98.0d
7823	FN-AP5-SR-550	Install Metal Base - HCAA Maint. - INTF - AP 5	5.0d	30-May-28	5-Jun-28	111.0d
7824	FN-AP5-SR-1240	Install BAS Trim Walls - HCAA Maint. - INTF - AP 5	5.0d	30-May-28	5-Jun-28	98.0d
7825	FN-AP5-SR-460	Apply Final Paint - HCAA Maint. - INTF - AP 5	7.0d	6-Jun-28	14-Jun-28	111.0d
7826	WBS - Mechanical Room - INTF - Apron 5		83.0d	12-Jan-28	5-May-28	138.0d
7827	FN-AP5-MR-1300	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 5	15.0d	12-Jan-28	1-Feb-28	111.0d
7828	FN-AP5-MR-1310	Prime & First Coat - Mech. Room - INTF - AP 5	5.0d	2-Feb-28	8-Feb-28	167.0d
7829	FN-AP5-MR-1370	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - AP 5	15.0d	2-Feb-28	22-Feb-28	129.0d
7830	FN-AP5-MR-1320	Install Light Fixtures & Trim - Mech. Room - INTF - AP 5	5.0d	9-Feb-28	15-Feb-28	167.0d
7831	FN-AP5-MR-1410	Install Fire Alarm Trim - Mech. Room - INTF - AP 5	5.0d	16-Feb-28	22-Feb-28	167.0d
7832	FN-AP5-MR-1340	Install Doors - Mech. Room - INTF - AP 5	2.0d	23-Feb-28	24-Feb-28	167.0d
7833	FN-AP5-MR-1350	Seal Concrete - Mech. Room - INTF - AP 5	5.0d	25-Feb-28	2-Mar-28	179.0d
7834	FN-AP5-MR-1360	Install Door Hardware - Mech. Room - INTF - AP 5	2.0d	25-Feb-28	28-Feb-28	167.0d
7835	FN-AP5-MR-1330	Apply Final Paint - Mech. Room - INTF - AP 5	5.0d	3-Mar-28	9-Mar-28	179.0d
7836	FN-AP5-MR-1380	Energize Power at AHU - Mech. Room - INTF - AP 5	5.0d	26-Apr-28	2-May-28	79.0d
7837	FN-AP5-MR-1390	Start-up AHU - Mech. Room - INTF - AP 5	3.0d	3-May-28	5-May-28	79.0d
7838	WBS - Trash Room 6299/Mech Mezz. 6536 - INTF - Apron 5		111.0d	29-Dec-27	2-Jun-28	119.0d
7839	FN-AP5-SR-1050	Install Wall Insulation - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	29-Dec-27	5-Jan-28	13.0d
7840	FN-AP5-SR-1060	Hang Drywall Walls - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	2.0d	12-Jan-28	13-Jan-28	18.0d
7841	FN-AP5-SR-1070	Tape & Finish Walls - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	10.0d	12-Jan-28	25-Jan-28	75.0d
7842	FN-AP5-SR-1080	Prime & One Coat Walls - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	7.0d	26-Jan-28	3-Feb-28	75.0d
7843	FN-AP5-SR-1090	Install Ceiling Light Fixtures & Trim - Trash Room 6299/Mech Mezz. 6536 - INT...	10.0d	4-Feb-28	17-Feb-28	85.0d
7844	FN-AP5-SR-1100	Install Fire Protection Trim - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	3.0d	4-Feb-28	8-Feb-28	92.0d
7845	FN-AP5-SR-1110	Install Low Voltage Trim - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	4-Feb-28	10-Feb-28	85.0d
7846	FN-AP5-SR-1120	Install Doors - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	4-Feb-28	10-Feb-28	75.0d
7847	FN-AP5-SR-1140	Install Door Hardware - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	3.0d	11-Feb-28	15-Feb-28	176.0d
7848	FN-AP5-SR-1210	Install Ships Ladder & Handrail - Trash Room 6299/Mech Mezz. 6536 - INTF - ...	5.0d	11-Feb-28	17-Feb-28	75.0d
7849	FN-AP5-SR-1130	Install Fire Alarm Trim - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	18-Feb-28	24-Feb-28	75.0d
7850	FN-AP5-SR-1230	Install Mech. Trim - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	25-Feb-28	2-Mar-28	75.0d
7851	FN-AP5-SR-1150	Install Resinous Flooring & Base - Trash Room 6299/Mech Mezz. 6536 - INTF -...	10.0d	1-May-28	12-May-28	34.0d
7852	FN-AP5-SR-1170	Install Light Fixtures & Trim Walls - Trash Room 6299/Mech Mezz. 6536 - INTF...	5.0d	15-May-28	19-May-28	108.0d
7853	FN-AP5-SR-1180	Install Low Voltage Trim Walls - Trash Room 6299/Mech Mezz. 6536 - INTF - A...	5.0d	15-May-28	19-May-28	108.0d
7854	FN-AP5-SR-1270	Install BAS Trim Walls - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	5.0d	15-May-28	19-May-28	108.0d

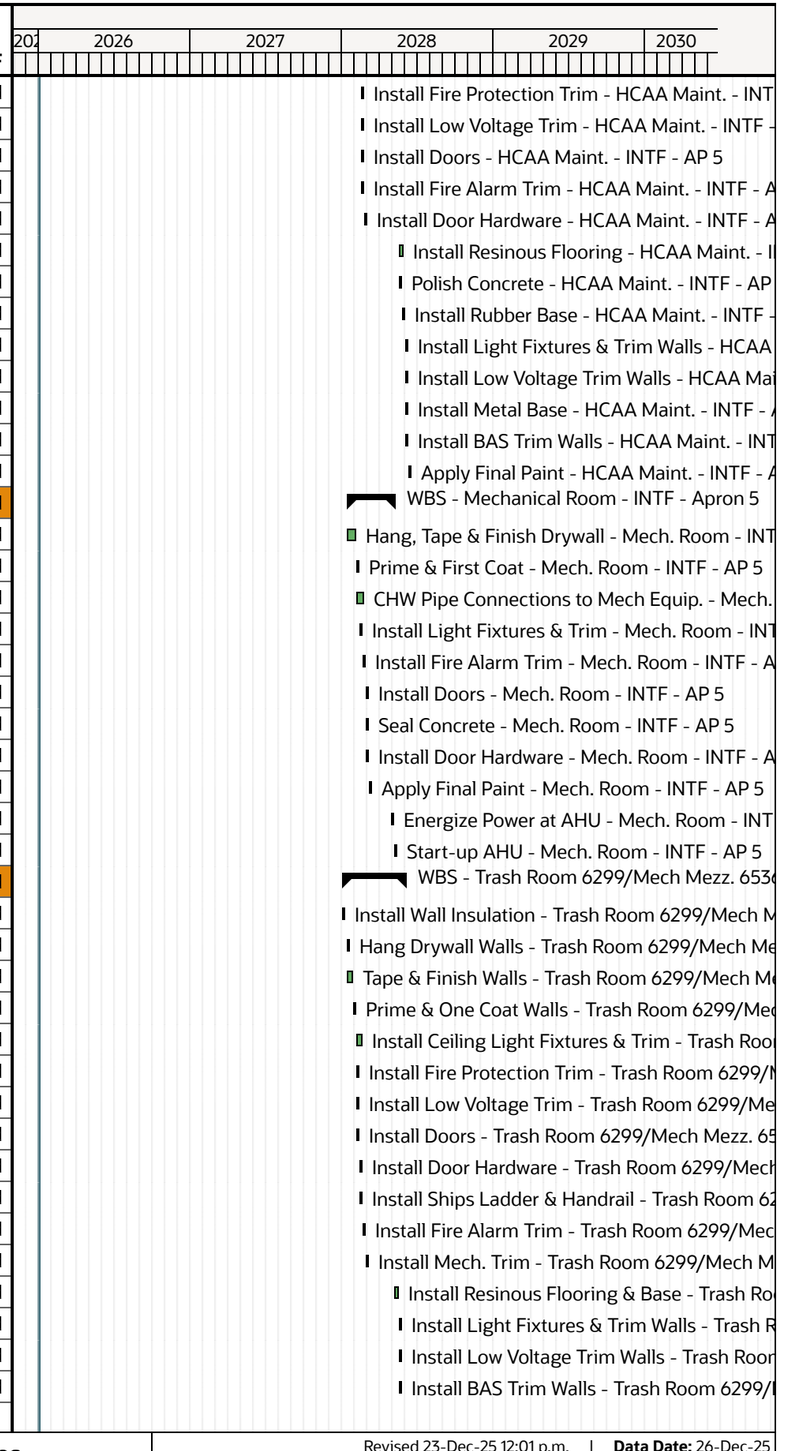


	ID	Name	Dur	Start	Finish	TF
7855	FN-AP5-SR-1220	Install Crash Rails & Corner Guards - Trash Room 6299/Mech Mezz. 6536 - INT...	2.0d	22-May-28	23-May-28	119.0d
7856	FN-AP5-SR-1190	Apply Final Paint - Trash Room 6299/Mech Mezz. 6536 - INTF - AP 5	7.0d	24-May-28	2-Jun-28	119.0d
7857	WBS - Baggage Storage 6157 - INTF - Apron 5		69.0d	14-Dec-27	21-Mar-28	171.0d
7858	FN-AP5-SR-570	Install Wall Insulation - Baggage Storage 6157 - INTF - AP 5	5.0d	14-Dec-27	20-Dec-27	13.0d
7859	FN-AP5-SR-580	Hang Drywall Walls - Baggage Storage 6157 - INTF - AP 5	2.0d	29-Dec-27	30-Dec-27	18.0d
7860	FN-AP5-SR-590	Hang Hard Lid Ceilings - Baggage Storage 6157 - INTF - AP 5	2.0d	3-Jan-28	4-Jan-28	18.0d
7861	FN-AP5-SR-600	Tape & Finish Walls - Baggage Storage 6157 - INTF - AP 5	10.0d	3-Jan-28	14-Jan-28	171.0d
7862	FN-AP5-SR-610	Tape & Finish Ceilings - Baggage Storage 6157 - INTF - AP 5	10.0d	5-Jan-28	18-Jan-28	176.0d
7863	FN-AP5-SR-620	Prime & One Coat Walls - Baggage Storage 6157 - INTF - AP 5	7.0d	17-Jan-28	25-Jan-28	171.0d
7864	FN-AP5-SR-640	Install Ceiling Light Fixtures & Trim - Baggage Storage 6157 - INTF - AP 5	10.0d	26-Jan-28	8-Feb-28	171.0d
7865	FN-AP5-SR-650	Install Fire Protection Trim - Baggage Storage 6157 - INTF - AP 5	3.0d	26-Jan-28	28-Jan-28	183.0d
7866	FN-AP5-SR-670	Install Doors - Baggage Storage 6157 - INTF - AP 5	5.0d	26-Jan-28	1-Feb-28	181.0d
7867	FN-AP5-SR-690	Install Door Hardware - Baggage Storage 6157 - INTF - AP 5	3.0d	2-Feb-28	4-Feb-28	183.0d
7868	FN-AP5-SR-770	Install Mech. Trim - HCAA Maint. - INTF - AP5	5.0d	2-Feb-28	8-Feb-28	181.0d
7869	FN-AP5-SR-660	Install Low Voltage Trim - Baggage Storage 6157 - INTF - AP 5	5.0d	9-Feb-28	15-Feb-28	171.0d
7870	FN-AP5-SR-680	Install Fire Alarm Trim - Baggage Storage 6157 - INTF - AP 5	5.0d	9-Feb-28	15-Feb-28	171.0d
7871	FN-AP5-SR-720	Install Light Fixtures & Trim Walls - Baggage Storage 6157 - INTF - AP 5	5.0d	9-Feb-28	15-Feb-28	176.0d
7872	FN-AP5-SR-730	Install Low Voltage Trim Walls - Baggage Storage 6157 - INTF - AP 5	5.0d	16-Feb-28	22-Feb-28	171.0d
7873	FN-AP5-SR-1250	Install BAS Trim Walls - Baggage Storage 6157 - INTF - AP 5	5.0d	16-Feb-28	22-Feb-28	171.0d
7874	FN-AP5-SR-700	Polish Concrete - Baggage Storage 6157 - INTF - AP 5	5.0d	23-Feb-28	29-Feb-28	171.0d
7875	FN-AP5-SR-710	Install Rubber Base - Baggage Storage 6157 - INTF - AP 5	5.0d	1-Mar-28	7-Mar-28	171.0d
7876	FN-AP5-SR-740	Apply Final Paint - Baggage Storage 6157 - INTF - AP 5	7.0d	8-Mar-28	16-Mar-28	171.0d
7877	FN-AP5-SR-760	Install Crash Rails & Corner Guards - Baggage Storage 6157 - INTF - AP 5	3.0d	17-Mar-28	21-Mar-28	171.0d
7878	WBS - Circulation 6148/FIS Exit Portal 6150 - INTF - Apron 5		229.0d	7-Dec-27	27-Oct-28	16.0d
7879	FN-AP5-SR-780	Install Wall Insulation - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	7-Dec-27	13-Dec-27	13.0d
7880	FN-AP5-SR-790	Hang Drywall Walls - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	14-Dec-27	20-Dec-27	18.0d
7881	FN-AP5-SR-800	Hang Hard Lid Ceilings - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	21-Dec-27	28-Dec-27	18.0d
7882	FN-AP5-SR-810	Tape & Finish Walls - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	10.0d	21-Dec-27	5-Jan-28	46.0d
7883	FN-AP5-SR-820	Tape & Finish Ceilings - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	10.0d	29-Dec-27	12-Jan-28	148.0d
7884	FN-AP5-SR-830	Prime & One Coat Walls - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	7.0d	6-Jan-28	14-Jan-28	46.0d
7885	FN-AP5-SR-990	Install ACT Ceiling Grid - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	17-Jan-28	21-Jan-28	46.0d
7886	FN-AP5-SR-860	Install Ceiling Light Fixtures & Trim - Circulation 6148/FIS Exit Portal 6150 - IN...	10.0d	17-Jan-28	28-Jan-28	146.0d
7887	FN-AP5-SR-870	Install Fire Protection Trim - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	3.0d	17-Jan-28	19-Jan-28	180.0d
7888	FN-AP5-SR-890	Install Doors - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	17-Jan-28	21-Jan-28	168.0d
7889	FN-AP5-SR-840	Install Light Fixtures & Trim Walls - Circulation 6148/FIS Exit Portal 6150 - INT...	5.0d	24-Jan-28	28-Jan-28	161.0d
7890	FN-AP5-SR-900	Install Door Hardware - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	3.0d	24-Jan-28	26-Jan-28	168.0d
7891	FN-AP5-SR-910	Install Mech. Trim - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	24-Jan-28	28-Jan-28	178.0d
7892	FN-AP5-SR-850	Install Low Voltage Trim Walls - Circulation 6148/FIS Exit Portal 6150 - INTF - ...	5.0d	31-Jan-28	4-Feb-28	161.0d
7893	FN-AP5-SR-880	Install Low Voltage Trim - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	31-Jan-28	4-Feb-28	146.0d
7894	FN-AP5-SR-930	Install Fire Alarm Trim - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	31-Jan-28	4-Feb-28	146.0d
7895	FN-AP5-SR-1260	Install BAS Trim Walls - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	31-Jan-28	4-Feb-28	161.0d
7896	FN-AP5-SR-920	Install Terrazzo Flooring at FIS/Circulation - Circulation 6148/FIS Exit Portal 61...	10.0d	9-Aug-28	22-Aug-28	16.0d

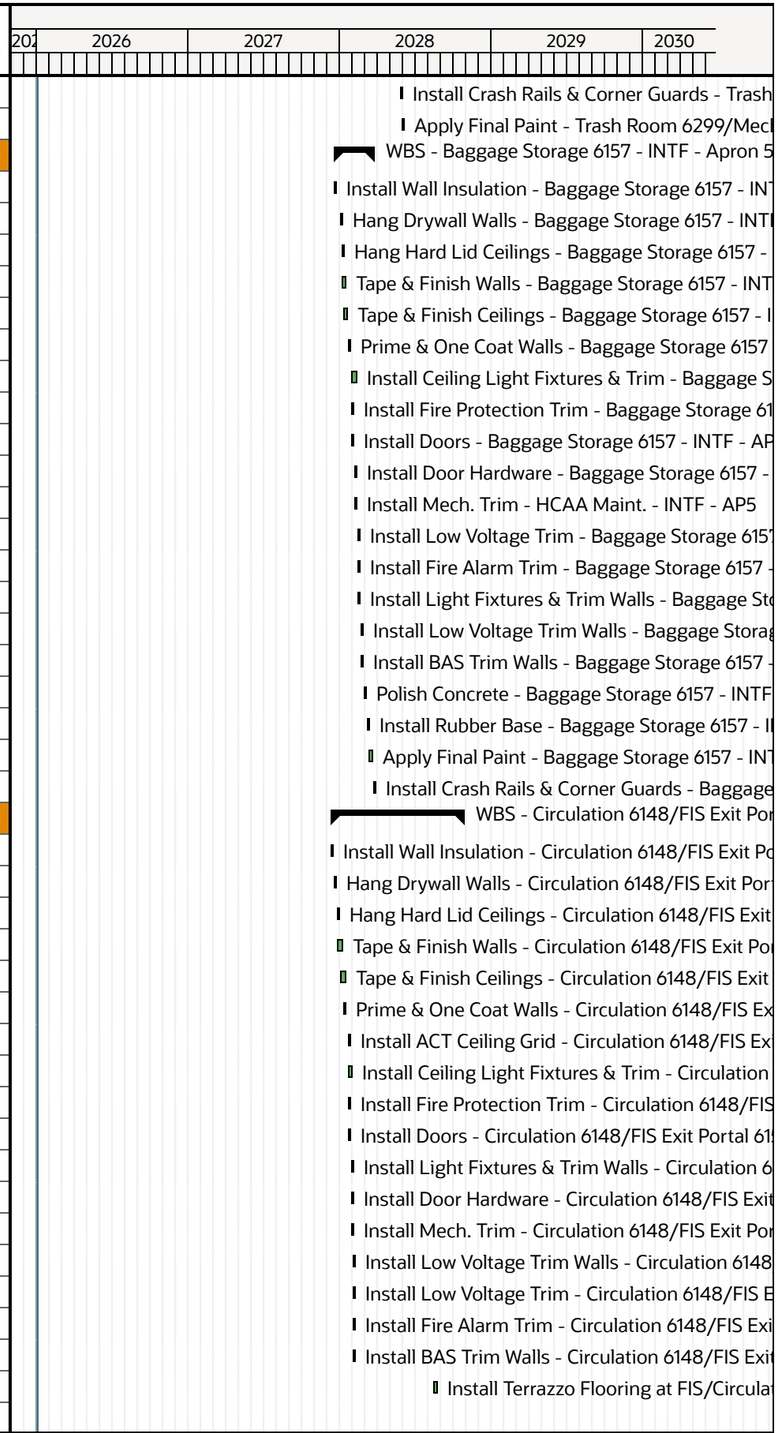


	ID	Name	Dur	Start	Finish	TF
7897	FN-AP5-SR-1020	Install Column Covers - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	10.0d	23-Aug-28	6-Sep-28	33.0d
7898	FN-AP5-SR-940	Install Rubber Base - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	23-Aug-28	29-Aug-28	16.0d
7899	FN-AP5-SR-1000	Install ACT Tiles - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	5.0d	23-Aug-28	29-Aug-28	16.0d
7900	FN-AP5-SR-950	Apply Final Paint - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	7.0d	30-Aug-28	8-Sep-28	16.0d
7901	FN-AP5-SR-980	Install Wall Tile (TL13 & TL21) - Circulation 6148/FIS Exit Portal 6150 - INTF - ...	7.0d	11-Sep-28	19-Sep-28	16.0d
7902	FN-AP5-SR-984	Install Millwork & Planter - Circulation 6148/FIS Exit Portals 6150 - INTF - AP 5	5.0d	11-Sep-28	15-Sep-28	31.0d
7903	FN-AP5-SR-960	Install Floor Mounted Bumper Rail - Circulation 6148/FIS Exit Portal 6150 - INT...	3.0d	20-Sep-28	22-Sep-28	16.0d
7904	FN-AP5-SR-1010	Install Interior Wall Panels - Baggage Storage 6157 - INTF - AP 5	10.0d	25-Sep-28	6-Oct-28	16.0d
7905	FN-AP5-SR-1030	Install FECs - Circulation 6148/FIS Exit Portal 6150 - INTF - AP 5	2.0d	25-Sep-28	26-Sep-28	39.0d
7906	FN-AP5-SR-1040	Install Signage - Baggage Storage 6157 - INTF - AP 5	5.0d	9-Oct-28	13-Oct-28	16.0d
7907	FN-AP5-SR-1280	Terrazzo Final Polish FIS/Circulation - Circulation 6148/FIS Exit Portal 6150 - I...	10.0d	16-Oct-28	27-Oct-28	16.0d
7908	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 6		367.0d	30-Apr-27	9-Oct-28	30.0d
7909	WBS - Overall - INTF - Apron 6		133.0d	3-Apr-28	9-Oct-28	30.0d
7910	FN-AP6-CR-10	Install Wall Insulation - Overall - INTF - AP 6	5.0d	3-Apr-28	7-Apr-28	0.0d
7911	FN-AP6-CR-20	Hang Drywall Walls - Overall - INTF - AP 6	5.0d	8-May-28	12-May-28	44.0d
7912	FN-AP6-CR-30	Tape & Finish Walls - Overall - INTF - AP 6	10.0d	15-May-28	26-May-28	44.0d
7913	FN-AP6-CR-190	Hang Drywall Ceilings - Overall - INTF - AP 6	5.0d	15-May-28	19-May-28	65.0d
7914	FN-AP6-CR-210	Tape & Finish Ceilings - Overall - INTF - AP 6	10.0d	22-May-28	5-Jun-28	65.0d
7915	FN-AP6-CR-40	Prime & One Coat Walls/Ceilings - Overall - INTF - AP 6	7.0d	30-May-28	7-Jun-28	44.0d
7916	FN-AP6-CR-70	Install ACT Ceiling Grid - Overall - INTF - AP 6	10.0d	21-Jun-28	5-Jul-28	35.0d
7917	FN-AP6-CR-50	Install Doors - Overall - INTF - AP 6	5.0d	21-Jun-28	27-Jun-28	44.0d
7918	FN-AP6-CR-140	Install Door Hardware - Overall - INTF - AP 6	5.0d	28-Jun-28	5-Jul-28	44.0d
7919	FN-AP6-CR-80	Install Diffusers - Overall - INTF - AP 6	5.0d	6-Jul-28	12-Jul-28	35.0d
7920	FN-AP6-CR-180	Install LTNG/Elec. Trim - Overall - INTF - AP 6	5.0d	6-Jul-28	12-Jul-28	44.0d
7921	FN-AP6-CR-100	Install Low Voltage Trim - Overall - INTF - AP 6	7.0d	13-Jul-28	21-Jul-28	35.0d
7922	FN-AP6-CR-170	Install Fire Alarm Trim - Overall - INTF - AP 6	5.0d	13-Jul-28	19-Jul-28	44.0d
7923	FN-AP6-CR-90	Install Fire Protection Trim - Overall - INTF - AP 6	3.0d	20-Jul-28	24-Jul-28	44.0d
7924	FN-AP6-CR-110	Drop Ceiling Tile - Overall - INTF - AP 6	10.0d	24-Jul-28	4-Aug-28	35.0d
7925	FN-AP6-CR-120	Install Light Fixtures & Trim Walls - Overall - INTF - AP 6	5.0d	7-Aug-28	11-Aug-28	35.0d
7926	FN-AP6-CR-200	Polish Exposed Concrete - Overall - INTF - AP 6	5.0d	14-Aug-28	18-Aug-28	35.0d
7927	FN-AP6-CR-60	Install Flooring & Base - Overall - INTF - AP 6	10.0d	28-Aug-28	11-Sep-28	25.0d
7928	FN-AP6-CR-150	Install Low Voltage Trim Walls - Overall - INTF - AP 6	5.0d	12-Sep-28	18-Sep-28	25.0d
7929	FN-AP6-CR-630	Install BAS Trim Walls - Overall - INTF - AP 6	5.0d	12-Sep-28	18-Sep-28	25.0d
7930	FN-AP6-CR-130	Apply Final Paint - Overall - INTF - AP 6	10.0d	19-Sep-28	2-Oct-28	30.0d
7931	FN-AP6-CR-160	Install Signage - Overall - INTF - AP 6	5.0d	3-Oct-28	9-Oct-28	30.0d
7932	WBS - Delta Airlines Operations #1 - INTF - Apron 6		33.0d	17-Apr-28	1-Jun-28	0.0d
7933	FN-AP6-O2-220	Install Wall Insulation - Delta Airlines Operations #1- INTF - AP 6	5.0d	17-Apr-28	21-Apr-28	0.0d
7934	FN-AP6-O2-230	Hang Drywall Walls - Delta Airlines Operations #1- INTF - AP 6	5.0d	8-May-28	12-May-28	0.0d
7935	FN-AP6-O2-240	Tape & Finish Walls - Delta Airlines Operations #1- INTF - AP 6	10.0d	15-May-28	26-May-28	0.0d
7936	FN-AP6-O2-450	Install Doors & Hardware - Delta Airlines Operations #1- INTF - AP 6	3.0d	30-May-28	1-Jun-28	0.0d
7937	WBS - Gang Bathroom #1 - INTF - Apron 6		265.0d	30-Apr-27	15-May-28	132.0d
7938	WBS - Men's Gang Bathroom #1 - INTF - Apron 6		244.0d	30-Apr-27	14-Apr-28	153.0d

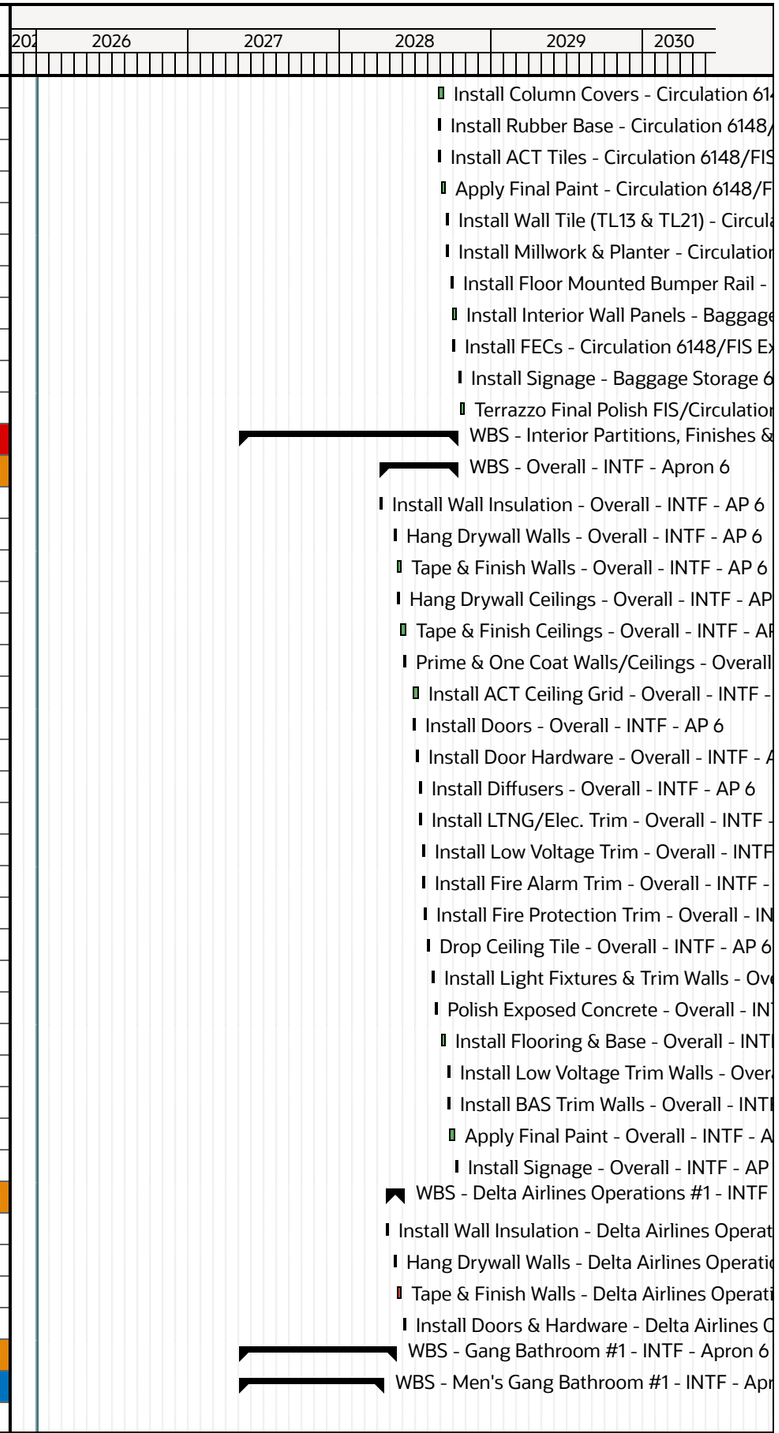

	ID	Name	Dur	Start	Finish	TF
7939	FN-AP6-R1-1830	Field Measure & Fab. Decorative Glass Panels - Men's Gang B/room #1 - INTF -...	70.0d	30-Apr-27	9-Aug-27	237.0d
7940	FN-AP6-R1-1620	Hang Drywall Lids & Walls - Men's Gang Bathroom #1 - INTR - AP 6	5.0d	25-Aug-27	31-Aug-27	136.0d
7941	FN-AP6-R1-1410	Tape & Finish Walls/Ceilings - Men's Gang B/room #1 - INTF - AP 6	10.0d	1-Sep-27	15-Sep-27	151.0d
7942	FN-AP6-R1-1840	Install Decorative Glass (GL01) - Men's Gang B/room #1 - INTF - AP 6	5.0d	1-Sep-27	8-Sep-27	221.0d
7943	FN-AP6-R1-1850	Install Vestibule Stone Cladding (ST01) - Men's Gang B/room #1 - INTF - AP 6	5.0d	9-Sep-27	15-Sep-27	221.0d
7944	FN-AP6-R1-1440	Prime & Paint Walls/Ceilings - Men's Gang B/room #1 - INTF - AP 6	5.0d	16-Sep-27	22-Sep-27	151.0d
7945	FN-AP6-R1-1420	Install Porcelain Floor Tile - Men's Gang B/room #1 - INTF - AP 6	15.0d	14-Oct-27	3-Nov-27	136.0d
7946	FN-AP6-R1-1430	Install Full Height Porcelain Wall Tile - Men's Gang B/room #1 - INTF - AP 6	15.0d	4-Nov-27	24-Nov-27	139.0d
7947	FN-AP6-R1-1470	Install Light Fixt. (Recessed & Cove LTNG, Sconces, Mirrors w/LTNG) & Trim - M...	7.0d	29-Nov-27	7-Dec-27	144.0d
7948	FN-AP6-R1-1460	Install Diffusers - Men's Gang B/room #1 - INTF - AP 6	3.0d	29-Nov-27	1-Dec-27	139.0d
7949	FN-AP6-R1-1490	Install Ceiling Speakers - Men's Gang B/room #1 - INTF - AP 6	5.0d	2-Dec-27	8-Dec-27	139.0d
7950	FN-AP6-R1-1790	Install Fire Alarm Trim - Men's Gang B/room #1 - INTF - AP 6	5.0d	2-Dec-27	8-Dec-27	140.0d
7951	FN-AP6-R1-1500	Install Fire Protection Trim - Men's Gang B/room #1 - INTF - AP 6	3.0d	10-Dec-27	14-Dec-27	139.0d
7952	FN-AP6-R1-1450	Set Restroom Vanities w/Quartz Finishes - Men's Gang B/room #1 - INTF - AP 6	5.0d	15-Dec-27	21-Dec-27	139.0d
7953	FN-AP6-R1-1480	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks - Men's Ga...	5.0d	22-Dec-27	29-Dec-27	139.0d
7954	FN-AP6-R1-1520	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - ...	5.0d	30-Dec-27	6-Jan-28	139.0d
7955	FN-AP6-R1-1530	Install Restroom Toilet Acc. (Grab Bars, Toilet Tissue Dispensers, Bag/Purse Ho...	5.0d	7-Jan-28	13-Jan-28	139.0d
7956	FN-AP6-R1-1510	Apply Final Paint - Men's Gang B/room #1 - INTF - AP 6	5.0d	14-Jan-28	20-Jan-28	139.0d
7957	FN-AP6-R1-1810	Install Signage & Dimensional Text - Men's Gang B/room #1 - INTF - AP 6	5.0d	6-Apr-28	12-Apr-28	85.0d
7958	FN-AP6-R1-1540	Install Wall Art - Men's Gang B/room #1 - INTF - AP 6	2.0d	13-Apr-28	14-Apr-28	153.0d
7959	WBS - Women's Gang Bathroom #1 - INTF - Apron 6		265.0d	30-Apr-27	15-May-28	132.0d
7960	FN-AP6-R1-1860	Field Measure & Fab. Decorative Glass Panels - Women's Gang B/room #1 - IN...	70.0d	30-Apr-27	9-Aug-27	258.0d
7961	FN-AP6-R1-1780	Hang Drywall Lids & Walls - Women's Gang B/room #1 - INTR - AP 6	5.0d	25-Aug-27	31-Aug-27	136.0d
7962	FN-AP6-R1-1550	Tape & Finish Walls/Ceilings - Women's Gang B/room #1 - INTF - AP 6	10.0d	1-Sep-27	15-Sep-27	166.0d
7963	FN-AP6-R1-1580	Prime & Paint Walls/Ceilings- Women's Gang B/room #1 - INTF - AP 6	5.0d	16-Sep-27	22-Sep-27	166.0d
7964	FN-AP6-R1-1560	Install Porcelain Floor Tile- Women's Gang B/room #1 - INTF - AP 6	15.0d	4-Nov-27	24-Nov-27	136.0d
7965	FN-AP6-R1-1570	Install Full Height Porcelain Wall Tile- Women's Gang B/room #1 - INTF - AP 6	15.0d	29-Nov-27	17-Dec-27	136.0d
7966	FN-AP6-R1-1600	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG)...	7.0d	20-Dec-27	29-Dec-27	150.0d
7967	FN-AP6-R1-1626	Install Diffusers- Women's Gang B/room #1 - INTF - AP 6	3.0d	20-Dec-27	22-Dec-27	136.0d
7968	FN-AP6-R1-1590	Set Restroom Vanities w/Quartz Finishes- Women's Gang B/room #1 - INTF - ...	5.0d	23-Dec-27	30-Dec-27	136.0d
7969	FN-AP6-R1-1610	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks- Women's ...	5.0d	3-Jan-28	7-Jan-28	136.0d
7970	FN-AP6-R1-1630	Install Ceiling Speakers - Women's Gang B/room #1 - INTF - AP 6	5.0d	10-Jan-28	14-Jan-28	136.0d
7971	FN-AP6-R1-1800	Install Fire Alarm Trim - Women's Gang B/room #1 - INTF - AP 6	5.0d	10-Jan-28	14-Jan-28	136.0d
7972	FN-AP6-R1-1640	Install Fire Protection Trim- Women's Gang B/room #1 - INTF - AP 6	3.0d	17-Jan-28	19-Jan-28	136.0d
7973	FN-AP6-R1-1660	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions- W...	5.0d	20-Jan-28	26-Jan-28	136.0d
7974	FN-AP6-R1-1670	Install Restroom Toilet Acc. (Grab Bars, Toilet Tissue Dispensers, Bag/Purse Ho...	5.0d	27-Jan-28	2-Feb-28	136.0d
7975	FN-AP6-R1-1870	Install Decorative Glass (GL01) - Women's Gang B/room #1 - INTF - AP 6	5.0d	3-Feb-28	9-Feb-28	136.0d
7976	FN-AP6-R1-1880	Install Vestibule Stone Cladding (ST01) - Women's Gang B/room #1 - INTF - AP 6	5.0d	10-Feb-28	16-Feb-28	136.0d
7977	FN-AP6-R1-1650	Apply Final Paint- Women's Gang B/room #1 - INTF - AP 6	5.0d	17-Feb-28	23-Feb-28	136.0d
7978	FN-AP6-R1-1820	Install Signage & Dimensional Text - Women's Gang B/room #1 - INTF - AP 6	5.0d	5-May-28	11-May-28	85.0d
7979	FN-AP6-R1-1680	Install Wall Art- Women's Gang B/room #1 - INTF - AP 6	2.0d	12-May-28	15-May-28	132.0d
7980	WBS - Mechanical Room 6191 - INTF - Apron 6		123.0d	2-Feb-28	25-Jul-28	83.0d

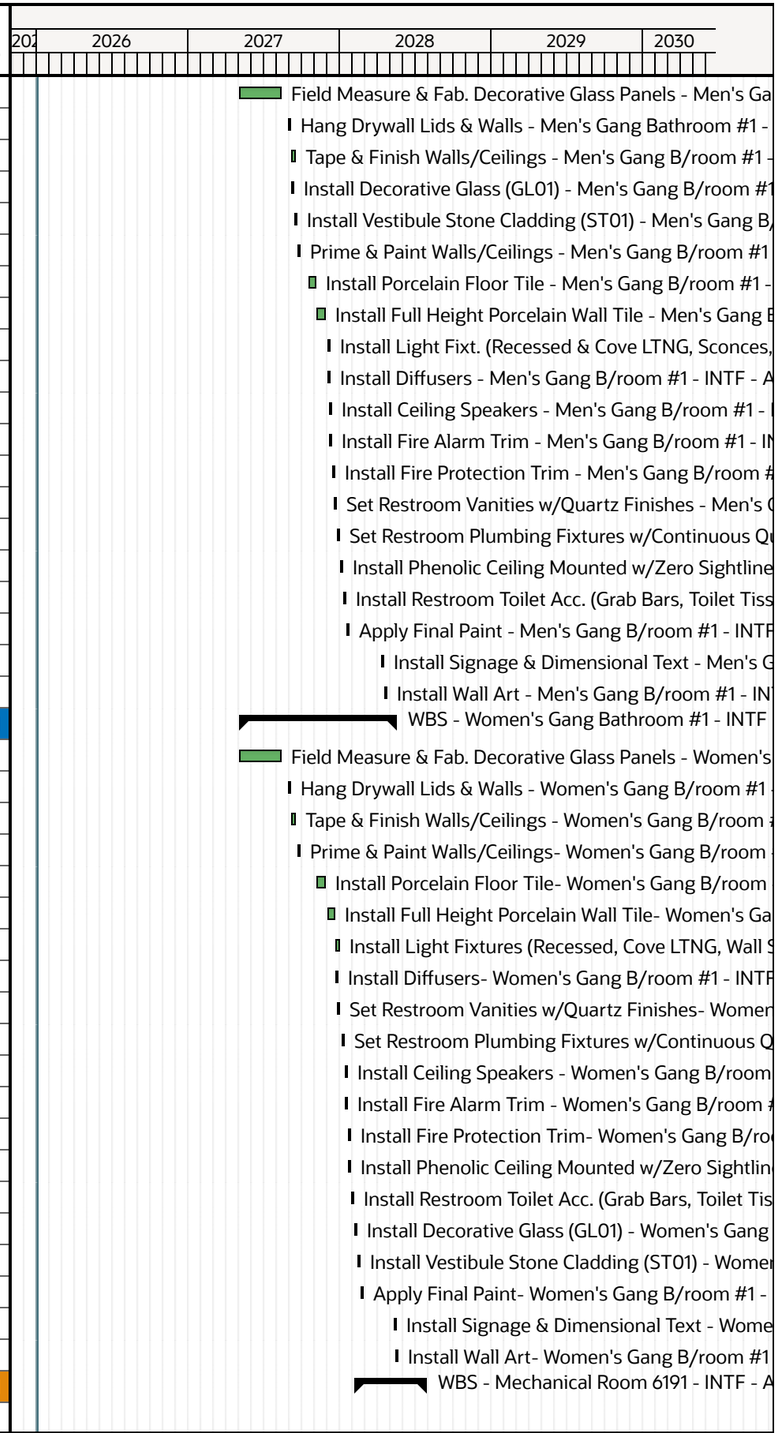


	ID	Name	Dur	Start	Finish	TF
7981	FN-AP6-MR-1400	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - AP 6	15.0d	2-Feb-28	22-Feb-28	121.0d
7982	FN-AP6-MR-1310	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 6	15.0d	17-May-28	7-Jun-28	81.0d
7983	FN-AP6-MR-1380	Set Floor Drains - Mech. Room - INTF - AP 6	3.0d	17-May-28	19-May-28	83.0d
7984	FN-AP6-MR-1320	Prime & First Coat - Mech. Room - INTF - AP 6	5.0d	8-Jun-28	14-Jun-28	81.0d
7985	FN-AP6-MR-1330	Install Light Fixtures & Trim - Mech. Room - INTF - AP 6	5.0d	15-Jun-28	21-Jun-28	81.0d
7986	FN-AP6-MR-1350	Install Doors - Mech. Room - INTF - AP 6	2.0d	15-Jun-28	16-Jun-28	82.0d
7987	FN-AP6-MR-1370	Install Door Hardware - Mech. Room - INTF - AP 6	2.0d	19-Jun-28	20-Jun-28	82.0d
7988	FN-AP6-MR-1440	Install Fire Alarm Trim - Mech. Room - INTF - AP 6	5.0d	22-Jun-28	28-Jun-28	81.0d
7989	FN-AP6-MR-1360	Seal Concrete - Mech. Room - INTF - AP 6	5.0d	29-Jun-28	6-Jul-28	91.0d
7990	FN-AP6-MR-1340	Apply Final Paint - Mech. Room - INTF - AP 6	5.0d	7-Jul-28	13-Jul-28	91.0d
7991	FN-AP6-MR-1410	Energize Power at AHU - Mech. Room - INTF - AP 6	5.0d	14-Jul-28	20-Jul-28	16.0d
7992	FN-AP6-MR-1420	Start-up AHU - Mech. Room - INTF - AP 6	3.0d	21-Jul-28	25-Jul-28	16.0d
7993	WBS - Electrical Rooms 6200 & 6175 - INTF - Apron 6		144.0d	19-Jan-28	9-Aug-28	72.0d
7994	WBS - Electrical Room 6200 - INTF - Apron 6		129.0d	19-Jan-28	19-Jul-28	87.0d
7995	FN-AP6-ER-2540	Hang, Tape & Finish Drywall - Elec. Room 6200 - INTRF - AP 6	15.0d	19-Jan-28	8-Feb-28	0.0d
7996	FN-AP6-ER-2550	Prime & First Coat - Elec. Room 6200 - INTRF - AP 6	5.0d	9-Feb-28	15-Feb-28	0.0d
7997	FN-AP6-ER-2570	Set Elec. Switchgear & Equip. - Elec. Room 6200 - INTRF - AP 6	10.0d	16-Feb-28	29-Feb-28	0.0d
7998	FN-AP6-ER-2640	Install Door & Hardware - Elec. Room 6200 - INTRF - AP 6	2.0d	16-Feb-28	17-Feb-28	174.0d
7999	RI-AP6-ER-2600	Install Elec. OH Rough-in - Elec. Room 6200 - INTRF - AP 6	20.0d	1-Mar-28	28-Mar-28	0.0d
8000	FN-AP6-ER-2580	Install Elec. Panels & Transformers - Elec. Room 6200 - INTRF - AP 6	15.0d	29-Mar-28	18-Apr-28	0.0d
8001	FN-AP6-ER-2590	Elec. Feeder Wire Measurements & Procurement - Elec. Room 6200 - INTRF - A...	10.0d	19-Apr-28	2-May-28	0.0d
8002	FN-AP6-ER-2600	Pull & Terminate Elec. - Elec. Room 6200 - INTRF - AP 6	20.0d	3-May-28	31-May-28	0.0d
8003	FN-AP6-ER-2610	Third Party Elec. Testing - Elec. Room 6200 - INTRF - AP 6	3.0d	1-Jun-28	5-Jun-28	0.0d
8004	FN-AP6-ER-2620	Install Light Fixtures & Trim - Elec. Room 6200 - INTRF - AP 6	10.0d	6-Jun-28	19-Jun-28	0.0d
8005	FN-AP6-ER-2650	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Elec. Room ...	2.0d	20-Jun-28	21-Jun-28	0.0d
8006	FN-AP6-ER-2690	Seal Concrete - Elec. Room 6200 - INTRF - AP 6	5.0d	20-Jun-28	26-Jun-28	93.0d
8007	FN-AP6-ER-2660	APG QC Procedure for Perm Power Available for Dist. - Elec. Room 6200 - INTR...	15.0d	22-Jun-28	13-Jul-28	0.0d
8008	FN-AP6-ER-2860	Install Rubber Base - Elec. Room 6200 - INTRF - AP 6	5.0d	27-Jun-28	3-Jul-28	93.0d
8009	FN-AP6-ER-2630	Apply Final Paint - Elec. Room 6200 - INTRF - AP 6	5.0d	5-Jul-28	11-Jul-28	93.0d
8010	FN-AP6-ER-2870	Final Checkout & Panel Startup - Elec. Room 6200 - INTRF - AP 6	2.0d	14-Jul-28	17-Jul-28	52.0d
8011	FN-AP6-ER-2880	Energize Equip. - Elec Room 6200 - INTRF - AP 6	2.0d	18-Jul-28	19-Jul-28	52.0d
8012	WBS - Electrical Room 6175 - INTF - Apron 6		129.0d	9-Feb-28	9-Aug-28	72.0d
8013	FN-AP6-ER-2700	Hang, Tape & Finish Drywall - Elec. Room CBP 6175 - INTRF - AP 6	15.0d	9-Feb-28	29-Feb-28	16.0d
8014	FN-AP6-ER-2710	Prime & First Coat - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	1-Mar-28	7-Mar-28	16.0d
8015	FN-AP6-ER-2730	Set Elec. Switchgear & Equip. - Elec. Room CBP 6175 - INTRF - AP 6	10.0d	8-Mar-28	21-Mar-28	16.0d
8016	FN-AP6-ER-2800	Install Door & Hardware - Elec. Room CBP 6175 - INTRF - AP 6	2.0d	8-Mar-28	9-Mar-28	102.0d
8017	RI-AP6-ER-2750	Install Elec. OH Rough-in - Elec. Room CBP 6175 - INTRF - AP 6	20.0d	22-Mar-28	18-Apr-28	16.0d
8018	FN-AP6-ER-2740	Install Elec. Panels & Transformers - Elec. Room CBP 6175 - INTRF - AP 6	20.0d	19-Apr-28	16-May-28	16.0d
8019	FN-AP6-ER-2750	Elec. Feeder Wire Measurements & Procurement - Elec. Room CBP 6175 - INTR...	10.0d	17-May-28	31-May-28	16.0d
8020	FN-AP6-ER-2760	Pull & Terminate Elec. - Elec. Room CBP 6175 - INTRF - AP 6	15.0d	1-Jun-28	21-Jun-28	16.0d
8021	FN-AP6-ER-2770	Third Party Elec. Testing - Elec. Room CBP 6175 - INTRF - AP 6	3.0d	22-Jun-28	26-Jun-28	16.0d
8022	FN-AP6-ER-2780	Install Light Fixtures & Trim - Elec. Room CBP 6175 - INTRF - AP 6	10.0d	27-Jun-28	11-Jul-28	16.0d

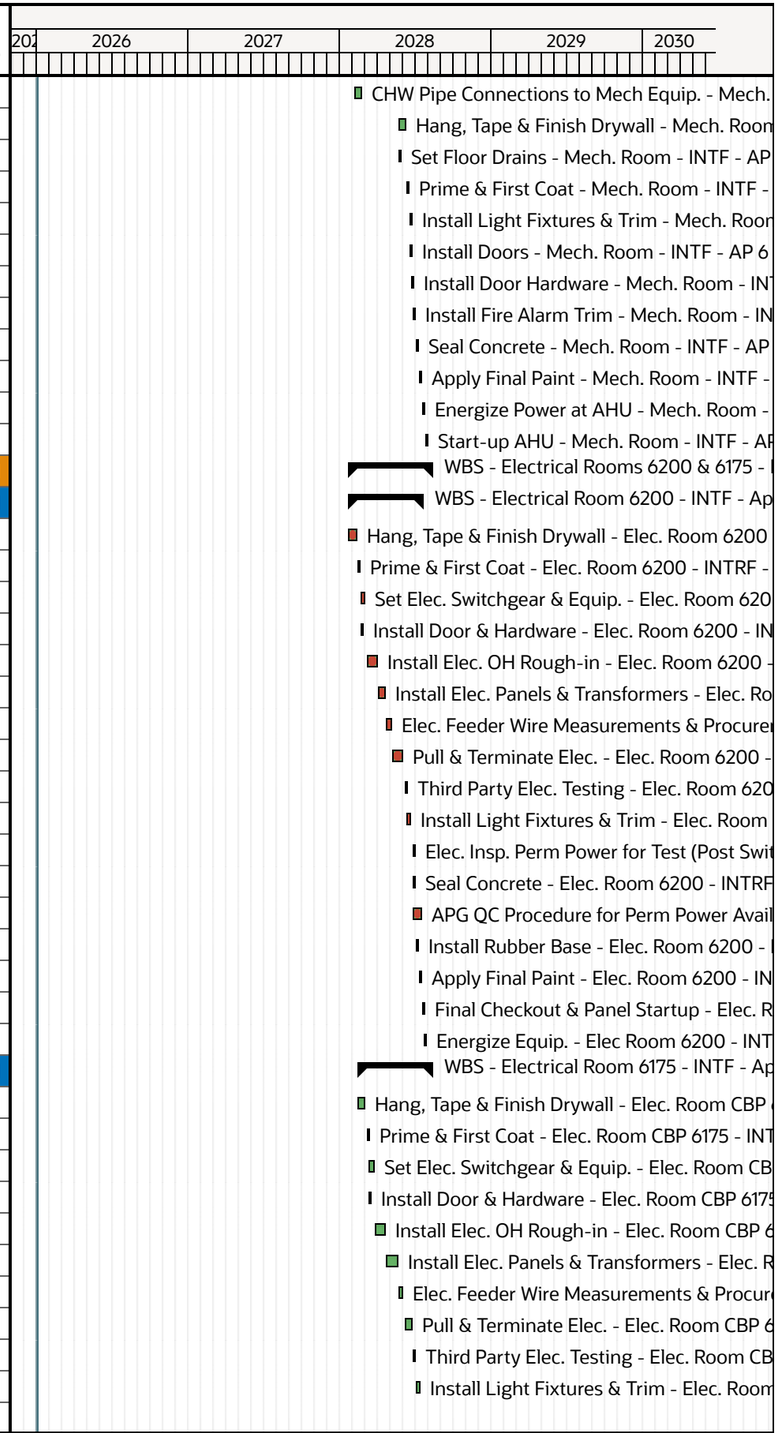

	ID	Name	Dur	Start	Finish	TF
8023	FN-AP6-ER-2810	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Elec. Room ...	2.0d	12-Jul-28	13-Jul-28	16.0d
8024	FN-AP6-ER-2850	Seal Concrete - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	12-Jul-28	18-Jul-28	78.0d
8025	FN-AP6-ER-2820	APG QC Procedure for Perm Power Available for Dist. - Elec. Room CBP 6175 - I...	15.0d	14-Jul-28	3-Aug-28	16.0d
8026	FN-AP6-ER-2890	Install Rubber Base - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	19-Jul-28	25-Jul-28	78.0d
8027	FN-AP6-ER-2790	Apply Final Paint - Elec. Room CBP 6175 - INTRF - AP 6	5.0d	26-Jul-28	1-Aug-28	78.0d
8028	FN-AP6-ER-740	Final Checkout & Panel Startup - Elec. Room CBP 6175 - INTRF - AP 6	2.0d	4-Aug-28	7-Aug-28	26.0d
8029	FN-AP6-ER-750	Energize Equip. - Elec Room CBP 6175 - INTRF - AP 6	2.0d	8-Aug-28	9-Aug-28	26.0d
8030	WBS - CBP Secondary - INTF - Apron 6		123.0d	10-Apr-28	2-Oct-28	6.0d
8031	FN-AP6-CR-220	Install Wall Insulation - CBP Secondary - INTF - AP 6	5.0d	10-Apr-28	14-Apr-28	0.0d
8032	FN-AP6-CR-230	Hang Drywall Walls - CBP Secondary - INTF - AP 6	5.0d	28-Apr-28	4-May-28	1.0d
8033	FN-AP6-CR-240	Tape & Finish Walls - CBP Secondary - INTF - AP 6	10.0d	5-May-28	18-May-28	16.0d
8034	FN-AP6-CR-250	Hang Drywall Ceilings - CBP Secondary - INTF - AP 6	5.0d	5-May-28	11-May-28	1.0d
8035	FN-AP6-CR-260	Tape & Finish Ceilings - CBP Secondary - INTF - AP 6	10.0d	12-May-28	25-May-28	42.0d
8036	FN-AP6-CR-270	Prime & One Coat Walls/Ceilings - CBP Secondary - INTF - AP 6	7.0d	19-May-28	30-May-28	16.0d
8037	FN-AP6-CR-280	Install ACT Ceiling Grid - CBP Secondary - INTF - AP 6	15.0d	31-May-28	20-Jun-28	16.0d
8038	FN-AP6-CR-290	Install Doors - CBP Secondary - INTF - AP 6	5.0d	31-May-28	6-Jun-28	30.0d
8039	FN-AP6-CR-300	Install Door Hardware - CBP Secondary - INTF - AP 6	5.0d	7-Jun-28	13-Jun-28	30.0d
8040	FN-AP6-CR-310	Install Diffusers - CBP Secondary - INTF - AP 6	5.0d	21-Jun-28	27-Jun-28	16.0d
8041	FN-AP6-CR-320	Install LTNG/Elec. Trim - CBP Secondary - INTF - AP 6	5.0d	21-Jun-28	27-Jun-28	25.0d
8042	FN-AP6-CR-330	Install Low Voltage Trim - CBP Secondary - INTF - AP 6	7.0d	28-Jun-28	7-Jul-28	16.0d
8043	FN-AP6-CR-340	Install Fire Alarm Trim - CBP Secondary - INTF - AP 6	5.0d	28-Jun-28	5-Jul-28	25.0d
8044	FN-AP6-CR-350	Install Fire Protection Trim - CBP Secondary - INTF - AP 6	3.0d	6-Jul-28	10-Jul-28	25.0d
8045	FN-AP6-CR-360	Drop Ceiling Tile - CBP Secondary - INTF - AP 6	10.0d	10-Jul-28	21-Jul-28	16.0d
8046	FN-AP6-CR-370	Install Light Fixtures & Trim Walls - CBP Secondary - INTF - AP 6	5.0d	24-Jul-28	28-Jul-28	16.0d
8047	FN-AP6-CR-380	Install Flooring & Base - CBP Secondary - INTF - AP 6	10.0d	14-Aug-28	25-Aug-28	6.0d
8048	FN-AP6-CR-390	Polish Exposed Concrete - CBP Secondary - INTF - AP 6	5.0d	28-Aug-28	1-Sep-28	6.0d
8049	FN-AP6-CR-400	Install Low Voltage Trim Walls - CBP Secondary - INTF - AP 6	5.0d	5-Sep-28	11-Sep-28	6.0d
8050	FN-AP6-CR-640	Install BAS Trim Walls - CBP Secondary - INTF - AP 6	5.0d	5-Sep-28	11-Sep-28	6.0d
8051	FN-AP6-CR-410	Apply Final Paint - CBP Secondary - INTF - AP 6	10.0d	12-Sep-28	25-Sep-28	6.0d
8052	FN-AP6-CR-420	Install Signage - CBP Secondary - INTF - AP 6	5.0d	26-Sep-28	2-Oct-28	6.0d
8053	WBS - Exit Passageway 6195 - INTF - Apron 6		67.0d	24-Apr-28	27-Jul-28	81.0d
8054	FN-AP6-CR-440	Install Wall Insulation - Exit Passageway 6195 - INTF - AP 6	5.0d	24-Apr-28	28-Apr-28	0.0d
8055	FN-AP6-CR-450	Hang Drywall Walls - Exit Passageway 6195 - INTF - AP 6	5.0d	1-May-28	5-May-28	0.0d
8056	FN-AP6-CR-460	Tape & Finish Walls - Exit Passageway 6195 - INTF - AP 6	10.0d	8-May-28	19-May-28	86.0d
8057	FN-AP6-CR-470	Hang Drywall Ceilings - Exit Passageway 6195 - INTF - AP 6	5.0d	8-May-28	12-May-28	0.0d
8058	FN-AP6-CR-480	Tape & Finish Ceilings - Exit Passageway 6195 - INTF - AP 6	10.0d	15-May-28	26-May-28	81.0d
8059	FN-AP6-CR-490	Prime & One Coat Walls/Ceilings - Exit Passageway 6195 - INTF - AP 6	7.0d	30-May-28	7-Jun-28	81.0d
8060	FN-AP6-CR-500	Install Doors - Exit Passageway 6195 - INTF - AP 6	5.0d	8-Jun-28	14-Jun-28	86.0d
8061	FN-AP6-CR-520	Install Diffusers - Exit Passageway 6195 - INTF - AP 6	5.0d	8-Jun-28	14-Jun-28	81.0d
8062	FN-AP6-CR-530	Install LTNG/Elec. Trim - Exit Passageway 6195 - INTF - AP 6	5.0d	8-Jun-28	14-Jun-28	81.0d
8063	FN-AP6-CR-510	Install Door Hardware - Exit Passageway 6195 - INTF - AP 6	5.0d	15-Jun-28	21-Jun-28	86.0d
8064	FN-AP6-CR-540	Install Low Voltage Trim - Exit Passageway 6195 - INTF - AP 6	7.0d	15-Jun-28	23-Jun-28	81.0d




	ID	Name	Dur	Start	Finish	TF
8065	FN-AP6-CR-550	Install Fire Alarm Trim - Exit Passageway 6195 - INTF - AP 6	5.0d	15-Jun-28	21-Jun-28	81.0d
8066	FN-AP6-CR-560	Install Fire Protection Trim - Exit Passageway 6195 - INTF - AP 6	3.0d	22-Jun-28	26-Jun-28	81.0d
8067	FN-AP6-CR-570	Seal Concrete - Exit Passageway 6195 - INTF - AP 6	5.0d	27-Jun-28	3-Jul-28	81.0d
8068	FN-AP6-CR-610	Install Rubber Base - Exit Passageway 6195 - INTF - AP 6	2.0d	5-Jul-28	6-Jul-28	81.0d
8069	FN-AP6-CR-620	Install Base - Exit Passageway 6195 - INTF - AP 6	5.0d	5-Jul-28	11-Jul-28	88.0d
8070	FN-AP6-CR-580	Apply Final Paint - Exit Passageway 6195 - INTF - AP 6	10.0d	7-Jul-28	20-Jul-28	81.0d
8071	FN-AP6-CR-600	Install FECs - Exit Passageway 6195 - INTF - AP 6	2.0d	21-Jul-28	24-Jul-28	84.0d
8072	FN-AP6-CR-590	Install Signage - Exit Passageway 6195 - INTF - AP 6	5.0d	21-Jul-28	27-Jul-28	81.0d
8073	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Apron 7		281.0d	25-Aug-27	2-Oct-28	35.0d
8074	WBS - Mechanical Room 6190 - INTF - Apron 7		51.0d	28-Dec-27	8-Mar-28	180.0d
8075	FN-AP7-MR-430	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 7	15.0d	28-Dec-27	18-Jan-28	0.0d
8076	FN-AP7-MR-440	Prime & First Coat - Mech. Room - INTF - AP 7	5.0d	19-Jan-28	25-Jan-28	116.0d
8077	FN-AP7-MR-460	Install Light Fixtures & Trim - Mech. Room - INTF - AP 7	5.0d	26-Jan-28	1-Feb-28	116.0d
8078	FN-AP7-MR-450	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - AP 7	15.0d	2-Feb-28	22-Feb-28	119.0d
8079	FN-AP7-MR-480	Install Doors - Mech. Room - INTF - AP 7	5.0d	2-Feb-28	8-Feb-28	116.0d
8080	FN-AP7-MR-500	Install Door Hardware - Mech. Room - INTF - AP 7	5.0d	9-Feb-28	15-Feb-28	116.0d
8081	FN-AP7-MR-2540	Energize Power at AHU Disconnect - Mech. Room - INTF - AP 7	5.0d	15-Feb-28	21-Feb-28	120.0d
8082	FN-AP7-MR-490	Seal Concrete - Mech. Room - INTF - AP 7	5.0d	16-Feb-28	22-Feb-28	116.0d
8083	FN-AP7-MR-2550	Set Floor Drains - Mech. Room - INTF - AP 7	3.0d	23-Feb-28	25-Feb-28	116.0d
8084	FN-AP7-MR-515	Start-up AHU - Mech. Room - INTF - AP 7	3.0d	28-Feb-28	1-Mar-28	116.0d
8085	FN-AP7-MR-470	Apply Final Paint - Mech. Room - INTF - AP 7	5.0d	2-Mar-28	8-Mar-28	180.0d
8086	WBS - CBP Secondary Processing - INTF - Apron 7		128.0d	13-Mar-28	11-Sep-28	21.0d
8087	FN-AP7-SD-1150	Install Wall Insulation - CBP Second. - INTF - AP 7	5.0d	13-Mar-28	17-Mar-28	0.0d
8088	FN-AP7-SD-1170	Hang Drywall Walls - CBP Second. - INTF - AP 7	5.0d	20-Mar-28	24-Mar-28	10.0d
8089	FN-AP7-SD-1190	Tape & Finish Walls - CBP Second. - INTF - AP 7	10.0d	20-Mar-28	31-Mar-28	30.0d
8090	FN-AP7-SD-1210	Prime & One Coat Walls - CBP Second. - INTF - AP 7	7.0d	3-Apr-28	11-Apr-28	30.0d
8091	FN-AP7-SD-1140	Insulate Ceilings & Soffits - CBP Second. - INTF - AP 7	7.0d	5-Apr-28	13-Apr-28	1.0d
8092	FN-AP7-SD-1160	Hang Hard Lid Ceilings - CBP Second. - INTF - AP 7	5.0d	14-Apr-28	20-Apr-28	1.0d
8093	FN-AP7-SD-1180	Tape & Finish Ceilings - CBP Second. - INTF - AP 7	10.0d	21-Apr-28	4-May-28	6.0d
8094	FN-AP7-SD-1200	Apply Prime, First, Paint Ceilings - CBP Second. - INTF - AP 7	7.0d	5-May-28	15-May-28	6.0d
8095	FN-AP7-SD-1230	Install ACT Ceiling Grid - CBP Second. - INTF - AP 7	10.0d	16-May-28	30-May-28	6.0d
8096	FN-AP7-SD-1240	Install Doors - CBP Second. - INTF - AP 7	5.0d	16-May-28	22-May-28	78.0d
8097	FN-AP7-SD-1370	Install Door Hardware - CBP Second. - INTF - AP 7	5.0d	23-May-28	30-May-28	78.0d
8098	FN-AP7-SD-1250	Install Ceiling Light Fixtures & Trim - CBP Second. - INTF - AP 7	10.0d	31-May-28	13-Jun-28	6.0d
8099	FN-AP7-SD-1260	Install Diffusers - CBP Second. - INTF - AP 7	5.0d	31-May-28	6-Jun-28	18.0d
8100	FN-AP7-SD-1270	Install Low Voltage Trim - CBP Second. - INTF - AP 7	7.0d	14-Jun-28	22-Jun-28	6.0d
8101	FN-AP7-SD-1410	Install Fire Alarm Trim - CBP Second. - INTF - AP 7	5.0d	14-Jun-28	20-Jun-28	10.0d
8102	FN-AP7-SD-1280	Install Fire Protection Trim - CBP Second. - INTF - AP 7	3.0d	21-Jun-28	23-Jun-28	10.0d
8103	FN-AP7-SD-1290	Drop Ceiling Tile - CBP Second. - INTF - AP 7	5.0d	23-Jun-28	29-Jun-28	6.0d
8104	FN-AP7-SD-1320	Install Access Floors - CBP Second. - INTF - AP 7	20.0d	30-Jun-28	28-Jul-28	6.0d
8105	FN-AP7-SD-1330	Install Column Covers - CBP Second. - INTF - AP 7	10.0d	31-Jul-28	11-Aug-28	21.0d
8106	FN-AP7-SD-1350	Install Interior Specialties/Mounting Brackets/OFOI - CBP Second. - INTF - AP 7	10.0d	14-Aug-28	25-Aug-28	21.0d

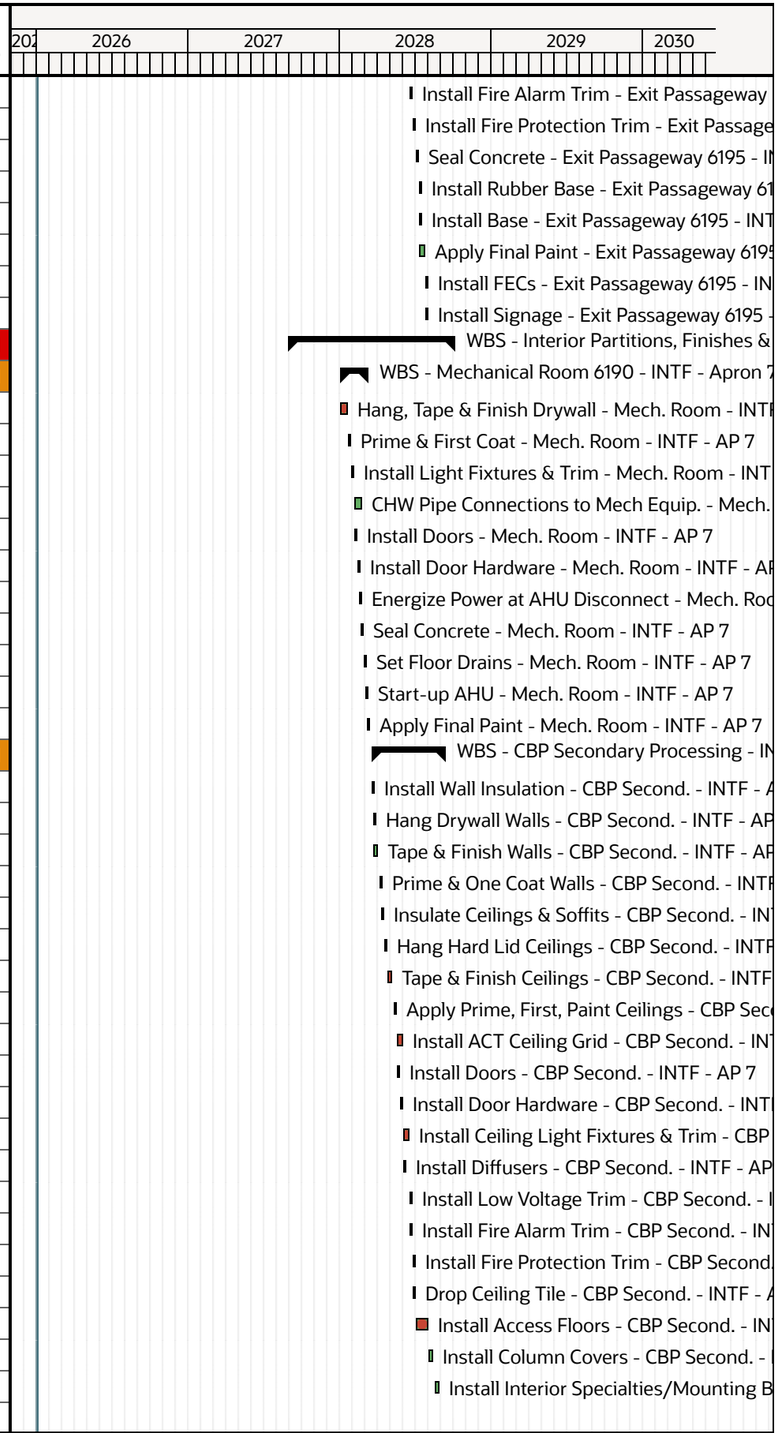

	ID	Name	Dur	Start	Finish	TF
8107	FN-AP7-SD-1360	Install Light Fixtures & Trim Walls/Columns - CBP Second. - INTF - AP 7	5.0d	14-Aug-28	18-Aug-28	31.0d
8108	FN-AP7-SD-1390	Install Low Voltage Trim Walls/Columns - CBP Second. - INTF - AP 7	5.0d	14-Aug-28	18-Aug-28	21.0d
8109	FN-AP7-SD-1420	Install BAS Trim Walls/Columns - CBP Second. - INTF - AP 7	5.0d	14-Aug-28	18-Aug-28	21.0d
8110	FN-AP7-SD-1340	Apply Final Paint - CBP Second. - INTF - AP 7	10.0d	21-Aug-28	1-Sep-28	21.0d
8111	FN-AP7-SD-1380	Install FF&E - CBP Second. - INTF - AP 7	10.0d	28-Aug-28	11-Sep-28	21.0d
8112	FN-AP7-SD-1400	Install Signage - CBP Second. - INTF - AP 7	5.0d	5-Sep-28	11-Sep-28	21.0d
8113	WBS - Delta Airlines Operations #2 & #3 - INTF - Apron 7		37.0d	27-Mar-28	16-May-28	11.0d
8114	FN-AP7-O3-930	Install Wall Insulation - Delta Airlines Operations #2 & #3 - INTF - AP 7	5.0d	27-Mar-28	31-Mar-28	0.0d
8115	FN-AP7-O3-940	Hang Drywall Walls - Delta Airlines Operations #2 & #3 - INTF - AP 7	5.0d	21-Apr-28	27-Apr-28	1.0d
8116	FN-AP7-O3-950	Tape & Finish Walls - Delta Airlines Operations #2 & #3 - INTF - AP 7	10.0d	28-Apr-28	11-May-28	11.0d
8117	FN-AP7-O3-1160	Install Doors & Hardware - Delta Airlines Operations #2 & #3 - INTF - AP 7	3.0d	12-May-28	16-May-28	11.0d
8118	WBS - CBP Support Restrooms - INTF - Apron 7		85.0d	20-Mar-28	18-Jul-28	54.0d
8119	FN-AP7-SR-200	Install Wall Insulation - CBP Support Restrooms - INTF - AP 7	5.0d	20-Mar-28	24-Mar-28	0.0d
8120	FN-AP7-SR-210	Hang Drywall Walls/Ceilings - CBP Support Restrooms - INTF - AP 7	5.0d	27-Mar-28	31-Mar-28	10.0d
8121	FN-AP7-SR-220	Tape & Finish Walls/Ceilings - CBP Support Restrooms - INTF - AP 7	10.0d	3-Apr-28	14-Apr-28	54.0d
8122	FN-AP7-SR-230	Prime & One Coat Walls - CBP Support Restrooms - INTF - AP 7	7.0d	17-Apr-28	25-Apr-28	54.0d
8123	FN-AP7-SR-280	Install Diffusers - CBP Support Restrooms - INTF - AP 7	5.0d	26-Apr-28	2-May-28	72.0d
8124	FN-AP7-SR-250	Install Doors - CBP Support Restrooms - INTF - AP 7	5.0d	26-Apr-28	2-May-28	54.0d
8125	FN-AP7-SR-240	Install Floor Tile & Base - CBP Support Restrooms - INTF - AP 7	10.0d	26-Apr-28	9-May-28	77.0d
8126	FN-AP7-SR-360	Install Door Hardware - CBP Support Restrooms - INTF - AP 7	5.0d	3-May-28	9-May-28	54.0d
8127	FN-AP7-SR-260	Install Ceiling Light Fixtures & Trim - CBP Support Restrooms - INTF - AP 7	10.0d	10-May-28	23-May-28	54.0d
8128	FN-AP7-SR-310	Install Partitions - CBP Support Restrooms - INTF - AP 7	10.0d	22-May-28	5-Jun-28	59.0d
8129	FN-AP7-SR-290	Install Low Voltage Trim - CBP Support Restrooms - INTF - AP 7	7.0d	24-May-28	2-Jun-28	54.0d
8130	FN-AP7-SR-400	Install Fire Alarm Trim - CBP Support Restrooms - INTF - AP 7	5.0d	24-May-28	31-May-28	54.0d
8131	FN-AP7-SR-300	Install Fire Protection Trim - CBP Support Restrooms - INTF - AP 7	3.0d	1-Jun-28	5-Jun-28	54.0d
8132	FN-AP7-SR-330	Install Vanities/Plumbing Trim - CBP Support Restrooms - INTF - AP 7	10.0d	6-Jun-28	19-Jun-28	54.0d
8133	FN-AP7-SR-340	Install Light Fixtures & Trim Walls/Columns - CBP Support Restrooms - INTF - ...	5.0d	6-Jun-28	12-Jun-28	74.0d
8134	FN-AP7-SR-380	Install Low Voltage Trim Walls/Columns - CBP Support Restrooms - INTF - AP 7	5.0d	6-Jun-28	12-Jun-28	59.0d
8135	FN-AP7-SR-410	Install BAS Trim Walls/Columns - CBP Support Restrooms - INTF - AP 7	5.0d	6-Jun-28	12-Jun-28	59.0d
8136	FN-AP7-SR-350	Apply Final Paint - CBP Support Restrooms - INTF - AP 7	10.0d	20-Jun-28	3-Jul-28	54.0d
8137	FN-AP7-SR-370	Install FF&E- CBP Support Restrooms - INTF - AP 7	10.0d	5-Jul-28	18-Jul-28	54.0d
8138	FN-AP7-SR-390	Install Signage - CBP Support Restrooms - INTF - AP 7	5.0d	12-Jul-28	18-Jul-28	54.0d
8139	WBS - Overall/Support Corridors- INTF - Apron 7		148.0d	6-Mar-28	2-Oct-28	35.0d
8140	FN-AP7-SC-10	Install Wall Insulation - Overall/Support Corridors - INTF - AP 7	5.0d	6-Mar-28	10-Mar-28	0.0d
8141	FN-AP7-SC-20	Hang Drywall Walls - Overall/Support Corridors - INTF - AP 7	5.0d	13-Mar-28	17-Mar-28	10.0d
8142	FN-AP7-SC-30	Tape & Finish Walls - Overall/Support Corridors - INTF - AP 7	10.0d	20-Mar-28	31-Mar-28	10.0d
8143	FN-AP7-SC-40	Prime & One Coat Walls - Overall/Support Corridors - INTF - AP 7	7.0d	3-Apr-28	11-Apr-28	10.0d
8144	FN-AP7-SC-80	Install Ceiling Light Fixtures & Trim - Overall/Support Corridors - INTF - AP 7	10.0d	12-Apr-28	25-Apr-28	62.0d
8145	FN-AP7-SC-50	Install ACT Ceiling Grid - Overall/Support Corridors - INTF - AP 7	20.0d	12-Apr-28	9-May-28	10.0d
8146	FN-AP7-SC-60	Install Doors - Overall/Support Corridors - INTF - AP 7	5.0d	12-Apr-28	18-Apr-28	126.0d
8147	FN-AP7-SC-90	Install Diffusers - Overall/Support Corridors - INTF - AP 7	5.0d	10-May-28	16-May-28	39.0d
8148	FN-AP7-SC-100	Install Low Voltage Trim - Overall/Support Corridors - INTF - AP 7	7.0d	17-May-28	25-May-28	39.0d



	ID	Name	Dur	Start	Finish	TF
8149	FN-AP7-SC-200	Install Fire Alarm Trim - Overall/Support Corridors - INTF - AP 7	5.0d	17-May-28	23-May-28	39.0d
8150	FN-AP7-SC-110	Install Fire Protection Trim - Overall/Support Corridors - INTF - AP 7	3.0d	24-May-28	26-May-28	39.0d
8151	FN-AP7-SC-120	Drop Ceiling Tile - Overall/Support Corridors - INTF - AP 7	10.0d	30-May-28	12-Jun-28	39.0d
8152	FN-AP7-SC-70	Install Flooring & Base - Overall/Support Corridors - INTF - AP 7	10.0d	31-Jul-28	11-Aug-28	6.0d
8153	FN-AP7-SC-130	Install Column Covers - Overall/Support Corridors - INTF - AP 7	10.0d	14-Aug-28	25-Aug-28	35.0d
8154	FN-AP7-SC-180	Install Door Hardware - Overall/Support Corridors - INTF - AP 7	5.0d	14-Aug-28	18-Aug-28	45.0d
8155	FN-AP7-SC-150	Install Interior Specialties/Mounting Brackets/OFOI - Overall/Support Corridor...	10.0d	28-Aug-28	11-Sep-28	35.0d
8156	FN-AP7-SC-140	Install Light Fixtures & Trim Walls/Columns - Overall/Support Corridors - INTF ...	5.0d	28-Aug-28	1-Sep-28	35.0d
8157	FN-AP7-SC-170	Install Low Voltage Trim Walls/Columns - Overall/Support Corridors - INTF - AP 7	5.0d	28-Aug-28	1-Sep-28	35.0d
8158	FN-AP7-SC-210	Install BAS Trim Walls/Columns - Overall/Support Corridors - INTF - AP 7	5.0d	28-Aug-28	1-Sep-28	35.0d
8159	FN-AP7-SC-160	Apply Final Paint - Overall/Support Corridors - INTF - AP 7	10.0d	12-Sep-28	25-Sep-28	35.0d
8160	FN-AP7-SC-190	Install Signage - Overall/Support Corridors - INTF - AP 7	5.0d	26-Sep-28	2-Oct-28	35.0d
8161	WBS - Distribution/Electrical Room #6197 - INTF - Apron 7		130.0d	25-Aug-27	29-Feb-28	186.0d
8162	FN-AP7-ER-610	Hang, Tape & Finish Drywall - Dist. Elec. Room 6197 - INTRF - AP 7	15.0d	25-Aug-27	15-Sep-27	0.0d
8163	FN-AP7-ER-620	Prime & First Coat - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	16-Sep-27	22-Sep-27	0.0d
8164	FN-AP7-ER-640	Set Elec. Switchgear & Equip. - Dist. Elec. Room 6197 - INTRF - AP 7	10.0d	23-Sep-27	6-Oct-27	0.0d
8165	FN-AP7-ER-710	Install Door & Hardware - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	23-Sep-27	24-Sep-27	8.0d
8166	RI-AP7-ER-880	Install Elec. OH Rough-in - Dist. Elec. Room 6197 - INTRF - AP 7	15.0d	7-Oct-27	27-Oct-27	0.0d
8167	FN-AP7-ER-650	Install Elec. Panels & Transformers - Dist. Elec. Room 6197 - INTRF - AP 7	10.0d	28-Oct-27	10-Nov-27	0.0d
8168	FN-AP7-ER-655	Elec. Feeder Wire Measurements & Procurement - Dist. Elec. Room 6197 - INTR...	10.0d	11-Nov-27	24-Nov-27	0.0d
8169	FN-AP7-ER-660	Pull & Terminate Elec. - Dist. Elec. Room 6197 - INTRF - AP 7	20.0d	29-Nov-27	27-Dec-27	0.0d
8170	FN-AP7-ER-667	Third Party Elec. Testing - Dist. Elec. Room 6197 - INTRF - AP 7	3.0d	28-Dec-27	30-Dec-27	110.0d
8171	FN-AP7-ER-670	Install Light Fixtures & Trim - Dist. Elec. Room 6197 - INTRF - AP 7	10.0d	3-Jan-28	14-Jan-28	110.0d
8172	FN-AP7-ER-715	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Dist. Elec. R...	2.0d	17-Jan-28	18-Jan-28	110.0d
8173	FN-AP7-ER-717	APG QC Procedure for Perm Power Available for Dist. - Dist. Elec. Room 6197 - I...	15.0d	19-Jan-28	8-Feb-28	110.0d
8174	FN-AP7-ER-720	Seal Concrete - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	9-Feb-28	15-Feb-28	186.0d
8175	FN-AP7-ER-700	Final Checkout & Panel Startup - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	9-Feb-28	10-Feb-28	120.0d
8176	FN-AP7-ER-690	Energize Equip. - Dist. Elec. Room 6197 - INTRF - AP 7	2.0d	11-Feb-28	14-Feb-28	120.0d
8177	FN-AP7-ER-730	Install Rubber Base - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	16-Feb-28	22-Feb-28	186.0d
8178	FN-AP7-ER-680	Apply Final Paint - Dist. Elec. Room 6197 - INTRF - AP 7	5.0d	23-Feb-28	29-Feb-28	186.0d
8179	WBS - Interior Partitions, Finishes & MEPT Trim-Out - Apron 8		379.0d	15-Apr-27	10-Oct-28	29.0d
8180	WBS - CBP Primary - INTF - Apron 8		173.0d	8-Feb-28	10-Oct-28	0.0d
8181	FN-AP8-PM-1690	Insulate Ceilings & Soffits - CBP Primary - INTF - AP 8	7.0d	8-Feb-28	16-Feb-28	30.0d
8182	FN-AP8-PM-1700	Install Wall Insulation - CBP Primary - INTF - AP 8	5.0d	8-Feb-28	14-Feb-28	0.0d
8183	FN-AP8-PM-1720	Hang Drywall Walls - CBP Primary - INTF - AP 8	5.0d	22-Feb-28	28-Feb-28	5.0d
8184	FN-AP8-PM-1740	Tape & Finish Walls - CBP Primary - INTF - AP 8	10.0d	22-Feb-28	6-Mar-28	39.0d
8185	FN-AP8-PM-1710	Hang Hard Lid Ceilings - CBP Primary - INTF - AP 8	5.0d	29-Feb-28	6-Mar-28	22.0d
8186	FN-AP8-PM-1730	Tape & Finish Ceilings - CBP Primary - INTF - AP 8	10.0d	7-Mar-28	20-Mar-28	22.0d
8187	FN-AP8-PM-1750	Apply Prime, First, Paint Ceilings - CBP Primary - INTF - AP 8	7.0d	21-Mar-28	29-Mar-28	22.0d
8188	FN-AP8-PM-1760	Prime & One Coat Walls - CBP Primary - INTF - AP 8	7.0d	30-Mar-28	7-Apr-28	22.0d
8189	FN-AP8-PM-1780	Install ACT Ceiling Grid - CBP Primary - INTF - AP 8	10.0d	10-Apr-28	21-Apr-28	22.0d
8190	FN-AP8-PM-1790	Install Doors - CBP Primary - INTF - AP 8	5.0d	10-Apr-28	14-Apr-28	114.0d

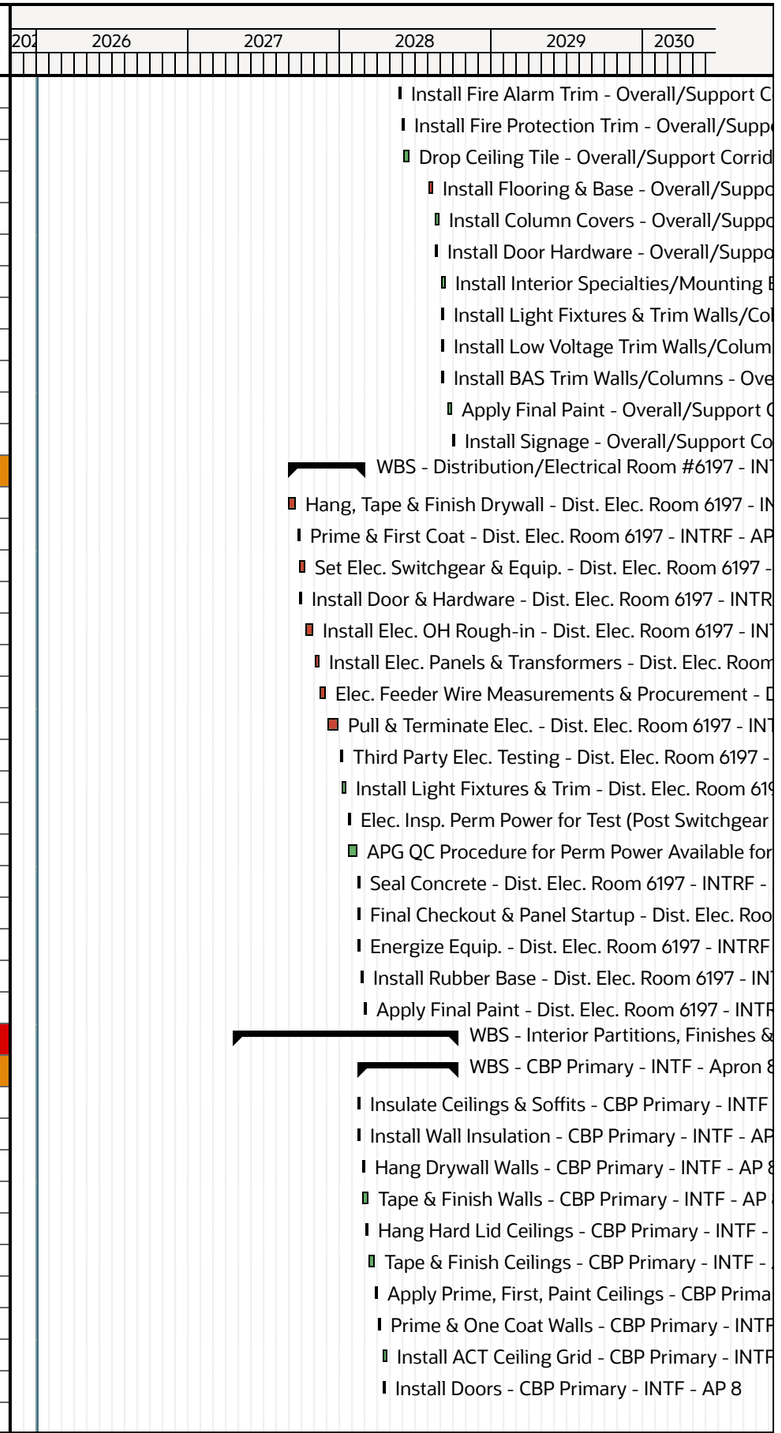


	ID	Name	Dur	Start	Finish	TF
8191	FN-AP8-PM-1920	Install Door Hardware - CBP Primary - INTF - AP 8	5.0d	17-Apr-28	21-Apr-28	114.0d
8192	FN-AP8-PM-1800	Install Ceiling Light Fixtures & Trim - CBP Primary - INTF - AP 8	10.0d	24-Apr-28	5-May-28	22.0d
8193	FN-AP8-PM-1810	Install Diffusers - CBP Primary - INTF - AP 8	5.0d	24-Apr-28	28-Apr-28	34.0d
8194	FN-AP8-PM-2020	Field Measure & Fab. Decorative Glass Panels (Exterior EL-7 & EL-6) - CBP Prim...	70.0d	5-May-28	14-Aug-28	0.0d
8195	FN-AP8-PM-1820	Install Low Voltage Trim - CBP Primary - INTF - AP 8	7.0d	8-May-28	16-May-28	22.0d
8196	FN-AP8-PM-1960	Install Fire Alarm Trim - CBP Primary - INTF - AP 8	5.0d	8-May-28	12-May-28	36.0d
8197	FN-AP8-PM-1830	Install Fire Protection Trim - CBP Primary - INTF - AP 8	3.0d	15-May-28	17-May-28	36.0d
8198	FN-AP8-PM-1840	Drop Ceiling Tile - CBP Primary - INTF - AP 8	10.0d	17-May-28	31-May-28	42.0d
8199	FN-AP8-PM-1850	Install Metal Ceiling Panels - CBP Primary - INTF - AP 8	15.0d	17-May-28	7-Jun-28	22.0d
8200	FN-AP8-PM-1970	Install Access Floors - CBP Primary - INTF - AP 8	10.0d	8-Jun-28	21-Jun-28	27.0d
8201	FN-AP8-PM-2010	Access Floor Elec/Low Voltage Rough-in - CBP Primary - INTF - AP 8	10.0d	8-Jun-28	21-Jun-28	27.0d
8202	FN-AP8-PM-1990	Install Terrazzo Flooring at - CBP Primary - INTF - AP 8	10.0d	21-Jun-28	5-Jul-28	13.0d
8203	FN-AP8-PM-1860	Install Base - CBP Primary - INTF - AP 8	5.0d	6-Jul-28	12-Jul-28	13.0d
8204	FN-AP8-PM-1870	Install Carpet Flooring - CBP Primary - INTF - AP 8	10.0d	13-Jul-28	26-Jul-28	13.0d
8205	FN-AP8-PM-1890	Install Column Covers - CBP Primary - INTF - AP 8	10.0d	27-Jul-28	9-Aug-28	13.0d
8206	FN-AP8-PM-1940	Install Low Voltage Trim Walls/Columns - CBP Primary - INTF - AP 8	5.0d	10-Aug-28	16-Aug-28	33.0d
8207	FN-AP8-PM-1900	Install Interior Specialties/Mounting Brackets/OFOI - CBP Primary - INTF - AP 8	10.0d	10-Aug-28	23-Aug-28	28.0d
8208	FN-AP8-PM-1910	Install Light Fixtures & Trim Walls/Columns - CBP Primary - INTF - AP 8	5.0d	10-Aug-28	16-Aug-28	13.0d
8209	FN-AP8-PM-2000	Install BAS Trim Walls/Columns - CBP Primary - INTF - AP 8	5.0d	10-Aug-28	16-Aug-28	33.0d
8210	FN-AP8-PM-2030	Install Decorative Glass (GL07A,B,C,D,E) - (Exterior EL-7 & EL-6) - CBP Primary ...	15.0d	15-Aug-28	5-Sep-28	0.0d
8211	FN-AP8-PM-1980	Terrazzo Final Polish - CBP Primary - INTF - AP 8	5.0d	6-Sep-28	12-Sep-28	0.0d
8212	FN-AP8-PM-1880	Apply Final Paint - CBP Primary - INTF - AP 8	10.0d	13-Sep-28	26-Sep-28	0.0d
8213	FN-AP8-PM-1930	Install FF&E - CBP Primary - INTF - AP 8	10.0d	27-Sep-28	10-Oct-28	0.0d
8214	FN-AP8-PM-1950	Install Signage & Dimensional Text - CBP Primary - INTF - AP 8	5.0d	4-Oct-28	10-Oct-28	0.0d
8215	WBS - Gang Bathroom #2 - INTF - Apron 8		202.0d	15-Apr-27	1-Feb-28	206.0d
8216	WBS - Men's Gang Bathroom #2 - INTF - Apron 8		202.0d	15-Apr-27	1-Feb-28	206.0d
8217	FN-AP8-R2-2290	Field Measure & Fab. Decorative Glass Panels - Men's Gang B/room #2 - INTF -...	70.0d	15-Apr-27	23-Jul-27	321.0d
8218	FN-AP8-R2-2136	Hang Drywall Lids & Walls - Men's Gang B/room #2 - INTF - AP 8	5.0d	1-Sep-27	8-Sep-27	136.0d
8219	FN-AP8-R2-1960	Tape & Finish Walls/Ceilings - Men's Gang B/room #2 - INTF - AP 8	10.0d	9-Sep-27	22-Sep-27	136.0d
8220	FN-AP8-R2-1970	Install Porcelain Floor Tile - Men's Gang B/room #2 - INTF - AP 8	15.0d	23-Sep-27	13-Oct-27	136.0d
8221	FN-AP8-R2-1980	Install Full Height Porcelain Wall Tile - Men's Gang B/room #2 - INTF - AP 8	15.0d	14-Oct-27	3-Nov-27	204.0d
8222	FN-AP8-R2-2000	Prime & Paint Walls/Ceilings - Men's Gang B/room #2 - INTF - AP 8	5.0d	4-Nov-27	10-Nov-27	204.0d
8223	FN-AP8-R2-1990	Set Restroom Vanities w/Quartz Finishes - Men's Gang B/room #2 - INTF - AP 8	5.0d	11-Nov-27	17-Nov-27	204.0d
8224	FN-AP8-R2-2010	Set Restroom Plumbing Fixtures - Men's Gang B/room #2 - INTF - AP 8	5.0d	18-Nov-27	24-Nov-27	204.0d
8225	FN-AP8-R2-2030	Install Diffusers - Men's Gang B/room #2 - INTF - AP 8	3.0d	29-Nov-27	1-Dec-27	212.0d
8226	FN-AP8-R2-2015	Set Cont. Quartz Trough Sinks - Men's Gang B/room #2 - INTF - AP 8	2.0d	29-Nov-27	30-Nov-27	204.0d
8227	FN-AP8-R2-2020	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	1-Dec-27	9-Dec-27	206.0d
8228	FN-AP8-R2-2040	Install Ceiling Speakers - Men's Gang B/room #2 - INTF - AP 8	5.0d	10-Dec-27	16-Dec-27	206.0d
8229	FN-AP8-R2-2240	Install Fire Alarm Trim - Men's Gang B/room #2 - INTF - AP 8	5.0d	10-Dec-27	16-Dec-27	207.0d
8230	FN-AP8-R2-2050	Install Fire Protection Trim - Men's Gang B/room #2 - INTF - AP 8	3.0d	20-Dec-27	22-Dec-27	206.0d
8231	FN-AP8-R2-2070	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - ...	5.0d	23-Dec-27	30-Dec-27	206.0d
8232	FN-AP8-R2-2080	Install Restroom Toilet Acc. (Grab Bars, Toilet Tissue Dispensers, Bag/Purse Ho...	5.0d	3-Jan-28	7-Jan-28	206.0d




	ID	Name	Dur	Start	Finish	TF
8233	FN-AP8-R2-2300	Install Decorative Glass (GL01) - Men's Gang B/room #2 - INTF - AP 8	5.0d	10-Jan-28	14-Jan-28	206.0d
8234	FN-AP8-R2-2310	Install Vestibule Stone Cladding (ST01)- Men's Gang B/room #2 - INTF - AP 8	5.0d	17-Jan-28	21-Jan-28	206.0d
8235	FN-AP8-R2-2060	Apply Final Paint - Men's Gang B/room #2 - INTF - AP 8	5.0d	24-Jan-28	28-Jan-28	206.0d
8236	FN-AP8-R2-2090	Install Wall Art - Men's Gang B/room #2 - INTF - AP 8	2.0d	31-Jan-28	1-Feb-28	206.0d
8237	WBS - Women's Gang Bathroom #2 - INTF - Apron 8		193.0d	15-Apr-27	19-Jan-28	215.0d
8238	FN-AP8-R2-2260	Field Measure & Fab. Decorative Glass Panels - Women's Gang B/room #2 - IN...	70.0d	15-Apr-27	23-Jul-27	321.0d
8239	RI-AP8-R2-2290	Hang Drywall Lids & Walls - Women's Gang B/room #2 - INTR - AP 8	5.0d	1-Sep-27	8-Sep-27	197.0d
8240	FN-AP8-R2-2100	Tape & Finish Walls/Ceilings - Women's Gang B/room #2 - INTF - AP 8	10.0d	9-Sep-27	22-Sep-27	197.0d
8241	FN-AP8-R2-2110	Install Porcelain Floor Tile - Women's Gang B/room #2 - INTF - AP 8	15.0d	23-Sep-27	13-Oct-27	197.0d
8242	FN-AP8-R2-2120	Install Full Height Porcelain Wall Tile - Women's Gang B/room #2 - INTF - AP 8	15.0d	14-Oct-27	3-Nov-27	197.0d
8243	FN-AP8-R2-2140	Prime & Paint Walls/Ceilings - Women's Gang B/room #2 - INTF - AP 8	5.0d	4-Nov-27	10-Nov-27	197.0d
8244	FN-AP8-R2-2170	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	11-Nov-27	19-Nov-27	197.0d
8245	FN-AP8-R2-2150	Install Diffusers - Women's Gang B/room #2 - INTF - AP 8	3.0d	11-Nov-27	15-Nov-27	203.0d
8246	FN-AP8-R2-2180	Install Ceiling Speakers - Women's Gang B/room #2 - INTF - AP 8	5.0d	16-Nov-27	22-Nov-27	203.0d
8247	FN-AP8-R2-2250	Install Fire Alarm Trim - Women's Gang B/room #2 - INTF - AP 8	5.0d	16-Nov-27	22-Nov-27	203.0d
8248	FN-AP8-R2-2130	Set Restroom Vanities w/Quartz Finishes - Women's Gang B/room #2 - INTF - ...	5.0d	22-Nov-27	30-Nov-27	197.0d
8249	FN-AP8-R2-2190	Install Fire Protection Trim - Women's Gang B/room #2 - INTF - AP 8	3.0d	23-Nov-27	29-Nov-27	203.0d
8250	FN-AP8-R2-2160	Set Restroom Plumbing Fixtures Trough Sinks - Women's Gang B/room #2 - IN...	5.0d	1-Dec-27	7-Dec-27	197.0d
8251	FN-AP8-R2-2165	Set Continuous Quartz Trough Sinks - Women's Gang B/room #2 - INTF - AP 8	2.0d	8-Dec-27	9-Dec-27	197.0d
8252	FN-AP8-R2-2210	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - ...	5.0d	10-Dec-27	16-Dec-27	215.0d
8253	FN-AP8-R2-2220	Install Restroom Toilet Acc. (Grab Bars, Toilet Tissue Dispensers, Bag/Purse Ho...	5.0d	17-Dec-27	23-Dec-27	215.0d
8254	FN-AP8-R2-2270	Install Decorative Glass (GL01)- Women's Gang B/room #2 - INTF - AP 8	5.0d	27-Dec-27	3-Jan-28	215.0d
8255	FN-AP8-R2-2280	Install Vestibule Stone Cladding (ST01) - Women's Gang B/room #2 - INTF - AP 8	5.0d	4-Jan-28	10-Jan-28	215.0d
8256	FN-AP8-R2-2200	Apply Final Paint - Women's Gang B/room #2 - INTF - AP 8	5.0d	11-Jan-28	17-Jan-28	215.0d
8257	FN-AP8-R2-2230	Install Wall Art - Women's Gang B/room #2 - INTF - AP 8	2.0d	18-Jan-28	19-Jan-28	215.0d
8258	WBS - Baggage Claim 1 - INTF - Apron 8		124.0d	1-Feb-28	25-Jul-28	49.0d
8259	FN-AP8-IB-2250	Install Wall Insulation - Baggage Claim 1 - INTF - AP 8	5.0d	1-Feb-28	7-Feb-28	0.0d
8260	FN-AP8-IB-2240	Insulate Ceilings & Soffits - Baggage Claim 1 - INTF - AP 8	7.0d	1-Feb-28	9-Feb-28	8.0d
8261	FN-AP8-IB-2270	Hang Drywall Walls - Baggage Claim 1 - INTF - AP 8	5.0d	8-Feb-28	14-Feb-28	5.0d
8262	FN-AP8-IB-2260	Hang Hard Lid Ceilings - Baggage Claim 1 - INTF - AP 8	5.0d	15-Feb-28	21-Feb-28	5.0d
8263	FN-AP8-IB-2290	Tape & Finish Walls - Baggage Claim 1 - INTF - AP 8	10.0d	15-Feb-28	28-Feb-28	33.0d
8264	FN-AP8-IB-2280	Tape & Finish Ceilings - Baggage Claim 1 - INTF - AP 8	10.0d	22-Feb-28	6-Mar-28	28.0d
8265	FN-AP8-IB-2310	Prime & One Coat Walls - Baggage Claim 1 - INTF - AP 8	7.0d	29-Feb-28	8-Mar-28	33.0d
8266	FN-AP8-IB-2300	Apply Prime, First, Paint Ceilings - Baggage Claim 1 - INTF - AP 8	7.0d	7-Mar-28	15-Mar-28	28.0d
8267	FN-AP8-IB-2320	Install Metal Ceiling Perimeter - Baggage Claim 1 - INTF - AP 8	10.0d	16-Mar-28	29-Mar-28	38.0d
8268	FN-AP8-IB-2340	Install Doors - Baggage Claim 1 - INTF - AP 8	5.0d	16-Mar-28	22-Mar-28	106.0d
8269	FN-AP8-IB-2330	Install ACT Ceiling Grid - Baggage Claim 1 - INTF - AP 8	10.0d	16-Mar-28	29-Mar-28	28.0d
8270	FN-AP8-IB-2480	Install Door Hardware - Baggage Claim 1 - INTF - AP 8	5.0d	23-Mar-28	29-Mar-28	106.0d
8271	FN-AP8-IB-2350	Install Ceiling Light Fixtures & Trim - Baggage Claim 1 - INTF - AP 8	10.0d	30-Mar-28	12-Apr-28	28.0d
8272	FN-AP8-IB-2360	Install Diffusers - Baggage Claim 1 - INTF - AP 8	7.0d	30-Mar-28	7-Apr-28	38.0d
8273	FN-AP8-IB-2370	Install Low Voltage Trim - Baggage Claim 1 - INTF - AP 8	7.0d	13-Apr-28	21-Apr-28	28.0d
8274	FN-AP8-IB-2510	Install Fire Alarm Trim - Baggage Claim 1 - INTF - AP 8	5.0d	13-Apr-28	19-Apr-28	42.0d



	ID	Name	Dur	Start	Finish	TF
8275	FN-AP8-IB-2380	Install Fire Protection Trim - Baggage Claim 1 - INTF - AP 8	3.0d	20-Apr-28	24-Apr-28	42.0d
8276	FN-AP8-IB-2400	Install Metal Ceiling Panels - Baggage Claim 1 - INTF - AP 8	15.0d	24-Apr-28	12-May-28	28.0d
8277	FN-AP8-IB-2390	Drop Ceiling Tile - Baggage Claim 1 - INTF - AP 8	10.0d	24-Apr-28	5-May-28	33.0d
8278	FN-AP8-IB-2440	Install Column Covers - Baggage Claim 1 - INTF - AP 8	10.0d	15-May-28	26-May-28	49.0d
8279	FN-AP8-IB-2470	Install Light Fixtures & Trim Walls/Columns - Baggage Claim 1 - INTF - AP 8	5.0d	30-May-28	5-Jun-28	69.0d
8280	FN-AP8-IB-2450	Install Low Voltage Trim Walls/Columns - Baggage Claim 1 - INTF - AP 8	5.0d	30-May-28	5-Jun-28	49.0d
8281	FN-AP8-IB-2520	Install BAS Trim Walls/Columns - Baggage Claim 1 - INTF - AP 8	5.0d	30-May-28	5-Jun-28	49.0d
8282	FN-AP8-IB-2460	Install Interior Specialties/Mounting Brackets/OFOI - Baggage Claim 1 - INTF - ...	10.0d	6-Jun-28	19-Jun-28	49.0d
8283	FN-AP8-IB-2430	Apply Final Paint - Baggage Claim 1 - INTF - AP 8	10.0d	20-Jun-28	3-Jul-28	49.0d
8284	FN-AP8-IB-2490	Install FF&E- Baggage Claim 1 - INTF - AP 8	10.0d	5-Jul-28	18-Jul-28	49.0d
8285	FN-AP8-IB-2500	Install Signage - Baggage Claim 1 - INTF - AP 8	5.0d	19-Jul-28	25-Jul-28	49.0d
8286	WBS - Distribution/Electrical Room #6290 - INTF - Apron 8		113.0d	29-Nov-27	5-May-28	138.0d
8287	FN-AP8-ER-2510	Hang, Tape & Finish Drywall - Dist. Elec. Room 6290 - INTRF - AP 8	15.0d	29-Nov-27	17-Dec-27	5.0d
8288	FN-AP8-ER-2520	Prime & First Coat - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	20-Dec-27	27-Dec-27	55.0d
8289	FN-AP8-ER-2545	Set Elec. Switchgear & Equip. - Dist. Elec. Room 6290 - INTRF - AP 8	10.0d	28-Dec-27	11-Jan-28	55.0d
8290	FN-AP8-ER-2615	Install Door & Hardware - Dist. Elec. Room 6290 - INTRF - AP 8	2.0d	28-Dec-27	29-Dec-27	118.0d
8291	RI-AP8-ER-2615	Install Elec. OH Rough-in - Dist. Elec. Room 6290 - INTRF - AP 8	15.0d	12-Jan-28	1-Feb-28	55.0d
8292	FN-AP8-ER-2555	Install Elec. Panels & Transformers - Dist. Elec. Room 6290 - INTRF - AP 8	10.0d	2-Feb-28	15-Feb-28	55.0d
8293	FN-AP8-ER-2565	Elec. Feeder Wire Measurements & Procurement - Dist. Elec. Room 6290 - INTR...	10.0d	16-Feb-28	29-Feb-28	55.0d
8294	FN-AP8-ER-2575	Pull & Terminate Elec. - Dist. Elec. Room 6290 - INTRF - AP 8	20.0d	1-Mar-28	28-Mar-28	55.0d
8295	FN-AP8-ER-2585	Third Party Elec. Testing - Dist. Elec. Room 6290 - INTRF - AP 8	3.0d	29-Mar-28	31-Mar-28	55.0d
8296	FN-AP8-ER-2595	Install Light Fixtures & Trim - Dist. Elec. Room 6290 - INTRF - AP 8	10.0d	3-Apr-28	14-Apr-28	133.0d
8297	FN-AP8-ER-2625	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Dist. Elec. R...	2.0d	3-Apr-28	4-Apr-28	55.0d
8298	FN-AP8-ER-2635	APG QC Procedure for Perm Power Available for Dist. - Dist. Elec. Room 6290 - I...	15.0d	5-Apr-28	25-Apr-28	55.0d
8299	FN-AP8-ER-2665	Seal Concrete - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	17-Apr-28	21-Apr-28	138.0d
8300	FN-AP8-ER-2675	Install Rubber Base - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	24-Apr-28	28-Apr-28	138.0d
8301	FN-AP8-ER-740	Final Checkout & Panel Startup - Dist. Elec Room 6290 - INTRF - AP 8	2.0d	26-Apr-28	27-Apr-28	80.0d
8302	FN-AP8-ER-750	Energize Equip. - Dist. Elec. Room 6290 - INTRF - AP 8	2.0d	28-Apr-28	1-May-28	80.0d
8303	FN-AP8-ER-2605	Apply Final Paint - Dist. Elec. Room 6290 - INTRF - AP 8	5.0d	1-May-28	5-May-28	138.0d
8304	WBS - HCAA Lift Storage - INTF - Apron 8		41.0d	15-Feb-28	11-Apr-28	136.0d
8305	FN-AP8-SR-2530	Install Wall Insulation - HCAA Lift Storage - INTF - AP 8	5.0d	15-Feb-28	21-Feb-28	136.0d
8306	FN-AP8-SR-1590	Hang Drywall Walls - HCAA Lift Storage - INTF - AP 8	5.0d	7-Mar-28	13-Mar-28	126.0d
8307	FN-AP8-SR-1600	Prime & First Coat - HCAA Lift Storage - INTF - AP 8	2.0d	14-Mar-28	15-Mar-28	126.0d
8308	FN-AP8-SR-1620	Install Light Fixtures & Trim - HCAA Lift Storage - INTF - AP 8	5.0d	16-Mar-28	22-Mar-28	130.0d
8309	FN-AP8-SR-1650	Install Door - HCAA Lift Storage - INTF - AP 8	2.0d	16-Mar-28	17-Mar-28	126.0d
8310	FN-AP8-SR-1660	Install Door Hardware - HCAA Lift Storage - INTF - AP 8	2.0d	20-Mar-28	21-Mar-28	126.0d
8311	FN-AP8-SR-1670	Seal Concrete - HCAA Lift Storage - INTF - AP 8	5.0d	22-Mar-28	28-Mar-28	126.0d
8312	FN-AP8-SR-1640	Install Fire Protection Trim - HCAA Lift Storage - INTF - AP 8	5.0d	23-Mar-28	29-Mar-28	140.0d
8313	FN-AP8-SR-1610	Install Metal Base - HCAA Lift Storage - INTF - AP 8	5.0d	29-Mar-28	4-Apr-28	126.0d
8314	FN-AP8-SR-1630	Install Fire Alarm Trim - HCAA Lift Storage - INTF - AP 8	5.0d	30-Mar-28	5-Apr-28	140.0d
8315	FN-AP8-SR-1680	Apply Final Paint - HCAA Lift Storage - INTF - AP 8	5.0d	5-Apr-28	11-Apr-28	126.0d
8316	WBS - Support Circulation 6542/Vestibule 6291 - INTF - Apron 8		71.0d	23-Mar-28	30-Jun-28	99.0d

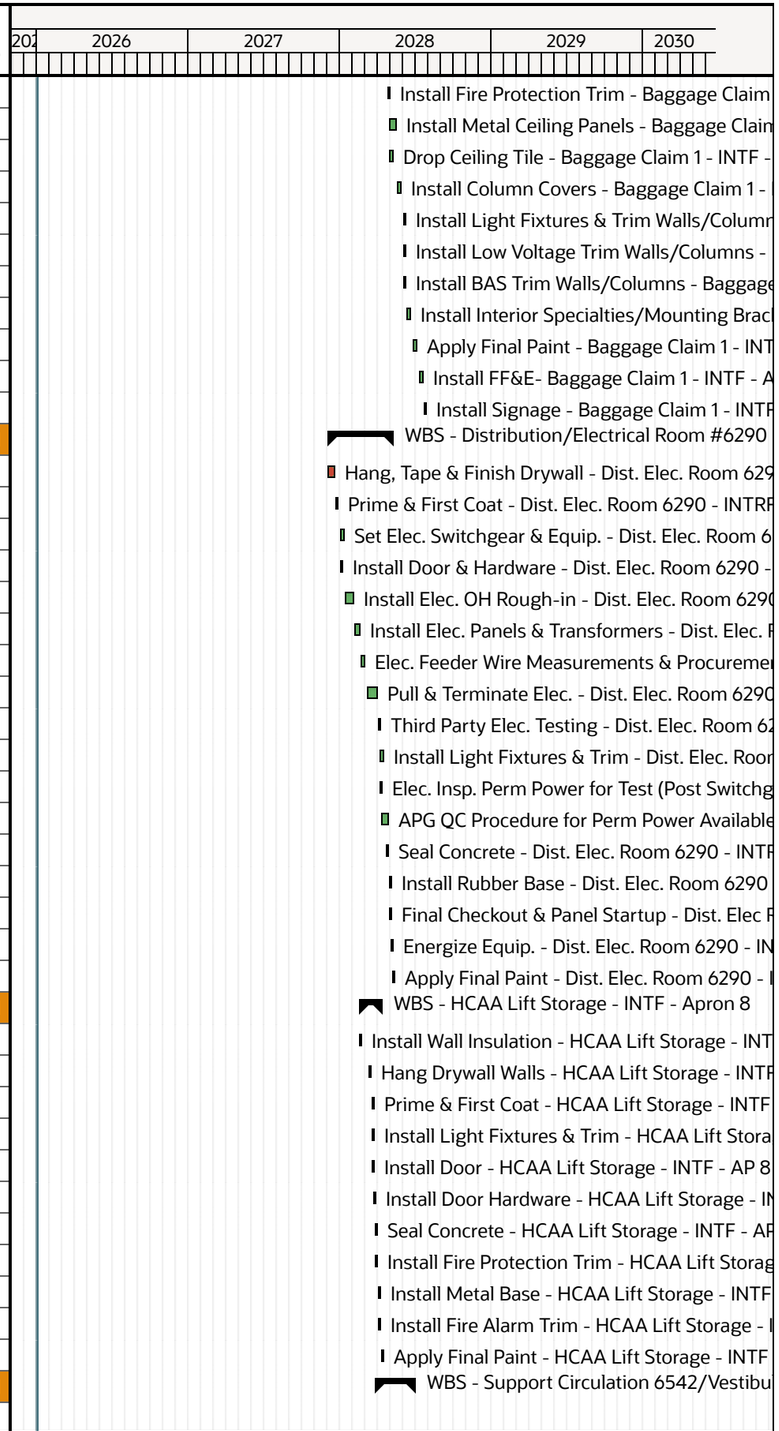

	ID	Name	Dur	Start	Finish	TF
8317	FN-AP3-SR-1400	Install Elec. Trim - Support Circulation 6542 - INTF - AP 8	5.0d	23-Mar-28	29-Mar-28	130.0d
8318	FN-AP3-SR-1410	Install Mech. Trim - Support Circulation 6542 - INTF - AP 8	5.0d	30-Mar-28	5-Apr-28	130.0d
8319	FN-AP3-SR-1420	Install Fire Protection Trim - Support Circulation 6542 - INTF - AP 8	5.0d	6-Apr-28	12-Apr-28	130.0d
8320	FN-AP3-SR-1430	Install Fire Alarm Trim - Support Circulation 6542 - INTF - AP 8	5.0d	13-Apr-28	19-Apr-28	130.0d
8321	FN-AP3-SR-1440	Install Doors & Hardware - Support Circulation 6542- INTF - AP 8	5.0d	13-Apr-28	19-Apr-28	130.0d
8322	FN-AP3-SR-1450	install Low Voltage & Security Trim - Support Circulation 6542 - INTF - AP 8	5.0d	13-Apr-28	19-Apr-28	130.0d
8323	FN-AP3-SR-1460	Seal Concrete Floor - Support Circulation 6542 - INTF - AP 8	5.0d	5-Jun-28	9-Jun-28	99.0d
8324	FN-AP3-SR-1470	Install Rubber Base - Support Circulation 6542 - INTF - AP 8	5.0d	12-Jun-28	16-Jun-28	99.0d
8325	FN-AP3-SR-1480	Apply Final Paint - Support Circulation 6542- INTF - AP 8	5.0d	19-Jun-28	23-Jun-28	99.0d
8326	FN-AP3-SR-1490	Install FEC Cabinets & Accessories - Support Circulation 6542 - INTF - AP 8	5.0d	26-Jun-28	30-Jun-28	99.0d
8327	WBS - Interior Partitions, Finishes & MEPT Trim-Out - Apron 9		102.0d	27-Oct-27	22-Mar-28	85.0d
8328	WBS - Outbound Baggage Makeup - INTF - Apron 9		102.0d	27-Oct-27	22-Mar-28	85.0d
8329	FN-AP9-BM-1670	Prime & One Coat Walls - O/Bound BHS Makeup - INTF - AP 9	7.0d	27-Oct-27	4-Nov-27	110.0d
8330	FN-AP9-BM-1690	Install Ceiling Light Fixtures & Trim - O/Bound BHS Makeup - INTF - AP 9	10.0d	5-Nov-27	18-Nov-27	110.0d
8331	FN-AP9-BM-1720	Install Diffusers - O/Bound BHS Makeup - INTF - AP 9	5.0d	5-Nov-27	11-Nov-27	120.0d
8332	FN-AP9-BM-1680	Install Doors - O/Bound BHS Makeup - INTF - AP 9	5.0d	5-Nov-27	11-Nov-27	148.0d
8333	FN-AP9-BM-1830	Install Door Hardware - O/Bound BHS Makeup - INTF - AP 9	5.0d	12-Nov-27	18-Nov-27	148.0d
8334	FN-AP9-BM-1740	Install Low Voltage Trim - O/Bound BHS Makeup - INTF - AP 9	7.0d	19-Nov-27	1-Dec-27	110.0d
8335	FN-AP9-BM-1870	Install Fire Alarm Trim - O/Bound BHS Makeup - INTF - AP 9	5.0d	19-Nov-27	29-Nov-27	110.0d
8336	FN-AP9-BM-1730	Install Fire Protection Trim - O/Bound BHS Makeup - INTF - AP 9	3.0d	30-Nov-27	2-Dec-27	110.0d
8337	FN-AP9-BM-1780	Seal Concrete Floor - O/Bound BHS Makeup - INTF - AP 9	20.0d	3-Dec-27	3-Jan-28	110.0d
8338	FN-AP9-BM-1840	Install Light Fixtures & Trim Walls - O/Bound BHS Makeup - INTF - AP 9	5.0d	4-Jan-28	10-Jan-28	110.0d
8339	FN-AP9-BM-1820	Install Low Voltage Trim Walls - O/Bound BHS Makeup - INTF - AP 9	5.0d	11-Jan-28	17-Jan-28	110.0d
8340	FN-AP9-BM-1800	Apply Final Paint - O/Bound BHS Makeup - INTF - AP 9	10.0d	18-Jan-28	31-Jan-28	110.0d
8341	FN-AP9-BM-1810	Install FF&E - O/Bound BHS Makeup - INTF - AP 9	10.0d	1-Feb-28	14-Feb-28	110.0d
8342	FN-AP9-BM-1860	Install Signage - O/Bound BHS Makeup - INTF - AP 9	7.0d	14-Mar-28	22-Mar-28	85.0d
8343	WBS - Interior Partitions, Finishes & MEPT Trim-Out - Apron 10		64.0d	2-Feb-28	1-May-28	85.0d
8344	WBS - Mechanical Room 6007 - INTF - Apron 10		64.0d	2-Feb-28	1-May-28	85.0d
8345	FN-AP10-MR-1210	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - AP 10	15.0d	2-Feb-28	22-Feb-28	120.0d
8346	FN-AP10-MR-1190	Hang, Tape & Finish Drywall - Mech. Room - INTF - AP 10	15.0d	23-Feb-28	14-Mar-28	96.0d
8347	FN-AP10-MR-1200	Prime & First Coat - Mech. Room - INTF - AP 10	5.0d	15-Mar-28	21-Mar-28	96.0d
8348	FN-AP10-MR-1240	Install Doors - Mech. Room - INTF - AP 10	5.0d	22-Mar-28	28-Mar-28	96.0d
8349	FN-AP10-MR-1220	Install Light Fixtures & Trim - Mech. Room - INTF - AP 10	5.0d	22-Mar-28	28-Mar-28	101.0d
8350	FN-AP10-MR-1250	Seal Concrete - Mech. Room - INTF - AP 10	5.0d	29-Mar-28	4-Apr-28	96.0d
8351	FN-AP10-MR-1260	Install Door Hardware - Mech. Room - INTF - AP 10	5.0d	29-Mar-28	4-Apr-28	96.0d
8352	FN-AP10-MR-1230	Apply Final Paint - Mech. Room - INTF - AP 10	5.0d	5-Apr-28	11-Apr-28	96.0d
8353	FN-AP10-MR-1290	Energize Power at AHU - Mech. Room - INTF - AP 10	5.0d	5-Apr-28	11-Apr-28	85.0d
8354	FN-AP10-MR-1280	Start-up AHU - Mech. Room - INTF - AP 10	3.0d	12-Apr-28	14-Apr-28	85.0d
8355	FN-AP10-MR-1300	Install Signage - Mech. Room - INTF - AP 10	3.0d	27-Apr-28	1-May-28	85.0d
8356	WBS - Interior Partitions, Finishes & MEPT Trim-Out - Apron 11		177.0d	9-Sep-27	18-May-28	129.0d
8357	WBS - Support Restrooms/Corridors 6008 - INTF - Apron 11		161.0d	9-Sep-27	26-Apr-28	85.0d
8358	FN-AP11-SRR-10	Install Wall Insulation - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	9-Sep-27	15-Sep-27	85.0d

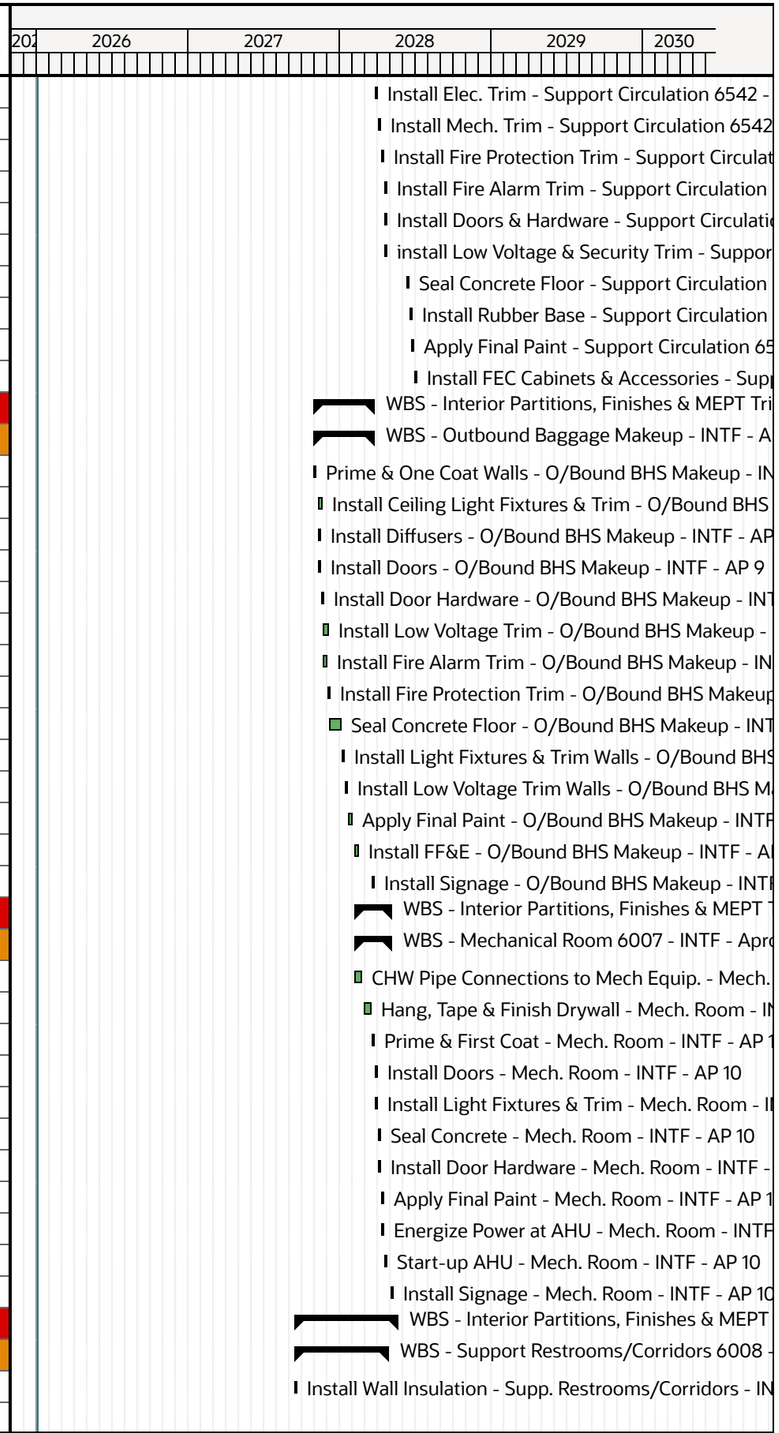


	ID	Name	Dur	Start	Finish	TF
8359	FN-AP11-SRR-20	Insulate Ceilings & Soffits - Supp. Restrooms/Corridors - INTF - AP 11	7.0d	9-Sep-27	17-Sep-27	164.0d
8360	FN-AP11-SRR-40	Hang Drywall Walls - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	22-Sep-27	28-Sep-27	81.0d
8361	FN-AP11-SRR-30	Hang Hard Lid Ceilings - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	29-Sep-27	5-Oct-27	157.0d
8362	FN-AP11-SRR-60	Tape & Finish Walls - Supp. Restrooms/Corridors - INTF - AP 11	10.0d	29-Sep-27	12-Oct-27	162.0d
8363	FN-AP11-SRR-50	Tape & Finish Ceilings - Supp. Restrooms/Corridors - INTF - AP 11	10.0d	6-Oct-27	19-Oct-27	157.0d
8364	FN-AP11-SRR-80	Prime & One Coat Walls - Supp. Restrooms/Corridors - INTF - AP 11	7.0d	13-Oct-27	21-Oct-27	162.0d
8365	FN-AP11-SRR-70	Apply Prime, First, Paint Ceilings - Supp. Restrooms/Corridors - INTF - AP 11	7.0d	20-Oct-27	28-Oct-27	157.0d
8366	FN-AP11-SRR-190	Install Doors - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	22-Oct-27	28-Oct-27	185.0d
8367	FN-AP11-SRR-120	Install Diffusers - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	29-Oct-27	4-Nov-27	162.0d
8368	FN-AP11-SRR-180	Install Door Hardware- Supp. Restrooms/Corridors - INTF - AP 11	10.0d	29-Oct-27	11-Nov-27	185.0d
8369	FN-AP11-SRR-220	Install Elec. Trim/LTNG - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	29-Oct-27	4-Nov-27	157.0d
8370	FN-AP11-SRR-100	Install Low Voltage Trim - Supp. Restrooms/Corridors - INTF - AP 11	7.0d	5-Nov-27	15-Nov-27	157.0d
8371	FN-AP11-SRR-230	Install Fire Alarm Trim - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	5-Nov-27	11-Nov-27	157.0d
8372	FN-AP11-SRR-130	Install Fire Protection Trim - Supp. Restrooms/Corridors - INTF - AP 11	3.0d	12-Nov-27	16-Nov-27	157.0d
8373	FN-AP11-SRR-140	Install Partitions - Supp. Restrooms/Corridors - INTF - AP 11	10.0d	17-Nov-27	2-Dec-27	157.0d
8374	FN-AP11-SRR-150	Install Plumbing Trim - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	17-Nov-27	23-Nov-27	162.0d
8375	FN-AP11-SRR-160	Install Light Fixtures & Trim Walls - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	3-Dec-27	9-Dec-27	162.0d
8376	FN-AP11-SRR-110	Install Tile Flooring & Base - Supp. Restrooms/Corridors - INTF - AP 11	10.0d	3-Dec-27	16-Dec-27	157.0d
8377	FN-AP11-SRR-200	Install Low Voltage Trim Walls - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	17-Dec-27	23-Dec-27	157.0d
8378	FN-AP11-SRR-240	Install BAS Trim Walls - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	17-Dec-27	23-Dec-27	157.0d
8379	FN-AP11-SRR-170	Apply Final Paint - Supp. Restrooms/Corridors - INTF - AP 11	10.0d	27-Dec-27	10-Jan-28	157.0d
8380	FN-AP11-SRR-210	Install Signage - Supp. Restrooms/Corridors - INTF - AP 11	5.0d	20-Apr-28	26-Apr-28	85.0d
8381	WBS - Airlines Operations - INTF - Apron 11		177.0d	9-Sep-27	18-May-28	129.0d
8382	FN-AP11-OP-270	Install Wall Insulation - Airlines Operations - INTF - AP 11	5.0d	9-Sep-27	15-Sep-27	85.0d
8383	FN-AP11-OP-280	Insulate Ceilings & Soffits - Airlines Operations - INTF - AP 11	7.0d	9-Sep-27	17-Sep-27	105.0d
8384	FN-AP11-OP-300	Hang Drywall Walls - Airlines Operations - INTF - AP 11	5.0d	22-Sep-27	28-Sep-27	81.0d
8385	FN-AP11-OP-320	Tape & Finish Walls - Airlines Operations - INTF - AP 11	10.0d	29-Sep-27	12-Oct-27	81.0d
8386	FN-AP11-OP-340	Prime & One Coat Walls - Airlines Operations - INTF - AP 11	7.0d	13-Oct-27	21-Oct-27	81.0d
8387	FN-AP11-OP-250	Install Doors - Airlines Operations - INTF - AP 11	5.0d	22-Oct-27	28-Oct-27	129.0d
8388	FN-AP11-OP-290	Install ACT Ceiling Grid - Airlines Operations - INTF - AP 11	10.0d	22-Oct-27	4-Nov-27	81.0d
8389	FN-AP11-OP-260	Install Door Hardware- Airlines Operations - INTF - AP 11	10.0d	29-Oct-27	11-Nov-27	129.0d
8390	FN-AP11-OP-350	Install Diffusers - Airlines Operations - INTF - AP 11	5.0d	5-Nov-27	11-Nov-27	86.0d
8391	FN-AP11-OP-360	Install Elec. Trim/LTNG - Airlines Operations - INTF - AP 11	5.0d	5-Nov-27	11-Nov-27	81.0d
8392	FN-AP11-OP-370	Install Low Voltage Trim - Airlines Operations - INTF - AP 11	7.0d	12-Nov-27	22-Nov-27	81.0d
8393	FN-AP11-OP-380	Install Fire Alarm Trim - Airlines Operations - INTF - AP 11	5.0d	12-Nov-27	18-Nov-27	81.0d
8394	FN-AP11-OP-390	Install Fire Protection Trim - Airlines Operations - INTF - AP 11	3.0d	19-Nov-27	23-Nov-27	81.0d
8395	FN-AP11-OP-400	Install Partitions - Airlines Operations - INTF - AP 11	10.0d	24-Nov-27	9-Dec-27	81.0d
8396	FN-AP11-OP-410	Install Plumbing Trim - Airlines Operations - INTF - AP 11	10.0d	24-Nov-27	9-Dec-27	96.0d
8397	FN-AP11-OP-420	Install Light Fixtures & Trim Walls - Airlines Operations - INTF - AP 11	5.0d	10-Dec-27	16-Dec-27	81.0d
8398	FN-AP11-OP-310	Install ACT Tiles - Airlines Operations - INTF - AP 11	10.0d	17-Dec-27	3-Jan-28	81.0d
8399	FN-AP11-OP-430	Install Flooring & Base - Airlines Operations - INTF - AP 11	10.0d	4-Jan-28	17-Jan-28	81.0d
8400	FN-AP11-OP-440	Install Low Voltage Trim Walls - Airlines Operations - INTF - AP 11	5.0d	18-Jan-28	24-Jan-28	81.0d




	ID	Name	Dur	Start	Finish	TF
8401	FN-AP11-OP-490	Install BAS Trim Walls - Airlines Operations - INTF - AP 11	5.0d	18-Jan-28	24-Jan-28	81.0d
8402	FN-AP11-OP-450	Apply Final Paint - Airlines Operations - INTF - AP 11	10.0d	25-Jan-28	7-Feb-28	81.0d
8403	FN-AP11-OP-480	Install Millwork - Airlines Operations - INTF - AP 11	10.0d	8-Feb-28	21-Feb-28	192.0d
8404	FN-AP11-OP-460	Install Signage - Airlines Operations - INTF - AP 11	5.0d	12-May-28	18-May-28	85.0d
8405	WBS - Distribution/Electrical Room #6003 - INTF - Apron 11		113.0d	4-Nov-27	14-Apr-28	153.0d
8406	FN-AP11-ER-2676	Hang, Tape & Finish Drywall - Dist. Elec. Room #6003 - INTF - AP 11	15.0d	4-Nov-27	24-Nov-27	5.0d
8407	FN-AP11-ER-2686	Prime & First Coat - Dist. Elec. Room #6003 - INTF - AP 11	5.0d	29-Nov-27	3-Dec-27	70.0d
8408	FN-AP11-ER-2700	Set Elec. Switchgear & Equip. - Dist. Elec. Room #6003 - INTF - AP 11	10.0d	6-Dec-27	17-Dec-27	70.0d
8409	FN-AP11-ER-2770	Install Door & Hardware - Dist. Elec. Room #6003 - INTF - AP 11	2.0d	6-Dec-27	7-Dec-27	168.0d
8410	RI-AP11-ER-2760	Install Elec. OH Rough-in - Dist. Elec. Room #6003 - INTF - AP 11	15.0d	20-Dec-27	11-Jan-28	70.0d
8411	FN-AP11-ER-2710	Install Elec. Panels & Transformers - Dist. Elec. Room #6003 - INTF - AP 11	10.0d	12-Jan-28	25-Jan-28	70.0d
8412	FN-AP11-ER-2720	Elec. Feeder Wire Measurements & Procurement - Dist. Elec. Room #6003 - IN...	10.0d	26-Jan-28	8-Feb-28	70.0d
8413	FN-AP11-ER-2730	Pull & Terminate Elec. - Dist. Elec. Room #6003 - INTF - AP 11	20.0d	9-Feb-28	7-Mar-28	70.0d
8414	FN-AP11-ER-2740	Third Party Elec. Testing - Dist. Elec. Room #6003 - INTF - AP 11	3.0d	8-Mar-28	10-Mar-28	70.0d
8415	FN-AP11-ER-2750	Install Light Fixtures & Trim - Dist. Elec. Room #6003 - INTF - AP 11	10.0d	13-Mar-28	24-Mar-28	148.0d
8416	FN-AP11-ER-2780	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Dist. Elec. R...	2.0d	13-Mar-28	14-Mar-28	70.0d
8417	FN-AP11-ER-2790	APG QC Procedure for Perm Power Available for Dist. - Dist. Elec. Room #6003 ...	15.0d	15-Mar-28	4-Apr-28	70.0d
8418	FN-AP11-ER-2820	Seal Concrete - Dist. Elec. Room #6003 - INTF - AP 11	5.0d	27-Mar-28	31-Mar-28	153.0d
8419	FN-AP11-ER-3480	Install Rubber Base - Dist. Elec. Room #6003 - INTF - AP 11	5.0d	3-Apr-28	7-Apr-28	153.0d
8420	FN-AP11-ER-3460	Final Checkout & Panel Startup - Dist. Elec. Room #6003 - INTF - AP 11	2.0d	5-Apr-28	6-Apr-28	86.0d
8421	FN-AP11-ER-3470	Energize Equip. - Dist. Elec. Room #6003 - INTF - AP 11	2.0d	7-Apr-28	10-Apr-28	86.0d
8422	FN-AP11-ER-2760	Apply Final Paint - Dist. Elec. Room #6003 - INTF - AP 11	5.0d	10-Apr-28	14-Apr-28	153.0d
8423	WBS - Interior Partitions, Finishes & MEPT Trim-Out - Apron 12		236.0d	17-May-27	19-Apr-28	132.0d
8424	WBS - Unassigned Airlines Operations - INTF - Apron 12		151.0d	1-Sep-27	5-Apr-28	85.0d
8425	FN-AP12-CR-20	Install Wall Insulation- Unassigned Airline Operations - INTF - AP 12	5.0d	1-Sep-27	8-Sep-27	85.0d
8426	FN-AP12-CR-10	Insulate Ceilings & Soffits - Unassigned Airline Operations - INTF - AP 12	5.0d	1-Sep-27	8-Sep-27	88.0d
8427	FN-AP12-CR-40	Hang Drywall Walls - Unassigned Airline Operations - INTF - AP 12	2.0d	16-Sep-27	17-Sep-27	81.0d
8428	FN-AP12-CR-30	Hang Hard Lid Ceilings - Unassigned Airline Operations - INTF - AP 12	2.0d	20-Sep-27	21-Sep-27	81.0d
8429	FN-AP12-CR-70	Tape & Finish Walls - Unassigned Airline Operations - INTF - AP 12	10.0d	20-Sep-27	1-Oct-27	83.0d
8430	FN-AP12-CR-50	Tape & Finish Ceilings - Unassigned Airline Operations - INTF - AP 12	10.0d	22-Sep-27	5-Oct-27	81.0d
8431	FN-AP12-CR-90	Prime & One Coat Walls - Unassigned Airline Operations - INTF - AP 12	7.0d	4-Oct-27	12-Oct-27	83.0d
8432	FN-AP12-CR-100	Install Base - Unassigned Airline Operations - INTF - AP 12	10.0d	4-Oct-27	15-Oct-27	174.0d
8433	FN-AP12-CR-80	Apply Prime, First, Paint Ceilings - Unassigned Airline Operations - INTF - AP 12	7.0d	6-Oct-27	14-Oct-27	81.0d
8434	FN-AP12-CR-60	Seal Concrete - Unassigned Airline Operations - INTF - AP 12	6.0d	13-Oct-27	20-Oct-27	161.0d
8435	FN-AP12-CR-120	Install ACT Ceiling Grid - Unassigned Airline Operations - INTF - AP 12	5.0d	15-Oct-27	21-Oct-27	81.0d
8436	FN-AP12-CR-110	Install Doors - Unassigned Airline Operations - INTF - AP 12	5.0d	15-Oct-27	21-Oct-27	180.0d
8437	FN-AP12-CR-290	Install Rubber Base - Unassigned Airline Operations - INTF - AP 12	10.0d	21-Oct-27	3-Nov-27	161.0d
8438	FN-AP12-CR-130	Install Ceiling Light Fixtures & Trim - Unassigned Airline Operations - INTF - AP...	10.0d	22-Oct-27	4-Nov-27	143.0d
8439	FN-AP12-CR-150	Install Diffusers - Unassigned Airline Operations - INTF - AP 12	5.0d	22-Oct-27	28-Oct-27	155.0d
8440	FN-AP12-CR-160	Install Low Voltage Trim - Unassigned Airline Operations - INTF - AP 12	7.0d	5-Nov-27	15-Nov-27	143.0d
8441	FN-AP12-CR-270	Install Fire Alarm Trim - Unassigned Airline Operations - INTF - AP 12	5.0d	5-Nov-27	11-Nov-27	152.0d
8442	FN-AP12-CR-180	Install Column Covers - Unassigned Airline Operations - INTF - AP 12	10.0d	16-Nov-27	1-Dec-27	153.0d




	ID	Name	Dur	Start	Finish	TF
8443	FN-AP12-CR-190	Drop Ceiling Tile - Unassigned Airline Operations - INTF - AP 12	10.0d	16-Nov-27	1-Dec-27	143.0d
8444	FN-AP12-CR-170	Install Fire Protection Trim - Unassigned Airline Operations - INTF - AP 12	3.0d	16-Nov-27	18-Nov-27	150.0d
8445	FN-AP12-CR-210	Install Millwork - Unassigned Airline Operations - INTF - AP 12	10.0d	2-Dec-27	15-Dec-27	143.0d
8446	FN-AP12-CR-200	Install Light Fixtures & Trim Walls/Columns - Unassigned Airline Operations - I...	5.0d	2-Dec-27	8-Dec-27	163.0d
8447	FN-AP12-CR-250	Install Low Voltage Trim Walls/Columns - Unassigned Airline Operations - INTF...	5.0d	2-Dec-27	8-Dec-27	153.0d
8448	FN-AP12-CR-310	Install BAS Trim Walls/Columns - Unassigned Airline Operations - INTF - AP 12	5.0d	2-Dec-27	8-Dec-27	153.0d
8449	FN-AP12-CR-240	Install Door Hardware - Unassigned Airline Operations - INTF - AP 12	5.0d	16-Dec-27	22-Dec-27	143.0d
8450	FN-AP12-CR-220	Apply Final Paint - Unassigned Airline Operations - INTF - AP 12	10.0d	23-Dec-27	7-Jan-28	143.0d
8451	FN-AP12-CR-260	Install Signage - Unassigned Airline Operations - INTF - AP 12	5.0d	30-Mar-28	5-Apr-28	85.0d
8452	WBS - AGI Offices/Break Room - INTF - Apron 12		161.0d	1-Sep-27	19-Apr-28	85.0d
8453	FN-AP12-O1-720	Install Wall Insulation - AGI Offices/Break Room - INTF - AP 12	5.0d	1-Sep-27	8-Sep-27	85.0d
8454	FN-AP12-O1-730	Hang Drywall Walls - AGI Offices/Break Room - INTF - AP 12	2.0d	16-Sep-27	17-Sep-27	81.0d
8455	FN-AP12-O1-740	Tape & Finish Walls - AGI Offices/Break Room - INTF - AP 12	10.0d	20-Sep-27	1-Oct-27	85.0d
8456	FN-AP12-O1-770	Install ACT Ceiling Grid - AGI Offices/Break Room - INTF - AP 12	5.0d	4-Oct-27	8-Oct-27	85.0d
8457	FN-AP12-O1-760	Install Doors - AGI Offices/Break Room - INTF - AP 12	5.0d	4-Oct-27	8-Oct-27	150.0d
8458	FN-AP12-O1-780	Install Diffusers - AGI Offices/Break Room - INTF - AP 12	4.0d	11-Oct-27	14-Oct-27	97.0d
8459	FN-AP12-O1-920	Install Light Fixtures/Elec. Trim - AGI Offices/Break Room - INTF - AP 12	5.0d	11-Oct-27	15-Oct-27	97.0d
8460	FN-AP12-O1-790	Install Low Voltage Trim - AGI Offices/Break Room - INTF - AP 12	5.0d	18-Oct-27	22-Oct-27	97.0d
8461	FN-AP12-O1-930	Install Fire Alarm Trim - AGI Offices/Break Room - INTF - AP 12	5.0d	18-Oct-27	22-Oct-27	97.0d
8462	FN-AP12-O1-800	Install Fire Protection Trim - AGI Offices/Break Room - INTF - AP 12	3.0d	25-Oct-27	27-Oct-27	97.0d
8463	FN-AP12-O1-810	Drop Ceiling Tile - AGI Offices/Break Room - INTF - AP 12	15.0d	28-Oct-27	17-Nov-27	97.0d
8464	FN-AP12-O1-820	Install Resilient Tile Flooring - AGI Offices/Break Room - INTF - AP 12	10.0d	18-Nov-27	3-Dec-27	97.0d
8465	FN-AP12-O1-860	Install Light Fixtures & Trim Walls- AGI Offices/Break Room - INTF - AP 12	5.0d	6-Dec-27	10-Dec-27	171.0d
8466	FN-AP12-O1-900	Install Low Voltage Trim Walls - AGI Offices/Break Room - INTF - AP 12	5.0d	6-Dec-27	10-Dec-27	171.0d
8467	FN-AP12-O1-960	Install Rubber Base- AGI Offices/Break Room - INTF - AP 12	10.0d	6-Dec-27	17-Dec-27	97.0d
8468	FN-AP12-O1-970	Install BAS Trim Walls - AGI Offices/Break Room - INTF - AP 12	5.0d	6-Dec-27	10-Dec-27	171.0d
8469	FN-AP12-O1-950	Install Millwork - AGI Offices/Break Room - INTF - AP 12	5.0d	20-Dec-27	27-Dec-27	97.0d
8470	FN-AP12-O1-890	Install Door Hardware - AGI Offices/Break Room - INTF - AP 12	3.0d	28-Dec-27	30-Dec-27	97.0d
8471	FN-AP12-CR-300	Apply Final Paint - AGI Offices/Breakroom - INTF - Apron 12	10.0d	3-Jan-28	14-Jan-28	97.0d
8472	FN-AP12-O1-910	Install Signage - AGI Offices/Break Room - INTF - AP 12	5.0d	13-Apr-28	19-Apr-28	85.0d
8473	WBS - BAS Control Room 6078 - INTF - Apron 12		153.0d	17-May-27	22-Dec-27	215.0d
8474	FN-AP12-BAS-2000	Low Voltage/Elec. in Wall Inspection (COT) - INTF - BAS Control Room 6078 - A...	2.0d	17-May-27	18-May-27	108.0d
8475	FN-AP12-BAS-2020	Hang, Tape & Finish Drywall - INTF - BAS Control Room 6078 - AP12	15.0d	14-Oct-27	3-Nov-27	5.0d
8476	FN-AP12-BAS-2030	Paint Drywall - INTF - BAS Control Room 6078 - AP12	2.0d	4-Nov-27	5-Nov-27	215.0d
8477	FN-AP12-BAS-2040	Firestopping - INTF - BAS Control Room 6078 - AP12	2.0d	8-Nov-27	9-Nov-27	215.0d
8478	FN-AP12-BAS-2085	Seal Concrete - INTF - BAS Control Room 6078 - AP12	2.0d	10-Nov-27	11-Nov-27	215.0d
8479	FN-AP12-BAS-2090	Low Voltage Testing - INTF - BAS Control Room 6078 - AP12	10.0d	12-Nov-27	29-Nov-27	215.0d
8480	FN-AP12-BAS-2120	Install Rubber Base - INTF - BAS Control Room 6078 - AP12	2.0d	12-Nov-27	15-Nov-27	223.0d
8481	FN-AP12-BAS-2100	Owner's Acceptance Walkthrough - INTF - BAS Control Room 6078 - AP12	2.0d	30-Nov-27	1-Dec-27	215.0d
8482	FN-AP12-BAS-2110	Owner Equip. Install - INTF - BAS Control Room 6078 - AP12	15.0d	2-Dec-27	22-Dec-27	215.0d
8483	WBS - Interior Partitions, Finishes & MEPTFP Trim - Sterile Corridor		351.0d	28-Jul-27	13-Dec-28	5.0d
8484	WBS - Sterile Corridor Milestones		148.0d	12-May-28	13-Dec-28	5.0d

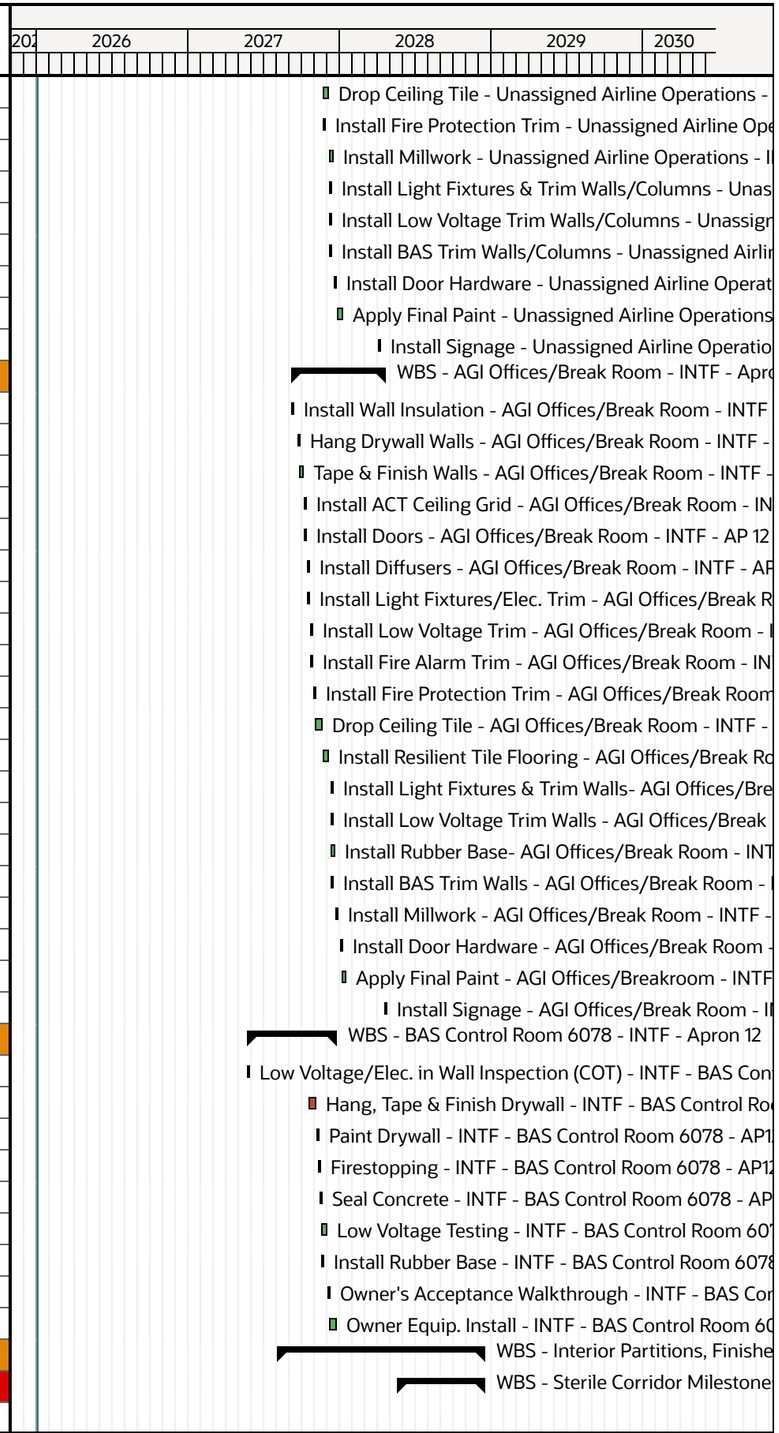


	ID	Name	Dur	Start	Finish	TF
8485	FN-MLS-SC-180	Sterile Level Fire Protection Trim Out Complete	0.0d		12-May-28	113.0d
8486	FN-MLS-SC-140	Sterile Level Mech. Trim Out Complete	0.0d		19-May-28	108.0d
8487	FN-MLS-SC-170	Sterile Level Fire Alarm Trim Out Complete	0.0d		26-May-28	103.0d
8488	FN-MLS-SC-160	Sterile Level Low Voltage Trim Out Complete	0.0d		7-Jun-28	96.0d
8489	FN-MLS-SC-150	Sterile Level Elec. Trim Out Complete	0.0d		28-Jun-28	81.0d
8490	FN-MLS-SC-200	Sterile Level Internal Punchlist	20.0d	14-Nov-28	13-Dec-28	5.0d
8491	FN-MLS-SC-190	Sterile Level Finishes Complete	0.0d		13-Dec-28	5.0d
8492	WBS - Interior Partitions, Finishes & Trim - Sterile Corr. 6		298.0d	28-Sep-27	29-Nov-28	5.0d
8493	FN-FI-1115	Hang Drywall Walls - Sterile Corr. 6	5.0d	28-Sep-27	4-Oct-27	173.0d
8494	FN-FI-1125	Tape & Finish Walls - Sterile Corr. 6	15.0d	5-Oct-27	25-Oct-27	173.0d
8495	FN-FI-690	Prime & One Coat Walls - Sterile Corr. 6	5.0d	26-Oct-27	1-Nov-27	173.0d
8496	FN-FI-710	Install ACT Ceiling Grid - Sterile Corr. 6	10.0d	30-Nov-27	13-Dec-27	155.0d
8497	FN-FI-620	Install Resilient Tile Flooring at Ramps - Sterile Corr. 6	7.0d	14-Dec-27	22-Dec-27	155.0d
8498	FN-FI-610	Install Terrazzo Flooring at Sterile Corridor - Sterile Corr. 6	10.0d	12-Jan-28	25-Jan-28	143.0d
8499	FN-FI-700	Apply Final Paint - Sterile Corr. 6	5.0d	26-Jan-28	1-Feb-28	156.0d
8500	FN-FI-660	Install Wall Paneling (WA03) - Sterile Corr. 6	5.0d	2-Feb-28	8-Feb-28	176.0d
8501	FN-FI-640	Install Wall Tile (TL21) - Sterile Corr. 6	5.0d	2-Feb-28	8-Feb-28	176.0d
8502	FN-FI-630	Install Column Covers - Sterile Corr. 6	18.0d	12-Apr-28	5-May-28	88.0d
8503	FN-FI-160	Install Fire Protection Trim - Sterile Corr. 6	5.0d	8-May-28	12-May-28	88.0d
8504	FN-FI-650	Install Metal Base - Sterile Corr. 6	5.0d	8-May-28	12-May-28	113.0d
8505	FN-FI-670	Install FECs - Sterile Corr. 6	2.0d	8-May-28	9-May-28	141.0d
8506	FN-FI-170	Install Mech. Trim - Sterile Corr. 6	5.0d	15-May-28	19-May-28	88.0d
8507	FN-FI-180	Install Fire Alarm Trim - Sterile Corr. 6	5.0d	22-May-28	26-May-28	88.0d
8508	FN-FI-560	Install Low Volt Trim - Sterile Corr. 6	5.0d	30-May-28	5-Jun-28	88.0d
8509	FN-FI-190	Install Elec. Trim - Sterile Corr. 6	5.0d	22-Jun-28	28-Jun-28	76.0d
8510	FN-FI-720	Install ACT Tile - Sterile Corr. 6	5.0d	29-Jun-28	6-Jul-28	76.0d
8511	FN-FI-150	Interior Glass Ramp Handrail - Sterile Corr. 6	10.0d	7-Jul-28	20-Jul-28	76.0d
8512	FN-FI-680	Install Gates at Ramps - Sterile Corr. 6	5.0d	21-Jul-28	27-Jul-28	76.0d
8513	FN-FI-1580	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 6	10.0d	7-Nov-28	20-Nov-28	5.0d
8514	FN-FI-730	Install Signage - Sterile Corr. 6	5.0d	21-Nov-28	29-Nov-28	5.0d
8515	WBS - Interior Partitions, Finishes & Trim - Sterile Corr. 7		311.0d	16-Sep-27	6-Dec-28	10.0d
8516	FN-FI-1215	Hang Drywall Walls - Sterile Corr. 7	5.0d	16-Sep-27	22-Sep-27	122.0d
8517	FN-FI-1225	Tape & Finish Walls - Sterile Corr. 7	15.0d	23-Sep-27	13-Oct-27	122.0d
8518	FN-FI-740	Prime & One Coat Walls - Sterile Corr. 7	10.0d	14-Oct-27	27-Oct-27	122.0d
8519	FN-FI-750	Install ACT Ceiling Grid - Sterile Corr. 7	10.0d	12-Nov-27	29-Nov-27	111.0d
8520	FN-FI-760	Install Resilient Tile Flooring at Ramps - Sterile Corr. 7	8.0d	30-Nov-27	9-Dec-27	111.0d
8521	FN-FI-770	Install Terrazzo Flooring at Sterile Corridor - Sterile Corr. 7	15.0d	20-Dec-27	11-Jan-28	105.0d
8522	FN-FI-790	Apply Final Paint - Sterile Corr. 7	10.0d	12-Jan-28	25-Jan-28	128.0d
8523	FN-FI-1630	Scan Stairs for Tread Fab. - Sterile Corr. 7	2.0d	12-Jan-28	13-Jan-28	196.0d
8524	FN-FI-810	Install Wall Paneling (WA03) - Sterile Corr. 7	10.0d	26-Jan-28	8-Feb-28	173.0d
8525	FN-FI-820	Install Wall Tile (TL21) - Sterile Corr. 7	9.0d	26-Jan-28	7-Feb-28	174.0d
8526	FN-FI-780	Install Column Covers North - Sterile Corr. 7	15.0d	25-Feb-28	16-Mar-28	73.0d

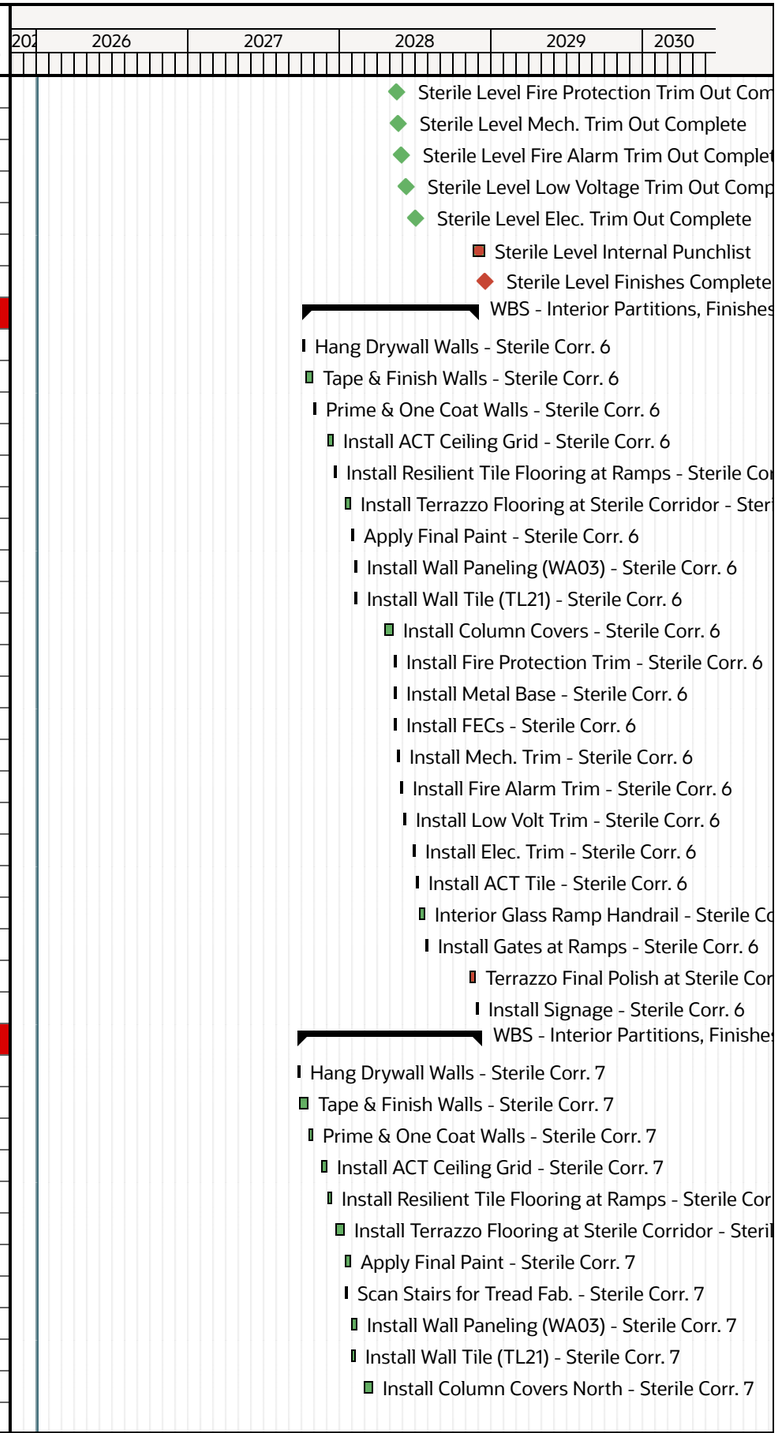


	ID	Name	Dur	Start	Finish	TF
8527	FN-FI-1500	Install Column Covers West - Sterile Corr. 7	18.0d	17-Mar-28	11-Apr-28	73.0d
8528	FN-FI-800	Install Fire Protection Trim - Sterile Corr. 7	10.0d	12-Apr-28	25-Apr-28	73.0d
8529	FN-FI-840	Install Metal Base - Sterile Corr. 7	10.0d	12-Apr-28	25-Apr-28	128.0d
8530	FN-FI-850	Install FECs - Sterile Corr. 7	5.0d	12-Apr-28	18-Apr-28	166.0d
8531	FN-FI-830	Install Mech. Trim - Sterile Corr. 7	10.0d	26-Apr-28	9-May-28	73.0d
8532	FN-FI-860	Install Fire Alarm Trim - Sterile Corr. 7	10.0d	10-May-28	23-May-28	73.0d
8533	FN-FI-870	Install Low Volt Trim - Sterile Corr. 7	10.0d	24-May-28	7-Jun-28	73.0d
8534	FN-FI-880	Install Elec. Trim - Sterile Corr. 7	10.0d	8-Jun-28	21-Jun-28	73.0d
8535	FN-FI-890	Install ACT Tile - Sterile Corr. 7	10.0d	22-Jun-28	6-Jul-28	73.0d
8536	FN-FI-1600	Install Terrazzo Flooring at Pre Cast Treads at Stairs - Sterile Corr. 7	5.0d	7-Jul-28	13-Jul-28	73.0d
8537	FN-FI-900	Interior Glass Ramp Handrail - Sterile Corr. 7	8.0d	14-Jul-28	25-Jul-28	73.0d
8538	FN-FI-910	Install Gates at Ramps - Sterile Corr. 7	5.0d	26-Jul-28	1-Aug-28	73.0d
8539	FN-FI-1570	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 7	15.0d	7-Nov-28	29-Nov-28	5.0d
8540	FN-FI-920	Install Signage - Sterile Corr. 7	5.0d	30-Nov-28	6-Dec-28	10.0d
8541	WBS - Interior Partitions, Finishes & Trim - Sterile Corr. 8		331.0d	28-Jul-27	13-Nov-28	5.0d
8542	FN-FI-1670	Field Measure & Fab. Decorative Glass Panels - Sterile Corr. 8	70.0d	28-Jul-27	3-Nov-27	194.0d
8543	FN-FI-1235	Hang Drywall Walls - Sterile Corr. 8	5.0d	9-Sep-27	15-Sep-27	108.0d
8544	FN-FI-1245	Tape & Finish Walls - Sterile Corr. 8	15.0d	16-Sep-27	6-Oct-27	108.0d
8545	FN-FI-930	Prime & One Coat Walls - Sterile Corr. 8	8.0d	7-Oct-27	18-Oct-27	108.0d
8546	FN-FI-940	Install ACT Ceiling Grid - Sterile Corr. 8	10.0d	29-Oct-27	11-Nov-27	100.0d
8547	FN-FI-950	Install Resilient Tile Flooring at Ramps - Sterile Corr. 8	5.0d	12-Nov-27	18-Nov-27	100.0d
8548	FN-FI-960	Install Terrazzo Flooring at Sterile Corridor - Sterile Corr. 8	15.0d	29-Nov-27	17-Dec-27	96.0d
8549	FN-FI-980	Apply Final Paint - Sterile Corr. 8	8.0d	20-Dec-27	30-Dec-27	139.0d
8550	FN-FI-1640	Scan Stairs for Tread Fab.- Sterile Corr. 8	3.0d	20-Dec-27	22-Dec-27	192.0d
8551	FN-FI-1000	Install Wall Paneling (WA03) - Sterile Corr. 8	8.0d	3-Jan-28	12-Jan-28	181.0d
8552	FN-FI-1010	Install Wall Tile (TL21) - Sterile Corr. 8	7.0d	3-Jan-28	11-Jan-28	182.0d
8553	FN-FI-970	Install Column Covers East - Sterile Corr. 8	12.0d	24-Jan-28	8-Feb-28	73.0d
8554	FN-FI-1510	Install Column Covers West - Sterile Corr. 8	12.0d	9-Feb-28	24-Feb-28	73.0d
8555	FN-FI-990	Install Fire Protection Trim - Sterile Corr. 8	8.0d	25-Feb-28	7-Mar-28	100.0d
8556	FN-FI-1030	Install Metal Base - Sterile Corr. 8	8.0d	25-Feb-28	7-Mar-28	150.0d
8557	FN-FI-1040	Install FECs - Sterile Corr. 8	5.0d	25-Feb-28	2-Mar-28	179.0d
8558	FN-FI-1660	Install Exterior Elevator Decorative Glass (GL07D/GLOZE)	7.0d	25-Feb-28	6-Mar-28	117.0d
8559	FN-FI-1020	Install Mech. Trim - Sterile Corr. 8	8.0d	8-Mar-28	17-Mar-28	100.0d
8560	FN-FI-1050	Install Fire Alarm Trim - Sterile Corr. 8	8.0d	20-Mar-28	29-Mar-28	100.0d
8561	FN-FI-1060	Install Low Volt Trim - Sterile Corr. 8	8.0d	30-Mar-28	10-Apr-28	100.0d
8562	FN-FI-1070	Install Elec. Trim - Sterile Corr. 8	8.0d	11-Apr-28	20-Apr-28	100.0d
8563	FN-FI-1080	Install ACT Tile - Sterile Corr. 8	8.0d	21-Apr-28	2-May-28	100.0d
8564	FN-FI-1610	Install Terrazzo Flooring at Pre Cast Treads at Monumental Stairs - Sterile Corr. 8	10.0d	3-May-28	16-May-28	100.0d
8565	FN-FI-1090	Install Glass Ramp & Stair Handrail - Sterile Corr. 8	6.0d	17-May-28	24-May-28	100.0d
8566	FN-FI-1100	Install Gates at Ramps - Sterile Corr. 8	5.0d	25-May-28	1-Jun-28	100.0d
8567	FN-FI-1560	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 8	15.0d	17-Oct-28	6-Nov-28	5.0d
8568	FN-FI-1110	Install Signage - Sterile Corr. 8	5.0d	7-Nov-28	13-Nov-28	5.0d

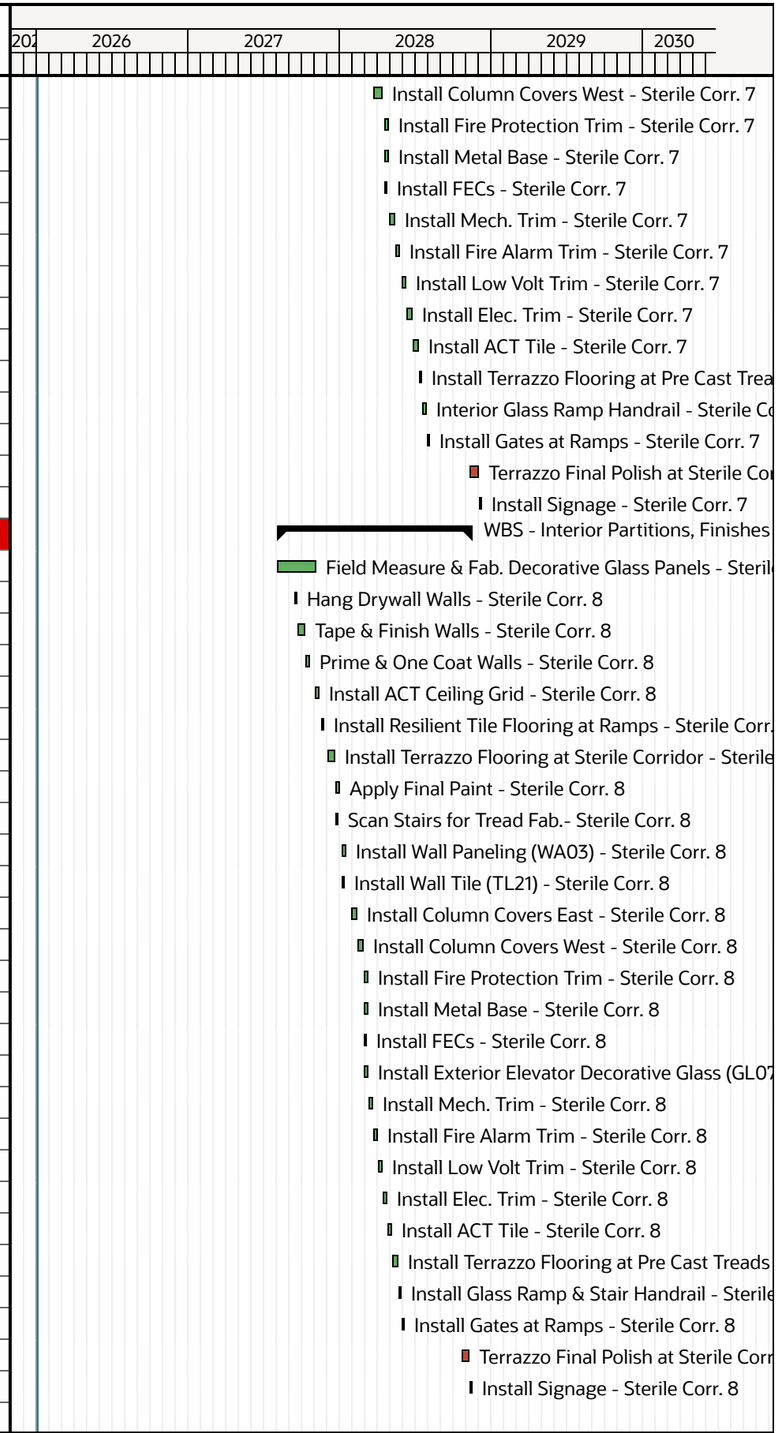


	ID	Name	Dur	Start	Finish	TF
8569	WBS - Interior Partitions, Finishes & Trim - Sterile Corr. 9		291.0d	1-Sep-27	23-Oct-28	20.0d
8570	FN-FI-1255	Hang Drywall Walls - Sterile Corr. 9	5.0d	1-Sep-27	8-Sep-27	93.0d
8571	FN-FI-1265	Tape & Finish Walls - Sterile Corr. 9	15.0d	9-Sep-27	29-Sep-27	93.0d
8572	FN-FI-1120	Prime & One Coat Walls - Sterile Corr. 9	7.0d	30-Sep-27	8-Oct-27	93.0d
8573	FN-FI-1130	Install ACT Ceiling Grid - Sterile Corr. 9	10.0d	15-Oct-27	28-Oct-27	89.0d
8574	FN-FI-1140	Install Resilient Tile Flooring at Ramps - Sterile Corr. 9	7.0d	29-Oct-27	8-Nov-27	89.0d
8575	FN-FI-1150	Install Terrazzo Flooring at Sterile Corridor - Sterile Corr. 9	10.0d	11-Nov-27	24-Nov-27	87.0d
8576	FN-FI-1170	Apply Final Paint - Sterile Corr. 9	7.0d	29-Nov-27	7-Dec-27	159.0d
8577	FN-FI-1190	Install Wall Paneling (WA03) - Sterile Corr. 9	7.0d	8-Dec-27	16-Dec-27	188.0d
8578	FN-FI-1200	Install Wall Tile (TL21) - Sterile Corr. 9	7.0d	8-Dec-27	16-Dec-27	188.0d
8579	FN-FI-1160	Install Column Covers East - Sterile Corr. 9	12.0d	17-Dec-27	5-Jan-28	73.0d
8580	FN-FI-1520	Install Column Covers West - Sterile Corr. 9	12.0d	6-Jan-28	21-Jan-28	73.0d
8581	FN-FI-1180	Install Fire Protection Trim - Sterile Corr. 9	7.0d	24-Jan-28	1-Feb-28	128.0d
8582	FN-FI-1220	Install Metal Base - Sterile Corr. 9	7.0d	24-Jan-28	1-Feb-28	164.0d
8583	FN-FI-1230	Install FECs - Sterile Corr. 9	5.0d	24-Jan-28	28-Jan-28	203.0d
8584	FN-FI-1210	Install Mech. Trim - Sterile Corr. 9	7.0d	2-Feb-28	10-Feb-28	128.0d
8585	FN-FI-1240	Install Fire Alarm Trim - Sterile Corr. 9	7.0d	11-Feb-28	21-Feb-28	128.0d
8586	FN-FI-1250	Install Low Volt Trim - Sterile Corr. 9	7.0d	11-Feb-28	21-Feb-28	128.0d
8587	FN-FI-1260	Install Elec. Trim - Sterile Corr. 9	7.0d	22-Feb-28	1-Mar-28	128.0d
8588	FN-FI-1270	Install ACT Tile - Sterile Corr. 9	7.0d	2-Mar-28	10-Mar-28	136.0d
8589	FN-FI-1280	Interior Ramp Handrail - Sterile Corr. 9	5.0d	13-Mar-28	17-Mar-28	136.0d
8590	FN-FI-1290	Install Gates at Ramps - Sterile Corr. 9	5.0d	20-Mar-28	24-Mar-28	136.0d
8591	FN-FI-1550	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 9	12.0d	29-Sep-28	16-Oct-28	5.0d
8592	FN-FI-1300	Install Signage - Sterile Corr. 9	5.0d	17-Oct-28	23-Oct-28	20.0d
8593	WBS - Interior Partitions, Finishes & Trim - Sterile Corr. 11		284.0d	25-Aug-27	5-Oct-28	32.0d
8594	FN-FI-1275	Hang Drywall Walls - Sterile Corr. 11	5.0d	25-Aug-27	31-Aug-27	73.0d
8595	FN-FI-1285	Tape & Finish Walls - Sterile Corr. 11	15.0d	1-Sep-27	22-Sep-27	73.0d
8596	FN-FI-1310	Prime & One Coat Walls - Sterile Corr. 11	6.0d	23-Sep-27	30-Sep-27	73.0d
8597	FN-FI-1320	Install ACT Ceiling Grid - Sterile Corr. 11	10.0d	1-Oct-27	14-Oct-27	73.0d
8598	FN-FI-1330	Install Resilient Tile Flooring at Ramps - Sterile Corr. 11	9.0d	15-Oct-27	27-Oct-27	73.0d
8599	FN-FI-1340	Install Terrazzo Flooring at Sterile Corridor - Sterile Corr. 11	10.0d	28-Oct-27	10-Nov-27	73.0d
8600	FN-FI-1350	Install Column Covers North - Sterile Corr. 11	12.0d	11-Nov-27	30-Nov-27	73.0d
8601	FN-FI-1360	Apply Final Paint - Sterile Corr. 11	6.0d	11-Nov-27	18-Nov-27	164.0d
8602	FN-FI-1650	Scan Stairs for Tread Fab. - Sterile Corr. 11	2.0d	11-Nov-27	12-Nov-27	198.0d
8603	FN-FI-1380	Install Wall Paneling (WA03) - Sterile Corr. 11	6.0d	19-Nov-27	30-Nov-27	187.0d
8604	FN-FI-1390	Install Wall Tile (TL21) - Sterile Corr. 11	7.0d	19-Nov-27	1-Dec-27	186.0d
8605	FN-FI-1530	Install Column Covers South - Sterile Corr. 11	12.0d	1-Dec-27	16-Dec-27	73.0d
8606	FN-FI-1370	Install Fire Protection Trim - Sterile Corr. 11	6.0d	17-Dec-27	27-Dec-27	146.0d
8607	FN-FI-1410	Install Metal Base - Sterile Corr. 11	6.0d	17-Dec-27	27-Dec-27	175.0d
8608	FN-FI-1420	Install FECs - Sterile Corr. 11	5.0d	17-Dec-27	23-Dec-27	227.0d
8609	FN-FI-1400	Install Mech. Trim - Sterile Corr. 11	6.0d	28-Dec-27	5-Jan-28	146.0d
8610	FN-FI-1430	Install Fire Alarm Trim - Sterile Corr. 11	6.0d	6-Jan-28	13-Jan-28	146.0d

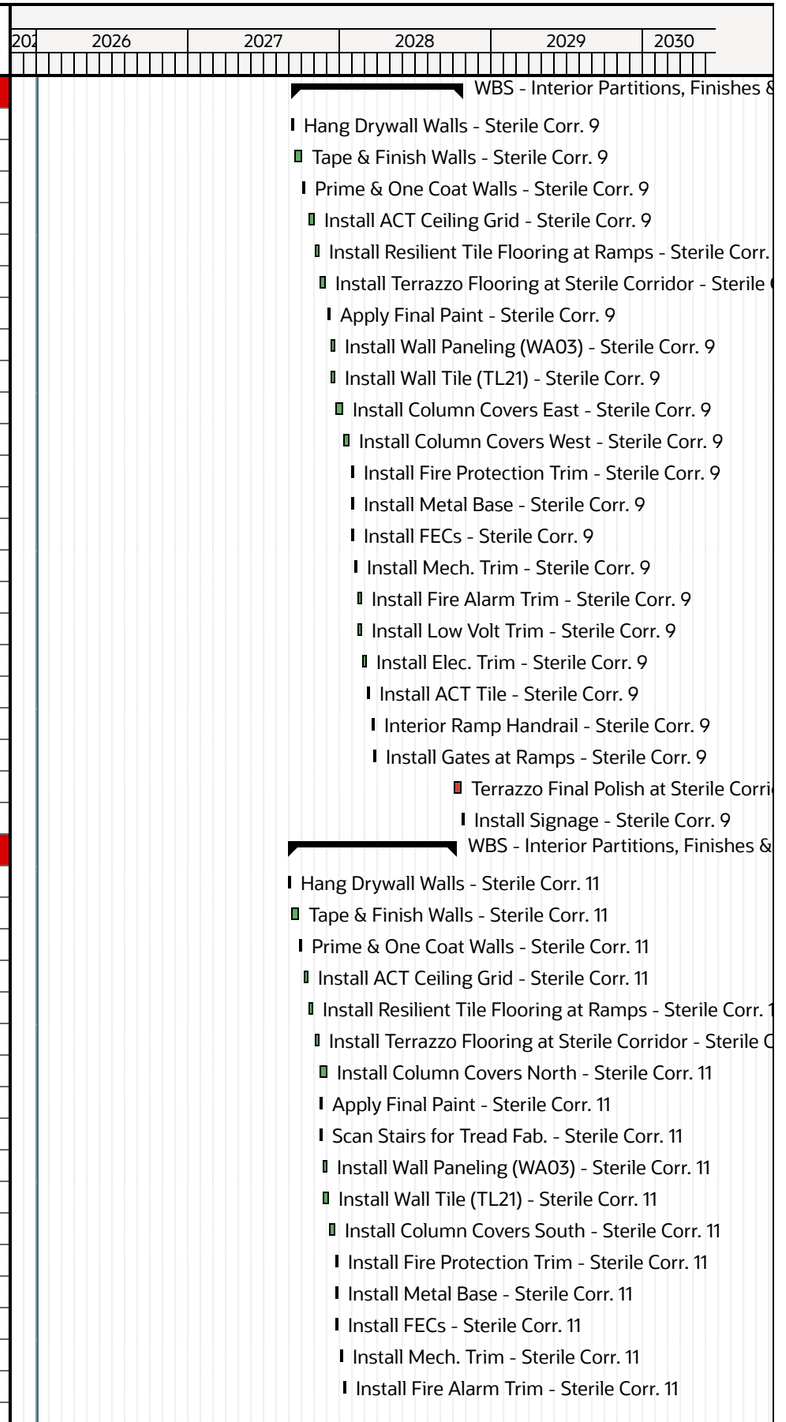


	ID	Name	Dur	Start	Finish	TF
8611	FN-FI-1440	Install Low Volt Trim - Sterile Corr. 11	6.0d	6-Jan-28	13-Jan-28	146.0d
8612	FN-FI-1450	Install Elec. Trim - Sterile Corr. 11	6.0d	14-Jan-28	21-Jan-28	146.0d
8613	FN-FI-1460	Install ACT Tile - Sterile Corr. 11	6.0d	24-Jan-28	31-Jan-28	146.0d
8614	FN-FI-1620	Install Terrazzo Flooring at Pre Cast Treads at Stairs - Sterile Corr. 11	5.0d	1-Feb-28	7-Feb-28	146.0d
8615	FN-FI-1590	Install Interior Ramp & Stair Handrail - Sterile Corr. 11	6.0d	8-Feb-28	15-Feb-28	146.0d
8616	FN-FI-1480	Install Gates at Ramps - Sterile Corr. 11	6.0d	16-Feb-28	23-Feb-28	146.0d
8617	FN-FI-1540	Terrazzo Final Polish at Sterile Corridor - Sterile Corr. 11	12.0d	13-Sep-28	28-Sep-28	5.0d
8618	FN-FI-1490	Install Signage - Sterile Corr. 11	5.0d	29-Sep-28	5-Oct-28	32.0d
8619	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse Level		572.0d	16-Dec-26	16-Mar-29	0.0d
8620	WBS - Concourse Level Milestones		164.0d	23-Jun-28	16-Feb-29	0.0d
8621	FN-MLS-CN-230	Concourse Level Fire Protection Trim Out Complete	0.0d		23-Jun-28	84.0d
8622	FN-MLS-CN-300	Concourse Level Plumbing Trim Out Complete	0.0d		14-Jul-28	45.0d
8623	FN-MLS-CN-190	Concourse Level Mech. Trim Out Complete	0.0d		21-Jul-28	65.0d
8624	FN-MLS-CN-210	Concourse Level Low Voltage Trim Out Complete	0.0d		21-Jul-28	65.0d
8625	FN-MLS-CN-200	Concourse Level Elec. Trim Out Complete	0.0d		28-Jul-28	60.0d
8626	FN-MLS-CN-220	Concourse Level Fire Alarm Trim Out Complete	0.0d		28-Jul-28	60.0d
8627	FN-MLS-CN-320	Concourse Level Doors & Hardware Complete	0.0d		7-Sep-28	32.0d
8628	FN-MLS-CN-330	Concourse Level Internal Punchlist	20.0d	18-Oct-28	14-Nov-28	64.0d
8629	FN-MLS-CN-310	Concourse Level Finishes Complete	0.0d		16-Feb-29	0.0d
8630	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 1		265.0d	20-Sep-27	3-Oct-28	64.0d
8631	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 1		265.0d	20-Sep-27	3-Oct-28	64.0d
8632	WBS - Support Corridors/HCAA IT Storage - INTF - Conc. 1		265.0d	20-Sep-27	3-Oct-28	64.0d
8633	FN-C1-SR-250	Hang Drywall - Support Corr./HCAA Storage - INTF - Conc. 1	3.0d	20-Sep-27	22-Sep-27	5.0d
8634	FN-C1-SR-915	Tape & Finish Drywall - Support Corr./HCAA Storage - INTF - Conc. 1	7.0d	23-Sep-27	1-Oct-27	181.0d
8635	FN-C1-SR-270	Prime & One Coat Walls - Support Corr./HCAA Storage - INTF - Conc. 1	7.0d	4-Oct-27	12-Oct-27	181.0d
8636	FN-C1-SR-290	Install Ceiling Grid - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	13-Oct-27	19-Oct-27	181.0d
8637	FN-C1-SR-300	Install Doors - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	13-Oct-27	19-Oct-27	252.0d
8638	FN-C1-SR-310	Install Diffusers - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	20-Oct-27	26-Oct-27	203.0d
8639	FN-C1-SR-350	Install Fire Protection Trim - Support Corr./HCAA Storage - INTF - Conc. 1	3.0d	27-Oct-27	29-Oct-27	210.0d
8640	FN-C1-SR-320	Install Low Voltage Trim - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	27-Oct-27	2-Nov-27	203.0d
8641	FN-C1-SR-470	Install Fire Alarm Trim - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	27-Oct-27	2-Nov-27	203.0d
8642	FN-C1-SR-280	Install Ceiling Light Fixtures & Trim - Support Corr./HCAA Storage - INTF - Con...	5.0d	10-Dec-27	16-Dec-27	146.0d
8643	FN-C1-SR-340	Drop Ceiling Tile - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	17-Dec-27	23-Dec-27	173.0d
8644	FN-C1-SR-360	Install Resilient Tile Flooring - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	27-Dec-27	3-Jan-28	173.0d
8645	FN-C1-SR-430	Install Door Hardware - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	4-Jan-28	10-Jan-28	202.0d
8646	FN-C1-SR-505	Seal Concrete - Support Corr./HCAA Storage - INTF - Conc. 1	10.0d	4-Jan-28	17-Jan-28	173.0d
8647	FN-C1-SR-380	Install Rubber Base - Support Corr./HCAA Storage - INTF - Conc. 1	7.0d	18-Jan-28	26-Jan-28	173.0d
8648	FN-C1-SR-515	Install Terrazzo Flooring at Employee Vestibule - Support Corr./HCAA Storage -...	5.0d	18-Jan-28	24-Jan-28	175.0d
8649	FN-C1-SR-905	Install Metal Base - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	25-Jan-28	31-Jan-28	175.0d
8650	FN-C1-SR-410	Install Light Fixtures & Trim Walls/Columns - Support Corr./HCAA Storage - IN...	5.0d	27-Jan-28	2-Feb-28	173.0d
8651	FN-C1-SR-450	Install Low Voltage Trim Walls/Columns - Support Corr./HCAA Storage - INTF -...	5.0d	27-Jan-28	2-Feb-28	183.0d
8652	FN-C1-SR-480	Install Fire Alarm Trim Walls/Columns - Support Corr./HCAA Storage - INTF - C...	5.0d	27-Jan-28	2-Feb-28	183.0d

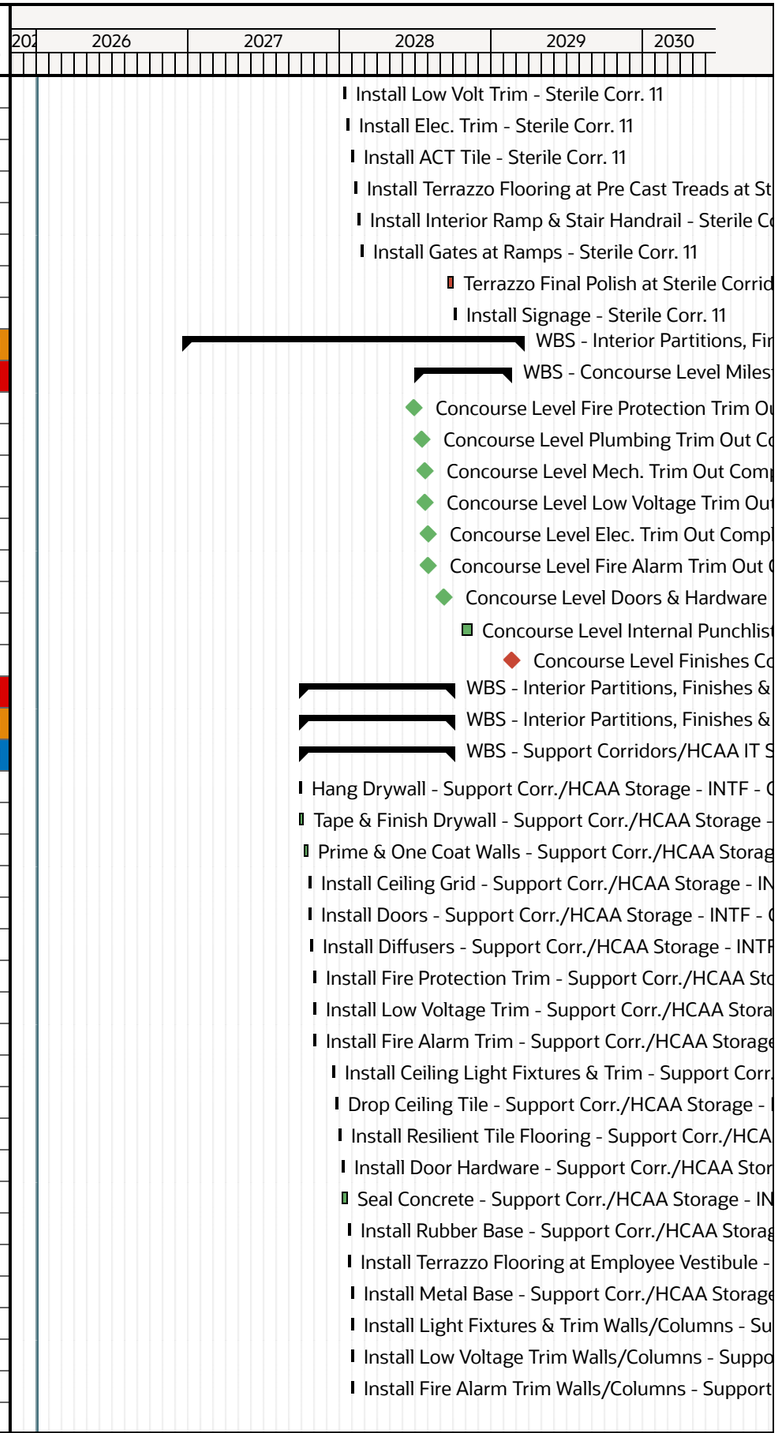


	ID	Name	Dur	Start	Finish	TF
8653	FN-C1-SR-955	Install BAS Trim Walls/Columns - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	27-Jan-28	2-Feb-28	183.0d
8654	FN-C1-SR-440	Install Crash Rails - Support Corr./HCAA Storage - INTF - Conc. 1	10.0d	3-Feb-28	16-Feb-28	173.0d
8655	FN-C1-SR-400	Apply Final Paint - Support Corr./HCAA Storage - INTF - Conc. 1	7.0d	11-Sep-28	19-Sep-28	29.0d
8656	FN-C1-SR-420	Install FF&E & Millwork - Support Corr./HCAA Storage - INTF - Conc. 1	10.0d	13-Sep-28	26-Sep-28	64.0d
8657	FN-C1-SR-460	Install Signage - Support Corr./HCAA Storage - INTF - Conc. 1	5.0d	27-Sep-28	3-Oct-28	64.0d
8658	WBS - Unassigned Airline Operations - INTF - C1		260.0d	20-Sep-27	26-Sep-28	64.0d
8659	FN-C1-O2-525	Hang Drywall - Un. Airline Ops. - INTF - C1	3.0d	20-Sep-27	22-Sep-27	5.0d
8660	FN-C1-O2-765	Tape & Finish Drywall - Un. Airline Ops. - INTF - C1	7.0d	23-Sep-27	1-Oct-27	137.0d
8661	FN-C1-O2-545	Prime & One Coat Walls - Un. Airline Ops. - INTF - C1	7.0d	4-Oct-27	12-Oct-27	137.0d
8662	FN-C1-O2-555	Install Ceiling Grid - Un. Airline Ops. - INTF - C1	5.0d	13-Oct-27	19-Oct-27	137.0d
8663	FN-C1-O2-565	Install Doors - Un. Airline Ops. - INTF - C1	5.0d	13-Oct-27	19-Oct-27	252.0d
8664	FN-C1-O2-595	Install Diffusers - Un. Airline Ops. - INTF - C1	5.0d	20-Oct-27	26-Oct-27	137.0d
8665	FN-C1-O2-605	Install Low Voltage Trim - Un. Airline Ops. - INTF - C1	5.0d	20-Oct-27	26-Oct-27	137.0d
8666	FN-C1-O2-615	Install Fire Alarm Trim - Un. Airline Ops. - INTF - C1	5.0d	20-Oct-27	26-Oct-27	137.0d
8667	FN-C1-O2-685	Install Door Hardware - Un. Airline Ops. - INTF - C1	5.0d	20-Oct-27	26-Oct-27	252.0d
8668	FN-C1-O2-635	Install Fire Protection Trim - Un. Airline Ops. - INTF - C1	3.0d	27-Oct-27	29-Oct-27	139.0d
8669	FN-C1-O2-585	Install Ceiling Light Fixtures & Trim - Un. Airline Ops. - INTF - C1	5.0d	24-Nov-27	2-Dec-27	112.0d
8670	FN-C1-O2-625	Drop Ceiling Tile - Un. Airline Ops. - INTF - C1	5.0d	3-Dec-27	9-Dec-27	112.0d
8671	FN-C1-O2-645	Install Tile Flooring - Un. Airline Ops. - INTF - C1	5.0d	10-Dec-27	16-Dec-27	112.0d
8672	FN-C1-O2-655	Install Plumbing Fixtures & Trim - Un. Airline Ops. - INTF - C1	20.0d	17-Dec-27	17-Jan-28	172.0d
8673	FN-C1-O2-695	Install Light Fixtures & Trim Walls/Columns - Un. Airline Ops. - INTF - C1	5.0d	17-Dec-27	23-Dec-27	196.0d
8674	FN-C1-O2-705	Install Low Voltage Trim Walls/Columns - Un. Airline Ops. - INTF - C1	5.0d	17-Dec-27	23-Dec-27	112.0d
8675	FN-C1-O2-715	Install Fire Alarm Trim Walls/Columns - Un. Airline Ops. - INTF - C1	5.0d	17-Dec-27	23-Dec-27	112.0d
8676	FN-C1-O2-775	Install BAS Trim Walls/Columns - Un. Airline Ops. - INTF - C1	5.0d	17-Dec-27	23-Dec-27	112.0d
8677	FN-C1-O2-735	Apply Final Paint - Un. Airline Ops. - INTF - C1	7.0d	21-Aug-28	29-Aug-28	29.0d
8678	FN-C1-O2-745	Install FF&E & Millwork - Un. Airline Ops. - INTF - C1	10.0d	23-Aug-28	6-Sep-28	73.0d
8679	FN-C1-O2-755	Install Signage - Un. Airline Ops. - INTF - C1	5.0d	20-Sep-28	26-Sep-28	64.0d
8680	WBS - Delta Airline Operations #4 - INTF - C1		21.0d	20-Sep-27	18-Oct-27	158.0d
8681	FN-C1-O4-470	Hang Drywall - Delta Airlines Operations #4 - INTF - C1	3.0d	20-Sep-27	22-Sep-27	5.0d
8682	FN-C1-O4-480	Tape & Finish Walls - Delta Airlines Operations #4 - INTF - C1	15.0d	23-Sep-27	13-Oct-27	158.0d
8683	FN-C1-O4-490	Install Doors & Hardware - Delta Airlines Operations #4 - INTF - C1	3.0d	14-Oct-27	18-Oct-27	158.0d
8684	WBS - Concession Storage - INTF - C1		255.0d	20-Sep-27	19-Sep-28	64.0d
8685	FN-C1-SR-525	Hang Drywall - Concession Storage - INTF - C1	3.0d	20-Sep-27	22-Sep-27	5.0d
8686	FN-C1-SR-925	Tape & Finish Drywall - Concession Storage - INTF - C1	7.0d	23-Sep-27	1-Oct-27	137.0d
8687	FN-C1-SR-545	Prime & One Coat Walls - Concession Storage - INTF - C1	7.0d	4-Oct-27	12-Oct-27	137.0d
8688	FN-C1-SR-555	Install Doors - Concession Storage - INTF - C1	5.0d	13-Oct-27	19-Oct-27	252.0d
8689	FN-C1-SR-645	Install Door Hardware - Concession Storage - INTF - C1	5.0d	20-Oct-27	26-Oct-27	252.0d
8690	FN-C1-SR-565	Install Ceiling Light Fixtures & Trim - Concession Storage - INTF - C1	5.0d	17-Nov-27	23-Nov-27	112.0d
8691	FN-C1-SR-575	Install Diffusers - Concession Storage - INTF - C1	5.0d	24-Nov-27	2-Dec-27	173.0d
8692	FN-C1-SR-605	Install Fire Protection Trim - Concession Storage - INTF - C1	3.0d	3-Dec-27	7-Dec-27	173.0d
8693	FN-C1-SR-585	Install Low Voltage Trim - Concession Storage - INTF - C1	5.0d	8-Dec-27	14-Dec-27	173.0d
8694	FN-C1-SR-595	Install Fire Alarm Trim - Concession Storage - INTF - C1	5.0d	8-Dec-27	14-Dec-27	173.0d

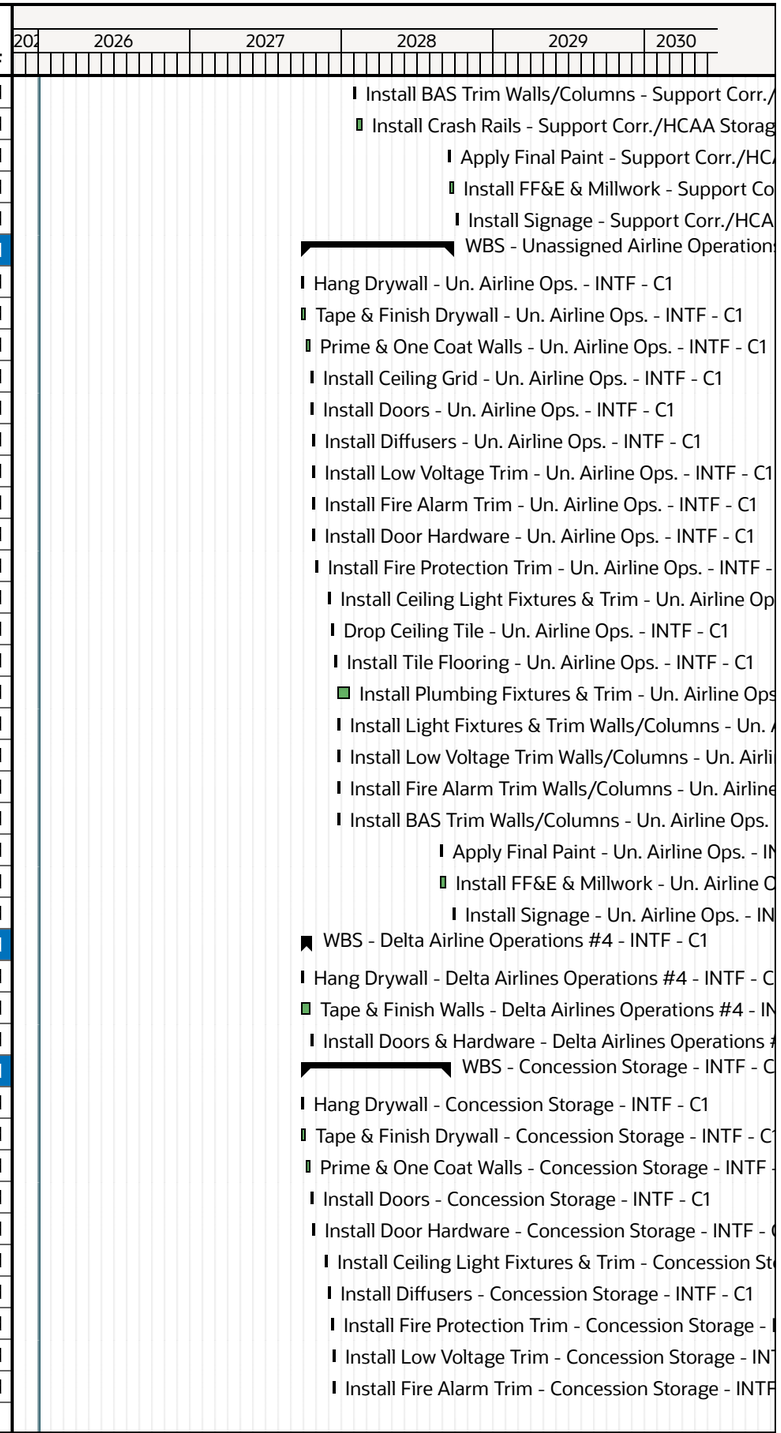


	ID	Name	Dur	Start	Finish	TF
8695	FN-C1-SR-615	Install Plumbing Fixtures & Trim - Concession Storage - INTF - C1	20.0d	15-Dec-27	13-Jan-28	173.0d
8696	FN-C1-SR-625	Seal Concrete - Concessions Storage - INTF - C1	10.0d	14-Jan-28	27-Jan-28	173.0d
8697	FN-C1-SR-635	Install Metal/Rubber Base - Concession Storage - INTF - C1	7.0d	28-Jan-28	7-Feb-28	173.0d
8698	FN-C1-SR-655	Apply Final Paint - Concession Storage - INTF - C1	7.0d	30-Aug-28	8-Sep-28	29.0d
8699	FN-C1-SR-665	Install Signage - Concession Storage - INTF - C1	5.0d	13-Sep-28	19-Sep-28	64.0d
8700	WBS - Employee Portal/Terminal Mgr. Office - INTF - C1		250.0d	20-Sep-27	12-Sep-28	64.0d
8701	FN-C1-SR-685	Hang Drywall - Employee Port/Term. Mgr. Office - INTF - C1	2.0d	20-Sep-27	21-Sep-27	5.0d
8702	FN-C1-SR-935	Tape & Finish Drywall - Employee Port/Term. Mgr. Office - INTF - C1	7.0d	22-Sep-27	30-Sep-27	177.0d
8703	FN-C1-SR-705	Prime & One Coat Walls - Employee Port/Term. Mgr. Office - INTF - C1	7.0d	1-Oct-27	11-Oct-27	177.0d
8704	FN-C1-SR-715	Install Ceiling Grid - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	12-Oct-27	18-Oct-27	177.0d
8705	FN-C1-SR-725	Install Doors - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	12-Oct-27	18-Oct-27	253.0d
8706	FN-C1-SR-745	Install Diffusers - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	19-Oct-27	25-Oct-27	213.0d
8707	FN-C1-SR-815	Install Door Hardware - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	19-Oct-27	25-Oct-27	253.0d
8708	FN-C1-SR-785	Install Fire Protection Trim - Employee Port/Term. Mgr. Office - INTF - C1	3.0d	26-Oct-27	28-Oct-27	215.0d
8709	FN-C1-SR-735	Install Ceiling Light Fixtures & Trim - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	3-Dec-27	9-Dec-27	146.0d
8710	FN-C1-SR-755	Install Low Voltage Trim - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	10-Dec-27	16-Dec-27	177.0d
8711	FN-C1-SR-765	Install Fire Alarm Trim - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	10-Dec-27	16-Dec-27	177.0d
8712	FN-C1-SR-775	Drop Ceiling Tile - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	17-Dec-27	23-Dec-27	177.0d
8713	FN-C1-SR-795	Install Carpet - Employee Port/Term. Mgr. Office - INTF - C1	2.0d	27-Dec-27	28-Dec-27	177.0d
8714	FN-C1-SR-825	Install Light Fixtures & Trim Walls/Columns - Employee Port/Term. Mgr. Office ...	5.0d	29-Dec-27	5-Jan-28	177.0d
8715	FN-C1-SR-835	Install Low Voltage Trim Walls/Columns - Employee Port/Term. Mgr. Office - IN...	5.0d	29-Dec-27	5-Jan-28	182.0d
8716	FN-C1-SR-845	Install Fire Alarm Trim Walls/Columns - Employee Port/Term. Mgr. Office - INT...	5.0d	29-Dec-27	5-Jan-28	182.0d
8717	FN-C1-SR-945	Install BAS Trim Walls/Columns - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	29-Dec-27	5-Jan-28	182.0d
8718	FN-C1-SR-855	Install Interior Specialties/Millwork/OFOI - Employee Port/Term. Mgr. Office - I...	5.0d	6-Jan-28	12-Jan-28	177.0d
8719	FN-C1-SR-865	Apply Final Paint - Employee Port/Term. Mgr. Office - INTF - C1	7.0d	10-Aug-28	18-Aug-28	29.0d
8720	FN-C1-SR-875	Install FF&E & Millwork - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	14-Aug-28	18-Aug-28	75.0d
8721	FN-C1-SR-885	Install Signage - Employee Port/Term. Mgr. Office - INTF - C1	5.0d	6-Sep-28	12-Sep-28	64.0d
8722	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 2		463.0d	16-Dec-26	10-Oct-28	64.0d
8723	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 2		463.0d	16-Dec-26	10-Oct-28	64.0d
8724	FN-C2-SP-1460	Field Measure & Fab. Decorative Glass Panels - APM Platform Area - INTF - C2	70.0d	31-Dec-26	8-Apr-27	387.0d
8725	FN-C2-SP-1490	Install High Ceiling Grid - APM Platform Area - INTF - C2	5.0d	30-Aug-27	3-Sep-27	0.0d
8726	FN-C2-SP-1210	Install Device Tiles High - APM Platform Area - INTF - C2	5.0d	7-Sep-27	13-Sep-27	0.0d
8727	FN-C2-SP-1430	Install High GFRP - APM Platform Area - INTF - C2	10.0d	14-Sep-27	27-Sep-27	0.0d
8728	FN-C2-SP-1500	Install Low Ceiling Grid - APM Platform Area - INTF - C2	10.0d	28-Sep-27	11-Oct-27	0.0d
8729	FN-C2-SP-1400	Install Device Tiles Low - APM Platform Area - INTF - C2	15.0d	12-Oct-27	1-Nov-27	0.0d
8730	FN-C2-SP-1530	Install Ceiling Light Fixtures & Low Trim - APM Platform Area - INTF - C2	15.0d	2-Nov-27	22-Nov-27	0.0d
8731	FN-C2-SP-1220	Install Ceiling Light Fixtures & High Trim - APM Platform Area - INTF - C2	10.0d	23-Nov-27	8-Dec-27	0.0d
8732	FN-C2-SP-1230	Drop Remaining Ceiling Tile High - APM Platform Area - INTF - C2	5.0d	9-Dec-27	15-Dec-27	0.0d
8733	FN-C2-SP-1520	Drop Remaining Ceiling Tile Low - APM Platform Area - INTF - C2	10.0d	16-Dec-27	30-Dec-27	0.0d
8734	FN-C2-SP-1540	Hang High Drywall - APM Platform Area - INTF - C2	10.0d	3-Jan-28	14-Jan-28	0.0d
8735	FN-C2-SP-1550	Tape & Finish High Level Walls - APM Platform Area - INTF - C2	10.0d	17-Jan-28	28-Jan-28	0.0d
8736	FN-C2-SP-1560	Prime & One Coat High Walls - APM Platform Area - INTF - C2	7.0d	31-Jan-28	8-Feb-28	0.0d

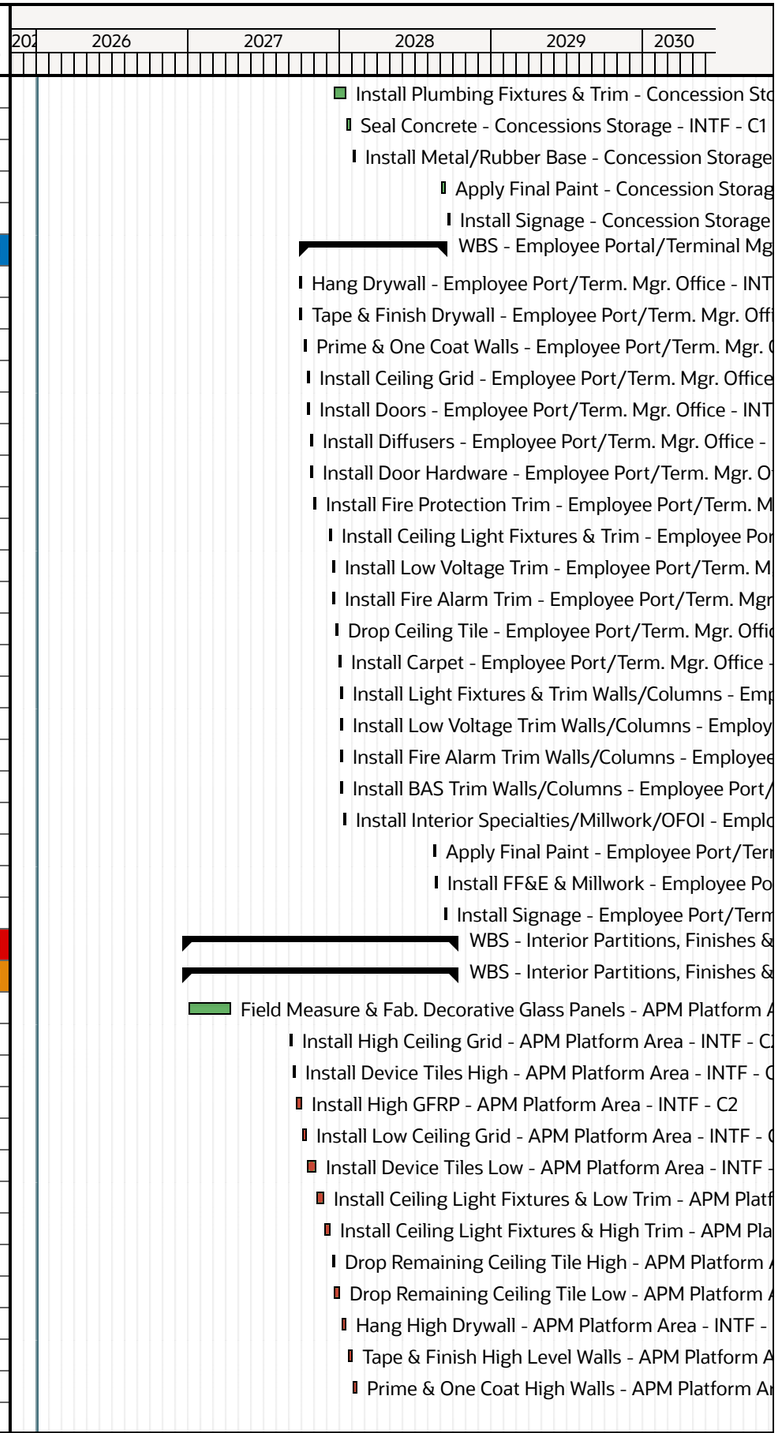


	ID	Name	Dur	Start	Finish	TF
8737	FN-C2-SP-1060	Trim Diffusers/Louvers - APM Platform Area - INTF - C2	5.0d	9-Feb-28	15-Feb-28	0.0d
8738	RI-C2-1490	Remove Dancefloor - APM Platform Area - INTF - C2	5.0d	16-Feb-28	22-Feb-28	0.0d
8739	FN-C2-SP-1580	Install Platform Level Ceiling Grid - APM Platform Area - INTF - C2	5.0d	23-Feb-28	29-Feb-28	0.0d
8740	FN-C2-SP-1570	Install Platform Level Device Tiles - APM Platform Area - INTF - C2	10.0d	1-Mar-28	14-Mar-28	0.0d
8741	FN-C2-SP-1410	Drop Remaining Ceiling Tile - Platform Level - APM Platform Area - INTF - C2	10.0d	15-Mar-28	28-Mar-28	0.0d
8742	FN-C2-SP-1480	Hang Platform Level Drywall - APM Platform Area - INTF - C2	10.0d	29-Mar-28	11-Apr-28	0.0d
8743	FN-C2-SP-1010	Tape & Finish Platform Level Walls - APM Platform Area - INTF - C2	10.0d	12-Apr-28	25-Apr-28	0.0d
8744	FN-C2-SP-1040	Install Doors - APM Platform Area - INTF - C2	5.0d	19-Apr-28	25-Apr-28	121.0d
8745	FN-C2-SP-1020	Prime & One Coat Platform Level Walls - APM Platform Area - INTF - C2	7.0d	26-Apr-28	4-May-28	0.0d
8746	FN-C2-SP-1140	Install Door Hardware - APM Platform Area - INTF - C2	5.0d	26-Apr-28	2-May-28	121.0d
8747	FN-C2-SP-1050	Install Terrazzo Flooring at APM/Circulation/SSCP Queue - APM Platform Area ...	20.0d	5-May-28	2-Jun-28	0.0d
8748	FN-C2-SP-1030	Install Low Voltage Trim - APM Platform Area - INTF - C2	7.0d	5-Jun-28	13-Jun-28	3.0d
8749	FN-C2-SP-1080	Install Column Covers at APM/Circulation - APM Platform Area - INTF - C2	10.0d	5-Jun-28	16-Jun-28	0.0d
8750	FN-C2-SP-1160	Install Fire Alarm Trim - APM Platform Area - INTF - C2	5.0d	5-Jun-28	9-Jun-28	10.0d
8751	FN-C2-SP-740	Interior Decorative Glass Panels (GL06)- Train Tube Glass A - APM Platform Are...	20.0d	19-Jun-28	17-Jul-28	64.0d
8752	FN-C2-SP-1070	Install Low Fire Protection Trim - APM Platform Area - INTF - C2	5.0d	19-Jun-28	23-Jun-28	84.0d
8753	FN-C2-SP-1100	Install Light Fixtures & Trim Walls/Columns - APM Platform Area - INTF - C2	5.0d	19-Jun-28	23-Jun-28	0.0d
8754	FN-C2-SP-1130	Install Low Voltage Trim Walls/Columns - APM Platform Area - INTF - C2	5.0d	26-Jun-28	30-Jun-28	0.0d
8755	FN-C2-SP-1470	Install BAS Trim Walls/Columns - APM Platform Area - INTF - C2	5.0d	26-Jun-28	30-Jun-28	0.0d
8756	FN-C2-SP-1170	Install Fire Alarm Trim Walls/Columns - APM Platform Area - INTF - C2	5.0d	3-Jul-28	10-Jul-28	0.0d
8757	FN-C2-SP-1110	Apply All Final Paint - APM Platform Area - INTF - C2	10.0d	11-Jul-28	24-Jul-28	0.0d
8758	FN-C2-SP-1190	Install Metal Base - APM Platform Area - INTF - C2	5.0d	11-Jul-28	17-Jul-28	84.0d
8759	FN-C2-SP-1420	Interior Decorative Glass Panels (GL06) - Train Tube Glass B - APM Platform Are...	20.0d	18-Jul-28	14-Aug-28	64.0d
8760	FN-C2-SP-1180	Install Entrance Floor Grilles at APM - APM Platform Area - INTF - C2	5.0d	25-Jul-28	31-Jul-28	74.0d
8761	FN-C2-SP-1120	Install FF&E - APM Platform Area - INTF - Conc. 2	10.0d	15-Aug-28	28-Aug-28	64.0d
8762	FN-C2-SP-1150	Install Signage - APM Platform Area - INTF - C2	5.0d	29-Aug-28	5-Sep-28	64.0d
8763	WBS - Shuttle Maintenance Platform/Train Tube - INTF - Concourse 2		90.0d	16-Dec-26	22-Apr-27	382.0d
8764	FN-C2-SP-1240	Hang Drywall / Plywood Walls - SMP/Train Tube - INTR - C2	10.0d	16-Dec-26	30-Dec-26	35.0d
8765	FN-C2-SP-1380	Install Resindek on Tubes - SMP/Train Tube - INTR - C2	6.0d	16-Dec-26	23-Dec-26	441.0d
8766	FN-C2-SP-1250	Apply Air Barrier- SMP/Train Tube - INTR - C2	5.0d	31-Dec-26	7-Jan-27	35.0d
8767	FN-C2-SP-1330	Install Stucco/Cement Plaster - SMP/Train Tube - INTR - C2	15.0d	8-Jan-27	28-Jan-27	35.0d
8768	FN-C2-SP-1260	Prime & One Coat Walls - SMP/Train Tube - INTR - C2	7.0d	8-Jan-27	18-Jan-27	48.0d
8769	FN-C2-SP-1340	Install Steel Pipe Guiderail - SMP/Train Tube - INTR - C2	5.0d	29-Jan-27	4-Feb-27	40.0d
8770	FN-C2-SP-1350	Install Joint Sealant - SMP/Train Tube - INTR - C2	5.0d	29-Jan-27	4-Feb-27	35.0d
8771	FN-C2-SP-1360	Install Wire Mesh Partition - SMP/Train Tube - INTR - C2	5.0d	5-Feb-27	11-Feb-27	35.0d
8772	FN-C2-SP-1450	Apply Final Paint - SMP/Train Tube - INTR - C2	5.0d	12-Feb-27	18-Feb-27	35.0d
8773	FN-C2-SP-1440	Install Metal Wall Panels - SMP/Train Tube - INTR - C2	20.0d	5-Mar-27	1-Apr-27	0.0d
8774	FN-C2-SP-1290	Install Ceiling Light Fixtures & Trim - SMP/Train Tube - INTR - C2	5.0d	2-Apr-27	8-Apr-27	0.0d
8775	FN-C2-SP-1270	Install Sliding Doors by Alstom - SMP/Train Tube - INTR - C2	10.0d	9-Apr-27	22-Apr-27	382.0d
8776	WBS - Exit Vestibules/Office Space/Support RR/Storage- INTF - Conc. 2		292.0d	18-Aug-27	10-Oct-28	64.0d
8777	FN-C2-SRR-940	Insulate Ceilings & Soffits - Exit Vestibules/Office Space/Support RR/Storage - I...	5.0d	18-Aug-27	24-Aug-27	5.0d
8778	FN-C2-SRR-970	Hang Hard Lid Ceilings - Support RR - INTF - C2	2.0d	25-Aug-27	26-Aug-27	5.0d

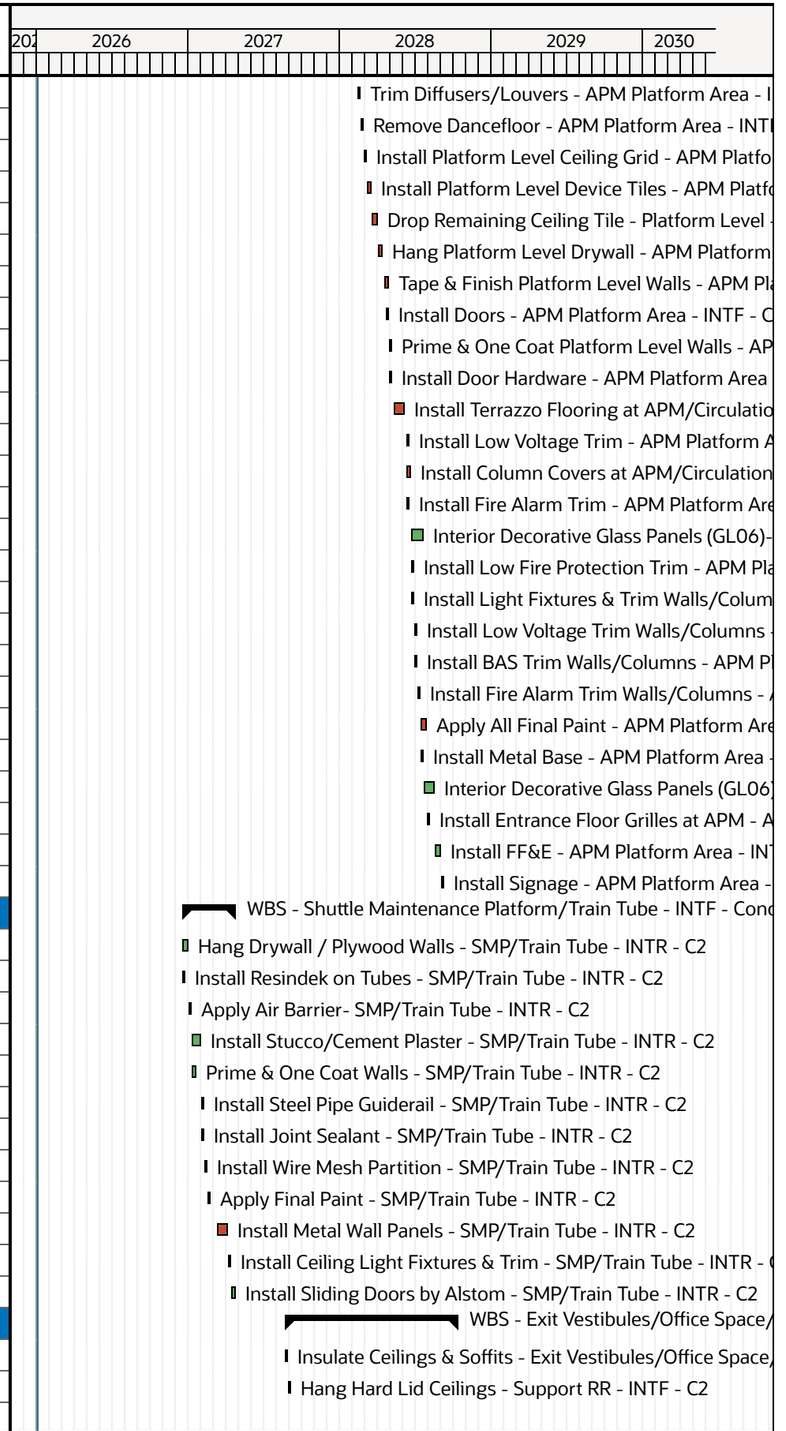

	ID	Name	Dur	Start	Finish	TF
8779	FN-C2-SRR-960	Hang Drywall Walls - Exit Vestibules/Office Space/Support RR/Storage - INTF -...	10.0d	3-Sep-27	17-Sep-27	5.0d
8780	FN-C2-SRR-1530	Tape Finish Drywall Walls - Exit Vestibules/Office Space/Support RR/Storage - I...	15.0d	20-Sep-27	8-Oct-27	106.0d
8781	FN-C2-SRR-1010	Prime & Paint Walls- Exit Vestibules/Office Space/Support RR/Storage - INTF - ...	7.0d	11-Oct-27	19-Oct-27	106.0d
8782	FN-C2-SRR-1040	Install Ceiling Grid & Device Tiles - Exit Vestibules/Office Space/Support RR/St...	10.0d	20-Oct-27	2-Nov-27	106.0d
8783	FN-C2-SRR-1020	Install Ceiling Light Fixtures & Trim - Exit Vestibules/Office Space/Support RR/...	10.0d	3-Nov-27	16-Nov-27	106.0d
8784	FN-C2-SRR-1050	Install Diffusers - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5.0d	3-Nov-27	9-Nov-27	111.0d
8785	FN-C2-SRR-1060	Install Low Voltage Trim - Exit Vestibules/Office Space/Support RR/Storage - I...	5.0d	3-Nov-27	9-Nov-27	111.0d
8786	FN-C2-SRR-1190	Install Fire Alarm Trim - Exit Vestibules/Office Space/Support RR/Storage - INT...	5.0d	3-Nov-27	9-Nov-27	111.0d
8787	FN-C2-SRR-1070	Install Fire Protection Trim - Exit Vestibules/Office Space/Support RR/Storage -...	3.0d	10-Nov-27	12-Nov-27	118.0d
8788	FN-C2-SRR-1080	Drop Remaining Ceiling Tile - Exit Vestibules/Office Space/Support RR/Storage...	10.0d	17-Nov-27	2-Dec-27	106.0d
8789	FN-C2-SRR-1090	Install Resilient Tile Flooring at 6461, 6462, 6465 - Exit Vestibules/Office Space...	10.0d	3-Dec-27	16-Dec-27	106.0d
8790	FN-C2-SRR-1220	Seal Concrete at Corridor - Exit Vestibules/Office Space/Support RR/Storage - I...	5.0d	3-Dec-27	9-Dec-27	106.0d
8791	FN-C2-SRR-1210	Install Resinous Flooring at Custodial 6470 - Exit Vestibules/Office Space/Supp...	5.0d	3-Dec-27	9-Dec-27	106.0d
8792	FN-C2-SRR-1510	Install Tile at Support RRs 6457, 6458 - Exit Vestibules/Office Space/Support R...	5.0d	3-Dec-27	9-Dec-27	111.0d
8793	FN-C2-SRR-1520	Install Carpet at TSM 6463 & Resolution Room 6464 - Exit Vestibules/Office Sp...	5.0d	10-Dec-27	16-Dec-27	106.0d
8794	FN-C2-SRR-1100	Install Partitions - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5.0d	17-Dec-27	23-Dec-27	106.0d
8795	FN-C2-SRR-1030	Install Doors - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5.0d	17-Dec-27	23-Dec-27	179.0d
8796	FN-C2-SRR-1110	Install Rubber Base - Exit Vestibules/Office Space/Support RR/Storage - INTF -...	5.0d	17-Dec-27	23-Dec-27	106.0d
8797	FN-C2-SRR-1160	Install Door Hardware - Exit Vestibules/Office Space/Support RR/Storage - INT...	3.0d	27-Dec-27	29-Dec-27	179.0d
8798	FN-C2-SRR-1120	Install Light Fixtures & Trim Walls/Columns - Exit Vestibules/Office Space/Sup...	5.0d	27-Dec-27	3-Jan-28	106.0d
8799	FN-C2-SRR-1130	Install Plumbing Trim - Exit Vestibules/Office Space/Support RR/Storage - INT...	2.0d	27-Dec-27	28-Dec-27	119.0d
8800	FN-C2-SRR-1150	Install Interior Specialties/Mounting Brackets/OFOI - Exit Vestibules/Office Spa...	10.0d	4-Jan-28	17-Jan-28	106.0d
8801	FN-C2-SRR-1170	Install Low Voltage Trim Walls/Columns - Exit Vestibules/Office Space/Support...	5.0d	18-Jan-28	24-Jan-28	106.0d
8802	FN-C2-SRR-1200	Install Fire Alarm Trim Walls/Columns - Exit Vestibules/Office Space/Support R...	5.0d	18-Jan-28	24-Jan-28	106.0d
8803	FN-C2-SRR-1540	Install BAS Trim Walls/Columns - Exit Vestibules/Office Space/Support RR/Sto...	5.0d	18-Jan-28	24-Jan-28	106.0d
8804	FN-C2-SRR-1140	Apply Final Paint - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	7.0d	1-Aug-28	9-Aug-28	29.0d
8805	FN-C2-SRR-1230	Install FF&E- Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5.0d	10-Aug-28	16-Aug-28	32.0d
8806	FN-C2-SRR-1240	Install Exterior Glazing & Doors at Exit Vestibule- Exit Vestibules/Office Space/...	15.0d	17-Aug-28	7-Sep-28	32.0d
8807	FN-C2-SRR-1180	Install Signage - Exit Vestibules/Office Space/Support RR/Storage - INTF - C2	5.0d	4-Oct-28	10-Oct-28	64.0d
8808	WBS - Delta Airlines Club Entry - INTF - C2		23.0d	27-Aug-27	29-Sep-27	171.0d
8809	FN-C2-CL-520	Hang Drywall Walls - Delta Airlines Club Entry/In-Flight Lounge - INTF - C2	5.0d	27-Aug-27	2-Sep-27	5.0d
8810	FN-C2-CL-530	Tape & Finish Walls - Delta Airlines Club Entry - INTF - C2	15.0d	3-Sep-27	24-Sep-27	171.0d
8811	FN-C2-CL-540	Install Doors & Hardware - Delta Airlines Club Entry - INTF - C2	3.0d	27-Sep-27	29-Sep-27	171.0d
8812	WBS - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2		245.0d	27-Aug-27	14-Aug-28	0.0d
8813	FN-C2-SR-1260	Hang Drywall Walls - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	27-Aug-27	2-Sep-27	5.0d
8814	FN-C2-SR-1510	Tape Finish Drywall Walls - HCAA Supp./Janitorial Break/Storage/Corridor - IN...	10.0d	3-Sep-27	17-Sep-27	111.0d
8815	FN-C2-SR-1270	Prime & Paint Walls- HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	7.0d	20-Sep-27	28-Sep-27	111.0d
8816	FN-C2-SR-1280	Install Ceiling Grid & Device Tiles - HCAA Supp./Janitorial Break/Storage/Corri...	10.0d	29-Sep-27	12-Oct-27	111.0d
8817	FN-C2-SR-1290	Install Ceiling Light Fixtures & Trim - HCAA Supp./Janitorial Break/Storage/Co...	10.0d	13-Oct-27	26-Oct-27	111.0d
8818	FN-C2-SR-1300	Install Diffusers - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	13-Oct-27	19-Oct-27	163.0d
8819	FN-C2-SR-1310	Install Low Voltage Trim - HCAA Supp./Janitorial Break/Storage/Corridor - INT...	5.0d	13-Oct-27	19-Oct-27	163.0d
8820	FN-C2-SR-1320	Install Fire Alarm Trim - HCAA Supp./Janitorial Break/Storage/Corridor - INTF ...	5.0d	13-Oct-27	19-Oct-27	163.0d

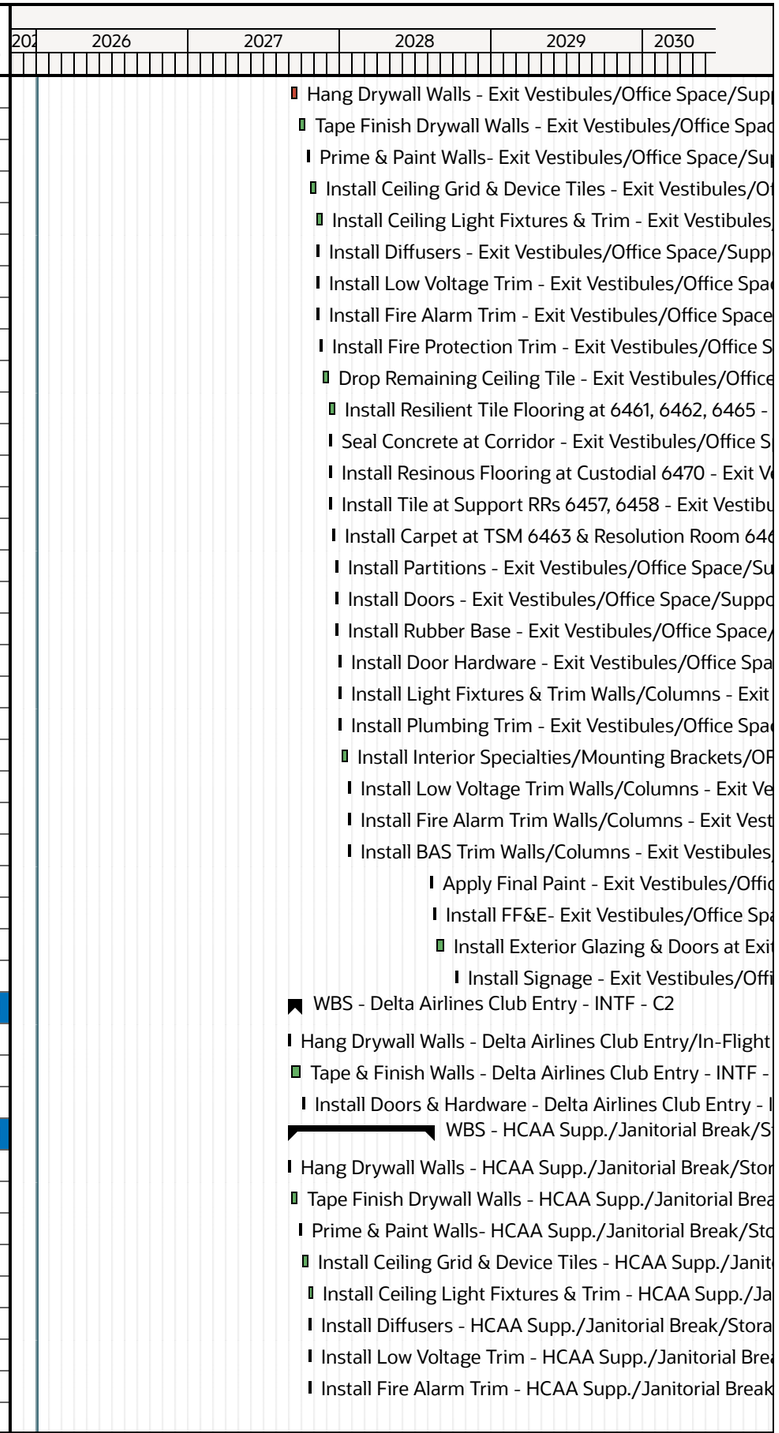


	ID	Name	Dur	Start	Finish	TF
8821	FN-C2-SR-1330	Install Fire Protection Trim - HCAA Supp./Janitorial Break/Storage/Corridor - I...	3.0d	20-Oct-27	22-Oct-27	165.0d
8822	FN-C2-SR-1340	Drop Remaining Ceiling Tile - HCAA Supp./Janitorial Break/Storage/Corridor - ...	5.0d	27-Oct-27	2-Nov-27	158.0d
8823	FN-C2-SR-1350	Install Resilient Tile Floor at Breakroom/Corridor 6496,6499 - HCAA Supp./Jan...	5.0d	3-Nov-27	9-Nov-27	158.0d
8824	FN-C2-SR-1380	Polish Concrete at HCAA Support 6498 - HCAA Supp./Janitorial Break/Storage...	5.0d	3-Nov-27	9-Nov-27	158.0d
8825	FN-C2-SR-1390	Install Resinous Flooring at Storage 6497 - HCAA Supp./Janitorial Break/Stora...	5.0d	3-Nov-27	9-Nov-27	158.0d
8826	FN-C2-SR-1360	Install Doors - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	10-Nov-27	16-Nov-27	173.0d
8827	FN-C2-SR-1370	Install Rubber Base - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	10-Nov-27	16-Nov-27	158.0d
8828	FN-C2-SR-1400	Install Partitions - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	10-Nov-27	16-Nov-27	158.0d
8829	FN-C2-SR-1410	Install Door Hardware - HCAA Supp./Janitorial Break/Storage/Corridor - INTF -...	3.0d	17-Nov-27	19-Nov-27	180.0d
8830	FN-C2-SR-1420	Install Plumbing Trim - HCAA Supp./Janitorial Break/Storage/Corridor - INTF -...	2.0d	17-Nov-27	18-Nov-27	166.0d
8831	FN-C2-SR-1430	Install Light Fixtures & Trim Walls/Columns - HCAA Supp./Janitorial Break/Sto...	5.0d	17-Nov-27	23-Nov-27	158.0d
8832	FN-C2-SR-1440	Install Interior Specialties/Mounting Brackets/OFOI - HCAA Supp./Janitorial Br...	5.0d	24-Nov-27	2-Dec-27	158.0d
8833	FN-C2-SR-1450	Install Low Voltage Trim Walls/Columns - HCAA Supp./Janitorial Break/Storag...	5.0d	3-Dec-27	9-Dec-27	158.0d
8834	FN-C2-SR-1460	Install Fire Alarm Trim Walls/Columns - HCAA Supp./Janitorial Break/Storage/...	5.0d	3-Dec-27	9-Dec-27	158.0d
8835	FN-C2-SR-1520	Install BAS Trim Walls/Columns - HCAA Supp./Janitorial Break/Storage/Corrid...	5.0d	3-Dec-27	9-Dec-27	158.0d
8836	FN-C2-SR-1470	Apply Final Paint - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	25-Jul-28	31-Jul-28	0.0d
8837	FN-C2-SR-1490	Install FF&E- HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	1-Aug-28	7-Aug-28	0.0d
8838	FN-C2-SR-1500	Install Signage - HCAA Supp./Janitorial Break/Storage/Corridor - INTF - C2	5.0d	8-Aug-28	14-Aug-28	0.0d
8839	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Mechanical - INTF - Conc. 2		73.0d	11-Nov-27	25-Feb-28	128.0d
8840	FN-C2-MR-2560	Hang, Tape & Finish Drywall - Mech. Room - INTF - C2	15.0d	11-Nov-27	3-Dec-27	85.0d
8841	FN-C2-MR-2570	Prime & First Coat - Mech. Room - INTF - C2	5.0d	6-Dec-27	10-Dec-27	113.0d
8842	FN-C2-MR-2580	Install Light Fixtures & Trim - Mech. Room - INTF - C2	5.0d	13-Dec-27	17-Dec-27	113.0d
8843	FN-C2-MR-2680	Install Fire Alarm Trim - Mech. Room - INTF - C2	5.0d	13-Dec-27	17-Dec-27	113.0d
8844	FN-C2-MR-2590	Install Doors - Mech. Room - INTF - C2	5.0d	20-Dec-27	27-Dec-27	113.0d
8845	FN-C2-MR-2660	Energize Power at AHU Disconnect - Mech. Room - INTF - C2	5.0d	20-Dec-27	27-Dec-27	168.0d
8846	FN-C2-MR-2610	Install Door Hardware - Mech. Room - INTF - C2	5.0d	28-Dec-27	4-Jan-28	113.0d
8847	FN-C2-MR-2630	Set Floor Drains - Mech. Room - INTF - C2	4.0d	5-Jan-28	10-Jan-28	113.0d
8848	FN-C2-MR-2620	Seal Concrete - Mech. Room - INTF - C2	5.0d	11-Jan-28	17-Jan-28	113.0d
8849	FN-C2-MR-2600	Apply Final Paint - Mech. Room - INTF - C2	10.0d	18-Jan-28	31-Jan-28	113.0d
8850	FN-C2-MR-2650	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - C2	15.0d	2-Feb-28	22-Feb-28	128.0d
8851	FN-C2-MR-2670	Start-up AHU - Mech. Room - INTF - C2	3.0d	23-Feb-28	25-Feb-28	128.0d
8852	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 3		341.0d	16-Jun-27	17-Oct-28	64.0d
8853	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - SSCP - INTF - Conc. 3		341.0d	16-Jun-27	17-Oct-28	64.0d
8854	WBS - SSCP - TSA Checkpoints - INTF - Conc. 3		331.0d	16-Jun-27	3-Oct-28	19.0d
8855	FN-C3-SS-1800	Field Measure & Fab. Decorative Glass Panels - SSCP Check Points - INTF - C3	70.0d	16-Jun-27	23-Sep-27	211.0d
8856	FN-C3-SS-140	Install Diffusers - SSCP Check Points - INTF - C3	5.0d	23-Jun-27	29-Jun-27	216.0d
8857	FN-C3-SS-10	Install Wall Insulation - SSCP Check Points - INTF - C3	5.0d	29-Jun-27	6-Jul-27	60.0d
8858	FN-C3-SS-20	Insulate Ceilings & Soffits - SSCP Check Points - INTF - C3	7.0d	29-Jun-27	8-Jul-27	220.0d
8859	FN-C3-SS-120	Install Doors - SSCP Check Points - INTF - C3	5.0d	9-Jul-27	15-Jul-27	220.0d
8860	FN-C3-SS-170	Install Wood Tile Baffle Ceiling - SSCP Check Points - INTF - C3	15.0d	25-Aug-27	15-Sep-27	177.0d
8861	FN-C3-SS-180	Apply Final Paint - SSCP Check Points - INTF - C3	10.0d	16-Sep-27	29-Sep-27	177.0d
8862	FN-C3-SS-190	Install Column Covers - SSCP Check Points - INTF - C3	10.0d	16-Sep-27	29-Sep-27	177.0d

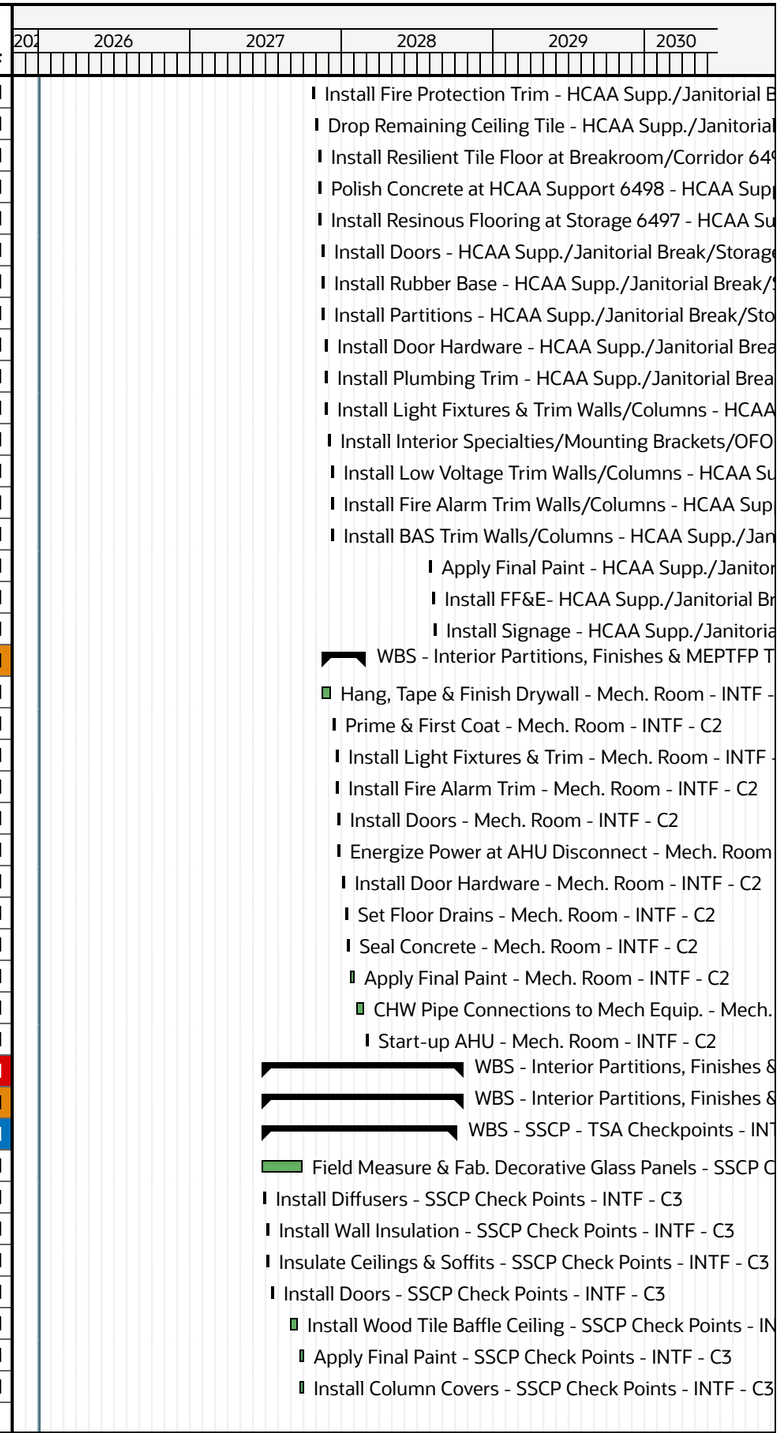

	ID	Name	Dur	Start	Finish	TF
8863	FN-C3-SS-30	Hang Drywall Walls - SSCP Check Points - INTF - C3	5.0d	23-Sep-27	29-Sep-27	5.0d
8864	FN-C3-SS-200	Install Door Hardware - SSCP Check Points - INTF - C3	5.0d	30-Sep-27	6-Oct-27	217.0d
8865	FN-C3-SS-210	Install Interior Specialties/Mounting Brackets/OFOI - SSCP Check Points - INTF...	10.0d	30-Sep-27	13-Oct-27	212.0d
8866	FN-C3-SS-50	Tape & Finish Walls - SSCP Check Points - INTF - C3	15.0d	30-Sep-27	20-Oct-27	185.0d
8867	FN-C3-SS-300	Install Stretched Fab.ric Wall System - East Wall - SSCP Check Points - INTF - C3	10.0d	30-Sep-27	13-Oct-27	177.0d
8868	FN-C3-SS-260	Install Carpet - SSCP Check Points - INTF - C3	10.0d	14-Oct-27	27-Oct-27	177.0d
8869	FN-C3-SS-70	Prime & One Coat Walls - SSCP Check Points - INTF - C3	7.0d	21-Oct-27	29-Oct-27	185.0d
8870	FN-C3-SS-240	Install FF&E - SSCP Check Points - INTF - Conc. 3	10.0d	28-Oct-27	10-Nov-27	182.0d
8871	FN-C3-SS-1770	Install Security Glazing - SSCP Check Points - INTF - C3	10.0d	28-Oct-27	10-Nov-27	177.0d
8872	FN-C3-SS-320	Install Millwork at Planter - SSCP Check Points - INTF - Conc. 3	5.0d	11-Nov-27	17-Nov-27	182.0d
8873	FN-C3-SS-1760	Install Stanchion Queue System - SSCP Check Points - INTF - Conc. 3	5.0d	11-Nov-27	17-Nov-27	187.0d
8874	FN-C3-SS-1790	Install Decorative Glass Panels (GL03A/B)- SSCP Check Points - INTF - C3	10.0d	11-Nov-27	24-Nov-27	177.0d
8875	FN-C3-SS-100	Install Ceiling Light Fixtures & Trim - SSCP Check Points - INTF - C3	10.0d	17-Dec-27	3-Jan-28	146.0d
8876	FN-C3-SS-150	Install Fire Protection Trim - SSCP Check Points - INTF - C3	3.0d	17-Dec-27	21-Dec-27	146.0d
8877	FN-C3-SS-160	Install Low Voltage Trim - SSCP Check Points - INTF - C3	7.0d	17-Dec-27	28-Dec-27	146.0d
8878	FN-C3-SS-270	Install Fire Alarm Trim - SSCP Check Points - INTF - C3	5.0d	17-Dec-27	23-Dec-27	148.0d
8879	FN-C3-SS-220	Install Light Fixtures & Trim Walls/Columns - SSCP Check Points - INTF - C3	5.0d	29-Dec-27	5-Jan-28	146.0d
8880	FN-C3-SS-230	Install Low Voltage Trim Walls/Columns - SSCP Check Points - INTF - C3	5.0d	6-Jan-28	12-Jan-28	146.0d
8881	FN-C3-SS-280	Install Fire Alarm Trim Walls/Columns - SSCP Check Points - INTF - C3	5.0d	6-Jan-28	12-Jan-28	146.0d
8882	FN-C3-SS-1820	Install BAS Trim Walls/Columns - SSCP Check Points - INTF - C3	5.0d	6-Jan-28	12-Jan-28	146.0d
8883	FN-C3-SS-310	Install Metal Base - SSCP Check Points - INTF - C3	10.0d	13-Jan-28	26-Jan-28	146.0d
8884	FN-C3-SS-250	Install Signage - SSCP Check Points - INTF - C3	5.0d	15-Aug-28	21-Aug-28	0.0d
8885	FN-C3-SS-290	Install Security Screening Equip. - SSCP - INTF - Conc. 3 (By Others)	30.0d	22-Aug-28	3-Oct-28	19.0d
8886	WBS - Police Office/Interview/Crew Corridor - INTF - Conc. 3		332.0d	29-Jun-27	17-Oct-28	64.0d
8887	FN-C3-SS-1750	Install Wall Insulation - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	29-Jun-27	6-Jul-27	108.0d
8888	FN-C3-SS-1530	Hang Drywall Walls - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	30-Sep-27	6-Oct-27	48.0d
8889	FN-C3-SS-1780	Tape Finish Drywall Walls - Police Office/Interview/Crew Corridor - INTF- C3	10.0d	7-Oct-27	20-Oct-27	182.0d
8890	FN-C3-SS-1540	Prime & Paint Walls- Police Office/Interview/Crew Corridor - INTF- C3	7.0d	21-Oct-27	29-Oct-27	182.0d
8891	FN-C3-SS-1550	Install Ceiling Grid & Device Tiles - Police Office/Interview/Crew Corridor - INTF...	10.0d	1-Nov-27	12-Nov-27	182.0d
8892	FN-C3-SS-1570	Install Diffusers - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Nov-27	19-Nov-27	187.0d
8893	FN-C3-SS-1580	Install Low Voltage Trim - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Nov-27	19-Nov-27	187.0d
8894	FN-C3-SS-1590	Install Fire Alarm Trim - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Nov-27	19-Nov-27	187.0d
8895	FN-C3-SS-1600	Install Fire Protection Trim - Police Office/Interview/Crew Corridor - INTF- C3	3.0d	22-Nov-27	24-Nov-27	194.0d
8896	FN-C3-SS-1560	Install Ceiling Light Fixtures & Trim - Police Office/Interview/Crew Corridor - IN...	10.0d	4-Jan-28	17-Jan-28	150.0d
8897	FN-C3-SS-1610	Drop Remaining Ceiling Tile - Police Office/Interview/Crew Corridor - INTF- C3	10.0d	18-Jan-28	31-Jan-28	150.0d
8898	FN-C3-SS-1620	Install Resilient Tile Flooring - Police Office/Interview/Crew Corridor - INTF- C3	10.0d	1-Feb-28	14-Feb-28	150.0d
8899	FN-C3-SS-1630	Install Carpet - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	1-Feb-28	7-Feb-28	155.0d
8900	FN-C3-SS-1640	Install Partitions - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Feb-28	21-Feb-28	150.0d
8901	FN-C3-SS-1650	Install Doors - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Feb-28	21-Feb-28	167.0d
8902	FN-C3-SS-1660	Install Rubber Base - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	15-Feb-28	21-Feb-28	150.0d
8903	FN-C3-SS-1670	Install Door Hardware - Police Office/Interview/Crew Corridor - INTF- C3	3.0d	22-Feb-28	24-Feb-28	167.0d
8904	FN-C3-SS-1680	Install Light Fixtures & Trim Walls/Columns - Police Office/Interview/Crew Corri...	5.0d	22-Feb-28	28-Feb-28	150.0d




	ID	Name	Dur	Start	Finish	TF
8905	FN-C3-SS-1690	Install Interior Specialties/Mounting Brackets/OFOI - Police Office/Interview/Cr...	10.0d	29-Feb-28	13-Mar-28	150.0d
8906	FN-C3-SS-1700	Install Low Voltage Trim Walls/Columns - Police Office/Interview/Crew Corridor...	5.0d	14-Mar-28	20-Mar-28	150.0d
8907	FN-C3-SS-1710	Install Fire Alarm Trim Walls/Columns - Police Office/Interview/Crew Corridor - ...	5.0d	14-Mar-28	20-Mar-28	150.0d
8908	FN-C3-SS-1810	Install BAS Trim Walls/Columns - Police Office/Interview/Crew Corridor - INTF- ...	5.0d	14-Mar-28	20-Mar-28	150.0d
8909	FN-C3-SS-1720	Apply Final Paint - Police Office/Interview/Crew Corridor - INTF- C3	7.0d	21-Mar-28	29-Mar-28	150.0d
8910	FN-C3-SS-1730	Install FF&E- Police Office/Interview/Crew Corridor - INTF- C3	5.0d	30-Mar-28	5-Apr-28	195.0d
8911	FN-C3-SS-1740	Install Signage - Police Office/Interview/Crew Corridor - INTF- C3	5.0d	11-Oct-28	17-Oct-28	64.0d
8912	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 4		187.0d	4-Jan-28	25-Sep-28	80.0d
8913	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 4		187.0d	4-Jan-28	25-Sep-28	80.0d
8914	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Holdrooms/Office Space - INTF - Conc. 4		187.0d	4-Jan-28	25-Sep-28	80.0d
8915	FN-CN-HR-1190	Hang, Tape & Finish Drywall Walls & Ceilings - Holdrooms/Offices - INTF - C4	20.0d	4-Jan-28	31-Jan-28	36.0d
8916	FN-CN-HR-1230	Install Ceiling Grid & Device Tiles - Holdrooms/Offices - INTF - C4	15.0d	1-Feb-28	21-Feb-28	36.0d
8917	FN-CN-HR-1240	Install Ceiling Light Fixtures & Trim - Holdrooms/Offices - INTF - C4	10.0d	22-Feb-28	6-Mar-28	46.0d
8918	FN-CN-HR-1250	Install Diffusers - Holdrooms/Offices - INTF - C4	20.0d	22-Feb-28	20-Mar-28	36.0d
8919	FN-CN-HR-1260	Install Ceiling Low Voltage Trim - Holdrooms/Offices - INTF - C4	10.0d	22-Feb-28	6-Mar-28	46.0d
8920	FN-CN-HR-1270	Install Ceiling Fire Alarm Trim - Holdrooms/Offices - INTF - C4	10.0d	22-Feb-28	6-Mar-28	46.0d
8921	FN-CN-HR-1400	Install Fire Protection Trim - Holdrooms/Offices - INTF - C4	10.0d	22-Feb-28	6-Mar-28	46.0d
8922	FN-CN-HR-1280	Install Remaining Ceiling Tile - Holdrooms/Offices - INTF - C4	15.0d	21-Mar-28	10-Apr-28	36.0d
8923	FN-CN-HR-1300	Install Column Covers - Holdrooms/Offices - INTF - C4	16.0d	11-Apr-28	2-May-28	41.0d
8924	FN-CN-HR-2210	Install Exterior Wall Tile at Interview/Waiting - Holdrooms/Offices - INTF - C4	5.0d	3-May-28	9-May-28	41.0d
8925	FN-CN-HR-2250	Install Metal Base at Interview/Waiting - Holdrooms/Offices - INTF - C4	5.0d	10-May-28	16-May-28	41.0d
8926	FN-CN-HR-1290	Install Carpet at Holdroom/Concessions Bar - Holdrooms/Offices - INTF - C4	8.0d	17-May-28	26-May-28	41.0d
8927	FN-CN-HR-1320	Install Pedestrian Control Devices - Holdrooms/Offices - INTF - C4	20.0d	30-May-28	26-Jun-28	41.0d
8928	FN-CN-HR-2170	Install Carpet Tile at Interview/Waiting- Holdrooms/Offices - INTF - C4	5.0d	30-May-28	5-Jun-28	88.0d
8929	FN-CN-HR-2400	Install Glass Glazing - Holdrooms/Offices - INTF - C4	5.0d	30-May-28	5-Jun-28	88.0d
8930	FN-CN-HR-2540	Install Walkway Threshold at PBB - Holdrooms/Offices - INTF - C4	2.0d	30-May-28	31-May-28	135.0d
8931	FN-CN-HR-1340	Install Light Fixtures & Trim Floor/Walls/Columns - Holdrooms/Offices - INTF -...	10.0d	27-Jun-28	11-Jul-28	73.0d
8932	FN-CN-HR-1350	Install Plumbing Trim - Holdrooms/Offices - INTF - C4	2.0d	27-Jun-28	28-Jun-28	41.0d
8933	FN-CN-HR-1380	Install Low Voltage Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C4	10.0d	27-Jun-28	11-Jul-28	53.0d
8934	FN-CN-HR-2550	Install BAS Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C4	10.0d	27-Jun-28	11-Jul-28	53.0d
8935	FN-CN-HR-2200	Install Mech. Trim - Holdrooms/Offices - INTF - C4	10.0d	29-Jun-28	13-Jul-28	41.0d
8936	FN-CN-HR-1360	Install Fire Alarm Trim Walls/Columns - Holdrooms/Offices - INTF - C4	10.0d	14-Jul-28	27-Jul-28	41.0d
8937	FN-CN-HR-1310	Install Doors & Hardware - Holdrooms/Offices - INTF - C4	5.0d	28-Jul-28	3-Aug-28	41.0d
8938	FN-CN-HR-1330	Apply Final Paint - Holdrooms/Offices - INTF - C4	5.0d	4-Aug-28	10-Aug-28	41.0d
8939	FN-CN-HR-1370	Install FF&E - Holdrooms/Offices - INTF - C4	15.0d	11-Aug-28	31-Aug-28	71.0d
8940	FN-CN-HR-2420	Install Millwork at Gate Podiums - Holdrooms/Offices - INTF - C4	20.0d	11-Aug-28	8-Sep-28	85.0d
8941	FN-CN-HR-2430	Install Misc. Millwork - Holdrooms/Offices - INTF - C4	6.0d	11-Sep-28	18-Sep-28	85.0d
8942	FN-CN-HR-1390	Install Signage & Dimensional Text - Holdrooms/Offices - INTF - C4	5.0d	19-Sep-28	25-Sep-28	60.0d
8943	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 5		223.0d	2-Nov-27	18-Sep-28	60.0d
8944	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 5		223.0d	2-Nov-27	18-Sep-28	60.0d
8945	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Holdrooms/Office Space - INTF - Conc. 5		223.0d	2-Nov-27	18-Sep-28	60.0d
8946	FN-CN-HR-1410	Hang, Tape & Finish Drywall Walls & Ceilings - Holdrooms/Offices - INTF - C5	20.0d	2-Nov-27	1-Dec-27	57.0d

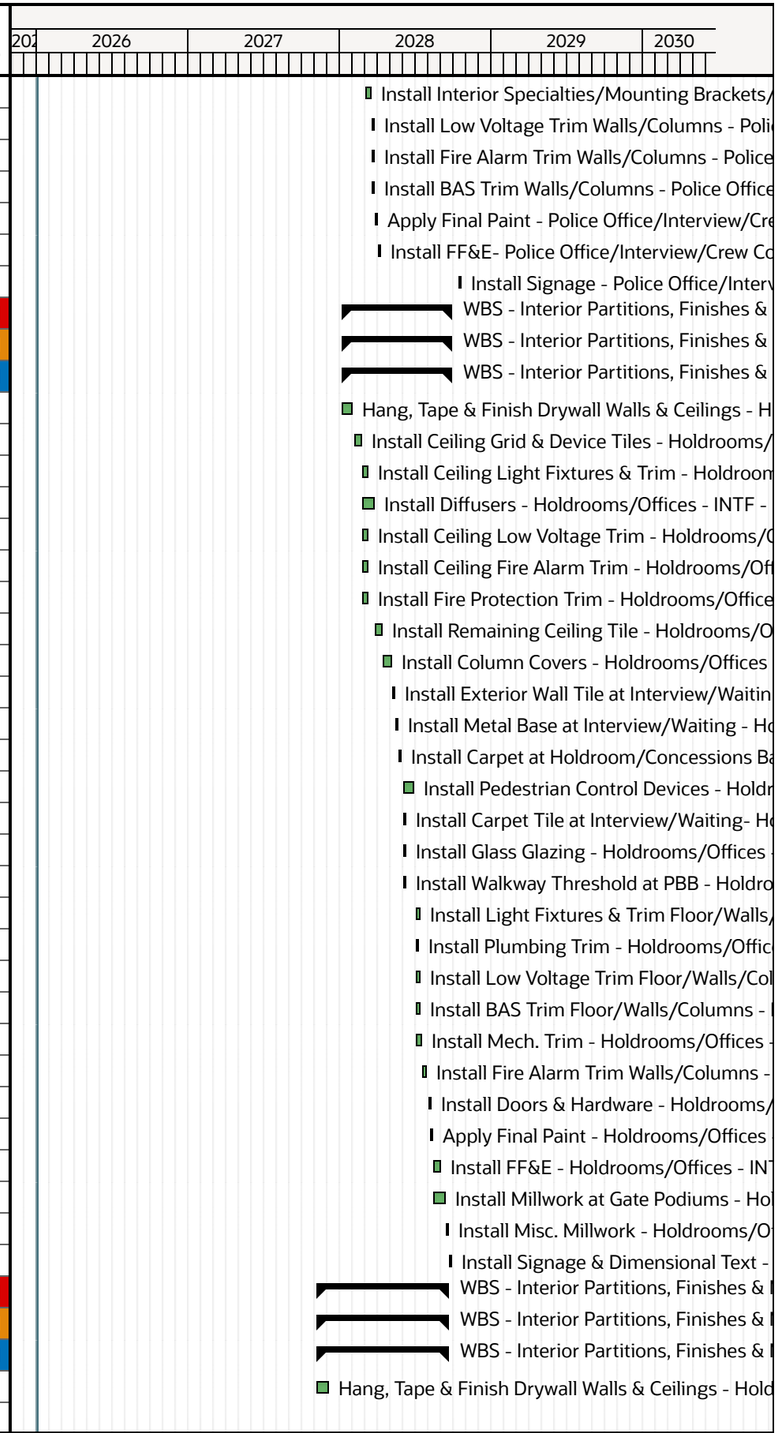


	ID	Name	Dur	Start	Finish	TF
8947	FN-CN-HR-1420	Install Ceiling Grid & Device Tiles - Holdrooms/Offices - INTF - C5	15.0d	2-Dec-27	22-Dec-27	80.0d
8948	FN-CN-HR-1440	Install Diffusers - Holdrooms/Offices - INTF - C5	5.0d	23-Dec-27	30-Dec-27	100.0d
8949	FN-CN-HR-1450	Install Ceiling Low Voltage Trim - Holdrooms/Offices - INTF - C5	7.0d	23-Dec-27	4-Jan-28	98.0d
8950	FN-CN-HR-1460	Install Ceiling Fire Alarm Trim - Holdrooms/Offices - INTF - C5	7.0d	23-Dec-27	4-Jan-28	98.0d
8951	FN-CN-HR-1470	Install Fire Protection Trim - Holdrooms/Offices - INTF - C5	7.0d	23-Dec-27	4-Jan-28	98.0d
8952	FN-CN-HR-1430	Install Ceiling Light Fixtures & Trim - Holdrooms/Offices - INTF - C5	7.0d	19-Jan-28	27-Jan-28	63.0d
8953	FN-CN-HR-1480	Drop Remaining Ceiling Tile - Holdrooms/Offices - INTF - C5	7.0d	28-Jan-28	7-Feb-28	81.0d
8954	FN-CN-HR-1490	Install Column Covers at Holdroom/Concessions Dining - Holdrooms/Offices - I...	20.0d	8-Feb-28	6-Mar-28	107.0d
8955	FN-CN-HR-1500	Apply Final Paint - Holdrooms/Offices - INTF - C5	5.0d	2-Jun-28	8-Jun-28	45.0d
8956	FN-CN-HR-1520	Install Carpet at Holdroom/Future Concessions Bar - Holdrooms/Offices - INTF...	8.0d	9-Jun-28	20-Jun-28	45.0d
8957	FN-CN-HR-1510	Install Pedestrian Control Devices - Holdrooms/Offices - INTF - C5	12.0d	21-Jun-28	7-Jul-28	45.0d
8958	FN-CN-HR-2260	Install Glass Wall System at Holdroom/Future Concessions (D53/D52) - Holdro...	10.0d	21-Jun-28	5-Jul-28	72.0d
8959	FN-CN-HR-2370	Install Exterior Tile/Base at Concessions Support - Holdrooms/Offices - INTF - C5	5.0d	21-Jun-28	27-Jun-28	77.0d
8960	FN-CN-HR-2410	Install Glass Glazing - Holdrooms/Offices - INTF - C5	15.0d	21-Jun-28	12-Jul-28	67.0d
8961	FN-CN-HR-2530	Install Walkway Threshold at PBB - Holdrooms/Offices - INTF - C5	2.0d	21-Jun-28	22-Jun-28	90.0d
8962	FN-CN-HR-1540	Install Plumbing Trim - Holdrooms/Offices - INTF - C5	5.0d	10-Jul-28	14-Jul-28	45.0d
8963	FN-CN-HR-1560	Install Low Voltage Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C5	5.0d	10-Jul-28	14-Jul-28	65.0d
8964	FN-CN-HR-2580	Install BAS Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C5	5.0d	10-Jul-28	14-Jul-28	65.0d
8965	FN-CN-HR-1530	Install Light Fixtures & Trim Floor/Walls/Columns - Holdrooms/Offices - INTF -...	5.0d	13-Jul-28	19-Jul-28	67.0d
8966	FN-CN-HR-2220	Install Mech. Trim - Holdrooms/Offices - INTF - C5	5.0d	17-Jul-28	21-Jul-28	55.0d
8967	FN-CN-HR-1550	Install Fire Alarm Trim Walls/Columns - Holdrooms/Offices - INTF - C5	5.0d	24-Jul-28	28-Jul-28	55.0d
8968	FN-CN-HR-1570	Install Doors & Hardware - Holdrooms/Offices - INTF - C5	5.0d	31-Jul-28	4-Aug-28	55.0d
8969	FN-CN-HR-2380	Install Millwork at Holdrooms/Concessions Dining (ALL) - Holdrooms/Offices - ...	15.0d	7-Aug-28	25-Aug-28	60.0d
8970	FN-CN-HR-1580	Install FF&E - Holdrooms/Offices - INTF - C5	10.0d	28-Aug-28	11-Sep-28	60.0d
8971	FN-CN-HR-1590	Install Signage & Dimensional Text - Holdrooms/Offices - INTF - C5	5.0d	12-Sep-28	18-Sep-28	60.0d
8972	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 6		205.0d	12-Oct-27	1-Aug-28	88.0d
8973	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 6		205.0d	12-Oct-27	1-Aug-28	88.0d
8974	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Holdrooms/Office Space - INTF - Conc. 6		205.0d	12-Oct-27	1-Aug-28	88.0d
8975	FN-CN-HR-1600	Hang, Tape & Finish Drywall Walls & Ceilings - Holdrooms/Offices - INTF - C6	15.0d	12-Oct-27	1-Nov-27	57.0d
8976	FN-CN-HR-2280	Install Exterior Wall Tile at Interview/Waiting/Mech.- Holdrooms/Offices - INTF...	5.0d	2-Nov-27	8-Nov-27	128.0d
8977	FN-CN-HR-2320	Install Planters at Interview/Waiting/Mech.- Holdrooms/Offices - INTF - C6	10.0d	9-Nov-27	22-Nov-27	128.0d
8978	FN-CN-HR-1610	Install Ceiling Grid & Device Tiles - Holdrooms/Offices - INTF - C6	10.0d	14-Dec-27	28-Dec-27	52.0d
8979	FN-CN-HR-1630	Install Diffusers - Holdrooms/Offices - INTF - C6	5.0d	29-Dec-27	5-Jan-28	54.0d
8980	FN-CN-HR-1640	Install Ceiling Low Voltage Trim - Holdrooms/Offices - INTF - C6	7.0d	29-Dec-27	7-Jan-28	52.0d
8981	FN-CN-HR-1650	Install Ceiling Fire Alarm Trim - Holdrooms/Offices - INTF - C6	7.0d	29-Dec-27	7-Jan-28	52.0d
8982	FN-CN-HR-1660	Install Fire Protection Trim - Holdrooms/Offices - INTF - C6	7.0d	29-Dec-27	7-Jan-28	52.0d
8983	FN-CN-HR-1620	Install Ceiling Light Fixtures & Trim - Holdrooms/Offices - INTF - C6	7.0d	10-Jan-28	18-Jan-28	45.0d
8984	FN-CN-HR-1670	Drop Remaining Ceiling Tile - Holdrooms/Offices - INTF - C6	7.0d	19-Jan-28	27-Jan-28	45.0d
8985	FN-CN-HR-2460	Install Column Cover Framing - Holdrooms/Offices - INTF - C6	12.0d	28-Jan-28	14-Feb-28	45.0d
8986	FN-CN-HR-1680	Install Column Covers - Holdrooms/Offices - INTF - C6	12.0d	15-Feb-28	1-Mar-28	45.0d
8987	FN-CN-HR-1700	Install Pedestrian Control Devices - Holdrooms/Offices - INTF - C6	15.0d	2-Mar-28	22-Mar-28	45.0d
8988	FN-CN-HR-1710	Install Carpet at Holdroom/Future Concessions - Holdrooms/Offices - INTF - C6	8.0d	23-Mar-28	3-Apr-28	45.0d




	ID	Name	Dur	Start	Finish	TF
8989	FN-CN-HR-2180	Install Carpet Tile at Waiting/Interview - Holdrooms/Offices - INTF - C6	5.0d	4-Apr-28	10-Apr-28	52.0d
8990	FN-CN-HR-2300	Install Athletic Resilient Flooring at KPA- Holdrooms/Offices - INTF - C6	5.0d	4-Apr-28	10-Apr-28	45.0d
8991	FN-CN-HR-2470	Install Glass Glazing - Holdrooms/Offices - INTF - C6	15.0d	4-Apr-28	24-Apr-28	113.0d
8992	FN-CN-HR-2310	Install Millwork at KPA/Concessions Future F&B - Holdrooms/Offices - INTF - C6	7.0d	11-Apr-28	19-Apr-28	45.0d
8993	FN-CN-HR-1720	Install Light Fixtures & Trim Floor/Walls/Columns - Holdrooms/Offices - INTF -...	5.0d	20-Apr-28	26-Apr-28	45.0d
8994	FN-CN-HR-2290	Install Metal Base - Holdrooms/Offices - INTF - C6	5.0d	20-Apr-28	26-Apr-28	55.0d
8995	FN-CN-HR-2520	Install Walkway Threshold at PBB - Holdrooms/Offices - INTF - C6	2.0d	25-Apr-28	26-Apr-28	113.0d
8996	FN-CN-HR-1730	Install Plumbing Trim - Holdrooms/Offices - INTF - C6	5.0d	27-Apr-28	3-May-28	45.0d
8997	FN-CN-HR-1750	Install Low Voltage Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C6	5.0d	27-Apr-28	3-May-28	55.0d
8998	FN-CN-HR-2570	Install BAS Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C6	5.0d	27-Apr-28	3-May-28	55.0d
8999	FN-CN-HR-2270	Install Mech. Trim - Holdrooms/Offices - INTF - C6	5.0d	4-May-28	10-May-28	45.0d
9000	FN-CN-HR-1740	Install Fire Alarm Trim Walls/Columns - Holdrooms/Offices - INTF - C6	5.0d	11-May-28	17-May-28	45.0d
9001	FN-CN-HR-1760	Install Doors & Hardware - Holdrooms/Offices - INTF - C6	5.0d	18-May-28	24-May-28	45.0d
9002	FN-CN-HR-1690	Apply Final Paint - Holdrooms/Offices - INTF - C6	5.0d	25-May-28	1-Jun-28	45.0d
9003	FN-CN-HR-2440	Install Millwork at Gate Podiums - Holdrooms/Offices - INTF - C6	12.0d	2-Jun-28	19-Jun-28	88.0d
9004	FN-CN-HR-2450	Install Misc. Millwork - Holdrooms/Offices - INTF - C6	15.0d	20-Jun-28	11-Jul-28	88.0d
9005	FN-CN-HR-1770	Install FF&E at Holdroom/Concessions/KPA - Holdrooms/Offices - INTF - C6	10.0d	12-Jul-28	25-Jul-28	88.0d
9006	FN-CN-HR-1780	Install Signage & Dimensional Text - Holdrooms/Offices - INTF - C6	5.0d	26-Jul-28	1-Aug-28	88.0d
9007	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 7		175.0d	25-Aug-27	2-May-28	121.0d
9008	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 7		175.0d	25-Aug-27	2-May-28	121.0d
9009	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Holdrooms/Office Space - INTF - Conc. 7		175.0d	25-Aug-27	2-May-28	121.0d
9010	FN-CN-HR-1790	Hang, Tape & Finish Drywall Walls & Ceilings - Holdrooms/Offices - INTF - C7	15.0d	25-Aug-27	15-Sep-27	75.0d
9011	FN-CN-HR-2340	Install Exterior Wall Tile at Waiting/Interview- Holdrooms/Offices - INTF - C7	5.0d	16-Sep-27	22-Sep-27	201.0d
9012	FN-CN-HR-2350	Install Planters at Waiting/Interview- Holdrooms/Offices - INTF - C7	5.0d	23-Sep-27	29-Sep-27	261.0d
9013	FN-CN-HR-2360	Install Metal Base- Holdrooms/Offices - INTF - C7	5.0d	30-Sep-27	6-Oct-27	261.0d
9014	FN-CN-HR-1800	Install Ceiling Grid & Device Tiles - Holdrooms/Offices - INTF - C7	10.0d	14-Dec-27	28-Dec-27	45.0d
9015	FN-CN-HR-1810	Install Ceiling Light Fixtures & Trim - Holdrooms/Offices - INTF - C7	7.0d	29-Dec-27	7-Jan-28	45.0d
9016	FN-CN-HR-1820	Install Diffusers - Holdrooms/Offices - INTF - C7	15.0d	29-Dec-27	19-Jan-28	72.0d
9017	FN-CN-HR-1830	Install Ceiling Low Voltage Trim - Holdrooms/Offices - INTF - C7	7.0d	29-Dec-27	7-Jan-28	80.0d
9018	FN-CN-HR-1840	Install Ceiling Fire Alarm Trim - Holdrooms/Offices - INTF - C7	7.0d	29-Dec-27	7-Jan-28	80.0d
9019	FN-CN-HR-1850	Install Fire Protection Trim - Holdrooms/Offices - INTF - C7	7.0d	29-Dec-27	7-Jan-28	80.0d
9020	FN-CN-HR-1860	Drop Remaining Ceiling Tile - Holdrooms/Offices - INTF - C7	10.0d	20-Jan-28	2-Feb-28	72.0d
9021	FN-CN-HR-2480	Install Column Cover Framing - Holdrooms/Offices - INTF - C7	10.0d	3-Feb-28	16-Feb-28	72.0d
9022	FN-CN-HR-1870	Install Column Covers - Holdrooms/Offices - INTF - C7	10.0d	17-Feb-28	1-Mar-28	72.0d
9023	FN-CN-HR-1890	Install Pedestrian Control Devices - Holdrooms/Offices - INTF - C7	9.0d	2-Mar-28	14-Mar-28	72.0d
9024	FN-CN-HR-1910	Install Light Fixtures & Trim Floor/Walls/Columns - Holdrooms/Offices - INTF -...	5.0d	15-Mar-28	21-Mar-28	146.0d
9025	FN-CN-HR-1920	Install Plumbing Trim - Holdrooms/Offices - INTF - C7	2.0d	15-Mar-28	16-Mar-28	72.0d
9026	FN-CN-HR-1950	Install Doors & Hardware - Holdrooms/Offices - INTF - C7	2.0d	17-Mar-28	20-Mar-28	72.0d
9027	FN-CN-HR-2330	Install Mech. Trim - Holdrooms/Offices - INTF - C7	5.0d	17-Mar-28	23-Mar-28	75.0d
9028	FN-CN-HR-1880	Apply Final Paint - Holdrooms/Offices - INTF - C7	5.0d	21-Mar-28	27-Mar-28	72.0d
9029	FN-CN-HR-1940	Install Low Voltage Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C7	5.0d	22-Mar-28	28-Mar-28	146.0d
9030	FN-CN-HR-2560	Install BAS Trim Floor/Walls/Columns - Holdrooms/Offices - INTF - C7	5.0d	22-Mar-28	28-Mar-28	146.0d

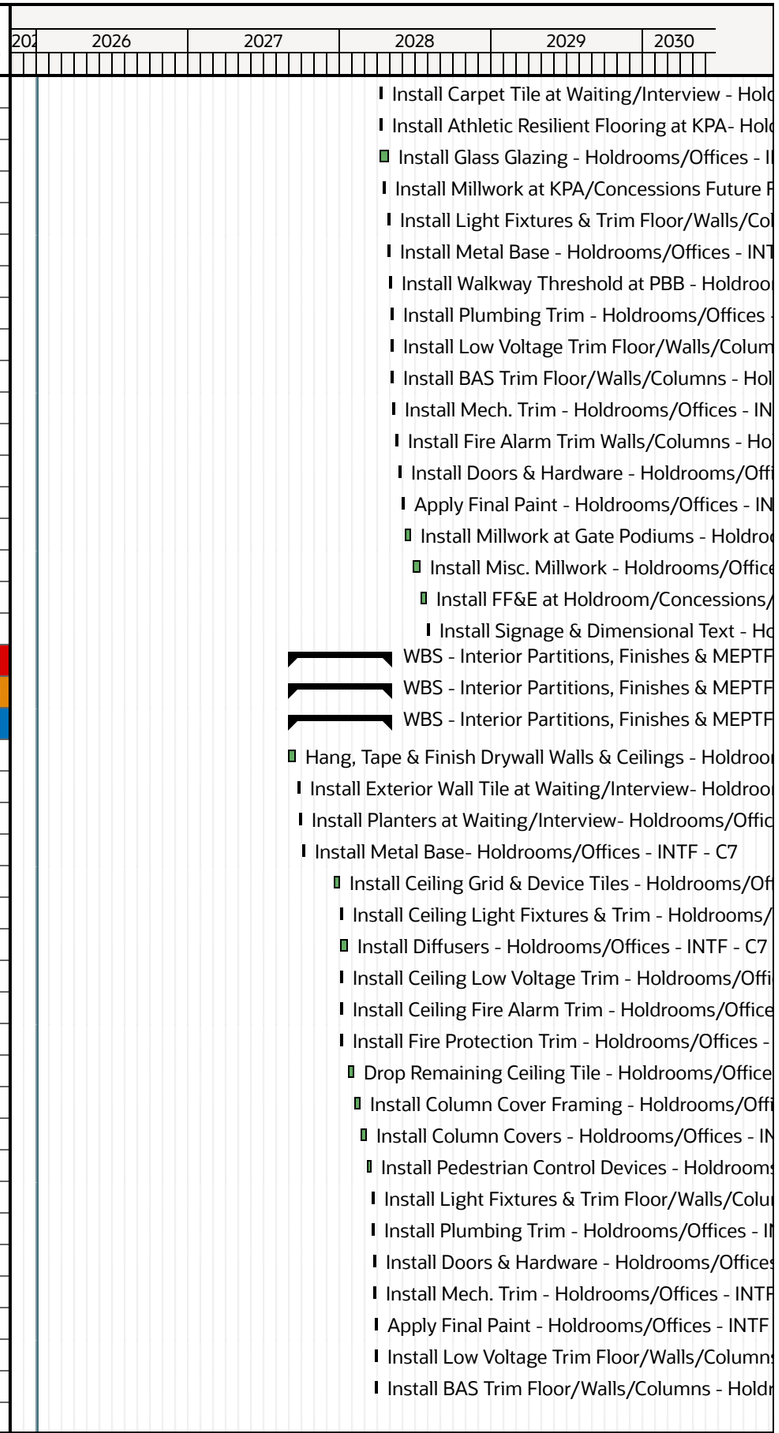


	ID	Name	Dur	Start	Finish	TF
9031	FN-CN-HR-1930	Install Fire Alarm Walls/Columns Trim - Holdrooms/Offices - INTF - C7	5.0d	24-Mar-28	30-Mar-28	144.0d
9032	FN-CN-HR-2500	Install Mlllwork - Holdrooms/Offices - INTF - C7	10.0d	24-Mar-28	6-Apr-28	75.0d
9033	FN-CN-HR-1900	Install Carpet at Holdroom- Holdrooms/Offices - INTF - C7	6.0d	28-Mar-28	4-Apr-28	72.0d
9034	FN-CN-HR-2190	Install Carpet at Waiting/Interview- Holdrooms/Offices - INTF - C7	2.0d	5-Apr-28	6-Apr-28	75.0d
9035	FN-CN-HR-2510	Install Walkway Threshold at PBB - Holdrooms/Offices - INTF - C7	3.0d	5-Apr-28	7-Apr-28	74.0d
9036	FN-CN-HR-2490	Install Glass Glazing - Holdrooms/Offices - INTF - C7	15.0d	5-Apr-28	25-Apr-28	72.0d
9037	FN-CN-HR-1960	Install FF&E - Holdrooms/Offices - INTF - C7	10.0d	10-Apr-28	21-Apr-28	74.0d
9038	FN-CN-HR-1970	Install Signage & Dimensional Text - Holdrooms/Offices - INTF - C7	5.0d	26-Apr-28	2-May-28	72.0d
9039	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 8		394.0d	27-Aug-27	16-Mar-29	0.0d
9040	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Overall - INTF - Conc. 8		394.0d	27-Aug-27	16-Mar-29	0.0d
9041	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - INTF - Conc. 8		311.0d	28-Dec-27	16-Mar-29	0.0d
9042	WBS - Architectural Forms (LED Screens) - INTF - Conc. 8		272.0d	22-Feb-28	16-Mar-29	0.0d
9043	FN-CN-3220	Install Concourse 9 Lid Fall Arrest Anchors- Architectural Forms (LED Screens) ...	5.0d	22-Feb-28	28-Feb-28	127.0d
9044	FN-CN-3230	Install Concourse 10 Lid Fall Arrest Anchors- Architectural Forms (LED Screens)...	5.0d	22-Feb-28	28-Feb-28	127.0d
9045	ASD-Bull-DT-400	Install LED Dancefloor for LED Screens - Architectural Forms (LED Screens) - IN...	20.0d	28-Aug-28	25-Sep-28	0.0d
9046	ASD-Bull-DT-390	HP Install LED Panel (21000sqft/1500 per week) - Architectural Forms (LED Sc...	70.0d	26-Sep-28	5-Jan-29	0.0d
9047	ASD-Bull-DT-380	HCAA Certify LED Panel Material & Install - Architectural Forms (LED Screens) -...	20.0d	8-Jan-29	2-Feb-29	30.0d
9048	ASD-Bull-DT-410	Remove LED Dancefloor for LED Screens - Architectural Forms (LED Screens) - ...	20.0d	8-Jan-29	2-Feb-29	0.0d
9049	FN-CN-3160	Install Resin Deck on Concourse 9 Lid - Architectural Forms (LED Screens) - INT...	10.0d	5-Feb-29	16-Feb-29	0.0d
9050	FN-CN-3170	Install Resin Deck on Concourse 10 Lid - Architectural Forms (LED Screens) - IN...	10.0d	5-Feb-29	16-Feb-29	0.0d
9051	ASD-Bull-DT-360	HCAA Certify Content & Hardware - Horizontal LED Screens - INTF - C8 (Worki...	20.0d	19-Feb-29	16-Mar-29	0.0d
9052	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - INTF - Phase 1 - Conc. 8		158.0d	22-Feb-28	3-Oct-28	94.0d
9053	FN-CN-1630	Place Back 12 Line Grout Joint - Overall - INTF - C8 - Ph 1	5.0d	22-Feb-28	28-Feb-28	0.0d
9054	FN-CN-2570	Layout - Overall - INTF - C8 - Ph 1	5.0d	29-Feb-28	6-Mar-28	0.0d
9055	FN-CN-2540	Frame Interior Partitions - Overall - INTF - C8 - Ph 1	15.0d	7-Mar-28	27-Mar-28	0.0d
9056	FN-CN-3190	Install Column Signage Supports/Backing - Overall - INTF - C8 - Ph 1	5.0d	7-Mar-28	13-Mar-28	10.0d
9057	FN-CN-3240	Frame Column Covers - Overall - INTF - C8 - Ph 1	15.0d	7-Mar-28	27-Mar-28	0.0d
9058	FN-CN-2580	Elec. In Wall Rough In - Overall - INTF - C8 - Ph 1	10.0d	28-Mar-28	10-Apr-28	0.0d
9059	FN-CN-2600	Low Voltage In Wall Rough In - Overall - INTF - C8 - Ph 1	10.0d	31-Mar-28	13-Apr-28	0.0d
9060	FN-CN-2590	Fire Alarm In Wall Rough In - Overall - INTF - C8 - Ph 1	10.0d	5-Apr-28	18-Apr-28	0.0d
9061	FN-CN-2610	Hang, Tape & Finish Drywall Partitions - Overall - INTF - C8 - Ph 1	10.0d	19-Apr-28	2-May-28	0.0d
9062	FN-CN-2620	Install Terrazzo Flooring at Circ./Restroom Vestibules/Concessions Ph.1 - Over...	20.0d	3-May-28	31-May-28	0.0d
9063	FN-CN-3130	Install Exterior Tile (TL21) at Concessions - Overall - INTF - C8 - Ph 1	15.0d	1-Jun-28	21-Jun-28	21.0d
9064	FN-CN-2660	Install Column Covers - Overall - INTF - C8 - Ph 1	36.0d	1-Jun-28	21-Jul-28	0.0d
9065	FN-CN-2690	Install Mech. Trim - Overall - INTF - C8 - Ph 1	10.0d	1-Jun-28	14-Jun-28	31.0d
9066	FN-CN-2640	Install Low Voltage Trim - Overall - INTF - C8 - Ph 1	5.0d	17-Jul-28	21-Jul-28	5.0d
9067	FN-CN-2630	Install Elec. Trim - Overall - INTF - C8 - Ph 1	5.0d	24-Jul-28	28-Jul-28	0.0d
9068	FN-CN-2650	Install Fire Alarm Trim - Overall - INTF - C8 - Ph 1	5.0d	24-Jul-28	28-Jul-28	0.0d
9069	FN-CN-2670	Terrazzo Final Polish at Circ./Restroom Vestibules/Concessions Ph.1 - Overall - ...	20.0d	31-Jul-28	25-Aug-28	0.0d
9070	FN-CN-2700	Apply Final Paint - Overall - INTF - C8 Ph 1	7.0d	28-Aug-28	6-Sep-28	23.0d
9071	FN-CN-2710	Install FF&E/Millwork - Overall - INTF - C8 - Ph 1	10.0d	28-Aug-28	11-Sep-28	85.0d
9072	FN-CN-2680	Install Metal Base - Overall - INTF - C8 - Ph 1	5.0d	12-Sep-28	18-Sep-28	85.0d

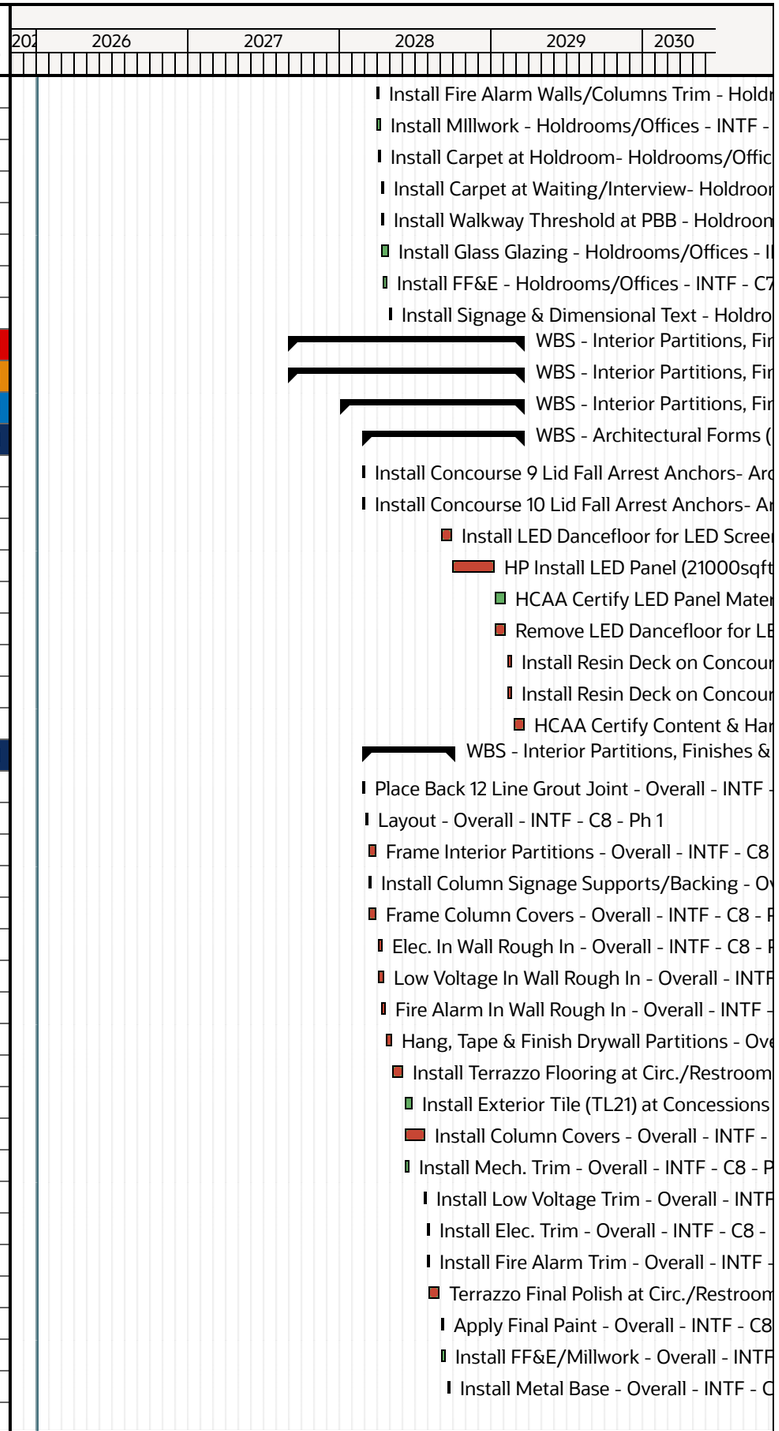


ID	Name	Dur	Start	Finish	TF
9073	FN-CN-2720	Install Signage - Overall - INTF - C8 - Ph 1	10.0d	20-Sep-28	3-Oct-28	94.0d
9074	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - INTF - Phase 2 - Conc. 8		157.0d	28-Dec-27	7-Aug-28	114.0d
9075	FN-CN-2730	Layout - Overall - INTF - C8 - Ph 2	5.0d	28-Dec-27	4-Jan-28	52.0d
9076	FN-CN-2740	Frame Interior Partitions - Overall - INTF - C8 - Ph 2	15.0d	5-Jan-28	25-Jan-28	52.0d
9077	FN-CN-3200	Install Column Signage Supports/Backing - Overall - INTF - C8 - Ph 2	5.0d	5-Jan-28	11-Jan-28	62.0d
9078	FN-CN-2750	Elec. In Wall Rough In - Overall - INTF - C8 - Ph 2	10.0d	26-Jan-28	8-Feb-28	52.0d
9079	FN-CN-2760	Low Voltage In Wall Rough In - Overall - INTF - C8 - Ph 2	10.0d	31-Jan-28	11-Feb-28	52.0d
9080	FN-CN-2770	Fire Alarm In Wall Rough In - Overall - INTF - C8 - Ph 2	10.0d	3-Feb-28	16-Feb-28	52.0d
9081	FN-CN-2780	Hang, Tape & Finish Drywall Partitions - Overall - INTF - C8 - Ph 2	10.0d	17-Feb-28	1-Mar-28	52.0d
9082	FN-CN-2790	Install Terrazzo Flooring at Circ./Restroom Vestibules/Concessions - Overall - I...	20.0d	2-Mar-28	29-Mar-28	52.0d
9083	FN-CN-2800	Install Column Covers - Overall - INTF - C8 - Ph 2	30.0d	30-Mar-28	10-May-28	52.0d
9084	FN-CN-3070	Install Tile Flooring at Future Concessions F&B - Overall - INTF - C8 - Ph 2	10.0d	30-Mar-28	12-Apr-28	65.0d
9085	FN-CN-3140	Install Exterior Tile (TL21) at Concessions - Overall - INTF - C8 - Ph 2	15.0d	30-Mar-28	19-Apr-28	65.0d
9086	FN-CN-2810	Install Mech. Trim - Overall - INTF - C8 - Ph 2	10.0d	13-Apr-28	26-Apr-28	65.0d
9087	FN-CN-2820	Install Signage - Overall - INTF - C8 - Ph 2	10.0d	4-May-28	17-May-28	83.0d
9088	FN-CN-2830	Install Elec. Trim - Overall - INTF - C8 - Ph 2	5.0d	9-May-28	15-May-28	52.0d
9089	FN-CN-2840	Install Low Voltage Trim - Overall - INTF - C8 - Ph 2	5.0d	9-May-28	15-May-28	52.0d
9090	FN-CN-2850	Install Fire Alarm Trim - Overall - INTF - C8 - Ph 2	5.0d	9-May-28	15-May-28	52.0d
9091	FN-CN-2860	Terrazzo Final Polish at Circ./Restroom Vestibules/Concessions - Overall - INTF...	20.0d	16-May-28	13-Jun-28	52.0d
9092	FN-CN-2870	Apply Final Paint - Overall - INTF - C8 Ph 2	7.0d	14-Jun-28	22-Jun-28	65.0d
9093	FN-CN-2880	Install FF&E/Millwork - Overall - INTF - C8 - Ph 2	10.0d	14-Jun-28	27-Jun-28	62.0d
9094	FN-CN-3080	Install Oasis Planter Casework - Overall - INTF - C8 - Ph 2	15.0d	14-Jun-28	5-Jul-28	114.0d
9095	FN-CN-2890	Install Metal Base - Overall - INTF - C8 - Ph 2	5.0d	28-Jun-28	5-Jul-28	137.0d
9096	FN-CN-3110	Install EVID Structure / Screens - Overall - INTF - C8 - Ph 2	5.0d	6-Jul-28	12-Jul-28	114.0d
9097	FN-CN-3090	Install Oasis Planter LED Pools - Overall - INTF - C8 - Ph 2	10.0d	13-Jul-28	26-Jul-28	114.0d
9098	FN-CN-3100	Install Oasis Planter Casework Trim - Overall - INTF - C8 - Ph 2	4.0d	27-Jul-28	1-Aug-28	114.0d
9099	FN-CN-3120	Install Oasis Planter Artificial Foliage - Overall - INTF - C8 - Ph 2	4.0d	2-Aug-28	7-Aug-28	114.0d
9100	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - INTF - Phase 3 - Conc. 8		193.0d	18-Jan-28	17-Oct-28	84.0d
9101	FN-CN-2900	Layout - Overall - INTF - C8 - Ph 3	5.0d	18-Jan-28	24-Jan-28	32.0d
9102	FN-CN-2910	Frame Interior Partitions - Overall - INTF - C8 - Ph 3	15.0d	25-Jan-28	14-Feb-28	32.0d
9103	FN-CN-3210	Install Column Signage Supports/Backing - Overall - INTF - C8 - Ph 3	5.0d	25-Jan-28	31-Jan-28	42.0d
9104	FN-CN-2920	Elec. In Wall Rough In - Overall - INTF - C8 - Ph 3	10.0d	15-Feb-28	28-Feb-28	32.0d
9105	FN-CN-2930	Low Voltage In Wall Rough In - Overall - INTF - C8 - Ph 3	10.0d	18-Feb-28	2-Mar-28	32.0d
9106	FN-CN-2940	Fire Alarm In Wall Rough In - Overall - INTF - C8 - Ph 3	10.0d	23-Feb-28	7-Mar-28	32.0d
9107	FN-CN-2950	Hang, Tape & Finish Drywall Partitions - Overall - INTF - C8 - Ph 3	10.0d	8-Mar-28	21-Mar-28	32.0d
9108	FN-CN-2960	Install Terrazzo Flooring at Circ./Restroom Vestibules/Concessions Ph.3 - Over...	20.0d	22-Mar-28	18-Apr-28	32.0d
9109	FN-CN-2970	Install Column Covers - Overall - INTF - C8 - Ph 3	36.0d	19-Apr-28	8-Jun-28	32.0d
9110	FN-CN-2980	Install Mech. Trim - Overall - INTF - C8 - Ph 3	10.0d	19-Apr-28	2-May-28	61.0d
9111	FN-CN-3150	Install Exterior Tile (TL21) at Concessions - Overall - INTF - C8 - Ph 3	15.0d	19-Apr-28	9-May-28	51.0d
9112	FN-CN-3000	Install Elec. Trim - Overall - INTF - C8 - Ph 3	5.0d	7-Jun-28	13-Jun-28	32.0d
9113	FN-CN-3010	Install Low Voltage Trim - Overall - INTF - C8 - Ph 3	5.0d	7-Jun-28	13-Jun-28	32.0d
9114	FN-CN-3020	Install Fire Alarm Trim - Overall - INTF - C8 - Ph 3	5.0d	7-Jun-28	13-Jun-28	32.0d

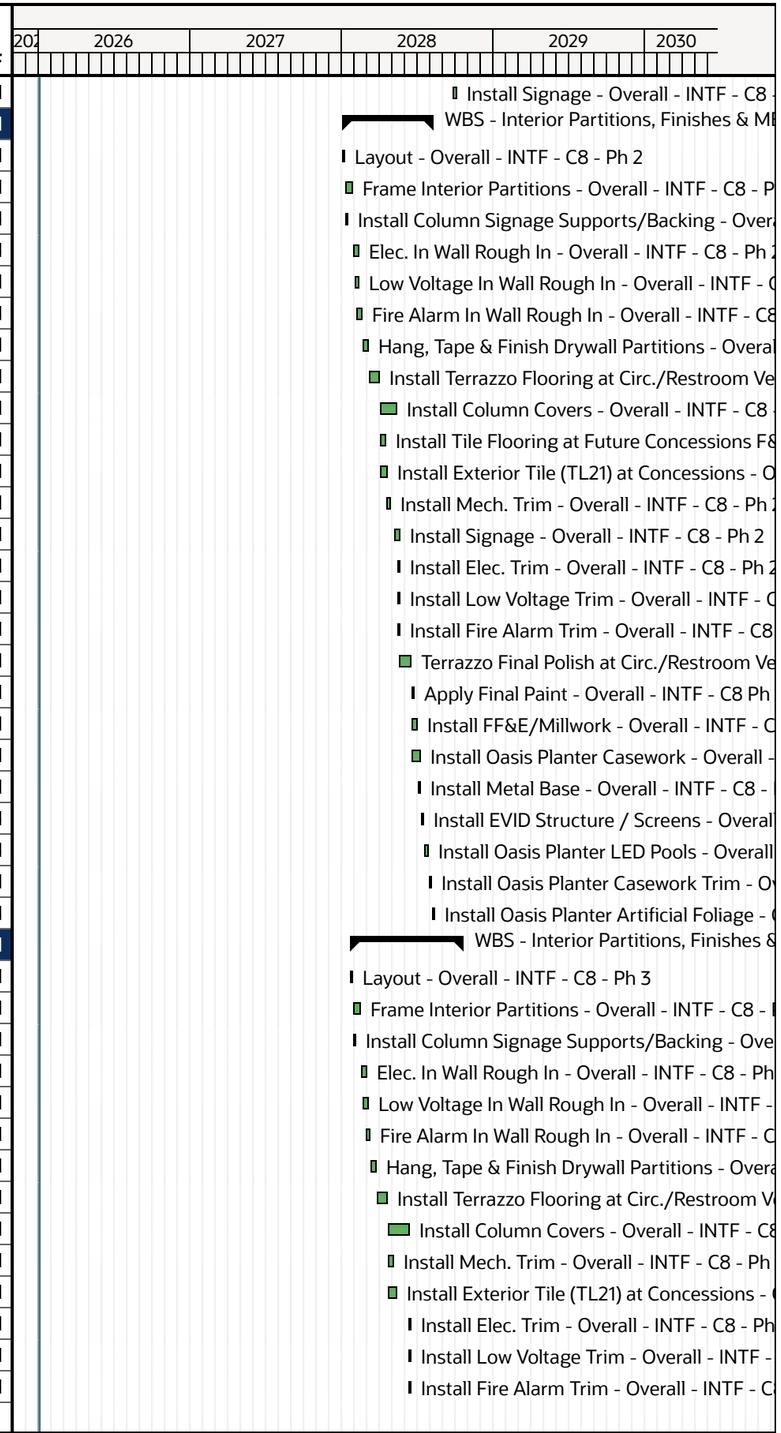


	ID	Name	Dur	Start	Finish	TF
9115	FN-CN-3030	Terrazzo Final Polish at Circ./Restroom Vestibules/Concessions Ph.3 - Overall - ...	20.0d	14-Jun-28	12-Jul-28	32.0d
9116	FN-CN-3040	Apply Final Paint - Overall - INTF - C8 Ph 3	7.0d	13-Jul-28	21-Jul-28	55.0d
9117	FN-CN-3050	Install FF&E/Millwork - Overall - INTF - C8 - Ph 3	10.0d	13-Jul-28	26-Jul-28	122.0d
9118	FN-CN-3060	Install Metal Base - Overall - INTF - C8 - Ph 3	5.0d	27-Jul-28	2-Aug-28	137.0d
9119	FN-CN-2990	Install Signage - Overall - INTF - C8 - Ph 3	10.0d	4-Oct-28	17-Oct-28	84.0d
9120	WBS - Delta In-Flight Lounge - INTF - C8		28.0d	27-Aug-27	6-Oct-27	166.0d
9121	FN-C8-CL-570	Hang Drywall Walls - Delta Airlines In-Flight Lounge - INTF - C8	10.0d	27-Aug-27	10-Sep-27	166.0d
9122	FN-C8-CL-580	Tape & Finish Walls - Delta Airlines In-Flight Lounge - INTF - C8	15.0d	13-Sep-27	1-Oct-27	166.0d
9123	FN-C8-CL-590	Install Doors & Hardware - Delta Airlines In-Flight Lounge - INTF - C8	3.0d	4-Oct-27	6-Oct-27	166.0d
9124	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 9		284.0d	23-Aug-27	3-Oct-28	74.0d
9125	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Restrooms - INTF - Conc.9		284.0d	23-Aug-27	3-Oct-28	74.0d
9126	WBS - HCAA IT 6609 - INTF - Concourse 09		28.0d	19-Oct-27	29-Nov-27	290.0d
9127	FN-C9-IT-1880	Hang Drywall Walls- HCAA IT 6609 - INTF - Concourse 9	5.0d	19-Oct-27	25-Oct-27	290.0d
9128	FN-C9-IT-1890	Tape & Finish Walls - HCAA IT 6609 - INTF- Conc. 9	5.0d	26-Oct-27	1-Nov-27	290.0d
9129	FN-C9-IT-1900	Prime & First Coat Walls - HCAA IT 6609 - INTF- Conc. 9	5.0d	2-Nov-27	8-Nov-27	290.0d
9130	FN-C9-IT-1960	Seal Concrete Floor - HCAA IT 6609 - INTF- Conc. 9	5.0d	9-Nov-27	15-Nov-27	290.0d
9131	FN-C9-IT-1970	Install Door & Hardware - HCAA IT 6609 - INTF- Conc. 9	2.0d	9-Nov-27	10-Nov-27	299.0d
9132	FN-C9-IT-1920	Install Fire Protection Trim - HCAA IT 6609 - INTF- Conc. 9	2.0d	16-Nov-27	17-Nov-27	290.0d
9133	FN-C9-IT-1910	Install Elec. Trim/Light Fixtures - HCAA IT 6609 - INTF- Conc. 9	2.0d	18-Nov-27	19-Nov-27	290.0d
9134	FN-C9-IT-1950	Install Low Voltage Trim - HCAA IT 6609 - INTF- Conc. 9	2.0d	22-Nov-27	23-Nov-27	290.0d
9135	FN-C9-IT-1930	Install Fire Alarm Trim - HCAA IT 6609 - INTF- Conc. 9	2.0d	22-Nov-27	23-Nov-27	290.0d
9136	FN-C9-IT-1940	Apply Final Paint - HCAA IT 6609 - INTF- Conc. 9	2.0d	24-Nov-27	29-Nov-27	290.0d
9137	WBS - Nursing Room, Service Animal Relief, BOH Corridor - INTF - Concourse 09		234.0d	2-Nov-27	3-Oct-28	74.0d
9138	FN-C9-R3-1606	Hang Drywall Lids & Walls- Nursing, Service Animal, BOH Corridor - INTF- Con...	5.0d	2-Nov-27	8-Nov-27	148.0d
9139	FN-C9-R3-1420	Tape & Finish Walls/Ceilings - Nursing, Service Animal, BOH Corridor - INTF- C...	15.0d	9-Nov-27	1-Dec-27	148.0d
9140	FN-C9-R3-1410	Prime & First Coat Walls/Ceilings - Nursing, Service Animal, BOH Corridor - INT...	5.0d	2-Dec-27	8-Dec-27	148.0d
9141	FN-C9-R3-1340	Install Porcelain Floor Tile - Nursing, Service Animal, BOH Corridor - INTF- Con...	15.0d	9-Dec-27	30-Dec-27	148.0d
9142	FN-C9-R3-1400	Install Full Height Porcelain Wall Tile - Nursing, Service Animal, BOH Corridor - I...	15.0d	3-Jan-28	21-Jan-28	148.0d
9143	FN-C9-R3-1350	Set Restroom Vanities w/Quartz Finishes - Nursing, Service Animal, BOH Corrid...	5.0d	24-Jan-28	28-Jan-28	153.0d
9144	FN-C9-R3-1880	Install SAR Flooring- Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	24-Jan-28	28-Jan-28	148.0d
9145	FN-C9-R3-1430	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	26-Jan-28	3-Feb-28	184.0d
9146	FN-C9-R3-1450	Install Diffusers - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	5.0d	31-Jan-28	4-Feb-28	175.0d
9147	FN-C9-R3-1910	Install Resinous Flooring (RF03) - Men's & Women's Gang B/room #3 - INTF - ...	5.0d	31-Jan-28	4-Feb-28	148.0d
9148	FN-C9-R3-1360	Set Restroom Plumbing Fixtures - Nursing, Service Animal, BOH Corridor - INT...	10.0d	7-Feb-28	18-Feb-28	148.0d
9149	FN-C9-R3-1580	Install Ceiling Speakers - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	5.0d	7-Feb-28	11-Feb-28	175.0d
9150	FN-C9-R3-1440	Install Fire Protection Trim Bathrooms/Future Concessions - Nursing, Service A...	3.0d	14-Feb-28	16-Feb-28	175.0d
9151	FN-C9-R3-1770	Install Fire Alarm Trim - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	3.0d	14-Feb-28	16-Feb-28	175.0d
9152	FN-C9-R3-1390	Apply Final Paint - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	5.0d	21-Feb-28	25-Feb-28	171.0d
9153	FN-C9-R3-1380	Install Restroom Toilet Acc. (Grab Bars, Tissue Dispensers, Bag/Purse Hooks) - ...	5.0d	28-Feb-28	3-Mar-28	203.0d
9154	FN-C9-R3-1840	Install Metal Base - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	5.0d	6-Mar-28	10-Mar-28	213.0d
9155	FN-C9-R3-1860	Install Signage - Nursing, Service Animal, BOH Corridor - INTF- Conc. 9	5.0d	27-Sep-28	3-Oct-28	74.0d
9156	WBS - Men's & Women's/Family Gang Bathroom #3 6642/6641/6640 - INTF - Concourse 09		279.0d	23-Aug-27	26-Sep-28	74.0d

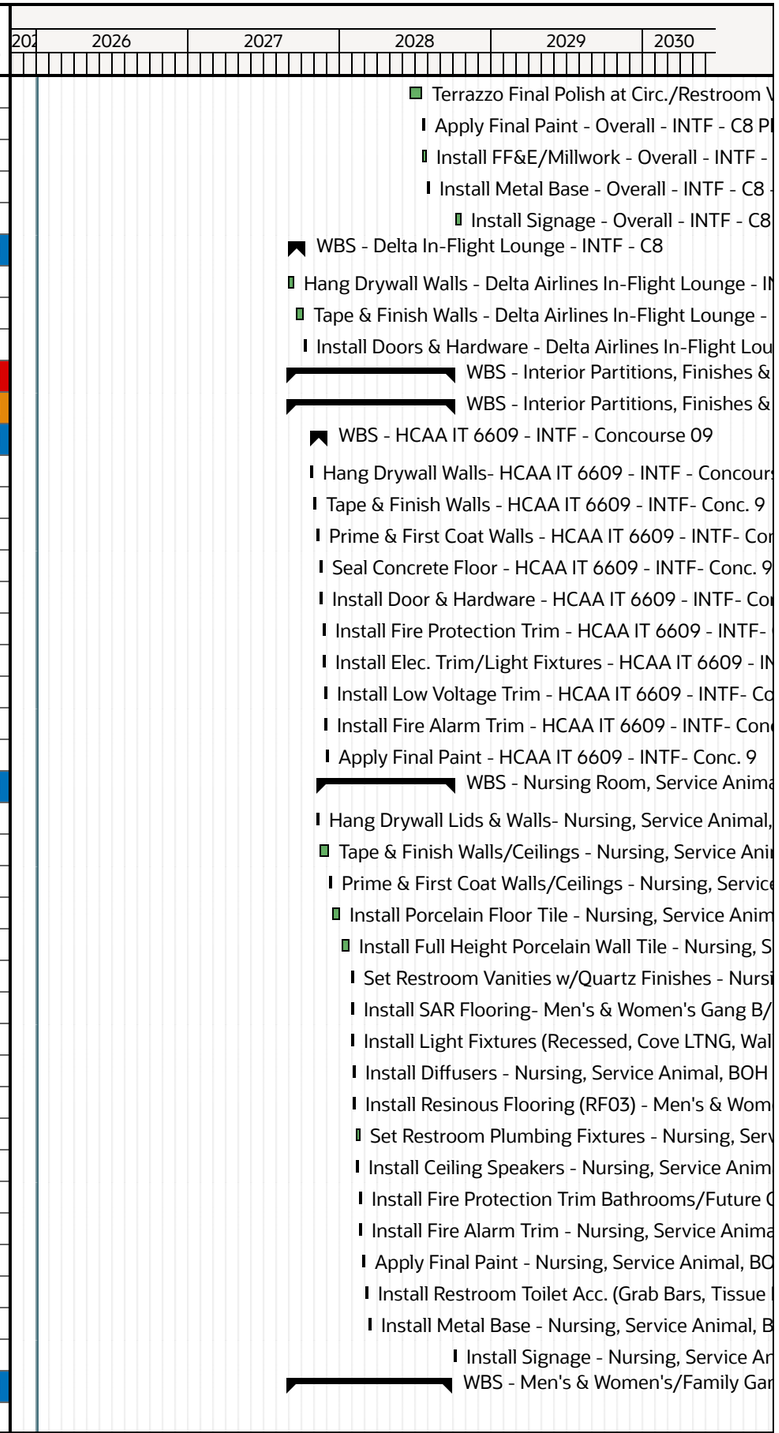


	ID	Name	Dur	Start	Finish	TF
9157	FN-C9-R3-1900	Field Measure & Fab. Decorative Glass Panels - Men's & Women's Gang B/room...	70.0d	23-Aug-27	1-Dec-27	268.0d
9158	FN-C9-R3-1760	Hang Drywall Lids & Walls - Men's & Women's Gang B/room #3 - INTF - Conc. 09	10.0d	19-Oct-27	1-Nov-27	148.0d
9159	FN-C9-R3-1540	Tape & Finish Walls/Ceilings - Men's & Women's Gang B/room #3 - INTF - Con...	15.0d	2-Nov-27	22-Nov-27	148.0d
9160	FN-C9-R3-1530	Prime & First Coat Walls/Ceilings - Men's & Women's Gang B/room #3 - INTF -...	5.0d	23-Nov-27	1-Dec-27	148.0d
9161	FN-C9-R3-1810	Install Resinous Flooring Plumbing Chase - Men's & Women's Gang B/room #3...	10.0d	23-Nov-27	8-Dec-27	153.0d
9162	FN-C9-R3-1460	Install Porcelain Floor Tile Womens/Family - Men's & Women's Gang B/room #...	15.0d	2-Dec-27	22-Dec-27	148.0d
9163	FN-C9-R3-1520	Install Full Height Porcelain Wall Tile Womens/Family - Men's & Women's Gang...	15.0d	23-Dec-27	14-Jan-28	148.0d
9164	FN-C9-R3-1470	Set Restroom Vanities w/Quartz Finishes - Men's & Women's Gang B/room #3 ...	10.0d	17-Jan-28	28-Jan-28	148.0d
9165	FN-C9-R3-1550	Install Light Fixt. (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) - M...	7.0d	17-Jan-28	25-Jan-28	184.0d
9166	FN-C9-R3-1570	Install Diffusers - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	17-Jan-28	21-Jan-28	183.0d
9167	FN-C9-R3-1590	Install Ceiling Speakers - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	24-Jan-28	28-Jan-28	183.0d
9168	FN-C9-R3-1480	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks - Men's & ...	15.0d	31-Jan-28	18-Feb-28	148.0d
9169	FN-C9-R3-1560	Install Fire Protection Trim - Men's & Women's Gang B/room #3 - INTF - Conc. ...	3.0d	31-Jan-28	2-Feb-28	183.0d
9170	FN-C9-R3-1780	Install Fire Alarm Trim - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	31-Jan-28	4-Feb-28	183.0d
9171	FN-C9-R3-1510	Finish Paint - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	21-Feb-28	25-Feb-28	171.0d
9172	FN-C9-R3-1490	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - ...	15.0d	28-Feb-28	17-Mar-28	188.0d
9173	FN-C9-R3-1500	Install Restroom Toilet Acc. (Grab Bars, Tissue Dispensers, Bag/Purse Hooks) - ...	5.0d	20-Mar-28	24-Mar-28	188.0d
9174	FN-C9-R3-1600	Install Wall Art/Decorative Glass (GL01) - Men's & Women's Gang B/room #3 - ...	5.0d	27-Mar-28	31-Mar-28	188.0d
9175	FN-C9-R3-1820	Install Vestibule Stone Cladding (ST01) - Men's & Women's Gang B/room #3 - I...	5.0d	27-Mar-28	31-Mar-28	188.0d
9176	FN-C9-R3-1850	Install Metal Base - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	3-Apr-28	7-Apr-28	188.0d
9177	FN-C9-R3-1870	Install Signage - Men's & Women's Gang B/room #3 - INTF - Conc. 09	5.0d	20-Sep-28	26-Sep-28	74.0d
9178	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 10		252.0d	23-Sep-27	19-Sep-28	74.0d
9179	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Restrooms - INTF - Conc. 10		252.0d	23-Sep-27	19-Sep-28	74.0d
9180	WBS - All User Gang Bathroom #2 6611 - INTF - Concourse 10		252.0d	23-Sep-27	19-Sep-28	74.0d
9181	FN-C10-R2-606	Hang Drywall Lids & Walls - All User B/room #2 - INTF - C10	10.0d	23-Sep-27	6-Oct-27	173.0d
9182	FN-C10-R2-50	Tape & Finish Walls/Ceilings - All User Gang B/room #2 - INTF C10	15.0d	7-Oct-27	27-Oct-27	173.0d
9183	FN-C10-R2-626	Install Resinous Flooring Plumbing Chase - All User Gang B/room #2 - INTF - C...	10.0d	28-Oct-27	10-Nov-27	173.0d
9184	FN-C10-R2-90	Install Porcelain Floor Tile User/Family - All User Gang B/room #2 - INTF - C10	15.0d	11-Nov-27	3-Dec-27	173.0d
9185	FN-C10-R2-190	Install Full Height Porcelain Wall Tile User/Family- All User Gang B/room #2 - I...	15.0d	6-Dec-27	27-Dec-27	173.0d
9186	FN-C10-R2-310	Set Restroom Vanities w/Quartz Finishes - All User Gang B/room #2 - INTF - C10	5.0d	28-Dec-27	4-Jan-28	173.0d
9187	FN-C10-R2-320	Prime & First Coat Walls/Ceilings - All User Gang B/room #2 - INTF - C10	5.0d	28-Dec-27	4-Jan-28	185.0d
9188	FN-C10-R2-350	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks - All User ...	8.0d	5-Jan-28	14-Jan-28	173.0d
9189	FN-C10-R2-360	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	5-Jan-28	13-Jan-28	185.0d
9190	FN-C10-R2-370	Install Diffusers - All User Gang B/room #2 - INTF - C10	5.0d	5-Jan-28	11-Jan-28	193.0d
9191	FN-C10-R2-390	Install Ceiling Speakers - All User Gang B/room #2 - INTF - C10	5.0d	12-Jan-28	18-Jan-28	193.0d
9192	FN-C10-R2-410	Finish Paint - All User Gang B/room #2 - INTF - C10	5.0d	17-Jan-28	21-Jan-28	198.0d
9193	FN-C10-R2-400	Install Fire Protection Trim - All User Gang B/room #2 - INTF - C10	3.0d	19-Jan-28	21-Jan-28	193.0d
9194	FN-C10-R2-616	Install Fire Alarm Trim Bathrooms/Future Concessions - All User Gang B/room ...	3.0d	19-Jan-28	21-Jan-28	193.0d
9195	FN-C10-R2-430	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - A...	5.0d	24-Jan-28	28-Jan-28	213.0d
9196	FN-C10-R2-460	Install Restroom Toilet Accessories (Grab Bars, Tissue Dispensers, Bag/Purse H...	5.0d	31-Jan-28	4-Feb-28	213.0d
9197	FN-C10-R2-646	Install Vestibule Stone Cladding (ST02) - All User Gang B/room #2 - INTF - C10	10.0d	7-Feb-28	18-Feb-28	213.0d
9198	FN-C10-R2-636	Install Metal Base - All User Gang B/room #2 - INTF - C10	5.0d	21-Feb-28	25-Feb-28	213.0d

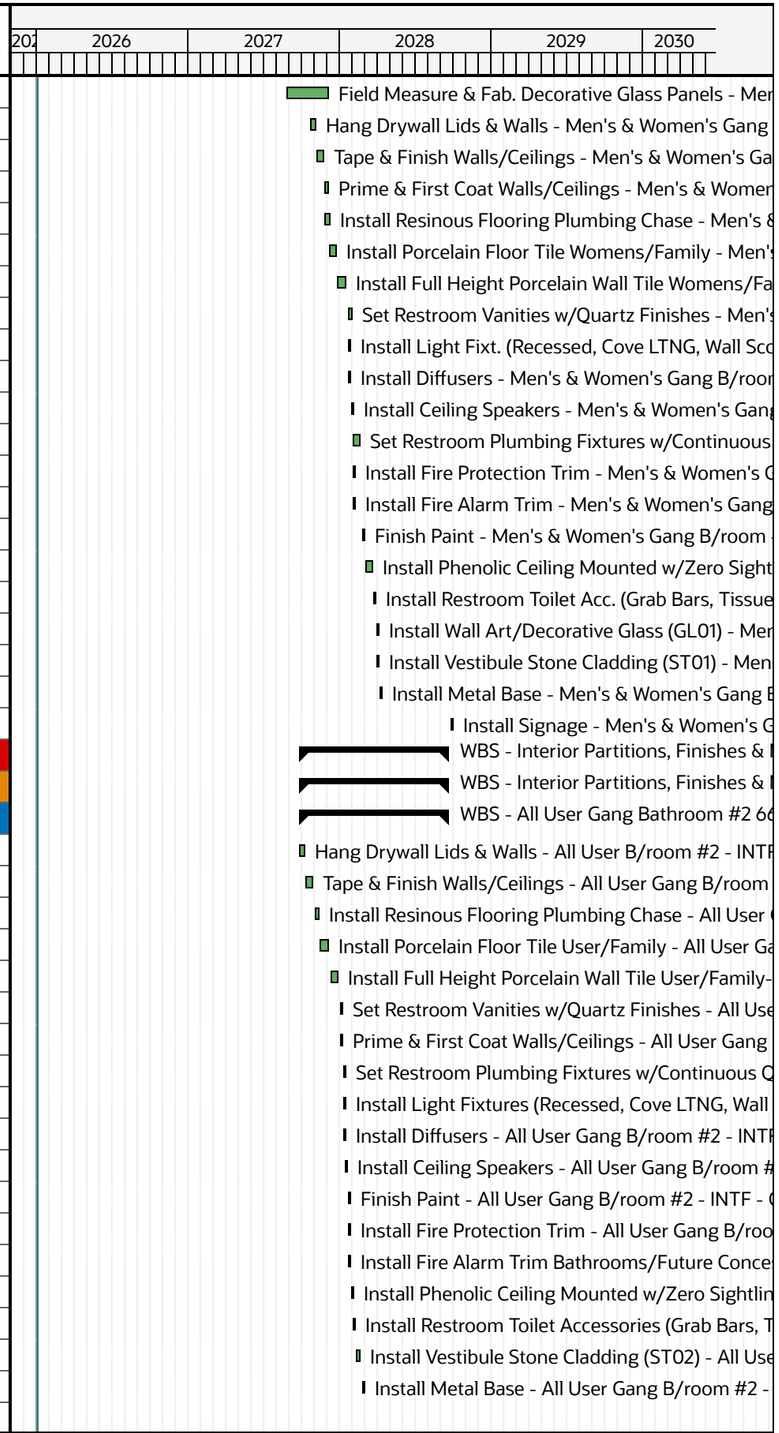


	ID	Name	Dur	Start	Finish	TF
9199	FN-C10-R2-656	Install Signage & Dimensional Text - All User Gang B/room #2 - INTF - C10	5.0d	13-Sep-28	19-Sep-28	74.0d
9200	WBS - Nursing Room, Family RR, Adult Changing, BOH Corridor, Trash Gondola Storage - INTF - Concourse 10		247.0d	23-Sep-27	12-Sep-28	74.0d
9201	FN-C10-R2-2020	Hang Drywall Lids & Walls- Nursing Room, Family RR, Adult Changing, BOH Co...	5.0d	23-Sep-27	29-Sep-27	176.0d
9202	FN-C10-R2-1960	Tape & Finish Walls/Ceilings - Nursing Room, Family RR, Adult Changing, BOH ...	15.0d	30-Sep-27	20-Oct-27	189.0d
9203	FN-C10-R2-1950	Prime & First Coat Walls/Ceilings - Nursing Room, Family RR, Adult Changing, ...	5.0d	21-Oct-27	27-Oct-27	189.0d
9204	FN-C10-R2-1890	Install Porcelain Floor Tile - Nursing Room, Family RR, Adult Changing, BOH Co...	15.0d	28-Oct-27	17-Nov-27	189.0d
9205	FN-C10-R2-1940	Install Full Height Porcelain Wall Tile - Nursing Room, Family RR, Adult Changin...	15.0d	18-Nov-27	10-Dec-27	189.0d
9206	FN-C10-R2-1990	Install Diffusers - Nursing Room, Family RR, Adult Changing, BOH Corridor, Tra...	5.0d	13-Dec-27	17-Dec-27	233.0d
9207	FN-C10-R2-2070	Install Resinous Flooring (RF03) - Nursing Room, Family RR, Adult Changing, B...	10.0d	13-Dec-27	27-Dec-27	189.0d
9208	FN-C10-R2-1970	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	17-Dec-27	28-Dec-27	189.0d
9209	FN-C10-R2-2000	Install Ceiling Speakers - Nursing Room, Family RR, Adult Changing, BOH Corri...	5.0d	20-Dec-27	27-Dec-27	233.0d
9210	FN-C10-R2-1900	Set Restroom Vanities w/Quartz Finishes - Nursing Room, Family RR, Adult Cha...	5.0d	28-Dec-27	4-Jan-28	189.0d
9211	FN-C10-R2-1980	Install Fire Protection Trim Bathrooms/Future Concessions - Nursing Room, Fa...	3.0d	28-Dec-27	30-Dec-27	233.0d
9212	FN-C10-R2-2030	Install Fire Alarm Trim - Nursing Room, Family RR, Adult Changing, BOH Corrid...	3.0d	28-Dec-27	30-Dec-27	233.0d
9213	FN-C10-R2-1910	Set Restroom Plumbing Fixtures - Nursing Room, Family RR, Adult Changing, B...	10.0d	5-Jan-28	18-Jan-28	189.0d
9214	FN-C10-R2-1930	Apply Final Paint - Nursing Room, Family RR, Adult Changing, BOH Corridor, Tr...	5.0d	19-Jan-28	25-Jan-28	189.0d
9215	FN-C10-R2-1920	Install Restroom Toilet Acc. (Grab Bars, Tissue Dispensers, Bag/Purse Hooks) - ...	5.0d	26-Jan-28	1-Feb-28	216.0d
9216	FN-C10-R2-2040	Install Vestibule Stone Cladding (ST01) - Nursing Room, Family RR, Adult Chan...	5.0d	2-Feb-28	8-Feb-28	216.0d
9217	FN-C10-R2-2050	Install Metal Base - Nursing Room, Family RR, Adult Changing, BOH Corridor, T...	5.0d	9-Feb-28	15-Feb-28	216.0d
9218	FN-C10-R2-2060	Install Signage - Nursing Room, Family RR, Adult Changing, BOH Corridor, Tras...	5.0d	6-Sep-28	12-Sep-28	74.0d
9219	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Concourse 11		317.0d	8-Jun-27	5-Sep-28	114.0d
9220	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Restrooms - INTF - Conc. 11		317.0d	8-Jun-27	5-Sep-28	94.0d
9221	WBS - Gang Bathroom #1 INTF - Concourse 11		317.0d	8-Jun-27	5-Sep-28	94.0d
9222	WBS - Men's Gang Bathroom #1 6388 INTF - Concourse 11		153.0d	8-Jun-27	14-Jan-28	258.0d
9223	FN-C11-R1-560	Field Measure & Fab. Decorative Glass Panels - Men's Gang Bathroom #1 - INT...	70.0d	8-Jun-27	15-Sep-27	336.0d
9224	FN-C11-R1-286	Hang Drywall Lids & Walls - Men's Gang Bathroom #1 - INTR - C11	5.0d	25-Aug-27	31-Aug-27	123.0d
9225	FN-C11-R1-10	Tape & Finish Walls/Ceilings - Men's Gang B/room #1 - INTF - C11	15.0d	1-Sep-27	22-Sep-27	189.0d
9226	FN-C11-R1-500	Install Resinous Flooring Plumbing Chase - Men's Gang B/room #1 - INTF - C11	10.0d	23-Sep-27	6-Oct-27	189.0d
9227	FN-C11-R1-20	Install Porcelain Floor Tile Mens/Family - Men's Gang B/room #1 - INTF - C11	15.0d	7-Oct-27	27-Oct-27	189.0d
9228	FN-C11-R1-40	Install Full Height Porcelain Wall Tile Mens/Family - Men's Gang B/room #1 - I...	15.0d	28-Oct-27	17-Nov-27	189.0d
9229	FN-C11-R1-70	Set Restroom Vanities w/Quartz Finishes - Men's Gang B/room #1 - INTF - C11	5.0d	18-Nov-27	24-Nov-27	193.0d
9230	FN-C11-R1-80	Prime & First Coat Walls/Ceilings - Men's Gang B/room #1 - INTF - C11	5.0d	18-Nov-27	24-Nov-27	189.0d
9231	FN-C11-R1-120	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks - Men's Ga...	5.0d	29-Nov-27	3-Dec-27	193.0d
9232	FN-C11-R1-130	Install Light Fixtures (Recessed, Cove LTNG, Sconces, Mirrors w/Int. LTNG) - Me...	7.0d	29-Nov-27	7-Dec-27	189.0d
9233	FN-C11-R1-140	Install Diffusers - Men's Gang B/room #1 - INTF - C11	5.0d	29-Nov-27	3-Dec-27	190.0d
9234	FN-C11-R1-490	Install Metal Base - Men's Gang B/room #1 - INTF - C11	5.0d	29-Nov-27	3-Dec-27	198.0d
9235	FN-C11-R1-170	Finish Paint - Men's Gang B/room #1 - INTF - C11	5.0d	6-Dec-27	10-Dec-27	193.0d
9236	FN-C11-R1-150	Install Ceiling Speakers - Men's Gang B/room #1 - INTF - C11	5.0d	6-Dec-27	10-Dec-27	190.0d
9237	FN-C11-R1-160	Install Fire Protection Trim - Men's Gang B/room #1 - INTF - C11	3.0d	13-Dec-27	15-Dec-27	190.0d
9238	FN-C11-R1-460	Install Fire Alarm Trim - Men's Gang B/room #1 - INTF - C11	3.0d	13-Dec-27	15-Dec-27	190.0d
9239	FN-C11-R1-180	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Partitions - ...	5.0d	16-Dec-27	22-Dec-27	190.0d
9240	FN-C11-R1-230	Install Restroom Toilet Acc. (Grab Bars, Toilet Tissue Dispensers, Bag/Purse Ho...	5.0d	23-Dec-27	30-Dec-27	190.0d

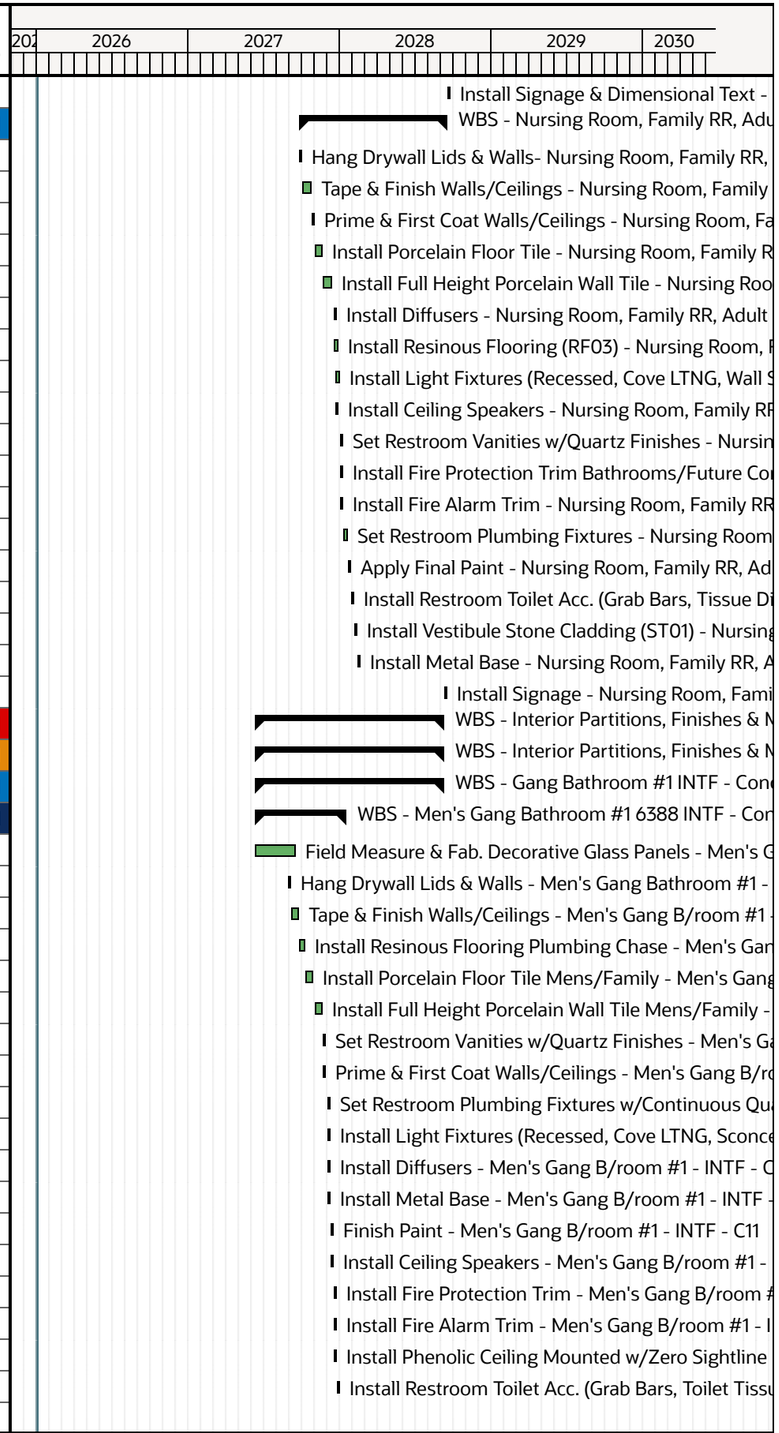


	ID	Name	Dur	Start	Finish	TF
9241	FN-C11-R1-300	Install Wall Art/Decorative Glass (GL01) - Men's Gang B/room #1 - INTF - C11	5.0d	3-Jan-28	7-Jan-28	263.0d
9242	FN-C11-R1-480	Install Vestibule Stone Cladding (ST01) - Men's Gang B/room #1 - INTF - C11	5.0d	3-Jan-28	7-Jan-28	190.0d
9243	FN-C11-R1-540	Install Signage - Men's Gang B/room #1 - INTF - C11	5.0d	10-Jan-28	14-Jan-28	223.0d
9244	WBS - Women's Gang Bathroom #1 6391 INTF - Concourse 11		317.0d	8-Jun-27	5-Sep-28	74.0d
9245	FN-C11-R1-570	Field Measure & Fab. Decorative Glass Panels - Women's Gang B/room #1 - IN...	70.0d	8-Jun-27	15-Sep-27	311.0d
9246	FN-C11-R1-450	Hang Drywall Lids & Walls - Women's Gang B/room #1 - INTR - C11	5.0d	25-Aug-27	31-Aug-27	123.0d
9247	FN-C11-R1-30	Tape & Finish Walls/Ceilings - Women's Gang B/room #1 - INTF - C11	15.0d	1-Sep-27	22-Sep-27	190.0d
9248	FN-C11-R1-510	Install Resinous Flooring Plumbing Chase - Women's Gang B/room #1 - INTF - ...	10.0d	23-Sep-27	6-Oct-27	190.0d
9249	FN-C11-R1-60	Install Porcelain Floor Tile Womens/Nursing - Women's Gang B/room #1 - INT...	15.0d	7-Oct-27	27-Oct-27	190.0d
9250	FN-C11-R1-100	Install Full Height Porcelain Wall Tile Womens/Nursing - Women's Gang B/roo...	15.0d	28-Oct-27	17-Nov-27	190.0d
9251	FN-C11-R1-200	Set Restroom Vanities w/Quartz Finishes - Women's Gang B/room #1 - INTF - ...	5.0d	18-Nov-27	24-Nov-27	190.0d
9252	FN-C11-R1-210	Prime & First Coat Walls/Ceilings - Women's Gang B/room #1 - INTF - C11	5.0d	18-Nov-27	24-Nov-27	190.0d
9253	FN-C11-R1-240	Set Restroom Plumbing Fixtures w/Continuous Quartz Trough Sinks - Women's...	8.0d	29-Nov-27	8-Dec-27	190.0d
9254	FN-C11-R1-260	Install Diffusers - Women's Gang B/room #1 - INTF - C11	5.0d	29-Nov-27	3-Dec-27	190.0d
9255	FN-C11-R1-530	Install Metal Base - Women's Gang B/room #1 - INTF - C11	5.0d	29-Nov-27	3-Dec-27	198.0d
9256	FN-C11-R1-270	Install Ceiling Speakers - WoWomen's Gang B/room #1 - INTF - C11	5.0d	6-Dec-27	10-Dec-27	190.0d
9257	FN-C11-R1-250	Install Light Fixtures (Recessed, Cove LTNG, Wall Sconces, Mirrors w/Int. LTNG) ...	7.0d	8-Dec-27	16-Dec-27	189.0d
9258	FN-C11-R1-290	Finish Paint - Women's Gang B/room #1 - INTF - C11	5.0d	9-Dec-27	15-Dec-27	190.0d
9259	FN-C11-R1-280	Install Fire Protection Trim - Women's Gang B/room #1 - INTF - C11	3.0d	13-Dec-27	15-Dec-27	190.0d
9260	FN-C11-R1-470	Install Fire Alarm Trim - Women's Gang B/room #1 - INTF - C11	3.0d	13-Dec-27	15-Dec-27	190.0d
9261	FN-C11-R1-330	Install Phenolic Ceiling Mounted w/Zero Sightline Restroom Toilet Part. - Wome...	5.0d	17-Dec-27	23-Dec-27	189.0d
9262	FN-C11-R1-380	Install Restroom Toilet Accessories (Grab Bars, Tissue Dispensers, Bag/Purse H...	5.0d	27-Dec-27	3-Jan-28	189.0d
9263	FN-C11-R1-520	Install Vestibule Stone Cladding (ST01) - Women's Gang B/room #1 - INTF - C11	5.0d	4-Jan-28	10-Jan-28	189.0d
9264	FN-C11-R1-420	Install Wall Art/Decorative Glass (GL01) - Women's Gang B/room #1 - INTF - C11	5.0d	11-Jan-28	17-Jan-28	232.0d
9265	FN-C11-R1-550	Install Signage - Women's Gang B/room #1 - INTF - C11	5.0d	29-Aug-28	5-Sep-28	74.0d
9266	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - HCAA Storage/Landscaping/Support - INTF - Conc. 11		277.0d	21-Jul-27	21-Aug-28	74.0d
9267	FN-C11-SR-520	Tape & Finish Ceilings at BOH Rooms - HCAA Storage/Landscaping/Support - ...	15.0d	21-Jul-27	10-Aug-27	175.0d
9268	FN-C11-SR-540	Apply Prime, First, Paint Ceilings - HCAA Storage/Landscaping/Support - INTF...	7.0d	11-Aug-27	19-Aug-27	175.0d
9269	FN-C11-SR-510	Hang Drywall Walls - HCAA Storage/Landscaping/Support - INTF - C11	10.0d	1-Sep-27	15-Sep-27	123.0d
9270	FN-C11-SR-530	Tape & Finish Walls - HCAA Storage/Landscaping/Support - INTF - C11	15.0d	16-Sep-27	6-Oct-27	135.0d
9271	FN-C11-SR-550	Prime & One Coat Walls - HCAA Storage/Landscaping/Support - INTF - C11	7.0d	7-Oct-27	15-Oct-27	135.0d
9272	FN-C11-SR-560	Install Doors - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	18-Oct-27	22-Oct-27	221.0d
9273	FN-C11-SR-570	Install Diffusers - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	18-Oct-27	22-Oct-27	140.0d
9274	FN-C11-SR-580	Install Elec. Trim/LTNG - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	18-Oct-27	22-Oct-27	135.0d
9275	FN-C11-SR-590	Install Door Hardware- HCAA Storage/Landscaping/Support - INTF - C11	10.0d	25-Oct-27	5-Nov-27	221.0d
9276	FN-C11-SR-600	Install Low Voltage Trim - HCAA Storage/Landscaping/Support - INTF - C11	7.0d	25-Oct-27	2-Nov-27	135.0d
9277	FN-C11-SR-610	Install Fire Alarm Trim - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	25-Oct-27	29-Oct-27	135.0d
9278	FN-C11-SR-620	Install Fire Protection Trim - HCAA Storage/Landscaping/Support - INTF - C11	3.0d	1-Nov-27	3-Nov-27	135.0d
9279	FN-C11-SR-630	Install Partitions - HCAA Storage/Landscaping/Support - INTF - C11	10.0d	4-Nov-27	17-Nov-27	135.0d
9280	FN-C11-SR-640	Install Plumbing Trim - HCAA Storage/Landscaping/Support - INTF - C11	10.0d	4-Nov-27	17-Nov-27	198.0d
9281	FN-C11-SR-650	Install Light Fixtures & Trim Walls - HCAA Storage/Landscaping/Support - INT...	5.0d	18-Nov-27	24-Nov-27	189.0d
9282	FN-C11-SR-710	Install Resinous Flooring in Janitor Storage 6428 - HCAA Storage/Landscaping...	10.0d	18-Nov-27	3-Dec-27	198.0d

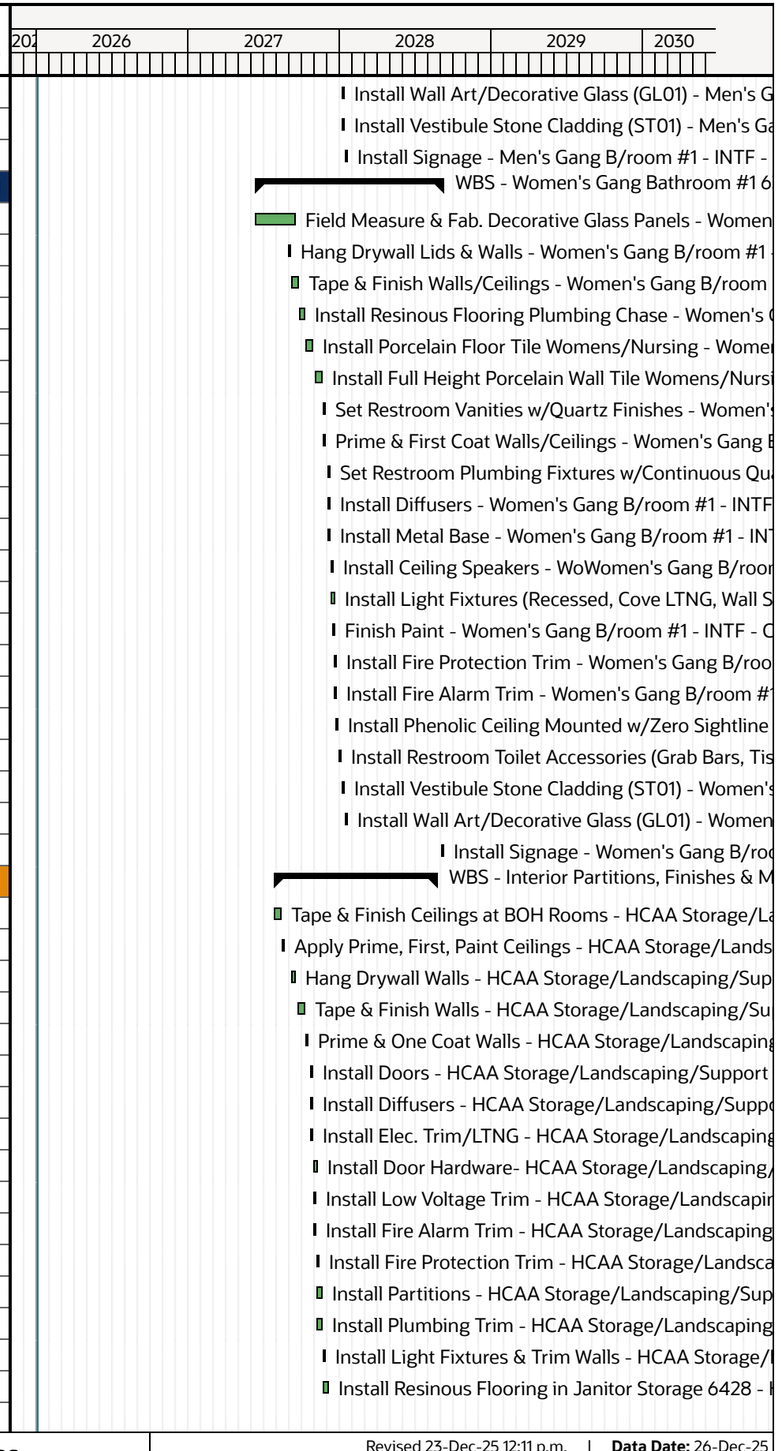

	ID	Name	Dur	Start	Finish	TF
9283	FN-C11-SR-740	Install Carpet in Wheelchair Storage 6383 - HCAA Storage/Landscaping/Supp...	5.0d	18-Nov-27	24-Nov-27	203.0d
9284	FN-C11-SR-750	Seal Concrete in BOH Rooms 6398, 6429, 6402, 6427, 6433 - HCAA Storage/L...	5.0d	18-Nov-27	24-Nov-27	203.0d
9285	FN-C11-SR-730	Install Rubber Base - BOH Rooms 6398, 6429, 6402, 6427, 6433 - HCAA Stora...	5.0d	29-Nov-27	3-Dec-27	203.0d
9286	FN-C11-SR-670	Install Low Voltage Trim Walls - HCAA Storage/Landscaping/Support - INTF - ...	5.0d	6-Dec-27	10-Dec-27	198.0d
9287	FN-C11-SR-770	Install BAS Trim Walls - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	6-Dec-27	10-Dec-27	198.0d
9288	FN-C11-SR-680	Apply Final Paint - HCAA Storage/Landscaping/Support - INTF - C11	10.0d	13-Dec-27	27-Dec-27	198.0d
9289	FN-C11-SR-760	Install FF&E - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	28-Dec-27	4-Jan-28	231.0d
9290	FN-C11-SR-690	Install Signage - HCAA Storage/Landscaping/Support - INTF - C11	5.0d	15-Aug-28	21-Aug-28	74.0d
9291	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Common Use Club Entry - INTF - Conc. 11		242.0d	16-Sep-27	28-Aug-28	119.0d
9292	FN-C11-CL-740	Hang Drywall Walls - Common Use Club Entry - INTF - C 11	5.0d	16-Sep-27	22-Sep-27	123.0d
9293	FN-C11-CL-750	Tape & Finish Walls - Common Use Club Entry - INTF - C 11	15.0d	23-Sep-27	13-Oct-27	123.0d
9294	FN-C11-CL-760	Prime & One Coat Walls - Common Use Club Entry - INTF - C 11	7.0d	14-Oct-27	22-Oct-27	123.0d
9295	FN-C11-CL-770	Install Elec. Trim/LTNG - Common Use Club Entry - INTF - C 11	5.0d	25-Oct-27	29-Oct-27	123.0d
9296	FN-C11-CL-790	Install FF&E & Millwork - Common Use Club Entry - INTF - C 11	10.0d	1-Nov-27	12-Nov-27	123.0d
9297	FN-C11-CL-800	Install Glazing & Doors - Common Use Club Entry - INTF - C 11	15.0d	15-Nov-27	7-Dec-27	123.0d
9298	FN-C11-CL-820	Terrazzo Final Polish at Common Use Club Entry - INTF - C 11	5.0d	31-Jul-28	4-Aug-28	135.0d
9299	FN-C11-CL-810	Install Signage - Common Use Club Entry - INTF - C 11	5.0d	22-Aug-28	28-Aug-28	74.0d
9300	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Mezzanine/Club Level		239.0d	3-Jun-27	10-May-28	155.0d
9301	WBS - Mezzanine/Club Level Milestones		91.0d	12-Oct-27	22-Feb-28	211.0d
9302	FN-MLS-MC-300	Club Level Plumbing Trim Out Complete	0.0d		12-Oct-27	237.0d
9303	FN-MLS-MC-240	Club Level Mech. Trim Out Complete	0.0d		30-Nov-27	229.0d
9304	FN-MLS-MC-250	Club Level Elec. Trim Out Complete	0.0d		5-Jan-28	205.0d
9305	FN-MLS-MC-280	Club Level Fire Protection Trim Out Complete	0.0d		12-Jan-28	200.0d
9306	FN-MLS-MC-260	Club Level Low Voltage Trim Out Complete	0.0d		13-Jan-28	199.0d
9307	FN-MLS-MC-270	Club Level Fire Alarm Trim Out Complete	0.0d		13-Jan-28	199.0d
9308	FN-MLS-MC-310	Club Level Doors & Hardware Complete	0.0d		13-Jan-28	199.0d
9309	FN-MLS-MC-320	Club Level Internal Punchlist	20.0d	26-Jan-28	22-Feb-28	211.0d
9310	FN-MLS-MC-290	Club Level Finishes Complete	0.0d		22-Feb-28	211.0d
9311	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Club 1		206.0d	21-Jul-27	10-May-28	79.0d
9312	WBS - BOH/Mechanical Space - INTF - Club 1		45.0d	21-Jul-27	22-Sep-27	201.0d
9313	FN-CL-MC1-60	Install Fire Protection Trim - BOH/Mech. Space - INTF - Club 1	15.0d	21-Jul-27	10-Aug-27	201.0d
9314	FN-CL-MC1-70	Install Mech. Trim - BOH/Mech. Space - INTF - Club 1	20.0d	28-Jul-27	24-Aug-27	201.0d
9315	FN-CL-MC1-90	Install Plumbing - BOH/Mech. Space - INTF - Club 1	5.0d	18-Aug-27	24-Aug-27	201.0d
9316	FN-CL-MC1-110	Install Elec. Trim - BOH/Mech. Space - INTF - Club 1	20.0d	25-Aug-27	22-Sep-27	201.0d
9317	FN-CL-MC1-160	Install Fire Alarm Trim - BOH/Mech. Space - INTF - Club 1	20.0d	25-Aug-27	22-Sep-27	201.0d
9318	WBS - Mechanical Room - INTF - Club 1		181.0d	25-Aug-27	10-May-28	79.0d
9319	FN-MC1-MR-200	Hang, Tape & Finish Drywall - Mech. Room - INTF - Club 1	15.0d	25-Aug-27	15-Sep-27	10.0d
9320	FN-MC1-MR-220	Prime & First Coat - Mech. Room - INTF - Club 1	5.0d	16-Sep-27	22-Sep-27	183.0d
9321	FN-MC1-MR-250	Install Doors- Mech. Room - INTF - Club 1	2.0d	23-Sep-27	24-Sep-27	186.0d
9322	FN-MC1-MR-270	Install Door Hardware - Mech. Room - INTF - Club 1	2.0d	23-Sep-27	24-Sep-27	186.0d
9323	FN-MC1-MR-230	Install Light Fixtures & Trim - Mech. Room - INTF - Club 1	5.0d	23-Sep-27	29-Sep-27	183.0d
9324	FN-MC1-MR-240	Apply Final Paint - Mech. Room - INTF - Club 1	5.0d	30-Sep-27	6-Oct-27	183.0d

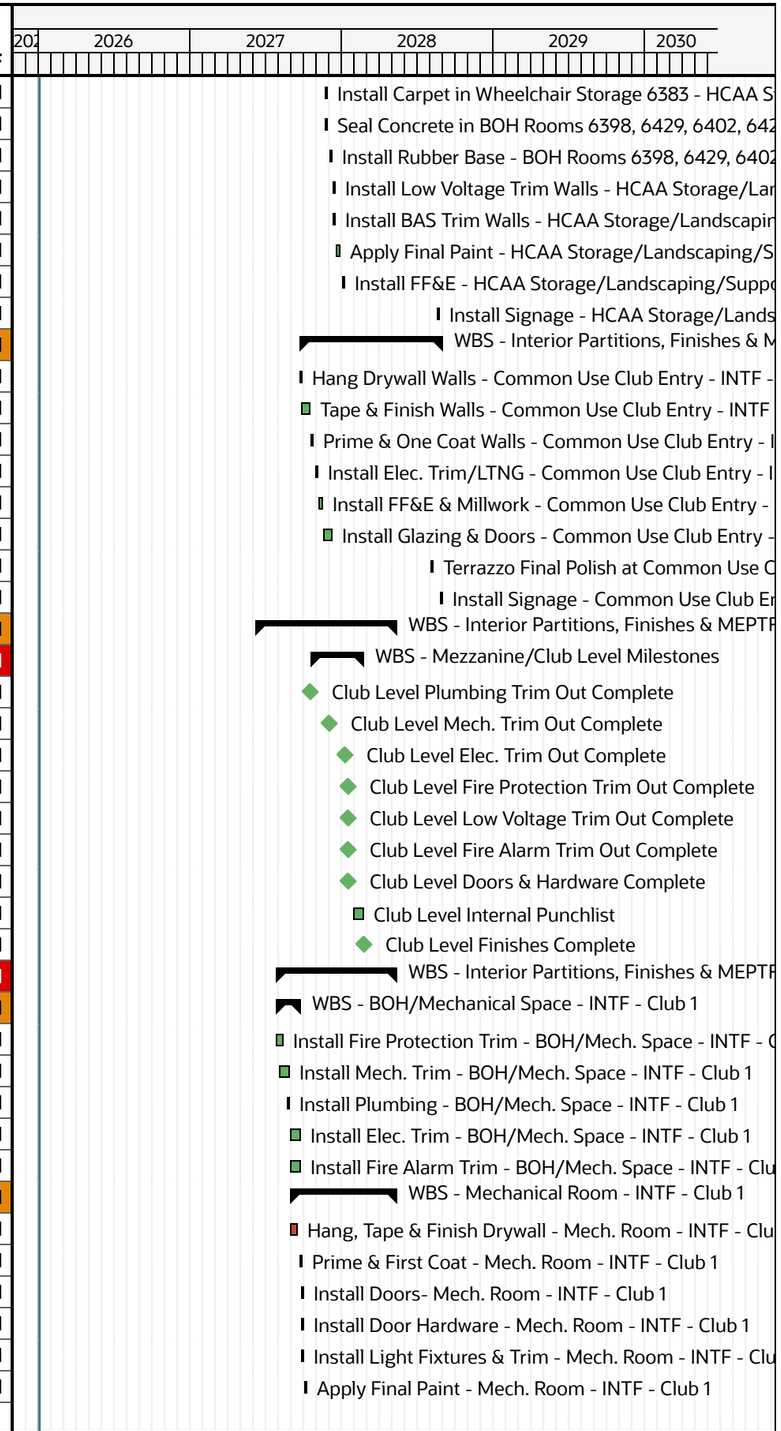


ID	Name	Dur	Start	Finish	TF
9325	FN-MC1-MR-7640	Set Floor Drains - Mech. Room - INTF - Club 1	4.0d	7-Oct-27	12-Oct-27	183.0d
9326	FN-MC1-MR-260	Seal Concrete - Mech. Room - INTF - Club 1	5.0d	13-Oct-27	19-Oct-27	183.0d
9327	FN-MC1-MR-210	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - Club 1 Sector J	20.0d	2-Feb-28	29-Feb-28	112.0d
9328	FN-MC1-MR-215	CHW Pipe Connections to Mech Equip. - Mech. Room - INTF - Club 1 Sector F	10.0d	1-Mar-28	14-Mar-28	112.0d
9329	FN-MC1-MR-7650	Energize Power at AHU Disconnect - Mech. Room - INTF - Club 1	5.0d	15-Mar-28	21-Mar-28	112.0d
9330	FN-MC1-MR-290	Start-up AHU - Mech. Room - INTF - Club 1	3.0d	8-May-28	10-May-28	79.0d
9331	WBS - Support Circulation/Corridors - INTF- Club 1		117.0d	4-Aug-27	20-Jan-28	154.0d
9332	FN-MC1-SC-10	Install Wall Insulation- Support Circ./Corridors - INTF - Club 1	5.0d	4-Aug-27	10-Aug-27	88.0d
9333	FN-MC1-SC-20	Hang Drywall Walls - Support Circ./Corridors - INTF - Club 1	10.0d	7-Oct-27	20-Oct-27	48.0d
9334	FN-MC1-SC-30	Tape & Finish Walls - Support Circ./Corridors - INTF - Club 1	15.0d	21-Oct-27	10-Nov-27	154.0d
9335	FN-MC1-SC-40	Prime & One Coat Walls - Support Circ./Corridors - INTF - Club 1	7.0d	11-Nov-27	19-Nov-27	154.0d
9336	FN-MC1-SC-50	Install Ceiling Light Fixtures & Trim - Support Circ./Corridors - INTF - Club 1	10.0d	22-Nov-27	7-Dec-27	154.0d
9337	FN-MC1-SC-90	Install Diffusers - Support Circ./Corridors - INTF - Club 1	5.0d	22-Nov-27	30-Nov-27	156.0d
9338	FN-MC1-SC-110	Install Low Voltage Trim - Support Circ./Corridors - INTF - Club 1	7.0d	22-Nov-27	2-Dec-27	157.0d
9339	FN-MC1-SC-80	Install Doors - Support Circ./Corridors - INTF - Club 1	5.0d	22-Nov-27	30-Nov-27	169.0d
9340	FN-MC1-SC-70	Install Flooring & Base - Support Circ./Corridors - INTF - Club 1	10.0d	22-Nov-27	7-Dec-27	174.0d
9341	FN-MC1-SC-200	Install Fire Alarm Trim - Support Circ./Corridors - INTF - Club 1	5.0d	22-Nov-27	30-Nov-27	159.0d
9342	FN-MC1-SC-100	Install Fire Protection Trim - Support Circ./Corridors - INTF - Club 1	3.0d	1-Dec-27	3-Dec-27	156.0d
9343	FN-MC1-SC-150	Install Interior Specialties/Mounting Brackets/OFOI - Support Circ./Corridors - I...	10.0d	8-Dec-27	21-Dec-27	154.0d
9344	FN-MC1-SC-160	Apply Final Paint - Support Circ./Corridors - INTF - Club 1	10.0d	22-Dec-27	6-Jan-28	154.0d
9345	FN-MC1-SC-180	Install Door Hardware - Support Circ./Corridors - INTF - Club 1	5.0d	7-Jan-28	13-Jan-28	154.0d
9346	FN-MC1-SC-170	Install Low Voltage Trim Walls/Columns - Support Circ./Corridors - INTF - Club 1	5.0d	7-Jan-28	13-Jan-28	154.0d
9347	FN-MC1-SC-210	Install Fire Alarm Trim Walls/Columns - Support Circ./Corridors - INTF - Club 1	5.0d	7-Jan-28	13-Jan-28	154.0d
9348	FN-MC1-SC-220	Install BAS Trim Walls/Columns - Support Circ./Corridors - INTF - Club 1	5.0d	7-Jan-28	13-Jan-28	154.0d
9349	FN-MC1-SC-190	Install Signage - Support Circ./Corridors - INTF - Club 1	5.0d	14-Jan-28	20-Jan-28	154.0d
9350	WBS - Elect. Room 6676- INTRF - Club 1		105.0d	16-Sep-27	15-Feb-28	137.0d
9351	FN-MC1-ER-3290	Hang, Tape & Finish Drywall - Elec. Room 6676 - INTRF - Club 1	5.0d	16-Sep-27	22-Sep-27	10.0d
9352	FN-MC1-ER-3300	Prime & First Coat - Elec. Room 6676 - INTRF - Club 1	5.0d	23-Sep-27	29-Sep-27	142.0d
9353	FN-MC1-ER-3320	Set Elec. Switchgear & Equip. - Elec. Room 6676 - INTRF - Club 1	10.0d	30-Sep-27	13-Oct-27	142.0d
9354	FN-MC1-ER-7640	Install FCU's-3-6676 - INTRF - Elec. Room 6676 - INTRF - Club 1	2.0d	30-Sep-27	1-Oct-27	200.0d
9355	FN-MC1-ER-7650	FCU Start Up - INTRF - Elec. Room 6676 - INTRF - Club 1	2.0d	4-Oct-27	5-Oct-27	213.0d
9356	FN-MC1-ER-3330	Install Elec. Panels & Transformers - Elec. Room 6676 - INTRF - Club 1	10.0d	14-Oct-27	27-Oct-27	142.0d
9357	FN-MC1-ER-3340	Elec. Feeder Wire Measurements & Procurement - Elec. Room 6676 - INTRF - C...	10.0d	28-Oct-27	10-Nov-27	142.0d
9358	FN-MC1-ER-3390	Install Door - Elec. Room 6676 - INTRF - Club 1	2.0d	28-Oct-27	29-Oct-27	185.0d
9359	FN-MC1-ER-3450	Install Door Hardware - Elec. Room 6676 - INTRF - Club 1	2.0d	1-Nov-27	2-Nov-27	188.0d
9360	FN-MC1-ER-3350	Pull & Terminate Elec. - Elec. Room 6676 - INTRF - Club 1	20.0d	11-Nov-27	10-Dec-27	142.0d
9361	FN-MC1-ER-3360	Third Party Elec. Testing - Elec. Room 6676 - INTRF - Club 1	3.0d	20-Dec-27	22-Dec-27	137.0d
9362	FN-MC1-ER-3444	Patch Fireproofing - Elec. Room 6676 - INTRF - Club 1	3.0d	23-Dec-27	28-Dec-27	141.0d
9363	FN-MC1-ER-3400	Elec. Insp. Perm Power for Test (Post Switchgear Power Available) - Elec. Room ...	2.0d	23-Dec-27	27-Dec-27	137.0d
9364	FN-MC1-ER-3410	APG QC Procedure for Perm Power Available for Dist. - Elec. Room 6676 - INTR...	10.0d	28-Dec-27	11-Jan-28	137.0d
9365	FN-MC1-ER-3370	Install Light Fixtures & Trim - Elec. Room 6676 - INTRF - Club 1	5.0d	29-Dec-27	5-Jan-28	141.0d
9366	FN-MC1-ER-230	Install Low Voltage Trim - Elec. Room 6676 - INTF - Club 1	5.0d	6-Jan-28	12-Jan-28	141.0d

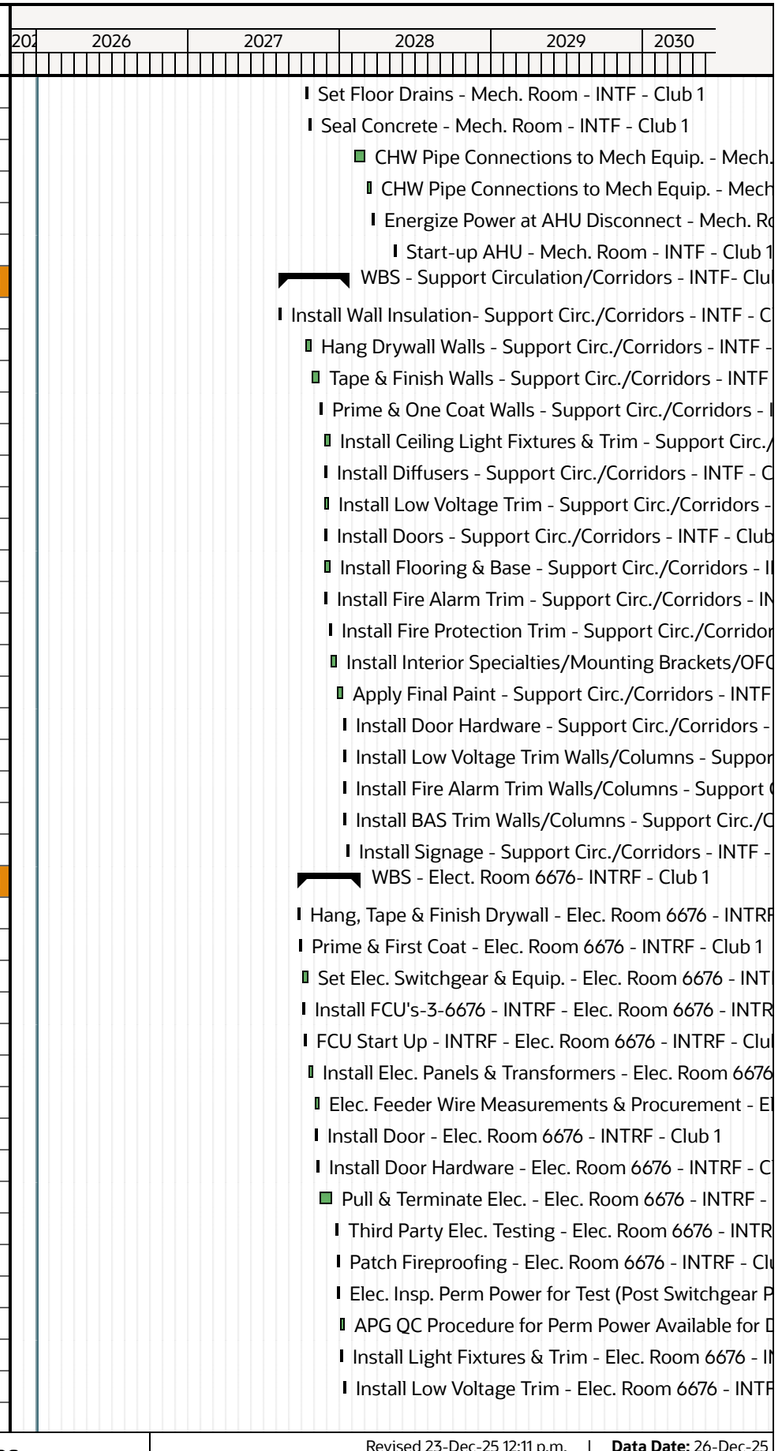


	ID	Name	Dur	Start	Finish	TF
9367	FN-MC1-ER-240	Install Fire Alarm Trim - Elec. Room 6676 - INTF - Club 1	5.0d	6-Jan-28	12-Jan-28	141.0d
9368	FN-MC1-ER-250	Install Fire Protection Trim -Elec. Room 6676 - INTF - Club 1	5.0d	6-Jan-28	12-Jan-28	141.0d
9369	FN-MC1-ER-3440	Seal Concrete - Elec. Room 6676 - INTRF - Club 1	5.0d	12-Jan-28	18-Jan-28	137.0d
9370	FN-MC1-ER-740	Final Checkout & Panel Startup - Elec. Room 6676 - INTRF - Club 1	10.0d	12-Jan-28	25-Jan-28	137.0d
9371	FN-MC1-ER-3380	Apply Final Paint - Elec. Room 6676 - INTRF - Club 1	5.0d	19-Jan-28	25-Jan-28	137.0d
9372	FN-MC1-ER-750	Energize Equip. - Elec. Room 6676 - INTRF - Club 1	15.0d	26-Jan-28	15-Feb-28	137.0d
9373	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Club 2		88.0d	11-Aug-27	15-Dec-27	173.0d
9374	WBS - Anchor Tenant Club/Future Unassigned Tenant - INTF - Club 2		88.0d	11-Aug-27	15-Dec-27	173.0d
9375	FN-CL-MC2-1120	Install Wall Insulation - Anchor Tenant Club - INTF - Club 2	5.0d	11-Aug-27	17-Aug-27	93.0d
9376	FN-CL-MC2-1130	Hang Drywall Walls - Anchor Tenant Club - INTF - Club 2	10.0d	21-Oct-27	3-Nov-27	48.0d
9377	FN-CL-MC2-1140	Tape & Finish Walls - Anchor Tenant Club - INTF - Club 2	10.0d	4-Nov-27	17-Nov-27	48.0d
9378	FN-CL-MC2-1380	Install Interior Glazing Anchor Tenant Club - Anchor Tenant Club - INTF - Club 2	10.0d	18-Nov-27	3-Dec-27	105.0d
9379	FN-CL-MC2-180	Install Elec. Trim - Anchor Tenant Club - INTF - Club 2	5.0d	18-Nov-27	24-Nov-27	100.0d
9380	FN-CL-MC2-170	Install Fire Protection Trim - Anchor Tenant Club - INTF - Club 2	5.0d	29-Nov-27	3-Dec-27	100.0d
9381	FN-CL-MC2-1400	Install Low Voltage Trim - Anchor Tenant Club - INTF - Club 2	5.0d	6-Dec-27	10-Dec-27	100.0d
9382	FN-CL-MC2-190	Install Fire Alarm Trim - Anchor Tenant Club - INTF - Club 2	5.0d	6-Dec-27	10-Dec-27	100.0d
9383	FN-CL-MC2-1410	Install BAS Trim - Anchor Tenant Club - INTF - Club 2	5.0d	6-Dec-27	10-Dec-27	100.0d
9384	FN-CL-MC2-1390	Install Signage - Anchor Tenant Club - INTF - Club 2	3.0d	13-Dec-27	15-Dec-27	173.0d
9385	WBS - Interior Partitions, Finishes & MEPTFP Trim-Out - Club 3		163.0d	3-Jun-27	25-Jan-28	154.0d
9386	WBS - Common Use Club/Unassigned Tenant/Terrace - INTF - Club 3		163.0d	3-Jun-27	25-Jan-28	154.0d
9387	FN-CL-MC3 -10	Install Wall Insulation - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	3-Jun-27	9-Jun-27	207.0d
9388	FN-CL-MC3 -50	Hang Drywall Walls - Common Use/Unassigned Tenant - INTF - Club 3	10.0d	4-Nov-27	17-Nov-27	104.0d
9389	FN-CL-MC3 -180	Tape & Finish Walls - Common Use/Unassigned Tenant - INTF - Club 3	10.0d	4-Nov-27	17-Nov-27	104.0d
9390	FN-CL-MC3 -210	Install Interior Glazing & Doors Common Use- Common Use/Unassigned Tena...	15.0d	18-Nov-27	10-Dec-27	104.0d
9391	FN-CL-MC3-1410	Install Elec. Trim - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	18-Nov-27	24-Nov-27	120.0d
9392	FN-CL-MC3-1420	Install Fire Protection Trim - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	29-Nov-27	3-Dec-27	120.0d
9393	FN-CL-MC3-1430	Install Fire Alarm Trim - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	6-Dec-27	10-Dec-27	120.0d
9394	FN-CL-MC3-1440	Install Low Voltage Trim - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	6-Dec-27	10-Dec-27	120.0d
9395	FN-CL-MC3-1450	Install BAS Trim - Common Use/Unassigned Tenant - INTF - Club 3	5.0d	6-Dec-27	10-Dec-27	120.0d
9396	FN-CL-MC3 -200	Install Column Covers at Terrace - Common Use/Unassigned Tenant - INTF - Cl...	6.0d	13-Dec-27	20-Dec-27	104.0d
9397	FN-CL-MC3 -190	Install Glass Handrail at Terrace - Common Use/Unassigned Tenant - INTF - Cl...	10.0d	21-Dec-27	5-Jan-28	104.0d
9398	FN-CL-MC3 -220	Install Signage - Common Use/Unassigned Tenant - INTF - Club 3	3.0d	21-Jan-28	25-Jan-28	154.0d
9399	WBS - Exterior Roof & Facade		424.0d	22-Jun-26	22-Feb-28	251.0d
9400	MLS-SK-RO-360	Quadrant 1 Structure Ready for Precast - Exterior Roof & Facade	0.0d	15-Dec-26		49.0d
9401	ASD-SK-700	Architectural Pre-Cast Wall Panels (LOE)	106.0d	15-Dec-26	13-May-27	25.0d
9402	MLS-SK-RO-390	Quadrant 4 Structure Ready for Precast - Exterior Roof & Facade	0.0d	26-Jan-27		55.0d
9403	MLS-SK-RO-380	Quadrant 3 Structure Ready for Precast - Exterior Roof & Facade	0.0d	1-Apr-27		17.0d
9404	MLS-SK-RO-400	Early Building Roof Dry In - Exterior Roof & Facade	0.0d		29-Apr-27	81.0d
9405	MLS-SK-RO-370	Quadrant 2 Structure Ready for Precast - Exterior Roof & Facade	0.0d	30-Apr-27		25.0d
9406	WBS - Low Roof		336.0d	14-Sep-26	11-Jan-28	130.0d
9407	WBS - Low Roof Area 1		296.0d	14-Sep-26	10-Nov-27	110.0d
9408	ST-LRF-A1-130	Install Scaffold Tower Roof Access - Low Roof Area 1	5.0d	14-Sep-26	18-Sep-26	53.0d



	ID	Name	Dur	Start	Finish	TF
9409	ST-LRF-A1-200	Install ISO Board & Peel & Stick - Low Roof Area 1.A	10.0d	16-Dec-26	30-Dec-26	53.0d
9410	ST-LRF-A1-10	Install ISO Board & Peel & Stick - Low Roof Area 1.B	10.0d	31-Dec-26	14-Jan-27	54.0d
9411	ST-LRF-A1-210	Install Metal Roofing - Low Roof Area 1.A	15.0d	25-Aug-27	15-Sep-27	100.0d
9412	ST-LRF-A1-100	Install Metal Roofing - Low Roof Area 1.B	15.0d	16-Sep-27	6-Oct-27	100.0d
9413	ST-LRF-A1-120	Install Fall Protection System - Low Roof Area 1	10.0d	7-Oct-27	20-Oct-27	125.0d
9414	ST-LRF-A1-110	Install Lightning Protection System - Low Roof Area 1	15.0d	7-Oct-27	27-Oct-27	110.0d
9415	ST-LRF-A1-90	Install High Mast Apron Lights - Low Roof Area 1	10.0d	28-Oct-27	10-Nov-27	110.0d
9416	WBS - Low Roof Area 2		278.0d	12-Nov-26	17-Dec-27	100.0d
9417	ST-LRF-A1-140	Install Scaffold Tower Roof Access - Low Roof Area 2	5.0d	12-Nov-26	18-Nov-26	118.0d
9418	ST-LRF-A2-130	Install ISO Board & Peel & Stick - Low Roof Area 2.A	10.0d	12-Jan-27	25-Jan-27	84.0d
9419	ST-LRF-A2-10	Install ISO Board & Peel & Stick - Low Roof Area 2.B	10.0d	26-Jan-27	8-Feb-27	102.0d
9420	ST-LRF-A2-140	Install Metal Roofing - Low Roof Area 2.A	15.0d	7-Oct-27	27-Oct-27	100.0d
9421	ST-LRF-A2-100	Install Metal Roofing - Low Roof Area 2.B	15.0d	28-Oct-27	17-Nov-27	100.0d
9422	ST-LRF-A2-110	Install Lightning Protection System - Low Roof Area 2	15.0d	18-Nov-27	10-Dec-27	100.0d
9423	ST-LRF-A2-120	Install Fall Protection System - Low Roof Area 2	10.0d	18-Nov-27	3-Dec-27	105.0d
9424	ST-LRF-A2-90	Install High Mast Apron Lights - Low Roof Area 2	10.0d	18-Nov-27	3-Dec-27	105.0d
9425	ST-LRF-A1-190	Remove Scaffold Tower Roof Access - Low Roof Area 2	5.0d	13-Dec-27	17-Dec-27	100.0d
9426	WBS - Low Roof Area 3		235.0d	8-Feb-27	11-Jan-28	130.0d
9427	ST-LRF-A1-150	Install Scaffold Tower Roof Access - Low Roof Area 3	5.0d	8-Feb-27	12-Feb-27	68.0d
9428	ST-LRF-A3-120	Install ISO Board & Peel & Stick - Low Roof Area 3.A	10.0d	19-Mar-27	1-Apr-27	44.0d
9429	ST-LRF-A3-10	Install ISO Board & Peel & Stick - Low Roof Area 3.B	10.0d	2-Apr-27	15-Apr-27	44.0d
9430	ST-LRF-A3-130	Install Metal Roofing - Low Roof Area 3.A	15.0d	16-Apr-27	6-May-27	44.0d
9431	ST-LRF-A3-90	Install Metal Roofing - Low Roof Area 3.B	15.0d	7-May-27	27-May-27	44.0d
9432	ST-LRF-A3-80	Install High Mast Apron Lights - Low Roof Area 3	10.0d	6-Dec-27	17-Dec-27	137.0d
9433	ST-LRF-A3-110	Install Fall Protection System - Low Roof Area 3	10.0d	6-Dec-27	17-Dec-27	137.0d
9434	ST-LRF-A3-100	Install Lightning Protection System - Low Roof Area 3	15.0d	13-Dec-27	4-Jan-28	125.0d
9435	ST-LRF-A1-180	Remove Scaffold Tower Roof Access - Low Roof Area 3	5.0d	5-Jan-28	11-Jan-28	130.0d
9436	WBS - Mid Roof TPO		240.0d	8-Feb-27	18-Jan-28	125.0d
9437	SK-RO-270	Install Concessions Equip. Curbs & Penetrations - Mid Roof TPO	10.0d	8-Feb-27	19-Feb-27	19.0d
9438	SK-RO-420	Install Fall Protection System (Anchors)- High Roof Metal	5.0d	8-Feb-27	12-Feb-27	340.0d
9439	SK-RO-450	Install TPO Roofing - Mid Roof TPO 1.A	15.0d	19-Mar-27	8-Apr-27	0.0d
9440	SK-RO-60	Install TPO Roofing - Mid Roof TPO 1.B	15.0d	9-Apr-27	29-Apr-27	0.0d
9441	SK-RO-260	Install TPO Walk Pads - Mid Roof TPO	5.0d	30-Apr-27	6-May-27	291.0d
9442	SK-RO-430	Install Fall Protection System (Cabling) - High Roof Metal	10.0d	30-Apr-27	13-May-27	286.0d
9443	SK-RO-250	Install Lightning Protection System - Mid Roof TPO	10.0d	5-Jan-28	18-Jan-28	125.0d
9444	WBS - High Roof Metal		323.0d	22-Jun-26	28-Sep-27	156.0d
9445	ST-LRF-A1-160	Install Scaffold Tower Roof Access - High Roof Metal	5.0d	22-Jun-26	26-Jun-26	151.0d
9446	SK-RO-200	Install ISO Board & Peel & Stick - High Roof Metal - Phase 1.B	10.0d	18-Dec-26	4-Jan-27	31.0d
9447	SK-RO-440	Install ISO Board & Peel & Stick - High Roof Metal - Phase 1.C	15.0d	18-Dec-26	11-Jan-27	26.0d
9448	SK-RO-460	Install ISO Board & Peel & Stick - High Roof Metal - Phase 1.A	15.0d	5-Apr-27	23-Apr-27	0.0d
9449	SK-RO-470	Install Metal Roofing - High Roof Metal 1.A	20.0d	28-May-27	25-Jun-27	44.0d
9450	SK-RO-480	Install Metal Roofing - High Roof Metal 1.B	20.0d	28-Jun-27	26-Jul-27	44.0d

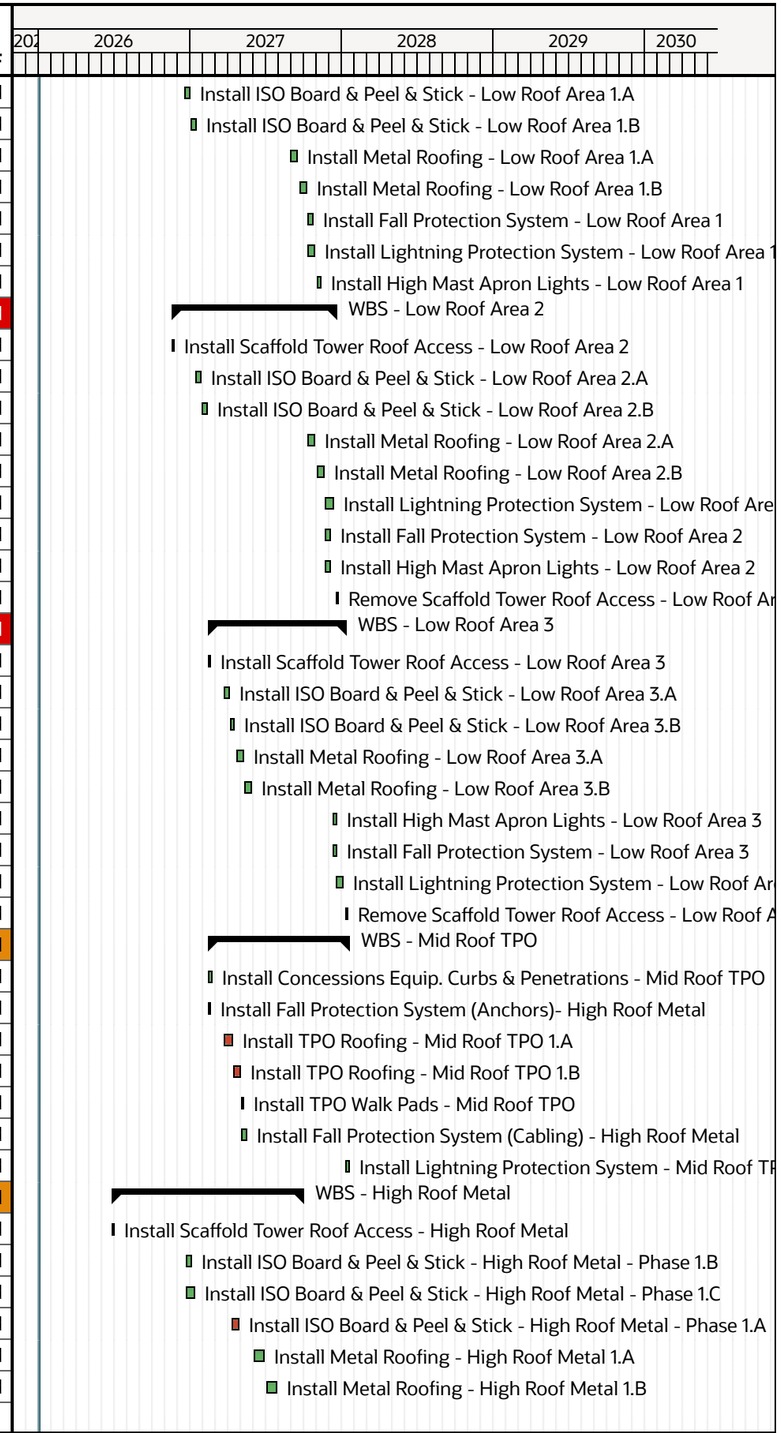


	ID	Name	Dur	Start	Finish	TF
9451	SK-RO-80	Install Metal Roofing - High Roof Metal 1.C	20.0d	27-Jul-27	23-Aug-27	44.0d
9452	SK-RO-90	Install Lightning Protection - High Roof Metal	20.0d	24-Aug-27	21-Sep-27	156.0d
9453	SK-RO-350	Install Fall Protection System - High Roof Metal	15.0d	24-Aug-27	14-Sep-27	161.0d
9454	ST-LRF-A1-170	Remove Scaffold Tower Roof Access - High Roof Metal	5.0d	22-Sep-27	28-Sep-27	156.0d
9455	WBS - Roof Depressed Areas		105.0d	18-Dec-26	17-May-27	445.0d
9456	WBS - North Roof Depressed Area		90.0d	12-Jan-27	17-May-27	445.0d
9457	SK-RO-1000	Install Wall Framing - North Roof Depressed Area	5.0d	12-Jan-27	18-Jan-27	76.0d
9458	SK-RO-1010	Install Ladder Support in Framing - North Roof Depressed Area	2.0d	19-Jan-27	20-Jan-27	76.0d
9459	SK-RO-1020	Install Exterior Sheathing - North Roof Depressed Area	3.0d	21-Jan-27	25-Jan-27	76.0d
9460	SK-RO-1030	Install Vapor-Retarding Air Barrier - North Roof Depressed Area	3.0d	26-Jan-27	28-Jan-27	76.0d
9461	SK-RO-1080	Install Floor Door/Access Hatch - North Roof Depressed Area	2.0d	29-Jan-27	1-Feb-27	76.0d
9462	SK-RO-1070	Install PVC Roof Membrane System - North Roof Depressed Area	4.0d	2-Feb-27	5-Feb-27	76.0d
9463	SK-RO-1040	Insulated Metal Panel Wall System Scan - North Roof Depressed Area	2.0d	8-Feb-27	9-Feb-27	76.0d
9464	SK-RO-1050	Insulated Metal Panel Wall System Fab - North Roof Depressed Area	50.0d	10-Feb-27	20-Apr-27	76.0d
9465	SK-RO-1060	Install Insulated Metal Panels - North Roof Depressed Area	5.0d	21-Apr-27	27-Apr-27	76.0d
9466	SK-RO-1140	Complete Caulking - North Roof Depressed Area	5.0d	28-Apr-27	4-May-27	76.0d
9467	SK-RO-1120	Install Ladder Fall Protection System - North Roof Depressed Area	2.0d	5-May-27	6-May-27	445.0d
9468	SK-RO-1130	Install Ships Ladder - North Roof Depressed Area	2.0d	5-May-27	6-May-27	76.0d
9469	SK-RO-1090	Install Gutter System - North Roof Depressed Area	3.0d	7-May-27	11-May-27	445.0d
9470	SK-RO-1100	Install Mini Split Units - North Roof Depressed Area	4.0d	12-May-27	17-May-27	445.0d
9471	WBS - East Roof Depressed Area		104.0d	18-Dec-26	14-May-27	349.0d
9472	SK-RO-2000	Install Wall Framing - East Roof Depressed Area	7.0d	18-Dec-26	29-Dec-26	80.0d
9473	SK-RO-2020	Install Ladder Support in Framing - East Roof Depressed Area	2.0d	30-Dec-26	31-Dec-26	80.0d
9474	SK-RO-2080	Install Louvered Access Door - East Roof Depressed Area	2.0d	4-Jan-27	5-Jan-27	80.0d
9475	SK-RO-2010	Install Exterior Sheathing - East Roof Depressed Area	5.0d	6-Jan-27	12-Jan-27	80.0d
9476	SK-RO-2040	Install Vapor-Retarding Air Barrier - East Roof Depressed Area	5.0d	13-Jan-27	19-Jan-27	80.0d
9477	SK-RO-2060	Install PVC Roof Membrane System - East Roof Depressed Area	5.0d	20-Jan-27	26-Jan-27	80.0d
9478	SK-RO-2030	Insulated Metal Panel Wall System Scan - East Roof Depressed Area	3.0d	27-Jan-27	29-Jan-27	80.0d
9479	SK-RO-2050	Insulated Metal Panel Wall System Fab - East Roof Depressed Area	50.0d	1-Feb-27	9-Apr-27	80.0d
9480	SK-RO-2110	Install Insulated Metal Panels - East Roof Depressed Area	10.0d	12-Apr-27	23-Apr-27	80.0d
9481	SK-RO-2120	Complete Caulking -East Roof Depressed Area	5.0d	26-Apr-27	30-Apr-27	80.0d
9482	SK-RO-2100	Install Ladder - East Roof Depressed Area	3.0d	3-May-27	5-May-27	349.0d
9483	SK-RO-2090	Install Ladder Fall Protection System - East Roof Depressed Area	2.0d	6-May-27	7-May-27	349.0d
9484	SK-RO-2070	Install Mini Split Units - East Roof Depressed Area	5.0d	10-May-27	14-May-27	349.0d
9485	WBS - Exterior Façade - Quadrant 1		236.0d	21-Sep-26	24-Aug-27	224.0d
9486	WBS - Quadrant 1 - Upper		236.0d	21-Sep-26	24-Aug-27	0.0d
9487	SK-Q1-UP-650	Install Scaffolding (Eave/Gutter) - Q1 Upper	10.0d	21-Sep-26	2-Oct-26	53.0d
9488	SK-Q1-UP-600	Exterior CFMF Framing (Eave/Gutter/Wall) - Q1 Upper	15.0d	5-Oct-26	23-Oct-26	53.0d
9489	SK-Q1-UP-610	Install Exterior Sheathing (Eave/Gutter/Wall) - Q1 Upper	10.0d	19-Oct-26	30-Oct-26	53.0d
9490	SK-Q1-UP-620	Air Barrier (Eave/Gutter/Wall) - Q1 Upper	10.0d	26-Oct-26	6-Nov-26	53.0d
9491	SK-Q1-UP-730	Install PVC Roof System Gutter - Q1 Upper	10.0d	9-Nov-26	20-Nov-26	53.0d
9492	SK-Q1-UP-750	Spray Insulation on Gutter Support Steel - Q1 Upper	5.0d	23-Nov-26	1-Dec-26	53.0d

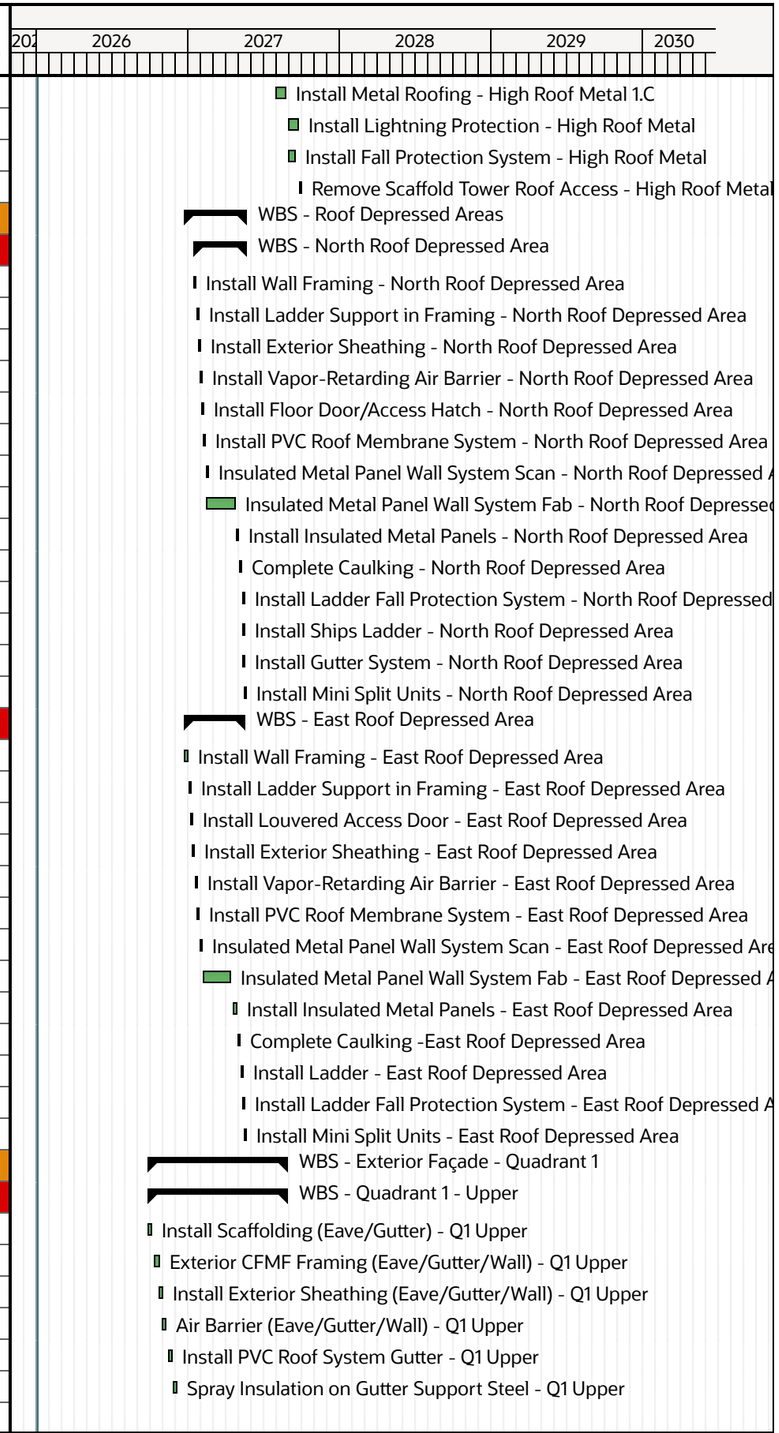


	ID	Name	Dur	Start	Finish	TF
9493	SK-Q1-LO-570	Metal Panel System Scan - Q1 Upper	5.0d	23-Nov-26	1-Dec-26	146.0d
9494	SK-Q1-UP-660	Remove Scaffolding (Eave/Gutter) - Q1 Upper	10.0d	2-Dec-26	15-Dec-26	53.0d
9495	SK-Q1-LO-630	ACM Metal Panel System Fab. - Q1 Upper	20.0d	2-Dec-26	30-Dec-26	146.0d
9496	SK-Q1-UP-630	Curtain Wall System - Q1 Upper	5.0d	21-Jul-27	27-Jul-27	0.0d
9497	SK-Q1-UP-720	Install Louvers - Q1 Upper	5.0d	28-Jul-27	3-Aug-27	15.0d
9498	SK-Q1-UP-640	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q1 Upper	20.0d	28-Jul-27	24-Aug-27	0.0d
9499	WBS - Quadrant 1 - Lower		122.0d	20-Oct-26	13-Apr-27	317.0d
9500	SK-Q1-LO-470	Exterior CFMF Framing (Eave/Gutter/Wall) - Q1 Lower	20.0d	20-Oct-26	16-Nov-26	57.0d
9501	SK-Q1-LO-480	Install Exterior Sheathing (Eave/Gutter/Wall) - Q1 Lower	10.0d	10-Nov-26	23-Nov-26	57.0d
9502	SK-Q1-LO-490	Air Barrier (Eave/Gutter/Wall) - Q1 Lower	10.0d	17-Nov-26	2-Dec-26	57.0d
9503	SK-Q1-UP-740	Install PVC Roof System Gutter - Q1 Lower	15.0d	3-Dec-26	23-Dec-26	135.0d
9504	SK-Q1-LO-500	Pre-Cast System - Q1 Lower	13.0d	15-Dec-26	4-Jan-27	49.0d
9505	SK-Q1-UP-760	Spray Insulation on Gutter Support Steel - Q1 Lower	5.0d	24-Dec-26	31-Dec-26	135.0d
9506	SK-Q1-LO-560	Metal Panel Wall System Scan - Q1 Lower	5.0d	5-Jan-27	11-Jan-27	49.0d
9507	SK-Q1-LO-510	Curtain Wall System - Q1 Lower	14.0d	12-Jan-27	29-Jan-27	49.0d
9508	SK-Q1-LO-690	ACM Metal Panel Wall System Fab. - Q1 Lower	20.0d	12-Jan-27	8-Feb-27	109.0d
9509	SK-Q1-LO-700	Insulated Metal Panel System Fab . - Q1 Lower	50.0d	12-Jan-27	22-Mar-27	93.0d
9510	SK-Q1-LO-520	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q1 Lower	20.0d	9-Feb-27	8-Mar-27	109.0d
9511	SK-Q1-LO-540	Exterior Steel Stairs - Q1 Lower	10.0d	9-Mar-27	22-Mar-27	333.0d
9512	SK-Q1-LO-550	Down Spout Install - Q1 Lower	20.0d	9-Mar-27	5-Apr-27	305.0d
9513	SK-Q1-LO-710	Install Insulated Metal Panels - PBB/Train Tube. - Q1 Lower	6.0d	23-Mar-27	30-Mar-27	93.0d
9514	SK-Q1-LO-530	Install Doors & Windows - Q1 Lower	10.0d	31-Mar-27	13-Apr-27	93.0d
9515	WBS - Exterior Façade - Quadrant 2		193.0d	30-Apr-27	3-Feb-28	124.0d
9516	WBS - Quadrant 2 - Lower		193.0d	30-Apr-27	3-Feb-28	124.0d
9517	SK-Q2-LO-150	Pre-Cast System - Q2 Lower	10.0d	30-Apr-27	13-May-27	25.0d
9518	SK-Q2-LO-30	Exterior CFMF Framing (Eave/Gutter/Wall) - Q2 Lower	20.0d	7-May-27	4-Jun-27	0.0d
9519	SK-Q2-LO-60	Install Exterior Sheathing (Eave/Gutter/Wall) - Q2 Lower	10.0d	28-May-27	11-Jun-27	0.0d
9520	SK-Q2-LO-80	Air Barrier (Eave/Gutter/Wall) - Q2 Lower	10.0d	7-Jun-27	18-Jun-27	0.0d
9521	SK-Q2-LO-170	Install PVC Roof System Gutter - Q2 Lower	10.0d	21-Jun-27	2-Jul-27	217.0d
9522	SK-Q1-LO-580	Metal Panel Wall System Scan - Q2 Lower	5.0d	21-Jun-27	25-Jun-27	0.0d
9523	SK-Q2-LO-190	Curtain Wall System - Q2.A Lower	16.0d	28-Jun-27	20-Jul-27	0.0d
9524	SK-Q1-LO-680	ACM Metal Panel Wall System Fab. - Q2 Lower	20.0d	28-Jun-27	26-Jul-27	207.0d
9525	SK-Q1-LO-720	Insulated Metal Panel System Fab. - Q2 Lower	50.0d	28-Jun-27	7-Sep-27	217.0d
9526	SK-Q2-LO-180	Spray Insulation on Gutter Support Steel - Q2 Lower	5.0d	6-Jul-27	12-Jul-27	217.0d
9527	SK-Q2-LO-120	Curtain Wall System - Q2.B Lower	15.0d	21-Jul-27	10-Aug-27	0.0d
9528	SK-Q2-LO-100	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q2 Lower	20.0d	28-Jul-27	24-Aug-27	206.0d
9529	SK-Q2-LO-130	Install Doors & Windows - Q2 Lower	10.0d	11-Aug-27	24-Aug-27	0.0d
9530	SK-Q2-LO-160	Down Spout Install - Q2 Lower	20.0d	25-Aug-27	22-Sep-27	206.0d
9531	SK-Q1-LO-730	Install Insulated Metal Panels - Q2 Lower	10.0d	8-Sep-27	21-Sep-27	217.0d
9532	SK-Q2-LO-140	Exterior Steel Stairs - Q2 Lower	10.0d	21-Jan-28	3-Feb-28	113.0d
9533	WBS - Exterior Façade - Quadrant 3		246.0d	5-Mar-27	22-Feb-28	111.0d
9534	WBS - Quadrant 3 - Upper		105.0d	5-Mar-27	2-Aug-27	196.0d




	ID	Name	Dur	Start	Finish	TF
9535	SK-Q3-UP-670	Install Scaffolding (Eave/Gutter) - Q3 Upper	15.0d	5-Mar-27	25-Mar-27	56.0d
9536	SK-Q3-UP-160	Exterior CFMF Framing (Eave/Gutter/Wall) - Q3 Upper	20.0d	26-Mar-27	22-Apr-27	56.0d
9537	SK-Q3-UP-170	Install Exterior Sheathing (Eave/Gutter/Wall) - Q3 Upper	10.0d	16-Apr-27	29-Apr-27	56.0d
9538	SK-Q3-UP-180	Air Barrier (Eave/Gutter/Wall) - Q3 Upper	10.0d	23-Apr-27	6-May-27	56.0d
9539	SK-Q3-UP-700	Remove Scaffolding (Eave/Gutter) - Q3 Upper	10.0d	7-May-27	20-May-27	58.0d
9540	SK-Q3-UP-710	Install PVC Roof System Gutter - Q3 Upper	10.0d	7-May-27	20-May-27	221.0d
9541	SK-Q1-LO-590	Metal Panel Wall System Scan - Q3 Upper	20.0d	7-May-27	4-Jun-27	196.0d
9542	SK-Q3-UP-720	Spray Insulation on Gutter Support Steel - Q3 Upper	5.0d	21-May-27	27-May-27	221.0d
9543	SK-Q3-UP-190	Install Curtain Wall System - Q3 Upper	8.0d	25-May-27	4-Jun-27	56.0d
9544	SK-Q1-LO-660	ACM Metal Panel System Fab. - Q3 Upper	20.0d	7-Jun-27	2-Jul-27	196.0d
9545	SK-Q3-UP-200	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q3 Upper	20.0d	6-Jul-27	2-Aug-27	196.0d
9546	WBS - Quadrant 3 - Lower		246.0d	5-Mar-27	22-Feb-28	111.0d
9547	SK-Q3-LO-390	Exterior CFMF Framing (Eave/Gutter/Wall) - Q3 Lower	20.0d	5-Mar-27	1-Apr-27	16.0d
9548	SK-Q3-LO-400	Install Exterior Sheathing (Eave/Gutter/Wall) - Q3 Lower	10.0d	26-Mar-27	8-Apr-27	16.0d
9549	SK-Q3-LO-420	Pre-Cast System - Q3 Lower	5.0d	1-Apr-27	7-Apr-27	17.0d
9550	SK-Q3-LO-410	Air Barrier (Eave/Gutter/Wall) - Q3 Lower	10.0d	2-Apr-27	15-Apr-27	16.0d
9551	SK-Q1-LO-600	Curtain Wall System Scan - Q3 Lower	5.0d	9-Apr-27	15-Apr-27	16.0d
9552	SK-Q3-LO-470	Install PVC Roof System Gutter - Q3 Lower	10.0d	16-Apr-27	29-Apr-27	46.0d
9553	SK-Q3-LO-500	Metal Panel Wall System Scan - Q3.A Lower	5.0d	16-Apr-27	22-Apr-27	16.0d
9554	SK-Q3-LO-430	Curtain Wall System - Q3.B Lower	12.0d	23-Apr-27	10-May-27	44.0d
9555	SK-Q1-LO-670	ACM Metal Panel Wall System Fab. - Q3 Lower	20.0d	23-Apr-27	20-May-27	36.0d
9556	SK-Q1-LO-740	Insulated Metal Panel System Fab. - Q3 Lower	50.0d	23-Apr-27	2-Jul-27	16.0d
9557	SK-Q3-LO-480	Spray Insulation on Gutter Support Steel - Q3 Lower	5.0d	30-Apr-27	6-May-27	46.0d
9558	SK-Q3-LO-440	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q3 Lower	20.0d	21-May-27	18-Jun-27	36.0d
9559	SK-Q1-LO-750	Install Insulated Metal Panels - Q3 Lower	10.0d	6-Jul-27	19-Jul-27	16.0d
9560	SK-Q3-LO-450	Install Doors & Windows - Q3 Lower	10.0d	20-Jul-27	2-Aug-27	16.0d
9561	SK-Q3-LO-490	Down Spout Install - Q3 Lower	10.0d	23-Sep-27	6-Oct-27	206.0d
9562	SK-Q3-LO-460	Exterior Steel Stairs - Q3 Lower	10.0d	9-Feb-28	22-Feb-28	100.0d
9563	WBS - Exterior Façade - Quadrant 4		284.0d	4-Dec-26	18-Jan-28	132.0d
9564	WBS - Quadrant 4 - Upper		90.0d	4-Dec-26	12-Apr-27	265.0d
9565	SK-Q4-UP-680	Install Scaffolding (Eave/Gutter) - Q4 Upper	15.0d	4-Dec-26	24-Dec-26	42.0d
9566	SK-Q4-UP-550	Exterior CFMF Framing (Eave/Gutter/Wall) - Q4 Upper	20.0d	28-Dec-26	25-Jan-27	42.0d
9567	SK-Q4-UP-560	Install Exterior Sheathing (Eave/Gutter/Wall) - Q4 Upper	10.0d	19-Jan-27	1-Feb-27	42.0d
9568	SK-Q4-UP-570	Air Barrier (Eave/Gutter/Wall) - Q4 Upper	10.0d	26-Jan-27	8-Feb-27	42.0d
9569	SK-Q4-UP-710	Remove Scaffolding (Eave/Gutter) - Q4 Upper	10.0d	9-Feb-27	22-Feb-27	46.0d
9570	SK-Q4-UP-730	Install PVC Roof System Gutter - Q4 Upper	10.0d	9-Feb-27	22-Feb-27	275.0d
9571	SK-Q1-LO-610	Metal Panel Wall System Scan - Q4 Upper	5.0d	9-Feb-27	15-Feb-27	51.0d
9572	SK-Q1-LO-640	ACM Metal Panel Wall System Fab. - Q4 Upper	20.0d	16-Feb-27	15-Mar-27	265.0d
9573	SK-Q4-UP-720	Spray Insulation on Gutter Support Steel - Q4 Upper	5.0d	23-Feb-27	1-Mar-27	275.0d
9574	SK-Q4-UP-580	Curtain Wall System - Q4 Upper	6.0d	1-Mar-27	8-Mar-27	42.0d
9575	SK-Q4-UP-590	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q4 Upper	20.0d	16-Mar-27	12-Apr-27	265.0d
9576	WBS - Quadrant 4 - Lower		284.0d	4-Dec-26	18-Jan-28	132.0d

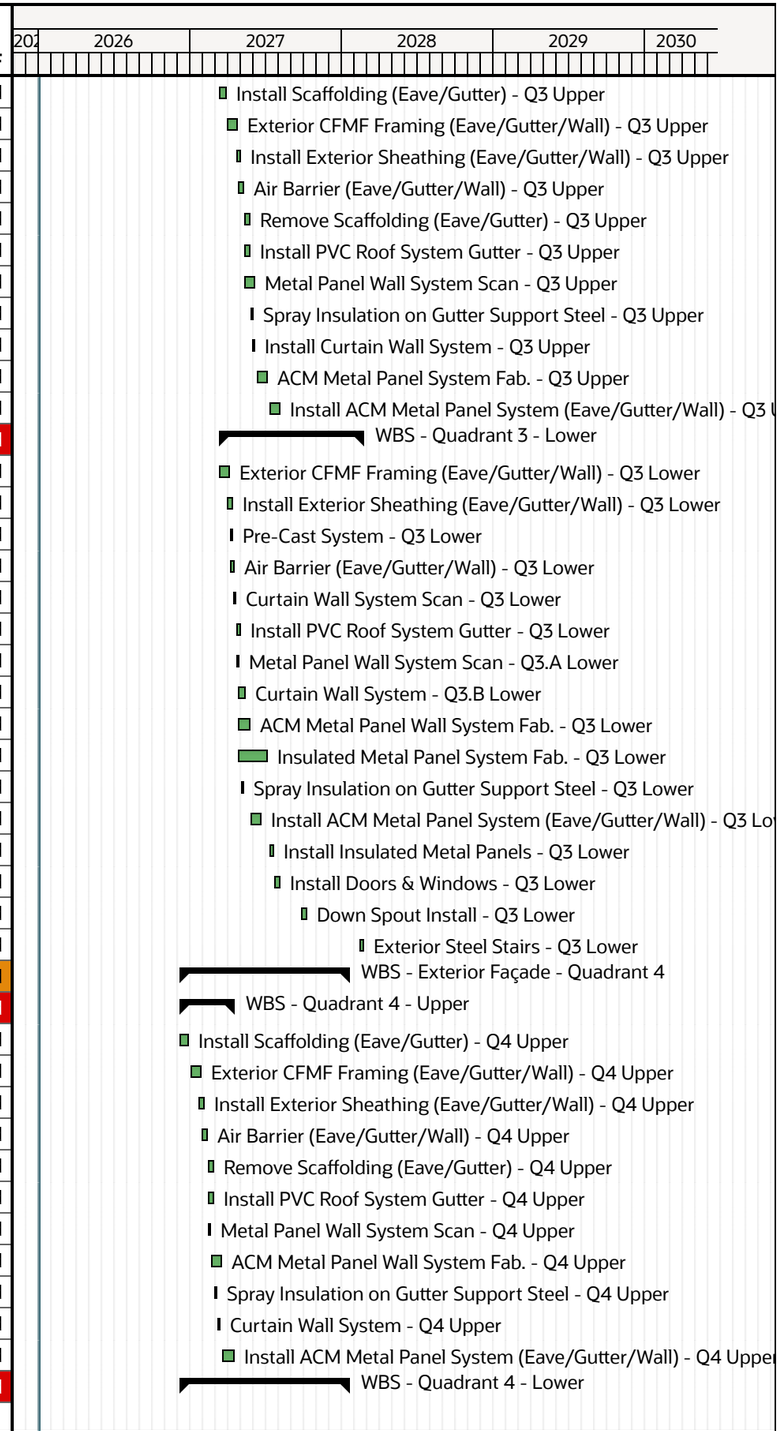


	ID	Name	Dur	Start	Finish	TF
9577	SK-Q4-LO-310	Exterior CFMF Framing (Eave/Gutter/Wall) - Q4 Lower	20.0d	4-Dec-26	4-Jan-27	61.0d
9578	SK-Q4-LO-320	Install Exterior Sheathing (Eave/Gutter/Wall) - Q4 Lower	10.0d	28-Dec-26	11-Jan-27	61.0d
9579	SK-Q4-LO-330	Air Barrier (Eave/Gutter/Wall) - Q4 Lower	10.0d	5-Jan-27	18-Jan-27	61.0d
9580	SK-Q4-LO-390	Install PVC Roof System Gutter - Q4 Lower	10.0d	19-Jan-27	1-Feb-27	109.0d
9581	SK-Q1-LO-620	Metal Panel Wall System Scan - Q4 Lower	5.0d	19-Jan-27	25-Jan-27	61.0d
9582	SK-Q4-LO-340	Pre-Cast System - Q4 Lower	6.0d	26-Jan-27	2-Feb-27	55.0d
9583	SK-Q1-LO-650	ACM Metal Panel Wall System Fab. - Q4 Lower	20.0d	26-Jan-27	22-Feb-27	99.0d
9584	SK-Q1-LO-760	Insulated Metal Panel System Fab. - Q4 Lower	50.0d	26-Jan-27	5-Apr-27	74.0d
9585	SK-Q4-LO-400	Spray Insulation on Gutter Support Steel - Q4 Lower	5.0d	2-Feb-27	8-Feb-27	109.0d
9586	SK-Q4-LO-350	Curtain Wall System - Q4.B Lower	11.0d	3-Feb-27	17-Feb-27	55.0d
9587	SK-Q4-LO-490	Curtain Wall System - Q4.A Lower	12.0d	18-Feb-27	5-Mar-27	107.0d
9588	SK-Q4-LO-360	Install ACM Metal Panel System (Eave/Gutter/Wall) - Q4 Lower	20.0d	23-Feb-27	22-Mar-27	99.0d
9589	SK-Q4-LO-410	Down Spout Install - Q4 Lower	10.0d	23-Mar-27	5-Apr-27	270.0d
9590	SK-Q1-LO-770	Install Insulated Metal Panels. - Q4 Lower	15.0d	6-Apr-27	26-Apr-27	74.0d
9591	SK-Q4-LO-370	Install Doors & Windows - Q4 Lower	10.0d	27-Apr-27	10-May-27	74.0d
9592	SK-Q4-LO-380	Install Exterior Steel Stairs - Q4 Lower	10.0d	5-Jan-28	18-Jan-28	125.0d
9593	WBS - Smoking Terrace		45.0d	18-Feb-27	21-Apr-27	319.0d
9594	SK-Q4-LO-480	FRP Footers - Q4 Smoking Terrace	5.0d	18-Feb-27	24-Feb-27	338.0d
9595	SK-Q4-LO-420	Erect Structural Steel/Decking - Q4 Smoking Terrace	5.0d	3-Mar-27	9-Mar-27	334.0d
9596	SK-Q4-LO-430	FRP SOMD - Q4 Smoking Terrace	4.0d	10-Mar-27	15-Mar-27	334.0d
9597	SK-Q4-LO-440	Install Perforated Metal Infill Panels - Q4 Smoking Terrace	5.0d	16-Mar-27	22-Mar-27	334.0d
9598	SK-Q4-LO-450	Install PVC Roofing W/ Gutter - Q4 Smoking Terrace	4.0d	23-Mar-27	26-Mar-27	334.0d
9599	SK-Q4-LO-470	Install Plumbing for Downspouts - Q4 Smoking Terrace	3.0d	6-Apr-27	8-Apr-27	328.0d
9600	SK-Q1-LO-780	Install Insulated Metal Panels. - Q4 Smoking Terrace	10.0d	6-Apr-27	19-Apr-27	319.0d
9601	SK-Q4-LO-460	Install FF&E - Q4 Smoking Terrace	2.0d	20-Apr-27	21-Apr-27	319.0d
9602	WBS - ASD - Baggage Handling Systems (BHS)		603.0d	25-Aug-26	10-Jan-29	305.0d
9603	WBS - ASD - Baggage Handling Systems (BHS) - Level of Efforts (LOE)		444.0d	18-Nov-26	17-Aug-28	404.0d
9604	WBS - ASD - BHS - Level of Effort - Apron 2		262.0d	18-Nov-26	1-Dec-27	238.0d
9605	BG-AP2-LOE-10	ASD - BHS - Steel Install - LOE - AP2	18.0d	18-Nov-26	15-Dec-26	340.0d
9606	BG-AP2-LOE-20	ASD - BHS - Install Conveyor - LOE - AP2	47.0d	15-Jan-27	22-Mar-27	392.0d
9607	BG-AP2-LOE-30	ASD - BHS - Install Catwalk - LOE - AP2	43.0d	20-Jan-27	19-Mar-27	393.0d
9608	BG-AP2-LOE-40	ASD - BHS - Elec.& Controls Rough-In - LOE - AP2	38.0d	4-Feb-27	29-Mar-27	392.0d
9609	BG-AP2-LOE-50	ASD - BHS - Testing & Commissioning - LOE - AP2	200.0d	18-Feb-27	1-Dec-27	238.0d
9610	WBS - ASD - BHS - Level of Effort - Apron 4		276.0d	26-Jan-27	24-Feb-28	527.0d
9611	BG-AP4-LOE-10	ASD - BHS - Steel Install - LOE - AP4	36.0d	26-Jan-27	16-Mar-27	262.0d
9612	BG-AP4-LOE-20	ASD - BHS - Install Conveyor - LOE - AP4	111.0d	10-Sep-27	17-Feb-28	165.0d
9613	BG-AP4-LOE-30	ASD - BHS - Install Catwalk - LOE - AP4	93.0d	17-Sep-27	31-Jan-28	176.0d
9614	BG-AP4-LOE-40	ASD - BHS - Elec. & Controls Rough-In - LOE - AP4	103.0d	27-Sep-27	22-Feb-28	528.0d
9615	BG-AP4-LOE-50	ASD - BHS - Testing & Commissioning - LOE - AP4	100.0d	4-Oct-27	24-Feb-28	164.0d
9616	WBS - ASD - BHS - Level of Effort - Apron 5		339.0d	20-Apr-27	17-Aug-28	41.0d
9617	BG-AP5-LOE-10	ASD - BHS - Steel Install - LOE - AP5	35.0d	20-Apr-27	8-Jun-27	225.0d
9618	BG-AP5-LOE-20	ASD - BHS - Install Conveyor - LOE - AP5	15.0d	16-Jun-27	7-Jul-27	220.0d

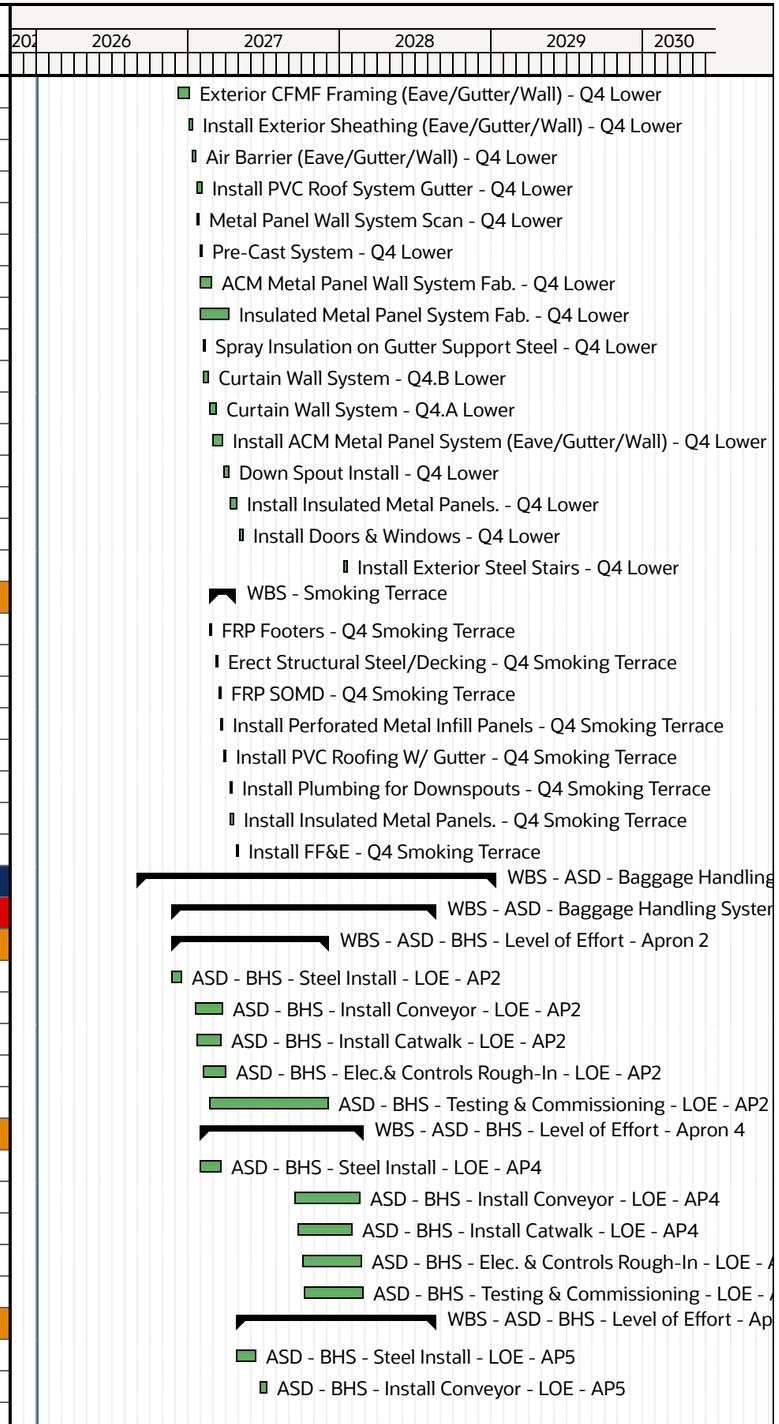


	ID	Name	Dur	Start	Finish	TF
9619	BG-AP5-LOE-30	ASD - BHS - Install Catwalk - LOE - AP5	73.0d	23-Jun-27	5-Oct-27	247.0d
9620	BG-AP5-LOE-40	ASD - BHS - Elec. & Controls Rough-In - LOE - AP5	282.0d	12-Jul-27	17-Aug-28	28.0d
9621	BG-AP5-LOE-50	ASD - BHS - Testing & Commissioning - LOE - AP5	5.0d	16-Jul-27	22-Jul-27	314.0d
9622	WBS - ASD - BHS - Level of Effort - Apron 8		259.0d	2-Jun-27	7-Jun-28	91.0d
9623	BG-AP8-LOE-10	ASD - BHS - Steel Install - LOE - AP8	11.0d	2-Jun-27	16-Jun-27	279.0d
9624	BG-AP8-LOE-20	ASD - BHS - Install Conveyor - LOE - AP8	33.0d	30-Jun-27	16-Aug-27	295.0d
9625	BG-AP8-LOE-30	ASD - BHS - Install Catwalk - LOE - AP8	10.0d	8-Jul-27	21-Jul-27	270.0d
9626	BG-AP8-LOE-40	ASD - BHS - Elec. & Controls Rough-In - LOE - AP8	224.0d	22-Jul-27	7-Jun-28	78.0d
9627	BG-AP8-LOE-50	ASD - BHS - Testing & Commissioning - LOE - AP8	3.0d	28-Jul-27	30-Jul-27	308.0d
9628	WBS - ASD - BHS - Level of Effort - Apron 9		164.0d	11-May-27	4-Jan-28	523.0d
9629	BG-AP9-LOE-10	ASD - BHS - Steel Install - LOE - AP9	36.0d	11-May-27	30-Jun-27	277.0d
9630	BG-AP9-LOE-20	ASD - BHS - Install Conveyor - LOE - AP9	0.0d	30-Sep-27	30-Sep-27	233.0d
9631	BG-AP9-LOE-30	ASD - BHS - Install Catwalk - LOE - AP9	20.0d	5-Oct-27	1-Nov-27	233.0d
9632	BG-AP9-LOE-40	ASD - BHS - Elec. & Controls Rough-In - LOE - AP9	52.0d	19-Oct-27	4-Jan-28	522.0d
9633	BG-AP9-LOE-50	ASD - BHS - Testing & Commissioning - LOE - AP9	5.0d	23-Nov-27	1-Dec-27	223.0d
9634	WBS - ASD - Baggage Handling Systems - (BHS) - Sector J - Apron 2		262.0d	18-Nov-26	1-Dec-27	586.0d
9635	WBS - ASD - BHS - Steel Erection - Apron 2		18.0d	18-Nov-26	15-Dec-26	340.0d
9636	BG-AP2-BS-10	Layout & Install Hangers & Steel - AP2	18.0d	18-Nov-26	15-Dec-26	66.0d
9637	BG-AP2-BS-20	Header Steel Inspection - AP2	2.0d	14-Dec-26	15-Dec-26	340.0d
9638	WBS - TD1 & TD2 - Apron 2		224.0d	15-Jan-27	1-Dec-27	586.0d
9639	WBS - TD1-42 - TD1-51 - Apron 2		27.0d	15-Jan-27	22-Feb-27	420.0d
9640	BG-AP2-TD1-30	Conveyor Layout & Install - TD1-42 - TD1-51 - Ceiling Mounted - AP2	10.0d	15-Jan-27	28-Jan-27	320.0d
9641	BG-AP2-TD1-40	Install Catwalk - TD1-42 - TD1-51 - Ceiling Mounted - AP2	10.0d	20-Jan-27	2-Feb-27	320.0d
9642	BG-AP2-TD1-50	Conveyor Detailing - TD1-42 - TD1-51 - Ceiling Mounted - AP2	8.0d	25-Jan-27	3-Feb-27	320.0d
9643	BG-AP2-TD1-60	Elec. & Controls Rough-In - TD1-42 - TD1-51 - Ceiling Mounted - AP2	10.0d	4-Feb-27	17-Feb-27	419.0d
9644	BG-AP2-TD1-80	Internal Mech. Statics - TD1-42 - TD1-51 - Ceiling Mounted - AP2	2.0d	18-Feb-27	19-Feb-27	420.0d
9645	BG-AP2-TD1-90	Owner Mech. Statics - TD1-42 - TD1-51 - Ceiling Mounted - AP2	1.0d	22-Feb-27	22-Feb-27	420.0d
9646	WBS - TD2-41 - TD2-51 - Apron 2		31.0d	4-Feb-27	18-Mar-27	402.0d
9647	BG-AP2-TD2-30	Install Conveyor - TD2-41 - TD2-52 - Ceiling Mounted - AP2	10.0d	4-Feb-27	17-Feb-27	335.0d
9648	BG-AP2-TD2-40	Install Catwalk - TD2-41 - TD2-52 - Ceiling Mounted - AP2	10.0d	9-Feb-27	22-Feb-27	339.0d
9649	BG-AP2-TD2-50	Conveyor Detailing - TD2-41 - TD2-52 - Ceiling Mounted - AP2	8.0d	18-Feb-27	1-Mar-27	335.0d
9650	BG-AP2-TD2-60	Elec. & Controls Rough-In - TD2-41 - TD2-52 - Ceiling Mounted - AP2	10.0d	2-Mar-27	15-Mar-27	401.0d
9651	BG-AP2-TD2-80	Internal Mech. Statics - TD2-41 - TD2-52 - Ceiling Mounted - AP2	2.0d	16-Mar-27	17-Mar-27	402.0d
9652	BG-AP2-TD2-90	Owner Mech. Statics - TD2-41 - TD2-52 - Ceiling Mounted - AP2	1.0d	18-Mar-27	18-Mar-27	402.0d
9653	WBS - TD1 & TD2 - ATR - Apron 2		20.0d	18-Feb-27	17-Mar-27	766.0d
9654	BG-AP2-ATR-10	Field Measure & Procurement - TD1 & TD2 - ATR - AP2	10.0d	18-Feb-27	3-Mar-27	765.0d
9655	BG-AP2-ATR-20	Mech. Install - TD1 & TD2 - ATR - AP2	5.0d	4-Mar-27	10-Mar-27	765.0d
9656	BG-AP2-ATR-30	Elec. & Controls Install - TD1 & TD2 - ATR - AP2	2.0d	9-Mar-27	10-Mar-27	765.0d
9657	BG-AP2-ATR-50	Testing - TD1 & TD2 - ATR - AP2	5.0d	11-Mar-27	17-Mar-27	765.0d
9658	WBS - TD1 & TD2 - Elec. Panel Install - Apron 2 & Sector J		197.0d	23-Feb-27	1-Dec-27	238.0d
9659	BG-AP2-TD1&2-MPP-10	TD1 & TD2 - Layout & Install Elec. Panel MPP-A30 & MPP-B30 - AP2 & Sector J	2.0d	23-Feb-27	24-Feb-27	408.0d
9660	BG-AP2-TD1&2-MPP-20	TD1 & TD2 - Elec. Feeder Wire Measurement & Procurement - MPP-A30 & MP...	10.0d	25-Feb-27	10-Mar-27	408.0d

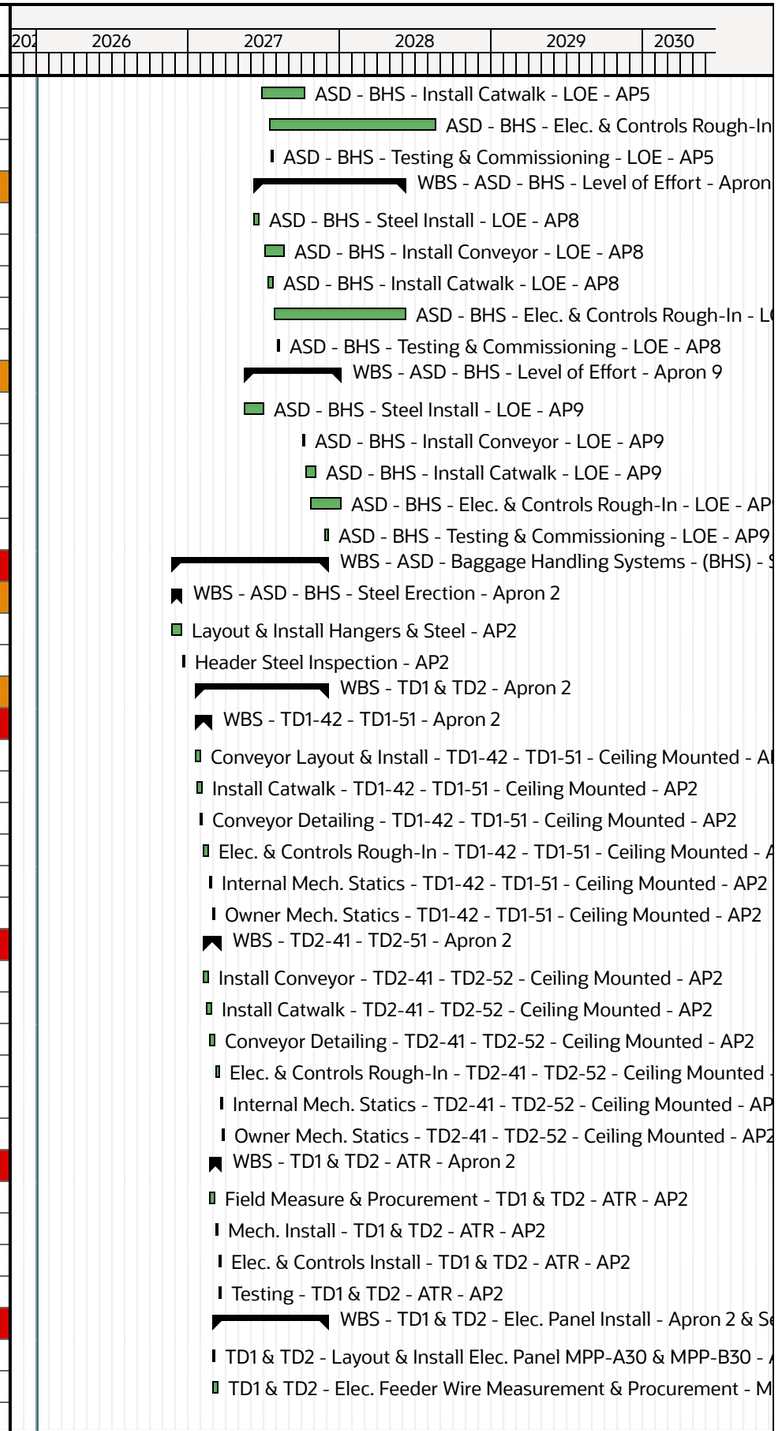


	ID	Name	Dur	Start	Finish	TF
9661	BG-AP2-TD1&2-MPP-30	TD1 & TD2 - Pull & Terminate Elec. - MPP-A30 & MPP-B30 - AP2 & Sector J	10.0d	11-Mar-27	24-Mar-27	408.0d
9662	BG-AP2-TD1&2-MPP-40	TD1 & TD2 - Elec. Testing & Inspection- MPP-A30 & MPP-B30 - AP2 & Sector J	5.0d	23-Nov-27	1-Dec-27	238.0d
9663	WBS - SD1 - Apron 2		14.0d	4-Feb-27	23-Feb-27	419.0d
9664	WBS - SD1-01 - SD1-03 - Apron 2		14.0d	4-Feb-27	23-Feb-27	419.0d
9665	BG-AP2-SD1-30	Install Conveyor - SD1-01 - SD1-03 - Ceiling Mounted - AP2	2.0d	4-Feb-27	5-Feb-27	320.0d
9666	BG-AP2-SD1-40	Install Catwalk - SD1-01 - SD1-03 - Ceiling Mounted - AP2	3.0d	5-Feb-27	9-Feb-27	320.0d
9667	BG-AP2-SD1-50	Conveyor Detailing - SD1-01 - SD1-03 - Ceiling Mounted - AP2	2.0d	8-Feb-27	9-Feb-27	320.0d
9668	BG-AP2-SD1-60	Elec. & Controls Rough-In - SD1-01 - SD1-03 - Ceiling Mounted - AP2	2.0d	18-Feb-27	19-Feb-27	419.0d
9669	BG-AP2-SD1-80	Internal Mech. Statics - SD1-01 - SD1-03 - Ceiling Mounted - AP2	1.0d	22-Feb-27	22-Feb-27	419.0d
9670	BG-AP2-SD1-90	Owner Mech. Statics - SD1-01 - SD1-03 - Ceiling Mounted - AP2	1.0d	23-Feb-27	23-Feb-27	419.0d
9671	WBS - SD2 - Apron 2		14.0d	2-Mar-27	19-Mar-27	401.0d
9672	WBS - SD2-01 & SD2-02 - Apron 2		14.0d	2-Mar-27	19-Mar-27	401.0d
9673	BG-AP2-SD2-30	Install Conveyor - SD2-01 & SD2-02 - Ceiling Mounted - AP2	2.0d	2-Mar-27	3-Mar-27	335.0d
9674	BG-AP2-SD2-40	Install Catwalk - SD2-01 & SD2-02 - Ceiling Mounted - AP2	3.0d	3-Mar-27	5-Mar-27	335.0d
9675	BG-AP2-SD2-50	Conveyor Detailing - SD2-01 & SD2-02 - Ceiling Mounted - AP2	2.0d	4-Mar-27	5-Mar-27	335.0d
9676	BG-AP2-SD2-60	Elec. & Controls Rough-In - SD2-01 & SD2-02 - Ceiling Mounted - AP2	2.0d	16-Mar-27	17-Mar-27	401.0d
9677	BG-AP2-SD2-80	Internal Mech. Statics - SD2-01 & SD2-02 - Ceiling Mounted - AP2	1.0d	18-Mar-27	18-Mar-27	401.0d
9678	BG-AP2-SD2-90	Owner Mech. Statics - SD2-01 & SD2-02 - Ceiling Mounted - AP2	1.0d	19-Mar-27	19-Mar-27	401.0d
9679	WBS - RID1 - Apron 2		19.0d	8-Mar-27	1-Apr-27	392.0d
9680	WBS - RID1-11 - RID1-16 - Apron 2		19.0d	8-Mar-27	1-Apr-27	392.0d
9681	BG-AP2-RID1-30	Install Conveyor - RID1-11 - RID1-16 - Ceiling Mounted - AP2	7.0d	8-Mar-27	16-Mar-27	392.0d
9682	BG-AP2-RID1-40	Install Catwalk - RID1-11 - RID1-16 - Ceiling Mounted - AP2	7.0d	11-Mar-27	19-Mar-27	393.0d
9683	BG-AP2-RID1-50	Conveyor Detailing - RID1-11 - RID1-16 - Ceiling Mounted - AP2	4.0d	17-Mar-27	22-Mar-27	392.0d
9684	BG-AP2-RID1-60	Elec. & Controls Rough-In - RID1-11 - RID1-16 - Ceiling Mounted - AP2	5.0d	23-Mar-27	29-Mar-27	392.0d
9685	BG-AP2-RID1-80	Internal Mech. Statics - RID1-11 - RID1-16 - Ceiling Mounted - AP2	2.0d	30-Mar-27	31-Mar-27	392.0d
9686	BG-AP2-RID1-90	Owner Mech. Statics - RID1-11 - RID1-16 - Ceiling Mounted - AP2	1.0d	1-Apr-27	1-Apr-27	392.0d
9687	WBS - ASD - Baggage Handling Systems - (BHS) - Sector F - Apron 4		276.0d	26-Jan-27	24-Feb-28	527.0d
9688	WBS - ASD - BHS - Steel Erection - Apron 4		36.0d	26-Jan-27	16-Mar-27	262.0d
9689	BG-AP4-BS-10	Layout & Install Hangers & Steel - AP4	36.0d	26-Jan-27	16-Mar-27	39.0d
9690	BG-AP4-BS-20	Header Steel Inspection - AP4	8.0d	5-Mar-27	16-Mar-27	262.0d
9691	WBS - SD1 & SD2 - Apron 4		103.0d	10-Sep-27	7-Feb-28	540.0d
9692	WBS - SD1-04 - SD1-16 - Apron 4		32.0d	10-Sep-27	25-Oct-27	248.0d
9693	BG-AP4-SD1-120	Install Conveyor - SD1-04 - SD1-16 - Ceiling Mounted - AP4	14.0d	10-Sep-27	29-Sep-27	171.0d
9694	BG-AP4-SD1-130	Install Catwalk - SD1-04 - SD1-16 - Ceiling Mounted - AP4	14.0d	17-Sep-27	6-Oct-27	171.0d
9695	BG-AP4-SD1-140	Conveyor Detailing - SD1 -04 - SD1-16 - Ceiling Mounted - AP4	8.0d	27-Sep-27	6-Oct-27	171.0d
9696	BG-AP4-SD1-150	Elec. & Controls Rough-In - SD1-04 - SD1-16 - Ceiling Mounted - AP4	10.0d	7-Oct-27	20-Oct-27	248.0d
9697	BG-AP4-SD1-170	Internal Mech. Statics - SD1-04 - SD-16 - Ceiling Mounted - AP4	2.0d	21-Oct-27	22-Oct-27	248.0d
9698	BG-AP4-SD1-180	Owner Mech. Statics - SD1-04 - SD-16 - Ceiling Mounted - AP4	1.0d	25-Oct-27	25-Oct-27	248.0d
9699	WBS - SD2-02 - SD2-13 - Apron 4		31.0d	10-Sep-27	22-Oct-27	249.0d
9700	BG-AP4-SD2-120	Install Conveyor - SD2-02 - SD2-13 - Ceiling Mounted - AP4	11.0d	10-Sep-27	24-Sep-27	204.0d
9701	BG-AP4-SD2-130	Install Catwalk - SD2-04 - SD2-13 - Ceiling Mounted - AP4	12.0d	17-Sep-27	4-Oct-27	223.0d
9702	BG-AP4-SD2-140	Conveyor Detailing - SD2-04 - SD2-13 - Ceiling Mounted - AP4	7.0d	27-Sep-27	5-Oct-27	222.0d

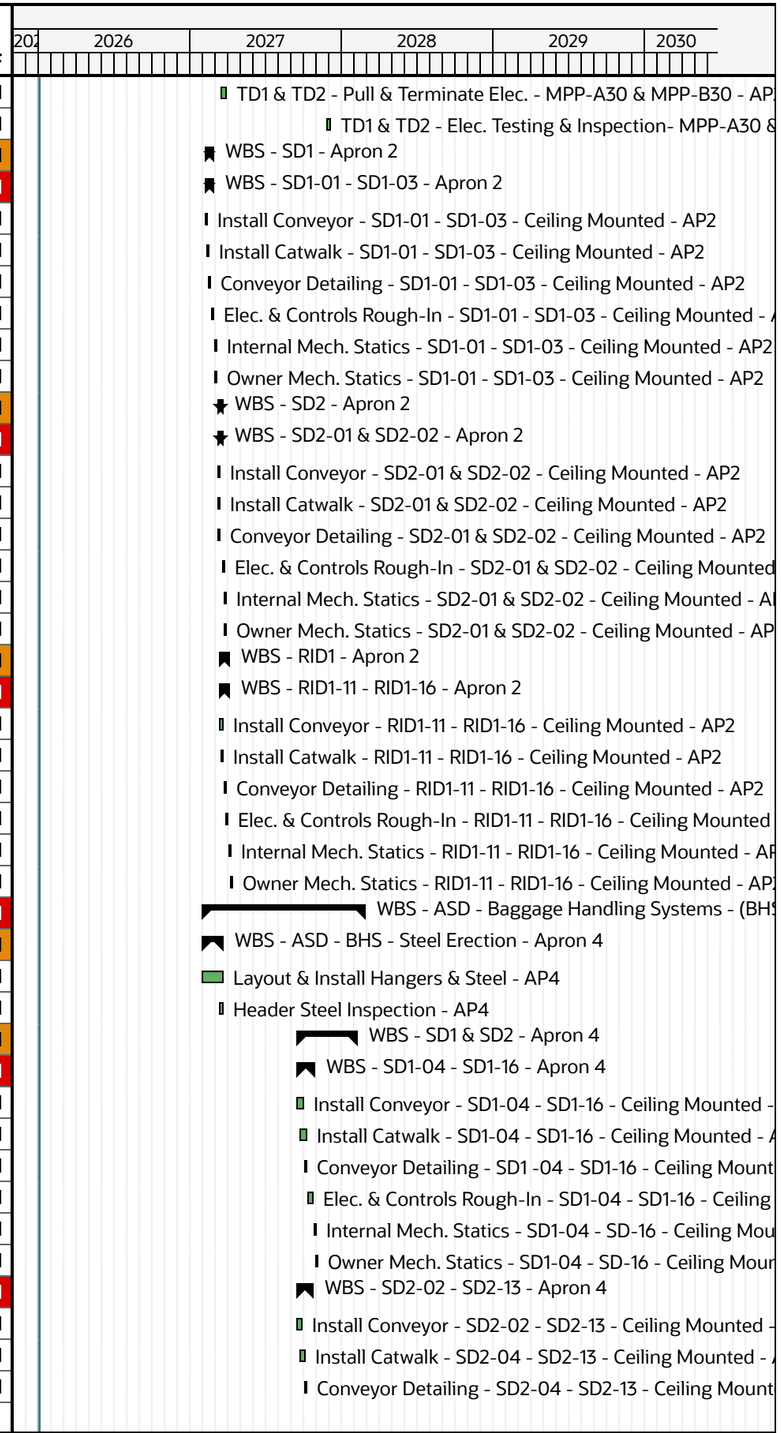


	ID	Name	Dur	Start	Finish	TF
9703	BG-AP4-SD2-150	Elec. & Controls Install - SD2-02 - SD2-13 - Ceiling Mounted - AP4	10.0d	6-Oct-27	19-Oct-27	249.0d
9704	BG-AP4-SD2-170	Internal Mech. Statics - SD2-02 - SD2-13 - Ceiling Mounted - AP4	2.0d	20-Oct-27	21-Oct-27	249.0d
9705	BG-AP4-SD2-180	Owner Mech. Statics - SD2-02 - SD2-13 - Ceiling Mounted - AP4	1.0d	22-Oct-27	22-Oct-27	249.0d
9706	WBS - SD2 - Elec. Panel Install - Apron 4		27.0d	30-Dec-27	7-Feb-28	540.0d
9707	WBS - SD2 - MPP-B31 & FCP-B31 - Apron 4		27.0d	30-Dec-27	7-Feb-28	540.0d
9708	BG-AP4-SD2-MPP-70	SD2 - Layout & Install Elec. Panel - MPP-B31 & FCP-B31 - AP4	2.0d	30-Dec-27	3-Jan-28	539.0d
9709	BG-AP4-SD2-MPP-80	SD2 - Elec. Feeder Wire Measurement & Procurement - MPP-B31 & FCP-B31 - ...	10.0d	4-Jan-28	17-Jan-28	539.0d
9710	BG-AP4-SD2-MPP-90	SD2 - Pull & Terminate Elec. - MPP-B31 & FCP-B31 - AP4	10.0d	18-Jan-28	31-Jan-28	539.0d
9711	BG-AP4-SD2-MPP-100	SD2 - Elec. Testing & Inspection- MPP-B31 & FCP-B31 - AP4	5.0d	1-Feb-28	7-Feb-28	539.0d
9712	WBS - MED1 & MED2 - Apron 4		34.0d	27-Sep-27	11-Nov-27	235.0d
9713	WBS - MED1-01 - MED1-12 - Make-Up - Apron 4		26.0d	7-Oct-27	11-Nov-27	235.0d
9714	BG-AP4-MED1-30	Install Conveyor - MED1-01 - MED1-12 - Ceiling Mounted - AP4	10.0d	7-Oct-27	20-Oct-27	235.0d
9715	BG-AP4-MED1-40	Install Catwalk - MED1-01 - MED1-12 - Ceiling Mounted - AP4	10.0d	14-Oct-27	27-Oct-27	235.0d
9716	BG-AP4-MED1-50	Conveyor Detailing - MED1-01 - MED1-12 - Ceiling Mounted - AP4	6.0d	20-Oct-27	27-Oct-27	235.0d
9717	BG-AP4-MED1-60	Elec. & Controls Rough-In - MED1-01 - MED1-12 - Ceiling Mounted - AP4	8.0d	28-Oct-27	8-Nov-27	235.0d
9718	BG-AP4-MED1-70	Internal Mech. Statics - MED1-01 - MED1-12 - Ceiling Mounted - AP4	2.0d	9-Nov-27	10-Nov-27	235.0d
9719	BG-AP4-MED1-80	Owner Mech. Statics - MED1-01 - MED1-12 - Ceiling Mounted - AP4	1.0d	11-Nov-27	11-Nov-27	235.0d
9720	WBS - MED2-01 - MED2-12 - Make-Up - Apron 4		26.0d	27-Sep-27	1-Nov-27	243.0d
9721	BG-AP4-MED2-30	Install Conveyor - MED2-01 - MED2-12 - Ceiling Mounted - AP4	10.0d	27-Sep-27	8-Oct-27	243.0d
9722	BG-AP4-MED2-40	Install Catwalk - MED2-01 - MED2-12 - Ceiling Mounted - AP4	10.0d	4-Oct-27	15-Oct-27	243.0d
9723	BG-AP4-MED2-50	Conveyor Detailing - MED2-01 - MED2-12 - Ceiling Mounted - AP4	6.0d	8-Oct-27	15-Oct-27	243.0d
9724	BG-AP4-MED2-60	Elec. & Controls Rough-In - MED2-01 - MED2-12 - Ceiling Mounted - AP4	8.0d	18-Oct-27	27-Oct-27	243.0d
9725	BG-AP4-MED2-70	Internal Mech. Statics - MED2-01 - MED2-12 - Ceiling Mounted - AP4	2.0d	28-Oct-27	29-Oct-27	243.0d
9726	BG-AP4-MED2-80	Owner Mech. Statics - MED2-01 - MED2-12 - Ceiling Mounted - AP4	1.0d	1-Nov-27	1-Nov-27	243.0d
9727	WBS - RID1 - Apron 4		31.0d	10-Sep-27	22-Oct-27	249.0d
9728	WBS - RID1-07 - RID1-10 - Apron 4		31.0d	10-Sep-27	22-Oct-27	249.0d
9729	BG-AP4-RID1-30	Install Conveyor - RID1-07 - RID1-10 - Ceiling Mounted - AP4	10.0d	10-Sep-27	23-Sep-27	246.0d
9730	BG-AP4-RID1-40	Install Catwalk - RID-07 - RID-10 - Ceiling Mounted - AP4	10.0d	17-Sep-27	30-Sep-27	251.0d
9731	BG-AP4-RID1-50	Conveyor Detailing - RID1-07 - RID1 - Ceiling Mounted - AP4	8.0d	24-Sep-27	5-Oct-27	249.0d
9732	BG-AP4-RID1-60	Elec. & Controls Rough-In - RID1-07 - RID1-10 - Ceiling Mounted - AP4	10.0d	6-Oct-27	19-Oct-27	249.0d
9733	BG-AP4-RID1-80	Internal Mech. Statics - RID1-07 - RID1-10 - Ceiling Mounted - AP4	2.0d	20-Oct-27	21-Oct-27	249.0d
9734	BG-AP4-RID1-90	Owner Mech. Statics - RID1-07 - RID1-10 - Ceiling Mounted - AP4	1.0d	22-Oct-27	22-Oct-27	249.0d
9735	WBS - MUD1 - Apron 4		42.0d	7-Oct-27	7-Dec-27	540.0d
9736	WBS - MDF1A-01 - MDF1A-09 - Make-Up Feed - Apron 4		36.0d	7-Oct-27	29-Nov-27	225.0d
9737	WBS - MDF1A-01 - MDF1A-08 - Make-Up Feed - Ceiling Mounted - Apron 4		36.0d	7-Oct-27	29-Nov-27	225.0d
9738	BG-AP4-MDF1A-30	Conveyor Layout & Install - MDF1A-01 - MDF1A-08 - Ceiling Mounted - AP4	10.0d	7-Oct-27	20-Oct-27	171.0d
9739	BG-AP4-MDF1A-40	Install Catwalk - MDF1A-01 - MDF1A-09 - Ceiling Mounted - AP4	8.0d	14-Oct-27	25-Oct-27	233.0d
9740	BG-AP4-MDF1A-50	Conveyor Detailing - MDF1A-01 - MDF1A-08 - Ceiling Mounted - AP4	4.0d	8-Nov-27	11-Nov-27	220.0d
9741	BG-AP4-MDF1A-60	Elec. & Controls Rough-In - MDF1A-01 - MDF1A-08 - Ceiling Mounted - AP4	8.0d	12-Nov-27	23-Nov-27	220.0d
9742	BG-AP4-MDF1A-70	Internal Mech. Statics - MDF1A-01 - MDF1A-08 - Ceiling Mounted - AP4	1.0d	24-Nov-27	24-Nov-27	225.0d
9743	BG-AP4-MDF1A-80	Owner Mech. Statics - MDF1A-01 - MDF1A-08 - Ceiling Mounted - AP4	1.0d	29-Nov-27	29-Nov-27	225.0d
9744	WBS - MDF1A-09 - Make-Up Feed - Floor Mount - Apron 4		20.0d	21-Oct-27	17-Nov-27	231.0d

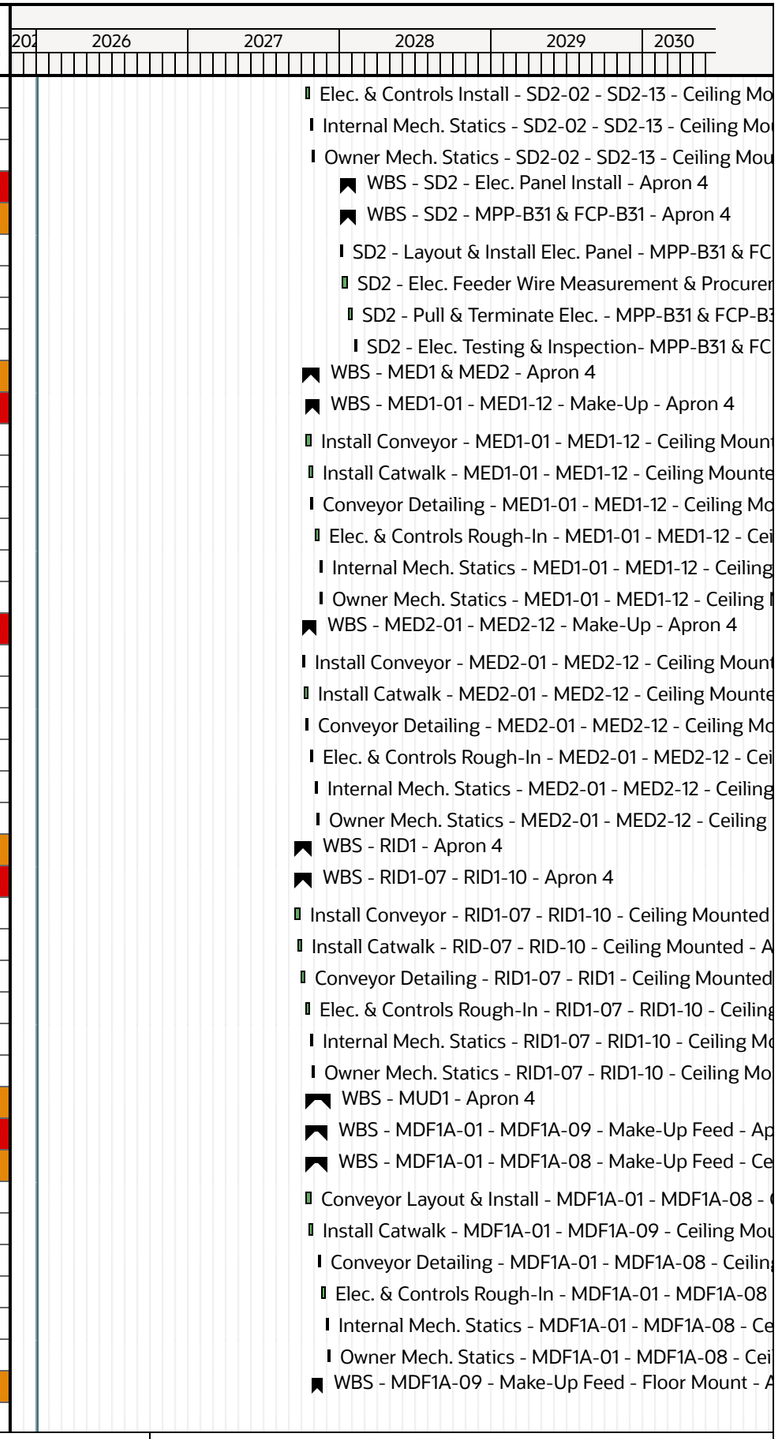


	ID	Name	Dur	Start	Finish	TF
9745	BG-AP4-MDF1A-100	Layout & Install Conveyor - MDF1A-09 - Floor Mounted - AP4	2.0d	21-Oct-27	22-Oct-27	171.0d
9746	BG-AP4-MDF1A-110	Conveyor Detailing - MDF1A-09 - Floor Mounted - AP4	2.0d	8-Nov-27	9-Nov-27	171.0d
9747	BG-AP4-MDF1A-120	Install Decking & Shrouding - MDF1A-09 - Floor Mounted - AP4	2.0d	10-Nov-27	11-Nov-27	231.0d
9748	BG-AP4-MDF1A-130	Elec. & Controls Rough-In - MDF1A-09 - Floor Mounted - AP4	2.0d	12-Nov-27	15-Nov-27	231.0d
9749	BG-AP4-MDF1A-140	Internal Mech. Statics - MDF1A-09 - Floor Mounted - AP4	1.0d	16-Nov-27	16-Nov-27	231.0d
9750	BG-AP4-MDF1A-150	Owner Mech. Statics - MDF1A-09 - Floor Mounted - AP4	1.0d	17-Nov-27	17-Nov-27	231.0d
9751	WBS - MDF1B-01 - MDF1B-05 - Make-Up Feed - Ceiling Mounted - Apron 4		31.0d	21-Oct-27	6-Dec-27	220.0d
9752	WBS - MDF1B-01 - MDF1B-04 - Make-Up Feed - Ceiling Mounted - Apron 4		31.0d	21-Oct-27	6-Dec-27	220.0d
9753	BG-AP4-MDF1B-30	Conveyor Layout & Install - MDF1B-01 - MDF1B-04 - Ceiling Mounted - AP4	6.0d	21-Oct-27	28-Oct-27	235.0d
9754	BG-AP4-MDF1B-40	Install Catwalk - MDF1B-01 - MDF1B-04 - Ceiling Mounted - AP4	5.0d	26-Oct-27	1-Nov-27	236.0d
9755	BG-AP4-MDF1B-50	Conveyor Detailing - MDF1B-01 - MDF1B-04 - Ceiling Mounted - AP4	3.0d	12-Nov-27	16-Nov-27	225.0d
9756	BG-AP4-MDF1B-60	Elec. & Controls Rough-In - MDF1B-01 - MDF1B-04 - Ceiling Mounted - AP4	5.0d	24-Nov-27	2-Dec-27	220.0d
9757	BG-AP4-MDF1B-70	Internal Mechancial Statics - MFD1B-01 - MDF1B-04 - Ceiling Mounted - AP4	1.0d	3-Dec-27	3-Dec-27	220.0d
9758	BG-AP4-MDF1B-80	Owner Mech. Statics - MFD1B-01 - MDF1B-04 - Ceiling Mounted - AP4	1.0d	6-Dec-27	6-Dec-27	220.0d
9759	WBS - MDF1B-05 - Make-Up Feed - Floor Mounted - Apron 4		10.0d	8-Nov-27	19-Nov-27	229.0d
9760	BG-AP4-MDF1B-100	Conveyor Layout & Install - MDF1B-05 - Floor Mounted - AP4	2.0d	8-Nov-27	9-Nov-27	229.0d
9761	BG-AP4-MDF1B-110	Conveyor Detailing - MDF1B-05 - Floor Mounted - AP4	2.0d	10-Nov-27	11-Nov-27	229.0d
9762	BG-AP4-MDF1B-120	Elec. & Controls Rough-In - MDF1B-05 - Floor Mounted - AP4	2.0d	12-Nov-27	15-Nov-27	229.0d
9763	BG-AP4-MDF1B-130	Install Decking & Shrouding - MDF1B-05 - Floor Mounted - AP4	2.0d	16-Nov-27	17-Nov-27	229.0d
9764	BG-AP4-MDF1B-140	Internal Mech. Statics - MDF1B-05 - Floor Mounted - AP4	1.0d	18-Nov-27	18-Nov-27	229.0d
9765	BG-AP4-MDF1B-150	Owner Mech. Statics - MDF1B-05 - Floor Mounted - AP4	1.0d	19-Nov-27	19-Nov-27	229.0d
9766	WBS - MUD1 - Make-Up - Floor Mounted - Apron 4		30.0d	25-Oct-27	7-Dec-27	219.0d
9767	BG-AP4-MUD1-10	Conveyor Layout & Install - MUD1 - Floor Mounted - AP4	10.0d	25-Oct-27	5-Nov-27	171.0d
9768	BG-AP4-MUD1-20	Impact Protection & Cross-Overs - Install - MUD1 - Floor Mounted - AP4	5.0d	10-Nov-27	16-Nov-27	171.0d
9769	BG-AP4-MUD1-30	Conveyor Detailing/Shrouding - MUD1 - Floor Mounted - AP4	9.0d	10-Nov-27	22-Nov-27	171.0d
9770	BG-AP4-MUD1-40	Elec. & Controls Rough-In - MUD1 - Floor Mounted - AP4	7.0d	23-Nov-27	3-Dec-27	219.0d
9771	BG-AP4-MUD1-50	Internal Mech. Statics - MUD1 - Floor Mounted - AP4	1.0d	6-Dec-27	6-Dec-27	219.0d
9772	BG-AP4-MUD1-60	Owner Mech. Statics - MUD1 - Floor Mounted - AP4	1.0d	7-Dec-27	7-Dec-27	219.0d
9773	WBS - MUD1 - Elec. Panel Install - MPP-A35 & FCP-A35 - Apron 4		22.0d	29-Oct-27	1-Dec-27	544.0d
9774	WBS - MUD1 - MPP-A35 & FCP-A35 - Apron 4		22.0d	29-Oct-27	1-Dec-27	544.0d
9775	BG-AP4-MUD1-MPP-20	MUD1 - Layout & Install Elec. Panel MPP-A35 & FCP-A35 - AP4	2.0d	29-Oct-27	1-Nov-27	541.0d
9776	BG-AP4-MUD1-MPP-30	MUD1 - Elec. Feeder Wire Measurement & Procurement - MPP-A35 & FCP-A35...	10.0d	2-Nov-27	15-Nov-27	543.0d
9777	BG-AP4-MUD1-MPP-40	MUD1 - Pull & Terminate Elec. - MPP-A35 & FCP-A35 - AP4	5.0d	16-Nov-27	22-Nov-27	543.0d
9778	BG-AP4-MUD1-MPP-50	MUD1 - Elec. Testing & Inspection- MPP-A35 & FCP-A35 - AP4	5.0d	23-Nov-27	1-Dec-27	543.0d
9779	WBS - MUD2 - Apron 4		56.0d	21-Oct-27	12-Jan-28	516.0d
9780	WBS - MDF2A - Make-Up Feed - Apron 4		43.0d	21-Oct-27	22-Dec-27	208.0d
9781	WBS - MDF2A-01 - MDF2A-04 - Make-Up Feed - Ceiling Mounted - Apron 4		13.0d	21-Oct-27	8-Nov-27	238.0d
9782	BG-AP4-MDF2A-30	Install Conveyor - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	3.0d	21-Oct-27	25-Oct-27	183.0d
9783	BG-AP4-MDF2A-40	Install Catwalk - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	5.0d	26-Oct-27	1-Nov-27	183.0d
9784	BG-AP4-MDF2A-50	Conveyor Detailing - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	3.0d	28-Oct-27	1-Nov-27	183.0d
9785	BG-AP4-MDF2A-60	Elec. & Controls Rough-in - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	3.0d	2-Nov-27	4-Nov-27	235.0d
9786	BG-AP4-MDF2A-70	Internal Mech. Statics - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	1.0d	5-Nov-27	5-Nov-27	238.0d

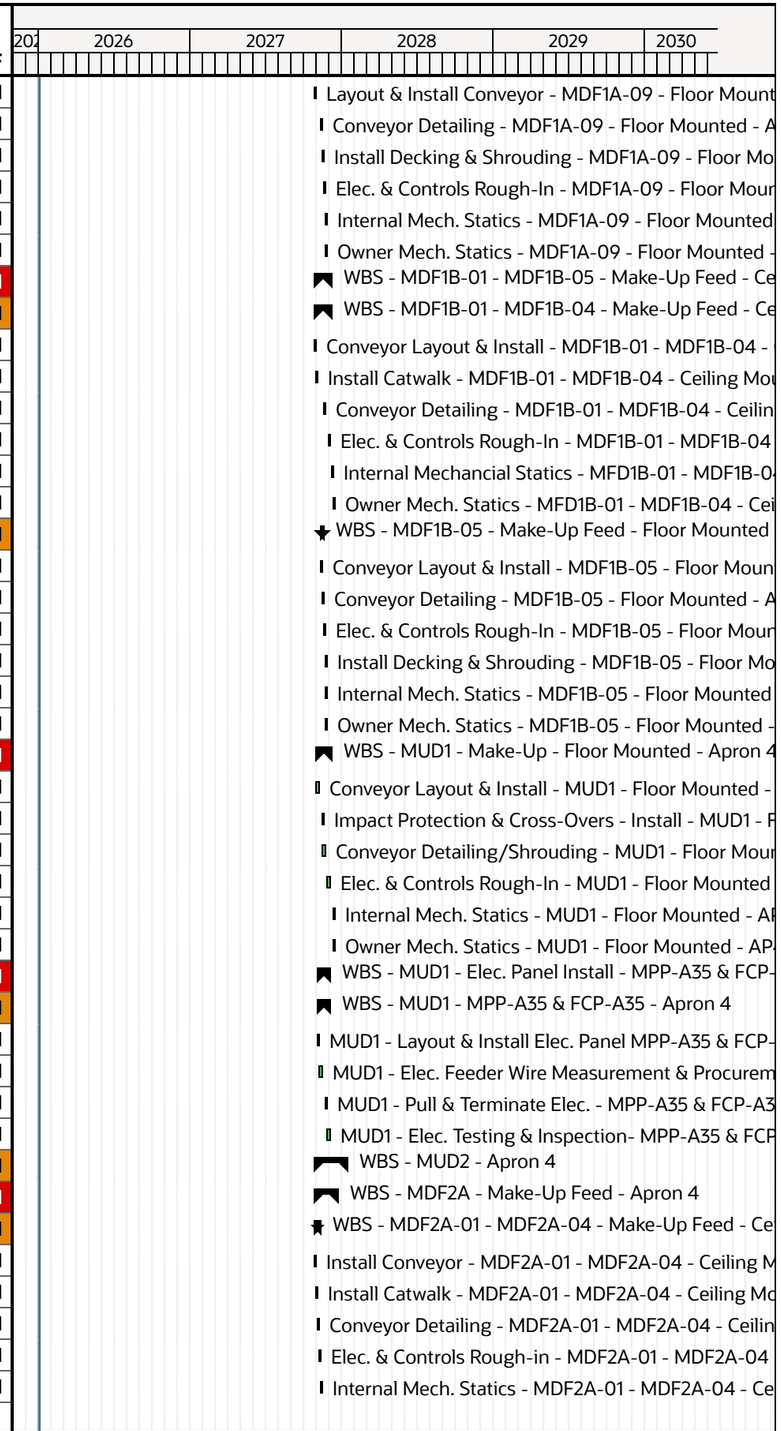


	ID	Name	Dur	Start	Finish	TF
9787	BG-AP4-MDF2A-80	Owner Mech. Statics - MDF2A-01 - MDF2A-04 - Ceiling Mounted - AP4	1.0d	8-Nov-27	8-Nov-27	238.0d
9788	WBS - MDF2A-05 - Make-Up Feed - Floor Mounted - Apron 4		10.0d	9-Dec-27	22-Dec-27	208.0d
9789	BG-AP4-MDF2A-100	Conveyor Layout & Install - MDF2A-05 - Floor Mounted - AP4	2.0d	9-Dec-27	10-Dec-27	208.0d
9790	BG-AP4-MDF2A-110	Conveyor Detailing - MDF2A-05 - Floor Mounted - AP4	2.0d	13-Dec-27	14-Dec-27	208.0d
9791	BG-AP4-MDF2A-120	Elec. & Controls Rough-In - MDF2A-05 - Floor Mounted - AP4	2.0d	15-Dec-27	16-Dec-27	208.0d
9792	BG-AP4-MDF2A-130	Install Decking & Shrouding - MDF2A-05 - Floor Mounted - AP4	2.0d	17-Dec-27	20-Dec-27	208.0d
9793	BG-AP4-MDF2A-140	Internal Mech. Statics - MDF2A-05 - Floor Mounted - AP4	1.0d	21-Dec-27	21-Dec-27	208.0d
9794	BG-AP4-MDF2A-150	Owner Mech. Statics - MDF2A-05 - Floor Mounted - AP4	1.0d	22-Dec-27	22-Dec-27	208.0d
9795	WBS - MDF2B- Make-Up Feed - Apron 4		40.0d	26-Oct-27	22-Dec-27	208.0d
9796	WBS - MDF2B-01 - MDF2B-04 - Make-Up Feed - Ceiling Mounted - Apron 4		13.0d	26-Oct-27	11-Nov-27	235.0d
9797	BG-AP4-MDF2B-30	Conveyor Layout & Install - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	3.0d	26-Oct-27	28-Oct-27	183.0d
9798	BG-AP4-MDF2B-40	Install Catwalk - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	5.0d	29-Oct-27	4-Nov-27	183.0d
9799	BG-AP4-MDF2B-50	Conveyor Detailing - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	3.0d	2-Nov-27	4-Nov-27	183.0d
9800	BG-AP4-MDF2B-60	Elec. & Controls Rough-in - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	3.0d	5-Nov-27	9-Nov-27	235.0d
9801	BG-AP4-MDF2B-70	Internal Mech. Statics - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	1.0d	10-Nov-27	10-Nov-27	235.0d
9802	BG-AP4-MDF2B-80	Owner Mech. Statics - MDF2B-01 - MDF2B-04 - Ceiling Mounted - AP4	1.0d	11-Nov-27	11-Nov-27	235.0d
9803	WBS - MDF2B-05 - Make-Up Feed - Floor Mounted - Apron 4		10.0d	9-Dec-27	22-Dec-27	208.0d
9804	BG-AP4-MDF2B-100	Conveyor Layout & Install - MDF2B-05 - Floor Mounted - AP4	2.0d	9-Dec-27	10-Dec-27	171.0d
9805	BG-AP4-MDF2B-110	Conveyor Detailing - MDF2B-05 - Floor Mounted - AP4	2.0d	13-Dec-27	14-Dec-27	208.0d
9806	BG-AP4-MDF2B-120	Elec. & Controls Rough-In - MDF2B-05 - Floor Mounted - AP4	2.0d	15-Dec-27	16-Dec-27	208.0d
9807	BG-AP4-MDF2B-130	Install Decking & Shrouding - MDF2B-05 - Floor Mounted - AP4	2.0d	17-Dec-27	20-Dec-27	208.0d
9808	BG-AP4-MDF2B-140	Internal Mech. Statics - MDF2B-05 - Floor Mounted - AP4	1.0d	21-Dec-27	21-Dec-27	208.0d
9809	BG-AP4-MDF2B-150	Owner Mech. Statics - MDF2B-05 - Floor Mounted - AP4	1.0d	22-Dec-27	22-Dec-27	208.0d
9810	WBS - MUD2 - Make-Up - Floor Mounted - Apron 4		33.0d	23-Nov-27	12-Jan-28	195.0d
9811	BG-AP4-MUD2-10	Conveyor Layout & Install - MUD2 - Floor Mounted - AP4	10.0d	23-Nov-27	8-Dec-27	171.0d
9812	BG-AP4-MUD2-20	Impact Protection & Cross-Overs - Install - MUD2 - Floor Mounted - AP4	5.0d	9-Dec-27	15-Dec-27	195.0d
9813	BG-AP4-MUD2-30	Conveyor Detailing/Shrouding - MUD2 - Floor Mounted - AP4	9.0d	16-Dec-27	29-Dec-27	195.0d
9814	BG-AP4-MUD2-40	Elec. & Controls Rough-In - MUD2 - Floor Mounted - AP4	7.0d	30-Dec-27	10-Jan-28	195.0d
9815	BG-AP4-MUD2-50	Internal Mech. Statics - MUD2 - Floor Mounted - AP4	1.0d	11-Jan-28	11-Jan-28	195.0d
9816	BG-AP4-MUD2-60	Owner Mech. Statics - MUD2 - Floor Mounted - AP4	1.0d	12-Jan-28	12-Jan-28	195.0d
9817	WBS - MUD2 - Elec. Panel Install - MPP-B35 & FCP-B35 - Apron 4		22.0d	29-Oct-27	1-Dec-27	544.0d
9818	WBS - MUD2 - MPP-B35 & FCP-B35 - Apron 4		22.0d	29-Oct-27	1-Dec-27	544.0d
9819	BG-AP4-MUD2-MPP-10	MUD2 - Layout & Install Elec. Panel MPP-B35 & FCP-B35 - AP4	2.0d	29-Oct-27	1-Nov-27	541.0d
9820	BG-AP4-MUD2-MPP-20	MUD2 - Elec. Feeder Wire Measurement & Procurement - MPP-B35 & FCP-B35...	10.0d	2-Nov-27	15-Nov-27	543.0d
9821	BG-AP4-MUD2-MPP-30	MUD2 - Pull & Terminate Elec. - MPP-B35 & FCP-B35 - AP4	5.0d	16-Nov-27	22-Nov-27	543.0d
9822	BG-AP4-MUD2-MPP-40	MUD2 - Elec. Testing & Inspection- MPP-B35 & FCP-B35 - AP4	5.0d	23-Nov-27	1-Dec-27	543.0d
9823	WBS - MUD3 - Apron 4		45.0d	13-Dec-27	15-Feb-28	492.0d
9824	WBS - MDF3A - Make-Up Feed - Apron 4		44.0d	13-Dec-27	14-Feb-28	172.0d
9825	WBS - MDF3A-01 - MDF3A-04 - Make-Up Feed - Ceiling Mounted - Apron 4		14.0d	13-Dec-27	3-Jan-28	202.0d
9826	BG-AP4-MDF3A-30	Conveyor Layout & Install - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	3.0d	13-Dec-27	15-Dec-27	171.0d
9827	BG-AP4-MDF3A-40	Install Catwalk - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	5.0d	16-Dec-27	22-Dec-27	171.0d
9828	BG-AP4-MDF3A-50	Conveyor Detailing - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	3.0d	21-Dec-27	23-Dec-27	171.0d

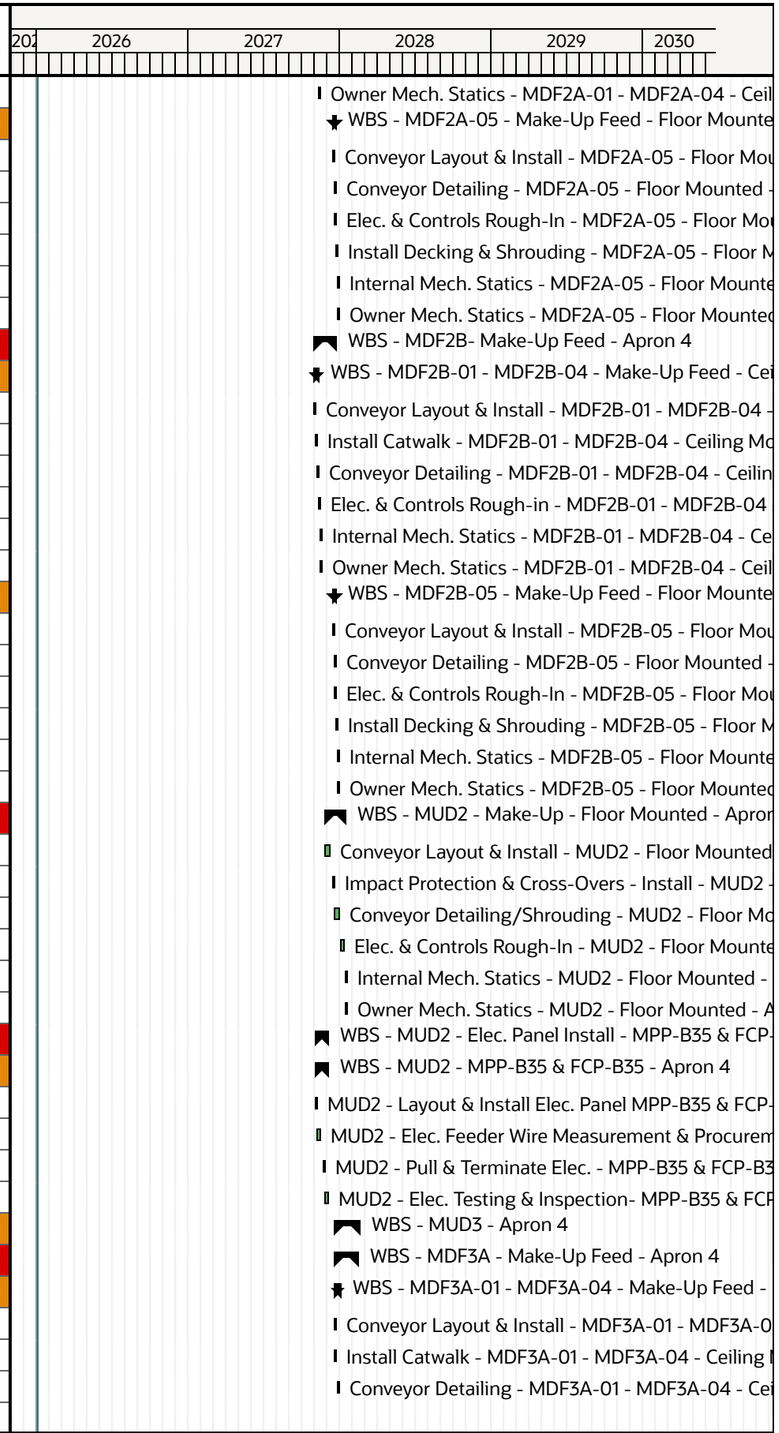


	ID	Name	Dur	Start	Finish	TF
9829	BG-AP4-MDF3A-60	Elec. & Controls Rough-in - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	3.0d	27-Dec-27	29-Dec-27	199.0d
9830	BG-AP4-MDF3A-70	Internal Mech. Statics - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	1.0d	30-Dec-27	30-Dec-27	202.0d
9831	BG-AP4-MDF3A-80	Owner Mech. Statics - MDF3A-01 - MDF3A-04 - Ceiling Mounted - AP4	1.0d	3-Jan-28	3-Jan-28	202.0d
9832	WBS - MDF3A-05 - Make-Up Feed - Floor Mounted - Apron 4		29.0d	5-Jan-28	14-Feb-28	172.0d
9833	BG-AP4-MDF3A-100	Conveyor Layout & Install - MDF3A-05 - Floor Mounted - AP4	2.0d	5-Jan-28	6-Jan-28	191.0d
9834	BG-AP4-MDF3A-110	Conveyor Detailing - MDF3A-05 - Floor Mounted - AP4	2.0d	3-Feb-28	4-Feb-28	172.0d
9835	BG-AP4-MDF3A-120	Elec. & Controls Rough-In - MDF3A-05 - Floor Mounted - AP4	2.0d	7-Feb-28	8-Feb-28	172.0d
9836	BG-AP4-MDF3A-130	Install Decking & Shrouding - MDF3A-05 - Floor Mounted - AP4	2.0d	9-Feb-28	10-Feb-28	172.0d
9837	BG-AP4-MDF3A-140	Internal Mech. Statics - MDF3A-05 - Floor Mounted - AP4	1.0d	11-Feb-28	11-Feb-28	172.0d
9838	BG-AP4-MDF3A-150	Owner Mech. Statics - MDF3A-05 - Floor Mounted - AP4	1.0d	14-Feb-28	14-Feb-28	172.0d
9839	WBS - MDF3B - Make-Up Feed - Apron 4		35.0d	27-Dec-27	14-Feb-28	172.0d
9840	WBS - MDF3B-01 - MDF3B-04 - Make-Up Feed - Ceiling Mounted - Apron 4		14.0d	27-Dec-27	14-Jan-28	193.0d
9841	BG-AP4-MDF3B-30	Conveyor Layout & Install - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	3.0d	27-Dec-27	29-Dec-27	171.0d
9842	BG-AP4-MDF3B-40	Install Catwalk - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	5.0d	30-Dec-27	6-Jan-28	193.0d
9843	BG-AP4-MDF3B-50	Conveyor Detailing - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	3.0d	5-Jan-28	7-Jan-28	193.0d
9844	BG-AP4-MDF3B-60	Elec. & Controls Rough-in - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	3.0d	10-Jan-28	12-Jan-28	193.0d
9845	BG-AP4-MDF3B-70	Internal Mech. Statics - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	1.0d	13-Jan-28	13-Jan-28	193.0d
9846	BG-AP4-MDF3B-80	Owner Mech. Statics - MDF3B-01 - MDF3B-04 - Ceiling Mounted - AP4	1.0d	14-Jan-28	14-Jan-28	193.0d
9847	WBS - MDF3B-05 - Make-Up Feed - Floor Mount - Apron 4		29.0d	5-Jan-28	14-Feb-28	172.0d
9848	BG-AP4-MDF3B-100	Conveyor Layout & Install - MDF3B-05 - Floor Mounted - AP4	2.0d	5-Jan-28	6-Jan-28	191.0d
9849	BG-AP4-MDF3B-110	Conveyor Detailing - MDF3B-05 - Floor Mounted - AP4	2.0d	3-Feb-28	4-Feb-28	172.0d
9850	BG-AP4-MDF3B-120	Elec. & Controls Rough-In - MDF3B-05 - Floor Mounted- AP4	2.0d	7-Feb-28	8-Feb-28	172.0d
9851	BG-AP4-MDF3B-130	Install Decking & Shrouding - Floor Mounted - AP4	2.0d	9-Feb-28	10-Feb-28	172.0d
9852	BG-AP4-MDF3B-140	Internal Mech. Statics - MDF3B-05 - Floor Mounted - AP4	1.0d	11-Feb-28	11-Feb-28	172.0d
9853	BG-AP4-MDF3B-150	Owner Mech. Statics - MDF3B-05 - Floor Mounted - AP4	1.0d	14-Feb-28	14-Feb-28	172.0d
9854	WBS - MUD3 - Make-Up - Apron 4		33.0d	30-Dec-27	15-Feb-28	171.0d
9855	BG-AP4-MUD3-10	Conveyor Layout & Install - MUD3 - Floor Mounted - AP4	10.0d	30-Dec-27	13-Jan-28	171.0d
9856	BG-AP4-MUD3-20	Impact Protection & Cross-Overs - Install - MUD3 - Floor Mounted - AP4	5.0d	14-Jan-28	20-Jan-28	171.0d
9857	BG-AP4-MUD3-30	Conveyor Detailing/Shrouding - MUD3 - Floor Mounted - AP4	9.0d	21-Jan-28	2-Feb-28	171.0d
9858	BG-AP4-MUD3-40	Elec. & Controls Rough-In - MUD3 - Floor Mounted - AP4	7.0d	3-Feb-28	11-Feb-28	171.0d
9859	BG-AP4-MUD3-50	Internal Mech. Statics - MUD3 - Floor Mounted - AP4	1.0d	14-Feb-28	14-Feb-28	171.0d
9860	BG-AP4-MUD3-60	Owner Mech. Statics - MUD3 - Floor Mounted - AP4	1.0d	15-Feb-28	15-Feb-28	171.0d
9861	WBS - MUD3 - Elec. Panel Install - MPP-A36 & FCP-A36 - Apron 4		22.0d	30-Dec-27	31-Jan-28	503.0d
9862	WBS - MUD3 - MPP-A36 & FCP-A36 - Apron 4		22.0d	30-Dec-27	31-Jan-28	503.0d
9863	BG-AP4-MUD3-MPP-10	MUD3 - Layout & Install Elec. Panel MPP-A36 & FCP-A36 - AP4	2.0d	30-Dec-27	3-Jan-28	502.0d
9864	BG-AP4-MUD3-MPP-20	MUD3 - Elec. Feeder Wire Measurement & Procurement - MPP-A36 & FCP-A36...	10.0d	4-Jan-28	17-Jan-28	502.0d
9865	BG-AP4-MUD3-MPP-30	MUD3 - Pull & Terminate Elec. - MPP-A36 & FCP-A36 - AP4	5.0d	18-Jan-28	24-Jan-28	502.0d
9866	BG-AP4-MUD3-MPP-40	MUD3 - Elec. Testing & Inspection- MPP-A36 & FCP-A36 - AP4	5.0d	25-Jan-28	31-Jan-28	502.0d
9867	WBS - CDD2 - Apron 4		57.0d	10-Sep-27	1-Dec-27	544.0d
9868	WBS - CFD2A - Claim Feed - Apron 4		27.0d	10-Sep-27	18-Oct-27	253.0d
9869	WBS - CFD2A-04 - CFD2A-06 - Claim Feed - Ceiling Mounted - Apron 4		18.0d	10-Sep-27	5-Oct-27	262.0d
9870	BG-AP4-CFD2A-120	Conveyer Layout & Install - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	5.0d	10-Sep-27	16-Sep-27	164.0d

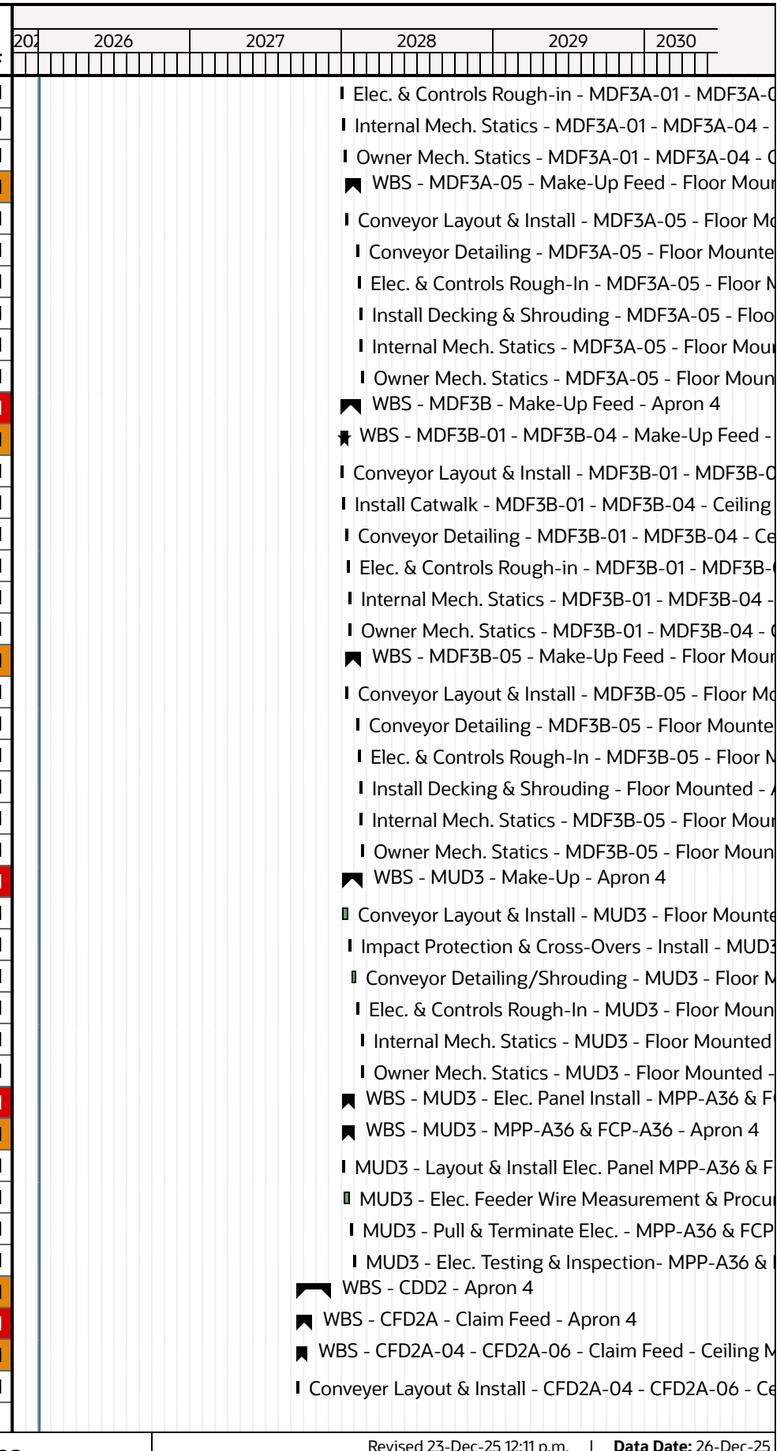


	ID	Name	Dur	Start	Finish	TF
9871	BG-AP4-CFD2A-130	Install Catwalk - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	5.0d	15-Sep-27	21-Sep-27	257.0d
9872	BG-AP4-CFD2A-140	Conveyor Detailing - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	5.0d	20-Sep-27	24-Sep-27	257.0d
9873	BG-AP4-CFD2A-150	Elec. & Controls Install - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	5.0d	27-Sep-27	1-Oct-27	257.0d
9874	BG-AP4-CFD2A-170	Internal Mech. Statics - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	1.0d	4-Oct-27	4-Oct-27	262.0d
9875	BG-AP4-CFD2A-180	Owner Mech. Statics - CFD2A-04 - CFD2A-06 - Ceiling Mounted - AP4	1.0d	5-Oct-27	5-Oct-27	262.0d
9876	WBS - CFD2A-01 - CFD2A-03 - Claim Feed - Floor Mounted - Apron 4		22.0d	17-Sep-27	18-Oct-27	253.0d
9877	BG-AP4-CFD2A-10	Conveyor Layout & Install - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	5.0d	17-Sep-27	23-Sep-27	164.0d
9878	BG-AP4-CFD2A-20	Install Impact Protection - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	5.0d	24-Sep-27	30-Sep-27	164.0d
9879	BG-AP4-CFD2A-30	Conveyor Detailing - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	5.0d	1-Oct-27	7-Oct-27	164.0d
9880	BG-AP4-CFD2A-40	Elec. & Controls Rough-In - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	5.0d	8-Oct-27	14-Oct-27	253.0d
9881	BG-AP4-CFD2A-50	Internal Mech. Statics - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	1.0d	15-Oct-27	15-Oct-27	253.0d
9882	BG-AP4-CFD2A-60	Owner Mech. Statics - CFD2A-01 - CFD2A-03 - Floor Mounted - AP4	1.0d	18-Oct-27	18-Oct-27	253.0d
9883	WBS - CFD2B - Claim Feed - Apron 4		18.0d	8-Oct-27	2-Nov-27	242.0d
9884	WBS - CFD2B-04 - CFD2B-06 - Claim Feed - Ceiling Mounted - Apron 4		18.0d	8-Oct-27	2-Nov-27	242.0d
9885	BG-AP4-CFD2B-120	Conveyor Layout & Install - CFD2B-04 - CFD2B-06 - Ceiling Mounted - AP4	5.0d	8-Oct-27	14-Oct-27	164.0d
9886	BG-AP4-CFD2B-130	Install Catwalk - CFD2B-04 - CFD2B-06 - Ceiliing Mounted - AP4	5.0d	13-Oct-27	19-Oct-27	242.0d
9887	BG-AP4-CFD2B-140	Conveyor Detailing - CFD2B-04 - CFD2B-06 - Ceiling Mounted - AP4	5.0d	18-Oct-27	22-Oct-27	242.0d
9888	BG-AP4-CFD2B-150	Elec. & Controls Rough-In - CFD2B-04 - CFD2B-06 - Ceiling Mounted - AP4	5.0d	25-Oct-27	29-Oct-27	242.0d
9889	BG-AP4-CFD2B-170	Internal Mech. Statics - CFD2B-04 - CFD2B-06 - Ceiling Mounted - AP4	1.0d	1-Nov-27	1-Nov-27	242.0d
9890	BG-AP4-CFD2B-180	Owner Mech. Statics - CFD2B-04 - CFD2B-06 - Ceiling Mounted - AP4	1.0d	2-Nov-27	2-Nov-27	242.0d
9891	WBS - CFD2B-01 - CFD2B-03 - Claim Feed - Floor Mounted - Apron 4		13.0d	8-Oct-27	26-Oct-27	247.0d
9892	BG-AP4-CFD2B-10	Conveyor Layout & Install - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	3.0d	8-Oct-27	12-Oct-27	164.0d
9893	BG-AP4-CFD2B-20	Install Impact Protection - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	3.0d	13-Oct-27	15-Oct-27	164.0d
9894	BG-AP4-CFD2B-30	Conveyor Detailing - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	2.0d	18-Oct-27	19-Oct-27	164.0d
9895	BG-AP4-CFD2B-40	Elec. & Controls Rough-In - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	3.0d	20-Oct-27	22-Oct-27	247.0d
9896	BG-AP4-CFD2B-50	Internal Mech. Statics - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	1.0d	25-Oct-27	25-Oct-27	247.0d
9897	BG-AP4-CFD2B-60	Owner Mech. Statics - CFD2B-01 - CFD2B-03 - Floor Mounted - AP4	1.0d	26-Oct-27	26-Oct-27	247.0d
9898	WBS - CCD2 - Elec. Panel Install - Apron 9		29.0d	20-Oct-27	1-Dec-27	544.0d
9899	WBS - CDD2 - MPP-B33 & FCP-B33 - Apron 9		29.0d	20-Oct-27	1-Dec-27	544.0d
9900	BG-AP4-CDD2-MPP-20	CDD2 - Layout & Install Elec. Panel MPP-B33 & FCP-B33 - AP9	2.0d	20-Oct-27	21-Oct-27	541.0d
9901	BG-AP4-CDD2-MPP-30	CCD2 - Elec. Feeder Wire Measurement & Procurement - MPP-B33 & FCP-B33 ...	10.0d	22-Oct-27	4-Nov-27	550.0d
9902	BG-AP4-CDD2-MPP-40	CDD2 - Pull & Terminate Elec. - MPP-B33 & FCP-B33 - AP9	5.0d	5-Nov-27	11-Nov-27	550.0d
9903	BG-AP4-CDD2-MPP-50	CCD2 - Elec. Testing & Inspection- MPP-B33 & FCP-B33 - AP9	5.0d	23-Nov-27	1-Dec-27	543.0d
9904	WBS - CDD3 - Apron 4		66.0d	20-Oct-27	25-Jan-28	201.0d
9905	WBS - CFD3A - Claim Feed - Apron 4		30.0d	20-Oct-27	2-Dec-27	222.0d
9906	WBS - CFD3A-04 - CFD3A-05 - Claim Feed - Ceiling Mounted - Apron 4		18.0d	20-Oct-27	12-Nov-27	234.0d
9907	BG-AP4-CFD3A-120	Conveyor Layout & Install - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	5.0d	20-Oct-27	26-Oct-27	164.0d
9908	BG-AP4-CFD3A-130	Install Catwalk - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	5.0d	25-Oct-27	29-Oct-27	164.0d
9909	BG-AP4-CFD3A-140	Conveyor Detailing - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	5.0d	28-Oct-27	3-Nov-27	234.0d
9910	BG-AP4-CFD3A-150	Elec. & Controls Rough-In - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	5.0d	4-Nov-27	10-Nov-27	234.0d
9911	BG-AP4-CFD3A-170	Internal Mech. Statics - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	1.0d	11-Nov-27	11-Nov-27	234.0d
9912	BG-AP4-CFD3A-180	Owner Mech. Statics - CFD3A-04 - CFD3A-05 - Ceiling Mounted - AP4	1.0d	12-Nov-27	12-Nov-27	234.0d

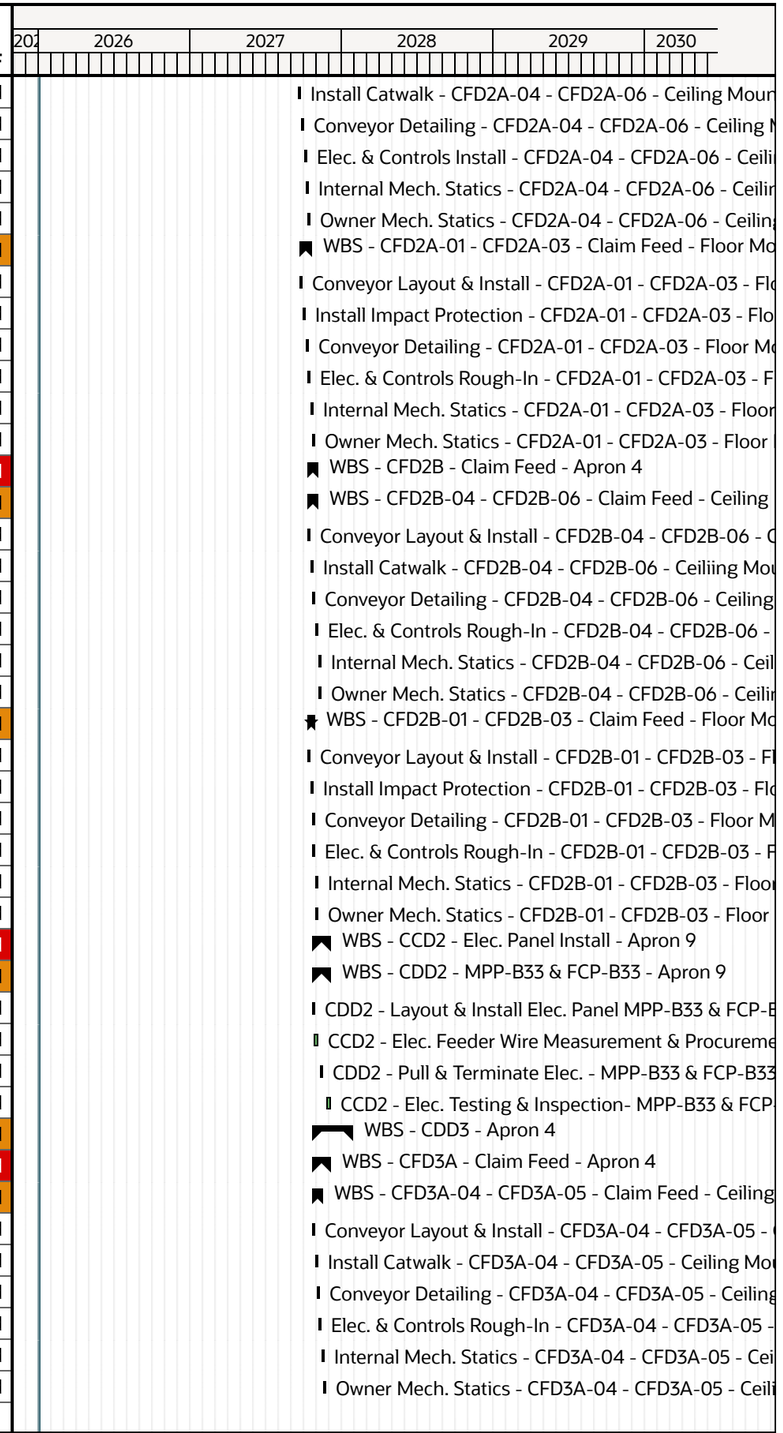

ID	Name	Dur	Start	Finish	TF
9913	WBS - CFD3A-01 - CFD3A-03 - Claim Feed - Floor Mounted - Apron 4	22.0d	1-Nov-27	2-Dec-27	222.0d
9914	BG-AP4-CFD3A-10	Conveyor Layout & Install - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	5.0d	1-Nov-27	5-Nov-27	164.0d
9915	BG-AP4-CFD3A-20	Install Impact Protection - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	5.0d	8-Nov-27	12-Nov-27	164.0d
9916	BG-AP4-CFD3A-30	Conveyor Detailing - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	5.0d	15-Nov-27	19-Nov-27	164.0d
9917	BG-AP4-CFD3A-40	Elec. & Controls Rough-In - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	5.0d	22-Nov-27	30-Nov-27	222.0d
9918	BG-AP4-CFD3A-50	Internal Mech. Statics - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	1.0d	1-Dec-27	1-Dec-27	222.0d
9919	BG-AP4-CFD3A-60	Owner Mech. Statics - CFD3A-01 - CFD3A-03 - Floor Mounted - AP4	1.0d	2-Dec-27	2-Dec-27	222.0d
9920	WBS - CFD3B - Claim Feed - Apron 4		19.0d	22-Nov-27	20-Dec-27	210.0d
9921	WBS - CFD3B-04 - CFD3B-06 - Claim Feed - Ceiling Mounted - Apron 4		19.0d	22-Nov-27	20-Dec-27	210.0d
9922	BG-AP4-CFD3B-120	Conveyor Layout & Install - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	5.0d	22-Nov-27	30-Nov-27	164.0d
9923	BG-AP4-CFD3B-130	Install Catwalk - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	5.0d	29-Nov-27	3-Dec-27	210.0d
9924	BG-AP4-CFD3B-140	Conveyor Detailing - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	5.0d	2-Dec-27	8-Dec-27	210.0d
9925	BG-AP4-CFD3B-150	Elec. & Controls Rough-In - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	5.0d	9-Dec-27	15-Dec-27	210.0d
9926	BG-AP4-CFD3B-170	Internal Mech. Statics - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	2.0d	16-Dec-27	17-Dec-27	210.0d
9927	BG-AP4-CFD3B-180	Owner Mech. Statics - CFD3B-04 - CFD3B-06 - Ceiling Mounted - AP4	1.0d	20-Dec-27	20-Dec-27	210.0d
9928	WBS - CFD3B-01 - CFD3B-03 - Claim Feed - Floor Mounted - Apron 4		13.0d	1-Dec-27	17-Dec-27	211.0d
9929	BG-AP4-CFD3B-10	Conveyor Layout & Install - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	3.0d	1-Dec-27	3-Dec-27	164.0d
9930	BG-AP4-CFD3B-20	Install Impact Protection - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	3.0d	6-Dec-27	8-Dec-27	164.0d
9931	BG-AP4-CFD3B-30	Conveyor Detailing - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	2.0d	9-Dec-27	10-Dec-27	164.0d
9932	BG-AP4-CFD3B-40	Elec. & Controls Rough-In - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	3.0d	13-Dec-27	15-Dec-27	211.0d
9933	BG-AP4-CFD3B-50	Internal Mech. Statics - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	1.0d	16-Dec-27	16-Dec-27	211.0d
9934	BG-AP4-CFD3B-60	Owner Mech. Statics - CFD3B-01 - CFD3B-03 - Floor Mounted - AP4	1.0d	17-Dec-27	17-Dec-27	211.0d
9935	WBS - CCD3- Elec. Panel Install - Apron 4		22.0d	23-Dec-27	25-Jan-28	201.0d
9936	WBS - CDD3 - MPP-A34 & FCP-A34 - Apron 4		22.0d	23-Dec-27	25-Jan-28	201.0d
9937	BG-AP4-CDD3-MPP-20	CDD3 - Layout & Install Elec. Panel MPP-A34 & FCP-A34 - AP4	2.0d	23-Dec-27	27-Dec-27	199.0d
9938	BG-AP4-CDD3-MPP-30	CCD3 - Elec. Feeder Wire Measurement & Procurement - MPP-A34 & FCP-A34 ...	10.0d	28-Dec-27	11-Jan-28	201.0d
9939	BG-AP4-CDD3-MPP-40	CDD3 - Pull & Terminate Elec. - MPP-A34 & FCP-A34 - AP4	5.0d	12-Jan-28	18-Jan-28	201.0d
9940	BG-AP4-CDD3-MPP-50	CCD3 - Elec. Testing & Inspection- MPP-A34 & FCP-A34 - AP4	5.0d	19-Jan-28	25-Jan-28	201.0d
9941	WBS - CDD4 - Apron 4		52.0d	13-Dec-27	24-Feb-28	179.0d
9942	WBS - CFD4A - Claim Feed - Apron 4		31.0d	13-Dec-27	26-Jan-28	185.0d
9943	WBS - CFD4A-04 - CFD4A-05 - Claim Feed - Ceiling Mounted - Apron 4		18.0d	13-Dec-27	7-Jan-28	198.0d
9944	BG-AP4-CFD4A-120	Conveyor Layout & Install - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	5.0d	13-Dec-27	17-Dec-27	164.0d
9945	BG-AP4-CFD4A-130	Install Catwalk - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	5.0d	16-Dec-27	22-Dec-27	164.0d
9946	BG-AP4-CFD4A-140	Conveyor Detailing - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	5.0d	21-Dec-27	28-Dec-27	164.0d
9947	BG-AP4-CFD4A-150	Elec. & Controls Rough-In - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	5.0d	29-Dec-27	5-Jan-28	198.0d
9948	BG-AP4-CFD4A-160	Internal Mech. Statics - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	1.0d	6-Jan-28	6-Jan-28	198.0d
9949	BG-AP4-CFD4A-170	Owner Mech. Statics - CFD4A-04 -CFD4A-05 - Ceiling Mounted - AP4	1.0d	7-Jan-28	7-Jan-28	198.0d
9950	WBS - CFD4A-01 - CFD4A-03 - Claim Feed - Floor Mounted - Apron 4		22.0d	27-Dec-27	26-Jan-28	185.0d
9951	BG-AP4-CFD4A-10	Conveyor Layout & Install - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	5.0d	27-Dec-27	3-Jan-28	164.0d
9952	BG-AP4-CFD4A-20	Install Impact Protection - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	5.0d	4-Jan-28	10-Jan-28	164.0d
9953	BG-AP4-CFD4A-30	Conveyor Detailing - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	5.0d	11-Jan-28	17-Jan-28	164.0d
9954	BG-AP4-CFD4A-40	Elec. & Controls Rough-In - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	5.0d	18-Jan-28	24-Jan-28	185.0d

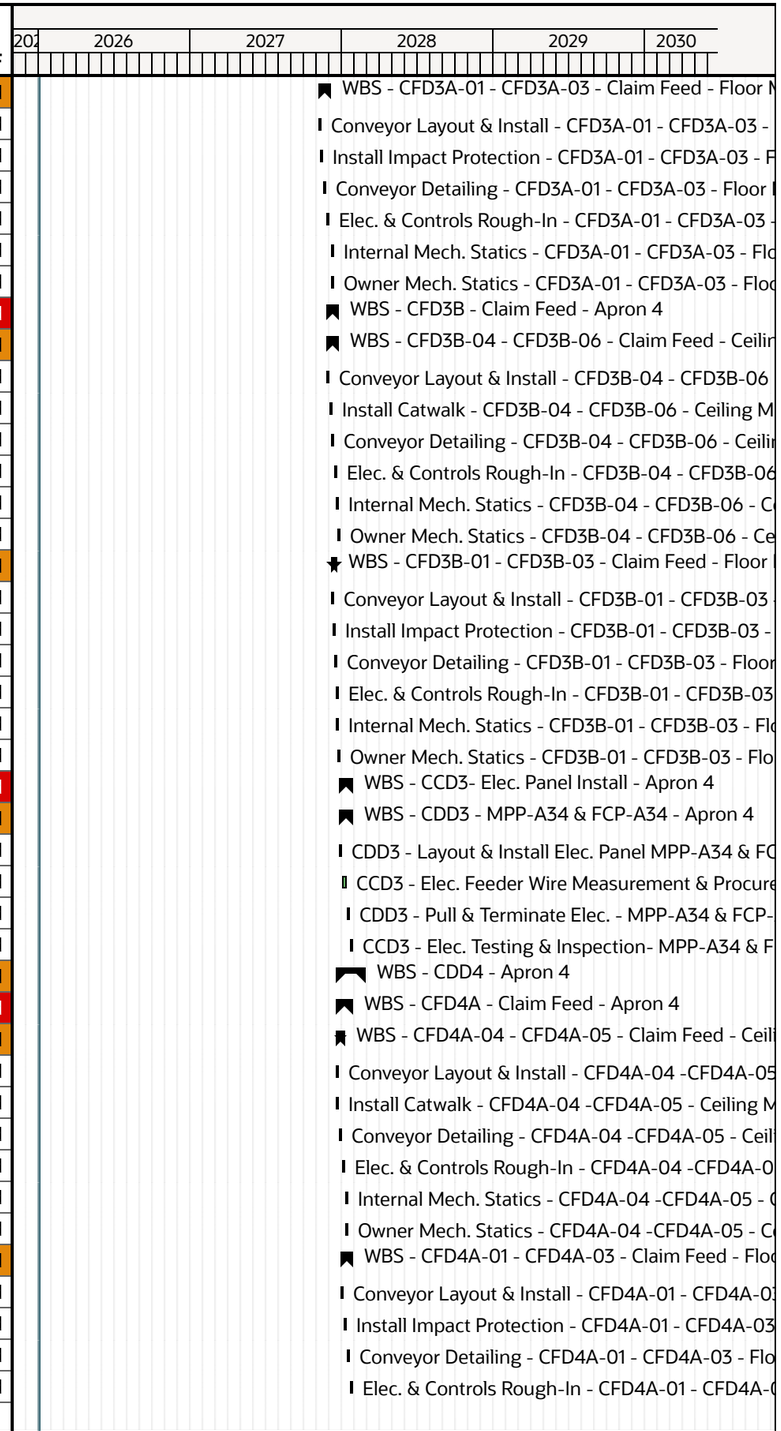


	ID	Name	Dur	Start	Finish	TF
9955	BG-AP4-CFD4A-50	Internal Mech. Statics - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	1.0d	25-Jan-28	25-Jan-28	185.0d
9956	BG-AP4-CFD4A-60	Owner Mech. Statics - CFD4A-01 - CFD4A-03 - Floor Mounted - AP4	1.0d	26-Jan-28	26-Jan-28	185.0d
9957	WBS - CFD4B - Claim Feed - Apron 4		28.0d	18-Jan-28	24-Feb-28	164.0d
9958	WBS - CFD4B-04 - CFD4B-05 - Claim Feed - Ceiling Mounted - Apron 4		22.0d	18-Jan-28	16-Feb-28	170.0d
9959	BG-AP4-CFD4B-120	Conveyor Layout & Install - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	5.0d	18-Jan-28	24-Jan-28	164.0d
9960	BG-AP4-CFD4B-130	Install Catwalk - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	5.0d	25-Jan-28	31-Jan-28	164.0d
9961	BG-AP4-CFD4B-140	Conveyor Detailing - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	5.0d	1-Feb-28	7-Feb-28	164.0d
9962	BG-AP4-CFD4B-150	Elec. & Controls Rough-In - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	5.0d	8-Feb-28	14-Feb-28	170.0d
9963	BG-AP4-CFD4B-160	Internal Mech. Statics - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	1.0d	15-Feb-28	15-Feb-28	170.0d
9964	BG-AP4-CFD4B-170	Owner Mech. Statics - CFD4B-04 - CFD4B-05 - Ceiling Mounted - AP4	1.0d	16-Feb-28	16-Feb-28	170.0d
9965	WBS - CFD4B-01 - CFD4B-03 - Claim Feed - Floor Mounted - Apron 4		13.0d	8-Feb-28	24-Feb-28	164.0d
9966	BG-AP4-CFD4B-10	Conveyor Layout & Install - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	3.0d	8-Feb-28	10-Feb-28	164.0d
9967	BG-AP4-CFD4B-20	Install Impact Protection - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	3.0d	11-Feb-28	15-Feb-28	164.0d
9968	BG-AP4-CFD4B-30	Conveyor Detailing - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	2.0d	16-Feb-28	17-Feb-28	164.0d
9969	BG-AP4-CFD4B-40	Elec. & Controls Rough-In - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	3.0d	18-Feb-28	22-Feb-28	164.0d
9970	BG-AP4-CFD4B-50	Internal Mech. Statics - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	1.0d	23-Feb-28	23-Feb-28	164.0d
9971	BG-AP4-CFD4B-60	Owner Mech. Statics - CFD4B-01 - CFD4B-03 - Floor Mounted - AP4	1.0d	24-Feb-28	24-Feb-28	164.0d
9972	WBS - CCD4 - Elec. Panel Install - Apron 4		22.0d	28-Dec-27	27-Jan-28	199.0d
9973	WBS - CDD4 - MPP-B34 & FCP-B34 - Apron 4		22.0d	28-Dec-27	27-Jan-28	199.0d
9974	BG-AP4-CDD4-MPP-20	CDD4 - Layout & Install Elec. Panel MPP-B34 & FCP-B34 - AP4	2.0d	28-Dec-27	29-Dec-27	199.0d
9975	BG-AP4-CDD4-MPP-30	CCD4 - Elec. Feeder Wire Measurement & Procurement - MPP-B34 & FCP-B34 ...	10.0d	30-Dec-27	13-Jan-28	199.0d
9976	BG-AP4-CDD4-MPP-40	CDD4 - Pull & Terminate Elec. - MPP-B34 & FCP-B34 - AP4	5.0d	14-Jan-28	20-Jan-28	199.0d
9977	BG-AP4-CDD4-MPP-50	CCD4 - Elec. Testing & Inspection- MPP-B34 & FCP-B34 - AP4	5.0d	21-Jan-28	27-Jan-28	199.0d
9978	WBS - OSD1 - Apron 4		27.0d	10-Sep-27	18-Oct-27	253.0d
9979	WBS - OSD1-01 - Conveyor - Apron 4		27.0d	10-Sep-27	18-Oct-27	253.0d
9980	BG-AP4-OSD1-10	Conveyor Layout & Install - OSD1-01 - Conveyor - AP4	6.0d	10-Sep-27	17-Sep-27	248.0d
9981	BG-AP4-OSD1-20	Install Impact Protection - OSD1-01 - Conveyor - AP4	3.0d	20-Sep-27	22-Sep-27	249.0d
9982	BG-AP4-OSD1-30	Conveyor Detailing - OSD1-01 - Conveyor - AP4	3.0d	23-Sep-27	27-Sep-27	249.0d
9983	BG-AP4-OSD1-40	Install OSD1-02/FSD - Conveyor - AP4	2.0d	28-Sep-27	29-Sep-27	249.0d
9984	BG-AP4-OSD1-50	Elec. & Controls Rough-In - OSD1-01 - Conveyor - AP4	5.0d	30-Sep-27	6-Oct-27	249.0d
9985	BG-AP4-OSD1-60	Install Shrouding - OSD1-01 - Conveyor - AP4	5.0d	7-Oct-27	13-Oct-27	253.0d
9986	BG-AP4-OSD1-70	Install Security Door & Draft Curtains - OSD1 - AP4	1.0d	14-Oct-27	14-Oct-27	253.0d
9987	BG-AP4-OSD1-80	Internal Mech. Statics - OSD1-01 - Conveyor - AP4	1.0d	15-Oct-27	15-Oct-27	253.0d
9988	BG-AP4-OSD1-90	Owner Mech. Statics - OSD1-01 - Conveyor - AP4	1.0d	18-Oct-27	18-Oct-27	253.0d
9989	WBS - IRD1 - Apron 4		24.0d	20-Sep-27	21-Oct-27	250.0d
9990	WBS - IRD1-06 - Conveyor- Apron 4		24.0d	20-Sep-27	21-Oct-27	250.0d
9991	BG-AP4-IRD1-10	Conveyor Layout & Install - IRD1-06 - Conveyor - AP4	3.0d	20-Sep-27	22-Sep-27	250.0d
9992	BG-AP4-IRD1-20	Install Impact Protection - IRD1-06 - Conveyor - AP4	3.0d	23-Sep-27	27-Sep-27	250.0d
9993	BG-AP4-IRD1-30	Conveyor Detailing - IRD1-06 - Conveyor - AP4	3.0d	28-Sep-27	30-Sep-27	250.0d
9994	BG-AP4-IRD1-40	Install IRD1-02/FSD - Conveyor - AP4	2.0d	1-Oct-27	4-Oct-27	250.0d
9995	BG-AP4-IRD1-50	Elec. & Controls Rough-In - IRD1-06 - Conveyor - AP4	5.0d	5-Oct-27	11-Oct-27	250.0d
9996	BG-AP4-IRD1-60	Install Shrouding - IRD1-06 - Conveyor - AP4	5.0d	12-Oct-27	18-Oct-27	250.0d

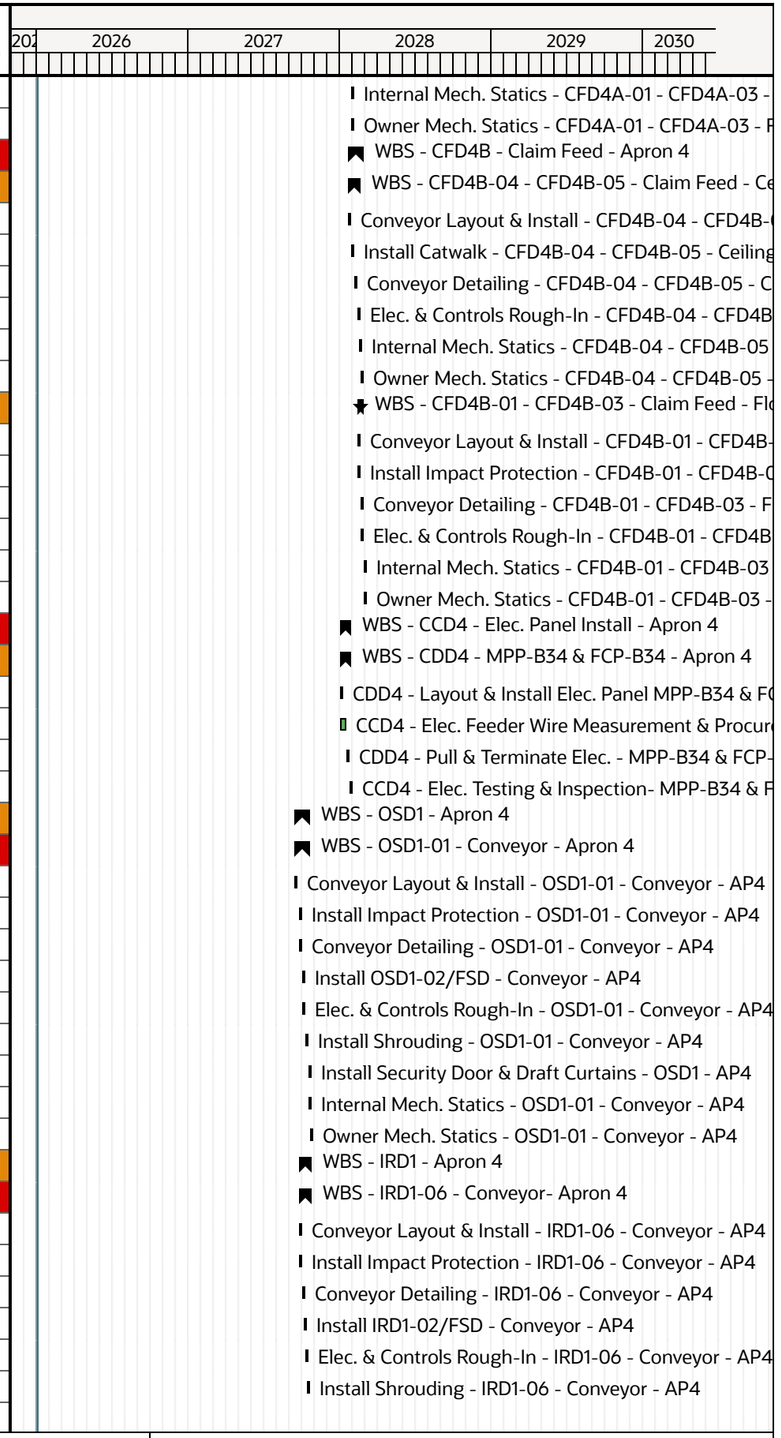


ID	Name	Dur	Start	Finish	TF
9997	BG-AP4-IRD1-70	Install Security Door & Draft Curtains - IRD1 - AP4	1.0d	19-Oct-27	19-Oct-27	250.0d
9998	BG-AP4-IRD1-80	Internal Mech. Statics - IRD1-06 - Conveyor - AP4	1.0d	20-Oct-27	20-Oct-27	250.0d
9999	BG-AP4-IRD1-90	Owner Mech. Statics - IRD1-06 - Conveyor - AP4	1.0d	21-Oct-27	21-Oct-27	250.0d
10000	WBS - ASD - Baggage Handling Systems - (BHS) - Sector E - Apron 5		352.0d	20-Apr-27	6-Sep-28	28.0d
10001	WBS - ASD - BHS - Steel Erection - Apron 5		35.0d	20-Apr-27	8-Jun-27	225.0d
10002	BG-AP5-BS-10	Layout & Install Hangers & Steel - AP5	30.0d	20-Apr-27	1-Jun-27	49.0d
10003	BG-AP5-BS-20	Header Steel Inspection - AP5	5.0d	2-Jun-27	8-Jun-27	225.0d
10004	WBS - CDD2 - Apron 5		282.0d	16-Jun-27	25-Jul-28	58.0d
10005	WBS - CFD2A - Claim Feed - Apron 5		30.0d	16-Jun-27	28-Jul-27	310.0d
10006	WBS - CFD2A-06 - CFD2A-07 - Claim Feed - Ceiling Mounted - Apron 5		26.0d	16-Jun-27	22-Jul-27	314.0d
10007	BG-AP5-CFD2A-30	Install Conveyor & Supports - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	5.0d	16-Jun-27	22-Jun-27	220.0d
10008	BG-AP5-CFD2A-40	Install Catwalk - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	5.0d	23-Jun-27	29-Jun-27	220.0d
10009	BG-AP5-CFD2A-50	Conveyor Detailing - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	5.0d	30-Jun-27	7-Jul-27	220.0d
10010	BG-AP5-CFD2A-60	Install CFD2A-07/FSD - Ceiling Mounted - AP5	2.0d	8-Jul-27	9-Jul-27	289.0d
10011	BG-AP5-CFD2A-70	Elec. & Controls Rough-In - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	4.0d	12-Jul-27	15-Jul-27	289.0d
10012	BG-AP5-CFD2A-80	Internal Mech. Statics - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	2.0d	16-Jul-27	19-Jul-27	314.0d
10013	BG-AP5-CFD2A-90	Owner Mech. Statics - CFD2A-06 - CFD2A-07 - Ceiling Mounted - AP5	1.0d	22-Jul-27	22-Jul-27	314.0d
10014	WBS - CFD2A-08 & CFD2A-09 - Claim Feed - Floor Mounted - Apron 5		25.0d	23-Jun-27	28-Jul-27	310.0d
10015	BG-AP5-CFD2A-110	Layout & Install Conveyor - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	5.0d	23-Jun-27	29-Jun-27	270.0d
10016	BG-AP5-CFD2A-120	Conveyor Detailing - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	5.0d	30-Jun-27	7-Jul-27	310.0d
10017	BG-AP5-CFD2A-130	Elec. & Controls Rough-In - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	7.0d	8-Jul-27	16-Jul-27	310.0d
10018	BG-AP5-CFD2A-140	Install Decking & Shrouding - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	5.0d	19-Jul-27	23-Jul-27	310.0d
10019	BG-AP5-CFD2A-150	Internal Mech. Statics - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	2.0d	26-Jul-27	27-Jul-27	310.0d
10020	BG-AP5-CFD2A-160	Owner Mech. Statics - CFD2A-08 & CFD2A-09 - Floor Mounted - AP5	1.0d	28-Jul-27	28-Jul-27	310.0d
10021	WBS - CFD2B - Claim Feed - Apron 5		45.0d	8-Jul-27	9-Sep-27	280.0d
10022	WBS - CFD2B-06 - CFD2B-12 - Claim Feed - Ceiling Mounted - Apron 5		33.0d	8-Jul-27	23-Aug-27	292.0d
10023	BG-AP5-CFD2B-30	Install Conveyor & Supports - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	10.0d	8-Jul-27	21-Jul-27	220.0d
10024	BG-AP5-CFD2B-40	Install Catwalk - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	10.0d	22-Jul-27	4-Aug-27	270.0d
10025	BG-AP5-CFD2B-50	Conveyor Detailing - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	5.0d	5-Aug-27	11-Aug-27	270.0d
10026	BG-AP5-CFD2B-60	Elec. & Controls Rough-in - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	5.0d	12-Aug-27	18-Aug-27	270.0d
10027	BG-AP5-CFD2B-70	Internal Mech. Statics - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	2.0d	19-Aug-27	20-Aug-27	292.0d
10028	BG-AP5-CFD2B-80	Owner Mech. Statics - CFD2B-06 - CFD2B-12 - Ceiling Mounted - AP5	1.0d	23-Aug-27	23-Aug-27	292.0d
10029	WBS - CFD2B-13 & CFD2B-14 - Claim Feed - Floor Mounted - Apron 5		35.0d	22-Jul-27	9-Sep-27	280.0d
10030	BG-AP5-CFD2B-100	Layout & Install Conveyor - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	10.0d	22-Jul-27	4-Aug-27	245.0d
10031	BG-AP5-CFD2B-110	Conveyor Detailing - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	5.0d	5-Aug-27	11-Aug-27	280.0d
10032	BG-AP5-CFD2B-120	Elec. & Controls Rough-In - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	7.0d	12-Aug-27	20-Aug-27	280.0d
10033	BG-AP5-CFD2B-130	Install Decking & Shrouding - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	10.0d	23-Aug-27	3-Sep-27	280.0d
10034	BG-AP5-CFD2B-140	Internal Mech. Statics - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	2.0d	7-Sep-27	8-Sep-27	280.0d
10035	BG-AP5-CFD2B-150	Owner Mech. Statics - CFD2B-13 & CFD2B-14 - Floor Mounted - AP5	1.0d	9-Sep-27	9-Sep-27	280.0d
10036	WBS - CDD2 - Claim Device - Apron 5		30.0d	13-Jun-28	25-Jul-28	58.0d
10037	BG-AP5-CDD2-10	Layout & Install Conveyor - CDD2 - Floor Mounted - AP5	10.0d	13-Jun-28	26-Jun-28	28.0d
10038	BG-AP5-CDD2-20	Conveyor Detailing - CDD2 - Floor Mounted - AP5	5.0d	20-Jun-28	26-Jun-28	58.0d




	ID	Name	Dur	Start	Finish	TF
10039	BG-AP5-CDD2-30	Elec. & Controls Rough-In - CDD2 - Floor Mounted - AP5	7.0d	27-Jun-28	6-Jul-28	58.0d
10040	BG-AP5-CDD2-40	Install Decking & Shrouding - CDD2 - Floor Mounted - AP5	10.0d	7-Jul-28	20-Jul-28	58.0d
10041	BG-AP5-CDD2-50	Internal Mech. Statics - CDD2 - Floor Mounted - AP5	2.0d	21-Jul-28	24-Jul-28	58.0d
10042	BG-AP5-CDD2-60	Owner Mech. Statics - CDD2 - Floor Mounted - AP5	1.0d	25-Jul-28	25-Jul-28	58.0d
10043	WBS - CDD3 - Apron 5		267.0d	22-Jul-27	8-Aug-28	48.0d
10044	WBS - CFD3A - Claim Feed - Apron 5		50.0d	22-Jul-27	30-Sep-27	265.0d
10045	WBS - CFD3A-05 - CFD3A-06 - Claim Feed - Ceiling Mounted - Apron 5		25.0d	22-Jul-27	25-Aug-27	290.0d
10046	BG-AP5-CFD3A-30	Install Conveyor & Supports - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	5.0d	22-Jul-27	28-Jul-27	220.0d
10047	BG-AP5-CFD3A-40	Install Catwalk - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	5.0d	29-Jul-27	4-Aug-27	220.0d
10048	BG-AP5-CFD3A-50	Conveyor Detailing - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	5.0d	5-Aug-27	11-Aug-27	220.0d
10049	BG-AP5-CFD3A-60	Install CFD3A-06/FSD - Ceiling Mounted - AP5	2.0d	12-Aug-27	13-Aug-27	263.0d
10050	BG-AP5-CFD3A-70	Elec. & Controls Rough-In - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	5.0d	16-Aug-27	20-Aug-27	263.0d
10051	BG-AP5-CFD3A-80	Internal Mech. Statics - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	2.0d	23-Aug-27	24-Aug-27	290.0d
10052	BG-AP5-CFD3A-90	Owner Mech. Statics - CFD3A-05 - CFD3A-06 - Ceiling Mounted - AP5	1.0d	25-Aug-27	25-Aug-27	290.0d
10053	WBS - CFD3A-07 - CFD3A-08 - Floor Mounted - Apron 5		35.0d	12-Aug-27	30-Sep-27	265.0d
10054	BG-AP5-CFD3A-110	Layout & Install Conveyor - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	10.0d	12-Aug-27	25-Aug-27	235.0d
10055	BG-AP5-CFD3A-120	Conveyor Detailing - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	5.0d	26-Aug-27	1-Sep-27	235.0d
10056	BG-AP5-CFD3A-130	Elec. & Controls Rough-In - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	7.0d	2-Sep-27	13-Sep-27	265.0d
10057	BG-AP5-CFD3A-140	Install Decking & Shrouding - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	10.0d	14-Sep-27	27-Sep-27	265.0d
10058	BG-AP5-CFD3A-150	Internal Mech. Statics - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	2.0d	28-Sep-27	29-Sep-27	265.0d
10059	BG-AP5-CFD3A-160	Owner Mech. Statics - CFD3A-07 - CFD3A-08 - Floor Mounted - AP5	1.0d	30-Sep-27	30-Sep-27	265.0d
10060	WBS - CFD3B - Claim Feed - Apron 5		50.0d	12-Aug-27	21-Oct-27	250.0d
10061	WBS - CFD3B-06 - CFD3B-12 - Claim Feed - Ceiling Mounted - Apron 5		25.0d	12-Aug-27	16-Sep-27	275.0d
10062	BG-AP5-CFD3B-30	Install Conveyor & Supports - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	5.0d	12-Aug-27	18-Aug-27	220.0d
10063	BG-AP5-CFD3B-40	Install Catwalk - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	5.0d	19-Aug-27	25-Aug-27	220.0d
10064	BG-AP5-CFD3B-50	Conveyor Detailing - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	5.0d	26-Aug-27	1-Sep-27	220.0d
10065	BG-AP5-CFD3B-60	Install CFD3B-12/FSD - AP5	2.0d	2-Sep-27	3-Sep-27	253.0d
10066	BG-AP5-CFD3B-70	Elec. & Controls Rough-In - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	5.0d	7-Sep-27	13-Sep-27	253.0d
10067	BG-AP5-CFD3B-80	Internal Mech. Statics - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	2.0d	14-Sep-27	15-Sep-27	275.0d
10068	BG-AP5-CFD3B-90	Owner Mech. Statics - CFD3B-06 - CFD3B-12 - Ceiling Mounted - AP5	1.0d	16-Sep-27	16-Sep-27	275.0d
10069	WBS - CFD3B-13 & CFD3B-14 - Claim Feed - Floor Mounted - Apron 5		35.0d	2-Sep-27	21-Oct-27	250.0d
10070	BG-AP5-CFD3B-100	Layout & Install Conveyor - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	10.0d	2-Sep-27	16-Sep-27	220.0d
10071	BG-AP5-CFD3B-110	Conveyor Detailing - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	5.0d	17-Sep-27	23-Sep-27	220.0d
10072	BG-AP5-CFD3B-120	Elec. & Controls Rough-In - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	7.0d	24-Sep-27	4-Oct-27	250.0d
10073	BG-AP5-CFD3B-130	Install Decking & Shrouding - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	10.0d	5-Oct-27	18-Oct-27	250.0d
10074	BG-AP5-CFD3B-140	Internal Mech. Statics - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	2.0d	19-Oct-27	20-Oct-27	250.0d
10075	BG-AP5-CFD3B-150	Owner Mech. Statics - CFD3B-13 & CFD3B-14 - Floor Mounted - AP5	1.0d	21-Oct-27	21-Oct-27	250.0d
10076	WBS - CDD3 - Claim Device - Apron 5		30.0d	27-Jun-28	8-Aug-28	48.0d
10077	BG-AP5-CDD3-10	Layout & Install Conveyor - CDD3 - Floor Mounted - AP5	10.0d	27-Jun-28	11-Jul-28	28.0d
10078	BG-AP5-CDD3-20	Conveyor Detailing - CDD3 - Floor Mounted - AP5	5.0d	5-Jul-28	11-Jul-28	48.0d
10079	BG-AP5-CDD3-30	Elec. & Controls Rough-In - CDD3 - Floor Mounted - AP5	7.0d	12-Jul-28	20-Jul-28	48.0d
10080	BG-AP5-CDD3-40	Install Decking & Shrouding - CDD3 - Floor Mounted - AP5	10.0d	21-Jul-28	3-Aug-28	48.0d

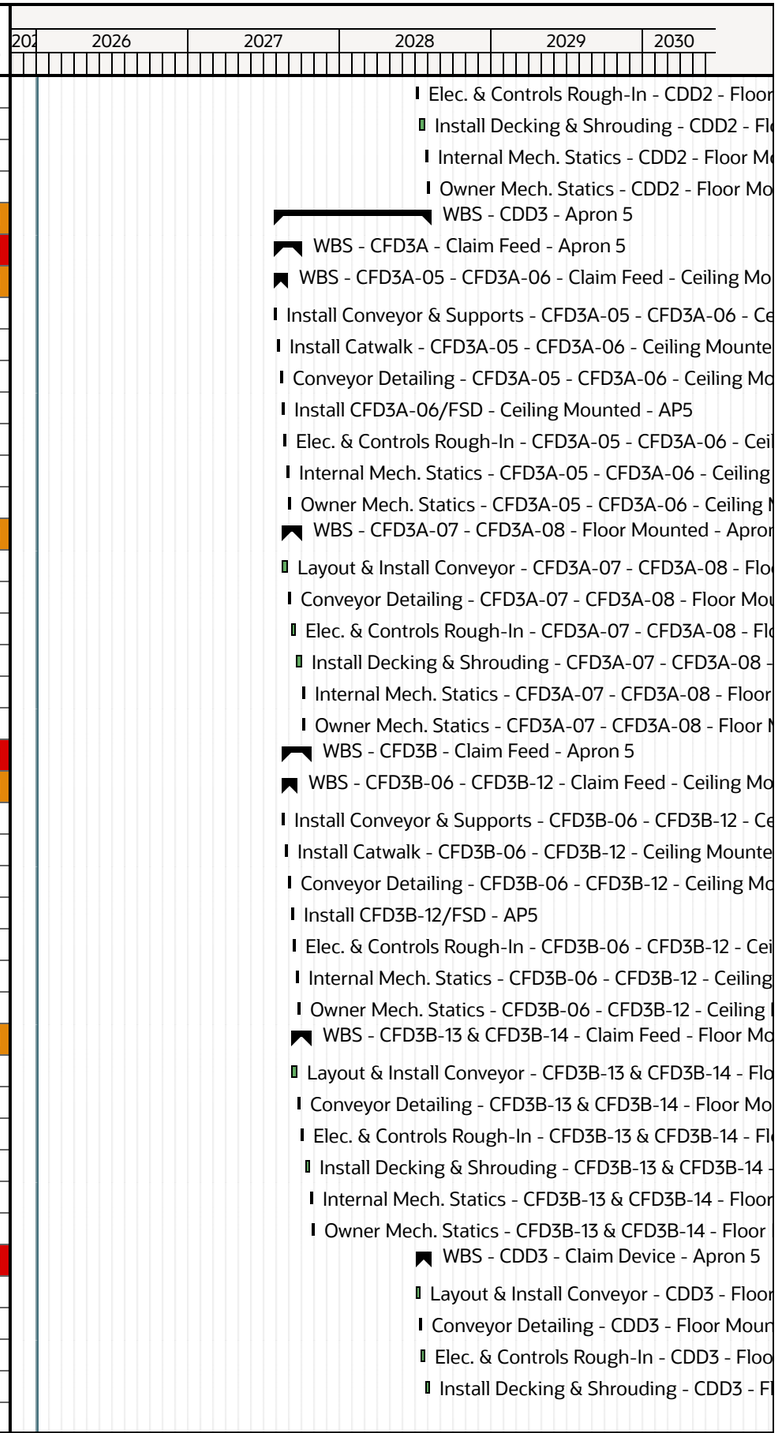


ID	Name	Dur	Start	Finish	TF
10081	BG-AP5-CDD3-50	Internal Mech. Statics - CDD3 - Floor Mounted - AP5	2.0d	4-Aug-28	7-Aug-28	48.0d
10082	BG-AP5-CDD3-60	Owner Mech. Statics - CDD3 - Floor Mounted - AP5	1.0d	8-Aug-28	8-Aug-28	48.0d
10083	WBS - CDD4 - Apron 5		267.0d	19-Aug-27	6-Sep-28	28.0d
10084	WBS - CFD4A - Claim Feed - Apron 5		267.0d	19-Aug-27	6-Sep-28	28.0d
10085	WBS - CFD4A-05 - CFD4A-07 - Claim Feed - Ceiling Mounted - Apron 5		28.0d	19-Aug-27	28-Sep-27	267.0d
10086	BG-AP5-CFD4A-30	Install Conveyor & Supports - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	5.0d	19-Aug-27	25-Aug-27	220.0d
10087	BG-AP5-CFD4A-40	Install Catwalk - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	5.0d	26-Aug-27	1-Sep-27	220.0d
10088	BG-AP5-CFD4A-50	Conveyor Detailing - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	5.0d	2-Sep-27	9-Sep-27	220.0d
10089	BG-AP5-CFD4A-60	Install CFD4A-07/FSD - Ceiling Mounted - AP5	5.0d	10-Sep-27	16-Sep-27	267.0d
10090	BG-AP5-CFD4A-70	Elec. & Controls Rough-In - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	5.0d	17-Sep-27	23-Sep-27	267.0d
10091	BG-AP5-CFD4A-80	Internal Mech. Statics - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	2.0d	24-Sep-27	27-Sep-27	267.0d
10092	BG-AP5-CFD4A-90	Owner Mech. Statics - CFD4A-05 - CFD4A-07 - Ceiling Mounted - AP5	1.0d	28-Sep-27	28-Sep-27	267.0d
10093	WBS - CFD4A-08 & CFD4A-09 - Claim Feed - Floor Mounted - Apron 5		30.0d	26-Jul-28	6-Sep-28	28.0d
10094	BG-AP5-CFD4A-100	Layout & Install Conveyor - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	5.0d	26-Jul-28	1-Aug-28	28.0d
10095	BG-AP5-CFD4A-110	Conveyor Detailing - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	5.0d	2-Aug-28	8-Aug-28	28.0d
10096	BG-AP5-CFD4A-120	Elec. & Controls Rough-In - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	7.0d	9-Aug-28	17-Aug-28	28.0d
10097	BG-AP5-CFD4A-130	Install Decking & Shrouding - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	10.0d	18-Aug-28	31-Aug-28	28.0d
10098	BG-AP5-CFD4A-140	Internal Mech. Statics - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	2.0d	1-Sep-28	5-Sep-28	28.0d
10099	BG-AP5-CFD4A-150	Owner Mech. Statics - CFD4A-08 & CFD4A-09 - Floor Mounted - AP5	1.0d	6-Sep-28	6-Sep-28	28.0d
10100	WBS - CFD4B - Claim Feed - Apron 5		45.0d	10-Sep-27	11-Nov-27	235.0d
10101	WBS - CFD4B-05 - CFD4B-12 - Claim Feed - Ceiling Mounted - Apron 5		33.0d	10-Sep-27	26-Oct-27	247.0d
10102	BG-AP5-CFD4B-30	Install Conveyor & Supports - CFD4B-05 - CFD4B-12 - Ceiling Mounted - AP5	10.0d	10-Sep-27	23-Sep-27	220.0d
10103	BG-AP5-CFD4B-40	Install Catwalk - CFD4B-05 - CFD4B-12 - Ceiling Mounted - AP5	8.0d	24-Sep-27	5-Oct-27	247.0d
10104	BG-AP5-CFD4B-50	Conveyor Detailing - CFD4B-05 - CFD4B-12 - Ceiling Mounted - AP5	5.0d	6-Oct-27	12-Oct-27	247.0d
10105	BG-AP5-CFD4B-60	Install CFD4B-12/FSD - Ceiling Mounted - AP5	2.0d	13-Oct-27	14-Oct-27	247.0d
10106	BG-AP5-CFD4B-70	Elec. & Controls Rough-In - CFD4B-04 - CFD4B-12 - Ceiling Mounted - AP5	5.0d	15-Oct-27	21-Oct-27	247.0d
10107	BG-AP5-CFD4B-80	Internal Mech. Statics - CFD4B-04 - CFD4B-12 - Ceiling Mounted - AP5	2.0d	22-Oct-27	25-Oct-27	247.0d
10108	BG-AP5-CFD4B-90	Owner Mech. Statics - CFD4B-04 - CFD4B-12 - Ceiling Mounted - AP5	1.0d	26-Oct-27	26-Oct-27	247.0d
10109	WBS - CFD4B-13 & CFD4B-14 - Claim Feed - Floor Mounted - Apron 5		35.0d	24-Sep-27	11-Nov-27	235.0d
10110	BG-AP5-CFD4B-100	Layout & Install Conveyor - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	10.0d	24-Sep-27	7-Oct-27	220.0d
10111	BG-AP5-CFD4B-110	Conveyor Detailing - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	5.0d	8-Oct-27	14-Oct-27	235.0d
10112	BG-AP5-CFD4B-120	Elec. & Controls Rough-In - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	7.0d	15-Oct-27	25-Oct-27	235.0d
10113	BG-AP5-CFD4B-130	Install Decking & Shrouding - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	10.0d	26-Oct-27	8-Nov-27	235.0d
10114	BG-AP5-CFD4B-140	Internal Mech. Statics - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	2.0d	9-Nov-27	10-Nov-27	235.0d
10115	BG-AP5-CFD4B-150	Owner Mech. Statics - CFD4B-13 & CFD4B-14 - Floor Mounted - AP5	1.0d	11-Nov-27	11-Nov-27	235.0d
10116	WBS - CDD4 - Claim Device - Apron 5		30.0d	12-Jul-28	22-Aug-28	38.0d
10117	BG-AP5-CDD4-10	Layout & Install Conveyor - CDD4 - Floor Mounted - AP5	10.0d	12-Jul-28	25-Jul-28	28.0d
10118	BG-AP5-CDD4-20	Conveyor Detailing - CDD4 - Floor Mounted - AP5	5.0d	19-Jul-28	25-Jul-28	38.0d
10119	BG-AP5-CDD4-30	Elec. & Controls Rough-In - CDD4 - Floor Mounted - AP5	7.0d	26-Jul-28	3-Aug-28	38.0d
10120	BG-AP5-CDD4-40	Install Decking & Shrouding - CDD4 - Floor Mounted - AP5	10.0d	4-Aug-28	17-Aug-28	38.0d
10121	BG-AP5-CDD4-50	Internal Mech. Statics - CDD4 - Floor Mounted - AP5	2.0d	18-Aug-28	21-Aug-28	38.0d
10122	BG-AP5-CDD4-60	Owner Mech. Statics - CDD4 - Floor Mounted - AP5	1.0d	22-Aug-28	22-Aug-28	38.0d

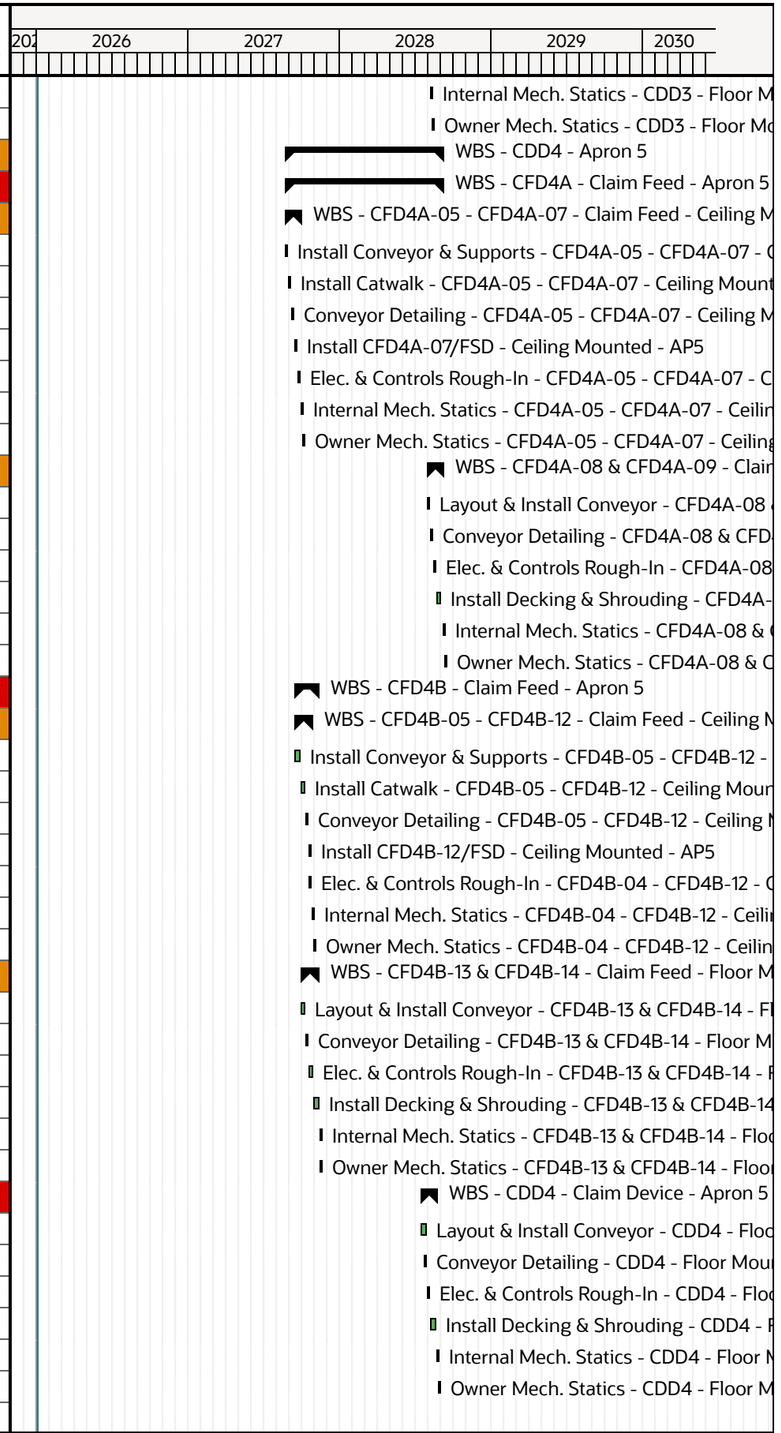


	ID	Name	Dur	Start	Finish	TF
10123	WBS - OSD1 - Apron 5		26.0d	20-Sep-27	25-Oct-27	248.0d
10124	WBS - OSD1-02 & OSD1-03 - Apron 5		26.0d	20-Sep-27	25-Oct-27	248.0d
10125	BG-AP5-OSD1-10	Layout & Install Conveyor - OSD1-02 & 03 - Floor Mounted - AP5	6.0d	20-Sep-27	27-Sep-27	248.0d
10126	BG-AP5-OSD1-20	Install Impact Protection - OSD1-02 & 03 - Floor Mounted - AP5	3.0d	28-Sep-27	30-Sep-27	248.0d
10127	BG-AP5-OSD1-30	Conveyor Detailing - OSD1-02 & 03 -Floor Mounted - AP5	3.0d	1-Oct-27	5-Oct-27	248.0d
10128	BG-AP5-OSD1-40	Install OSD1-02/FSD - Floor Mounted - AP5	2.0d	6-Oct-27	7-Oct-27	248.0d
10129	BG-AP5-OSD1-50	Elec. & Controls Rough-In - OSD1-02 & 03 - Floor Mounted - AP5	5.0d	8-Oct-27	14-Oct-27	248.0d
10130	BG-AP5-OSD1-60	Install Shrouding - OSD1-02 & 03 - Floor Mounted - AP5	5.0d	15-Oct-27	21-Oct-27	248.0d
10131	BG-AP5-OSD1-70	Internal Mech. Statics - OSD1-02 & 03 - Floor Mounted - AP5	1.0d	22-Oct-27	22-Oct-27	248.0d
10132	BG-AP5-OSD1-80	Owner Mech. Statics - OSD1-02 & 03 - Floor Mounted - AP5	1.0d	25-Oct-27	25-Oct-27	248.0d
10133	WBS - IRD1 - Apron 5		25.0d	20-Sep-27	22-Oct-27	249.0d
10134	WBS - IRD1-01 - IRD1-05 - Conveyor - Apron 5		25.0d	20-Sep-27	22-Oct-27	249.0d
10135	BG-AP5-IRD1-10	Layout & Install Conveyor - IRD1-01 - IRD1-05 - Floor Mounted - AP5	3.0d	20-Sep-27	22-Sep-27	251.0d
10136	BG-AP5-IRD1-20	Install Impact Protection - IRD1-01 - IRD1-05 - Floor Mounted - AP5	3.0d	23-Sep-27	27-Sep-27	251.0d
10137	BG-AP5-IRD1-30	Conveyor Detailing - IRD1-01 - IRD1-05 - Floor Mounted - AP5	3.0d	28-Sep-27	30-Sep-27	251.0d
10138	BG-AP5-IRD1-40	Install - IRD1-02/FSD - Floor Mounted - AP5	2.0d	1-Oct-27	4-Oct-27	251.0d
10139	BG-AP5-IRD1-50	Elec. & Controls Rough-In - IRD1-01 - IRD1-05 - Floor Mounted - AP5	5.0d	7-Oct-27	13-Oct-27	249.0d
10140	BG-AP5-IRD1-60	Install Shrouding - IRD1-01 - IRD1-05 - Floor Mounted - AP5	5.0d	14-Oct-27	20-Oct-27	249.0d
10141	BG-AP5-IRD1-70	Internal Mech. Statics - IRD1-01 - IRD1-05 - Floor Mounted - AP5	1.0d	21-Oct-27	21-Oct-27	249.0d
10142	BG-AP5-IRD1-80	Owner Mech. Statics - IRD1-01 - IRD1-05 - Floor Mounted - AP5	1.0d	22-Oct-27	22-Oct-27	249.0d
10143	WBS - ASD - Baggage Handling Systems - (BHS) - Sector B -Apron 8		272.0d	2-Jun-27	26-Jun-28	78.0d
10144	WBS - ASD - BHS - Steel Erection - Apron 8		11.0d	2-Jun-27	16-Jun-27	279.0d
10145	BG-AP8-BS-10	Layout & Install Hangers & Steel - AP8	10.0d	2-Jun-27	15-Jun-27	57.0d
10146	BG-AP8-BS-20	Header Steel Inspection - AP8	1.0d	16-Jun-27	16-Jun-27	279.0d
10147	WBS - CDD1 - Apron 8		252.0d	30-Jun-27	26-Jun-28	78.0d
10148	WBS - CFD1A - Claim Feed - Apron 8		35.0d	30-Jun-27	18-Aug-27	295.0d
10149	WBS - CFD1A-06 - CFD1A-07 - Claim Feed - Ceiling Mounted - Apron 8		22.0d	30-Jun-27	30-Jul-27	308.0d
10150	BG-AP8-CFD1A-30	Layout & Install Conveyor - CFD1A-06- CFD1A-07 - Ceiling Mounted - AP8	5.0d	30-Jun-27	7-Jul-27	270.0d
10151	BG-AP8-CFD1A-40	Install Catwalk - CFD1A-06 - CFD1A-07 - Ceiling Mounted - AP8	5.0d	8-Jul-27	14-Jul-27	282.0d
10152	BG-AP8-CFD1A-50	Conveyor Detailing - CFD1A-06 - CFD1A-07 - Ceiling Mounted - AP8	3.0d	15-Jul-27	19-Jul-27	282.0d
10153	BG-AP8-CFD1A-60	Install CFD1A-07/FSD - Ceiling Mounted - AP8	2.0d	20-Jul-27	21-Jul-27	303.0d
10154	BG-AP8-CFD1A-70	Elec. & Controls Rough-In - CFD1A-06 - CFD1A-07 - Ceiling Mounted - AP8	4.0d	22-Jul-27	27-Jul-27	303.0d
10155	BG-AP8-CFD1A-80	Internal Mech. Statics - CFD1A-06 - CFD1A-07 - Ceiling Mount - AP8	2.0d	28-Jul-27	29-Jul-27	308.0d
10156	BG-AP8-CFD1A-90	Owner Mech. Statics - CFD1A-06 - CFD1A-07 - Ceiling Mount - AP8	1.0d	30-Jul-27	30-Jul-27	308.0d
10157	WBS - CFD1A-08 & CFD1A-09 - Claim Feed - Floor Mounted - Apron 8		22.0d	20-Jul-27	18-Aug-27	295.0d
10158	BG-AP8-CFD1A-100	Layout & Install Conveyor - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	5.0d	20-Jul-27	26-Jul-27	282.0d
10159	BG-AP8-CFD1A-110	Conveyor Detailing - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	5.0d	27-Jul-27	2-Aug-27	295.0d
10160	BG-AP8-CFD1A-120	Elec. & Controls Rough-In - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	5.0d	3-Aug-27	9-Aug-27	295.0d
10161	BG-AP8-CFD1A-130	Install Decking & Shrouding - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	5.0d	10-Aug-27	16-Aug-27	295.0d
10162	BG-AP8-CFD1A-140	Internal Mech. Statics - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	1.0d	17-Aug-27	17-Aug-27	295.0d
10163	BG-AP8-CFD1A-150	Owner Mech. Statics - CFD1A-08 & CFD1A-09 - Floor Mounted - AP8	1.0d	18-Aug-27	18-Aug-27	295.0d
10164	WBS - CFD1B - Claim Feed - Apron 8		50.0d	8-Jul-27	16-Sep-27	275.0d

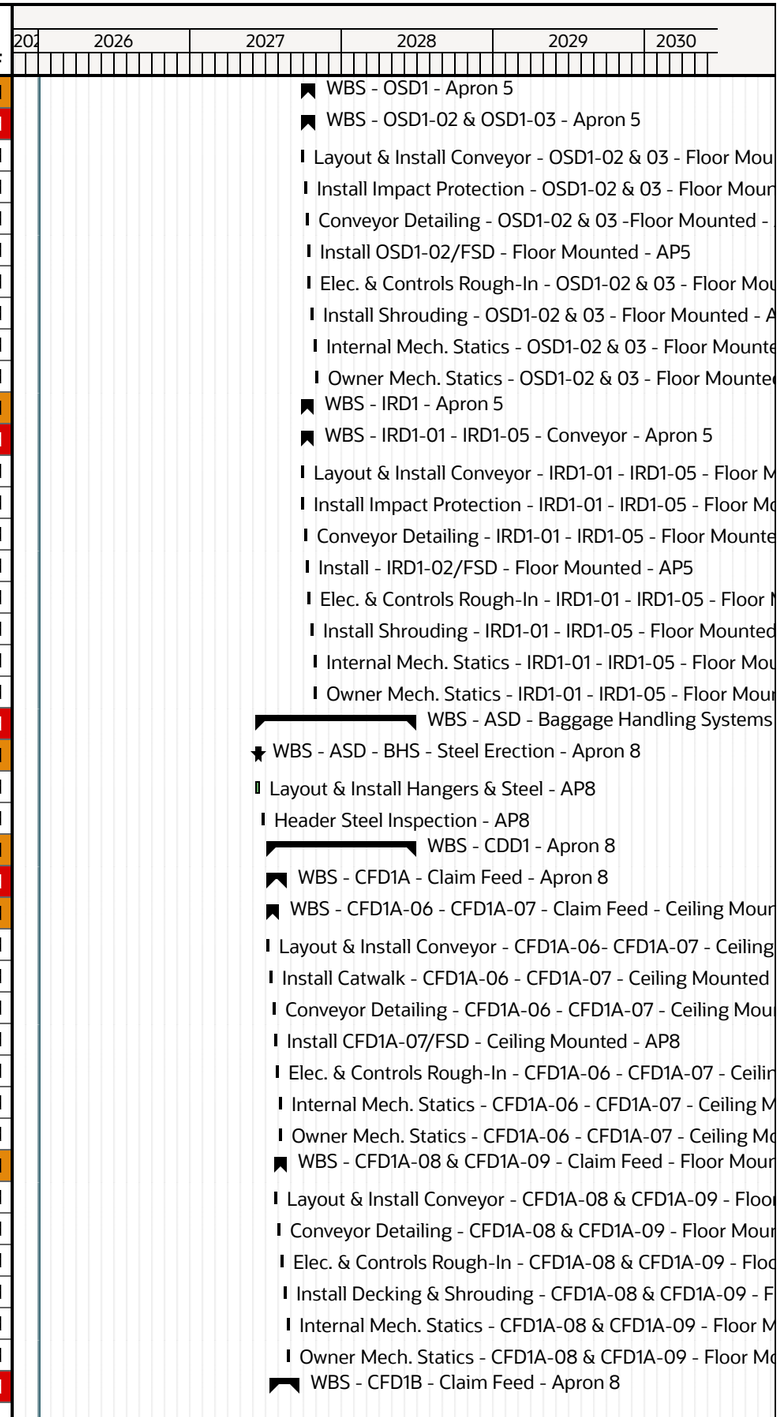


	ID	Name	Dur	Start	Finish	TF
10165	WBS - CFD1B-06 - CFD1B-12 - Claim Feed - Ceiling Mounted - Apron 8		28.0d	8-Jul-27	16-Aug-27	297.0d
10166	BG-AP8-CFD1B-30	Layout & Install Conveyor - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	5.0d	8-Jul-27	14-Jul-27	270.0d
10167	BG-AP8-CFD1B-40	Install Catwalk - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	5.0d	15-Jul-27	21-Jul-27	270.0d
10168	BG-AP8-CFD1B-50	Conveyor Detailing - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	5.0d	22-Jul-27	28-Jul-27	270.0d
10169	BG-AP8-CFD1B-60	Install CFD1B-12/FSD - Ceiling Mounted - AP8	5.0d	29-Jul-27	4-Aug-27	297.0d
10170	BG-AP8-CFD1B-70	Elec. & Controls Rough-In - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	5.0d	5-Aug-27	11-Aug-27	297.0d
10171	BG-AP8-CFD1B-80	Internal Mech. Statics - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	2.0d	12-Aug-27	13-Aug-27	297.0d
10172	BG-AP8-CFD1B-90	Owner Mech. Statics - CFD1B-06 - CFD1B-12 - Ceiling Mounted - AP8	1.0d	16-Aug-27	16-Aug-27	297.0d
10173	WBS - CFD1B-13 & CFD1B-14 - Claim Feed - Floor Mounted - Apron 8		35.0d	29-Jul-27	16-Sep-27	275.0d
10174	BG-AP8-CFD1B-100	Layout & Install Conveyor - CFD1B-13 &14 - Floor Mounted - AP8	10.0d	29-Jul-27	11-Aug-27	270.0d
10175	BG-AP8-CFD1B-110	Conveyor Detailing - CFD1B-13 &14 - Floor Mounted - AP8	5.0d	12-Aug-27	18-Aug-27	275.0d
10176	BG-AP8-CFD1B-120	Elec. & Controls Rough-in - CFD1B-13 &14 - Floor Mounted - AP8	7.0d	19-Aug-27	27-Aug-27	275.0d
10177	BG-AP8-CFD1B-130	Install Decking & Shrouding - CFD1B-13 &14 - Floor Mounted - AP8	10.0d	30-Aug-27	13-Sep-27	275.0d
10178	BG-AP8-CFD1B-140	Internal Mech. Statics - CFD1B-13 &14 - Floor Mounted - AP8	2.0d	14-Sep-27	15-Sep-27	275.0d
10179	BG-AP8-CFD1B-150	Owner Mech. Statics - CFD1B-13 &14 - Floor Mounted - AP8	1.0d	16-Sep-27	16-Sep-27	275.0d
10180	WBS - CDD1 - Claim Device - Apron 8		30.0d	15-May-28	26-Jun-28	78.0d
10181	BG-AP8-CDD1-10	Layout & Install Conveyor - CDD1 - Floor Mounted - AP8	10.0d	15-May-28	26-May-28	78.0d
10182	BG-AP8-CDD1-20	Conveyor Detailing - CDD1 - Floor Mounted - AP8	5.0d	22-May-28	26-May-28	78.0d
10183	BG-AP8-CDD1-30	Elec. & Controls Rough-In - CDD1 - Floor Mounted - AP8	7.0d	30-May-28	7-Jun-28	78.0d
10184	BG-AP8-CDD1-40	Install Decking & Shrouding - CDD1 - Floor Mounted - AP8	10.0d	8-Jun-28	21-Jun-28	78.0d
10185	BG-AP8-CDD1-50	Internal Mech. Statics - CDD1 - Floor Mounted - AP8	2.0d	22-Jun-28	23-Jun-28	78.0d
10186	BG-AP8-CDD1-60	Owner Mech. Statics - CDD1 - Floor Mounted - AP8	1.0d	26-Jun-28	26-Jun-28	78.0d
10187	WBS - ASD - Baggage Handling Systems - (BHS) - Sector C - Apron 9		231.0d	9-Feb-27	6-Jan-28	562.0d
10188	WBS - ASD - BHS - Steel Erection - Apron 9		36.0d	11-May-27	30-Jun-27	277.0d
10189	BG-AP9-BS-10	Layout & Install Hangers & Steel - AP9	32.0d	11-May-27	24-Jun-27	0.0d
10190	BG-AP9-BS-20	Header Steel Inspection - AP9	4.0d	25-Jun-27	30-Jun-27	277.0d
10191	WBS - SD1/SD2 - Apron 9		207.0d	9-Feb-27	1-Dec-27	586.0d
10192	WBS - SD1-16 - SD1-22 - Apron 9		43.0d	30-Sep-27	1-Dec-27	223.0d
10193	BG-AP9-SD1-30	Install Conveyor - SD1-16 - SD1-22 - Ceiling Mounted - AP9	12.0d	30-Sep-27	15-Oct-27	214.0d
10194	BG-AP9-SD1-40	Install Catwalk - SD1-16 - SD1-22 - Ceiling Mounted - AP9	10.0d	5-Oct-27	18-Oct-27	228.0d
10195	BG-AP9-SD1-50	Conveyor Detailing - SD1-16 - SD1-22 - Ceiling Mounted - AP9	5.0d	12-Oct-27	18-Oct-27	228.0d
10196	BG-AP9-SD1-60	Elec. & Controls Rough-in - SD1-16 - SD1-22 - Ceiling Mounted - AP9	10.0d	19-Oct-27	1-Nov-27	228.0d
10197	BG-AP9-SD1-70	Internal Mech. Statics - SD1-16 - SD1-22 - Ceiling Mounted - AP9	2.0d	2-Nov-27	3-Nov-27	238.0d
10198	BG-AP9-SD1-80	Owner Mech. Statics - SD1-16-SD1-22 - Ceiling Mounted - AP9	1.0d	1-Dec-27	1-Dec-27	223.0d
10199	WBS - SD2-13 - SD2-22 - Apron 9		31.0d	18-Oct-27	1-Dec-27	223.0d
10200	BG-AP9-SD2-30	Install Conveyor - SD2-13 - SD2-22 - Ceiling Mounted - AP9	10.0d	18-Oct-27	29-Oct-27	214.0d
10201	BG-AP9-SD2-40	Install Catwalk - SD2-13 - SD2-22 - Ceiling Mounted - AP9	10.0d	21-Oct-27	3-Nov-27	217.0d
10202	BG-AP9-SD2-50	Conveyor Detailing - SD2-13 - SD2-22 - Ceiling Mounted - AP9	6.0d	1-Nov-27	8-Nov-27	214.0d
10203	BG-AP9-SD2-60	Elec. & Controls Rough-In - SD2-13 - SD2-22 - Ceiling Mounted - AP9	10.0d	9-Nov-27	22-Nov-27	223.0d
10204	BG-AP9-SD2-70	Internal Mech. Statics - SD2-13 - SD2-22 - Ceiling Mounted - AP9	2.0d	23-Nov-27	24-Nov-27	223.0d
10205	BG-AP9-SD2-80	Owner Mech. Statics - SD2-13 - SD2-22 - Ceiling Mounted - AP9	1.0d	1-Dec-27	1-Dec-27	223.0d
10206	WBS - SD1 - Elec. Panel Install - Apron 9		207.0d	9-Feb-27	1-Dec-27	586.0d

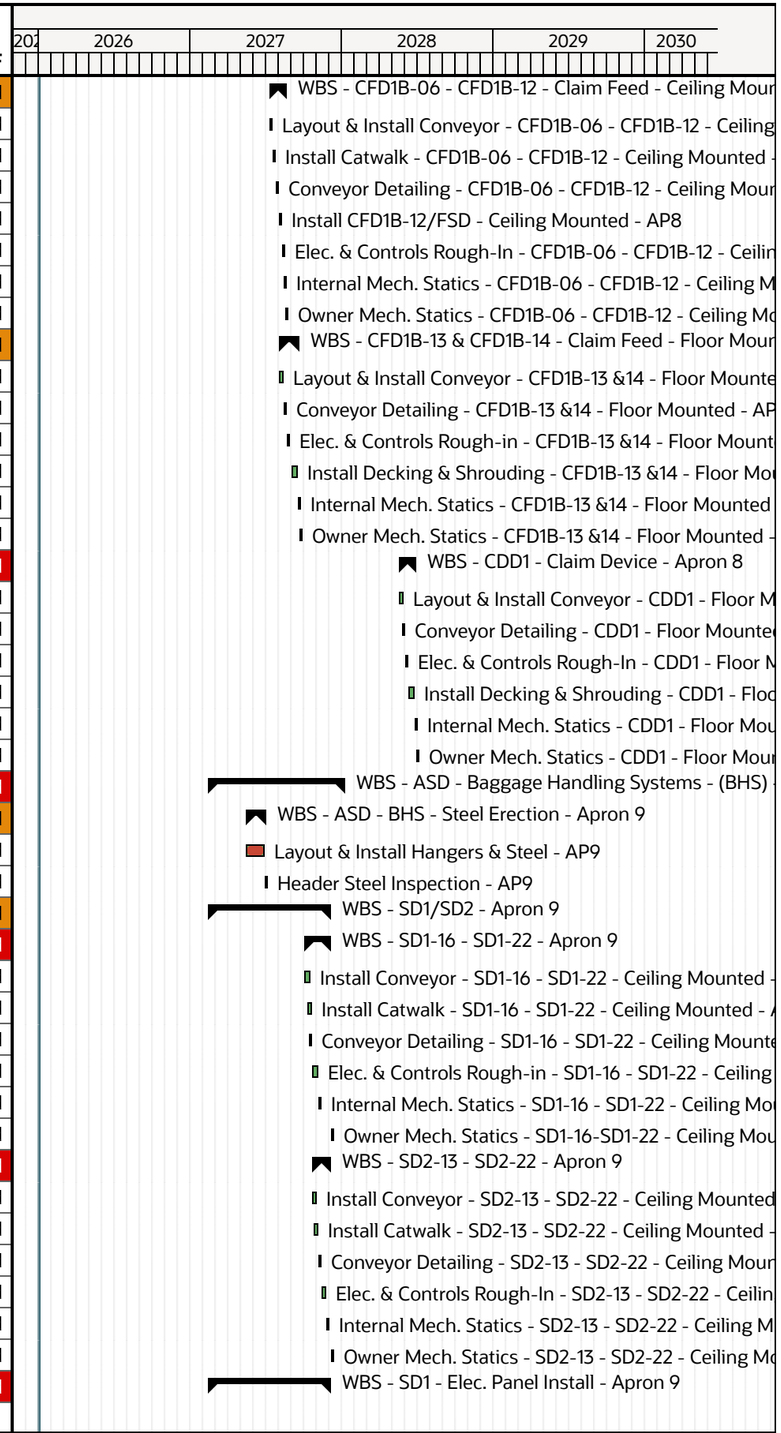


ID	Name	Dur	Start	Finish	TF
10207	WBS - SD1 - MPP-A31 & FCP-A31 - Apron 9	207.0d	9-Feb-27	1-Dec-27	586.0d
10208	BG-AP9-SD1-MPP-10 — SD1 - Layout & Install Elec. Panel - MPP-A31 & FCP-A31 - AP9	2.0d	9-Feb-27	10-Feb-27	371.0d
10209	BG-AP9-SD1-MPP-20 — SD1 - Elec. Feeder Wire Measurement & Procurement - MPP-A31 & FCP-A31 - ...	10.0d	11-Feb-27	24-Feb-27	765.0d
10210	BG-AP9-SD1-MPP-30 — SD1 - Pull & Terminate Elec. - MPP-A31 & FCP-A31 - AP9	10.0d	25-Feb-27	10-Mar-27	765.0d
10211	BG-AP9-SD1-MPP-40 — SD1 - Elec. Testing & Inspection- MPP-A31 & FCP-A31 - AP9	5.0d	23-Nov-27	1-Dec-27	585.0d
10212	WBS - RID1 - Apron 9	196.0d	9-Mar-27	14-Dec-27	577.0d
10213	WBS - RID1-01 - RID1-09 - Apron 9	24.0d	9-Nov-27	14-Dec-27	214.0d
10214	BG-AP9-RID1-30 — Install Conveyor - RID1-01 - RID1-09 - Ceiling Mounted - AP9	8.0d	9-Nov-27	18-Nov-27	214.0d
10215	BG-AP9-RID1-40 — Install Catwalk - RID1-01 - RID1-09 - Ceiling Mounted - AP9	10.0d	12-Nov-27	29-Nov-27	214.0d
10216	BG-AP9-RID1-50 — Conveyor Detailing - RID1-01 - RID-09 - Ceiling Mounted - AP9	5.0d	19-Nov-27	29-Nov-27	214.0d
10217	BG-AP9-RID1-60 — Elec. & Controls Rough-In - RID1-01 - RID1-09 - Ceiling Mounted - AP9	8.0d	30-Nov-27	9-Dec-27	214.0d
10218	BG-AP9-RID1-70 — Internal Mech. Statics - RID1-01 - RID1-09 - Ceiling Mounted - AP9	2.0d	10-Dec-27	13-Dec-27	214.0d
10219	BG-AP9-RID1-80 — Owner Mech. Statics - RID1-01 - RID1-09 - Ceiling Mounted - AP9	1.0d	14-Dec-27	14-Dec-27	214.0d
10220	WBS - RID1 - Elec. Panel Install - Apron 9	187.0d	9-Mar-27	1-Dec-27	586.0d
10221	WBS - RID1 - MPP-B32 & FCP-B32 - Apron 9	187.0d	9-Mar-27	1-Dec-27	586.0d
10222	BG-AP9-RID1-MPP-110 — RID1 - Layout & Install Elec. Panel - MPP-B32 & FCP-B32 - AP9	2.0d	9-Mar-27	10-Mar-27	351.0d
10223	BG-AP9-RID1-MPP-120 — RID1 - Elec. Feeder Wire Measurement & Procurement - MPP-B32 & FCP-B32 -...	10.0d	11-Mar-27	24-Mar-27	745.0d
10224	BG-AP9-RID1-MPP-130 — RID1 - Pull & Terminate Elec. - MPP-B32 & FCP-B32 - AP9	10.0d	25-Mar-27	7-Apr-27	745.0d
10225	BG-AP9-RID1-MPP-140 — RID1 - Elec. Testing & Inspection- MPP-B32 & FCP-B32 - AP9	5.0d	23-Nov-27	1-Dec-27	585.0d
10226	WBS - CDD1 - Apron 9	107.0d	1-Jul-27	2-Dec-27	542.0d
10227	WBS - CFD1A - Claim Feed - Apron 9	27.0d	1-Jul-27	9-Aug-27	302.0d
10228	WBS - CFD1A-04 - CFD1A-06 - Claim Feed - Ceiling Mounted - Apron 9	19.0d	1-Jul-27	28-Jul-27	310.0d
10229	BG-AP9-CFD1A-120 — Install Conveyor - CFD1A-04 - CFD1A-06 - Ceiling Mounted - AP9	5.0d	1-Jul-27	8-Jul-27	280.0d
10230	BG-AP9-CFD1A-130 — Install Catwalk - CFD1A-04 - CFD1A-06 - Ceiling Mounted - AP9	8.0d	7-Jul-27	16-Jul-27	280.0d
10231	BG-AP9-CFD1A-140 — Conveyor Detailing - CFD1A-04 - CFD1A-06 - Ceiling Mounted - AP9	5.0d	12-Jul-27	16-Jul-27	280.0d
10232	BG-AP9-CFD1A-150 — Elec. & Controls Rough-In - CFD1A-04 - CFD1A-06 - Ceiling Mounted - AP9	5.0d	19-Jul-27	23-Jul-27	310.0d
10233	BG-AP9-CFD1A-160 — Internal Mech. Statics - CFD1A-04 - CFD1A-06 - Ceiling Mount - AP9	2.0d	26-Jul-27	27-Jul-27	310.0d
10234	BG-AP9-CFD1A-170 — Owner Mech. Statics - CFD1A-04 - CFD1A-06 - Ceiling Mount - AP9	1.0d	28-Jul-27	28-Jul-27	310.0d
10235	WBS - CFD1A-01 - CFD1A-03 - Floor Mounted - Apron 9	18.0d	15-Jul-27	9-Aug-27	302.0d
10236	BG-AP9-CFD1A-10 — Layout & Install Conveyor - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	5.0d	15-Jul-27	21-Jul-27	280.0d
10237	BG-AP9-CFD1A-20 — Install Impact Protection - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	5.0d	20-Jul-27	26-Jul-27	280.0d
10238	BG-AP9-CFD1A-30 — Conveyor Detailing - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	5.0d	23-Jul-27	29-Jul-27	280.0d
10239	BG-AP9-CFD1A-40 — Elec. & Controls Rough-In - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	5.0d	30-Jul-27	5-Aug-27	302.0d
10240	BG-AP9-CFD1A-50 — Internal Mech. Statics - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	1.0d	6-Aug-27	6-Aug-27	302.0d
10241	BG-AP9-CFD1A-60 — Owner Mech. Statics - CFD1A-01 - CFD1A-03 - Floor Mounted - AP9	1.0d	9-Aug-27	9-Aug-27	302.0d
10242	WBS - CFD1B - Claim Feed - Apron 9	29.0d	30-Jul-27	9-Sep-27	280.0d
10243	WBS - CFD1B-04 - CFD1B-06 - Claim Feed - Ceiling Mounted - Apron 9	19.0d	30-Jul-27	25-Aug-27	290.0d
10244	BG-AP9-CFD1B-120 — Install Conveyor - CFD1B-04 - CFD1B-06 - Ceiling Mounted - AP9	5.0d	30-Jul-27	5-Aug-27	280.0d
10245	BG-AP9-CFD1B-130 — Install Catwalk - CFD1B-04 - CFD1B-06 - Ceiling Mounted - AP9	8.0d	4-Aug-27	13-Aug-27	280.0d
10246	BG-AP9-CFD1B-140 — Conveyor Detailing - CFD1B-04 - CFD1B-06 - Ceiling Mounted - AP9	5.0d	9-Aug-27	13-Aug-27	280.0d
10247	BG-AP9-CFD1B-150 — Elec. & Controls Rough-In - CFD1B-04 - CFD1B-06 - Ceiling Mounted - AP9	5.0d	16-Aug-27	20-Aug-27	290.0d
10248	BG-AP9-CFD1B-160 — Internal Mech. Statics - CFD1B-04 - CFD1B-06 - Ceiling Mount - AP9	2.0d	23-Aug-27	24-Aug-27	290.0d

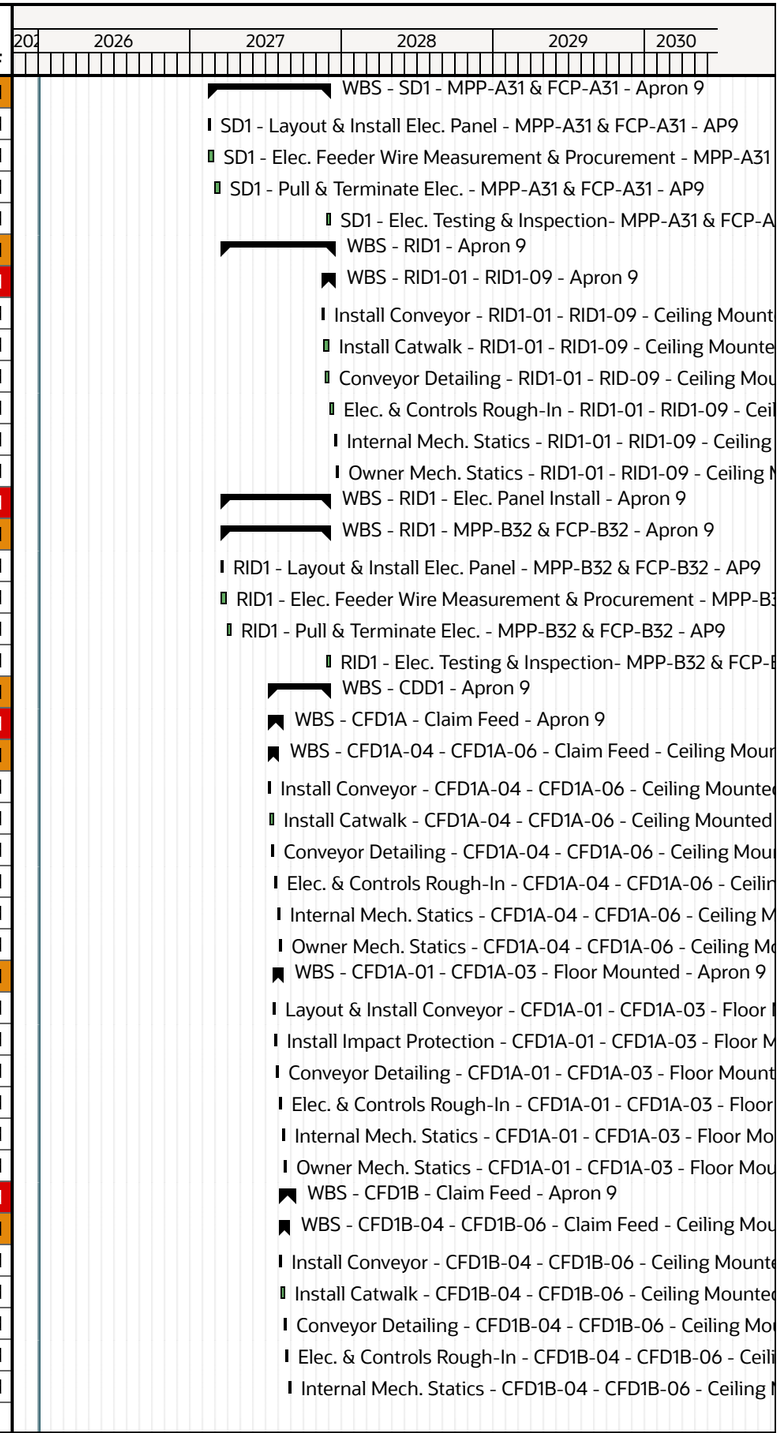


	ID	Name	Dur	Start	Finish	TF
10249	BG-AP9-CFD1B-170	Owner Mech. Statics - CFD1B-04 - CFD1B-06 - Ceiling Mount - AP9	1.0d	25-Aug-27	25-Aug-27	290.0d
10250	WBS - CFD1B-01 - 03 - Claim Feed - Floor Mounted - Apron 9		18.0d	16-Aug-27	9-Sep-27	280.0d
10251	BG-AP9-CFD1B-10	Layout & Install Conveyor - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	5.0d	16-Aug-27	20-Aug-27	280.0d
10252	BG-AP9-CFD1B-20	Install Impact Protection - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	5.0d	19-Aug-27	25-Aug-27	280.0d
10253	BG-AP9-CFD1B-30	Conveyor Detailing - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	5.0d	24-Aug-27	30-Aug-27	280.0d
10254	BG-AP9-CFD1B-40	Elec. & Controls Rough-In - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	5.0d	31-Aug-27	7-Sep-27	280.0d
10255	BG-AP9-CFD1B-50	Internal Mech. Statics - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	1.0d	8-Sep-27	8-Sep-27	280.0d
10256	BG-AP9-CFD1B-60	Owner Mech. Statics - CFD1B-01 - CFD1B-03 - Floor Mounted - AP9	1.0d	9-Sep-27	9-Sep-27	280.0d
10257	WBS - CCD1 - Elec. Panel Install - Apron 9		28.0d	22-Oct-27	2-Dec-27	542.0d
10258	WBS - CDD1 - MPP-A33 & FCP-A33 - Apron 9		28.0d	22-Oct-27	2-Dec-27	542.0d
10259	BG-AP9-CDD1-MPP-10	CDD1 - Layout Elec. Panel - MPP-A33 & FCP-A33 - AP9	1.0d	22-Oct-27	22-Oct-27	541.0d
10260	BG-AP9-CDD1-MPP-20	CDD1 - Install Elec. Panel MPP-A33 & FCP-A33 - AP9	2.0d	25-Oct-27	26-Oct-27	541.0d
10261	BG-AP9-CDD1-MPP-30	CCD1 - Elec. Feeder Wire Measurement & Procurement - MPP-A33 & FCP-A33 ...	10.0d	27-Oct-27	9-Nov-27	541.0d
10262	BG-AP9-CDD1-MPP-40	CDD1 - Pull & Terminate Elec. - MPP-A33 & FCP-A33 - AP9	10.0d	10-Nov-27	23-Nov-27	541.0d
10263	BG-AP9-CDD1-MPP-50	CCD1 - Elec. Testing & Inspection- MPP-A33 & FCP-A33 - AP9	5.0d	24-Nov-27	2-Dec-27	541.0d
10264	WBS - MUD4 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10265	WBS - MDF4A - Make-Up Feed - Apron 9		21.0d	18-Oct-27	15-Nov-27	233.0d
10266	WBS - MDF4A-01 - MDF4A-04 - Make-Up Feed - Ceiling Mounted - Apron 9		14.0d	18-Oct-27	4-Nov-27	240.0d
10267	BG-AP9-MDF4A-30	Install Conveyor - MDF4A-01 - MDF4A-04 - Ceiling Mounted - AP9	3.0d	18-Oct-27	20-Oct-27	230.0d
10268	BG-AP9-MDF4A-40	Install Catwalk - MDF4A-01 - MDF4A-04 - Ceiling Mounted - AP9	5.0d	21-Oct-27	27-Oct-27	233.0d
10269	BG-AP9-MDF4A-50	Conveyor Detailing - MDF4A-01 - MDF4A-04 - Ceiling Mounted - AP9	3.0d	26-Oct-27	28-Oct-27	233.0d
10270	BG-AP9-MDF4A-60	Elec. & Controls Rough-in - MDF4A-01 - MDF4A - Ceiling Mounted - AP9	3.0d	29-Oct-27	2-Nov-27	240.0d
10271	BG-AP9-MDF4A-70	Internal Mech. Statics - MDF4A-01 - MDF4A-04A - Ceiling Mounted - AP9	1.0d	3-Nov-27	3-Nov-27	240.0d
10272	BG-AP9-MDF4A-80	Owner Mech. Statics - MDF4A-05 - Ceiling Mounted - AP9	1.0d	4-Nov-27	4-Nov-27	240.0d
10273	WBS - MDF4A-05 - Make-Up Feed - Floor Mounted - Apron 9		12.0d	29-Oct-27	15-Nov-27	233.0d
10274	BG-AP9-MDF4A-100	Layout & Install Conveyor - MDF4A-05 - Floor Mounted - AP9	2.0d	29-Oct-27	1-Nov-27	233.0d
10275	BG-AP9-MDF4A-110	Conveyor Detailing - MDF4A-05 - Floor Mounted - AP9	2.0d	3-Nov-27	4-Nov-27	233.0d
10276	BG-AP9-MDF4A-120	Elec. & Controls Rough-In - MDF4A-05 - Floor Mounted - AP9	2.0d	8-Nov-27	9-Nov-27	233.0d
10277	BG-AP9-MDF4A-130	Install Decking & Shrouding - MDF4A-05 - Floor Mounted - AP9	2.0d	10-Nov-27	11-Nov-27	233.0d
10278	BG-AP9-MDF4A-140	Internal Mech. Statics - MDF4A-05 - Floor Mounted - AP9	1.0d	12-Nov-27	12-Nov-27	233.0d
10279	BG-AP9-MDF4A-150	Owner Mech. Statics - MDF4A-05 - Floor Mounted - AP9	1.0d	15-Nov-27	15-Nov-27	233.0d
10280	WBS - MDF4B - Make-Up Feed - Apron 9		18.0d	21-Oct-27	15-Nov-27	233.0d
10281	WBS - MDF4B-01 - MDF4B-04 - Make-Up Feed - Ceiling Mounted - Apron 9		18.0d	21-Oct-27	15-Nov-27	233.0d
10282	BG-AP9-MDF4B-30	Install Conveyor - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	3.0d	21-Oct-27	25-Oct-27	233.0d
10283	BG-AP9-MDF4B-40	Install Catwalk - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	5.0d	26-Oct-27	1-Nov-27	233.0d
10284	BG-AP9-MDF4B-50	Conveyor Detailing - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	5.0d	2-Nov-27	8-Nov-27	233.0d
10285	BG-AP9-MDF4B-60	Elec. & Controls Rough-in - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	3.0d	9-Nov-27	11-Nov-27	233.0d
10286	BG-AP9-MDF4B-70	Internal Mech. Statics - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	1.0d	12-Nov-27	12-Nov-27	233.0d
10287	BG-AP9-MDF4B-80	Owner Mech. Statics - MDF4B-01 - MDF4B-04 - Ceiling Mounted - AP9	1.0d	15-Nov-27	15-Nov-27	233.0d
10288	WBS - MDF4B-05 - Make-Up Feed - Floor Mount - Apron 9		10.0d	26-Oct-27	8-Nov-27	238.0d
10289	BG-AP9-MDF4B-100	Layout & Install Conveyor - MDF4B-05 - Floor Mounted - AP9	2.0d	26-Oct-27	27-Oct-27	238.0d
10290	BG-AP9-MDF4B-110	Conveyor Detailing - MDF4B-05 - Floor Mounted - AP9	2.0d	28-Oct-27	29-Oct-27	238.0d

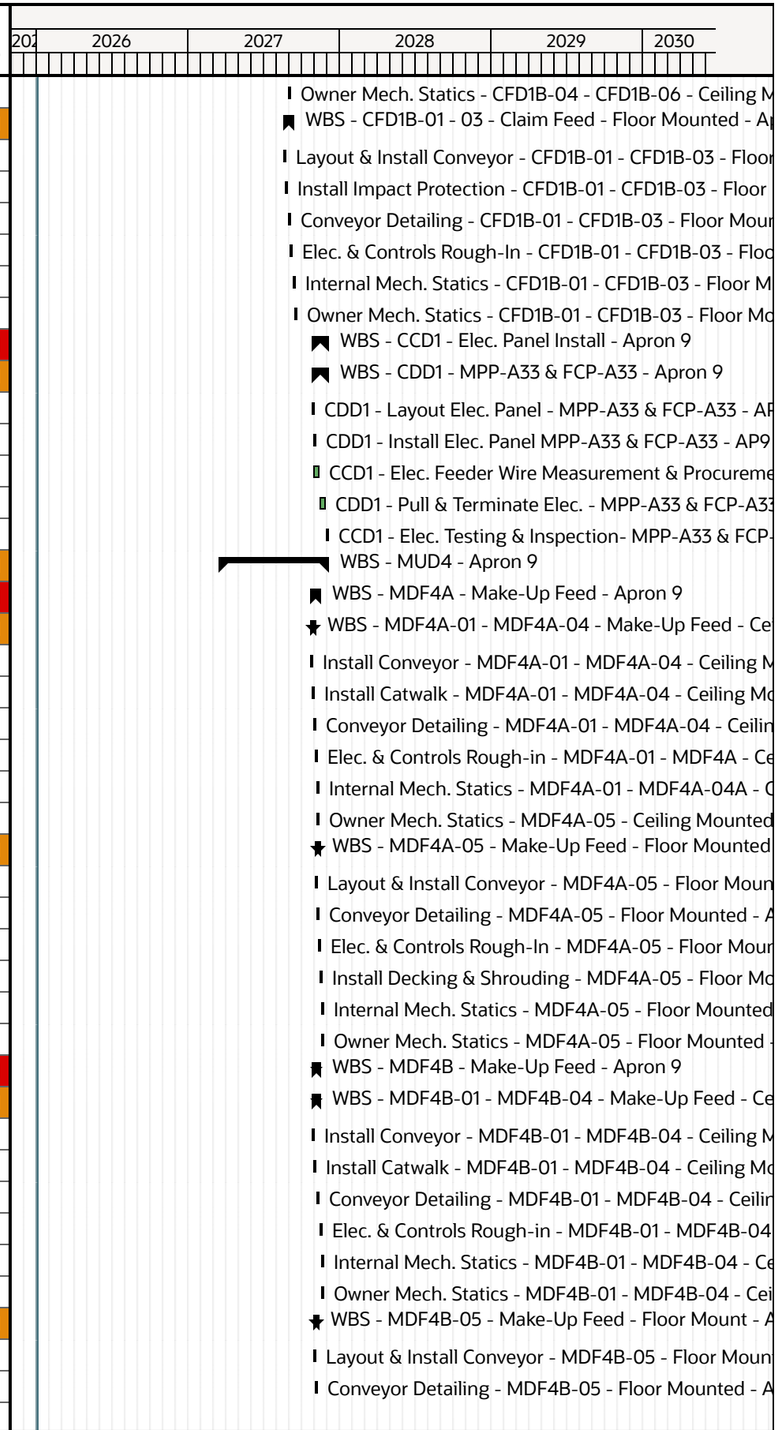


	ID	Name	Dur	Start	Finish	TF
10291	BG-AP9-MDF4B-120	Elec. & Controls Rough-In - MDF4B-05 - Floor Mounted - AP9	2.0d	1-Nov-27	2-Nov-27	238.0d
10292	BG-AP9-MDF4B-130	Install Decking & Shrouding - MDF4B-05 - Floor Mounted - AP9	2.0d	3-Nov-27	4-Nov-27	238.0d
10293	BG-AP9-MDF4B-140	Internal Mech. Statics - MDF4B-05 - Floor Mounted - AP9	1.0d	5-Nov-27	5-Nov-27	238.0d
10294	BG-AP9-MDF4B-150	Owner Mech. Statics - MDF4B-05 - Floor Mounted - AP9	1.0d	8-Nov-27	8-Nov-27	238.0d
10295	WBS - MUD4 - Make-Up - Floor Mounted - Apron 9		33.0d	11-Mar-27	26-Apr-27	375.0d
10296	BG-AP9-MUD4-10	Layout & Install Conveyor - MUD4 - Floor Mounted - AP9	10.0d	11-Mar-27	24-Mar-27	351.0d
10297	BG-AP9-MUD4-20	Impact Protection & Cross-Overs - Install - MUD4 - Floor Mounted - AP9	5.0d	25-Mar-27	31-Mar-27	351.0d
10298	BG-AP9-MUD4-30	Conveyor Detailing/Shrouding - MUD4 - Floor Mounted - AP9	9.0d	1-Apr-27	13-Apr-27	351.0d
10299	BG-AP9-MUD4-40	Elec. & Controls Rough-In - MUD4 - Floor Mounted - AP9	7.0d	14-Apr-27	22-Apr-27	375.0d
10300	BG-AP9-MUD4-50	Internal Mech. Statics - MUD4 - Floor Mounted - AP9	1.0d	23-Apr-27	23-Apr-27	375.0d
10301	BG-AP9-MUD4-60	Owner Mech. Statics - MUD4 - Floor Mounted - AP9	1.0d	26-Apr-27	26-Apr-27	375.0d
10302	WBS - MUD4 - Elec. Panel Install - MPP-B36 & FCP-B36 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10303	WBS - MUD4 - MPP-B36 & FCP-B36 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10304	BG-AP9-MUD4-MPP-10	MUD4 - Layout & Install Elec. Panel - MPP-B36 & FCP-B36 - AP9	2.0d	9-Mar-27	10-Mar-27	351.0d
10305	BG-AP9-MUD4-MPP-20	MUD4 - Elec. Feeder Wire Measurement & Procurement - MPP-B36 & FCP-B36...	10.0d	11-Mar-27	24-Mar-27	750.0d
10306	BG-AP9-MUD4-MPP-30	MUD4 - Pull & Terminate Elec. - MPP-B36 & FCP-B36 - AP9	5.0d	25-Mar-27	31-Mar-27	750.0d
10307	BG-AP9-MUD4-MPP-40	MUD4 - Elec. Testing & Inspection- MPP-B36 & FCP-B36 - AP9	5.0d	23-Nov-27	1-Dec-27	585.0d
10308	WBS - MUD5 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10309	WBS - MDF5A - Make-Up Feed - Apron 9		18.0d	21-Oct-27	15-Nov-27	233.0d
10310	WBS - MDF5A-01 - MDF5A-04 - Make-Up Feed - Ceiling Mount		18.0d	21-Oct-27	15-Nov-27	233.0d
10311	BG-AP9-MDF5A-30	Layout & Install Conveyor - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	3.0d	21-Oct-27	25-Oct-27	230.0d
10312	BG-AP9-MDF5A-40	Install Catwalk - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	5.0d	26-Oct-27	1-Nov-27	230.0d
10313	BG-AP9-MDF5A-50	Conveyor Detailing - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	5.0d	2-Nov-27	8-Nov-27	230.0d
10314	BG-AP9-MDF5A-60	Elec. & Controls Rough-In - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	3.0d	9-Nov-27	11-Nov-27	230.0d
10315	BG-AP9-MDF5A-70	Internal Mech. Statics - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	1.0d	12-Nov-27	12-Nov-27	233.0d
10316	BG-AP9-MDF5A-80	Owner Mech. Statics - MDF5A-01 - MDF5A-04 - Ceiling Mount - AP9	1.0d	15-Nov-27	15-Nov-27	233.0d
10317	WBS - MDF5A-05 - Make-Up Feed - Floor Mount		10.0d	26-Oct-27	8-Nov-27	238.0d
10318	BG-AP9-MDF5A-100	Layout & Install Conveyor - MDF5A-05 - Floor Mounted - AP9	2.0d	26-Oct-27	27-Oct-27	238.0d
10319	BG-AP9-MDF5A-110	Conveyor Detailing - MDF5A-05 - Floor Mounted - AP9	2.0d	28-Oct-27	29-Oct-27	238.0d
10320	BG-AP9-MDF5A-120	Elec. & Controls Rough-In - MDF5A-05 - Floor Mounted - AP9	2.0d	1-Nov-27	2-Nov-27	238.0d
10321	BG-AP9-MDF5A-130	Install Decking & Shrouding - MDF5A-05 - Floor Mounted - AP9	2.0d	3-Nov-27	4-Nov-27	238.0d
10322	BG-AP9-MDF5A-140	Internal Mech. Statics - MDF5A-05 - Floor Mounted - AP9	1.0d	5-Nov-27	5-Nov-27	238.0d
10323	BG-AP9-MDF5A-150	Owner Mech. Statics - MDF5A-05 - Floor Mounted - AP9	1.0d	8-Nov-27	8-Nov-27	238.0d
10324	WBS - MDF5B - Make-Up Feed - Apron 9		18.0d	26-Oct-27	18-Nov-27	230.0d
10325	WBS - MDF5B-01 - MDF5B-04 - Make-Up Feed - Ceiling Mount - Apron 9		18.0d	26-Oct-27	18-Nov-27	230.0d
10326	BG-AP9-MDF5B-30	Layout & Install Conveyor - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	3.0d	26-Oct-27	28-Oct-27	230.0d
10327	BG-AP9-MDF5B-40	Install Catwalk - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	5.0d	29-Oct-27	4-Nov-27	230.0d
10328	BG-AP9-MDF5B-50	Conveyor Detailing - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	5.0d	5-Nov-27	11-Nov-27	230.0d
10329	BG-AP9-MDF5B-60	Elec. & Controls Rough-In - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	3.0d	12-Nov-27	16-Nov-27	230.0d
10330	BG-AP9-MDF5B-70	Internal Mech. Statics - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	1.0d	17-Nov-27	17-Nov-27	230.0d
10331	BG-AP9-MDF5B-80	Owner Mech. Statics - MDF5B-01 - MDF5B-04 - Ceiling Mount - AP9	1.0d	18-Nov-27	18-Nov-27	230.0d
10332	WBS - MDF5B-05 - Make-Up Feed - Floor Mount - Apron 9		10.0d	29-Oct-27	11-Nov-27	235.0d

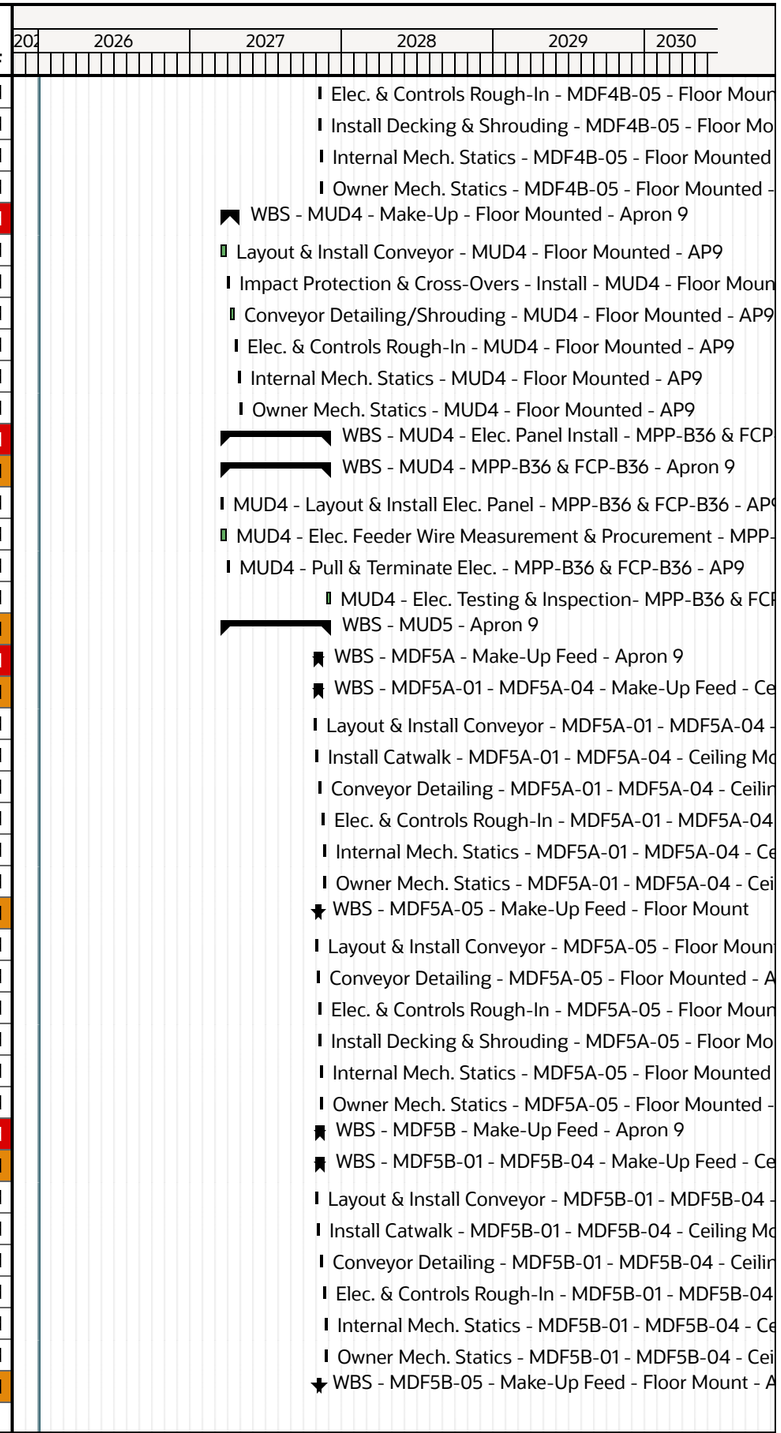


ID	Name	Dur	Start	Finish	TF
10333	BG-AP9-MDF5B-100	Layout & Install Conveyor - MDF5B-05 - AP9	2.0d	29-Oct-27	1-Nov-27	235.0d
10334	BG-AP9-MDF5B-110	Conveyor Detailing - MDF5B-05 - Floor Mount - AP9	2.0d	2-Nov-27	3-Nov-27	235.0d
10335	BG-AP9-MDF5B-120	Elec. & Controls Rough-In - MDF5B-05 - Floor Mount - AP9	2.0d	4-Nov-27	5-Nov-27	235.0d
10336	BG-AP9-MDF5B-130	Install Decking & Shrouding - MDF5B-05 - Floor Mount - AP9	2.0d	8-Nov-27	9-Nov-27	235.0d
10337	BG-AP9-MDF5B-140	Internal Mech. Statics - MDF5B-05 - Floor Mount - AP9	1.0d	10-Nov-27	10-Nov-27	235.0d
10338	BG-AP9-MDF5B-150	Owner Mech. Statics - MDF5B-05 - Floor Mount - AP9	1.0d	11-Nov-27	11-Nov-27	235.0d
10339	WBS - MUD5 - Make-Up - Floor Mounted - Apron 9		33.0d	14-Apr-27	28-May-27	351.0d
10340	BG-AP9-MUD5-10	Layout & Install Conveyor ation - MUD5 - Floor Mount - AP9	10.0d	14-Apr-27	27-Apr-27	351.0d
10341	BG-AP9-MUD5-20	Impact Protection & Cross-Overs - Install - MUD5 - Floor Mount - AP9	5.0d	28-Apr-27	4-May-27	351.0d
10342	BG-AP9-MUD5-30	Conveyor Detailing/Shrouding - MUD5 - Floor Mount - AP9	9.0d	5-May-27	17-May-27	351.0d
10343	BG-AP9-MUD5-40	Elec. & Controls Rough-In - MUD5 - Floor Mount - AP9	7.0d	18-May-27	26-May-27	351.0d
10344	BG-AP9-MUD5-50	Internal Mech. Statics - MUD5 - Floor Mount - AP9	1.0d	27-May-27	27-May-27	351.0d
10345	BG-AP9-MUD5-60	Owner Mech. Statics - MUD5 - Floor Mount - AP9	1.0d	28-May-27	28-May-27	351.0d
10346	WBS - MUD5 - Elec. Panel Install - MPP-A37 & FCP-A37 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10347	WBS - MUD5 - MPP-A37 & FCP-A37 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10348	BG-AP9-MUD5-MPP-10	MUD5 - Layout & Install Elec. Panel - MPP-A37 & FCP-A37 - AP9	2.0d	9-Mar-27	10-Mar-27	375.0d
10349	BG-AP9-MUD5-MPP-20	MUD5 - Elec. Feeder Wire Measurement & Procurement - MPP-A37 & FCP-A37...	10.0d	11-Mar-27	24-Mar-27	750.0d
10350	BG-AP9-MUD5-MPP-30	MUD5 - Pull & Terminate Elec. - MPP-A37 & FCP-A37 - AP9	5.0d	25-Mar-27	31-Mar-27	750.0d
10351	BG-AP9-MUD5-MPP-40	MUD5 - Elec. Testing & Inspection- MPP-A37 & FCP-A37 - AP9	5.0d	23-Nov-27	1-Dec-27	585.0d
10352	WBS - MUD6 - Apron 9		211.0d	9-Mar-27	6-Jan-28	562.0d
10353	WBS - MDF6A - Make-Up Feed - Apron 9		26.0d	26-Oct-27	2-Dec-27	546.0d
10354	WBS - MDF6A-01 - MDF6A-04 - Make-Up Feed - Ceiling Mounted - Apron 9		18.0d	26-Oct-27	18-Nov-27	554.0d
10355	BG-AP9-MDF6A-30	Layout & Install Conveyor - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	3.0d	26-Oct-27	28-Oct-27	522.0d
10356	BG-AP9-MDF6A-40	Install Catwalk - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	5.0d	29-Oct-27	4-Nov-27	525.0d
10357	BG-AP9-MDF6A-50	Conveyor Detailing - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	5.0d	5-Nov-27	11-Nov-27	525.0d
10358	BG-AP9-MDF6A-60	Elec. & Controls Rough-In - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	3.0d	12-Nov-27	16-Nov-27	550.0d
10359	BG-AP9-MDF6A-70	Internal Mech. Statics - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	1.0d	17-Nov-27	17-Nov-27	553.0d
10360	BG-AP9-MDF6A-80	Owner Mech. Statics - MDF6A-01 - MDF6A-04 - Ceiling Mounted - AP9	1.0d	18-Nov-27	18-Nov-27	553.0d
10361	WBS - MDF6A-05 - Make-up Feed - Floor Mounted - Apron 9		10.0d	17-Nov-27	2-Dec-27	542.0d
10362	BG-AP9-MDF6A-100	Layout & Install Conveyor - MDF6A-05 - Floor Mounted - AP9	2.0d	17-Nov-27	18-Nov-27	541.0d
10363	BG-AP9-MDF6A-110	Conveyor Detailing - MDF6A-05 - Floor Mounted - AP9	2.0d	19-Nov-27	22-Nov-27	541.0d
10364	BG-AP9-MDF6A-120	Elec. & Controls Rough-In - MDF6A-05 - Floor Mounted - AP9	2.0d	23-Nov-27	24-Nov-27	541.0d
10365	BG-AP9-MDF6A-130	Install Decking & Shrouding - MDF6A-05 - Floor Mounted - AP9	2.0d	29-Nov-27	30-Nov-27	541.0d
10366	BG-AP9-MDF6A-140	Internal Mech. Statics - MDF6A-05 - Floor Mounted - AP9	1.0d	1-Dec-27	1-Dec-27	541.0d
10367	BG-AP9-MDF6A-150	Owner Mech. Statics - MDF6A-05 - Floor Mounted - AP9	1.0d	2-Dec-27	2-Dec-27	541.0d
10368	WBS - MDF6B - Make-Up Feed - Apron 9		23.0d	29-Oct-27	2-Dec-27	546.0d
10369	WBS - MDF6B-01 - MDF6B-04 - Ceiling Mounted - Apron 9		18.0d	29-Oct-27	23-Nov-27	551.0d
10370	BG-AP9-MDF6B-30	Install Conveyor - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	3.0d	29-Oct-27	2-Nov-27	522.0d
10371	BG-AP9-MDF6B-40	Install Catwalk - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	5.0d	3-Nov-27	9-Nov-27	522.0d
10372	BG-AP9-MDF6B-50	Conveyor Detailing - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	5.0d	10-Nov-27	16-Nov-27	522.0d
10373	BG-AP9-MDF6B-60	Elec. & Controls Rough-In - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	3.0d	17-Nov-27	19-Nov-27	550.0d
10374	BG-AP9-MDF6B-70	Internal Mech. Statics - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	1.0d	22-Nov-27	22-Nov-27	550.0d

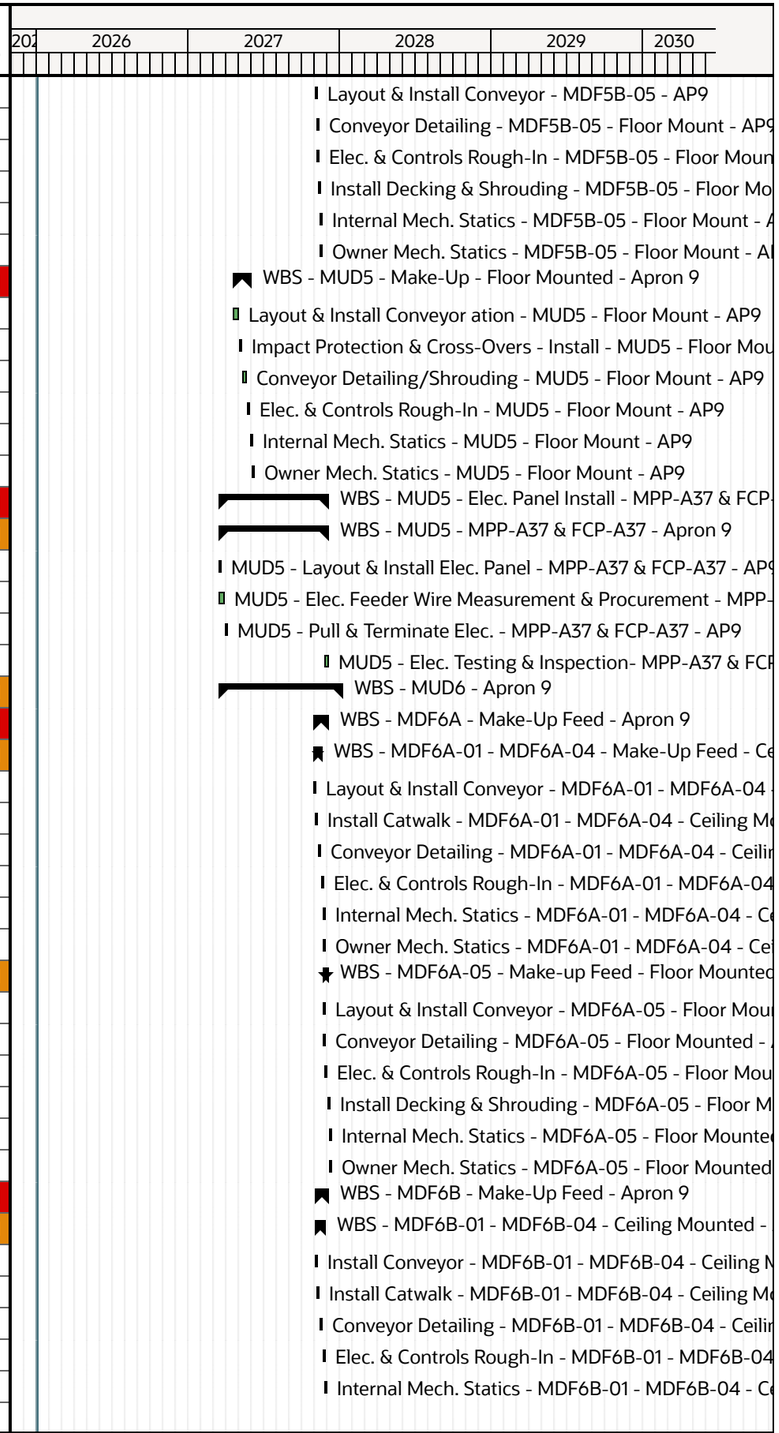


	ID	Name	Dur	Start	Finish	TF
10375	BG-AP9-MDF6B-80	Owner Mech. Statics - MDF6B-01 - MDF6B-04 - Ceiling Mounted - AP9	1.0d	23-Nov-27	23-Nov-27	550.0d
10376	WBS - MDF6B-05 - Floor Mounted - Apron 9		10.0d	17-Nov-27	2-Dec-27	542.0d
10377	BG-AP9-MDF6B-100	Layout & Install Conveyor - MDF6B-05 - Floor Mounted - AP9	2.0d	17-Nov-27	18-Nov-27	541.0d
10378	BG-AP9-MDF6B-110	Conveyor Detailing - MDF6B-05 - Floor Mounted - AP9	2.0d	19-Nov-27	22-Nov-27	541.0d
10379	BG-AP9-MDF6B-120	Elec. & Controls Rough-In - MDF6B-05 - Floor Mounted - AP9	2.0d	23-Nov-27	24-Nov-27	541.0d
10380	BG-AP9-MDF6B-130	Install Decking & Shrouding - MDF6B-05 - Floor Mounted - AP9	2.0d	29-Nov-27	30-Nov-27	541.0d
10381	BG-AP9-MDF6B-140	Internal Mech. Statics - MDF6B-05 - Floor Mounted - AP9	1.0d	1-Dec-27	1-Dec-27	541.0d
10382	BG-AP9-MDF6B-150	Owner Mech. Statics - MDF6B-05 - Floor Mounted - AP9	1.0d	2-Dec-27	2-Dec-27	541.0d
10383	WBS - MUD6 - Make-Up Feed - Apron 9		33.0d	17-Nov-27	6-Jan-28	523.0d
10384	BG-AP9-MUD6-10	Layout & Install Conveyor - MUD6 - Floor Mount - AP9	10.0d	17-Nov-27	2-Dec-27	522.0d
10385	BG-AP9-MUD6-20	Impact Protection & Cross-Overs - Install - MUD6 - Floor Mount - AP9	5.0d	3-Dec-27	9-Dec-27	522.0d
10386	BG-AP9-MUD6-30	Conveyor Detailing/Shrouding - MUD6 - Floor Mount - AP9	9.0d	10-Dec-27	22-Dec-27	522.0d
10387	BG-AP9-MUD6-40	Elec. & Controls Rough-In - MUD6 - Floor Mount - AP9	7.0d	23-Dec-27	4-Jan-28	522.0d
10388	BG-AP9-MUD6-50	Internal Mech. Statics - MUD6 - Floor Mount - AP9	1.0d	5-Jan-28	5-Jan-28	522.0d
10389	BG-AP9-MUD6-60	Owner Mech. Statics - MUD6 - Floor Mount - AP9	1.0d	6-Jan-28	6-Jan-28	522.0d
10390	WBS - MUD6 - Elec. Panel Install - MPP-B37 & FCP-B37 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10391	WBS - MUD6 - MPP-B37 & FCP-B37 - Apron 9		187.0d	9-Mar-27	1-Dec-27	586.0d
10392	BG-AP9-MUD6-MPP-10	MUD6 - Layout & Install Elec. Panel - MPP-B37 & FCP-B37 - AP9	2.0d	9-Mar-27	10-Mar-27	698.0d
10393	BG-AP9-MUD6-MPP-20	MUD6 - Elec. Feeder Wire Measurement & Procurement - MPP-B37 & FCP-B37...	10.0d	11-Mar-27	24-Mar-27	750.0d
10394	BG-AP9-MUD6-MPP-30	MUD6 - Pull & Terminate Elec. - MPP-B37 & FCP-B37 - AP9	5.0d	25-Mar-27	31-Mar-27	750.0d
10395	BG-AP9-MUD6-MPP-40	MUD6 - Elec. Testing & Inspection- MPP-B37 & FCP-B37 - AP9	5.0d	23-Nov-27	1-Dec-27	585.0d
10396	WBS - ASD - Baggage Handling Systems - (BHS) - Section K		49.0d	25-Nov-26	5-Feb-27	431.0d
10397	WBS - TD1 & TD2 - Section K		49.0d	25-Nov-26	5-Feb-27	431.0d
10398	WBS - TD1-39 - TD1-43 - Section K		41.0d	25-Nov-26	26-Jan-27	439.0d
10399	BG-SCK-TD1-10	Layout & Install BHS Hanger & Header Steel - TD1-39 - TD1-43 - Ceiling Mounted - Section K	10.0d	25-Nov-26	10-Dec-26	383.0d
10400	BG-SCK-TD1-20	Header Steel Inspection - TD1-39 - TD1-43 - Ceiling Mounted - Section K	1.0d	11-Dec-26	11-Dec-26	383.0d
10401	BG-SCK-TD1-30	Install Conveyor - TD1-39 - TD1-43 - Ceiling Mounted - Section K	10.0d	14-Dec-26	28-Dec-26	383.0d
10402	BG-SCK-TD1-40	Install Catwalk - TD1-39 - TD1-43 - Ceiling Mounted - Section K	8.0d	23-Dec-26	5-Jan-27	383.0d
10403	BG-SCK-TD1-50	Conveyor Detailing - TD1-39 - TD1-43 - Ceiling Mounted - Section K	4.0d	6-Jan-27	11-Jan-27	383.0d
10404	BG-SCK-TD1-60	Elec. & Controls Rough-in - TD1-39 - TD1-43 - Ceiling Mounted - Section K	8.0d	12-Jan-27	21-Jan-27	434.0d
10405	BG-SCK-TD1-70	Internal Mech. Statics - TD1-39 - TD1-43 - Ceiling Mounted - Section K	2.0d	22-Jan-27	25-Jan-27	439.0d
10406	BG-SCK-TD1-80	Owner Mech. Statics - TD1-39 - TD1-43 - Ceiling Mounted - Section K	1.0d	26-Jan-27	26-Jan-27	439.0d
10407	WBS - TD2-38 - TD2-42 - Section K		39.0d	11-Dec-26	5-Feb-27	431.0d
10408	BG-SCK-TD2-10	Layout & Install BHS Hangers & Header Steel - TD2-38 - TD2-42 - Ceiling Mounted - Section K	10.0d	11-Dec-26	24-Dec-26	431.0d
10409	BG-SCK-TD2-20	Header Steel Inspection - TD2-38 - TD2-42 - Ceiling Mounted - Section K	1.0d	28-Dec-26	28-Dec-26	431.0d
10410	BG-SCK-TD2-30	Install Conveyor - TD2-38 - TD2-42 - Ceiling Mounted - Section K	8.0d	29-Dec-26	8-Jan-27	431.0d
10411	BG-SCK-TD2-40	Install Catwalk TD2-38 - TD2-42 - Ceiling Mounted - Section K	8.0d	11-Jan-27	20-Jan-27	431.0d
10412	BG-SCK-TD2-50	Conveyor Detailing - TD2-38 - TD2-42 - Ceiling Mounted - Section K	4.0d	21-Jan-27	26-Jan-27	431.0d
10413	BG-SCK-TD2-60	Elec. & Controls Rough-In -TD2-38 - TD2-42 - Ceiling Mounted - Section K	5.0d	27-Jan-27	2-Feb-27	431.0d
10414	BG-SCK-TD2-70	Internal Mech. Statics - TD2-38 - TD2-42 - Ceiling Mounted - Section K	2.0d	3-Feb-27	4-Feb-27	431.0d
10415	BG-SCK-TD2-80	Owner Mech. Statics - TD2-38 - TD2-42 - Ceiling Mounted - Section K	1.0d	5-Feb-27	5-Feb-27	431.0d
10416	WBS - ASD - Baggage Handling Systems - (BHS) - Section L		86.0d	18-Nov-26	23-Mar-27	399.0d

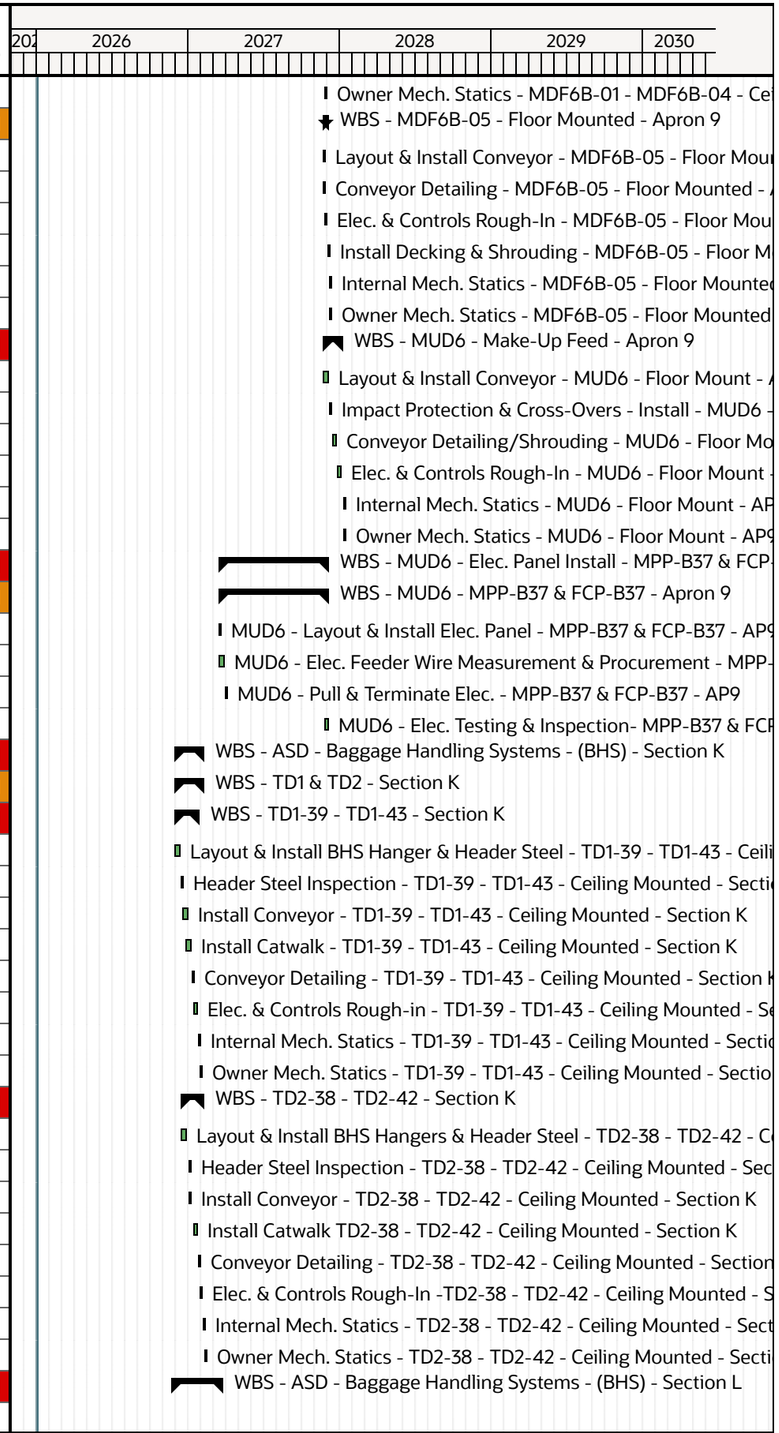


ID	Name	Dur	Start	Finish	TF
10417	WBS - TD1 & TD2 - Section L	86.0d	18-Nov-26	23-Mar-27	399.0d
10418	WBS - TD1-34 - TD1-38 - Section L	66.0d	18-Nov-26	23-Feb-27	419.0d
10419	BG-SCL-TD1-10	Layout & Install BHS Hangers & Header Steel - TD1-34 - TD1-38 - Ceiling Mou...	10.0d	18-Nov-26	3-Dec-26	407.0d
10420	BG-SCL-TD1-20	Header Steel Inspection - TD1-34 - TD1-38 - Ceiling Mounted - Section L	1.0d	4-Dec-26	4-Dec-26	407.0d
10421	BG-SCL-TD1-30	Install Conveyor - TD1-34 - TD1-38 - Ceiling Mounted - Section L	8.0d	12-Jan-27	21-Jan-27	383.0d
10422	BG-SCL-TD1-40	Install Catwalk - TD1-34 - TD1-38 - Ceiling Mounted - Section L	8.0d	22-Jan-27	2-Feb-27	383.0d
10423	BG-SCL-TD1-50	Conveyor Detailing - TD1-34 - TD1-38 - Ceiling Mounted - Section L	4.0d	3-Feb-27	8-Feb-27	383.0d
10424	BG-SCL-TD1-60	Elec. & Controls Rough-In - TD1-34 - TD1-38 - Ceiling Mounted - Section L	8.0d	9-Feb-27	18-Feb-27	419.0d
10425	BG-SCL-TD1-70	Internal Mech. Statics - TD1-34 - TD1-38 - Ceiling Mounted - Section L	2.0d	19-Feb-27	22-Feb-27	419.0d
10426	BG-SCL-TD1-80	Owner Mech. Statics - TD1-34 - TD1-38 - Ceiling Mounted - Section L	1.0d	23-Feb-27	23-Feb-27	419.0d
10427	WBS - TD2-33 - TD2-37 - Section L	76.0d	4-Dec-26	23-Mar-27	399.0d
10428	BG-SCL-TD2-10	Layout & Install BHS Hanger & Header Steel - TD2-33 - TD2-37 - Ceiling Moun...	10.0d	4-Dec-26	17-Dec-26	433.0d
10429	BG-SCL-TD2-20	Header Steel Inspection - TD2-33 - TD2-37 - Ceiling Mounted - Section L	1.0d	18-Dec-26	18-Dec-26	433.0d
10430	BG-SCL-TD2-30	Install Conveyor - TD2-33 - TD2-37 - Ceiling Mounted - Section L	8.0d	9-Feb-27	18-Feb-27	399.0d
10431	BG-SCL-TD2-40	Install Catwalk - TD2-33 - TD2-37 - Ceiling Mounted - Section L	8.0d	19-Feb-27	2-Mar-27	399.0d
10432	BG-SCL-TD2-50	Conveyor Detailing - TD2-33 - TD2-37 - Ceiling Mounted - Section L	4.0d	3-Mar-27	8-Mar-27	399.0d
10433	BG-SCL-TD2-60	Elec. & Controls Rough-In - TD2-33 - TD2-37 - Ceiling Mounted - Section L	8.0d	9-Mar-27	18-Mar-27	399.0d
10434	BG-SCL-TD2-70	Internal Mech. Statics - TD2-33 - TD2-37 - Ceiling Mounted - Section L	2.0d	19-Mar-27	22-Mar-27	399.0d
10435	BG-SCL-TD2-80	Owner Mech. Statics - TD2-33 - TD2-37 - Ceiling Mounted - Section L	1.0d	23-Mar-27	23-Mar-27	399.0d
10436	WBS - ASD - Baggage Handling Systems - (BHS) - Section M	322.0d	25-Aug-26	1-Dec-27	586.0d
10437	WBS - TD1 & TD2 - Section M	322.0d	25-Aug-26	1-Dec-27	586.0d
10438	WBS - TD1-31 - TD1-33 - Section M	88.0d	11-Nov-26	18-Mar-27	402.0d
10439	BG-SCM-TD1-10	Layout & Install BHS Hangers & Header Steel - TD1-31 - TD1-33 - Ceiling Mou...	10.0d	11-Nov-26	24-Nov-26	432.0d
10440	BG-SCM-TD1-20	Header Steel Inspection - TD1-31 - TD1-33 - Ceiling Mounted - Section M	1.0d	25-Nov-26	25-Nov-26	432.0d
10441	BG-SCM-TD1-30	Install Conveyor - TD1-31 - TD1-33 - Ceiling Mounted - Section M	8.0d	9-Feb-27	18-Feb-27	383.0d
10442	BG-SCM-TD1-40	Install Catwalk - TD1-31 - TD1-33 - Ceiling Mounted - Section M	8.0d	19-Feb-27	2-Mar-27	383.0d
10443	BG-SCM-TD1-50	Conveyor Detailing - TD1-31 - TD1-33 - Ceiling Mounted - Section M	3.0d	3-Mar-27	5-Mar-27	383.0d
10444	BG-SCM-TD1-60	Elec. & Controls Rough-In - TD1-31 - TD1-33 - Ceiling Mounted - Section M	6.0d	8-Mar-27	15-Mar-27	402.0d
10445	BG-SCM-TD1-70	Internal Mech. Statics - TD1-31 - TD1-33 - Ceiling Mounted - Section M	2.0d	16-Mar-27	17-Mar-27	402.0d
10446	BG-SCM-TD1-80	Owner Mech. Statics - TD1-31 - TD1-33 - Ceiling Mounted - Section M	1.0d	18-Mar-27	18-Mar-27	402.0d
10447	WBS - TD2-30 - TD2-32 - Section M	97.0d	25-Nov-26	14-Apr-27	383.0d
10448	BG-SCM-TD2-10	Layout & Install BHS Hangers & Header Steel - TD2-30 - TD2-32 - Ceiling Mou...	10.0d	25-Nov-26	10-Dec-26	441.0d
10449	BG-SCM-TD2-20	Header Steel Inspection - TD2-30 - TD2-32 - Ceiling Mounted - Section M	1.0d	11-Dec-26	11-Dec-26	441.0d
10450	BG-SCM-TD2-30	Install Conveyor - TD2-30 - TD2-32 - Ceiling Mounted - Section M	8.0d	8-Mar-27	17-Mar-27	383.0d
10451	BG-SCM-TD2-40	Install Catwalk - TD2-30 - TD2-32 - Ceiling Mounted - Section M	8.0d	18-Mar-27	29-Mar-27	383.0d
10452	BG-SCM-TD2-50	Conveyor Detailing -TD2-30 - TD2-32 - Ceiling Mounted - Section M	3.0d	30-Mar-27	1-Apr-27	383.0d
10453	BG-SCM-TD2-60	Elec. & Controls Rough-In -TD2-30 - TD2-32 - Ceiling Mounted - Section M	6.0d	2-Apr-27	9-Apr-27	383.0d
10454	BG-SCM-TD2-70	Internal Mech. Statics - TD2-30 - TD2-32 - Ceiling Mounted - Section M	2.0d	12-Apr-27	13-Apr-27	383.0d
10455	BG-SCM-TD2-80	Owner Mech. Statics - TD2-30 - TD2-32 - Ceiling Mounted - Section M	1.0d	14-Apr-27	14-Apr-27	383.0d
10456	WBS - TD1 & TD2 - Elec. Panel Install - Section L & M	322.0d	25-Aug-26	1-Dec-27	586.0d
10457	BG-TD1&2-MPP-10	TD1 & TD2 - Layout Elec. Panel - MPP-A20 & MPP-B20 - Section M	1.0d	25-Aug-26	25-Aug-26	879.0d
10458	BG-TD1&2-MPP-20	TD1 & TD2 - Install Elec. Panel MPP-A20 & MPP-B20 - Section M	2.0d	26-Aug-26	27-Aug-26	879.0d

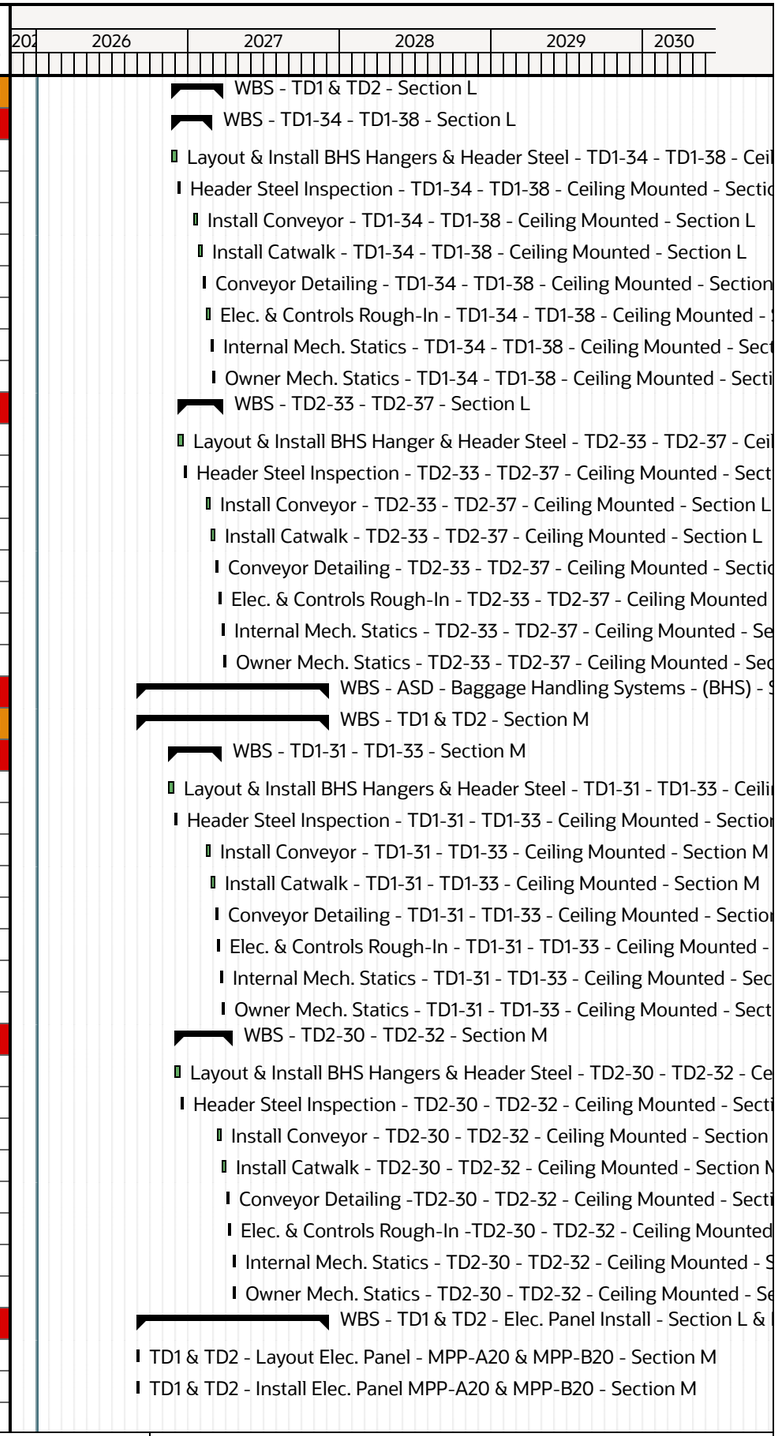


ID	Name	Dur	Start	Finish	TF
10459	BG-TD1&2-MPP-30	TD1 & TD2 - Elec. Feeder Wire Measurement & Procurement - MPP-A20 & MP...	10.0d	28-Aug-26	11-Sep-26	879.0d
10460	BG-TD1&2-MPP-40	TD1 & TD2 - Pull & Terminate Elec. - MPP-A20 & MPP-B20 - Section M	10.0d	14-Sep-26	25-Sep-26	879.0d
10461	BG-TD1&2-MPP-50	TD1 & TD2 - Elec. Testing & Inspection- MPP-A20 & MPP-B20 - Section M	5.0d	23-Nov-27	1-Dec-27	585.0d
10462	WBS - ASD - BHS Commissioning &Testing		242.0d	27-Jan-28	10-Jan-29	275.0d
10463	COM-BHS-10	BHS System Start Up Complete - Overall BHS Commissioning & Testing	0.0d		27-Jan-28	199.0d
10464	COM-BHS-20	BHS System Static Insp.s - Overall BHS Commissioning & Testing	15.0d	7-Sep-28	27-Sep-28	28.0d
10465	COM-BHS-30	BHS System Dynamic Insp.s - Overall BHS Commissioning & Testing	20.0d	28-Sep-28	25-Oct-28	28.0d
10466	COM-BHS-40	BHS System Load Testing - Overall BHS Commissioning & Testing	10.0d	26-Oct-28	8-Nov-28	28.0d
10467	COM-BHS-50	BHS System Functional Testing - Overall BHS Commissioning & Testing	20.0d	9-Nov-28	8-Dec-28	28.0d
10468	COM-BHS-60	BHS System Operational - Overall BHS Commissioning & Testing	0.0d		8-Dec-28	28.0d
10469	COM-BHS-70	BHS System Run-in - Overall BHS Commissioning & Testing	20.0d	11-Dec-28	9-Jan-29	28.0d
10470	WBS - Inbound		6.0d	4-Oct-28	11-Oct-28	336.0d
10471	A102220	Owner Witnessed Testing - Inbound	6.0d	4-Oct-28	11-Oct-28	335.0d
10472	WBS - Sortation		21.0d	11-Dec-28	10-Jan-29	275.0d
10473	A102150	Learn Tracking Sectors - Sortation Testing	2.0d	11-Dec-28	12-Dec-28	274.0d
10474	A102160	Merge / Diverter Set-Up - Sortation Testing	3.0d	13-Dec-28	15-Dec-28	274.0d
10475	A102170	Internal Manual Encode - Sortation Testing	5.0d	18-Dec-28	22-Dec-28	274.0d
10476	A102180	ATR Internal Sort Testing - Sortation Testing	5.0d	26-Dec-28	2-Jan-29	274.0d
10477	A102190	Owner Witnessed Merge - Sortation Testing	2.0d	3-Jan-29	4-Jan-29	274.0d
10478	A102200	Owner Manuel Encode - Sortation Testing	2.0d	5-Jan-29	8-Jan-29	274.0d
10479	A102210	Owner Witnessed ATR Sort Testing - Sortation Testing	2.0d	9-Jan-29	10-Jan-29	274.0d
10480	WBS - ASD - BHS Electrical		445.0d	6-Jan-27	3-Oct-28	340.0d
10481	WBS - MPP / CSC A20 (TD1 34/36)		60.0d	22-Jan-27	15-Apr-27	709.0d
10482	A104010	Elec. Homeruns / Cable Tray - MPP / CSC A20	5.0d	22-Jan-27	28-Jan-27	747.0d
10483	A104020	Wire Pull - MPP / CSC A20	5.0d	29-Jan-27	4-Feb-27	747.0d
10484	A104110	Primary Wire Pull & Coiled-Up to MPP (By Others) - MPP / CSC A20	0.0d		4-Feb-27	754.0d
10485	A104030	Terminate Wire at CSC - MPP / CSC A20	5.0d	5-Feb-27	11-Feb-27	747.0d
10486	A104040	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A20	5.0d	5-Feb-27	11-Feb-27	747.0d
10487	A104050	Internal Elec. Statics - MPP / CSC A20	1.0d	12-Feb-27	12-Feb-27	747.0d
10488	A104060	Owner Elec. Statics - MPP / CSC A20	1.0d	15-Feb-27	15-Feb-27	747.0d
10489	A104070	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A20	1.0d	16-Feb-27	16-Feb-27	747.0d
10490	A104080	Mech. Dynamic Testing - MPP / CSC A20	1.0d	17-Feb-27	17-Feb-27	747.0d
10491	A104090	I/O & Functional Testing - MPP / CSC A20	1.0d	14-Apr-27	14-Apr-27	708.0d
10492	A104100	Owner Functional Testing - MPP / CSC A20	1.0d	15-Apr-27	15-Apr-27	708.0d
10493	WBS - MPP / CSC B20 (TD2 32/34)		32.0d	3-Mar-27	15-Apr-27	709.0d
10494	A102250	Elec. Homeruns / Cable Tray - MPP / CSC B20	5.0d	3-Mar-27	9-Mar-27	719.0d
10495	A102260	Wire Pull - MPP / CSC B20	5.0d	10-Mar-27	16-Mar-27	719.0d
10496	A102350	Primary Wire Pull & Coiled-Up to MPP (By Others) - MPP / CSC B20	0.0d		16-Mar-27	726.0d
10497	A102270	Terminate Wire at CSC - MPP / CSC B20	5.0d	17-Mar-27	23-Mar-27	719.0d
10498	A102280	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B20	5.0d	17-Mar-27	23-Mar-27	719.0d
10499	A102290	Internal Elec. Statics - MPP / CSC B20	1.0d	24-Mar-27	24-Mar-27	719.0d
10500	A102300	Owner Elec. Statics - MPP / CSC B20	1.0d	25-Mar-27	25-Mar-27	719.0d

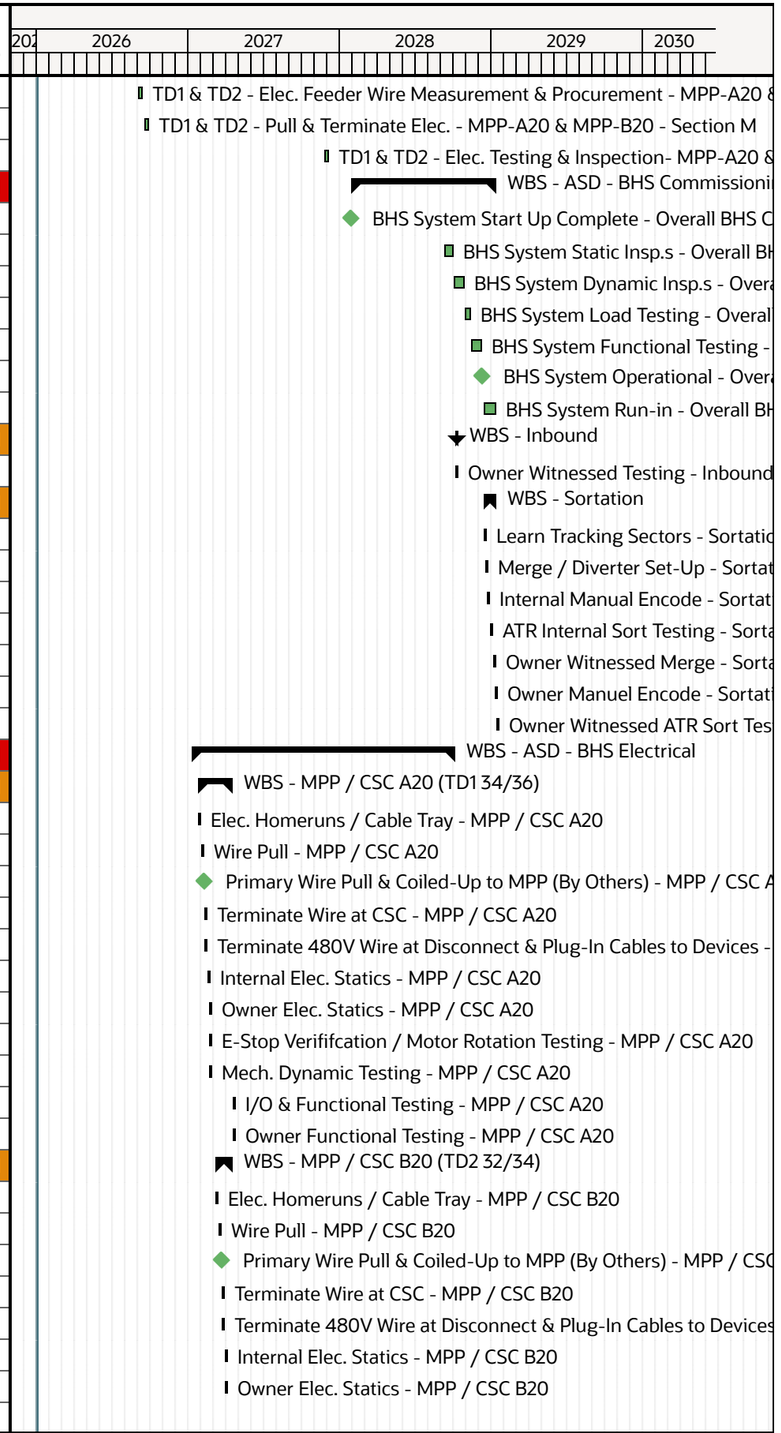


	ID	Name	Dur	Start	Finish	TF
10501	A102310	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B20	1.0d	26-Mar-27	26-Mar-27	719.0d
10502	A102320	Mech. Dynamic Testing - MPP / CSC B20	1.0d	29-Mar-27	29-Mar-27	719.0d
10503	A102330	I/O & Functional Testing - MPP / CSC B20	1.0d	14-Apr-27	14-Apr-27	708.0d
10504	A102340	Owner Functional Testing - MPP / CSC B20	1.0d	15-Apr-27	15-Apr-27	708.0d
10505	WBS - MPP / CSC A30 (TD1 37/52)		158.0d	6-Jan-27	17-Aug-27	623.0d
10506	A102360	Elec. Homeruns / Cable Tray - MPP / CSC A30	7.0d	6-Jan-27	14-Jan-27	750.0d
10507	A102370	Wire Pull - MPP / CSC A30	7.0d	15-Jan-27	25-Jan-27	750.0d
10508	A102380	Terminate Wire at CSC - MPP / CSC A30	7.0d	26-Jan-27	3-Feb-27	750.0d
10509	A102390	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A30	7.0d	26-Jan-27	3-Feb-27	750.0d
10510	A102400	Internal Elec. Statics - MPP / CSC A30	1.0d	4-Feb-27	4-Feb-27	750.0d
10511	A102410	Owner Elec. Statics - MPP / CSC A30	1.0d	5-Feb-27	5-Feb-27	750.0d
10512	A102420	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A30	1.0d	9-Aug-27	9-Aug-27	622.0d
10513	A102430	Mech. Dynamic Testing - MPP / CSC A30	2.0d	10-Aug-27	11-Aug-27	622.0d
10514	A102440	I/O & Functional Testing - MPP / CSC A30	3.0d	12-Aug-27	16-Aug-27	622.0d
10515	A102450	Owner Functional Testing - MPP / CSC A30	1.0d	17-Aug-27	17-Aug-27	622.0d
10516	WBS - MPP / CSC B30 (TD2 35/51)		138.0d	3-Feb-27	17-Aug-27	623.0d
10517	A102470	Elec. Homeruns / Cable Tray - MPP / CSC B30	7.0d	3-Feb-27	11-Feb-27	730.0d
10518	A102480	Wire Pull - MPP / CSC B30	7.0d	12-Feb-27	22-Feb-27	730.0d
10519	A102490	Terminate Wire at CSC - MPP / CSC B30	7.0d	23-Feb-27	3-Mar-27	730.0d
10520	A102500	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B30	7.0d	23-Feb-27	3-Mar-27	730.0d
10521	A102510	Internal Elec. Statics - MPP / CSC B30	1.0d	4-Mar-27	4-Mar-27	730.0d
10522	A102520	Owner Elec. Statics - MPP / CSC B30	1.0d	5-Mar-27	5-Mar-27	730.0d
10523	A102530	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B30	1.0d	9-Aug-27	9-Aug-27	622.0d
10524	A102540	Mech. Dynamic Testing - MPP / CSC B30	2.0d	10-Aug-27	11-Aug-27	622.0d
10525	A102550	I/O & Functional Testing - MPP / CSC B30	3.0d	12-Aug-27	16-Aug-27	622.0d
10526	A102560	Owner Functional Testing - MPP / CSC B30	1.0d	17-Aug-27	17-Aug-27	622.0d
10527	WBS - MPP / CSC A31 (MED1 01/12, TD1 53/74)		31.0d	4-Nov-27	20-Dec-27	537.0d
10528	A102580	Elec. Homeruns / Cable Tray - MPP / CSC A31	7.0d	4-Nov-27	12-Nov-27	536.0d
10529	A102590	Wire Pull - MPP / CSC A31	7.0d	15-Nov-27	23-Nov-27	536.0d
10530	A102600	Terminate Wire at CSC - MPP / CSC A31	7.0d	24-Nov-27	6-Dec-27	536.0d
10531	A102610	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A31	7.0d	24-Nov-27	6-Dec-27	536.0d
10532	A102620	Internal Elec. Statics - MPP / CSC A31	1.0d	7-Dec-27	7-Dec-27	536.0d
10533	A102630	Owner Elec. Statics - MPP / CSC A31	1.0d	8-Dec-27	8-Dec-27	536.0d
10534	A102640	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A31	1.0d	9-Dec-27	9-Dec-27	536.0d
10535	A102650	Mech. Dynamic Testing - MPP / CSC A31	2.0d	10-Dec-27	13-Dec-27	536.0d
10536	A102660	I/O & Functional Testing - MPP / CSC A31	4.0d	14-Dec-27	17-Dec-27	536.0d
10537	A102670	Owner Functional Testing - MPP / CSC A31	1.0d	20-Dec-27	20-Dec-27	536.0d
10538	WBS - MPP / CSC B31 (MED2 01/12, TD2 52/72)		31.0d	4-Nov-27	20-Dec-27	537.0d
10539	A102800	Elec. Homeruns / Cable Tray - MPP / CSC B31	7.0d	4-Nov-27	12-Nov-27	536.0d
10540	A102810	Wire Pull - MPP / CSC B31	7.0d	15-Nov-27	23-Nov-27	536.0d
10541	A102820	Terminate Wire at CSC - MPP / CSC B31	7.0d	24-Nov-27	6-Dec-27	536.0d
10542	A102830	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B31	7.0d	24-Nov-27	6-Dec-27	536.0d

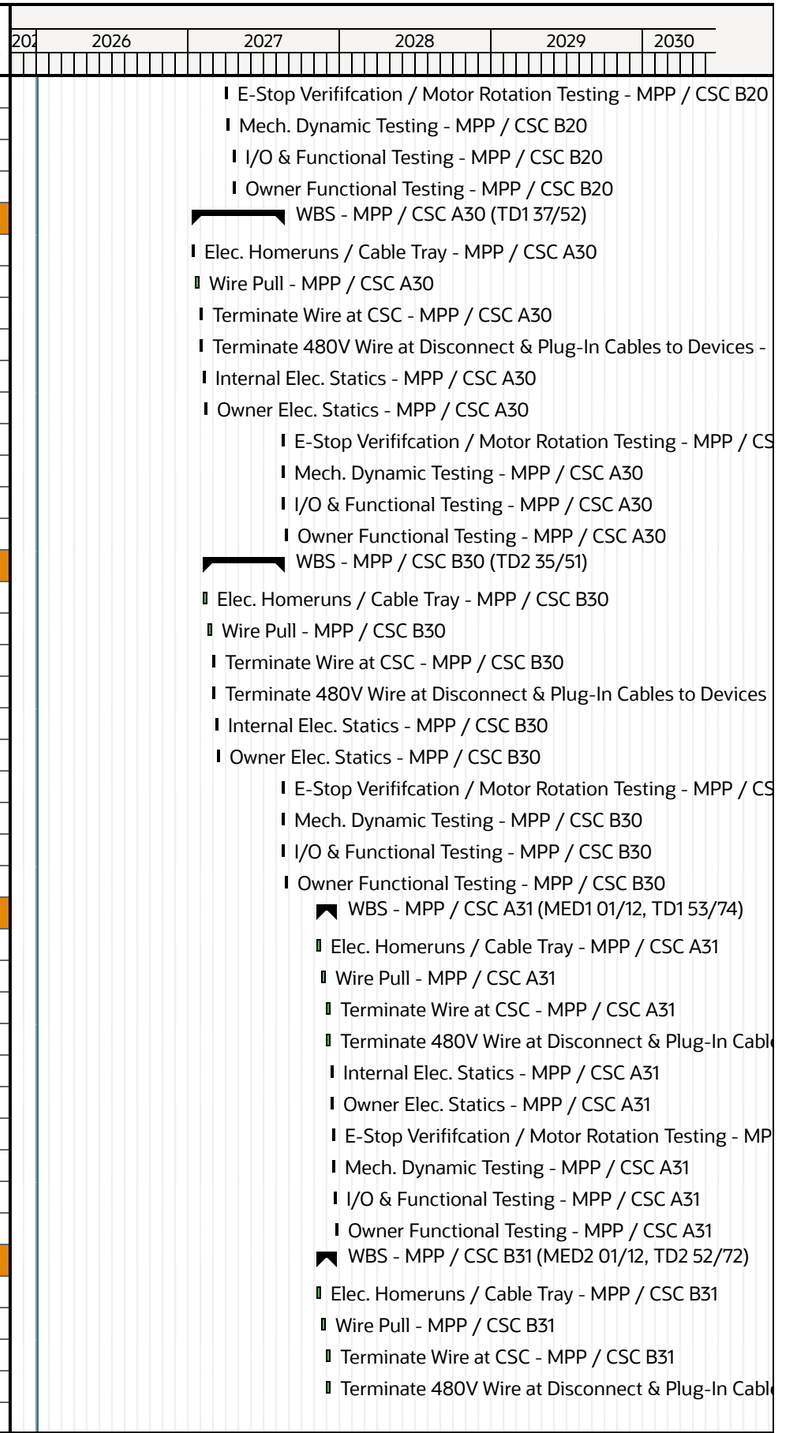


	ID	Name	Dur	Start	Finish	TF
10543	A102840	Internal Elec. Statics - MPP / CSC B31	1.0d	7-Dec-27	7-Dec-27	536.0d
10544	A102850	Owner Elec. Statics - MPP / CSC B31	1.0d	8-Dec-27	8-Dec-27	536.0d
10545	A102860	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B31	1.0d	9-Dec-27	9-Dec-27	536.0d
10546	A102870	Mech. Dynamic Testing - MPP / CSC B31	2.0d	10-Dec-27	13-Dec-27	536.0d
10547	A102880	I/O & Functional Testing - MPP / CSC B31	4.0d	14-Dec-27	17-Dec-27	536.0d
10548	A102890	Owner Functional Testing - MPP / CSC B31	1.0d	20-Dec-27	20-Dec-27	536.0d
10549	WBS - MPP / CSC B32 (RID1 01/16, TD1 75, TD2 73/74)		27.0d	30-Nov-27	7-Jan-28	525.0d
10550	A102690	Elec. Homeruns / Cable Tray - MPP / CSC B32	6.0d	30-Nov-27	7-Dec-27	524.0d
10551	A102700	Wire Pull - MPP / CSC B32	6.0d	8-Dec-27	15-Dec-27	524.0d
10552	A102710	Terminate Wire at CSC - MPP / CSC B32	6.0d	16-Dec-27	23-Dec-27	524.0d
10553	A102720	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B32	6.0d	16-Dec-27	23-Dec-27	524.0d
10554	A102730	Internal Elec. Statics - MPP / CSC B32	1.0d	27-Dec-27	27-Dec-27	524.0d
10555	A102740	Owner Elec. Statics - MPP / CSC B32	1.0d	28-Dec-27	28-Dec-27	524.0d
10556	A102750	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B32	1.0d	29-Dec-27	29-Dec-27	524.0d
10557	A102760	Mech. Dynamic Testing - MPP / CSC B32	2.0d	30-Dec-27	3-Jan-28	524.0d
10558	A102770	I/O & Functional Testing - MPP / CSC B32	3.0d	4-Jan-28	6-Jan-28	524.0d
10559	A102780	Owner Functional Testing - MPP / CSC B32	1.0d	7-Jan-28	7-Jan-28	524.0d
10560	WBS - MPP / CSC A33 (CFD1A 01/09, CFD1B 01/14)		94.0d	3-Aug-27	15-Dec-27	540.0d
10561	A103570	Elec. Homeruns / Cable Tray - MPP / CSC A33	8.0d	3-Aug-27	12-Aug-27	600.0d
10562	A103580	Wire Pull - MPP / CSC A33	8.0d	13-Aug-27	24-Aug-27	600.0d
10563	A103590	Terminate Wire at CSC - MPP / CSC A33	8.0d	25-Aug-27	3-Sep-27	600.0d
10564	A103600	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A33	8.0d	25-Aug-27	3-Sep-27	600.0d
10565	A103610	Internal Elec. Statics - MPP / CSC A33	1.0d	7-Sep-27	7-Sep-27	600.0d
10566	A103620	Owner Elec. Statics - MPP / CSC A33	1.0d	8-Sep-27	8-Sep-27	600.0d
10567	A103630	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A33	1.0d	7-Dec-27	7-Dec-27	539.0d
10568	A103640	Mech. Dynamic Testing - MPP / CSC A33	2.0d	8-Dec-27	9-Dec-27	539.0d
10569	A103650	I/O & Functional Testing - MPP / CSC A33	3.0d	10-Dec-27	14-Dec-27	539.0d
10570	A103660	Owner Functional Testing - MPP / CSC A33	1.0d	15-Dec-27	15-Dec-27	539.0d
10571	WBS - MPP / CSC B33 (CFD2A 01/09, CFD2B 01/14)		108.0d	8-Jul-27	9-Dec-27	544.0d
10572	A103680	Elec. Homeruns / Cable Tray - MPP / CSC B33	8.0d	8-Jul-27	19-Jul-27	618.0d
10573	A103690	Wire Pull - MPP / CSC B33	8.0d	20-Jul-27	29-Jul-27	618.0d
10574	A103700	Terminate Wire at CSC - MPP / CSC B33	8.0d	30-Jul-27	10-Aug-27	618.0d
10575	A103710	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B33	8.0d	30-Jul-27	10-Aug-27	618.0d
10576	A103720	Internal Elec. Statics - MPP / CSC B33	1.0d	11-Aug-27	11-Aug-27	618.0d
10577	A103730	Owner Elec. Statics - MPP / CSC B33	1.0d	12-Aug-27	12-Aug-27	618.0d
10578	A103740	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B33	1.0d	1-Dec-27	1-Dec-27	543.0d
10579	A103750	Mech. Dynamic Testing - MPP / CSC B33	2.0d	2-Dec-27	3-Dec-27	543.0d
10580	A103760	I/O & Functional Testing - MPP / CSC B33	3.0d	6-Dec-27	8-Dec-27	543.0d
10581	A103770	Owner Functional Testing - MPP / CSC B33	1.0d	9-Dec-27	9-Dec-27	543.0d
10582	WBS - MPP / CSC A34 (CFD3A 01/08, CFD3B 01/14, IRD1 01/06)		39.0d	1-Oct-27	24-Nov-27	553.0d
10583	A103790	Elec. Homeruns / Cable Tray - MPP / CSC A34	9.0d	1-Oct-27	13-Oct-27	552.0d
10584	A103800	Wire Pull - MPP / CSC A34	9.0d	14-Oct-27	26-Oct-27	552.0d

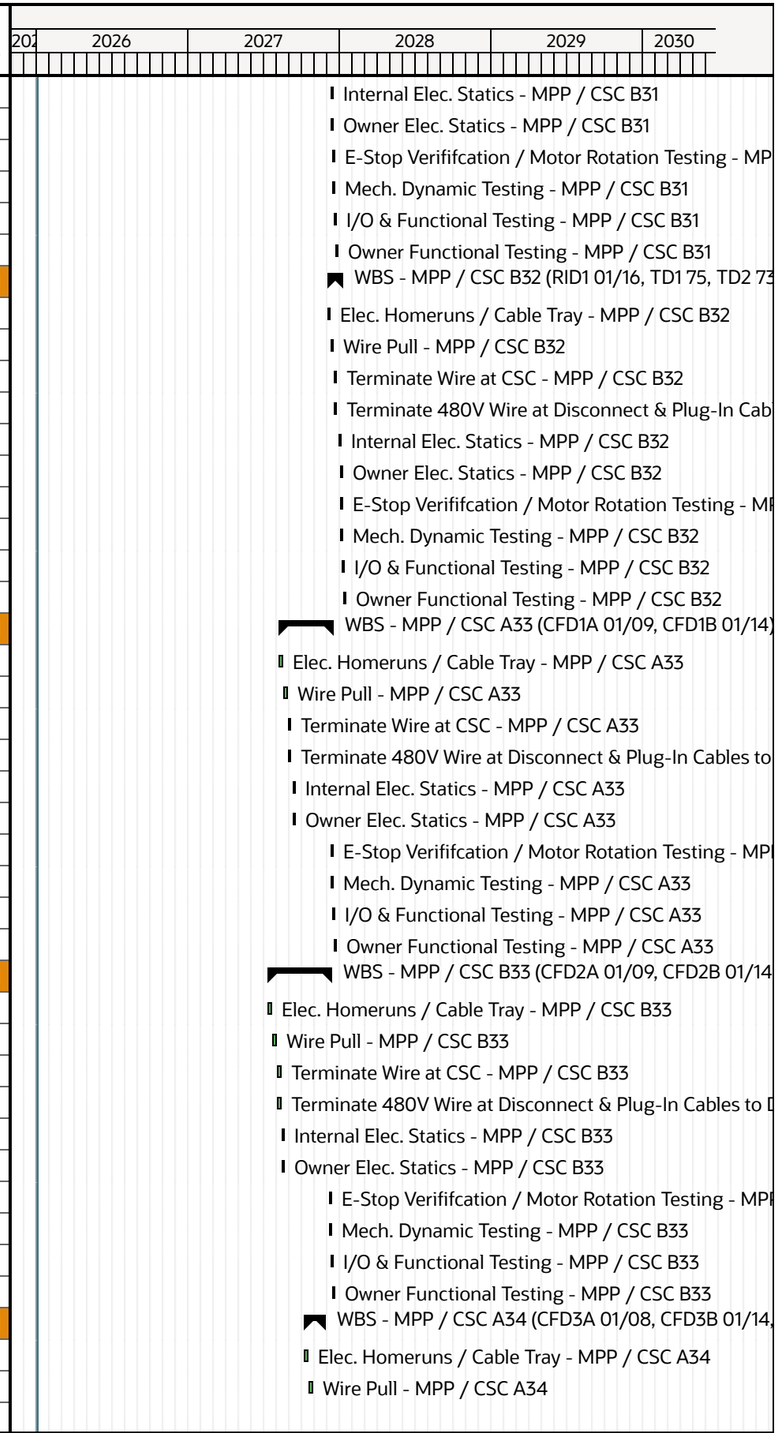


	ID	Name	Dur	Start	Finish	TF
10585	A103810	Terminate Wire at CSC - MPP / CSC A34	9.0d	27-Oct-27	8-Nov-27	552.0d
10586	A103820	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A34	9.0d	27-Oct-27	8-Nov-27	552.0d
10587	A103830	Internal Elec. Statics - MPP / CSC A34	1.0d	9-Nov-27	9-Nov-27	552.0d
10588	A103840	Owner Elec. Statics - MPP / CSC A34	1.0d	10-Nov-27	10-Nov-27	552.0d
10589	A103850	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A34	1.0d	11-Nov-27	11-Nov-27	552.0d
10590	A103860	Mech. Dynamic Testing - MPP / CSC A34	3.0d	12-Nov-27	16-Nov-27	552.0d
10591	A103870	I/O & Functional Testing - MPP / CSC A34	5.0d	17-Nov-27	23-Nov-27	552.0d
10592	A103880	Owner Functional Testing - MPP / CSC A34	1.0d	24-Nov-27	24-Nov-27	552.0d
10593	WBS - MPP / CSC B34 (CFD4A 01/09, CFD4B 01/14, OSD1 01/03)		39.0d	9-Aug-28	3-Oct-28	336.0d
10594	A103900	Elec. Homeruns / Cable Tray - MPP / CSC B34	9.0d	9-Aug-28	21-Aug-28	335.0d
10595	A103910	Wire Pull - MPP / CSC B34	9.0d	22-Aug-28	1-Sep-28	335.0d
10596	A103920	Terminate Wire at CSC - MPP / CSC B34	9.0d	5-Sep-28	15-Sep-28	335.0d
10597	A103930	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B34	9.0d	5-Sep-28	15-Sep-28	335.0d
10598	A103940	Internal Elec. Statics - MPP / CSC B34	1.0d	18-Sep-28	18-Sep-28	335.0d
10599	A103950	Owner Elec. Statics - MPP / CSC B34	1.0d	19-Sep-28	19-Sep-28	335.0d
10600	A103960	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B34	1.0d	20-Sep-28	20-Sep-28	335.0d
10601	A103970	Mech. Dynamic Testing - MPP / CSC B34	3.0d	21-Sep-28	25-Sep-28	335.0d
10602	A103980	I/O & Functional Testing - MPP / CSC B34	5.0d	26-Sep-28	2-Oct-28	335.0d
10603	A103990	Owner Functional Testing - MPP / CSC B34	1.0d	3-Oct-28	3-Oct-28	335.0d
10604	WBS - MPP / CSC A35 (MFD1A 01/09, MFD1B 01/05, MUD1)		24.0d	12-Nov-27	17-Dec-27	538.0d
10605	A103020	Elec. Homeruns / Cable Tray - MPP / CSC A35	5.0d	12-Nov-27	18-Nov-27	537.0d
10606	A103030	Wire Pull - MPP / CSC A35	5.0d	19-Nov-27	29-Nov-27	537.0d
10607	A103040	Terminate Wire at CSC - MPP / CSC A35	5.0d	30-Nov-27	6-Dec-27	537.0d
10608	A103050	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A35	5.0d	30-Nov-27	6-Dec-27	537.0d
10609	A103060	Internal Elec. Statics - MPP / CSC A35	1.0d	7-Dec-27	7-Dec-27	537.0d
10610	A103070	Owner Elec. Statics - MPP / CSC A35	1.0d	8-Dec-27	8-Dec-27	537.0d
10611	A103080	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A35	1.0d	9-Dec-27	9-Dec-27	537.0d
10612	A103090	Mech. Dynamic Testing - MPP / CSC A35	2.0d	10-Dec-27	13-Dec-27	537.0d
10613	A103100	I/O & Functional Testing - MPP / CSC A35	3.0d	14-Dec-27	16-Dec-27	537.0d
10614	A103110	Owner Functional Testing - MPP / CSC A35	1.0d	17-Dec-27	17-Dec-27	537.0d
10615	WBS - MPP / CSC B35 (MFD2A 01/04, MFD2B 01/05, MUD2)		24.0d	17-Nov-27	22-Dec-27	535.0d
10616	A103240	Elec. Homeruns / Cable Tray - MPP / CSC B35	5.0d	17-Nov-27	23-Nov-27	534.0d
10617	A103250	Wire Pull - MPP / CSC B35	5.0d	24-Nov-27	2-Dec-27	534.0d
10618	A103260	Terminate Wire at CSC - MPP / CSC B35	5.0d	3-Dec-27	9-Dec-27	534.0d
10619	A103270	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B35	5.0d	3-Dec-27	9-Dec-27	534.0d
10620	A103280	Internal Elec. Statics - MPP / CSC B35	1.0d	10-Dec-27	10-Dec-27	534.0d
10621	A103290	Owner Elec. Statics - MPP / CSC B35	1.0d	13-Dec-27	13-Dec-27	534.0d
10622	A103300	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B35	1.0d	14-Dec-27	14-Dec-27	534.0d
10623	A103310	Mech. Dynamic Testing - MPP / CSC B35	2.0d	15-Dec-27	16-Dec-27	534.0d
10624	A103320	I/O & Functional Testing - MPP / CSC B35	3.0d	17-Dec-27	21-Dec-27	534.0d
10625	A103330	Owner Functional Testing - MPP / CSC B35	1.0d	22-Dec-27	22-Dec-27	534.0d
10626	WBS - MPP / CSC A36 (MFD3A 01/05, MFD3B 01/05, MUD3)		31.0d	27-Dec-27	8-Feb-28	503.0d

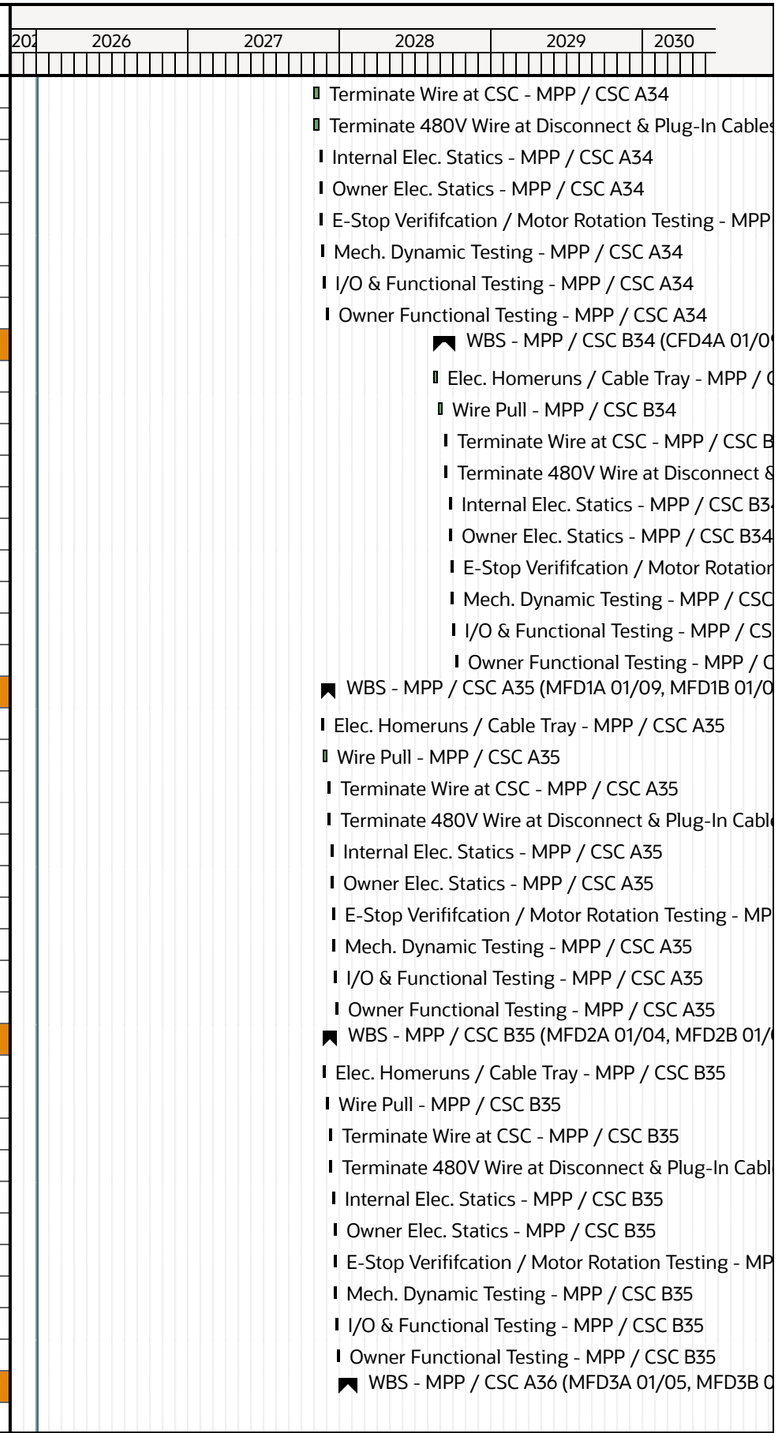

	ID	Name	Dur	Start	Finish	TF
10627	A102910	Elec. Homeruns / Cable Tray - MPP / CSC A36	5.0d	27-Dec-27	3-Jan-28	509.0d
10628	A102920	Wire Pull - MPP / CSC A36	5.0d	4-Jan-28	10-Jan-28	509.0d
10629	A103010	Primary Wire Pull & Coiled-Up to MPP (By Others) - MPP / CSC A36	0.0d		10-Jan-28	516.0d
10630	A102930	Terminate Wire at CSC - MPP / CSC A36	5.0d	11-Jan-28	17-Jan-28	509.0d
10631	A102940	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A36	5.0d	11-Jan-28	17-Jan-28	509.0d
10632	A102950	Internal Elec. Statics - MPP / CSC A36	1.0d	18-Jan-28	18-Jan-28	509.0d
10633	A102960	Owner Elec. Statics - MPP / CSC A36	1.0d	19-Jan-28	19-Jan-28	509.0d
10634	A102970	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A36	1.0d	31-Jan-28	31-Jan-28	502.0d
10635	A102980	Mech. Dynamic Testing - MPP / CSC A36	2.0d	1-Feb-28	2-Feb-28	502.0d
10636	A102990	I/O & Functional Testing - MPP / CSC A36	3.0d	3-Feb-28	7-Feb-28	502.0d
10637	A103000	Owner Functional Testing - MPP / CSC A36	1.0d	8-Feb-28	8-Feb-28	502.0d
10638	WBS - MPP / CSC B36 (MFD4A 01/05, MFD4B 01/05, MUD4)		24.0d	9-Nov-27	14-Dec-27	541.0d
10639	A103130	Elec. Homeruns / Cable Tray - MPP / CSC B36	5.0d	9-Nov-27	15-Nov-27	540.0d
10640	A103140	Wire Pull - MPP / CSC B36	5.0d	16-Nov-27	22-Nov-27	540.0d
10641	A103150	Terminate Wire at CSC - MPP / CSC B36	5.0d	23-Nov-27	1-Dec-27	540.0d
10642	A103160	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B36	5.0d	23-Nov-27	1-Dec-27	540.0d
10643	A103170	Internal Elec. Statics - MPP / CSC B36	1.0d	2-Dec-27	2-Dec-27	540.0d
10644	A103180	Owner Elec. Statics - MPP / CSC B36	1.0d	3-Dec-27	3-Dec-27	540.0d
10645	A103190	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B36	1.0d	6-Dec-27	6-Dec-27	540.0d
10646	A103200	Mech. Dynamic Testing - MPP / CSC B36	2.0d	7-Dec-27	8-Dec-27	540.0d
10647	A103210	I/O & Functional Testing - MPP / CSC B36	3.0d	9-Dec-27	13-Dec-27	540.0d
10648	A103220	Owner Functional Testing - MPP / CSC B36	1.0d	14-Dec-27	14-Dec-27	540.0d
10649	WBS - MPP / CSC A37 (MFD5A 01/05, MFD5B 01/05, MUD5)		24.0d	9-Nov-27	14-Dec-27	541.0d
10650	A103350	Elec. Homeruns / Cable Tray - MPP / CSC A37	5.0d	9-Nov-27	15-Nov-27	540.0d
10651	A103360	Wire Pull - MPP / CSC A37	5.0d	16-Nov-27	22-Nov-27	540.0d
10652	A103370	Terminate Wire at CSC - MPP / CSC A37	5.0d	23-Nov-27	1-Dec-27	540.0d
10653	A103380	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC A37	5.0d	23-Nov-27	1-Dec-27	540.0d
10654	A103390	Internal Elec. Statics - MPP / CSC A37	1.0d	2-Dec-27	2-Dec-27	540.0d
10655	A103400	Owner Elec. Statics - MPP / CSC A37	1.0d	3-Dec-27	3-Dec-27	540.0d
10656	A103410	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC A37	1.0d	6-Dec-27	6-Dec-27	540.0d
10657	A103420	Mech. Dynamic Testing - MPP / CSC A37	2.0d	7-Dec-27	8-Dec-27	540.0d
10658	A103430	I/O & Functional Testing - MPP / CSC A37	3.0d	9-Dec-27	13-Dec-27	540.0d
10659	A103440	Owner Functional Testing - MPP / CSC A37	1.0d	14-Dec-27	14-Dec-27	540.0d
10660	WBS - MPP / CSC B37 (MFD6A 01/05, MFD6B 01/05, MUD6)		43.0d	12-Nov-27	17-Jan-28	523.0d
10661	A103460	Elec. Homeruns / Cable Tray - MPP / CSC B37	5.0d	12-Nov-27	18-Nov-27	541.0d
10662	A103470	Wire Pull - MPP / CSC B37	5.0d	19-Nov-27	29-Nov-27	541.0d
10663	A103480	Terminate Wire at CSC - MPP / CSC B37	5.0d	30-Nov-27	6-Dec-27	541.0d
10664	A103490	Terminate 480V Wire at Disconnect & Plug-In Cables to Devices - MPP / CSC B37	5.0d	30-Nov-27	6-Dec-27	541.0d
10665	A103500	Internal Elec. Statics - MPP / CSC B37	1.0d	7-Dec-27	7-Dec-27	541.0d
10666	A103510	Owner Elec. Statics - MPP / CSC B37	1.0d	8-Dec-27	8-Dec-27	541.0d
10667	A103520	E-Stop Verifiфcation / Motor Rotation Testing - MPP / CSC B37	1.0d	7-Jan-28	7-Jan-28	522.0d
10668	A103530	Mech. Dynamic Testing - MPP / CSC B37	2.0d	10-Jan-28	11-Jan-28	522.0d

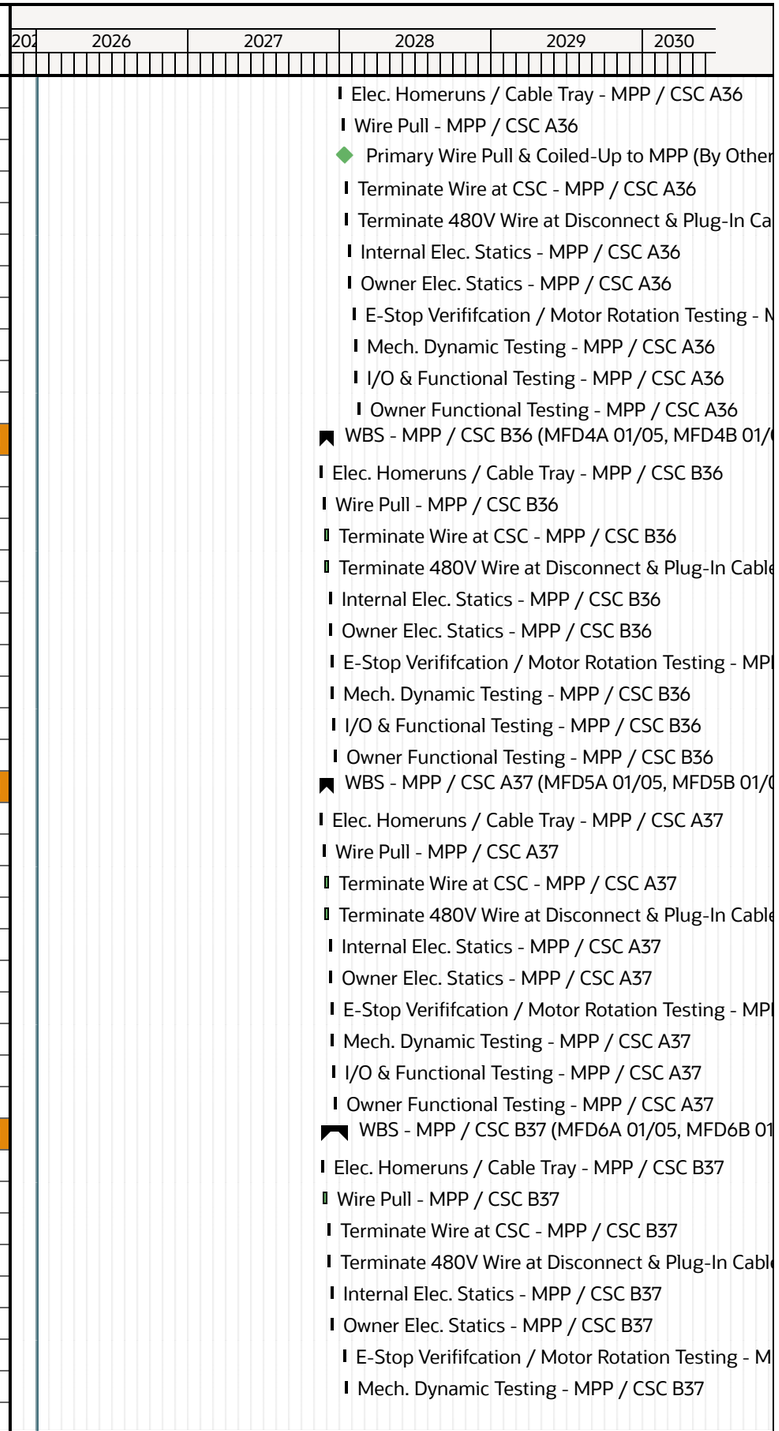

	ID	Name	Dur	Start	Finish	TF
10669	A103540	I/O & Functional Testing - MPP / CSC B37	3.0d	12-Jan-28	14-Jan-28	522.0d
10670	A103550	Owner Functional Testing - MPP / CSC B37	1.0d	17-Jan-28	17-Jan-28	522.0d
10671	WBS - Equipment Rooms		20.0d	17-Mar-27	13-Apr-27	709.0d
10672	D5856	Set Up FAT Equip. - Airside D	20.0d	17-Mar-27	13-Apr-27	708.0d
10673	WBS - Civil		844.0d	14-Oct-25 A	9-Feb-29	25.0d
10674	TC-GP-290	Demo Old Bessie Coleman Blvd & Rough Grade Area	10.0d	11-Jun-26	24-Jun-26	3.0d
10675	TC-FS-120	Install New Temp Barrier Mounted AOA Fence (Includes TSA Inspections)	20.0d	30-Jun-26	28-Jul-26	0.0d
10676	TC-FS-50	Remove Temp AOA Fence (Installed During Enabling)	20.0d	29-Jul-26	25-Aug-26	0.0d
10677	TC-GP-300	Demo Bessie Coleman / George Bean Bypass	5.0d	17-Sep-27	23-Sep-27	296.0d
10678	TC-FS-80	ASD - Truck Court Area Complete	0.0d		21-Sep-27	337.0d
10679	TC-FS-90	ASD - Bessie Coleman Blvd Complete	0.0d		20-Oct-27	296.0d
10680	TC-FS-110	Install New AOA Fence (Excellence Drive/Trailer City)	10.0d	29-Dec-28	12-Jan-29	5.0d
10681	TC-FS-100	Remove Temp Access Roads, Guard Booths & Infrastructure (Installed During E...	20.0d	15-Jan-29	9-Feb-29	25.0d
10682	TC-FS-130	Remove Temp AOA Fence (Final)	20.0d	15-Jan-29	9-Feb-29	5.0d
10683	WBS - GSE Paving Area		254.0d	9-Mar-27	7-Mar-28	101.0d
10684	WBS - GSE Paving - Quadrant 2		132.0d	11-Aug-27	17-Feb-28	114.0d
10685	U&P-UND-60	Install Underground Storm S-806 to S-825 (Inc Roof & Condensate Pipes) - Qu...	15.0d	11-Aug-27	31-Aug-27	0.0d
10686	U&P-UND-70	Install Underground Sanitary MH-202 to S-201 - Quadrant 2	20.0d	1-Sep-27	29-Sep-27	0.0d
10687	U&P-UND-170	Install Underground Sanitary MH-201 to S-202 - Quadrant 2	5.0d	30-Sep-27	6-Oct-27	0.0d
10688	U&P-UND-80	Install Building Roof Drain Laterals - Quadrant 2	5.0d	7-Oct-27	13-Oct-27	0.0d
10689	U&P-GP-130	Install Underground Fire Protection STA-32+00 to STA-25+00 - Quadrant 2	10.0d	14-Oct-27	27-Oct-27	0.0d
10690	U&P-GP-60	VDGS Found. & Conduit - Quadrant 2	10.0d	28-Oct-27	10-Nov-27	0.0d
10691	U&P-GP-100	Install Underground Electric & Communications - Quadrant 2	15.0d	28-Oct-27	17-Nov-27	113.0d
10692	U&P-GP-350	Install Underground Low Volt Conduit to PBB Rotunda - Quadrant 2	15.0d	28-Oct-27	17-Nov-27	113.0d
10693	U&P-GP-260	EFSO Duct Bank to Fuel Vault - Quadrant 2	5.0d	15-Nov-27	19-Nov-27	113.0d
10694	U&P-GP-90	Fine Grade Area - Quadrant 2	5.0d	22-Nov-27	30-Nov-27	113.0d
10695	U&P-UND-50	Install GSE Paving Base - Quadrant 2	15.0d	1-Dec-27	21-Dec-27	113.0d
10696	U&P-GP-110	Install GSE Paving & Trench Drains- Quadrant 2	20.0d	22-Dec-27	20-Jan-28	113.0d
10697	U&P-GP-120	Install Curbs & Sidewalks - Quadrant 2	10.0d	21-Jan-28	3-Feb-28	113.0d
10698	U&P-GP-320	Install Concrete Joint Sealants - Quadrant 2	10.0d	4-Feb-28	17-Feb-28	114.0d
10699	WBS - GSE Paving - Quadrant 3		191.0d	7-Jun-27	7-Mar-28	101.0d
10700	U&P-UND-90	Install Underground Storm S-825 to S-827 (Inc Roof & Condensate Pipes) - Qu...	15.0d	7-Jun-27	25-Jun-27	61.0d
10701	U&P-GP-140	Install Underground Fire Protection STA-25+00 to STA-20+00 - Quadrant 3	10.0d	28-Jun-27	12-Jul-27	61.0d
10702	U&P-UND-160	Install Underground Storm S-828 to S-831- Quadrant 3	10.0d	28-Jun-27	12-Jul-27	201.0d
10703	U&P-GP-150	Install Underground Electric & Communications - Quadrant 3	15.0d	13-Jul-27	2-Aug-27	61.0d
10704	U&P-GP-360	Install Underground Low Volt Conduit to PBB Rotunda - Quadrant 3	15.0d	13-Jul-27	2-Aug-27	61.0d
10705	U&P-GP-270	EFSO Duct Bank to Fuel Vault - Quadrant 3	5.0d	28-Jul-27	3-Aug-27	185.0d
10706	U&P-GP-160	VDGS Found. & Conduit - Quadrant 3	10.0d	3-Aug-27	16-Aug-27	61.0d
10707	U&P-GP-170	Fine Grade Area - Quadrant 3	5.0d	17-Aug-27	23-Aug-27	176.0d
10708	U&P-UND-110	Install Building Roof Drain Laterals - Quadrant 3	5.0d	24-Aug-27	30-Aug-27	176.0d
10709	U&P-UND-120	Install GSE Paving Base - Quadrant 3	15.0d	20-Dec-27	11-Jan-28	100.0d
10710	U&P-GP-180	Install GSE Paving & Trench Drains - Quadrant 3	20.0d	12-Jan-28	8-Feb-28	100.0d

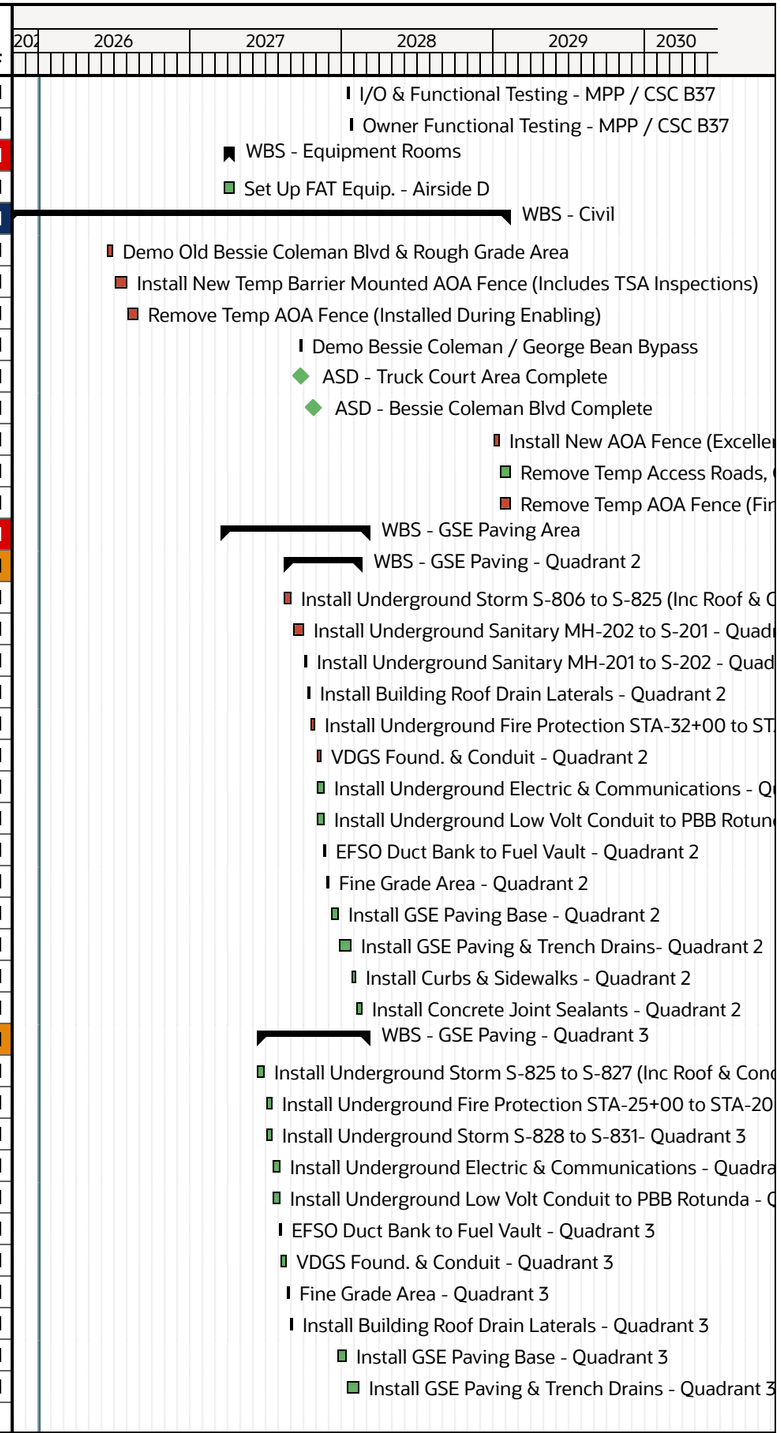


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:11 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
10711	U&P-GP-190	Install Curbs & Sidewalks - Quadrant 3	10.0d	9-Feb-28	22-Feb-28	100.0d
10712	U&P-GP-330	Install Concrete Joint Sealants - Quadrant 3	10.0d	23-Feb-28	7-Mar-28	101.0d
10713	WBS - GSE Paving - Quadrant 4		229.0d	9-Mar-27	1-Feb-28	116.0d
10714	U&P-UND-130	Install Underground Storm S-831 to S- 811 (Inc Roof & Condensate Pipes) - Qu...	15.0d	9-Mar-27	29-Mar-27	119.0d
10715	U&P-UND-140	Install Building Roof Drain Laterals - Quadrant 4	5.0d	30-Mar-27	5-Apr-27	119.0d
10716	U&P-GP-200	Install Underground Fire Protection STA-20+00 to STA-12+00 - Quadrant 4	10.0d	6-Apr-27	19-Apr-27	119.0d
10717	U&P-GP-50	Telecom & Power Conduit to Blast Wall - Utilities & Paving GSE	10.0d	20-Apr-27	3-May-27	245.0d
10718	U&P-GP-210	Install Underground Electric & Communications - Quadrant 4	15.0d	20-Apr-27	10-May-27	119.0d
10719	U&P-GP-370	Install Underground Low Volt Conduit to PBB Rotunda - Quadrant 4	15.0d	20-Apr-27	10-May-27	119.0d
10720	U&P-GP-280	EFSO Duct Bank to Fuel Vault - Quadrant 4	5.0d	4-May-27	10-May-27	240.0d
10721	U&P-GP-220	VDGS Found. & Conduit - Quadrant 4	10.0d	11-May-27	24-May-27	119.0d
10722	U&P-GP-230	Fine Grade Area - Quadrant 4	5.0d	25-May-27	1-Jun-27	230.0d
10723	U&P-UND-150	Install GSE Paving Base - Quadrant 4	15.0d	11-Nov-27	3-Dec-27	116.0d
10724	U&P-GP-240	Install GSE Paving & Trench Drains - Quadrant 4	20.0d	6-Dec-27	4-Jan-28	116.0d
10725	U&P-GP-250	Install Curbs & Sidewalks - Quadrant 4	10.0d	5-Jan-28	18-Jan-28	116.0d
10726	U&P-GP-340	Install Concrete Joint Sealants - Quadrant 4	10.0d	19-Jan-28	1-Feb-28	116.0d
10727	WBS - Truck Court		492.0d	14-Oct-25 A	21-Sep-27	230.0d
10728	TC-UND-50	TECO Install Transformers & Switches - Truck Court	20.0d	3-Nov-26	2-Dec-26	224.0d
10729	WBS - CIP Foundations, Retaining Walls & Equipment Pads- Truck Court		172.0d	15-Sep-26	18-May-27	254.0d
10730	TC-FS-40	FRP Retaining Walls - Truck Court East	20.0d	13-Oct-26	9-Nov-26	366.0d
10731	TC-UND-80	Install MEPF Equip. Concrete Pads - Truck Court	10.0d	20-Oct-26	2-Nov-26	224.0d
10732	TC-FS-30	FRP Retaining Walls - Truck Court West	20.0d	21-Apr-27	18-May-27	254.0d
10733	WBS - Cooling Tower Foundations & Basin		36.0d	15-Sep-26	3-Nov-26	329.0d
10734	GI-FS-A1-6860	Excavate Area For Found. - Cooling Tower	3.0d	15-Sep-26	17-Sep-26	229.0d
10735	GI-FS-A1-6870	FRP Found. - Cooling Tower	15.0d	16-Sep-26	6-Oct-26	229.0d
10736	GI-FS-A1-6880	Install Waterproofing On Found. - Cooling Tower	15.0d	17-Sep-26	7-Oct-26	229.0d
10737	GI-FS-A1-6890	MEPF In-Wall R/I - Cooling Tower	10.0d	18-Sep-26	1-Oct-26	232.0d
10738	GI-FS-A1-6900	Backfill Found. - Cooling Tower	7.0d	2-Oct-26	12-Oct-26	229.0d
10739	GI-FS-A3-6820	28 Day Cure on All Concrete - Cooling Tower	28.0d	7-Oct-26	3-Nov-26	461.0d
10740	WBS - Underground Utilities - Truck Court		400.0d	14-Oct-25 A	11-May-27	288.0d
10741	WBS - Underground Utilities - Truck Court - West		72.0d	1-Feb-27	11-May-27	179.0d
10742	TC-UND-20	Install Underground Storm S-801 to S-806 - Truck Court West	15.0d	1-Feb-27	19-Feb-27	128.0d
10743	TC-UND-40	Install Grease Traps & Oil Water Separator - Truck Court West	5.0d	15-Feb-27	19-Feb-27	138.0d
10744	TC-UND-120	Install Underground Sanitary MH-202 to MH-000 - Truck Court West	10.0d	22-Feb-27	5-Mar-27	128.0d
10745	TC-UND-140	Install Underground Sanitary MH-203 to GT, OWS & Trash Comp - Truck Court ...	5.0d	8-Mar-27	12-Mar-27	128.0d
10746	TC-UND-150	Install Underground Sanitary MH-400 to MH-102 - Truck Court West	7.0d	15-Mar-27	23-Mar-27	128.0d
10747	TC-UND-90	Install Gas Main (TECO) - Truck Court West	15.0d	24-Mar-27	13-Apr-27	133.0d
10748	TC-UND-110	Install Underground Fire Protection STA-34+65 to STA-32+00 - Truck Court West	10.0d	24-Mar-27	6-Apr-27	128.0d
10749	TC-UND-160	Install Underground Communications Ductbank - Truck Court West	10.0d	7-Apr-27	20-Apr-27	128.0d
10750	TC-UND-170	Install Shallow Underground Elec. & Comm - Truck Court West	10.0d	28-Apr-27	11-May-27	179.0d
10751	WBS - Underground Utilities - Truck Court - East		207.0d	20-Jul-26	11-May-27	128.0d
10752	TC-UND-30	Install Underground Storm S-817 - S-811 - Truck Court East	15.0d	20-Jul-26	7-Aug-26	57.0d

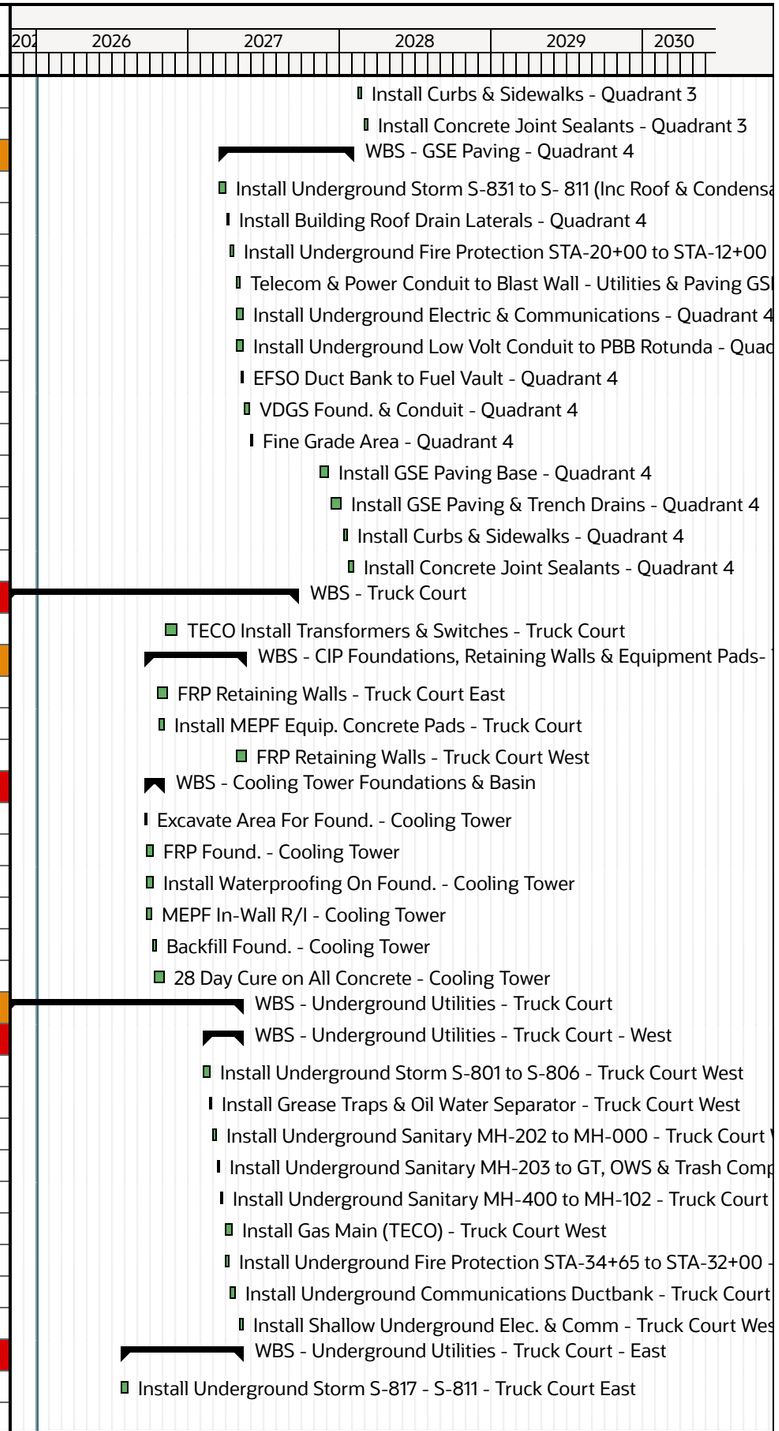


ID	Name	Dur	Start	Finish	TF
10753	TC-UND-7020	TECO 30 Day Advanced Schedule Notice for PDS Room 6097 Pathways - Truck ...	30.0d	25-Jul-26	23-Aug-26	102.0d
10754	TC-UND-60	Install Underground Sanitary MH-102 to MH-100 - Truck Court East	10.0d	10-Aug-26	21-Aug-26	57.0d
10755	TC-UND-240	TECO Install Primary Feeders for ASD Service - Truck Court East	20.0d	17-Aug-26	14-Sep-26	82.0d
10756	TC-UND-100	Install Underground Elec. - Truck Court East	15.0d	24-Aug-26	14-Sep-26	57.0d
10757	TC-UND-7030	TECO Install Conduit Pathways for PDS Rm 6097 - Truck Court East	10.0d	24-Aug-26	4-Sep-26	72.0d
10758	TC-UND-190	Install Underground Sanitary MH-100 to Cooling Tower - Truck Court East	5.0d	24-Aug-26	28-Aug-26	122.0d
10759	TC-UND-230	Install Underground CHW/Condenser Water- Truck Court East	10.0d	24-Aug-26	4-Sep-26	72.0d
10760	TC-UND-70	Install Underground Water & Fire Protection- Truck Court East	10.0d	15-Sep-26	28-Sep-26	102.0d
10761	TC-UND-200	Install Underground Fire Protection STA-10+00 to STA-12+00 - Truck Court East	10.0d	15-Sep-26	28-Sep-26	102.0d
10762	TC-UND-210	Install Underground Non-Potable Water STA-10+00 to STA-11+80 - Truck Cour...	10.0d	15-Sep-26	28-Sep-26	57.0d
10763	TC-UND-180	Install Underground Storm S-813 - S-815 - Truck Court East	15.0d	29-Sep-26	19-Oct-26	57.0d
10764	TC-UND-220	Install Shallow Underground Elec. & Comm - Truck Court East	10.0d	28-Apr-27	11-May-27	128.0d
10765	WBS - Pipe Bursting		172.0d	14-Oct-25 A	17-Jun-26	516.0d
10766	UND-PB-2700	CCTV For Design - Pipe Bursting	2.0d	14-Oct-25 A	15-Oct-25 A	
10767	UND-PB-2710	Mobilize - Pipe Bursting	25.0d	18-Feb-26	24-Mar-26	359.0d
10768	UND-PB-2780	Install Bypass Systems - Pipe Bursting	10.0d	25-Mar-26	7-Apr-26	516.0d
10769	UND-PB-2720	Burst Section 1 - Pipe Bursting	5.0d	8-Apr-26	14-Apr-26	516.0d
10770	UND-PB-2730	Burst Section 2 - Pipe Bursting	5.0d	15-Apr-26	21-Apr-26	516.0d
10771	UND-PB-2740	Burst Section 3 - Pipe Bursting	5.0d	22-Apr-26	28-Apr-26	516.0d
10772	UND-PB-2750	Burst Section 4 - Pipe Bursting	5.0d	29-Apr-26	5-May-26	516.0d
10773	UND-PB-2760	Restore All Areas - Pipe Bursting	15.0d	6-May-26	27-May-26	516.0d
10774	UND-PB-2770	Final Camera Post Bursting - Pipe Bursting	15.0d	28-May-26	17-Jun-26	516.0d
10775	WBS - Area Development - Truck Court		107.0d	21-Apr-27	21-Sep-27	230.0d
10776	TC-GP-10	Rough Grade - Truck Court	5.0d	21-Apr-27	27-Apr-27	128.0d
10777	TC-GP-60	Install Irrigation Sleeves - Truck Court	3.0d	28-Apr-27	30-Apr-27	186.0d
10778	TC-GP-200	Set Light Poles - Truck Court	5.0d	28-Apr-27	4-May-27	184.0d
10779	TC-GP-30	Fine Grade / Stabilize Soil for Paving Areas - Truck Court	5.0d	12-May-27	18-May-27	179.0d
10780	TC-GP-40	Install Road Base - Truck Court	5.0d	19-May-27	25-May-27	179.0d
10781	TC-GP-50	Install Edge Curbs, Raised Sidewalks, Dumpster & Guard Booth Pads - Truck Co...	12.0d	26-May-27	11-Jun-27	179.0d
10782	TC-GP-70	Concrete Paving - Placement 1 - Truck Court	7.0d	14-Jun-27	22-Jun-27	179.0d
10783	TC-GP-80	Concrete Paving - Placement 2 - Truck Court	7.0d	23-Jun-27	1-Jul-27	179.0d
10784	TC-GP-90	Concrete Paving - Placement 3 - Truck Court	7.0d	2-Jul-27	13-Jul-27	179.0d
10785	TC-GP-100	Concrete Paving - Placement 4 - Truck Court	7.0d	14-Jul-27	22-Jul-27	179.0d
10786	TC-GP-110	Concrete Paving - Placement 5 - Truck Court	7.0d	23-Jul-27	2-Aug-27	179.0d
10787	TC-GP-190	Concrete Paving - Placement 6 - Truck Court	7.0d	3-Aug-27	11-Aug-27	179.0d
10788	TC-GP-120	Fine Grade for Landscape Areas - Truck Court	3.0d	12-Aug-27	16-Aug-27	230.0d
10789	TC-GP-170	Install Guard Booths, Gate Arms & Associated Equip. - Truck Court	20.0d	12-Aug-27	9-Sep-27	233.0d
10790	TC-GP-310	Truck Court Concrete Paving Cure - Truck Court	7.0d	12-Aug-27	20-Aug-27	179.0d
10791	TC-GP-130	Install Irrigation - Truck Court	6.0d	17-Aug-27	24-Aug-27	232.0d
10792	TC-GP-150	Install Fencing - Truck Court	15.0d	17-Aug-27	7-Sep-27	230.0d
10793	TC-GP-180	Install Bollards - Truck Court	5.0d	25-Aug-27	31-Aug-27	232.0d
10794	TC-GP-280	Install Handrail / Guardrail - Truck Court	7.0d	1-Sep-27	10-Sep-27	232.0d

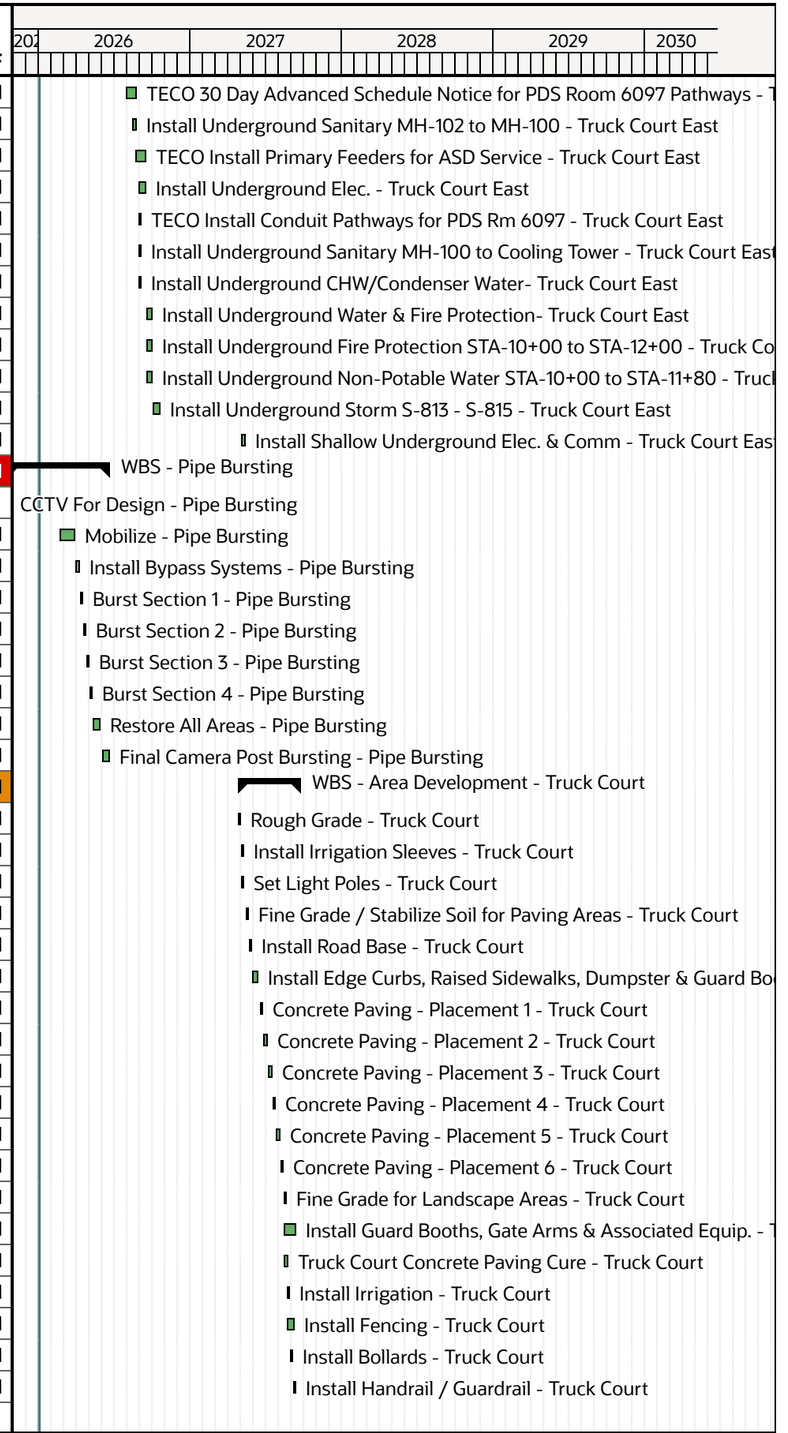

	ID	Name	Dur	Start	Finish	TF
10795	TC-GP-140	Install Trees, Plants & Shrubs - Truck Court	5.0d	8-Sep-27	14-Sep-27	230.0d
10796	TC-GP-160	Install Curb Stops, Pavement Striping & Roadway Signage - Truck Court	5.0d	15-Sep-27	21-Sep-27	230.0d
10797	WBS - Cooling Towers		181.0d	8-Oct-26	8-Jun-27	290.0d
10798	WBS - Infrastructure, Mech. Equipment - Cooling Towers		123.0d	4-Jan-27	8-Jun-27	290.0d
10799	CLT-RI-AP-200	Cooling Tower Install - Infrastructure, Mech. Equip. - Cooling Tower Building	10.0d	4-Jan-27	15-Jan-27	290.0d
10800	CLT-RI-AP-210	Cooling Tower Base Install - Infrastructure, Mech. Equip. - Cooling Tower Building	10.0d	18-Jan-27	29-Jan-27	290.0d
10801	CLT-RI-AP-220	Set Cells for the Cooling Tower #1 - Infrastructure, Mech. Equip. - Cooling Towe...	10.0d	1-Feb-27	12-Feb-27	290.0d
10802	CLT-RI-AP-230	Set Cells for the Cooling Tower #2 - Infrastructure, Mech. Equip. - Cooling Towe...	10.0d	15-Feb-27	26-Feb-27	290.0d
10803	CLT-RI-AP-240	Set Cells for the Cooling Tower 3 - Infrastructure, Mech. Equip. - Cooling Tower ...	10.0d	1-Mar-27	12-Mar-27	290.0d
10804	CLT-RI-AP-255	Set Steel Pipe Racks - Infrastructure, Mech. Equip. - Cooling Tower Building	10.0d	15-Mar-27	26-Mar-27	328.0d
10805	CLT-RI-AP-265	Install CWS/CWR & Isolation Valves/Pumps - Infrastructure, Mech. Equip. - Coo...	10.0d	29-Mar-27	9-Apr-27	328.0d
10806	CLT-RI-AP-245	Start-up Mech. Pumps - Infrastructure, Mech. Equip. - Cooling Tower Building	3.0d	4-Jun-27	8-Jun-27	290.0d
10807	WBS - Infrastructure, Elec. Rough-in - Cooling Towers		166.0d	8-Oct-26	3-Jun-27	290.0d
10808	CLT-RI-AP-70	Install UG Elec. - Infrastructure, Elec. Rough-in - Cooling Tower Building	15.0d	8-Oct-26	28-Oct-26	333.0d
10809	CLT-RI-AP-130	Install Elec. Hangers - Infrastructure, Elec. Rough-in - Cooling Tower Building	2.0d	15-Mar-27	16-Mar-27	290.0d
10810	CLT-RI-AP-140	Install Elec. Rough-in Walls Power & LTNG - Infrastructure, Elec. Rough-in - Coo...	8.0d	17-Mar-27	26-Mar-27	290.0d
10811	CLT-RI-AP-150	Install Elec. Connections to Pumps / Fans / VFDs - Infrastructure, Elec. Rough-i...	20.0d	29-Mar-27	23-Apr-27	290.0d
10812	CLT-RI-AP-160	Measure & Procure Elec. Feeder Wire - Infrastructure, Elec. Rough-in - Cooling ...	10.0d	26-Apr-27	7-May-27	290.0d
10813	CLT-RI-AP-170	Pull & Term Elec. Wire - Infrastructure, Elec. Rough-in - Cooling Tower Building	10.0d	10-May-27	21-May-27	290.0d
10814	CLT-RI-AP-190	Install Elec. Trim - Infrastructure, Elec. Rough-in - Cooling Tower Building	5.0d	24-May-27	28-May-27	290.0d
10815	CLT-RI-AP-180	Perform Third Party Elec. Testing - Infrastructure, Elec. Rough-in - Cooling Tow...	3.0d	1-Jun-27	3-Jun-27	290.0d
10816	WBS - Bessie Coleman Blvd		49.0d	12-Aug-27	20-Oct-27	296.0d
10817	TC-UND-130	Install S-819 to S-818 - Bessie Coleman	5.0d	12-Aug-27	18-Aug-27	296.0d
10818	TC-GP-220	Fine Grade / Stabilize Soil for Paving Areas - Bessie Coleman	5.0d	19-Aug-27	25-Aug-27	296.0d
10819	TC-GP-230	Install Road Base - Bessie Coleman	5.0d	26-Aug-27	1-Sep-27	296.0d
10820	TC-GP-20	Install Asphalt Paving - Bessie Coleman	5.0d	2-Sep-27	9-Sep-27	296.0d
10821	TC-GP-240	Install Pavement Striping & Roadway Signage - Bessie Coleman	5.0d	10-Sep-27	16-Sep-27	296.0d
10822	TC-FS-60	New Bessie Coleman Drive Complete for Switchover - Bessie Coleman	0.0d		16-Sep-27	296.0d
10823	TC-GP-250	Fine Grade for Landscape Areas - Bessie Coleman	3.0d	24-Sep-27	28-Sep-27	296.0d
10824	TC-GP-260	Repair Irrigation - Bessie Coleman	6.0d	29-Sep-27	6-Oct-27	296.0d
10825	TC-GP-270	Repair Trees, Plants & Shrubs - Bessie Coleman	10.0d	7-Oct-27	20-Oct-27	296.0d
10826	WBS - Performance Park North Craft Parking Lot		96.0d	29-Dec-25	12-May-26	72.0d
10827	CP-FS-150	Layout/Survey - PP North Craft Parking Lot	3.0d	29-Dec-25	31-Dec-25	72.0d
10828	CP-FS-160	Install BMP SWPPP Measures - PP North Craft Parking Lot	5.0d	2-Jan-26	8-Jan-26	72.0d
10829	CP-FS-170	Install Dust Control Measure - Wheel/Tire Wash - PP North Craft Parking Lot	2.0d	9-Jan-26	12-Jan-26	72.0d
10830	CP-FS-200	Demolish Fencing - PP North Craft Parking Lot	5.0d	13-Jan-26	19-Jan-26	72.0d
10831	CP-FS-140	Removal of Unsuitable Material - PP North Craft Parking Lot	10.0d	20-Jan-26	2-Feb-26	72.0d
10832	CP-FS-190	Remove & Relocate P219 Stockpile - PP North Craft Parking Lot	10.0d	3-Feb-26	16-Feb-26	72.0d
10833	CP-FS-210	Clear & Grub Remaining Debris & Vegetation - PP North Craft Parking Lot	5.0d	17-Feb-26	23-Feb-26	72.0d
10834	CP-FS-350	Remove Existing Stockpiles/Unsuitable Material East of Performance Park - PP ...	10.0d	17-Feb-26	2-Mar-26	115.0d
10835	CP-FS-220	Cut Existing Grade & Level to Base Elevation - PP North Craft Parking Lot	10.0d	24-Feb-26	9-Mar-26	72.0d
10836	CP-FS-360	Restore Vegetation East of Performance Park - PP North Craft Parking Lot	5.0d	3-Mar-26	9-Mar-26	115.0d

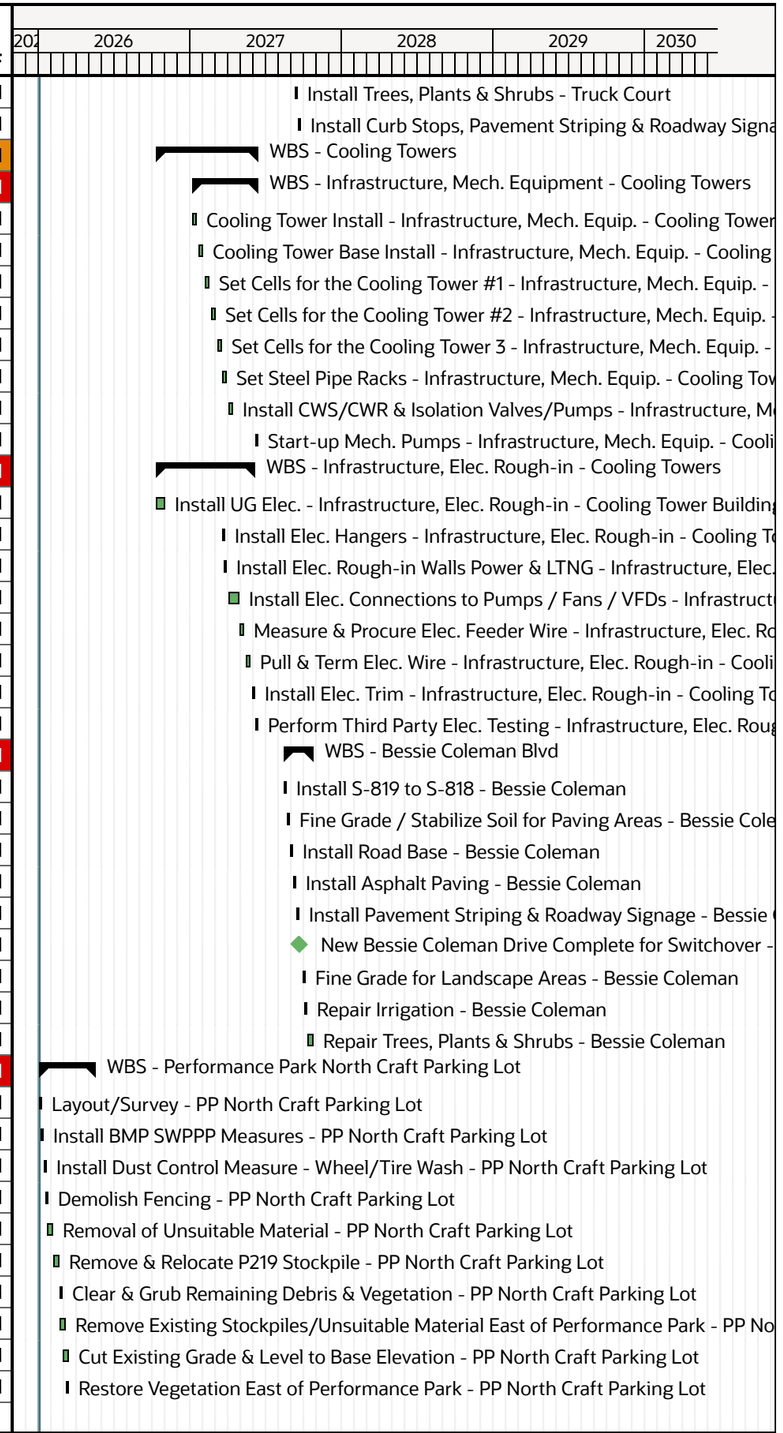

	ID	Name	Dur	Start	Finish	TF
10837	CP-FS-230	Install Base - Conex Laydown Area - PP North Craft Parking Lot	5.0d	10-Mar-26	16-Mar-26	72.0d
10838	CP-FS-250	Fill & Compact Subgrade Layer - PP North Craft Parking Lot	10.0d	10-Mar-26	23-Mar-26	72.0d
10839	CP-FS-240	Install 8" Base W/Grid - ITB Laydown Area - PP North Craft Parking Lot	5.0d	17-Mar-26	23-Mar-26	72.0d
10840	CP-FS-260	Install 3" Asphalt Surface Layer (Millings/Recycled Concrete) - PP North Craft P...	10.0d	24-Mar-26	6-Apr-26	72.0d
10841	CP-FS-270	Seal Surface Layer - PP North Craft Parking Lot	5.0d	7-Apr-26	13-Apr-26	72.0d
10842	CP-FS-340	Surface Layer Cure - PP North Craft Parking Lot	2.0d	14-Apr-26	15-Apr-26	72.0d
10843	CP-FS-280	Install Striping & Markings - PP North Craft Parking Lot	5.0d	16-Apr-26	22-Apr-26	72.0d
10844	CP-FS-290	Install MOT Signage - PP North Craft Parking Lot	5.0d	23-Apr-26	29-Apr-26	72.0d
10845	CP-FS-310	Mobilize Temporary Solar Power Light Plants - PP North Craft Parking Lot	3.0d	30-Apr-26	4-May-26	72.0d
10846	CP-FS-320	Install Gate Arms at Entrances - PP North Craft Parking Lot	3.0d	5-May-26	7-May-26	72.0d
10847	CP-FS-300	Install Temporary Toilets - PP North Craft Parking Lot	3.0d	5-May-26	7-May-26	72.0d
10848	CP-FS-330	Final Clean & Parking Lot Turnover - PP North Craft Parking Lot	3.0d	8-May-26	12-May-26	72.0d
10849	WBS - Main Terminal Shuttle Platform Construction		35.0d	10-Jan-29	27-Feb-29	146.0d
10850	MT-SP-10	Demo Temp Partitions, Walls, Doors, & Signage - Main Terminal Shuttle Platfor...	5.0d	10-Jan-29	16-Jan-29	145.0d
10851	MT-SP-20	Demo Terrazzo for Walk-off Mat Install - Main Terminal Shuttle Platform Const.	5.0d	10-Jan-29	16-Jan-29	145.0d
10852	MT-SP-30	Install Walk-off Mats - Main Terminal Shuttle Platform Const.	5.0d	17-Jan-29	23-Jan-29	145.0d
10853	MT-SP-40	Patch & Repair Weatherproofing & Finishes - Main Terminal Shuttle Platform C...	5.0d	17-Jan-29	23-Jan-29	145.0d
10854	MT-SP-50	Install Exit Signs/Lights - Main Terminal Shuttle Platform Const.	5.0d	24-Jan-29	30-Jan-29	145.0d
10855	MT-SP-60	Install Door Hardware - Main Terminal Shuttle Platform Const.	5.0d	24-Jan-29	30-Jan-29	150.0d
10856	MT-SP-70	Enable BHS Floor Hatch - Main Terminal Shuttle Platform Const.	5.0d	31-Jan-29	6-Feb-29	145.0d
10857	MT-SP-80	Demo Temp Pedestals Over Stub-ups - Main Terminal Shuttle Platform Const.	5.0d	7-Feb-29	13-Feb-29	145.0d
10858	MT-SP-90	Install E-Gates (By Owner) - Main Terminal Shuttle Platform Const.	5.0d	14-Feb-29	20-Feb-29	145.0d
10859	MT-SP-100	Remove Temp Wall System - Main Terminal Shuttle Platform Const.	5.0d	21-Feb-29	27-Feb-29	145.0d
10860	WBS - HCAA Stakeholders		509.0d	17-Mar-27	16-Mar-29	0.0d
10861	WBS - Alstom Construction		558.0d	17-Mar-27	24-Sep-28	173.0d
10862	WBS - Alstom Project Milestones		558.0d	17-Mar-27	24-Sep-28	173.0d
10863	AL-SUM-200	Both Lanes - Construction/Testing - Alstom Construction	558.0d	17-Mar-27	24-Sep-28	173.0d
10864	AL-SUM-270	Alstom Substantial Completion - Alstom Construction	0.0d		24-Sep-28	173.0d
10865	WBS - Concessions Program Construction (by Others)		1.0d	24-May-28	24-May-28	4.0d
10866	HA-AL-CP-168	Concessions - Construction NTP	1.0d	24-May-28	24-May-28	4.0d
10867	WBS - Turn Over Milestones		376.0d	23-Sep-27	16-Mar-29	0.0d
10868	WBS - Apron Milestones		308.0d	3-Jan-28	16-Mar-29	0.0d
10869	WBS - Apron Airlines Milestones		303.0d	10-Jan-28	16-Mar-29	0.0d
10870	MLS-AP-110	Unassigned Airline Operations A12.1 Turnover - AP12	0.0d	10-Jan-28		193.0d
10871	MLS-AP-115	Unassigned Airline Operations A12.1 - AP12 - Construction Period	90.0d	10-Jan-28	12-May-28	193.0d
10872	MLS-AP-130	Delta Airlines Operations A7.2 Turnover - AP7	0.0d	17-May-28		11.0d
10873	MLS-AP-140	Delta Airlines Operations A7.1 Turnover - AP7	0.0d	17-May-28		11.0d
10874	MLS-AP-135	Delta Airlines Operations A7.2 - AP7 - Construction Period	200.0d	17-May-28	1-Mar-29	11.0d
10875	MLS-AP-145	Delta Airlines Operations A7.1 - AP7 - Construction Period	200.0d	17-May-28	1-Mar-29	11.0d
10876	MLS-AP-120	Delta Airlines Operations A6.1 Turnover - AP6	0.0d	2-Jun-28		0.0d
10877	MLS-AP-125	Delta Airlines Operations A6.1 - AP6 - Construction Period	200.0d	2-Jun-28	16-Mar-29	0.0d
10878	WBS - Apron Artwork Milestones		258.0d	3-Jan-28	5-Jan-29	50.0d

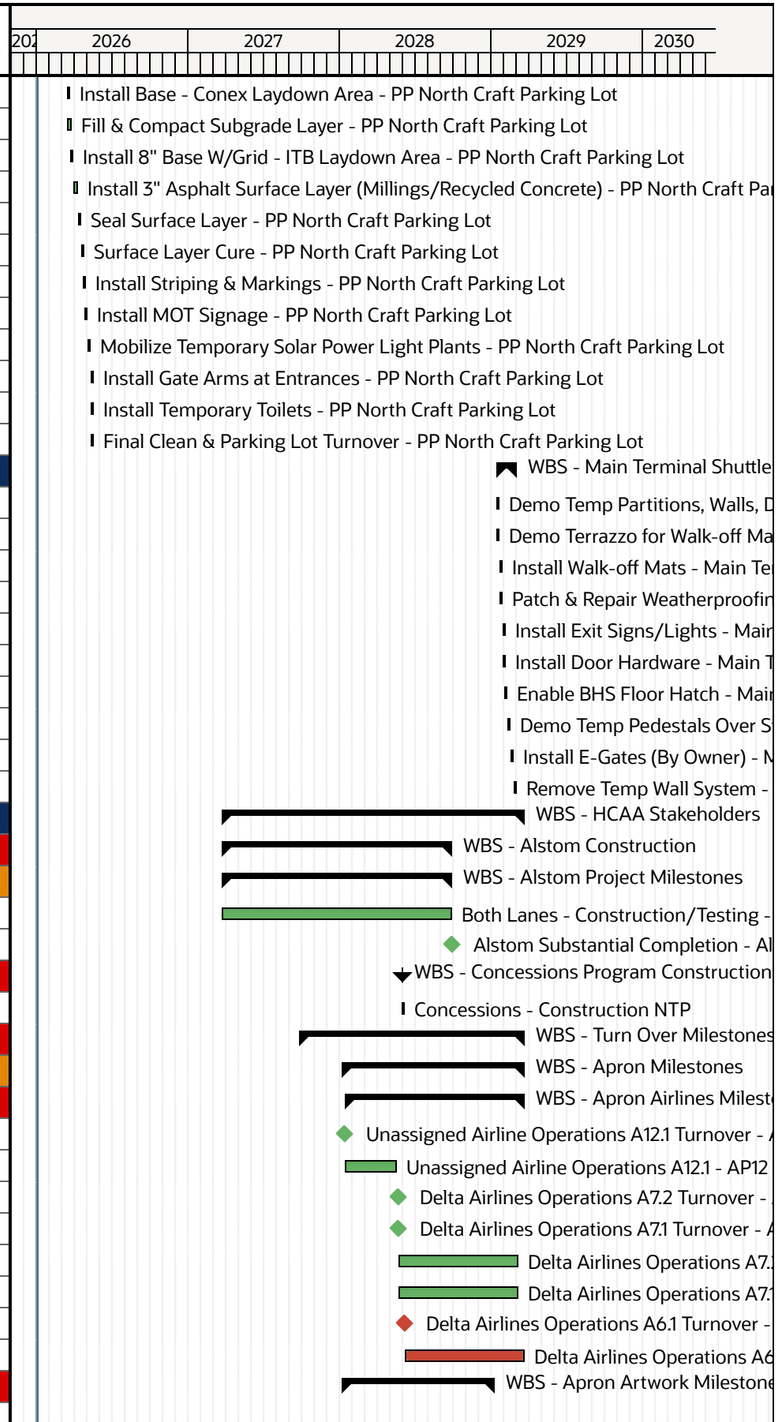


	ID	Name	Dur	Start	Finish	TF
10879	MLS-SC-AW-160	ASD1 Artwork Turnover - FIS Sterile Corridor - Turnover - SC8	0.0d	3-Jan-28		248.0d
10880	MLS-AP-AW-170	ASD2 Artwork Turnover - FIS Bag Claim East Wall - Turnover - AP5	0.0d	20-Jun-28		128.0d
10881	MLS-AP-AW-175	ASD2 Artwork Install Period - FIS Bag Claim East Wall AP5	60.0d	10-Oct-28	5-Jan-29	50.0d
10882	MLS-SC-AW-165	ASD1 Artwork Install Period - FIS Sterile Corridor SC8	60.0d	10-Oct-28	5-Jan-29	50.0d
10883	WBS - Apron Office Suite Milestones		61.0d	17-Jan-28	10-Apr-28	237.0d
10884	MLS-AP-100	AGI Offices & Break A12.2 Turnover - AP12	0.0d	17-Jan-28		97.0d
10885	MLS-AP-105	AGI Offices & Break A12.2 - AP12 - Construction Period	30.0d	17-Jan-28	25-Feb-28	268.0d
10886	MLS-AP-150	BA Storage Break & Office A11.8 Turnover - AP11	0.0d	8-Feb-28		81.0d
10887	MLS-AP-10	Unifi Break & Office A11.7 Turnover - AP11	0.0d	8-Feb-28		96.0d
10888	MLS-AP-20	Jet Aircraft Break & Office A11.10 Turnover - AP11	0.0d	8-Feb-28		96.0d
10889	MLS-AP-30	Unassigned Ops Suite A11.5 Turnover - AP11	0.0d	8-Feb-28		96.0d
10890	MLS-AP-40	Unassigned Ops Suite A11.1 Turnover - AP11	0.0d	8-Feb-28		96.0d
10891	MLS-AP-50	Unassigned Ops Suite A11.2 Turnover - AP11	0.0d	8-Feb-28		96.0d
10892	MLS-AP-60	Unassigned Ops Suite A11.4 Turnover - AP11	0.0d	8-Feb-28		96.0d
10893	MLS-AP-70	Unassigned Ops Suite A11.6 Turnover - AP11	0.0d	8-Feb-28		96.0d
10894	MLS-AP-80	FENIX Office & Break A11.9 Turnover - AP11	0.0d	8-Feb-28		96.0d
10895	MLS-AP-90	Unassigned Ops Suite A11.3 Turnover - AP11	0.0d	8-Feb-28		96.0d
10896	MLS-AP-45	Unassigned Ops Suite A11.1 AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10897	MLS-AP-65	Unassigned Ops Suite A11.4 AP11 - Construction Period	45.0d	8-Feb-28	10-Apr-28	237.0d
10898	MLS-AP-75	Unassigned Ops Suite A11.6 AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10899	MLS-AP-95	Unassigned Ops Suite A11.3 AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10900	MLS-AP-35	Unassigned Ops Suite A11.5 AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10901	MLS-AP-55	Unassigned Ops Suite A11.2 AP11 - Construction Period	20.0d	8-Feb-28	6-Mar-28	262.0d
10902	MLS-AP-25	Jet Aircraft Break & Office A11.10 T - AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10903	MLS-AP-15	Unifi Break & Office A11.7 - AP11 - Construction Period	30.0d	8-Feb-28	20-Mar-28	252.0d
10904	MLS-AP-155	BA Storage Break & Office A11.8 - AP11 - Construction Period	20.0d	8-Feb-28	6-Mar-28	262.0d
10905	MLS-AP-85	FENIX Office & Break A11.9 - AP11 - Construction Period	20.0d	8-Feb-28	6-Mar-28	262.0d
10906	WBS - Concourse Milestones		326.0d	23-Sep-27	5-Jan-29	50.0d
10907	WBS - Concourse Airlines Milestones		292.0d	7-Oct-27	30-Nov-28	74.0d
10908	MLS-CN-90	Delta Airlines In-Flight Lounge C2.2 Turnover - C2	0.0d	7-Oct-27		166.0d
10909	MLS-CN-95	Delta Airlines In-Flight Lounge C2.2 C2 - Construction Period	200.0d	7-Oct-27	20-Jul-28	166.0d
10910	MLS-CN-80	Delta Airlines Ops C1.3 Turnover C1	0.0d	27-Dec-27		112.0d
10911	MLS-CN-85	Delta Airlines Ops C1.3 C1 - Construction Period	200.0d	27-Dec-27	5-Oct-28	112.0d
10912	MLS-CN-100	Delta Airlines Club Entry & Storage C2.1 Turnover - C2	0.0d	14-Apr-28		48.0d
10913	MLS-CN-105	Delta Airlines Club Entry & Storage C2.1 - C2 - Construction Period	40.0d	14-Apr-28	9-Jun-28	194.0d
10914	MLS-CN-110	Unassigned Airline Operations C1.1 Turnover - C1	0.0d	27-Sep-28		74.0d
10915	MLS-CN-120	Unassigned Airline Operations C1.2 Turnover - C1	0.0d	27-Sep-28		89.0d
10916	MLS-CN-125	Unassigned Airline Operations C1.2 C1 - Construction Period	30.0d	27-Sep-28	7-Nov-28	89.0d
10917	MLS-CN-115	Unassigned Airline Operations C1.1 C1 - Construction Period	45.0d	27-Sep-28	30-Nov-28	74.0d
10918	WBS - Concourse Artwork Milestones		189.0d	7-Apr-28	5-Jan-29	50.0d
10919	MLS-CN-AW-180	ASD3 Artwork - Gate 47 Wall - Turnover - C7	0.0d	7-Apr-28		179.0d
10920	MLS-CN-AW-200	ASD5 Artwork - Concourse Curved Wall to Guideway -Turnover - C2	0.0d	10-Aug-28		92.0d




	ID	Name	Dur	Start	Finish	TF
10921	MLS-CN-AW-210	ASD6 Artwork - Guideway Boarding Floor - Turnover - C2	0.0d	6-Sep-28		74.0d
10922	MLS-CN-AW-190	ASD4 Artwork - South Gates 60& 61 (Ceiling Hung) - Turnover - C4	0.0d	26-Sep-28		60.0d
10923	MLS-CN-AW-215	ASD6 Artwork Install Period - Guideway Boarding Floor - C2	60.0d	10-Oct-28	5-Jan-29	50.0d
10924	MLS-CN-AW-185	ASD3 Artwork Install Period- Gate 47 Wall - C7	60.0d	10-Oct-28	5-Jan-29	50.0d
10925	MLS-CN-AW-205	ASD5 Artwork Install Period - Concourse Curved Wall to Guideway - C2	60.0d	10-Oct-28	5-Jan-29	50.0d
10926	MLS-CN-AW-195	ASD4 Artwork Install Period - South Gates 60& 61 (Ceiling Hung) - C4	60.0d	10-Oct-28	5-Jan-29	50.0d
10927	WBS - Concourse Concessions Milestones		314.0d	23-Sep-27	18-Dec-28	62.0d
10928	WBS - PAL 1 Concessions		314.0d	23-Sep-27	18-Dec-28	62.0d
10929	MLS-CN-30	Concessions Storage C1.4 - Turnover C1	0.0d	23-Sep-27		175.0d
10930	MLS-CN-200	Concessions Casual Dining C5.1 - Turnover C5	0.0d	8-Feb-28		81.0d
10931	MLS-CN-150	Concessions Bar C4.1 - Turnover C4	0.0d	11-Apr-28		36.0d
10932	MLS-CN-160	Concessions Coffee C8.8 - Turnover C8	0.0d	25-May-28		4.0d
10933	MLS-CN-10	Concessions Retail C8.1 - Turnover C8	0.0d	25-May-28		4.0d
10934	MLS-CN-20	Concessions News/Convenience C8.6 - Turnover C8	0.0d	25-May-28		4.0d
10935	MLS-CN-170	Concessions Quick Serve C9.2 - Turnover C9	0.0d	25-May-28		4.0d
10936	MLS-CN-180	Concessions Quick Serve C9.3 Turnover - C9	0.0d	25-May-28		4.0d
10937	MLS-CN-50	Concessions Gourmet Market C8.5 - Turnover C8	0.0d	25-May-28		4.0d
10938	MLS-CN-190	Concessions Quick Serve C9.1 - Turnover C9	0.0d	25-May-28		4.0d
10939	MLS-CN-60	Concessions Retail C8.3 - Turnover C8	0.0d	25-May-28		4.0d
10940	MLS-CN-70	Concessions Retail C9.4 - Turnover C9	0.0d	25-May-28		4.0d
10941	MLS-CN-35	Concessions Storage C1.4 - Construction Period C1	120.0d	25-May-28	13-Nov-28	85.0d
10942	MLS-CN-205	Concessions Casual Dining C5.1 - Construction Period C5	120.0d	25-May-28	13-Nov-28	85.0d
10943	MLS-CN-75	Concessions Retail C9.4 - Construction Period C9	120.0d	25-May-28	13-Nov-28	85.0d
10944	MLS-CN-55	Concessions Gourmet Market C8.5 - Construction Period C8	120.0d	25-May-28	13-Nov-28	85.0d
10945	MLS-CN-185	Concessions Quick Serve C9.3 - Construction Period C9	120.0d	25-May-28	13-Nov-28	85.0d
10946	MLS-CN-15	Concessions Retail C8.1 - Construction Period C8	120.0d	25-May-28	13-Nov-28	85.0d
10947	MLS-CN-165	Concessions Coffee C8.8 - Construction Period C8	120.0d	25-May-28	13-Nov-28	85.0d
10948	MLS-CN-175	Concessions Quick Serve C9.2 - Construction Period C9	120.0d	25-May-28	13-Nov-28	85.0d
10949	MLS-CN-155	Concessions Bar C4.1 - Construction Period C4	120.0d	25-May-28	13-Nov-28	85.0d
10950	MLS-CN-130	Common Use Club Entry C11.1 - Turnover C11	0.0d	1-Jun-28		0.0d
10951	MLS-CN-40	Concessions Retail C8.2 - Turnover C8	0.0d	1-Jun-28		0.0d
10952	MLS-CN-250	Concessions Future Retail C8.7 - Turnover C8	0.0d	1-Jun-28		0.0d
10953	MLS-CN-255	Concessions Future Retail C8.7 - Construction Period C8	120.0d	1-Jun-28	17-Nov-28	81.0d
10954	MLS-CN-135	Common Use Club Entry C11.1 - Construction Period C11	120.0d	1-Jun-28	17-Nov-28	81.0d
10955	MLS-CN-45	Concessions Retail C8.2- Construction Period C8	120.0d	1-Jun-28	17-Nov-28	81.0d
10956	MLS-CN-25	Concessions News/Convenience C8.6 - Construction Period C8	120.0d	28-Jun-28	18-Dec-28	62.0d
10957	MLS-CN-195	Concessions Quick Serve C9.1 - Construction Period C9	120.0d	28-Jun-28	18-Dec-28	62.0d
10958	MLS-CN-65	Concessions Retail C8.3 - Construction Period C8	120.0d	28-Jun-28	18-Dec-28	62.0d
10959	WBS - Future Conessions		85.0d	26-Apr-28	25-Aug-28	140.0d
10960	MLS-CN-230	Concessions Future F&B C6.1 Complete per 100% IFC Design - C6	0.0d		26-Apr-28	225.0d
10961	MLS-CN-240	Concessions Future F&B C8.10 Complete per 100% IFC Design - C8	0.0d		27-Jun-28	182.0d
10962	MLS-CN-220	Concessions Future Bar C5.3 Complete per 100% IFC Design - C5	0.0d		5-Jul-28	177.0d



ID	Name	Dur	Start	Finish	TF
10963	MLS-CN-140 Concessions Future Casual Dining C8.9 Complete per 100% IFC Design - C8	0.0d		28-Jul-28	160.0d
10964	MLS-CN-210 Concessions Dining C5.2 Complete per 100% IFC Design - C5	0.0d		25-Aug-28	140.0d
10965	WBS - Mezzanine Milestones	226.0d	3-Dec-27	23-Oct-28	100.0d
10966	MLS-MC-30 Future Unassigned Tenant MC2.2 Turnover - MC2	0.0d		3-Dec-27	140.0d
10967	MLS-MC-40 Delta Airlines Club MC2.1 Turnover - MC2	0.0d		10-Dec-27	100.0d
10968	MLS-MC-45 Delta Airlines Club MC2.1 Construction Period	221.0d	13-Dec-27	23-Oct-28	100.0d
10969	MLS-MC-10 Common Use Club & Terrace MC3.1 Turnover - MC3	0.0d		5-Jan-28	104.0d
10970	MLS-MC-20 Future Unassigned Tenant MC3.2 Turnover - MC3	0.0d	6-Jan-28		119.0d
10971	MLS-MC-15 Common Use Club & Terrace MC3.1 - Construction Period	200.0d	6-Jan-28	16-Oct-28	105.0d
10972	MLS-MC-25 Future Unassigned Tenant MC3.2 - Construction Period	100.0d	25-May-28	16-Oct-28	105.0d
10973	MLS-MC-35 Future Unassigned Tenant MC2.2 - Construction Period	100.0d	25-May-28	16-Oct-28	105.0d
10974	WBS - Invitation To Bid (ITB)	939.0d	19-Jun-25 A	1-Mar-29	11.0d
10975	WBS - ITB -1 - Apron Pavement & Hydrant Fueling Construction	925.0d	19-Jun-25 A	9-Feb-29	25.0d
10976	WBS - Inter Project Relationships (IPR)	925.0d	19-Jun-25 A	9-Feb-29	25.0d
10977	IPR-ITB1-MLS31 ITB1 Overall Project Duration SC 9.30.2028	1,187.0d	19-Jun-25 A	15-Oct-28 C	148.0d
10978	IPR-ITB1-MLS18 MLS18 - Enabling Works - Demo Exist. AOA Fence - Phase C Complete	0.0d		22-Aug-25 A	
10979	IPR-ITB1-MLS19 MLS - Demolition of Half of the Tunnel Structure Complete	0.0d		3-Oct-25 A	
10980	IPR-ITB1-MLS1 MLS1 - Start Fuel Main Re-route (Crisdel)	0.0d	21-Oct-25 A		
10981	IPR-ITB1-MLS20 MLS20 - Fuel Main Install Complete (Crisdel)	0.0d		30-Jan-26 C	0.0d
10982	IPR-ITB1-MLS21 MLS21 - New Apron Cured & Ready for AOA Fence Relocation (Crisdel)	0.0d		30-Jun-26 C	0.0d
10983	IPR-ITB1-MLS14 MLS14 - ASD Contractor Job Site Trailer (FOB) Demobilized (HP)	0.0d		31-Jul-26 C	666.0d
10984	IPR-ITB1-MLS7 MLS7 - East Side Retaining Wall Complete (HP)	0.0d		9-Nov-26	366.0d
10985	IPR-ITB1-MLS6 MLS6 - West Side Retaining Wall Complete (HP)	0.0d		18-May-27	254.0d
10986	IPR-ITB1-MLS8 MLS8 - Condensate Drainage Pipe Complete (HP)	0.0d		31-Aug-27	391.0d
10987	IPR-ITB1-MLS11 MLS11 - Install of ASD Building Waterline Complete (HP)	0.0d		27-Oct-27	351.0d
10988	IPR-ITB1-MLS13 MLS13 - Telecom Conduit Install Complete (HP)	0.0d		17-Nov-27	336.0d
10989	IPR-ITB1-MLS16 MLS16 - EFSO Conduit Install Completed (Bldg. Interface) (HP)	0.0d		17-Nov-27	336.0d
10990	IPR-ITB1-MLS9-17 MLS9-17 - EFSO Duct Bank to Fuel Vault Complete (HP)	0.0d		19-Nov-27	334.0d
10991	IPR-ITB1-MLS12 MLS12 - GSE Paving Operations Complete (HP)	5.0d		1-Mar-28	246.0d
10992	IPR-ITB1-MLS41 ITB1 Project Complete	0.0d		15-Oct-28 C	148.0d
10993	IPR-ITB1-MLS15 MLS15 - Demolition of Access Drive Completed (HP)	0.0d		9-Feb-29	25.0d
10994	WBS - ITB -2- Passenger Boarding Bridges (PBB) Construction	285.0d	18-Jan-28	1-Mar-29	11.0d
10995	WBS - Inter Project Relationships (IPR)	285.0d	18-Jan-28	1-Mar-29	11.0d
10996	IPR-ASD-ITB2-80 ASD - Quadrant 4 Ready for ITB2 PBB Install (HP)	0.0d		18-Jan-28	125.0d
10997	IPR-ASD-ITB2-60 ASD - Quadrant 2 Ready for ITB2 PBB Install (HP)	0.0d		3-Feb-28	113.0d
10998	IPR-ASD-ITB2-70 ASD - Quadrant 3 Ready for ITB2 PBB Install (HP)	0.0d		22-Feb-28	100.0d
10999	IPR-ASD-ITB2-50 ASD - Glycol, Power, Data & LV Ready for ITB2 PBB Install (HP)	0.0d		13-Jul-28	0.0d
11000	IPR-ASD-ITB2-90 ITB2 - Phase 1 Overall Duration - Onsite Construction & Testing (By Others)	160.0d	14-Jul-28	1-Mar-29	11.0d
11001	WBS - ITB - 3 - Guideway Superstructure Construction	781.0d	25-Aug-25 A	20-Sep-28	123.0d
11002	WBS - Inter Project Relationships (IPR)	781.0d	25-Aug-25 A	20-Sep-28	123.0d
11003	IPR-ASD-ITB3-210 ITB 3 - Total Project Duration SC 2.16.2027 (By Others)	556.0d	25-Aug-25 A	16-Mar-27	169.0d
11004	IPR-ASD-ITB3-90 ITB 3 - Pier 2 Drilled Shafts (By Others)	14.0d	4-Feb-26 C	23-Feb-26	272.0d

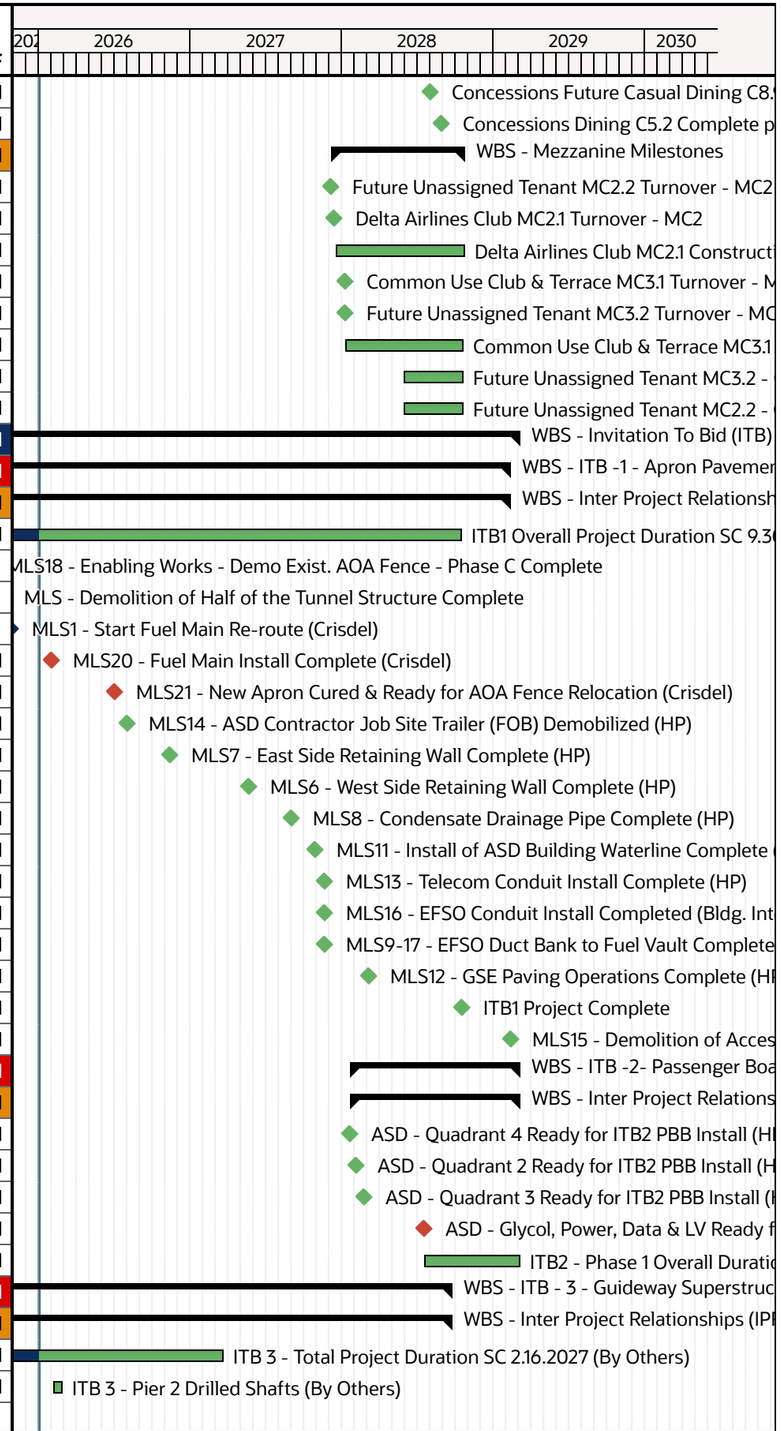

ID	Name	Dur	Start	Finish	TF
11005	IPR-ASD-ITB3-140	ITB 3 - Pier 1 Drilled Shafts (By Others)	11.0d	24-Feb-26 C	10-Mar-26	272.0d
11006	IPR-ASD-ITB3-180	ITB 3 - Pier 2 Construction (By Others)	86.0d	24-Feb-26 C	24-Jun-26	308.0d
11007	IPR-ASD-ITB3-150	ITB 3 - Pier 1 Construction (By Others)	111.0d	12-Mar-26 C	17-Aug-26	271.0d
11008	IPR-ASD-ITB3-120	ITB 3 - Span 2 Beams (Pier 3 - Pier 2) (By Others)	6.0d	19-Jun-26 C	26-Jun-26	144.0d
11009	IPR-ASD-ITB3-190	ITB 3 - Span 2 Superstructure (Pier 3 - Pier 2) (By Others)	16.0d	1-Jul-26 C	18-Jul-26	201.0d
11010	IPR-ASD-ITB3-170	ITB 3 - Span 1 Beams (Pier 2 - Pier 1) (By Others)	4.0d	6-Aug-26 C	11-Aug-26	129.0d
11011	IPR-ASD-ITB3-200	ITB 3 - Span 1 Superstructure (Pier 2 - Pier 1) (By Others)	10.0d	18-Aug-26 C	31-Aug-26	125.0d
11012	IPR-ASD-ITB3-110	ITB 3 - Guideway Superstructure Ready for ASD BHS Install (By Others)	0.0d		15-Oct-26 C	411.0d
11013	IPR-ASD-ITB3-220	ITB 3 Project Complete	540.0d	17-Mar-27	20-Sep-28	173.0d
11014	WBS - ASD - COMMISSIONING PHASE		1,076.0d	29-Dec-25	21-Mar-30	0.0d
11015	WBS - ASD - Commissioning - Administrative		290.0d	29-Dec-25	17-Feb-27	786.0d
11016	COM-ADM-100	Develop & Submit Cx Plan (Design) - Admin Commissioning	15.0d	29-Dec-25	19-Jan-26	785.0d
11017	COM-ADM-110	Review & Approve Cx Plan (Design) - Admin Commissioning	20.0d	20-Jan-26	16-Feb-26	785.0d
11018	COM-ADM-120	Approved Sequence of Operations - Admin Commissioning	0.0d		16-Feb-26	785.0d
11019	COM-ADM-130	Develop & Submit Cx Plan (Construction) - Admin Commissioning	15.0d	17-Feb-26	9-Mar-26	785.0d
11020	COM-ADM-140	Review & Approve Cx Plan (Construction) - Admin Commissioning	20.0d	10-Mar-26	6-Apr-26	785.0d
11021	COM-ADM-150	Develop & Submit PFC Checklist Template - Admin Commissioning	35.0d	7-Apr-26	26-May-26	785.0d
11022	COM-ADM-160	Review & Approve PFC Checklist Template - Admin Commissioning	20.0d	27-May-26	23-Jun-26	785.0d
11023	COM-ADM-170	Develop & Submit FPT & IST Scripts - Admin Commissioning	105.0d	24-Jun-26	19-Nov-26	785.0d
11024	COM-ADM-180	Review & Approve FPT & IST Scripts - Admin Commissioning	20.0d	20-Nov-26	21-Dec-26	785.0d
11025	COM-ADM-190	Submit Completed PFC - Admin Commissioning	0.0d		21-Dec-26	785.0d
11026	COM-ADM-195	Review & Approve Completed PFC - Admin Commissioning	20.0d	22-Dec-26	20-Jan-27	785.0d
11027	COM-ADM-200	Submit Final Cx Report Milestone - Admin Commissioning	0.0d		20-Jan-27	785.0d
11028	COM-ADM-210	Review & Approve Final Commissioning Report - Admin Commissioning	20.0d	21-Jan-27	17-Feb-27	785.0d
11029	WBS - Final Commissioning/Punchlist		574.0d	20-Dec-27	21-Mar-30	0.0d
11030	WBS - Internal Punch List Development		514.0d	20-Dec-27	26-Dec-29	0.0d
11031	FCPL-40	Skin & Envelope - Internal Completion / Punchlist Development	15.0d	20-Dec-27	11-Jan-28	413.0d
11032	FCPL-30	Club Level - Internal Completion / Punchlist Development	15.0d	23-Feb-28	14-Mar-28	368.0d
11033	FCPL-50	Civil - Internal Completion / Punchlist Development	15.0d	8-Mar-28	28-Mar-28	358.0d
11034	FCPL-70	Concourse Level - Internal Completion / Punchlist Development	15.0d	15-Nov-28	7-Dec-28	181.0d
11035	FCPL-20	Apron Level - Internal Completion / Punchlist Development	15.0d	29-Nov-28	19-Dec-28	173.0d
11036	FCPL-60	Sterile Level - Internal Completion / Punchlist Development	15.0d	14-Dec-28	5-Jan-29	162.0d
11037	FCPL-150	CCBS - Internal Completion / Punchlist Development	15.0d	14-Dec-28	5-Jan-29	182.0d
11038	FCPL-10	Owner Final Commissioning/Punchlist Development Phase 1 (ASD & CCBS)	65.0d	5-Mar-29	4-Jun-29	142.0d
11039	FCPL-160	CCBS Post-ISAT - Internal Completion / Punchlist Development	15.0d	31-Aug-29	21-Sep-29	0.0d
11040	FCPL-170	Owner Final Commissioning/Punchlist Development Phase 2 (ASD & CCBS)	65.0d	24-Sep-29	26-Dec-29	0.0d
11041	WBS - Internal Punch List Completion		559.0d	12-Jan-28	21-Mar-30	0.0d
11042	FCPL-120	Skin & Envelope - Internal Completion / Punchlist Completion	20.0d	12-Jan-28	8-Feb-28	413.0d
11043	FCPL-80	Club Level - Internal Completion / Punchlist Completion	20.0d	15-Mar-28	11-Apr-28	368.0d
11044	FCPL-110	Civil - Internal Completion / Punchlist Completion	20.0d	29-Mar-28	25-Apr-28	358.0d
11045	FCPL-130	Concourse Level - Internal Completion / Punchlist Completion	20.0d	8-Dec-28	8-Jan-29	181.0d
11046	FCPL-90	Apron Level - Internal Completion / Punchlist Completion	20.0d	20-Dec-28	18-Jan-29	173.0d

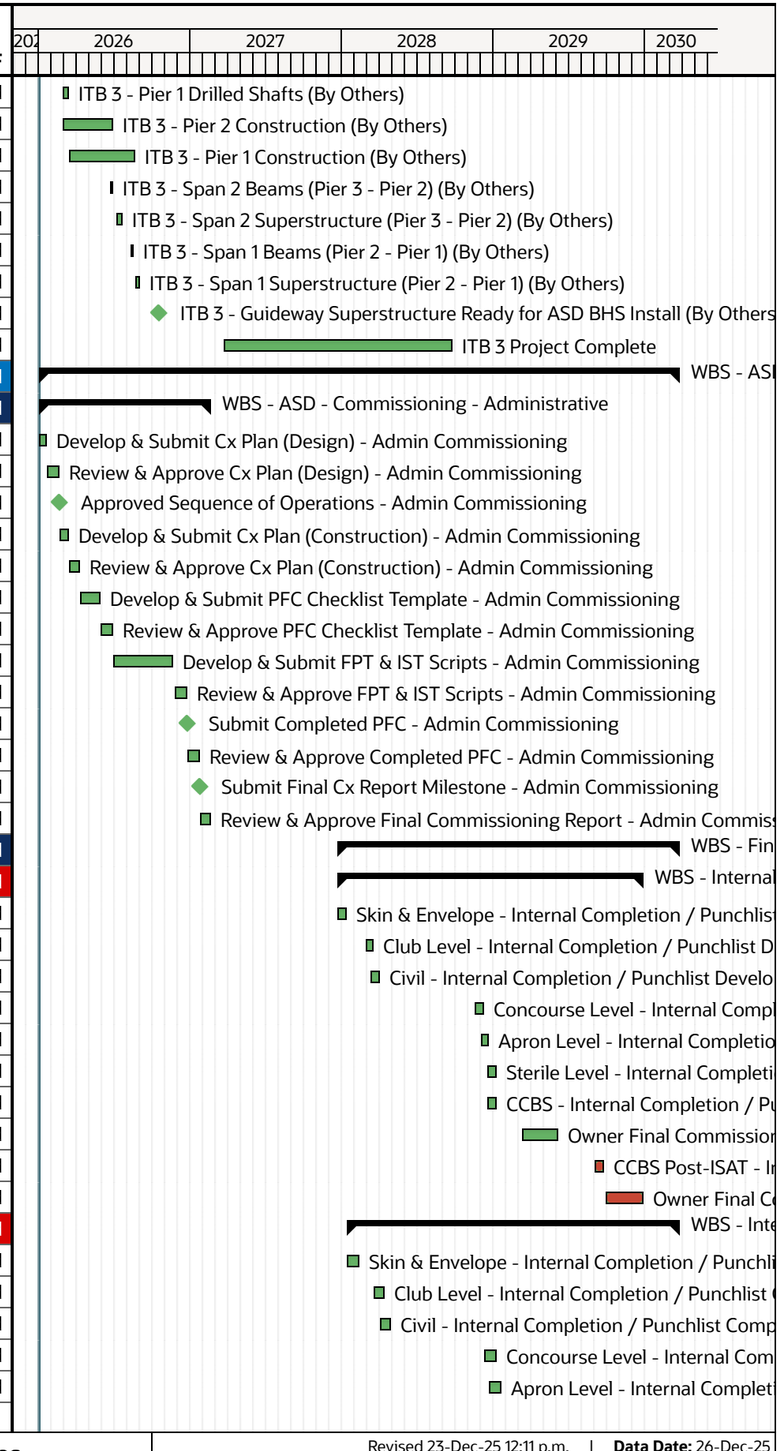

HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport

ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25

Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:11 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
11047	A110460	CCBS - Internal Completion / Punchlist Completion	20.0d	8-Jan-29	2-Feb-29	227.0d
11048	FCPL-140	Sterile Level - Internal Completion / Punchlist Completion	20.0d	8-Jan-29	2-Feb-29	162.0d
11049	FCPL-100	Owner Final Commissioning/Punchlist Completion Phase 1 (ASD & CCBS)	60.0d	5-Jun-29	28-Aug-29	142.0d
11050	A110470	CCBS Post-ISAT - Internal Completion / Punchlist Completion	20.0d	24-Sep-29	19-Oct-29	45.0d
11051	FCPL-180	Owner Final Commissioning/Punchlist Completion Phase 2 (ASD & CCBS)	60.0d	27-Dec-29	21-Mar-30	0.0d
11052	WBS - ASD - Commissioning - Electrical		87.0d	4-Aug-28	7-Dec-28	49.0d
11053	WBS - ASD - Commissioning - Emergency Power (Electrical)		81.0d	4-Aug-28	29-Nov-28	55.0d
11054	COM-ELE-170	Approve Equip. from Outside Agency Testing - Emer. Power Elec. Commissioning	15.0d	4-Aug-28	24-Aug-28	16.0d
11055	COM-ELE-180	Vendor Startup - Emer. Power Elec. Commissioning	15.0d	25-Aug-28	15-Sep-28	16.0d
11056	COM-ELE-190	Integrate Equip. with BAS (includes submetering) - Emer. Power Elec. Commissi…	10.0d	18-Sep-28	29-Sep-28	16.0d
11057	COM-ELE-200	Perform Pre-FPT - Emer. Power Elec. Commissioning	5.0d	2-Oct-28	6-Oct-28	16.0d
11058	COM-ELE-210	Perform FPT - Emer. Power Elec. Commissioning	20.0d	9-Oct-28	3-Nov-28	16.0d
11059	COM-ELE-230	Perform Owner Training - Emer. Power Elec. Commissioning	16.0d	6-Nov-28	29-Nov-28	55.0d
11060	WBS - ASD - Commissioning - Main Distribution Power (Electrical)		81.0d	4-Aug-28	29-Nov-28	55.0d
11061	COM-ELE-240	Approve Equip. from Outside Agency Testing - Main Dist. Power Elec. Commiss…	15.0d	4-Aug-28	24-Aug-28	16.0d
11062	COM-ELE-250	Vendor Startup - Main Dist. Power Elec. Commissioning	15.0d	25-Aug-28	15-Sep-28	16.0d
11063	COM-ELE-260	Integrate Equip. with BAS (includes submetering) - Main Dist. Power Elec. Com…	10.0d	18-Sep-28	29-Sep-28	16.0d
11064	COM-ELE-270	Perform Pre-FPT - Main Dist. Power Elec. Commissioning	5.0d	2-Oct-28	6-Oct-28	16.0d
11065	COM-ELE-280	Perform FPT - Main Dist. Power Elec. Commissioning	20.0d	9-Oct-28	3-Nov-28	16.0d
11066	COM-ELE-300	Perform Owner Training - Main Dist. Power Elec. Commissioning	16.0d	6-Nov-28	29-Nov-28	55.0d
11067	WBS - ASD - Commissioning - Lighting Controls (Electrical)		87.0d	4-Aug-28	7-Dec-28	49.0d
11068	COM-ELE-310	Approve Equip. from Outside Agency Testing - Light. Controls Elec. Commissio…	15.0d	4-Aug-28	24-Aug-28	21.0d
11069	COM-ELE-380	Owner/Designer/Developer Lighting Operation Review - Light. Controls Elec. C…	15.0d	4-Aug-28	24-Aug-28	31.0d
11070	COM-ELE-320	Vendor Startup - Light. Controls Elec. Commissioning	15.0d	25-Aug-28	15-Sep-28	21.0d
11071	COM-ELE-330	Integrate Equip. with BAS (includes submetering) - Light. Controls Elec. Commi…	10.0d	18-Sep-28	29-Sep-28	21.0d
11072	COM-ELE-400	Lighting Controls Programming Interior/White Light- Light. Controls Elec. Com…	5.0d	26-Sep-28	2-Oct-28	10.0d
11073	COM-ELE-410	Lighting Controls Programming Theatrical Light. Controls Elec. Commissioning	5.0d	3-Oct-28	9-Oct-28	10.0d
11074	COM-ELE-390	Lighting Controls Programming RGB Light. Controls Elec. Commissioning	5.0d	10-Oct-28	16-Oct-28	10.0d
11075	COM-ELE-340	Perform Pre-FPT - Light. Controls Elec. Commissioning	5.0d	17-Oct-28	23-Oct-28	10.0d
11076	COM-ELE-350	Perform FPT - Light. Controls Elec. Commissioning	15.0d	24-Oct-28	13-Nov-28	10.0d
11077	COM-ELE-370	Perform Owner Training - Light. Controls Elec. Commissioning	16.0d	14-Nov-28	7-Dec-28	49.0d
11078	WBS - ASD - Commissioning - Mechanical		191.0d	28-Feb-28	27-Nov-28	57.0d
11079	COM-M&P-10	Vendor Startup - Mech. Start-Up AP12 CUP Room #6079	15.0d	28-Feb-28	17-Mar-28	108.0d
11080	COM-M&P-20	Vendor Startup - Mech. Start-Up CN2 AHU Room #6459	5.0d	28-Feb-28	3-Mar-28	128.0d
11081	COM-M&P-70	Vendor Startup - Mech. Start-Up AP7 AHU Room #6190	5.0d	2-Mar-28	8-Mar-28	116.0d
11082	COM-M&P-330	BAS Integration - Mech. Start-Up CN2 AHU Room #6459	5.0d	6-Mar-28	10-Mar-28	128.0d
11083	MLS-1230	BAS Integration - Mech. Start-Up AP7 AHU Room #6190	5.0d	9-Mar-28	15-Mar-28	125.0d
11084	COM-M&P-530	Perform Test & Balance - AHU-1-3 Apron	6.0d	13-Mar-28	20-Mar-28	163.0d
11085	COM-M&P-480	Perform Test & Balance - AHU-2-9 Concourse	6.0d	13-Mar-28	20-Mar-28	163.0d
11086	COM-M&P-550	Perform Test & Balance - AHU-2-3 Concourse	6.0d	16-Mar-28	23-Mar-28	160.0d
11087	COM-M&P-340	BAS Integration - Mech. Start-Up AP12 CUP Room #6079	15.0d	20-Mar-28	7-Apr-28	108.0d
11088	COM-M&P-690	Submit TAB Report - AHU-2-9 Concourse	2.0d	21-Mar-28	22-Mar-28	163.0d




	ID	Name	Dur	Start	Finish	TF
11089	COM-M&P-790	Submit TAB Report - AHU-1-3 Apron	2.0d	21-Mar-28	22-Mar-28	163.0d
11090	COM-M&P-700	Review & Approve TAB Report - AHU-2-9 Concourse	10.0d	23-Mar-28	5-Apr-28	163.0d
11091	COM-M&P-800	Review & Approve TAB Report - AHU-1-3 Apron	10.0d	23-Mar-28	5-Apr-28	163.0d
11092	COM-M&P-830	Submit TAB Report - AHU-2-3 Concourse	2.0d	24-Mar-28	27-Mar-28	160.0d
11093	COM-M&P-840	Review & Approve TAB Report - AHU-2-3 Concourse	10.0d	28-Mar-28	10-Apr-28	160.0d
11094	COM-M&P-620	Perform Test & Balance - CUP - AHU-1-6 Apron	6.0d	10-Apr-28	17-Apr-28	143.0d
11095	COM-M&P-40	Vendor Startup - Mech. Start-Up AP10 AHU Room #6007	4.0d	17-Apr-28	20-Apr-28	85.0d
11096	COM-M&P-950	Submit TAB Report - CUP - AHU-1-6 Apron	2.0d	18-Apr-28	19-Apr-28	143.0d
11097	COM-M&P-960	Review & Approve TAB Report - CUP - AHU-1-6 Apron	10.0d	20-Apr-28	3-May-28	143.0d
11098	MLS-1200	BAS Integration - Mech. Start-Up AP10 AHU Room #6007	4.0d	21-Apr-28	26-Apr-28	95.0d
11099	COM-M&P-510	Perform Test & Balance - AHU-1-1 Apron	6.0d	27-Apr-28	4-May-28	130.0d
11100	COM-M&P-440	Perform Test & Balance - AHU-1.5-3 Sterr. Corr.	6.0d	27-Apr-28	4-May-28	130.0d
11101	COM-M&P-750	Submit TAB Report - AHU-1-1 Apron	2.0d	5-May-28	8-May-28	130.0d
11102	COM-M&P-1110	Submit TAB Report - AHU-1.5-3 Sterr. Corr.	2.0d	5-May-28	8-May-28	130.0d
11103	COM-M&P-50	Vendor Startup - Mech. Start-Up AP5 Trash Room #6299	2.0d	8-May-28	9-May-28	84.0d
11104	COM-M&P-760	Review & Approve TAB Report - AHU-1-1 Apron	10.0d	9-May-28	22-May-28	130.0d
11105	COM-M&P-1120	Review & Approve TAB Report - AHU-1.5-3 Sterr. Corr.	10.0d	9-May-28	22-May-28	130.0d
11106	MLS-1210	BAS Integration - Mech. Start-Up AP5 Trash Room #6299	2.0d	10-May-28	11-May-28	84.0d
11107	COM-M&P-30	Vendor Startup - Mech. Start-Up CL1 AHU Room #6682	3.0d	11-May-28	15-May-28	79.0d
11108	COM-M&P-350	BAS Integration - Mech. Start-Up CL1 AHU Room #6682	3.0d	16-May-28	18-May-28	79.0d
11109	COM-M&P-580	Perform Test & Balance - AHU-3-1 Club	6.0d	19-May-28	26-May-28	114.0d
11110	COM-M&P-590	Perform Test & Balance - AHU-3-2 Club	6.0d	19-May-28	26-May-28	114.0d
11111	COM-M&P-460	Perform Test & Balance - AHU-2-6 Concourse	6.0d	19-May-28	26-May-28	114.0d
11112	COM-M&P-470	Perform Test & Balance - AHU-2-1.1 & AHU-2-1.2 Concourse	6.0d	25-May-28	2-Jun-28	108.0d
11113	COM-M&P-650	Submit TAB Report - AHU-2-6 Concourse	2.0d	30-May-28	31-May-28	114.0d
11114	COM-M&P-870	Submit TAB Report - AHU-3-1 Club	2.0d	30-May-28	31-May-28	114.0d
11115	COM-M&P-890	Submit TAB Report -AHU-3-2 Club	2.0d	30-May-28	31-May-28	114.0d
11116	COM-M&P-660	Review & Approve TAB Report - AHU-2-6 Concourse	10.0d	1-Jun-28	14-Jun-28	114.0d
11117	COM-M&P-880	Review & Approve TAB Report - AHU-3-1 Club	10.0d	1-Jun-28	14-Jun-28	114.0d
11118	COM-M&P-900	Review & Approve TAB Report -AHU-3-2 Club	10.0d	1-Jun-28	14-Jun-28	114.0d
11119	COM-M&P-520	Perform Test & Balance - AHU-1-2 Apron	6.0d	2-Jun-28	9-Jun-28	105.0d
11120	COM-M&P-670	Submit TAB Report - AHU-2-1.1 & AHU-2-1.2 Concourse	2.0d	5-Jun-28	6-Jun-28	108.0d
11121	COM-M&P-680	Review & Approve TAB Report - AHU-2-1.1 & AHU-2-1.2 Concourse	10.0d	7-Jun-28	20-Jun-28	108.0d
11122	COM-M&P-770	Submit TAB Report - AHU-1-2 Apron	2.0d	12-Jun-28	13-Jun-28	105.0d
11123	COM-M&P-600	Perform Test & Balance - AHU-0-2 Apron	6.0d	13-Jun-28	20-Jun-28	98.0d
11124	COM-M&P-780	Review & Approve TAB Report - AHU-1-2 Apron	10.0d	14-Jun-28	27-Jun-28	105.0d
11125	COM-M&P-490	Perform Test & Balance - AHU-2-10 Concourse	6.0d	19-Jun-28	26-Jun-28	94.0d
11126	COM-M&P-910	Submit TAB Report - AHU-0-2 Apron	2.0d	21-Jun-28	22-Jun-28	98.0d
11127	COM-M&P-920	Review & Approve TAB Report - AHU-0-2 Apron	10.0d	23-Jun-28	7-Jul-28	98.0d
11128	COM-M&P-710	Submit TAB Report -AHU-2-10 Concourse	2.0d	27-Jun-28	28-Jun-28	94.0d
11129	COM-M&P-720	Review & Approve TAB Report -AHU-2-10 Concourse	10.0d	29-Jun-28	13-Jul-28	94.0d
11130	COM-M&P-390	Perform Test & Balance - AHU-1.5-1 Sterr. Corr.	6.0d	7-Jul-28	14-Jul-28	81.0d




	ID	Name	Dur	Start	Finish	TF
11131	COM-M&P-420	Perform Test & Balance - AHU-1.5-2 Sterr. Corr.	6.0d	7-Jul-28	14-Jul-28	81.0d
11132	COM-M&P-1010	Submit TAB Report - AHU-1.5-1 Sterr. Corr.	2.0d	17-Jul-28	18-Jul-28	81.0d
11133	COM-M&P-1070	Submit TAB Report - AHU-1.5-2 Sterr. Corr.	2.0d	17-Jul-28	18-Jul-28	81.0d
11134	COM-M&P-1020	Review & Approve TAB Report - AHU-1.5-1 Sterr. Corr.	10.0d	19-Jul-28	1-Aug-28	81.0d
11135	COM-M&P-1080	Review & Approve TAB Report - AHU-1.5-2 Sterr. Corr.	10.0d	19-Jul-28	1-Aug-28	81.0d
11136	COM-M&P-450	Perform Test & Balance - AHU-2-5 Concourse	6.0d	24-Jul-28	31-Jul-28	52.0d
11137	COM-M&P-60	Vendor Startup - Mech. Start-Up AP6 AHU Room #6191	8.0d	26-Jul-28	4-Aug-28	16.0d
11138	COM-M&P-630	Submit TAB Report -AHU-2-5 Concourse	2.0d	1-Aug-28	2-Aug-28	52.0d
11139	COM-M&P-640	Review & Approve TAB Report -AHU-2-5 Concourse	10.0d	3-Aug-28	16-Aug-28	52.0d
11140	COM-M&P-400	Perform Test & Balance - AHU-2-4.1 & AHU-2-4.2 Concourse	6.0d	4-Aug-28	11-Aug-28	59.0d
11141	COM-M&P-122	BAS Integration - Mech. Start-Up AP6 AHU Room #6191	8.0d	7-Aug-28	16-Aug-28	17.0d
11142	COM-M&P-380	Perform Test & Balance - AHU-2-2 Concourse	6.0d	7-Aug-28	14-Aug-28	60.0d
11143	COM-M&P-560	Perform Test & Balance - AHU-2-7 Concourse	6.0d	10-Aug-28	17-Aug-28	57.0d
11144	COM-M&P-1030	Submit TAB Report - AHU-2-4.1 & AHU-2-4.2 Concourse	2.0d	14-Aug-28	15-Aug-28	59.0d
11145	COM-M&P-990	Submit TAB Report - AHU-2-2 Concourse	2.0d	15-Aug-28	16-Aug-28	60.0d
11146	COM-M&P-1040	Review & Approve TAB Report - AHU-2-4.1 & AHU-2-4.2 Concourse	10.0d	16-Aug-28	29-Aug-28	59.0d
11147	COM-M&P-130	BAS Programming - Mech. Commissioning	30.0d	17-Aug-28	28-Sep-28	17.0d
11148	COM-M&P-410	Perform Test & Balance - AHU-0-1 Apron	6.0d	17-Aug-28	24-Aug-28	52.0d
11149	COM-M&P-610	Perform Test & Balance - AHU-0-3 Apron	6.0d	17-Aug-28	24-Aug-28	52.0d
11150	COM-M&P-1000	Review & Approve TAB Report - AHU-2-2 Concourse	10.0d	17-Aug-28	30-Aug-28	60.0d
11151	COM-M&P-850	Submit TAB Report - AHU-2-7 Concourse	2.0d	18-Aug-28	21-Aug-28	57.0d
11152	COM-M&P-860	Review & Approve TAB Report - AHU-2-7 Concourse	10.0d	22-Aug-28	5-Sep-28	57.0d
11153	COM-M&P-930	Submit TAB Report -AHU-0-3 Apron	2.0d	25-Aug-28	28-Aug-28	52.0d
11154	COM-M&P-1050	Submit TAB Report - AHU-0-1 Apron	2.0d	25-Aug-28	28-Aug-28	52.0d
11155	COM-M&P-940	Review & Approve TAB Report -AHU-0-3 Apron	10.0d	29-Aug-28	12-Sep-28	52.0d
11156	COM-M&P-1060	Review & Approve TAB Report - AHU-0-1 Apron	10.0d	29-Aug-28	12-Sep-28	52.0d
11157	COM-M&P-540	Perform Test & Balance - AHU-1-4 Apron	6.0d	30-Aug-28	7-Sep-28	43.0d
11158	COM-M&P-810	Submit TAB Report - AHU-1-4 Apron	2.0d	8-Sep-28	11-Sep-28	43.0d
11159	COM-M&P-820	Review & Approve TAB Report - AHU-1-4 Apron	10.0d	12-Sep-28	25-Sep-28	43.0d
11160	COM-M&P-570	Perform Test & Balance - AHU-2-8 Concourse	6.0d	20-Sep-28	27-Sep-28	29.0d
11161	COM-M&P-970	Submit TAB Report - AHU-2-8 Concourse	2.0d	28-Sep-28	29-Sep-28	29.0d
11162	COM-M&P-1150	Perform pre-FPT AHU-2-10 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11163	COM-M&P-1160	Perform pre-FPT AHU-2-7 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11164	COM-M&P-1210	Perform pre-FPT AHU-1.5-3 - Sterr. Corr. Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11165	COM-M&P-1220	Perform pre-FPT AHU-2-3 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11166	COM-M&P-1240	Perform Pre-FPT AHU-0-2 - Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11167	COM-M&P-1250	Perform Pre-FPT AHU-0-3 - Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11168	COM-M&P-1260	Perform Pre-FPT AHU-1-2 - Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11169	COM-M&P-1270	Perform pre-FPT AHU-2-6 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11170	COM-M&P-1280	Perform Pre-FPT AHU-2-1.1 & 2-1.2 - Sterr. Corr. Mech. Commissioning (5 day...	10.0d	29-Sep-28	12-Oct-28	28.0d
11171	COM-M&P-1130	Perform pre-FPT AHU-1-3 - Apron Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11172	COM-M&P-1140	Perform pre-FPT AHU-2-9 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d

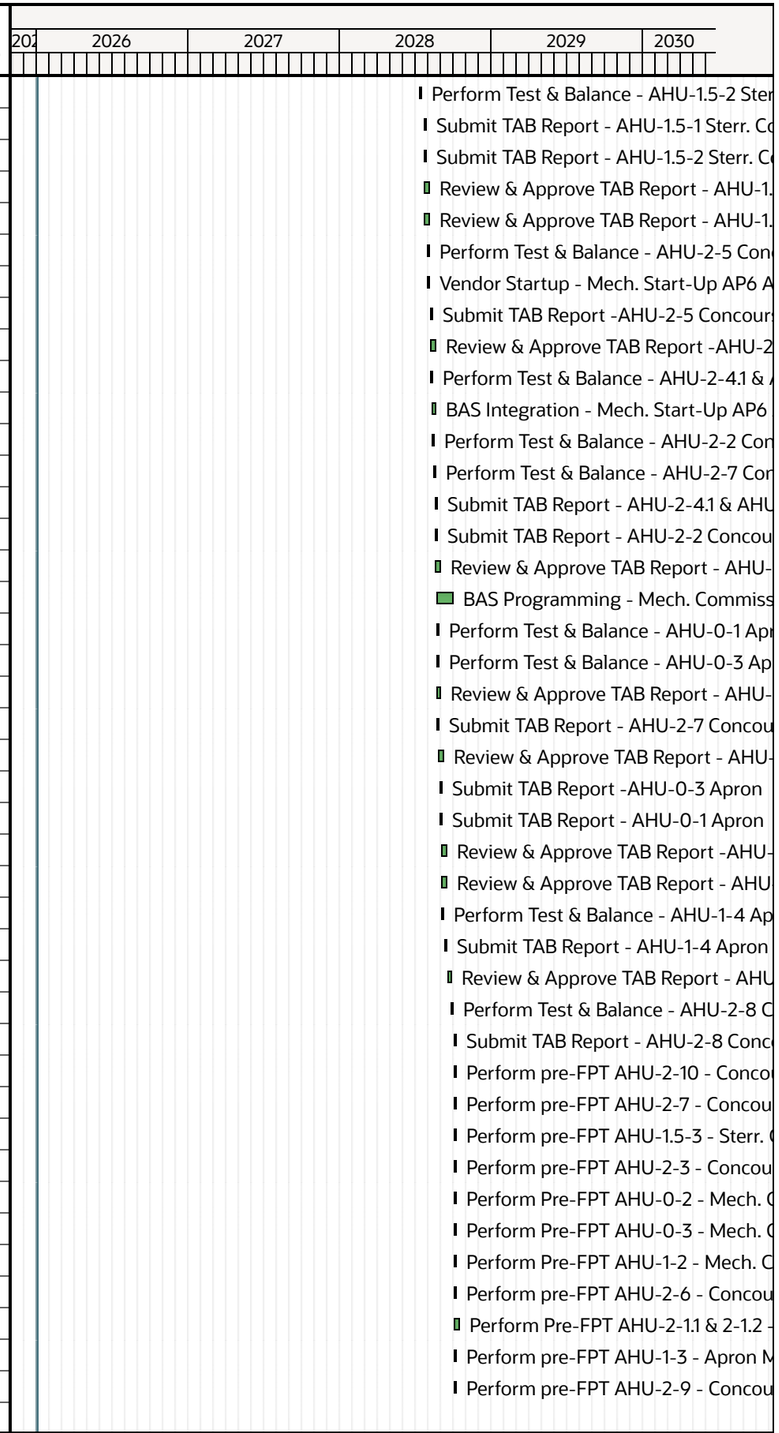


	ID	Name	Dur	Start	Finish	TF
11173	COM-M&P-1170	Perform Pre-FPT AHU-1-1 - Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11174	COM-M&P-1180	Perform pre-FPT AHU-1-6 - Apron Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11175	COM-M&P-1190	Perform pre-FPT AHU-3-1 - Club Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11176	COM-M&P-1200	Perform pre-FPT AHU-3-2 -Club Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11177	COM-M&P-1290	Perform Pre-FPT AHU-0-1 - Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11178	COM-M&P-1300	Perform pre-FPT AHU-1-4 - Apron Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11179	COM-M&P-1310	Perform pre-FPT AHU-1.5-1 - Sterr. Corr. Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11180	COM-M&P-1320	Perform pre-FPT AHU-1.5-2 - Sterr. Corr. Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11181	COM-M&P-1330	Perform pre-FPT AHU-2-4.1 & 2-4.2 - Concourse Mech. Commissioning (5 day...	5.0d	29-Sep-28	5-Oct-28	33.0d
11182	COM-M&P-1340	Perform pre-FPT AHU-2-2 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	35.0d
11183	COM-M&P-1350	Perform pre-FPT AHU-2-5 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	29-Sep-28	5-Oct-28	17.0d
11184	COM-M&P-980	Review & Approve TAB Report - AHU-2-8 Concourse	10.0d	2-Oct-28	13-Oct-28	29.0d
11185	COM-M&P-1230	Perform pre-FPT AHU-2-8 - Concourse Mech. Commissioning (5 days per AHU)	5.0d	2-Oct-28	6-Oct-28	34.0d
11186	COM-M&P-190	Perform FPT AHU-1-3 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11187	COM-M&P-1390	Perform FPT AHU-2-9 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11188	COM-M&P-1400	Perform FPT AHU-2-10 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11189	COM-M&P-1410	Perform FPT AHU-2-7 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11190	COM-M&P-1420	Perform FPT AHU-1-1 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11191	COM-M&P-1360	Perform FPT AHU-1-6 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11192	COM-M&P-1370	Perform FPT AHU-3-1 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11193	COM-M&P-1380	Perform FPT AHU-3-2 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11194	COM-M&P-1430	Perform FPT AHU-1.5-3 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11195	COM-M&P-1440	Perform FPT AHU-2-3 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11196	COM-M&P-1460	Perform FPT AHU-0-2 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11197	COM-M&P-1470	Perform FPT AHU-0-3 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11198	COM-M&P-1480	Perform FPT AHU-1-2 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11199	COM-M&P-1490	Perform FPT AHU-2-6 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11200	COM-M&P-1520	Perform FPT AHU-0-1 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11201	COM-M&P-1530	Perform FPT AHU-1-4 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11202	COM-M&P-1540	Perform FPT AHU-1.5-1 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11203	COM-M&P-1550	Perform FPT AHU-1.5-2 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11204	COM-M&P-1560	Perform FPT AHU-2-4.1 & 2-4.2 - Mech. Commissioning (2 days per AHU)	4.0d	6-Oct-28	11-Oct-28	33.0d
11205	COM-M&P-1570	Perform FPT AHU-2-2 - Mech. Commissioning (2 days per AHU)	2.0d	6-Oct-28	9-Oct-28	35.0d
11206	COM-M&P-1580	Perform FPT AHU-2-5 - Mech. Commissioning (2 days per AHU)	20.0d	6-Oct-28	2-Nov-28	17.0d
11207	COM-M&P-1500	Perform FPT AHU-2-1.1 & 2-1.2 - Mech. Commissioning (2 days per AHU)	4.0d	13-Oct-28	18-Oct-28	28.0d
11208	COM-M&P-1450	Perform FPT AHU-2-8 - Mech. Commissioning (2 days per AHU)	2.0d	16-Oct-28	17-Oct-28	29.0d
11209	COM-M&P-210	Perform Owner Training - Mech. Commissioning	15.0d	3-Nov-28	27-Nov-28	57.0d
11210	WBS - ASD - Commissioning - Plumbing		60.0d	17-Jul-28	9-Oct-28	90.0d
11211	COM-M&P-370	Flush & Chlorinate - Plumbing Commissioning	5.0d	17-Jul-28	21-Jul-28	45.0d
11212	COM-M&P-250	Vendor Startup - Plumbing Commissioning	5.0d	24-Jul-28	28-Jul-28	45.0d
11213	COM-M&P-260	Integrate Equip. with BAS (includes submetering) - Plumbing Commissioning	5.0d	31-Jul-28	4-Aug-28	45.0d
11214	COM-M&P-270	BAS Programming - Plumbing Commissioning	5.0d	7-Aug-28	11-Aug-28	45.0d

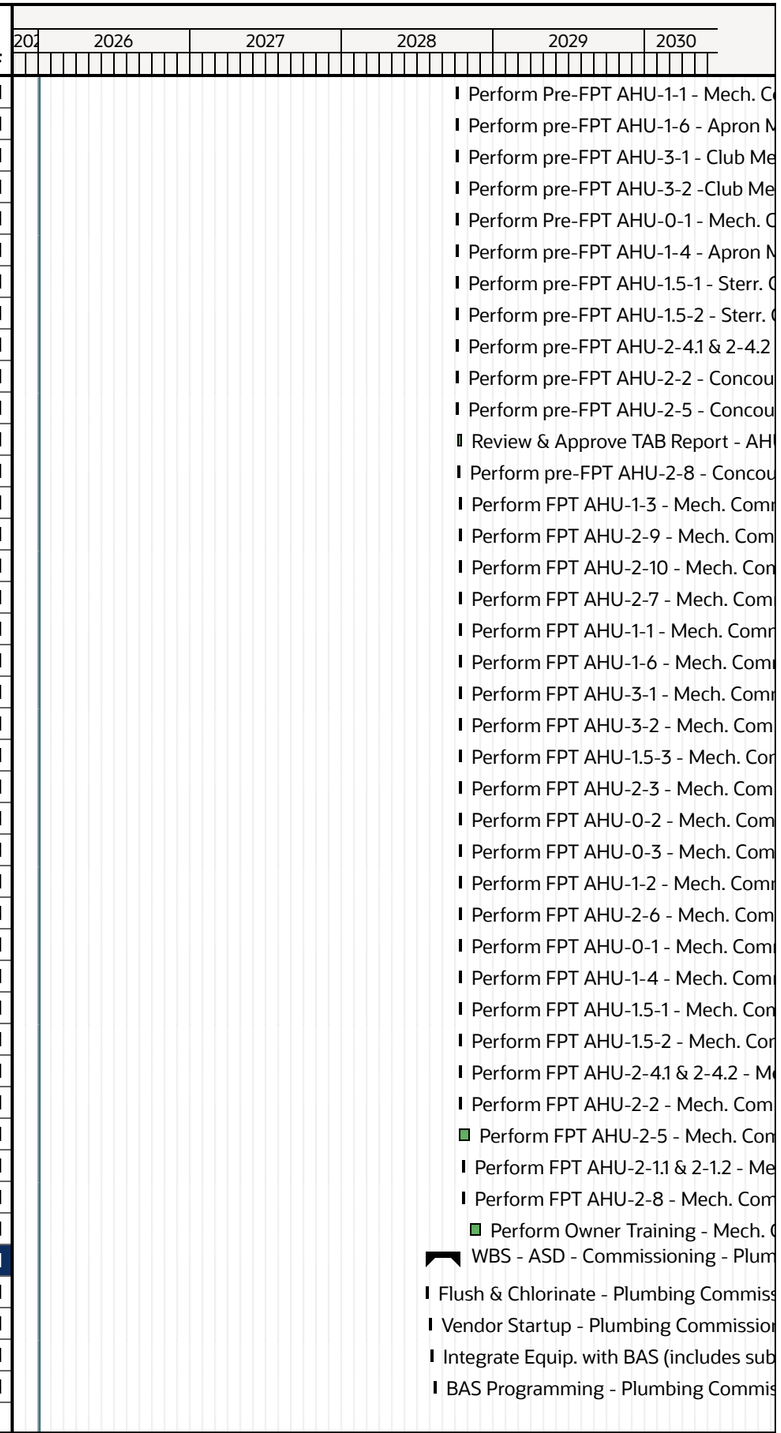


	ID	Name	Dur	Start	Finish	TF
11215	COM-M&P-320	Perform Water Test & Balance - Plumbing Commissioning	5.0d	14-Aug-28	18-Aug-28	45.0d
11216	COM-M&P-280	Perform Pre-FPT - Plumbing Commissioning	5.0d	21-Aug-28	25-Aug-28	45.0d
11217	COM-M&P-290	Perform FPT - Plumbing Commissioning	5.0d	19-Sep-28	25-Sep-28	45.0d
11218	COM-M&P-310	Perform Owner Training - Plumbing Commissioning	10.0d	26-Sep-28	9-Oct-28	90.0d
11219	WBS - Operational Readiness Activation & Transition (ORAT)		110.0d	26-Sep-28	2-Mar-29	0.0d
11220	ORAT-10	ORAT Initiation - Operational Readiness Activation & Transition (ORAT)	110.0d	26-Sep-28	2-Mar-29	0.0d
11221	WBS - ASD - Commissioning - Fire Alarm		73.0d	3-Aug-28	15-Nov-28	63.0d
11222	COM-FLS-100	Fire Alarm Ready to Pre-Test - Fire Alarm Commissioning	0.0d		3-Aug-28	56.0d
11223	COM-FLS-140	Perform Owner Training - Fire Alarm Commissioning	4.0d	10-Nov-28	15-Nov-28	63.0d
11224	WBS - ASD - Commissioning - Fire/Life Safety Door & Pull Stations FA Testing		30.0d	19-Sep-28	30-Oct-28	25.0d
11225	COM-FLS-145	Pre-Test Fire Alarm Loop Check - Door & Pull Stations FA Testing	15.0d	19-Sep-28	9-Oct-28	25.0d
11226	COM-FLS-150	Pre-Test Fire Alarm - Door & Pull Stations FA Testing	15.0d	10-Oct-28	30-Oct-28	25.0d
11227	WBS - ASD - Commissioning - Fire/Life Safety Mechanical FA Testing		30.0d	29-Sep-28	9-Nov-28	17.0d
11228	COM-FLS-165	Pre-Test Fire Alarm Loop Check - Mech. FA Testing	15.0d	29-Sep-28	19-Oct-28	17.0d
11229	COM-FLS-170	Pre-Test Fire Alarm - Mech. FA Testing	15.0d	20-Oct-28	9-Nov-28	17.0d
11230	WBS - ASD - Commissioning - Fire/Life Safety BHS FA Testing		30.0d	4-Aug-28	15-Sep-28	56.0d
11231	COM-FLS-185	Pre-Test Fire Alarm Loop Check - BHS FA Testing	15.0d	4-Aug-28	24-Aug-28	56.0d
11232	COM-FLS-190	Pre-Test Fire Alarm - BHS FA Testing	15.0d	25-Aug-28	15-Sep-28	56.0d
11233	WBS - ASD - Commissioning - Fire/Life Safety Fire Protection FA Testing		30.0d	4-Aug-28	15-Sep-28	56.0d
11234	COM-FLS-205	Pre-Test Fire Alarm Loop Check - Fire Protection FA Testing	15.0d	4-Aug-28	24-Aug-28	56.0d
11235	COM-FLS-210	Pre-Test Fire Alarm - Fire Protection FA Testing	15.0d	25-Aug-28	15-Sep-28	56.0d
11236	WBS - ASD - Commissioning - Security		25.0d	19-Sep-28	23-Oct-28	80.0d
11237	COM-SEC-95	Vendor Startup Loop Checks - Security Commissioning	10.0d	19-Sep-28	2-Oct-28	27.0d
11238	COM-SEC-100	Vendor Startup - Security Commissioning	10.0d	3-Oct-28	16-Oct-28	27.0d
11239	COM-SEC-110	Perform Integrated System Testing (IST) - Security Commissioning	3.0d	17-Oct-28	19-Oct-28	27.0d
11240	COM-SEC-120	Perform Owner Training - Security Commissioning	2.0d	20-Oct-28	23-Oct-28	80.0d
11241	WBS - ASD - Commissioning - Vertical Transport		12.0d	10-Nov-28	29-Nov-28	55.0d
11242	COM-VT-120	Perform Owner Training - Vertical Transp. Commissioning	2.0d	28-Nov-28	29-Nov-28	55.0d
11243	WBS - ASD - Commissioning - Vertical Transport Elev. #1 & #2		10.0d	10-Nov-28	27-Nov-28	55.0d
11244	VC-EL-AP3-2480	Testing of FA Recall/Generator - Service(#1)/Freight Elevator(#2) - INTR - AP 3	2.0d	10-Nov-28	13-Nov-28	55.0d
11245	VC-EL-AP3-2140	State Elevator Insp. - Service (#1)/Freight Elevator (#2) - INTR - AP 3	3.0d	14-Nov-28	16-Nov-28	55.0d
11246	VC-EL-AP3-2150	Punchlist Completion - Service(#1)/Freight Elevator(#2) - INTR - AP 3	3.0d	17-Nov-28	21-Nov-28	55.0d
11247	VC-EL-AP3-2260	Acceptance By State Elevator Inspector - Service(#1)/Freight Elevator(#2) - IN...	2.0d	22-Nov-28	27-Nov-28	55.0d
11248	WBS - ASD - Commissioning - Vertical Transport Elev. #3 & #4		10.0d	10-Nov-28	27-Nov-28	55.0d
11249	VC-EL-AP1-2010	Testing of FA Recall/Generator - Service(#4)/Freight Elevator(#3) - INTR - AP 1	2.0d	10-Nov-28	13-Nov-28	55.0d
11250	VC-EL-AP1-1670	State Elevator Insp. - Service (#4)/Freight Elevator (#3) - INTR - AP 1	3.0d	14-Nov-28	16-Nov-28	55.0d
11251	VC-EL-AP1-1680	Punchlist Completion - Service(#4)/Freight Elevator(#3) - INTR - AP 1	3.0d	17-Nov-28	21-Nov-28	55.0d
11252	VC-EL-AP1-1690	Acceptance By State Elevator Inspector - Service(#4)/Freight Elevator(#3) - IN...	2.0d	22-Nov-28	27-Nov-28	55.0d
11253	WBS - ASD - Commissioning - Vertical Transport Elev. #5		10.0d	10-Nov-28	27-Nov-28	55.0d
11254	VC-EL-AP5-2280	Testing of FA Recall/Generator - Service(#5) - INTR - AP 5	2.0d	10-Nov-28	13-Nov-28	55.0d
11255	VC-EL-AP5-2140	State Elevator Insp. - Service(#5) - INTR - AP 5	3.0d	14-Nov-28	16-Nov-28	55.0d
11256	VC-EL-AP5-2150	Punchlist Completion - Service(#5) - INTR - AP 5	3.0d	17-Nov-28	21-Nov-28	55.0d

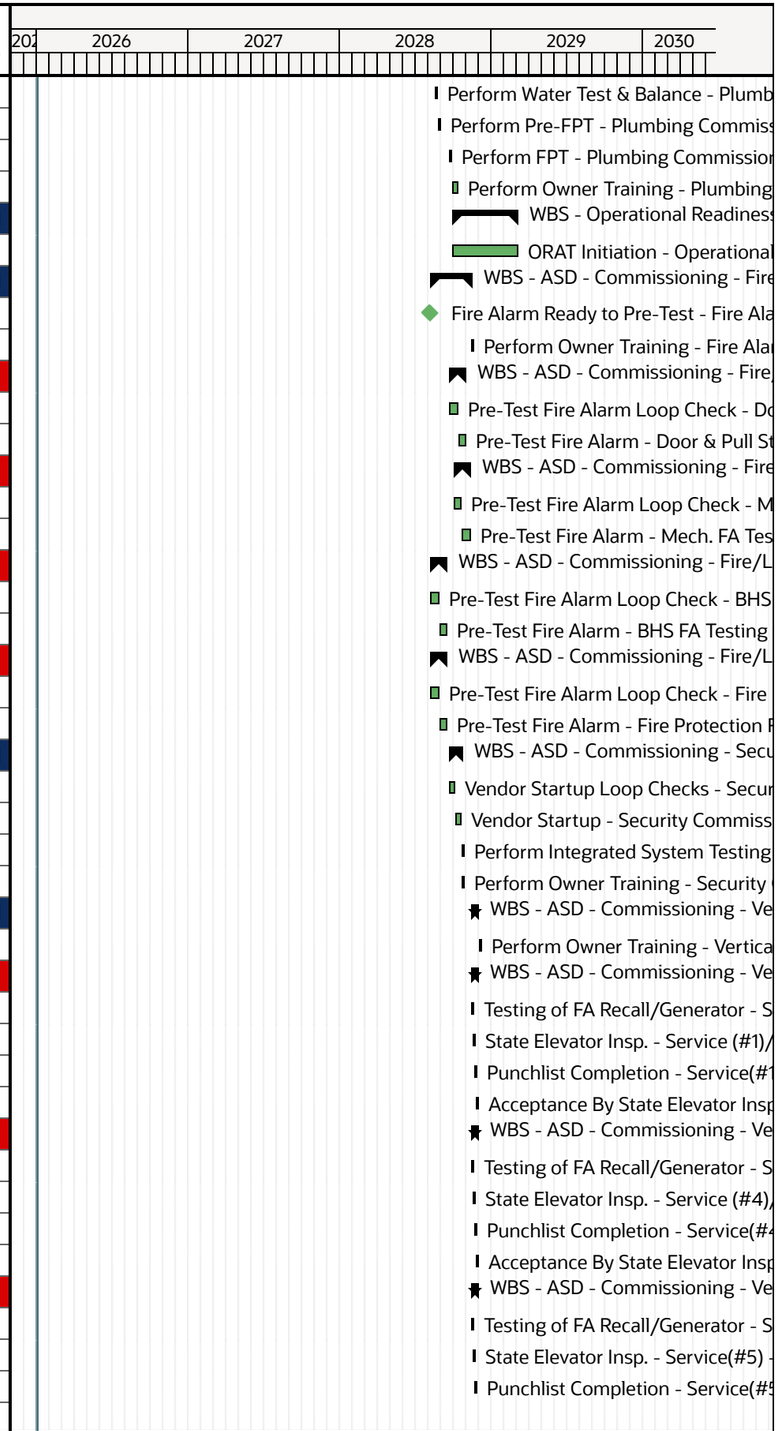


	ID	Name	Dur	Start	Finish	TF
11257	VC-EL-AP5-2160	Acceptance By State Elevator Inspector - Service(#5) - INTR - AP 5	2.0d	22-Nov-28	27-Nov-28	55.0d
11258	WBS - ASD - Commissioning - Vertical Transport Elev. #6 & #7		10.0d	10-Nov-28	27-Nov-28	55.0d
11259	VC-EL-AP8-3330	Testing of FA Recall/Generator - Service (#6 & #7) Elevator Cabs/Shaft - INTR ...	2.0d	10-Nov-28	13-Nov-28	55.0d
11260	VC-EL-AP8-2980	State Elevator Insp. - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3.0d	14-Nov-28	16-Nov-28	55.0d
11261	VC-EL-AP8-2990	Punchlist Completion - Service (#6 & #7) Elevator Cabs/Shaft - INTR - AP 8	3.0d	17-Nov-28	21-Nov-28	55.0d
11262	VC-EL-AP8-3000	Acceptance By State Elevator Inspector - Service (#6 & #7) Elevator Cabs/Shaf...	2.0d	22-Nov-28	27-Nov-28	55.0d
11263	WBS - ASD - Commissioning - Vertical Transport Elev. #8		10.0d	10-Nov-28	27-Nov-28	55.0d
11264	VC-EL-AP6-2600	Testing of FA Recall/Generator - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	2.0d	10-Nov-28	13-Nov-28	55.0d
11265	VC-EL-AP6-2470	State Elevator Insp. - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	3.0d	14-Nov-28	16-Nov-28	55.0d
11266	VC-EL-AP6-2480	Punchlist Completion - Service (#8) Elevator Cabs/Shaft - INTR - AP 6	3.0d	17-Nov-28	21-Nov-28	55.0d
11267	VC-EL-AP6-2490	Acceptance By State Elevator Inspector - Service (#8) Elevator Cabs/Shaft - IN...	2.0d	22-Nov-28	27-Nov-28	55.0d
11268	WBS - ASD - Commissioning - Vertical Transport Elev. #9, #10, & #11		10.0d	10-Nov-28	27-Nov-28	55.0d
11269	VC-EL-AP5-4150	Testing of FA Recall/Generator - Passenger (#9, 10, 11) Elevator Cabs/Shaft - I...	2.0d	10-Nov-28	13-Nov-28	55.0d
11270	VC-EL-AP5-4020	State Elevator Insp. - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	3.0d	14-Nov-28	16-Nov-28	55.0d
11271	VC-EL-AP5-4030	Punchlist Completion - Passenger (#9, 10, 11) Elevator Cabs/Shaft - INTR - AP 5	3.0d	17-Nov-28	21-Nov-28	55.0d
11272	VC-EL-AP5-4040	Acceptance By State Elevator Inspector - Passenger (#9, 10, 11) Elevator Cabs/...	2.0d	22-Nov-28	27-Nov-28	55.0d
11273	WBS - ASD - Commissioning - Vertical Transport Elev. #12 & #13		10.0d	10-Nov-28	27-Nov-28	55.0d
11274	VC-EL-C2-3910	Testing of FA Recall/Generator - Passenger (#12 & #13) Elevator Cabs/Shaft - I...	2.0d	10-Nov-28	13-Nov-28	55.0d
11275	VC-EL-C2-3780	State Elevator Insp. - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	3.0d	14-Nov-28	16-Nov-28	55.0d
11276	VC-EL-C2-3790	Punchlist Completion - Passenger (#12 & #13) Elevator Cabs/Shaft - INTR - C2	3.0d	17-Nov-28	21-Nov-28	55.0d
11277	VC-EL-C2-3800	Acceptance By State Elevator Inspector - Passenger (#12 & #13) Elevator Cabs...	2.0d	22-Nov-28	27-Nov-28	55.0d
11278	WBS - ASD - Commissioning - Vertical Transport Elev. #14 & #15		10.0d	10-Nov-28	27-Nov-28	55.0d
11279	VC-EL-C11-3670	Testing of FA Recall/Generator - Service (#14 & #15) Elevator Cabs/Shaft - INT...	2.0d	10-Nov-28	13-Nov-28	55.0d
11280	VC-EL-C11-3540	State Elevator Insp. - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	3.0d	14-Nov-28	16-Nov-28	55.0d
11281	VC-EL-C11-3550	Punchlist Completion - Service (#14 & #15) Elevator Cabs/Shaft - INTR - C11	3.0d	17-Nov-28	21-Nov-28	55.0d
11282	VC-EL-C11-3560	Acceptance By State Elevator Inspector - Service (#14 & #15) Elevator Cabs/Sh...	2.0d	22-Nov-28	27-Nov-28	55.0d
11283	WBS - ASD - Commissioning - Vertical Transport Escalator #1 & #2		10.0d	10-Nov-28	27-Nov-28	55.0d
11284	VC-ESC-AP8-3410	Testing of FA Recall/Generator - Escalator (#1 & #2) - INTR - AP 8	2.0d	10-Nov-28	13-Nov-28	55.0d
11285	VC-ESC-AP8-3420	State Elevator Insp. - Escalator (#1 & #2) - INTR - AP 8	3.0d	14-Nov-28	16-Nov-28	55.0d
11286	VC-ESC-AP8-3430	Punchlist Completion - Escalator (#1 & #2) - INTR - AP 8	3.0d	17-Nov-28	21-Nov-28	55.0d
11287	VC-ESC-AP8-3440	Acceptance By State Elevator Inspector - Escalator (#1 & #2) - INTR - AP 8	2.0d	22-Nov-28	27-Nov-28	55.0d
11288	WBS - ASD - Commissioning - Vertical Transport Escalator #3 & #4		10.0d	10-Nov-28	27-Nov-28	55.0d
11289	VC-ESC-AP5-2340	Testing of FA Recall/Generator - Escalator (#3 & #4) - INTR - AP5	2.0d	10-Nov-28	13-Nov-28	55.0d
11290	VC-ESC-AP5-2350	State Elevator Insp. - Escalator (#3 & #4) - INTR - AP 5	3.0d	14-Nov-28	16-Nov-28	55.0d
11291	VC-ESC-AP5-2360	Punchlist Completion - Escalator (#3 & #4) - INTR - AP 5	3.0d	17-Nov-28	21-Nov-28	55.0d
11292	VC-ESC-AP5-2370	Acceptance By State Elevator Inspector - Escalator (#3 & #4) - INTR - AP 5	2.0d	22-Nov-28	27-Nov-28	55.0d
11293	WBS - ASD - Commissioning - Security Screening Checkpoints Construction (SSCP)		20.0d	4-Oct-28	31-Oct-28	74.0d
11294	SSCP-30	Commissioning - SSCP Equip. (By Others)	20.0d	4-Oct-28	31-Oct-28	19.0d
11295	SSCP-40	SSCP Operational - SSCP Equip. (By Others)	0.0d		31-Oct-28	74.0d
11296	WBS - ASD - Commissioning - Security Screening Checkpoints Construction (CBP)		20.0d	11-Oct-28	7-Nov-28	69.0d
11297	SSCP-50	Commissioning - CBP Equip. (By Others)	20.0d	11-Oct-28	7-Nov-28	14.0d
11298	SSCP-60	CBP Operational - CBP Equip. (By Others)	0.0d		7-Nov-28	69.0d

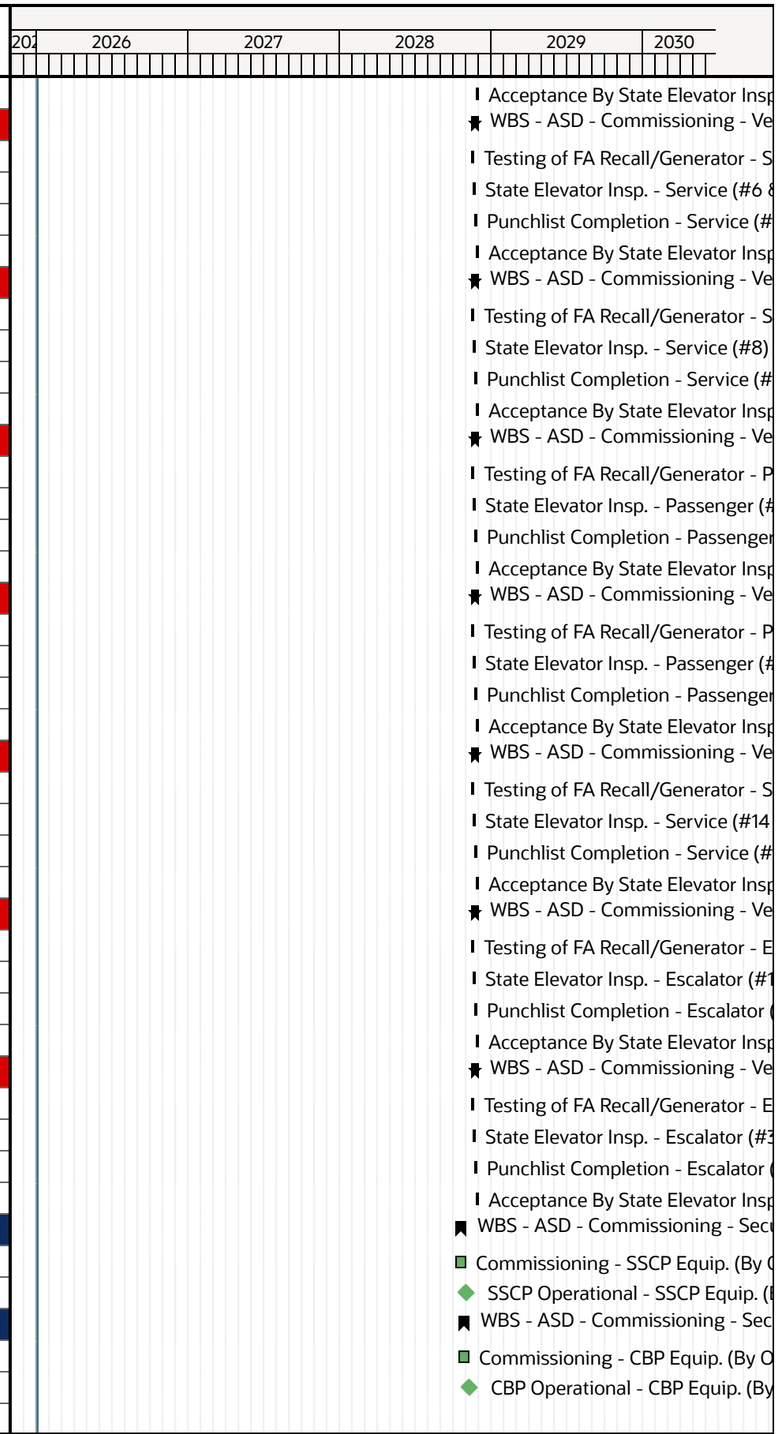


ID	Name	Dur	Start	Finish	TF
11299	WBS - ASD - Commissioning - IST/Life Safety	251.0d	8-Mar-28	2-Mar-29	0.0d
11300	A109700 ASD - COT Utilities Final Inspections - IST/Life Safety	10.0d	8-Mar-28	21-Mar-28	186.0d
11301	A109710 ASD - COT Site Final Inspections - IST/Life Safety	10.0d	8-Mar-28	21-Mar-28	186.0d
11302	A109660 ASD - COT Plumbing Final Inspections - IST/Life Safety	10.0d	26-Sep-28	9-Oct-28	45.0d
11303	A109670 ASD - COT Mech. Final Inspections - IST/Life Safety	10.0d	3-Nov-28	16-Nov-28	17.0d
11304	A109690 ASD - COT Low Voltage Final Inspections - IST/Life Safety	10.0d	8-Nov-28	21-Nov-28	14.0d
11305	A109680 ASD - COT Elec.Final Inspections - IST/Life Safety	10.0d	14-Nov-28	29-Nov-28	10.0d
11306	A109720 ASD - COT Fire Alarm Final Inspections - IST/Life Safety	10.0d	21-Nov-28	6-Dec-28	10.0d
11307	A109730 ASD - COT AHJ Life Safety Final Inspections (TCO) - IST/Life Safety	5.0d	14-Dec-28	20-Dec-28	5.0d
11308	A109740 ASD - COT Building Final Inspections (TCO) - IST/Life Safety	5.0d	21-Dec-28	28-Dec-28	5.0d
11309	A110440 ASD - COT AHJ Life Safety Final Inspections (CO)- IST/Life Safety	5.0d	19-Feb-29	23-Feb-29	0.0d
11310	A110450 ASD - COT Building Final Inspections (CO) - IST/Life Safety	5.0d	26-Feb-29	2-Mar-29	0.0d
11311	WBS - ASD - PROJECT CLOSEOUT PHASE	198.0d	5-Mar-29	11-Dec-29	70.0d
11312	WBS - ASD - Project Closeout Management	198.0d	5-Mar-29	11-Dec-29	70.0d
11313	CO-CLO-PM-10 Supplement C Project Closeout - Phase 1 (ASD)	80.0d	5-Mar-29	25-Jun-29	187.0d
11314	CO-CLO-PM-20 Supplement C Project Closeout - Phase 2 (CCBS)	60.0d	17-Sep-29	11-Dec-29	70.0d
11315	WBS - CENTRALIZED CHECKED BAGGAGE SYSTEM RELOCATION AND UPGRADES	1,103.0d	8-Aug-25 A	11-Dec-29	70.0d
11316	WBS - CCBS - DESIGN & ENGINEERING PHASE	76.0d	8-Aug-25 A	24-Nov-25 A	
11317	WBS - CFRP - Design	76.0d	8-Aug-25 A	24-Nov-25 A	
11318	CFRP-CC-DD-100 CFRP - Kick off Structural Requirements - Basis of Design (BOD)	1.0d	8-Aug-25 A	8-Aug-25 A	
11319	CFRP-CC-DD-110 CFRP - Design Proposal (HNTB-Base) Submit to HP	2.0d	11-Aug-25 A	12-Aug-25 A	
11320	WBS - CFRP Design Document Part 1	37.0d	13-Aug-25 A	3-Oct-25 A	
11321	CFRP-CC-DD-120 CFRP - Basis of Design Documents - Part 1	28.0d	13-Aug-25 A	22-Sep-25 A	
11322	CFRP-CC-DD-130 CFRP - Submit Part 1 Documents - Base to HNTB	1.0d	23-Sep-25 A	23-Sep-25 A	
11323	CFRP-CC-DD-140 CFRP - HNTB Review & Submit Documents to Structural Tec / HP Part 1	1.0d	23-Sep-25 A	23-Sep-25 A	
11324	CFRP-CC-DD-150 CFRP - Structural Tec. Design Part 1 (first 2 sectors)	3.0d	24-Sep-25 A	26-Sep-25 A	
11325	CFRP-CC-DD-160 CFRP - Structural Tec. Submits Design Part 1 (first 2 sectors)	5.0d	29-Sep-25 A	3-Oct-25 A	
11326	WBS - CFRP Design Document Part 2	44.0d	24-Sep-25 A	24-Nov-25 A	
11327	CFRP-CC-DD-170 CFRP - Basis of Design Documents - Part 2	9.0d	24-Sep-25 A	6-Oct-25 A	
11328	CFRP-CC-DD-175 CFRP - Submit Part 2 Documents - Base to HNTB	1.0d	7-Oct-25 A	7-Oct-25 A	
11329	CFRP-CC-DD-180 CFRP - HNTB Review & Submit Documents to Structural Tec / HP Part 2	1.0d	8-Oct-25 A	8-Oct-25 A	
11330	CFRP-CC-DD-185 CFRP - Structural Tec. Design Part 2 (second 2 sectors)	8.0d	9-Oct-25 A	20-Oct-25 A	
11331	CFRP-CC-DD-190 CFRP - Structural Tec. Submits Design Part 2 (second 2 sectors)	1.0d	21-Oct-25 A	21-Oct-25 A	
11332	CFRP-CC-DD-200 CFRP - DB / Structural Tec. Verification Review	1.0d	22-Oct-25 A	22-Oct-25 A	
11333	CFRP-CC-DD-210 CFRP - Base to Respond to Comment (as applicable)	1.0d	23-Oct-25 A	23-Oct-25 A	
11334	CFRP-CC-DD-220 CFRP Contract Finalization	20.0d	28-Oct-25 A	24-Nov-25 A	
11335	WBS - CCBS - PROCUREMENT PHASE	1,057.0d	14-Oct-25 A	11-Dec-29	70.0d
11336	WBS - Owner Furnished Contractor Installed (OFCI)	84.0d	14-Oct-25 A	12-Feb-26	81.0d
11337	WBS - Tag & Trace Submittals	84.0d	14-Oct-25 A	12-Feb-26	81.0d
11338	WBS - Electrical Tag & Trace Submittals	41.0d	14-Oct-25 A	11-Dec-25 A	
11339	A64120 Prep & Submit Product Data for Elec. Tag & Trace Relocation	11.0d	14-Oct-25 A	28-Oct-25 A	
11340	A106440 Review & Approve (HP) Product Data for Elec.Tag & Trace Relocation	4.0d	29-Oct-25 A	3-Nov-25 A	

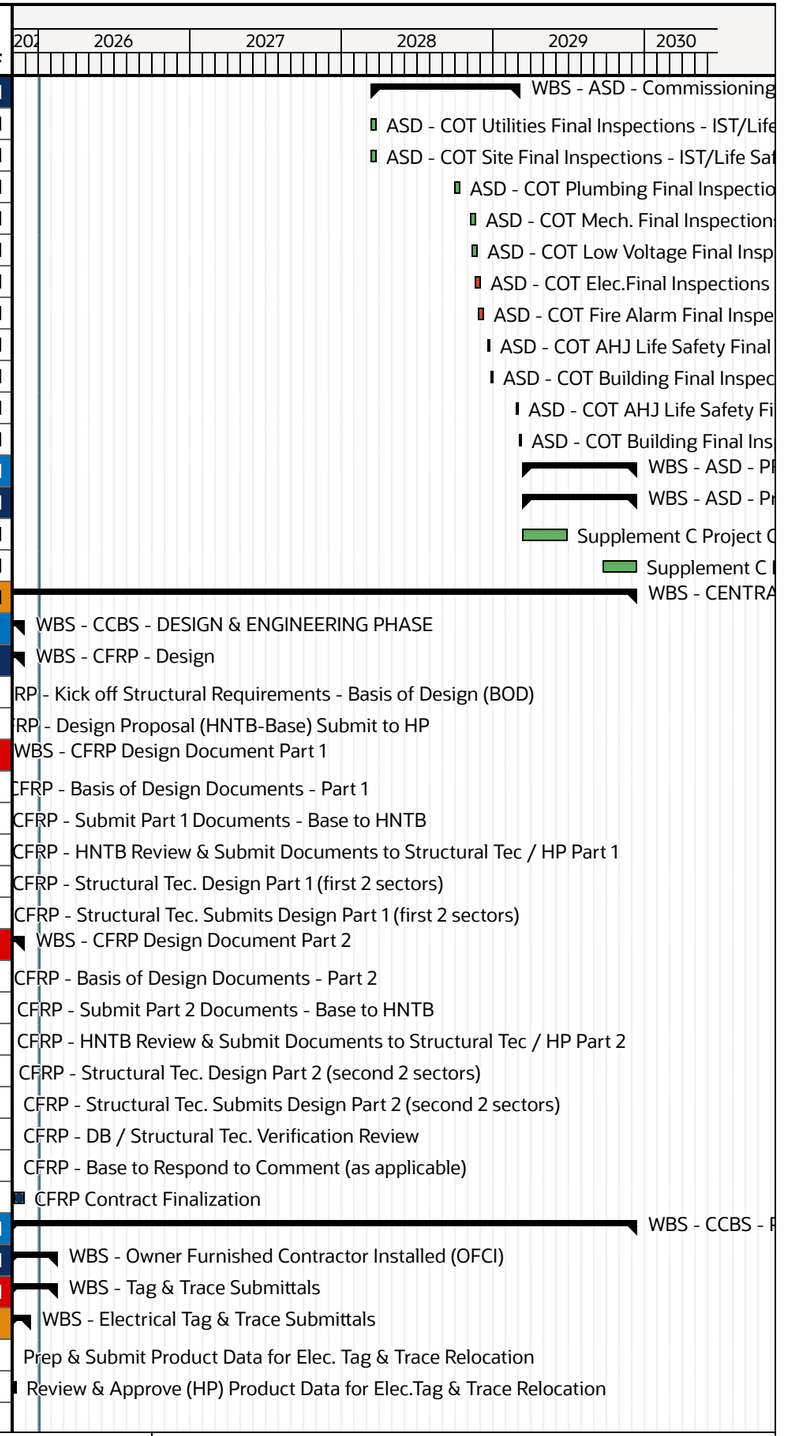


	ID	Name	Dur	Start	Finish	TF
11341	A64130	Review & Approve (HNTB) Product Data for Elec. Tag & Trace Relocation	10.0d	4-Nov-25 A	17-Nov-25 A	
11342	A64140	HCAA Review & Approve Product Data for Elec. Tag & Trace Relocation	16.0d	18-Nov-25 A	11-Dec-25 A	
11343	WBS - Low Volt Tag & Trace Submittals		61.0d	14-Nov-25 A	12-Feb-26	81.0d
11344	A64150	Prep & Submit Product Data for Low Voltage Tag & Trace Relocation	31.0d	14-Nov-25 A	31-Dec-25	81.0d
11345	A106450	Review & Approve (HP) Product Data for Low Voltage Tag & Trace Relocation	5.0d	2-Jan-26	8-Jan-26	81.0d
11346	A64160	Review & Approve (HNTB) Product Data for Low Voltage Tag & Trace Relocation	10.0d	9-Jan-26	22-Jan-26	81.0d
11347	A64170	HCAA Review & Approve Product Data for Low Voltage Tag & Trace Relocation	15.0d	23-Jan-26	12-Feb-26	81.0d
11348	WBS - Contractor Furnished & Install (CFCI)		1,053.0d	20-Oct-25 A	11-Dec-29	70.0d
11349	WBS - Part 2 Supplement B - Centralized Checked Baggage Etc.		1,018.0d	20-Oct-25 A	19-Oct-29	105.0d
11350	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supp. B		1,018.0d	20-Oct-25 A	19-Oct-29	105.0d
11351	WBS - General BHS Submittals & Procurement - Part 2 Supp. B		1,018.0d	20-Oct-25 A	19-Oct-29	105.0d
11352	WBS - System Inspection, Functional Specification, and Test Plan Submittals		61.0d	18-Nov-25 A	16-Feb-26	135.0d
11353	D1056	Prep & Submit System Inspection, Functional Specification, & Test Plan	31.0d	18-Nov-25 A	5-Jan-26	135.0d
11354	A101440	Review & Approve (HP) System Inspection, Functional Specification, & Test Plan	5.0d	6-Jan-26	12-Jan-26	135.0d
11355	A106430	Review & Approve (HNTB) System Inspection, Functional Specification, & Test ...	10.0d	13-Jan-26	26-Jan-26	135.0d
11356	D1061	Review & Approve (HCAA) System Inspection, Functional Specification, & Test ...	15.0d	27-Jan-26	16-Feb-26	135.0d
11357	WBS - Computer/Software/Hardware Inventory Submittals - Part 2 Supp. B		35.0d	31-Aug-29	19-Oct-29	105.0d
11358	A101180	Prep & Submit Computer/Software/Hardware Inventory	5.0d	31-Aug-29	7-Sep-29	105.0d
11359	A101340	Review & Approve (HP) Computer/Software/Hardware Inventory	5.0d	10-Sep-29	14-Sep-29	105.0d
11360	A106510	Review & Approve (HNTB) Computer/Software/Hardware Inventory	10.0d	17-Sep-29	28-Sep-29	105.0d
11361	A106520	Review & Approve (HCAA) Computer/Software/Hardware Inventory	15.0d	1-Oct-29	19-Oct-29	105.0d
11362	WBS - Quality Control Manual Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	139.0d
11363	A101190	Prep & Submit Quality Control Manual	48.0d	20-Oct-25 A	29-Dec-25	139.0d
11364	A101380	Review & Approve (HP) Quality Control Manual	5.0d	30-Dec-25	6-Jan-26	139.0d
11365	A106570	Review & Approve (HNTB) Quality Control Manual	10.0d	7-Jan-26	20-Jan-26	139.0d
11366	A106580	Review & Approve (HCAA) Quality Control Manual	15.0d	21-Jan-26	10-Feb-26	139.0d
11367	WBS - Site Specific Safety Plans Submittals - Part 2 Supp. B		35.0d	20-Oct-25 A	9-Dec-25 A	
11368	A101330	Prep & Submit Site Specific Safety Plans	13.0d	20-Oct-25 A	5-Nov-25 A	
11369	A101360	Review & Approve (HP) Site Specific Safety Plans	2.0d	6-Nov-25 A	7-Nov-25 A	
11370	A106590	Review & Approve (HNTB) Site Specific Safety Plans	11.0d	10-Nov-25 A	24-Nov-25 A	
11371	A106600	Review & Approve (HCAA) Site Specific Safety Plans	9.0d	25-Nov-25 A	9-Dec-25 A	
11372	WBS - Environmental Requirements Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	777.0d
11373	A101290	Prep & Submit Environmental Requirements	48.0d	20-Oct-25 A	29-Dec-25	777.0d
11374	A101430	Review & Approve (HP) Environmental Requirements	5.0d	30-Dec-25	6-Jan-26	777.0d
11375	A106610	Review & Approve (HNTB) Environmental Requirements	10.0d	7-Jan-26	20-Jan-26	777.0d
11376	A106620	Review & Approve (HCAA) Environmental Requirements	15.0d	21-Jan-26	10-Feb-26	777.0d
11377	WBS - Project Organizational Chart & Management Team Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	118.0d
11378	A101280	Prep & Submit Project Organizational Chart & Management Team	48.0d	20-Oct-25 A	29-Dec-25	118.0d
11379	A101370	Review & Approve (HP) Project Organizational Chart & Management Team	5.0d	30-Dec-25	6-Jan-26	118.0d
11380	A106630	Review & Approve (HNTB) Project Organizational Chart & Management Team	10.0d	7-Jan-26	20-Jan-26	118.0d
11381	A106640	Review & Approve (HCAA) Project Organizational Chart & Management Team	15.0d	21-Jan-26	10-Feb-26	118.0d
11382	WBS - Detailed Master Schedule Submittals - Part 2 Supp. B		78.0d	20-Oct-25 A	10-Feb-26	118.0d

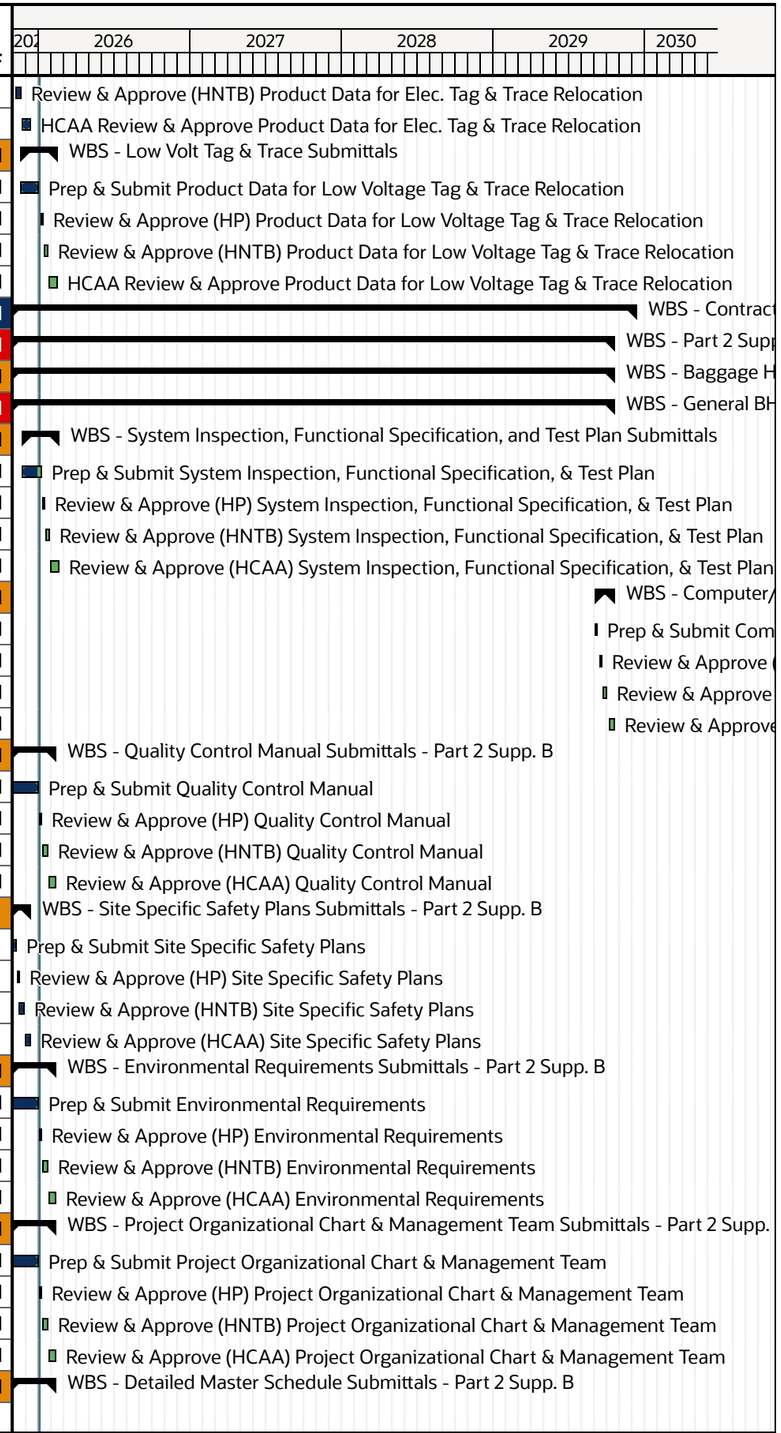


	ID	Name	Dur	Start	Finish	TF
11383	A101220	Prep & Submit Detailed Master Schedule	48.0d	20-Oct-25 A	29-Dec-25	118.0d
11384	A101420	Review & Approve (HP) Detailed Master Schedule	5.0d	30-Dec-25	6-Jan-26	118.0d
11385	A106670	Review & Approve (HNTB) Detailed Master Schedule	10.0d	7-Jan-26	20-Jan-26	118.0d
11386	A106680	Review & Approve (HCAA) Detailed Master Schedule	15.0d	21-Jan-26	10-Feb-26	118.0d
11387	WBS - O&M Manual Submittals - Part 2 Supp. B		85.0d	17-Feb-26	16-Jun-26	55.0d
11388	A101480	Prep & Submit O&M Manual - Draft	30.0d	17-Feb-26	30-Mar-26	55.0d
11389	A106710	Review & Approve (HP) O&M Manual - Draft	5.0d	31-Mar-26	6-Apr-26	55.0d
11390	A106720	Review & Approve (HNTB) O&M Manual - Draft	10.0d	7-Apr-26	20-Apr-26	55.0d
11391	A101500	Review & Approve (HCAA) O&M Manual - Draft	15.0d	21-Apr-26	11-May-26	55.0d
11392	A101530	Submit O&M Manual - Final	25.0d	12-May-26	16-Jun-26	55.0d
11393	WBS - Phasing Schedule Submittals - Part 2 Supp. B		61.0d	18-Nov-25 A	16-Feb-26	114.0d
11394	A101270	Prep & Submit Phasing Schedule	31.0d	18-Nov-25 A	5-Jan-26	114.0d
11395	A101410	Review & Approve (HP) Phasing Schedule	5.0d	6-Jan-26	12-Jan-26	114.0d
11396	A106770	Review & Approve (HNTB) Phasing Schedule	10.0d	13-Jan-26	26-Jan-26	114.0d
11397	A106780	Review & Approve (HCAA) Phasing Schedule	15.0d	27-Jan-26	16-Feb-26	114.0d
11398	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supp. B		261.0d	28-Oct-25 A	5-Nov-26	55.0d
11399	WBS - General Mechanical BHS Submittals & Procurement - Part 2 Supp. B		96.0d	28-Oct-25 A	16-Mar-26	220.0d
11400	WBS - Mechanical Catalog Cut / Equipment Specs Submittals - Part 2 Supp. B		66.0d	28-Oct-25 A	2-Feb-26	0.0d
11401	A101620	Prep & Submit Mech. Catalog Cut / Equip. Specs	11.0d	28-Oct-25 A	11-Nov-25 A	
11402	A106820	Review & Approve (HP) Mech. Catalog Cut / Equip. Specs	2.0d	12-Nov-25 A	13-Nov-25 A	
11403	A106810	Review & Approve (HNTB) Mech. Catalog Cut / Equip. Specs	15.0d	14-Nov-25 A	8-Dec-25 A	
11404	A110550	Revise & Resubmit (Daifuku) Mech. Catalog Cut / Equip. Specs	13.0d	9-Dec-25 A	26-Dec-25 A	
11405	A110560	Review & Approve (HNTB) Mech. Catalog Cut / Equip. Specs	10.0d	29-Dec-25	12-Jan-26	0.0d
11406	D1083	Review & Approve (HCAA) Mech. Catalog Cut / Equip. Specs	15.0d	13-Jan-26	2-Feb-26	0.0d
11407	WBS - Motor Schedule Submittals - Part 2 Supp. B		61.0d	18-Nov-25 A	16-Feb-26	55.0d
11408	A101610	Prep & Submit Motor Schedule	31.0d	18-Nov-25 A	5-Jan-26	55.0d
11409	A106830	Review & Approve (HP) Motor Schedule	5.0d	6-Jan-26	12-Jan-26	55.0d
11410	A106840	Review & Approve (HNTB) Motor Schedule	10.0d	13-Jan-26	26-Jan-26	55.0d
11411	A101660	Review & Approve (HCAA) Motor Schedule	15.0d	27-Jan-26	16-Feb-26	55.0d
11412	WBS - CBRA Egress Pathway Landing Submittals - Part 2 Supp. B		50.0d	6-Jan-26	16-Mar-26	220.0d
11413	A101580	Prep & Submit CBRA Egress Pathway Landing	20.0d	6-Jan-26	2-Feb-26	220.0d
11414	A101670	Review & Approve (HP) CBRA Egress Pathway Landing	5.0d	3-Feb-26	9-Feb-26	220.0d
11415	A106850	Review & Approve (HNTB) CBRA Egress Pathway Landing	10.0d	10-Feb-26	23-Feb-26	220.0d
11416	A106860	Review & Approve (HCAA) CBRA Egress Pathway Landing	15.0d	24-Feb-26	16-Mar-26	220.0d
11417	WBS - General Mechanical Assembly Detail Drawings Submittals - Part 2 Supp. B		56.0d	28-Oct-25 A	19-Jan-26	0.0d
11418	A101590	Prep & Submit General Mech. Assembly Detail Drawings	11.0d	28-Oct-25 A	11-Nov-25 A	
11419	A101650	Review & Approve (HP) General Mech. Assembly Detail Drawings	4.0d	12-Nov-25 A	17-Nov-25 A	
11420	A106870	Review & Approve (HNTB) General Mech. Assembly Detail Drawings	11.0d	18-Nov-25 A	4-Dec-25 A	
11421	D1084	Review & Approve (HCAA) General Mech. Assembly Detail Drawings	30.0d	5-Dec-25 A	19-Jan-26	0.0d
11422	WBS - Seq 1-Stage 1-Step 1 - Part 2 Supp. B		181.0d	18-Nov-25 A	5-Aug-26	0.0d
11423	WBS - BHS Mechanical Submittals [01-01-01]		81.0d	18-Nov-25 A	16-Mar-26	0.0d
11424	D1092	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-01]	9.0d	18-Nov-25 A	2-Dec-25 A	

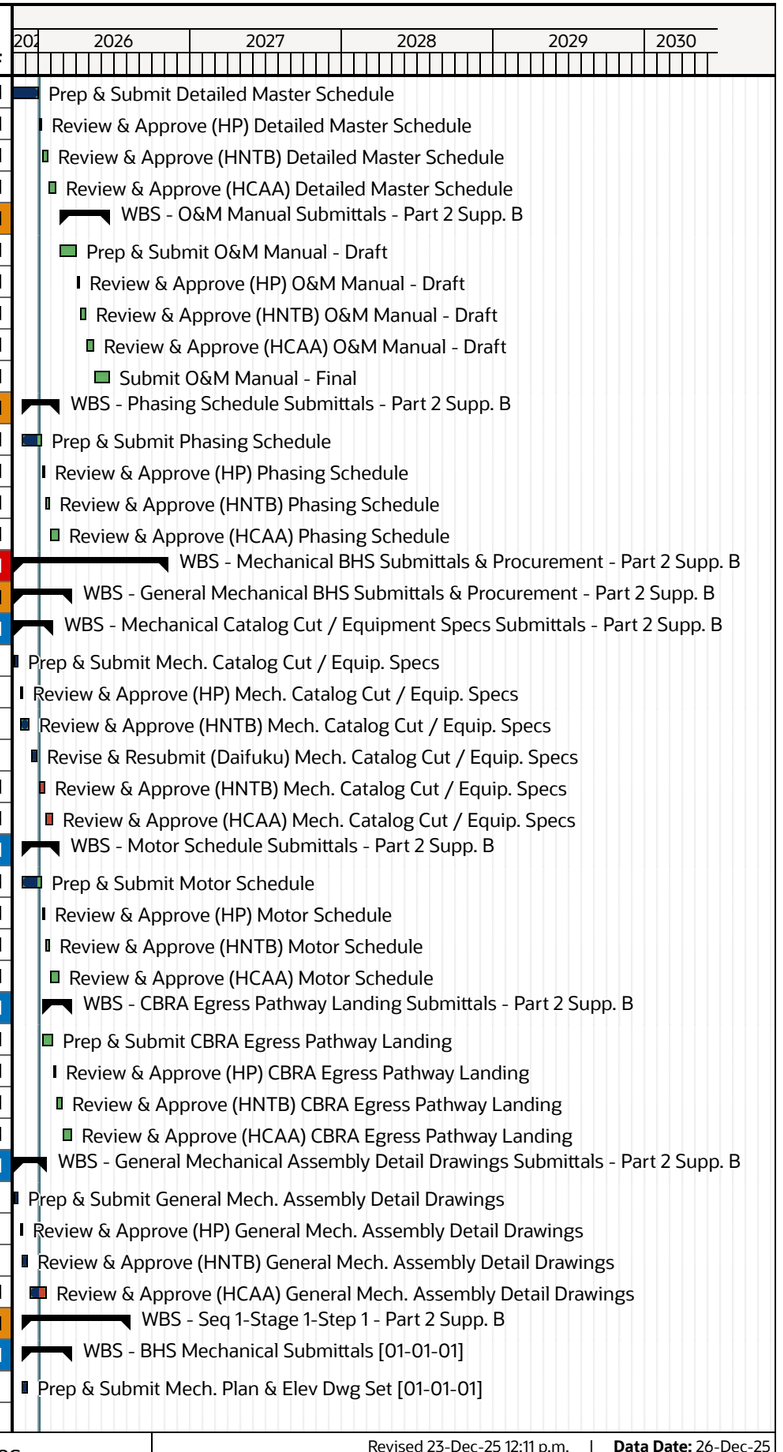


	ID	Name	Dur	Start	Finish	TF
11425	D3536	Review & Approve (HP) Mech Plan & Elev Dwg Set [01-01-01]	2.0d	3-Dec-25 A	4-Dec-25 A	
11426	D3546	Review & Approve (HNTB) Mech Plan & Elev Dwg Set [01-01-01]	9.0d	5-Dec-25 A	17-Dec-25 A	
11427	D1093	Review & Approve (HCAA) Mech Plan & Elev Dwg Set [01-01-01]	16.0d	18-Dec-25 A	12-Jan-26	0.0d
11428	D1095	Prep & Submit Header Steel Dwg Set [01-01-01]	10.0d	20-Jan-26	2-Feb-26	0.0d
11429	D3556	Review & Approve (HP) Header Steel Dwg Set [01-01-01]	5.0d	3-Feb-26	9-Feb-26	0.0d
11430	D3566	Review & Approve (HNTB) Header Steel Dwg Set [01-01-01]	10.0d	10-Feb-26	23-Feb-26	0.0d
11431	D1097	Review & Approve (HCAA) Header Steel Dwg Set [01-01-01]	15.0d	24-Feb-26	16-Mar-26	0.0d
11432	WBS - BHS Mechanical Fabrication [01-01-01]		145.0d	13-Jan-26	5-Aug-26	0.0d
11433	D1094	Fab. & Deliver Conveyor Batch 1 (15) [01-01-01]	120.0d	13-Jan-26	30-Jun-26	0.0d
11434	D1096	Fab. & Deliver Conveyor Batch 2 (14) [01-01-01]	120.0d	20-Jan-26	8-Jul-26	0.0d
11435	D1098	Fab. & Deliver Header Steel / Platform / Sills [01-01-01]	80.0d	17-Mar-26	8-Jul-26	0.0d
11436	D1099	Prep Mech. Matl for Install [01-01-01]	20.0d	9-Jul-26	5-Aug-26	0.0d
11437	WBS - Seq 1 - Stage 1 - Step 2		193.0d	2-Dec-25 A	2-Sep-26	0.0d
11438	WBS - BHS Mechanical Submittals [01-01-02]		77.0d	2-Dec-25 A	20-Mar-26	16.0d
11439	D1100	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-02]	8.0d	2-Dec-25 A	11-Dec-25 A	
11440	D3586	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-02]	2.0d	12-Dec-25 A	15-Dec-25 A	
11441	D3576	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-02]	12.0d	16-Dec-25 A	2-Jan-26	16.0d
11442	D1102	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-02]	15.0d	5-Jan-26	23-Jan-26	16.0d
11443	D1103	Prep & Submit Header Steel Dwg Set [01-01-02]	10.0d	26-Jan-26	6-Feb-26	16.0d
11444	D3596	Review & Approve Header Steel Dwg Set (HP) [01-01-02]	5.0d	9-Feb-26	13-Feb-26	16.0d
11445	D3606	Review & Approve Header Steel Dwg Set (HNTB) [01-01-02]	10.0d	16-Feb-26	27-Feb-26	16.0d
11446	D1105	Review & Approve Header Steel Dwg Set (HCAA) [01-01-02]	15.0d	2-Mar-26	20-Mar-26	16.0d
11447	WBS - BHS Mechanical Fabrication [01-01-02]		156.0d	26-Jan-26	2-Sep-26	0.0d
11448	D1104	Fab. & Deliver Conveyor (9) [01-01-02]	120.0d	26-Jan-26	14-Jul-26	16.0d
11449	D1101	Fab. & Deliver HSD T18A 1 [01-01-02]	130.0d	3-Feb-26	5-Aug-26	0.0d
11450	D1106	Fab. & Deliver Header Steel / Platform / Sills [01-01-02]	80.0d	23-Mar-26	14-Jul-26	16.0d
11451	D1107	Prep Mech. Matl for Install [01-01-02]	20.0d	6-Aug-26	2-Sep-26	0.0d
11452	WBS - Seq 1 - Stage 1 - Step 3		182.0d	2-Dec-25 A	18-Aug-26	21.0d
11453	WBS - BHS Mechanical Submittals [01-01-03]		82.0d	2-Dec-25 A	27-Mar-26	21.0d
11454	D1108	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-03]	8.0d	2-Dec-25 A	11-Dec-25 A	
11455	D3616	Review & Approve Mech Plan & Elev Dwg Set (HP)t [01-01-03]	3.0d	11-Dec-25 A	15-Dec-25 A	
11456	D3626	Review & Approve Mech Plan & Elev Dwg Set (HNTB)t [01-01-03]	12.0d	16-Dec-25 A	2-Jan-26	21.0d
11457	D1109	Review & Approve Mech Plan & Elev Dwg Set (HCAA)t [01-01-03]	15.0d	5-Jan-26	23-Jan-26	21.0d
11458	D1110	Prep & Submit Header Steel Dwg Sett [01-01-03]	10.0d	26-Jan-26	6-Feb-26	21.0d
11459	D3636	Review & Approve Header Steel Dwg Set (HP)t [01-01-03]	10.0d	9-Feb-26	20-Feb-26	21.0d
11460	D3646	Review & Approve Header Steel Dwg Set (HNTB)t [01-01-03]	10.0d	23-Feb-26	6-Mar-26	21.0d
11461	D1112	Review & Approve Header Steel Dwg Set (HCAA)t [01-01-03]	15.0d	9-Mar-26	27-Mar-26	21.0d
11462	WBS - BHS Mechanical Fabrication [01-01-03]		145.0d	26-Jan-26	18-Aug-26	21.0d
11463	D1111	Fab. & Deliver Conveyor (8) [01-01-03]	120.0d	26-Jan-26	14-Jul-26	26.0d
11464	D1113	Fab. & Deliver Header Steel / Platform / Sillst [01-01-03]	80.0d	30-Mar-26	21-Jul-26	21.0d
11465	D1114	Prep Mech. Matl for Install [01-01-03]	20.0d	22-Jul-26	18-Aug-26	21.0d
11466	WBS - Seq 1 - Stage 1 - Step 4		197.0d	2-Dec-25 A	9-Sep-26	18.0d

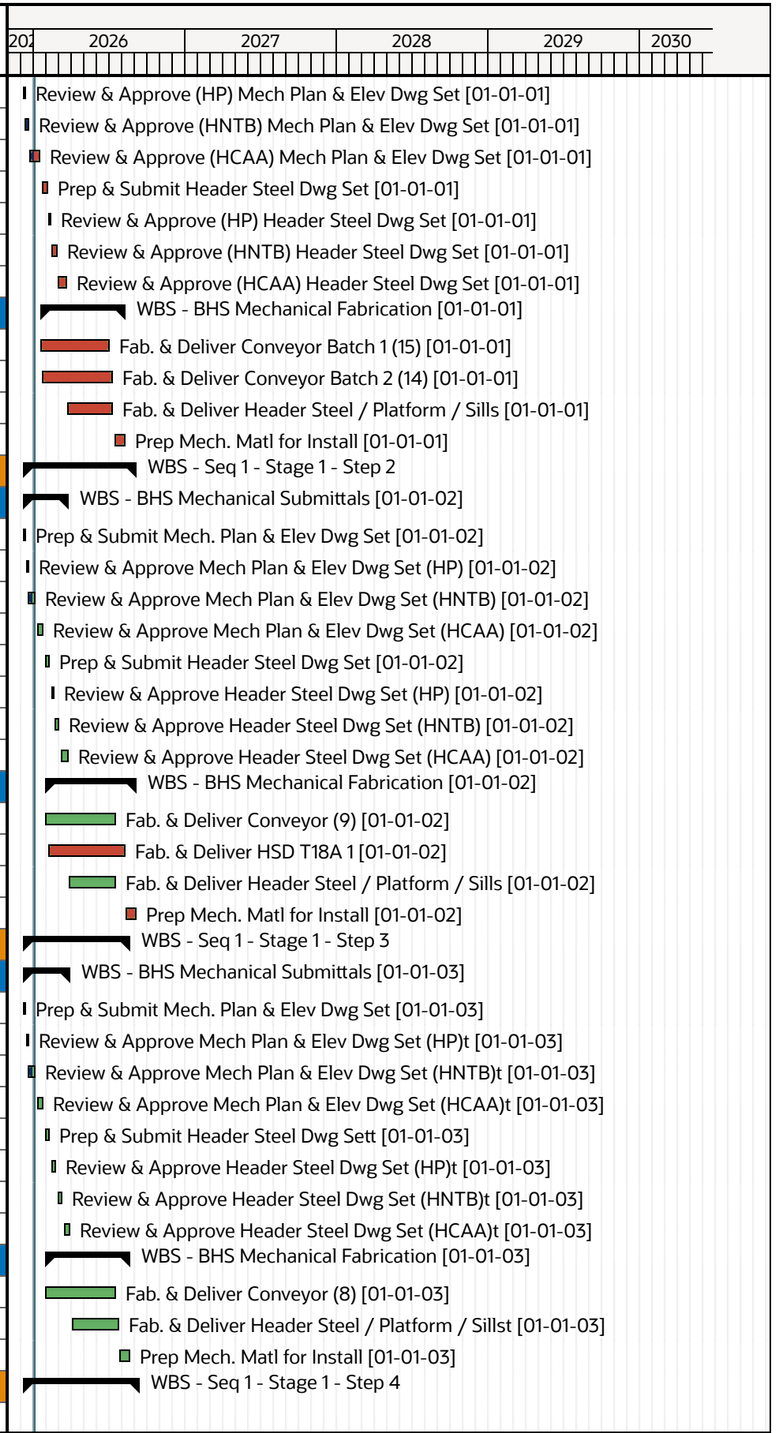


	ID	Name	Dur	Start	Finish	TF
11467	WBS - BHS Mechanical Submittals [01-01-04]		77.0d	2-Dec-25 A	20-Mar-26	38.0d
11468	D1115	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-04]	8.0d	2-Dec-25 A	11-Dec-25 A	
11469	D3656	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-04]	2.0d	12-Dec-25 A	15-Dec-25 A	
11470	D3666	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-04]	12.0d	16-Dec-25 A	2-Jan-26	18.0d
11471	D1116	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-04]	15.0d	5-Jan-26	23-Jan-26	18.0d
11472	D1117	Prep & Submit Header Steel Dwg Set [01-01-04]	10.0d	26-Jan-26	6-Feb-26	38.0d
11473	D3676	Review & Approve Header Steel Dwg Set (HP) [01-01-04]	5.0d	9-Feb-26	13-Feb-26	38.0d
11474	D3686	Review & Approve Header Steel Dwg Set (HNTB) [01-01-04]	10.0d	16-Feb-26	27-Feb-26	38.0d
11475	D1120	Review & Approve Header Steel Dwg Set (HCAA) [01-01-04]	15.0d	2-Mar-26	20-Mar-26	38.0d
11476	WBS - BHS Mechanical Fabrication [01-01-04]		160.0d	26-Jan-26	9-Sep-26	18.0d
11477	D1118	Fab. & Deliver Conveyor (4) [01-01-04]	140.0d	26-Jan-26	11-Aug-26	18.0d
11478	D1119	Fab. & Deliver T17 4 FSD [01-01-04]	60.0d	26-Jan-26	17-Apr-26	98.0d
11479	D1121	Fab. & Deliver Header Steel / Platform / Sills [01-01-04]	80.0d	23-Mar-26	14-Jul-26	38.0d
11480	D1122	Prep Mech. Matl for Install [01-01-04]	20.0d	12-Aug-26	9-Sep-26	18.0d
11481	WBS - Seq 1 - Stage 1 - Step 5		185.0d	29-Dec-25	17-Sep-26	25.0d
11482	WBS - BHS Mechanical Submittals [01-01-05]		45.0d	29-Dec-25	2-Mar-26	25.0d
11483	D1123	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-05]	15.0d	29-Dec-25	19-Jan-26	6.0d
11484	D3696	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-05]	5.0d	20-Jan-26	26-Jan-26	25.0d
11485	D3706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-01-05]	10.0d	27-Jan-26	9-Feb-26	25.0d
11486	D1124	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-01-05]	15.0d	10-Feb-26	2-Mar-26	25.0d
11487	WBS - BHS Mechanical Fabrication [01-01-05]		140.0d	3-Mar-26	17-Sep-26	25.0d
11488	D1125	Fab. & Deliver Conveyor (4 conveyor) [01-01-05]	120.0d	3-Mar-26	19-Aug-26	25.0d
11489	D1126	Fab. & Deliver T15 2 FSD [01-01-05]	60.0d	3-Mar-26	26-May-26	85.0d
11490	D1127	Prep Mech. Matl for Install [01-01-05]	20.0d	20-Aug-26	17-Sep-26	25.0d
11491	WBS - Seq 1 - Stage 2 - Step 1		200.0d	20-Jan-26	29-Oct-26	6.0d
11492	WBS - BHS Mechanical Submittals [01-02-01]		100.0d	20-Jan-26	9-Jun-26	6.0d
11493	D1128	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-01]	20.0d	20-Jan-26	16-Feb-26	6.0d
11494	D3716	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-01]	5.0d	17-Feb-26	23-Feb-26	6.0d
11495	D3726	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-01]	10.0d	24-Feb-26	9-Mar-26	6.0d
11496	D1129	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-01]	15.0d	10-Mar-26	30-Mar-26	6.0d
11497	D1130	Prep & Submit Header Steel Dwg Set [01-02-01]	20.0d	31-Mar-26	27-Apr-26	6.0d
11498	D3736	Review & Approve Header Steel Dwg Set (HP) [01-02-01]	5.0d	28-Apr-26	4-May-26	6.0d
11499	D3746	Review & Approve Header Steel Dwg Set (HNTB) [01-02-01]	10.0d	5-May-26	18-May-26	6.0d
11500	D1132	Review & Approve Header Steel Dwg Set (HCAA) [01-02-01]	15.0d	19-May-26	9-Jun-26	6.0d
11501	WBS - BHS Mechanical Fabrication [01-02-01]		150.0d	31-Mar-26	29-Oct-26	6.0d
11502	D1131	Fab. & Deliver Conveyor (3) [01-02-01]	120.0d	31-Mar-26	17-Sep-26	16.0d
11503	D1133	Fab. & Deliver Header Steel / Platform / Sills [01-02-01]	80.0d	10-Jun-26	1-Oct-26	6.0d
11504	D1134	Prep Mech. Matl for Install [01-02-01]	20.0d	2-Oct-26	29-Oct-26	6.0d
11505	WBS - Seq 1 - Stage 2 - Step 2		200.0d	20-Jan-26	29-Oct-26	11.0d
11506	WBS - BHS Mechanical Submittals [01-02-02]		100.0d	20-Jan-26	9-Jun-26	11.0d
11507	D1135	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-02]	20.0d	20-Jan-26	16-Feb-26	11.0d
11508	D3756	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-02]	5.0d	17-Feb-26	23-Feb-26	11.0d

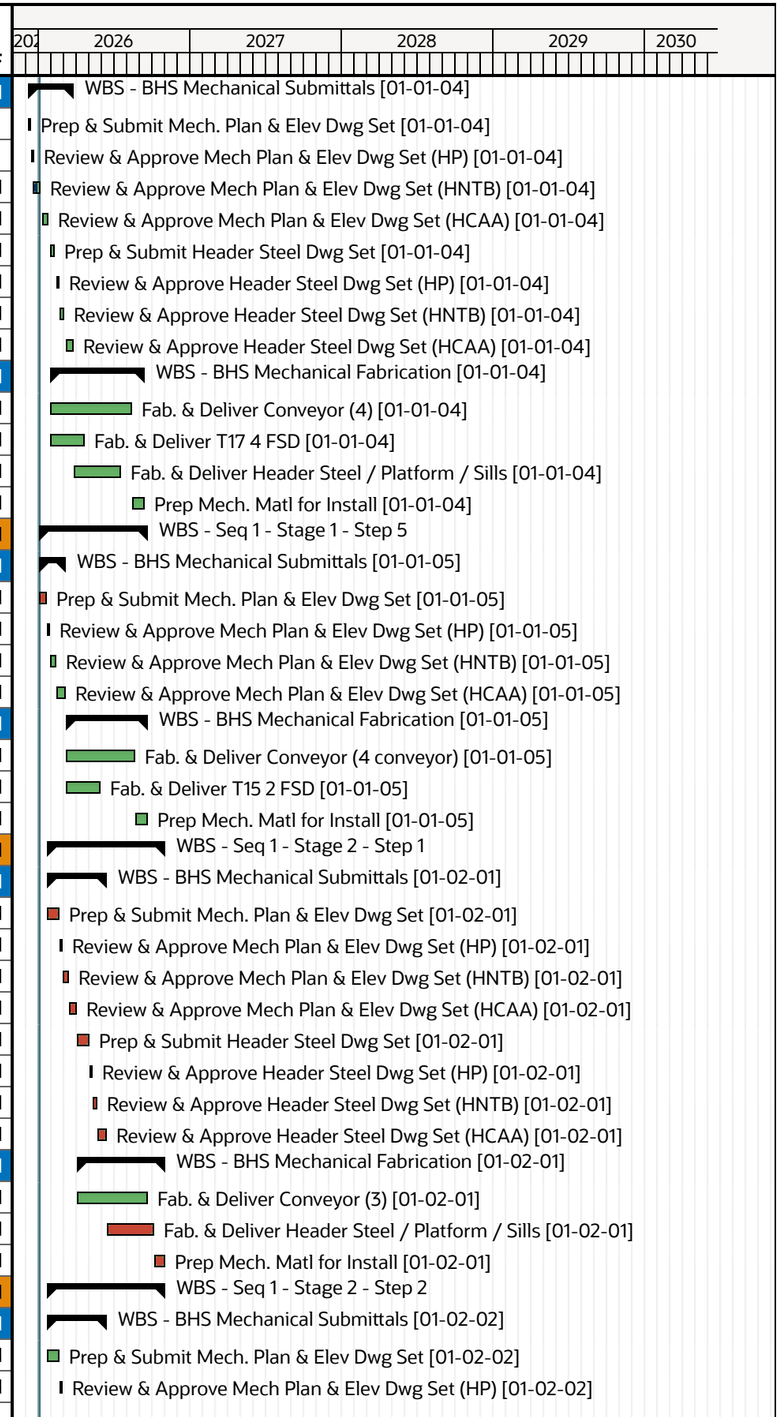


	ID	Name	Dur	Start	Finish	TF
11509	D3766	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-02]	10.0d	24-Feb-26	9-Mar-26	11.0d
11510	D1136	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-02]	15.0d	10-Mar-26	30-Mar-26	11.0d
11511	D1137	Prep & Submit Header Steel Dwg Set [01-02-02]	20.0d	31-Mar-26	27-Apr-26	11.0d
11512	D3776	Review & Approve Header Steel Dwg Set (HP) [01-02-02]	5.0d	28-Apr-26	4-May-26	11.0d
11513	D3786	Review & Approve Header Steel Dwg Set (HNTB) [01-02-02]	10.0d	5-May-26	18-May-26	11.0d
11514	D1139	Review & Approve Header Steel Dwg Set (HCAA) [01-02-02]	15.0d	19-May-26	9-Jun-26	11.0d
11515	WBS - BHS Mechanical Fabrication [01-02-02]		150.0d	31-Mar-26	29-Oct-26	11.0d
11516	D1138	Fab. & Deliver Conveyor (11) [01-02-02]	120.0d	31-Mar-26	17-Sep-26	21.0d
11517	D1140	Fab. & Deliver Header Steel / Platform / Sills [01-02-02]	80.0d	10-Jun-26	1-Oct-26	11.0d
11518	D1141	Prep Mech. Matl for Install [01-02-02]	20.0d	2-Oct-26	29-Oct-26	11.0d
11519	WBS - Seq 1 - Stage 2 - Step 3		200.0d	20-Jan-26	29-Oct-26	31.0d
11520	WBS - BHS Mechanical Submittals [01-02-03]		100.0d	20-Jan-26	9-Jun-26	31.0d
11521	D1142	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-03]	20.0d	20-Jan-26	16-Feb-26	30.0d
11522	D3796	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-03]	5.0d	17-Feb-26	23-Feb-26	31.0d
11523	D3806	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-03]	10.0d	24-Feb-26	9-Mar-26	31.0d
11524	D1143	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-03]	15.0d	10-Mar-26	30-Mar-26	31.0d
11525	D1144	Prep & Submit Header Steel Dwg Set [01-02-03]	20.0d	31-Mar-26	27-Apr-26	31.0d
11526	D3816	Review & Approve Header Steel Dwg Set (HP) [01-02-03]	5.0d	28-Apr-26	4-May-26	31.0d
11527	D3826	Review & Approve Header Steel Dwg Set (HNTB) [01-02-03]	10.0d	5-May-26	18-May-26	31.0d
11528	D1146	Review & Approve Header Steel Dwg Set (HCAA) [01-02-03]	15.0d	19-May-26	9-Jun-26	31.0d
11529	WBS - BHS Mechanical Fabrication [01-02-03]		150.0d	31-Mar-26	29-Oct-26	31.0d
11530	D1145	Fab. & Deliver Conveyor (6) [01-02-03]	120.0d	31-Mar-26	17-Sep-26	41.0d
11531	D1147	Fab. & Deliver Header Steel / Platform / Sills [01-02-03]	80.0d	10-Jun-26	1-Oct-26	31.0d
11532	D1148	Prep Mech. Matl for Install [01-02-03]	20.0d	2-Oct-26	29-Oct-26	31.0d
11533	WBS - Seq 1 - Stage 2 - Step 4		205.0d	20-Jan-26	5-Nov-26	30.0d
11534	WBS - BHS Mechanical Submittals [01-02-04]		105.0d	20-Jan-26	16-Jun-26	30.0d
11535	D1149	Prep & Submit Mech. Plan & Elev Dwg Set [01-02-04]	20.0d	20-Jan-26	16-Feb-26	30.0d
11536	D3836	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-02-04]	10.0d	17-Feb-26	2-Mar-26	30.0d
11537	D3846	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-02-04]	10.0d	3-Mar-26	16-Mar-26	30.0d
11538	D1150	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-02-04]	15.0d	17-Mar-26	6-Apr-26	30.0d
11539	D1151	Prep & Submit Header Steel Dwg Set [01-02-04]	20.0d	7-Apr-26	4-May-26	30.0d
11540	D3856	Review & Approve Header Steel Dwg Set (HP) [01-02-04]	5.0d	5-May-26	11-May-26	30.0d
11541	D3866	Review & Approve Header Steel Dwg Set (HNTB) [01-02-04]	10.0d	12-May-26	26-May-26	30.0d
11542	D1153	Review & Approve Header Steel Dwg Set (HCAA) [01-02-04]	15.0d	27-May-26	16-Jun-26	30.0d
11543	WBS - BHS Mechanical Fabrication [01-02-04]		150.0d	7-Apr-26	5-Nov-26	30.0d
11544	D1152	Fab. & Deliver Conveyor (4) [01-02-04]	120.0d	7-Apr-26	24-Sep-26	40.0d
11545	D1154	Fab. & Deliver Header Steel / Platform / Sills [01-02-04]	80.0d	17-Jun-26	8-Oct-26	30.0d
11546	D1155	Prep Mech. Matl for Install [01-02-04]	20.0d	9-Oct-26	5-Nov-26	30.0d
11547	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		483.0d	28-Oct-25 A	22-Sep-27	634.0d
11548	WBS - General Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supp. B		176.0d	28-Oct-25 A	8-Jul-26	941.0d
11549	WBS - Operator Interface / Control Station Typicals Submittals		45.0d	29-Dec-25	2-Mar-26	1,031.0d
11550	A101900	Prep & Submit Operator Interface / Control Station Typicals	15.0d	29-Dec-25	19-Jan-26	1,030.0d

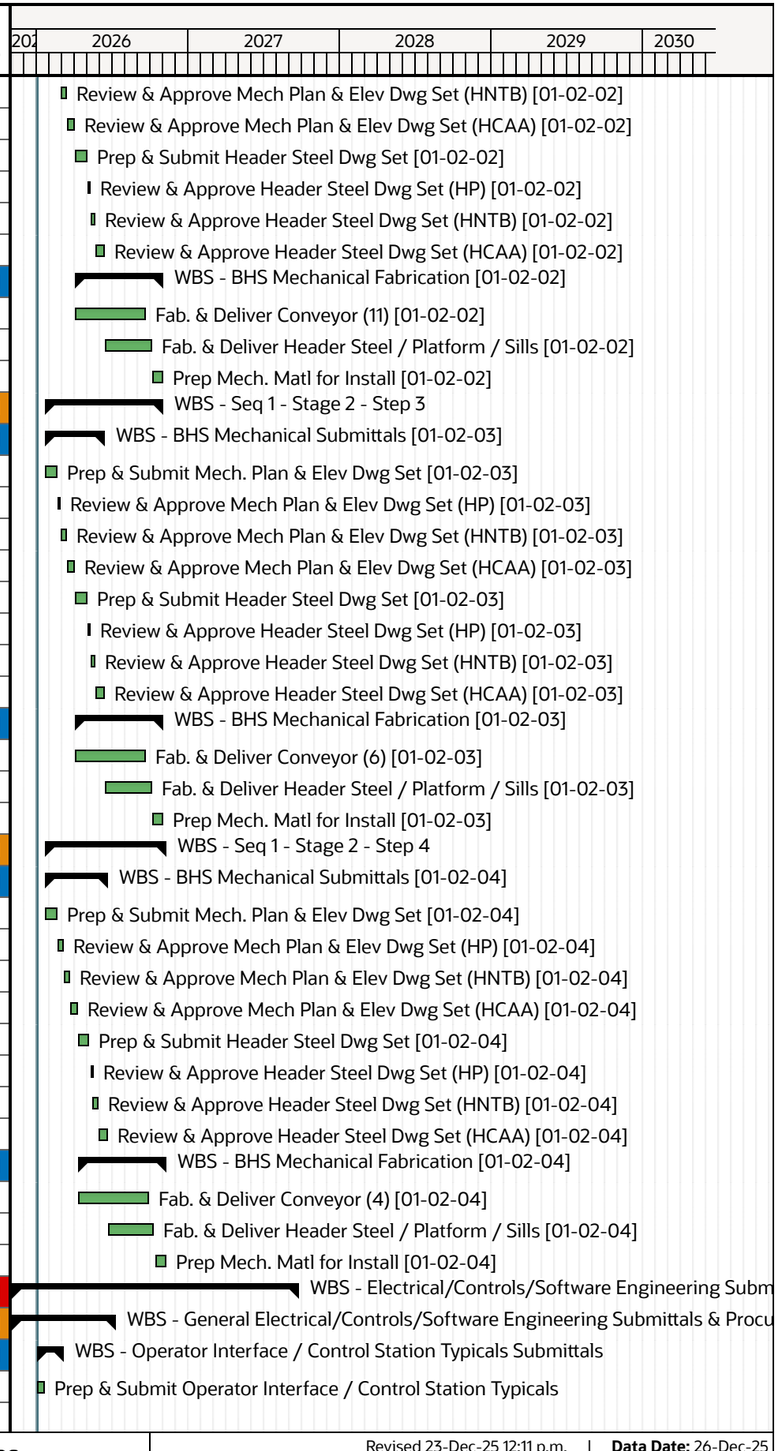


	ID	Name	Dur	Start	Finish	TF
11551	A107240	Review & Approve (HP) Operator Interface / Control Station Typicals	5.0d	20-Jan-26	26-Jan-26	1,030.0d
11552	A107250	Review & Approve (HNTB) Operator Interface / Control Station Typicals	10.0d	27-Jan-26	9-Feb-26	1,030.0d
11553	A102030	Review & Approve (HCAA) Operator Interface / Control Station Typicals	15.0d	10-Feb-26	2-Mar-26	1,030.0d
11554	WBS - Cross-Belt Sorter XBM2 Elect Drawing Sets Submittals		111.0d	29-Dec-25	3-Jun-26	416.0d
11555	A92270	Prep & Submit Cross-Belt Sorter XBM2 Elect Drawing Sets	1.0d	29-Dec-25	29-Dec-25	416.0d
11556	A107280	Review & Approve (HP) Cross-Belt Sorter XBM2 Elect Dwg Sets	5.0d	30-Dec-25	6-Jan-26	416.0d
11557	A107290	Review & Approve (HNTB) Cross-Belt Sorter XBM2 Elect Dwg Sets	10.0d	7-Jan-26	20-Jan-26	416.0d
11558	A92280	Review & Approve (HCAA) Cross-Belt Sorter XBM2 Elect Dwg Sets	15.0d	21-Jan-26	10-Feb-26	416.0d
11559	A92880	Fab./ Del XBM2 Power Panels (13)	80.0d	11-Feb-26	3-Jun-26	416.0d
11560	A92890	Fab./ Del XBM2 Field Control Panels (?), Elect Field Devices, Cabling	1.0d	11-Feb-26	11-Feb-26	495.0d
11561	WBS - Electrical Installation Catalog Cuts & Equipment Specs Submittals		117.0d	28-Oct-25 A	14-Apr-26	1,000.0d
11562	A101910	Prep & Submit Elec. Install Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	368.0d
11563	A107300	Review & Approve (HP) Elec.Install Catalog Cuts & Equip. Specs	10.0d	30-Dec-25	13-Jan-26	368.0d
11564	A107310	Review & Approve (HNTB) Elec. Install Catalog Cuts & Equip. Specs	10.0d	14-Jan-26	27-Jan-26	368.0d
11565	A102010	Review & Approve (HCAA) Elec. Install Catalog Cuts & Equip. Specs	15.0d	28-Jan-26	17-Feb-26	368.0d
11566	A101690	Fab. & Ship BHS Control Room Equip.	56.0d	18-Feb-26	14-Apr-26	1,404.0d
11567	A101700	Fab. & Ship BHS Server Room Equip.	56.0d	18-Feb-26	14-Apr-26	1,404.0d
11568	A101710	Fab. & Ship PLC Enclosure(s) Equip. [3 Mos Prior to FAT]	56.0d	18-Feb-26	14-Apr-26	1,322.0d
11569	A101720	Fab. & Ship CBRA Room Computer Equip.	56.0d	18-Feb-26	14-Apr-26	515.0d
11570	A101730	Fab. & Ship OSR Room Computer Equip.	56.0d	18-Feb-26	14-Apr-26	1,404.0d
11571	A101740	Fab. & Ship CBIS Area Status Displays	56.0d	18-Feb-26	14-Apr-26	918.0d
11572	A101750	Fab. & Ship Manual Encode Consoles	56.0d	18-Feb-26	14-Apr-26	1,404.0d
11573	A108580	Deliver CBIS Area Status Displays	0.0d		14-Apr-26	655.0d
11574	A108590	Deliver BHS Server Room Equip.	0.0d		14-Apr-26	999.0d
11575	A108600	Deliver OSR Room Computer Equip.	0.0d		14-Apr-26	999.0d
11576	A108570	Deliver Manual Encode Consoles	0.0d		14-Apr-26	999.0d
11577	A108620	Deliver BHS Control Room Equip.	0.0d		14-Apr-26	999.0d
11578	A108530	Deliver PLC Enclosure(s) Equip. [3 Mos Prior to FAT]	0.0d		14-Apr-26	941.0d
11579	A108610	Deliver CBRA Room Computer Equip.	0.0d		14-Apr-26	368.0d
11580	WBS - Electrical / Controls / Computer Catalog Cuts & Equipment Specs Submittals		72.0d	28-Oct-25 A	10-Feb-26	373.0d
11581	A101930	Prep & Submit Elec. / Controls / Computer Catalog Cuts & Equip. Specs	42.0d	28-Oct-25 A	29-Dec-25	373.0d
11582	A101990	Review & Approve (HP) Elec./ Controls / Computer Catalog Cuts & Equip. Specs	5.0d	30-Dec-25	6-Jan-26	373.0d
11583	A107320	Review & Approve (HNTB) Elec./ Controls / Computer Catalog Cuts & Equip. Sp...	10.0d	7-Jan-26	20-Jan-26	373.0d
11584	A107330	Review & Approve (HCAA) Elec. / Controls / Computer Catalog Cuts & Equip. S...	15.0d	21-Jan-26	10-Feb-26	373.0d
11585	WBS - ATR / BMA Catalog Cuts & Equipment Specs Submittals		103.0d	29-Dec-25	21-May-26	973.0d
11586	A101890	Prep & Submit ATR / BMA Catalog Cuts & Equip. Specs	15.0d	29-Dec-25	19-Jan-26	972.0d
11587	A102020	Review & Approve (HP) ATR / BMA Catalog Cuts & Equip. Specs	5.0d	20-Jan-26	26-Jan-26	972.0d
11588	A107340	Review & Approve (HNTB) ATR / BMA Catalog Cuts & Equip. Specs	10.0d	27-Jan-26	9-Feb-26	972.0d
11589	A107350	Review & Approve (HCAA) ATR / BMA Catalog Cuts & Equip. Specs	15.0d	10-Feb-26	2-Mar-26	972.0d
11590	A101760	Fab. & Ship ATR Equip.- ASD Conveyors	80.0d	3-Mar-26	21-May-26	1,367.0d
11591	A108540	Deliver ATR Equip.- ASD Conveyors	0.0d		21-May-26	972.0d
11592	WBS - Lower-Level Network Architecture Drawings Submittals		60.0d	29-Dec-25	23-Mar-26	89.0d

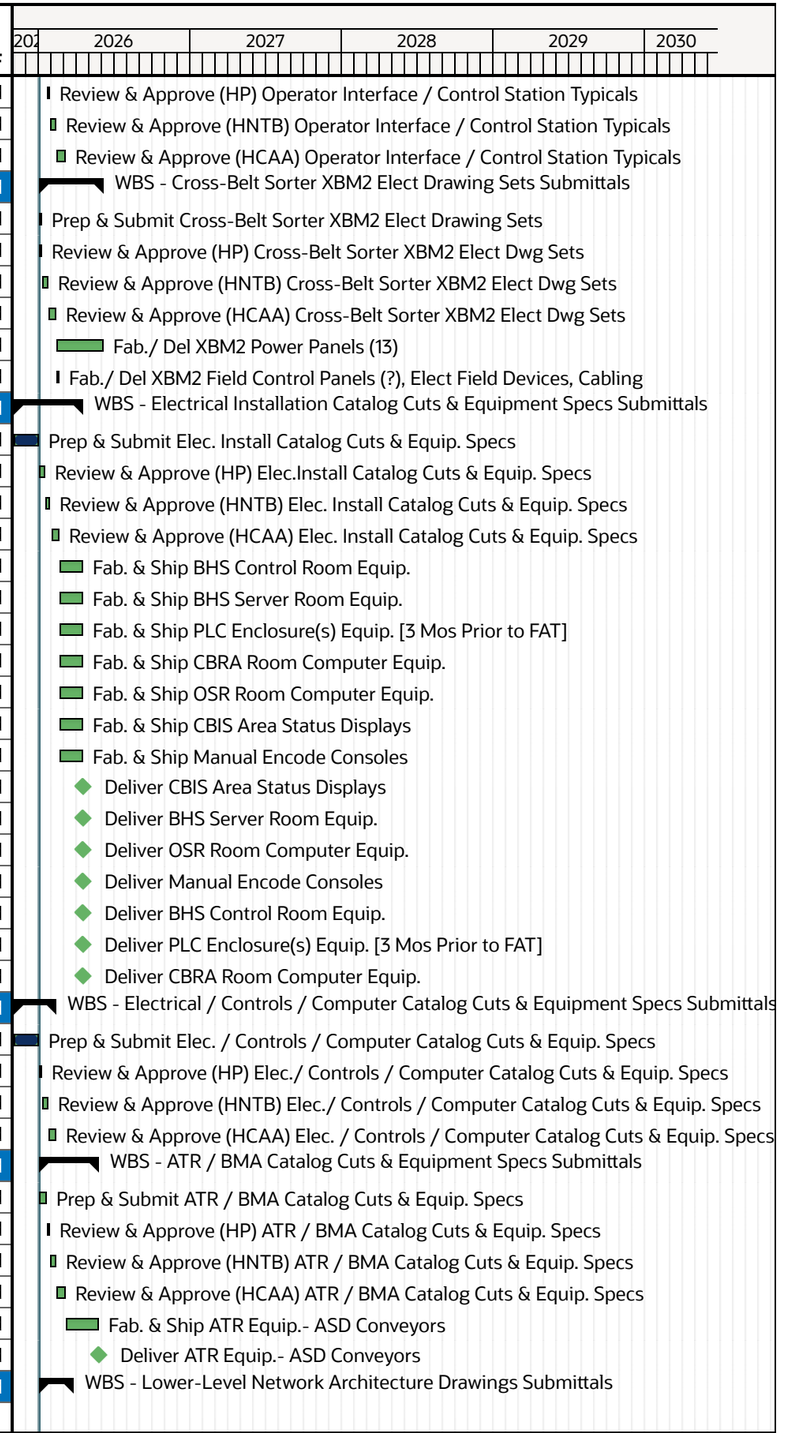


	ID	Name	Dur	Start	Finish	TF
11593	A101920	Prep & Submit Lower-Level Network Architecture Drawings	30.0d	29-Dec-25	9-Feb-26	89.0d
11594	A107370	Review & Approve (HP) Lower-Level Network Architecture Drawings	5.0d	10-Feb-26	16-Feb-26	89.0d
11595	A107360	Review & Approve (HNTB) Lower-Level Network Architecture Drawings	10.0d	17-Feb-26	2-Mar-26	89.0d
11596	A102080	Review & Approve (HCAA) Lower-Level Network Architecture Drawings	15.0d	3-Mar-26	23-Mar-26	89.0d
11597	WBS - Factory Acceptance Test Plan & Agenda Submittals		45.0d	29-Dec-25	2-Mar-26	596.0d
11598	A101870	Prep & Submit Factory Acceptance Test Plan & Agenda [40 days prior to FAT da...	15.0d	29-Dec-25	19-Jan-26	596.0d
11599	A102050	Review & Approve (HP) Factory Acceptance Test Plan & Agenda	5.0d	20-Jan-26	26-Jan-26	596.0d
11600	A107380	Review & Approve (HNTB) Factory Acceptance Test Plan & Agenda	10.0d	27-Jan-26	9-Feb-26	596.0d
11601	A107390	Review & Approve (HCAA) Factory Acceptance Test Plan & Agenda	15.0d	10-Feb-26	2-Mar-26	596.0d
11602	WBS - Controls System Descriptions and BHS Redundancy Schematic Diagrams Submittals		120.0d	29-Dec-25	16-Jun-26	511.0d
11603	A101860	Prep & Submit Controls System Description & BHS Redundancy Schematic Dia...	90.0d	29-Dec-25	4-May-26	511.0d
11604	A102110	Review & Approve (HP) Controls System Descriptions & BHS Redundancy Sche...	5.0d	5-May-26	11-May-26	511.0d
11605	A107400	Review & Approve (HNTB) Controls System Descriptions & BHS Redundancy Sc...	10.0d	12-May-26	26-May-26	511.0d
11606	A107410	Review & Approve (HCAA) Controls System Descriptions & BHS Redundancy Sc...	15.0d	27-May-26	16-Jun-26	511.0d
11607	WBS - Upper-Level Network Architecture Drawings Submittals		60.0d	29-Dec-25	23-Mar-26	384.0d
11608	A101880	Prep & Submit Upper-Level Network Architecture Drawings	30.0d	29-Dec-25	9-Feb-26	384.0d
11609	A102070	Review & Approve (HP) Upper-Level Network Architecture Drawings	5.0d	10-Feb-26	16-Feb-26	384.0d
11610	A107420	Review & Approve (HNTB) Upper-Level Network Architecture Drawings	10.0d	17-Feb-26	2-Mar-26	384.0d
11611	A107430	Review & Approve (HCAA) Upper-Level Network Architecture Drawings	15.0d	3-Mar-26	23-Mar-26	384.0d
11612	WBS - Control Room Equipment Drawings Submittals		120.0d	29-Dec-25	16-Jun-26	557.0d
11613	A101820	Prep & Submit Control Room Equip. Drawings	90.0d	29-Dec-25	4-May-26	557.0d
11614	A102120	Review & Approve (HP) Control Room Equip. Drawings	5.0d	5-May-26	11-May-26	557.0d
11615	A107440	Review & Approve (HNTB) Control Room Equip. Drawings	10.0d	12-May-26	26-May-26	557.0d
11616	A107450	Review & Approve (HCAA) Control Room Equip. Drawings	15.0d	27-May-26	16-Jun-26	557.0d
11617	WBS - Cross-Belt Sorter Functional Specification Submittals		31.0d	29-Dec-25	10-Feb-26	600.0d
11618	A101840	Prep & Submit Cross-Belt Sorter Functional Specification	1.0d	29-Dec-25	29-Dec-25	600.0d
11619	A101980	Review & Approve (HP) Cross-Belt Sorter Functional Specification	5.0d	30-Dec-25	6-Jan-26	600.0d
11620	A107460	Review & Approve (HNTB) Cross-Belt Sorter Functional Specification	10.0d	7-Jan-26	20-Jan-26	600.0d
11621	A107470	Review & Approve (HCAA) Cross-Belt Sorter Functional Specification	15.0d	21-Jan-26	10-Feb-26	600.0d
11622	WBS - Cross-Belt Sorter Control System Description of Operations Submittals		31.0d	29-Dec-25	10-Feb-26	600.0d
11623	A101810	Prep & Submit Cross-Belt Sorter Control System Description of Operations	1.0d	29-Dec-25	29-Dec-25	600.0d
11624	A101970	Review & Approve (HP) Cross-Belt Sorter Control System Description of Operati...	5.0d	30-Dec-25	6-Jan-26	600.0d
11625	A107480	Review & Approve (HNTB) Cross-Belt Sorter Control System Description of Ope...	10.0d	7-Jan-26	20-Jan-26	600.0d
11626	A107490	Review & Approve (HCAA) Cross-Belt Sorter Control System Description of Ope...	15.0d	21-Jan-26	10-Feb-26	600.0d
11627	WBS - Power Requirements and MCP/MPP/CSC/FCP Sizes Submittals		75.0d	29-Dec-25	13-Apr-26	74.0d
11628	A101940	Prep & Submit Power Requirements & MCP/MPP/CSC/FCP Sizes	45.0d	29-Dec-25	2-Mar-26	14.0d
11629	A107520	Review & Approve (HP) Power Requirements & MCP/MPP/CSC/FCP Sizes	5.0d	3-Mar-26	9-Mar-26	74.0d
11630	A107530	Review & Approve (HNTB) Power Requirements & MCP/MPP/CSC/FCP Sizes	10.0d	10-Mar-26	23-Mar-26	74.0d
11631	A102090	Review & Approve (HCAA) Power Requirements & MCP/MPP/CSC/FCP Sizes	15.0d	24-Mar-26	13-Apr-26	74.0d
11632	WBS - E-Stop Zone Drawings Submittals		90.0d	3-Mar-26	8-Jul-26	14.0d
11633	A102100	Prep & Submit E-Stop Zone Drawings	60.0d	3-Mar-26	26-May-26	14.0d
11634	A102140	Review & Approve (HP) E-Stop Zone Drawings	5.0d	27-May-26	2-Jun-26	14.0d

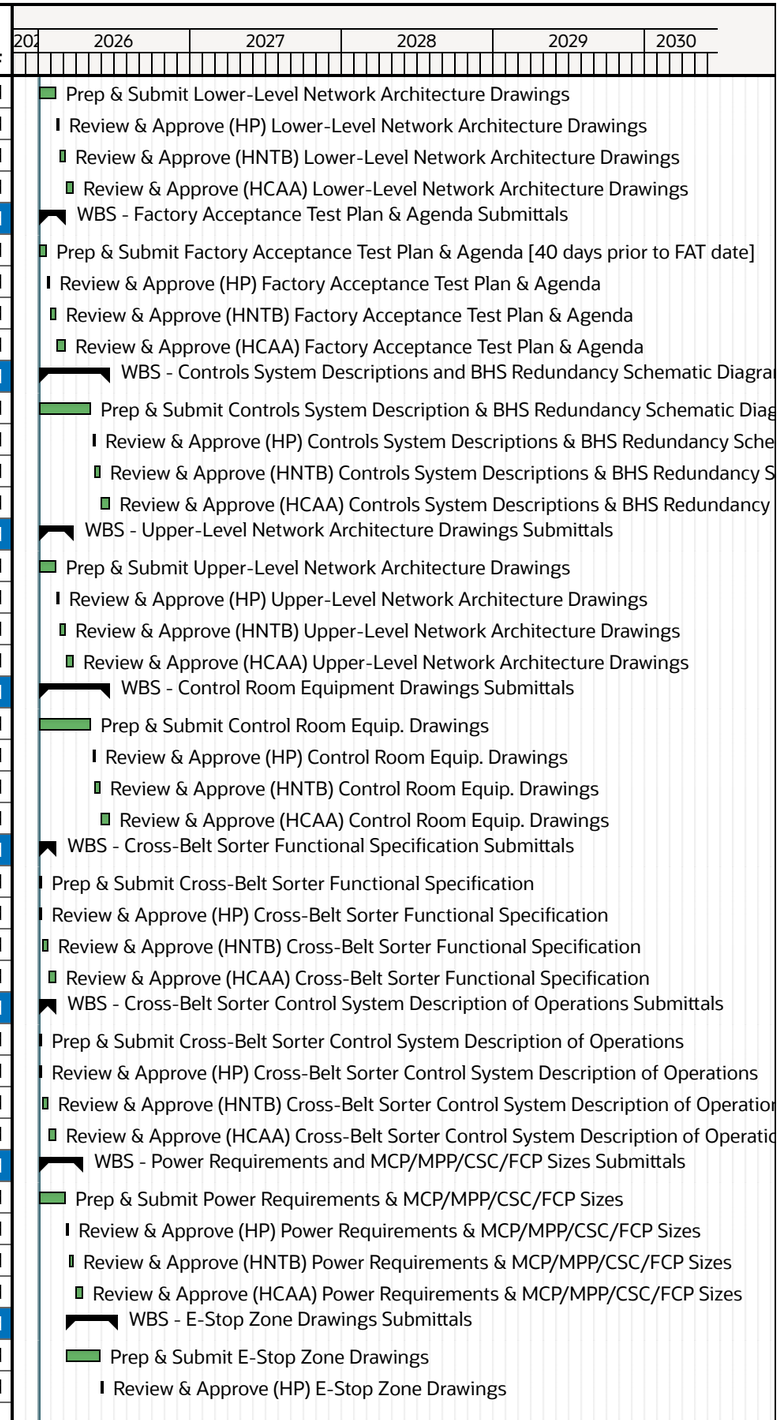


	ID	Name	Dur	Start	Finish	TF
11635	A107540	Review & Approve (HNTB) E-Stop Zone Drawings	10.0d	3-Jun-26	16-Jun-26	14.0d
11636	A107550	Review & Approve (HCAA) E-Stop Zone Drawings	15.0d	17-Jun-26	8-Jul-26	14.0d
11637	WBS - Functional Specification Submittals		116.0d	18-Nov-25 A	4-May-26	80.0d
11638	A101960	Prep & Submit Functional Specification [180 days prior to pre-TRR]	86.0d	18-Nov-25 A	23-Mar-26	80.0d
11639	A102130	Review & Approve (HP) Functional Specification	5.0d	24-Mar-26	30-Mar-26	80.0d
11640	A107560	Review & Approve (HNTB) Functional Specification	10.0d	31-Mar-26	13-Apr-26	80.0d
11641	A107570	Review & Approve (HCAA) Functional Specification	15.0d	14-Apr-26	4-May-26	80.0d
11642	WBS - Site Specific Test Plan Submittals		45.0d	26-Mar-26	28-May-26	42.0d
11643	A101830	Prep & Submit Site Specific Test Plan [60 days prior to Pre-TRR]	15.0d	26-Mar-26	15-Apr-26	42.0d
11644	A102040	Review & Approve (HP) Site Specific Test Plan	5.0d	16-Apr-26	22-Apr-26	42.0d
11645	A107580	Review & Approve (HNTB) Site Specific Test Plan	10.0d	23-Apr-26	6-May-26	42.0d
11646	A107590	Review & Approve (HCAA) Site Specific Test Plan	15.0d	7-May-26	28-May-26	42.0d
11647	WBS - Cybersecurity Plan Submittals		50.0d	29-Dec-25	9-Mar-26	120.0d
11648	A101850	Prep & Submit Cybersecurity Plan [5 days prior to beneficial use by phase]	20.0d	29-Dec-25	26-Jan-26	120.0d
11649	A102060	Review & Approve (HP) Cybersecurity Plan	5.0d	27-Jan-26	2-Feb-26	120.0d
11650	A107600	Review & Approve (HNTB) Cybersecurity Plan	10.0d	3-Feb-26	16-Feb-26	120.0d
11651	A107610	Review & Approve (HCAA) Cybersecurity Plan	15.0d	17-Feb-26	9-Mar-26	120.0d
11652	WBS - Seq 1 - Stage 1 - Step 1		85.0d	29-Dec-25	27-Apr-26	64.0d
11653	D1695	Prep & Submit Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-B17 [01-01-...	15.0d	29-Dec-25	19-Jan-26	64.0d
11654	D5866	Review & Approve (HP) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-B1...	5.0d	20-Jan-26	26-Jan-26	64.0d
11655	D5876	Review & Approve (HNTB) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-...	10.0d	27-Jan-26	9-Feb-26	64.0d
11656	D1696	Review & Approve (HCAA) Elec. Drawings MPP-A17, FCP-A17, MPP-B17, FCP-...	15.0d	10-Feb-26	2-Mar-26	64.0d
11657	D1697	Fab. & Deliver MPP-A17, FCP-A17, MPP-B17, FCP-B17, Elect Field Devices, Ca...	40.0d	3-Mar-26	27-Apr-26	64.0d
11658	WBS - Seq 1 - Stage 1 - Step 2		80.0d	20-Jan-26	11-May-26	80.0d
11659	D1698	Prep & Submit Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	10.0d	20-Jan-26	2-Feb-26	80.0d
11660	D5886	Review & Approve (HP) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	5.0d	3-Feb-26	9-Feb-26	80.0d
11661	D5896	Review & Approve (HNTB) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	10.0d	10-Feb-26	23-Feb-26	80.0d
11662	D1699	Review & Approve (HCAA) Elec. Drawings MPP-B9, FCP-B9 [01-01-02]	15.0d	24-Feb-26	16-Mar-26	80.0d
11663	D1700	Fab. & Deliver MPP-B9, FCP-B9, Elect Field Devices, Cabling [01-01-02]	40.0d	17-Mar-26	11-May-26	80.0d
11664	WBS - Seq 1 - Stage 1 - Step 4		80.0d	3-Feb-26	26-May-26	92.0d
11665	D1701	Prep & Submit Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	10.0d	3-Feb-26	16-Feb-26	92.0d
11666	D5906	Review & Approve (HP) Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	5.0d	17-Feb-26	23-Feb-26	92.0d
11667	D5916	Review & Approve (HNTB) Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	10.0d	24-Feb-26	9-Mar-26	92.0d
11668	D1702	Review & Approve (HCAA) Elec. Drawings MPP-B8, FCP-B8 [01-01-04]	15.0d	10-Mar-26	30-Mar-26	92.0d
11669	D1703	Fab. & Deliver MPP-B8, FCP-B8, Elect Field Devices, Cabling [01-01-04]	40.0d	31-Mar-26	26-May-26	92.0d
11670	WBS - Seq 1 - Stage 2 - Step 1		80.0d	17-Feb-26	9-Jun-26	106.0d
11671	D1704	Prep & Submit Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	10.0d	17-Feb-26	2-Mar-26	106.0d
11672	D5926	Review & Approve (HP) Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	5.0d	3-Mar-26	9-Mar-26	106.0d
11673	D5936	Review & Approve (HNTB) Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	10.0d	10-Mar-26	23-Mar-26	106.0d
11674	D1705	Review & Approve (HCAA) Elec. Drawings MPP-B2, FCP-B2 [01-02-01]	15.0d	24-Mar-26	13-Apr-26	106.0d
11675	D1706	Fab. & Deliver MPP-B2, FCP-B2, Elect Field Devices, Cabling [01-02-01]	40.0d	14-Apr-26	9-Jun-26	106.0d
11676	WBS - Seq 1 - Stage 2 - Step 2		85.0d	3-Mar-26	30-Jun-26	106.0d

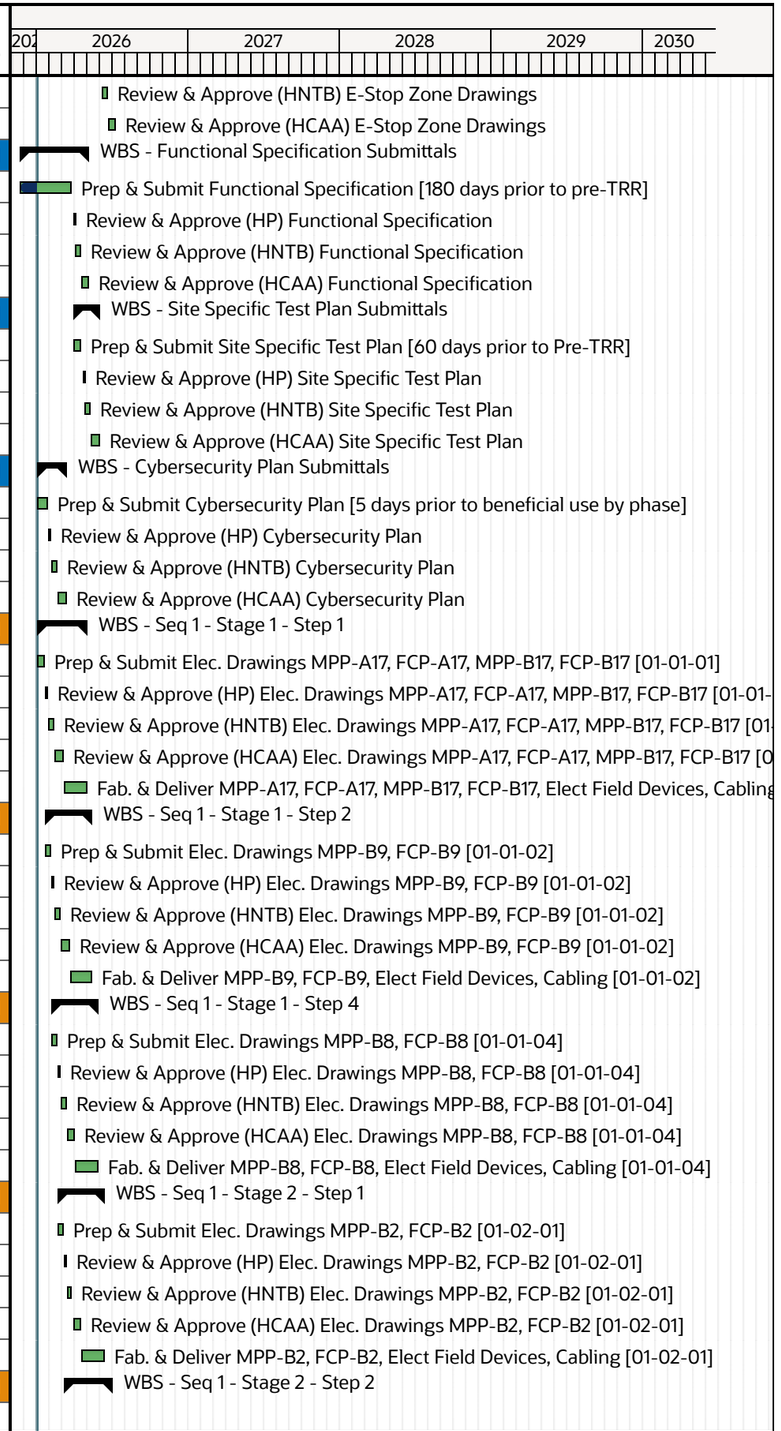


	ID	Name	Dur	Start	Finish	TF
11677	D1707	Prep & Submit Elec. Drawings MPP-A1, FCP-A1, MPP-A9, FCP-A9 [01-02-02]	15.0d	3-Mar-26	23-Mar-26	106.0d
11678	D5946	Review & Approve (HP) Elec. Drawings MPP-A1, FCP-A1, MPP-A9, FCP-A9 [01-...	5.0d	24-Mar-26	30-Mar-26	106.0d
11679	D5956	Review & Approve (HNTB) Elec. Drawings MPP-A1, FCP-A1, MPP-A9, FCP-A9 [...	10.0d	31-Mar-26	13-Apr-26	106.0d
11680	D1708	Review & Approve (HCAA) Elec. Drawings MPP-A1, FCP-A1, MPP-A9, FCP-A9 [...	15.0d	14-Apr-26	4-May-26	106.0d
11681	D1709	Fab. & Deliver MPP-A1, FCP-A1, MPP-A9, FCP-A9, Elect Field Devices, Cabling ...	40.0d	5-May-26	30-Jun-26	106.0d
11682	WBS - XBM-R & XBM-B Electrical/Controls Submittals & Procurement		284.0d	11-Aug-26	22-Sep-27	85.0d
11683	WBS - XBM-R & XBM-B Electrical/Controls Submittals		204.0d	11-Aug-26	28-May-27	85.0d
11684	D1687	Prep & Submit Cross Belt Sorter XBM1 Elec. Drawings	80.0d	11-Aug-26	3-Dec-26	7.0d
11685	D1689	Prep & Submit Cross Belt Sorter XBM2 Elec. Drawings	79.0d	4-Dec-26	26-Mar-27	85.0d
11686	D6146	Review & Approve (HP) Cross Belt Sorter XBM1 Elect Dwg Sets	14.0d	4-Dec-26	23-Dec-26	7.0d
11687	D6156	Review & Approve (HNTB) Cross Belt Sorter XBM1 Elect Dwg Sets	14.0d	24-Dec-26	14-Jan-27	7.0d
11688	D1688	Review & Approve (HCAA) Cross Belt Sorter XBM1 Elect Dwg Sets	14.0d	15-Jan-27	3-Feb-27	7.0d
11689	D6166	Review & Approve (HP) Cross Belt Sorter XBM2 Elect Dwg Sets	15.0d	29-Mar-27	16-Apr-27	85.0d
11690	D6176	Review & Approve (HNTB) Cross Belt Sorter XBM2 Elect Dwg Sets	15.0d	19-Apr-27	7-May-27	85.0d
11691	D1692	Review & Approve (HCAA) Cross Belt Sorter XBM2 Elect Dwg Sets	15.0d	10-May-27	28-May-27	85.0d
11692	WBS - XBM-R & XBM-B Electrical/Controls Fabrication		162.0d	4-Feb-27	22-Sep-27	85.0d
11693	D1690	Fab. & Deliver XBM1 Power Panels (13)	80.0d	4-Feb-27	26-May-27	7.0d
11694	D1691	Fab. & Deliver XBM1 Field Control Panels, Elect Field Devices, Cabling	80.0d	4-Feb-27	26-May-27	7.0d
11695	D1693	Fab. & Deliver XBM2 Power Panels (13)	80.0d	1-Jun-27	22-Sep-27	85.0d
11696	D1694	Fab. & Deliver XBM2 Field Control Panels, Elect Field Devices, Cabling	80.0d	1-Jun-27	22-Sep-27	85.0d
11697	WBS - Electrical Long Lead System Procurement - CCBS - Part 2 Supp. B		260.0d	29-Dec-25	6-Jan-27	145.0d
11698	A108940	Prep & Submit Long Lead Elec. Equip. Submittals - Part 2 Supp. B	5.0d	29-Dec-25 C	5-Jan-26	11.0d
11699	A108950	Review & Approve (HP) Long Lead Elec.Equip. Submittals - Part 2 Supp. B	5.0d	6-Jan-26	12-Jan-26	11.0d
11700	A108960	Review & Approve (HNTB) Long Lead Elec. Equip. Submittals - Part 2 Supp. B	10.0d	13-Jan-26	26-Jan-26	11.0d
11701	A108970	Review & Approve (HCAA) Long Lead Elec. Equip. Submittals - Part 2 Supp. B	15.0d	27-Jan-26	16-Feb-26	11.0d
11702	A108980	Fab. & Ship Electrical Distribution Panels - Part 2 Supp. B	110.0d	17-Feb-26	7-Jun-26	15.0d
11703	A110500	Fab. & Ship Switchboards EDS3 & EDS 4 - Part 2 Supp. B	225.0d	17-Feb-26	6-Jan-27	145.0d
11704	A108990	Delivery on Site Electrical Distribution Panels - Part 2 Supp. B	0.0d		7-Jun-26	15.0d
11705	A110510	Delivery on Site Switchboards EDS3 & EDS 4 - Part 2 Supp. B	0.0d		6-Jan-27	145.0d
11706	WBS - Part 2 Supplement C Wave 1 - Core & Shell Procurement		1,006.0d	29-Dec-25	11-Dec-29	70.0d
11707	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supplement C Wave 1		991.0d	20-Jan-26	11-Dec-29	70.0d
11708	WBS - General BHS Submittals & Procurement - Part 2 Supplement C Wave 1		966.0d	20-Jan-26	2-Nov-29	95.0d
11709	WBS - Computer Log Submittals		45.0d	31-Aug-29	2-Nov-29	95.0d
11710	D1073	Prep & Submit Computer Log	15.0d	31-Aug-29	21-Sep-29	95.0d
11711	A106360	Review & Approve (HP) Computer Log	5.0d	24-Sep-29	28-Sep-29	95.0d
11712	A106370	Review & Approve (HNTB) Computer Log	10.0d	1-Oct-29	12-Oct-29	95.0d
11713	D1076	Review & Approve (HCAA) Computer Log	15.0d	15-Oct-29	2-Nov-29	95.0d
11714	WBS - O&M Training Plan & Proposed Agenda Submittals		45.0d	20-Jan-26	23-Mar-26	110.0d
11715	D1065	Prep & Submit O&M Training Plan & Proposed Agenda	15.0d	20-Jan-26	9-Feb-26	110.0d
11716	A101390	Review & Approve (HP) O&M Training Plan & Proposed Agenda	5.0d	10-Feb-26	16-Feb-26	110.0d
11717	A106390	Review & Approve (HNTB) O&M Training Plan & Proposed Agenda	10.0d	17-Feb-26	2-Mar-26	110.0d
11718	D1067	Review & Approve (HCAA) O&M Training Plan & Proposed Agenda	15.0d	3-Mar-26	23-Mar-26	110.0d

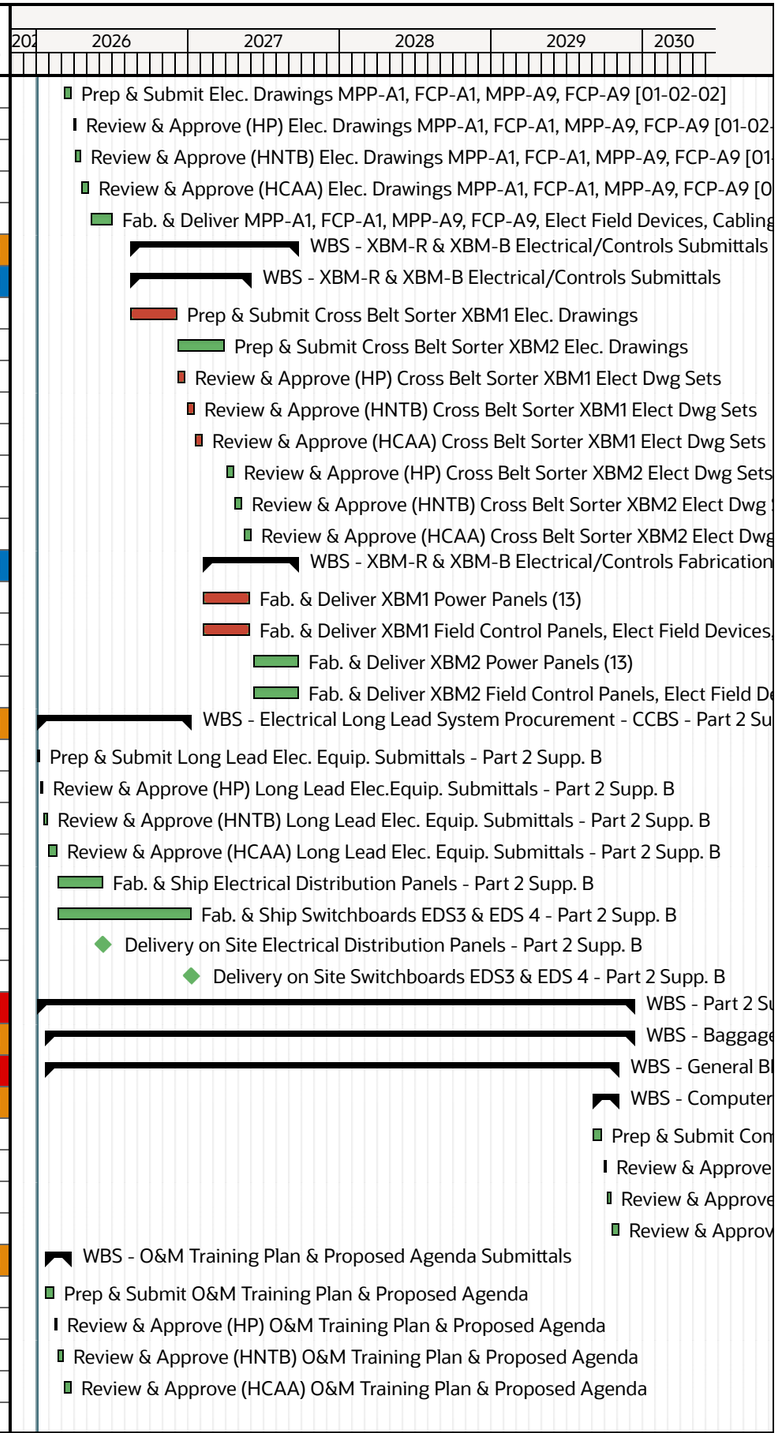


	ID	Name	Dur	Start	Finish	TF
11719	WBS - Final Parts List Submittals		60.0d	13-Feb-26	7-May-26	983.0d
11720	A101210	Prep & Submit Final Parts List[90 days prior to beneficial use of Equip.]	30.0d	13-Feb-26	26-Mar-26	982.0d
11721	A101450	Review & Approve (HP) Final Parts List	5.0d	27-Mar-26	2-Apr-26	982.0d
11722	A106410	Review & Approve (HNTB) Final Parts List	10.0d	3-Apr-26	16-Apr-26	982.0d
11723	A106400	Review & Approve (HCAA) Final Parts List	15.0d	17-Apr-26	7-May-26	982.0d
11724	WBS - Configuration Management Plan Submittals		60.0d	13-Feb-26	7-May-26	548.0d
11725	A101170	Prep & Submit Configuration Management Plan	30.0d	13-Feb-26	26-Mar-26	548.0d
11726	A101400	Review & Approve (HP) Configuration Management Plan	5.0d	27-Mar-26	2-Apr-26	548.0d
11727	A106530	Review & Approve (HNTB) Configuration Management Plan	10.0d	3-Apr-26	16-Apr-26	548.0d
11728	A106540	Review & Approve (HCAA) Configuration Management Plan	15.0d	17-Apr-26	7-May-26	548.0d
11729	WBS - Baggage Tag Verification Report Submittals		40.0d	13-Feb-26	9-Apr-26	568.0d
11730	D1049	Prep & Submit Baggage Tag Verification Report	10.0d	13-Feb-26	26-Feb-26	568.0d
11731	A101490	Review & Approve (HP) Baggage Tag Verification Report	5.0d	27-Feb-26	5-Mar-26	568.0d
11732	A106550	Review & Approve (HNTB) Baggage Tag Verification Report	10.0d	6-Mar-26	19-Mar-26	568.0d
11733	D1055	Review & Approve (HCAA) Baggage Tag Verification Report	15.0d	20-Mar-26	9-Apr-26	568.0d
11734	WBS - BHS Equipment Combined Heat Output Figures Submittals		120.0d	13-Feb-26	3-Aug-26	923.0d
11735	A101260	Prep & Submit BHS Equip. Combined Heat Output Figures	90.0d	13-Feb-26	19-Jun-26	922.0d
11736	A101520	Review & Approve (HP) BHS Equip. Combined Heat Output Figures	5.0d	22-Jun-26	26-Jun-26	922.0d
11737	A106650	Review & Approve (HNTB) BHS Equip. Combined Heat Output Figures	10.0d	29-Jun-26	13-Jul-26	922.0d
11738	A106660	Review & Approve (HCAA) BHS Equip. Combined Heat Output Figures	15.0d	14-Jul-26	3-Aug-26	922.0d
11739	WBS - CBRA Magnetic Lock / UPS / Emergency Egress Description of Operations Submittals		50.0d	20-Mar-26	29-May-26	167.0d
11740	D1057	Prep & Submit CBRA Magnetic Lock / UPS / Emergency Egress Description of ...	20.0d	20-Mar-26	16-Apr-26	48.0d
11741	A101510	Review & Approve (HP) CBRA Magnetic Lock / UPS / Emergency Egress Descri...	5.0d	17-Apr-26	23-Apr-26	167.0d
11742	A106690	Review & Approve (HNTB) CBRA Magnetic Lock / UPS / Emergency Egress Des...	10.0d	24-Apr-26	7-May-26	167.0d
11743	D1060	Review & Approve (HCAA) CBRA Magnetic Lock / UPS / Emergency Egress Des...	15.0d	8-May-26	29-May-26	167.0d
11744	WBS - List of Lubricants Submittals		90.0d	13-Feb-26	19-Jun-26	54.0d
11745	D1050	Prep & Submit List of Lubricants	60.0d	13-Feb-26	7-May-26	54.0d
11746	A101540	Review & Approve (HP) List of Lubricants	5.0d	8-May-26	14-May-26	54.0d
11747	A106750	Review & Approve (HNTB) List of Lubricants	10.0d	15-May-26	29-May-26	54.0d
11748	D1063	Review & Approve (HCAA) List of Lubricants	15.0d	1-Jun-26	19-Jun-26	54.0d
11749	WBS - Periodic Maintenance Inspection & Lubrication Chart		90.0d	13-Feb-26	19-Jun-26	47.0d
11750	D1051	Prep & Submit Periodic Maintenance Inspection & Lubrication Chart	60.0d	13-Feb-26	7-May-26	47.0d
11751	D2966	Review & Approve (HP) Periodic Maintenance Inspection & Lubrication Chart	5.0d	8-May-26	14-May-26	47.0d
11752	D2956	Review & Approve (HNTB) Periodic Maintenance Inspection & Lubrication Chart	10.0d	15-May-26	29-May-26	47.0d
11753	D1064	Review & Approve (HCAA) Periodic Maintenance Inspection & Lubrication Chart	15.0d	1-Jun-26	19-Jun-26	47.0d
11754	WBS - Estimated Parts List		60.0d	27-May-26	19-Aug-26	5.0d
11755	D1062	Prep & Submit Estimated Parts List	30.0d	27-May-26	8-Jul-26	5.0d
11756	D3036	Review & Approve (HP) Estimated Parts List	5.0d	9-Jul-26	15-Jul-26	5.0d
11757	D3046	Review & Approve (HNTB) Estimated Parts List	10.0d	16-Jul-26	29-Jul-26	5.0d
11758	D1066	Review & Approve (HCAA) Estimated Parts List	15.0d	30-Jul-26	19-Aug-26	5.0d
11759	WBS - Final Parts List		60.0d	15-Jun-27	8-Sep-27	644.0d
11760	D1068	Prep & Submit Final Parts List	30.0d	15-Jun-27	27-Jul-27	643.0d

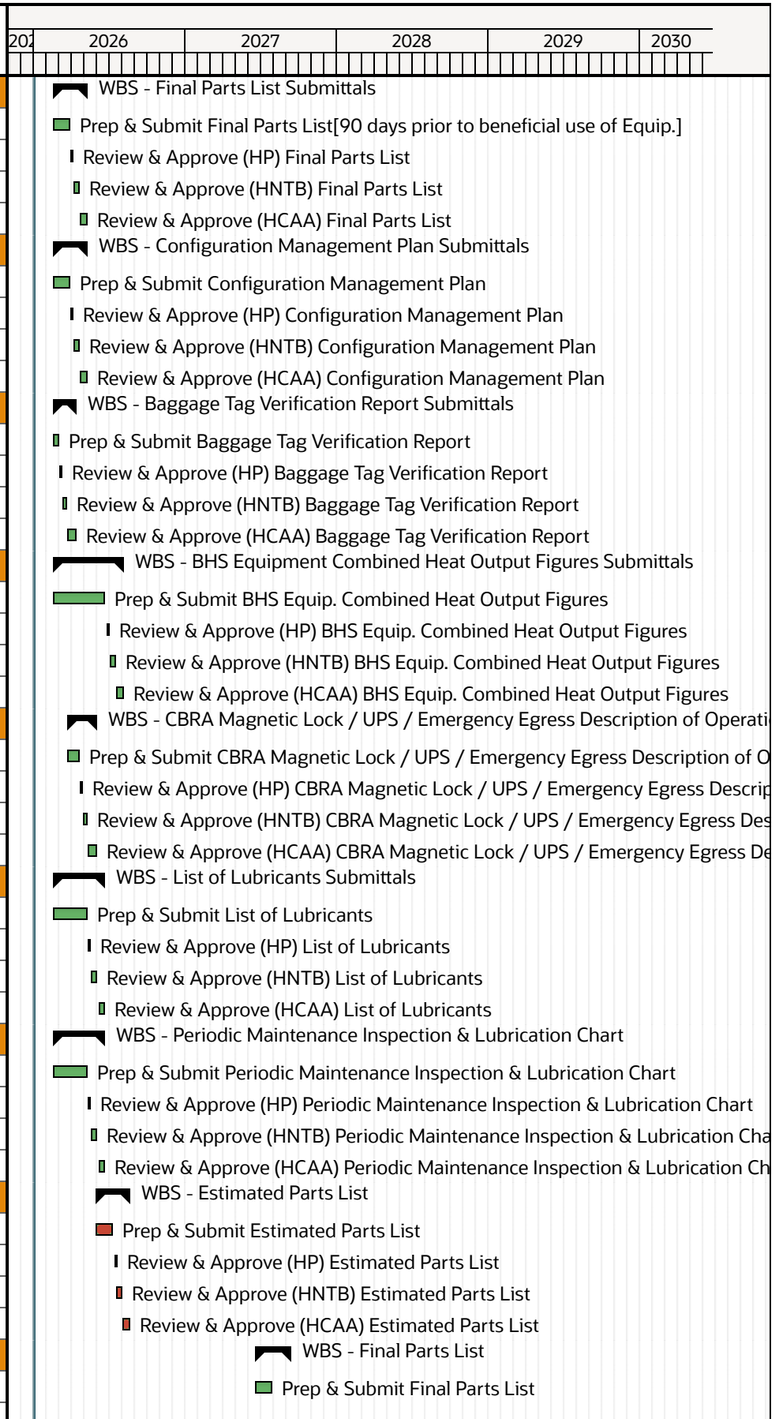


	ID	Name	Dur	Start	Finish	TF
11761	D3116	Review & Approve (HP) Final Parts List	5.0d	28-Jul-27	3-Aug-27	643.0d
11762	D3126	Review & Approve (HNTB) Final Parts List	10.0d	4-Aug-27	17-Aug-27	643.0d
11763	D1069	Review & Approve (HCAA) Final Parts List	15.0d	18-Aug-27	8-Sep-27	643.0d
11764	WBS - Computer/Software/Hardware Inventory		45.0d	31-Aug-29	2-Nov-29	95.0d
11765	D1072	Prep & Submit Computer/Software/Hardware Inventory	15.0d	31-Aug-29	21-Sep-29	95.0d
11766	D3176	Review & Approve (HP) Computer/Software/Hardware Inventory	5.0d	24-Sep-29	28-Sep-29	95.0d
11767	D3186	Review & Approve (HNTB) Computer/Software/Hardware Inventory	10.0d	1-Oct-29	12-Oct-29	95.0d
11768	D1075	Review & Approve (HCAA) Computer/Software/Hardware Inventory	15.0d	15-Oct-29	2-Nov-29	95.0d
11769	WBS - Operational Run-In and Closeout Data Documentation		45.0d	31-Aug-29	2-Nov-29	95.0d
11770	D1074	Prep & Submit Operational Run-in & Closeout Data Documentation	15.0d	31-Aug-29	21-Sep-29	95.0d
11771	D3256	Review & Approve (HP) Operational Run-in & Closeout Data Documentation	5.0d	24-Sep-29	28-Sep-29	95.0d
11772	D3266	Review & Approve (HNTB) Operational Run-in & Closeout Data Documentation	10.0d	1-Oct-29	12-Oct-29	95.0d
11773	D1077	Review & Approve (HCAA) Operational Run-in & Closeout Data Documentation	15.0d	15-Oct-29	2-Nov-29	95.0d
11774	WBS - Certificate of Installation Compliance		45.0d	31-Aug-29	2-Nov-29	95.0d
11775	D1071	Prep & Submit Certificate of Install Compliance	15.0d	31-Aug-29	21-Sep-29	95.0d
11776	D3316	Review & Approve (HP) Certificate of Install Compliance	5.0d	24-Sep-29	28-Sep-29	95.0d
11777	D3326	Review & Approve (HNTB) Certificate of Install Compliance	10.0d	1-Oct-29	12-Oct-29	95.0d
11778	D1079	Review & Approve (HCAA) Certificate of Install Compliance	15.0d	15-Oct-29	2-Nov-29	95.0d
11779	WBS - Certificate of Testing Compliance		40.0d	31-Aug-29	26-Oct-29	100.0d
11780	D1070	Prep & Submit Certificate of Testing Compliance	15.0d	31-Aug-29	21-Sep-29	100.0d
11781	D3376	Review & Approve (HP) Certificate of Testing Compliance	5.0d	24-Sep-29	28-Sep-29	100.0d
11782	D3386	Review & Approve (HNTB) Certificate of Testing Compliance	5.0d	1-Oct-29	5-Oct-29	100.0d
11783	D1078	Review & Approve (HCAA) Certificate of Testing Compliance	15.0d	8-Oct-29	26-Oct-29	100.0d
11784	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supplement C Wave 1		961.0d	3-Feb-26	9-Nov-29	90.0d
11785	WBS - General Mechanical BHS Submittals & Procurement		953.0d	13-Feb-26	9-Nov-29	90.0d
11786	WBS - Cross Belt Mechanical Catalog Cut / Equipment Specs		45.0d	13-Feb-26	16-Apr-26	7.0d
11787	D1086	Prep & Submit Cross Belt Mech. Catalog Cut / Equip. Specs	15.0d	13-Feb-26	5-Mar-26	7.0d
11788	D3436	Review & Approve (HP) Cross Belt Mech. Catalog Cut / Equip. Specs	5.0d	6-Mar-26	12-Mar-26	7.0d
11789	D3446	Review & Approve (HNTB) Cross Belt Mech. Catalog Cut / Equip. Specs	10.0d	13-Mar-26	26-Mar-26	7.0d
11790	D1087	Review & Approve (HCAA) Cross Belt Mech. Catalog Cut / Equip. Specs	15.0d	27-Mar-26	16-Apr-26	7.0d
11791	WBS - CBRA Egress Pathway Landing		45.0d	20-Mar-26	21-May-26	172.0d
11792	D1088	Prep & Submit CBRA Egress Pathway Landing	20.0d	20-Mar-26	16-Apr-26	48.0d
11793	D3456	Review & Approve (HP) CBRA Egress Pathway Landing	5.0d	17-Apr-26	23-Apr-26	172.0d
11794	D3466	Review & Approve (HNTB) CBRA Egress Pathway Landing	5.0d	24-Apr-26	30-Apr-26	172.0d
11795	D1089	Review & Approve (HCAA) CBRA Egress Pathway Landing	15.0d	1-May-26	21-May-26	172.0d
11796	WBS - Mechanical As-Built Drawings		50.0d	31-Aug-29	9-Nov-29	90.0d
11797	D1090	Prep & Submit Mech. As-Built Drawings	20.0d	31-Aug-29	28-Sep-29	90.0d
11798	D3476	Review & Approve (HP) Mech. As-Built Drawings	5.0d	1-Oct-29	5-Oct-29	90.0d
11799	D3486	Review & Approve (HNTB) Mech. As-Built Drawings	10.0d	8-Oct-29	19-Oct-29	90.0d
11800	D1091	Review & Approve (HCAA) Mech. As-Built Drawings	15.0d	22-Oct-29	9-Nov-29	90.0d
11801	WBS - Seq 1 - Stage 3 - Step 1		322.0d	3-Feb-26	7-May-27	169.0d
11802	D1156	Fab. & Deliver RLM1 1 HSD [01-03-01]	140.0d	3-Feb-26	19-Aug-26	90.0d

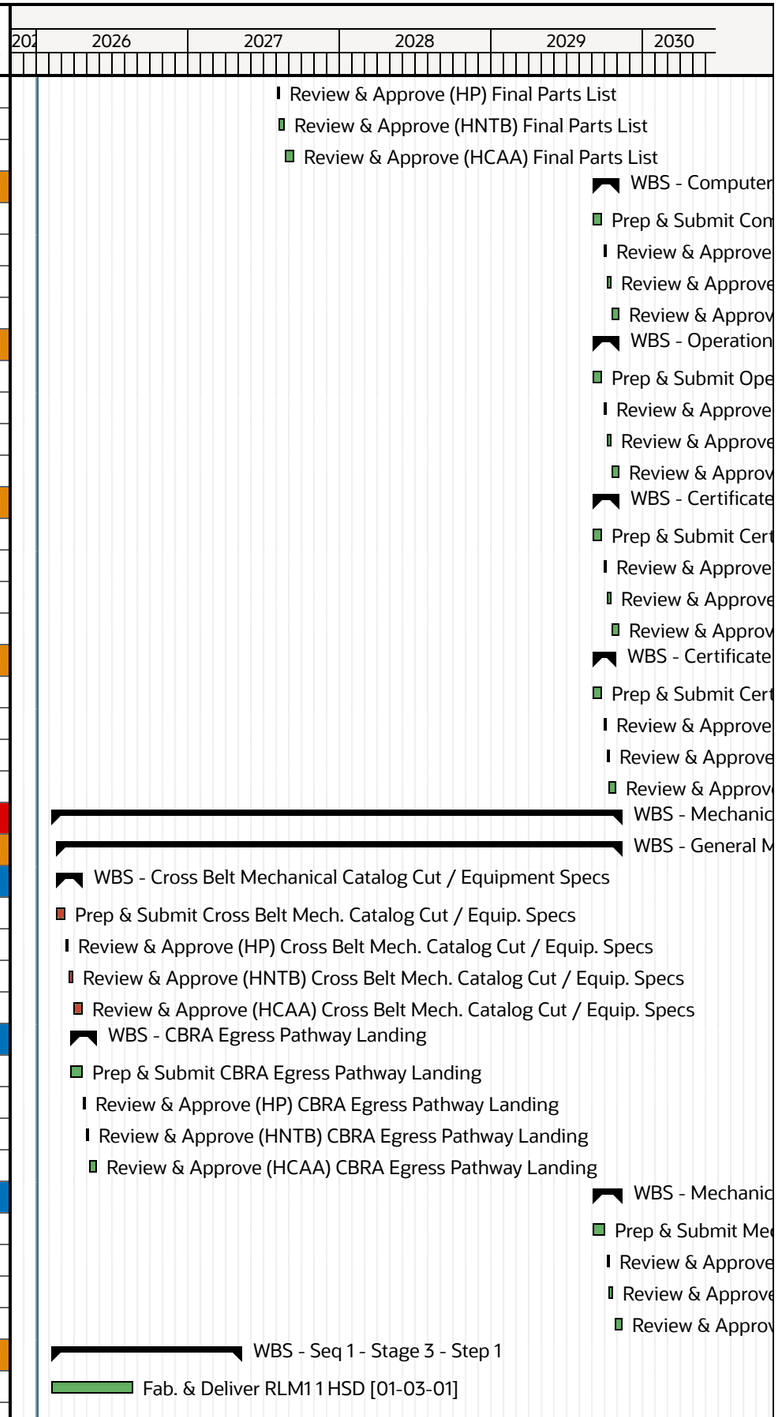


	ID	Name	Dur	Start	Finish	TF
11803	D1157	Fab. & Deliver SFM7A 1 HSD [01-03-01]	140.0d	3-Feb-26	19-Aug-26	90.0d
11804	D1158	Fab. & Deliver ALM1 34 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11805	D1159	Fab. & Deliver ALM1 22 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11806	D1160	Fab. & Deliver ALM2 4 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11807	D1161	Fab. & Deliver ALM2 22 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11808	D1162	Fab. & Deliver CLM2 2 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11809	D1163	Fab. & Deliver RLM2 5 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11810	D1164	Fab. & Deliver TD1 6 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11811	D1165	Fab. & Deliver TD1 33 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11812	D1166	Fab. & Deliver TD2 9 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11813	D1167	Fab. & Deliver TD2 29 FSD [01-03-01]	60.0d	3-Feb-26	27-Apr-26	170.0d
11814	WBS - Seq 1 - Stage 3 - Step 1 - Sector J		200.0d	13-Feb-26	24-Nov-26	42.0d
11815	WBS - BHS Mechanical Submittals (Sector J) [01-03-01]		100.0d	13-Feb-26	6-Jul-26	42.0d
11816	D1168	Prep & Submit Mech. Plan & Elev Dwg Set (Sector J) [01-03-01]	25.0d	13-Feb-26	19-Mar-26	38.0d
11817	D3876	Review & Approve Mech Plan & Elev Dwg Set (HP) (Sector J) [01-03-01]	5.0d	20-Mar-26	26-Mar-26	42.0d
11818	D3886	Review & Approve Mech Plan & Elev Dwg Set (HNTB) (Sector J) [01-03-01]	10.0d	27-Mar-26	9-Apr-26	42.0d
11819	D1169	Review & Approve Mech Plan & Elev Dwg Set (HCAA) (Sector J) [01-03-01]	15.0d	10-Apr-26	30-Apr-26	42.0d
11820	D1170	Prep & Submit Header Steel Dwg Set (Sector J) [01-03-01]	15.0d	1-May-26	21-May-26	42.0d
11821	D3896	Review & Approve Header Steel Dwg Set (HP) (Sector J) [01-03-01]	5.0d	22-May-26	29-May-26	42.0d
11822	D3906	Review & Approve Header Steel Dwg Set (HNTB) (Sector J) [01-03-01]	10.0d	1-Jun-26	12-Jun-26	42.0d
11823	D1174	Review & Approve Header Steel Dwg Set (HCAA) (Sector J) [01-03-01]	15.0d	15-Jun-26	6-Jul-26	42.0d
11824	WBS - BHS Mechanical Fabrication (Sector J) [01-03-01]		145.0d	1-May-26	24-Nov-26	42.0d
11825	D1171	Fab. & Deliver Conveyor Batch 1 (15) (Sector J) [01-03-01]	120.0d	1-May-26	20-Oct-26	47.0d
11826	D1172	Fab. & Deliver Conveyor Batch 2 (15) (Sector J) [01-03-01]	120.0d	8-May-26	27-Oct-26	47.0d
11827	D1173	Fab. & Deliver Conveyor Batch 3 (15) (Sector J) [01-03-01]	120.0d	15-May-26	3-Nov-26	47.0d
11828	D1175	Fab. & Deliver Conveyor Batch 4 (15) (Sector J) [01-03-01]	120.0d	22-May-26	10-Nov-26	47.0d
11829	D1176	Fab. & Deliver Conveyor Batch 5 (5) (Sector J) [01-03-01]	120.0d	1-Jun-26	17-Nov-26	47.0d
11830	D1177	Fab. & Deliver Header Steel / Platform / Sills (Sector J) [01-03-01]	80.0d	7-Jul-26	27-Oct-26	42.0d
11831	D1178	Prep Mech. Matl for Install (Sector J) [01-03-01]	20.0d	28-Oct-26	24-Nov-26	42.0d
11832	WBS - Seq 1 - Stage 3 - Step 1 - Sector H		240.0d	20-Mar-26	1-Mar-27	82.0d
11833	WBS - BHS Mechanical Submittals (Sector H) [01-03-01]		140.0d	20-Mar-26	6-Oct-26	63.0d
11834	WBS - Mechanical Submittals Sector H.1 [01-03-01]		110.0d	20-Mar-26	24-Aug-26	38.0d
11835	D1179	Prep & Submit Mech. Plan & Elev Dwg Set (Sector H.1) [01-03-01]	30.0d	20-Mar-26	30-Apr-26	38.0d
11836	D3916	Review & Approve Mech Plan & Elev Dwg Set (HP) (Sector H.1) [01-03-01]	5.0d	1-May-26	7-May-26	38.0d
11837	D3926	Review & Approve Mech Plan & Elev Dwg Set (HNTB) (Sector H.1) [01-03-01]	10.0d	8-May-26	21-May-26	38.0d
11838	D1180	Review & Approve Mech Plan & Elev Dwg Set (HCAA) (Sector H.1) [01-03-01]	15.0d	22-May-26	12-Jun-26	38.0d
11839	D1182	Prep & Submit Header Steel Dwg Set (Sector H.1) [01-03-01]	20.0d	15-Jun-26	13-Jul-26	38.0d
11840	D3936	Review & Approve Header Steel Dwg Set (HP) (Sector H.1) [01-03-01]	5.0d	14-Jul-26	20-Jul-26	38.0d
11841	D3946	Review & Approve Header Steel Dwg Set (HNTB) (Sector H.1) [01-03-01]	10.0d	21-Jul-26	3-Aug-26	38.0d
11842	D1188	Review & Approve Header Steel Dwg Set (HCAA) (Sector H.1) [01-03-01]	15.0d	4-Aug-26	24-Aug-26	38.0d
11843	WBS - Mechanical Submittals Sector H.2 [01-03-01]		110.0d	1-May-26	6-Oct-26	63.0d
11844	D1181	Prep & Submit Mech. Plan & Elev Dwg Set (Sector H.2) [01-03-01]	30.0d	1-May-26	12-Jun-26	43.0d

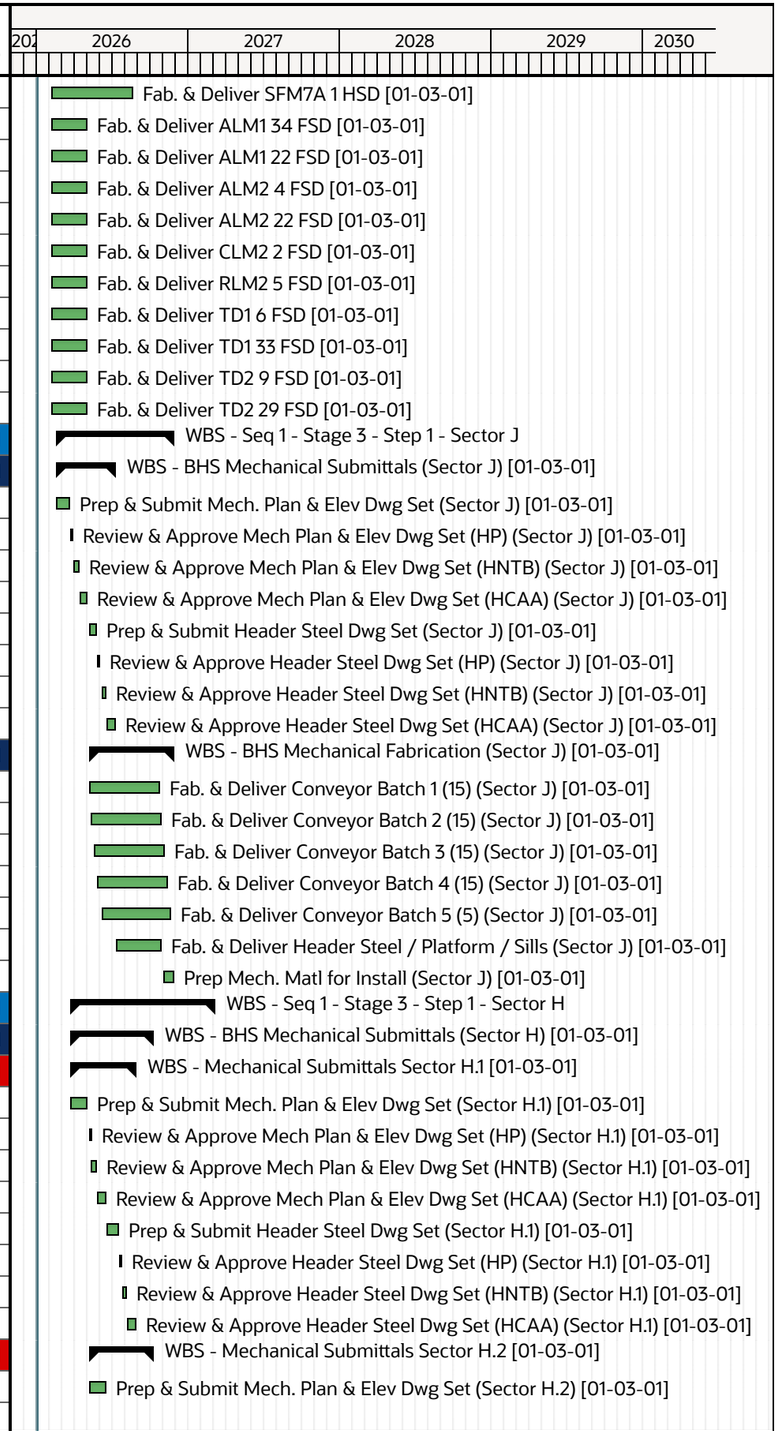


	ID	Name	Dur	Start	Finish	TF
11845	D3956	Review & Approve Mech Plan & Elev Dwg Set (HP) (Sector H.2) [01-03-01]	5.0d	15-Jun-26	19-Jun-26	63.0d
11846	D3966	Review & Approve Mech Plan & Elev Dwg Set (HNTB) (Sector H.2) [01-03-01]	10.0d	22-Jun-26	6-Jul-26	63.0d
11847	D1186	Review & Approve Mech Plan & Elev Dwg Set (HCAA) (Sector H.2) [01-03-01]	15.0d	7-Jul-26	27-Jul-26	63.0d
11848	D1191	Prep & Submit Header Steel Dwg Set (Sector H.2) [01-03-01]	20.0d	28-Jul-26	24-Aug-26	63.0d
11849	D3976	Review & Approve Header Steel Dwg Set (HP) (Sector H.2) [01-03-01]	5.0d	25-Aug-26	31-Aug-26	63.0d
11850	D3996	Review & Approve Header Steel Dwg Set (HNTB) (Sector H.2) [01-03-01]	10.0d	1-Sep-26	15-Sep-26	63.0d
11851	D1197	Review & Approve Header Steel Dwg Set (HCAA) (Sector H.2) [01-03-01]	15.0d	16-Sep-26	6-Oct-26	63.0d
11852	WBS - BHS Mechanical Fabrication (Sector H) [01-03-01]		180.0d	15-Jun-26	1-Mar-27	82.0d
11853	D1183	Fab. & Deliver Conveyor Batch 1 (15) (Sector H) [01-03-01]	120.0d	15-Jun-26	3-Dec-26	48.0d
11854	D1184	Fab. & Deliver Conveyor Batch 2 (15) (Sector H) [01-03-01]	120.0d	22-Jun-26	10-Dec-26	82.0d
11855	D1185	Fab. & Deliver Conveyor Batch 3 (15) (Sector H) [01-03-01]	120.0d	29-Jun-26	17-Dec-26	82.0d
11856	D1187	Fab. & Deliver Conveyor Batch 4 (15) (Sector H) [01-03-01]	119.0d	8-Jul-26	24-Dec-26	82.0d
11857	D1189	Fab. & Deliver Conveyor Batch 5 (15) (Sector H) [01-03-01]	119.0d	15-Jul-26	4-Jan-27	82.0d
11858	D1190	Fab. & Deliver Conveyor Batch 6 (15) (Sector H) [01-03-01]	119.0d	22-Jul-26	11-Jan-27	82.0d
11859	D1192	Fab. & Deliver Conveyor Batch 7 (15) (Sector H) [01-03-01]	119.0d	29-Jul-26	18-Jan-27	82.0d
11860	D1194	Fab. & Deliver Conveyor Batch 8 (15) (Sector H) [01-03-01]	119.0d	5-Aug-26	25-Jan-27	82.0d
11861	D1195	Fab. & Deliver Conveyor Batch 9 (15) (Sector H) [01-03-01]	119.0d	12-Aug-26	1-Feb-27	82.0d
11862	D1196	Fab. & Deliver Conveyor Batch 10 (15) (Sector H) [01-03-01]	119.0d	19-Aug-26	8-Feb-27	82.0d
11863	D1193	Fab. & Deliver Header Steel / Platform / Sills (Sector H.1) [01-03-01]	80.0d	25-Aug-26	17-Dec-26	38.0d
11864	D1198	Fab. & Deliver Conveyor Batch 11 (15) (Sector H) [01-03-01]	119.0d	26-Aug-26	15-Feb-27	82.0d
11865	D1199	Fab. & Deliver Conveyor Batch 12 (15) (Sector H) [01-03-01]	119.0d	2-Sep-26	22-Feb-27	82.0d
11866	D1200	Fab. & Deliver Conveyor Batch 13 (12) (Sector H) [01-03-01]	119.0d	10-Sep-26	1-Mar-27	82.0d
11867	D1201	Fab. & Deliver Header Steel / Platform / Sills (Sector H.2) [01-03-01]	79.0d	7-Oct-26	29-Jan-27	63.0d
11868	D1202	Prep Mech. Matl for Install (Sector H) [01-03-01]	19.0d	18-Dec-26	15-Jan-27	38.0d
11869	WBS - Seq 1 - Stage 3 - Step 1 - Sector G		219.0d	15-Jun-26	23-Apr-27	43.0d
11870	WBS - BHS Mechanical Submittals (Sector G) [01-03-01]		120.0d	15-Jun-26	3-Dec-26	43.0d
11871	D1203	Prep & Submit Mech. Plan & Elev Dwg Set (Sector G) [01-03-01]	25.0d	15-Jun-26	20-Jul-26	43.0d
11872	D4006	Review & Approve Mech Plan & Elev Dwg Set (HP) (Sector G) [01-03-01]	5.0d	21-Jul-26	27-Jul-26	43.0d
11873	D4016	Review & Approve Mech Plan & Elev Dwg Set (HNTB) (Sector G) [01-03-01]	10.0d	28-Jul-26	10-Aug-26	43.0d
11874	D1204	Review & Approve Mech Plan & Elev Dwg Set (HCAA) (Sector G) [01-03-01]	15.0d	11-Aug-26	31-Aug-26	43.0d
11875	D1206	Prep & Submit Header Steel Dwg Set (Sector G) [01-03-01]	30.0d	1-Sep-26	13-Oct-26	43.0d
11876	D4026	Review & Approve Header Steel Dwg Set (HP) (Sector G) [01-03-01]	10.0d	14-Oct-26	27-Oct-26	43.0d
11877	D4036	Review & Approve Header Steel Dwg Set (HNTB) (Sector G) [01-03-01]	10.0d	28-Oct-26	10-Nov-26	43.0d
11878	D1211	Review & Approve Header Steel Dwg Set (HCAA) (Sector G) [01-03-01]	15.0d	11-Nov-26	3-Dec-26	43.0d
11879	WBS - BHS Mechanical Fabrication (Sector G) [01-03-01]		164.0d	1-Sep-26	23-Apr-27	43.0d
11880	D1205	Fab. & Deliver Conveyor Batch 1 (15) (Sector G) [01-03-01]	119.0d	1-Sep-26	19-Feb-27	68.0d
11881	D1207	Fab. & Deliver Conveyor Batch 2 (15) (Sector G) [01-03-01]	119.0d	9-Sep-26	26-Feb-27	68.0d
11882	D1208	Fab. & Deliver Conveyor Batch 3 (15) (Sector G) [01-03-01]	119.0d	16-Sep-26	5-Mar-27	68.0d
11883	D1209	Fab. & Deliver Conveyor Batch 4 (15) (Sector G) [01-03-01]	119.0d	23-Sep-26	12-Mar-27	68.0d
11884	D1210	Fab. & Deliver Conveyor Batch 5 (5) (Sector G) [01-03-01]	119.0d	30-Sep-26	19-Mar-27	68.0d
11885	D1212	Fab. & Deliver Header Steel / Platform / Sills (Sector G) [01-03-01]	79.0d	4-Dec-26	26-Mar-27	43.0d
11886	D1213	Prep Mech. Matl for Install (Sector G) [01-03-01]	20.0d	29-Mar-27	23-Apr-27	43.0d

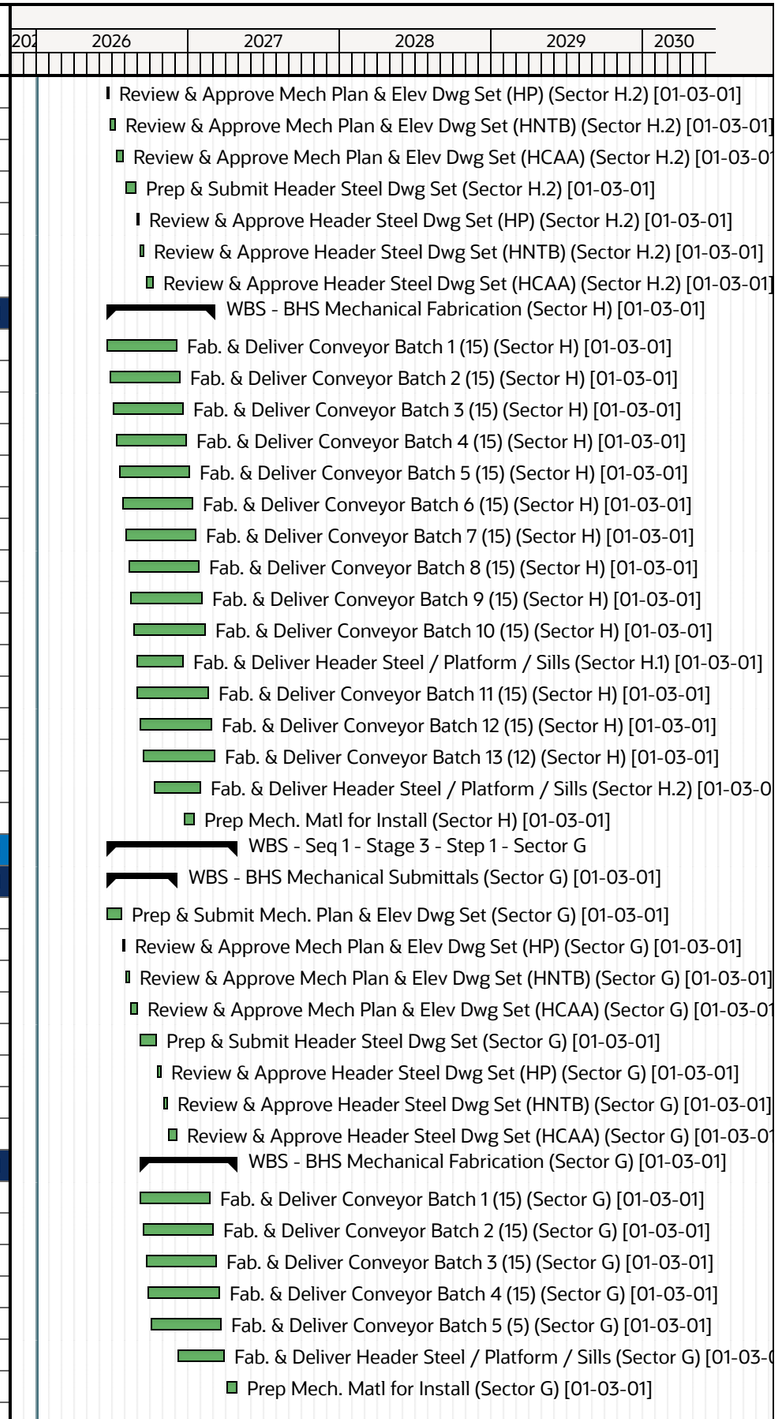


ID	Name	Dur	Start	Finish	TF
11887	WBS - Seq 1 - Stage 3 - Step 1 - TD1 & TD2 paths to ASD	204.0d	21-Jul-26	7-May-27	169.0d
11888	WBS - BHS Mechanical Submittals (TD1 & TD2 paths to ASD) [01-03-01]	100.0d	21-Jul-26	10-Dec-26	174.0d
11889	D1214 Prep & Submit Mech. Plan & Elev Dwg Set (TD1 & TD2 to ASD) [01-03-01]	20.0d	21-Jul-26	17-Aug-26	78.0d
11890	D4086 Review & Approve Mech Plan & Elev Dwg Set (HP) (TD1 & TD2 to ASD) [01-03-...	5.0d	18-Aug-26	24-Aug-26	169.0d
11891	D4096 Review & Approve Mech Plan & Elev Dwg Set (HNTB) (TD1 & TD2 to ASD) [01-...	10.0d	25-Aug-26	8-Sep-26	169.0d
11892	D1215 Review & Approve Mech Plan & Elev Dwg Set (HCAA) (TD1 & TD2 to ASD) [01-...	15.0d	9-Sep-26	29-Sep-26	169.0d
11893	D1217 Prep & Submit Header Steel Dwg Set (TD1 & TD2 to ASD) [01-03-01]	20.0d	30-Sep-26	27-Oct-26	174.0d
11894	D4106 Review & Approve Header Steel Dwg Set (HP) (TD1 & TD2 to ASD) [01-03-01]	5.0d	28-Oct-26	3-Nov-26	174.0d
11895	D4116 Review & Approve Header Steel Dwg Set (HNTB) (TD1 & TD2 to ASD) [01-03-01]	10.0d	4-Nov-26	17-Nov-26	174.0d
11896	D1221 Review & Approve Header Steel Dwg Set (HCAA) (TD1 & TD2 to ASD) [01-03-01]	15.0d	18-Nov-26	10-Dec-26	174.0d
11897	WBS - BHS Mechanical Fabrication (TD1 & TD2 paths to ASD) [01-03-01]	154.0d	30-Sep-26	7-May-27	169.0d
11898	D1216 Fab. & Deliver Conveyor Batch 1 (15) (TD1 & TD2 to ASD) [01-03-01]	119.0d	30-Sep-26	19-Mar-27	169.0d
11899	D1218 Fab. & Deliver Conveyor Batch 2 (15) (TD1 & TD2 to ASD) [01-03-01]	119.0d	7-Oct-26	26-Mar-27	169.0d
11900	D1219 Fab. & Deliver Conveyor Batch 3 (15) (TD1 & TD2 to ASD) [01-03-01]	119.0d	14-Oct-26	2-Apr-27	169.0d
11901	D1220 Fab. & Deliver Conveyor Batch 4 (11) (TD1 & TD2 to ASD) [01-03-01]	119.0d	21-Oct-26	9-Apr-27	169.0d
11902	D1222 Fab. & Deliver Header Steel / Platform / Sills (TD1 & TD2 to ASD) [01-03-01]	79.0d	11-Dec-26	2-Apr-27	174.0d
11903	D1223 Prep Mech. Matl for Install (TD1 & TD2 to ASD) [01-03-01]	20.0d	12-Apr-27	7-May-27	169.0d
11904	WBS - Seq 1 - Stage 3 - Step 1 - Cross-Belt Sorter (XBM1)	269.0d	17-Apr-26	7-May-27	20.0d
11905	WBS - BHS Mechanical Submittals (Cross-Belt Sorter (XBM1) [01-03-01]	170.0d	17-Apr-26	17-Dec-26	20.0d
11906	D1224 Prep & Submit Mech. Plan & Elev Dwg Set (XBM1) [01-03-01]	80.0d	17-Apr-26	10-Aug-26	7.0d
11907	D4046 Review & Approve Mech Plan & Elev Dwg Set (HP) (XBM1) [01-03-01]	5.0d	11-Aug-26	17-Aug-26	20.0d
11908	D4056 Review & Approve Mech Plan & Elev Dwg Set (HNTB) (XBM1) [01-03-01]	10.0d	18-Aug-26	31-Aug-26	20.0d
11909	D1225 Review & Approve Mech Plan & Elev Dwg Set (HCAA) (XBM1) [01-03-01]	15.0d	1-Sep-26	22-Sep-26	20.0d
11910	D1227 Prep & Submit Header Steel Dwg Set (XBM1) [01-03-01]	30.0d	23-Sep-26	3-Nov-26	20.0d
11911	D4066 Review & Approve Header Steel Dwg Set (HP) (XBM1) [01-03-01]	5.0d	4-Nov-26	10-Nov-26	20.0d
11912	D4076 Review & Approve Header Steel Dwg Set (HNTB) (XBM1) [01-03-01]	10.0d	11-Nov-26	24-Nov-26	20.0d
11913	D1228 Review & Approve Header Steel Dwg Set (HCAA) (XBM1) [01-03-01]	15.0d	25-Nov-26	17-Dec-26	20.0d
11914	WBS - BHS Mechanical Fabrication (Cross-Belt Sorter (XBM1) [01-03-01]	159.0d	23-Sep-26	7-May-27	20.0d
11915	D1226 Fab. & Deliver Conveyor (XBM1) [01-03-01]	119.0d	23-Sep-26	12-Mar-27	40.0d
11916	D1229 Fab. & Deliver Header Steel / Platform / Sills (XBM1) [01-03-01]	79.0d	18-Dec-26	9-Apr-27	20.0d
11917	D1230 Prep Mech. Matl for Install (XBM1) [01-03-01]	20.0d	12-Apr-27	7-May-27	20.0d
11918	WBS - Seq 1 - Stage 3 - Step 2	327.0d	3-Feb-26	14-May-27	78.0d
11919	WBS - BHS Mechanical Submittals [01-03-02]	90.0d	18-Aug-26	24-Dec-26	78.0d
11920	D1232 Prep & Submit Mech. Plan & Elev Dwg Set [01-03-02]	20.0d	18-Aug-26	15-Sep-26	78.0d
11921	D4126 Review & Approve Mech Plan & Elev Dwg Set (HP) [01-03-02]	5.0d	16-Sep-26	22-Sep-26	78.0d
11922	D4136 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-03-02]	10.0d	23-Sep-26	6-Oct-26	78.0d
11923	D1233 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-03-02]	15.0d	7-Oct-26	27-Oct-26	78.0d
11924	D1235 Prep & Submit Header Steel Dwg Set [01-03-02]	10.0d	28-Oct-26	10-Nov-26	78.0d
11925	D4146 Review & Approve Header Steel Dwg Set (HP) [01-03-02]	5.0d	11-Nov-26	17-Nov-26	78.0d
11926	D4156 Review & Approve Header Steel Dwg Set (HNTB) [01-03-02]	10.0d	18-Nov-26	3-Dec-26	78.0d
11927	D1236 Review & Approve Header Steel Dwg Set (HCAA) [01-03-02]	15.0d	4-Dec-26	24-Dec-26	78.0d
11928	WBS - BHS Mechanical Fabrication [01-03-02]	327.0d	3-Feb-26	14-May-27	78.0d

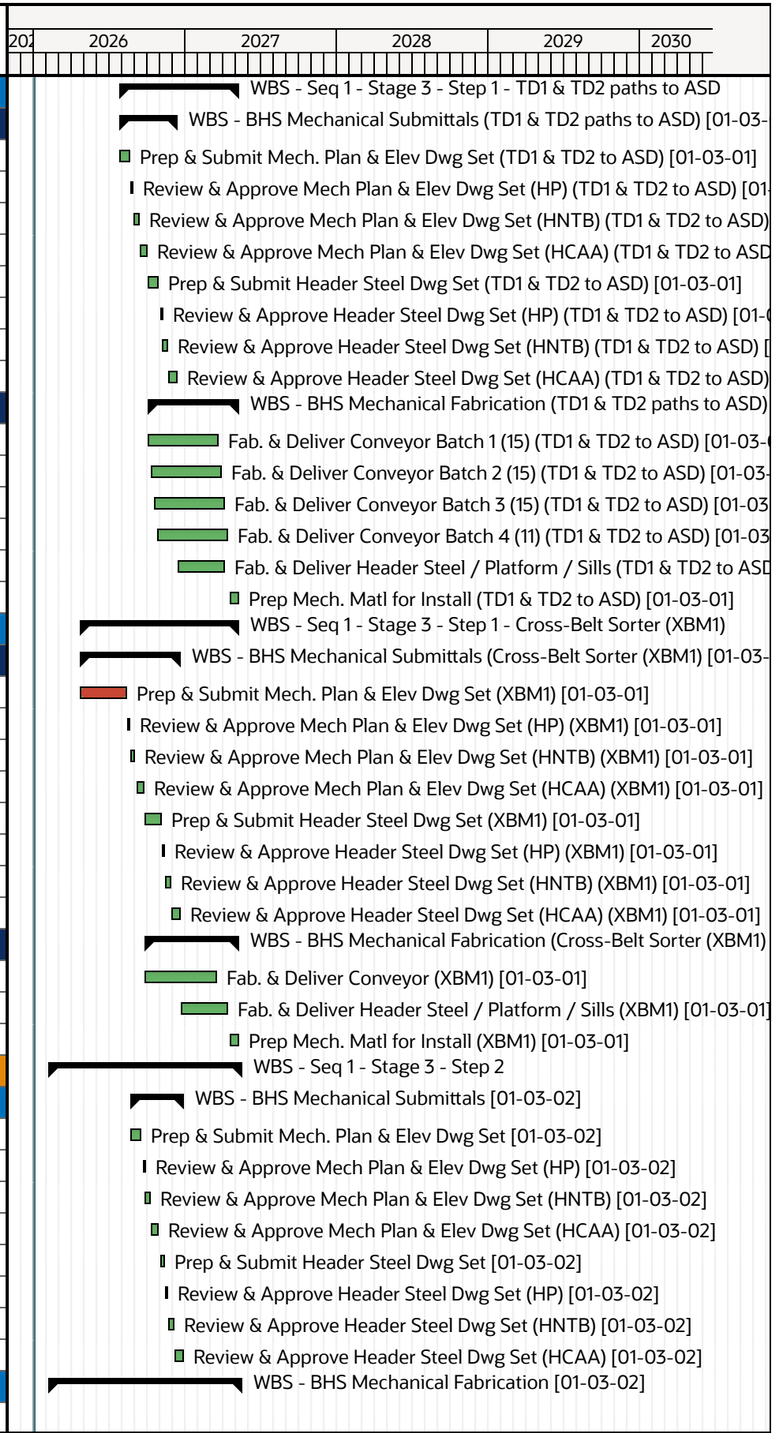


	ID	Name	Dur	Start	Finish	TF
11929	D1231	Fab. & Deliver T BX2 1/DV HSD [01-03-02]	140.0d	3-Feb-26	19-Aug-26	245.0d
11930	D1234	Fab. & Deliver Conveyor (5) [01-03-02]	119.0d	28-Oct-26	16-Apr-27	78.0d
11931	D1237	Fab. & Deliver Header Steel / Platform / Sills [01-03-02]	79.0d	28-Dec-26	16-Apr-27	78.0d
11932	D1238	Prep Mech. Matl for Install [01-03-02]	20.0d	19-Apr-27	14-May-27	78.0d
11933	WBS - Seq 1 - Stage 3 - Step 3		194.0d	18-Aug-26	21-May-27	410.0d
11934	WBS - BHS Mechanical Submittals [01-03-03]		95.0d	18-Aug-26	4-Jan-27	410.0d
11935	D1239	Prep & Submit Mech. Plan & Elev Dwg Set [01-03-03]	20.0d	18-Aug-26	15-Sep-26	201.0d
11936	D4166	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-03-03]	5.0d	16-Sep-26	22-Sep-26	410.0d
11937	D4176	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-03-03]	10.0d	23-Sep-26	6-Oct-26	410.0d
11938	D1240	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-03-03]	15.0d	7-Oct-26	27-Oct-26	410.0d
11939	D1241	Prep & Submit Header Steel Dwg Set [01-03-03]	15.0d	28-Oct-26	17-Nov-26	410.0d
11940	D4186	Review & Approve Header Steel Dwg Set (HP) [01-03-03]	5.0d	18-Nov-26	24-Nov-26	410.0d
11941	D4196	Review & Approve Header Steel Dwg Set (HNTB) [01-03-03]	10.0d	25-Nov-26	10-Dec-26	410.0d
11942	D1243	Review & Approve Header Steel Dwg Set (HCAA) [01-03-03]	15.0d	11-Dec-26	4-Jan-27	410.0d
11943	WBS - BHS Mechanical Fabrication [01-03-03]		144.0d	28-Oct-26	21-May-27	410.0d
11944	D1242	Fab. & Deliver Conveyor (3) [01-03-03]	119.0d	28-Oct-26	16-Apr-27	415.0d
11945	D1244	Fab. & Deliver Header Steel / Platform / Sills [01-03-03]	79.0d	5-Jan-27	23-Apr-27	410.0d
11946	D1245	Prep Mech. Matl for Install [01-03-03]	20.0d	26-Apr-27	21-May-27	410.0d
11947	WBS - Seq 1 - Stage 3 - Step 4		332.0d	3-Feb-26	21-May-27	128.0d
11948	WBS - BHS Mechanical Submittals [01-03-04]		95.0d	18-Aug-26	4-Jan-27	128.0d
11949	D1247	Prep & Submit Mech. Plan & Elev Dwg Set [01-03-04]	20.0d	18-Aug-26	15-Sep-26	128.0d
11950	D4206	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-03-04]	5.0d	16-Sep-26	22-Sep-26	128.0d
11951	D4216	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-03-04]	10.0d	23-Sep-26	6-Oct-26	128.0d
11952	D1248	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-03-04]	15.0d	7-Oct-26	27-Oct-26	128.0d
11953	D1249	Prep & Submit Header Steel Dwg Set [01-03-04]	15.0d	28-Oct-26	17-Nov-26	128.0d
11954	D4226	Review & Approve Header Steel Dwg Set (HP) [01-03-04]	5.0d	18-Nov-26	24-Nov-26	128.0d
11955	D4236	Review & Approve Header Steel Dwg Set (HNTB) [01-03-04]	10.0d	25-Nov-26	10-Dec-26	128.0d
11956	D1251	Review & Approve Header Steel Dwg Set (HCAA) [01-03-04]	15.0d	11-Dec-26	4-Jan-27	128.0d
11957	WBS - BHS Mechanical Fabrication [01-03-04]		332.0d	3-Feb-26	21-May-27	128.0d
11958	D1246	Fab. & Deliver T AS3 6 HSD [01-03-04]	140.0d	3-Feb-26	19-Aug-26	300.0d
11959	D1250	Fab. & Deliver Conveyor (5) [01-03-04]	119.0d	28-Oct-26	16-Apr-27	133.0d
11960	D1252	Fab. & Deliver Header Steel / Platform / Sills [01-03-04]	79.0d	5-Jan-27	23-Apr-27	128.0d
11961	D1253	Prep Mech. Matl for Install [01-03-04]	20.0d	26-Apr-27	21-May-27	128.0d
11962	WBS - Seq 1 - Stage 3 - Step 5		342.0d	3-Feb-26	7-Jun-27	146.0d
11963	WBS - BHS Mechanical Submittals [01-03-05]		85.0d	18-Aug-26	17-Dec-26	166.0d
11964	D1256	Prep & Submit Mech. Plan & Elev Dwg Set [01-03-05]	20.0d	18-Aug-26	15-Sep-26	138.0d
11965	D4246	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-03-05]	5.0d	16-Sep-26	22-Sep-26	146.0d
11966	D4256	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-03-05]	10.0d	23-Sep-26	6-Oct-26	146.0d
11967	D1257	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-03-05]	15.0d	7-Oct-26	27-Oct-26	146.0d
11968	D1258	Prep & Submit Header Steel Dwg Set [01-03-05]	5.0d	28-Oct-26	3-Nov-26	166.0d
11969	D4266	Review & Approve Header Steel Dwg Set (HP) [01-03-05]	5.0d	4-Nov-26	10-Nov-26	166.0d
11970	D4276	Review & Approve Header Steel Dwg Set (HNTB) [01-03-05]	10.0d	11-Nov-26	24-Nov-26	166.0d

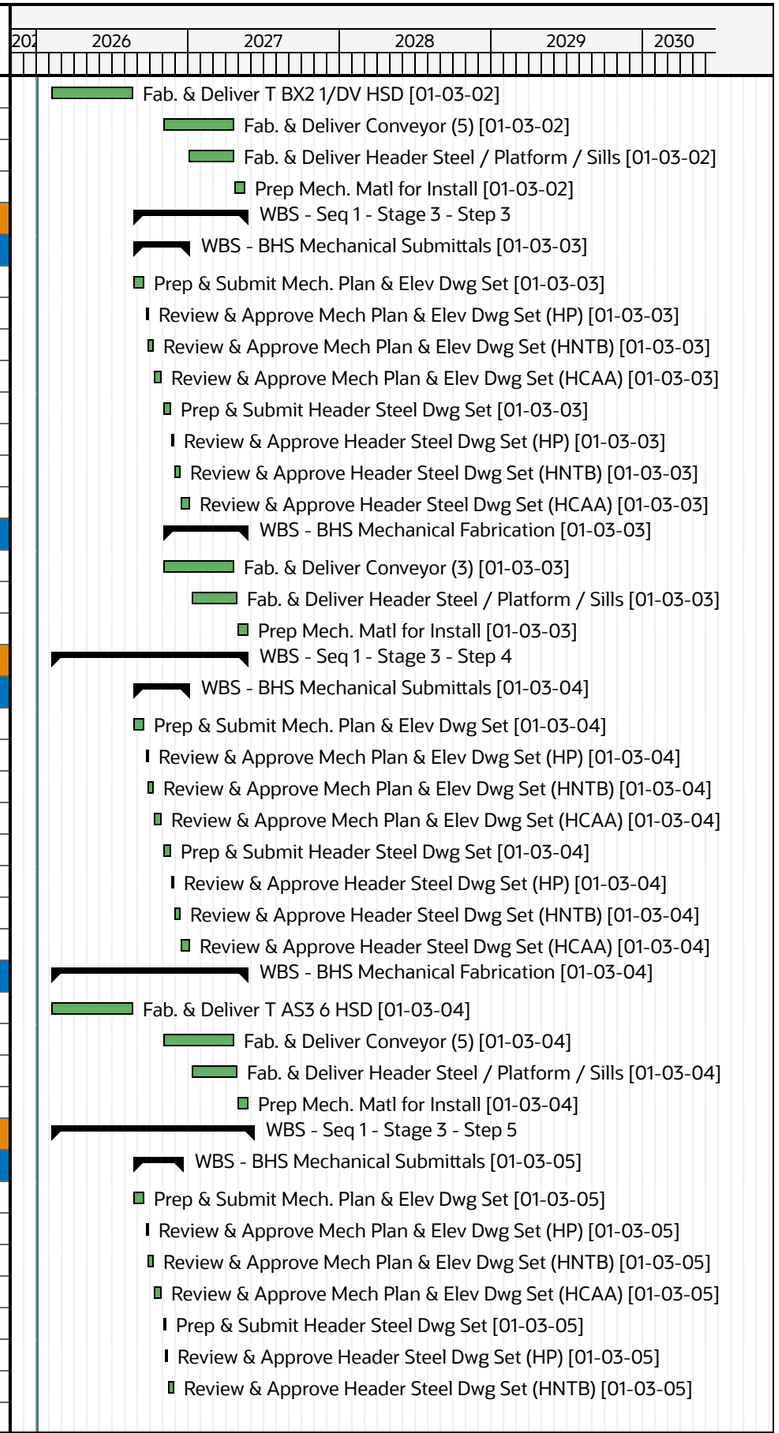


	ID	Name	Dur	Start	Finish	TF
11971	D1260	Review & Approve Header Steel Dwg Set (HCAA) [01-03-05]	15.0d	25-Nov-26	17-Dec-26	166.0d
11972	WBS - BHS Mechanical Fabrication [01-03-05]		342.0d	3-Feb-26	7-Jun-27	146.0d
11973	D1254	Fab. & Deliver TXM2A 1 HSDs [01-03-05]	140.0d	3-Feb-26	19-Aug-26	328.0d
11974	D1255	Fab. & Deliver T AS3 3 DV HSD [01-03-05]	140.0d	3-Feb-26	19-Aug-26	328.0d
11975	D1259	Fab. & Deliver Conveyors Batch 1 (15) [01-03-05]	119.0d	28-Oct-26	16-Apr-27	146.0d
11976	D1261	Fab. & Deliver Conveyors Batch 2 (15) [01-03-05]	119.0d	4-Nov-26	23-Apr-27	146.0d
11977	D1262	Fab. & Deliver Conveyors Batch 3 (15) [01-03-05]	119.0d	11-Nov-26	30-Apr-27	146.0d
11978	D1263	Fab. & Deliver Conveyors Batch 4 (13) [01-03-05]	119.0d	18-Nov-26	7-May-27	146.0d
11979	D1264	Fab. & Deliver Header Steel / Platform / Sills [01-03-05]	79.0d	18-Dec-26	9-Apr-27	166.0d
11980	D1265	Prep Mech. Matl for Install [01-03-05]	20.0d	10-May-27	7-Jun-27	146.0d
11981	WBS - Seq 1 - Stage 3 - Step 6		352.0d	3-Feb-26	21-Jun-27	138.0d
11982	WBS - BHS Mechanical Submittals [01-03-06]		104.0d	16-Sep-26	12-Feb-27	148.0d
11983	D1267	Prep & Submit Mech. Plan & Elev Dwg Set [01-03-06]	20.0d	16-Sep-26	13-Oct-26	138.0d
11984	D4286	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-03-06]	5.0d	14-Oct-26	20-Oct-26	138.0d
11985	D4296	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [01-03-06]	10.0d	21-Oct-26	3-Nov-26	138.0d
11986	D1268	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [01-03-06]	15.0d	4-Nov-26	24-Nov-26	138.0d
11987	D1270	Prep & Submit Header Steel Dwg Set [01-03-06]	19.0d	25-Nov-26	23-Dec-26	148.0d
11988	D4306	Review & Approve Header Steel Dwg Set (HP) [01-03-06]	10.0d	24-Dec-26	8-Jan-27	148.0d
11989	D4316	Review & Approve Header Steel Dwg Set (HNTB) [01-03-06]	10.0d	11-Jan-27	22-Jan-27	148.0d
11990	D1272	Review & Approve Header Steel Dwg Set (HCAA) [01-03-06]	15.0d	25-Jan-27	12-Feb-27	148.0d
11991	WBS - BHS Mechanical Fabrication [01-03-06]		352.0d	3-Feb-26	21-Jun-27	138.0d
11992	D1266	Fab. & Deliver T11A 1 HSD [01-03-06]	140.0d	3-Feb-26	19-Aug-26	330.0d
11993	D1269	Fab. & Deliver Conveyors Batch 1 (15) [01-03-06]	119.0d	25-Nov-26	14-May-27	138.0d
11994	D1271	Fab. & Deliver Conveyors Batch 2 (8) [01-03-06]	119.0d	4-Dec-26	21-May-27	138.0d
11995	D1273	Fab. & Deliver Header Steel / Platform / Sills [01-03-06]	80.0d	15-Feb-27	7-Jun-27	148.0d
11996	D1274	Prep Mech. Matl for Install [01-03-06]	20.0d	24-May-27	21-Jun-27	138.0d
11997	WBS - Seq 2 - Stage 1 - Step 1A		200.0d	14-Oct-26	28-Jul-27	193.0d
11998	WBS - BHS Mechanical Submittals [02-01-01A]		100.0d	14-Oct-26	8-Mar-27	193.0d
11999	D1275	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-01A]	20.0d	14-Oct-26	10-Nov-26	193.0d
12000	D4326	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-01A]	5.0d	11-Nov-26	17-Nov-26	193.0d
12001	D4336	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-01A]	10.0d	18-Nov-26	3-Dec-26	193.0d
12002	D1276	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-01A]	15.0d	4-Dec-26	24-Dec-26	193.0d
12003	D1277	Prep & Submit Header Steel Dwg Set [02-01-01A]	20.0d	28-Dec-26	25-Jan-27	193.0d
12004	D4346	Review & Approve Header Steel Dwg Set (HP) [02-01-01A]	5.0d	26-Jan-27	1-Feb-27	193.0d
12005	D4356	Review & Approve Header Steel Dwg Set (HNTB) [02-01-01A]	10.0d	2-Feb-27	15-Feb-27	193.0d
12006	D1279	Review & Approve Header Steel Dwg Set (HCAA) [02-01-01A]	15.0d	16-Feb-27	8-Mar-27	193.0d
12007	WBS - BHS Mechanical Fabrication [02-01-01A]		150.0d	28-Dec-26	28-Jul-27	193.0d
12008	D1278	Fab. & Deliver Conveyors (4) [02-01-01A]	120.0d	28-Dec-26	15-Jun-27	203.0d
12009	D1280	Fab. & Deliver Header Steel / Platform / Sills [02-01-01A]	80.0d	9-Mar-27	29-Jun-27	193.0d
12010	D1281	Prep Mech. Matl for Install [02-01-01A]	20.0d	30-Jun-27	28-Jul-27	193.0d
12011	WBS - Seq 2 - Stage 1 - Step 1B		200.0d	14-Oct-26	28-Jul-27	201.0d
12012	WBS - BHS Mechanical Submittals [02-01-01B]		100.0d	14-Oct-26	8-Mar-27	201.0d

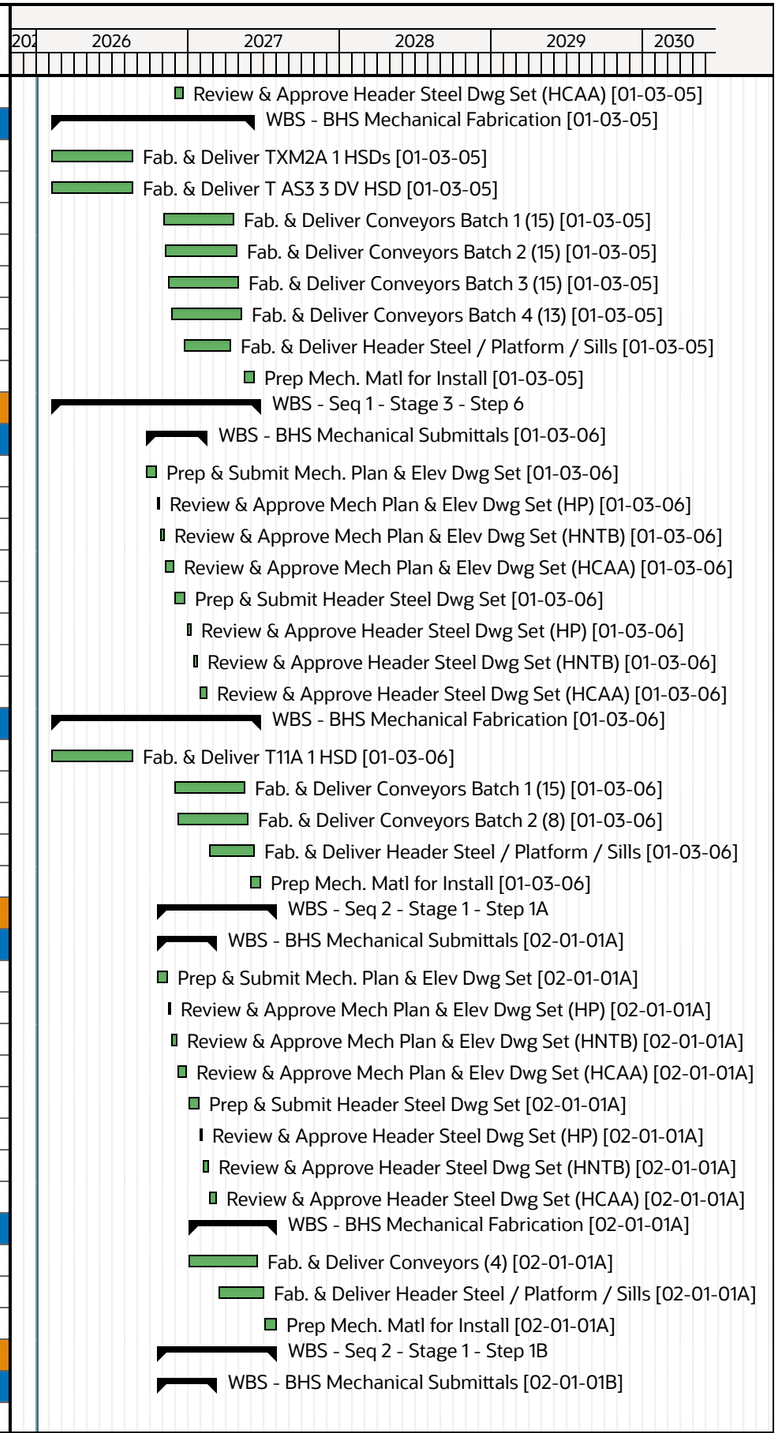


	ID	Name	Dur	Start	Finish	TF
12013	D1282	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-01B]	20.0d	14-Oct-26	10-Nov-26	197.0d
12014	D4366	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-01B]	5.0d	11-Nov-26	17-Nov-26	201.0d
12015	D4376	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-01B]	10.0d	18-Nov-26	3-Dec-26	201.0d
12016	D1283	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-01B]	15.0d	4-Dec-26	24-Dec-26	201.0d
12017	D1284	Prep & Submit Header Steel Dwg Set [02-01-01B]	20.0d	28-Dec-26	25-Jan-27	201.0d
12018	D4386	Review & Approve Header Steel Dwg Set (HP) [02-01-01B]	5.0d	26-Jan-27	1-Feb-27	201.0d
12019	D4396	Review & Approve Header Steel Dwg Set (HNTB) [02-01-01B]	10.0d	2-Feb-27	15-Feb-27	201.0d
12020	D1286	Review & Approve Header Steel Dwg Set (HCAA) [02-01-01B]	15.0d	16-Feb-27	8-Mar-27	201.0d
12021	WBS - BHS Mechanical Fabrication [02-01-01B]		150.0d	28-Dec-26	28-Jul-27	201.0d
12022	D1285	Fab. & Deliver Conveyors (1) [02-01-01B]	120.0d	28-Dec-26	15-Jun-27	211.0d
12023	D1287	Fab. & Deliver Header Steel / Platform / Sills [02-01-01B]	80.0d	9-Mar-27	29-Jun-27	201.0d
12024	D1288	Prep Mech. Matl for Install [02-01-01B]	20.0d	30-Jun-27	28-Jul-27	201.0d
12025	WBS - Seq 2 - Stage 1 - Step 1C		430.0d	3-Feb-26	11-Oct-27	150.0d
12026	WBS - BHS Mechanical Submittals [02-01-01C]		197.0d	11-Aug-26	19-May-27	150.0d
12027	D1290	Prep & Submit Mech Plan & Elev Dwg Set (XBM2) [02-01-01c]	80.0d	11-Aug-26	3-Dec-26	72.0d
12028	D1291	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-01C]	20.0d	14-Oct-26	10-Nov-26	197.0d
12029	D4406	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-01C]	5.0d	11-Nov-26	17-Nov-26	197.0d
12030	D4416	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-01C]	10.0d	18-Nov-26	3-Dec-26	197.0d
12031	D1293	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-01C]	15.0d	4-Dec-26	24-Dec-26	197.0d
12032	D6186	Review & Approve Mech Plan & Elev Dwg Set (HP) (XBM2) [02-01-01c]	14.0d	4-Dec-26	23-Dec-26	72.0d
12033	D6196	Review & Approve Mech Plan & Elev Dwg Set (HNTB) (XBM2) [02-01-01c]	14.0d	24-Dec-26	14-Jan-27	72.0d
12034	D1295	Prep & Submit Header Steel Dwg Set [02-01-01C]	20.0d	28-Dec-26	25-Jan-27	202.0d
12035	D1292	Review & Approve Mech Plan & Elev Dwg Set (HCAA) (XBM2) [02-01-01c]	14.0d	15-Jan-27	3-Feb-27	72.0d
12036	D4426	Review & Approve Header Steel Dwg Set (HP) [02-01-01C]	5.0d	26-Jan-27	1-Feb-27	202.0d
12037	D4436	Review & Approve Header Steel Dwg Set (HNTB) [02-01-01C]	10.0d	2-Feb-27	15-Feb-27	202.0d
12038	D1296	Prep & Submit Header Steel Dwg Set (XBM2) [02-01-01c]	30.0d	4-Feb-27	17-Mar-27	72.0d
12039	D1301	Review & Approve Header Steel Dwg Set (HCAA) [02-01-01C]	15.0d	16-Feb-27	8-Mar-27	202.0d
12040	D6206	Review & Approve Header Steel Dwg Set (HP) (XBM2) [02-01-01c]	15.0d	18-Mar-27	7-Apr-27	72.0d
12041	D6216	Review & Approve Header Steel Dwg Set (HNTB) (XBM2) [02-01-01c]	15.0d	8-Apr-27	28-Apr-27	72.0d
12042	D1302	Review & Approve Header Steel Dwg Set (HCAA) (XBM2) [02-01-01c]	15.0d	29-Apr-27	19-May-27	72.0d
12043	WBS - BHS Mechanical Fabrication [02-01-01C]		430.0d	3-Feb-26	11-Oct-27	150.0d
12044	D1289	Fab. & Deliver C8A 1 HSD [02-01-01C]	140.0d	3-Feb-26	19-Aug-26	420.0d
12045	D1297	Fab. & Deliver Conveyors Batch 1 (15) [02-01-01C]	120.0d	28-Dec-26	15-Jun-27	197.0d
12046	D1298	Fab. & Deliver Conveyors Batch 2 (15) [02-01-01C]	120.0d	5-Jan-27	22-Jun-27	197.0d
12047	D1299	Fab. & Deliver Conveyors Batch 3 (15) [02-01-01C]	120.0d	12-Jan-27	29-Jun-27	197.0d
12048	D1300	Fab. & Deliver Conveyors Batch 4 (11) [02-01-01C]	120.0d	19-Jan-27	7-Jul-27	197.0d
12049	D1294	Fab. & Deliver Conveyor (XBM2) [02-01-01c]	120.0d	4-Feb-27	23-Jul-27	107.0d
12050	D1303	Fab. & Deliver Header Steel / Platform / Sills [02-01-01C]	80.0d	9-Mar-27	29-Jun-27	202.0d
12051	D1304	Fab. & Deliver Header Steel / Platform / Sills (XBM2) [02-01-01c]	80.0d	20-May-27	13-Sep-27	72.0d
12052	D1306	Prep Mech. Matl for Install [02-01-01C]	20.0d	8-Jul-27	4-Aug-27	197.0d
12053	D1305	Prep Mech. Matl for Install (XBM2) [02-01-01c]	20.0d	14-Sep-27	11-Oct-27	72.0d
12054	WBS - Seq 2 - Stage 1 - Step 2A		199.0d	11-Nov-26	24-Aug-27	230.0d

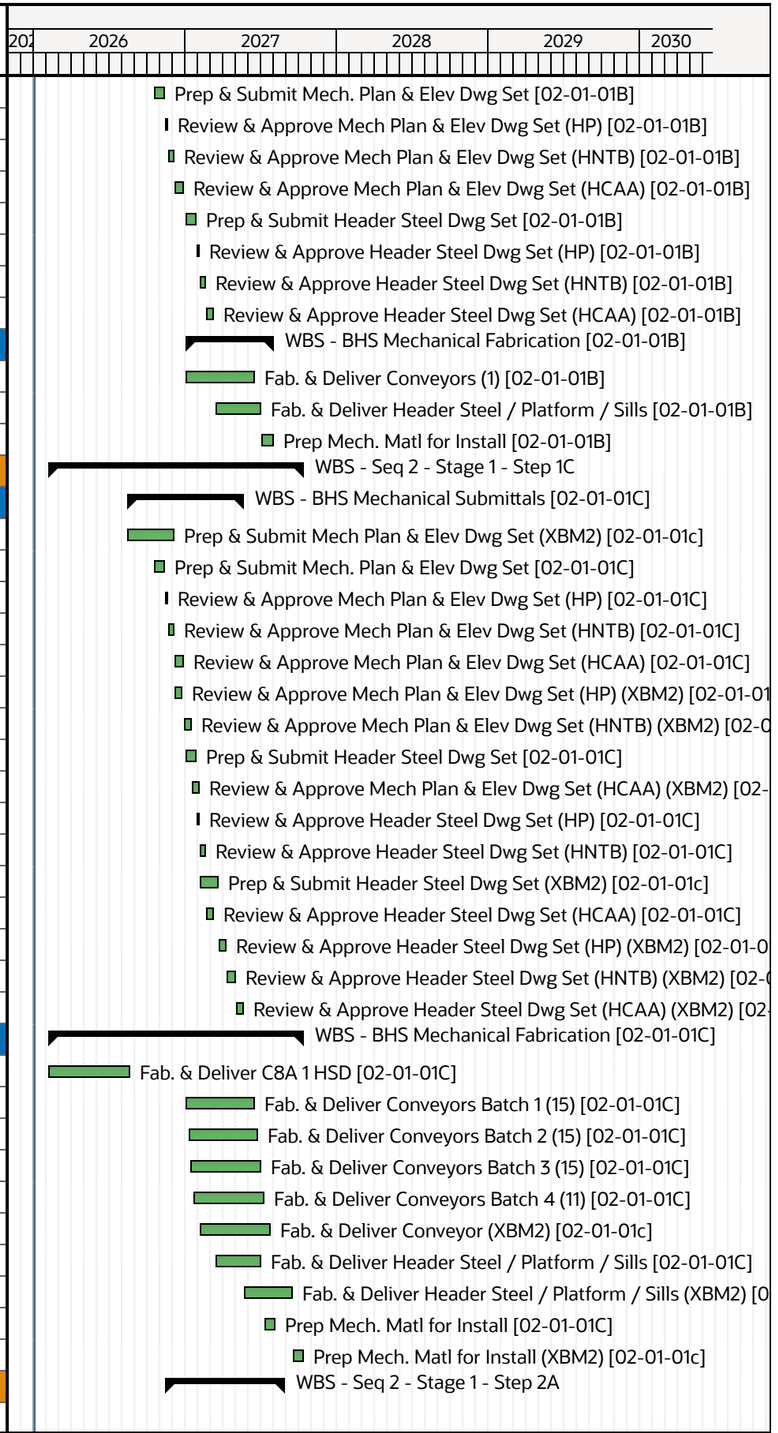


	ID	Name	Dur	Start	Finish	TF
12055	WBS - BHS Mechanical Submittals [02-01-01A]		99.0d	11-Nov-26	2-Apr-27	230.0d
12056	D1307	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-02A]	19.0d	11-Nov-26	9-Dec-26	230.0d
12057	D4446	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-02A]	5.0d	10-Dec-26	16-Dec-26	230.0d
12058	D4456	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-02A]	10.0d	17-Dec-26	31-Dec-26	230.0d
12059	D1308	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-02A]	15.0d	4-Jan-27	22-Jan-27	230.0d
12060	D1309	Prep & Submit Header Steel Dwg Set [02-01-02A]	20.0d	25-Jan-27	19-Feb-27	230.0d
12061	D4466	Review & Approve Header Steel Dwg Set (HP) [02-01-02A]	5.0d	22-Feb-27	26-Feb-27	230.0d
12062	D4476	Review & Approve Header Steel Dwg Set (HNTB) [02-01-02A]	10.0d	1-Mar-27	12-Mar-27	230.0d
12063	D1311	Review & Approve Header Steel Dwg Set (HCAA) [02-01-02A]	15.0d	15-Mar-27	2-Apr-27	230.0d
12064	WBS - BHS Mechanical Fabrication [02-01-01A]		150.0d	25-Jan-27	24-Aug-27	230.0d
12065	D1310	Fab. & Deliver Conveyors (2) [02-01-02A]	120.0d	25-Jan-27	13-Jul-27	240.0d
12066	D1312	Fab. & Deliver Header Steel / Platform / Sills [02-01-02A]	80.0d	5-Apr-27	27-Jul-27	230.0d
12067	D1313	Prep Mech. Matl for Install [02-01-02A]	20.0d	28-Jul-27	24-Aug-27	230.0d
12068	WBS - Seq 2 - Stage 1 - Step 2B		199.0d	11-Nov-26	24-Aug-27	233.0d
12069	WBS - BHS Mechanical Submittals [02-01-02B]		99.0d	11-Nov-26	2-Apr-27	233.0d
12070	D1314	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-02B]	19.0d	11-Nov-26	9-Dec-26	233.0d
12071	D4486	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-02B]	5.0d	10-Dec-26	16-Dec-26	233.0d
12072	D4496	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-02B]	10.0d	17-Dec-26	31-Dec-26	233.0d
12073	D1315	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-02B]	15.0d	4-Jan-27	22-Jan-27	233.0d
12074	D1316	Prep & Submit Header Steel Dwg Set [02-01-02B]	20.0d	25-Jan-27	19-Feb-27	233.0d
12075	D4506	Review & Approve Header Steel Dwg Set (HP) [02-01-02B]	5.0d	22-Feb-27	26-Feb-27	233.0d
12076	D4516	Review & Approve Header Steel Dwg Set (HNTB) [02-01-02B]	10.0d	1-Mar-27	12-Mar-27	233.0d
12077	D1318	Review & Approve Header Steel Dwg Set (HCAA) [02-01-02B]	15.0d	15-Mar-27	2-Apr-27	233.0d
12078	WBS - BHS Mechanical Fabrication [02-01-02B]		150.0d	25-Jan-27	24-Aug-27	233.0d
12079	D1317	Fab. & Deliver Conveyors (1) [02-01-02B]	120.0d	25-Jan-27	13-Jul-27	243.0d
12080	D1319	Fab. & Deliver Header Steel / Platform / Sills [02-01-02B]	80.0d	5-Apr-27	27-Jul-27	233.0d
12081	D1320	Prep Mech. Matl for Install [02-01-02B]	20.0d	28-Jul-27	24-Aug-27	233.0d
12082	WBS - Seq 2 - Stage 1 - Step 2C		199.0d	11-Nov-26	24-Aug-27	236.0d
12083	WBS - BHS Mechanical Submittals [02-01-02C]		99.0d	11-Nov-26	2-Apr-27	236.0d
12084	D1321	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-02C]	19.0d	11-Nov-26	9-Dec-26	236.0d
12085	D4526	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-02C]	5.0d	10-Dec-26	16-Dec-26	236.0d
12086	D4536	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-02C]	10.0d	17-Dec-26	31-Dec-26	236.0d
12087	D1322	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-02C]	15.0d	4-Jan-27	22-Jan-27	236.0d
12088	D1323	Prep & Submit Header Steel Dwg Set [02-01-02C]	20.0d	25-Jan-27	19-Feb-27	236.0d
12089	D4546	Review & Approve Header Steel Dwg Set (HP) [02-01-02C]	5.0d	22-Feb-27	26-Feb-27	236.0d
12090	D4556	Review & Approve Header Steel Dwg Set (HNTB) [02-01-02C]	10.0d	1-Mar-27	12-Mar-27	236.0d
12091	D1325	Review & Approve Header Steel Dwg Set (HCAA) [02-01-02C]	15.0d	15-Mar-27	2-Apr-27	236.0d
12092	WBS - BHS Mechanical Fabrication [02-01-02C]		150.0d	25-Jan-27	24-Aug-27	236.0d
12093	D1324	Fab. & Deliver Conveyor (3) [02-01-02C]	120.0d	25-Jan-27	13-Jul-27	246.0d
12094	D1326	Fab. & Deliver Header Steel / Platform / Sills [02-01-02C]	80.0d	5-Apr-27	27-Jul-27	236.0d
12095	D1327	Prep Mech. Matl for Install [02-01-02C]	20.0d	28-Jul-27	24-Aug-27	236.0d
12096	WBS - Seq 2 - Stage 1 - Step 2D		199.0d	11-Nov-26	24-Aug-27	239.0d

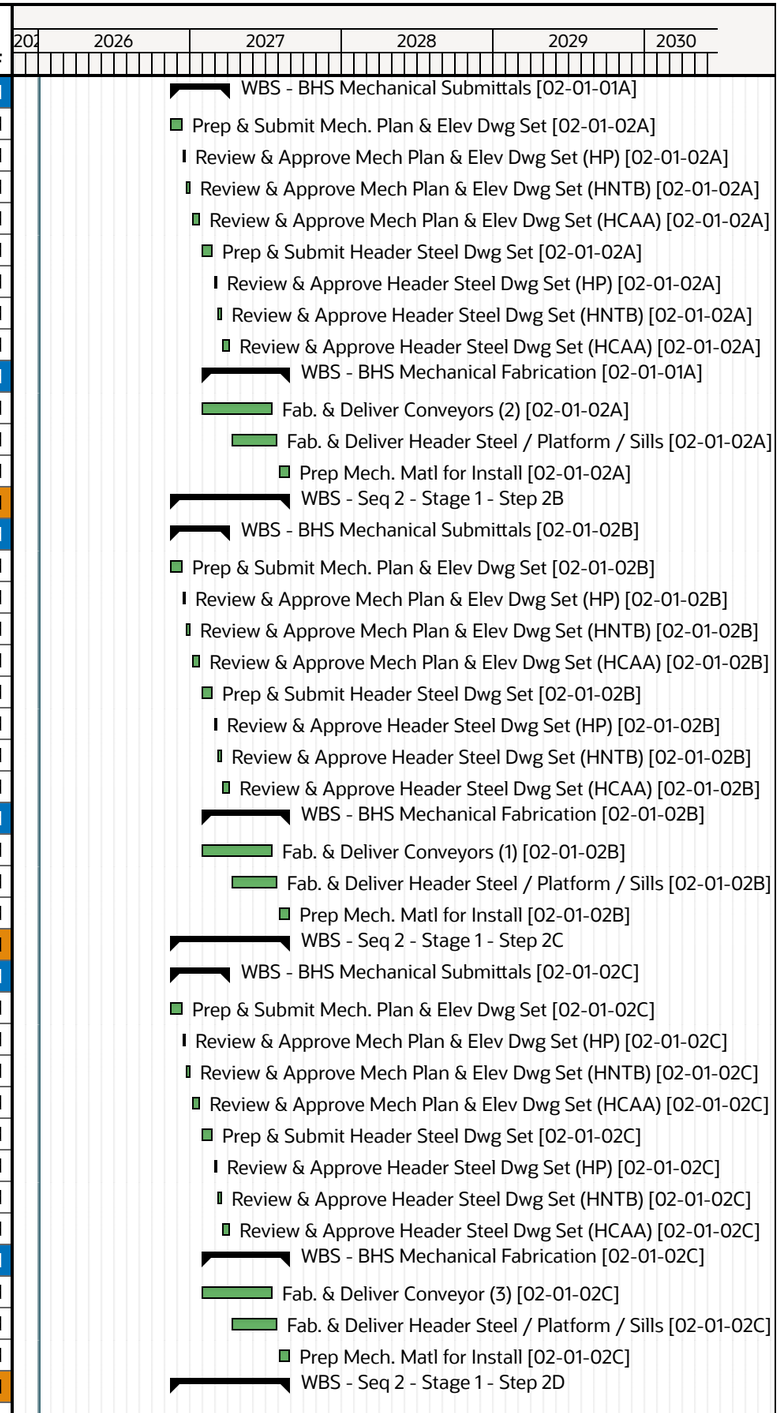


ID	Name	Dur	Start	Finish	TF
12097	WBS - BHS Mechanical Submittals [02-01-02D]	99.0d	11-Nov-26	2-Apr-27	239.0d
12098	D1328 Prep & Submit Mech. Plan & Elev Dwg Set [02-01-02D]	19.0d	11-Nov-26	9-Dec-26	239.0d
12099	D4566 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-02D]	5.0d	10-Dec-26	16-Dec-26	239.0d
12100	D4576 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-02D]	10.0d	17-Dec-26	31-Dec-26	239.0d
12101	D1329 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-02D]	15.0d	4-Jan-27	22-Jan-27	239.0d
12102	D1330 Prep & Submit Header Steel Dwg Set [02-01-02D]	20.0d	25-Jan-27	19-Feb-27	239.0d
12103	D4596 Review & Approve Header Steel Dwg Set (HP) [02-01-02D]	5.0d	22-Feb-27	26-Feb-27	239.0d
12104	D4606 Review & Approve Header Steel Dwg Set (HNTB) [02-01-02D]	10.0d	1-Mar-27	12-Mar-27	239.0d
12105	D1332 Review & Approve Header Steel Dwg Set (HCAA) [02-01-02D]	15.0d	15-Mar-27	2-Apr-27	239.0d
12106	WBS - BHS Mechanical Fabrication [02-01-02D]	150.0d	25-Jan-27	24-Aug-27	239.0d
12107	D1331 Fab. & Deliver Conveyors (5) [02-01-02D]	120.0d	25-Jan-27	13-Jul-27	249.0d
12108	D1333 Fab. & Deliver Header Steel / Platform / Sills [02-01-02D]	80.0d	5-Apr-27	27-Jul-27	239.0d
12109	D1334 Prep Mech. Matl for Install [02-01-02D]	20.0d	28-Jul-27	24-Aug-27	239.0d
12110	WBS - Seq 2 - Stage 1 - Step 3A	194.0d	11-Nov-26	17-Aug-27	256.0d
12111	WBS - BHS Mechanical Submittals [02-01-03A]	94.0d	11-Nov-26	26-Mar-27	256.0d
12112	D1335 Prep & Submit Mech. Plan & Elev Dwg Set [02-01-03A]	19.0d	11-Nov-26	9-Dec-26	244.0d
12113	D4616 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-03A]	5.0d	10-Dec-26	16-Dec-26	256.0d
12114	D4626 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-03A]	10.0d	17-Dec-26	31-Dec-26	256.0d
12115	D1336 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-03A]	15.0d	4-Jan-27	22-Jan-27	256.0d
12116	D1337 Prep & Submit Header Steel Dwg Set [02-01-03A]	15.0d	25-Jan-27	12-Feb-27	256.0d
12117	D4636 Review & Approve Header Steel Dwg Set (HP) [02-01-03A]	5.0d	15-Feb-27	19-Feb-27	256.0d
12118	D4646 Review & Approve Header Steel Dwg Set (HNTB) [02-01-03A]	10.0d	22-Feb-27	5-Mar-27	256.0d
12119	D1340 Review & Approve Header Steel Dwg Set (HCAA) [02-01-03A]	15.0d	8-Mar-27	26-Mar-27	256.0d
12120	WBS - BHS Mechanical Fabrication [02-01-03A]	145.0d	25-Jan-27	17-Aug-27	256.0d
12121	D1338 Fab. & Deliver Conveyors Batch 1 (15) [02-01-03A]	120.0d	25-Jan-27	13-Jul-27	256.0d
12122	D1339 Fab. & Deliver Conveyors Batch 2 (12) [02-01-03A]	120.0d	1-Feb-27	20-Jul-27	256.0d
12123	D1341 Fab. & Deliver Header Steel / Platform / Sills [02-01-03A]	80.0d	29-Mar-27	20-Jul-27	256.0d
12124	D1342 Prep Mech. Matl for Install [02-01-03A]	20.0d	21-Jul-27	17-Aug-27	256.0d
12125	WBS - Seq 2 - Stage 1 - Step 3B	209.0d	11-Nov-26	8-Sep-27	244.0d
12126	WBS - BHS Mechanical Submittals [02-01-03B]	99.0d	11-Nov-26	2-Apr-27	254.0d
12127	D1343 Prep & Submit Mech. Plan & Elev Dwg Set [02-01-03B]	19.0d	11-Nov-26	9-Dec-26	244.0d
12128	D4656 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-03B]	5.0d	10-Dec-26	16-Dec-26	244.0d
12129	D4666 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-03B]	10.0d	17-Dec-26	31-Dec-26	244.0d
12130	D1344 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-03B]	15.0d	4-Jan-27	22-Jan-27	244.0d
12131	D1345 Prep & Submit Header Steel Dwg Set [02-01-03B]	20.0d	25-Jan-27	19-Feb-27	254.0d
12132	D4676 Review & Approve Header Steel Dwg Set (HP) [02-01-03B]	5.0d	22-Feb-27	26-Feb-27	254.0d
12133	D4686 Review & Approve Header Steel Dwg Set (HNTB) [02-01-03B]	10.0d	1-Mar-27	12-Mar-27	254.0d
12134	D1347 Review & Approve Header Steel Dwg Set (HCAA) [02-01-03B]	15.0d	15-Mar-27	2-Apr-27	254.0d
12135	WBS - BHS Mechanical Fabrication [02-01-03B]	160.0d	25-Jan-27	8-Sep-27	244.0d
12136	D1346 Fab. & Deliver Conveyors TBD [02-01-03B]	140.0d	25-Jan-27	10-Aug-27	244.0d
12137	D1348 Fab. & Deliver Header Steel / Platform / Sills [02-01-03B]	80.0d	5-Apr-27	27-Jul-27	254.0d
12138	D1349 Prep Mech. Matl for Install [02-01-03B]	20.0d	11-Aug-27	8-Sep-27	244.0d

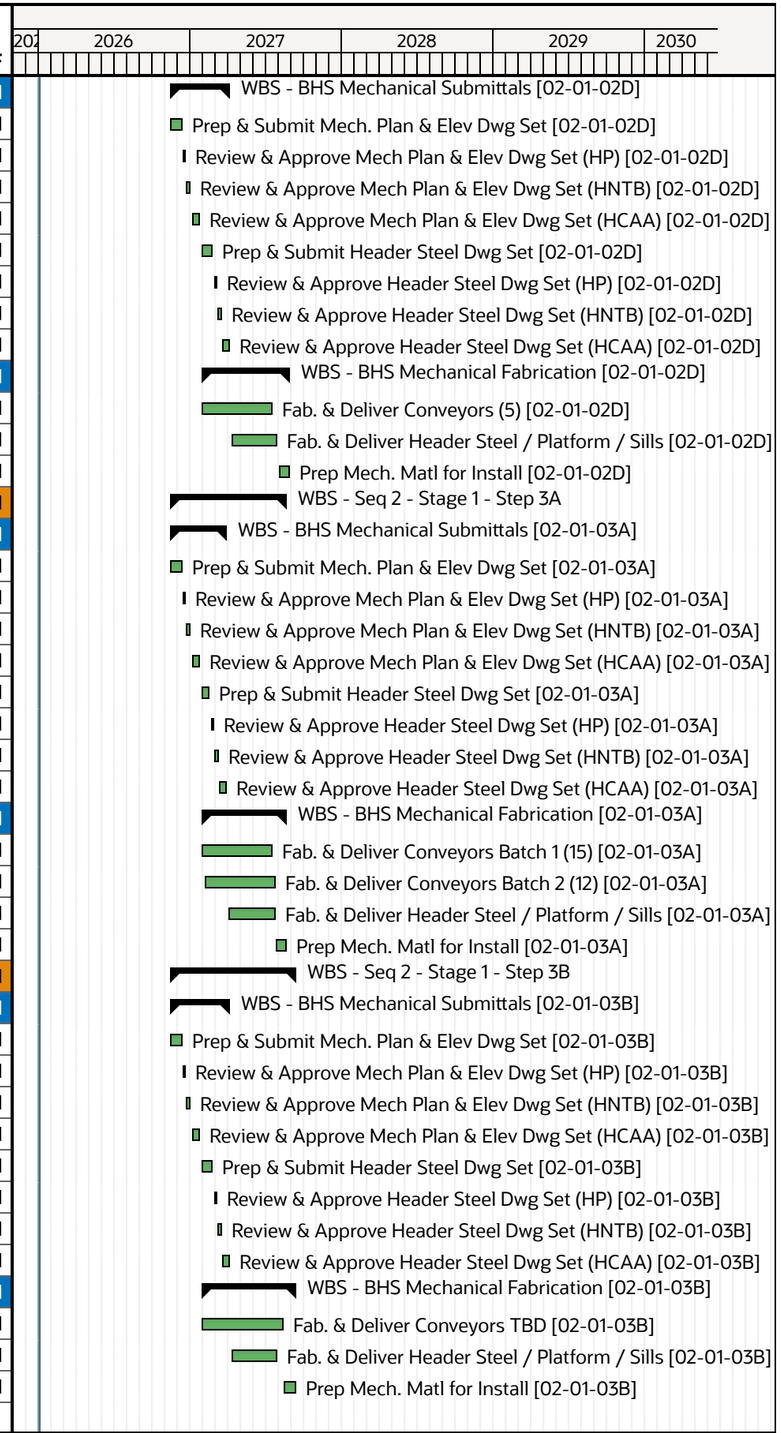

	ID	Name	Dur	Start	Finish	TF
12139	WBS - Seq 2 - Stage 1 - Step 4A		180.0d	10-Dec-26	24-Aug-27	334.0d
12140	WBS - BHS Mechanical Submittals [02-01-04A]		80.0d	10-Dec-26	2-Apr-27	334.0d
12141	D1350	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-04A]	10.0d	10-Dec-26	23-Dec-26	328.0d
12142	D4696	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-04A]	5.0d	24-Dec-26	31-Dec-26	334.0d
12143	D4706	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-04A]	10.0d	4-Jan-27	15-Jan-27	334.0d
12144	D1351	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-04A]	15.0d	18-Jan-27	5-Feb-27	334.0d
12145	D1352	Prep & Submit Header Steel Dwg Set [02-01-04A]	10.0d	8-Feb-27	19-Feb-27	334.0d
12146	D4716	Review & Approve Header Steel Dwg Set (HP) [02-01-04A]	5.0d	22-Feb-27	26-Feb-27	334.0d
12147	D4726	Review & Approve Header Steel Dwg Set (HNTB) [02-01-04A]	10.0d	1-Mar-27	12-Mar-27	334.0d
12148	D1354	Review & Approve Header Steel Dwg Set (HCAA) [02-01-04A]	15.0d	15-Mar-27	2-Apr-27	334.0d
12149	WBS - BHS Mechanical Fabrication [02-01-04A]		140.0d	8-Feb-27	24-Aug-27	334.0d
12150	D1353	Fab. & Deliver Conveyor (1) [02-01-04A]	120.0d	8-Feb-27	27-Jul-27	334.0d
12151	D1355	Fab. & Deliver Header Steel / Platform / Sills [02-01-04A]	80.0d	5-Apr-27	27-Jul-27	334.0d
12152	D1356	Prep Mech. Matl for Install [02-01-04A]	20.0d	28-Jul-27	24-Aug-27	334.0d
12153	WBS - Seq 2 - Stage 1 - Step 4B		180.0d	10-Dec-26	24-Aug-27	337.0d
12154	WBS - BHS Mechanical Submittals [02-01-04B]		80.0d	10-Dec-26	2-Apr-27	337.0d
12155	D1357	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-04B]	10.0d	10-Dec-26	23-Dec-26	328.0d
12156	D4736	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-04B]	5.0d	24-Dec-26	31-Dec-26	337.0d
12157	D4746	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-04B]	10.0d	4-Jan-27	15-Jan-27	337.0d
12158	D1358	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-04B]	15.0d	18-Jan-27	5-Feb-27	337.0d
12159	D1359	Prep & Submit Header Steel Dwg Set [02-01-04B]	10.0d	8-Feb-27	19-Feb-27	337.0d
12160	D4756	Review & Approve Header Steel Dwg Set (HP) [02-01-04B]	5.0d	22-Feb-27	26-Feb-27	337.0d
12161	D4766	Review & Approve Header Steel Dwg Set (HNTB) [02-01-04B]	10.0d	1-Mar-27	12-Mar-27	337.0d
12162	D1361	Review & Approve Header Steel Dwg Set (HCAA) [02-01-04B]	15.0d	15-Mar-27	2-Apr-27	337.0d
12163	WBS - BHS Mechanical Fabrication [02-01-04B]		140.0d	8-Feb-27	24-Aug-27	337.0d
12164	D1360	Fab. & Deliver Conveyor (9) [02-01-04B]	120.0d	8-Feb-27	27-Jul-27	337.0d
12165	D1362	Fab. & Deliver Header Steel / Platform / Sills [02-01-04B]	80.0d	5-Apr-27	27-Jul-27	337.0d
12166	D1363	Prep Mech. Matl for Install [02-01-04B]	20.0d	28-Jul-27	24-Aug-27	337.0d
12167	WBS - Seq 2 - Stage 1 - Step 4C		180.0d	10-Dec-26	24-Aug-27	349.0d
12168	WBS - BHS Mechanical Submittals [02-01-04C]		80.0d	10-Dec-26	2-Apr-27	349.0d
12169	D1364	Prep & Submit Mech. Plan & Elev Dwg Set [02-01-04C]	10.0d	10-Dec-26	23-Dec-26	328.0d
12170	D4776	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-01-04C]	5.0d	24-Dec-26	31-Dec-26	349.0d
12171	D4786	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-01-04C]	10.0d	4-Jan-27	15-Jan-27	349.0d
12172	D1365	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-01-04C]	15.0d	18-Jan-27	5-Feb-27	349.0d
12173	D1366	Prep & Submit Header Steel Dwg Set [02-01-04C]	10.0d	8-Feb-27	19-Feb-27	349.0d
12174	D4796	Review & Approve Header Steel Dwg Set (HP) [02-01-04C]	5.0d	22-Feb-27	26-Feb-27	349.0d
12175	D4806	Review & Approve Header Steel Dwg Set (HNTB) [02-01-04C]	10.0d	1-Mar-27	12-Mar-27	349.0d
12176	D1368	Review & Approve Header Steel Dwg Set (HCAA) [02-01-04C]	15.0d	15-Mar-27	2-Apr-27	349.0d
12177	WBS - BHS Mechanical Fabrication [02-01-04C]		140.0d	8-Feb-27	24-Aug-27	349.0d
12178	D1367	Fab. & Deliver Conveyor (2) [02-01-04C]	120.0d	8-Feb-27	27-Jul-27	349.0d
12179	D1369	Fab. & Deliver Header Steel / Platform / Sills [02-01-04C]	80.0d	5-Apr-27	27-Jul-27	349.0d
12180	D1370	Prep Mech. Matl for Install [02-01-04C]	20.0d	28-Jul-27	24-Aug-27	349.0d

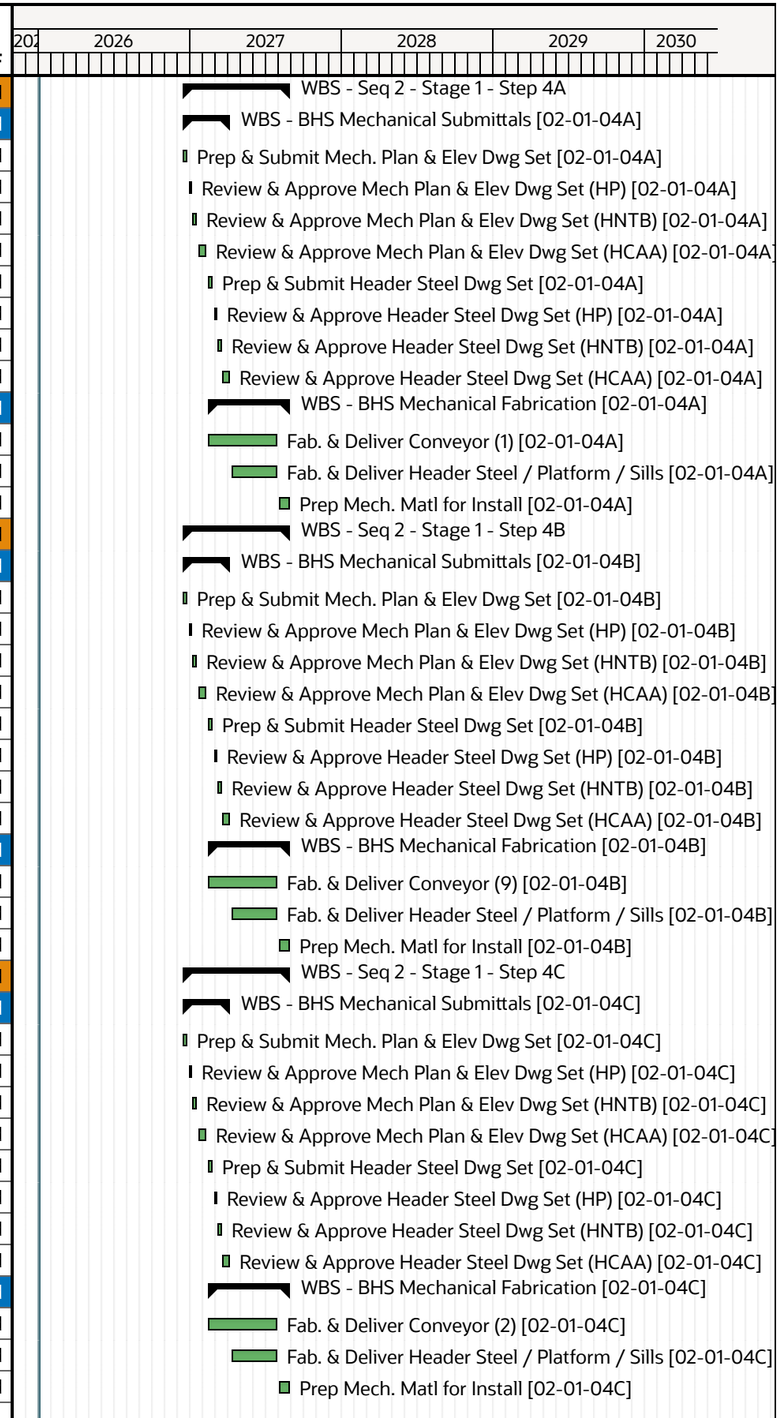

	ID	Name	Dur	Start	Finish	TF
12181	WBS - Seq 2 - Stage 2 - Step 1A		417.0d	3-Feb-26	22-Sep-27	352.0d
12182	WBS - BHS Mechanical Submittals [02-02-01A]		85.0d	24-Dec-26	23-Apr-27	357.0d
12183	D1372	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-01A]	15.0d	24-Dec-26	15-Jan-27	328.0d
12184	D4816	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-01A]	5.0d	18-Jan-27	22-Jan-27	352.0d
12185	D4826	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-01A]	10.0d	25-Jan-27	5-Feb-27	352.0d
12186	D1373	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-01A]	15.0d	8-Feb-27	26-Feb-27	352.0d
12187	D1374	Prep & Submit Header Steel Dwg Set [02-02-01A]	10.0d	1-Mar-27	12-Mar-27	357.0d
12188	D4836	Review & Approve Header Steel Dwg Set (HP) [02-02-01A]	5.0d	15-Mar-27	19-Mar-27	357.0d
12189	D4846	Review & Approve Header Steel Dwg Set (HNTB) [02-02-01A]	10.0d	22-Mar-27	2-Apr-27	357.0d
12190	D1377	Review & Approve Header Steel Dwg Set (HCAA) [02-02-01A]	15.0d	5-Apr-27	23-Apr-27	357.0d
12191	WBS - BHS Mechanical Fabrication [02-02-01A]		417.0d	3-Feb-26	22-Sep-27	352.0d
12192	D1371	Fab. & Deliver T1A 1 HSD [02-02-01A]	140.0d	3-Feb-26	19-Aug-26	609.0d
12193	D1375	Fab. & Deliver Conveyor Batch 1 (15) [02-02-01A]	120.0d	1-Mar-27	17-Aug-27	352.0d
12194	D1376	Fab. & Deliver Conveyor Batch 1 (5) [02-02-01A]	120.0d	8-Mar-27	24-Aug-27	352.0d
12195	D1378	Fab. & Deliver Header Steel / Platform / Sills [02-02-01A]	80.0d	26-Apr-27	17-Aug-27	357.0d
12196	D1379	Prep Mech. Matl for Install [02-02-01A]	20.0d	25-Aug-27	22-Sep-27	352.0d
12197	WBS - Seq 2 - Stage 2 - Step 1B		185.0d	24-Dec-26	15-Sep-27	355.0d
12198	WBS - BHS Mechanical Submittals [02-02-01B]		85.0d	24-Dec-26	23-Apr-27	355.0d
12199	D1380	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-01B]	15.0d	24-Dec-26	15-Jan-27	355.0d
12200	D4856	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-01B]	5.0d	18-Jan-27	22-Jan-27	355.0d
12201	D4866	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-01B]	10.0d	25-Jan-27	5-Feb-27	355.0d
12202	D1381	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-01B]	15.0d	8-Feb-27	26-Feb-27	355.0d
12203	D1382	Prep & Submit Header Steel Dwg Set [02-02-01B]	10.0d	1-Mar-27	12-Mar-27	355.0d
12204	D4876	Review & Approve Header Steel Dwg Set (HP) [02-02-01B]	5.0d	15-Mar-27	19-Mar-27	355.0d
12205	D4886	Review & Approve Header Steel Dwg Set (HNTB) [02-02-01B]	10.0d	22-Mar-27	2-Apr-27	355.0d
12206	D1384	Review & Approve Header Steel Dwg Set (HCAA) [02-02-01B]	15.0d	5-Apr-27	23-Apr-27	355.0d
12207	WBS - BHS Mechanical Fabrication [02-02-01B]		140.0d	1-Mar-27	15-Sep-27	355.0d
12208	D1383	Fab. & Deliver Conveyor Batch 1 (XX) [02-02-01B]	120.0d	1-Mar-27	17-Aug-27	355.0d
12209	D1385	Fab. & Deliver Header Steel / Platform / Sills [02-02-01B]	80.0d	26-Apr-27	17-Aug-27	355.0d
12210	D1386	Prep Mech. Matl for Install [02-02-01B]	20.0d	18-Aug-27	15-Sep-27	355.0d
12211	WBS - Seq 2 - Stage 2 - Step 2A		442.0d	3-Feb-26	27-Oct-27	328.0d
12212	WBS - BHS Mechanical Submittals [02-02-02A]		100.0d	18-Jan-27	7-Jun-27	328.0d
12213	D1389	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02A]	20.0d	18-Jan-27	12-Feb-27	328.0d
12214	D4896	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02A]	5.0d	15-Feb-27	19-Feb-27	328.0d
12215	D4906	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02A]	10.0d	22-Feb-27	5-Mar-27	328.0d
12216	D1390	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02A]	15.0d	8-Mar-27	26-Mar-27	328.0d
12217	D1391	Prep & Submit Header Steel Dwg Set [02-02-02A]	20.0d	29-Mar-27	23-Apr-27	328.0d
12218	D4916	Review & Approve Header Steel Dwg Set (HP) [02-02-02A]	5.0d	26-Apr-27	30-Apr-27	328.0d
12219	D4926	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02A]	10.0d	3-May-27	14-May-27	328.0d
12220	D1395	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02A]	15.0d	17-May-27	7-Jun-27	328.0d
12221	WBS - BHS Mechanical Fabrication [02-02-02A]		442.0d	3-Feb-26	27-Oct-27	328.0d
12222	D1387	Fab. & Deliver C3A 1 HSD [02-02-02A]	140.0d	3-Feb-26	19-Aug-26	610.0d

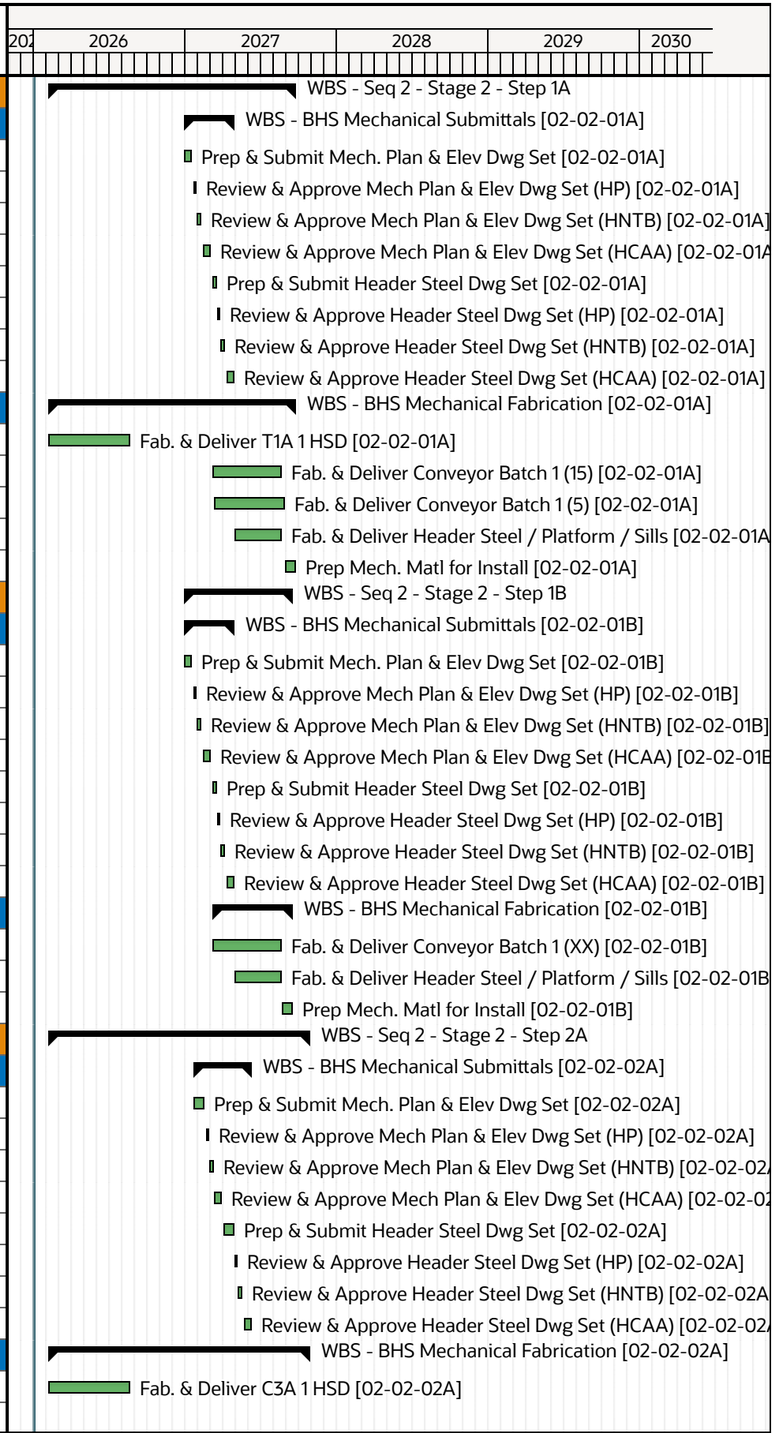


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:11 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
12223	D1388	Fab. & Deliver C3A 5A 1 HSD [02-02-02A]	140.0d	3-Feb-26	19-Aug-26	610.0d
12224	D1392	Fab. & Deliver Conveyor Batch 1 (15) [02-02-02A]	120.0d	29-Mar-27	15-Sep-27	328.0d
12225	D1393	Fab. & Deliver Conveyor Batch 2 (15) [02-02-02A]	120.0d	5-Apr-27	22-Sep-27	328.0d
12226	D1394	Fab. & Deliver Conveyor Batch 3 (3) [02-02-02A]	120.0d	12-Apr-27	29-Sep-27	328.0d
12227	D1396	Fab. & Deliver Header Steel / Platform / Sills [02-02-02A]	80.0d	8-Jun-27	29-Sep-27	328.0d
12228	D1397	Prep Mech. Matl for Install [02-02-02A]	20.0d	30-Sep-27	27-Oct-27	328.0d
12229	WBS - Seq 2 - Stage 2 - Step 2B		442.0d	3-Feb-26	27-Oct-27	349.0d
12230	WBS - BHS Mechanical Submittals [02-02-02B]		100.0d	18-Jan-27	7-Jun-27	349.0d
12231	D1399	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02B]	20.0d	18-Jan-27	12-Feb-27	348.0d
12232	D4936	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02B]	5.0d	15-Feb-27	19-Feb-27	349.0d
12233	D4946	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02B]	10.0d	22-Feb-27	5-Mar-27	349.0d
12234	D1400	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02B]	15.0d	8-Mar-27	26-Mar-27	349.0d
12235	D1401	Prep & Submit Header Steel Dwg Set [02-02-02B]	20.0d	29-Mar-27	23-Apr-27	349.0d
12236	D4956	Review & Approve Header Steel Dwg Set (HP) [02-02-02B]	5.0d	26-Apr-27	30-Apr-27	349.0d
12237	D4966	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02B]	10.0d	3-May-27	14-May-27	349.0d
12238	D1403	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02B]	15.0d	17-May-27	7-Jun-27	349.0d
12239	WBS - BHS Mechanical Fabrication [02-02-02B]		442.0d	3-Feb-26	27-Oct-27	349.0d
12240	D1398	Fab. & Deliver T5A 1 HSD [02-02-02B]	140.0d	3-Feb-26	19-Aug-26	631.0d
12241	D1402	Fab. & Deliver Conveyor (2) [02-02-02B]	120.0d	29-Mar-27	15-Sep-27	359.0d
12242	D1404	Fab. & Deliver Header Steel / Platform / Sills [02-02-02B]	80.0d	8-Jun-27	29-Sep-27	349.0d
12243	D1405	Prep Mech. Matl for Install [02-02-02B]	20.0d	30-Sep-27	27-Oct-27	349.0d
12244	WBS - Seq 2 - Stage 2 - Step 2C		200.0d	18-Jan-27	27-Oct-27	352.0d
12245	WBS - BHS Mechanical Submittals [02-02-02C]		100.0d	18-Jan-27	7-Jun-27	352.0d
12246	D1406	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02C]	20.0d	18-Jan-27	12-Feb-27	348.0d
12247	D4976	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02C]	5.0d	15-Feb-27	19-Feb-27	352.0d
12248	D4986	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02C]	10.0d	22-Feb-27	5-Mar-27	352.0d
12249	D1407	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02C]	15.0d	8-Mar-27	26-Mar-27	352.0d
12250	D1408	Prep & Submit Header Steel Dwg Set [02-02-02C]	20.0d	29-Mar-27	23-Apr-27	352.0d
12251	D4996	Review & Approve Header Steel Dwg Set (HP) [02-02-02C]	5.0d	26-Apr-27	30-Apr-27	352.0d
12252	D5006	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02C]	10.0d	3-May-27	14-May-27	352.0d
12253	D1410	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02C]	15.0d	17-May-27	7-Jun-27	352.0d
12254	WBS - BHS Mechanical Fabrication [02-02-02C]		150.0d	29-Mar-27	27-Oct-27	352.0d
12255	D1409	Fab. & Deliver Conveyor (7) [02-02-02C]	120.0d	29-Mar-27	15-Sep-27	362.0d
12256	D1411	Fab. & Deliver Header Steel / Platform / Sills [02-02-02C]	80.0d	8-Jun-27	29-Sep-27	352.0d
12257	D1412	Prep Mech. Matl for Install [02-02-02C]	20.0d	30-Sep-27	27-Oct-27	352.0d
12258	WBS - Seq 2 - Stage 2 - Step 2D		190.0d	18-Jan-27	13-Oct-27	373.0d
12259	WBS - BHS Mechanical Submittals [02-02-02D]		90.0d	18-Jan-27	21-May-27	373.0d
12260	D1413	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02D]	20.0d	18-Jan-27	12-Feb-27	348.0d
12261	D5016	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02D]	5.0d	15-Feb-27	19-Feb-27	373.0d
12262	D5026	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02D]	10.0d	22-Feb-27	5-Mar-27	373.0d
12263	D1414	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02D]	15.0d	8-Mar-27	26-Mar-27	373.0d
12264	D1415	Prep & Submit Header Steel Dwg Set [02-02-02D]	10.0d	29-Mar-27	9-Apr-27	373.0d

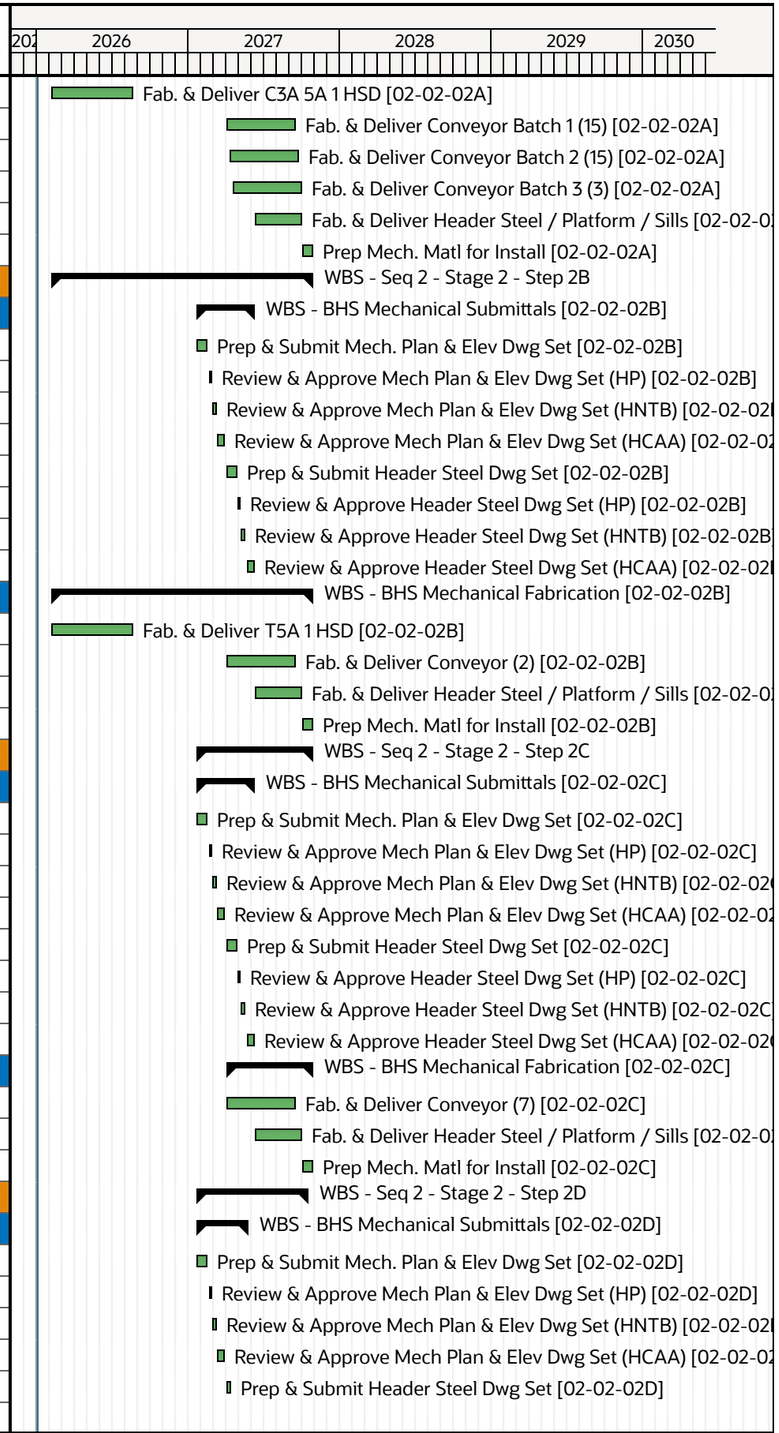


	ID	Name	Dur	Start	Finish	TF
12265	D5036	Review & Approve Header Steel Dwg Set (HP) [02-02-02D]	5.0d	12-Apr-27	16-Apr-27	373.0d
12266	D5046	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02D]	10.0d	19-Apr-27	30-Apr-27	373.0d
12267	D1417	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02D]	15.0d	3-May-27	21-May-27	373.0d
12268	WBS - BHS Mechanical Fabrication [02-02-02D]		140.0d	29-Mar-27	13-Oct-27	373.0d
12269	D1416	Fab. & Deliver Conveyor (1) [02-02-02D]	120.0d	29-Mar-27	15-Sep-27	373.0d
12270	D1418	Fab. & Deliver Header Steel / Platform / Sills [02-02-02D]	80.0d	24-May-27	15-Sep-27	373.0d
12271	D1419	Prep Mech. Matl for Install [02-02-02D]	20.0d	16-Sep-27	13-Oct-27	373.0d
12272	WBS - Seq 2 - Stage 2 - Step 2E		200.0d	15-Feb-27	24-Nov-27	348.0d
12273	WBS - BHS Mechanical Submittals [02-02-02E]		100.0d	15-Feb-27	6-Jul-27	348.0d
12274	D1420	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02E]	20.0d	15-Feb-27	12-Mar-27	348.0d
12275	D5056	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02E]	5.0d	15-Mar-27	19-Mar-27	348.0d
12276	D5066	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02E]	10.0d	22-Mar-27	2-Apr-27	348.0d
12277	D1421	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02E]	15.0d	5-Apr-27	23-Apr-27	348.0d
12278	D1422	Prep & Submit Header Steel Dwg Set [02-02-02E]	20.0d	26-Apr-27	21-May-27	348.0d
12279	D5076	Review & Approve Header Steel Dwg Set (HP) [02-02-02E]	5.0d	24-May-27	28-May-27	348.0d
12280	D5086	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02E]	10.0d	1-Jun-27	14-Jun-27	348.0d
12281	D1424	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02E]	15.0d	15-Jun-27	6-Jul-27	348.0d
12282	WBS - BHS Mechanical Fabrication [02-02-02E]		150.0d	26-Apr-27	24-Nov-27	348.0d
12283	D1423	Fab. & Deliver Conveyor (1) [02-02-02E]	120.0d	26-Apr-27	13-Oct-27	358.0d
12284	D1425	Fab. & Deliver Header Steel / Platform / Sills [02-02-02E]	80.0d	7-Jul-27	27-Oct-27	348.0d
12285	D1426	Prep Mech. Matl for Install [02-02-02E]	20.0d	28-Oct-27	24-Nov-27	348.0d
12286	WBS - Seq 2 - Stage 2 - Step 2F		190.0d	15-Feb-27	10-Nov-27	367.0d
12287	WBS - BHS Mechanical Submittals [02-02-02F]		85.0d	15-Feb-27	14-Jun-27	372.0d
12288	D1427	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02F]	20.0d	15-Feb-27	12-Mar-27	367.0d
12289	D5096	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02F]	5.0d	15-Mar-27	19-Mar-27	367.0d
12290	D5106	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02F]	10.0d	22-Mar-27	2-Apr-27	367.0d
12291	D1428	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02F]	15.0d	5-Apr-27	23-Apr-27	367.0d
12292	D1429	Prep & Submit Header Steel Dwg Set [02-02-02F]	5.0d	26-Apr-27	30-Apr-27	372.0d
12293	D5116	Review & Approve Header Steel Dwg Set (HP) [02-02-02F]	5.0d	3-May-27	7-May-27	372.0d
12294	D5126	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02F]	10.0d	10-May-27	21-May-27	372.0d
12295	D1431	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02F]	15.0d	24-May-27	14-Jun-27	372.0d
12296	WBS - BHS Mechanical Fabrication [02-02-02F]		140.0d	26-Apr-27	10-Nov-27	367.0d
12297	D1430	Fab. & Deliver Conveyor (1) [02-02-02F]	120.0d	26-Apr-27	13-Oct-27	367.0d
12298	D1432	Fab. & Deliver Header Steel / Platform / Sills [02-02-02F]	80.0d	15-Jun-27	6-Oct-27	372.0d
12299	D1433	Prep Mech. Matl for Install [02-02-02F]	20.0d	14-Oct-27	10-Nov-27	367.0d
12300	WBS - Seq 2 - Stage 2 - Step 2G		190.0d	15-Feb-27	10-Nov-27	368.0d
12301	WBS - BHS Mechanical Submittals [02-02-02G]		90.0d	15-Feb-27	21-Jun-27	368.0d
12302	D1434	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-02G]	20.0d	15-Feb-27	12-Mar-27	368.0d
12303	D5136	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-02G]	5.0d	15-Mar-27	19-Mar-27	368.0d
12304	D5146	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-02G]	10.0d	22-Mar-27	2-Apr-27	368.0d
12305	D1435	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-02G]	15.0d	5-Apr-27	23-Apr-27	368.0d
12306	D1436	Prep & Submit Header Steel Dwg Set [02-02-02G]	10.0d	26-Apr-27	7-May-27	368.0d

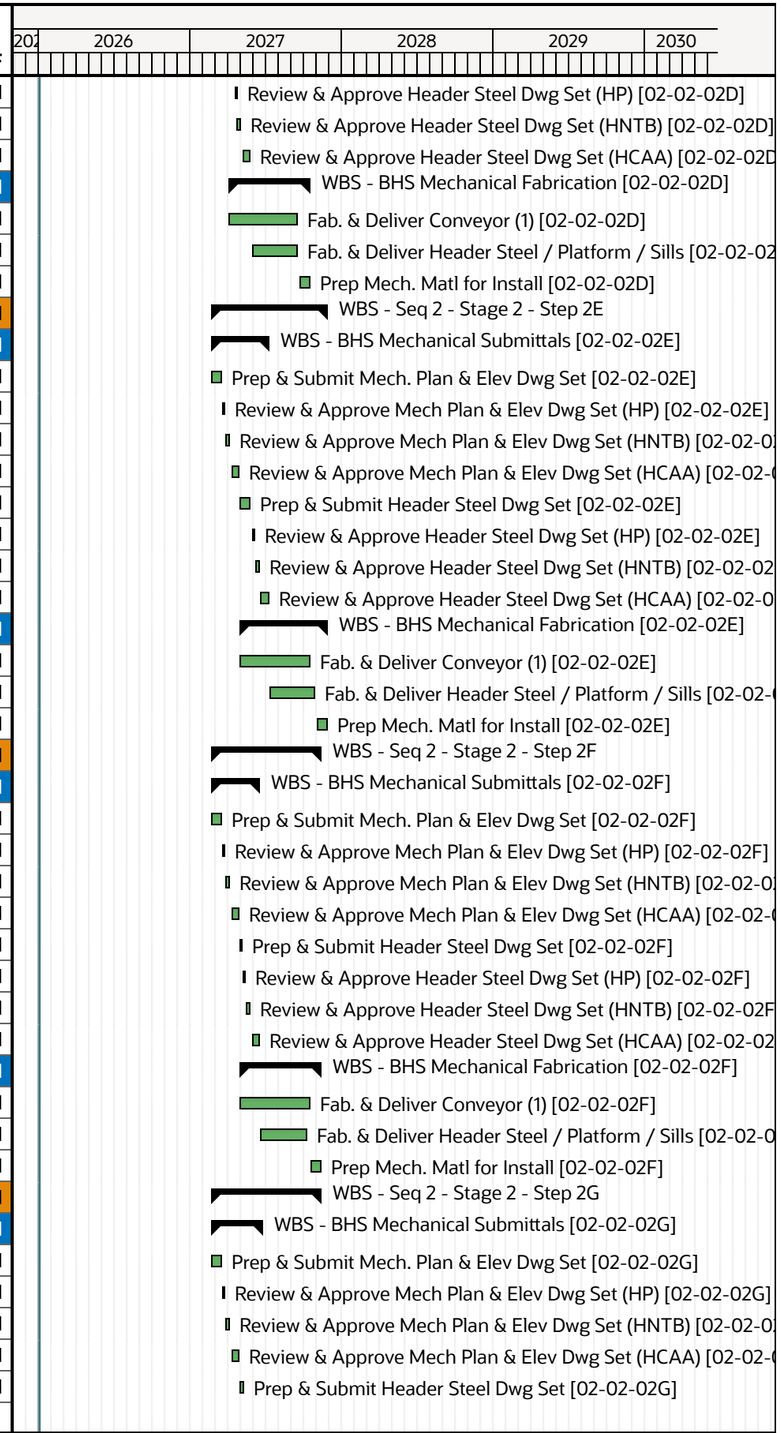


	ID	Name	Dur	Start	Finish	TF
12307	D5156	Review & Approve Header Steel Dwg Set (HP) [02-02-02G]	5.0d	10-May-27	14-May-27	368.0d
12308	D5166	Review & Approve Header Steel Dwg Set (HNTB) [02-02-02G]	10.0d	17-May-27	28-May-27	368.0d
12309	D1438	Review & Approve Header Steel Dwg Set (HCAA) [02-02-02G]	15.0d	1-Jun-27	21-Jun-27	368.0d
12310	WBS - BHS Mechanical Fabrication [02-02-02G]		140.0d	26-Apr-27	10-Nov-27	368.0d
12311	D1437	Fab. & Deliver Conveyor (1) [02-02-02G]	120.0d	26-Apr-27	13-Oct-27	368.0d
12312	D1439	Fab. & Deliver Header Steel / Platform / Sills [02-02-02G]	80.0d	22-Jun-27	13-Oct-27	368.0d
12313	D1440	Prep Mech. Matl for Install [02-02-02G]	20.0d	14-Oct-27	10-Nov-27	368.0d
12314	WBS - Seq 2 - Stage 2 - Step 3A		200.0d	15-Feb-27	24-Nov-27	364.0d
12315	WBS - BHS Mechanical Submittals [02-02-03A]		85.0d	15-Feb-27	14-Jun-27	379.0d
12316	D1441	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-03A]	20.0d	15-Feb-27	12-Mar-27	364.0d
12317	D5176	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-03A]	5.0d	15-Mar-27	19-Mar-27	364.0d
12318	D5186	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-03A]	10.0d	22-Mar-27	2-Apr-27	364.0d
12319	D1442	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-03A]	15.0d	5-Apr-27	23-Apr-27	364.0d
12320	D1443	Prep & Submit Header Steel Dwg Set [02-02-03A]	5.0d	26-Apr-27	30-Apr-27	379.0d
12321	D5196	Review & Approve Header Steel Dwg Set (HP) [02-02-03A]	5.0d	3-May-27	7-May-27	379.0d
12322	D5206	Review & Approve Header Steel Dwg Set (HNTB) [02-02-03A]	10.0d	10-May-27	21-May-27	379.0d
12323	D1445	Review & Approve Header Steel Dwg Set (HCAA) [02-02-03A]	15.0d	24-May-27	14-Jun-27	379.0d
12324	WBS - BHS Mechanical Fabrication [02-02-03A]		150.0d	26-Apr-27	24-Nov-27	364.0d
12325	D1444	Fab. & Deliver Conveyor Batch 1 (15) [02-02-03A]	120.0d	26-Apr-27	13-Oct-27	364.0d
12326	D1446	Fab. & Deliver Conveyor Batch 2 (15) [02-02-03A]	120.0d	3-May-27	20-Oct-27	364.0d
12327	D1447	Fab. & Deliver Conveyor Batch 1 (11) [02-02-03A]	120.0d	10-May-27	27-Oct-27	364.0d
12328	D1448	Fab. & Deliver Header Steel / Platform / Sills [02-02-03A]	80.0d	15-Jun-27	6-Oct-27	379.0d
12329	D1449	Prep Mech. Matl for Install [02-02-03A]	20.0d	28-Oct-27	24-Nov-27	364.0d
12330	WBS - Seq 2 - Stage 2 - Step 3B		190.0d	15-Feb-27	10-Nov-27	380.0d
12331	WBS - BHS Mechanical Submittals [02-02-03B]		50.0d	15-Feb-27	23-Apr-27	380.0d
12332	D1450	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-03B]	20.0d	15-Feb-27	12-Mar-27	373.0d
12333	D5216	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-03B]	5.0d	15-Mar-27	19-Mar-27	380.0d
12334	D5226	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-03B]	10.0d	22-Mar-27	2-Apr-27	380.0d
12335	D1451	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-03B]	15.0d	5-Apr-27	23-Apr-27	380.0d
12336	WBS - BHS Mechanical Fabrication [02-02-03B]		140.0d	26-Apr-27	10-Nov-27	380.0d
12337	D1452	Fab. & Deliver Conveyor Batch 1 (15) [02-02-03B]	120.0d	26-Apr-27	13-Oct-27	380.0d
12338	D1453	Prep Mech. Matl for Install [02-02-03B]	20.0d	14-Oct-27	10-Nov-27	380.0d
12339	WBS - Seq 2 - Stage 2 - Step 3C		195.0d	15-Mar-27	17-Dec-27	374.0d
12340	WBS - BHS Mechanical Submittals [02-02-03C]		95.0d	15-Mar-27	27-Jul-27	373.0d
12341	D1454	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-03C]	20.0d	15-Mar-27	9-Apr-27	373.0d
12342	D5236	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-03C]	5.0d	12-Apr-27	16-Apr-27	373.0d
12343	D5246	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-03C]	10.0d	19-Apr-27	30-Apr-27	373.0d
12344	D1455	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-03C]	15.0d	3-May-27	21-May-27	373.0d
12345	D1456	Prep & Submit Header Steel Dwg Set [02-02-03C]	15.0d	24-May-27	14-Jun-27	373.0d
12346	D5256	Review & Approve Header Steel Dwg Set (HP) [02-02-03C]	5.0d	15-Jun-27	21-Jun-27	373.0d
12347	D5266	Review & Approve Header Steel Dwg Set (HNTB) [02-02-03C]	10.0d	22-Jun-27	6-Jul-27	373.0d
12348	D1458	Review & Approve Header Steel Dwg Set (HCAA) [02-02-03C]	15.0d	7-Jul-27	27-Jul-27	373.0d

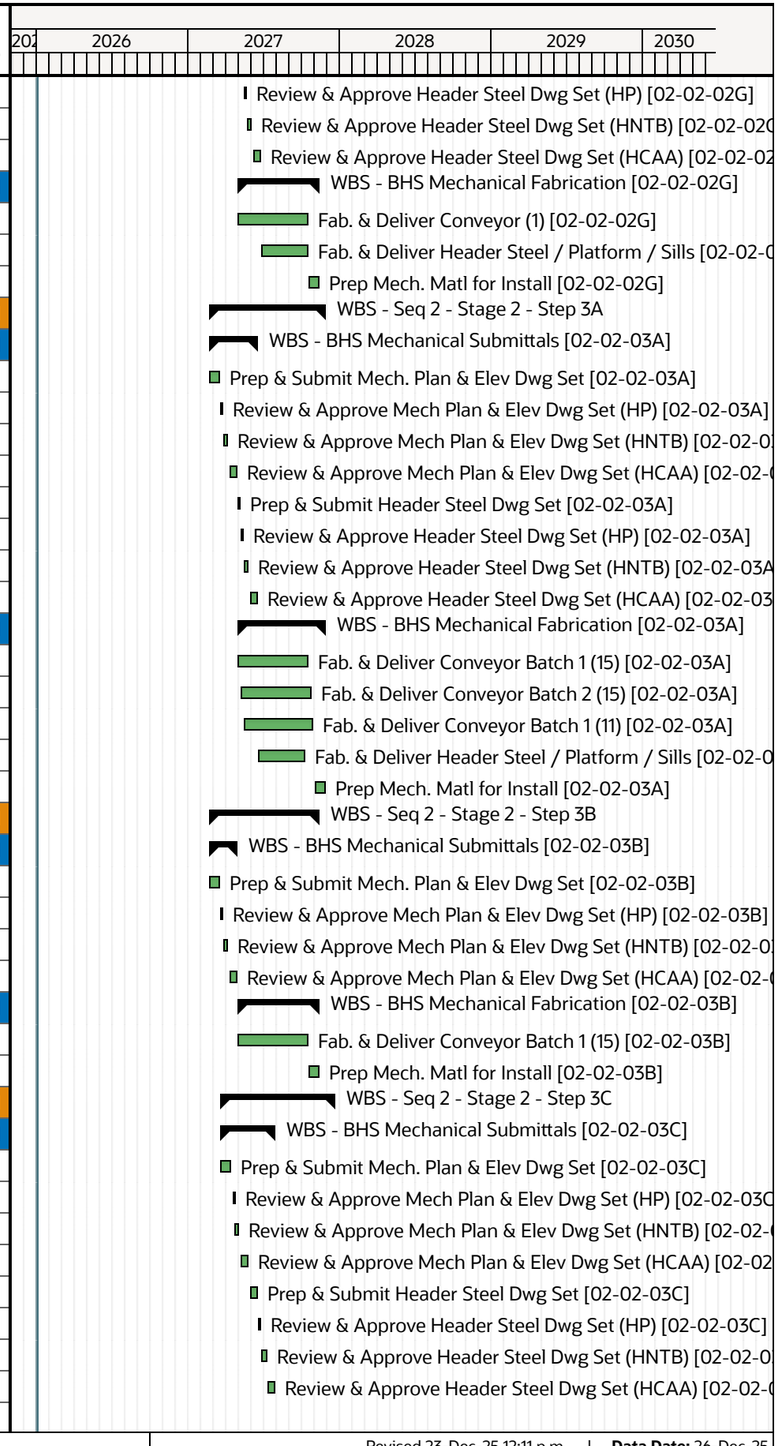


	ID	Name	Dur	Start	Finish	TF
12349	WBS - BHS Mechanical Fabrication [02-02-03C]		145.0d	24-May-27	17-Dec-27	374.0d
12350	D1457	Fab. & Deliver Conveyor Batch 1 (15) [02-02-03C]	120.0d	24-May-27	10-Nov-27	378.0d
12351	D1459	Fab. & Deliver Header Steel / Platform / Sills [02-02-03C]	80.0d	28-Jul-27	17-Nov-27	373.0d
12352	D1460	Prep Mech. Matl for Install [02-02-03C]	20.0d	18-Nov-27	17-Dec-27	373.0d
12353	WBS - Seq 2 - Stage 2 - Step 4A		195.0d	15-Mar-27	17-Dec-27	378.0d
12354	WBS - BHS Mechanical Submittals [02-02-04A]		95.0d	15-Mar-27	27-Jul-27	377.0d
12355	D1461	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-04A]	20.0d	15-Mar-27	9-Apr-27	377.0d
12356	D5276	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-04A]	5.0d	12-Apr-27	16-Apr-27	377.0d
12357	D5286	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-04A]	10.0d	19-Apr-27	30-Apr-27	377.0d
12358	D1462	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-04A]	15.0d	3-May-27	21-May-27	377.0d
12359	D1463	Prep & Submit Header Steel Dwg Set [02-02-04A]	15.0d	24-May-27	14-Jun-27	377.0d
12360	D5296	Review & Approve Header Steel Dwg Set (HP) [02-02-04A]	5.0d	15-Jun-27	21-Jun-27	377.0d
12361	D5306	Review & Approve Header Steel Dwg Set (HNTB) [02-02-04A]	10.0d	22-Jun-27	6-Jul-27	377.0d
12362	D1465	Review & Approve Header Steel Dwg Set (HCAA) [02-02-04A]	15.0d	7-Jul-27	27-Jul-27	377.0d
12363	WBS - BHS Mechanical Fabrication [02-02-04A]		145.0d	24-May-27	17-Dec-27	378.0d
12364	D1464	Fab. & Deliver Conveyors (3) [02-02-04A]	120.0d	24-May-27	10-Nov-27	382.0d
12365	D1466	Fab. & Deliver Header Steel / Platform / Sills [02-02-04A]	80.0d	28-Jul-27	17-Nov-27	377.0d
12366	D1467	Prep Mech. Matl for Install [02-02-04A]	20.0d	18-Nov-27	17-Dec-27	377.0d
12367	WBS - Seq 2 - Stage 2 - Step 4B		195.0d	15-Mar-27	17-Dec-27	382.0d
12368	WBS - BHS Mechanical Submittals [02-02-04B]		95.0d	15-Mar-27	27-Jul-27	381.0d
12369	D1468	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-04B]	20.0d	15-Mar-27	9-Apr-27	381.0d
12370	D5316	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-04B]	5.0d	12-Apr-27	16-Apr-27	381.0d
12371	D5326	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-04B]	10.0d	19-Apr-27	30-Apr-27	381.0d
12372	D1469	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-04B]	15.0d	3-May-27	21-May-27	381.0d
12373	D1470	Prep & Submit Header Steel Dwg Set [02-02-04B]	15.0d	24-May-27	14-Jun-27	381.0d
12374	D5336	Review & Approve Header Steel Dwg Set (HP) [02-02-04B]	5.0d	15-Jun-27	21-Jun-27	381.0d
12375	D5346	Review & Approve Header Steel Dwg Set (HNTB) [02-02-04B]	10.0d	22-Jun-27	6-Jul-27	381.0d
12376	D1472	Review & Approve Header Steel Dwg Set (HCAA) [02-02-04B]	15.0d	7-Jul-27	27-Jul-27	381.0d
12377	WBS - BHS Mechanical Fabrication [02-02-04B]		145.0d	24-May-27	17-Dec-27	382.0d
12378	D1471	Fab. & Deliver Conveyors (2) [02-02-04B]	120.0d	24-May-27	10-Nov-27	386.0d
12379	D1473	Fab. & Deliver Header Steel / Platform / Sills [02-02-04B]	80.0d	28-Jul-27	17-Nov-27	381.0d
12380	D1474	Prep Mech. Matl for Install [02-02-04B]	20.0d	18-Nov-27	17-Dec-27	381.0d
12381	WBS - Seq 2 - Stage 2 - Step 5		185.0d	12-Apr-27	4-Jan-28	395.0d
12382	WBS - BHS Mechanical Submittals [02-02-05]		85.0d	12-Apr-27	10-Aug-27	394.0d
12383	D1475	Prep & Submit Mech. Plan & Elev Dwg Set [02-02-05]	15.0d	12-Apr-27	30-Apr-27	394.0d
12384	D5356	Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-05]	5.0d	3-May-27	7-May-27	394.0d
12385	D5366	Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-05]	10.0d	10-May-27	21-May-27	394.0d
12386	D1476	Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-05]	15.0d	24-May-27	14-Jun-27	394.0d
12387	D1477	Prep & Submit Header Steel Dwg Set [02-02-05]	10.0d	15-Jun-27	28-Jun-27	394.0d
12388	D5376	Review & Approve Header Steel Dwg Set (HP) [02-02-05]	5.0d	29-Jun-27	6-Jul-27	394.0d
12389	D5386	Review & Approve Header Steel Dwg Set (HNTB) [02-02-05]	10.0d	7-Jul-27	20-Jul-27	394.0d
12390	D1479	Review & Approve Header Steel Dwg Set (HCAA) [02-02-05]	15.0d	21-Jul-27	10-Aug-27	394.0d

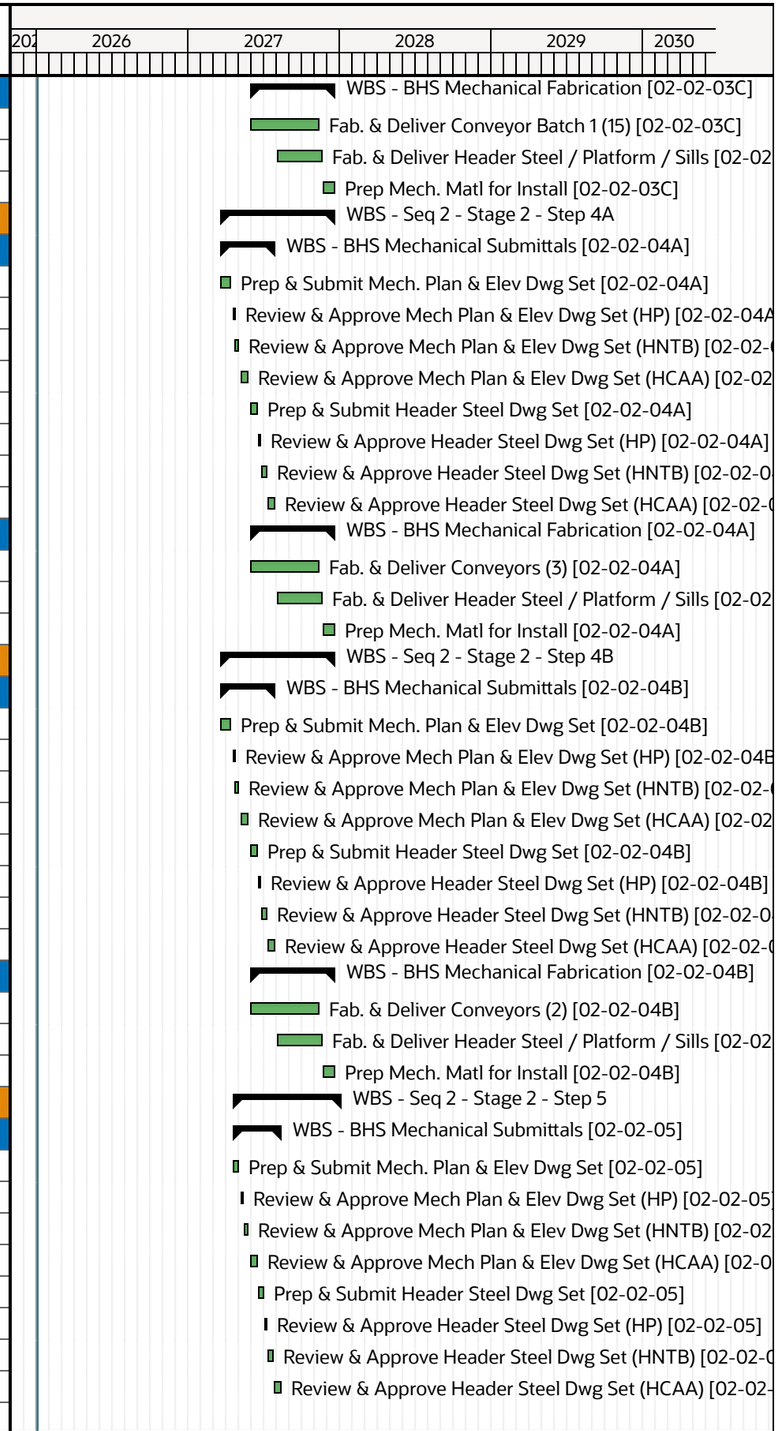


ID	Name	Dur	Start	Finish	TF
12391	WBS - BHS Mechanical Fabrication [02-02-05]	140.0d	15-Jun-27	4-Jan-28	395.0d
12392	D1478 Fab. & Deliver Conveyors (11) [02-02-05]	120.0d	15-Jun-27	3-Dec-27	394.0d
12393	D1480 Fab. & Deliver Header Steel / Platform / Sills [02-02-05]	80.0d	11-Aug-27	3-Dec-27	394.0d
12394	D1481 Prep Mech. Matl for Install [02-02-05]	20.0d	6-Dec-27	4-Jan-28	394.0d
12395	WBS - Seq 2 - Stage 2 - Step 6	185.0d	12-Apr-27	4-Jan-28	410.0d
12396	WBS - BHS Mechanical Submittals [02-02-06]	45.0d	12-Apr-27	14-Jun-27	409.0d
12397	D1482 Prep & Submit Mech. Plan & Elev Dwg Set [02-02-06]	15.0d	12-Apr-27	30-Apr-27	409.0d
12398	D5396 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-06]	5.0d	3-May-27	7-May-27	409.0d
12399	D5406 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-06]	10.0d	10-May-27	21-May-27	409.0d
12400	D1483 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-06]	15.0d	24-May-27	14-Jun-27	409.0d
12401	WBS - BHS Mechanical Fabrication [02-02-06]	140.0d	15-Jun-27	4-Jan-28	410.0d
12402	D1484 Fab. & Deliver Conveyors (2) [02-02-06]	120.0d	15-Jun-27	3-Dec-27	409.0d
12403	D1485 Prep Mech. Matl for Install [02-02-06]	20.0d	6-Dec-27	4-Jan-28	409.0d
12404	WBS - Seq 2 - Stage 2 - Step 7	185.0d	12-Apr-27	4-Jan-28	414.0d
12405	WBS - BHS Mechanical Submittals [02-02-07]	80.0d	12-Apr-27	3-Aug-27	418.0d
12406	D1486 Prep & Submit Mech. Plan & Elev Dwg Set [02-02-07]	15.0d	12-Apr-27	30-Apr-27	413.0d
12407	D5416 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-07]	5.0d	3-May-27	7-May-27	413.0d
12408	D5426 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-07]	10.0d	10-May-27	21-May-27	413.0d
12409	D1487 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-07]	15.0d	24-May-27	14-Jun-27	413.0d
12410	D1488 Prep & Submit Header Steel Dwg Set [02-02-07]	5.0d	15-Jun-27	21-Jun-27	418.0d
12411	D5436 Review & Approve Header Steel Dwg Set (HP) [02-02-07]	5.0d	22-Jun-27	28-Jun-27	418.0d
12412	D5446 Review & Approve Header Steel Dwg Set (HNTB) [02-02-07]	10.0d	29-Jun-27	13-Jul-27	418.0d
12413	D1490 Review & Approve Header Steel Dwg Set (HCAA) [02-02-07]	15.0d	14-Jul-27	3-Aug-27	418.0d
12414	WBS - BHS Mechanical Fabrication [02-02-07]	140.0d	15-Jun-27	4-Jan-28	414.0d
12415	D1489 Fab. & Deliver Conveyors (X) [02-02-07]	120.0d	15-Jun-27	3-Dec-27	413.0d
12416	D1491 Fab. & Deliver Header Steel / Platform / Sills [02-02-07]	80.0d	4-Aug-27	24-Nov-27	418.0d
12417	D1492 Prep Mech. Matl for Install [02-02-07]	20.0d	6-Dec-27	4-Jan-28	413.0d
12418	WBS - Seq 2 - Stage 2 - Step 8	45.0d	12-Apr-27	14-Jun-27	560.0d
12419	D1493 Prep & Submit Mech. Plan & Elev Dwg Set [02-02-08]	15.0d	12-Apr-27	30-Apr-27	559.0d
12420	D5456 Review & Approve Mech Plan & Elev Dwg Set (HP) [02-02-08]	5.0d	3-May-27	7-May-27	559.0d
12421	D5466 Review & Approve Mech Plan & Elev Dwg Set (HNTB) [02-02-08]	10.0d	10-May-27	21-May-27	559.0d
12422	D1494 Review & Approve Mech Plan & Elev Dwg Set (HCAA) [02-02-08]	15.0d	24-May-27	14-Jun-27	559.0d
12423	WBS - Electrical/Controls/Software Engineering Submittals & Procurement - Part 2 Supplement C Wave 1	975.0d	11-Feb-26	11-Dec-29	70.0d
12424	WBS - General Electrical/Controls/Software Engineering Submittals & Procurement	975.0d	11-Feb-26	11-Dec-29	70.0d
12425	WBS - Cross-Belt Electrical Catalog Cut / Equipment Specs Submittals	45.0d	13-Feb-26	16-Apr-26	209.0d
12426	A91270 Prep & Submit Cross-Belt Elec Catalog Cut / Equip. Specs	15.0d	13-Feb-26	5-Mar-26	209.0d
12427	A91280 Review & Approve (HP) Cross-Belt Elec. Catalog Cut / Equip. Specs	5.0d	6-Mar-26	12-Mar-26	209.0d
12428	A106790 Review & Approve (HNTB) Cross-Belt Elec. Catalog Cut / Equip. Specs	10.0d	13-Mar-26	26-Mar-26	209.0d
12429	A106800 Review & Approve (HCAA) Cross-Belt Elec. Catalog Cut / Equip. Specs	15.0d	27-Mar-26	16-Apr-26	209.0d
12430	WBS - Factory Acceptance Test Plan & Agenda	45.0d	13-Feb-26	16-Apr-26	563.0d
12431	D1648 Prep & Submit Factory Acceptance Test Plan & Agenda	15.0d	13-Feb-26	5-Mar-26	563.0d
12432	D5966 HP Review & Approve Factory Acceptance Test Plan & Agenda	5.0d	6-Mar-26	12-Mar-26	563.0d

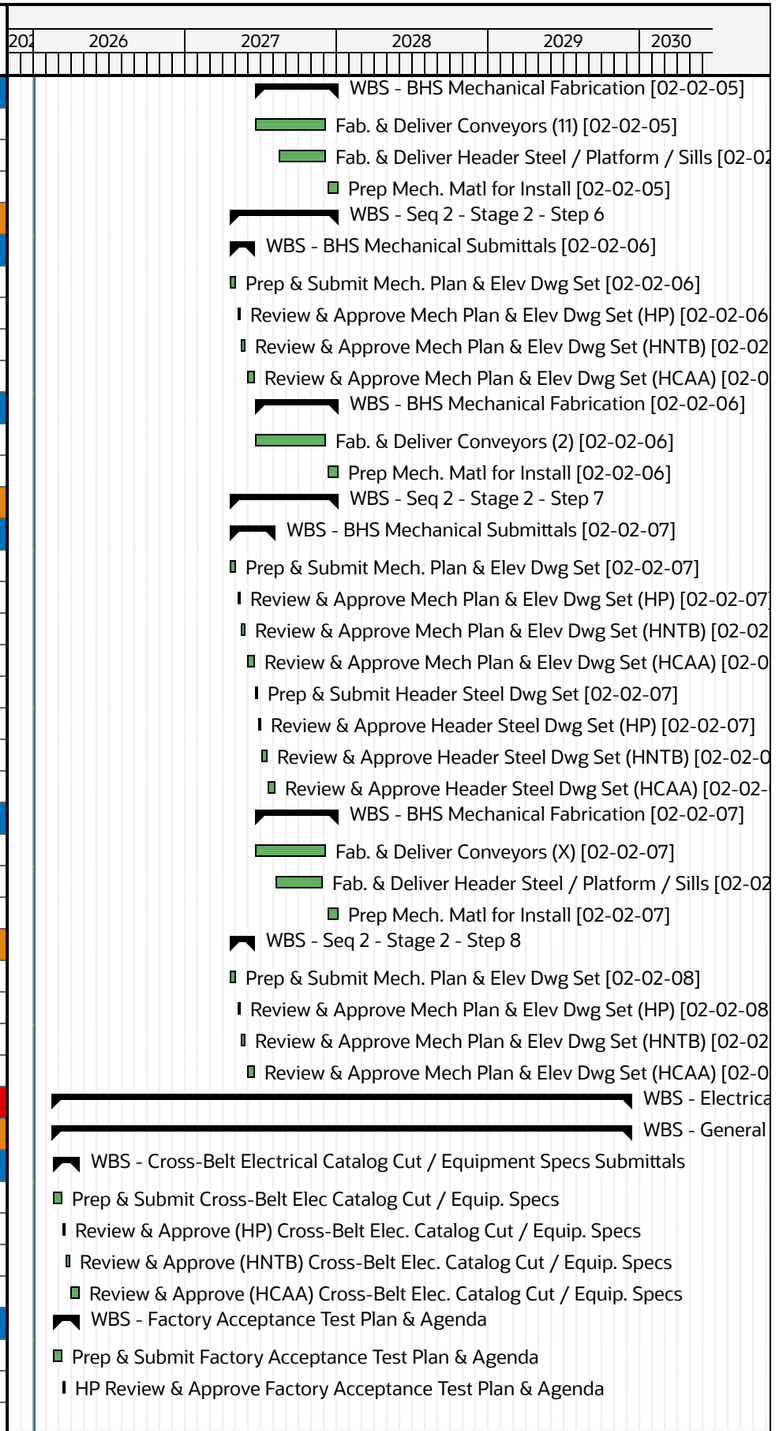


	ID	Name	Dur	Start	Finish	TF
12433	D5976	HNTB Review & Approve Factory Acceptance Test Plan & Agenda	10.0d	13-Mar-26	26-Mar-26	563.0d
12434	D1654	HCAA Review & Approve Factory Acceptance Test Plan & Agenda	15.0d	27-Mar-26	16-Apr-26	563.0d
12435	WBS - Final Electrical As-Built Drawings		70.0d	31-Aug-29	11-Dec-29	70.0d
12436	D1685	Prep & Submit Final Electrical As-Built Drawings	25.0d	31-Aug-29	5-Oct-29	70.0d
12437	D6226	Review & Approve (HP) Final Elec. As-Built Drawings	15.0d	8-Oct-29	26-Oct-29	70.0d
12438	D6236	Review & Approve (HNTB) Final Elec. As-Built Drawings	15.0d	29-Oct-29	16-Nov-29	70.0d
12439	D1686	Review & Approve (HCAA) Final Elec. As-Built Drawings	15.0d	19-Nov-29	11-Dec-29	70.0d
12440	WBS - Electrical & Controls Equipment Procurement		127.0d	11-Feb-26	10-Aug-26	353.0d
12441	D1656	Procure BHS Control Room Equip.	40.0d	11-Feb-26	7-Apr-26	373.0d
12442	D1657	Procure BHS Server Room Equip.	40.0d	11-Feb-26	7-Apr-26	373.0d
12443	D1658	Procure PLC Enclosure(s) Equip.	40.0d	11-Feb-26	7-Apr-26	373.0d
12444	D1659	Procure CBRA Room Computer Equip.	40.0d	11-Feb-26	7-Apr-26	373.0d
12445	D1660	Procure OSR Room Computer Equip.	40.0d	11-Feb-26	7-Apr-26	373.0d
12446	D1661	Procure CBIS Area Status Displays	40.0d	11-Feb-26	7-Apr-26	373.0d
12447	D1662	Procure Manual Encode Consoles	40.0d	11-Feb-26	7-Apr-26	373.0d
12448	D1678	Procure Cross Belt Sorter PLC Enclosures	40.0d	11-Feb-26	7-Apr-26	373.0d
12449	D1675	Procure Cross Belt Induction Units 2-Head ATR & BMA Equip. (13 for XBM1, 13...	80.0d	17-Apr-26	10-Aug-26	209.0d
12450	D1676	Procure Cross Belt ATR & BMA Equip. (4 for XBM1, 4 for XBM2)	80.0d	17-Apr-26	10-Aug-26	209.0d
12451	D1677	Procure Cross Belt Sorter Servers / Computers	40.0d	17-Apr-26	12-Jun-26	393.0d
12452	WBS - Seq 1 - Stage 3 - Step 1		224.0d	20-Mar-26	5-Feb-27	681.0d
12453	WBS - Sector J		95.0d	20-Mar-26	3-Aug-26	123.0d
12454	D1710	Prep & Submit Elec. Drawings MPP-B13, FCP-B13 (Sector J) [01-03-01]	10.0d	20-Mar-26	2-Apr-26	83.0d
12455	D6246	Review & Approve (HP) Elec. Drawings MPP-B13, FCP-B13 (Sector J) [01-03-01]	15.0d	3-Apr-26	23-Apr-26	123.0d
12456	D6256	Review & Approve (HNTB) Elec. Drawings MPP-B13, FCP-B13 (Sector J) [01-03...	15.0d	24-Apr-26	14-May-26	123.0d
12457	D1711	Review & Approve (HCAA) Elec. Drawings MPP-B13, FCP-B13 (Sector J) [01-03...	15.0d	15-May-26	5-Jun-26	123.0d
12458	D1712	Fab. & Deliver MPP-B13, FCP-B13, Elect Field Devices, Cabling (Sector J) [01-0...	40.0d	8-Jun-26	3-Aug-26	123.0d
12459	WBS - Sector H		125.0d	1-May-26	27-Oct-26	63.0d
12460	D1713	Prep & Submit Elec. Drawings MPP / FCP (A2, A4, A5, B1, B4, B5, B14) (Sector ...	40.0d	1-May-26	26-Jun-26	63.0d
12461	D6266	Review & Approve (HP) Elec. Drawings MPP / FCP (A2, A4, A5, B1, B4, B5, B14)...	15.0d	29-Jun-26	20-Jul-26	63.0d
12462	D6276	Review & Approve (HNTB) Elec. Drawings MPP / FCP (A2, A4, A5, B1, B4, B5, B...	15.0d	21-Jul-26	10-Aug-26	63.0d
12463	D1714	Review & Approve (HCAA) Elec. Drawings MPP / FCP (A2, A4, A5, B1, B4, B5, B...	15.0d	11-Aug-26	31-Aug-26	63.0d
12464	D1715	Fab. & Deliver MPP / FCP (A2, A4, A5, B1, B4, B5, B14), Elect Field Devices, Cab...	40.0d	1-Sep-26	27-Oct-26	63.0d
12465	WBS - Sector G		115.0d	21-Jul-26	4-Jan-27	97.0d
12466	D1716	Prep & Submit Elec. Drawings MPP / FCP (A3, A6, A7, B3, B6, B11) (Sector G) [...	30.0d	21-Jul-26	31-Aug-26	97.0d
12467	D6286	Review & Approve (HP) Elec. Drawings MPP / FCP (A3, A6, A7, B3, B6, B11) (Se...	15.0d	1-Sep-26	22-Sep-26	97.0d
12468	D6296	Review & Approve (HNTB) Elec. Drawings MPP / FCP (A3, A6, A7, B3, B6, B11) ...	15.0d	23-Sep-26	13-Oct-26	97.0d
12469	D1717	Review & Approve (HCAA) Elec. Drawings MPP / FCP (A3, A6, A7, B3, B6, B11) ...	15.0d	14-Oct-26	3-Nov-26	97.0d
12470	D1718	Fab. & Deliver MPP / FCP (A3, A6, A7, B3, B6, B11) Elect Field Devices, Cabling ...	40.0d	4-Nov-26	4-Jan-27	97.0d
12471	WBS - TD1 & TD2 paths to ASD		109.0d	1-Sep-26	5-Feb-27	681.0d
12472	D1719	Prep & Submit Elec. Drawings MPP / CSC (A18, A19, B18, B19) (TD1 / TD2) [0...	25.0d	1-Sep-26	6-Oct-26	680.0d
12473	D6306	Review & Approve (HP) Elec. Drawings MPP / CSC (A18, A19, B18, B19) (TD1 / ...	15.0d	7-Oct-26	27-Oct-26	680.0d
12474	D6316	Review & Approve (HNTB) Elec. Drawings MPP / CSC (A18, A19, B18, B19) (TD...	15.0d	28-Oct-26	17-Nov-26	680.0d

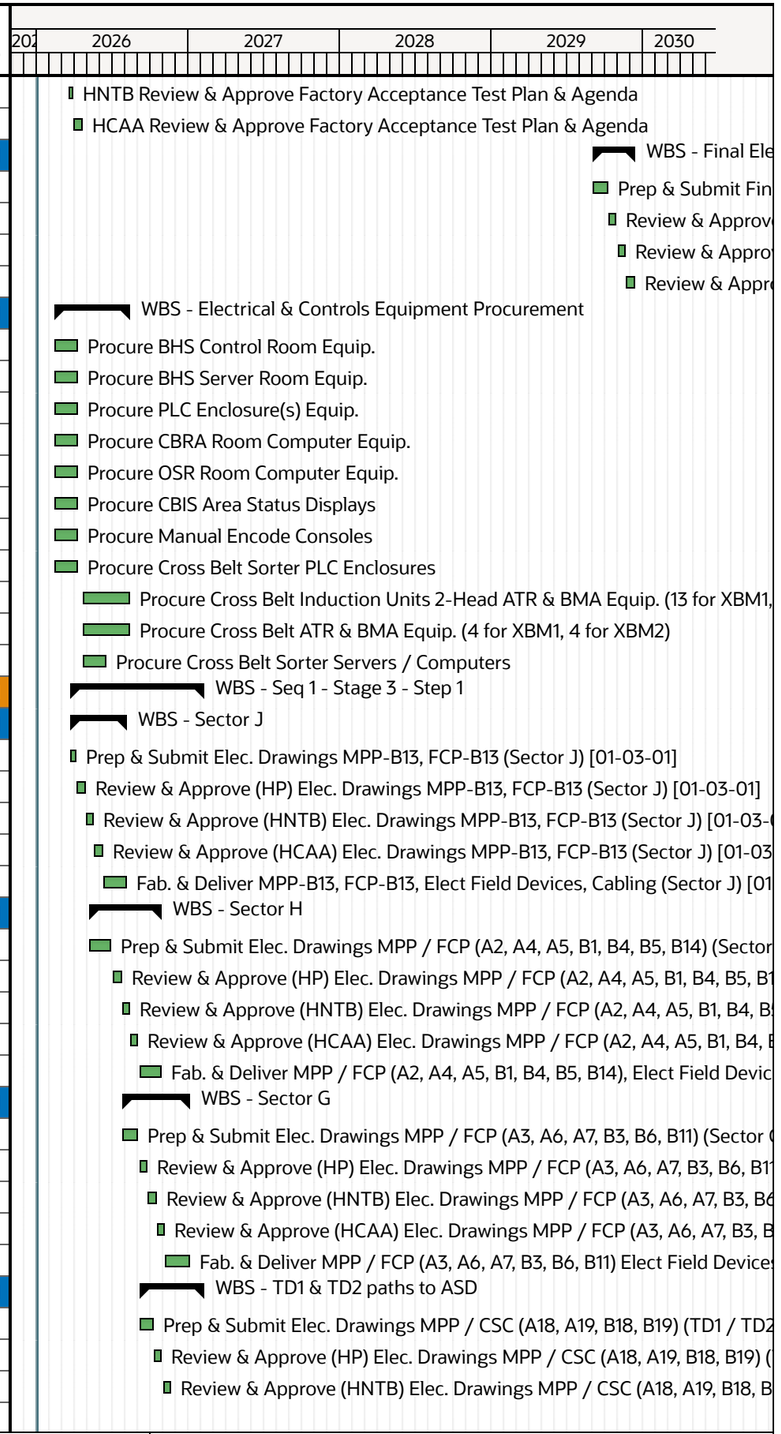


	ID	Name	Dur	Start	Finish	TF
12475	D1720	Review & Approve (HCAA) Elec. Drawings MPP / CSC (A18, A19, B18, B19) (TD...	15.0d	18-Nov-26	10-Dec-26	680.0d
12476	D1721	Fab. & Deliver MPP / CSC (A18, A19, B18, B19) Elect Field Devices, Cabling (TD...	39.0d	11-Dec-26	5-Feb-27	680.0d
12477	WBS - Seq 1 - Stage 3 - Step 3		124.0d	16-Sep-26	12-Mar-27	460.0d
12478	D1722	Prep & Submit Elec. Drawings MPP / FCP (A10, A11, A14, A15, B12, B16) [01-...	30.0d	16-Sep-26	27-Oct-26	201.0d
12479	D6326	Review & Approve (HP) Elec. Drawings MPP / FCP (A10, A11, A14, A15, B12, B...	15.0d	28-Oct-26	17-Nov-26	460.0d
12480	D6336	Review & Approve (HNTB) Elec. Drawings MPP / FCP (A10, A11, A14, A15, B12...	15.0d	18-Nov-26	10-Dec-26	460.0d
12481	D1723	Review & Approve (HCAA) Elec. Drawings MPP / FCP (A10, A11, A14, A15, B12...	15.0d	11-Dec-26	4-Jan-27	460.0d
12482	D1724	Fab. & Deliver MPP / FCP (A10, A11, A14, A15, B12, B16), Elect Field Devices, ...	49.0d	5-Jan-27	12-Mar-27	460.0d
12483	WBS - Seq 1 - Stage 3 - Step 6-1		134.0d	28-Oct-26	7-May-27	201.0d
12484	D1725	Prep & Submit Elec. Drawings MPP / FCP (A8, A13, A16, B7, B10, B13, B15, B1...	39.0d	28-Oct-26	23-Dec-26	201.0d
12485	D6346	Review & Approve (HP) Elec. Drawings MPP / FCP (A8, A13, A16, B7, B10, B13,...	15.0d	24-Dec-26	15-Jan-27	201.0d
12486	D6356	Review & Approve (HNTB) Elec. Drawings MPP / FCP (A8, A13, A16, B7, B10, B...	15.0d	18-Jan-27	5-Feb-27	201.0d
12487	D1726	Review & Approve (HCAA) Elec. Drawings MPP / FCP (A8, A13, A16, B7, B10, B...	15.0d	8-Feb-27	26-Feb-27	201.0d
12488	D1727	Fab. & Deliver MPP / FCP (A8, A13, A16, B7, B10, B13, B15, B16), Elect Field D...	50.0d	1-Mar-27	7-May-27	201.0d
12489	WBS - Seq 2 - Stage 2 - Step 3C-1		105.0d	12-Apr-27	8-Sep-27	444.0d
12490	D1728	Prep & Submit Elec. Drawings MPP-AOS, FCP-AOS, MPP-BOS, FCP-BOS [02-02...	10.0d	12-Apr-27	23-Apr-27	443.0d
12491	D6366	Review & Approve (HP) Elec. Drawings MPP-AOS, FCP-AOS, MPP-BOS, FCP-BO...	15.0d	26-Apr-27	14-May-27	443.0d
12492	D6376	Review & Approve (HNTB) Elec. Drawings MPP-AOS, FCP-AOS, MPP-BOS, FCP-...	15.0d	17-May-27	7-Jun-27	443.0d
12493	D1729	Review & Approve (HCAA) Elec. Drawings MPP-AOS, FCP-AOS, MPP-BOS, FCP-...	15.0d	8-Jun-27	28-Jun-27	443.0d
12494	D1730	Fab. & Deliver MPP-AOS, FCP-AOS, MPP-BOS, FCP-BOS, Elect Field Devices, Ca...	50.0d	29-Jun-27	8-Sep-27	443.0d
12495	WBS - Software Development/Testing & Factory Acceptance Testing - Part 2 Supplement C Wave 1		233.0d	15-Apr-26	16-Mar-27	368.0d
12496	D1746	Software Development / Testing - Main Terminal FAT	60.0d	15-Apr-26	9-Jul-26	505.0d
12497	D1747	PLC Code Development - Main Terminal FAT	197.0d	15-Apr-26	25-Jan-27	368.0d
12498	D1748	Cross Belt Sorter Software & PLC Development / Testing - Main Terminal FAT	120.0d	15-Jun-26	3-Dec-26	393.0d
12499	D1749	Cross Belt Sorter Internal FAT - Main Terminal FAT	10.0d	4-Dec-26	17-Dec-26	393.0d
12500	D1750	Internal FAT - Main Terminal FAT	8.0d	26-Jan-27	4-Feb-27	368.0d
12501	D1751	Customer FAT - Main Terminal FAT	5.0d	5-Feb-27	11-Feb-27	368.0d
12502	D1752	FAT Remediation - Main Terminal FAT	9.0d	12-Feb-27	24-Feb-27	368.0d
12503	D1753	FAT Remediation / Customer Demonstration - Main Terminal FAT	4.0d	25-Feb-27	2-Mar-27	368.0d
12504	D1754	FAT Clean Up / Ship to Site - Main Terminal FAT	10.0d	3-Mar-27	16-Mar-27	368.0d
12505	WBS - Concrete Procurement SOG & SOMD - CCBS		55.0d	13-Feb-26	30-Apr-26	212.0d
12506	PR-P1-1C1-2480	Prep Concrete Submittal (Contractor)- CCBS	20.0d	13-Feb-26	12-Mar-26	212.0d
12507	PR-P1-1C1-2510	Review & Submit Concrete Submittal (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	212.0d
12508	PR-P1-1C1-2500	Review & Approve Concrete Submittal (HNTB) - CCBS	10.0d	27-Mar-26	9-Apr-26	212.0d
12509	PR-P1-1C1-2520	Review & Approve Concrete Submittal (HCAA) - CCBS	15.0d	10-Apr-26	30-Apr-26	212.0d
12510	PR-P1-1C1-2490	Concrete Mix Design Approved - CCBS	0.0d		30-Apr-26	212.0d
12511	WBS - Masonry Procurement - CCBS		95.0d	13-Feb-26	27-Jun-26	54.0d
12512	PR-P2-1C1-8030	Prep Masonry Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	54.0d
12513	PR-P2-1C1-8040	Review & Submit Masonry Submittals (HP) - CCBS	5.0d	27-Mar-26	2-Apr-26	54.0d
12514	PR-P2-1C1-8050	Review & Approve Masonry Submittals (HNTB) - CCBS	10.0d	3-Apr-26	16-Apr-26	54.0d
12515	PR-P2-1C1-8060	Review & Approve Masonry Submittals (HCAA) - CCBS	15.0d	17-Apr-26	7-May-26	54.0d
12516	PR-P2-1C1-8070	Fab. & Ship Masonry - CCBS	50.0d	8-May-26	27-Jun-26	76.0d

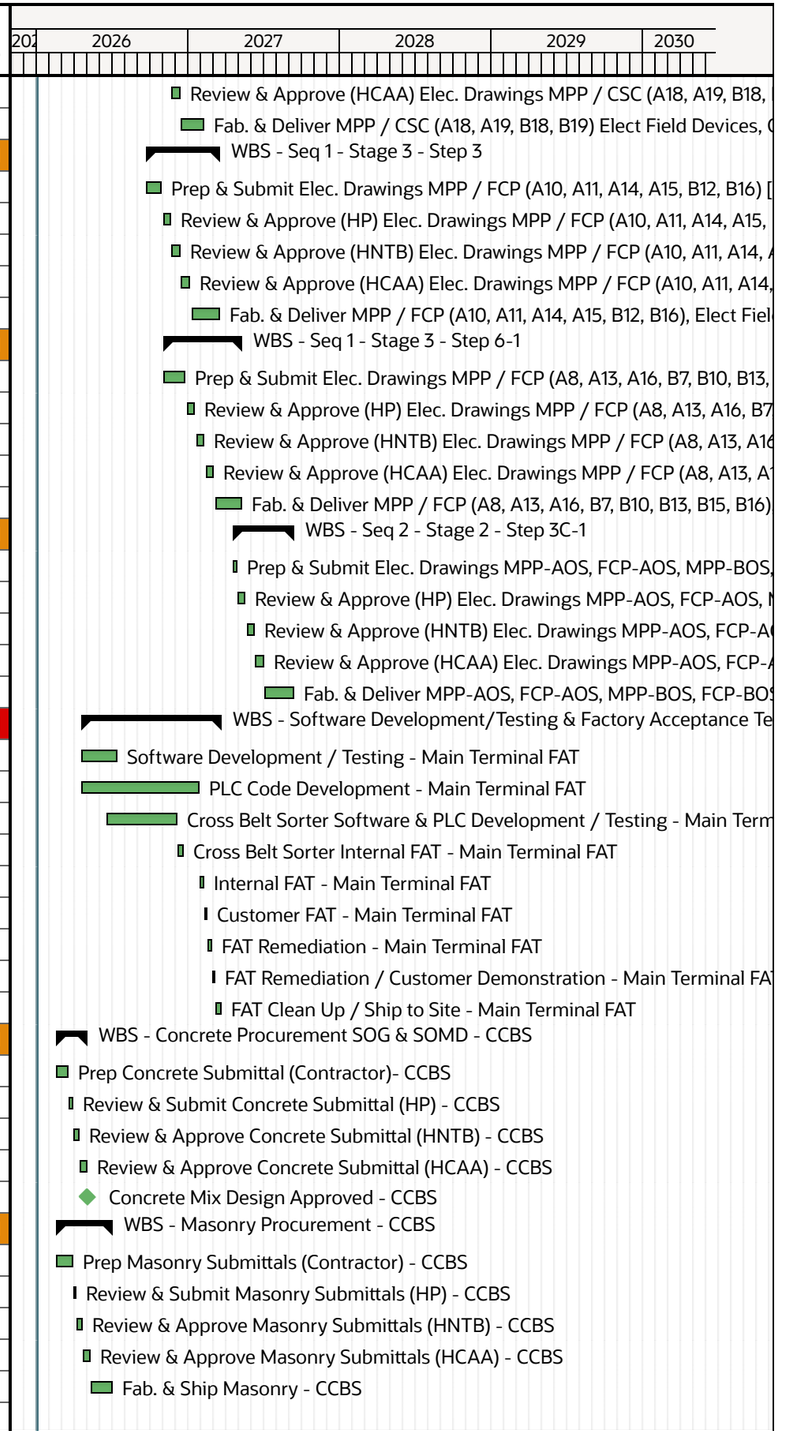


	ID	Name	Dur	Start	Finish	TF
12517	PR-P2-1C1-8080	Delivery of Masonry on Site - CCBS	0.0d		27-Jun-26	76.0d
12518	WBS - Wall & Door Protection Procurement - CCBS		93.0d	13-Feb-26	24-Jun-26	950.0d
12519	PR-P2-1C1-8090	Prep Wall & Door Protection Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	948.0d
12520	PR-P2-1C1-8100	Review & Submit Wall & Door Protection Submittals (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	948.0d
12521	PR-P2-1C1-8110	Review & Approve Wall & Door Protection Submittals (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	948.0d
12522	PR-P2-1C1-8120	Review & Approve Wall & Door Protection Submittals (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	948.0d
12523	PR-P2-1C1-8130	Fab. & Ship Wall & Door Protection - CCBS	40.0d	15-May-26	24-Jun-26	1,334.0d
12524	PR-P2-1C1-8140	Delivery of Wall & Door Protection on Site - CCBS	0.0d		24-Jun-26	1,334.0d
12525	WBS - Spray Fireproofing & Insulation (K-13) Procurement - CCBS		129.0d	13-Feb-26	16-Aug-26	914.0d
12526	PR-P1-1C1-2530	Prep Spray Fireproofing & Insulation Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	912.0d
12527	PR-P1-1C1-2810	Review & Submit Spray Fireproofing & Insulation Submittals (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	912.0d
12528	PR-P1-1C1-2560	Review & Approve Spray Fireproofing & Insulation Submittals (HNTB) - CCBS	10.0d	27-Mar-26	9-Apr-26	912.0d
12529	PR-P1-1C1-2820	Review & Approve Spray Fireproofing & Insulation Submittals (HCAA) - CCBS	15.0d	10-Apr-26	30-Apr-26	912.0d
12530	PR-P1-1C1-2540	Fab. & Ship Spray Fireproofing & Insulation - CCBS	105.0d	1-May-26	16-Aug-26	1,283.0d
12531	PR-P1-1C1-2550	Delivery of Spray Fireproofing & Insulation on Site - CCBS	0.0d		16-Aug-26	1,283.0d
12532	WBS - Back-Painted Glass Procurement - CCBS		160.0d	13-Feb-26	29-Sep-26	511.0d
12533	PR-P1-1C1-2570	Prep Back-Painted Glass Submittals (Contractor) - CCBS	40.0d	13-Feb-26	9-Apr-26	511.0d
12534	PR-P1-1C1-2830	Review & Submit Back-Painted Glass Submittals (HP) - CCBS	10.0d	10-Apr-26	23-Apr-26	511.0d
12535	PR-P1-1C1-2600	Review & Approve Back-Painted Glass Submittals (HNTB) - CCBS	10.0d	24-Apr-26	7-May-26	511.0d
12536	PR-P1-1C1-2840	Review & Approve Back-Painted Glass Submittals (HCAA) - CCBS	15.0d	8-May-26	29-May-26	511.0d
12537	PR-P1-1C1-2580	Fab. & Ship Back-Painted Glass - CCBS	120.0d	30-May-26	29-Sep-26	717.0d
12538	PR-P1-1C1-2590	Delivery of Back-Painted Glass on Site - CCBS	0.0d		29-Sep-26	717.0d
12539	WBS - Drywall & Related Procurement - CCBS		90.0d	13-Feb-26	19-Jun-26	717.0d
12540	PR-P1-1C1-2610	Prep Drywall & Related Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	717.0d
12541	PR-P1-1C1-2850	Review & Submit Drywall & Related Submittals (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	717.0d
12542	PR-P1-1C1-2640	Review & Approve Drywall & Related Submittals (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	717.0d
12543	PR-P1-1C1-2860	Review & Approve Drywall & Related Submittals (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	717.0d
12544	PR-P1-1C1-2620	Fab. & Ship Drywall & Related - CCBS	35.0d	15-May-26	19-Jun-26	1,008.0d
12545	PR-P1-1C1-2630	Delivery of Drywall & Related on Site - CCBS	0.0d		19-Jun-26	1,008.0d
12546	WBS - Acoustical Panel Ceilings Procurement - CCBS		111.0d	13-Feb-26	21-Jul-26	932.0d
12547	PR-P2-1C1-8220	Prep Acoustical Panel Ceilings Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	930.0d
12548	PR-P2-1C1-8580	Prep Acoustical Panel Ceiling Selective Demo Submittals (Contractor) - CCBS	5.0d	13-Feb-26	19-Feb-26	26.0d
12549	PR-P2-1C1-8590	Review & Submit Acoustical Panel Ceiling Selective Demo Submittals (HP) - CCBS	10.0d	20-Feb-26	5-Mar-26	26.0d
12550	PR-P2-1C1-8600	Review & Approve Acoustical Panel Ceiling Selective Demo Submittals (HNTB) -...	10.0d	6-Mar-26	19-Mar-26	26.0d
12551	PR-P2-1C1-8610	Review & Approve Acoustical Panel Ceiling Selective Demo Submittals (HCAA) -...	15.0d	20-Mar-26	9-Apr-26	26.0d
12552	PR-P2-1C1-8230	Review & Submit Acoustical Panel Ceilings Submittals (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	930.0d
12553	PR-P2-1C1-8240	Review & Approve Acoustical Panel Ceilings Submittals (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	930.0d
12554	PR-P2-1C1-8250	Review & Approve Acoustical Panel Ceilings Submittals (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	930.0d
12555	PR-P2-1C1-8260	Fab. & Ship Acoustical Panel Ceilings - CCBS	65.0d	15-May-26	21-Jul-26	1,309.0d
12556	PR-P2-1C1-8270	Delivery of Acoustical Panel Ceilings on Site - CCBS	0.0d		21-Jul-26	1,309.0d
12557	WBS - Fire Suppression Procurement - CCBS		100.0d	13-Feb-26	6-Jul-26	943.0d
12558	PR-P1-1C1-2650	Prep Fire Suppression Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	941.0d

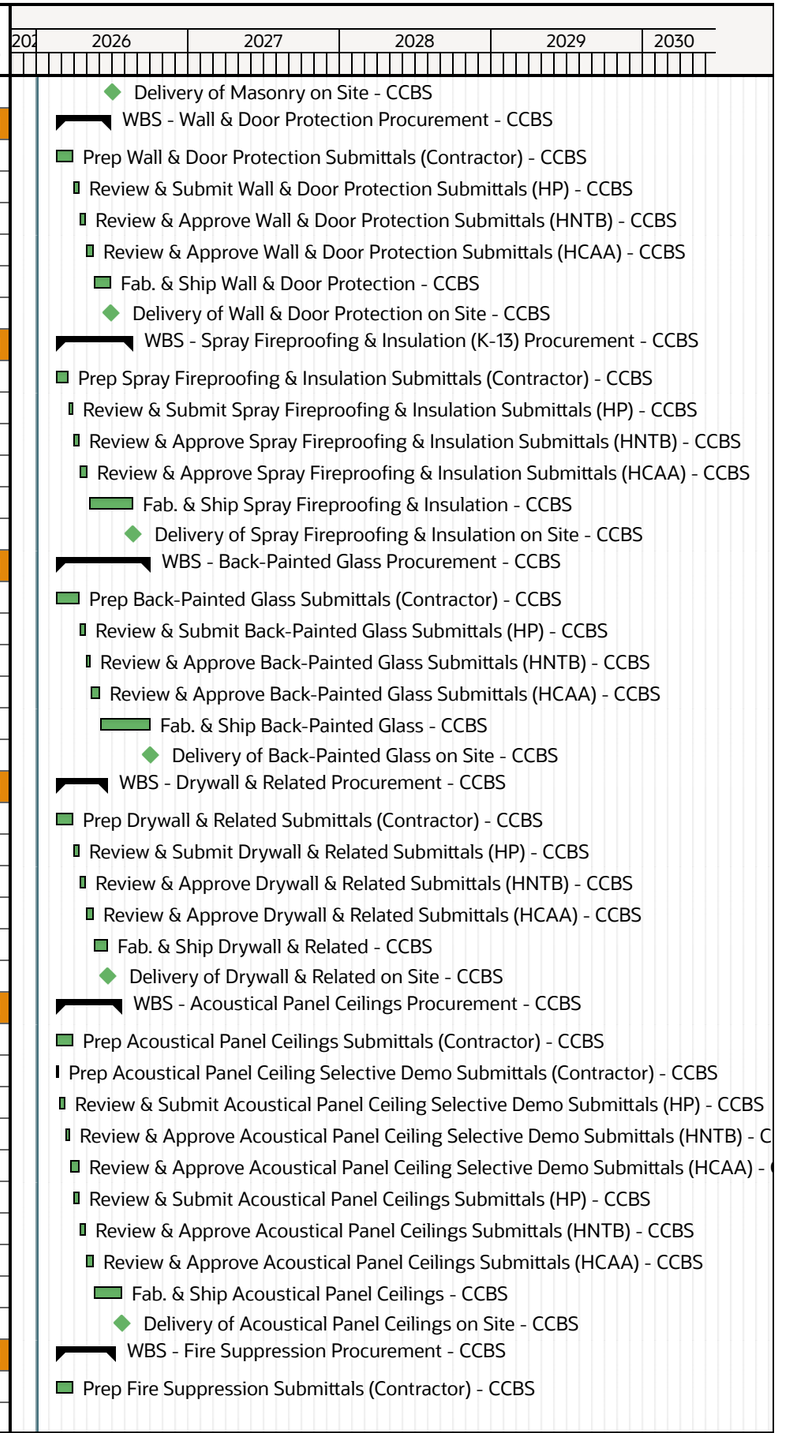

	ID	Name	Dur	Start	Finish	TF
12559	PR-P1-1C1-2870	Review & Submit Fire Suppression Submittals (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	941.0d
12560	PR-P1-1C1-2680	Review & Approve Fire Suppression Submittals (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	941.0d
12561	PR-P1-1C1-2880	Review & Approve Fire Suppression Submittals (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	941.0d
12562	PR-P1-1C1-2660	Fab. & Ship Fire Suppression - CCBS	50.0d	15-May-26	6-Jul-26	1,324.0d
12563	PR-P1-1C1-2670	Delivery of Fire Suppression on Site - CCBS	0.0d		6-Jul-26	1,324.0d
12564	WBS - Roadway Work (Sitework) Procurement - CCBS		85.0d	13-Feb-26	12-Jun-26	958.0d
12565	PR-P1-1C1-2770	Prep Roadway Work Submittals (Sitework) (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	957.0d
12566	PR-P1-1C1-2930	Review & Submit Roadway Work Submittals (Sitework) (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	957.0d
12567	PR-P1-1C1-2800	Review & Approve Roadway Work Submittals Structures (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	957.0d
12568	PR-P1-1C1-2940	Review & Approve Roadway Work Submittals (Sitework) (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	957.0d
12569	PR-P1-1C1-2780	Fab. & Ship Roadway Work Submittals - CCBS	28.0d	15-May-26	12-Jun-26	1,346.0d
12570	PR-P1-1C1-2790	Delivery of Roadway Materials on Site - CCBS	0.0d		12-Jun-26	1,346.0d
12571	WBS - Exterior Metal Framing - CCBS		108.0d	13-Feb-26	16-Jul-26	699.0d
12572	PR-P2-1C1-8150	Prep Exterior Metal Framing Submittals (Contractor) - CCBS	30.0d	13-Feb-26	26-Mar-26	700.0d
12573	PR-P2-1C1-8190	Review & Submit Exterior Metal Framing Submittals (HP) - CCBS	10.0d	27-Mar-26	9-Apr-26	700.0d
12574	PR-P2-1C1-8180	Review & Approve Exterior Metal Framing Submittals (HNTB) - CCBS	10.0d	10-Apr-26	23-Apr-26	700.0d
12575	PR-P2-1C1-8200	Review & Approve Exterior Metal Framing Submittals (HCAA) - CCBS	15.0d	24-Apr-26	14-May-26	700.0d
12576	PR-P2-1C1-8160	Fab. & Ship Exterior Metal Framing - CCBS	60.0d	15-May-26	16-Jul-26	983.0d
12577	PR-P2-1C1-8170	Delivery of Exterior Metal Framing on Site - CCBS	0.0d		16-Jul-26	983.0d
12578	WBS - Electrical Procurement - CCBS		98.0d	13-Feb-26	1-Jul-26	259.0d
12579	PR-P1-1C1-2690	Prep Elec Submittals (Contractor) - CCBS	15.0d	13-Feb-26	5-Mar-26	259.0d
12580	PR-P1-1C1-2890	Review & Submit Elec.Submittals (HP) - CCBS	5.0d	6-Mar-26	12-Mar-26	259.0d
12581	PR-P1-1C1-2720	Review & Approve Elec. Submittals (HNTB) - CCBS	10.0d	13-Mar-26	26-Mar-26	259.0d
12582	PR-P1-1C1-2900	Review & Approve Elec. Submittals (HCAA) - CCBS	15.0d	27-Mar-26	16-Apr-26	259.0d
12583	PR-P1-1C1-2700	Fab & Ship Electrical Panels - CCBS	75.0d	17-Apr-26	1-Jul-26	364.0d
12584	PR-P1-1C1-2710	Delivery of Electrical Panels on Site - CCBS	0.0d		1-Jul-26	364.0d
12585	WBS - Low Voltage System Procurement - CCBS		69.0d	13-Feb-26	20-May-26	18.0d
12586	PR-P1-1C1-2730	Prep Low Voltage System Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	18.0d
12587	PR-P1-1C1-2910	Review & Submit Low Voltage System Submittals (HP) - CCBS	10.0d	13-Mar-26	26-Mar-26	18.0d
12588	PR-P1-1C1-2760	Review & Approve Low Voltage System Submittals (HNTB) - CCBS	10.0d	27-Mar-26	9-Apr-26	18.0d
12589	PR-P1-1C1-2920	Review & Approve Low Voltage System Submittals (HCAA) - CCBS	15.0d	10-Apr-26	30-Apr-26	18.0d
12590	PR-P1-1C1-2740	Fab. & Ship Low Voltage System - CCBS	20.0d	1-May-26	20-May-26	26.0d
12591	PR-P1-1C1-2750	Delivery of Low Voltage System on Site - CCBS	0.0d		20-May-26	26.0d
12592	WBS - Demolition Safety Plan Submittal - CCBS		45.0d	13-Feb-26	16-Apr-26	68.0d
12593	PR-P2-1C1-8620	Prep Demolition Submittals (Contractor) - CCBS	10.0d	13-Feb-26	26-Feb-26	68.0d
12594	PR-P2-1C1-8630	Review & Submit Demolition Submittals (HP) - CCBS	10.0d	27-Feb-26	12-Mar-26	68.0d
12595	PR-P2-1C1-8640	Review & Approve Demolition Submittals (HNTB) - CCBS	10.0d	13-Mar-26	26-Mar-26	68.0d
12596	PR-P2-1C1-8650	Review & Approve Demolition Submittals (HCAA) - CCBS	15.0d	27-Mar-26	16-Apr-26	68.0d
12597	WBS - Ductwork/Mechanical Systems - CCBS		83.0d	13-Feb-26	10-Jun-26	960.0d
12598	PR-P2-1C1-8340	Prep Ductwork/Mech. Systems Submittals (Contractor) - CCBS	25.0d	13-Feb-26	19-Mar-26	958.0d
12599	PR-P2-1C1-8350	Review & Submit Ductwork/Mech. Systems Submittals (HP) - CCBS	5.0d	20-Mar-26	26-Mar-26	958.0d
12600	PR-P2-1C1-8360	Review & Approve Ductwork/Mech. Systems Submittals (HNTB) - CCBS	10.0d	27-Mar-26	9-Apr-26	958.0d

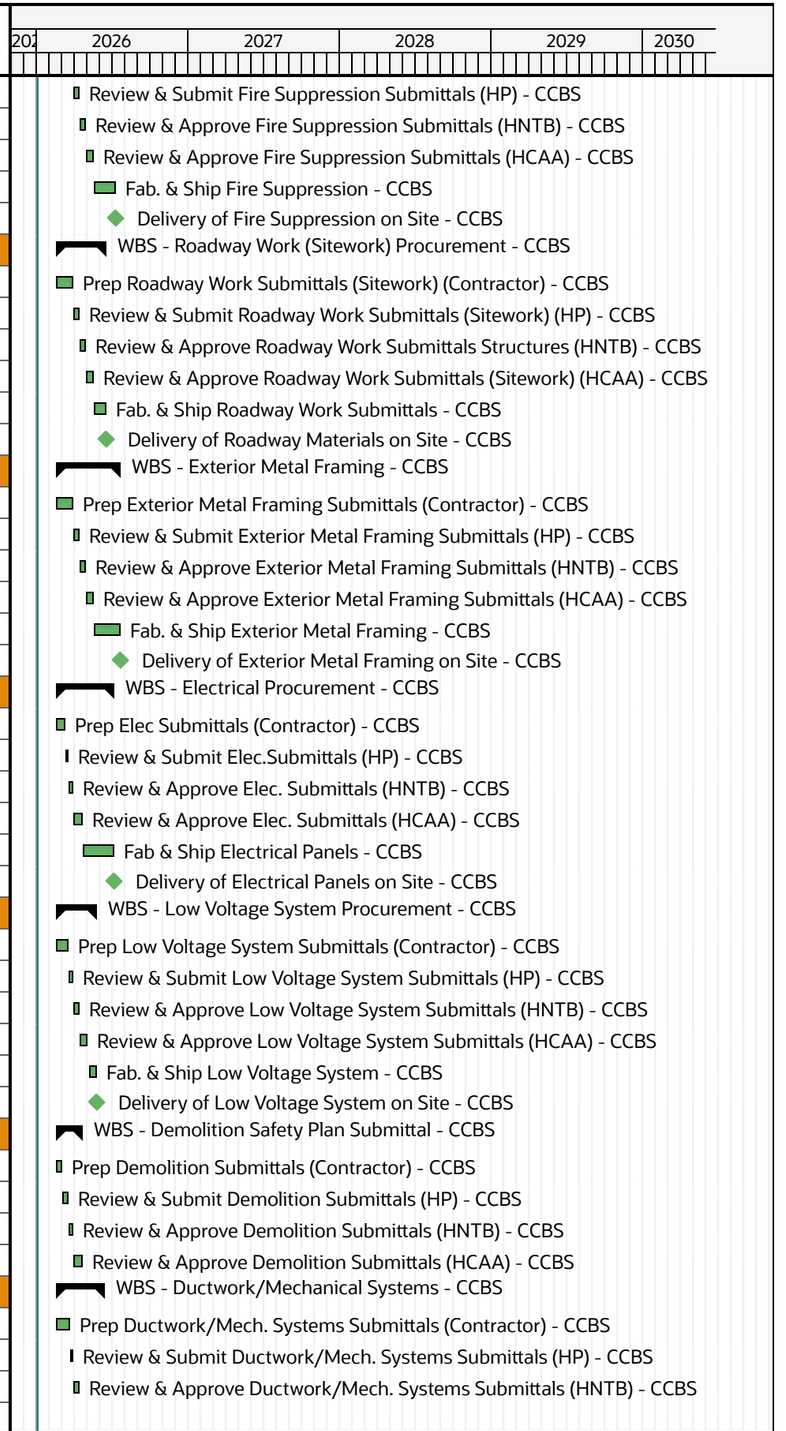

	ID	Name	Dur	Start	Finish	TF
12601	PR-P2-1C1-8370	Review & Approve Ductwork/Mech. Systems Submittals (HCAA) - CCBS	15.0d	10-Apr-26	30-Apr-26	958.0d
12602	PR-P2-1C1-8380	Fab. & Ship Ductwork/Mech. Systems - CCBS	40.0d	1-May-26	10-Jun-26	1,348.0d
12603	PR-P2-1C1-8390	Delivery of Ductwork/Mech. Systems on Site - CCBS	0.0d		10-Jun-26	1,348.0d
12604	WBS - Plumbing Systems - CCBS		88.0d	13-Feb-26	17-Jun-26	955.0d
12605	PR-P2-1C1-8460	Prep Plumbing Systems Submittals (Contractor) - CCBS	25.0d	13-Feb-26	19-Mar-26	953.0d
12606	PR-P2-1C1-8470	Review & Submit Plumbing Systems Submittals (HP) - CCBS	10.0d	20-Mar-26	2-Apr-26	953.0d
12607	PR-P2-1C1-8480	Review & Approve Plumbing Systems Submittals (HNTB) - CCBS	10.0d	3-Apr-26	16-Apr-26	953.0d
12608	PR-P2-1C1-8490	Review & Approve Plumbing Systems Submittals (HCAA) - CCBS	15.0d	17-Apr-26	7-May-26	953.0d
12609	PR-P2-1C1-8500	Fab. & Ship Plumbing Systems - CCBS	40.0d	8-May-26	17-Jun-26	1,341.0d
12610	PR-P2-1C1-8510	Delivery of Plumbing Systems on Site - CCBS	0.0d		17-Jun-26	1,341.0d
12611	WBS - Carbon Fiber Reinforcement Polymer (CFRP) - CCBS		59.0d	29-Dec-25	21-Mar-26	65.0d
12612	PR-P2-1C1-8520	Prep CFRP Submittals (Contractor) - CCBS	25.0d	29-Dec-25	2-Feb-26	54.0d
12613	PR-P2-1C1-8530	Review & Submit CFRP Submittals (HP) - CCBS	5.0d	3-Feb-26	9-Feb-26	54.0d
12614	PR-P2-1C1-8540	Review & Approve CFRP Submittals (HNTB) - CCBS	10.0d	10-Feb-26	23-Feb-26	54.0d
12615	PR-P2-1C1-8550	Review & Approve CFRP Submittals (HCAA) - CCBS	15.0d	24-Feb-26	16-Mar-26	54.0d
12616	PR-P2-1C1-8560	Fab. & Ship CFRP Systems - CCBS	5.0d	17-Mar-26	21-Mar-26	92.0d
12617	PR-P2-1C1-8570	Delivery of CFRP on Site - CCBS	0.0d		21-Mar-26	92.0d
12618	WBS - Structural Steel Procurement - CCBS		168.0d	20-Feb-26	18-Oct-26	296.0d
12619	WBS - Structural Steel Procurement - T17 [01-01-04]		88.0d	20-Feb-26	24-Jun-26	58.0d
12620	BG-PR-2C-ST-210	Prep T17 Structural Steel Detailed Drawings (Contractor) [01-01-04]	20.0d	20-Feb-26	19-Mar-26	58.0d
12621	BG-PR-2C-ST-250	Review & Submit T17 Structural Steel Detailed Drawings (HP) [01-01-04]	5.0d	20-Mar-26	26-Mar-26	58.0d
12622	BG-PR-2C-ST-220	Review & Approve T17 Structural Steel Detailed Drawings (HNTB) [01-01-04]	10.0d	27-Mar-26	9-Apr-26	58.0d
12623	BG-PR-2C-ST-230	Review & Approve T17 Structural Steel Detailed Drawings (HCAA) [01-01-04]	15.0d	10-Apr-26	30-Apr-26	58.0d
12624	BG-PR-2C-ST-240	Detailer Review & Clean Up T17 Structural Steel Detailed Drawings (Contractor)...	10.0d	1-May-26	14-May-26	58.0d
12625	BG-PR-2C-ST-260	Fab. & Ship T17 Structural Steel Structural Steel [01-01-04]	40.0d	15-May-26	24-Jun-26	81.0d
12626	WBS - Structural Steel Procurement - T16 [01-01-05]		89.0d	20-Mar-26	24-Jul-26	242.0d
12627	BG-PR-2C-ST-270	Prep T16 Detailed Drawings (Contractor) [01-01-05]	20.0d	20-Mar-26	16-Apr-26	181.0d
12628	BG-PR-2C-ST-280	Review & Submit T16 Detailed Drawings (HP) [01-01-05]	5.0d	17-Apr-26	23-Apr-26	242.0d
12629	BG-PR-2C-ST-290	Review & Approve T16 Detailed Drawings (HNTB) [01-01-05]	10.0d	24-Apr-26	7-May-26	242.0d
12630	BG-PR-2C-ST-300	Review & Approve T16 Detailed Drawings (HCAA) [01-01-05]	15.0d	8-May-26	29-May-26	242.0d
12631	BG-PR-2C-ST-310	Detailer Review & Clean Up T16 Detailed Drawings (Contractor) [01-01-05]	10.0d	1-Jun-26	12-Jun-26	242.0d
12632	BG-PR-2C-ST-320	Fab. & Ship T16 Structural Steel [01-01-05]	40.0d	13-Jun-26	24-Jul-26	340.0d
12633	WBS - Structural Steel Procurement - XBM-R [01-03-01]		89.0d	17-Apr-26	22-Aug-26	180.0d
12634	BG-PR-2C-ST-330	Prep XBM-R Detailed Drawings (Contractor) [01-03-01]	20.0d	17-Apr-26	14-May-26	181.0d
12635	BG-PR-2C-ST-340	Review & Submit XBM-R Detailed Drawings (HP) [01-03-01]	5.0d	15-May-26	21-May-26	181.0d
12636	BG-PR-2C-ST-350	Review & Approve XBM-R Detailed Drawings (HNTB) [01-03-01]	10.0d	22-May-26	5-Jun-26	181.0d
12637	BG-PR-2C-ST-360	Review & Approve XBM-R Detailed Drawings (HCAA) [01-03-01]	15.0d	8-Jun-26	26-Jun-26	181.0d
12638	BG-PR-2C-ST-370	Detailer Review & Clean Up XBM-R Detailed Drawings (Contractor) [01-03-01]	10.0d	29-Jun-26	13-Jul-26	181.0d
12639	BG-PR-2C-ST-380	Fab. & Ship XBM-R Structural Steel [01-03-01]	40.0d	14-Jul-26	22-Aug-26	255.0d
12640	WBS - Structural Steel Procurement - Drive Aisle [01-03-01]		88.0d	15-May-26	20-Sep-26	315.0d
12641	BG-PR-2C-ST-390	Prep Drive Aisle Detailed Drawings (Contractor) [01-03-01]	20.0d	15-May-26	12-Jun-26	296.0d
12642	BG-PR-2C-ST-400	Review & Submit Drive Aisle Detailed Drawings (HP) [01-03-01]	5.0d	15-Jun-26	19-Jun-26	315.0d

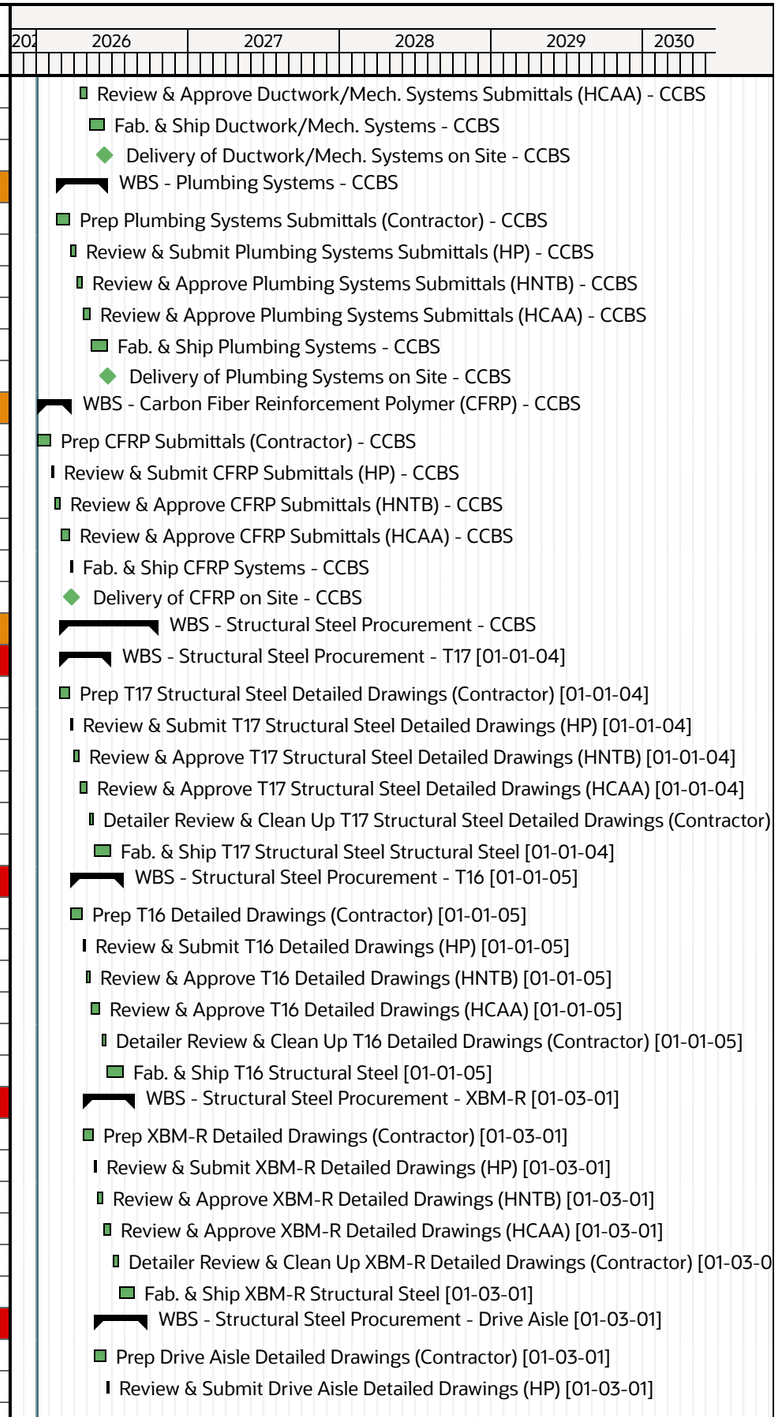


HENSEL PHELPS
Plan. Build. Manage.

Airside D - Tampa International Airport
ASD Development Program
Overall Project Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 12:11 p.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


ID	Name	Dur	Start	Finish	TF
12643	BG-PR-2C-ST-410 Review & Approve Drive Aisle Detailed Drawings (HNTB) [01-03-01]	10.0d	22-Jun-26	6-Jul-26	315.0d
12644	BG-PR-2C-ST-420 Review & Approve Drive Aisle Detailed Drawings (HCAA) [01-03-01]	15.0d	7-Jul-26	27-Jul-26	315.0d
12645	BG-PR-2C-ST-430 Detailer Review & Clean Up Drive Aisle Detailed Drawings (Contractor) [01-03-01]	10.0d	28-Jul-26	10-Aug-26	315.0d
12646	BG-PR-2C-ST-440 Fab. & Ship Drive Aisle Structural Steel [01-03-01]	40.0d	11-Aug-26	20-Sep-26	441.0d
12647	WBS - Structural Steel Procurement - XBM-B [01-03-06]	88.0d	15-Jun-26	18-Oct-26	296.0d
12648	BG-PR-2C-ST-450 Prep XBM-B Detailed Drawings (Contractor) [01-03-06]	20.0d	15-Jun-26	13-Jul-26	296.0d
12649	BG-PR-2C-ST-460 Review & Submit XBM-B Detailed Drawings (HP) [01-03-06]	5.0d	14-Jul-26	20-Jul-26	296.0d
12650	BG-PR-2C-ST-470 Review & Approve XBM-B Detailed Drawings (HNTB) [01-03-06]	10.0d	21-Jul-26	3-Aug-26	296.0d
12651	BG-PR-2C-ST-480 Review & Approve XBM-B Detailed Drawings (HCAA) [01-03-06]	15.0d	4-Aug-26	24-Aug-26	296.0d
12652	BG-PR-2C-ST-490 Detailer Review & Clean Up XBM-B Detailed Drawings (Contractor) [01-03-06]	10.0d	25-Aug-26	8-Sep-26	296.0d
12653	BG-PR-2C-ST-500 Fab. & Ship XBM-B Structural Steel [01-03-06]	40.0d	9-Sep-26	18-Oct-26	416.0d
12654	WBS - Part 2 Supplement C Wave 2 - Finishes Procurement	202.0d	13-Feb-26	30-Nov-26	841.0d
12655	WBS - Metal Doors, Frames, Hardware Procurement - CCBS	54.0d	6-Apr-26	21-Jun-26	19.0d
12656	PR-P1-1C1-2950 Prep Metal Doors, Frames, Hardware Submittals (Contractor) - CCBS	10.0d	6-Apr-26	17-Apr-26	19.0d
12657	PR-P1-1C1-2960 Review & Submit Metal Doors, Frames, Hardware Submittals (HP) - CCBS	5.0d	20-Apr-26	24-Apr-26	19.0d
12658	PR-P1-1C1-2970 Review & Approve Metal Doors, Frames, Hardware Submittals (HNTB) - CCBS	10.0d	27-Apr-26	8-May-26	19.0d
12659	PR-P1-1C1-2980 Review & Approve Metal Doors, Frames, Hardware Submittals (HCAA) - CCBS	15.0d	11-May-26	1-Jun-26	19.0d
12660	PR-P1-1C1-2990 Fab. & Ship Metal Doors, Frames, Hardware - CCBS	20.0d	2-Jun-26	21-Jun-26	26.0d
12661	PR-P1-1C1-3000 Delivery of Metal Doors, Frames, Hardware on Site - CCBS	0.0d		21-Jun-26	26.0d
12662	WBS - Airport Access Controls Procurement - CCBS	78.0d	13-Feb-26	3-Jun-26	9.0d
12663	PR-P2-1C2-8160 Prep Airport Access Controls Submittals (Contractor) - CCBS	20.0d	13-Feb-26	12-Mar-26	9.0d
12664	PR-P2-1C2-8170 Review & Submit Airport Access Controls Submittals (HP) - CCBS	5.0d	13-Mar-26	19-Mar-26	9.0d
12665	PR-P2-1C2-8180 Review & Approve Airport Access Controls Submittals (HNTB) - CCBS	10.0d	20-Mar-26	2-Apr-26	9.0d
12666	PR-P2-1C2-8190 Review & Approve Airport Access Controls Submittals (HCAA) - CCBS	15.0d	3-Apr-26	23-Apr-26	9.0d
12667	PR-P2-1C2-8200 Fab. & Ship Airport Access Controls - CCBS	40.0d	24-Apr-26	3-Jun-26	13.0d
12668	PR-P2-1C2-8210 Delivery of Airport Access Controls on Site - CCBS	0.0d		3-Jun-26	13.0d
12669	WBS - Architectural Millwork Procurement - CCBS	164.0d	8-Apr-26	30-Nov-26	841.0d
12670	PR-P2-1C2-7900 Prep Architectural Millwork Submittals (Contractor) - CCBS	30.0d	8-Apr-26	19-May-26	839.0d
12671	PR-P2-1C2-8100 Review & Submit Architectural Millwork Submittals (HP) - CCBS	10.0d	20-May-26	3-Jun-26	839.0d
12672	PR-P2-1C2-7930 Review & Approve Architectural Millwork Submittals (HNTB) - CCBS	10.0d	4-Jun-26	17-Jun-26	839.0d
12673	PR-P2-1C2-8110 Review & Approve Architectural Millwork Submittals (HCAA) - CCBS	15.0d	18-Jun-26	9-Jul-26	839.0d
12674	PR-P2-1C2-7910 Fab. & Ship Architectural Millwork - CCBS	141.0d	10-Jul-26	30-Nov-26	1,180.0d
12675	PR-P2-1C2-7920 Delivery of Architectural Millwork on Site - CCBS	0.0d		30-Nov-26	1,180.0d
12676	WBS - Overhead Coiling Doors Procurement - CCBS	93.0d	9-Apr-26	19-Aug-26	911.0d
12677	PR-P2-1C2-8020 Prep Overhead Coiling Doors Submittals (Contractor) - CCBS	30.0d	9-Apr-26	20-May-26	909.0d
12678	PR-P2-1C2-8340 Review & Submit Overhead Coiling Doors Submittals (HP) - CCBS	10.0d	21-May-26	4-Jun-26	909.0d
12679	PR-P2-1C2-8050 Review & Approve Overhead Coiling Doors Submittals (HNTB) - CCBS	10.0d	5-Jun-26	18-Jun-26	909.0d
12680	PR-P2-1C2-8350 Review & Approve Overhead Coiling Doors Submittals (HCAA) - CCBS	15.0d	19-Jun-26	10-Jul-26	909.0d
12681	PR-P2-1C2-8030 Fab. & Ship Overhead Coiling Doors - CCBS	40.0d	11-Jul-26	19-Aug-26	1,280.0d
12682	PR-P2-1C2-8040 Delivery of Overhead Coiling Doors on Site - CCBS	0.0d		19-Aug-26	1,280.0d
12683	WBS - Tile & Stone Procurement - CCBS	107.0d	14-Apr-26	14-Sep-26	382.0d
12684	PR-P2-1C2-8280 Prep Tile & Stone Submittals (Contractor) - CCBS	30.0d	14-Apr-26	26-May-26	380.0d

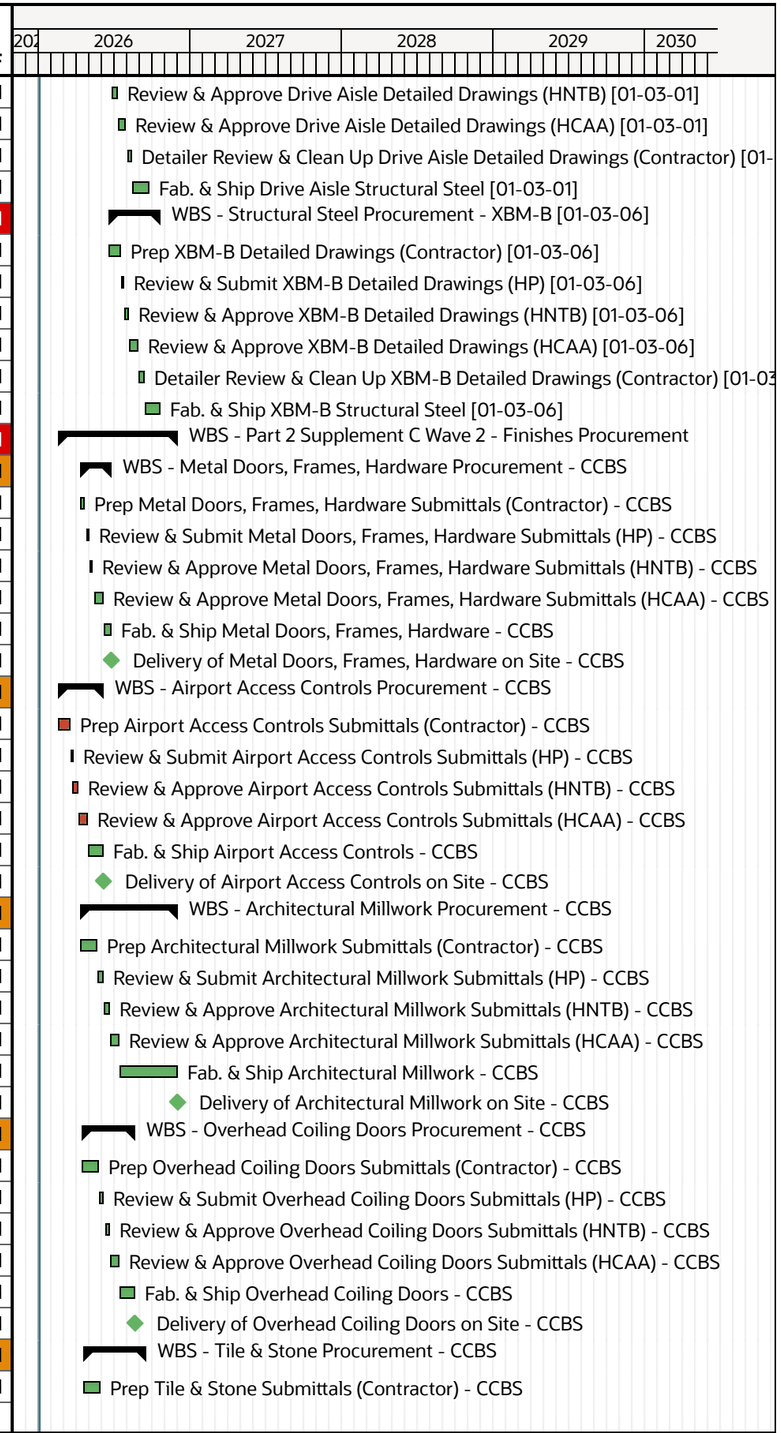


	ID	Name	Dur	Start	Finish	TF
12685	PR-P2-1C2-8290	Review & Submit Tile & Stone Submittals (HP) - CCBS	10.0d	27-May-26	9-Jun-26	380.0d
12686	PR-P2-1C2-8300	Review & Approve Tile & Stone Submittals (HNTB) - CCBS	10.0d	10-Jun-26	23-Jun-26	380.0d
12687	PR-P2-1C2-8310	Review & Approve Tile & Stone Submittals (HCAA) - CCBS	15.0d	24-Jun-26	15-Jul-26	380.0d
12688	PR-P2-1C2-8320	Fab. & Ship Tile & Stone - CCBS	60.0d	16-Jul-26	14-Sep-26	534.0d
12689	PR-P2-1C2-8330	Delivery of Tile & Stone on Site - CCBS	0.0d		14-Sep-26	534.0d
12690	WBS - Flooring Procurement - CCBS		48.0d	7-Apr-26	12-Jun-26	17.0d
12691	PR-P2-1C2-8220	Prep Flooring Submittals (Contractor) - CCBS	10.0d	7-Apr-26	20-Apr-26	18.0d
12692	PR-P2-1C2-8230	Review & Submit Flooring Submittals (HP) - CCBS	5.0d	21-Apr-26	27-Apr-26	18.0d
12693	PR-P2-1C2-8240	Review & Approve Flooring Submittals (HNTB) - CCBS	10.0d	28-Apr-26	11-May-26	18.0d
12694	PR-P2-1C2-8250	Review & Approve Flooring Submittals (HCAA) - CCBS	15.0d	12-May-26	2-Jun-26	18.0d
12695	PR-P2-1C2-8260	Fab. & Ship Flooring - CCBS	10.0d	3-Jun-26	12-Jun-26	24.0d
12696	PR-P2-1C2-8270	Delivery of Flooring on Site - CCBS	0.0d		12-Jun-26	24.0d
12697	WBS - Specialty Flooring Procurement - CCBS		107.0d	7-Apr-26	6-Sep-26	899.0d
12698	PR-P2-1C2-8380	Prep Specialty Flooring Submittals (Contractor) - CCBS	30.0d	7-Apr-26	18-May-26	896.0d
12699	PR-P2-1C2-8390	Review & Submit Specialty Flooring Submittals (HP) - CCBS	10.0d	19-May-26	2-Jun-26	896.0d
12700	PR-P2-1C2-8400	Review & Approve Specialty Flooring Submittals (HNTB) - CCBS	10.0d	3-Jun-26	16-Jun-26	896.0d
12701	PR-P2-1C2-8410	Review & Approve Specialty Flooring Submittals (HCAA) - CCBS	15.0d	17-Jun-26	8-Jul-26	896.0d
12702	PR-P2-1C2-8420	Fab. & Ship Specialty Flooring - CCBS	60.0d	9-Jul-26	6-Sep-26	1,262.0d
12703	PR-P2-1C2-8430	Delivery of Specialty Flooring on Site - CCBS	0.0d		6-Sep-26	1,262.0d
12704	WBS - Paints & Wall Coverings Procurement - CCBS		43.0d	21-Apr-26	21-Jun-26	22.0d
12705	PR-P2-1C2-7940	Prep Paints & Wall Coverings Submittals (Contractor) - CCBS	10.0d	21-Apr-26	4-May-26	22.0d
12706	PR-P2-1C2-8120	Review & Submit Paints & Wall Coverings Submittals (HP) - CCBS	5.0d	5-May-26	11-May-26	22.0d
12707	PR-P2-1C2-7950	Review & Approve Paints & Wall Coverings (HNTB) - CCBS	10.0d	12-May-26	26-May-26	22.0d
12708	PR-P2-1C2-7970	Review & Approve Paints & Wall Coverings (HCAA) - CCBS	15.0d	27-May-26	16-Jun-26	22.0d
12709	PR-P2-1C2-8150	Fab. & Ship Paints & Wall Coverings - CCBS	5.0d	17-Jun-26	21-Jun-26	29.0d
12710	PR-P2-1C2-7960	Delivery of Paints & Wall Coverings on Site - CCBS	0.0d		21-Jun-26	29.0d
12711	WBS - Signage Procurement - CCBS		82.0d	15-Apr-26	10-Aug-26	398.0d
12712	PR-P2-1C2-8060	Prep Signage Submittals (Contractor) - CCBS	30.0d	15-Apr-26	27-May-26	398.0d
12713	PR-P2-1C2-8360	Review & Submit Signage Submittals (HP) - CCBS	10.0d	28-May-26	10-Jun-26	398.0d
12714	PR-P2-1C2-8090	Review & Approve Signage Submittals (HNTB) - CCBS	10.0d	11-Jun-26	24-Jun-26	398.0d
12715	PR-P2-1C2-8370	Review & Approve Signage Submittals (HCAA) - CCBS	15.0d	25-Jun-26	16-Jul-26	398.0d
12716	PR-P2-1C2-8070	Fab. & Ship Signage - CCBS	25.0d	17-Jul-26	10-Aug-26	558.0d
12717	PR-P2-1C2-8080	Delivery of Signage on Site - CCBS	0.0d		10-Aug-26	558.0d
12718	WBS - Wire Mesh Partitions Procurement - CCBS		83.0d	29-Apr-26	25-Aug-26	907.0d
12719	PR-P2-1C2-7980	Prep Wire Mesh Partitions Submittals (Contractor) - CCBS	20.0d	29-Apr-26	27-May-26	905.0d
12720	PR-P2-1C2-8130	Review & Submit Wire Mesh Partitions Submittals (HP) - CCBS	10.0d	28-May-26	10-Jun-26	905.0d
12721	PR-P2-1C2-8010	Review & Approve Wire Mesh Partitions Submittals (HNTB) - CCBS	10.0d	11-Jun-26	24-Jun-26	905.0d
12722	PR-P2-1C2-8140	Review & Approve Wire Mesh Partitions Submittals (HCAA) - CCBS	15.0d	25-Jun-26	16-Jul-26	905.0d
12723	PR-P2-1C2-8000	Fab. & Ship Wire Mesh Partitions - CCBS	40.0d	17-Jul-26	25-Aug-26	1,274.0d
12724	PR-P2-1C2-7990	Delivery of Wire Mesh Partitions on Site - CCBS	0.0d		25-Aug-26	1,274.0d
12725	WBS - CCBS - CONSTRUCTION PHASE		993.0d	20-Oct-25 A	14-Sep-29	130.0d
12726	WBS - Main Terminal CCBS Consolidation		993.0d	20-Oct-25 A	14-Sep-29	130.0d

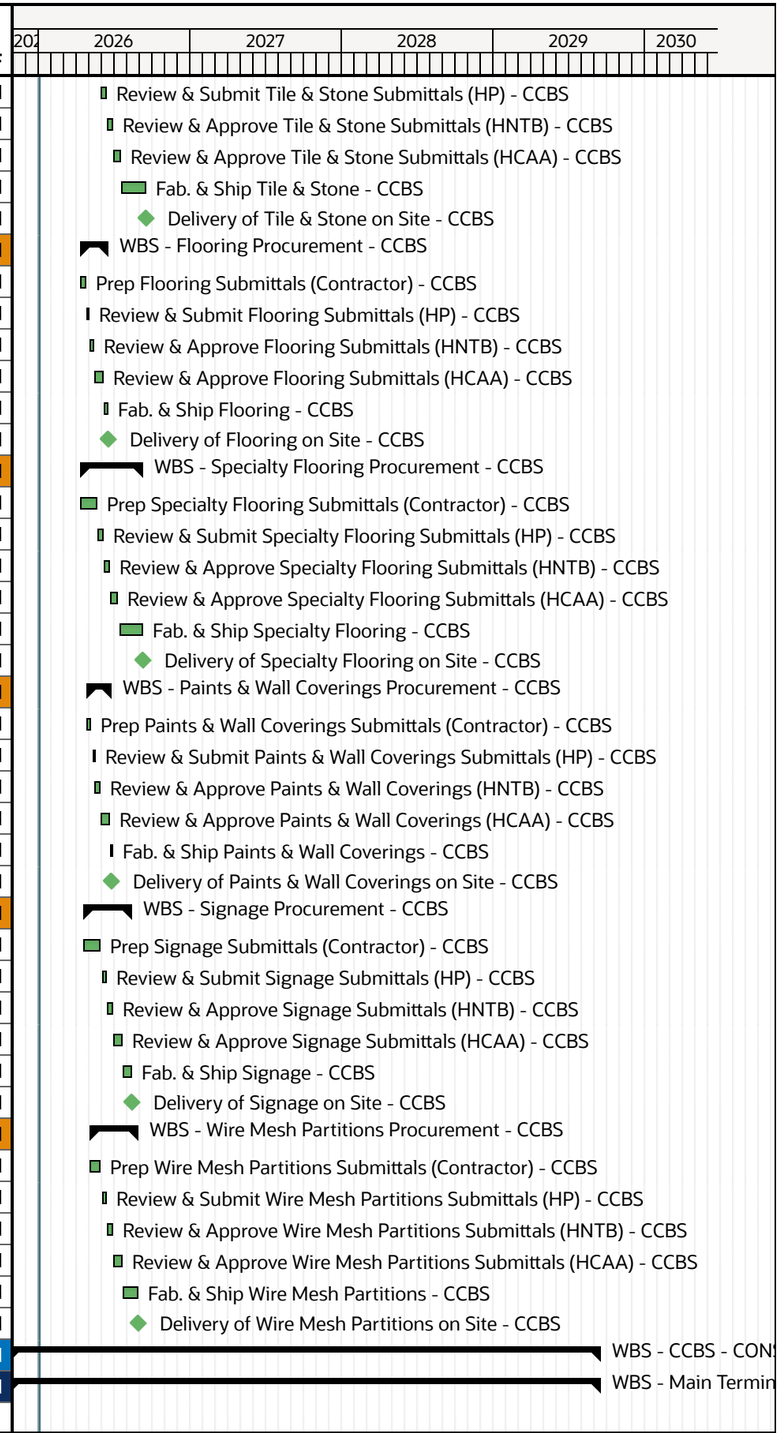


	ID	Name	Dur	Start	Finish	TF
12727	WBS - Operational Impact Windows		830.0d	27-Feb-26	1-Jun-29	150.0d
12728	BG-MLS-OPS-10	Tug Lane Crossover Between OS Line & Pod 5 - Permanently Shut Down	0.0d		27-Feb-26	376.0d
12729	A108640	Existing Kitchen/Breakroom & Existing IT Room on Level 2 - Permanently Out ...	0.0d		16-Apr-26	32.0d
12730	BG-OPS-BC-10	Bag Claim Carousel C14 - Out of Service (LOE)	450.0d	8-May-26	16-Feb-28	24.0d
12731	BG-OPS-BC-20	Bag Claim Carousel C15 - Out of Service (LOE)	450.0d	8-May-26	16-Feb-28	24.0d
12732	BG-OPS-TC-50	Ticket Counter T17 Structural Steel - Out of Service (LOE)	125.0d	15-May-26	10-Nov-26	168.0d
12733	BG-OPS-TC-40	Ticket Counter T18 - Out of Service (LOE)	53.0d	14-Jul-26	25-Sep-26	0.0d
12734	BG-OPS-TC-30	Ticket Counter C11E - Out of Service (LOE)	10.0d	3-Sep-26	17-Sep-26	0.0d
12735	BG-OPS-TC-60	Ticket Counter T15 - Out of Service (LOE)	43.0d	21-Oct-26	22-Dec-26	168.0d
12736	BG-OPS-TC-70	Ticket Counter T16 - Out of Service (LOE)	43.0d	21-Oct-26	22-Dec-26	168.0d
12737	BG-OPS-TC-90	TA2 - Out of Service [Contingency Porters Required] (LOE)	4.0d	16-Dec-26	21-Dec-26	0.0d
12738	BG-OPS-TC-100	TA1 - Out of Service [Contingency Porters Required] (LOE)	5.0d	22-Dec-26	29-Dec-26	0.0d
12739	BG-MLS-OPS-20	MEM1 - Permanently Out of Service	0.0d		30-Dec-26	0.0d
12740	BG-OPS-BC-30	Bag Claim Carousel C12 - Out of Service (LOE)	211.0d	19-Apr-27	16-Feb-28	24.0d
12741	BG-OPS-BC-40	Bag Claim Carousel C13 - Out of Service (LOE)	208.0d	19-Apr-27	11-Feb-28	24.0d
12742	BG-OPS-RS-10	Red Side Drive Aisle - Open Ceiling (LOE)	75.0d	25-Jun-27	11-Oct-27	567.0d
12743	BG-OPS-RS-30	Red Side Curbside Pickup Roadway - Open Ceiling (LOE)	75.0d	25-Jun-27	11-Oct-27	567.0d
12744	BG-OPS-RS-40	Below Red Side Airside D Shuttle Platform - Open Ceiling (LOE)	75.0d	25-Jun-27	11-Oct-27	567.0d
12745	BG-OPS-AS-30	AS4 Screening Loop - Permanently Out of Service	0.0d		10-Sep-27	39.0d
12746	BG-OPS-TC-130	T4 - Out of Service - American Airlines Shift to T6 (LOE)	1.0d	9-Feb-29	9-Feb-29	0.0d
12747	BG-OPS-TC-140	C2 - Out of Service - American Airlines Shift to T6 (LOE)	23.0d	12-Feb-29	14-Mar-29	0.0d
12748	BG-OPS-TC-80	TC2 - Out of Service [Contingency Porters Required] (LOE)	21.0d	3-May-29	1-Jun-29	61.0d
12749	BG-OPS-TC-110	Ticket Counter T2 - Partially Out of Service (LOE)	21.0d	3-May-29	1-Jun-29	61.0d
12750	BG-OPS-TC-120	Ticket Counter T3 - Out of Service (LOE)	21.0d	3-May-29	1-Jun-29	61.0d
12751	WBS - BHS Testing & Integration		913.0d	13-Feb-26	14-Sep-29	0.0d
12752	WBS - Factory Acceptance Test (FAT)		5.0d	5-Feb-27	11-Feb-27	368.0d
12753	BG-TST-10	Factory Acceptance Test (FAT) (SUM) - BHS Testing & Integration	5.0d	5-Feb-27	11-Feb-27	368.0d
12754	WBS - ISAT - AS3 Temporary Condition		8.0d	28-Sep-27	7-Oct-27	314.0d
12755	D1887	Internal Commissioning / Functional Testing (AS3 CBRA Loop Temp) [01-03-02]	5.0d	28-Sep-27	4-Oct-27	0.0d
12756	D1888	Owner / TRR Testing (AS3 CBRA Loop Temp) [01-03-02]	5.0d	28-Sep-27	4-Oct-27	314.0d
12757	D1889	ISAT Travel (AS3 CBRA Loop Temp) [01-03-02]	1.0d	5-Oct-27	5-Oct-27	314.0d
12758	D1890	ISAT (AS3 CBRA Loop Temp) [01-03-02]	2.0d	6-Oct-27	7-Oct-27	314.0d
12759	WBS - XBM-R		25.0d	16-Nov-27	22-Dec-27	7.0d
12760	D1932	Commissioning / Testing (XBM1 Cross Belt) [01-03-04]	20.0d	16-Nov-27	15-Dec-27	7.0d
12761	D1933	Owner Testing (XBM1 Cross Belt) [01-03-04]	4.0d	16-Dec-27	21-Dec-27	7.0d
12762	D1934	Go Live (XBM1 Cross Belt) [01-03-04]	1.0d	22-Dec-27	22-Dec-27	7.0d
12763	WBS - XBM-B		25.0d	15-Jun-28	20-Jul-28	0.0d
12764	D1982	Commissioning / Testing (XBM2 Cross Belt) [02-01-01C]	20.0d	15-Jun-28	13-Jul-28	0.0d
12765	D1983	Owner Testing (XBM2 Cross Belt) [02-01-01C]	4.0d	14-Jul-28	19-Jul-28	0.0d
12766	D1984	Go Live (XBM2 Cross Belt) [02-01-01C]	1.0d	20-Jul-28	20-Jul-28	0.0d
12767	WBS - EDS Machines		267.0d	28-Sep-27	13-Oct-28	20.0d
12768	BG-TST-270	Site Acceptance Test - AS3 Temp EDS Machine (SAT) (SUM) - BHS Testing & Int...	5.0d	28-Sep-27	4-Oct-27	0.0d

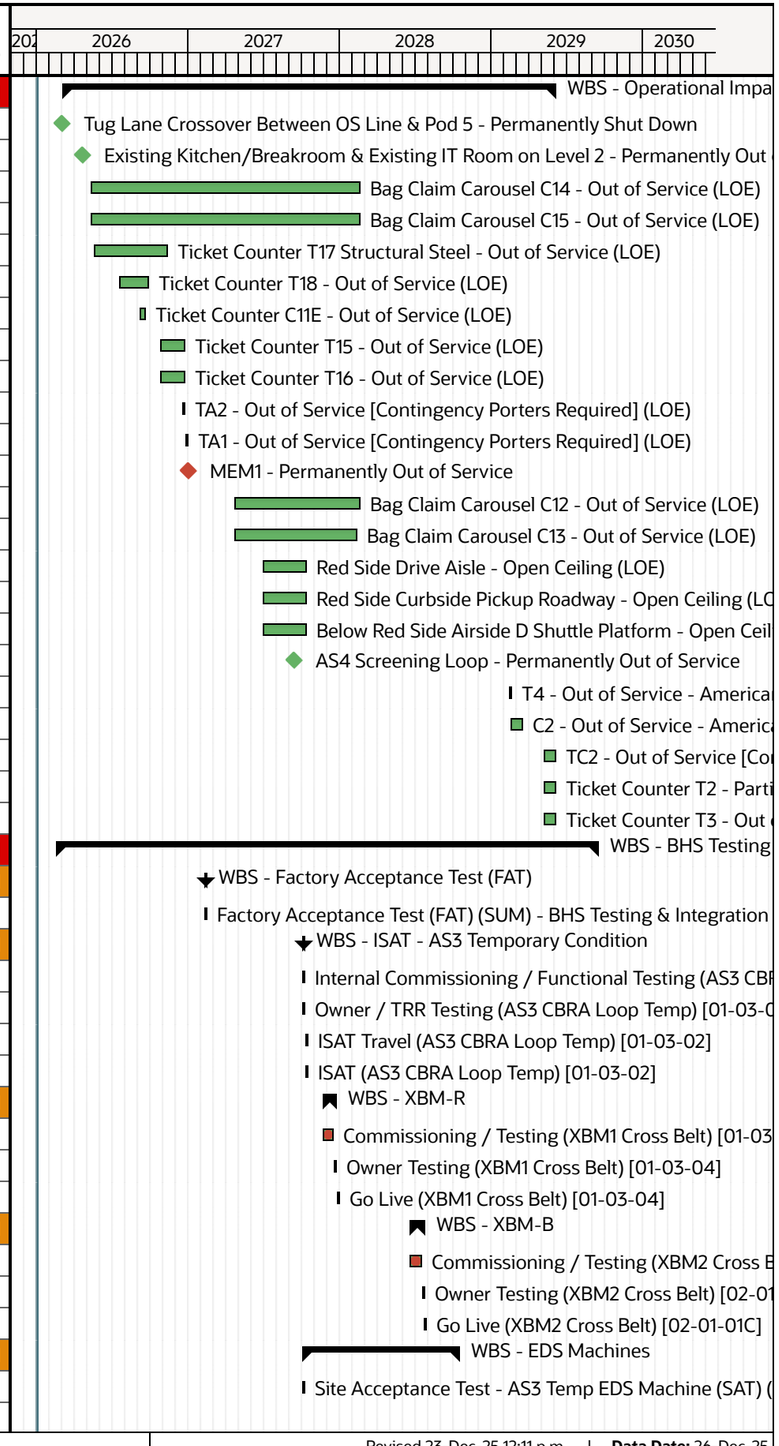


ID	Name	Dur	Start	Finish	TF
12769	BG-TST-60	Site Acceptance Test (SAT) (SUM) - BHS Testing & Integration	15.0d	11-Sep-28	29-Sep-28	20.0d
12770	BG-TST-90	EDS/BHS Integration - BHS Testing & Integration	10.0d	2-Oct-28	13-Oct-28	20.0d
12771	WBS - TRR		45.0d	25-Sep-28	28-Nov-28	0.0d
12772	D2031	Internal Pre-TRR / Internal System Level Testing [02-01-03B]	20.0d	25-Sep-28	20-Oct-28	0.0d
12773	D2032	Owner Witnessed Testing / Pre-TRR [02-01-03B]	15.0d	23-Oct-28	10-Nov-28	0.0d
12774	D2033	TRR [02-01-03B]	10.0d	13-Nov-28	28-Nov-28	0.0d
12775	WBS - ISAT - Full System		763.0d	13-Feb-26	14-Feb-29	117.0d
12776	BG-TST-30	Site Survey Data Collection Planning Checklist provided to the PROJECT SPON...	1.0d	13-Feb-26	13-Feb-26	60.0d
12777	BG-TST-50	Completed Site Survey Data Collection Checklist & supporting site documentati...	1.0d	15-Apr-26	15-Apr-26	60.0d
12778	BG-TST-70	On-site Site Survey Meeting - BHS Testing & Integration	1.0d	16-Apr-26	16-Apr-26	836.0d
12779	BG-TST-100	Test Review Meeting - BHS Testing & Integration	1.0d	2-Jun-26	2-Jun-26	836.0d
12780	BG-TST-150	Shipment of Test Articles - BHS Testing & Integration	14.0d	6-Jul-26	19-Jul-26	843.0d
12781	BG-TST-130	CBIS Pre-Testing - BHS Testing & Integration	1.0d	9-Jul-26	9-Jul-26	596.0d
12782	D2034	ISAT Travel Day [02-01-03B]	1.0d	29-Nov-28	29-Nov-28	0.0d
12783	D2035	ISAT [02-01-03B]	10.0d	30-Nov-28	13-Dec-28	0.0d
12784	BG-TST-200	Go Live - BHS Testing & Integration	0.0d		13-Dec-28	139.0d
12785	BG-TST-210	QLR Submission - BHS Testing & Integration	5.0d	14-Dec-28	20-Dec-28	118.0d
12786	BG-TST-180	TSR Approval & Distribution - BHS Testing & Integration	5.0d	14-Dec-28	20-Dec-28	118.0d
12787	D2036	TRN [02-01-03B]	3.0d	14-Dec-28	18-Dec-28	0.0d
12788	BG-TST-230	ISAT Review Board - BHS Testing & Integration	1.0d	29-Dec-28	29-Dec-28	118.0d
12789	BG-TST-240	QLR Review & Distribution - BHS Testing & Integration	5.0d	9-Jan-29	15-Jan-29	118.0d
12790	BG-TST-250	Run-In/Monitor Period - BHS Testing & Integration	30.0d	16-Jan-29	14-Feb-29	164.0d
12791	WBS - Oversized Screening		20.0d	17-Aug-29	14-Sep-29	0.0d
12792	D2191	Internal Commissioning / Functional Testing- Oversized Screening [02-02-05]	5.0d	17-Aug-29	23-Aug-29	0.0d
12793	D2192	Owner / TRR Testing- Oversized Screening [02-02-05]	5.0d	24-Aug-29	30-Aug-29	0.0d
12794	D2193	ISAT Travel Day [02-02-05]	1.0d	31-Aug-29	31-Aug-29	0.0d
12795	D2194	ISAT Testing (Oversized Screening) [02-02-05]	4.0d	4-Sep-29	7-Sep-29	0.0d
12796	D2195	TRN (Oversized Screening) [02-02-05]	5.0d	10-Sep-29	14-Sep-29	0.0d
12797	WBS - EDS Machines		246.0d	22-Sep-27	8-Sep-28	20.0d
12798	A104190	Delivery of TSA AS3 Temp EDS Machine	1.0d	22-Sep-27	22-Sep-27	0.0d
12799	A104200	TSA Install of AS3 Temp EDS Machine	3.0d	23-Sep-27	27-Sep-27	0.0d
12800	TSA-EDS-60	Delivery of TSA EDS Machines	1.0d	24-Aug-28	24-Aug-28	30.0d
12801	TSA-EDS-30	TSA Install of EDS Machines	10.0d	25-Aug-28	8-Sep-28	20.0d
12802	WBS - Construction Phases		908.0d	6-Feb-26	30-Aug-29	140.0d
12803	WBS - Seq 1 - Stage 1 - Step 1		132.0d	27-Feb-26	2-Sep-26	130.0d
12804	A106020	Pre-Test & Balance Pre-HVAC Demo/Modification [01-01-01]	5.0d	27-Feb-26	5-Mar-26	51.0d
12805	BI-ROW-BCC-80	Pre-BHS HVAC & Plumbing Systems Modifications [01-01-01]	20.0d	10-Apr-26	7-May-26	26.0d
12806	BI-ROW-BCC-60	Pre-BHS Elec. Systems Modifications [01-01-01]	20.0d	10-Apr-26	7-May-26	26.0d
12807	BI-ROW-BCC-90	Remove & Store Ceiling Panels & Grid [01-01-01]	10.0d	10-Apr-26	23-Apr-26	26.0d
12808	BI-ROW-BCC-100	Pre-BHS Fire Sprinkler System Modifications [01-01-01]	20.0d	10-Apr-26	7-May-26	26.0d
12809	BI-ROW-BCC-110	Pre-BHS Technology & Data Systems Modifications [01-01-01]	20.0d	10-Apr-26	7-May-26	26.0d
12810	BI-ROW-BCC-690	Demo Hard-Lid Ceiling & Framing [01-01-01]	10.0d	10-Apr-26	23-Apr-26	26.0d

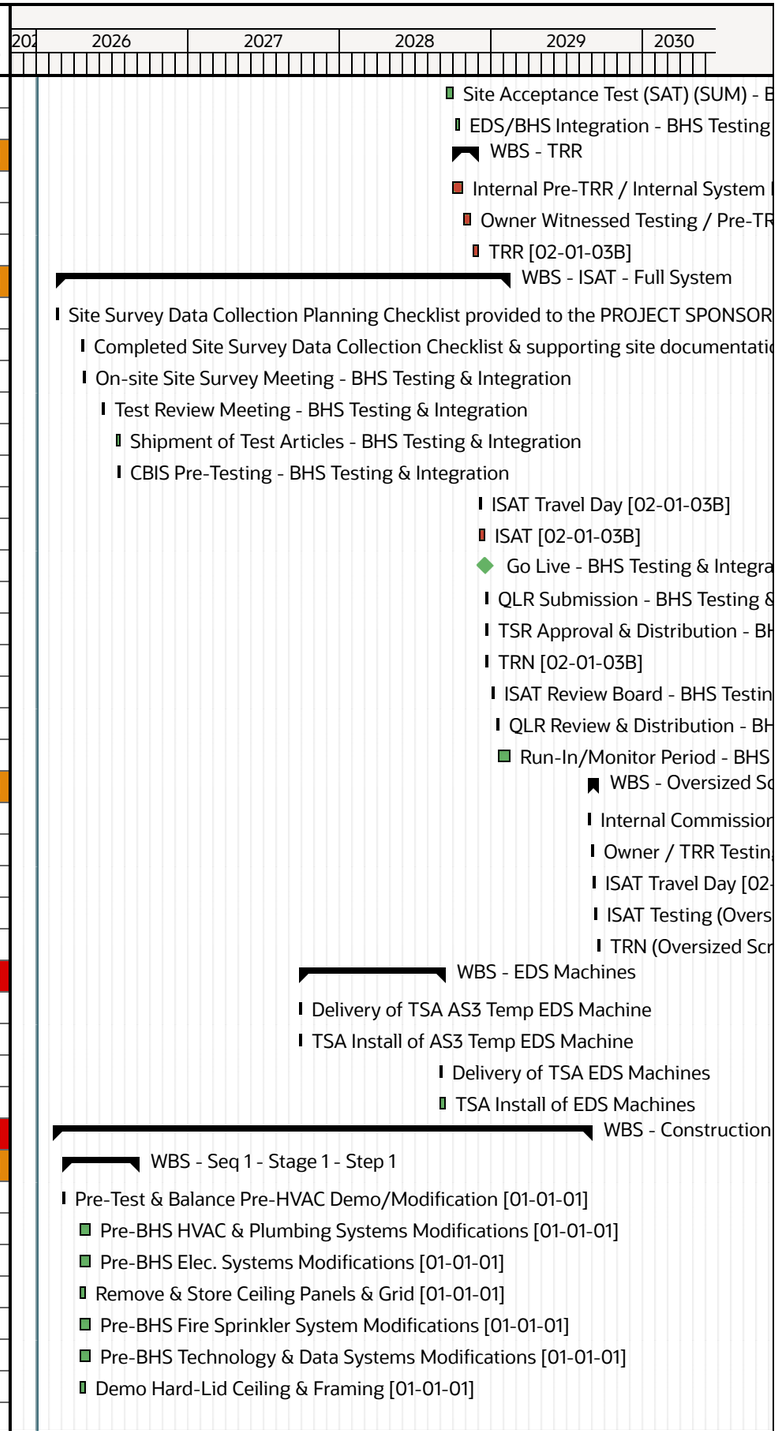


	ID	Name	Dur	Start	Finish	TF
12811	BI-ROW-BCC-10	Layout CFRP [01-01-01]	5.0d	17-Apr-26	23-Apr-26	31.0d
12812	BI-ROW-BCC-40	Remove & Store Signage [01-01-01]	2.0d	22-Apr-26	23-Apr-26	41.0d
12813	BI-ROW-BCC-610	Create Openings (T-T18 Subsystem) [01-01-01]	3.0d	24-Apr-26	28-Apr-26	63.0d
12814	BI-ROW-BCC-30	Install Temp Wall Partitions & Temp Signage C14 & C15 [01-01-01]	5.0d	8-May-26	14-May-26	26.0d
12815	BI-ROW-BCC-20	Prep & Apply CFRP at Bag Claim Ceiling [01-01-01]	25.0d	15-May-26	19-Jun-26	26.0d
12816	A	BHS - Mech/Elec/Panel Demo & Install [01-01-01]	16.0d	14-Jul-26	4-Aug-26	11.0d
12817	BG-DM-MCP-3800	Demo MCP 38 Feeder Back to Source [HMCP-10] [01-01-01]	10.0d	5-Aug-26	18-Aug-26	136.0d
12818	BG-DM-MCP-3900	Demo MCP 4 Feeder Back to Source [HMCP-3] [01-01-01]	10.0d	5-Aug-26	18-Aug-26	11.0d
12819	BI-ROW-BCC-180	Post-BHS Fire Sprinkler System Modifications - Area A [01-01-01]	20.0d	6-Aug-26	2-Sep-26	5.0d
12820	BI-ROW-BCC-650	Post-BHS Technology & Data Systems Modifications - Area A [01-01-01]	20.0d	6-Aug-26	2-Sep-26	5.0d
12821	BG-DM-MCP-4020	Post-BHS Elec. Systems Modifications - Area A [01-01-01]	20.0d	6-Aug-26	2-Sep-26	5.0d
12822	BI-ROW-BCC-640	Post-BHS HVAC & Plumbing Systems Modifications [01-01-01]	20.0d	6-Aug-26	2-Sep-26	5.0d
12823	B	BHS - Mech & Elec. Install [01-01-01]	15.0d	6-Aug-26	26-Aug-26	0.0d
12824	BG-DM-MCP-3830	Demo, Patch, & Seal Concrete @ Former MCP 38 Housekeeping Pad [01-01-01]	5.0d	19-Aug-26	25-Aug-26	136.0d
12825	BG-DM-MCP-3930	Demo, Patch & Seal Concrete @ Former MCP 4 Housekeeping Pad [01-01-01]	5.0d	19-Aug-26	25-Aug-26	81.0d
12826	C	BHS - T-T18 Tie-in & Overall Testing [01-01-01]	5.0d	27-Aug-26	2-Sep-26	0.0d
12827	WBS - Seq 1 - Stage 1 - Step 2		18.0d	3-Sep-26	29-Sep-26	62.0d
12828	A105680	HVAC & Plumbing Systems Modifications [01-01-02]	5.0d	3-Sep-26	10-Sep-26	5.0d
12829	A105690	Technology & Data Systems Modifications [01-01-02]	5.0d	3-Sep-26	10-Sep-26	5.0d
12830	A105700	Fire Protection System Modifications [01-01-02]	5.0d	3-Sep-26	10-Sep-26	5.0d
12831	A105670	Elec. Systems Modifications [01-01-02]	5.0d	3-Sep-26	10-Sep-26	5.0d
12832	A1	BHS - Mech / Elec. Demo & Install of C11 & T18 [01-01-02]	7.0d	3-Sep-26	14-Sep-26	0.0d
12833	B1	BHS - Testing [01-01-02]	8.0d	8-Sep-26	17-Sep-26	0.0d
12834	BG-BI-ROW-90	Demo MCP 5 Feeder Back to Source [HMCP-3] [01-01-02]	10.0d	9-Sep-26	22-Sep-26	3.0d
12835	A104130	Infill C11-01 Penetration Along Grid L [01-01-02]	4.0d	15-Sep-26	18-Sep-26	0.0d
12836	BG-BI-ROW-230	Demo, Patch & Seal Concrete @ Former MCP 5 Housekeeping Pad [01-01-02]	5.0d	23-Sep-26	29-Sep-26	62.0d
12837	WBS - Seq 1 - Stage 1 - Step 3		12.0d	18-Sep-26	5-Oct-26	19.0d
12838	A105720	HVAC & Plumbing Systems Modifications [01-01-03]	5.0d	18-Sep-26	24-Sep-26	6.0d
12839	A105740	Fire Protection Systems Modifications [01-01-03]	5.0d	18-Sep-26	24-Sep-26	6.0d
12840	A105710	Elec. Systems Modifications [01-01-03]	5.0d	18-Sep-26	24-Sep-26	6.0d
12841	A105730	Technology & Data Systems Modifications [01-01-03]	5.0d	18-Sep-26	24-Sep-26	6.0d
12842	A3	BHS - Mech / Elec. Demo & Install of T18 [01-01-03]	5.0d	18-Sep-26	24-Sep-26	0.0d
12843	A104150	Infill T18 Penetration Along Grid L [01-01-03]	5.0d	21-Sep-26	25-Sep-26	0.0d
12844	A104160	Cut New Penetration for T-TC2 Along Grid L [01-01-03]	4.0d	25-Sep-26	30-Sep-26	22.0d
12845	D1788	BHS - Testing T18 [01-01-03]	1.0d	25-Sep-26	25-Sep-26	0.0d
12846	A3.5	BHS - Mech / Elec. Demo & Install of TC2 [01-01-03]	5.0d	28-Sep-26	2-Oct-26	0.0d
12847	D1793	Internal Commissioning / Functional Testing / Owner Testing [01-01-03]	1.0d	5-Oct-26	5-Oct-26	0.0d
12848	WBS - Seq 1 - Stage 1 - Step 4 - Ticket Counter 17		127.0d	15-May-26	12-Nov-26	168.0d
12849	CON-TC17-10	Secure Access & Temp Partitions to Ticket Counter 17 Work Area [01-01-04]	2.0d	15-May-26	18-May-26	65.0d
12850	A105750	Demo @ 1603 - Medical Infirmary [01-01-04]	5.0d	19-May-26	26-May-26	65.0d
12851	A105780	Relocate Fire Alarm Devices @ 1603 - Medical Infirmary [01-01-04]	5.0d	19-May-26	26-May-26	65.0d
12852	A105830	Trim Out HVAC Grilles @ 1603 - Medical Infirmary [01-01-04]	1.0d	27-May-26	27-May-26	70.0d

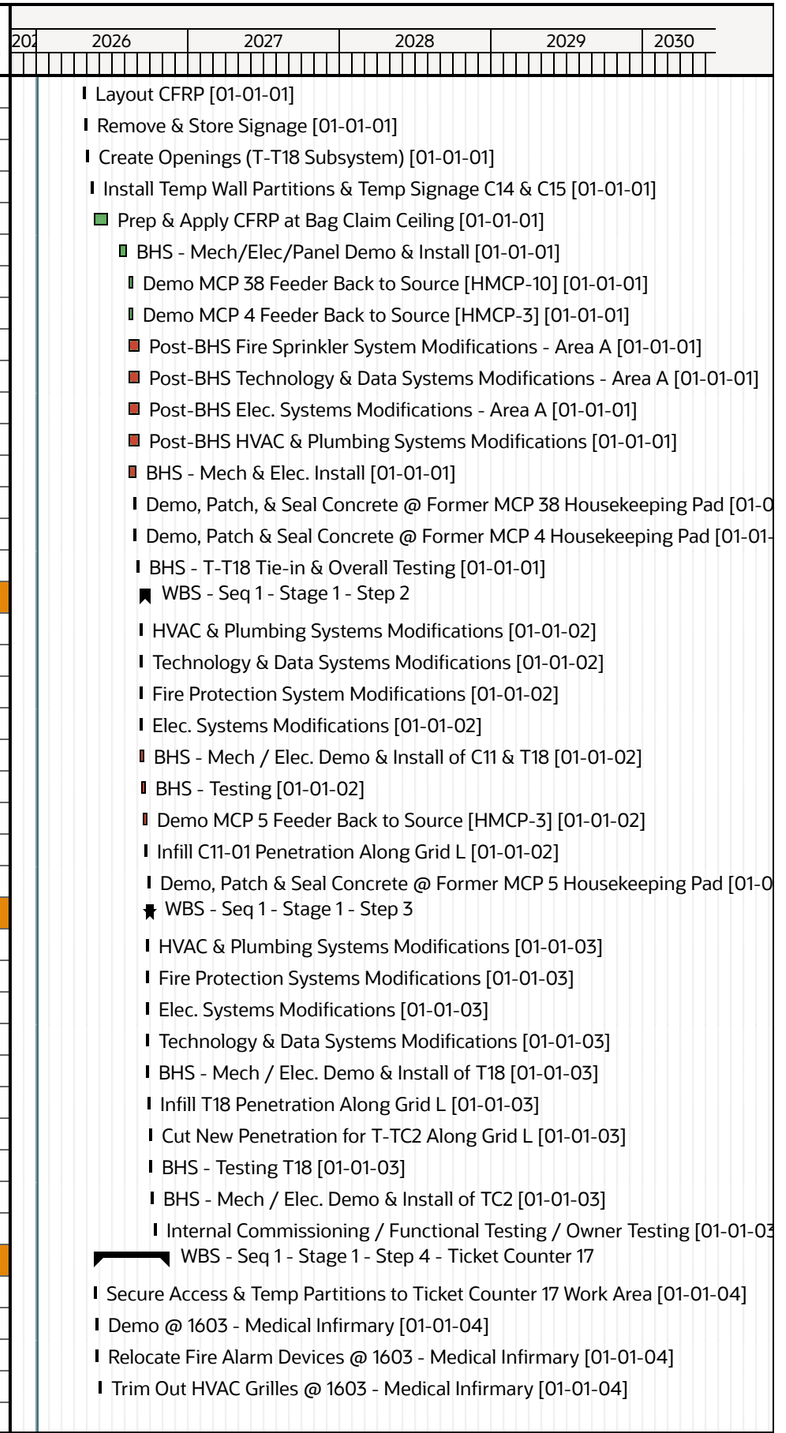


	ID	Name	Dur	Start	Finish	TF
12853	A105840	Relocate Fire Sprinkler @ 1603 - Medical Infirmary [01-01-04]	2.0d	27-May-26	28-May-26	69.0d
12854	A105820	Reinstall Acoustical Ceiling Grid & Tiles @ 1603 - Medical Infirmary [01-01-04]	3.0d	27-May-26	29-May-26	65.0d
12855	A105850	Install New Lights & Switches @ 1603 - Medical Infirmary [01-01-04]	3.0d	1-Jun-26	3-Jun-26	65.0d
12856	CON-TC17-50	Cut Slab Penetration for T17 Conveyor [01-01-04]	5.0d	4-Jun-26	10-Jun-26	65.0d
12857	CON-TC17-160	Cut Existing Steel Framing @ Penetration for T17 Conveyor [01-01-04]	3.0d	11-Jun-26	15-Jun-26	65.0d
12858	A81860	Erect Steel at New T17 Opening [01-01-04]	5.0d	25-Jun-26	1-Jul-26	58.0d
12859	CON-TC17-40	Frame Walls for New T17 Conveyor Penetration [01-01-04]	4.0d	2-Jul-26	8-Jul-26	58.0d
12860	CON-TC17-80	Hang, Tape, & Finish T17 Doghouse Walls [01-01-04]	4.0d	9-Jul-26	14-Jul-26	58.0d
12861	A4	BHS - Mech / Elec. Demo & Install of T17 [01-01-04]	5.0d	6-Oct-26	12-Oct-26	0.0d
12862	D1800	Internal Commissioning / Functional Testing / Owner Testing (T17 03/04, T17 ...	1.0d	12-Oct-26	12-Oct-26	0.0d
12863	D1801	Mech Remove Stainless Shrouding (T17 01/02) [01-01-04]	1.0d	13-Oct-26	13-Oct-26	0.0d
12864	D1802	Elec. Recontrol (Reverse) (T17 01/02) [01-01-04]	2.0d	14-Oct-26	15-Oct-26	0.0d
12865	D1805	Mech Stainless Shrouding (T17 01/02) [01-01-04]	1.0d	16-Oct-26	16-Oct-26	0.0d
12866	D1804	Internal Commissioning / Functional Testing / Owner Testing (T17 01/02) [01-...	1.0d	16-Oct-26	16-Oct-26	0.0d
12867	D1806	Elec. Demo (T17 03/04) [01-01-04]	1.0d	19-Oct-26	19-Oct-26	0.0d
12868	D1807	Mech Demo (T17 03/04) [01-01-04]	1.0d	20-Oct-26	20-Oct-26	0.0d
12869	A105860	Install Steel at Old T17 Penetration [01-01-04]	5.0d	21-Oct-26	27-Oct-26	168.0d
12870	CON-TC17-110	Infill Slab at Old T17 Conveyor Penetration [01-01-04]	5.0d	28-Oct-26	3-Nov-26	168.0d
12871	A105870	Apply Fireproofing to New Steel @ T17 Penetrations [01-01-04]	2.0d	28-Oct-26	29-Oct-26	176.0d
12872	CON-TC17-130	Frame Wall at Old T17 Conveyor Penetration [01-01-04]	1.0d	4-Nov-26	4-Nov-26	168.0d
12873	CON-TC17-140	Hang, Tape, & Finish Wall at Old T17 Conveyor Penetration [01-01-04]	2.0d	5-Nov-26	6-Nov-26	168.0d
12874	CON-TC17-100	Apply Final Paint - T17 Doghouse Walls at New T17 & Old T17 Penetrations [0...	2.0d	9-Nov-26	10-Nov-26	168.0d
12875	CON-TC17-150	Remove Temp Walls Around T17 Penetration Work & Relocate to T15 & T16 Pe...	2.0d	11-Nov-26	12-Nov-26	168.0d
12876	WBS - Seq 1 - Stage 1 - Step 5 - Ticket Counters 15 & 16		43.0d	21-Oct-26	22-Dec-26	168.0d
12877	A107620	Install Temp Partition Walls Around T15 & T16 Counters [01-01-05]	2.0d	21-Oct-26	22-Oct-26	0.0d
12878	A5	BHS - Mech / Elec. Demo & Install of T15 [01-01-05]	5.0d	23-Oct-26	29-Oct-26	0.0d
12879	D1813	Internal Commissioning / Functional Testing / Owner Testing T15 [01-01-05]	1.0d	30-Oct-26	30-Oct-26	0.0d
12880	B5	BHS - Mech / Elec. Demo & Install of T16 [01-01-05]	4.0d	2-Nov-26	5-Nov-26	0.0d
12881	A106010	Install Steel & Decking Old T16 Penetration [01-01-05]	5.0d	4-Nov-26	10-Nov-26	171.0d
12882	BG-DM-MCP-200	Demo MCP 2 Feeder Back to Source & Remove [HMCP-3] [01-01-05]	10.0d	6-Nov-26	19-Nov-26	21.0d
12883	D1820	Internal Commissioning / Functional Testing / Owner Testing T16 [01-01-05]	1.0d	6-Nov-26	6-Nov-26	0.0d
12884	CON-TC15&16-10	Clear Out Tenant Storage Room Behind T15 & T16 Ticket Counters [01-01-05]	3.0d	11-Nov-26	13-Nov-26	168.0d
12885	A105920	Apply Fireproofing Patching [01-01-05]	2.0d	11-Nov-26	12-Nov-26	175.0d
12886	CON-TC15&16-40	Infill Slab at Old T16 Penetration [01-01-05]	6.0d	13-Nov-26	20-Nov-26	169.0d
12887	CON-TC15&16-30	Demo Drywall Walls & Door at T15 & T16 Rooms 1661 & 1657 [01-01-05]	3.0d	16-Nov-26	18-Nov-26	168.0d
12888	A105900	Demo & Relocate Elec. Fixtures & Switches in New AV Training Rm [01-01-05]	5.0d	16-Nov-26	20-Nov-26	169.0d
12889	A105890	Demo LV Cabling, Data Outlets & Screens [01-01-05]	3.0d	19-Nov-26	23-Nov-26	168.0d
12890	BG-DM-MCP-3850	Demo, Patch & Seal Concrete @ Former MCP 2 Housekeeping Pad [01-01-05]	4.0d	20-Nov-26	25-Nov-26	21.0d
12891	CON-TC15&16-50	Modify Fire Sprinkler Heads in New T15 & T16 Rooms [01-01-05]	5.0d	24-Nov-26	2-Dec-26	175.0d
12892	CON-TC15&16-60	Install New Door & Frame to Relocated Storage Room Behind T16 [01-01-05]	2.0d	24-Nov-26	25-Nov-26	178.0d
12893	CON-TC15&16-70	Frame Walls for Relocated Storage Room Behind T16 & Wall Infill at New AV Tra...	3.0d	24-Nov-26	30-Nov-26	168.0d
12894	CON-TC15&16-120	Hang, Tape, & Finish Walls in Relocated Storage Room & New AV Training Roo...	5.0d	1-Dec-26	7-Dec-26	168.0d

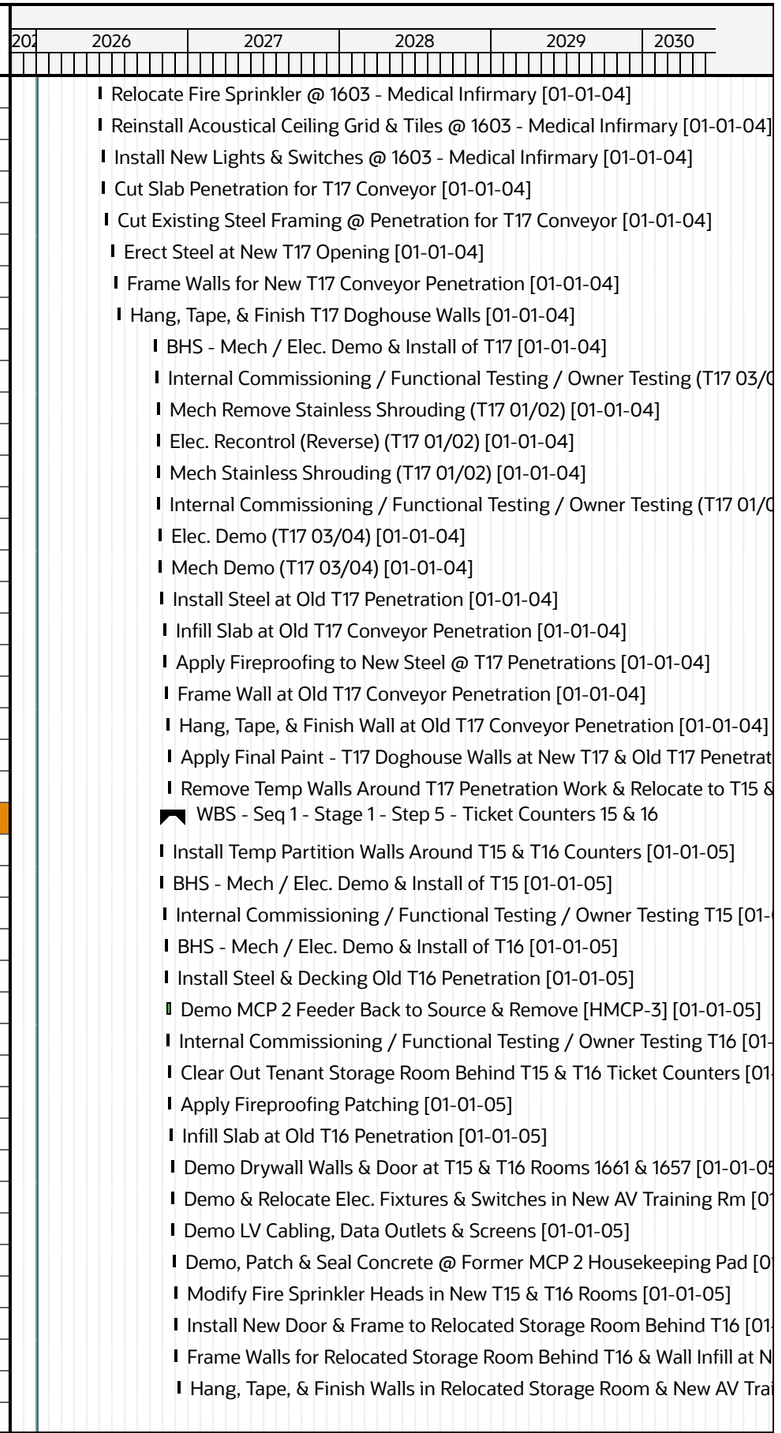


	ID	Name	Dur	Start	Finish	TF
12895	A106470	Install LV Cabling, Data Outlets & Screens in New Location [01-01-05]	3.0d	1-Dec-26	3-Dec-26	168.0d
12896	CON-TC15&16-140	Apply Final Paint - Relocated Storage Room Behind T16 & Wall Infill at New AV ...	2.0d	8-Dec-26	9-Dec-26	172.0d
12897	A105980	Install/Modify Ceiling in New AV Training Room & Relocated Storage [01-01-05]	3.0d	8-Dec-26	10-Dec-26	168.0d
12898	A105990	Install/Relocate Light Fixtures & Switches i Rooms 1661 & 1659 [01-01-05]	4.0d	9-Dec-26	14-Dec-26	169.0d
12899	CON-TC15&16-90	Relocate/Install New Supply Grilles, Diffusers & Plenums in Rooms 1661, 1657,...	3.0d	11-Dec-26	15-Dec-26	168.0d
12900	CON-TC15&16-150	Final Clean T15 & T16 Ticket Counter & BOH Spaces [01-01-05]	3.0d	16-Dec-26	18-Dec-26	168.0d
12901	CON-TC15&16-160	Remove Temp Partitions Around T15 & T16 Ticket Counters [01-01-05]	2.0d	21-Dec-26	22-Dec-26	168.0d
12902	WBS - Seq 1 - Stage 2 - Step 1		47.0d	1-Oct-26	8-Dec-26	64.0d
12903	A104170	Modify Wall Penetration (TC2) [01-02-01]	5.0d	1-Oct-26	7-Oct-26	22.0d
12904	A6	BHS - Mech / Elec. Demo & Install of TC2 [01-02-01]	4.0d	9-Nov-26	12-Nov-26	0.0d
12905	BG-DM-MCP-3860	Demo MCP 36 Feeder Back to Source [HMCP-3] [01-02-01]	10.0d	13-Nov-26	30-Nov-26	64.0d
12906	D1828	Internal Commissioning / Functional Testing / Owner Testing [01-02-01]	1.0d	13-Nov-26	13-Nov-26	0.0d
12907	BG-DM-MCP-3870	Demo Exist. Housekeeping Pad Beneath Former MCP 36 & Remove MCP 36 [0...	3.0d	1-Dec-26	3-Dec-26	64.0d
12908	BG-DM-MCP-3890	Patch & Seal Concrete @ Former MCP 36 Housekeeping Pad [01-02-01]	3.0d	4-Dec-26	8-Dec-26	64.0d
12909	WBS - Seq 1 - Stage 2 - Step 2		20.0d	16-Nov-26	15-Dec-26	0.0d
12910	D1833	Elec. Demo (AS7 03C/03D, ATR) [01-02-02]	1.0d	16-Nov-26	16-Nov-26	17.0d
12911	D1834	Mech Demo (AS7 03C/03D, ATR) [01-02-02]	1.0d	16-Nov-26	16-Nov-26	17.0d
12912	D1835	Mech Install (AS7 3B/3D, AX9 01) [01-02-02]	1.0d	16-Nov-26	16-Nov-26	0.0d
12913	D1832	Elec. Install MPP A1, FCP A1, MPP A9, FCP A9 [01-02-02]	9.0d	16-Nov-26	30-Nov-26	10.0d
12914	D1837	Elec. Install (AS7 3B/3D, AX9 01) [01-02-02]	12.0d	17-Nov-26	4-Dec-26	0.0d
12915	D1836	Mech Install (AX9 12/15, C8A 11/12, T12 25/26) [01-02-02]	7.0d	17-Nov-26	25-Nov-26	11.0d
12916	D1839	Internal Commissioning / Functional Testing / Owner Testing (AS7 3B/3D, AX9...	1.0d	7-Dec-26	7-Dec-26	5.0d
12917	D1838	Elec. Install (AX9 12/15, C8A 11/12, T12 25/26) [01-02-02]	6.0d	7-Dec-26	14-Dec-26	0.0d
12918	D1841	Internal Commissioning / Functional Testing / Owner Testing (AX9 12/15, C8A...	1.0d	15-Dec-26	15-Dec-26	0.0d
12919	WBS - Seq 1 - Stage 2 - Step 3		4.0d	16-Dec-26	21-Dec-26	0.0d
12920	D1845	Elec. Demo (T12 24/25, TA2 06) [01-02-03]	1.0d	16-Dec-26	16-Dec-26	2.0d
12921	D1846	Mech Demo (T12 24/25, TA2 06) [01-02-03]	1.0d	16-Dec-26	16-Dec-26	2.0d
12922	D1843	Mech Install (T-T12 24/25 & 27/28, T-AX9 11, Temp Diverter Plate PS-AX8 01...	3.0d	16-Dec-26	18-Dec-26	0.0d
12923	D1844	Elec. Install (T12 24, T 25/28, AX9 11) [01-02-03]	3.0d	16-Dec-26	18-Dec-26	0.0d
12924	D1847	Internal Commissioning / Functional Testing / Owner Testing [01-02-03]	1.0d	21-Dec-26	21-Dec-26	0.0d
12925	WBS - Seq 1 - Stage 2 - Step 4		5.0d	22-Dec-26	29-Dec-26	0.0d
12926	D1850	Elec. Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1.0d	22-Dec-26	22-Dec-26	3.0d
12927	D1851	Mech Demo (AX9 10, AX10 24/25, TA1 14, TA2 05) [01-02-04]	1.0d	22-Dec-26	22-Dec-26	3.0d
12928	D1852	Mec Install (AX9 10/11, TA1 12/14) [01-02-04]	4.0d	22-Dec-26	28-Dec-26	0.0d
12929	D1853	Elec. Install (AX9 10/11, TA1 12/14) [01-02-04]	4.0d	22-Dec-26	28-Dec-26	0.0d
12930	D1854	Internal Commissioning / Functional Testing / Owner Testing [01-02-04]	1.0d	29-Dec-26	29-Dec-26	0.0d
12931	WBS - Seq 1 - Stage 3 - Step 1		454.0d	6-Feb-26	17-Nov-27	594.0d
12932	WBS - Baggage Handling System [01-03-01]		244.0d	4-Dec-26	17-Nov-27	543.0d
12933	WBS - General		244.0d	4-Dec-26	17-Nov-27	543.0d
12934	BG-DM-MCP-3610	Demo & Remove MCP 36 [01-03-01]	1.0d	4-Dec-26	4-Dec-26	137.0d
12935	D1856	Elec. Demo [01-03-01]	30.0d	30-Dec-26	10-Feb-27	0.0d
12936	D1857	Mech Demo [01-03-01]	30.0d	30-Dec-26	10-Feb-27	0.0d

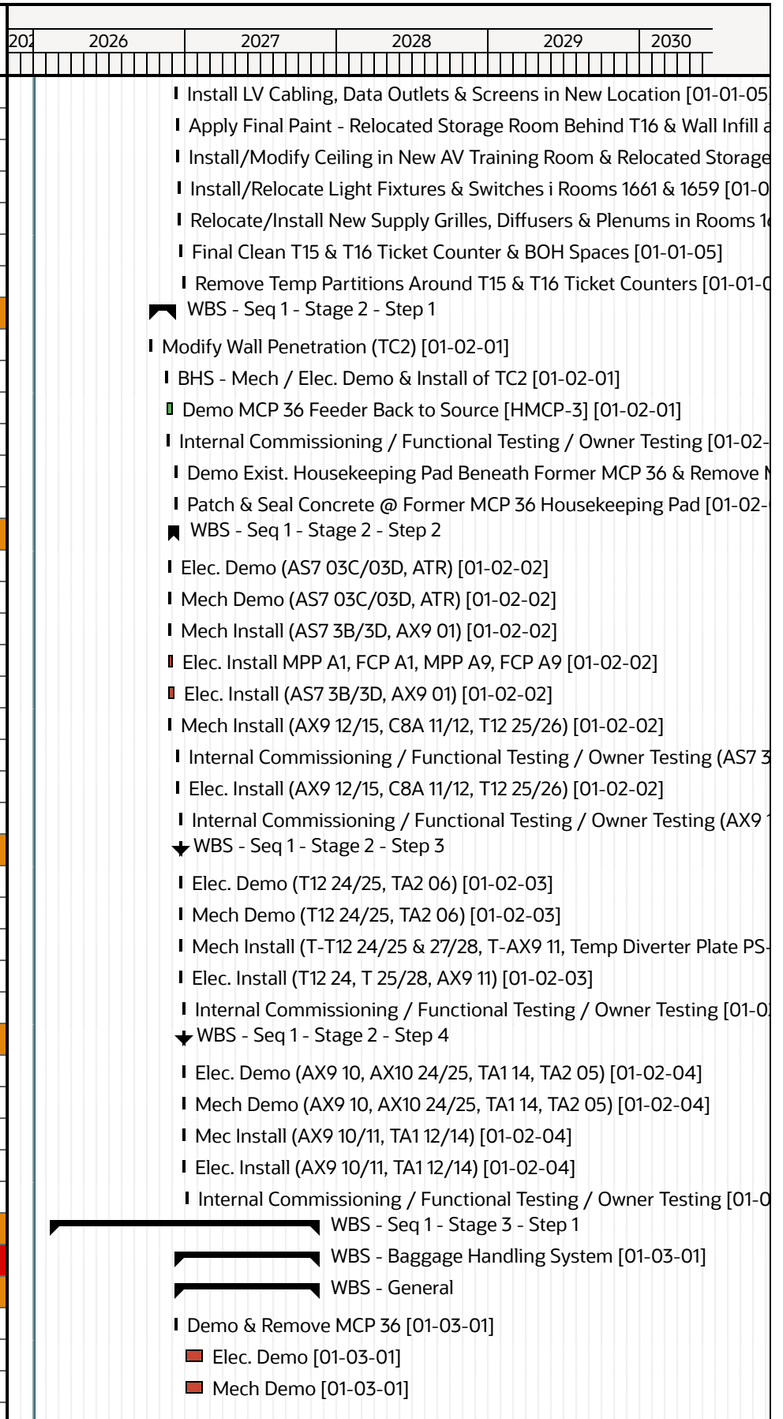


	ID	Name	Dur	Start	Finish	TF
12937	D1864	Elec. MPP Install (MPP-A2, FCP-A2, MPP-A3, FCP-A3, MPP-A4, FCP-A4, MPP-...	139.0d	7-Jan-27	22-Jul-27	16.0d
12938	D1861	Elec. MPP Install (MPP-A6, FCP-A6, MPP-A7, FCP-A7, MPP-B1, FCP-B1, MPP-...	139.0d	7-Jan-27	22-Jul-27	16.0d
12939	D1860	Elec. MPP Install (MPP-B4, FCP-B4, MPP-B5, FCP-B5, MPP-B6, FCP-B6, MPP-B...	139.0d	7-Jan-27	22-Jul-27	16.0d
12940	D1862	Mech Install (Sector J) [01-03-01]	30.0d	28-Jan-27	10-Mar-27	0.0d
12941	D1863	Elec. Install (Sector J) [01-03-01]	30.0d	28-Jan-27	10-Mar-27	110.0d
12942	D1867	Mech Install (Sector H) [01-03-01]	75.0d	11-Mar-27	24-Jun-27	0.0d
12943	D1866	Elec. Install (Sector H) [01-03-01]	75.0d	11-Mar-27	24-Jun-27	35.0d
12944	D1870	Mech Install (Sector G) [01-03-01]	35.0d	25-Jun-27	13-Aug-27	0.0d
12945	D1869	Elec. Install (Sector G) [01-03-01]	33.0d	25-Jun-27	11-Aug-27	2.0d
12946	D1871	Internal Commissioning / Functional Testing (Main Terminal Core) [01-03-01]	30.0d	19-Jul-27	27-Aug-27	0.0d
12947	D1873	Mech Install (TD1 02/34, TD2 05/30) [01-03-01]	50.0d	16-Aug-27	25-Oct-27	101.0d
12948	D1875	Owner Testing (Main Terminal Core) [01-03-01]	10.0d	23-Aug-27	3-Sep-27	0.0d
12949	D1876	Elec. Install (TD1 02/34, TD2 05/30) [01-03-01]	50.0d	23-Aug-27	1-Nov-27	542.0d
12950	D1874	Elec. MPP Install (MPP-A18, FCP-A18, MPP-B18, FCP-B18, MPP-A19, FCP-A19...	50.0d	23-Aug-27	1-Nov-27	542.0d
12951	D1877	Internal Commissioning / Functional Testing (TD1 / TD2) [01-03-01]	10.0d	2-Nov-27	15-Nov-27	542.0d
12952	D1878	Owner Testing (TD1 / TD2) [01-03-01]	2.0d	16-Nov-27	17-Nov-27	542.0d
12953	WBS - XBM1		133.0d	10-May-27	15-Nov-27	7.0d
12954	D1881	Mech Install (XBM1 Cross Belt) [01-03-01]	120.0d	10-May-27	27-Oct-27	20.0d
12955	D1880	Elec. Install (XBM1 Cross Belt) [01-03-01]	120.0d	27-May-27	15-Nov-27	7.0d
12956	D1879	Elec. MPP Install (MPP-XBM1-A 13 Enclosures) [01-03-01]	120.0d	27-May-27	15-Nov-27	7.0d
12957	WBS - North Tug Lane [01-03-01]		267.0d	6-Feb-26	24-Feb-27	72.0d
12958	WBS - Structural - North Tug Lane [01-03-01]		212.0d	24-Apr-26	24-Feb-27	72.0d
12959	BG-BI-ROW-200	Demo CMU Wall Opening for T-18A Line at CL L [01-03-01]	5.0d	24-Apr-26	30-Apr-26	187.0d
12960	BG-BI-ROW-240	Demo Slab @ North Tug Lane Column Found. Locations [01-03-01]	15.0d	14-Jan-27	3-Feb-27	72.0d
12961	BG-BI-ROW-250	FRP North Tug Lane Column Found. [01-03-01]	15.0d	28-Jan-27	17-Feb-27	72.0d
12962	BG-BI-ROW-260	Set Anchor Rods at North Tug Lane Column Found. [01-03-01]	15.0d	28-Jan-27	17-Feb-27	72.0d
12963	BG-BI-ROW-270	Erect Secondary Steel at North Tug Lane [01-03-01]	20.0d	28-Jan-27	24-Feb-27	72.0d
12964	WBS - Electrical - North Tug Lane [01-03-01]		8.0d	6-Feb-26	17-Feb-26	234.0d
12965	BG-BI-ROW-170	Rough-In New Conduit for Relocation at T-18A Wall Opening [01-03-01]	2.0d	6-Feb-26	9-Feb-26	234.0d
12966	BG-BI-ROW-180	Pull Wire & Terminate w/ Shutdowns for Relocation at T-18A Wall Opening [01-...	5.0d	10-Feb-26	16-Feb-26	234.0d
12967	BG-BI-ROW-190	Demo Exist. Conduit at T-18A Wall Opening [01-03-01]	1.0d	17-Feb-26	17-Feb-26	234.0d
12968	WBS - Technology - North Tug Lane [01-03-01]		30.0d	8-Jun-26	20-Jul-26	204.0d
12969	A109150	Modify Cable Tray & Cabling - North Tug Lane [01-03-01]	30.0d	8-Jun-26	20-Jul-26	204.0d
12970	WBS - AS8 (Pod 8) [01-03-01]		254.0d	27-Feb-26	26-Feb-27	779.0d
12971	WBS - Structural - AS8 (Pod 8) [01-03-01]		254.0d	27-Feb-26	26-Feb-27	779.0d
12972	BI-ROW-BR-P5-20	Remove Moveable Concrete Barriers at OH Door Openings in AS5 thru AS8 [01...	2.0d	27-Feb-26	2-Mar-26	210.0d
12973	BI-ROW-BR-P5-40	Demo Exist. Metal Rail Impact Protection & Bollards Around East Pods [01-03-...	2.0d	3-Mar-26	4-Mar-26	363.0d
12974	BI-ROW-BR-P8-130	Demo Housekeeping Pad Beneath Former AHU-B9 [01-03-01]	2.0d	24-Mar-26	25-Mar-26	370.0d
12975	BI-ROW-BR-P8-150	Demo BHS Access Platform in AS8 - Area G [01-03-01]	3.0d	4-Jan-27	6-Jan-27	15.0d
12976	BI-ROW-BR-P8-100	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS8 [01-03-01]	15.0d	7-Jan-27	27-Jan-27	0.0d
12977	BI-ROW-BR-P8-160	Patch & Seal Concrete @ Former BHS Access Platform in AS8 - Area G [01-03-...	3.0d	7-Jan-27	11-Jan-27	117.0d
12978	BI-ROW-BR-P8-170	Patch & Seal Concrete @ Former Concrete Barrier Wall Locations in AS8 [01-03...	5.0d	28-Jan-27	3-Feb-27	129.0d

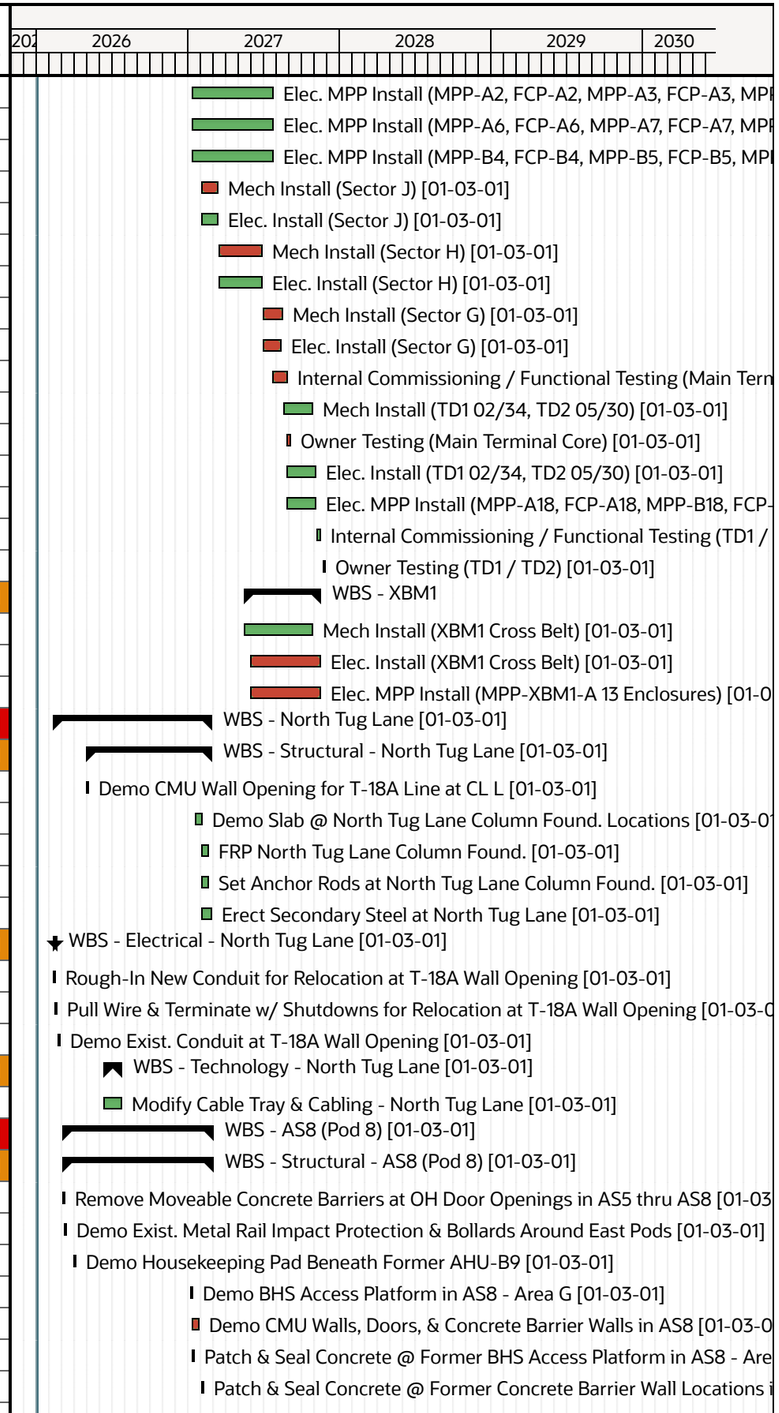


	ID	Name	Dur	Start	Finish	TF
12979	BG-DM-MCP-1120	Demo Exist. Housekeeping Pad Beneath Former MCP 11 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	138.0d
12980	BG-DM-MCP-3960	Demo Exist. Housekeeping Pad Beneath Former MCP 16 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	783.0d
12981	BG-DM-MCP-AS-460	Demo Exist. Housekeeping Pad Beneath Former MCP 39 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	786.0d
12982	BG-DM-MCP-1130	Patch & Seal Concrete @ Former MCP 11 Housekeeping Pad [01-03-01]	3.0d	12-Feb-27	16-Feb-27	138.0d
12983	BG-DM-MCP-3970	Patch & Seal Concrete @ Former MCP 16 Housekeeping Pad [01-03-01]	3.0d	12-Feb-27	16-Feb-27	783.0d
12984	BI-ROW-BR-P5-110	Patch & Seal Concrete @ Former Metal Rail & Bollard Locations at AS5 thru AS...	5.0d	17-Feb-27	23-Feb-27	138.0d
12985	BG-DM-MCP-AS-470	Patch & Seal Concrete @ Former MCP 39 Housekeeping Pad [01-03-01]	3.0d	17-Feb-27	19-Feb-27	783.0d
12986	BI-ROW-BR-P8-140	Patch & Seal Concrete @ Former AHU-B9 Housekeeping Pad [01-03-01]	3.0d	24-Feb-27	26-Feb-27	138.0d
12987	WBS - Architectural - AS8 (Pod 8) [01-03-01]		2.0d	27-Feb-26	2-Mar-26	210.0d
12988	BI-ROW-BR-P5-10	Set-Up Temp Barriers Around AS5 thru AS8 & Tug Lane Crossover Near Existin...	2.0d	27-Feb-26	2-Mar-26	210.0d
12989	WBS - Electrical - AS8 (Pod 8) [01-03-01]		30.0d	27-Feb-26	9-Apr-26	187.0d
12990	BI-ROW-BR-P5-140	Install Temp Lighting Throughout East End of Main Terminal [01-03-01]	5.0d	27-Feb-26	5-Mar-26	187.0d
12991	BI-ROW-BR-P8-70	Demo/Relocate Existing Elec. Devices, Lighting, & Conduit in AS8 [01-03-01]	15.0d	6-Mar-26	26-Mar-26	187.0d
12992	BI-ROW-BR-P8-80	Re-Support Elec. Panels in AS8 [01-03-01]	10.0d	27-Mar-26	9-Apr-26	187.0d
12993	WBS - Mechanical/Plumbing - AS8 (Pod 8) [01-03-01]		12.0d	6-Mar-26	23-Mar-26	222.0d
12994	BI-ROW-BR-P8-10	Demo Exist. Wall Louvers & Wall-Mounted Circulation Fan in AS8 [01-03-01]	2.0d	6-Mar-26	9-Mar-26	210.0d
12995	BI-ROW-BR-P8-20	Demo & Cap Existing High Supply Ductwork in AS8 [01-03-01]	5.0d	10-Mar-26	16-Mar-26	222.0d
12996	BI-ROW-BR-P8-120	Demo & Remove AHU-B9, Associated Ductwork, & Associated Chilled Water Pi...	5.0d	17-Mar-26	23-Mar-26	222.0d
12997	WBS - Technology - AS8 (Pod 8) [01-03-01]		15.0d	27-Feb-26	19-Mar-26	202.0d
12998	BI-ROW-BR-P8-30	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS8 - Area G [...	10.0d	27-Feb-26	12-Mar-26	207.0d
12999	BI-ROW-BR-P8-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring in AS8 - ...	15.0d	27-Feb-26	19-Mar-26	202.0d
13000	WBS - AS7 (Pod 7)		243.0d	13-Mar-26	25-Feb-27	118.0d
13001	WBS - Structural - AS7 (Pod 7) [01-03-01]		224.0d	9-Apr-26	25-Feb-27	118.0d
13002	BI-ROW-BR-P7-110	Demo Housekeeping Pad Beneath Former AHU-B8 [01-03-01]	2.0d	9-Apr-26	10-Apr-26	303.0d
13003	BI-ROW-BR-P7-120	Patch & Seal Concrete @ Former AHU-B8 Housekeeping Pad [01-03-01]	3.0d	13-Apr-26	15-Apr-26	303.0d
13004	BI-ROW-BR-P7-70	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS7 [01-03-01]	15.0d	28-Jan-27	17-Feb-27	9.0d
13005	BG-DM-MCP-4000	Demo Exist. Housekeeping Pad Beneath Former MCP 15 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	16.0d
13006	BG-DM-MCP-4010	Patch & Seal Concrete @ Former MCP 15 Housekeeping Pad [01-03-01]	3.0d	12-Feb-27	16-Feb-27	16.0d
13007	BI-ROW-BR-P7-130	Demo BHS Access Platform in AS7 [01-03-01]	3.0d	18-Feb-27	22-Feb-27	9.0d
13008	BI-ROW-BR-P7-150	Patch & Seal Concrete @ Former Concrete Barrier Wall Locations in AS7 [01-03...	5.0d	18-Feb-27	24-Feb-27	119.0d
13009	BI-ROW-BR-P7-140	Patch & Seal Concrete @ Former BHS Access Platform in AS7 [01-03-01]	3.0d	23-Feb-27	25-Feb-27	9.0d
13010	WBS - Electrical - AS7 (Pod 7) [01-03-01]		25.0d	10-Apr-26	14-May-26	194.0d
13011	BI-ROW-BR-P7-60	Demo/Relocate Existing Elec. Devices, Lighting, & Conduit in AS7 - Area F [01-...	15.0d	10-Apr-26	30-Apr-26	194.0d
13012	BI-ROW-BR-P7-90	Re-Support Elec. Panels in AS7 - Area F [01-03-01]	10.0d	1-May-26	14-May-26	194.0d
13013	WBS - Mechanical/Plumbing - AS7 (Pod 7) [01-03-01]		12.0d	24-Mar-26	8-Apr-26	262.0d
13014	BI-ROW-BR-P7-10	Demo Exist. Wall Louver in AS7 [01-03-01]	2.0d	24-Mar-26	25-Mar-26	222.0d
13015	BI-ROW-BR-P7-20	Demo & Cap Existing High & Low Supply Ductwork in AS7 01-03-01]	5.0d	26-Mar-26	1-Apr-26	262.0d
13016	BI-ROW-BR-P7-100	Demo & Remove AHU-B8, Associated Ductwork, & Associated Chilled Water Pi...	5.0d	2-Apr-26	8-Apr-26	262.0d
13017	WBS - Technology - AS7 (Pod 7) [01-03-01]		20.0d	13-Mar-26	9-Apr-26	211.0d
13018	BI-ROW-BR-P7-30	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS7 - Area F [...	10.0d	13-Mar-26	26-Mar-26	221.0d
13019	BI-ROW-BR-P7-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring in AS7 - ...	15.0d	20-Mar-26	9-Apr-26	204.0d
13020	WBS - AS6 (Pod 6)		257.0d	27-Mar-26	31-Mar-27	99.0d

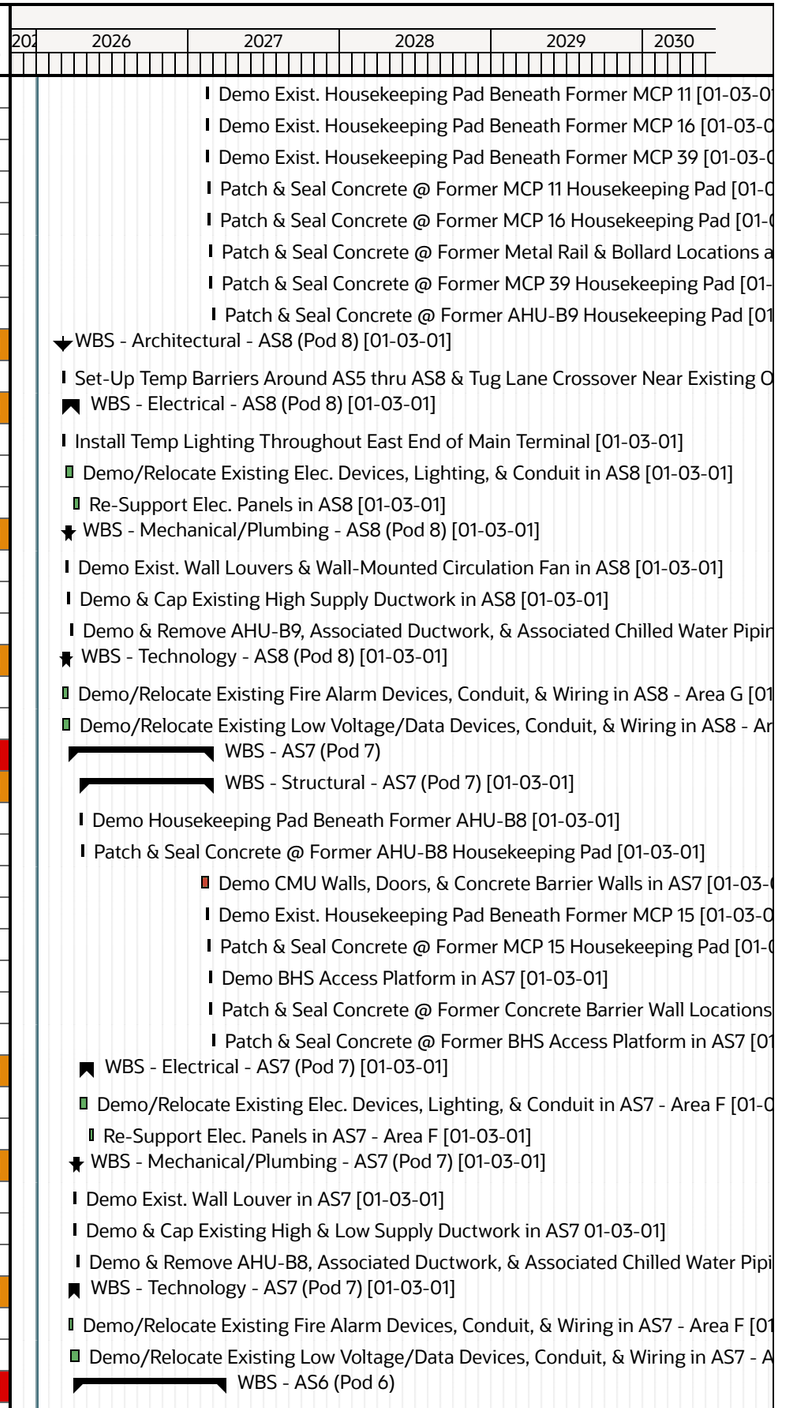


ID	Name	Dur	Start	Finish	TF
13021	WBS - Structural - AS6 (Pod 6) [01-03-01]	235.0d	28-Apr-26	31-Mar-27	99.0d
13022	BI-ROW-BR-P6-50	Demo Housekeeping Pad Beneath Former AHU-B7 [01-03-01]	2.0d	28-Apr-26	29-Apr-26	290.0d
13023	BI-ROW-BR-P6-60	Patch & Seal Concrete @ Former AHU-B7 Housekeeping Pad [01-03-01]	3.0d	30-Apr-26	4-May-26	290.0d
13024	BG-DM-MCP-3620	Demo Exist. Housekeeping Pad Beneath Former MCP 36 [01-03-01]	1.0d	7-Dec-26	7-Dec-26	137.0d
13025	BG-DM-MCP-3630	Patch & Seal Concrete @ Former MCP 36 Housekeeping Pad [01-03-01]	3.0d	8-Dec-26	10-Dec-26	137.0d
13026	BG-DM-MCP-3720	Demo Exist. Housekeeping Pad Beneath Former MCP 37 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	91.0d
13027	BG-DM-MCP-3730	Patch & Seal Concrete @ Former MCP 37 Housekeeping Pad [01-03-01]	3.0d	12-Feb-27	16-Feb-27	91.0d
13028	BI-ROW-BR-P6-140	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS6 [01-03-01]	15.0d	18-Feb-27	10-Mar-27	47.0d
13029	BI-ROW-BR-P6-150	Patch & Seal Concrete @ Former Concrete Barrier Wall Locations in AS6 [01-03...	5.0d	11-Mar-27	17-Mar-27	109.0d
13030	BI-ROW-BR-P5-250	Demo Elevated Metal Deck, Stairs, & Handrails Between AS5 & AS6 - Areas D &...	5.0d	25-Mar-27	31-Mar-27	47.0d
13031	WBS - Electrical - AS6 (Pod 6) [01-03-01]	35.0d	15-May-26	6-Jul-26	194.0d
13032	BI-ROW-BR-P6-100	Demo/Relocate Existing Elec. Devices, Lighting, & Conduit in AS6 - Area E [01-...	15.0d	15-May-26	5-Jun-26	194.0d
13033	BI-ROW-BR-P6-130	Re-Support Elec. Panels in AS6 - Area E [01-03-01]	10.0d	8-Jun-26	19-Jun-26	194.0d
13034	BI-ROW-BR-P5-210	Demo/Relocate Existing Elec. Devices, Lighting & Conduit Attached to Platform...	10.0d	22-Jun-26	6-Jul-26	194.0d
13035	WBS - Mechanical/Plumbing - AS6 (Pod 6) [01-03-01]	13.0d	9-Apr-26	27-Apr-26	264.0d
13036	BI-ROW-BR-P6-40	Demo Exist. Wall Mounted Circulation Fan & Wall Louver in AS6 [01-03-01]	3.0d	9-Apr-26	13-Apr-26	262.0d
13037	BI-ROW-BR-P6-70	Demo & Cap Existing High Supply Ductwork in AS6 [01-03-01]	5.0d	14-Apr-26	20-Apr-26	264.0d
13038	BI-ROW-BR-P6-30	Demo & Remove AHU-B7, Associated Ductwork, & Associated Chilled Water Pi...	5.0d	21-Apr-26	27-Apr-26	264.0d
13039	WBS - Technology - AS6 (Pod 6) [01-03-01]	35.0d	27-Mar-26	14-May-26	244.0d
13040	BI-ROW-BR-P6-80	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS6 - Area E [...	10.0d	27-Mar-26	9-Apr-26	259.0d
13041	BI-ROW-BR-P5-180	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring Attached to Platf...	10.0d	10-Apr-26	23-Apr-26	259.0d
13042	BI-ROW-BR-P6-90	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring in AS6 - ...	15.0d	10-Apr-26	30-Apr-26	204.0d
13043	BI-ROW-BR-P5-190	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring Attache...	10.0d	1-May-26	14-May-26	204.0d
13044	WBS - AS5 (Pod 5)	276.0d	5-Mar-26	5-Apr-27	753.0d
13045	WBS - Structural - AS5 (Pod 5) [01-03-01]	273.0d	5-Mar-26	31-Mar-27	756.0d
13046	BI-ROW-BR-P5-80	Demo (12) Existing Free-Standing Bollards Surrounding OS Line - Area H [01-0...	4.0d	5-Mar-26	10-Mar-26	363.0d
13047	BI-ROW-BR-P5-260	Patch & Seal Concrete @ Former Metal Rail & Bollard Locations Surrounding O...	5.0d	11-Mar-26	17-Mar-26	363.0d
13048	BI-ROW-BR-P5-120	Remove Existing Tug Lane Striping at Tug Crossover Between AS5 & OS Line - ...	5.0d	18-Mar-26	24-Mar-26	363.0d
13049	BI-ROW-BR-P5-60	Demo Housekeeping Pad Beneath Former AHU-B12 [01-03-01]	2.0d	15-May-26	18-May-26	972.0d
13050	BI-ROW-BR-P5-90	Patch & Seal Concrete @ Former AHU-B12 Housekeeping Pad [01-03-01]	3.0d	19-May-26	21-May-26	972.0d
13051	BG-DM-MCP-3220	Demo Exist. Housekeeping Pad Beneath Former MCP 32 [01-03-01]	1.0d	11-Feb-27	11-Feb-27	364.0d
13052	BG-DM-MCP-3230	Patch & Seal Concrete @ Former MCP 32 Housekeeping Pad [01-03-01]	3.0d	12-Feb-27	16-Feb-27	364.0d
13053	BI-ROW-BR-P5-230	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS5 - Area D [01-03-01]	10.0d	11-Mar-27	24-Mar-27	47.0d
13054	BI-ROW-BR-P5-270	Patch & Seal Concrete @ Former Concrete Barrier Wall Locations in AS5 [01-03...	5.0d	25-Mar-27	31-Mar-27	104.0d
13055	WBS - Architectural - AS5 (Pod 5) [01-03-01]	3.0d	1-Apr-27	5-Apr-27	104.0d
13056	BI-ROW-BR-P5-130	Paint New Tug Lane Striping at Former Tug Crossover Between AS5 & OS Line -...	3.0d	1-Apr-27	5-Apr-27	104.0d
13057	WBS - Electrical - AS5 (Pod 5) [01-03-01]	25.0d	7-Jul-26	10-Aug-26	194.0d
13058	BI-ROW-BR-P5-170	Demo/Relocate Existing Elec. Devices, Lighting & Conduit in AS5- Area D [01-0...	15.0d	7-Jul-26	27-Jul-26	194.0d
13059	BI-ROW-BR-P5-200	Re-Support Elec. Panels in AS5 - Area D [01-03-01]	10.0d	28-Jul-26	10-Aug-26	194.0d
13060	WBS - Mechanical/Plumbing - AS5 (Pod 5) [01-03-01]	13.0d	28-Apr-26	14-May-26	973.0d
13061	BI-ROW-BR-P5-70	Demo Exist. Wall Mounted Circulation Fan & Wall Louvers in AS5 [01-03-01]	3.0d	28-Apr-26	30-Apr-26	264.0d
13062	BI-ROW-BR-P5-100	Demo & Cap Existing High Supply Ductwork in AS5 [01-03-01]	5.0d	1-May-26	7-May-26	972.0d

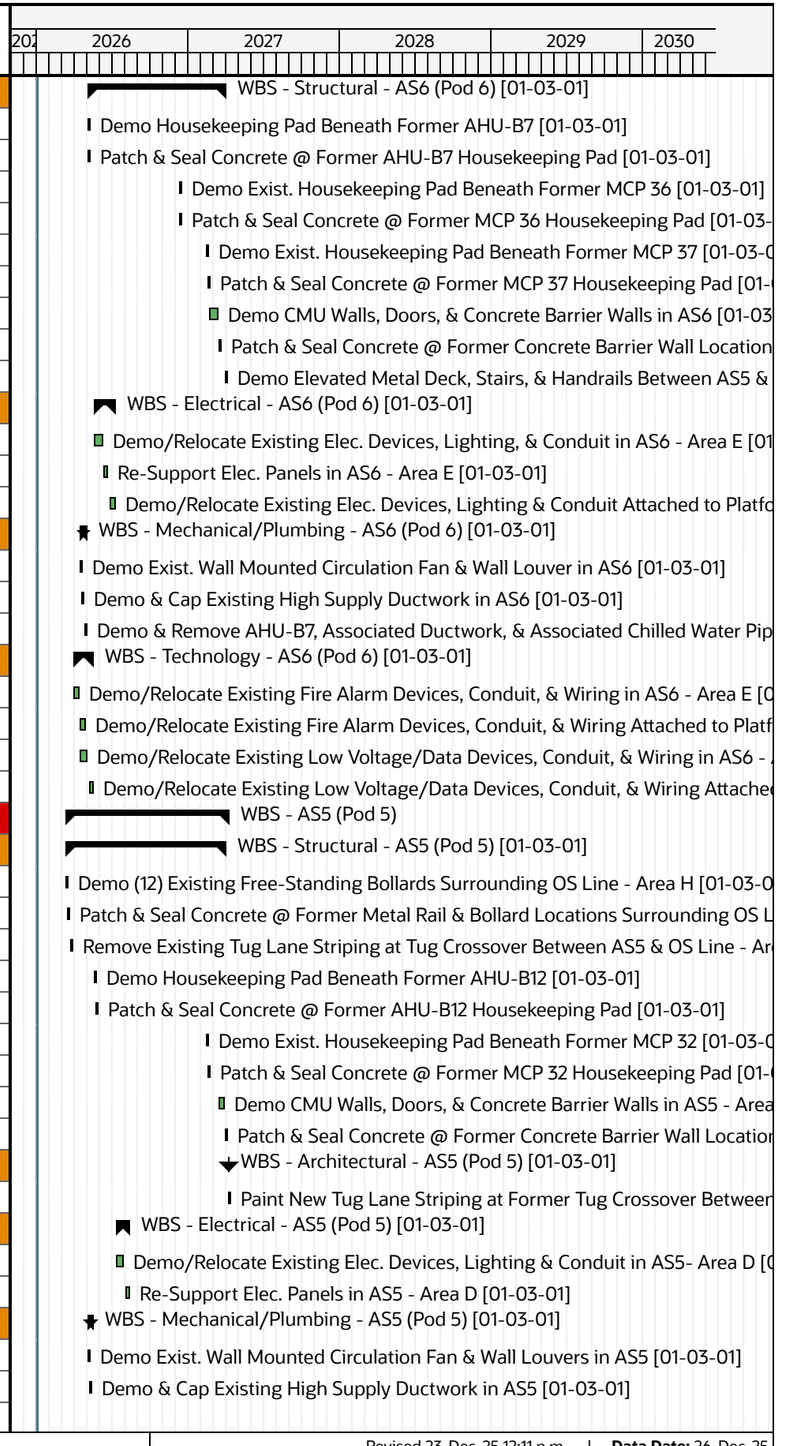


	ID	Name	Dur	Start	Finish	TF
13063	BI-ROW-BR-P5-30	Demo & Remove AHU-B12, Associated Ductwork, & Associated Chilled Water P...	5.0d	8-May-26	14-May-26	972.0d
13064	WBS - Technology - AS5 (Pod 5) [01-03-01]		30.0d	24-Apr-26	5-Jun-26	239.0d
13065	BI-ROW-BR-P5-150	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS5 - Area D [...	10.0d	24-Apr-26	7-May-26	259.0d
13066	BI-ROW-BR-P5-160	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring in AS5 - ...	15.0d	15-May-26	5-Jun-26	204.0d
13067	WBS - Bag Claim Ceiling - Carousels C12 & C13		387.0d	6-Mar-26	13-Sep-27	641.0d
13068	WBS - Structural - Bag Claim Ceiling (C12 & C13) [01-03-01]		53.0d	15-Mar-27	26-May-27	716.0d
13069	BI-ROW-BCC-226	Layout CFRP - Bag Claim Ceiling (C12 & C13) [01-03-01]	5.0d	15-Mar-27	19-Mar-27	87.0d
13070	BI-ROW-BCC-306	Apply CFRP - Bag Claim Ceiling (C12 & C13) [01-03-01]	25.0d	22-Apr-27	26-May-27	715.0d
13071	WBS - Architectural - Bag Claim Ceiling (C12 & C13) [01-03-01]		30.0d	11-Mar-27	21-Apr-27	716.0d
13072	BI-ROW-BCC-700	Remove & Store Signage [01-03-01]	2.0d	11-Mar-27	12-Mar-27	743.0d
13073	BI-ROW-BCC-710	Remove & Store Ceiling Panels & Grid [01-03-01]	10.0d	11-Mar-27	24-Mar-27	87.0d
13074	BI-ROW-BCC-720	Demo Hard-Lid Ceiling & Framing [01-03-01]	10.0d	11-Mar-27	24-Mar-27	87.0d
13075	BI-ROW-BCC-230	Install Temp Wall Partitions Around Baggage Claim Ceiling Demo [01-03-01]	3.0d	19-Apr-27	21-Apr-27	87.0d
13076	WBS - Electrical - Bag Claim Ceiling (C12 & C13) [01-03-01]		123.0d	22-Mar-27	13-Sep-27	101.0d
13077	BI-ROW-BCC-740	Pre-BHS Elec. Systems Modifications [01-03-01]	20.0d	22-Mar-27	16-Apr-27	87.0d
13078	BG-DM-MCP-4030	Post-BHS Elec. Systems Modifications [01-03-01]	20.0d	16-Aug-27	13-Sep-27	101.0d
13079	WBS - Mechanical/Plumbing - Bag Claim Ceiling (C12 & C13) [01-03-01]		387.0d	6-Mar-26	13-Sep-27	101.0d
13080	A109000	Test & Balance Pre-HVAC Demo/Modification [01-03-01]	5.0d	6-Mar-26	12-Mar-26	346.0d
13081	BI-ROW-BCC-750	Pre-BHS HVAC & Plumbing Systems Modifications [01-03-01]	20.0d	22-Mar-27	16-Apr-27	87.0d
13082	BI-ROW-BCC-760	Post-BHS HVAC & Plumbing Systems Modifications [01-03-01]	20.0d	16-Aug-27	13-Sep-27	101.0d
13083	WBS - Technology - Bag Claim Ceiling (C12 & C13) [01-03-01]		123.0d	22-Mar-27	13-Sep-27	101.0d
13084	BI-ROW-BCC-770	Pre-BHS Technology & Data Systems Modifications [01-03-01]	20.0d	22-Mar-27	16-Apr-27	87.0d
13085	BI-ROW-BCC-780	Post-BHS Technology & Data Systems Modifications [01-03-01]	20.0d	16-Aug-27	13-Sep-27	101.0d
13086	WBS - Fire Protection - Bag Claim Ceiling (C12 & C13) [01-03-01]		57.0d	28-Jan-27	16-Apr-27	691.0d
13087	BI-ROW-BCC-800	Post-BHS Fire Sprinkler System Modifications [01-03-01]	20.0d	28-Jan-27	24-Feb-27	727.0d
13088	BI-ROW-BCC-790	Pre-BHS Fire Sprinkler System Modifications [01-03-01]	20.0d	22-Mar-27	16-Apr-27	87.0d
13089	WBS - Transport Line Enclosure		110.0d	29-Apr-27	4-Oct-27	573.0d
13090	WBS - Structural/Demo - Transport Line Enclosure [01-03-01]		53.0d	6-May-27	21-Jul-27	275.0d
13091	BI-ROW-TSL-50	Demo & Remove Existing Curbside Airline Counters, Miscellaneous Millwork, & ...	5.0d	6-May-27	12-May-27	49.0d
13092	BI-ROW-TSL-320	Remove & Demo Plaster Ceiling & Grid in Enclosure - Transport Line Enclosure ...	3.0d	13-May-27	17-May-27	49.0d
13093	BI-ROW-TSL-100	Demo & Remove Existing Store Front Glazing & Wall - Transport Line Enclosure...	5.0d	18-May-27	24-May-27	49.0d
13094	BI-ROW-TSL-340	Demo Structural Steel Framing & AHU Pans in Mech. Mezzanine - Transport Lin...	10.0d	25-May-27	8-Jun-27	49.0d
13095	BI-ROW-TSL-330	Demo Exist. Tile & Carpet Flooring - Transport Line Enclosure [01-03-01]	5.0d	9-Jun-27	15-Jun-27	49.0d
13096	BI-ROW-TSL-300	Slab Cut-Out at Existing Corridor - Transport Line Enclosure [01-03-01]	5.0d	16-Jun-27	22-Jun-27	49.0d
13097	BI-ROW-TSL-60	Demo Interior Access Doors - Transport Line Enclosure [01-03-01]	1.0d	23-Jun-27	23-Jun-27	294.0d
13098	A109010	Erect Steel at BHS Slab Openings - Transport Line Enclosure [01-03-01]	10.0d	23-Jun-27	7-Jul-27	128.0d
13099	A109020	Retrofit Slab at BHS Slab Openings - Transport Line Enclosure [01-03-01]	10.0d	8-Jul-27	21-Jul-27	138.0d
13100	WBS - Architectural - Transport Line Enclosure [01-03-01]		108.0d	29-Apr-27	30-Sep-27	294.0d
13101	BI-ROW-TSL-70	Relocate Existing Cart Station [New Location TBD] - Transport Line Enclosure [...	2.0d	29-Apr-27	30-Apr-27	49.0d
13102	BI-ROW-TSL-10	Install Temp Wall Partitions Around C7 & C9 Curbside Ticket Counter Space & C...	3.0d	3-May-27	5-May-27	49.0d
13103	BI-ROW-TSL-30	Remove & Store Existing Ceiling Tile & Grid in Corridor - Transport Line Enclosu...	3.0d	6-May-27	10-May-27	69.0d
13104	BI-ROW-TSL-130	Frame Walls for New BHS Enclosure, Doghouse, & Door Infills - Transport Line ...	15.0d	24-Jun-27	15-Jul-27	294.0d

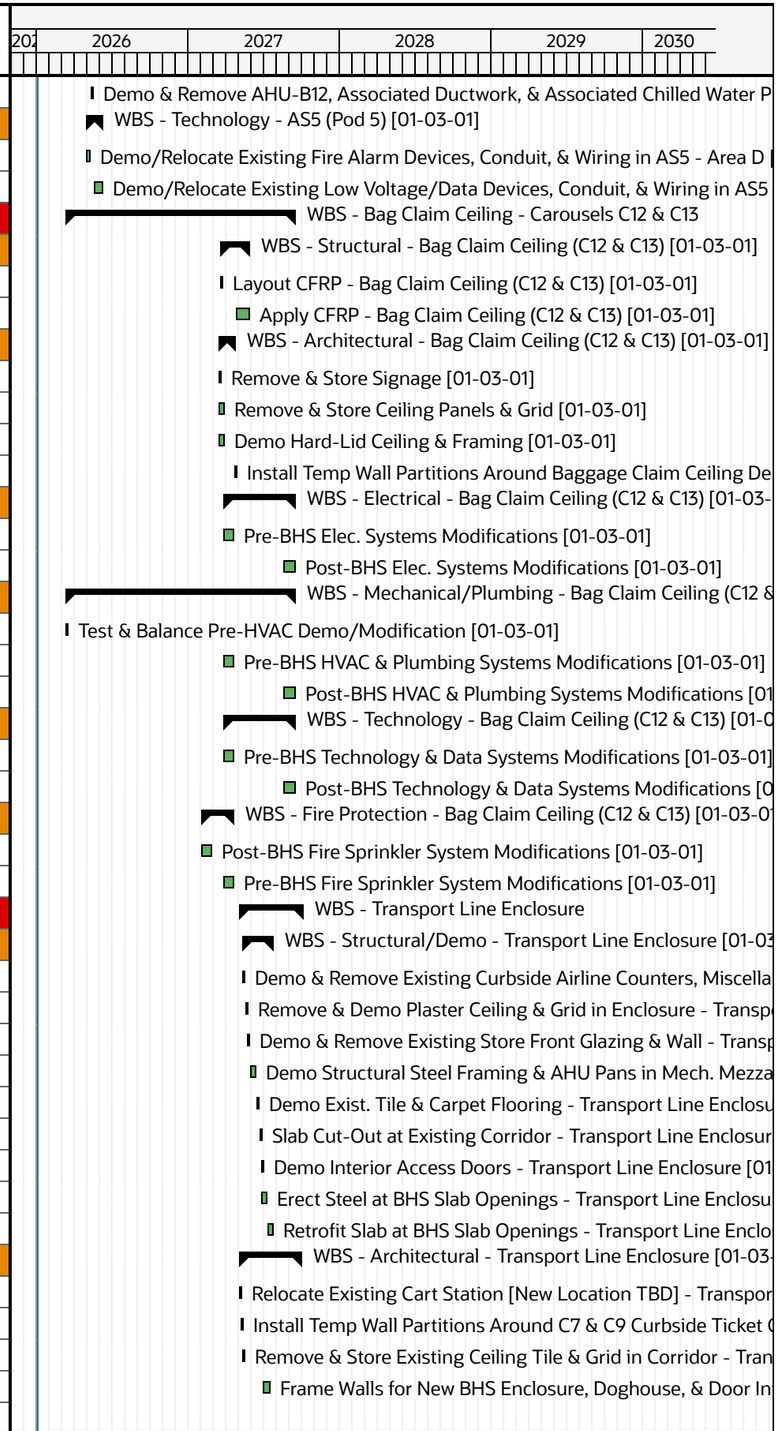

	ID	Name	Dur	Start	Finish	TF
13105	BI-ROW-TSL-190	Wall Close-In Inspection - Transport Line Enclosure [01-03-01]	1.0d	16-Jul-27	16-Jul-27	294.0d
13106	BI-ROW-TSL-170	Install Door Frames - Transport Line Enclosure [01-03-01]	1.0d	16-Jul-27	16-Jul-27	327.0d
13107	BI-ROW-TSL-200	Insulate & Install Wood Blocking - Transport Line Enclosure [01-03-01]	5.0d	19-Jul-27	23-Jul-27	294.0d
13108	BI-ROW-TSL-180	Install Doors - Transport Line Enclosure [01-03-01]	2.0d	19-Jul-27	20-Jul-27	327.0d
13109	BI-ROW-TSL-210	Hang, Tape, & Finish Exterior Walls - Transport Line Enclosure [01-03-01]	10.0d	26-Jul-27	6-Aug-27	294.0d
13110	BI-ROW-TSL-220	Hang, Tape, & Finish Interior Walls - Transport Line Enclosure [01-03-01]	10.0d	9-Aug-27	20-Aug-27	304.0d
13111	BI-ROW-TSL-230	Install Exterior Glazing Finish - Transport Line Enclosure [01-03-01]	20.0d	9-Aug-27	3-Sep-27	294.0d
13112	BI-ROW-TSL-290	Apply Head of Wall Sealant - Transport Line Enclosure [01-03-01]	5.0d	30-Aug-27	3-Sep-27	304.0d
13113	BI-ROW-TSL-260	Install Tile Flooring to Match Existing - Transport Line Enclosure [01-03-01]	10.0d	7-Sep-27	20-Sep-27	294.0d
13114	BI-ROW-TSL-310	Remove Temp Wall Partitions Around C7 & C9 Curbside Ticket Counter Space - ...	3.0d	21-Sep-27	23-Sep-27	294.0d
13115	A110540	Ticket Counter Internal Punchlist	5.0d	24-Sep-27	30-Sep-27	294.0d
13116	WBS - Electrical - Transport Line Enclosure [01-03-01]		85.0d	3-May-27	31-Aug-27	307.0d
13117	BI-ROW-TSL-20	Install Temp Lighting - Transport Line Enclosure [01-03-01]	2.0d	3-May-27	4-May-27	50.0d
13118	BI-ROW-TSL-350	Demo Exist. Lighting in Ceilings - Transport Line Enclosure [01-03-01]	3.0d	13-May-27	17-May-27	54.0d
13119	BI-ROW-TSL-140	In-Wall Elec. Rough-In - Transport Line Enclosure [01-03-01]	10.0d	1-Jul-27	15-Jul-27	294.0d
13120	BI-ROW-TSL-240	Trim-Out Elec.Devices - Transport Line Enclosure [01-03-01]	5.0d	23-Aug-27	27-Aug-27	307.0d
13121	BI-ROW-TSL-280	Remove Temporary Lighting - Transport Line Enclosure [01-03-01]	2.0d	30-Aug-27	31-Aug-27	307.0d
13122	WBS - Mechanical/Plumbing - Transport Line Enclosure [01-03-01]		97.0d	18-May-27	4-Oct-27	573.0d
13123	A109030	Pre-BHS Demo/Modification of HVAC Systems - Transport Line Enclosure [01-...	10.0d	18-May-27	1-Jun-27	153.0d
13124	BI-ROW-TSL-250	Trim-Out Mech. Devices - Transport Line Enclosure [01-03-01]	5.0d	23-Aug-27	27-Aug-27	309.0d
13125	A109040	Post-BHS Demo/Modification of HVAC Systems - Transport Line Enclosure [01...	10.0d	21-Sep-27	4-Oct-27	572.0d
13126	WBS - Technology - Transport Line Enclosure [01-03-01]		41.0d	1-Jul-27	27-Aug-27	304.0d
13127	BI-ROW-TSL-150	In-Wall Technology Rough-In - Transport Line Enclosure [01-03-01]	10.0d	1-Jul-27	15-Jul-27	294.0d
13128	BI-ROW-TSL-270	Trim-Out Low-Voltage Devices - Transport Line Enclosure [01-03-01]	5.0d	23-Aug-27	27-Aug-27	304.0d
13129	WBS - Fire Protection - Transport Line Enclosure [01-03-01]		100.0d	13-May-27	4-Oct-27	563.0d
13130	BI-ROW-BCC-810	Pre-BHS Fire Sprinkler System Modifications - Transport Line Enclosure [01-03...	10.0d	13-May-27	26-May-27	652.0d
13131	BI-ROW-BCC-820	Post-BHS Fire Sprinkler System Modifications - Transport Line Enclosure [01-0...	10.0d	21-Sep-27	4-Oct-27	562.0d
13132	WBS - Transport Lines ROW [01-03-01]		75.0d	25-Jun-27	11-Oct-27	568.0d
13133	WBS - Structural - Transport Lines ROW [01-03-01]		20.0d	2-Jul-27	30-Jul-27	116.0d
13134	A109070	Erect Secondary Steel @ Drive Aisle - Transport Lines ROW [01-03-01]	20.0d	2-Jul-27	30-Jul-27	116.0d
13135	WBS - Architectural - Transport Lines ROW [01-03-01]		75.0d	25-Jun-27	11-Oct-27	568.0d
13136	BI-ROW-DA-40	Remove & Store Ceiling & Bottom Member of BHS ROW - Transport Lines ROW ...	20.0d	25-Jun-27	23-Jul-27	116.0d
13137	A109100	Re-Install Ceiling & Bottom Member of BHS ROW - Transport Lines ROW [01-0...	20.0d	14-Sep-27	11-Oct-27	567.0d
13138	WBS - Electrical - Transport Lines ROW [01-03-01]		75.0d	25-Jun-27	11-Oct-27	568.0d
13139	A109050	Pre-BHS Elec. Systems Modifications - Transport Lines ROW [01-03-01]	20.0d	25-Jun-27	23-Jul-27	116.0d
13140	A109080	Post-BHS Elec. Systems Modifications - Transport Lines ROW [01-03-01]	20.0d	14-Sep-27	11-Oct-27	567.0d
13141	WBS - Mechanical/Plumbing - Transport Lines ROW [01-03-01]		50.0d	12-Jul-27	20-Sep-27	583.0d
13142	A109110	Pre-BHS HVAC Systems Modifications - Transport Lines ROW [01-03-01]	5.0d	12-Jul-27	16-Jul-27	171.0d
13143	A109130	Post-BHS HVAC Systems Modifications - Transport Lines ROW [01-03-01]	5.0d	14-Sep-27	20-Sep-27	582.0d
13144	WBS - Technology - Transport Lines ROW [01-03-01]		55.0d	2-Jul-27	20-Sep-27	583.0d
13145	A109120	Pre-BHS Technology Systems Modifications - Transport Lines ROW [01-03-01]	5.0d	2-Jul-27	9-Jul-27	176.0d
13146	A109140	Post-BHS Technology Systems Modifications - Transport Lines ROW [01-03-01]	5.0d	14-Sep-27	20-Sep-27	582.0d

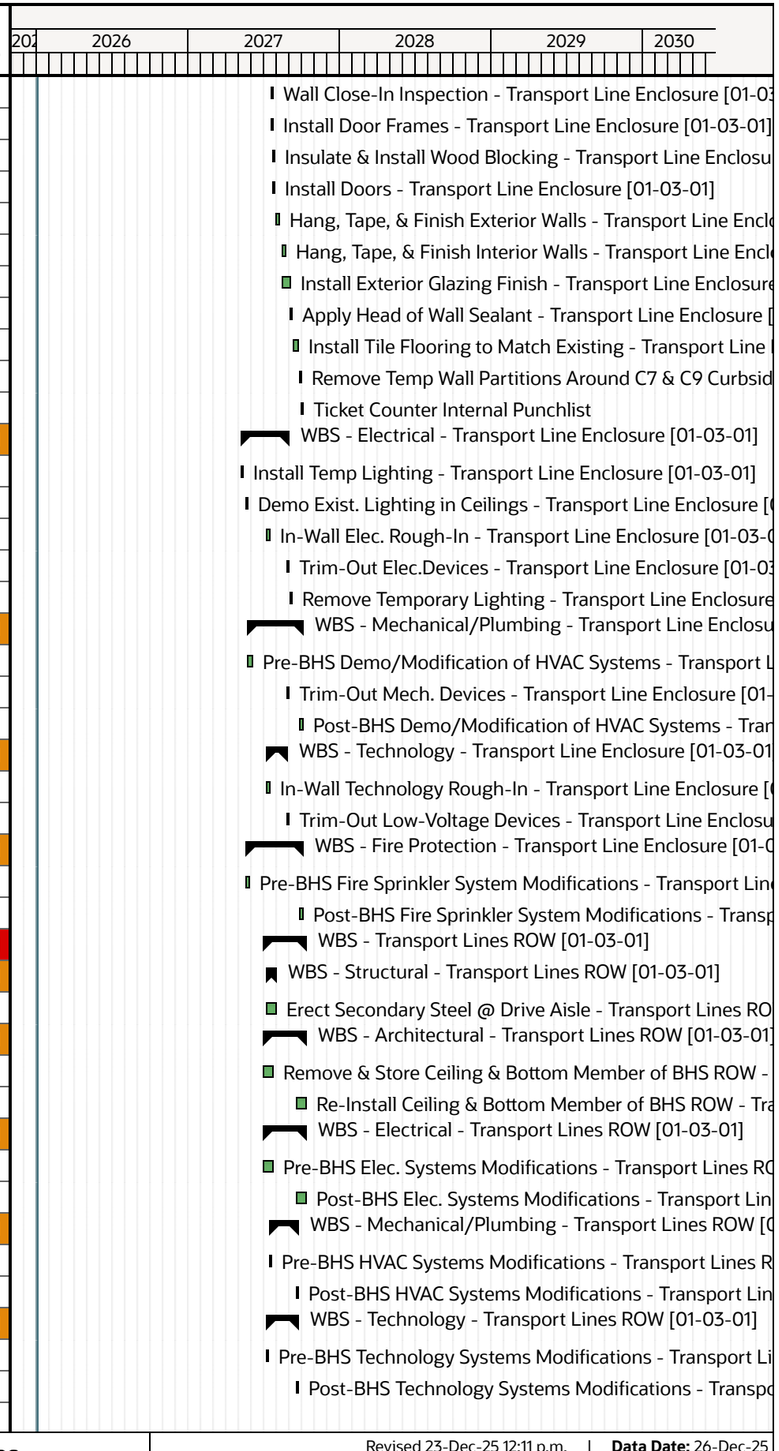


	ID	Name	Dur	Start	Finish	TF
13147	WBS - Fire Protection - Transport Lines ROW [01-03-01]		70.0d	25-Jun-27	4-Oct-27	573.0d
13148	A109060	Pre-BHS Fire Sprinkler System Modifications - Transport Lines ROW [01-03-01]	15.0d	25-Jun-27	16-Jul-27	116.0d
13149	A109090	Post-BHS Fire Sprinkler System Modifications - Transport Lines ROW [01-03-01]	15.0d	14-Sep-27	4-Oct-27	572.0d
13150	WBS - Seq 1 - Stage 3 - Step 2		63.0d	23-Jun-27	21-Sep-27	4.0d
13151	A109200	Demo CMU Wall for Temp AS3 Loop T-AL3-03 & T-BX9-06A [01-03-02]	3.0d	23-Jun-27	25-Jun-27	49.0d
13152	A109170	Elec. Systems Modifications [01-03-02]	5.0d	7-Sep-27	13-Sep-27	10.0d
13153	A109160	Fire Protection Systems Modifications [01-03-02]	5.0d	7-Sep-27	13-Sep-27	10.0d
13154	B7	BHS - Mech / Elec. Demo & Install of AS3 CBRA Loop (01-03-02)	11.0d	7-Sep-27	21-Sep-27	0.0d
13155	A7	BHS - Mech / Elec. Demo & Install of T3 & BX2 Lines (01-03-02)	3.0d	7-Sep-27	9-Sep-27	0.0d
13156	WBS - Seq 1 - Stage 3 - Step 3		402.0d	24-Apr-26	22-Nov-27	451.0d
13157	BG-CON-ER-10	Modify/Re-Route Fire Sprinkler Line at Southwest Corner of Elec. Room [01-03...	3.0d	24-Apr-26	28-Apr-26	840.0d
13158	BG-CON-ER-20	Demo Section of CMU Wall at Southwest Corner of Elec. Room [01-03-03]	3.0d	29-Apr-26	1-May-26	840.0d
13159	BG-CON-ER-30	Frame New Ceiling Infill at Southwest Corner of Elec. Room [01-03-03]	3.0d	4-May-26	6-May-26	840.0d
13160	BI-ROW-BR-P4-20	Demo Exist. Free-Standing Bollards Surrounding AS1 thru AS4 & Existing Elec. ...	10.0d	7-Sep-27	20-Sep-27	5.0d
13161	BI-ROW-BR-P4-30	Install Temp Lighting in AS4 [01-03-03]	3.0d	7-Sep-27	9-Sep-27	5.0d
13162	BI-ROW-BR-P4-40	Demo/Relocate Existing Elec. Devices, Lighting & Conduit (Including Attached t...	15.0d	10-Sep-27	30-Sep-27	6.0d
13163	BI-ROW-BR-P4-10	Re-Support Elec. Panels in AS4 [01-03-03]	10.0d	10-Sep-27	23-Sep-27	13.0d
13164	BI-ROW-BR-P4-60	Demo Exist. Wall Louvers & Wall-Mounted Circulation Fan in AS4 [01-03-03]	2.0d	10-Sep-27	13-Sep-27	11.0d
13165	BI-ROW-BR-P4-70	Demo/Relocate Existing Fire Alarm Devices, Conduit, & Wiring in AS4 [01-03-03]	10.0d	10-Sep-27	23-Sep-27	13.0d
13166	BI-ROW-BR-P4-80	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring (Includin...	15.0d	10-Sep-27	30-Sep-27	6.0d
13167	BI-ROW-BR-P3-60	Demo/Relocate Existing Elec. Devices, LTNG & Conduit at T-TXM2 Opening on ...	5.0d	10-Sep-27	16-Sep-27	12.0d
13168	BI-ROW-BR-P4-100	Demo Fire Sprinkler Piping & Heads Attached to Access Platform in AS4 [01-03...	4.0d	10-Sep-27	15-Sep-27	33.0d
13169	BI-ROW-BR-P4-110	Demo & Cap Existing High & Low Supply Ductwork in AS4 [01-03-03]	5.0d	14-Sep-27	20-Sep-27	11.0d
13170	BI-ROW-BR-P4-210	Modify Existing Sprinkler Heads in Temp System [01-03-03]	2.0d	16-Sep-27	17-Sep-27	33.0d
13171	BI-ROW-BR-P4-50	Patch & Seal Concrete @ Former Bollard Locations Outside of AS1 thru AS4 & ...	5.0d	21-Sep-27	27-Sep-27	5.0d
13172	BI-ROW-BR-P3-20	Demo Southeast Portion of EDS Platform for T-TXM2 ROW [01-03-03]	3.0d	21-Sep-27	23-Sep-27	10.0d
13173	BI-ROW-BR-P3-30	Remove Moveable Concrete Barriers Along South Wall of AS3 [01-03-03]	1.0d	21-Sep-27	21-Sep-27	10.0d
13174	BI-ROW-BR-P3-10	Demo & Cap High Supply Ductwork to T Underneath Platform [01-03-03]	3.0d	21-Sep-27	23-Sep-27	11.0d
13175	BI-ROW-BR-P3-70	Demo CMU Wall Opening for T-TXM2 Line [01-03-03]	5.0d	24-Sep-27	30-Sep-27	11.0d
13176	BI-ROW-BR-P4-120	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS4 [01-03-03]	15.0d	1-Oct-27	21-Oct-27	8.0d
13177	BI-ROW-BR-P4-170	Demo Feeders to (3) EDS UPS Machines in AS4 [01-03-03]	5.0d	1-Oct-27	7-Oct-27	6.0d
13178	BI-ROW-BR-P3-50	Install Temp Lighting in AS3 [01-03-03]	3.0d	1-Oct-27	5-Oct-27	10.0d
13179	BI-ROW-BR-P3-40	Demo/Relocate Existing Low Voltage/Data Devices, Conduit, & Wiring at T-TX...	5.0d	1-Oct-27	7-Oct-27	6.0d
13180	B8	BHS - Mech / Elec. Demo & Install of T5 / C5 [01-03-03]	2.0d	5-Oct-27	6-Oct-27	0.0d
13181	D1903	Internal Commissioning / Functional Testing / Owner Testing (C5 06/08) [01-0...	1.0d	7-Oct-27	7-Oct-27	0.0d
13182	D1905	Elec. Install MPP / FCP (A10, A11, A14, A15, B12, B16) [01-03-03]	16.0d	8-Oct-27	29-Oct-27	8.0d
13183	A8	BHS - Mech / Elec. Demo & Install of T5, BX3 & BX4 [01-03-03]	2.0d	8-Oct-27	11-Oct-27	314.0d
13184	C9	BHS - Mech / Elec. Demo [01-03-03]	6.0d	8-Oct-27	15-Oct-27	0.0d
13185	BG-DM-MCP-BX-300	Demo MCP BX3 Feeder Back to Source [HMCP-6] [01-03-03]	10.0d	12-Oct-27	25-Oct-27	334.0d
13186	BG-DM-MCP-BX-310	Demo & Remove MCP BX3 [01-03-03]	1.0d	12-Oct-27	12-Oct-27	334.0d
13187	D1896	BHS - Mech / Elec. Demo & Install of T5 / C5 [01-03-03]	1.0d	12-Oct-27	12-Oct-27	314.0d
13188	BG-DM-MCP-BX-330	Demo, Patch & Seal Concrete @ Former MCP BX3 Housekeeping Pad [01-03-03]	5.0d	13-Oct-27	19-Oct-27	334.0d

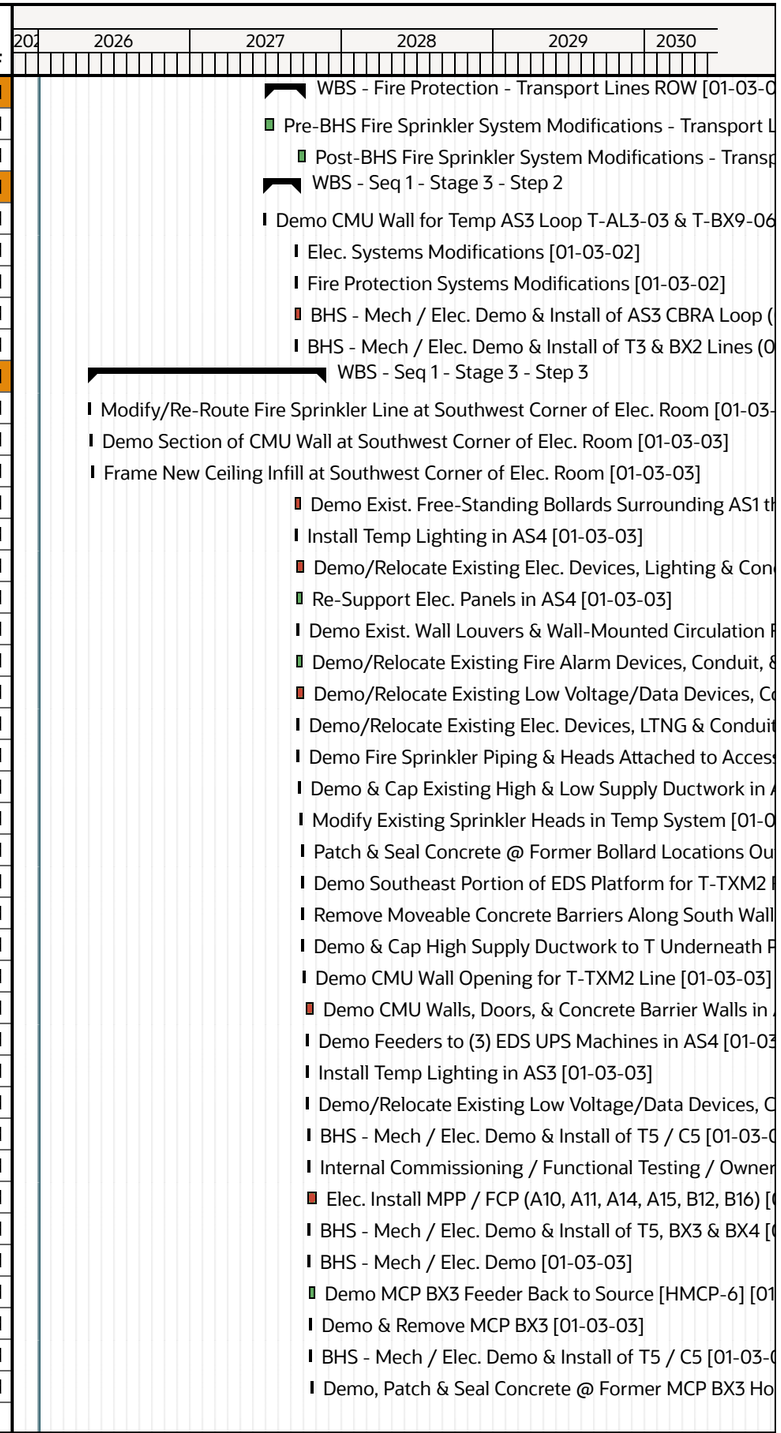


	ID	Name	Dur	Start	Finish	TF
13189	BG-DM-MCP-TF-200	Demo MCP TF2 Feeder Back to Source [HMCP-6] [01-03-03]	10.0d	18-Oct-27	29-Oct-27	298.0d
13190	BG-DM-MCP-TF-210	Demo & Remove MCP TF2 [01-03-03]	1.0d	18-Oct-27	18-Oct-27	298.0d
13191	BI-ROW-BR-P4-180	Demo BHS Access Platform in AS4 [01-03-03]	5.0d	18-Oct-27	22-Oct-27	13.0d
13192	D9	BHS - Mech / Elec. Install [01-03-03]	13.0d	18-Oct-27	3-Nov-27	0.0d
13193	BG-DM-MCP-TF-230	Demo, Patch & Seal Concrete @ Former MCP TF2 Housekeeping Pad [01-03-03]	5.0d	19-Oct-27	25-Oct-27	298.0d
13194	BI-ROW-BR-P4-140	Demo & Remove AHU-B11, Associated Ductwork, & Associated Chilled Water P…	5.0d	22-Oct-27	28-Oct-27	8.0d
13195	BI-ROW-BR-P4-190	Patch & Seal Concrete @ Former BHS Access Platform in AS4 [01-03-03]	3.0d	25-Oct-27	27-Oct-27	13.0d
13196	BI-ROW-BR-P4-200	Demo EDS Condensate Lines in AS4 [01-03-03]	3.0d	25-Oct-27	27-Oct-27	462.0d
13197	BI-ROW-BR-P4-220	Patch Fireproofing [01-03-03]	3.0d	28-Oct-27	1-Nov-27	462.0d
13198	BI-ROW-BR-P4-150	Demo Housekeeping Pad Beneath Former AHU-B11 [01-03-03]	2.0d	29-Oct-27	1-Nov-27	8.0d
13199	BI-ROW-BR-P4-160	Patch & Seal Concrete @ Former AHU-B11 Housekeeping Pad [01-03-03]	3.0d	2-Nov-27	4-Nov-27	8.0d
13200	BG-CON-ER-40	Hang, Tape, & Finish New Ceiling Infill at Southwest Corner of Elec. Room [01-0…	3.0d	2-Nov-27	4-Nov-27	462.0d
13201	D1910	Internal Commissioning / Functional Testing [01-03-03]	7.0d	4-Nov-27	12-Nov-27	0.0d
13202	D1914	Elec. Demo (T8 12/13) [01-03-03]	1.0d	15-Nov-27	15-Nov-27	0.0d
13203	D1913	Mech Demo (T8 12/13) [01-03-03]	1.0d	16-Nov-27	16-Nov-27	0.0d
13204	D1912	Mech Install (T8 12) [01-03-03]	2.0d	17-Nov-27	18-Nov-27	0.0d
13205	D1915	Elec. Install (T8 12) [01-03-03]	2.0d	19-Nov-27	22-Nov-27	0.0d
13206	D1917	Internal Commissioning / Functional Testing / Owner Testing (T8 12) [01-03-03]	1.0d	22-Nov-27	22-Nov-27	0.0d
13207	WBS - Seq 1 - Stage 3 - Step 4		58.0d	23-Nov-27	16-Feb-28	80.0d
13208	A10	BHS - Mech / Elec. Demo & Install of AS4 02/04, C9 10, T10 04/09, T11 04/0…	10.0d	23-Nov-27	8-Dec-27	0.0d
13209	B10	BHS - Inspection (01-03-04)	5.0d	9-Dec-27	15-Dec-27	0.0d
13210	C10	BHS - Mech / Elec. Demo & Install of T10 10/15, T11 10/12, TC2 02/04, MCP …	10.0d	16-Dec-27	30-Dec-27	0.0d
13211	D1930	Internal Commissioning / Functional Testing / Owner Testing [01-03-04]	2.0d	3-Jan-28	4-Jan-28	0.0d
13212	BI-ROW-BCC-150	Re-Install Stored Carousel Signage [01-03-04]	5.0d	5-Jan-28	11-Jan-28	44.0d
13213	BI-ROW-BCC-170	Re-Install Stored Ceiling Panels, Hard Lid, Grid, & Access Panels	15.0d	5-Jan-28	25-Jan-28	24.0d
13214	BI-ROW-BCC-140	Re-Install Stored Downlight Fixtures [01-03-04]	20.0d	12-Jan-28	8-Feb-28	24.0d
13215	BI-ROW-BCC-160	Re-Install Stored Speakers [01-03-04]	10.0d	12-Jan-28	25-Jan-28	34.0d
13216	BI-ROW-BCC-190	Re-Install/Trim-Out Stored Fire Alarm Devices [01-03-04]	10.0d	17-Jan-28	28-Jan-28	31.0d
13217	BG-DM-MCP-3510	Demo & Remove MCP 35	1.0d	26-Jan-28	26-Jan-28	83.0d
13218	BG-DM-MCP-3500	Demo MCP 35 Feeder Back to Source [MSB EDS 2]	10.0d	26-Jan-28	8-Feb-28	83.0d
13219	BG-DM-MCP-3520	Demo Exist. Housekeeping Pad Beneath Former MCP 35	1.0d	27-Jan-28	27-Jan-28	91.0d
13220	BG-DM-MCP-3530	Patch & Seal Concrete @ Former MCP 35 Housekeeping Pad	3.0d	28-Jan-28	1-Feb-28	91.0d
13221	BI-ROW-BCC-210	Final Clean Baggage Claim Area [01-03-04]	3.0d	9-Feb-28	11-Feb-28	24.0d
13222	BI-ROW-BCC-220	Remove Temp Wall Partitions Around Baggage Claim Ceiling Work	3.0d	14-Feb-28	16-Feb-28	24.0d
13223	WBS - Seq 1 - Stage 3 - Step 5		32.0d	4-Jan-28	16-Feb-28	83.0d
13224	D1939	Elec. Install / Recontrol (T13 01/04) [01-03-05]	2.0d	4-Jan-28	5-Jan-28	1.0d
13225	D1936	Elec. Demo (T13 05/06) [01-03-05]	1.0d	5-Jan-28	5-Jan-28	0.0d
13226	D1938	Mech Install (T13 05/06) [01-03-05]	1.0d	5-Jan-28	5-Jan-28	1.0d
13227	D1937	Mech Demo (T13 05/06) [01-03-05]	1.0d	6-Jan-28	6-Jan-28	0.0d
13228	D1940	Internal Commissioning / Functional Testing / Owner Testing [01-03-05]	1.0d	7-Jan-28	7-Jan-28	0.0d
13229	BG-DM-MCP-2820	Demo Exist. Housekeeping Pad Beneath Former MCP 28 & Remove MCP 28	2.0d	27-Jan-28	28-Jan-28	83.0d
13230	BG-DM-MCP-2800	Demo MCP 28 Feeder Back to Source [HMCP-4]	10.0d	31-Jan-28	11-Feb-28	83.0d




	ID	Name	Dur	Start	Finish	TF
13231	BG-DM-MCP-2830	Patch & Seal Concrete @ Former MCP 28 Housekeeping Pad	3.0d	14-Feb-28	16-Feb-28	83.0d
13232	WBS - Seq 1 - Stage 3 - Step 6		258.0d	22-Apr-27	26-Apr-28	66.0d
13233	A110530	Install Temp Wall Partitions [01-03-06]	5.0d	22-Apr-27	28-Apr-27	149.0d
13234	BI-ROW-BCC-850	Remove & Store Ceiling Panels & Grid [01-03-06]	10.0d	18-Oct-27	29-Oct-27	15.0d
13235	BI-ROW-BCC-860	Demo Hard-Lid Ceiling & Framing [01-03-06]	10.0d	18-Oct-27	29-Oct-27	15.0d
13236	BI-ROW-BCC-660	Layout CFRP - Sectors G & L	5.0d	1-Nov-27	5-Nov-27	15.0d
13237	BI-ROW-BCC-670	Apply CFRP at Bag Claim Ceiling - Sectors G & L	25.0d	8-Nov-27	14-Dec-27	15.0d
13238	D1942	BHS ROW Cleared, & Ceiling Removed (By Others) [01-03-06]	1.0d	15-Dec-27	15-Dec-27	15.0d
13239	A11	BHS - Mech / Elec. Demo & Install of T14 06/10, OS1 07 (O1-03-06)	26.0d	10-Jan-28	14-Feb-28	0.0d
13240	BG-DM-MCP-2700	Demo MCP 27 Feeder Back to Source [HMCP-4]	10.0d	27-Jan-28	9-Feb-28	86.0d
13241	BG-DM-MCP-2720	Demo Exist. Housekeeping Pad Beneath Former MCP 27 & Remove MCP 27	2.0d	10-Feb-28	11-Feb-28	86.0d
13242	D1948	Internal Commissioning / Functional Testing / Owner Testing (T10 & T14) [01-...	2.0d	15-Feb-28	16-Feb-28	0.0d
13243	BG-DM-MCP-2730	Patch & Seal Concrete @ Former MCP 27 Housekeeping Pad	3.0d	17-Feb-28	21-Feb-28	83.0d
13244	D1952	Elec. MPP Install (MPP-B10, FCP-B10, MPP-B13, FCP-B13, MPP-B15, FCP-B15...	45.0d	17-Feb-28	19-Apr-28	5.0d
13245	D1954	Mech Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-0...	3.0d	17-Feb-28	21-Feb-28	0.0d
13246	D1953	Elec. Demo (AX8 01/05, OS1 01/06, OS1 EDS, T13 07/14, T14 11/15) [01-03...	3.0d	17-Feb-28	21-Feb-28	0.0d
13247	D1951	Elec. Demo / Reconnect ControlNet (MCP-14, MCP-26, MCP-27, MCP-28, MCP...	5.0d	17-Feb-28	23-Feb-28	33.0d
13248	BG-DM-MCP-3100	Demo MCP 31 Feeder Back to Source [HMCP-10]	10.0d	22-Feb-28	6-Mar-28	83.0d
13249	BG-DM-MCP-3110	Demo & Remove MCP 31	1.0d	22-Feb-28	22-Feb-28	94.0d
13250	D1955	Mech Install [01-03-06]	45.0d	22-Feb-28	24-Apr-28	0.0d
13251	D1956	Elec. Install [01-03-06]	45.0d	22-Feb-28	24-Apr-28	0.0d
13252	BG-DM-MCP-3120	Demo Exist. Housekeeping Pad Beneath Former MCP 31	1.0d	23-Feb-28	23-Feb-28	94.0d
13253	BG-DM-MCP-2600	Demo MCP 26 Feeder Back to Source [HMCP-9]	10.0d	23-Feb-28	7-Mar-28	96.0d
13254	BG-DM-MCP-2610	Demo & Remove MCP 26	1.0d	23-Feb-28	23-Feb-28	96.0d
13255	BG-DM-MCP-3130	Patch & Seal Concrete @ Former MCP 31 Housekeeping Pad	3.0d	24-Feb-28	28-Feb-28	94.0d
13256	BG-DM-MCP-2620	Demo Exist. Housekeeping Pad Beneath Former MCP 26	1.0d	24-Feb-28	24-Feb-28	96.0d
13257	BG-DM-MCP-2630	Patch & Seal Concrete @ Former MCP 26 Housekeeping Pad	3.0d	29-Feb-28	2-Mar-28	94.0d
13258	BG-DM-MCP-3000	Demo MCP 30 Feeder Back to Source [HMCP-XXX]	10.0d	7-Mar-28	20-Mar-28	83.0d
13259	BG-DM-MCP-3010	Demo & Remove MCP 30	1.0d	7-Mar-28	7-Mar-28	90.0d
13260	BG-DM-MCP-3020	Demo Exist. Housekeeping Pad Beneath Former MCP 30	1.0d	8-Mar-28	8-Mar-28	90.0d
13261	BG-DM-MCP-3030	Patch & Seal Concrete @ Former MCP 30 Housekeeping Pad	3.0d	9-Mar-28	13-Mar-28	90.0d
13262	BG-DM-MCP-1400	Demo MCP 14 Feeder Back to Source [HMCP-9]	10.0d	21-Mar-28	3-Apr-28	83.0d
13263	BG-DM-MCP-1410	Demo & Remove MCP 14	1.0d	21-Mar-28	21-Mar-28	83.0d
13264	BG-DM-MCP-1420	Demo Exist. Housekeeping Pad Beneath Former MCP 14	1.0d	22-Mar-28	22-Mar-28	83.0d
13265	BG-DM-MCP-1430	Patch & Seal Concrete @ Former MCP 14 Housekeeping Pad	3.0d	23-Mar-28	27-Mar-28	83.0d
13266	D1957	Internal Commissioning / Functional Testing / Owner Testing [01-03-06]	12.0d	11-Apr-28	26-Apr-28	0.0d
13267	WBS - Seq 2 - Stage 1 - Step 1A		7.0d	27-Apr-28	5-May-28	0.0d
13268	D1960	Elec. Install (TA1 03/04 & 08/09) [02-01-01A]	2.0d	27-Apr-28	28-Apr-28	0.0d
13269	D1961	Mech Demo (TA1 15/16 & 19) [02-01-01A]	1.0d	1-May-28	1-May-28	0.0d
13270	D1962	Mech Install (TA1 03/04 & 08/09) [02-01-01A]	2.0d	2-May-28	3-May-28	0.0d
13271	D1963	Elec. Demo (TA1 15/16 & 19, MCP-13) [02-01-01A]	1.0d	4-May-28	4-May-28	0.0d
13272	D1965	Internal Commissioning / Functional Testing / Owner Testing [02-01-01A]	1.0d	5-May-28	5-May-28	0.0d

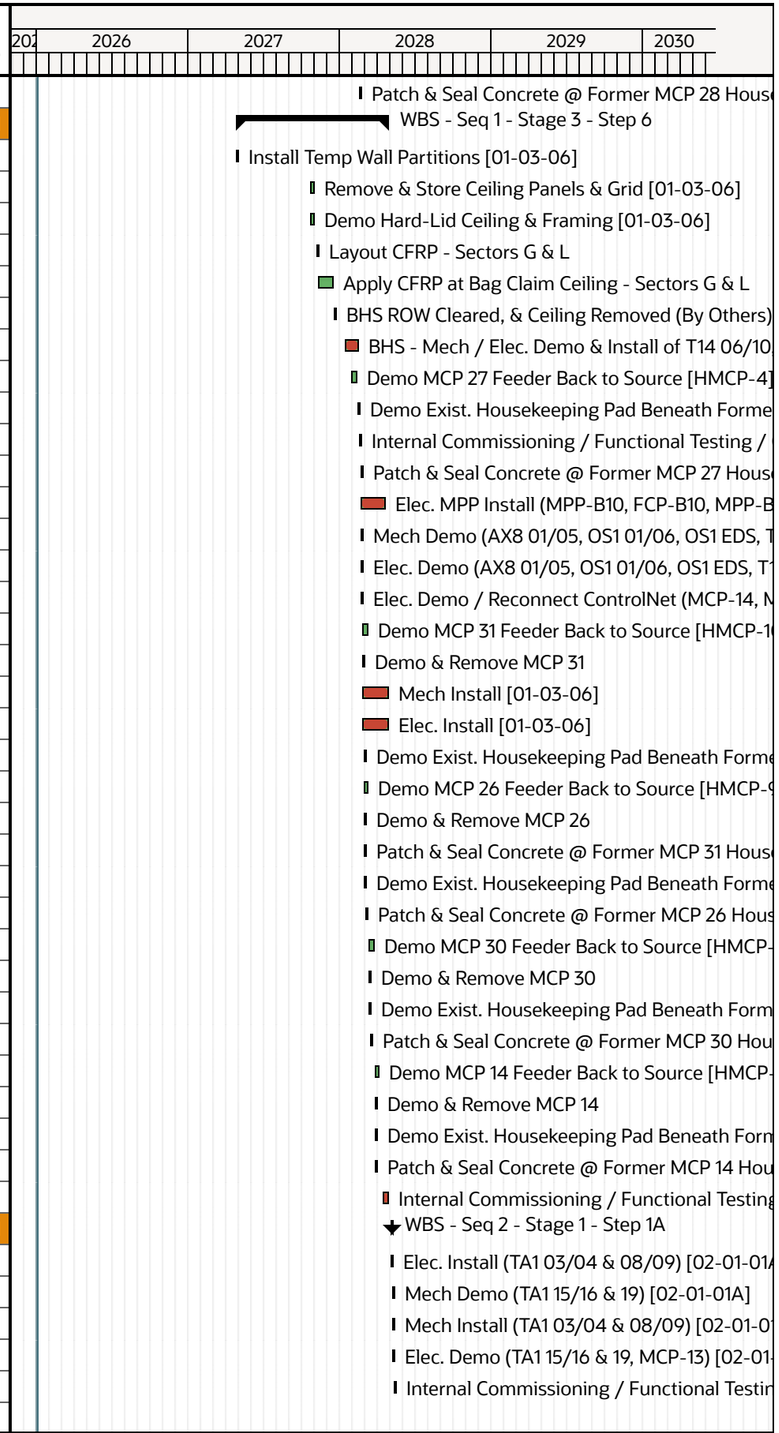


ID	Name	Dur	Start	Finish	TF
13273	WBS - Seq 2 - Stage 1 - Step 1B	5.0d	8-May-28	12-May-28	0.0d
13274	D1967 Elec. Demo (T12 26) [02-01-01B]	1.0d	8-May-28	8-May-28	0.0d
13275	D1968 Elec. Install (C8A 13) [02-01-01B]	1.0d	9-May-28	9-May-28	0.0d
13276	D1969 Internal Commissioning / Functional Testing / Owner Testing [02-01-01B]	1.0d	10-May-28	10-May-28	0.0d
13277	D1970 Mech Demo (T12 26) [02-01-01B]	1.0d	11-May-28	11-May-28	0.0d
13278	D1971 Mech Install (C8A 13) [02-01-01B]	1.0d	12-May-28	12-May-28	0.0d
13279	WBS - Seq 2 - Stage 1 - Step 1C	421.0d	19-Oct-26	14-Jun-28	31.0d
13280	A109640 Erect Secondary Steel at South Tug Lane [01-03-06]	25.0d	19-Oct-26	20-Nov-26	296.0d
13281	BI-ROW-BCC-830 Remove & Store Ceiling Panels & Grid [02-01-1C]	10.0d	22-Feb-28	6-Mar-28	21.0d
13282	BI-ROW-BCC-840 Demo Hard-Lid Ceiling & Framing [02-01-1C]	10.0d	22-Feb-28	6-Mar-28	21.0d
13283	BI-ROW-BCC-620 Layout CFRP - Sectors H & M	5.0d	7-Mar-28	13-Mar-28	21.0d
13284	BI-ROW-BCC-630 Apply CFRP at Bag Claim Ceiling - Sectors H & M	25.0d	14-Mar-28	17-Apr-28	21.0d
13285	BG-DM-MCP-1300 Demo MCP 13 Feeder Back to Source [HMCP-4]	10.0d	5-May-28	18-May-28	39.0d
13286	D1976 Elec. Conveyor Demo, MCP-07, MCP-09, MCP-17 (Reconnect ControlNet as Re…	5.0d	15-May-28	19-May-28	2.0d
13287	D1974 Mech Demo [02-01-01C]	5.0d	15-May-28	19-May-28	2.0d
13288	D1975 Mech Install [02-01-01C]	20.0d	15-May-28	12-Jun-28	0.0d
13289	D1977 Elec. Install [02-01-01C]	20.0d	15-May-28	12-Jun-28	0.0d
13290	BG-DM-MCP-900 Demo MCP 9 Feeder Back to Source [HMCP-5]	10.0d	22-May-28	5-Jun-28	38.0d
13291	BG-DM-MCP-700 Demo MCP 7 Feeder Back to Source [HMCP-5]	10.0d	22-May-28	5-Jun-28	28.0d
13292	BG-DM-MCP-1700 Demo MCP 17 Feeder Back to Source [HMCP-9]	10.0d	22-May-28	5-Jun-28	28.0d
13293	BG-DM-MCP-910 Demo & Remove MCP 9 , MCP 7, MCP 13, MCP 17	1.0d	6-Jun-28	6-Jun-28	28.0d
13294	D1978 Internal Commissioning / Functional Testing / Owner Testing [02-01-01C]	7.0d	6-Jun-28	14-Jun-28	0.0d
13295	BG-DM-MCP-920 Demo Exist. Housekeeping Pad Beneath Former MCP 9, MCP 7, MCP 13, MCP 17	2.0d	7-Jun-28	8-Jun-28	28.0d
13296	BG-DM-MCP-930 Patch & Seal Concrete @ Former MCP 9, MCP 7, MCP 13, MCP 17 Housekeepin…	3.0d	9-Jun-28	13-Jun-28	28.0d
13297	WBS - Baggage Handling System [02-01-1C]	100.0d	24-Jan-28	12-Jun-28	2.0d
13298	WBS - XBM2	100.0d	24-Jan-28	12-Jun-28	2.0d
13299	D1980 Mech Install (XBM2 Cross Belt) [02-01-01C]	100.0d	24-Jan-28	12-Jun-28	2.0d
13300	D1981 Elec. Install (XBM2 Cross Belt) [02-01-01C]	100.0d	24-Jan-28	12-Jun-28	2.0d
13301	WBS - Seq 2 - Stage 1 - Step 2A	3.0d	21-Jul-28	25-Jul-28	0.0d
13302	A12 BHS - Mech / Elec. Demo & Install of C6 04/05 (02-01-2A)	3.0d	21-Jul-28	25-Jul-28	0.0d
13303	D1991 Internal Commissioning / Functional Testing / Owner Testing [02-01-02A]	1.0d	25-Jul-28	25-Jul-28	0.0d
13304	WBS - Seq 2 - Stage 1 - Step 2B	32.0d	14-Jun-28	28-Jul-28	0.0d
13305	D1993 BHS ROW Cleared, & Ceiling Removed (By Others) [02-01-2B]	1.0d	14-Jun-28	14-Jun-28	28.0d
13306	A13 BHS - Mech / Elec. Demo & Install of T12E 01/03 [02-01-02B]	3.0d	26-Jul-28	28-Jul-28	0.0d
13307	D2000 Internal Commissioning / Functional Testing / Owner Testing [02-01-02B]	1.0d	28-Jul-28	28-Jul-28	0.0d
13308	WBS - Seq 2 - Stage 1 - Step 2C	3.0d	31-Jul-28	2-Aug-28	0.0d
13309	A14 BHS - Mech / Elec. Demo & Install of C5 17 (02-01-02C)	2.0d	31-Jul-28	1-Aug-28	0.0d
13310	D2007 Internal Commissioning / Functional Testing [02-01-02C]	1.0d	2-Aug-28	2-Aug-28	0.0d
13311	WBS - Seq 2 - Stage 1 - Step 2D	20.0d	3-Aug-28	30-Aug-28	21.0d
13312	A15 BHS - Mech / Elec. Demo & Install of C5 09/10, T8 11, OSRM6 01, OSRM7 01 (…	10.0d	3-Aug-28	16-Aug-28	0.0d
13313	BG-DM-MCP-300 Demo MCP 1 Feeder Back to Source [HMCP-3]	10.0d	17-Aug-28	30-Aug-28	21.0d
13314	BG-DM-MCP-310 Demo & Remove MCP 1	1.0d	17-Aug-28	17-Aug-28	21.0d

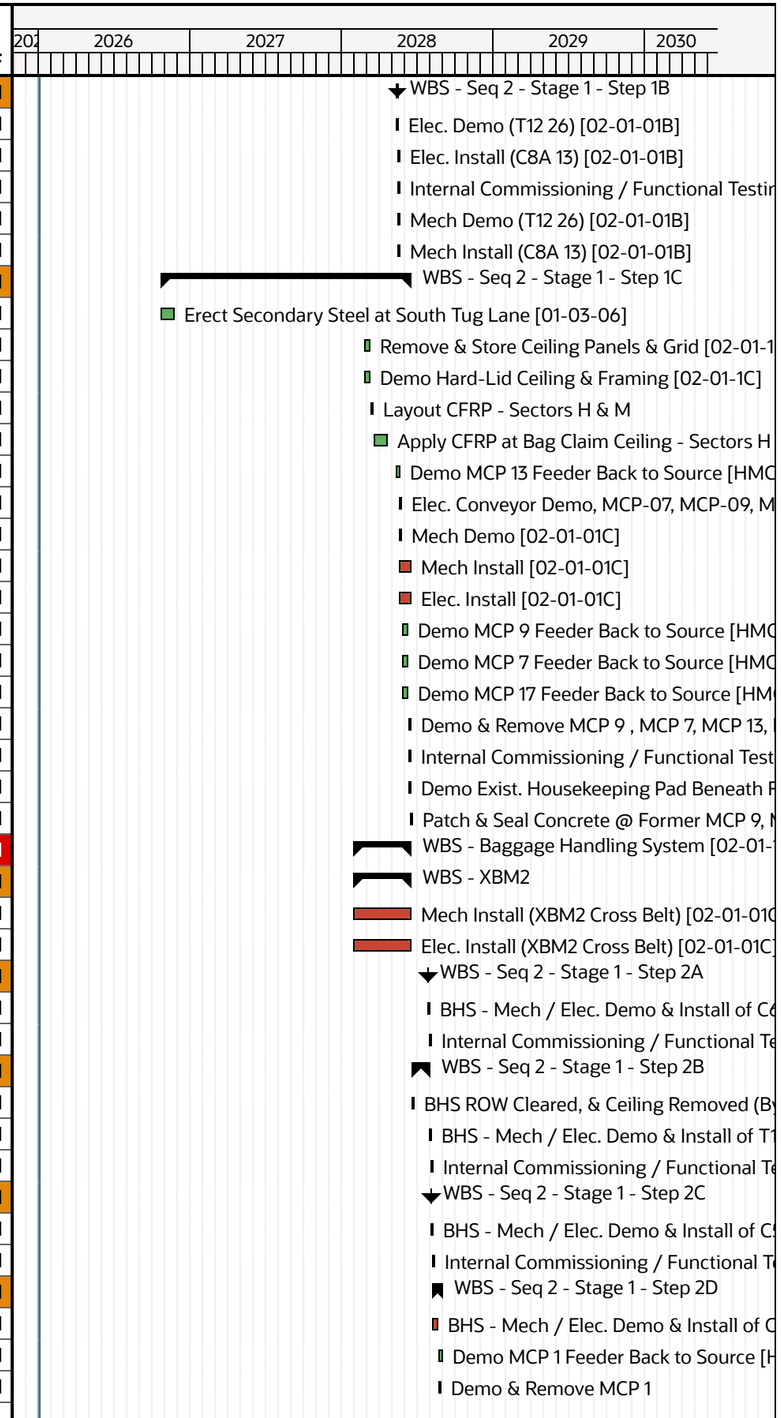


	ID	Name	Dur	Start	Finish	TF
13315	D2015	Internal Commissioning / Functional Testing / Owner Testing [02-01-02D]	2.0d	17-Aug-28	18-Aug-28	0.0d
13316	BG-DM-MCP-320	Demo Exist. Housekeeping Pad Beneath Former MCP 1	1.0d	18-Aug-28	18-Aug-28	21.0d
13317	BG-DM-MCP-330	Patch & Seal Concrete @ Former MCP 1 Housekeeping Pad	3.0d	21-Aug-28	23-Aug-28	21.0d
13318	WBS - Seq 2 - Stage 1 - Step 3A		3.0d	21-Aug-28	23-Aug-28	0.0d
13319	A16	BHS - Mech / Elec. Demo & Install of T15 06, C8 11 (02-01-03A)	2.0d	21-Aug-28	22-Aug-28	0.0d
13320	D2023	Internal Commissioning / Functional Testing / Owner Testing[02-01-03A]	1.0d	23-Aug-28	23-Aug-28	0.0d
13321	WBS - Seq 2 - Stage 1 - Step 3B		21.0d	24-Aug-28	22-Sep-28	0.0d
13322	A17	BHS - Mech / Elec. Demo & Install of C6A 03/13, C8A 02/10, ALM2 01/02, CL...	16.0d	24-Aug-28	15-Sep-28	0.0d
13323	D2029	Internal Commissioning / Functional Testing /Owner Testing [02-01-03B]	5.0d	18-Sep-28	22-Sep-28	0.0d
13324	WBS - Seq 2 - Stage 1 - Step 4A		3.0d	19-Dec-28	21-Dec-28	0.0d
13325	A18	BHS - Mech / Elec. Demo & Install of T8 01/06 (02-01-04A)	3.0d	19-Dec-28	21-Dec-28	0.0d
13326	D2043	Internal Commissioning / Functional Testing / Owner Testing [02-01-04A]	1.0d	21-Dec-28	21-Dec-28	0.0d
13327	WBS - Seq 2 - Stage 1 - Step 4B		20.0d	22-Dec-28	22-Jan-29	1.0d
13328	A19	BHS - Mech / Elec. Demo & Install of C5 05/06, TF1 01/03, T5 11, T-T5 16/17...	10.0d	22-Dec-28	8-Jan-29	0.0d
13329	D2051	Internal Commissioning / Functional Testing / Owner Testing [02-01-04B]	3.0d	8-Jan-29	10-Jan-29	0.0d
13330	BG-DM-MCP-C-500	Demo MCP C5 Feeder Back to Source [HMCP-7]	10.0d	9-Jan-29	22-Jan-29	1.0d
13331	BG-DM-MCP-C-510	Demo & Remove MCP C5	1.0d	9-Jan-29	9-Jan-29	1.0d
13332	BG-DM-MCP-C-530	Demo, Patch & Seal Concrete @ Former MCP C5 Housekeeping Pad	5.0d	10-Jan-29	16-Jan-29	1.0d
13333	WBS - Seq 2 - Stage 1 - Step 4C		6.0d	11-Jan-29	18-Jan-29	0.0d
13334	A20	BHS - Mech / Elec. Demo (BX4 02/05, MCP BX4) & Install of (T5 14/15) [02-0...	5.0d	11-Jan-29	17-Jan-29	0.0d
13335	D2058	Internal Commissioning / Functional Testing / Owner Testing [02-01-04C]	1.0d	18-Jan-29	18-Jan-29	0.0d
13336	WBS - Seq 2 - Stage 2 - Step 1A		33.0d	22-Dec-28	8-Feb-29	0.0d
13337	A109770	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS3 [02-01-1A]	15.0d	22-Dec-28	15-Jan-29	4.0d
13338	D2060	BHS ROW Cleared (By Others) [02-02-1A]	1.0d	19-Jan-29	19-Jan-29	0.0d
13339	D2063	Elec. MPP Install (B17) [02-02-01A]	9.0d	22-Jan-29	1-Feb-29	4.0d
13340	A21	BHS - Mech / Elec. Demo & Install of C3 11, T1 11, T1A 01/03, T5A 06/08, TX...	13.0d	22-Jan-29	7-Feb-29	0.0d
13341	D2066	Internal Commissioning / Functional Testing / Owner Testing [02-02-01A]	3.0d	6-Feb-29	8-Feb-29	0.0d
13342	WBS - Seq 2 - Stage 2 - Step 1B		1.0d	9-Feb-29	9-Feb-29	0.0d
13343	D2071	Internal Commissioning / Functional Testing / Owner Testing [02-02-01B]	1.0d	9-Feb-29	9-Feb-29	0.0d
13344	A22	BHS - Mech / Elec. Demo & Install of T-T4 06 (02-02-01B)	1.0d	9-Feb-29	9-Feb-29	0.0d
13345	WBS - Seq 2 - Stage 2 - Step 2A		34.0d	6-Feb-29	23-Mar-29	33.0d
13346	A109780	Demo Ceiling Tile and Erect Temp Walls	4.0d	6-Feb-29	9-Feb-29	2.0d
13347	BG-DM-MCP-BX-400	Demo MCP BX4 Feeder Back to Source [HMCP-6]	10.0d	12-Feb-29	23-Feb-29	7.0d
13348	D2075	Elec. Recontrol (C2 01/08) [02-02-02A]	5.0d	12-Feb-29	16-Feb-29	0.0d
13349	A23	BHS - Mech / Elec. Demo & Install (02-02-02A)	20.0d	12-Feb-29	9-Mar-29	2.0d
13350	D2078	Elec. MPP Install (B13) [02-02-02A]	16.0d	19-Feb-29	12-Mar-29	0.0d
13351	BG-DM-MCP-BX-410	Demo & Remove MCP BX4	1.0d	26-Feb-29	26-Feb-29	7.0d
13352	BG-DM-MCP-BX-430	Demo, Patch & Seal Concrete @ Former MCP BX4 Housekeeping Pad	5.0d	27-Feb-29	5-Mar-29	7.0d
13353	D2081	Internal Commissioning / Functional Testing / Owner Testing [02-02-02A]	5.0d	8-Mar-29	14-Mar-29	0.0d
13354	BG-DM-MCP-BX-200	Demo MCP BX2 Feeder Back to Source [HMCP-6]	10.0d	12-Mar-29	23-Mar-29	33.0d
13355	BG-DM-MCP-BX-210	Demo & Remove MCP BX2	1.0d	12-Mar-29	12-Mar-29	33.0d
13356	BG-DM-MCP-BX-230	Demo, Patch & Seal Concrete @ Former MCP BX2 Housekeeping Pad	5.0d	13-Mar-29	19-Mar-29	33.0d

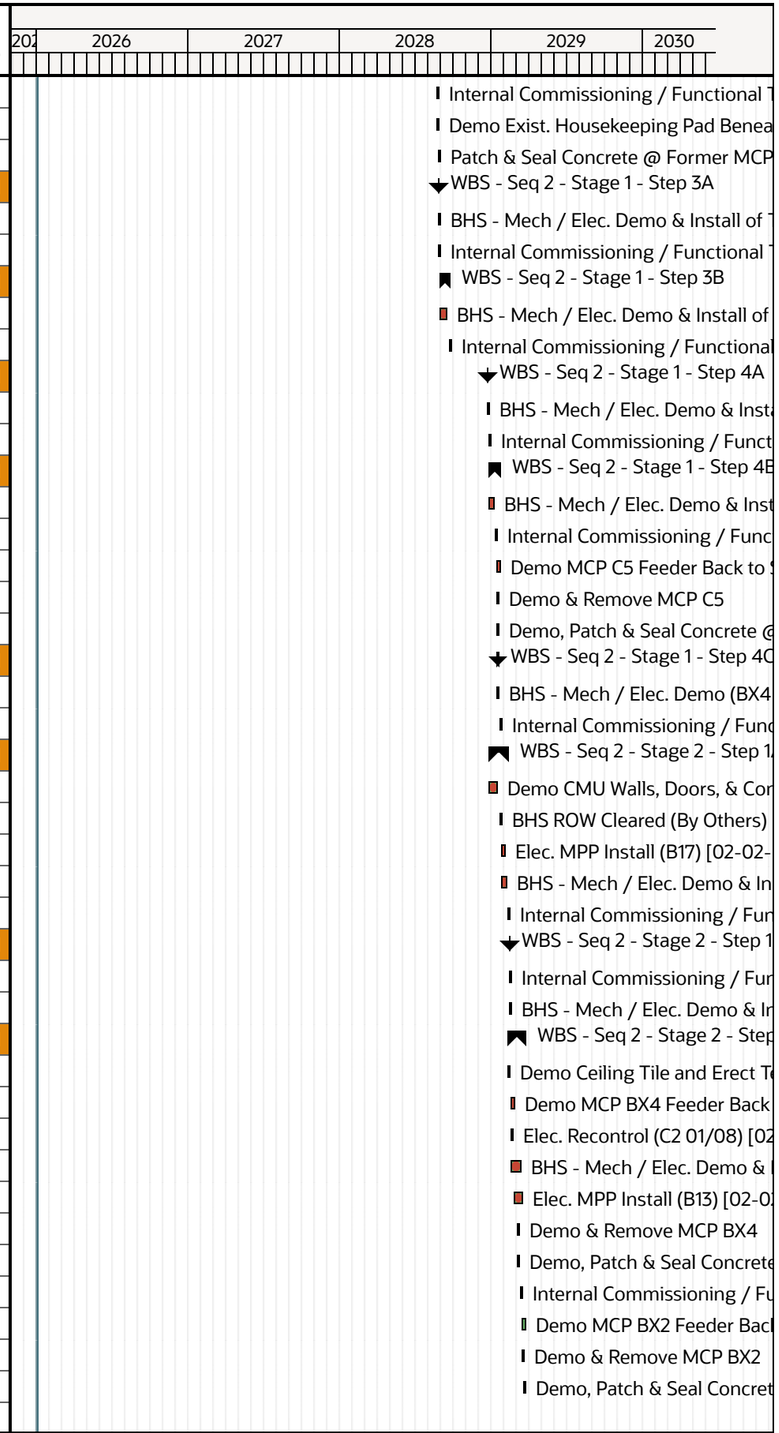


	ID	Name	Dur	Start	Finish	TF
13357	WBS - Seq 2 - Stage 2 - Step 2B		3.0d	15-Mar-29	19-Mar-29	0.0d
13358	A24	BHS - Mech / Elec. Demo & Install of T5 04 & T-T5 16/17 (02-02-02B)	2.0d	15-Mar-29	16-Mar-29	0.0d
13359	D2089	Internal Commissioning / Functional Testing / Owner Testing [02-02-02B]	1.0d	19-Mar-29	19-Mar-29	0.0d
13360	WBS - Seq 2 - Stage 2 - Step 2C		10.0d	20-Mar-29	2-Apr-29	0.0d
13361	A25	BHS - Mech / Elec. Demo & Install of C4 08/09, T11A 12/15, T5A 01/03 (02-0...	9.0d	20-Mar-29	30-Mar-29	0.0d
13362	D2095	Internal Commissioning / Functional Testing / Owner Testing [02-02-02C]	2.0d	30-Mar-29	2-Apr-29	0.0d
13363	WBS - Seq 2 - Stage 2 - Step 2D		6.0d	3-Apr-29	10-Apr-29	0.0d
13364	D2098	Elec. Recontrol (T4 01/03) [02-02-02D]	4.0d	3-Apr-29	6-Apr-29	0.0d
13365	A26	BHS - Mech / Elec. Demo (T4 04/08) & Install of C3 11, T4 04/06, C1 07/09 (0...	5.0d	3-Apr-29	9-Apr-29	1.0d
13366	D2103	Internal Commissioning / Functional Testing / Owner Testing [02-02-02D]	2.0d	9-Apr-29	10-Apr-29	0.0d
13367	WBS - Seq 2 - Stage 2 - Step 2E		9.0d	11-Apr-29	23-Apr-29	0.0d
13368	D2106	Elec. Recontrol (C1 01/05) [02-02-02E]	3.0d	11-Apr-29	13-Apr-29	5.0d
13369	A27	BHS - Mech / Elec. Demo & Install of TE1 09/11, T-TE1 12/16, T-TE2 05/07 (0...	7.0d	11-Apr-29	19-Apr-29	0.0d
13370	D2113	Internal Commissioning / Functional Testing / Owner Testing (C1) [02-02-02E]	1.0d	17-Apr-29	17-Apr-29	4.0d
13371	D2115	Internal Commissioning / Functional Testing / Owner Testing (TE1 / TE2) [02-...	2.0d	20-Apr-29	23-Apr-29	0.0d
13372	WBS - Seq 2 - Stage 2 - Step 2F		1.0d	24-Apr-29	24-Apr-29	0.0d
13373	D2122	Internal Commissioning / Functional Testing / Owner Testing [02-02-02F]	1.0d	24-Apr-29	24-Apr-29	0.0d
13374	A28	BHS - Mech / Elec. Demo & Install of C3 06 (02-02-02F)	1.0d	24-Apr-29	24-Apr-29	0.0d
13375	WBS - Seq 2 - Stage 2 - Step 2G		6.0d	25-Apr-29	2-May-29	0.0d
13376	A29	BHS - Mech / Elec. Demo & Install of T3 04/11 (02-02-02G)	5.0d	25-Apr-29	1-May-29	0.0d
13377	D2129	Internal Commissioning / Functional Testing / Owner Testing [02-02-02G]	1.0d	2-May-29	2-May-29	0.0d
13378	WBS - Seq 2 - Stage 2 - Step 3A		24.0d	3-May-29	5-Jun-29	61.0d
13379	D2132	Elec. Recontrol (T3 02/03) [02-02-03A]	2.0d	3-May-29	4-May-29	0.0d
13380	A30	BHS - Mech / Elec. Demo & Install of T3 02/03 02-02-03A	2.0d	3-May-29	4-May-29	0.0d
13381	A31	BHS - Mech / Elec. Demo & Install of T1 10, T-SS8 06/07, TXM1 07/08 02-02-...	4.0d	4-May-29	9-May-29	0.0d
13382	D2140	Internal Commissioning / Functional Testing / Owner Testing [02-02-03A]	1.0d	10-May-29	10-May-29	0.0d
13383	WBS - Ticket Counters 2 & 3		24.0d	3-May-29	5-Jun-29	61.0d
13384	CON-TC2&3-10	Erect Temp Partitions Around Partial T2 & T3 Ticket Counters	2.0d	3-May-29	4-May-29	61.0d
13385	CON-TC2&3-20	Install New Access Doors to BOH Spaces - Not Shown in Documents At this Time	5.0d	7-May-29	11-May-29	61.0d
13386	CON-TC2&3-30	Slab Infill at Former T3-04 Penetration	5.0d	7-May-29	11-May-29	66.0d
13387	CON-TC2&3-40	Demo Two Existing Doors at Future T2/T3 Connection	5.0d	14-May-29	18-May-29	61.0d
13388	CON-TC2&3-50	Frame & Insulate New Wall Infill at Demoed Doors Location	2.0d	21-May-29	22-May-29	61.0d
13389	CON-TC2&3-60	Wall Close-In Inspection T2&3	1.0d	23-May-29	23-May-29	61.0d
13390	CON-TC2&3-70	Hang, Tape, & Finish New Wall Infill	2.0d	24-May-29	25-May-29	61.0d
13391	CON-TC2&3-80	Paint New Wall Infill to Match Existing	2.0d	29-May-29	30-May-29	61.0d
13392	CON-TC2&3-90	Remove Temp Partitions Around T2 & T3 Ticket Counters	2.0d	31-May-29	1-Jun-29	61.0d
13393	CON-TC2&3-100	Develop Punchlist T2 & T3 Ticket Counters	2.0d	4-Jun-29	5-Jun-29	61.0d
13394	WBS - Seq 2 - Stage 2 - Step 3B		3.0d	11-May-29	15-May-29	0.0d
13395	D2146	Demo EDS Machine (SS7) [02-02-03B]	2.0d	11-May-29	14-May-29	0.0d
13396	A32	BHS - Mech / Elec. Demo & Install of SS7 06/07 & T-SS8 05 (02-02-03B)	2.0d	11-May-29	14-May-29	0.0d
13397	D2150	Internal Commissioning / Functional Testing / Owner Testing [02-02-03B]	1.0d	15-May-29	15-May-29	0.0d
13398	WBS - Seq 2 - Stage 2 - Step 3C		56.0d	16-May-29	2-Aug-29	160.0d

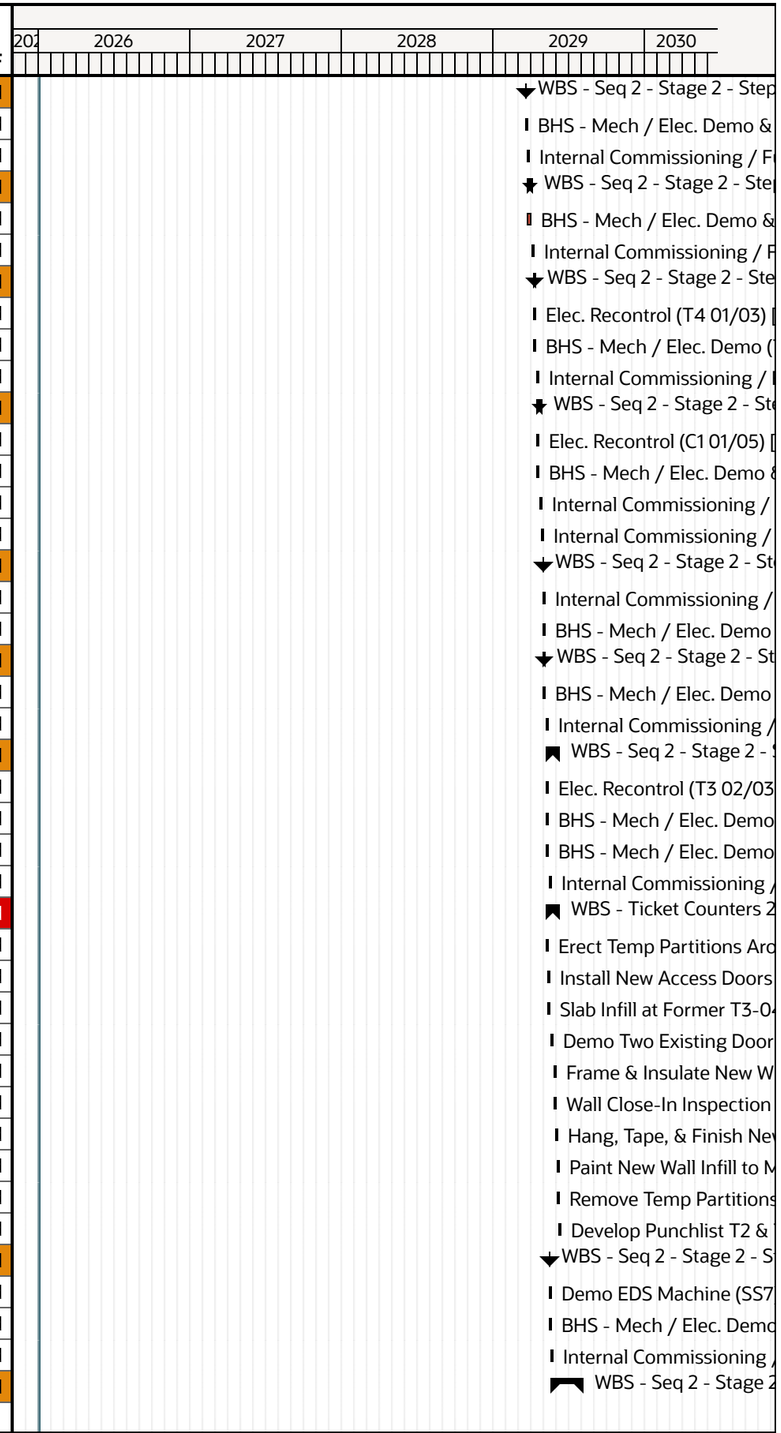


	ID	Name	Dur	Start	Finish	TF
13399	WBS - Enabling for Steps 4A & 4B		4.0d	7-Jun-29	12-Jun-29	0.0d
13400	D2157	Mech Install (T1 07/09) [02-02-03C]	3.0d	7-Jun-29	11-Jun-29	0.0d
13401	D2156	Elec. Install (T1 07/09) [02-02-03C]	3.0d	7-Jun-29	11-Jun-29	0.0d
13402	D2158	Internal Commissioning / Functional Testing (T1 07/09) [02-02-03C]	1.0d	12-Jun-29	12-Jun-29	0.0d
13403	WBS - Enabling for Steps 4C		18.0d	12-Jun-29	6-Jul-29	23.0d
13404	D2160	Mech Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-...	15.0d	12-Jun-29	2-Jul-29	2.0d
13405	D2159	Elec. Install (TE1 13/14, TE1 17/24, TE2 06/08, TE2 11/15, TE2 18) [02-02-0...	15.0d	12-Jun-29	2-Jul-29	2.0d
13406	D2161	Internal Commissioning / Functional Testing (TE1, TE2 Tie-Ins) [02-02-03C]	3.0d	3-Jul-29	6-Jul-29	23.0d
13407	WBS - Oversized Screening Area		22.0d	3-Jul-29	2-Aug-29	0.0d
13408	D2163	Elec. Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18) [02-02-03C]	20.0d	3-Jul-29	31-Jul-29	2.0d
13409	D2164	Mech Install (OSM1 02/05, OSM1A 04/18, OSM1B 02/18, Inspection Tables) [...	20.0d	6-Jul-29	2-Aug-29	0.0d
13410	D2162	Elec. Install (MPP-AOS, FCP-AOS, MPP-BOS, FCP-BOS) [02-02-03C]	20.0d	6-Jul-29	2-Aug-29	0.0d
13411	WBS - Baggage Handling System [02-02-3C]		37.0d	16-May-29	6-Jul-29	44.0d
13412	D2152	Elec. Demo [02-02-03C]	10.0d	16-May-29	30-May-29	0.0d
13413	D2153	Mech Demo [02-02-03C]	10.0d	31-May-29	13-Jun-29	0.0d
13414	D2154	ControlNet Rework / Elec Demo (MCP-T3, MCP-AS1, MCP-CX1/CX3, MCP-MC...	15.0d	14-Jun-29	5-Jul-29	0.0d
13415	BG-DM-MCP-C-750	Demo & Remove MCP CX1/CX3	1.0d	6-Jul-29	6-Jul-29	44.0d
13416	BG-DM-MCP-C-790	Demo & Remove MCP CX2	1.0d	6-Jul-29	6-Jul-29	44.0d
13417	WBS - Structural [02-02-3C]		30.0d	1-Jun-29	13-Jul-29	174.0d
13418	BG-DM-MCP-C-850	Demo, Patch & Seal Concrete @ Former MCP BX1 Housekeeping Pad	5.0d	1-Jun-29	7-Jun-29	199.0d
13419	A110480	Demo CMU Walls, Doors, & Concrete Barrier Walls in AS1 [02-02-03C]	15.0d	14-Jun-29	5-Jul-29	0.0d
13420	A110490	Demo EDS Access Platform in AS1 [02-02-03C]	5.0d	28-Jun-29	5-Jul-29	0.0d
13421	BG-DM-MCP-C-770	Demo, Patch & Seal Concrete @ Former MCP CX1/CX3 Housekeeping Pad	5.0d	9-Jul-29	13-Jul-29	44.0d
13422	BG-DM-MCP-C-810	Demo, Patch & Seal Concrete @ Former MCP CX2 Housekeeping Pad	5.0d	9-Jul-29	13-Jul-29	44.0d
13423	WBS - Electrical [02-02-3C]		35.0d	31-May-29	19-Jul-29	170.0d
13424	BG-DM-MCP-C-820	Demo MCP BX1 Feeder Back to Source [XXX]	10.0d	31-May-29	13-Jun-29	195.0d
13425	BG-DM-MCP-C-740	Demo MCP CX1/CX3 Feeder Back to Source [HMCP-2]	10.0d	6-Jul-29	19-Jul-29	20.0d
13426	BG-DM-MCP-C-780	Demo MCP CX2 Feeder Back to Source [HMCP-2]	10.0d	6-Jul-29	19-Jul-29	20.0d
13427	WBS - Seq 2 - Stage 2 - Step 4A		4.0d	13-Jun-29	18-Jun-29	0.0d
13428	D2166	Elec. Recontrol (T2 01/04) [02-02-04A]	3.0d	13-Jun-29	15-Jun-29	0.0d
13429	A33	BHS - Mech / Elec. Demo & Install T2 05/07 (02-02-04A)	3.0d	13-Jun-29	15-Jun-29	0.0d
13430	D2172	Internal Commissioning / Functional Testing / Owner Testing [02-02-04A]	1.0d	18-Jun-29	18-Jun-29	0.0d
13431	WBS - Seq 2 - Stage 2 - Step 4B		4.0d	19-Jun-29	22-Jun-29	0.0d
13432	D2174	Elec. Recontrol (T1 01/04) [02-02-04B]	3.0d	19-Jun-29	21-Jun-29	0.0d
13433	A34	BHS - Mech / Elec. Demo & Install T1 05/06 (02-02-04B)	3.0d	19-Jun-29	21-Jun-29	0.0d
13434	D2179	Internal Commissioning / Functional Testing / Owner Training [02-02-04B]	1.0d	22-Jun-29	22-Jun-29	0.0d
13435	WBS - Seq 2 - Stage 2 - Step 5		38.0d	25-Jun-29	16-Aug-29	0.0d
13436	D2182	ControlNet Rework / Elec Demo (MCP-T1/T2, MCP-AS2) [02-02-05]	5.0d	25-Jun-29	29-Jun-29	0.0d
13437	B35	BHS - Mech / Elec. Demo & Install of (AS2 01/07, T1 07/09, T2 06/10, SS7 01...	10.0d	2-Jul-29	16-Jul-29	0.0d
13438	BG-DM-MCP-AS-220	Demo Exist. Housekeeping Pad Beneath Former MCP AS2	1.0d	17-Jul-29	17-Jul-29	0.0d
13439	BG-DM-MCP-AS-230	Patch & Seal Concrete @ Former MCP AS2 Housekeeping Pad	3.0d	18-Jul-29	20-Jul-29	0.0d
13440	A35	BHS - Mech / Elec. Demo & Install of TE1 15/16, TE2 09/10, TXM1 01/06 (02-...	13.0d	23-Jul-29	8-Aug-29	0.0d

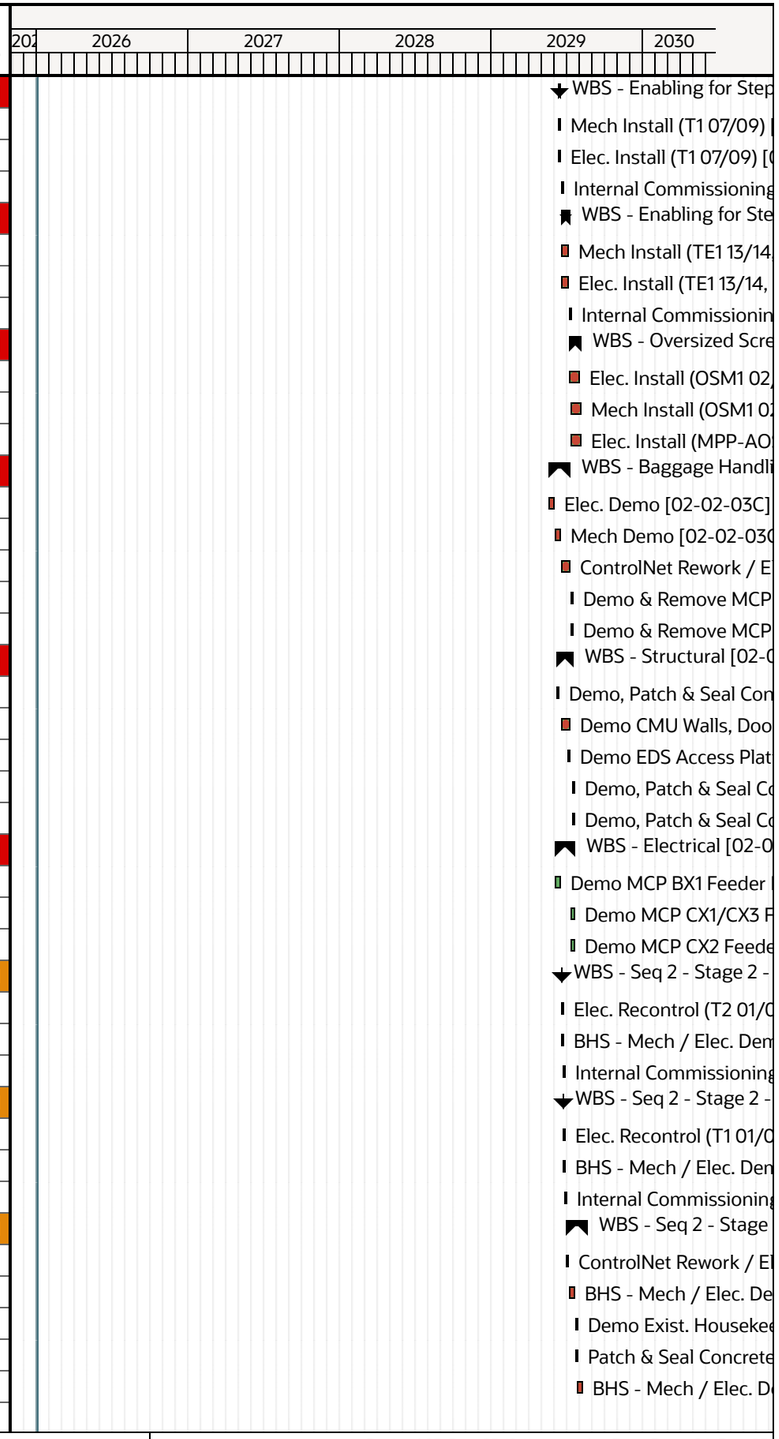


	ID	Name	Dur	Start	Finish	TF
13441	D2187	Internal Commissioning / Functional Testing [02-02-05]	2.0d	9-Aug-29	10-Aug-29	0.0d
13442	D2188	Owner Testing [02-02-05]	1.0d	10-Aug-29	10-Aug-29	0.0d
13443	WBS - Oversized Screening & Tie-Ins / Testing / Certification Testing		10.0d	3-Aug-29	16-Aug-29	0.0d
13444	D2190	Mech Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10.0d	3-Aug-29	16-Aug-29	0.0d
13445	D2189	Elec. Install (OSM1 06/07, OSM1 VSU, OSM1A 01/03, OSM1B 01) [02-02-05]	10.0d	3-Aug-29	16-Aug-29	0.0d
13446	WBS - Seq 2 - Stage 2 - Step 6		4.0d	13-Aug-29	16-Aug-29	0.0d
13447	A36	BHS - Mech / Elec. Demo & Install of (TE1 12) [02-02-06]	3.0d	13-Aug-29	15-Aug-29	0.0d
13448	D2201	Internal Commissioning / Functional Testing / Owner Testing [02-02-06]	1.0d	16-Aug-29	16-Aug-29	0.0d
13449	WBS - Seq 2 - Stage 2 - Step 7		6.0d	17-Aug-29	24-Aug-29	0.0d
13450	A37	BHS - Mech / Elec. Demo & Install of (T-TE2 05, EX2 07) & (TE2 05, TE2 16/17...	5.0d	17-Aug-29	23-Aug-29	0.0d
13451	D2208	Internal Commissioning / Functional Testing / Owner Testing [02-02-07]	1.0d	24-Aug-29	24-Aug-29	0.0d
13452	WBS - Seq 2 - Stage 2 - Step 8		65.0d	31-May-29	30-Aug-29	135.0d
13453	BG-DM-MCP-C-830	Demo & Remove MCP BX1	1.0d	31-May-29	31-May-29	199.0d
13454	A38	BHS - Mech / Elec. Demo & Install of (T-TE2 06/07, T-TE1 14/16, EX2 01/06, ...	4.0d	27-Aug-29	30-Aug-29	0.0d
13455	WBS - Equipment Rooms		21.0d	6-Jul-27	4-Aug-27	289.0d
13456	D2213	CBRA Room Finishes Complete / Temp Power Available (By Others) - Main Ter...	0.0d		6-Jul-27	289.0d
13457	D2215	BHS Server Room Finishes Complete / Temp Power Available (By Others) - Mai...	0.0d		7-Jul-27	289.0d
13458	D2214	OSR Room Finishes Complete / Temp Power Available (By Others) - Main Termi...	0.0d		7-Jul-27	289.0d
13459	D2216	Set Up FAT Equip. - Main Terminal	20.0d	8-Jul-27	4-Aug-27	289.0d
13460	WBS - CCBS - Building Infrastructure		963.0d	20-Oct-25 A	2-Aug-29	135.0d
13461	WBS - BHS ROW Prep		963.0d	20-Oct-25 A	2-Aug-29	135.0d
13462	WBS - Power Distribution Panel Demo		93.0d	26-Mar-29	2-Aug-29	20.0d
13463	BI-ROW-PDP-40	Demo HMCP-6 & Feeder Back to Source [MSB EDS2]	10.0d	26-Mar-29	6-Apr-29	102.0d
13464	BI-ROW-PDP-110	Demo HMCP-2 & Feeder Back to Source [MSB EDS1]	10.0d	20-Jul-29	2-Aug-29	20.0d
13465	WBS - Tag & Trace		481.0d	20-Oct-25 A	10-Sep-27	617.0d
13466	CCBS-LOE-1000	Tag & Trace Elec.& Low Voltage (LOE)	481.0d	20-Oct-25 A	10-Sep-27	0.0d
13467	WBS - Tag & Trace - Sequence 1 - Stage 1		140.0d	20-Oct-25 A	7-May-26	31.0d
13468	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 1		140.0d	20-Oct-25 A	7-May-26	31.0d
13469	TT-SQ1-SG1-A1-10	Tag & Trace - Sequence 1 - Stage 1 - Area 1	21.0d	20-Oct-25 A	17-Nov-25 A	
13470	TT-SQ1-SG1-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	19-Nov-25 A	29-Dec-25	103.0d
13471	TT-SQ1-SG1-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 1	10.0d	30-Dec-25	13-Jan-26	103.0d
13472	TT-SQ1-SG1-A1-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 1 - Area 1	10.0d	24-Apr-26	7-May-26	31.0d
13473	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 2		123.0d	12-Nov-25 A	7-May-26	31.0d
13474	TT-SQ1-SG1-A2-10	Tag & Trace - Sequence 1 - Stage 1 - Area 2	6.0d	12-Nov-25 A	19-Nov-25 A	
13475	TT-SQ1-SG1-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	26.0d	20-Nov-25 A	30-Dec-25	102.0d
13476	TT-SQ1-SG1-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 2	10.0d	31-Dec-25	14-Jan-26	102.0d
13477	TT-SQ1-SG1-A2-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 1 - Area 2	10.0d	24-Apr-26	7-May-26	31.0d
13478	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 3		120.0d	16-Nov-25 A	7-May-26	31.0d
13479	TT-SQ1-SG1-A3-10	Tag & Trace - Sequence 1 - Stage 1 - Area 3	30.0d	16-Nov-25 A	31-Dec-25	0.0d
13480	TT-SQ1-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	2-Jan-26	8-Jan-26	96.0d
13481	TT-SQ1-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 3	10.0d	9-Jan-26	22-Jan-26	96.0d
13482	TT-SQ1-SG1-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 1 - Area 3	10.0d	24-Apr-26	7-May-26	31.0d

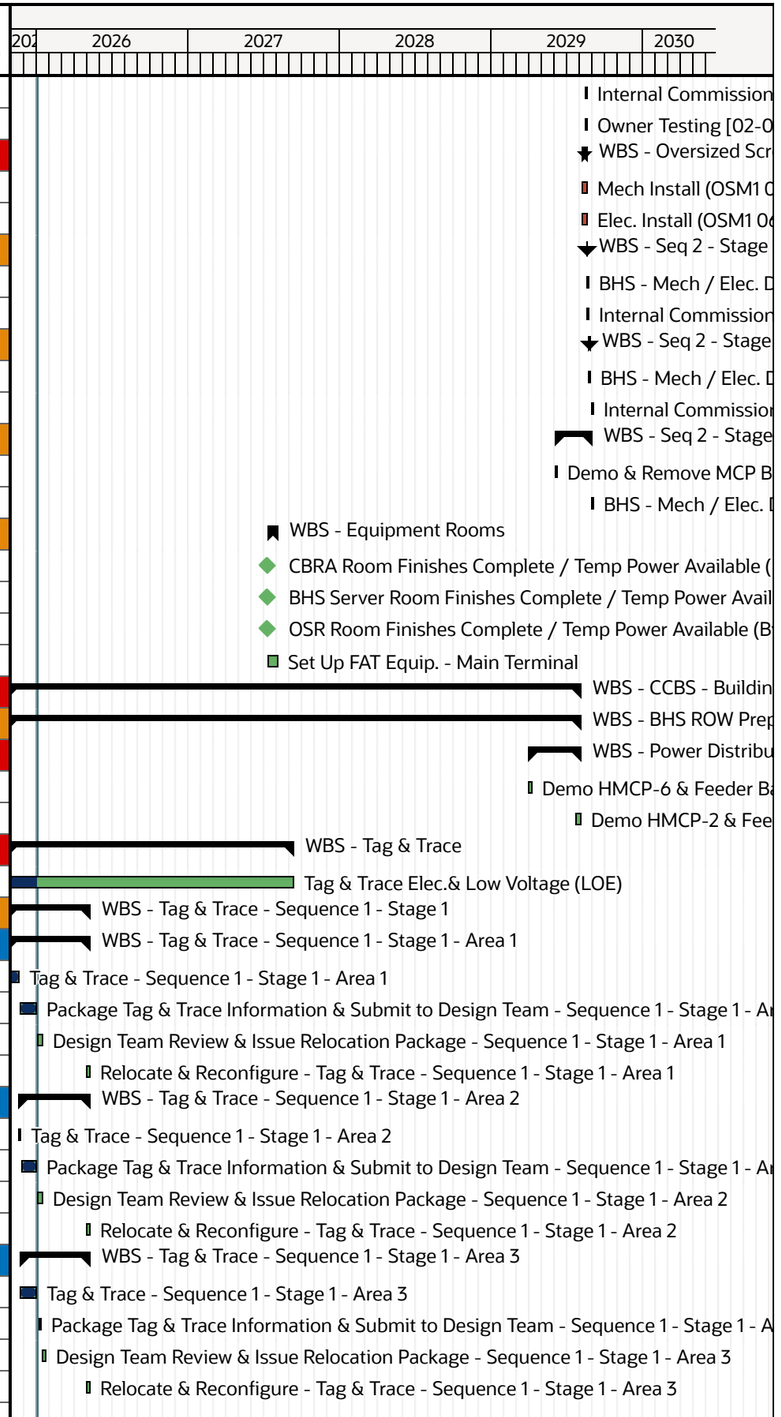


	ID	Name	Dur	Start	Finish	TF
13483	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 4		117.0d	20-Nov-25 A	7-May-26	31.0d
13484	TT-SQ1-SG1-A4-10	Tag & Trace - Sequence 1 - Stage 1 - Area 4	29.0d	20-Nov-25 A	5-Jan-26	0.0d
13485	TT-SQ1-SG1-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
13486	TT-SQ1-SG1-A4-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 4	10.0d	13-Jan-26	26-Jan-26	94.0d
13487	TT-SQ1-SG1-A4-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 1 - Area 4	10.0d	24-Apr-26	7-May-26	31.0d
13488	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 5		110.0d	3-Dec-25 A	7-May-26	31.0d
13489	TT-SQ1-SG1-A5-10	Tag & Trace - Sequence 1 - Stage 1 - Area 5	22.0d	3-Dec-25 A	5-Jan-26	0.0d
13490	TT-SQ1-SG1-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-26	12-Jan-26	94.0d
13491	TT-SQ1-SG1-A5-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 1 - Area 5	10.0d	13-Jan-26	26-Jan-26	94.0d
13492	TT-SQ1-SG1-A5-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 1 - Area 5	10.0d	24-Apr-26	7-May-26	31.0d
13493	WBS - Tag & Trace - Sequence 1 - Stage 2		79.0d	6-Jan-26	24-Apr-26	268.0d
13494	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 1		35.0d	6-Jan-26	23-Feb-26	312.0d
13495	TT-SQ1-SG2-A1-10	Tag & Trace - Sequence 1 - Stage 2 - Area 1	10.0d	6-Jan-26	19-Jan-26	0.0d
13496	TT-SQ1-SG2-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	20-Jan-26	26-Jan-26	312.0d
13497	TT-SQ1-SG2-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 1	10.0d	27-Jan-26	9-Feb-26	312.0d
13498	TT-SQ1-SG2-A1-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 1	10.0d	10-Feb-26	23-Feb-26	312.0d
13499	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 2		35.0d	12-Jan-26	27-Feb-26	199.0d
13500	TT-SQ1-SG2-A2-10	Tag & Trace - Sequence 1 - Stage 2 - Area 2	10.0d	12-Jan-26	23-Jan-26	0.0d
13501	TT-SQ1-SG2-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	26-Jan-26	30-Jan-26	199.0d
13502	TT-SQ1-SG2-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 2	10.0d	2-Feb-26	13-Feb-26	199.0d
13503	TT-SQ1-SG2-A2-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 2	10.0d	16-Feb-26	27-Feb-26	199.0d
13504	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 3		35.0d	26-Jan-26	13-Mar-26	189.0d
13505	TT-SQ1-SG2-A3-10	Tag & Trace - Sequence 1 - Stage 2 - Area 3	10.0d	26-Jan-26	6-Feb-26	0.0d
13506	TT-SQ1-SG2-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	9-Feb-26	13-Feb-26	189.0d
13507	TT-SQ1-SG2-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 Stage 2 - Area 3	10.0d	16-Feb-26	27-Feb-26	189.0d
13508	TT-SQ1-SG2-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 3	10.0d	2-Mar-26	13-Mar-26	189.0d
13509	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 4		35.0d	9-Feb-26	27-Mar-26	191.0d
13510	TT-SQ1-SG2-A4-10	Tag & Trace - Sequence 1 - Stage 2 - Area 4	10.0d	9-Feb-26	20-Feb-26	0.0d
13511	TT-SQ1-SG2-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	23-Feb-26	27-Feb-26	191.0d
13512	TT-SQ1-SG2-A4-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 4	10.0d	2-Mar-26	13-Mar-26	191.0d
13513	TT-SQ1-SG2-A4-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 4	10.0d	16-Mar-26	27-Mar-26	191.0d
13514	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 5		35.0d	23-Feb-26	10-Apr-26	181.0d
13515	TT-SQ1-SG2-A5-10	Tag & Trace - Sequence 1 - Stage 2 - Area 5	10.0d	23-Feb-26	6-Mar-26	0.0d
13516	TT-SQ1-SG2-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	9-Mar-26	13-Mar-26	181.0d
13517	TT-SQ1-SG2-A5-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 5	10.0d	16-Mar-26	27-Mar-26	181.0d
13518	TT-SQ1-SG2-A5-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 5	10.0d	30-Mar-26	10-Apr-26	181.0d
13519	WBS - Tag & Trace - Sequence 1 - Stage 2 - Area 6		35.0d	9-Mar-26	24-Apr-26	171.0d
13520	TT-SQ1-SG2-A6-10	Tag & Trace - Sequence 1 - Stage 2 - Area 6	10.0d	9-Mar-26	20-Mar-26	0.0d
13521	TT-SQ1-SG2-A6-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	23-Mar-26	27-Mar-26	171.0d
13522	TT-SQ1-SG2-A6-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 2 - Area 6	10.0d	30-Mar-26	10-Apr-26	171.0d
13523	TT-SQ1-SG2-A6-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 2 - Area 6	10.0d	13-Apr-26	24-Apr-26	171.0d
13524	WBS - Tag & Trace - Sequence 1 - Stage 3		345.0d	23-Mar-26	29-Jul-27	647.0d

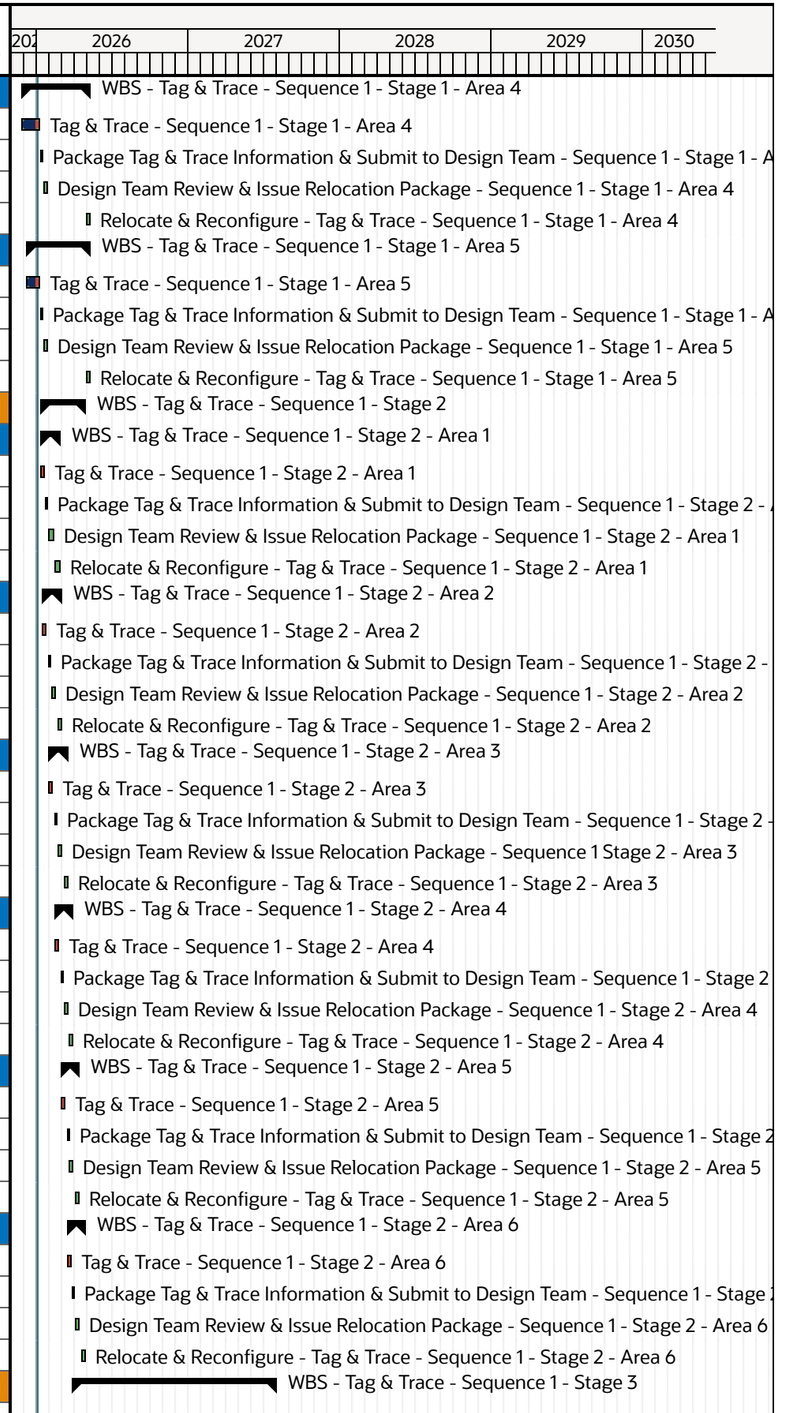


ID	Name	Dur	Start	Finish	TF
13525	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 1	35.0d	23-Mar-26	8-May-26	161.0d
13526	TT-SQ1-SG3-A1-10	Tag & Trace - Sequence 1 - Stage 3 - Area 1	10.0d	23-Mar-26	3-Apr-26	0.0d
13527	TT-SQ1-SG3-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Apr-26	10-Apr-26	161.0d
13528	TT-SQ1-SG3-A1-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 1	10.0d	13-Apr-26	24-Apr-26	161.0d
13529	TT-SQ1-SG3-A1-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 1	10.0d	27-Apr-26	8-May-26	161.0d
13530	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 2	35.0d	6-Apr-26	22-May-26	151.0d
13531	TT-SQ1-SG3-A2-10	Tag & Trace - Sequence 1 - Stage 3 - Area 2	10.0d	6-Apr-26	17-Apr-26	0.0d
13532	TT-SQ1-SG3-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	20-Apr-26	24-Apr-26	151.0d
13533	TT-SQ1-SG3-A2-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 2	10.0d	27-Apr-26	8-May-26	151.0d
13534	TT-SQ1-SG3-A2-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 2	10.0d	11-May-26	22-May-26	151.0d
13535	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 3	35.0d	20-Apr-26	8-Jun-26	653.0d
13536	TT-SQ1-SG3-A3-10	Tag & Trace - Sequence 1 - Stage 3 - Area 3	10.0d	20-Apr-26	1-May-26	0.0d
13537	TT-SQ1-SG3-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	4-May-26	8-May-26	653.0d
13538	TT-SQ1-SG3-A3-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 3	10.0d	11-May-26	22-May-26	653.0d
13539	TT-SQ1-SG3-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 3	10.0d	26-May-26	8-Jun-26	653.0d
13540	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 4	35.0d	4-May-26	22-Jun-26	131.0d
13541	TT-SQ1-SG3-A4-10	Tag & Trace - Sequence 1 - Stage 3 - Area 4	10.0d	4-May-26	15-May-26	0.0d
13542	TT-SQ1-SG3-A4-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	18-May-26	22-May-26	131.0d
13543	TT-SQ1-SG3-A4-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 4	10.0d	26-May-26	8-Jun-26	131.0d
13544	TT-SQ1-SG3-A4-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 4	10.0d	9-Jun-26	22-Jun-26	131.0d
13545	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 5	35.0d	18-May-26	7-Jul-26	121.0d
13546	TT-SQ1-SG3-A5-10	Tag & Trace - Sequence 1 - Stage 3 - Area 5	10.0d	18-May-26	1-Jun-26	0.0d
13547	TT-SQ1-SG3-A5-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	2-Jun-26	8-Jun-26	121.0d
13548	TT-SQ1-SG3-A5-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 5	10.0d	9-Jun-26	22-Jun-26	121.0d
13549	TT-SQ1-SG3-A5-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 5	10.0d	23-Jun-26	7-Jul-26	121.0d
13550	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 6	35.0d	2-Jun-26	21-Jul-26	111.0d
13551	TT-SQ1-SG3-A6-10	Tag & Trace - Sequence 1 - Stage 3 - Area 6	10.0d	2-Jun-26	15-Jun-26	0.0d
13552	TT-SQ1-SG3-A6-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	16-Jun-26	22-Jun-26	111.0d
13553	TT-SQ1-SG3-A6-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 6	10.0d	23-Jun-26	7-Jul-26	111.0d
13554	TT-SQ1-SG3-A6-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 6	10.0d	8-Jul-26	21-Jul-26	111.0d
13555	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 7	35.0d	16-Jun-26	4-Aug-26	101.0d
13556	TT-SQ1-SG3-A7-10	Tag & Trace - Sequence 1 - Stage 3 - Area 7	10.0d	16-Jun-26	29-Jun-26	0.0d
13557	TT-SQ1-SG3-A7-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	30-Jun-26	7-Jul-26	101.0d
13558	TT-SQ1-SG3-A7-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 7	10.0d	8-Jul-26	21-Jul-26	101.0d
13559	TT-SQ1-SG3-A7-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 7	10.0d	22-Jul-26	4-Aug-26	101.0d
13560	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 8	35.0d	30-Jun-26	18-Aug-26	91.0d
13561	TT-SQ1-SG3-A8-10	Tag & Trace - Sequence 1 - Stage 3 - Area 8	10.0d	30-Jun-26	14-Jul-26	0.0d
13562	TT-SQ1-SG3-A8-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	15-Jul-26	21-Jul-26	91.0d
13563	TT-SQ1-SG3-A8-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 8	10.0d	22-Jul-26	4-Aug-26	91.0d
13564	TT-SQ1-SG3-A8-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 8	10.0d	5-Aug-26	18-Aug-26	91.0d
13565	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 9	35.0d	15-Jul-26	1-Sep-26	81.0d
13566	TT-SQ1-SG3-A9-10	Tag & Trace - Sequence 1 - Stage 3 - Area 9	10.0d	15-Jul-26	28-Jul-26	0.0d

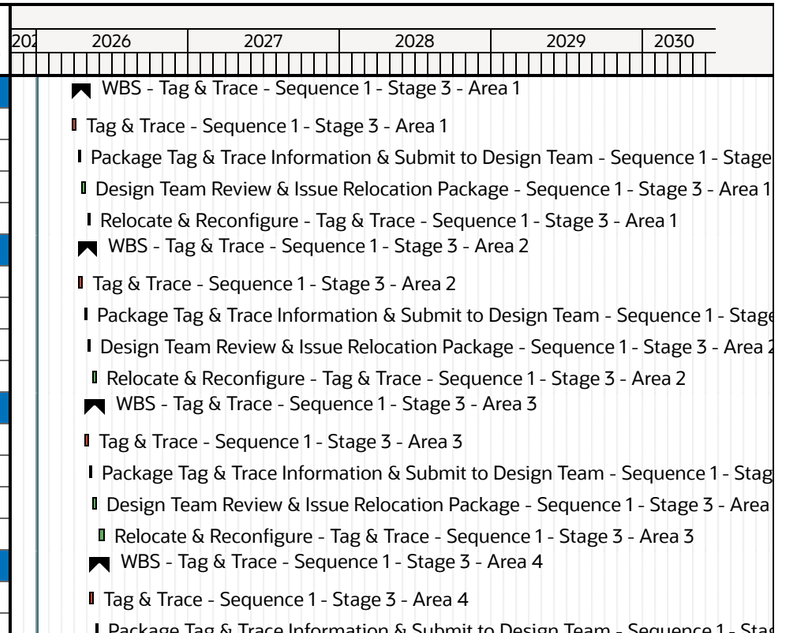


	ID	Name	Dur	Start	Finish	TF
13567	TT-SQ1-SG3-A9-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	29-Jul-26	4-Aug-26	81.0d
13568	TT-SQ1-SG3-A9-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area 9	10.0d	5-Aug-26	18-Aug-26	81.0d
13569	TT-SQ1-SG3-A9-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 9	10.0d	19-Aug-26	1-Sep-26	81.0d
13570	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 10		35.0d	29-Jul-26	16-Sep-26	71.0d
13571	TT-SQ1-SG3-A10-10	Tag & Trace - Sequence 1 - Stage 3 - Area 10	10.0d	29-Jul-26	11-Aug-26	0.0d
13572	TT-SQ1-SG3-A10-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	12-Aug-26	18-Aug-26	71.0d
13573	TT-SQ1-SG3-A10-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	19-Aug-26	1-Sep-26	71.0d
13574	TT-SQ1-SG3-A10-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 10	10.0d	2-Sep-26	16-Sep-26	71.0d
13575	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 11		35.0d	12-Aug-26	30-Sep-26	61.0d
13576	TT-SQ1-SG3-A11-10	Tag & Trace - Sequence 1 - Stage 3 - Area 11	10.0d	12-Aug-26	25-Aug-26	0.0d
13577	TT-SQ1-SG3-A11-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	26-Aug-26	1-Sep-26	61.0d
13578	TT-SQ1-SG3-A11-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	2-Sep-26	16-Sep-26	61.0d
13579	TT-SQ1-SG3-A11-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 11	10.0d	17-Sep-26	30-Sep-26	61.0d
13580	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 12		35.0d	26-Aug-26	14-Oct-26	51.0d
13581	TT-SQ1-SG3-A12-10	Tag & Trace - Sequence 1 - Stage 3 - Area 12	10.0d	26-Aug-26	9-Sep-26	0.0d
13582	TT-SQ1-SG3-A12-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	10-Sep-26	16-Sep-26	51.0d
13583	TT-SQ1-SG3-A12-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	17-Sep-26	30-Sep-26	51.0d
13584	TT-SQ1-SG3-A12-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 12	10.0d	1-Oct-26	14-Oct-26	51.0d
13585	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 13		35.0d	10-Sep-26	28-Oct-26	41.0d
13586	TT-SQ1-SG3-A13-10	Tag & Trace - Sequence 1 - Stage 3 - Area 13	10.0d	10-Sep-26	23-Sep-26	0.0d
13587	TT-SQ1-SG3-A13-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	24-Sep-26	30-Sep-26	41.0d
13588	TT-SQ1-SG3-A13-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	1-Oct-26	14-Oct-26	41.0d
13589	TT-SQ1-SG3-A13-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 13	10.0d	15-Oct-26	28-Oct-26	41.0d
13590	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 14		35.0d	24-Sep-26	11-Nov-26	31.0d
13591	TT-SQ1-SG3-A14-10	Tag & Trace - Sequence 1 - Stage 3 - Area 14	10.0d	24-Sep-26	7-Oct-26	0.0d
13592	TT-SQ1-SG3-A14-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	8-Oct-26	14-Oct-26	31.0d
13593	TT-SQ1-SG3-A14-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	15-Oct-26	28-Oct-26	31.0d
13594	TT-SQ1-SG3-A14-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 14	10.0d	29-Oct-26	11-Nov-26	31.0d
13595	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 15		35.0d	8-Oct-26	25-Nov-26	817.0d
13596	TT-SQ1-SG3-A15-10	Tag & Trace - Sequence 1 - Stage 3 - Area 15	10.0d	8-Oct-26	21-Oct-26	0.0d
13597	TT-SQ1-SG3-A15-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	22-Oct-26	28-Oct-26	816.0d
13598	TT-SQ1-SG3-A15-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	29-Oct-26	11-Nov-26	816.0d
13599	TT-SQ1-SG3-A15-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 15	10.0d	12-Nov-26	25-Nov-26	816.0d
13600	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 16		35.0d	22-Oct-26	11-Dec-26	807.0d
13601	TT-SQ1-SG3-A16-10	Tag & Trace - Sequence 1 - Stage 3 - Area 16	10.0d	22-Oct-26	4-Nov-26	0.0d
13602	TT-SQ1-SG3-A16-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	5-Nov-26	11-Nov-26	806.0d
13603	TT-SQ1-SG3-A16-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	12-Nov-26	25-Nov-26	806.0d
13604	TT-SQ1-SG3-A16-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 16	10.0d	30-Nov-26	11-Dec-26	806.0d
13605	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 17		35.0d	5-Nov-26	28-Dec-26	797.0d
13606	TT-SQ1-SG3-A17-10	Tag & Trace - Sequence 1 - Stage 3 - Area 17	10.0d	5-Nov-26	18-Nov-26	0.0d
13607	TT-SQ1-SG3-A17-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	19-Nov-26	25-Nov-26	796.0d
13608	TT-SQ1-SG3-A17-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	30-Nov-26	11-Dec-26	796.0d

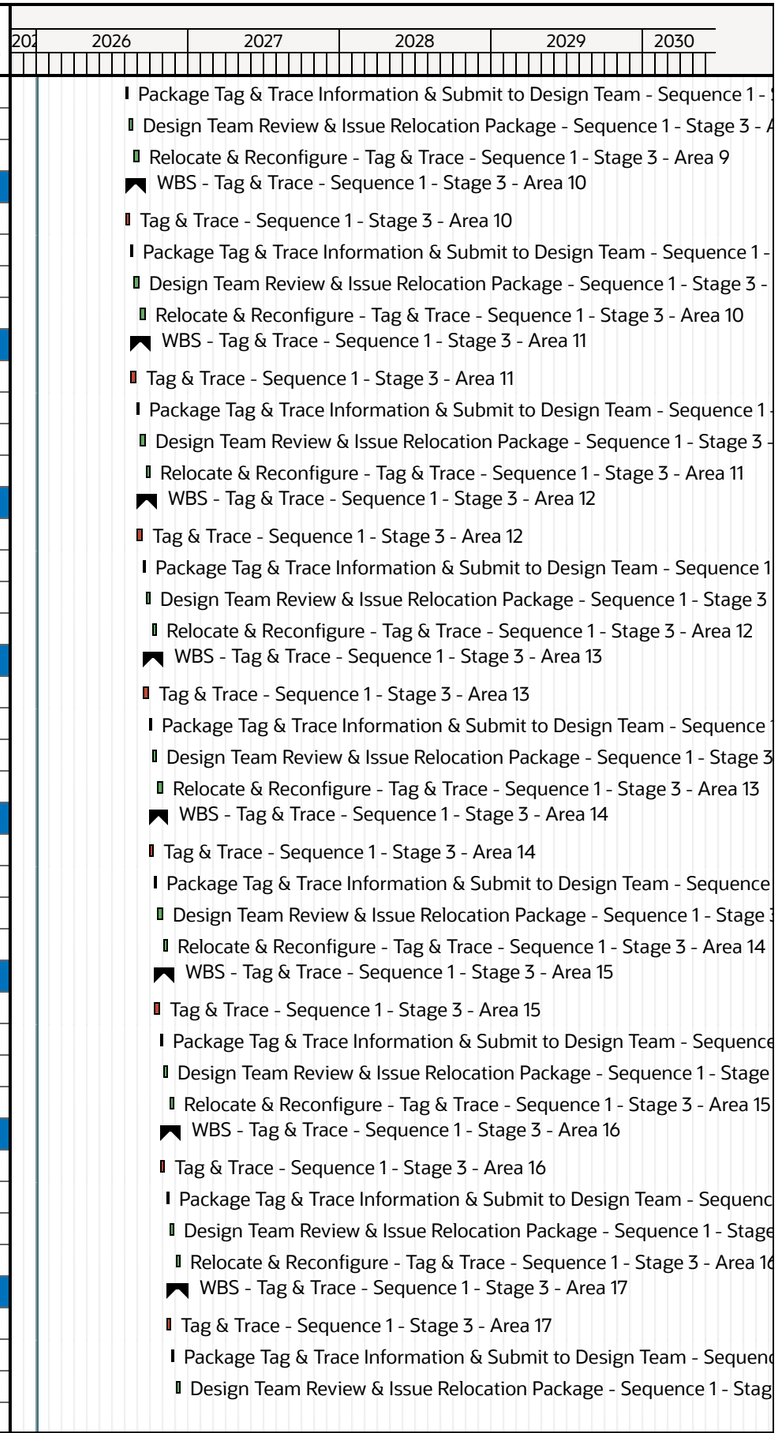


	ID	Name	Dur	Start	Finish	TF
13609	TT-SQ1-SG3-A17-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 17	10.0d	14-Dec-26	28-Dec-26	796.0d
13610	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 18		35.0d	19-Nov-26	12-Jan-27	503.0d
13611	TT-SQ1-SG3-A18-10	Tag & Trace - Sequence 1 - Stage 3 - Area 18	10.0d	19-Nov-26	4-Dec-26	0.0d
13612	TT-SQ1-SG3-A18-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	7-Dec-26	11-Dec-26	503.0d
13613	TT-SQ1-SG3-A18-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	14-Dec-26	28-Dec-26	503.0d
13614	TT-SQ1-SG3-A18-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 18	10.0d	29-Dec-26	12-Jan-27	503.0d
13615	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 19		35.0d	7-Dec-26	26-Jan-27	504.0d
13616	TT-SQ1-SG3-A19-10	Tag & Trace - Sequence 1 - Stage 3 - Area 19	10.0d	7-Dec-26	18-Dec-26	0.0d
13617	TT-SQ1-SG3-A19-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	21-Dec-26	28-Dec-26	504.0d
13618	TT-SQ1-SG3-A19-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	29-Dec-26	12-Jan-27	504.0d
13619	TT-SQ1-SG3-A19-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 19	10.0d	13-Jan-27	26-Jan-27	504.0d
13620	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 20		35.0d	21-Dec-26	9-Feb-27	483.0d
13621	TT-SQ1-SG3-A20-10	Tag & Trace - Sequence 1 - Stage 3 - Area 20	10.0d	21-Dec-26	5-Jan-27	0.0d
13622	TT-SQ1-SG3-A20-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	6-Jan-27	12-Jan-27	483.0d
13623	TT-SQ1-SG3-A20-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	13-Jan-27	26-Jan-27	483.0d
13624	TT-SQ1-SG3-A20-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 20	10.0d	27-Jan-27	9-Feb-27	483.0d
13625	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 21		35.0d	6-Jan-27	23-Feb-27	484.0d
13626	TT-SQ1-SG3-A21-10	Tag & Trace - Sequence 1 - Stage 3 - Area 21	10.0d	6-Jan-27	19-Jan-27	0.0d
13627	TT-SQ1-SG3-A21-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	20-Jan-27	26-Jan-27	484.0d
13628	TT-SQ1-SG3-A21-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	27-Jan-27	9-Feb-27	484.0d
13629	TT-SQ1-SG3-A21-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 21	10.0d	10-Feb-27	23-Feb-27	484.0d
13630	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 22		35.0d	20-Jan-27	9-Mar-27	567.0d
13631	TT-SQ1-SG3-A22-10	Tag & Trace - Sequence 1 - Stage 3 - Area 22	10.0d	20-Jan-27	2-Feb-27	0.0d
13632	TT-SQ1-SG3-A22-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	3-Feb-27	9-Feb-27	566.0d
13633	TT-SQ1-SG3-A22-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	10-Feb-27	23-Feb-27	566.0d
13634	TT-SQ1-SG3-A22-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 22	10.0d	24-Feb-27	9-Mar-27	566.0d
13635	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 23		35.0d	3-Feb-27	23-Mar-27	557.0d
13636	TT-SQ1-SG3-A23-10	Tag & Trace - Sequence 1 - Stage 3 - Area 23	10.0d	3-Feb-27	16-Feb-27	0.0d
13637	TT-SQ1-SG3-A23-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	17-Feb-27	23-Feb-27	556.0d
13638	TT-SQ1-SG3-A23-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	24-Feb-27	9-Mar-27	556.0d
13639	TT-SQ1-SG3-A23-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 23	10.0d	10-Mar-27	23-Mar-27	556.0d
13640	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 24		35.0d	17-Feb-27	6-Apr-27	547.0d
13641	TT-SQ1-SG3-A24-10	Tag & Trace - Sequence 1 - Stage 3 - Area 24	10.0d	17-Feb-27	2-Mar-27	0.0d
13642	TT-SQ1-SG3-A24-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	3-Mar-27	9-Mar-27	546.0d
13643	TT-SQ1-SG3-A24-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	10-Mar-27	23-Mar-27	546.0d
13644	TT-SQ1-SG3-A24-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 24	10.0d	24-Mar-27	6-Apr-27	546.0d
13645	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 25		35.0d	3-Mar-27	20-Apr-27	537.0d
13646	TT-SQ1-SG3-A25-10	Tag & Trace - Sequence 1 - Stage 3 - Area 25	10.0d	3-Mar-27	16-Mar-27	0.0d
13647	TT-SQ1-SG3-A25-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	17-Mar-27	23-Mar-27	536.0d
13648	TT-SQ1-SG3-A25-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	24-Mar-27	6-Apr-27	536.0d
13649	TT-SQ1-SG3-A25-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 25	10.0d	7-Apr-27	20-Apr-27	536.0d
13650	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 26		35.0d	17-Mar-27	4-May-27	527.0d

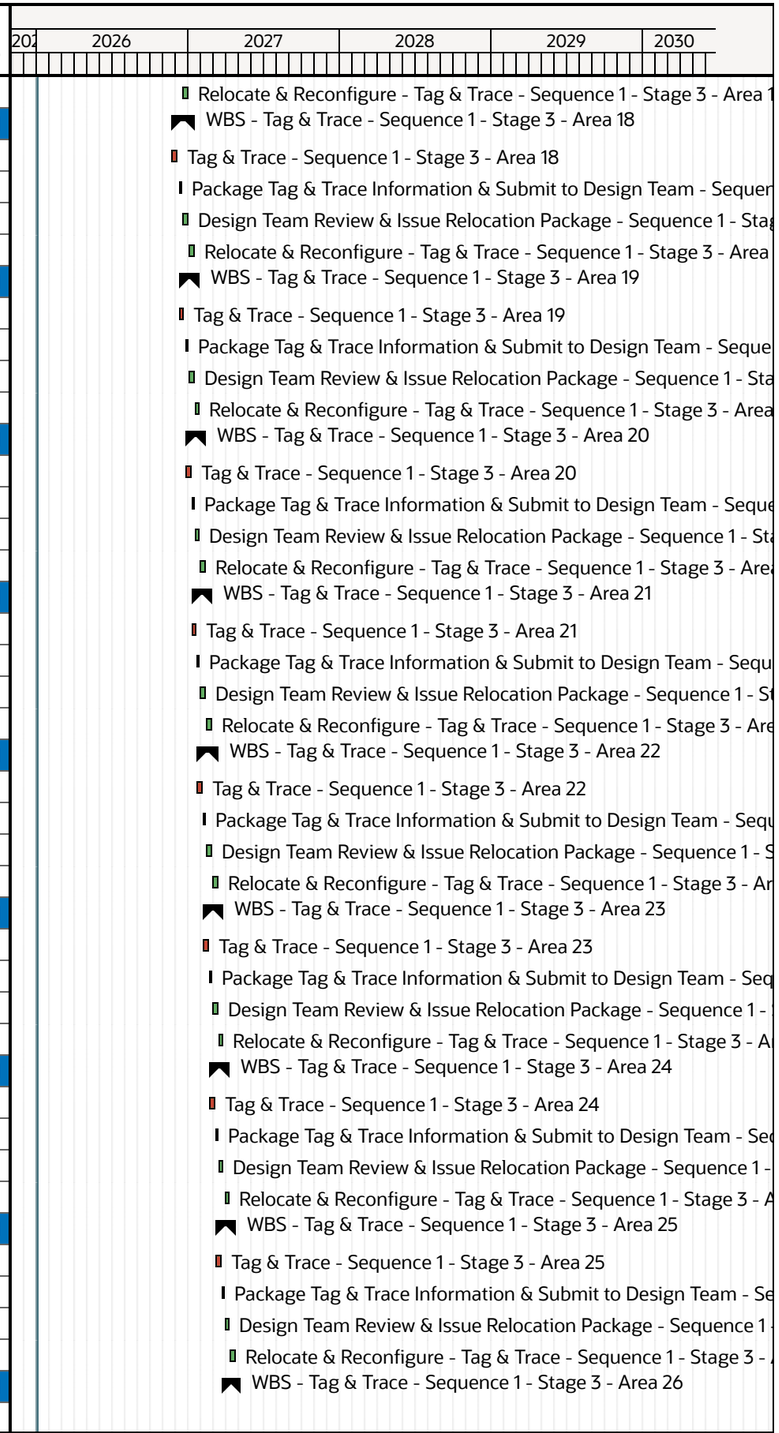


ID	Name	Dur	Start	Finish	TF
13651	TT-SQ1-SG3-A26-10	Tag & Trace - Sequence 1 - Stage 3 - Area 26	10.0d	17-Mar-27	30-Mar-27	0.0d
13652	TT-SQ1-SG3-A26-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	31-Mar-27	6-Apr-27	526.0d
13653	TT-SQ1-SG3-A26-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	7-Apr-27	20-Apr-27	526.0d
13654	TT-SQ1-SG3-A26-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 26	10.0d	21-Apr-27	4-May-27	526.0d
13655	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 27		35.0d	31-Mar-27	18-May-27	517.0d
13656	TT-SQ1-SG3-A27-10	Tag & Trace - Sequence 1 - Stage 3 - Area 27	10.0d	31-Mar-27	13-Apr-27	0.0d
13657	TT-SQ1-SG3-A27-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	14-Apr-27	20-Apr-27	516.0d
13658	TT-SQ1-SG3-A27-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	21-Apr-27	4-May-27	516.0d
13659	TT-SQ1-SG3-A27-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 27	10.0d	5-May-27	18-May-27	516.0d
13660	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 28		35.0d	14-Apr-27	2-Jun-27	507.0d
13661	TT-SQ1-SG3-A28-10	Tag & Trace - Sequence 1 - Stage 3 - Area 28	10.0d	14-Apr-27	27-Apr-27	0.0d
13662	TT-SQ1-SG3-A28-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	28-Apr-27	4-May-27	506.0d
13663	TT-SQ1-SG3-A28-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	5-May-27	18-May-27	506.0d
13664	TT-SQ1-SG3-A28-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 28	10.0d	19-May-27	2-Jun-27	506.0d
13665	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 29		35.0d	28-Apr-27	16-Jun-27	497.0d
13666	TT-SQ1-SG3-A29-10	Tag & Trace - Sequence 1 - Stage 3 - Area 29	10.0d	28-Apr-27	11-May-27	0.0d
13667	TT-SQ1-SG3-A29-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	12-May-27	18-May-27	496.0d
13668	TT-SQ1-SG3-A29-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	19-May-27	2-Jun-27	496.0d
13669	TT-SQ1-SG3-A29-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 29	10.0d	3-Jun-27	16-Jun-27	496.0d
13670	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 30		35.0d	12-May-27	30-Jun-27	487.0d
13671	TT-SQ1-SG3-A30-10	Tag & Trace - Sequence 1 - Stage 3 - Area 30	10.0d	12-May-27	25-May-27	0.0d
13672	TT-SQ1-SG3-A30-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	26-May-27	2-Jun-27	486.0d
13673	TT-SQ1-SG3-A30-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	3-Jun-27	16-Jun-27	486.0d
13674	TT-SQ1-SG3-A30-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 30	10.0d	17-Jun-27	30-Jun-27	486.0d
13675	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 31		35.0d	26-May-27	15-Jul-27	477.0d
13676	TT-SQ1-SG3-A31-10	Tag & Trace - Sequence 1 - Stage 3 - Area 31	10.0d	26-May-27	9-Jun-27	0.0d
13677	TT-SQ1-SG3-A31-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	10-Jun-27	16-Jun-27	476.0d
13678	TT-SQ1-SG3-A31-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	17-Jun-27	30-Jun-27	476.0d
13679	TT-SQ1-SG3-A31-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 31	10.0d	1-Jul-27	15-Jul-27	476.0d
13680	WBS - Tag & Trace - Sequence 1 - Stage 3 - Area 32		35.0d	10-Jun-27	29-Jul-27	467.0d
13681	TT-SQ1-SG3-A32-10	Tag & Trace - Sequence 1 - Stage 3 - Area 32	10.0d	10-Jun-27	23-Jun-27	0.0d
13682	TT-SQ1-SG3-A32-20	Package Tag & Trace Information & Submit to Design Team - Sequence 1 - Stag...	5.0d	24-Jun-27	30-Jun-27	466.0d
13683	TT-SQ1-SG3-A32-30	Design Team Review & Issue Relocation Package - Sequence 1 - Stage 3 - Area ...	10.0d	1-Jul-27	15-Jul-27	466.0d
13684	TT-SQ1-SG3-A32-40	Relocate & Reconfigure - Tag & Trace - Sequence 1 - Stage 3 - Area 32	10.0d	16-Jul-27	29-Jul-27	466.0d
13685	WBS - Tag & Trace - Sequence 2 - Stage 1		55.0d	24-Jun-27	10-Sep-27	173.0d
13686	WBS - Tag & Trace - Sequence 2 - Stage 1 - Area 1		35.0d	24-Jun-27	12-Aug-27	193.0d
13687	TT-SQ2-SG1-A1-10	Tag & Trace - Sequence 2 - Stage 1 - Area 1	10.0d	24-Jun-27	8-Jul-27	0.0d
13688	TT-SQ2-SG1-A1-20	Package Tag & Trace Information & Submit to Design Team - Sequence 2 - Stag...	5.0d	9-Jul-27	15-Jul-27	193.0d
13689	TT-SQ2-SG1-A1-30	Design Team Review & Issue Relocation Package - Sequence 2 - Stage 1 - Area 1	10.0d	16-Jul-27	29-Jul-27	193.0d
13690	TT-SQ2-SG1-A1-40	Relocate & Reconfigure - Tag & Trace - Sequence 2 - Stage 1 - Area 1	10.0d	30-Jul-27	12-Aug-27	193.0d
13691	WBS - Tag & Trace - Sequence 2 - Stage 1 - Area 2		35.0d	9-Jul-27	26-Aug-27	183.0d
13692	TT-SQ2-SG1-A2-10	Tag & Trace - Sequence 2 - Stage 1 - Area 2	10.0d	9-Jul-27	22-Jul-27	0.0d

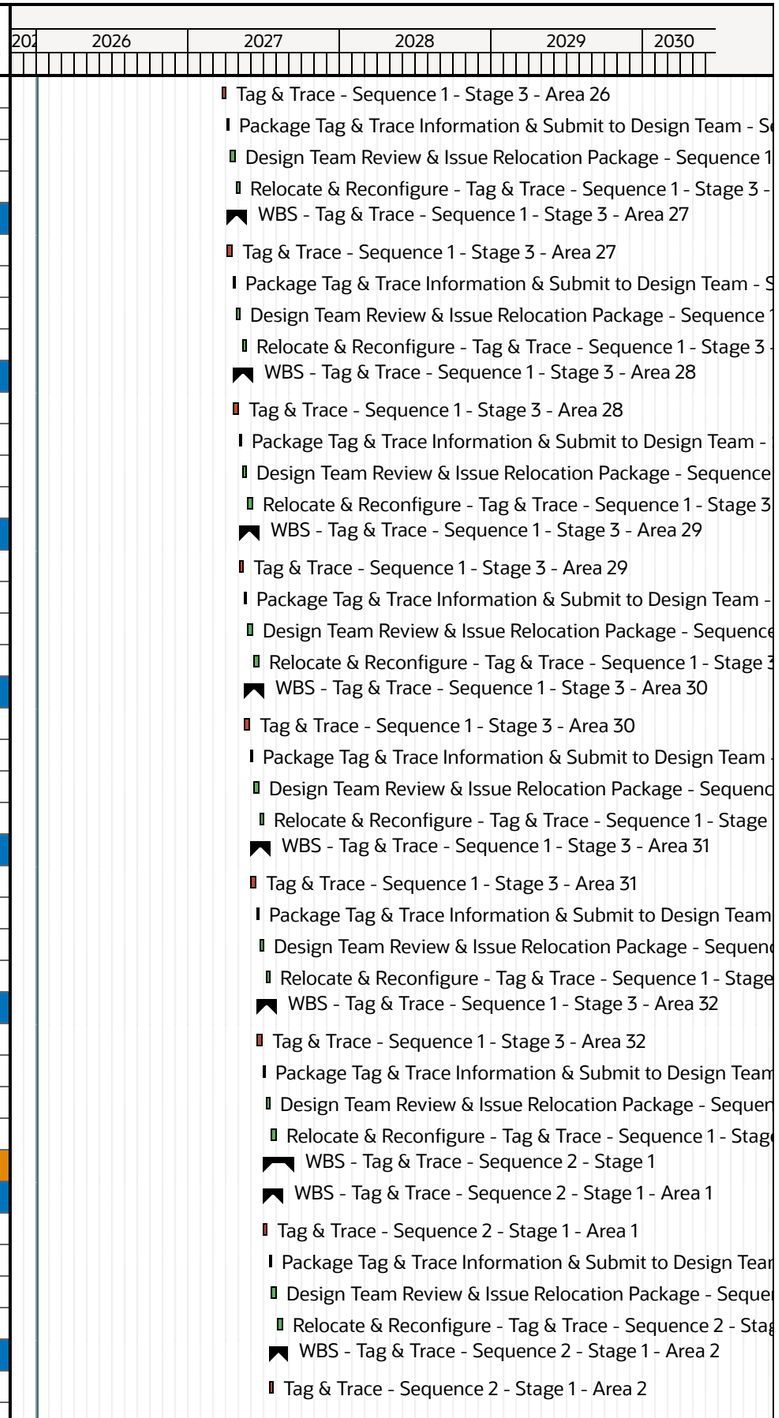


	ID	Name	Dur	Start	Finish	TF
13693	TT-SQ2-SG1-A2-20	Package Tag & Trace Information & Submit to Design Team - Sequence 2 - Stag...	5.0d	23-Jul-27	29-Jul-27	183.0d
13694	TT-SQ2-SG1-A2-30	Design Team Review & Issue Relocation Package - Sequence 2 - Stage 1 - Area 2	10.0d	30-Jul-27	12-Aug-27	183.0d
13695	TT-SQ2-SG1-A2-40	Relocate & Reconfigure - Tag & Trace - Sequence 2 - Stage 1 - Area 2	10.0d	13-Aug-27	26-Aug-27	183.0d
13696	WBS - Tag & Trace - Sequence 2 - Stage 3 - Area 3		35.0d	23-Jul-27	10-Sep-27	0.0d
13697	TT-SQ2-SG1-A3-10	Tag & Trace - Sequence 2 - Stage 1 - Area 3	10.0d	23-Jul-27	5-Aug-27	0.0d
13698	TT-SQ2-SG1-A3-20	Package Tag & Trace Information & Submit to Design Team - Sequence 2 - Stag...	5.0d	6-Aug-27	12-Aug-27	0.0d
13699	TT-SQ2-SG1-A3-30	Design Team Review & Issue Relocation Package - Sequence 2 - Stage 1 - Area 3	10.0d	13-Aug-27	26-Aug-27	0.0d
13700	TT-SQ2-SG1-A3-40	Relocate & Reconfigure - Tag & Trace - Sequence 2 - Stage 1 - Area 3	10.0d	27-Aug-27	10-Sep-27	0.0d
13701	WBS - BHS Power		227.0d	8-Jun-26	28-Apr-27	623.0d
13702	WBS - BHS Power Feeds		227.0d	8-Jun-26	28-Apr-27	623.0d
13703	WBS - HMPP-1		25.0d	8-Jun-26	13-Jul-26	277.0d
13704	BG-PF-MPPA-2010	Install & Test HMPP-1 [01-01-01]	10.0d	8-Jun-26	19-Jun-26	26.0d
13705	BG-PF-MPPA-2030	Install & Test Feeder to MPP/FCP A2 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	138.0d
13706	BG-PF-MPPA-2040	Install & Test Feeder to MPP/FCP A5 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	138.0d
13707	BG-PF-MPPA-2050	Install & Test Feeder to MPP/FCP A17 [01-01-01]	15.0d	22-Jun-26	13-Jul-26	26.0d
13708	BG-PF-MPPB-410	Install & Test Feeder to CLM1-11-XBI [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13709	BG-PF-MPPB-430	Install & Test Feeder to MEM1-13-XBI [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13710	BG-PF-MPPB-470	Install & Test Feeder to OSRM5A-14-XBI [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13711	BG-PF-MPPB-450	Install & Test Feeder to OSRM1A-17-XBI [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13712	WBS - HMPP-2		25.0d	8-Jun-26	13-Jul-26	410.0d
13713	BG-PF-MPPB-230	Install & Test HMPP-2 [01-01-02]	10.0d	8-Jun-26	19-Jun-26	37.0d
13714	BG-PF-MPPB-240	Install & Test Feeder to MPP/FCP B9 [01-01-02]	15.0d	22-Jun-26	13-Jul-26	37.0d
13715	BG-PF-MPPB-250	Install & Test Feeder to MPP/FCP B13 [01-03-06]	15.0d	22-Jun-26	13-Jul-26	410.0d
13716	WBS - HMPP-3		25.0d	8-Jun-26	13-Jul-26	277.0d
13717	BG-PF-MPPB-110	Install & Test HMPP-3 [01-01-01]	10.0d	8-Jun-26	19-Jun-26	11.0d
13718	BG-PF-MPPB-120	Install & Test Feeder to MPP/FCP B1 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13719	BG-PF-MPPB-130	Install & Test Feeder to MPP/FCP B2 [01-02-01]	15.0d	22-Jun-26	13-Jul-26	83.0d
13720	BG-PF-MPPB-290	Install & Test Feeder to MPP/FCP B17 [01-01-01]	15.0d	22-Jun-26	13-Jul-26	11.0d
13721	WBS - HMPP-4		25.0d	8-Jun-26	13-Jul-26	535.0d
13722	BG-PF-MPPB-190	Install & Test HMPP-4 [01-01-05]	10.0d	8-Jun-26	19-Jun-26	72.0d
13723	BG-PF-MPPB-200	Install & Test Feeder to MPP/FCP B4 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13724	BG-PF-MPPB-220	Install & Test Feeder to MPP/FCP B8 [01-01-05]	15.0d	22-Jun-26	13-Jul-26	72.0d
13725	BG-PF-MPPB-420	Install & Test Feeder to CLM2-12-XBI [02-01-1C]	15.0d	22-Jun-26	13-Jul-26	487.0d
13726	BG-PF-MPPB-210	Install & Test Feeder to MPP/FCP B5 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13727	BG-PF-MPPB-390	Install & Test Feeder to C8-11-XBI [02-01-3A]	15.0d	22-Jun-26	13-Jul-26	535.0d
13728	BG-PF-MPPB-440	Install & Test Feeder to MEM2-13-XBI [02-01-1C]	15.0d	22-Jun-26	13-Jul-26	487.0d
13729	WBS - HMPP-5		25.0d	8-Jun-26	13-Jul-26	410.0d
13730	BG-PF-MPPB-300	Install & Test HMPP-5 [01-03-03]	10.0d	8-Jun-26	19-Jun-26	323.0d
13731	BG-PF-MPPB-310	Install & Test Feeder to MPP/FCP B15 [01-03-06]	15.0d	22-Jun-26	13-Jul-26	410.0d
13732	BG-PF-MPPB-320	Install & Test Feeder to MPP/FCP B16 [01-03-03]	15.0d	22-Jun-26	13-Jul-26	323.0d
13733	WBS - HMPP-6		25.0d	25-Mar-27	28-Apr-27	208.0d
13734	BG-PF-MPPA-2060	Install & Test HMPP-6 [01-03-01]	10.0d	25-Mar-27	7-Apr-27	75.0d

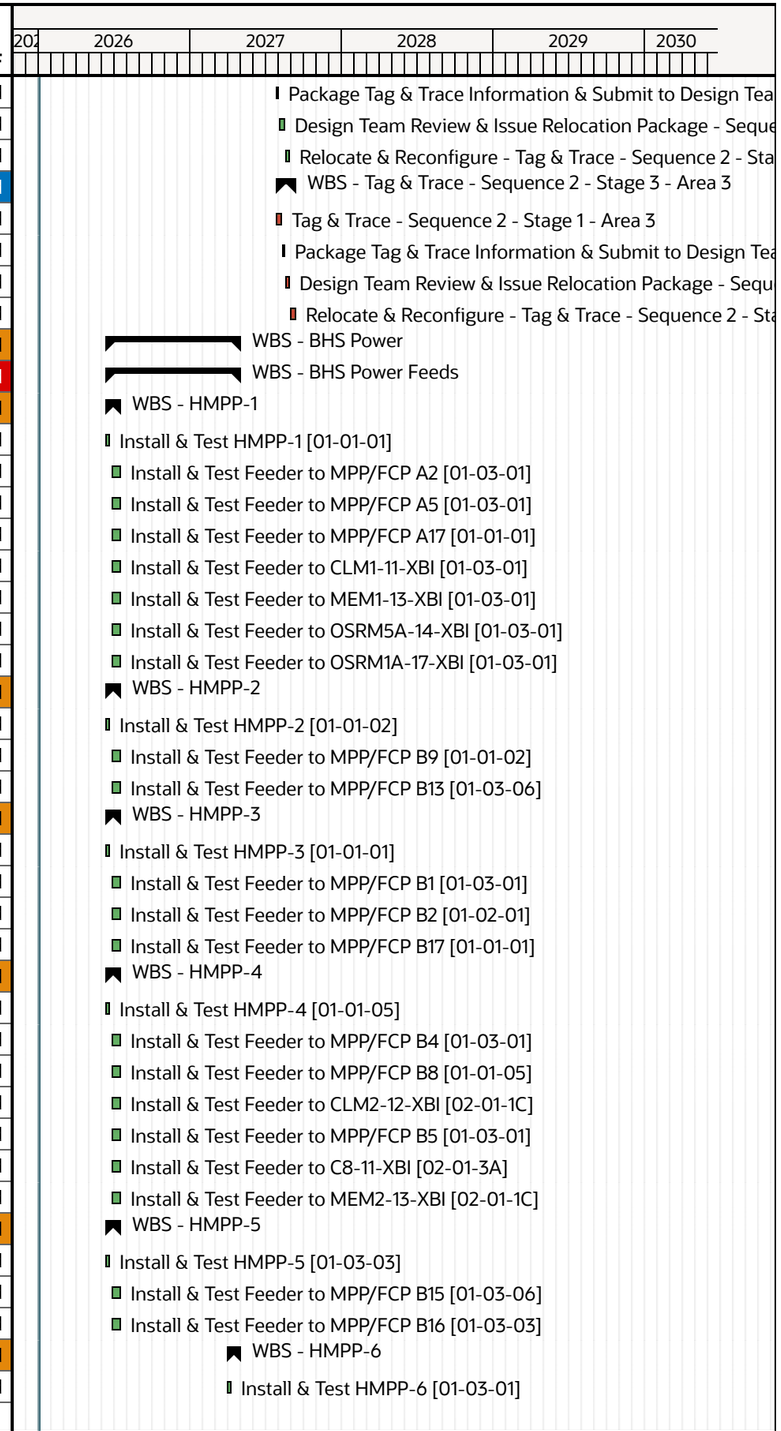


	ID	Name	Dur	Start	Finish	TF
13735	BG-PF-MPPA-2070	Install & Test Feeder to MPP/FCP A3 [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13736	BG-PF-MPPA-2080	Install & Test Feeder to MPP/FCP A6 [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13737	BG-PF-MPPA-2090	Install & Test Feeder to MPP/FCP A8 [01-03-06]	15.0d	8-Apr-27	28-Apr-27	208.0d
13738	WBS - HMPP-7		25.0d	25-Mar-27	28-Apr-27	251.0d
13739	BG-PF-MPPB-140	Install & Test HMPP-7 [01-03-01]	10.0d	25-Mar-27	7-Apr-27	75.0d
13740	BG-PF-MPPB-160	Install & Test Feeder to MPP/FCP B6 [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13741	BG-PF-MPPB-150	Install & Test Feeder to MPP/FCP B3 [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13742	BG-PF-MPPB-170	Install & Test Feeder to MPP/FCP B7 [01-03-06]	15.0d	8-Apr-27	28-Apr-27	208.0d
13743	BG-PF-MPPB-180	Install & Test Feeder to MPP/FCP B11 [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13744	BG-PF-MPPB-460	Install & Test Feeder to OSRM1B-12-XBI [01-03-01]	15.0d	8-Apr-27	28-Apr-27	75.0d
13745	BG-PF-MPPB-380	Install & Test Feeder to C5-16-XBI [01-03-06]	15.0d	8-Apr-27	28-Apr-27	251.0d
13746	WBS - HMPP-8		25.0d	8-Jun-26	13-Jul-26	825.0d
13747	BG-PF-MPPB-330	Install & Test HMPP-8 [01-03-01]	10.0d	8-Jun-26	19-Jun-26	824.0d
13748	BG-PF-MPPB-340	Install & Test Feeder to MPP/FCP B18 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	824.0d
13749	BG-PF-MPPB-350	Install & Test Feeder to MPP/FCP B19 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	824.0d
13750	WBS - HMPP-9		25.0d	2-Jul-26	6-Aug-26	626.0d
13751	BG-PF-MPPA-2100	Install & Test HMPP-9 [01-03-03]	10.0d	2-Jul-26	16-Jul-26	305.0d
13752	BG-PF-MPPA-2110	Install & Test Feeder to MPP/FCP A10 [01-03-03]	15.0d	17-Jul-26	6-Aug-26	305.0d
13753	BG-PF-MPPA-2140	Install & Test Feeder to MPP/FCP A15 [01-03-03]	15.0d	17-Jul-26	6-Aug-26	305.0d
13754	BG-PF-MPPA-2120	Install & Test Feeder to MPP/FCP A12 [02-02-1A]	15.0d	17-Jul-26	6-Aug-26	626.0d
13755	BG-PF-MPPA-2130	Install & Test Feeder to MPP/FCP A14 [01-03-03]	15.0d	17-Jul-26	6-Aug-26	305.0d
13756	BG-PF-MPPB-370	Install & Test Feeder to C3-14-XBI [01-03-03]	15.0d	17-Jul-26	6-Aug-26	316.0d
13757	WBS - HMPP-11		25.0d	8-Jun-26	13-Jul-26	410.0d
13758	BG-PF-MPPA-1990	Install & Test HMPP-11 [01-01-02]	10.0d	8-Jun-26	19-Jun-26	98.0d
13759	BG-PF-MPPA-910	Install & Test Feeder to MPP/FCP A9 [01-01-02]	15.0d	22-Jun-26	13-Jul-26	98.0d
13760	BG-PF-MPPA-120	Install & Test Feeder to MPP/FCP A1 [01-01-02]	15.0d	22-Jun-26	13-Jul-26	98.0d
13761	BG-PF-MPPA-1310	Install & Test Feeder to MPP/FCP A13 [01-03-06]	15.0d	22-Jun-26	13-Jul-26	410.0d
13762	BG-PF-MPPA-2000	Install & Test Feeder to MPP/FCP A4 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	138.0d
13763	BG-PF-MPPB-400	Install & Test Feeder to C8A-25-XBI [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13764	WBS - HMPP-12		25.0d	8-Jun-26	13-Jul-26	453.0d
13765	BG-PF-MPPB-260	Install & Test HMPP-12 [01-03-01]	10.0d	8-Jun-26	19-Jun-26	277.0d
13766	BG-PF-MPPB-270	Install & Test Feeder to MPP/FCP B10 [01-03-06]	15.0d	22-Jun-26	13-Jul-26	410.0d
13767	BG-PF-MPPB-280	Install & Test Feeder to MPP/FCP B14 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	277.0d
13768	BG-PF-MPPB-360	Install & Test Feeder to C2-16-XBI [01-03-06]	15.0d	22-Jun-26	13-Jul-26	453.0d
13769	WBS - HMPP-13		25.0d	8-Jun-26	13-Jul-26	825.0d
13770	BG-PF-MPPA-2230	Install & Test HMPP-13 [01-03-01]	10.0d	8-Jun-26	19-Jun-26	824.0d
13771	BG-PF-MPPA-2240	Install & Test Feeder to MPP/FCP A18 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	824.0d
13772	BG-PF-MPPA-2250	Install & Test Feeder to MPP/FCP A19 [01-03-01]	15.0d	22-Jun-26	13-Jul-26	824.0d
13773	WBS - HMPP-14		25.0d	2-Jul-26	6-Aug-26	740.0d
13774	BG-PF-MPPA-2150	Install & Test HMPP-14 [01-03-03]	10.0d	2-Jul-26	16-Jul-26	305.0d
13775	BG-PF-MPPA-2160	Install & Test Feeder to MPP/FCP A10 [01-03-03]	15.0d	17-Jul-26	6-Aug-26	305.0d
13776	BG-PF-MPPA-2170	Install & Test Feeder to MPP/FCP AOS [02-02-3C]	15.0d	17-Jul-26	6-Aug-26	739.0d

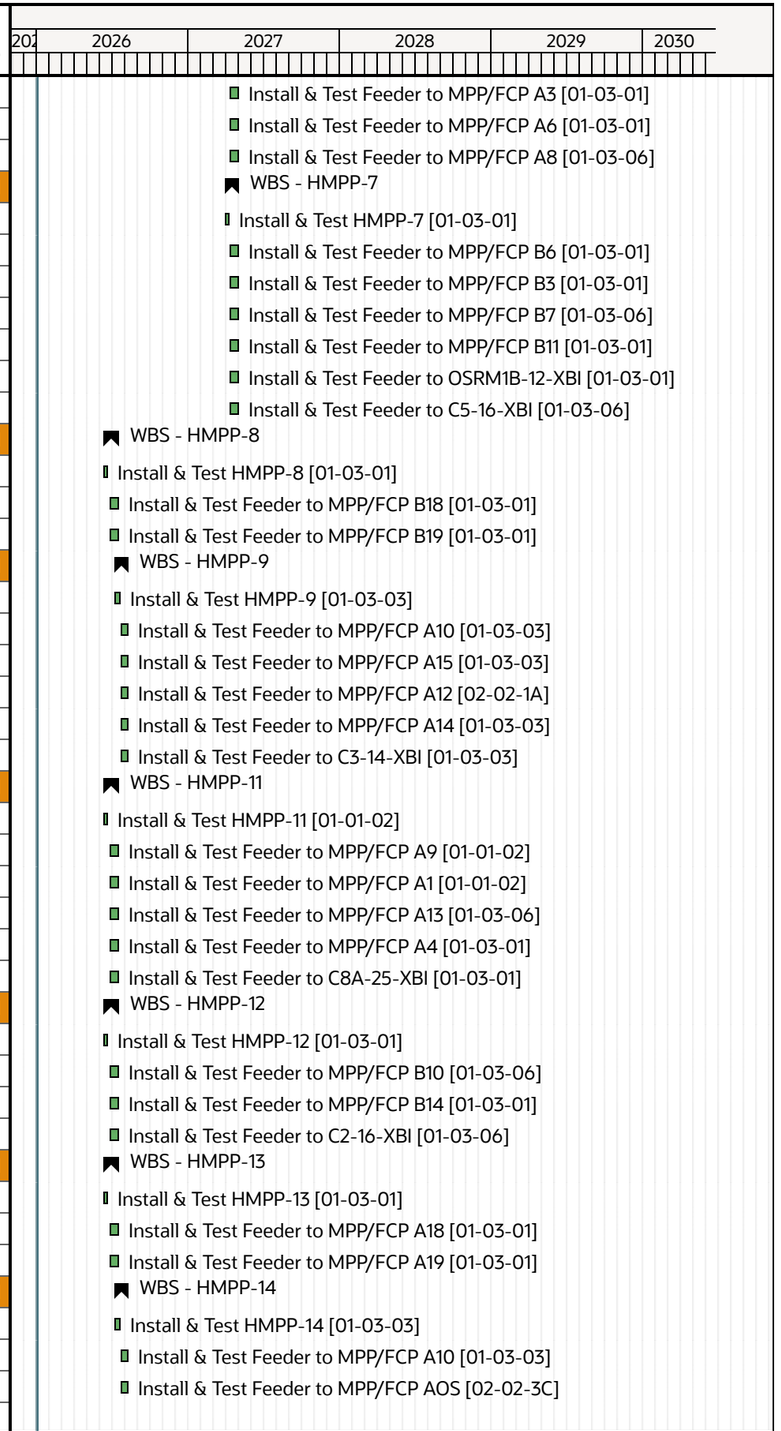


	ID	Name	Dur	Start	Finish	TF
13777	WBS - EDS-UPS1		18.0d	25-Mar-27	19-Apr-27	364.0d
13778	BG-PF-EDS-100	Elec. Install - Set MPP EDS-UPS1	2.0d	25-Mar-27	26-Mar-27	364.0d
13779	BG-PF-EDS-110	Install Hangers for Feeder From MSB-EDS1 to EDS-UPS1	2.0d	29-Mar-27	30-Mar-27	364.0d
13780	BG-PF-EDS-120	Elec. Install - Rough-In Elec. From EDS-UPS1 to Conveyor Location [West EDS ...	10.0d	29-Mar-27	9-Apr-27	370.0d
13781	BG-PF-EDS-130	Rough-In OH Conduit for Feeder From MSB-EDS1 to EDS-UPS1	8.0d	31-Mar-27	9-Apr-27	364.0d
13782	BG-PF-EDS-140	Pull Feeder From MSB-EDS1 to EDS-UPS1	2.0d	12-Apr-27	13-Apr-27	364.0d
13783	BG-PF-EDS-150	Third-Party Testing of Feeder From MSB-EDS1 to EDS-UPS1	1.0d	14-Apr-27	14-Apr-27	364.0d
13784	BG-PF-EDS-160	Termination of Feeder From MSB-EDS1 to EDS-UPS1	2.0d	15-Apr-27	16-Apr-27	364.0d
13785	BG-PF-EDS-170	Inspection of Feeder From MSB-EDS1 to EDS-UPS1	1.0d	19-Apr-27	19-Apr-27	364.0d
13786	WBS - EDS-UPS2		18.0d	11-Mar-27	5-Apr-27	374.0d
13787	BG-PF-EDS-200	Elec. Install - Set MPP EDS-UPS2	2.0d	11-Mar-27	12-Mar-27	374.0d
13788	BG-PF-EDS-210	Install Hangers for Feeder From MSB-EDS2 to EDS-UPS2	2.0d	15-Mar-27	16-Mar-27	374.0d
13789	BG-PF-EDS-220	Elec. Install - Rough-In Elec. From EDS-UPS2 to Conveyor Location [East EDS M...	10.0d	15-Mar-27	26-Mar-27	380.0d
13790	BG-PF-EDS-230	Rough-In OH Conduit for Feeder From MSB-EDS2 to EDS-UPS2	8.0d	17-Mar-27	26-Mar-27	374.0d
13791	BG-PF-EDS-240	Pull Feeder From MSB-EDS2 to EDS-UPS2	2.0d	29-Mar-27	30-Mar-27	374.0d
13792	BG-PF-EDS-250	Third-Party Testing of Feeder From MSB-EDS2 to EDS-UPS2	1.0d	31-Mar-27	31-Mar-27	374.0d
13793	BG-PF-EDS-260	Termination of Feeder From MSB-EDS2 to EDS-UPS2	2.0d	1-Apr-27	2-Apr-27	374.0d
13794	BG-PF-EDS-270	Inspection of Feeder From MSB-EDS2 to EDS-UPS2	1.0d	5-Apr-27	5-Apr-27	374.0d
13795	WBS - EDS-1 (Existing)		15.0d	8-Jun-26	26-Jun-26	333.0d
13796	A110520	Install & Test Feeder to MPP/FCP B12	15.0d	8-Jun-26	26-Jun-26	333.0d
13797	WBS - EDS-2 (Existing)		15.0d	25-Mar-27	14-Apr-27	85.0d
13798	BG-PF-MPPA-2220	Install & Test Feeder to MPP/FCP A7	15.0d	25-Mar-27	14-Apr-27	85.0d
13799	WBS - EDS-4		25.0d	7-Jan-27	10-Feb-27	263.0d
13800	BG-PF-MPPA-2180	Install & Test EDS-4	10.0d	7-Jan-27	20-Jan-27	145.0d
13801	BG-PF-MPPA-2200	Install & Test Feeder to MPP/FCP A16	15.0d	21-Jan-27	10-Feb-27	263.0d
13802	BG-PF-MPPA-2190	Install & Test Feeder to MPP/FCP A11	15.0d	21-Jan-27	10-Feb-27	145.0d
13803	WBS - CBRA Room		111.0d	28-Jan-27	2-Jul-27	289.0d
13804	A33270	Frame Walls - CBRA Room	15.0d	28-Jan-27	17-Feb-27	289.0d
13805	A33290	Low-Voltage In-Wall Rough-In - CBRA Room	10.0d	4-Feb-27	17-Feb-27	319.0d
13806	A33280	Elec. In-Wall Rough-In - CBRA Room	10.0d	4-Feb-27	17-Feb-27	319.0d
13807	A33300	Mech. In-Wall Rough-In - CBRA Room	10.0d	4-Feb-27	17-Feb-27	289.0d
13808	A33410	Mech. Ceiling Rough-In - CBRA Room	10.0d	18-Feb-27	3-Mar-27	289.0d
13809	A33310	Insulate Walls & Install Wood Blocking - CBRA Room	10.0d	4-Mar-27	17-Mar-27	289.0d
13810	A33320	Wall Close-In Inspection - CBRA Room	1.0d	18-Mar-27	18-Mar-27	313.0d
13811	A33360	Set Door Frames - CBRA Room	5.0d	18-Mar-27	24-Mar-27	289.0d
13812	A33330	Hang, Tape, & Finish Interior Walls - CBRA Room	15.0d	19-Mar-27	8-Apr-27	313.0d
13813	A33370	Install Doors & Hardware - CBRA Room	5.0d	25-Mar-27	31-Mar-27	289.0d
13814	A33380	Pull Wire & Terminate Door Power & Security - CBRA Room	10.0d	1-Apr-27	14-Apr-27	289.0d
13815	A33390	Elec. OH Rough-In - CBRA Room	10.0d	15-Apr-27	28-Apr-27	289.0d
13816	A33400	Low-Voltage OH Rough-In - CBRA Room	10.0d	29-Apr-27	12-May-27	289.0d
13817	A33340	Hang, Tape, & Install FRP @ Exterior Walls - CBRA Room	15.0d	13-May-27	3-Jun-27	289.0d
13818	A33350	Apply Head-of-Wall Sealant - CBRA Room	5.0d	4-Jun-27	10-Jun-27	289.0d

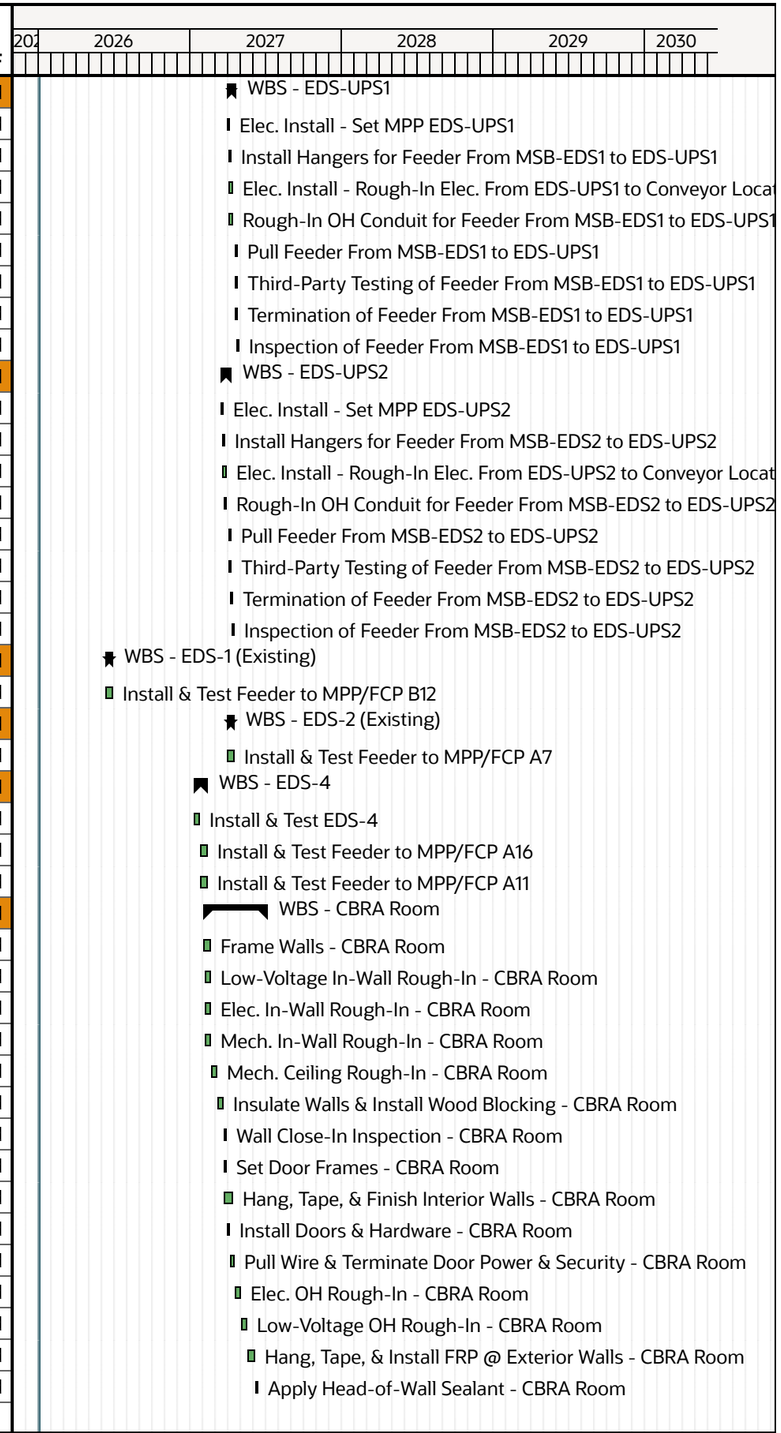


	ID	Name	Dur	Start	Finish	TF
13819	A64060	Install Ceiling Grid - CBRA Room	10.0d	11-Jun-27	24-Jun-27	289.0d
13820	A64070	Ceiling Close-In Inspection - CBRA Room	1.0d	25-Jun-27	25-Jun-27	289.0d
13821	A64080	Install ACT Ceiling - CBRA Room	5.0d	28-Jun-27	2-Jul-27	289.0d
13822	WBS - CBIS West		90.0d	25-Mar-27	30-Jul-27	338.0d
13823	A43980	Frame Walls - CBIS West	15.0d	25-Mar-27	14-Apr-27	338.0d
13824	A43990	Low-Voltage In-Wall Rough-In - CBIS West	10.0d	1-Apr-27	14-Apr-27	363.0d
13825	A44000	Elec. In-Wall Rough-In - CBIS West	10.0d	1-Apr-27	14-Apr-27	363.0d
13826	A44010	Mech. In-Wall Rough-In - CBIS West	5.0d	1-Apr-27	7-Apr-27	338.0d
13827	A44020	Mech. Ceiling Rough-In - CBIS West	10.0d	8-Apr-27	21-Apr-27	338.0d
13828	A44030	Insulate Walls & Install Wood Blocking - CBIS West	10.0d	22-Apr-27	5-May-27	338.0d
13829	A44040	Wall Close-In Inspection - CBIS West	1.0d	6-May-27	6-May-27	362.0d
13830	A44050	Set Door Frames - CBIS West	5.0d	6-May-27	12-May-27	338.0d
13831	A44060	Hang, Tape, & Finish Interior Walls - CBIS West	15.0d	7-May-27	27-May-27	362.0d
13832	A44070	Install Doors & Hardware - CBIS West	5.0d	13-May-27	19-May-27	338.0d
13833	A44080	Pull Wire & Terminate Door Power & Security - CBIS West	10.0d	20-May-27	3-Jun-27	338.0d
13834	A44090	Elec. OH Rough-In - CBIS West	10.0d	4-Jun-27	17-Jun-27	338.0d
13835	A44100	Low-Voltage OH Rough-In - CBIS West	10.0d	18-Jun-27	1-Jul-27	338.0d
13836	A44110	Hang, Tape, & Install FRP @ Exterior Walls - CBIS West	15.0d	2-Jul-27	23-Jul-27	338.0d
13837	A44120	Apply Head-of-Wall Sealant - CBIS West	5.0d	26-Jul-27	30-Jul-27	338.0d
13838	WBS - CBIS East		95.0d	9-Dec-26	22-Apr-27	600.0d
13839	A44130	Frame Walls - CBIS East	15.0d	9-Dec-26	30-Dec-26	599.0d
13840	A44140	Low-Voltage In-Wall Rough-In - CBIS East	10.0d	16-Dec-26	30-Dec-26	629.0d
13841	A44150	Elec. In-Wall Rough-In - CBIS East	10.0d	16-Dec-26	30-Dec-26	629.0d
13842	A44160	Mech. In-Wall Rough-In - CBIS East	10.0d	16-Dec-26	30-Dec-26	599.0d
13843	A44170	Mech. Ceiling Rough-In - CBIS East	10.0d	31-Dec-26	14-Jan-27	599.0d
13844	A44180	Insulate Walls & Install Wood Blocking - CBIS East	10.0d	15-Jan-27	28-Jan-27	599.0d
13845	A44190	Wall Close-In Inspection - CBIS East	1.0d	29-Jan-27	29-Jan-27	623.0d
13846	A44200	Set Door Frames - CBIS East	5.0d	29-Jan-27	4-Feb-27	599.0d
13847	A44210	Hang, Tape, & Finish Interior Walls - CBIS East	15.0d	1-Feb-27	19-Feb-27	623.0d
13848	A44220	Install Doors & Hardware - CBIS East	5.0d	5-Feb-27	11-Feb-27	599.0d
13849	A44230	Pull Wire & Terminate Door Power & Security - CBIS East	10.0d	12-Feb-27	25-Feb-27	599.0d
13850	A44240	Elec. OH Rough-In - CBIS East	10.0d	26-Feb-27	11-Mar-27	599.0d
13851	A44250	Low-Voltage OH Rough-In - CBIS East	10.0d	12-Mar-27	25-Mar-27	599.0d
13852	A44260	Hang, Tape, & Install FRP @ Exterior Walls - CBIS East	15.0d	26-Mar-27	15-Apr-27	599.0d
13853	A44270	Apply Head-of-Wall Sealant - CBIS East	5.0d	16-Apr-27	22-Apr-27	599.0d
13854	WBS - PLC Room		73.0d	10-Apr-26	23-Jul-26	9.0d
13855	A108650	HCAA Clear Out Existing Level 2 Kitchen/Breakroom & IT Room - PLC Room	5.0d	10-Apr-26	16-Apr-26	26.0d
13856	A108630	Erect Temp Walls @ PLC/SRE Room - PLC Room	1.0d	17-Apr-26	17-Apr-26	26.0d
13857	A108690	Remove & Store Existing Ceiling Tiles - PLC Room	5.0d	20-Apr-26	24-Apr-26	26.0d
13858	A108660	Demo Walls, Doors, & Millwork @ Existing Level 2 Kitchen/Breakroom & IT Roo...	5.0d	27-Apr-26	1-May-26	26.0d
13859	A108670	Demo/Temp Support Existing Elec. Wiring, Devices, & Lighting - PLC Room	5.0d	27-Apr-26	1-May-26	26.0d
13860	A108730	HVAC Ceiling Rough-In - PLC Room	10.0d	27-Apr-26	8-May-26	46.0d

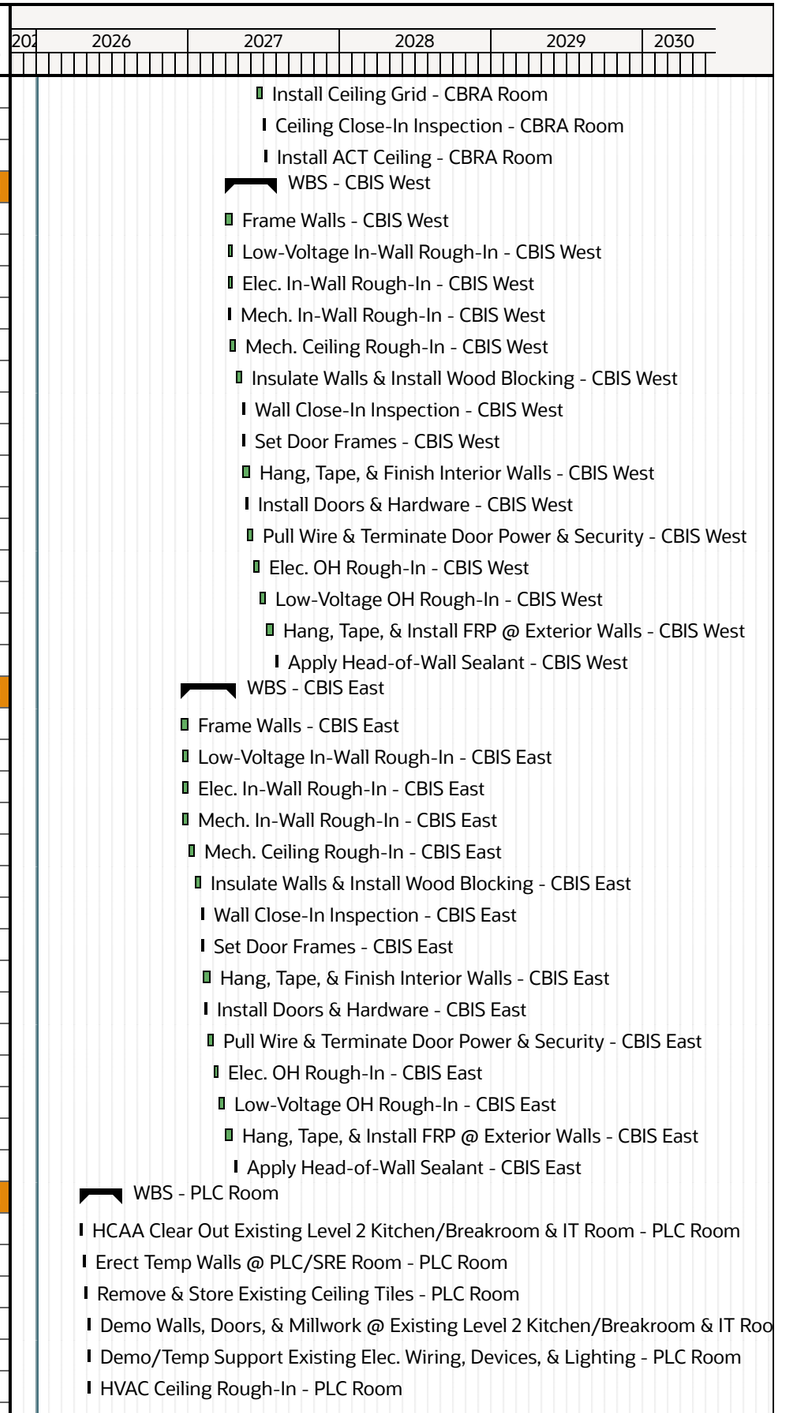

	ID	Name	Dur	Start	Finish	TF
13861	A108680	Demo/Temp Support Existing Low Voltage Wiring & Devices - PLC Room	5.0d	27-Apr-26	1-May-26	26.0d
13862	A108700	Frame New Walls at PLC/SRE Rooms - PLC Room	5.0d	4-May-26	8-May-26	26.0d
13863	A108710	Elec. Ceiling & In-Wall Rough-In - PLC Room	10.0d	11-May-26	22-May-26	26.0d
13864	A108720	Low Voltage Ceiling & In-Wall Rough-In - PLC Room	10.0d	4-Jun-26	17-Jun-26	9.0d
13865	A108740	Hang, Tape, & Finish New Walls - PLC Room	5.0d	18-Jun-26	24-Jun-26	9.0d
13866	A108750	Drop Ceiling Tile - PLC Room	5.0d	25-Jun-26	1-Jul-26	14.0d
13867	A108760	Install Doors & Frames - PLC Room	3.0d	25-Jun-26	29-Jun-26	16.0d
13868	A108770	Install Flooring - PLC Room	10.0d	25-Jun-26	9-Jul-26	9.0d
13869	A108780	Apply Final Paint - PLC Room	5.0d	10-Jul-26	16-Jul-26	9.0d
13870	A108790	Install OFCI Equip. & Furniture - PLC Room	5.0d	17-Jul-26	23-Jul-26	9.0d
13871	WBS - A-SORTATION & AIRSIDE C		100.0d	2-Jan-29	21-May-29	212.0d
13872	WBS - A-Sortation		60.0d	2-Jan-29	26-Mar-29	222.0d
13873	A81790	TA1 Tie-In - A Sortation	15.0d	2-Jan-29	22-Jan-29	211.0d
13874	A81800	TA2 Tie-In - A Sortation	15.0d	23-Jan-29	12-Feb-29	211.0d
13875	A81810	Salvage Abandoned-In-Place Conveyor - A Sortation	30.0d	13-Feb-29	26-Mar-29	221.0d
13876	WBS - Airside C		70.0d	13-Feb-29	21-May-29	212.0d
13877	A81820	TC1 Tie-In - Airside C	20.0d	13-Feb-29	12-Mar-29	211.0d
13878	A81830	TC2 Tie-In - Airside C	20.0d	13-Mar-29	9-Apr-29	211.0d
13879	A81840	Salvage Abandoned-In-Place Conveyor - Airside C	30.0d	10-Apr-29	21-May-29	211.0d
13880	WBS - AIRSDE E OPTIMIZATION		181.0d	19-Mar-29	30-Nov-29	77.0d
13881	A81850	Airside E Optimization Work Placeholder	180.0d	19-Mar-29	30-Nov-29	77.0d

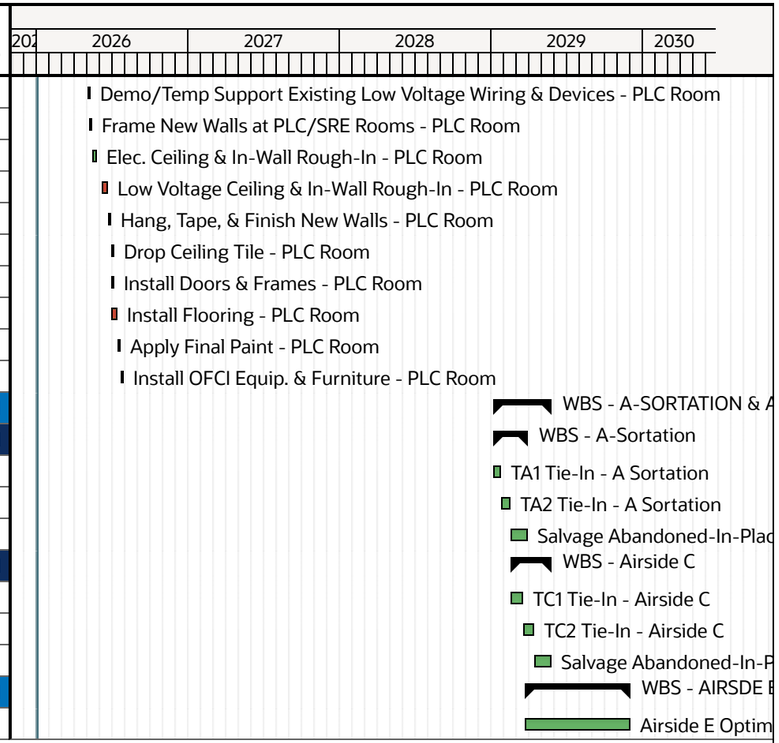

	ID	Name	Dur	Start	Finish	TF
1	WBS - Airside D - Tampa International Airport		610.0d	3-Aug-23 A	26-Dec-25 A	
2	WBS - PROJECT TIME TABLE SUMMARY		591.0d	3-Aug-23 A	1-Dec-25 A	
3	MLS-05	MLS - ASD Project Start	0.0d	3-Aug-23 A		
4	MLS-10	MLS - Design Kickoff Mtg.	0.0d	8-Aug-23 A		
5	WBS - Airside D - Supplement C Contractual Milestones		0.0d	25-Nov-25	25-Nov-25 A	
6	MLS-SUPP.C-01	MLS 1 - Enabling Substantial Completion	0.0d		25-Nov-25 A	
7	WBS - Airside D - Other Major Milestones		530.0d	30-Oct-23 A	1-Dec-25 A	
8	MLS-20	MLS - City Of Tampa Permitting Office Kick-Off Mtg.	0.0d	30-Oct-23 A		
9	MLS-30	MLS - Notice to Proceed/Enabling Construction Start	0.0d	13-Dec-24 A		
10	MLS-40	MLS - Approval Of FAA 7460 For Crane Plan	0.0d	27-Dec-24 A		
11	MLS-70	MLS - Ground Improvements Start	0.0d	3-Nov-25 A		
12	MLS-390	MLS - CIP Concrete Found. Start	0.0d	1-Dec-25 A		
13	WBS - Airside D - SOV LOE's		211.0d	27-Jan-25 A	20-Nov-25 A	
14	EN-HAM-50	Enabling - Demo Apron Concrete - (LOE)	94.0d	27-Jan-25 A	6-Jun-25 A	
15	EN-HAM-40	Performance Park/Office Trailers - (LOE)	211.0d	27-Jan-25 A	20-Nov-25 A	
16	EN-HAM-70	Enabling Apron Site Work - (LOE)	65.0d	18-Aug-25 A	17-Nov-25 A	
17	WBS - HCAA Board Approvals		551.0d	3-Aug-23	2-Oct-25 A	
18	MLS-BA-10	HCAA Board Approval Award Part 1 Agreement - 8.3.23	0.0d		3-Aug-23 A	
19	MLS-BA-20	Part 1 Agreement Design Notice to Proceed - 8.4.23	0.0d		4-Aug-23 A	
20	MLS-BA-30	HCAA Board Approval Enabling Pkg. - 12.5.24	0.0d		5-Dec-24 A	
21	MLS-BA-40	ITB 1 Pkg. - 6.5.25	0.0d		5-Jun-25 A	
22	MLS-BA-60	Part 2 Supp. A Agreement - Ground Improvement & Found. Pkg. - 8.7.25	0.0d		7-Aug-25 A	
23	MLS-BA-80	ITB 2 & 3 Pkg.s - 8.7.25	0.0d		7-Aug-25 A	
24	MLS-BA-90	HCAA June Board Approval of NST Credit Purchase Agreement - 8.7.25	0.0d		7-Aug-25 A	
25	MLS-BA-100	Part 2 Supp. B Agreement - Centralized Checked Baggage - 10.2.25	0.0d		2-Oct-25 A	
26	MLS-BA-110	Part 2 Supplement B - Board Approval	0.0d		2-Oct-25 A	
27	WBS - Design Milestones		260.0d	13-Aug-24	21-Aug-25 A	
28	MLS-DM-10	100% Enabling Pkg./BOD Due To HCAA Complete	0.0d		13-Aug-24 A	
29	MLS-DM-20	30% SD - ITB Pkg.s Submittals Due To HCAA Complete	0.0d		1-Oct-24 A	
30	MLS-DM-30	30% SD Final - 30% SD Due To HCAA Complete	0.0d		21-Nov-24 A	
31	MLS-DM-40	FAA/60% DD - ITB 1 Pkg. Submittals Due To HCAA Complete	0.0d		20-Dec-24 A	
32	MLS-DM-140	FAA/60% DD - ITB 3 Pkg. Submittals Due To HCAA Complete	0.0d		20-Dec-24 A	
33	MLS-DM-220	TSA SD/15% BHS Submission Complete	0.0d		20-Dec-24 A	
34	MLS-DM-130	FAA/60% DD - ITB 2 Pkg. Submittals Due To HCAA Complete	0.0d		10-Jan-25 A	
35	MLS-DM-50	60% Early Found. - 60% DD Subm. Due To HCAA Complete	0.0d		11-Feb-25 A	
36	MLS-DM-190	TSA CBIS 30% Deliverable Complete	0.0d		17-Mar-25 A	
37	MLS-DM-60	IFB/90% CD - ITB 1 Pkg. Subm. Due To HCAA Complete	0.0d		20-Mar-25 A	
38	MLS-DM-80	100% Early Found. - 100% DD Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
39	MLS-DM-160	IFB/90% CD - ITB 3 Pkg. Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
40	MLS-DM-150	ITB/90% CD - ITB 2 Pkg. Subm. Due To HCAA Complete	0.0d		10-Apr-25 A	
41	MLS-DM-170	Final Addendum CD - ITB 1 Subm. Due To HCAA Complete	0.0d		22-Apr-25 A	
42	MLS-DM-70	60% DD - 60% DD Due To HCAA Complete	0.0d		8-May-25 A	

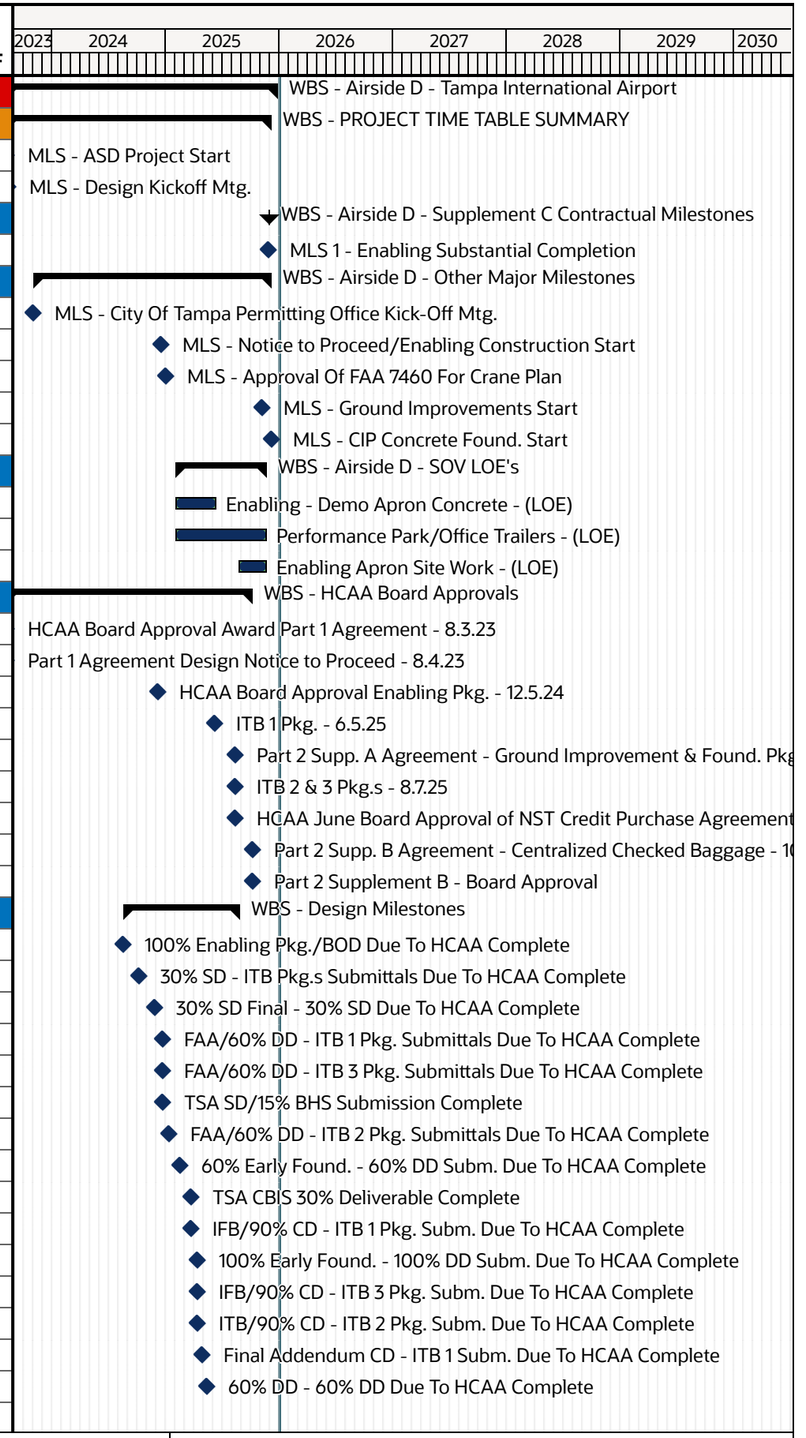

HENSEL PHELPS
Plan. Build. Manage.


Airside D - Tampa International Airport

ASD Development Program
Completed Activities Schedule
December 2025 - DD 12.26.25


Current
Progress
Critical
Milestones
Summary

Revised 23-Dec-25 11:43 a.m. | **Data Date:** 26-Dec-25
HP Project ID No: 8023226 | Region Code: HP-800
HCAA Package #8500 23
View Name: Schedule Submission to HCAA (Owner)
Printed By: Alex Melguizovski


	ID	Name	Dur	Start	Finish	TF
43	MLS-DM-90	Final Addendum CD - ITB 2 Subm. Due To HCAA Complete	0.0d		16-May-25 A	
44	MLS-DM-180	Final Addendum CD - ITB 3 Subm. Due To HCAA Complete	0.0d		16-May-25 A	
45	MLS-DM-100	75% Long Lead Pkg. - Procurement Subm. Due To HCAA Complete	0.0d		12-Jun-25 A	
46	MLS-DM-110	90% CD's/Permit - Final CD's Due To HCAA Complete	0.0d		21-Aug-25 A	
47	MLS-DM-200	TSA 70% BHS Submission Complete	0.0d		21-Aug-25 A	
48	WBS - Request For Information (RFI)		46.0d	17-Jul-25 A	19-Sep-25 A	
49	RFI-EN-00078	RFI - EN - 00078 - Trailer 4 Drainage Clarification	46.0d	17-Jul-25 A	19-Sep-25 A	
50	WBS - TAMPA AIRSIDE D TERMINAL		610.0d	3-Aug-23 A	26-Dec-25 A	
51	WBS - ASD - DESIGN & ENGINEERING PHASE		608.0d	3-Aug-23 A	23-Dec-25 A	
52	WBS - PDD Validation		148.0d	3-Aug-23 A	4-Mar-24 A	
53	WBS - Design Kickoff		24.0d	3-Aug-23 A	6-Sep-23 A	
54	DS-PDD-10	Summary/Analysis -PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
55	DS-PDD-20	Aircraft Planning - PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
56	DS-PDD-30	Building Footprint Development -PDD Validation	20.0d	3-Aug-23 A	30-Aug-23 A	
57	WBS - Design Charrette #1		22.0d	7-Aug-23 A	6-Sep-23 A	
58	DS-PDD-60	Forms & Mass Coord. - Validation Design Charrette #1	20.0d	7-Aug-23 A	1-Sep-23 A	
59	DS-PDD-70	Charrette In KC - Validation Design Charrette #1	2.0d	5-Sep-23 A	6-Sep-23 A	
60	WBS - Design Presentation #1 HCAA		3.0d	5-Sep-23 A	7-Sep-23 A	
61	DS-PDD-80	Design Presentation #1 - Steering Committee Mtg. Prep	2.0d	5-Sep-23 A	6-Sep-23 A	
62	DS-PDD-90	Design Presentation #1 - Steering Committee Mtg. #1 - Building Program	1.0d	7-Sep-23 A	7-Sep-23 A	
63	WBS - Design Presentation #2 HCAA		30.0d	3-Aug-23 A	14-Sep-23 A	
64	DS-PDD-40	BHS Kickoff Prep & Coord. - Design Presentation #2	28.0d	3-Aug-23 A	12-Sep-23 A	
65	DS-PDD-150	VTC Discussion - Design Presentation #2	1.0d	13-Sep-23 A	13-Sep-23 A	
66	DS-PDD-160	BHS Kickoff CBIS Mtg. - Design Presentation #2	1.0d	14-Sep-23 A	14-Sep-23 A	
67	WBS - Design Presentation #3 - Terminal Program		33.0d	3-Aug-23 A	19-Sep-23 A	
68	DS-PDD-50	Presentation Prep & Coord. - Design Presentation #3	32.0d	3-Aug-23 A	18-Sep-23 A	
69	DS-PDD-180	Building Space Program Allocation Mtg. - 9/19/23 - Design Presentation #3	1.0d	19-Sep-23 A	19-Sep-23 A	
70	WBS - Design Presentation #4 - CBP/Concessions Update		11.0d	7-Sep-23 A	21-Sep-23 A	
71	DS-PDD-100	Presentation Prep & Coord. - Design Presentation #4	10.0d	7-Sep-23 A	20-Sep-23 A	
72	DS-PDD-210	Stakeholder Engagement Kickoff Mtg. - Design Presentation #4	1.0d	21-Sep-23 A	21-Sep-23 A	
73	WBS - Design Presentation #5 - Aircraft Layout		16.0d	7-Sep-23 A	28-Sep-23 A	
74	DS-PDD-110	Aircraft Diagrams & Layout - Design Presentation #5	15.0d	7-Sep-23 A	27-Sep-23 A	
75	DS-PDD-250	Site Review Mtg. - Design Presentation #5	1.0d	28-Sep-23 A	28-Sep-23 A	
76	WBS - Design Presentation - 9/27/23 Benchmarking		14.0d	8-Sep-23 A	27-Sep-23 A	
77	DS-PDD-120	Benchmarking - Alstom/BHS Coord.	13.0d	8-Sep-23 A	26-Sep-23 A	
78	DS-PDD-230	Mtg. With HCAA - 9/27/23	1.0d	27-Sep-23 A	27-Sep-23 A	
79	WBS - Design Presentation #6 - Aircraft Parking Lot		15.0d	8-Sep-23 A	28-Sep-23 A	
80	DS-PDD-130	Aircraft Layout Coord. - Design Presentation #6	14.0d	8-Sep-23 A	27-Sep-23 A	
81	DS-PDD-260	Mtg. With HCAA - 9/28/23 - Design Presentation #6	1.0d	28-Sep-23 A	28-Sep-23 A	
82	WBS - VDC - BIM		4.0d	22-Sep-23 A	27-Sep-23 A	
83	DS-PDD-220	VDC - BIM Coord.	3.0d	22-Sep-23 A	26-Sep-23 A	
84	DS-PDD-240	BIM Coord. Mtg.	1.0d	27-Sep-23 A	27-Sep-23 A	

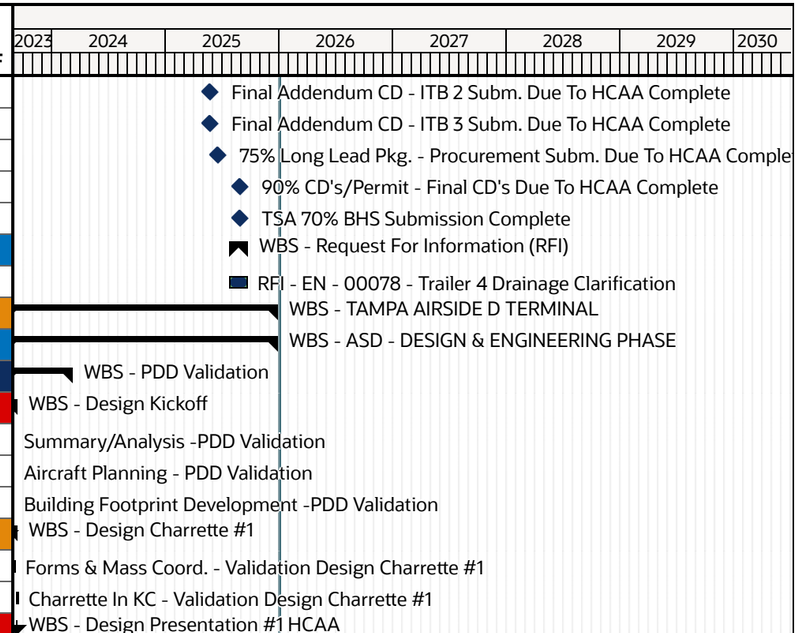


	ID	Name	Dur	Start	Finish	TF
85	WBS - Design Presentation #7 - CUP/Resiliency		25.0d	8-Sep-23 A	12-Oct-23 A	
86	DS-PDD-140	White Paper Studies/Preparation - Design Presentation #7	24.0d	8-Sep-23 A	11-Oct-23 A	
87	DS-PDD-320	White Paper/Studies/CUP Presentation Follow Up - Design Presentation #7	1.0d	12-Oct-23 A	12-Oct-23 A	
88	WBS - Design Presentation #8 - Building Form		68.0d	29-Sep-23 A	8-Jan-24 A	
89	DS-PDD-270	Building Forms & Interior Coord. - Design Presentation #8	8.0d	29-Sep-23 A	10-Oct-23 A	
90	DS-PDD-290	Building Forms/Interiors Mtg. - Design Presentation #8	1.0d	11-Oct-23 A	11-Oct-23 A	
91	DS-PDD-570	Building Form Analysis - Design Presentation #8	29.0d	22-Nov-23 A	5-Jan-24 A	
92	DS-PDD-930	Building Form Follow Up Mtg. - Design Presentation #8	1.0d	8-Jan-24 A	8-Jan-24 A	
93	WBS - Design Presentation #9 - Visioning Workshop 10/12/23		10.0d	29-Sep-23 A	12-Oct-23 A	
94	DS-PDD-280	Visioning Prep & Coord. - Design Presentation #9	8.0d	29-Sep-23 A	10-Oct-23 A	
95	DS-PDD-300	Visioning & Programming Workshop - Design Presentation #9	2.0d	11-Oct-23 A	12-Oct-23 A	
96	WBS - APM/MW Study		39.0d	13-Oct-23 A	8-Dec-23 A	
97	DS-PDD-340	APM Vs. Moving Walk Concept	20.0d	13-Oct-23 A	9-Nov-23 A	
98	DS-PDD-490	APM Vs. Moving Walk Analysis	13.0d	10-Nov-23 A	30-Nov-23 A	
99	DS-PDD-610	APM Vs. Moving Walk Review	2.0d	1-Dec-23 A	4-Dec-23 A	
100	DS-PDD-640	APM Vs. Moving Walk Presentation	1.0d	5-Dec-23 A	5-Dec-23 A	
101	DS-PDD-650	APM Vs. Moving Walk Decision (HCAA)	3.0d	6-Dec-23 A	8-Dec-23 A	
102	WBS - BHS - MT Study		76.0d	14-Sep-23 A	3-Jan-24 A	
103	DS-PDD-170	PDD Validation BHS MT Study - Site Visits - Analysis	25.0d	14-Sep-23 A	18-Oct-23 A	
104	DS-PDD-380	BHS MT Site Walk	1.0d	19-Oct-23 A	19-Oct-23 A	
105	DS-PDD-390	BHS MT Documentation Study Completion	2.0d	20-Oct-23 A	23-Oct-23 A	
106	DS-PDD-400	BHS VTC Internal QA/QC	3.0d	24-Oct-23 A	26-Oct-23 A	
107	DS-PDD-420	BHS VTC Finalize Document	1.0d	27-Oct-23 A	27-Oct-23 A	
108	DS-PDD-430	BHS MT Study QA/QC	5.0d	30-Oct-23 A	3-Nov-23 A	
109	DS-PDD-470	BHS MT Study Compilation & Final Document	4.0d	6-Nov-23 A	9-Nov-23 A	
110	DS-PDD-500	BHS Subm. To HCAA	1.0d	10-Nov-23 A	10-Nov-23 A	
111	DS-PDD-510	BHS Review (HCAA)	19.0d	13-Nov-23 A	11-Dec-23 A	
112	DS-PDD-680	BHS Final Presentation (HCAA)	1.0d	12-Dec-23 A	12-Dec-23 A	
113	DS-PDD-720	BHS Owner Review & Determination	13.0d	13-Dec-23 A	2-Jan-24 A	
114	DS-PDD-840	HCAA Determination ON 1/3/24	1.0d	3-Jan-24 A	3-Jan-24 A	
115	WBS - Design Presentation #10 - Aircraft Parking		27.0d	11-Oct-23 A	16-Nov-23 A	
116	DS-PDD-310	Aircraft Parking Development - Design Presentation #10	15.0d	11-Oct-23 A	31-Oct-23 A	
117	DS-PDD-440	Aircraft Parking Exhibit If Northside Development - Design Presentation #10	5.0d	1-Nov-23 A	7-Nov-23 A	
118	DS-PDD-480	Aircraft Parking Presentation - Design Presentation #10	4.0d	8-Nov-23 A	13-Nov-23 A	
119	DS-PDD-520	Aircraft Parking Presentation - Airline Anchor Discussion - Design Presentation ...	1.0d	14-Nov-23 A	14-Nov-23 A	
120	DS-PDD-530	Aircraft Layout 3B Decision Made 11/16/23 - Design Presentation #10	2.0d	15-Nov-23 A	16-Nov-23 A	
121	WBS - Presentations		116.0d	19-Sep-23 A	4-Mar-24 A	
122	WBS - Executive Meeting		3.0d	17-Nov-23 A	21-Nov-23 A	
123	DS-PDD-550	Status Report	2.0d	17-Nov-23 A	20-Nov-23 A	
124	DS-PDD-560	Executive Mtg.	1.0d	21-Nov-23 A	21-Nov-23 A	
125	WBS - Design Presentation Kickoff Meeting - Airline Relocation		21.0d	19-Sep-23 A	17-Oct-23 A	
126	DS-PDD-190	Airline Relocation Coord.	20.0d	19-Sep-23 A	16-Oct-23 A	

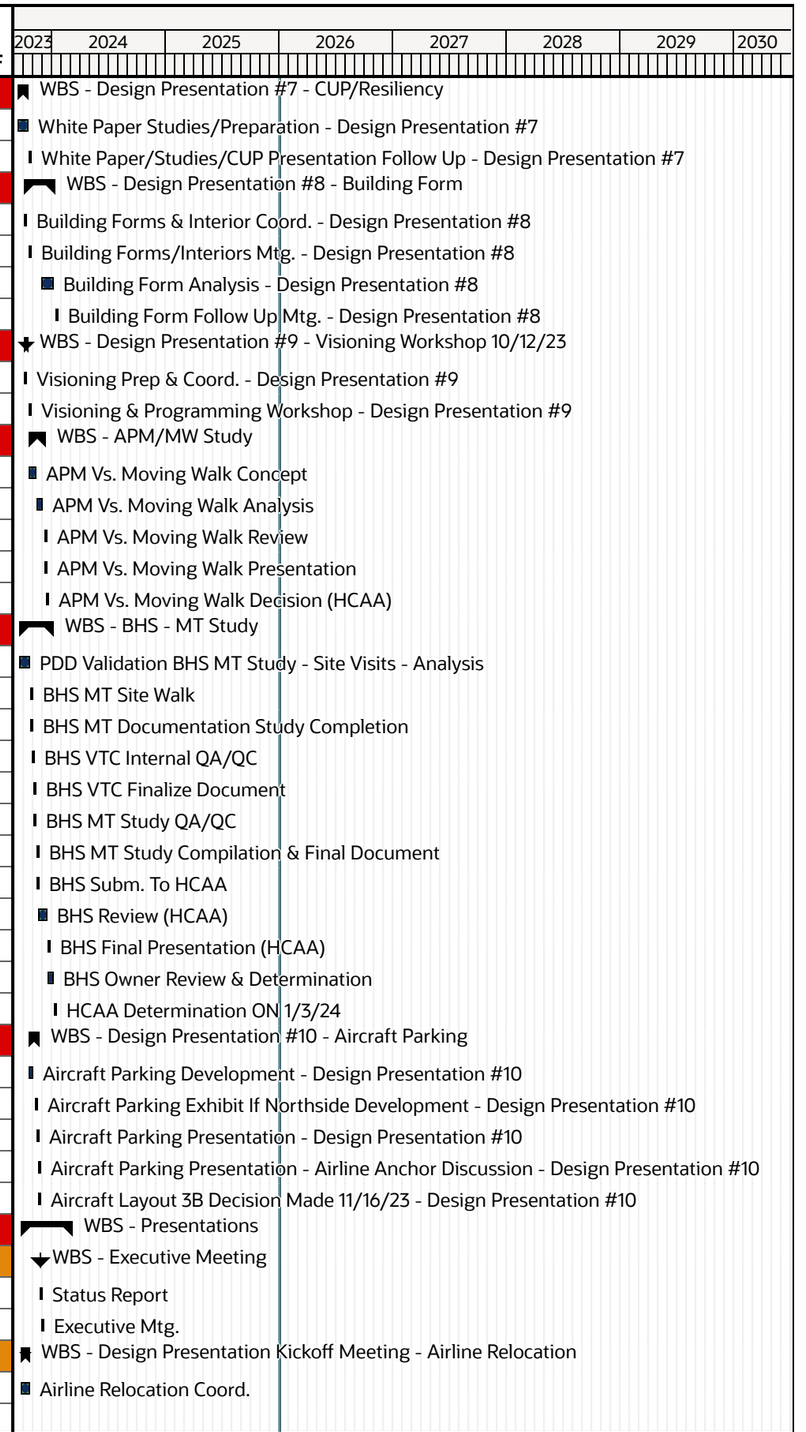


ID	Name	Dur	Start	Finish	TF
127	DS-PDD-360 Airline Relocation Mtg. 10/17/23	1.0d	17-Oct-23 A	17-Oct-23 A	
128	WBS - AHJ Meeting With City Of Tampa	10.0d	12-Oct-23 A	25-Oct-23 A	
129	DS-PDD-330 AHJ Mtg. With City Of Tampa	9.0d	12-Oct-23 A	24-Oct-23 A	
130	DS-PDD-410 AHJ Mtg. - 10/25/23	1.0d	25-Oct-23 A	25-Oct-23 A	
131	WBS - CUP Study/Resiliency	48.0d	13-Oct-23 A	21-Dec-23 A	
132	DS-PDD-350 CUP Study	29.0d	13-Oct-23 A	24-Nov-23 A	
133	DS-PDD-590 CUP Study Review	5.0d	27-Nov-23 A	1-Dec-23 A	
134	DS-PDD-630 CUP Discussion & Questions	6.0d	4-Dec-23 A	11-Dec-23 A	
135	DS-PDD-690 CUP Presentation	1.0d	12-Dec-23 A	12-Dec-23 A	
136	DS-PDD-730 CUP Review & Determination	6.0d	13-Dec-23 A	20-Dec-23 A	
137	DS-PDD-810 CUP Determined (HCAA)	1.0d	21-Dec-23 A	21-Dec-23 A	
138	WBS - Line Of Site	70.0d	22-Nov-23 A	4-Mar-24 A	
139	DS-PDD-580 Siteline/Building Form Analysis	9.0d	22-Nov-23 A	6-Dec-23 A	
140	DS-PDD-660 Siteline/Building Form Overview	3.0d	7-Dec-23 A	11-Dec-23 A	
141	DS-PDD-700 Line Of Site Presentation	1.0d	12-Dec-23 A	12-Dec-23 A	
142	DS-PDD-740 Siteline Pkg. Determination For FAA	10.0d	13-Dec-23 A	27-Dec-23 A	
143	DS-PDD-820 Subm. To FAA	1.0d	27-Dec-23 A	27-Dec-23 A	
144	DS-PDD-830 FAA Review & Determination (45 Day Per FAA)	46.0d	28-Dec-23 A	1-Mar-24 A	
145	DS-PDD-960 Confirmation Of Line Of Site Presentation	1.0d	4-Mar-24 A	4-Mar-24 A	
146	WBS - Apron Grading And Finished Floor Elevations	6.0d	13-Dec-23 A	20-Dec-23 A	
147	DS-PDD-750 Grading & Finish Floor Elevation Analysis	4.0d	13-Dec-23 A	18-Dec-23 A	
148	DS-PDD-780 Grading & Finish Floor Presentation	1.0d	19-Dec-23 A	19-Dec-23 A	
149	DS-PDD-800 Finish Floor Determination	1.0d	20-Dec-23 A	20-Dec-23 A	
150	WBS - PDD Validation Report	181.0d	20-Sep-23 A	4-Jun-24 A	
151	DS-PDD-200 PDD Outline - Template	20.0d	20-Sep-23 A	17-Oct-23 A	
152	DS-PDD-370 PDD Validation Development	11.0d	18-Oct-23 A	1-Nov-23 A	
153	DS-PDD-450 PDD Draft	1.0d	2-Nov-23 A	2-Nov-23 A	
154	DS-PDD-460 PDD Document	8.0d	3-Nov-23 A	14-Nov-23 A	
155	DS-PDD-540 PDD Discipline Check/Sr. Technical Review	9.0d	15-Nov-23 A	29-Nov-23 A	
156	DS-PDD-600 PDD - Post Docs. To Bluebeam	1.0d	30-Nov-23 A	30-Nov-23 A	
157	DS-PDD-620 PDD - QA/QC	5.0d	1-Dec-23 A	7-Dec-23 A	
158	DS-PDD-670 PDD Docs. Complete	2.0d	8-Dec-23 A	11-Dec-23 A	
159	DS-PDD-710 Table Top Review	1.0d	12-Dec-23 A	12-Dec-23 A	
160	DS-PDD-760 Submit PDD Validation Report To HCAA	1.0d	13-Dec-23 A	13-Dec-23 A	
161	DS-PDD-770 PDD Validation HCAA Review	3.0d	14-Dec-23 A	18-Dec-23 A	
162	DS-PDD-790 PDD Validation With HCAA	1.0d	19-Dec-23 A	19-Dec-23 A	
163	WBS - Airline Anchor Tenant Designation	109.0d	4-Jan-24 A	4-Jun-24 A	
164	DS-PDD-850 Anchor Airline Tenant Determination	108.0d	4-Jan-24 A	4-Jun-24 A	
165	DS-PDD-860 Fleet Mix Design Confirmation	21.0d	5-Jan-24 A	2-Feb-24 A	
166	DS-PDD-870 Hold Room Design	21.0d	5-Jan-24 A	2-Feb-24 A	
167	DS-PDD-880 Gate Design	21.0d	5-Jan-24 A	2-Feb-24 A	
168	DS-PDD-890 Technology	21.0d	5-Jan-24 A	2-Feb-24 A	

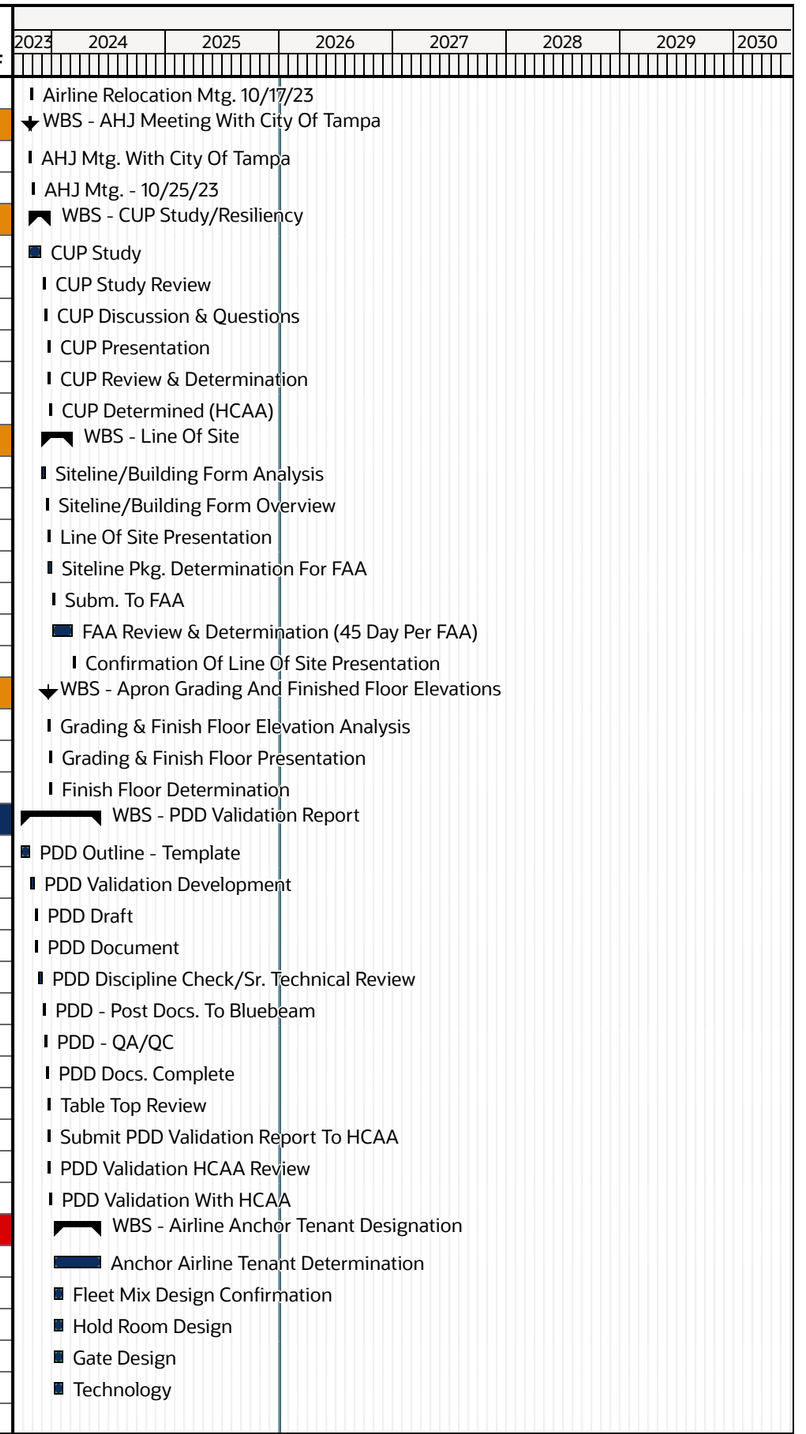


	ID	Name	Dur	Start	Finish	TF
169	DS-PDD-900	Operations/Administration Design	21.0d	5-Jan-24 A	2-Feb-24 A	
170	DS-PDD-910	FIS Design	21.0d	5-Jan-24 A	2-Feb-24 A	
171	DS-PDD-920	Airline Club Design	21.0d	5-Jan-24 A	2-Feb-24 A	
172	DS-PDD-940	Review Requirements For Airline Prior To BOD	10.0d	5-Feb-24 A	16-Feb-24 A	
173	DS-PDD-950	Docs. Airline Requirements For BOD	2.0d	19-Feb-24 A	20-Feb-24 A	
174	WBS - ASD - BOD		86.0d	3-Jan-24 A	1-May-24 A	
175	WBS - ASD - BOD Program Development		30.0d	3-Jan-24 A	13-Feb-24 A	
176	DS-BOD-10	Program SF Development & Prep	4.0d	3-Jan-24 A	8-Jan-24 A	
177	DS-BOD-20	Program SF Mtg. with HCAA Executives & Ricondo	1.0d	9-Jan-24 A	9-Jan-24 A	
178	DS-BOD-30	Program SF Workshop Development	3.0d	10-Jan-24 A	12-Jan-24 A	
179	DS-BOD-40	Program SF Workshop With HCAA - 1/16/24	1.0d	16-Jan-24 A	16-Jan-24 A	
180	DS-BOD-50	Program SF Analysis/Review/Presentation Prep	19.0d	17-Jan-24 A	12-Feb-24 A	
181	DS-BOD-60	Program SF Confirmation/Presentation - 2/13/24	1.0d	13-Feb-24 A	13-Feb-24 A	
182	WBS - ASD - BOD Documents		44.0d	14-Feb-24 A	15-Apr-24 A	
183	DS-BOD-70	Refine SF & Development Terminal BOD Plans	19.0d	14-Feb-24 A	11-Mar-24 A	
184	DS-BOD-80	Truck Loading Dock Layout & CUP Coord. - 2/20/24	5.0d	14-Feb-24 A	20-Feb-24 A	
185	DS-BOD-90	Conceptual Interior Design Development	19.0d	15-Feb-24 A	12-Mar-24 A	
186	DS-BOD-100	Finalize Floor Plan Adjacencies	6.0d	19-Feb-24 A	26-Feb-24 A	
187	DS-BOD-110	Finalize Gate Tower Locations	6.0d	19-Feb-24 A	26-Feb-24 A	
188	DS-BOD-120	Building Form Development	6.0d	19-Feb-24 A	26-Feb-24 A	
189	DS-BOD-130	Loading Dock Coord. Development	24.0d	21-Feb-24 A	25-Mar-24 A	
190	DS-BOD-140	Building Form Coord. Mtg. - 2/27/24	1.0d	27-Feb-24 A	27-Feb-24 A	
191	DS-BOD-150	Preliminary Hold Room Design Development	14.0d	27-Feb-24 A	15-Mar-24 A	
192	DS-BOD-160	BOD Target Program Accepted (BHS-Transfer Bus Hold Room)	1.0d	28-Feb-24 A	28-Feb-24 A	
193	DS-BOD-170	Struct. Grid & Floor To Floor Heights	9.0d	29-Feb-24 A	12-Mar-24 A	
194	DS-BOD-180	Final PDD & BOD Program Docs.	24.0d	29-Feb-24 A	2-Apr-24 A	
195	DS-BOD-190	FAA Approval Of Line Of Site	10.0d	13-Mar-24 A	26-Mar-24 A	
196	DS-BOD-200	Conceptual Interior Design Mtg. - 3/12/24	18.0d	13-Mar-24 A	5-Apr-24 A	
197	DS-BOD-210	Preliminary Hold Room Design Mtg. - 3/19/24	1.0d	19-Mar-24 A	19-Mar-24 A	
198	DS-BOD-220	Submit Draft Design To HP For Cost Estimating	1.0d	19-Mar-24 A	19-Mar-24 A	
199	DS-BOD-230	Preliminary Cost Estimate Pkg. To HP	20.0d	19-Mar-24 A	15-Apr-24 A	
200	DS-BOD-240	Loading Dock Bessie Coleman Coord. Mtg. - 3/26/24	1.0d	26-Mar-24 A	26-Mar-24 A	
201	WBS - ASD - BOD Review QA/QC		11.0d	3-Apr-24 A	17-Apr-24 A	
202	DS-BOD-250	BOD Review - QA/QC DQC - Post Docs.	1.0d	3-Apr-24 A	3-Apr-24 A	
203	DS-BOD-260	BOD Review - QA/QC - DQC	3.0d	3-Apr-24 A	5-Apr-24 A	
204	DS-BOD-270	Sr. Technical Review Discipline QC	3.0d	3-Apr-24 A	5-Apr-24 A	
205	DS-BOD-280	Post Docs. to Bluebeam IDR Review	1.0d	8-Apr-24 A	8-Apr-24 A	
206	DS-BOD-290	BOD/Validation QA/QC - IDR	5.0d	8-Apr-24 A	12-Apr-24 A	
207	DS-BOD-300	Docs. Complete - Visual Check	2.0d	15-Apr-24 A	16-Apr-24 A	
208	DS-BOD-310	QAR Check	1.0d	17-Apr-24 A	17-Apr-24 A	
209	WBS - ASD - BOD Submittal To HCAA		10.0d	18-Apr-24 A	1-May-24 A	
210	DS-BOD-320	Submit BOD Report Due To HCAA	1.0d	18-Apr-24 A	18-Apr-24 A	

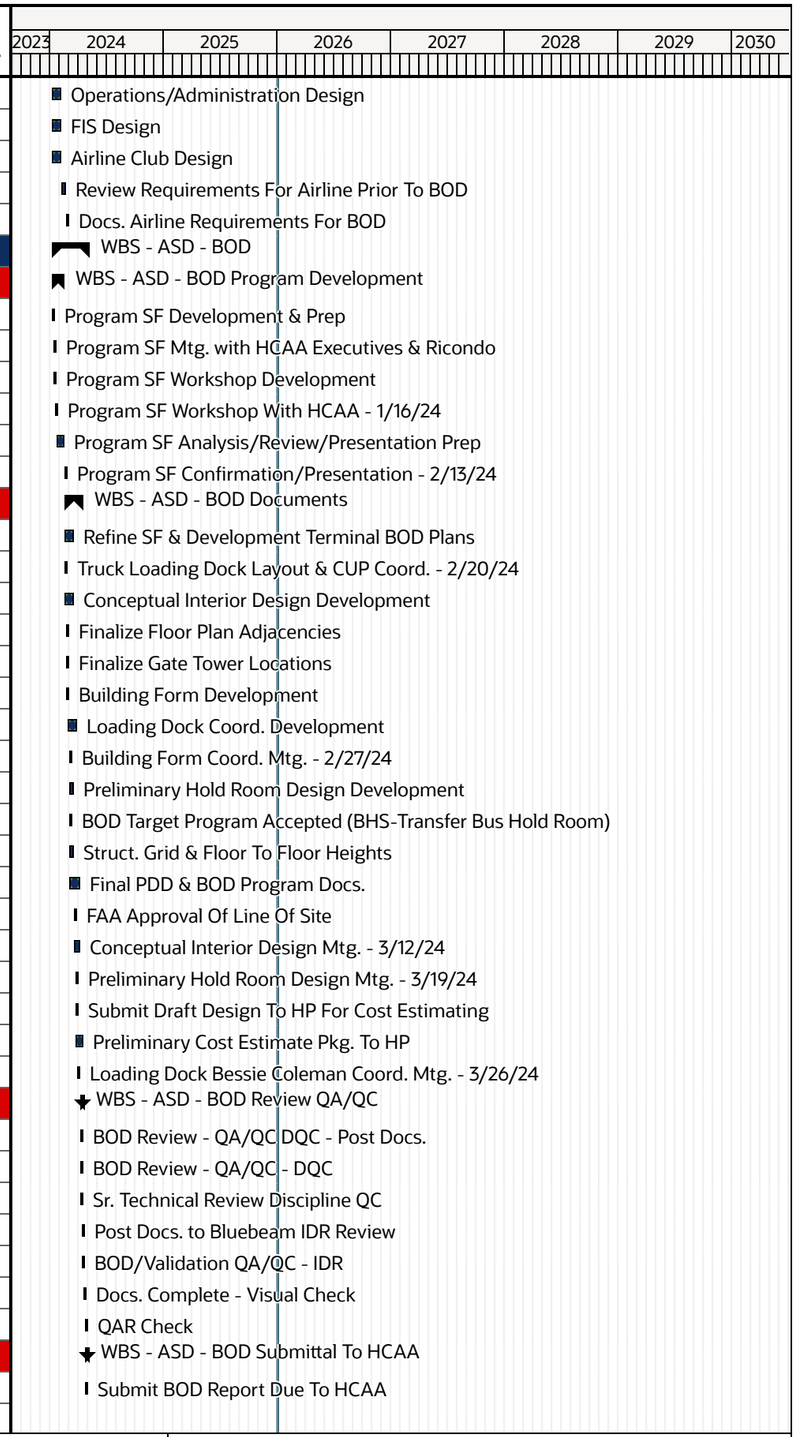


	ID	Name	Dur	Start	Finish	TF
211	DS-BOD-330	ASD - BOD Subm. - HCAA Review	9.0d	19-Apr-24 A	1-May-24 A	
212	WBS - Budget Reconciliation		90.0d	23-Apr-24 A	27-Aug-24 A	
213	DS-BR-10	HCAA Hold On Airside D 30% Progress	1.0d	23-Apr-24 A	23-Apr-24 A	
214	DS-BR-20	Cost Reduction Effort	23.0d	24-Apr-24 A	24-May-24 A	
215	DS-BR-30	Update Plans - Building Stacking	4.0d	28-May-24 A	31-May-24 A	
216	DS-BR-40	HP Cost Estimating	9.0d	3-Jun-24 A	14-Jun-24 A	
217	DS-BR-50	HCAA Administration Mtg. - NTP 6/10/24	1.0d	10-Jun-24 A	10-Jun-24 A	
218	DS-BR-60	Executive Team Decision Day	23.0d	11-Jun-24 A	15-Jul-24 A	
219	WBS - Revised BOD		14.0d	11-Jun-24 A	28-Jun-24 A	
220	DS-BR-RBOD-10	Develop Concept Plans (3 Massing/Form Options)	10.0d	11-Jun-24 A	24-Jun-24 A	
221	DS-BR-RBOD-20	FIS Study & Concept Options	10.0d	11-Jun-24 A	24-Jun-24 A	
222	DS-BR-RBOD-30	Concept Plan Presentation	1.0d	25-Jun-24 A	25-Jun-24 A	
223	DS-BR-RBOD-40	Respond To FIS Comments	3.0d	25-Jun-24 A	27-Jun-24 A	
224	DS-BR-RBOD-50	Respond To Presentation Comments	2.0d	26-Jun-24 A	27-Jun-24 A	
225	DS-BR-RBOD-60	Executive Mtg. - Decision On The Massing Options	1.0d	28-Jun-24 A	28-Jun-24 A	
226	DS-BR-RBOD-70	Executive Mtg. - FIS Direction	1.0d	28-Jun-24 A	28-Jun-24 A	
227	WBS - Program SF Development		16.0d	1-Jul-24 A	23-Jul-24 A	
228	DS-BR-70	Revise Program SF Analysis	5.0d	1-Jul-24 A	8-Jul-24 A	
229	DS-BR-110	Program SF Mtg.	1.0d	9-Jul-24 A	9-Jul-24 A	
230	DS-BR-120	Update Program SF Development Plan	9.0d	10-Jul-24 A	22-Jul-24 A	
231	DS-BR-160	Program Area Confirmation Mtg.	1.0d	23-Jul-24 A	23-Jul-24 A	
232	WBS - MEP/Truck Court Coordination		16.0d	1-Jul-24 A	23-Jul-24 A	
233	DS-BR-80	MEP Revision	15.0d	1-Jul-24 A	22-Jul-24 A	
234	DS-BR-90	Develop Truck Court Layout	15.0d	1-Jul-24 A	22-Jul-24 A	
235	DS-BR-150	Truck Court/MEP Mtg. - GDWY Alignment	1.0d	23-Jul-24 A	23-Jul-24 A	
236	WBS - Apron Level Development		13.0d	1-Jul-24 A	18-Jul-24 A	
237	DS-BR-100	Apron Lvl. Development With New Scheme	12.0d	1-Jul-24 A	17-Jul-24 A	
238	DS-BR-140	Apron Lvl. Civil Focus Team/Mtg.	1.0d	18-Jul-24 A	18-Jul-24 A	
239	WBS - Finalize BOD		2.0d	24-Jul-24 A	25-Jul-24 A	
240	DS-BR-170	Finalize BOD Docs.	1.0d	24-Jul-24 A	24-Jul-24 A	
241	DS-BR-180	BOD Docs. Ready For QA/QC	1.0d	24-Jul-24 A	24-Jul-24 A	
242	DS-BR-200	BOD - CBP Mtg. Workshop	1.0d	25-Jul-24 A	25-Jul-24 A	
243	WBS - Revised BOD Review QA/QC		22.0d	12-Jul-24 A	12-Aug-24 A	
244	DS-BR-130	Docs. To HP For Pricing	22.0d	12-Jul-24 A	12-Aug-24 A	
245	DS-BR-190	BOD Review - DQC - Post Docs.	1.0d	25-Jul-24 A	25-Jul-24 A	
246	DS-BR-210	BOD Review - DQC	3.0d	26-Jul-24 A	30-Jul-24 A	
247	DS-BR-220	BOD Review - Sr. Technical Review Discipline QC	3.0d	26-Jul-24 A	30-Jul-24 A	
248	DS-BR-230	BOD Review - Post Docs. To Bluebeam IDR Review	1.0d	31-Jul-24 A	31-Jul-24 A	
249	DS-BR-240	BOD QA/QC - IDR	5.0d	1-Aug-24 A	7-Aug-24 A	
250	DS-BR-250	BOD Review - Docs. Complete - Visual Check	2.0d	8-Aug-24 A	9-Aug-24 A	
251	DS-BR-260	BOD Review - QAR Check	1.0d	12-Aug-24 A	12-Aug-24 A	
252	WBS - ASD - Revised BOD Submittal To HCAA		11.0d	13-Aug-24 A	27-Aug-24 A	

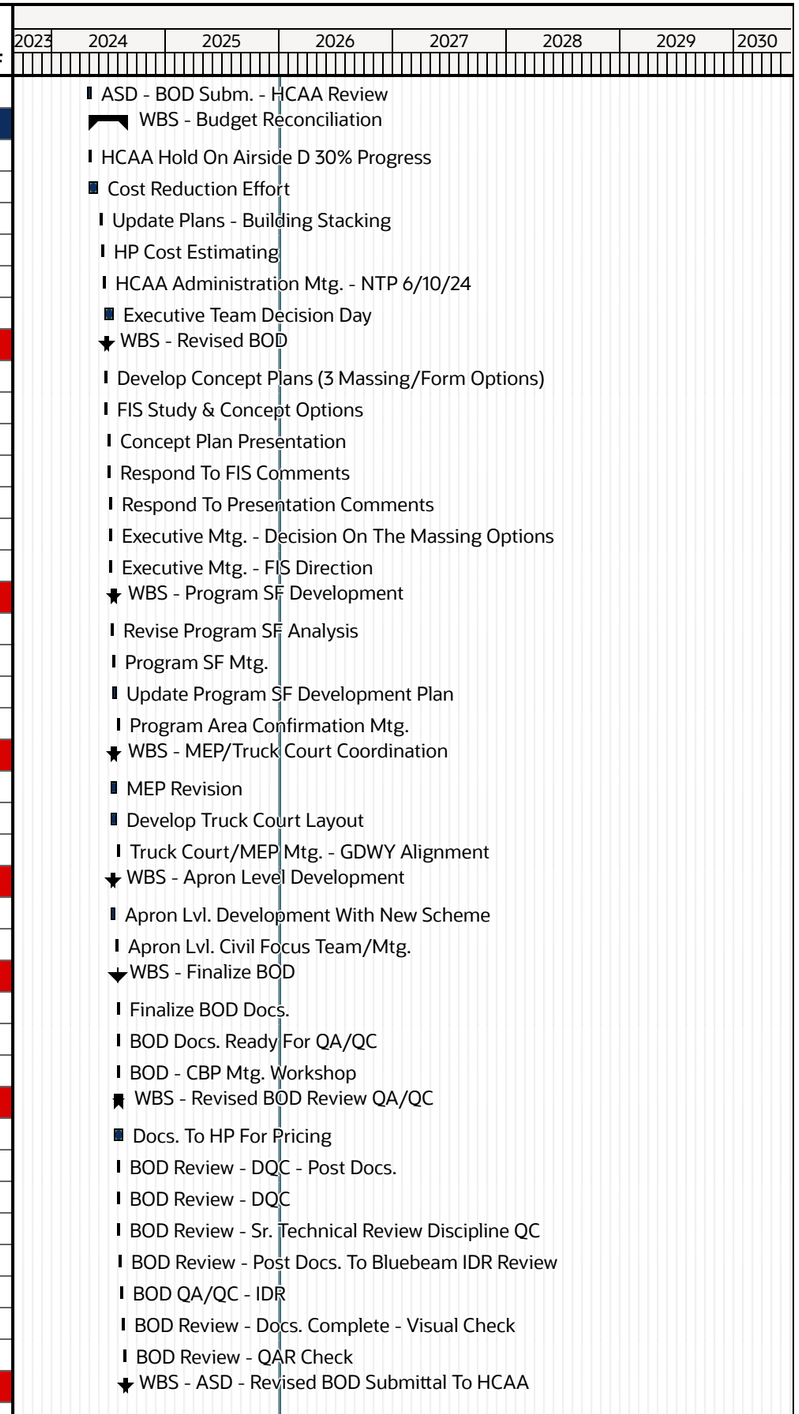


	ID	Name	Dur	Start	Finish	TF
253	DS-BR-270	Submit Revised BOD Report Due To HCAA	1.0d	13-Aug-24 A	13-Aug-24 A	
254	DS-BR-280	ASD - BOD - HCAA Review	10.0d	14-Aug-24 A	27-Aug-24 A	
255	WBS - Main Terminal Ticket Counter Relocation		279.0d	19-Apr-24 A	22-May-25 A	
256	WBS - MT - Ticketing Counter Relocation - Evaluation		55.0d	19-Apr-24 A	5-Jul-24 A	
257	DS-MT-10	HCAA Ticket Counter Relo. Coord. With Ricondo - Ticket Counter Relo.	14.0d	19-Apr-24 A	8-May-24 A	
258	DS-MT-20	Kick Off Mtg. With HCAA - Ricondo Presentation - Ticket Counter Relo.	1.0d	9-May-24 A	9-May-24 A	
259	DS-MT-30	Develop Initial List Of Questions & Review Program - Ticket Counter Relo.	13.0d	10-May-24 A	29-May-24 A	
260	DS-MT-40	Site Walk - Ticket Counter Relo.	1.0d	30-May-24 A	30-May-24 A	
261	DS-MT-50	Evaluate Ricondo Program - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
262	DS-MT-60	Develop Ticket Counter Matrix - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
263	DS-MT-70	Develop Plans Identifying Relocation Of Ticket Counters - Ticket Counter Relo.	9.0d	31-May-24 A	12-Jun-24 A	
264	DS-MT-80	Submit Draft Plans & Matrix for Review (Including HP) - Ticket Counter Relo.	1.0d	13-Jun-24 A	13-Jun-24 A	
265	DS-MT-90	Develop Presentation Of Evaluation Of Program/Scope To HCAA - Ticket Count…	4.0d	14-Jun-24 A	19-Jun-24 A	
266	DS-MT-100	Presentation To HCAA - Ticket Counter Relo.	1.0d	20-Jun-24 A	20-Jun-24 A	
267	DS-MT-110	HCAA Review & Comment - Ticket Counter Relo.	10.0d	21-Jun-24 A	5-Jul-24 A	
268	WBS - MT - Ticketing Counter Relocation - Concept Design/Stakeholder Engagement		52.0d	21-Jun-24 A	4-Sep-24 A	
269	DS-MT-120	Incorporate Comments from HCAA - Ticket Counter Relo. - Concept Design	10.0d	21-Jun-24 A	5-Jul-24 A	
270	DS-MT-130	Confirmation of Proprietary Use Component for Each Airline - Ticket Counter R…	5.0d	8-Jul-24 A	12-Jul-24 A	
271	DS-MT-140	Airline Stakeholder Mtg.s/Questionnaires - Ticket Counter Relo. - Concept Design	20.0d	15-Jul-24 A	9-Aug-24 A	
272	DS-MT-150	Provide Update to HCAA - Airline Matrix - Ticket Counter Relo. - Concept Design	17.0d	12-Aug-24 A	4-Sep-24 A	
273	DS-MT-160	Confirmation of BHS System Determination (East End Sortation) - Ticket Count…	1.0d	19-Aug-24 A	19-Aug-24 A	
274	WBS - MT - Ticketing Counter Relocation - Focus Team Meeting		24.0d	5-Sep-24 A	8-Oct-24 A	
275	DS-MT-170	Mtg. With HCAA Regarding Ticket Counter/Airline Relocation - Ticket Counter R…	1.0d	5-Sep-24 A	5-Sep-24 A	
276	DS-MT-180	BHS Coord. - Ticket Counter Relo.	8.0d	6-Sep-24 A	17-Sep-24 A	
277	DS-MT-190	Develop Phasing Plan/Matrix for Each Ticket Counter Relo.	8.0d	6-Sep-24 A	17-Sep-24 A	
278	DS-MT-200	Submit Matrix & Questions To HCAA. - Ticket Counter Relo.	1.0d	18-Sep-24 A	18-Sep-24 A	
279	DS-MT-210	Update Plans. - Ticket Counter Relo.	4.0d	19-Sep-24 A	24-Sep-24 A	
280	DS-MT-220	Mtg. With HCAA (Tony O'Brian). - Ticket Counter Relo.	1.0d	25-Sep-24 A	25-Sep-24 A	
281	DS-MT-230	Update Docs. Based on Communication From HCAA. - Ticket Counter Relo.	7.0d	26-Sep-24 A	4-Oct-24 A	
282	DS-MT-240	Mtg. With HP/Gensler/HNTB. - Ticket Counter Relo.	1.0d	7-Oct-24 A	7-Oct-24 A	
283	DS-MT-250	Airside D Support Spaces Presentation. - Ticket Counter Relo.	1.0d	8-Oct-24 A	8-Oct-24 A	
284	WBS - MT - Ticketing Counter Relocation - SD - 30%		50.0d	26-Sep-24 A	6-Dec-24 A	
285	WBS - MT - Ticketing Counter Relocation - SD - 30% Docs		41.0d	26-Sep-24 A	21-Nov-24 A	
286	DS-MT-SD-10	SD - 30% - MT Ticket Counter Relo. SD	7.0d	26-Sep-24 A	4-Oct-24 A	
287	DS-MT-SD-20	SD 30% Hurricane Milton Impact (10/7-10/11) - MT Ticket Counter Relo. SD	5.0d	7-Oct-24 A	11-Oct-24 A	
288	DS-MT-SD-30	30% Architecture Docs. Complete - MT Ticket Counter Relo. SD	10.0d	14-Oct-24 A	25-Oct-24 A	
289	DS-MT-SD-40	30% Cost Estimating Pkg. - MT Ticket Counter Relo. SD	22.0d	23-Oct-24 A	21-Nov-24 A	
290	WBS - MT - Ticketing Counter Relocation - SD - 30% QA/QC		17.0d	28-Oct-24 A	19-Nov-24 A	
291	DS-MT-SD-50	30% DQC - MT Ticket Counter Relo. SD	5.0d	28-Oct-24 A	1-Nov-24 A	
292	DS-MT-SD-60	30% Sr. Technical Review - MT Ticket Counter Relo. SD	5.0d	28-Oct-24 A	1-Nov-24 A	
293	DS-MT-SD-70	30% Post to Bluebeam Session - MT Ticket Counter Relo. SD	1.0d	4-Nov-24 A	4-Nov-24 A	
294	DS-MT-SD-80	30% IDR - MT Ticket Counter Relo. SD	7.0d	5-Nov-24 A	13-Nov-24 A	

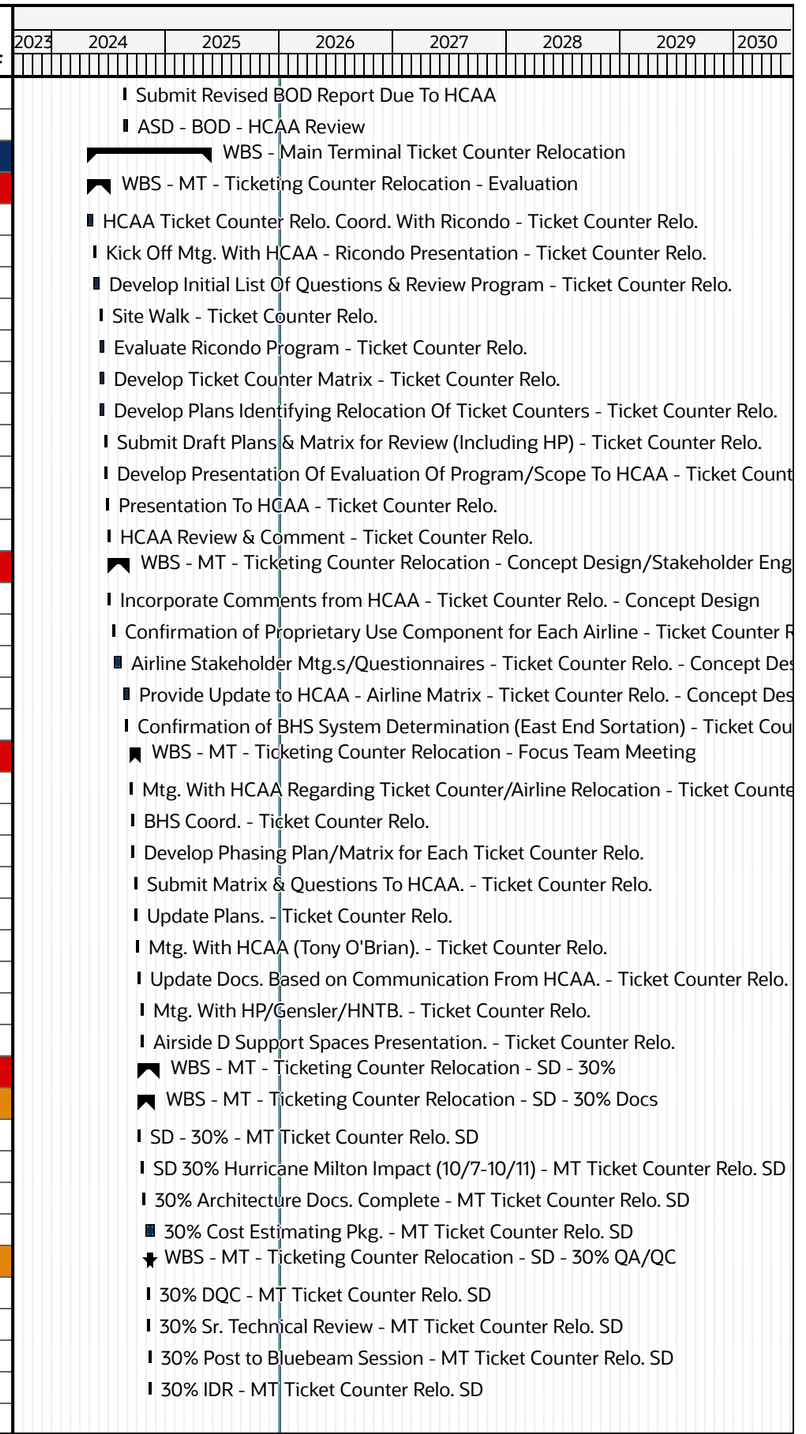


	ID	Name	Dur	Start	Finish	TF
295	DS-MT-SD-90	30% Visual Check - MT Ticket Counter Relo. SD	2.0d	14-Nov-24 A	15-Nov-24 A	
296	DS-MT-SD-100	30% QA Check - MT Ticket Counter Relo. SD	2.0d	18-Nov-24 A	19-Nov-24 A	
297	WBS - MT - Ticketing Counter Relocation - SD - 30% Submittal To HCAA		11.0d	20-Nov-24 A	6-Dec-24 A	
298	DS-MT-SD-110	30% Complete Docs. & Assemble Pkg. - MT Ticket Counter Relo. SD	1.0d	20-Nov-24 A	20-Nov-24 A	
299	DS-MT-SD-120	30% Subm. To HCAA - MT Ticket Counter Relo. SD	1.0d	21-Nov-24 A	21-Nov-24 A	
300	DS-MT-SD-130	30% HCAA Review - MT Ticket Counter Relo. SD	9.0d	22-Nov-24 A	6-Dec-24 A	
301	WBS - MT - Ticketing Counter Relocation - DD - 60%		126.0d	22-Nov-24 A	22-May-25 A	
302	WBS - MT - Ticketing Counter Relocation - DD - 60% Docs		95.0d	22-Nov-24 A	9-Apr-25 A	
303	DS-MT-DD-10	60% Docs - MT Ticket Counter Relo. DD	95.0d	22-Nov-24 A	9-Apr-25 A	
304	WBS - MT - Ticketing Counter Relocation - DD - 60% QA/QC		19.0d	10-Apr-25 A	6-May-25 A	
305	DS-MT-DD-20	60% - Cost Estimating Pkg. - MT Ticket Counter Relo. - DD	19.0d	10-Apr-25 A	6-May-25 A	
306	DS-MT-DD-30	60% - DQC - MT Ticket Counter Relo. - DD	3.0d	10-Apr-25 A	14-Apr-25 A	
307	DS-MT-DD-40	60% - Post to Bluebeam Session - MT Ticket Counter Relo. - DD	1.0d	15-Apr-25 A	15-Apr-25 A	
308	DS-MT-DD-50	60% - IDR - MT Ticket Counter Relo. - DD	12.0d	16-Apr-25 A	1-May-25 A	
309	DS-MT-DD-60	60% - Visual Check - MT Ticket Counter Relo. - DD	2.0d	2-May-25 A	5-May-25 A	
310	DS-MT-DD-70	60% - QA Check - MT Ticket Counter Relo. - DD	1.0d	6-May-25 A	6-May-25 A	
311	WBS - MT - Ticketing Counter Relocation - DD - 60% Submittal To HCAA		12.0d	7-May-25 A	22-May-25 A	
312	DS-MT-DD-80	60% - Complete Docs. & Assemble Pkg. - MT Ticket Counter Relo. - DD	1.0d	7-May-25 A	7-May-25 A	
313	DS-MT-DD-90	60% - Subm. To HCAA - MT Ticket Counter Relo. - DD	1.0d	8-May-25 A	8-May-25 A	
314	DS-MT-DD-100	60% - HCAA Review - MT Ticket Counter Relo. - DD	10.0d	9-May-25 A	22-May-25 A	
315	WBS - Enabling Package		215.0d	5-Jan-24 A	4-Nov-24 A	
316	WBS - Enabling Package/Apron Demo 60% (Footprint +50')		89.0d	5-Jan-24 A	8-May-24 A	
317	DS-EN-10	Gate Layout - Building Outline (4 Gate - Late Opening) - Enabling Pkg/Apron D...	30.0d	5-Jan-24 A	15-Feb-24 A	
318	DS-EN-20	North Site Development & Coord. - Enabling Pkg/Apron Demo 60%	30.0d	5-Jan-24 A	15-Feb-24 A	
319	DS-EN-30	Submit Fee Proposal for Review & Approval - Enabling Pkg/Apron Demo 60%	22.0d	16-Feb-24 A	18-Mar-24 A	
320	DS-EN-40	SWFWMD Mtg. Prep - 3/27/24 - Enabling Pkg/Apron Demo 60%	29.0d	16-Feb-24 A	27-Mar-24 A	
321	DS-EN-50	Civil Docs. - Enabling Pkg/Apron Demo 60%	20.0d	27-Feb-24 A	25-Mar-24 A	
322	DS-EN-60	Define Civil Apron Limits - Enabling Pkg/Apron Demo 60%	30.0d	27-Feb-24 A	8-Apr-24 A	
323	DS-EN-70	Building Outline/Footprint - Enabling Pkg/Apron Demo 60%	15.0d	27-Feb-24 A	18-Mar-24 A	
324	DS-EN-80	Apron Demo 60% NTP - Enabling Pkg/Apron Demo 60%	1.0d	19-Mar-24 A	19-Mar-24 A	
325	DS-EN-90	Develop Struct. Grid - Enabling Pkg/Apron Demo 60%	16.0d	19-Mar-24 A	9-Apr-24 A	
326	DS-EN-100	Survey - Geotech - Site Investigation - Enabling Pkg/Apron Demo 60%	20.0d	20-Mar-24 A	16-Apr-24 A	
327	DS-EN-110	Utility Coord. - Enabling Pkg/Apron Demo 60%	22.0d	20-Mar-24 A	18-Apr-24 A	
328	DS-EN-120	North Site Drainage Design - Enabling Pkg/Apron Demo 60%	25.0d	20-Mar-24 A	23-Apr-24 A	
329	DS-EN-130	North Site Utility & Paving Plans - Enabling Pkg/Apron Demo 60%	25.0d	20-Mar-24 A	23-Apr-24 A	
330	DS-EN-140	North Site Trailer Layout & Design - Enabling Pkg/Apron Demo 60%	20.0d	20-Mar-24 A	16-Apr-24 A	
331	DS-EN-150	SWFWMD Mtg. - 3/28/24 - Enabling Pkg/Apron Demo 60%	1.0d	28-Mar-24 A	28-Mar-24 A	
332	DS-EN-160	Finalize Civil Demo Docs. - Enabling Pkg/Apron Demo 60%	5.0d	9-Apr-24 A	15-Apr-24 A	
333	DS-EN-170	Civil Docs. - Apron D Site - Enabling Pkg/Apron Demo 60%	16.0d	9-Apr-24 A	30-Apr-24 A	
334	DS-EN-180	Identify Pilot Hole Locations - Enabling Pkg/Apron Demo 60%	10.0d	10-Apr-24 A	23-Apr-24 A	
335	DS-EN-190	Submit Survey Information to The Design Team - Enabling Pkg/Apron Demo 60%	5.0d	17-Apr-24 A	23-Apr-24 A	
336	DS-EN-200	Finalize Architectural Docs. - Enabling Pkg/Apron Demo 60%	10.0d	17-Apr-24 A	30-Apr-24 A	

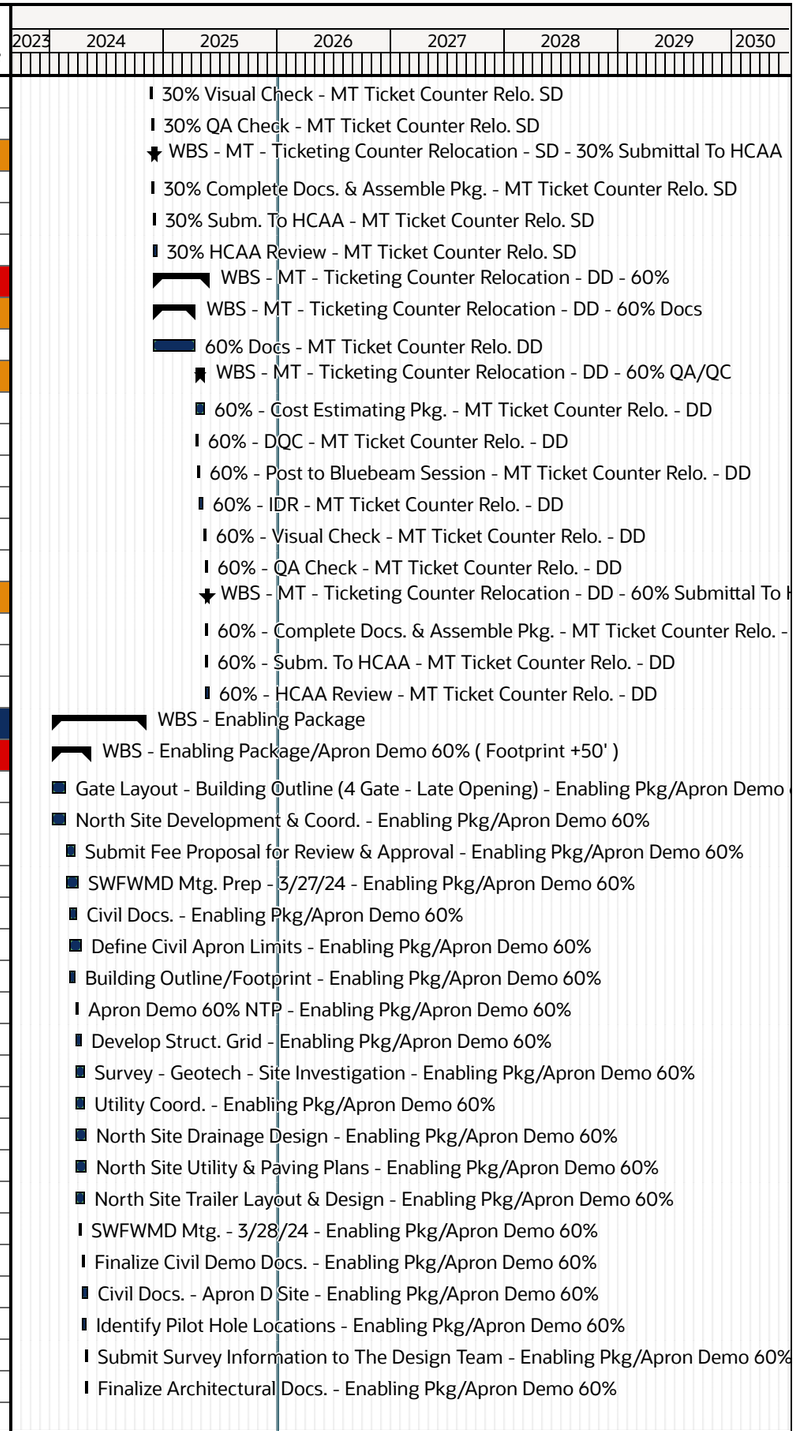


	ID	Name	Dur	Start	Finish	TF
337	DS-EN-210	Finalize Struct. Docs. - Enabling Pkg/Apron Demo 60%	5.0d	24-Apr-24 A	30-Apr-24 A	
338	DS-EN-220	Finalize Civil Docs. - North Site - Enabling Pkg/Apron Demo 60%	5.0d	24-Apr-24 A	30-Apr-24 A	
339	WBS - APN - Enabling Package 60% Submittal		6.0d	1-May-24 A	8-May-24 A	
340	DS-EN-230	Enabling Pkg. 60% Document - QA/QC	5.0d	1-May-24 A	7-May-24 A	
341	DS-EN-240	Enabling Pkg. 60% Draft HCAA Review	1.0d	8-May-24 A	8-May-24 A	
342	WBS - APN - Enabling Package 100% Submittal		49.0d	9-May-24 A	17-Jul-24 A	
343	DS-EN-250	Incorporate Comments from HCAA Review into Document - APN Enabling Pckg...	12.0d	9-May-24 A	24-May-24 A	
344	DS-EN-260	APN Enabling Pckg. 100% - HCAA Review & Comments - APN Enabling Pckg. 1...	17.0d	9-May-24 A	3-Jun-24 A	
345	DS-EN-270	HCAA Comments Received 6/4/24 - APN Enabling Pckg. 100%	1.0d	4-Jun-24 A	4-Jun-24 A	
346	DS-EN-280	Comment Resolution Subm. - APN Enabling Pckg. 100%	9.0d	5-Jun-24 A	17-Jun-24 A	
347	DS-EN-290	Incorporate HCAA Comments - APN Enabling Pckg. 100%	10.0d	5-Jun-24 A	18-Jun-24 A	
348	DS-EN-300	Incorporate New Building Footprint into Enabling Pkg. - APN Enabling Pckg. 10...	6.0d	11-Jun-24 A	18-Jun-24 A	
349	DS-EN-310	Civil Design Subm. - APN Enabling Pckg. 100%	20.0d	19-Jun-24 A	17-Jul-24 A	
350	DS-EN-320	Architectural Design Subm. - APN Enabling Pckg. 100%	20.0d	19-Jun-24 A	17-Jul-24 A	
351	WBS - APN - Enabling Package 100% Review QA/QC		21.0d	12-Jul-24 A	9-Aug-24 A	
352	DS-EN-330	Submit Draft Design To HP For Cost Estimating Review - APN Enabling Pckg. 1...	1.0d	12-Jul-24 A	12-Jul-24 A	
353	DS-EN-340	DQC Review - APN Enabling Pckg. 100%	5.0d	18-Jul-24 A	24-Jul-24 A	
354	DS-EN-350	Enabling Pkg. Sr. Technical Review - APN Enabling Pckg. 100%	5.0d	18-Jul-24 A	24-Jul-24 A	
355	DS-EN-360	Submit Document to Bluebeam - APN Enabling Pckg. 100%	1.0d	25-Jul-24 A	25-Jul-24 A	
356	DS-EN-370	IDR - APN Enabling Pckg. 100%	7.0d	26-Jul-24 A	5-Aug-24 A	
357	DS-EN-380	Docs. Complete Visual Check - APN Enabling Pckg. 100%	2.0d	6-Aug-24 A	7-Aug-24 A	
358	DS-EN-390	QA Review - APN Enabling Pckg. 100%	2.0d	8-Aug-24 A	9-Aug-24 A	
359	WBS - APN - Enabling Package Submittal To HCAA		12.0d	12-Aug-24 A	27-Aug-24 A	
360	DS-EN-400	Complete Docs. & Assemble Pkg. - APN Enabling Pckg. 100%	1.0d	12-Aug-24 A	12-Aug-24 A	
361	DS-EN-410	Submit Enabling/Demo Pkg. To HCAA - APN Enabling Pckg. 100%	1.0d	13-Aug-24 A	13-Aug-24 A	
362	DS-EN-420	Submit to City Of Tampa & HCAA Review - APN Enabling Pckg. 100%	10.0d	14-Aug-24 A	27-Aug-24 A	
363	WBS - APN - Enabling Permit And Comment Resolution		58.0d	14-Aug-24 A	4-Nov-24 A	
364	DS-EN-430	Bidding RFI's - APN - Enabling Permit & Comment Resol.	20.0d	14-Aug-24 A	11-Sep-24 A	
365	DS-EN-440	HCAA Comments Received - APN - Enabling Permit & Comment Resol.	5.0d	28-Aug-24 A	4-Sep-24 A	
366	DS-EN-450	Comment Resolution Subm. - APN - Enabling Permit & Comment Resol.	14.0d	5-Sep-24 A	24-Sep-24 A	
367	DS-EN-460	Contractor Bid Date - APN - Enabling Permit & Comment Resol.	1.0d	12-Sep-24 A	12-Sep-24 A	
368	DS-EN-470	HCAA Comment Resolution Mtg. #1 - APN - Enabling Permit & Comment Resol.	1.0d	25-Sep-24 A	25-Sep-24 A	
369	DS-EN-480	Follow Up Comment Resolution Clarification - APN - Enabling Permit & Comme...	16.0d	26-Sep-24 A	17-Oct-24 A	
370	DS-EN-490	Submit to COT Building Department - APN - Enabling Permit & Comment Resol.	1.0d	2-Oct-24 A	2-Oct-24 A	
371	DS-EN-500	COT Building Department Comments Received - APN - Enabling Permit & Com...	12.0d	3-Oct-24 A	18-Oct-24 A	
372	DS-EN-510	HCAA Comment Resolution Mtg. #2 - APN - Enabling Permit & Comment Resol.	1.0d	18-Oct-24 A	18-Oct-24 A	
373	DS-EN-520	Respond To COT Building Comments - APN - Enabling Permit & Comment Resol.	10.0d	21-Oct-24 A	1-Nov-24 A	
374	DS-EN-530	Submit to COT Including All Comment Resolution - APN - Enabling Permit & Co...	1.0d	4-Nov-24 A	4-Nov-24 A	
375	WBS - Design Assist Procurement		65.0d	11-Nov-24 A	13-Feb-25 A	
376	WBS - Request for Proposal		56.0d	11-Nov-24 A	31-Jan-25 A	
377	DS-DAP-100	Assemble Design Assist RFP Pkg. - Design Assist Procurement	5.0d	11-Nov-24 A	15-Nov-24 A	
378	DS-DAP-200	Review DA RFP Pkg. with HCAA - Design Assist Procurement	4.0d	18-Nov-24 A	22-Nov-24 A	

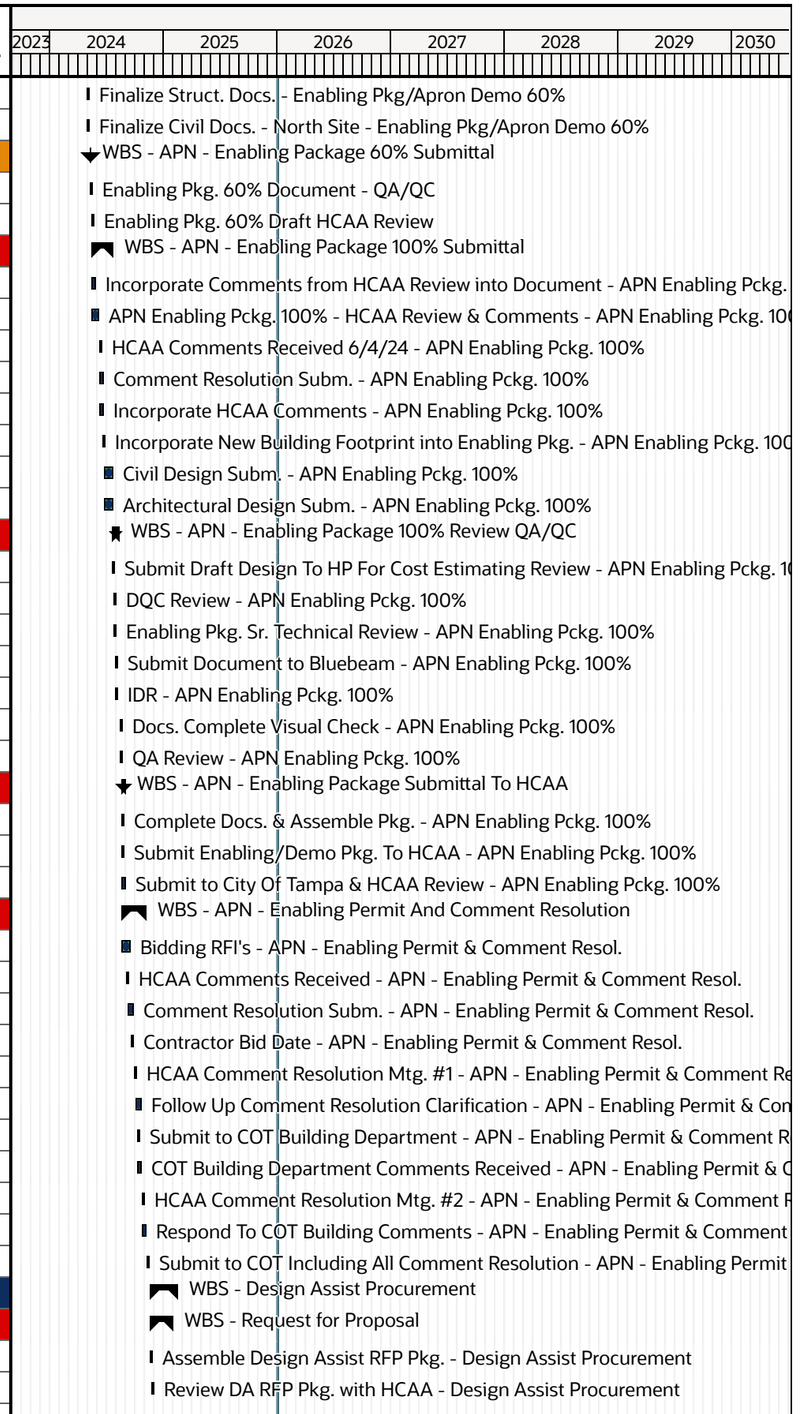


	ID	Name	Dur	Start	Finish	TF
379	DS-DAP-300	Address DA RFP Pkg. Comments from HCAA - Design Assist Procurement	4.0d	25-Nov-24 A	29-Nov-24 A	
380	DS-DAP-400	Issue DA RFP to Bidders - Design Assist Procurement	0.0d		2-Dec-24 A	
381	DS-DAP-410	RFI's Due from Bidders - Design Assist Procurement	0.0d		10-Dec-24 A	
382	DS-DAP-420	Addendum Issued - Design Assist Procurement	5.0d		17-Dec-24 A	
383	DS-DAP-440	Bids Due - Design Assist Procurement	0.0d		9-Jan-25 A	
384	DS-DAP-450	HP Review Bids & Shortlist for Interviews - Design Assist Procurement	12.0d	16-Jan-25 A	31-Jan-25 A	
385	WBS - Interviews		8.0d	3-Feb-25	13-Feb-25 A	
386	DS-DAP-460	Steel Contractors Complete - HP & HCAA Interview	0.0d		3-Feb-25 A	
387	DS-DAP-470	Mech. & Plumbing Contractors Complete - HP & HCAA Interview	0.0d		4-Feb-25 A	
388	DS-DAP-490	Low Voltage Contractors Complete - HP & HCAA Interview	0.0d		10-Feb-25 A	
389	DS-DAP-480	Elec. Contractors Complete - HP & HCAA Interview	0.0d		11-Feb-25 A	
390	DS-DAP-500	Ground Improvement Contractors Complete - HP & HCAA Interview	0.0d		11-Feb-25 A	
391	DS-DAP-510	BHS Handling Contractors Complete - HP & HCAA Interview	0.0d		13-Feb-25 A	
392	WBS - Contract Award		8.0d	3-Feb-25	13-Feb-25 A	
393	DS-DAP-530	Steel Contract GMF Complete - Award Design Assist	0.0d		3-Feb-25 A	
394	DS-DAP-520	Mech. & Plumbing Contract BCH Mech. Complete - Award Design Assist	0.0d		4-Feb-25 A	
395	DS-DAP-550	Low Voltage Contract MC Dean Complete - Award Design Assist	0.0d		11-Feb-25 A	
396	DS-DAP-540	Elec. Contract APG Complete - Award Design Assist	0.0d		11-Feb-25 A	
397	DS-DAP-560	Ground Improvement Contract Menard Complete - Award Design Assist	0.0d		12-Feb-25 A	
398	DS-DAP-570	BHS Handling Contract Daifuku Complete - Award Design Assist	0.0d		13-Feb-25 A	
399	WBS - ASD - 30% Schematic Design		137.0d	17-Jul-24 A	30-Jan-25 A	
400	DS-SD-ASD-10	ASD - 30% Schematic Design NTP - ITB's	1.0d	17-Jul-24 A	17-Jul-24 A	
401	WBS - ASD - 30% Design		136.0d	18-Jul-24 A	30-Jan-25 A	
402	WBS - ASD - 30% Design Documents		136.0d	18-Jul-24 A	30-Jan-25 A	
403	WBS - Airside D Terminal		52.0d	14-Aug-24 A	25-Oct-24 A	
404	DS-SD-ASD-80	Architectural Design - ASD 30% DD	47.0d	14-Aug-24 A	18-Oct-24 A	
405	DS-SD-ASD-120	Floor Plan Development (Restrooms/Retail) - ASD 30% DD	5.0d	14-Aug-24 A	20-Aug-24 A	
406	DS-SD-ASD-130	Architectural Look & Feel - ASD 30% DD	7.0d	14-Aug-24 A	22-Aug-24 A	
407	DS-SD-ASD-140	PBB Locations & Gate Layout 30% Review - ASD 30% DD	4.0d	23-Aug-24 A	28-Aug-24 A	
408	DS-SD-ASD-160	Holdroom Layout & Gate Portal Location - ASD 30% DD	8.0d	29-Aug-24 A	10-Sep-24 A	
409	DS-SD-ASD-240	Building Footprint Refinement - ASD 30% DD	5.0d	11-Sep-24 A	17-Sep-24 A	
410	DS-SD-ASD-290	Exterior Door Locations (OHD) - ASD 30% DD	10.0d	18-Sep-24 A	1-Oct-24 A	
411	DS-SD-ASD-330	Architectural Coord. & Implementation - ASD 30% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
412	DS-SD-ASD-340	Hurricane Milton Impact (10/7-10/11) - ASD SD 30%	5.0d	7-Oct-24 A	11-Oct-24 A	
413	DS-SD-ASD-360	Architecture Docs. Complete - ASD 30% DD	10.0d	14-Oct-24 A	25-Oct-24 A	
414	WBS - CBP		59.0d	25-Jul-24 A	16-Oct-24 A	
415	DS-SD-ASD-60	CBP Workshop #1	1.0d	25-Jul-24 A	25-Jul-24 A	
416	DS-SD-ASD-70	CBP Development	24.0d	26-Jul-24 A	28-Aug-24 A	
417	DS-SD-ASD-170	CBP Workshop #2	1.0d	29-Aug-24 A	29-Aug-24 A	
418	DS-SD-ASD-180	CBP Design Implementation	33.0d	30-Aug-24 A	16-Oct-24 A	
419	WBS - TSA		45.0d	14-Aug-24 A	16-Oct-24 A	
420	DS-SD-ASD-90	TSA Screening	45.0d	14-Aug-24 A	16-Oct-24 A	

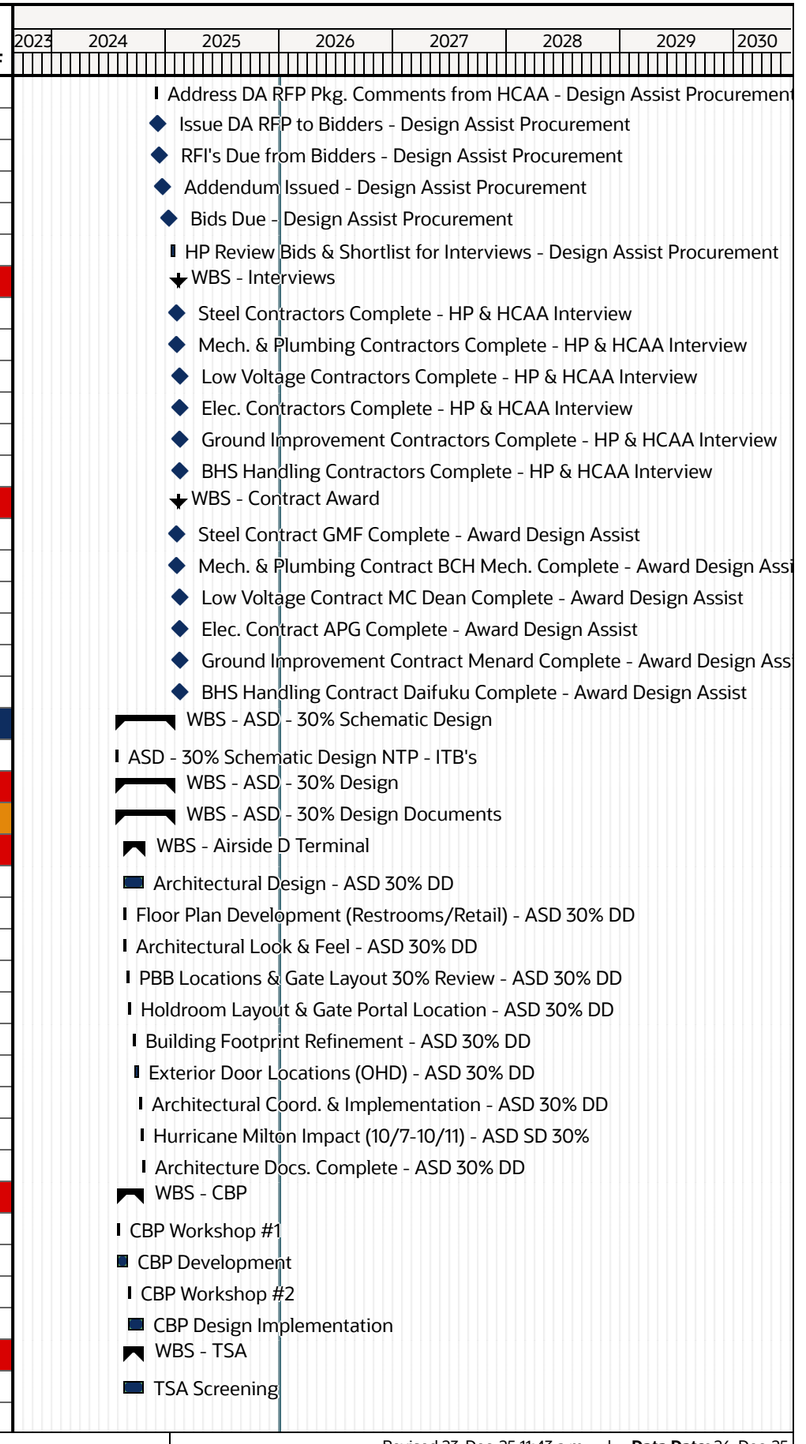


	ID	Name	Dur	Start	Finish	TF
421	WBS - Civil Coordination		45.0d	14-Aug-24 A	16-Oct-24 A	
422	DS-SD-ASD-100	Civil Coord. Design	45.0d	14-Aug-24 A	16-Oct-24 A	
423	WBS - Structural Design		45.0d	14-Aug-24 A	16-Oct-24 A	
424	DS-SD-ASD-110	Struct. Design	45.0d	14-Aug-24 A	16-Oct-24 A	
425	WBS - White Papers		35.0d	5-Sep-24 A	23-Oct-24 A	
426	DS-SD-ASD-190	Solar Power - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
427	DS-SD-ASD-200	CUP At Airside vs. MTCE CUP - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
428	DS-SD-ASD-210	Resiliency - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
429	DS-SD-ASD-220	Electrochromatic Glazing - White Paper	25.0d	5-Sep-24 A	9-Oct-24 A	
430	DS-SD-ASD-350	Incorporate Information Into 30% Design - White Paper	10.0d	10-Oct-24 A	23-Oct-24 A	
431	WBS - APN - 30% Apron Site		136.0d	18-Jul-24 A	30-Jan-25 A	
432	WBS - PBB Layout		23.0d	29-Aug-24 A	1-Oct-24 A	
433	DS-SD-ASD-150	PBB Initial Layout 30% Apron Site	8.0d	29-Aug-24 A	10-Sep-24 A	
434	DS-SD-ASD-230	PBB Refinement 30% Apron Site	5.0d	11-Sep-24 A	17-Sep-24 A	
435	DS-SD-ASD-280	PBB Found. Location 30% Apron Site	5.0d	18-Sep-24 A	24-Sep-24 A	
436	DS-SD-ASD-310	PBB Layout Confirmation 30% Apron Site	5.0d	25-Sep-24 A	1-Oct-24 A	
437	WBS - Architectural Coordination		64.0d	18-Jul-24 A	16-Oct-24 A	
438	DS-SD-ASD-20	Truck Court Layout & Retaining Wall - Arch. Coord.	43.0d	18-Jul-24 A	17-Sep-24 A	
439	DS-SD-ASD-250	Building Footprint Identified for Civil - Arch. Coord.	1.0d	18-Sep-24 A	18-Sep-24 A	
440	DS-SD-ASD-260	FF Elevation Established for Civil - Arch. Coord.	1.0d	18-Sep-24 A	18-Sep-24 A	
441	DS-SD-ASD-270	Civil Layout & Refinement - Arch. Coord.	21.0d	18-Sep-24 A	16-Oct-24 A	
442	DS-SD-ASD-320	Exterior Door Locations (OHD) - Arch. Coord.	1.0d	2-Oct-24 A	2-Oct-24 A	
443	WBS - Wind Study		90.0d	23-Sep-24 A	30-Jan-25 A	
444	DS-SD-ASD-300	Wind Study (Expert Opinion)	20.0d	23-Sep-24 A	18-Oct-24 A	
445	DS-SD-ASD-370	Wind Study Summary - Recap Overview	2.0d	21-Oct-24 A	22-Oct-24 A	
446	DS-SD-ASD-380	Wind Study Model	25.0d	21-Oct-24 A	25-Nov-24 A	
447	DS-SD-ASD-470	Wind Study Analysis - Full Report	10.0d	26-Nov-24 A	10-Dec-24 A	
448	DS-SD-ASD-510	Wind Study HNTB Review Analysis	10.0d	11-Dec-24 A	24-Dec-24 A	
449	DS-SD-ASD-520	Wind Study Update Superstructure	10.0d	26-Dec-24 A	9-Jan-25 A	
450	DS-SD-ASD-530	Wind Study Update Found.	10.0d	10-Jan-25 A	23-Jan-25 A	
451	DS-SD-ASD-540	Wind Study Finalize Found.	5.0d	24-Jan-25 A	30-Jan-25 A	
452	WBS - Civil Plans		50.0d	18-Jul-24 A	26-Sep-24 A	
453	DS-SD-ASD-30	Civil Paving/Hydrant Fueling 30% Design Apron Site	50.0d	18-Jul-24 A	26-Sep-24 A	
454	DS-SD-ASD-40	Civil Apron Demo Plans	50.0d	18-Jul-24 A	26-Sep-24 A	
455	DS-SD-ASD-50	Civil Site Utilities	50.0d	18-Jul-24 A	26-Sep-24 A	
456	WBS - Preliminary Cost Estimate		1.0d	23-Oct-24 A	23-Oct-24 A	
457	DS-SD-ASD-390	Preliminary Set To HP For Cost Estimating	1.0d	23-Oct-24 A	23-Oct-24 A	
458	WBS - ASD - 30% Review QA/QC		17.0d	28-Oct-24 A	19-Nov-24 A	
459	DS-SD-ASD-400	DQC - ASD 30%	5.0d	28-Oct-24 A	1-Nov-24 A	
460	DS-SD-ASD-410	Sr. Technical Review - ASD 30%	5.0d	28-Oct-24 A	1-Nov-24 A	
461	DS-SD-ASD-420	Post to Bluebeam Session - ASD 30%	1.0d	4-Nov-24 A	4-Nov-24 A	
462	DS-SD-ASD-430	IDR Comments - ASD 30%	5.0d	5-Nov-24 A	11-Nov-24 A	

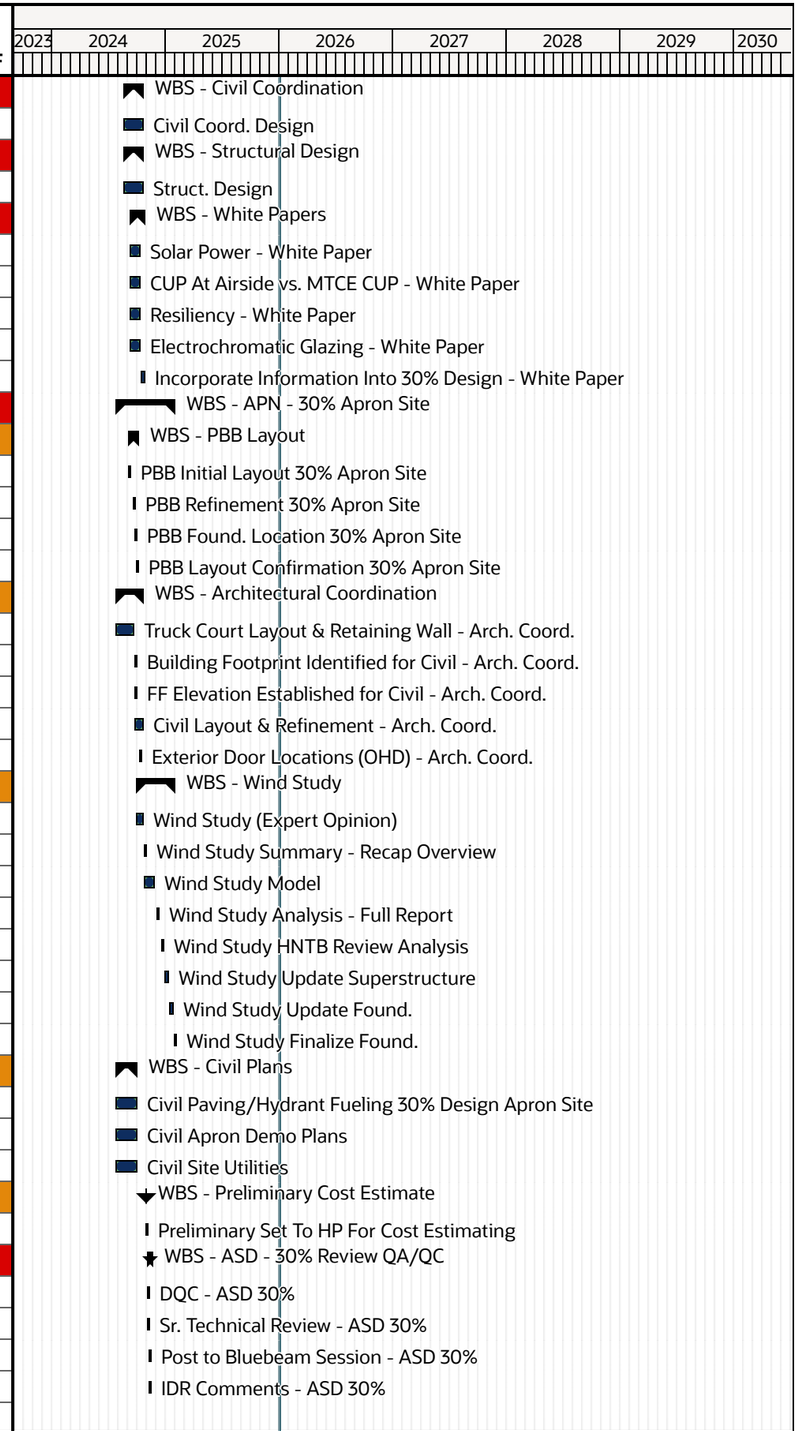


	ID	Name	Dur	Start	Finish	TF
463	DS-SD-ASD-440	IDR - Pick Up Comments - ASD 30%	2.0d	12-Nov-24 A	13-Nov-24 A	
464	DS-SD-ASD-450	Visual Check - ASD 30%	2.0d	14-Nov-24 A	15-Nov-24 A	
465	DS-SD-ASD-460	QA Check - ASD 30%	2.0d	18-Nov-24 A	19-Nov-24 A	
466	WBS - ASD - 30% Submittal To HCAA		11.0d	20-Nov-24 A	6-Dec-24 A	
467	DS-SD-ASD-480	ASD - Docs. Complete & Assemble Pkg.	1.0d	20-Nov-24 A	20-Nov-24 A	
468	DS-SD-ASD-490	ASD - 30% Subm. Due To HCAA	1.0d	21-Nov-24 A	21-Nov-24 A	
469	DS-SD-ASD-500	ASD - 30% HCAA Review	9.0d	22-Nov-24 A	6-Dec-24 A	
470	WBS - ASD - 60% Design Development		130.0d	21-Nov-24 A	28-May-25 A	
471	DS-DD-ASD-10	ASD - 60% DD NTP	1.0d	21-Nov-24 A	21-Nov-24 A	
472	WBS - ASD - 60% Design		130.0d	21-Nov-24 A	28-May-25 A	
473	WBS - ASD - 60% Design Documents		117.0d	21-Nov-24 A	8-May-25 A	
474	WBS - Airside D Terminal		96.0d	21-Nov-24 A	9-Apr-25 A	
475	DS-DD-ASD-20	Civil Design - ASD 60% DD Airside D Terminal	71.0d	21-Nov-24 A	5-Mar-25 A	
476	DS-DD-ASD-30	Struct. Design - ASD 60% DD Airside D Terminal	71.0d	21-Nov-24 A	5-Mar-25 A	
477	DS-DD-ASD-40	Architectural Design - ASD 60% DD Airside D Terminal	75.0d	22-Nov-24 A	12-Mar-25 A	
478	DS-DD-ASD-60	Ground Improvements Pkg. Coord. - ASD 60% DD Airside D Terminal	70.0d	22-Nov-24 A	5-Mar-25 A	
479	DS-DD-ASD-270	ASCEND Passenger Experience Extension - ASD 60% DD Airside D Terminal	20.0d	13-Mar-25 A	9-Apr-25 A	
480	WBS - Wind Study Report		74.0d	26-Nov-24 A	12-Mar-25 A	
481	DS-DD-ASD-220	Analysis Full Report - ASD 60% DD Wind Study Report	10.0d	26-Nov-24 A	10-Dec-24 A	
482	DS-DD-ASD-230	HNTB Review Analysis - ASD 60% DD Wind Study Report	10.0d	11-Dec-24 A	24-Dec-24 A	
483	DS-DD-ASD-240	Update Superstructure - ASD 60% DD Wind Study Report	10.0d	26-Dec-24 A	9-Jan-25 A	
484	DS-DD-ASD-100	Wind Tunnel - ASD 60% DD Wind Study Report	26.0d	31-Dec-24 A	5-Feb-25 A	
485	DS-DD-ASD-260	Finalize Found. - ASD 60% DD Wind Study Report	15.0d	10-Jan-25 A	30-Jan-25 A	
486	DS-DD-ASD-110	Incorporate White Paper Into 60% - ASD 60% DD Wind Study Report	25.0d	6-Feb-25 A	12-Mar-25 A	
487	WBS - APN - Apron Site		75.0d	22-Nov-24 A	12-Mar-25 A	
488	DS-DD-ASD-50	Civil Design Docs. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
489	DS-DD-ASD-70	Architectural/Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
490	DS-DD-ASD-80	MEP/Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
491	DS-DD-ASD-90	Struct./Civil Coord. - ASD 60% DD Apron Site	75.0d	22-Nov-24 A	12-Mar-25 A	
492	WBS - Preliminary Cost Estimate		23.0d	8-Apr-25 A	8-May-25 A	
493	DS-DD-ASD-120	Preliminary Set to HP For Cost Estimating - ASD 60% DD	23.0d	8-Apr-25 A	8-May-25 A	
494	WBS - ASD - 60% Review QA/QC		19.0d	10-Apr-25 A	6-May-25 A	
495	DS-DD-ASD-130	Design Review - DQC - ASD 60% Review QA/QC	5.0d	10-Apr-25 A	16-Apr-25 A	
496	DS-DD-ASD-140	Sr. Technical Review - ASD 60% Review QA/QC	5.0d	10-Apr-25 A	16-Apr-25 A	
497	DS-DD-ASD-150	Post Docs. - ASD 60% Review QA/QC	1.0d	17-Apr-25 A	17-Apr-25 A	
498	DS-DD-ASD-160	IDR - ASD 60% Review QA/QC	9.0d	18-Apr-25 A	30-Apr-25 A	
499	DS-DD-ASD-170	Visual Check - ASD 60% Review QA/QC	2.0d	1-May-25 A	2-May-25 A	
500	DS-DD-ASD-180	QAR Check - ASD 60% Review QA/QC	2.0d	5-May-25 A	6-May-25 A	
501	WBS - ASD - 60% Submittal To HCAA		15.0d	7-May-25 A	28-May-25 A	
502	DS-DD-ASD-190	Complete Docs. & Assemble Pkg. - ASD 60% Subm. to HCAA	1.0d	7-May-25 A	7-May-25 A	
503	DS-DD-ASD-200	Airside D Subm. Due - ASD 60% Subm. to HCAA	1.0d	8-May-25 A	8-May-25 A	
504	DS-DD-ASD-210	HCAA Review - ASD 60% Subm. to HCAA	13.0d	9-May-25 A	28-May-25 A	

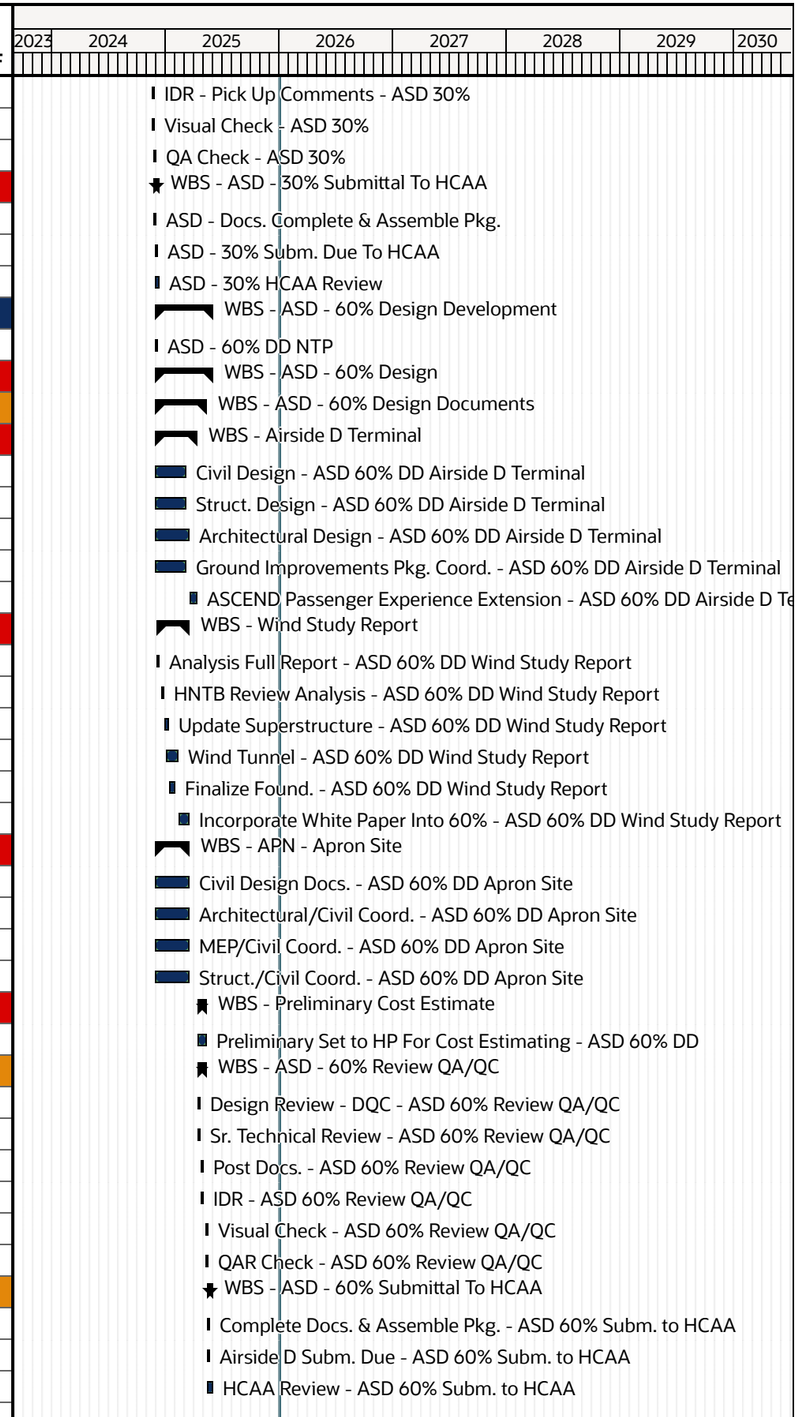


	ID	Name	Dur	Start	Finish	TF
505	WBS - ASD 90% Construction Documents		86.0d	8-May-25 A	9-Sep-25 A	
506	WBS - ASD 90% NTP		1.0d	8-May-25 A	8-May-25 A	
507	DS-CD-ASD-40	ASD - 90% CD NTP	1.0d	8-May-25 A	8-May-25 A	
508	WBS - ASD 90% Design		86.0d	8-May-25 A	9-Sep-25 A	
509	WBS - ASD 90% Design Documents		70.0d	8-May-25 A	15-Aug-25 A	
510	WBS - Airside D Terminal		45.0d	8-May-25 A	11-Jul-25 A	
511	DS-CD-ASD-10	Architectural Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
512	DS-CD-ASD-20	Civil Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
513	DS-CD-ASD-30	Struct. Design - ASD 90% DD Airside D Terminal	45.0d	8-May-25 A	11-Jul-25 A	
514	WBS - APN - Apron Site		47.0d	9-May-25 A	16-Jul-25 A	
515	DS-CD-ASD-50	Civil Design Docs. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
516	DS-CD-ASD-60	Architectural/Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
517	DS-CD-ASD-70	MEP/Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
518	DS-CD-ASD-80	Struct./Civil Coord. - ASD 90% DD PN Apron Side	47.0d	9-May-25 A	16-Jul-25 A	
519	WBS - Preliminary Cost Estimate		22.0d	17-Jul-25 A	15-Aug-25 A	
520	DS-CD-ASD-90	Preliminary Print Set For Cost Estimate To HP - ASD 90% DD	22.0d	17-Jul-25 A	15-Aug-25 A	
521	WBS - ASD 90% Review QA/QC		24.0d	17-Jul-25 A	19-Aug-25 A	
522	DS-CD-ASD-100	CD Review - DQC - ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
523	DS-CD-ASD-110	Sr. Technical Review - ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
524	DS-CD-ASD-095	Start CD Review - ASD 90% Review QA/QC	0.0d	17-Jul-25 A		
525	DS-CD-ASD-120	Post to Bluebeam - ASD 90% Review QA/QC	0.0d	29-Jul-25 A	29-Jul-25 A	
526	DS-CD-ASD-130	IDR - ASD 90% Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
527	DS-CD-ASD-140	Visual Check - ASD 90% Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
528	DS-CD-ASD-150	QAR Check - ASD 90% Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
529	WBS - ASD 90% Submittal To HCAA		14.0d	20-Aug-25 A	9-Sep-25 A	
530	DS-CD-ASD-160	Complete Docs. & Assemble Pkg. - ASD 90% Subm.	1.0d	20-Aug-25 A	20-Aug-25 A	
531	DS-CD-ASD-170	Subm. Due to HCAA - ASD 90% Subm.	1.0d	21-Aug-25 A	21-Aug-25 A	
532	DS-CD-ASD-180	HCAA Review - ASD 90% Subm.	12.0d	22-Aug-25 A	9-Sep-25 A	
533	WBS - ASD 100% Construction Documents		50.0d	21-Aug-25 A	30-Oct-25 A	
534	WBS - ASD 100% NTP		1.0d	21-Aug-25 A	21-Aug-25 A	
535	DS-CD-ASD-1000	ASD - 100% CD NTP	1.0d	21-Aug-25 A	21-Aug-25 A	
536	WBS - ASD 100% Design		49.0d	22-Aug-25 A	30-Oct-25 A	
537	WBS - ASD 100% Design Documents		36.0d	22-Aug-25 A	13-Oct-25 A	
538	WBS - Airside D Terminal		30.0d	22-Aug-25 A	3-Oct-25 A	
539	DS-CD-ASD-1010	Architectural Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
540	DS-CD-ASD-1030	Civil Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
541	DS-CD-ASD-1040	Struct. Design - ASD 100% DD	30.0d	22-Aug-25 A	3-Oct-25 A	
542	WBS - Apron Site		30.0d	22-Aug-25 A	3-Oct-25 A	
543	DS-CD-ASD-1020	Civil Design Docs. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
544	DS-CD-ASD-1050	Architectural/Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
545	DS-CD-ASD-1060	MEP/Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	
546	DS-CD-ASD-1070	Struct./Civil Coord. - ASD 100% DD Apron Site	30.0d	22-Aug-25 A	3-Oct-25 A	

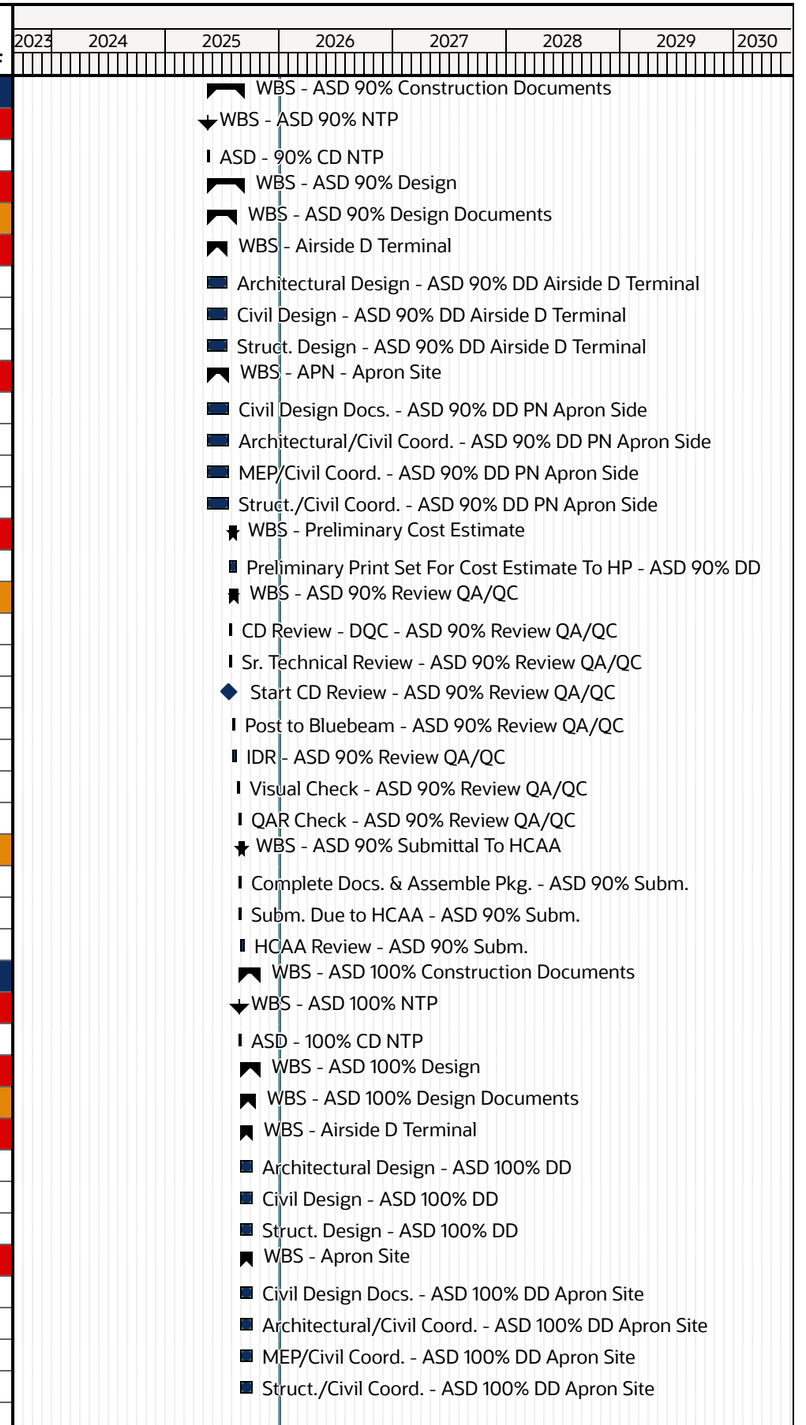


	ID	Name	Dur	Start	Finish	TF
547	WBS - Preliminary Cost Estimate		12.0d	26-Sep-25 A	13-Oct-25 A	
548	DS-CD-ASD-1080	Preliminary Print Set for Cost Estimate to HP - ASD 100% DD Apron Site	12.0d	26-Sep-25 A	13-Oct-25 A	
549	WBS - ASD 100% Review QA/QC		17.0d	6-Oct-25 A	28-Oct-25 A	
550	DS-CD-ASD-1090	DQC - ASD 100% CD Review QA/QC	5.0d	6-Oct-25 A	10-Oct-25 A	
551	DS-CD-ASD-1100	Sr. Technical Review - ASD 100% CD Review QA/QC	5.0d	6-Oct-25 A	10-Oct-25 A	
552	DS-CD-ASD-1110	Post to Bluebeam - ASD 100% CD Review QA/QC	1.0d	13-Oct-25 A	13-Oct-25 A	
553	DS-CD-ASD-1120	IDR - ASD 100% CD Review QA/QC	8.0d	14-Oct-25 A	23-Oct-25 A	
554	DS-CD-ASD-1130	Visual Check - ASD 100% CD Review QA/QC	2.0d	24-Oct-25 A	27-Oct-25 A	
555	DS-CD-ASD-1140	QAR Check - ASD 100% CD Review QA/QC	1.0d	28-Oct-25 A	28-Oct-25 A	
556	WBS - ASD 100% Submittal To HCAA		2.0d	29-Oct-25 A	30-Oct-25 A	
557	DS-CD-ASD-1150	Complete Docs. & Assemble Pkg. - ASD 100% Subm. to HCAA	1.0d	29-Oct-25 A	29-Oct-25 A	
558	DS-CD-ASD-1160	Submittal Due to HP/HCAA - ASD 100% Subm. to HCAA	1.0d	30-Oct-25 A	30-Oct-25 A	
559	WBS - Airside E Optimization		323.0d	16-Sep-24 A	23-Dec-25 A	
560	WBS - ASE Optimization Proposal		168.0d	16-Sep-24 A	13-May-25 A	
561	DS-AE-10	Proposal Submitted (HNTB) - ASE Optimization	1.0d	16-Sep-24 A	16-Sep-24 A	
562	DS-AE-20	Owner Proposal Review - ASE Optimization	159.0d	17-Sep-24 A	1-May-25 A	
563	DS-AE-30	Anticipated NTP - ASE Optimization	1.0d	13-May-25 A	13-May-25 A	
564	WBS - ASE Optimization 15%		44.0d	14-May-25 A	16-Jul-25 A	
565	WBS - ASE Optimization 15% Documents		22.0d	14-May-25 A	13-Jun-25 A	
566	DS-AE-40	Exist. Conditions Investigation - ASE Optimization 15%	5.0d	14-May-25 A	20-May-25 A	
567	DS-AE-50	Concept Design - ASE Optimization 15%	12.0d	21-May-25 A	6-Jun-25 A	
568	DS-AE-60	Focus Team Mtg. With HCAA - ASE Optimization 15%	3.0d	9-Jun-25 A	11-Jun-25 A	
569	DS-AE-70	Incorporate Comments into Design - ASE Optimization 15%	2.0d	12-Jun-25 A	13-Jun-25 A	
570	WBS - ASE Optimization 15% QA/QC		10.0d	16-Jun-25 A	27-Jun-25 A	
571	DS-AE-90	DQC - ASE Optimization 15% QA/QC	4.0d	16-Jun-25 A	19-Jun-25 A	
572	DS-AE-80	Sr. Technical Review - ASE Optimization 15% QA/QC	4.0d	16-Jun-25 A	19-Jun-25 A	
573	DS-AE-100	Post Docs. - ASE Optimization 15% QA/QC	1.0d	19-Jun-25 A	19-Jun-25 A	
574	DS-AE-110	IDR - ASE Optimization 15% QA/QC	4.0d	20-Jun-25 A	25-Jun-25 A	
575	DS-AE-120	Visual Check - ASE Optimization 15% QA/QC	1.0d	26-Jun-25 A	26-Jun-25 A	
576	DS-AE-130	QAR - ASE Optimization 15% QA/QC	1.0d	27-Jun-25 A	27-Jun-25 A	
577	WBS - ASE Optimization 15% Submittal To HCAA		12.0d	30-Jun-25 A	16-Jul-25 A	
578	DS-AE-140	Complete Docs. & Assemble Pkg. - ASE Optimization 15% Subm.	1.0d	30-Jun-25 A	30-Jun-25 A	
579	DS-AE-150	Subm. Due to HCAA - ASE Optimization 15% Subm.	1.0d	1-Jul-25 A	1-Jul-25 A	
580	DS-AE-160	Review (HCAA) - ASE Optimization 15% Subm.	10.0d	2-Jul-25 A	16-Jul-25 A	
581	WBS - ASE Optimization 50%		86.0d	3-Jul-25 A	3-Nov-25 A	
582	WBS - ASE Optimization 50% Documents		62.0d	3-Jul-25 A	30-Sep-25 A	
583	DS-AE-290	Design Docs. - ASE Optimization 50% Docs.	24.0d	3-Jul-25 A	6-Aug-25 A	
584	DS-AE-300	Focus Team Mtg. With HCAA - ASE Optimization 50% Docs.	5.0d	7-Aug-25 A	13-Aug-25 A	
585	DS-AE-310	Incorporate Comments into Design - ASE Optimization 50% Docs.	10.0d	14-Aug-25 A	27-Aug-25 A	
586	DS-AE-315	Decision Date for BHS Make-up System - ASE Optimization 50% Docs.	1.0d	28-Aug-25 A	28-Aug-25 A	
587	DS-AE-640	BNP Readiness for Coordination Update Documents - ASE Optimization 50% D...	4.0d	29-Aug-25 A	4-Sep-25 A	
588	DS-AE-650	Consultant Update Documents - ASE Optimization 50% Docs.	15.0d	5-Sep-25 A	25-Sep-25 A	

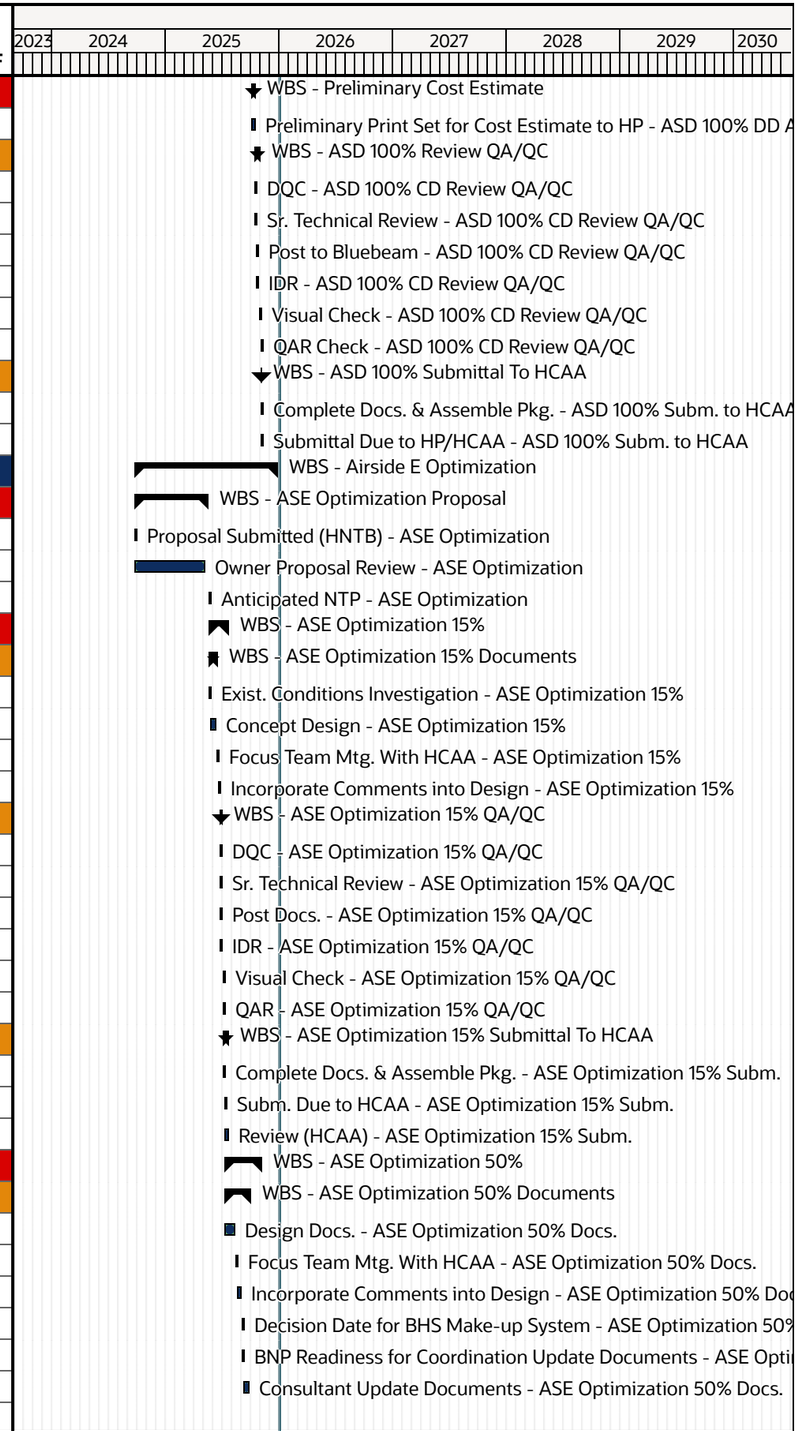


ID	Name	Dur	Start	Finish	TF
589	DS-AE-660 Finalize 50% Documents- ASE Optimization 50% Docs.	3.0d	26-Sep-25 A	30-Sep-25 A	
590	WBS - ASE Optimization 50% QA/QC	13.0d	1-Oct-25 A	17-Oct-25 A	
591	DS-AE-320 Sr. Technical Review - ASE Optimization 50% QA/QC	5.0d	1-Oct-25 A	7-Oct-25 A	
592	DS-AE-330 DQC - ASE Optimization 50% QA/QC	5.0d	1-Oct-25 A	7-Oct-25 A	
593	DS-AE-340 Post Docs. - ASE Optimization 50% QA/QC	1.0d	8-Oct-25 A	8-Oct-25 A	
594	DS-AE-350 IDR - ASE Optimization 50% QA/QC	5.0d	9-Oct-25 A	15-Oct-25 A	
595	DS-AE-360 Visual Check - ASE Optimization 50% QA/QC	1.0d	16-Oct-25 A	16-Oct-25 A	
596	DS-AE-370 QAR - ASE Optimization 50% QA/QC	1.0d	17-Oct-25 A	17-Oct-25 A	
597	WBS - ASE Optimization 50% Submittal To HCAA	12.0d	17-Oct-25 A	3-Nov-25 A	
598	DS-AE-380 Complete Docs. & Assemble Pkg. - ASE Optimization 50% Subm.	1.0d	17-Oct-25 A	17-Oct-25 A	
599	DS-AE-390 Subm. Due to HCAA - ASE Optimization 50% Subm.	1.0d	20-Oct-25 A	20-Oct-25 A	
600	DS-AE-400 Review by HCAA - ASE Optimization 50% Subm.	10.0d	21-Oct-25 A	3-Nov-25 A	
601	WBS - ASE Optimization 90%	44.0d	21-Oct-25 A	23-Dec-25 A	
602	WBS - ASE Optimization 90% Documents	32.0d	21-Oct-25 A	5-Dec-25 A	
603	DS-AE-410 Design Docs. - ASE Optimization 90% Docs.	25.0d	21-Oct-25 A	24-Nov-25 A	
604	DS-AE-420 Focus Team Mtg. With HCAA - ASE Optimization 90% Docs.	1.0d	25-Nov-25 A	25-Nov-25 A	
605	DS-AE-430 Incorporate Comments into Design - ASE Optimization 90% Docs.	6.0d	26-Nov-25 A	5-Dec-25 A	
606	WBS - ASE Optimization 90% QA/QC	9.0d	8-Dec-25 A	19-Dec-25 A	
607	DS-AE-440 Sr. Technical Review - ASE Optimization 90% QA/QC	3.0d	8-Dec-25 A	11-Dec-25 A	
608	DS-AE-450 DQC - ASE Optimization 90% QA/QC	3.0d	8-Dec-25 A	11-Dec-25 A	
609	DS-AE-460 Post Docs. - ASE Optimization 90% QA/QC	1.0d	12-Dec-25 A	12-Dec-25 A	
610	DS-AE-470 IDR - ASE Optimization 90% QA/QC	4.0d	15-Dec-25 A	18-Dec-25 A	
611	DS-AE-480 Visual Check / QA - ASE Optimization 90% QA/QC	1.0d	19-Dec-25 A	19-Dec-25 A	
612	WBS - ASE Optimization 90% Submittal To HCAA	2.0d	22-Dec-25 A	23-Dec-25 A	
613	DS-AE-500 Complete Docs. & Assemble Pkg. - ASE Optimization 90% Subm.	1.0d	22-Dec-25 A	22-Dec-25 A	
614	DS-AE-510 Subm. Due to HCAA - ASE Optimization 90% Subm.	1.0d	23-Dec-25 A	23-Dec-25 A	
615	WBS - A-Sortation & Airside C Screening Integration	26.0d	8-Sep-25 A	13-Oct-25 A	
616	DS-AA-120 NTP - A-Sortation & Airside C Screening Integration (First $150k)	1.0d	8-Sep-25 A	8-Sep-25 A	
617	DS-AA-100 Proposal Submitted (HNTB) - A-Sortation & Airside C Screening Integration	1.0d	13-Oct-25 A	13-Oct-25 A	
618	WBS - NST Application	95.0d	3-Apr-25 A	15-Aug-25 A	
619	DS-DD-NST-10 NST Mtg. - NST Appl.	1.0d	3-Apr-25 A	3-Apr-25 A	
620	DS-DD-NST-20 HNTB to Coordinate & Provide Information to NST - NST Appl.	3.0d	4-Apr-25 A	8-Apr-25 A	
621	DS-DD-NST-22 NST Draft Purchase Order - NST Appl.	5.0d	9-Apr-25 A	15-Apr-25 A	
622	DS-DD-NST-24 NST Reservation Letter - Email Received - NST Appl.	1.0d	28-Apr-25 A	28-Apr-25 A	
623	DS-DD-NST-30 HCAA Agreement Via Email - NST Appl.	5.0d	29-Apr-25 A	5-May-25 A	
624	DS-DD-NST-40 NST Reservation Letter - NST Appl.	5.0d	6-May-25 A	12-May-25 A	
625	DS-DD-NST-42 NST Revised Purchase Agreement HCAA Acceptance - NST Appl.	8.0d	13-May-25 A	22-May-25 A	
626	DS-DD-NST-43 NST & HCAA Agreement of Terms for Board Approval - NST Appl.	50.0d	23-May-25 A	4-Aug-25 A	
627	DS-DD-NST-44 NST HCAA Board Approval - NST Appl.	1.0d	7-Aug-25 A	7-Aug-25 A	
628	DS-DD-NST-46 NST Approval & Purchase Credit - NST Appl.	5.0d	8-Aug-25 A	14-Aug-25 A	
629	DS-DD-NST-50 NST Issuance & Completion of Credit Transfer - NST Appl.	1.0d	15-Aug-25 A	15-Aug-25 A	
630	WBS - SWFWMD Submittal Permit	137.0d	21-Mar-25 A	2-Oct-25 A	

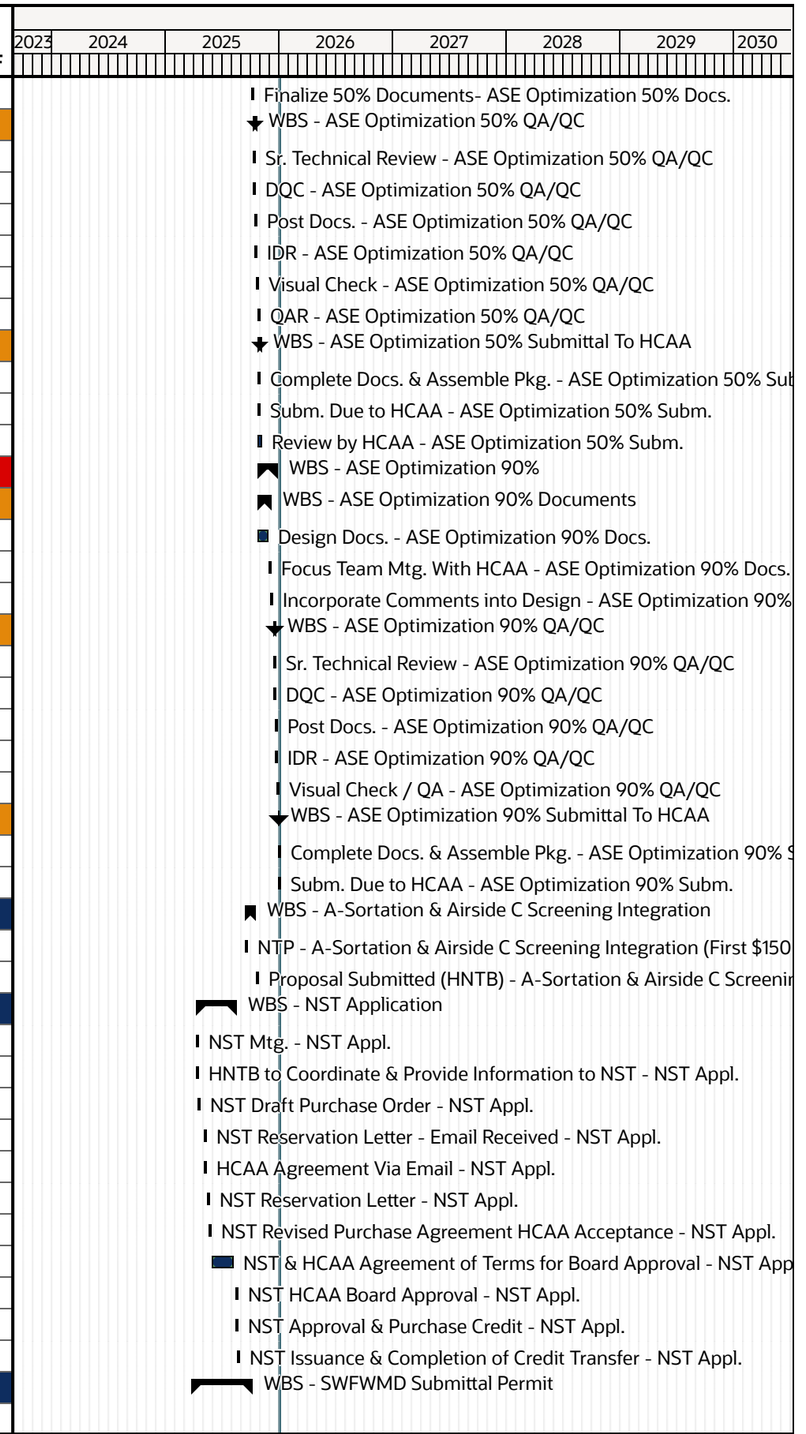


ID	Name	Dur	Start	Finish	TF
631	PM-SW-ITB1-30	ITB 1 & Apron Docs. Complete - SWFWMD Sub. Permit	1.0d	21-Mar-25 A	21-Mar-25 A	
632	PM-SW-40	Prepare Docs. Complete 60% - SWFWMD Sub. Permit	34.0d	24-Mar-25 A	8-May-25 A	
633	PM-SW-45	Revise Model & Adjust Drainage Information - SWFWMD Sub. Permit	10.0d	9-May-25 A	22-May-25 A	
634	PM-SW-50	Prepare Application Docs. - SWFWMD Sub. Permit	15.0d	23-May-25 A	13-Jun-25 A	
635	PM-SW-ITB1-55	ASD/ITB 1 Subm. to AHJ - SWFWMD Sub. Permit	1.0d	16-Jun-25 A	16-Jun-25 A	
636	PM-SW-58	SWFWMD DQC - SWFWMD Sub. Permit	4.0d	17-Jun-25 A	20-Jun-25 A	
637	WBS - SWFWMD IDR		72.0d	23-Jun-25 A	2-Oct-25 A	
638	PM-SW-60	SWFWMD Initial Submittal to HCAA for Review - SWFWMD Sub. Permit	1.0d	23-Jun-25 A	23-Jun-25 A	
639	PM-SW-65	SWFWMD Submittal Review - SWFWMD Sub. Permit	1.0d	24-Jun-25 A	24-Jun-25 A	
640	PM-SW-80	Design Team Respond to Initial Comments - SWFWMD Sub. Permit	1.0d	25-Jun-25 A	25-Jun-25 A	
641	PM-SW-85	Visual Check - SWFWMD Sub. Permit	1.0d	26-Jun-25 A	26-Jun-25 A	
642	PM-SW-ITB1-90	Submit SWFWMD ASD/ITB1 Revision #1 to AHJ - SWFWMD Sub. Permit	1.0d	27-Jun-25 A	27-Jun-25 A	
643	PM-SW-70	AHJ Conducts SWFWMD Final Review - SWFWMD Sub. Permit	22.0d	30-Jun-25 A	30-Jul-25 A	
644	PM-SW-100	Design Team Update & Respond to Comments - SWFWMD Sub. Permit	9.0d	31-Jul-25 A	12-Aug-25 A	
645	PM-SW-110	Design Team Submit Revisions to AHJ - SWFWMD Sub. Permit	1.0d	13-Aug-25 A	13-Aug-25 A	
646	PM-SW-115	AHJ - RAI Review - SWFWMD Sub. Permit	22.0d	14-Aug-25 A	15-Sep-25 A	
647	PM-SW-120	SWFWMD Write up After Confirming no Comments - SWFWMD Sub. Permit	12.0d	16-Sep-25 A	1-Oct-25 A	
648	PM-SW-130	SWFWMD Permit Issuance - SWFWMD Sub. Permit	1.0d	2-Oct-25 A	2-Oct-25 A	
649	WBS - ASD - Site Plan		112.0d	27-Jan-25 A	2-Jul-25 A	
650	DS-DD-ASDSPR-10	Define Requirements - ASD Site Plan	10.0d	27-Jan-25 A	7-Feb-25 A	
651	DS-DD-ASDSPR-30	COT Informs ASD of SPR Requirement - ASD Site Plan	0.0d	27-Jan-25 A	27-Jan-25 A	
652	DS-DD-ASDSPR-20	COT Mtg. - ASD Site Plan	1.0d	10-Feb-25 A	10-Feb-25 A	
653	DS-DD-ASDSPR-40	Develop Site Plan - ASD Site Plan	10.0d	11-Feb-25 A	24-Feb-25 A	
654	DS-DD-ASDSPR-140	HCAA Approve rk Order Authorization - ASD Site Plan	10.0d	25-Feb-25 A	10-Mar-25 A	
655	DS-DD-ASDSPR-50	Complete SPR Document Pkg. - ASD Site Plan	1.0d	20-Mar-25 A	20-Mar-25 A	
656	DS-DD-ASDSPR-70	Prepare Docs. for HCAA Review - ASD Site Plan	5.0d	21-Mar-25 A	27-Mar-25 A	
657	DS-DD-ASDSPR-80	Submit SPR to COT for Review - ASD Site Plan	1.0d	28-Mar-25 A	28-Mar-25 A	
658	DS-DD-ASDSPR-90	COT SPR Review - ASD Site Plan	34.0d	1-Apr-25 A	16-May-25 A	
659	DS-DD-ASDSPR-100	COT SPR Comments Received - ASD Site Plan	1.0d	19-May-25 A	19-May-25 A	
660	DS-DD-ASDSPR-110	COT Design Team Respond to Comments - ASD Site Plan	13.0d	20-May-25 A	6-Jun-25 A	
661	DS-DD-ASDSPR-60	Submit SPR Revision #1 to COT - ASD Site Plan	1.0d	9-Jun-25 A	9-Jun-25 A	
662	DS-DD-ASDSPR-120	COT Review Responses - ASD Site Plan	14.0d	10-Jun-25 A	27-Jun-25 A	
663	DS-DD-ASDSPR-130	Anticipated SPR Permit Approval by COT - ASD Site Plan	1.0d	2-Jul-25 A	2-Jul-25 A	
664	WBS - ASD - Early Foundations		217.0d	22-Nov-24 A	1-Oct-25 A	
665	WBS - ASD - Early Foundations 60%		72.0d	22-Nov-24 A	7-Mar-25 A	
666	WBS - ASD - Early Foundations 60% Design Documents		41.0d	22-Nov-24 A	23-Jan-25 A	
667	DS-DD-ASDEF-10	Struct. Design Docs. - ASD Early Found. 60% DD	41.0d	22-Nov-24 A	23-Jan-25 A	
668	DS-DD-ASDEF-20	Architectural/Struct. Design Coord. - ASD Early Found. 60% DD	41.0d	22-Nov-24 A	23-Jan-25 A	
669	DS-DD-ASDEF-130	Update Found. Per Wind Study - ASD Early Found. 60% DD	10.0d	10-Jan-25 A	23-Jan-25 A	
670	WBS - ASD - Early Foundations 60% Review Progress Print		31.0d	24-Jan-25 A	7-Mar-25 A	
671	DS-DD-ASDEF-100	Progress Printed - ASD Early Found. 60% Review Progress Print	1.0d	24-Jan-25 A	24-Jan-25 A	
672	DS-DD-ASDEF-110	Bluebeam Review - ASD Early Found. 60% Review Progress Print	5.0d	27-Jan-25 A	31-Jan-25 A	

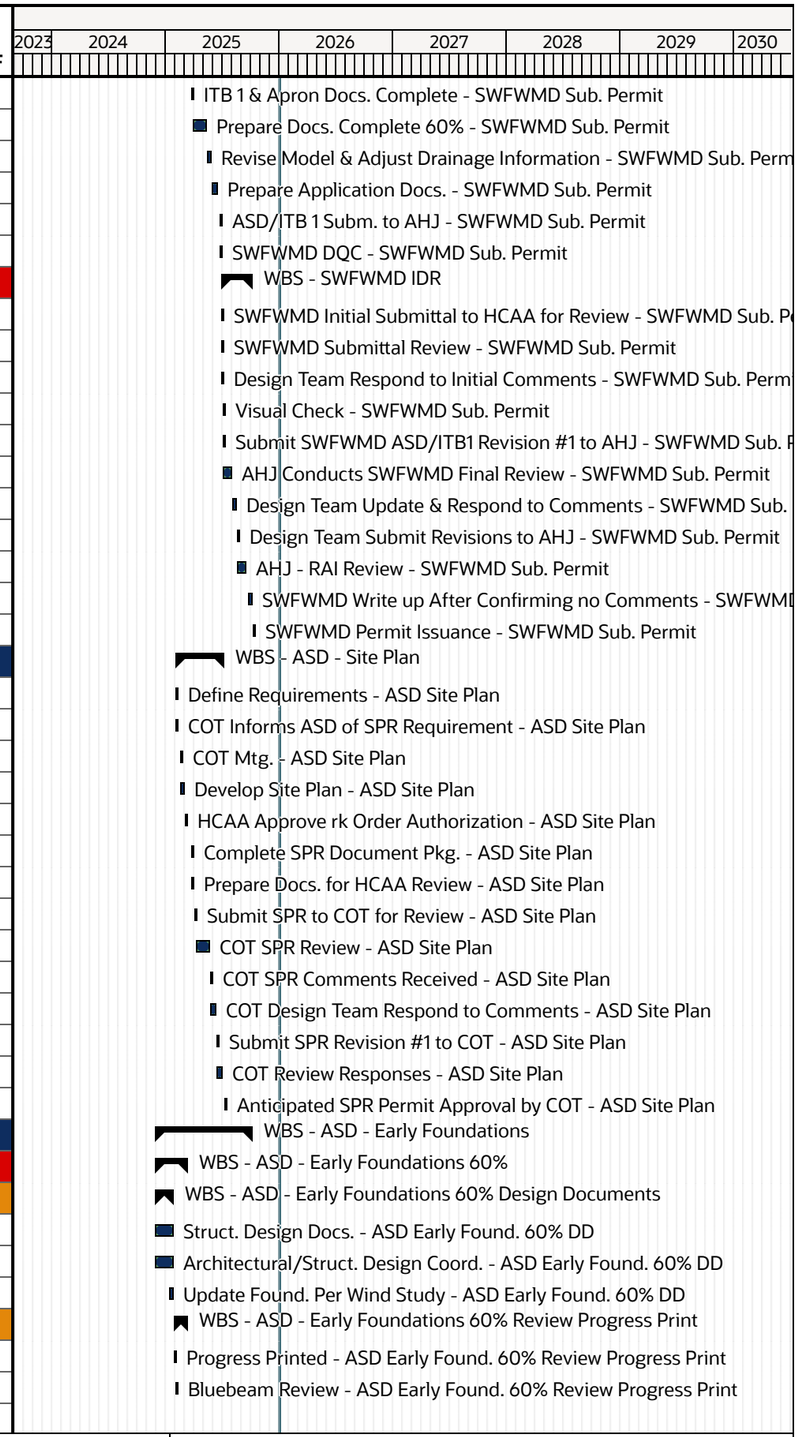


	ID	Name	Dur	Start	Finish	TF
673	DS-DD-ASDEF-120	Address Comments Incorporate into Docs. - ASD Early Found. 60% Review Pro…	25.0d	3-Feb-25 A	7-Mar-25 A	
674	DS-DD-ASDEF-140	Focus Team Review With HCAA - ASD Early Found. 60% Review Progress Print	2.0d	10-Feb-25 A	11-Feb-25 A	
675	WBS - ASD - Early Foundations 100%		163.0d	12-Feb-25 A	1-Oct-25 A	
676	WBS - ASD - Early Foundations 100% Design Documents		21.0d	12-Feb-25 A	12-Mar-25 A	
677	DS-CD-ASDEF-10	Struct. Design Docs. - ASD Early Found. 100% DD	21.0d	12-Feb-25 A	12-Mar-25 A	
678	DS-CD-ASDEF-20	Architectural/Struct. Design Coord. - ASD Early Found. 100% DD	21.0d	12-Feb-25 A	12-Mar-25 A	
679	WBS - ASD - EF Preliminary Cost Estimate		20.0d	13-Mar-25 A	9-Apr-25 A	
680	DS-CD-ASDEF-30	ASD - Preliminary Set To HP For Cost Estimating	20.0d	13-Mar-25 A	9-Apr-25 A	
681	WBS - ASD - Early Foundations 100% Review QA/QC		18.0d	14-Mar-25 A	8-Apr-25 A	
682	DS-CD-ASDEF-40	DQC - ASD Early Found. 100% Review QA/QC	5.0d	14-Mar-25 A	20-Mar-25 A	
683	DS-CD-ASDEF-50	Sr. Technical Review - ASD Early Found. 100% Review QA/QC	5.0d	14-Mar-25 A	20-Mar-25 A	
684	DS-CD-ASDEF-60	Post to Bluebeam - ASD Early Found. 100% Review QA/QC	1.0d	21-Mar-25 A	21-Mar-25 A	
685	DS-CD-ASDEF-70	IDR - ASD Early Found. 100% Review QA/QC	8.0d	24-Mar-25 A	2-Apr-25 A	
686	DS-CD-ASDEF-80	Visual Check - ASD Early Found. 100% Review QA/QC	2.0d	3-Apr-25 A	4-Apr-25 A	
687	DS-CD-ASDEF-90	QA Check - ASD Early Found. 100% Review QA/QC	2.0d	7-Apr-25 A	8-Apr-25 A	
688	WBS - ASD - Early Foundations 100% Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
689	DS-CD-ASDEF-100	Complete Docs. & Assemble Pkg. - ASD Early Found. 100% Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
690	DS-CD-ASDEF-110	Bid/Permit Set Subm. Due - ASD Early Found. 100% Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
691	DS-CD-ASDEF-120	HCAA Review - ASD Early Found. 100% Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
692	WBS - ASD - FND - Bidding and Negotiations		51.0d	11-Apr-25 A	23-Jun-25 A	
693	DS-FND-B&N-10	Update Plans with New Loads - ASD-FND-Bidding & Negotiations	24.0d	11-Apr-25 A	14-May-25 A	
694	DS-FND-B&N-20	Issued load impact to Base - ASD-FND-Bidding & Negotiations	1.0d	15-May-25 A	15-May-25 A	
695	DS-FND-B&N-30	Base to Update Found. Design /Details - ASD-FND-Bidding & Negotiations	14.0d	16-May-25 A	5-Jun-25 A	
696	DS-FND-B&N-40	Design Updates Finalized - ASD-FND-Bidding & Negotiations	0.0d		5-Jun-25 A	
697	DS-FND-B&N-50	Design Updates DQC Start - ASD-FND-Bidding & Negotiations	1.0d	6-Jun-25 A	6-Jun-25 A	
698	DS-FND-B&N-60	DQC - ASD-FND-Bidding & Negotiations	2.0d	6-Jun-25 A	9-Jun-25 A	
699	DS-FND-B&N-70	Post to IDR Bluebeam - ASD-FND-Bidding & Negotiations	0.0d		9-Jun-25 A	
700	DS-FND-B&N-80	IDR - ASD-FND-Bidding & Negotiations	2.0d	10-Jun-25 A	11-Jun-25 A	
701	DS-FND-B&N-90	VC / QA - ASD-FND-Bidding & Negotiations	1.0d	12-Jun-25 A	12-Jun-25 A	
702	DS-FND-B&N-100	Addendum Issued to HP - ASD-FND-Bidding & Negotiations	0.0d		12-Jun-25 A	
703	DS-FND-B&N-110	Bidding - ASD-FND-Bidding & Negotiations	4.0d	13-Jun-25 A	18-Jun-25 A	
704	DS-FND-B&N-120	Bids Due Date - ASD-FND-Bidding & Negotiations	1.0d	19-Jun-25 A	19-Jun-25 A	
705	DS-FND-B&N-130	Ready to submit to COT - ASD-FND-Bidding & Negotiations	1.0d	23-Jun-25 A	23-Jun-25 A	
706	WBS - ASD - FND Bulletin 1		48.0d	25-Jul-25 A	1-Oct-25 A	
707	DS-FND-B&N-140	ASD - FND Bulletin 1 - Update Drawings	35.0d	25-Jul-25 A	12-Sep-25 A	
708	DS-FND-B&N-150	ASD - FND Bulletin 1 - Finalize Documents	1.0d	15-Sep-25 A	15-Sep-25 A	
709	WBS - ASD FND Bulletin 1 QA/QC		9.0d	16-Sep-25 A	26-Sep-25 A	
710	DS-FND-B&N-160	ASD - FND Bulletin 1 - DQC	2.0d	16-Sep-25 A	17-Sep-25 A	
711	DS-FND-B&N-170	ASD - FND Bulletin 1 - IDR	6.0d	18-Sep-25 A	25-Sep-25 A	
712	DS-FND-B&N-180	ASD - FND Bulletin 1 - Visual Check / QAR	1.0d	26-Sep-25 A	26-Sep-25 A	
713	WBS - ASD FND Bulletin 1 - Submittal to HP		3.0d	29-Sep-25 A	1-Oct-25 A	
714	DS-FND-B&N-190	ASD - FND Bulletin 1 - Complete Documents & Assemble Package	1.0d	29-Sep-25 A	29-Sep-25 A	

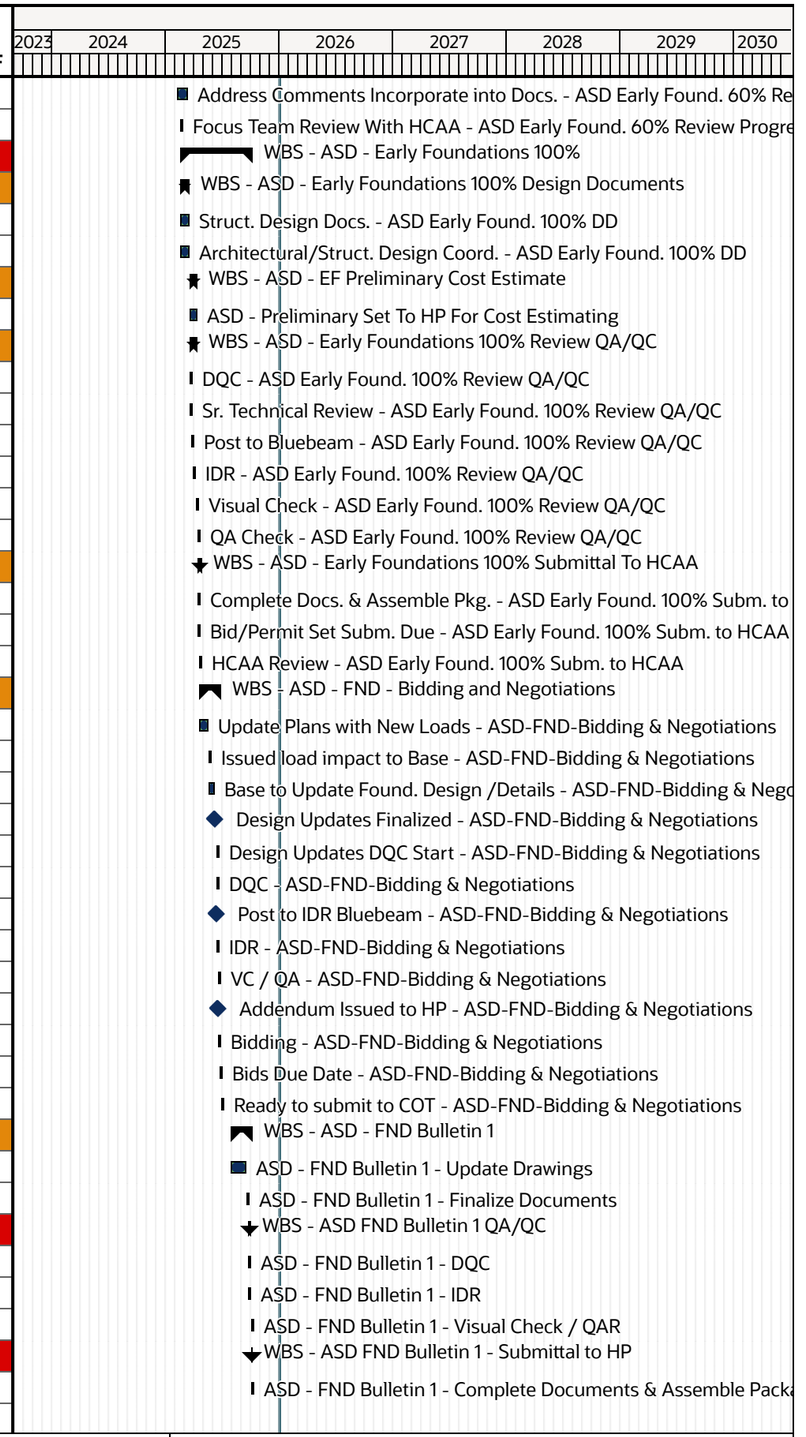


ID	Name	Dur	Start	Finish	TF
715	DS-FND-B&N-200 ASD - FND Bulletin 1 - FND Addendum 2 Submittal to HP	1.0d	30-Sep-25 A	30-Sep-25 A	
716	DS-FND-B&N-210 ASD - FND Bulletin 1 - Submit to COT	1.0d	1-Oct-25 A	1-Oct-25 A	
717	WBS - ASD - Long Lead Package (Steel, Chillers, AHU, Switchgear, VT, etc)	30.0d	9-May-25 A	20-Jun-25 A	
718	WBS - ASD - Long Lead Package Design Documents	18.0d	9-May-25 A	4-Jun-25 A	
719	DS-DD-ASDLL-10 Struct. Design - Steel Pkg. Mill Order - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
720	DS-DD-ASDLL-20 Vertical Transportation - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
721	DS-DD-ASDLL-30 Mech. Design AHU - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
722	DS-DD-ASDLL-40 Elec. Power & Feeders - ASD Long Lead Pckg. DD	18.0d	9-May-25 A	4-Jun-25 A	
723	WBS - ASD - LLP Preliminary Cost Estimate	21.0d	9-May-25 A	9-Jun-25 A	
724	DS-DD-ASDLL-50 ASD - LLP Preliminary Set to HP For Cost Estimating	21.0d	9-May-25 A	9-Jun-25 A	
725	WBS - ASD - Long Lead Package Review QA/QC	5.0d	5-Jun-25 A	11-Jun-25 A	
726	DS-DD-ASDLL-60 DQC - ASD Long Lead Pckg. Review QA/QC	2.0d	5-Jun-25 A	6-Jun-25 A	
727	DS-DD-ASDLL-70 Sr. Technical Review - ASD Long Lead Pckg. Review QA/QC	2.0d	5-Jun-25 A	6-Jun-25 A	
728	DS-DD-ASDLL-80 Post to Bluebeam - ASD Long Lead Pckg. Review QA/QC	0.0d		6-Jun-25 A	
729	DS-DD-ASDLL-90 IDR - ASD Long Lead Pckg. Review QA/QC	2.0d	9-Jun-25 A	10-Jun-25 A	
730	DS-DD-ASDLL-100 Visual Check - ASD Long Lead Pckg. Review QA/QC	1.0d	11-Jun-25 A	11-Jun-25 A	
731	DS-DD-ASDLL-110 QA Check - ASD Long Lead Pckg. Review QA/QC	1.0d	11-Jun-25 A	11-Jun-25 A	
732	WBS - ASD - Long Lead Package Submittal To HCAA	8.0d	11-Jun-25 A	20-Jun-25 A	
733	DS-DD-ASDLL-120 Complete & Assemble Docs. - ASD Long Lead Pckg. Subm. to HCAA	1.0d	11-Jun-25 A	11-Jun-25 A	
734	DS-DD-ASDLL-130 Submit Pkg. to HCAA - ASD Long Lead Pckg. Subm. to HCAA	1.0d	12-Jun-25 A	12-Jun-25 A	
735	DS-DD-ASDLL-140 HCAA Review - ASD Long Lead Pckg. Subm. to HCAA	6.0d	13-Jun-25 A	20-Jun-25 A	
736	WBS - ITB's - FAA Submittal Review	102.0d	1-Oct-24 A	25-Feb-25 A	
737	WBS - APN - ITB 1 - Paving - Hydrant Fueling - FAA Submittal	102.0d	1-Oct-24 A	25-Feb-25 A	
738	WBS - APN - ITB 1 - Design Documents	51.0d	1-Oct-24 A	12-Dec-24 A	
739	DS-DD-ITB1-AP-10 APN - ITB1 Hydrant Fueling - Civil - Paving Design	4.0d	1-Oct-24 A	4-Oct-24 A	
740	DS-DD-ITB1-AP-20 APN - ITB1 Hydrant Fueling - Civil - Paving Hydrant Fueling FAA	4.0d	1-Oct-24 A	4-Oct-24 A	
741	DS-DD-ITB1-AP-30 ATB1 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
742	DS-DD-ITB1-AP-40 ITB1 Hydrant Fueling - Civil - Civil - Docs.	30.0d	14-Oct-24 A	25-Nov-24 A	
743	DS-DD-ITB1-AP-50 ITB1 Hydrant Fueling - Civil - Preliminary Set to HP For Cost Estimating	16.0d	19-Nov-24 A	12-Dec-24 A	
744	WBS - APN - ITB 1 - Review QA/QC	16.0d	26-Nov-24 A	18-Dec-24 A	
745	DS-DD-ITB1-AP-170 Start QA/QC Review - APN - ITB1 Hydrant Fueling	1.0d	26-Nov-24 A	26-Nov-24 A	
746	DS-DD-ITB1-AP-60 Review - DQC - APN - ITB1 Hydrant Fueling	5.0d	27-Nov-24 A	4-Dec-24 A	
747	DS-DD-ITB1-AP-70 Sr. Technical Review - APN - ITB1 Hydrant Fueling	5.0d	27-Nov-24 A	4-Dec-24 A	
748	DS-DD-ITB1-AP-80 Post to Bluebeam - APN - ITB1 Hydrant Fueling	1.0d	5-Dec-24 A	5-Dec-24 A	
749	DS-DD-ITB1-AP-90 IDR - APN - ITB1 Hydrant Fueling	5.0d	6-Dec-24 A	12-Dec-24 A	
750	DS-DD-ITB1-AP-100 Visual Check - APN - ITB1 Hydrant Fueling	2.0d	16-Dec-24 A	17-Dec-24 A	
751	DS-DD-ITB1-AP-110 Review QA/QC Hydrant Fueling FAA - QA Check - APN - ITB1 Hydrant Fueling	1.0d	18-Dec-24 A	18-Dec-24 A	
752	WBS - APN - ITB 1 - Submittal To HCAA	47.0d	19-Dec-24 A	25-Feb-25 A	
753	DS-DD-ITB1-AP-120 Complete Docs. & Assemble Pkg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	19-Dec-24 A	19-Dec-24 A	
754	DS-DD-ITB1-AP-130 Subm. To HCAA - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	20-Dec-24 A	20-Dec-24 A	
755	DS-DD-ITB1-AP-140 FAA Review - APN - ITB1 Sub. to HCAA Hydrant Fueling	20.0d	23-Dec-24 A	21-Jan-25 A	
756	DS-DD-ITB1-AP-160 HCAA Review - APN - ITB1 Sub. to HCAA Hydrant Fueling	9.0d	23-Dec-24 A	6-Jan-25 A	

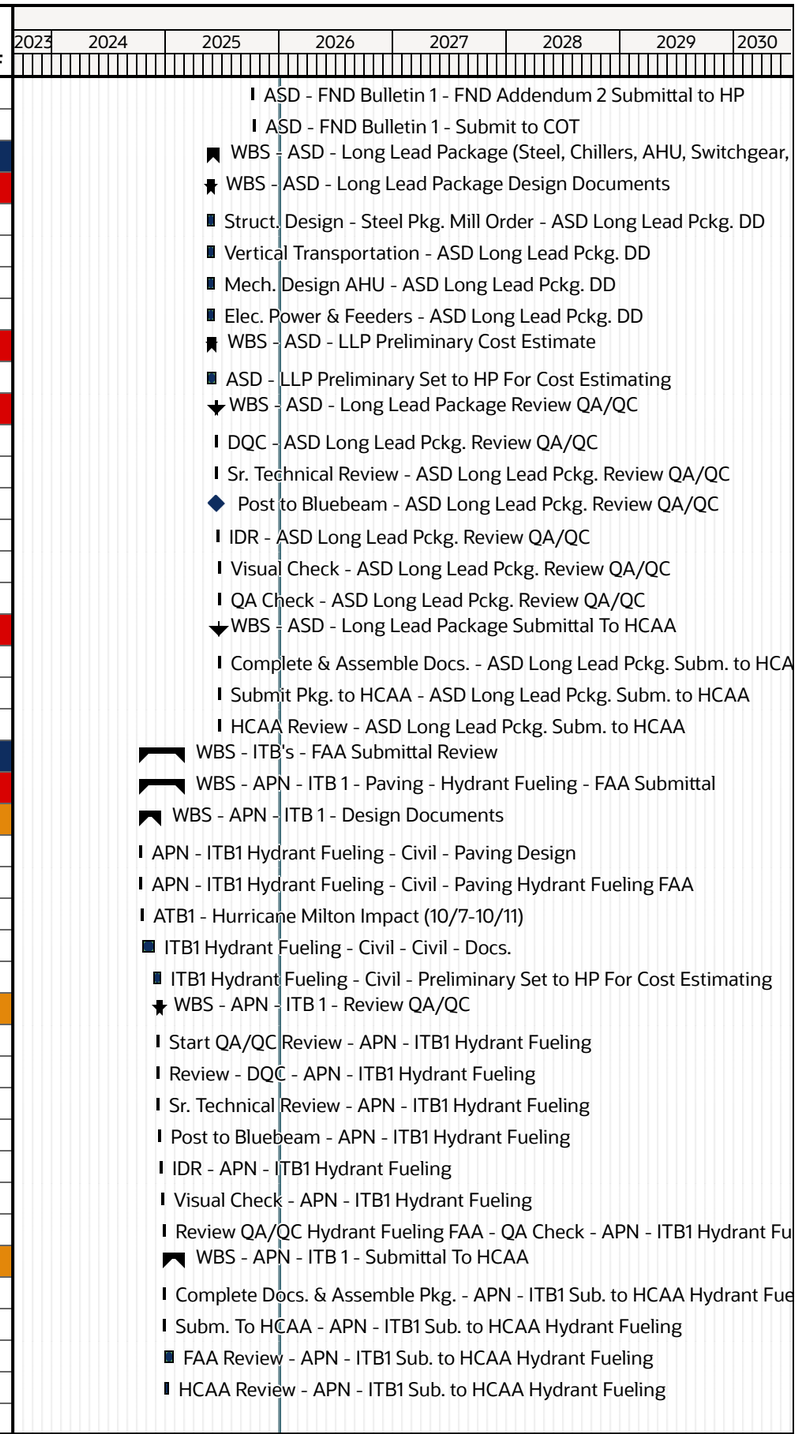


	ID	Name	Dur	Start	Finish	TF
757	DS-DD-ITB1-AP-180	Respond to HCAA Comments - APN - ITB1 Sub. to HCAA Hydrant Fueling	7.0d	7-Jan-25 A	15-Jan-25 A	
758	DS-DD-ITB1-AP-150	HCAA Comment Resolution Mtg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	16-Jan-25 A	16-Jan-25 A	
759	DS-DD-ITB1-AP-200	Respond to FAA Comments - APN - ITB1 Sub. to HCAA Hydrant Fueling	3.0d	22-Jan-25 A	24-Jan-25 A	
760	DS-DD-ITB1-AP-190	FAA Comment Resolution Mtg. - APN - ITB1 Sub. to HCAA Hydrant Fueling	1.0d	25-Feb-25 A	25-Feb-25 A	
761	WBS - ASD - ITB 2 - PBB Design - FAA Submittal (60%)		95.0d	2-Oct-24 A	17-Feb-25 A	
762	WBS - ASD - ITB 2 - PBB Design Documents		68.0d	2-Oct-24 A	9-Jan-25 A	
763	DS-DD-ITB2-PB-10	Architectural Design Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
764	DS-DD-ITB2-PB-20	Civil Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
765	DS-DD-ITB2-PB-30	Utility Coord. - ASD ITB 2 PBB 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
766	DS-DD-ITB2-PB-40	ATB2 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
767	DS-DD-ITB2-PB-50	Civil - Docs. - ASD ITB 2 PBB 60% DD	43.0d	14-Oct-24 A	13-Dec-24 A	
768	DS-DD-ITB2-PB-60	Preliminary Set to HP For Cost Estimating - ASD ITB 2 PBB 60% DD	22.0d	9-Dec-24 A	9-Jan-25 A	
769	WBS - ASD - ITB 2 - PBB Review QA/QC		16.0d	16-Dec-24 A	8-Jan-25 A	
770	DS-DD-ITB2-PB-170	Start QA/QC - ASD ITB 2 PBB 60% Design Review QA/QC	1.0d	16-Dec-24 A	16-Dec-24 A	
771	DS-DD-ITB2-PB-70	DQC - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	17-Dec-24 A	23-Dec-24 A	
772	DS-DD-ITB2-PB-80	Sr. Technical Review - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	17-Dec-24 A	23-Dec-24 A	
773	DS-DD-ITB2-PB-90	Post to Bluebeam - ASD ITB 2 PBB 60% Design Review QA/QC	1.0d	24-Dec-24 A	24-Dec-24 A	
774	DS-DD-ITB2-PB-100	IDR - ASD ITB 2 PBB 60% Design Review QA/QC	5.0d	26-Dec-24 A	2-Jan-25 A	
775	DS-DD-ITB2-PB-110	Visual Check - ASD ITB 2 PBB 60% Design Review QA/QC	2.0d	3-Jan-25 A	6-Jan-25 A	
776	DS-DD-ITB2-PB-120	QA Check - ASD ITB 2 PBB 60% Design Review QA/QC	2.0d	7-Jan-25 A	8-Jan-25 A	
777	WBS - ASD - ITB 2 - PBB Submittal To HCAA		28.0d	9-Jan-25 A	17-Feb-25 A	
778	DS-DD-ITB2-PB-130	Complete Docs. & Assemble Pkg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	9-Jan-25 A	9-Jan-25 A	
779	DS-DD-ITB2-PB-140	Subm. to HCAA Due - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	10-Jan-25 A	10-Jan-25 A	
780	DS-DD-ITB2-PB-150	FAA Review - ASD ITB 2 PBB 60% Subm. to HCAA	21.0d	13-Jan-25 A	10-Feb-25 A	
781	DS-DD-ITB2-PB-180	HCAA Review - ASD ITB 2 PBB 60% Subm. to HCAA	10.0d	13-Jan-25 A	27-Jan-25 A	
782	DS-DD-ITB2-PB-160	HCAA Comment Resolution Mtg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	28-Jan-25 A	28-Jan-25 A	
783	DS-DD-ITB2-PB-190	FAA Comment Resolution Mtg. - ASD ITB 2 PBB 60% Subm. to HCAA	1.0d	17-Feb-25 A	17-Feb-25 A	
784	WBS - GDY - ITB 3 - Guideway Structure - FAA Submittal (60%)		80.0d	2-Oct-24 A	27-Jan-25 A	
785	WBS - GDY - ITB 3 - Guideway Design Documents		50.0d	2-Oct-24 A	12-Dec-24 A	
786	DS-DD-ITB3-GS-10	Architectural Coord. & Design - GDY ITB3 GDWY Structure 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
787	DS-DD-ITB3-GS-20	Struct. Design - GDY ITB3 GDWY Structure 60% DD	3.0d	2-Oct-24 A	4-Oct-24 A	
788	DS-DD-ITB3-GS-30	ATB3 - Hurricane Milton Impact (10/7-10/11)	5.0d	7-Oct-24 A	11-Oct-24 A	
789	DS-DD-ITB3-GS-40	Civil - Docs. - GDY ITB3 GDWY Structure 60% DD	31.0d	14-Oct-24 A	26-Nov-24 A	
790	DS-DD-ITB3-GS-50	Preliminary Set to HP For Cost Estimating - GDY ITB3 GDWY Structure 60% DD	21.0d	12-Nov-24 A	12-Dec-24 A	
791	WBS - GDY - ITB 3 - Guideway Review QA/QC		15.0d	27-Nov-24 A	18-Dec-24 A	
792	DS-DD-ITB3-GS-160	Start QA/QC - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	27-Nov-24 A	27-Nov-24 A	
793	DS-DD-ITB3-GS-60	Review -DQC - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	29-Nov-24 A	5-Dec-24 A	
794	DS-DD-ITB3-GS-70	Sr. Technical Review - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	29-Nov-24 A	5-Dec-24 A	
795	DS-DD-ITB3-GS-80	Post to Bluebeam - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	6-Dec-24 A	6-Dec-24 A	
796	DS-DD-ITB3-GS-90	IDR - GDY ITB3 GDWY Structure 60% QA/QC	5.0d	9-Dec-24 A	13-Dec-24 A	
797	DS-DD-ITB3-GS-100	Visual Check - GDY ITB3 GDWY Structure 60% QA/QC	2.0d	16-Dec-24 A	17-Dec-24 A	
798	DS-DD-ITB3-GS-110	QA Check - GDY ITB3 GDWY Structure 60% QA/QC	1.0d	18-Dec-24 A	18-Dec-24 A	

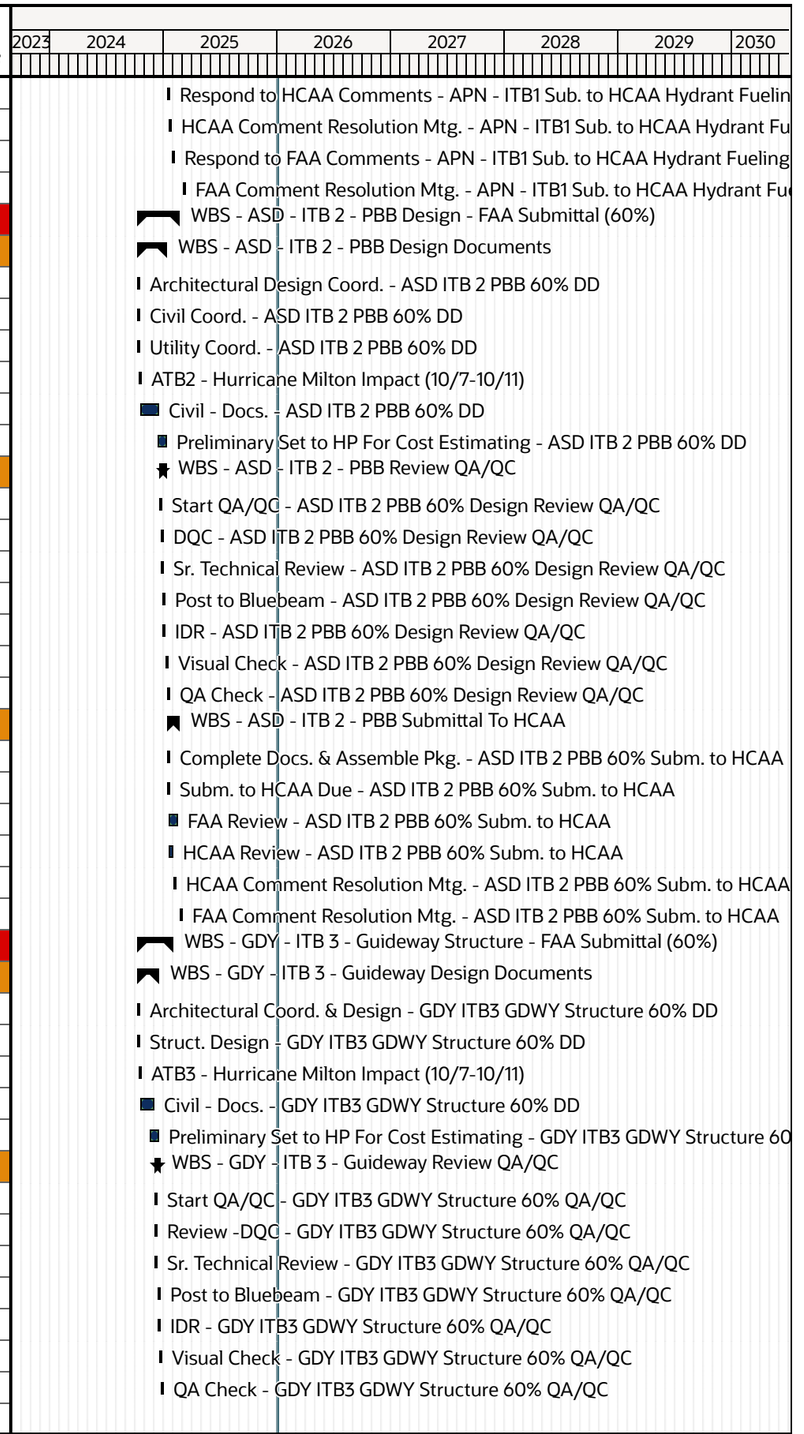

	ID	Name	Dur	Start	Finish	TF
799	WBS - GDY - ITB 3 - Guideway Submittal To HCAA		26.0d	19-Dec-24 A	27-Jan-25 A	
800	DS-DD-ITB3-GS-120	Complete Docs. & Assemble Pkg. - GDY ITB3 GDWY Structure 60% Subm. to H...	1.0d	19-Dec-24 A	19-Dec-24 A	
801	DS-DD-ITB3-GS-130	Subm. To HCAA - GDY ITB3 GDWY Structure 60% Subm. to HCAA	1.0d	20-Dec-24 A	20-Dec-24 A	
802	DS-DD-ITB3-GS-140	FAA Review - GDY ITB3 GDWY Structure 60% Subm. to HCAA	23.0d	23-Dec-24 A	24-Jan-25 A	
803	DS-DD-ITB3-GS-170	HCAA Review - GDY ITB3 GDWY Structure 60% Subm. to HCAA	24.0d	23-Dec-24 A	27-Jan-25 A	
804	DS-DD-ITB3-GS-150	Comment Resolution Mtg. - GDY ITB3 GDWY Structure 60% Subm. to HCAA	1.0d	27-Jan-25 A	27-Jan-25 A	
805	WBS - CCBS - 30% Design - TSA Submittals - Main Terminal		414.0d	13-Sep-23 A	28-Apr-25 A	
806	WBS - CCBS - 30% Design		238.0d	13-Sep-23 A	16-Aug-24 A	
807	WBS - CCBS - 30% - MT Study		77.0d	13-Sep-23 A	3-Jan-24 A	
808	DS-CC-SD-10	CCBS - 30% DD NTP - Main Terminal	1.0d	13-Sep-23 A	13-Sep-23 A	
809	DS-CC-SD-20	Site Visits - Analysis - CCBS 30% MT Study	25.0d	14-Sep-23 A	18-Oct-23 A	
810	DS-CC-SD-30	Site Walk - CCBS 30% MT Study	1.0d	19-Oct-23 A	19-Oct-23 A	
811	DS-CC-SD-40	Document Study Completion - CCBS 30% MT Study	2.0d	20-Oct-23 A	23-Oct-23 A	
812	DS-CC-SD-50	VTC - Internal QA/QC - CCBS 30% MT Study	3.0d	24-Oct-23 A	26-Oct-23 A	
813	DS-CC-SD-60	VTC - Finalize Document - CCBS 30% MT Study	1.0d	27-Oct-23 A	27-Oct-23 A	
814	DS-CC-SD-70	Study QA/QC - CCBS 30% MT Study	5.0d	30-Oct-23 A	3-Nov-23 A	
815	DS-CC-SD-80	Compilation & Final Document - CCBS 30% MT Study	4.0d	6-Nov-23 A	9-Nov-23 A	
816	DS-CC-SD-90	Subm. To HCAA - CCBS 30% MT Study	1.0d	10-Nov-23 A	10-Nov-23 A	
817	DS-CC-SD-100	Review (HCAA) - CCBS 30% MT Study	19.0d	13-Nov-23 A	11-Dec-23 A	
818	DS-CC-SD-110	Final Presentation (HCAA) - CCBS 30% MT Study	1.0d	12-Dec-23 A	12-Dec-23 A	
819	DS-CC-SD-120	Owner Review & Determination - CCBS 30% MT Study	13.0d	13-Dec-23 A	2-Jan-24 A	
820	DS-CC-SD-130	HCAA Determination On CCBS 30% MT Study	1.0d	3-Jan-24 A	3-Jan-24 A	
821	WBS - CCBS - East End Sortation Study NTP		121.0d	11-Jan-24 A	27-Jun-24 A	
822	DS-CC-SD-140	East End Sortation ROM Subm. - East End Sortation Study	1.0d	11-Jan-24 A	11-Jan-24 A	
823	DS-CC-SD-150	NTP - East End Sortation Study	66.0d	16-Jan-24 A	16-Apr-24 A	
824	DS-CC-SD-160	Complete Study - East End Sortation Study	39.0d	17-Apr-24 A	11-Jun-24 A	
825	DS-CC-SD-170	Submit Docs. To HNTB - East End Sortation Study	1.0d	12-Jun-24 A	12-Jun-24 A	
826	DS-CC-SD-180	QA/QC - Start IDR - East End Sortation Study	5.0d	13-Jun-24 A	19-Jun-24 A	
827	DS-CC-SD-190	QA - East End Sortation Study	1.0d	20-Jun-24 A	20-Jun-24 A	
828	DS-CC-SD-200	Submit To HCAA - East End Sortation Study	1.0d	21-Jun-24 A	21-Jun-24 A	
829	DS-CC-SD-210	VTC Owner Presentation (Tentative) - East End Sortation Study	1.0d	27-Jun-24 A	27-Jun-24 A	
830	WBS - CCBS - Develop New BHS Concepts at Main Terminal		35.0d	28-Jun-24 A	16-Aug-24 A	
831	DS-CC-SD-220	Develop Updated Concept (No Single Point of Failure) - New Concept	7.0d	28-Jun-24 A	9-Jul-24 A	
832	DS-CC-SD-230	Conceptual Review Mtg. - HNTB/HP/VTC - New Concept	1.0d	10-Jul-24 A	10-Jul-24 A	
833	DS-CC-SD-240	Update Concepts & Validate Constructability - New Concept	4.0d	11-Jul-24 A	16-Jul-24 A	
834	DS-CC-SD-250	Develop Constraints & Limitations Based On Concepts - New Concept	4.0d	11-Jul-24 A	16-Jul-24 A	
835	DS-CC-SD-260	Mtg. to Review Updated Concepts - HNTB/HP/VTC - New Concept	1.0d	17-Jul-24 A	17-Jul-24 A	
836	DS-CC-SD-270	Develop Preliminary Docs. For Focus Team - New Concept	5.0d	18-Jul-24 A	24-Jul-24 A	
837	DS-CC-SD-280	Preliminary Review Constraints & Limitations with BHS Focus Team - New Conc...	1.0d	25-Jul-24 A	25-Jul-24 A	
838	DS-CC-SD-290	Incorporate New Concept Feedback From HCAA - New Concept	3.0d	26-Jul-24 A	30-Jul-24 A	
839	DS-CC-SD-300	Complete New Concept Study - New Concept	4.0d	26-Jul-24 A	31-Jul-24 A	
840	DS-CC-SD-310	Submit Docs. To HNTB - New Concept	1.0d	1-Aug-24 A	1-Aug-24 A	

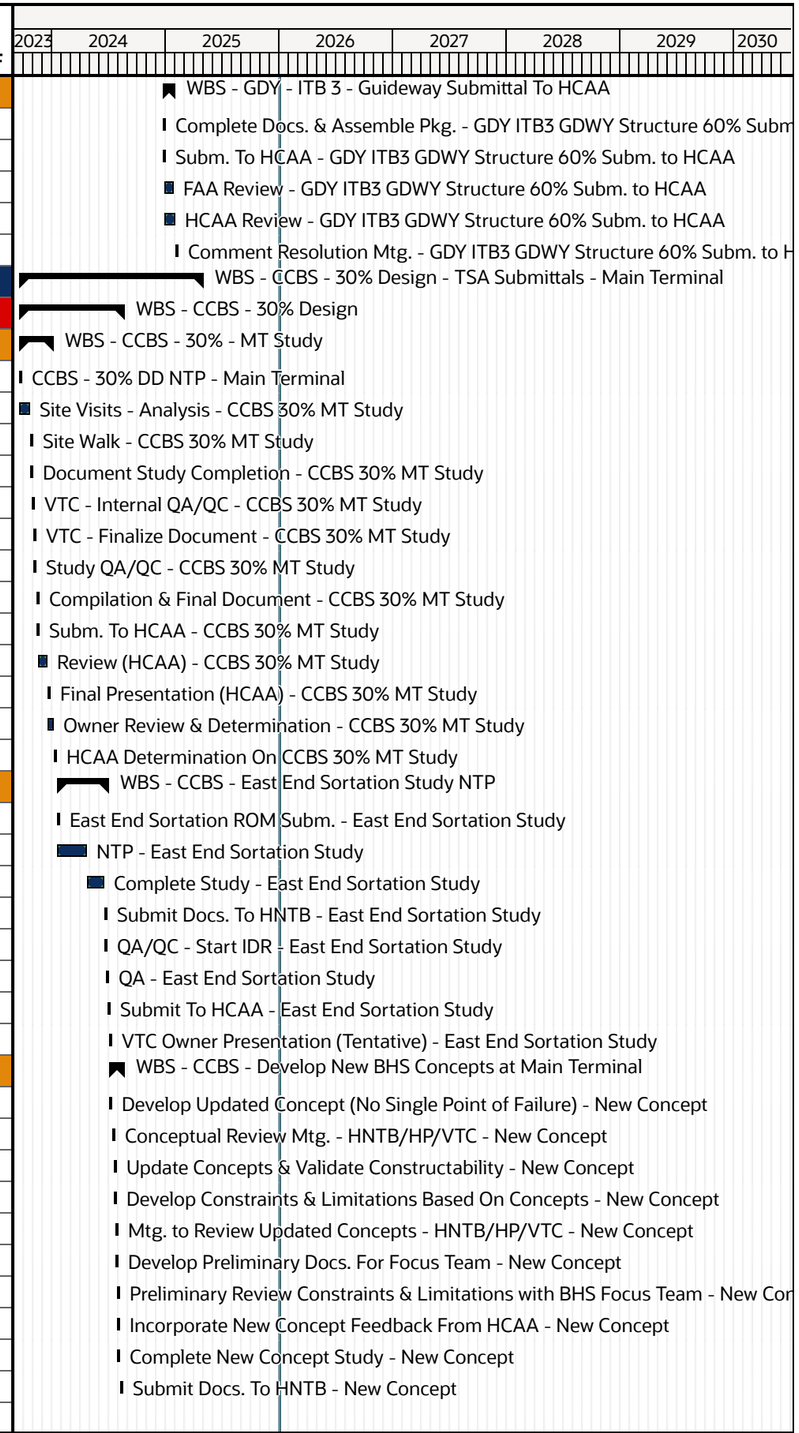


	ID	Name	Dur	Start	Finish	TF
841	DS-CC-SD-320	QA/QC - Start IDR - New Concept	3.0d	2-Aug-24 A	6-Aug-24 A	
842	DS-CC-SD-330	QA - New Concept	1.0d	7-Aug-24 A	7-Aug-24 A	
843	DS-CC-SD-340	Resubmit to HCAA - New Concept	1.0d	8-Aug-24 A	8-Aug-24 A	
844	DS-CC-SD-350	HCAA Review & Presentation - New Concept	5.0d	9-Aug-24 A	15-Aug-24 A	
845	DS-CC-SD-360	Decision on East End Sortation Study - New Concept	1.0d	16-Aug-24 A	16-Aug-24 A	
846	WBS - CCBS - Airside E Optimization		193.0d	24-May-24 A	26-Feb-25 A	
847	DS-AE-SD-10	Proposal Subm. - Airside E Optimization	1.0d	24-May-24 A	24-May-24 A	
848	DS-AE-SD-20	HCAA Proposal Comments Returned 6/17/24 - Airside E Optimization	14.0d	28-May-24 A	17-Jun-24 A	
849	DS-AE-SD-30	Revised Proposal - Airside E Optimization	10.0d	18-Jun-24 A	1-Jul-24 A	
850	DS-AE-SD-40	Submitted Revised Proposal To HP - Airside E Optimization	1.0d	2-Jul-24 A	2-Jul-24 A	
851	DS-AE-SD-50	Rev. 3 Submission To HCAA - Airside E Optimization	1.0d	3-Jul-24 A	3-Jul-24 A	
852	DS-AE-SD-60	HCAA Review Of Rev. 3 - Airside E Optimization	12.0d	8-Jul-24 A	23-Jul-24 A	
853	DS-AE-SD-70	Rescinded to Rev. 3 From HCAA - Airside E Optimization	1.0d	23-Jul-24 A	23-Jul-24 A	
854	DS-AE-SD-80	HNTB Develop & Submit Rev. 4 (CE021) To HP - Airside E Optimization	38.0d	24-Jul-24 A	16-Sep-24 A	
855	DS-AE-SD-90	HP Review & Submit Rev. 4 (CE021) To HCAA - Airside E Optimization	7.0d	17-Sep-24 A	25-Sep-24 A	
856	DS-AE-SD-100	HCAA Review of Rev. 4 (CE021) - Airside E Optimization	105.0d	26-Sep-24 A	25-Feb-25 A	
857	DS-AE-SD-110	Airside E Optimization NTP - Airside E Optimization	1.0d	26-Feb-25 A	26-Feb-25 A	
858	WBS - CCBS - TSA Submittals - VTC		141.0d	4-Jan-24 A	19-Jul-24 A	
859	WBS - CCBS - TSA - Predesign CBIS		85.0d	4-Jan-24 A	1-May-24 A	
860	DS-CC-SD-1000	Develop Predesign CBIS - CCBS TSA	46.0d	4-Jan-24 A	7-Mar-24 A	
861	DS-CC-SD-1010	VTC DQC - CCBS TSA	6.0d	11-Mar-24 A	18-Mar-24 A	
862	DS-CC-SD-1020	HCAA Review - CCBS TSA	1.0d	19-Mar-24 A	19-Mar-24 A	
863	DS-CC-SD-1030	IDR/CCBS Predesign Document-Incorporated Comments - CCBS TSA	7.0d	20-Mar-24 A	28-Mar-24 A	
864	DS-CC-SD-1040	Predesign CBIS To TSA - CCBS TSA	4.0d	29-Mar-24 A	3-Apr-24 A	
865	DS-CC-SD-1050	Review by TSA - CCBS TSA	20.0d	4-Apr-24 A	1-May-24 A	
866	WBS - CCBS - TSA - Predesign Revision		56.0d	2-May-24 A	19-Jul-24 A	
867	DS-CC-SD-1070	VTC Resubmit to HNTB - CCBS TSA	11.0d	2-May-24 A	16-May-24 A	
868	DS-CC-SD-1080	HCAA Feedback - CCBS TSA	4.0d	17-May-24 A	22-May-24 A	
869	DS-CC-SD-1090	QA/QC Bluebeam Session - CCBS TSA	4.0d	17-May-24 A	22-May-24 A	
870	DS-CC-SD-1100	HNTB/HP VTC Review Of HCAA Comments - CCBS TSA	2.0d	23-May-24 A	24-May-24 A	
871	DS-CC-SD-1110	VTC to Respond to BB Session & HCAA Comments - CCBS TSA	5.0d	23-May-24 A	30-May-24 A	
872	DS-CC-SD-1120	Back Check Comments From HCAA & BB - CCBS TSA	1.0d	31-May-24 A	31-May-24 A	
873	DS-CC-SD-1130	QA HNTB On Process - CCBS TSA	1.0d	3-Jun-24 A	3-Jun-24 A	
874	DS-CC-SD-1140	Mtg. With HCAA - Validate Document - CCBS TSA	1.0d	4-Jun-24 A	4-Jun-24 A	
875	DS-CC-SD-1150	Final Corrections - CCBS TSA	1.0d	5-Jun-24 A	5-Jun-24 A	
876	DS-CC-SD-1160	ReSubm. to TSA - CCBS TSA	1.0d	6-Jun-24 A	6-Jun-24 A	
877	DS-CC-SD-1170	TSA Review - CCBS TSA	10.0d	7-Jun-24 A	20-Jun-24 A	
878	DS-CC-SD-1200	TSA Review Mtg. - CCBS TSA	9.0d	21-Jun-24 A	3-Jul-24 A	
879	DS-CC-SD-1210	TSA Predesign Approval - CCBS TSA	2.0d	5-Jul-24 A	8-Jul-24 A	
880	DS-CC-SD-1990	TSA (CLOSE GAP) - CCBS TSA	9.0d	9-Jul-24 A	19-Jul-24 A	
881	WBS - CCBS - Consultant Change - BNP		196.0d	22-Jul-24 A	28-Apr-25 A	
882	DS-CC-SD-1220	Notice To VTC - Stop work	1.0d	22-Jul-24 A	22-Jul-24 A	

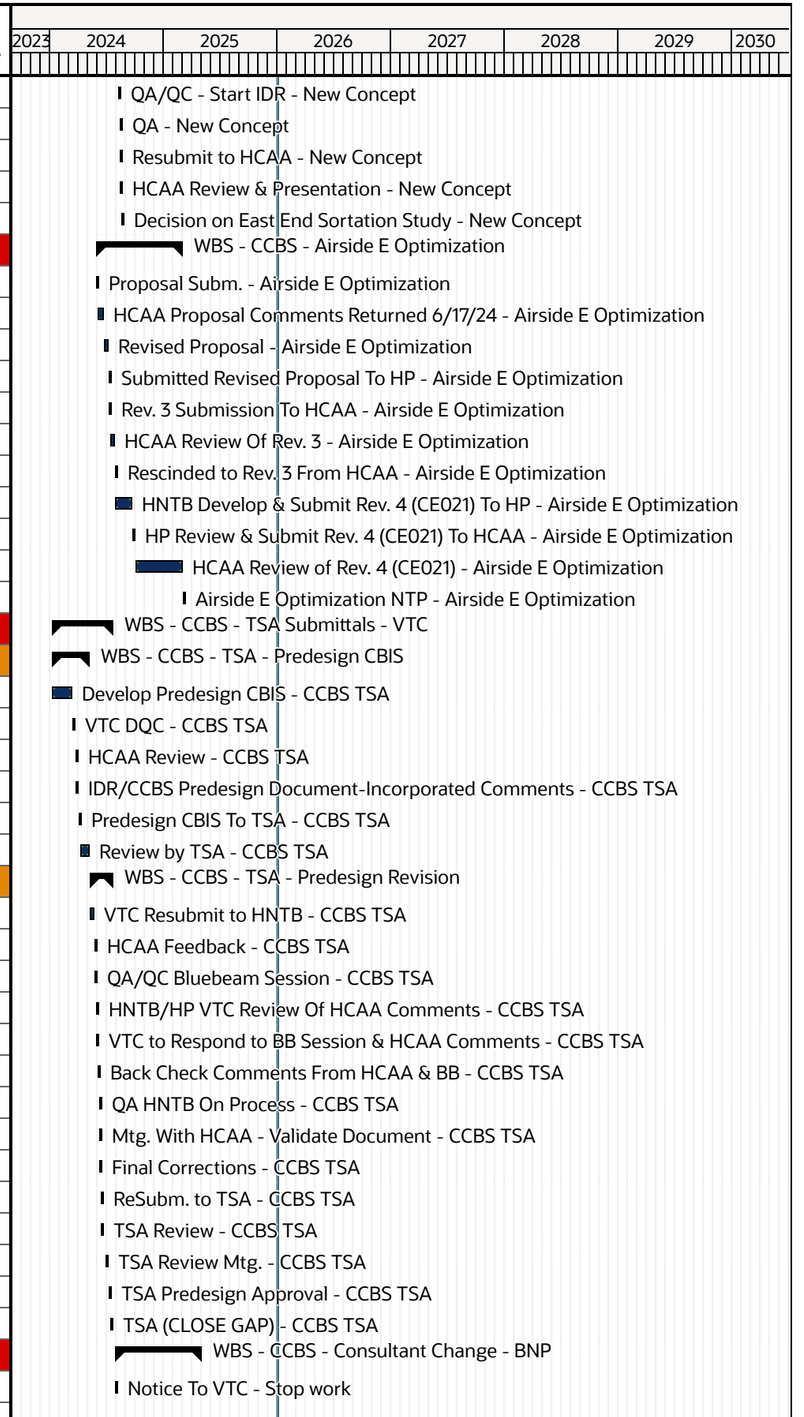


	ID	Name	Dur	Start	Finish	TF
883	DS-CC-SD-1230	BNP Engagement	5.0d	23-Jul-24 A	29-Jul-24 A	
884	DS-CC-SD-1300	BNP Contract Negotiations	30.0d	30-Jul-24 A	10-Sep-24 A	
885	DS-CC-SD-1400	BNP Executed Agreement	1.0d	11-Sep-24 A	11-Sep-24 A	
886	WBS - CCBS - TSA Predesign BNP		29.0d	12-Sep-24 A	22-Oct-24 A	
887	WBS - CCBS - TSA Predesign - BNP Documents		29.0d	12-Sep-24 A	22-Oct-24 A	
888	DS-CC-SD-1410	CCBS Coord. & Review Exist. Docs. - CCBS TSA Predesign	10.0d	12-Sep-24 A	25-Sep-24 A	
889	DS-CC-SD-1510	Concept Design & CCBS Model - CCBS TSA Predesign	8.0d	26-Sep-24 A	7-Oct-24 A	
890	DS-CC-SD-1520	Mtg. With TSA - Question Predesign Subm. Requirements - CCBS TSA Predesign	1.0d	8-Oct-24 A	8-Oct-24 A	
891	DS-CC-SD-1530	Submit Analysis of Predesign to TSA Per Mtg. - CCBS TSA Predesign	1.0d	8-Oct-24 A	8-Oct-24 A	
892	DS-CC-SD-1540	TSA Comments Received - CCBS TSA Predesign	3.0d	9-Oct-24 A	11-Oct-24 A	
893	DS-CC-SD-1550	BNP Response to Comments - CCBS TSA Predesign	3.0d	14-Oct-24 A	16-Oct-24 A	
894	DS-CC-SD-1560	TSA Acceptance of Predesign Analysis - CCBS TSA Predesign	4.0d	17-Oct-24 A	22-Oct-24 A	
895	WBS - CCBS - TSA Schematic Design		64.0d	22-Oct-24 A	23-Jan-25 A	
896	WBS - CCBS - TSA Schematic Design Documents		21.0d	22-Oct-24 A	19-Nov-24 A	
897	DS-CC-SD-1570	TSA Acceptance of Predesign Analysis - CCBS TSA DD	1.0d	22-Oct-24 A	22-Oct-24 A	
898	DS-CC-SD-1580	CCBS Schematic Design & Development - CCBS TSA DD	10.0d	23-Oct-24 A	5-Nov-24 A	
899	DS-CC-SD-1590	Incorporate TSA Comments - CCBS TSA DD	7.0d	23-Oct-24 A	31-Oct-24 A	
900	DS-CC-SD-1600	Complete Schematic Design - CCBS TSA DD	10.0d	6-Nov-24 A	19-Nov-24 A	
901	WBS - CCBS - TSA Schematic Design QA/QC		20.0d	20-Nov-24 A	19-Dec-24 A	
902	DS-CC-SD-1640	BNP Internal Review - DQC - CCBS TSA Schematic Design	4.0d	20-Nov-24 A	26-Nov-24 A	
903	DS-CC-SD-1660	IDR - CCBS Predesign Document - Incorporate Comments - Include HCAA - CC...	5.0d	27-Nov-24 A	4-Dec-24 A	
904	DS-CC-SD-1690	Prepare Docs. For HCAA Review - CCBS TSA Schematic Design	3.0d	9-Dec-24 A	11-Dec-24 A	
905	DS-CC-SD-1710	HCAA Review - CCBS TSA Schematic Design	1.0d	12-Dec-24 A	12-Dec-24 A	
906	DS-CC-SD-1720	HCAA Comment Resolution - CCBS TSA Schematic Design	1.0d	13-Dec-24 A	13-Dec-24 A	
907	DS-CC-SD-1740	Pick Up Comments - CCBS TSA Schematic Design	2.0d	16-Dec-24 A	17-Dec-24 A	
908	DS-CC-SD-1760	Visual Check - CCBS TSA Schematic Design	1.0d	18-Dec-24 A	18-Dec-24 A	
909	DS-CC-SD-1780	QA - CCBS TSA Schematic Design	1.0d	19-Dec-24 A	19-Dec-24 A	
910	WBS - CCBS - TSA Schematic Design Submittal		23.0d	20-Dec-24 A	23-Jan-25 A	
911	DS-CC-SD-1800	Docs. Complete & Assemble Pkg. - TSA SD Subm.	1.0d	20-Dec-24 A	20-Dec-24 A	
912	DS-CC-SD-1810	CBIS Schematic Design to TSA - TSA SD Subm.	1.0d	23-Dec-24 A	23-Dec-24 A	
913	DS-CC-SD-1820	SD Review - TSA SD Subm.	21.0d	24-Dec-24 A	23-Jan-25 A	
914	WBS - CCBS - TSA 30% Design - 3rd Submittal		88.0d	24-Dec-24 A	28-Apr-25 A	
915	WBS - CCBS - TSA 30% Design - 3rd Submittal		33.0d	24-Dec-24 A	10-Feb-25 A	
916	DS-CC-SD-1830	Design Development - TSA 30% Design	31.0d	24-Dec-24 A	6-Feb-25 A	
917	DS-CC-SD-1840	MEP / FP Coord. & Docs. - TSA 30% Design	31.0d	24-Dec-24 A	6-Feb-25 A	
918	DS-CC-SD-1850	Incorporate TSA Comments. - TSA 30% Design	10.0d	24-Jan-25 A	6-Feb-25 A	
919	DS-CC-SD-1860	Complete Docs. - TSA 30% Design	2.0d	7-Feb-25 A	10-Feb-25 A	
920	WBS - CCBS - TSA 30% Design QA/QC		23.0d	11-Feb-25 A	13-Mar-25 A	
921	DS-CC-SD-1870	BNP Internal Review - DQC - TSA 30% Design	5.0d	11-Feb-25 A	17-Feb-25 A	
922	DS-CC-SD-1880	IDR Predesign Document - Incorporate Comments - Include HCAA - TSA 30% ...	5.0d	18-Feb-25 A	24-Feb-25 A	
923	DS-CC-SD-1890	Prepare Docs. for HCAA Review - TSA 30% Design	5.0d	25-Feb-25 A	3-Mar-25 A	
924	DS-CC-SD-1900	HCAA Over the Shoulder Review - TSA 30% Design	1.0d	4-Mar-25 A	4-Mar-25 A	




	ID	Name	Dur	Start	Finish	TF
925	DS-CC-SD-1910	HCAA Comment Resolution - TSA 30% Design	1.0d	5-Mar-25 A	5-Mar-25 A	
926	DS-CC-SD-1920	Pick Up Comments - TSA 30% Design	2.0d	6-Mar-25 A	7-Mar-25 A	
927	DS-CC-SD-1930	Visual Check QA/QC - TSA 30% Design	2.0d	10-Mar-25 A	11-Mar-25 A	
928	DS-CC-SD-1940	CCBS - TSA 30% Design	2.0d	12-Mar-25 A	13-Mar-25 A	
929	WBS - CCBS - TSA 30% Design Submittal		32.0d	14-Mar-25 A	28-Apr-25 A	
930	DS-CC-SD-1950	Sub. Complete & Assemble Docs. - TSA 30% Design	1.0d	14-Mar-25 A	14-Mar-25 A	
931	DS-CC-SD-1960	CBIS Deliverable Due - TSA 30% Design	1.0d	17-Mar-25 A	17-Mar-25 A	
932	DS-CC-SD-1970	Review - TSA 30% Design	30.0d	18-Mar-25 A	28-Apr-25 A	
933	WBS - CCBS - 70% Design - Main Terminal		142.0d	17-Mar-25 A	3-Oct-25 A	
934	DS-CC-DD-90	CCBS 70% DD NTP - Main Terminal	0.0d	17-Mar-25 A		
935	WBS - CCBS - Main Terminal (70% BHS to TSA) Design Documents		86.0d	17-Mar-25 A	16-Jul-25 A	
936	DS-CC-DD-150	Architectural Design - Coord. (70% Subm. to TSA)	52.0d	17-Mar-25 A	28-May-25 A	
937	DS-CC-DD-160	Struct. Design - Coord. (70% Subm. to TSA)	52.0d	17-Mar-25 A	28-May-25 A	
938	DS-CC-DD-100	CCBS Coord. Assist with BNP & Contractor - Development to TSA 70%	57.0d	25-Apr-25 A	16-Jul-25 A	
939	DS-CC-DD-220	Incorporate TSA Comments From 30%	20.0d	25-Apr-25 A	22-May-25 A	
940	WBS - CCBS - Main Terminal (70% BHS to TSA) Review QA/QC		24.0d	17-Jul-25 A	19-Aug-25 A	
941	DS-CC-DD-230	DQC 0 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
942	DS-CC-DD-225	Start QA/QC 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	0.0d	17-Jul-25 A		
943	DS-CC-DD-250	Post to Bluebeam 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	1.0d	29-Jul-25 A	29-Jul-25 A	
944	DS-CC-DD-260	IDR 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
945	DS-CC-DD-300	Visual Check 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
946	DS-CC-DD-270	Prepare Docs. for Over the Shoulder Review 70% Subm. to TSA - CCBS (70% B…	1.0d	14-Aug-25 A	14-Aug-25 A	
947	DS-CC-DD-280	HCAA Over the Shoulder Review 70% Subm. to TSA - CCBS (70% BHS to TSA) …	1.0d	15-Aug-25 A	15-Aug-25 A	
948	DS-CC-DD-310	QA Check 70% Subm. to TSA - CCBS (70% BHS to TSA) Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
949	WBS - CCBS - Main Terminal (70% BHS to TSA) Submittal		32.0d	20-Aug-25 A	3-Oct-25 A	
950	DS-CC-DD-320	Complete Docs. & Assemble Package - CCBS 70% Subm. to TSA	1.0d	20-Aug-25 A	20-Aug-25 A	
951	DS-CC-DD-340	TSA - CBIS 70% Subm. Due - CCBS 70% Subm. to TSA	1.0d	21-Aug-25 A	21-Aug-25 A	
952	DS-CC-DD-360	TSA Review - CCBS 70% Subm. to TSA	20.0d	22-Aug-25 A	19-Sep-25 A	
953	DS-CC-DD-370	Respond to Comments - CCBS 70% Subm. to TSA	5.0d	22-Sep-25 A	26-Sep-25 A	
954	DS-CC-DD-380	Incorporate TSA & HCAA Comments - CCBS 70% Subm. to TSA	4.0d	29-Sep-25 A	3-Oct-25 A	
955	DS-CC-DD-390	Submit HCAA 90% Pkg. (TSA 70%) - CCBS 70% Subm. to TSA	0.0d		3-Oct-25 A	
956	WBS - CCBS - 100% Construction Documents - CCBS Main Terminal		73.0d	21-Aug-25 A	5-Dec-25 A	
957	WBS - CCBS - 100% NTP		1.0d	21-Aug-25 A	21-Aug-25 A	
958	DS-CC-CD-2200	NTP - CCBS Main Terminal CCBS 100% CD	0.0d	21-Aug-25 A	21-Aug-25 A	
959	WBS - CCBS - 100% CCBS Docs to TSA/HCAA		30.0d	22-Aug-25 A	3-Oct-25 A	
960	DS-CC-CD-90	TSA Review - 100% CCBS to TSA	20.0d	22-Aug-25 A	19-Sep-25 A	
961	DS-CC-CD-100	Design - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
962	DS-CC-CD-110	Architectural Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
963	DS-CC-CD-120	MEP Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
964	DS-CC-CD-130	Struct. Coord. - 100% CCBS to TSA	30.0d	22-Aug-25 A	3-Oct-25 A	
965	WBS - CCBS - 100% Review QA/QC (100% CCBS To TSA/HCAA)		17.0d	6-Oct-25 A	28-Oct-25 A	
966	DS-CC-CD-210	DQC - 100% Review QA/QC (100% CCBS To TSA)	5.0d	6-Oct-25 A	10-Oct-25 A	

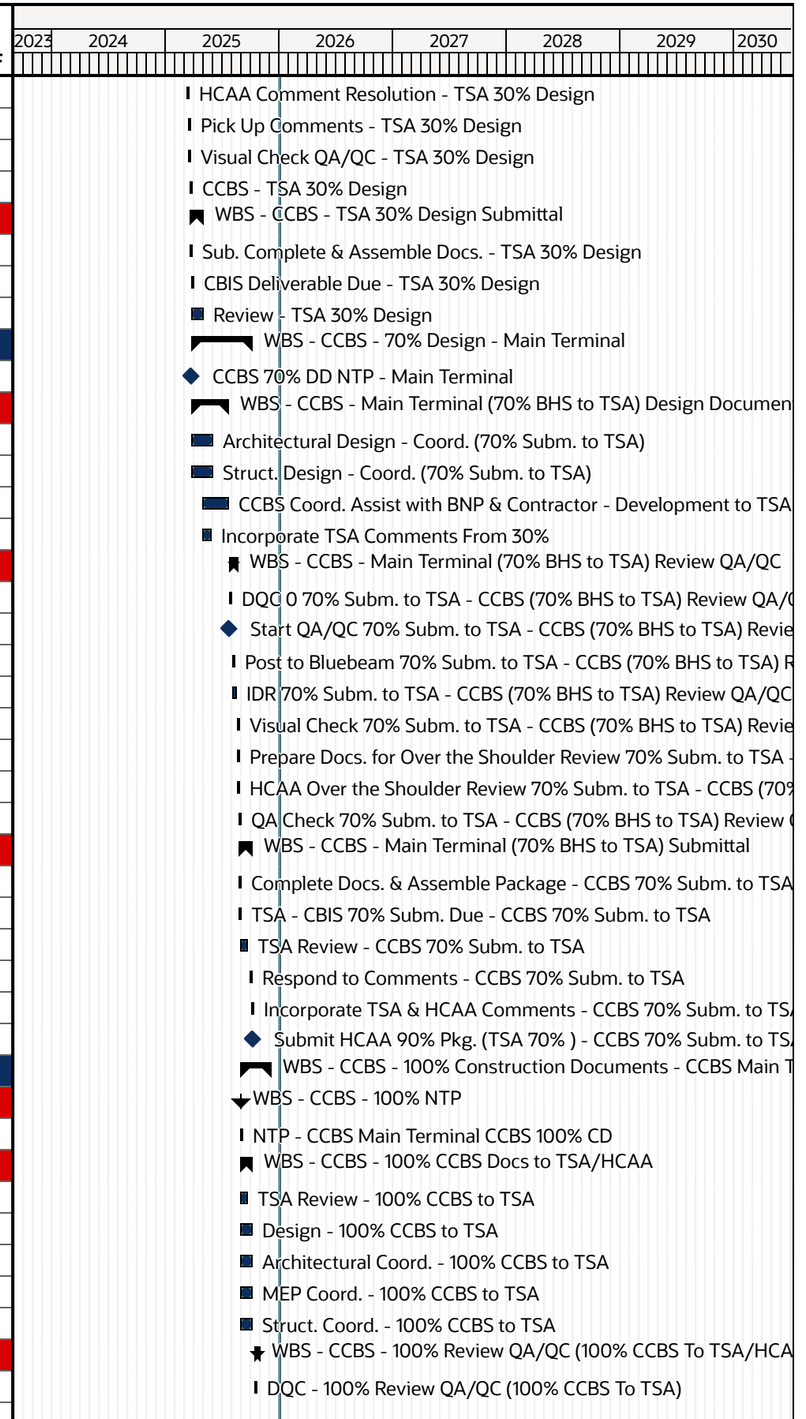


	ID	Name	Dur	Start	Finish	TF
967	DS-CC-CD-220	3rd Party Review - 100% Review QA/QC (100% CCBS To TSA)	5.0d	6-Oct-25 A	10-Oct-25 A	
968	DS-CC-CD-230	Post to Bluebeam - 100% Review QA/QC (100% CCBS To TSA)	1.0d	13-Oct-25 A	13-Oct-25 A	
969	DS-CC-CD-240	IDR - 100% Review QA/QC (100% CCBS To TSA)	8.0d	14-Oct-25 A	23-Oct-25 A	
970	DS-CC-CD-250	Visual Check - 100% Review QA/QC (100% CCBS To TSA)	2.0d	24-Oct-25 A	27-Oct-25 A	
971	DS-CC-CD-260	QA Check - 100% Review QA/QC (100% CCBS To TSA)	1.0d	28-Oct-25 A	28-Oct-25 A	
972	WBS - CCBS - 100% Submittal (100% CCBS To TSA/HCAA)		26.0d	29-Oct-25 A	5-Dec-25 A	
973	DS-CC-CD-270	Complete Docs. & Assemble Pkg. - 100% Submittal (100% CCBS To TSA)	2.0d	29-Oct-25 A	30-Oct-25 A	
974	DS-CC-CD-1240	HCAA - CBIS 100% Subm. Due - 100% Submittal (100% CCBS To TSA)	1.0d	30-Oct-25 A	30-Oct-25 A	
975	DS-CC-CD-290	HCAA Review - 100% Submittal (100% CCBS To TSA)	19.0d	31-Oct-25 A	26-Nov-25 A	
976	DS-CC-CD-285	HNTB to Submit to the City of Tampa (COT) - 100% Submittal (100% CCBS To T…	1.0d	7-Nov-25 A	7-Nov-25 A	
977	DS-CC-CD-2320	Respond to Comments - 100% CCBS	5.0d	1-Dec-25 A	5-Dec-25 A	
978	WBS - BHS - 30% Design Documents - ASD		181.0d	19-Apr-24 A	6-Jan-25 A	
979	WBS - BHS - 30% Design Docs - ASD		92.0d	19-Apr-24 A	27-Aug-24 A	
980	WBS - BHS - 30% Document Start - ASD		68.0d	19-Apr-24 A	24-Jul-24 A	
981	DS-SD-BHS-1060	BHS Schematic Design At Airside D - Start 30%	1.0d	19-Apr-24 A	19-Apr-24 A	
982	DS-SD-BHS-1180	BHS Restart On 30% Airside D Design	1.0d	10-Jun-24 A	10-Jun-24 A	
983	DS-SD-BHS-1190	BHS Revise 30% BOD - ASD	31.0d	11-Jun-24 A	24-Jul-24 A	
984	WBS - BHS Revised BOD Review QA/QC		12.0d	25-Jul-24 A	9-Aug-24 A	
985	DS-SD-BHS-1250	Sr. Technical Review Discipline QC - BHS 30% BOD	3.0d	25-Jul-24 A	29-Jul-24 A	
986	DS-SD-BHS-1260	DQC - Post Docs. - BHS 30% BOD	1.0d	25-Jul-24 A	25-Jul-24 A	
987	DS-SD-BHS-1270	DQC - BHS 30% BOD	2.0d	26-Jul-24 A	29-Jul-24 A	
988	DS-SD-BHS-1290	Post Docs. to Bluebeam Session/IDR Review - BHS 30% BOD	1.0d	30-Jul-24 A	30-Jul-24 A	
989	DS-SD-BHS-1320	Basis of Design QA/QC - IDR - BHS 30% BOD	5.0d	31-Jul-24 A	6-Aug-24 A	
990	DS-SD-BHS-1330	Docs. Complete - Visual Check - BHS 30% BOD	2.0d	7-Aug-24 A	8-Aug-24 A	
991	DS-SD-BHS-1340	QAR Check - BHS 30% BOD	1.0d	9-Aug-24 A	9-Aug-24 A	
992	WBS - BHS ASD - Revised BOD Submittal To HCAA		12.0d	12-Aug-24 A	27-Aug-24 A	
993	DS-SD-BHS-1350	Assemble Pkg. - BHS 30% BOD	1.0d	12-Aug-24 A	12-Aug-24 A	
994	DS-SD-BHS-1360	Submit Revised BOD Report Due To HCAA - BHS 30% BOD	1.0d	13-Aug-24 A	13-Aug-24 A	
995	DS-SD-BHS-1370	HCAA Review - BHS 30% BOD	10.0d	14-Aug-24 A	27-Aug-24 A	
996	WBS - BHS - 30% Design Documents Per Revised BOD - BNP		115.0d	23-Jul-24 A	6-Jan-25 A	
997	WBS - BHS - 30% Design Documents - ASD - BNP		84.0d	23-Jul-24 A	18-Nov-24 A	
998	DS-SD-BHS-1240	BNP Kickoff & Coord. - BHS 30% DD	4.0d	23-Jul-24 A	26-Jul-24 A	
999	DS-SD-BHS-1280	BNP Concept Design Understanding Scope - BHS 30% DD	1.0d	29-Jul-24 A	29-Jul-24 A	
1000	DS-SD-BHS-1310	BNP Validation & Concept Study - BHS 30% DD	21.0d	30-Jul-24 A	27-Aug-24 A	
1001	DS-SD-BHS-1380	BHS Focus Team Mtg. 8/28/24 - BHS 30% DD	1.0d	28-Aug-24 A	28-Aug-24 A	
1002	DS-SD-BHS-1390	Program Docs. for Ricondo Mtg. - BHS 30% DD	9.0d	29-Aug-24 A	11-Sep-24 A	
1003	DS-SD-BHS-1420	BNP / Ricondo Centralized Baggage Mtg. 9/12/24 - BHS 30% DD	1.0d	12-Sep-24 A	12-Sep-24 A	
1004	DS-SD-BHS-1430	CBIS Design Update Mtg. 9/13/24 - BHS 30% DD	1.0d	13-Sep-24 A	13-Sep-24 A	
1005	DS-SD-BHS-1440	Architectural Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1006	DS-SD-BHS-1450	Struct. Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1007	DS-SD-BHS-1460	MEP Coord. - BHS 30% DD	25.0d	16-Sep-24 A	18-Oct-24 A	
1008	DS-SD-BHS-1470	Concept Plans & Model Development - BHS 30% DD	4.0d	16-Sep-24 A	19-Sep-24 A	

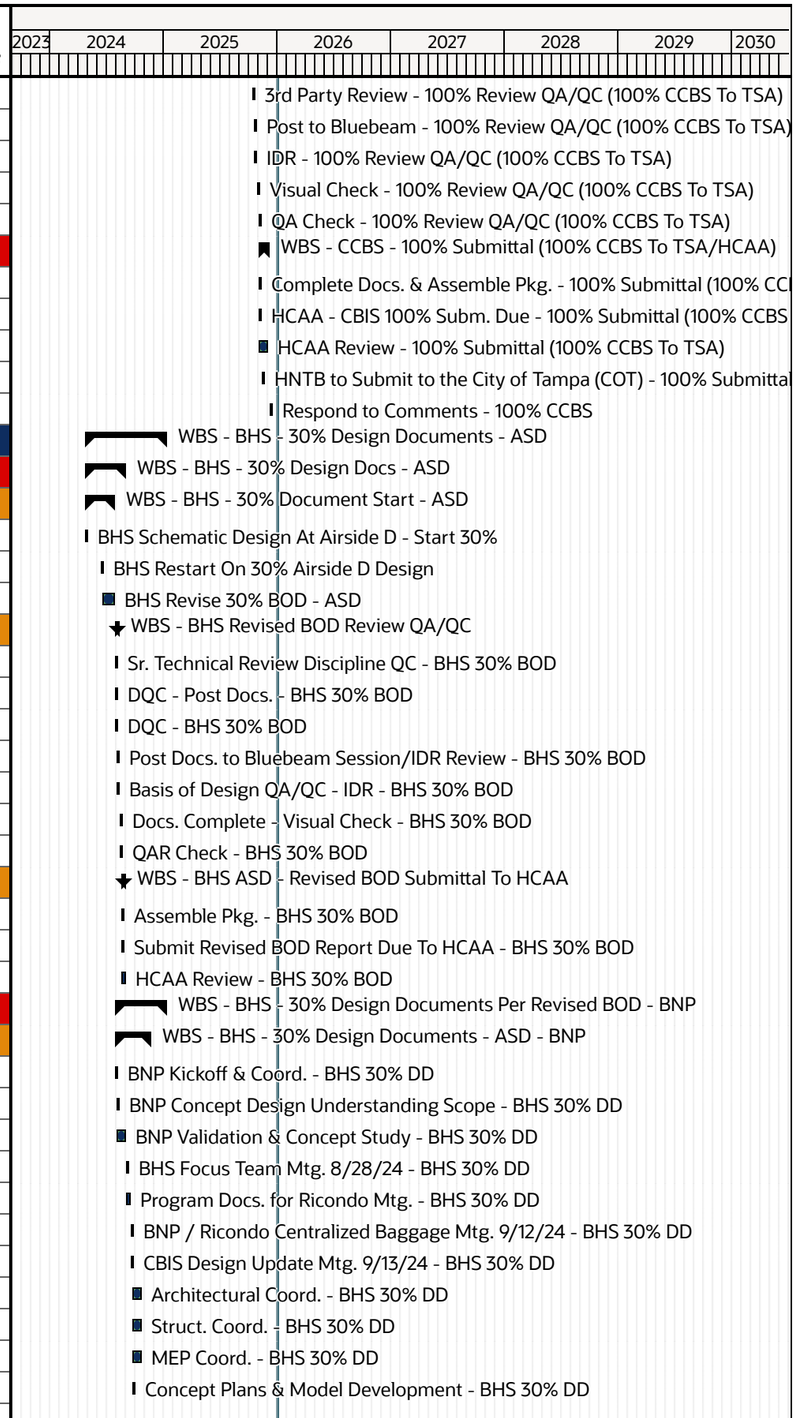


	ID	Name	Dur	Start	Finish	TF
1009	DS-SD-BHS-1480	TSA Monthly Check in & BHS Focus Team Mtg. 9/20/24 - BHS 30% DD	1.0d	20-Sep-24 A	20-Sep-24 A	
1010	DS-SD-BHS-1500	Design Docs. - BHS 30% DD	41.0d	23-Sep-24 A	18-Nov-24 A	
1011	WBS - Preliminary Cost Estimate To HP For 30% Package		35.0d	20-Sep-24 A	7-Nov-24 A	
1012	DS-SD-BHS-1490	Basis Of Design & 30% Cost Estimate Document - BHS 30%	34.0d	20-Sep-24 A	6-Nov-24 A	
1013	DS-SD-BHS-1610	Cost Estimate Pkg. To HP - BHS 30%	1.0d	7-Nov-24 A	7-Nov-24 A	
1014	WBS - BHS - 30% Review QA/QC - ASD		19.0d	19-Nov-24 A	17-Dec-24 A	
1015	DS-SD-BHS-1620	DQC - BHS 30% Review QA/QC	4.0d	19-Nov-24 A	25-Nov-24 A	
1016	DS-SD-BHS-1630	Sr. Technical Review - BHS 30% Review QA/QC	4.0d	19-Nov-24 A	25-Nov-24 A	
1017	DS-SD-BHS-1650	Post to Bluebeam - BHS 30% Review QA/QC	1.0d	26-Nov-24 A	26-Nov-24 A	
1018	DS-SD-BHS-1680	IDR - BHS 30% Review QA/QC	10.0d	27-Nov-24 A	11-Dec-24 A	
1019	DS-SD-BHS-1700	Visual Check - BHS 30% Review QA/QC	2.0d	12-Dec-24 A	13-Dec-24 A	
1020	DS-SD-BHS-1730	QA Check - BHS 30% Review QA/QC	2.0d	16-Dec-24 A	17-Dec-24 A	
1021	WBS - BHS - 30% Submittal To HCAA - ASD		12.0d	18-Dec-24 A	6-Jan-25 A	
1022	DS-SD-BHS-1750	Docs. Complete & Assemble Pkg. - BHS 30% Subm.	1.0d	18-Dec-24 A	18-Dec-24 A	
1023	DS-SD-BHS-1770	Airside D Subm. Due To HCAA - BHS 30% Subm.	1.0d	19-Dec-24 A	19-Dec-24 A	
1024	DS-SD-BHS-1790	HCAA Review - BHS 30% Subm.	10.0d	20-Dec-24 A	6-Jan-25 A	
1025	WBS - BHS - 60% Design Development - ASD		109.0d	19-Dec-24 A	22-May-25 A	
1026	DS-DD-BHS-10	BHS 60% DD ASD - NTP	1.0d	19-Dec-24 A	19-Dec-24 A	
1027	WBS - BHS - 60% Design Development - ASD Documents		77.0d	20-Dec-24 A	9-Apr-25 A	
1028	DS-DD-BHS-20	Develop ASD Docs. - BHS 60% Design Docs.	56.0d	20-Dec-24 A	11-Mar-25 A	
1029	DS-DD-BHS-25	Ascend Passenger Experience Extension - BHS 60% Design Docs.	20.0d	12-Mar-25 A	8-Apr-25 A	
1030	DS-DD-BHS-30	Complete & Assemble ASD Docs. - BHS 60% Design Docs.	1.0d	9-Apr-25 A	9-Apr-25 A	
1031	WBS - BHS - 60% Preliminary Cost Estimate To HP For 60% Package		2.0d	10-Apr-25 A	11-Apr-25 A	
1032	DS-DD-BHS-40	BHS 60% Basis of Design & 60% Cost Estimate Document	1.0d	10-Apr-25 A	10-Apr-25 A	
1033	DS-DD-BHS-50	BHS 60% Cost Estimate Pkg. to HP	1.0d	11-Apr-25 A	11-Apr-25 A	
1034	WBS - BHS - 60% Review QA/QC - ASD		19.0d	10-Apr-25 A	6-May-25 A	
1035	DS-DD-BHS-70	Sr. Technical Review - BHS 60% Review QA/QC ASD	5.0d	10-Apr-25 A	16-Apr-25 A	
1036	DS-DD-BHS-55	Start QA/QC - BHS 60% Review QA/QC ASD	0.0d	10-Apr-25 A		
1037	DS-DD-BHS-60	DQC - BHS 60% Review QA/QC ASD	3.0d	14-Apr-25 A	16-Apr-25 A	
1038	DS-DD-BHS-110	Post to Bluebeam Session - BHS 60% Review QA/QC ASD	1.0d	17-Apr-25 A	17-Apr-25 A	
1039	DS-DD-BHS-120	IDR - BHS 60% Review QA/QC ASD	9.0d	18-Apr-25 A	30-Apr-25 A	
1040	DS-DD-BHS-170	Visual Check - BHS 60% Review QA/QC ASD	2.0d	1-May-25 A	2-May-25 A	
1041	DS-DD-BHS-180	QA Check - BHS 60% Review QA/QC ASD	2.0d	5-May-25 A	6-May-25 A	
1042	WBS - BHS - 60% Submittal To Owner - ASD		12.0d	7-May-25 A	22-May-25 A	
1043	DS-DD-BHS-190	Docs. Complete & Assemble Pkg. - BHS 60% Subm.	1.0d	7-May-25 A	7-May-25 A	
1044	DS-DD-BHS-200	ASD - Subm. Due to HCAA - BHS 60% Subm.	1.0d	8-May-25 A	8-May-25 A	
1045	DS-DD-BHS-210	HCAA Review - BHS 60% Subm.	10.0d	9-May-25 A	22-May-25 A	
1046	WBS - BHS - 90% Design Development - ASD		84.0d	8-May-25 A	5-Sep-25 A	
1047	DS-CD-BHS-10	BHS 90% CD NTP - ASD	1.0d	8-May-25 A	8-May-25 A	
1048	WBS - BHS - 90% Design Development - ASD Documents		47.0d	9-May-25 A	16-Jul-25 A	
1049	DS-CD-BHS-20	ASD - Design Docs. - BHS 90% DD	46.0d	9-May-25 A	15-Jul-25 A	
1050	DS-CD-BHS-30	Complete & Assemble ASD Docs. - BHS 90% DD	1.0d	16-Jul-25 A	16-Jul-25 A	

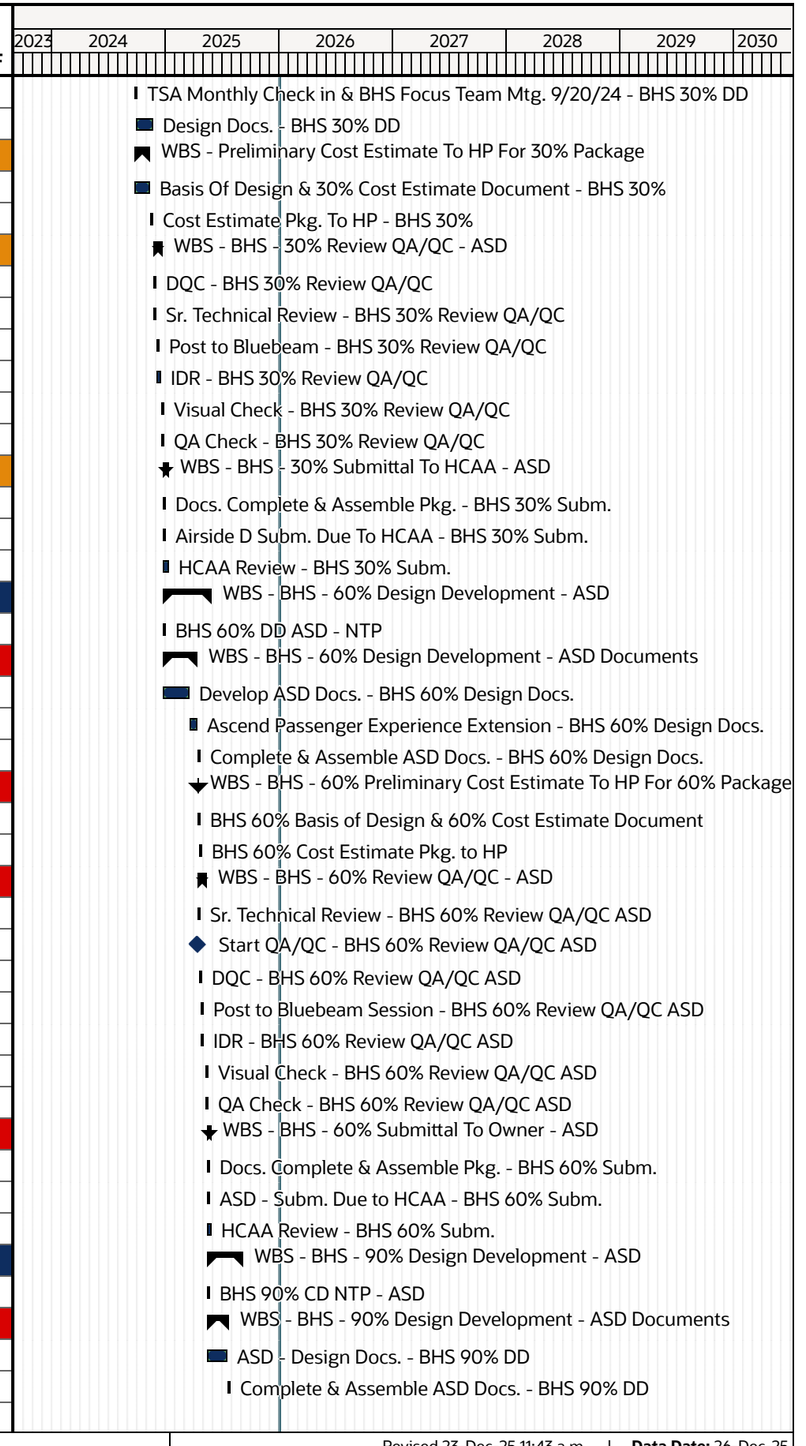


ID	Name	Dur	Start	Finish	TF
1051	WBS - Preliminary Cost Estimate To HP For 90% Package	1.0d	17-Jul-25 A	17-Jul-25 A	
1052	DS-CD-BHS-40 BHS Basis Of Design & 90% Cost Estimate Document	1.0d	17-Jul-25 A	17-Jul-25 A	
1053	DS-CD-BHS-50 BHS 90% Cost Estimate Pkg. To HP	1.0d	17-Jul-25 A	17-Jul-25 A	
1054	WBS - BHS - 90% Review QA/QC - ASD	24.0d	17-Jul-25 A	19-Aug-25 A	
1055	DS-CD-BHS-60 DQC - BHS ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
1056	DS-CD-BHS-70 Sr. Technical Review - BHS ASD 90% Review QA/QC	8.0d	17-Jul-25 A	28-Jul-25 A	
1057	DS-CD-BHS-140 Post to Bluebeam Session - BHS ASD 90% Review QA/QC	1.0d	29-Jul-25 A	29-Jul-25 A	
1058	DS-CD-BHS-150 IDR - BHS ASD 90% Review QA/QC	11.0d	30-Jul-25 A	13-Aug-25 A	
1059	DS-CD-BHS-160 Visual Check - BHS ASD 90% Review QA/QC	2.0d	14-Aug-25 A	15-Aug-25 A	
1060	DS-CD-BHS-170 QA Check - BHS ASD 90% Review QA/QC	2.0d	18-Aug-25 A	19-Aug-25 A	
1061	WBS - BHS - 90% Submittal To HCAA - ASD	11.0d	20-Aug-25 A	5-Sep-25 A	
1062	DS-CD-BHS-180 Docs. Complete & Assemble Pkg. - BHS ASD 90% Subm.	0.0d	20-Aug-25 A	20-Aug-25 A	
1063	DS-CD-BHS-190 Due To HCAA - BHS ASD 90% Subm.	1.0d	21-Aug-25 A	21-Aug-25 A	
1064	DS-CD-BHS-200 HCAA Review - BHS ASD 90% Subm.	10.0d	22-Aug-25 A	5-Sep-25 A	
1065	WBS - BHS - 100% Design Development - ASD	78.0d	21-Aug-25 A	11-Dec-25 A	
1066	DS-CD-BHS-1100 BHS 100% CD NTP - ASD	0.0d	21-Aug-25 A		
1067	WBS - BHS - 100% Design Development - ASD Documents	31.0d	21-Aug-25 A	3-Oct-25 A	
1068	DS-CD-BHS-1110 ASD - Design Docs. - BHS 100% DD	30.0d	21-Aug-25 A	2-Oct-25 A	
1069	DS-CD-BHS-1130 ASD - Complete & Assemble Docs. - BHS 100% DD	1.0d	3-Oct-25 A	3-Oct-25 A	
1070	WBS - BHS - 100% Preliminary Cost Estimate to HP For 100% Package - ASD	30.0d	25-Aug-25 A	6-Oct-25 A	
1071	DS-CD-BHS-1120 BHS 100% Cost Estimate Pkg. To HP	29.0d	25-Aug-25 A	3-Oct-25 A	
1072	DS-CD-BHS-1140 Basis Of Design & BHS 100% Cost Estimate Document	1.0d	6-Oct-25 A	6-Oct-25 A	
1073	WBS - BHS - 100% Review QA/QC - ASD	17.0d	6-Oct-25 A	28-Oct-25 A	
1074	DS-CD-BHS-1150 DQC - BHS 100% Review QA/QC ASD	5.0d	6-Oct-25 A	10-Oct-25 A	
1075	DS-CD-BHS-1160 Technical Review - BHS 100% Review QA/QC ASD	5.0d	6-Oct-25 A	10-Oct-25 A	
1076	DS-CD-BHS-1170 Post to Bluebeam Session - BHS 100% Review QA/QC ASD	1.0d	13-Oct-25 A	13-Oct-25 A	
1077	DS-CD-BHS-1180 IDR - BHS 100% Review QA/QC ASD	8.0d	14-Oct-25 A	23-Oct-25 A	
1078	DS-CD-BHS-1190 Visual Check - BHS 100% Review QA/QC ASD	2.0d	24-Oct-25 A	27-Oct-25 A	
1079	DS-CD-BHS-1200 QA Check - BHS 100% Review QA/QC ASD	1.0d	28-Oct-25 A	28-Oct-25 A	
1080	WBS - BHS - 100% Submittal To HCAA - ASD	30.0d	29-Oct-25 A	11-Dec-25 A	
1081	DS-CD-BHS-1210 Docs. Complete & Assemble Pkg. - BHS 100% Subm. to HCAA	1.0d	29-Oct-25 A	29-Oct-25 A	
1082	DS-CD-BHS-1220 Subm. Due to HCAA - BHS 100% Subm. to HCAA	1.0d	30-Oct-25 A	30-Oct-25 A	
1083	DS-CD-BHS-1230 Owner Review - 100% BHS Submittal	10.0d	26-Nov-25 A	11-Dec-25 A	
1084	WBS - ITB's - 30%	77.0d	8-Jul-24 A	23-Oct-24 A	
1085	WBS - APN - ITB 1 - 30% Site Utilities, Paving, Fueling	69.0d	18-Jul-24 A	23-Oct-24 A	
1086	WBS - APN - ITB 1 - 30% Site Design Documents	52.0d	18-Jul-24 A	30-Sep-24 A	
1087	DS-SD-ITB1-AP-10 Site Civil Paving Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1088	DS-SD-ITB1-AP-20 Site Civil Airfield LTNG Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1089	DS-SD-ITB1-AP-30 Site Civil Drainage Design - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1090	DS-SD-ITB1-AP-40 Site Civil Hydrant Fueling Design ITB1 30% Site Utilities - APN - ITB1 30% DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1091	DS-SD-ITB1-AP-50 Preliminary Set to HP For Cost Estimating - APN - ITB1 30% DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1092	WBS - APN - ITB 1 - 30% QA/QC	10.0d	16-Sep-24 A	27-Sep-24 A	

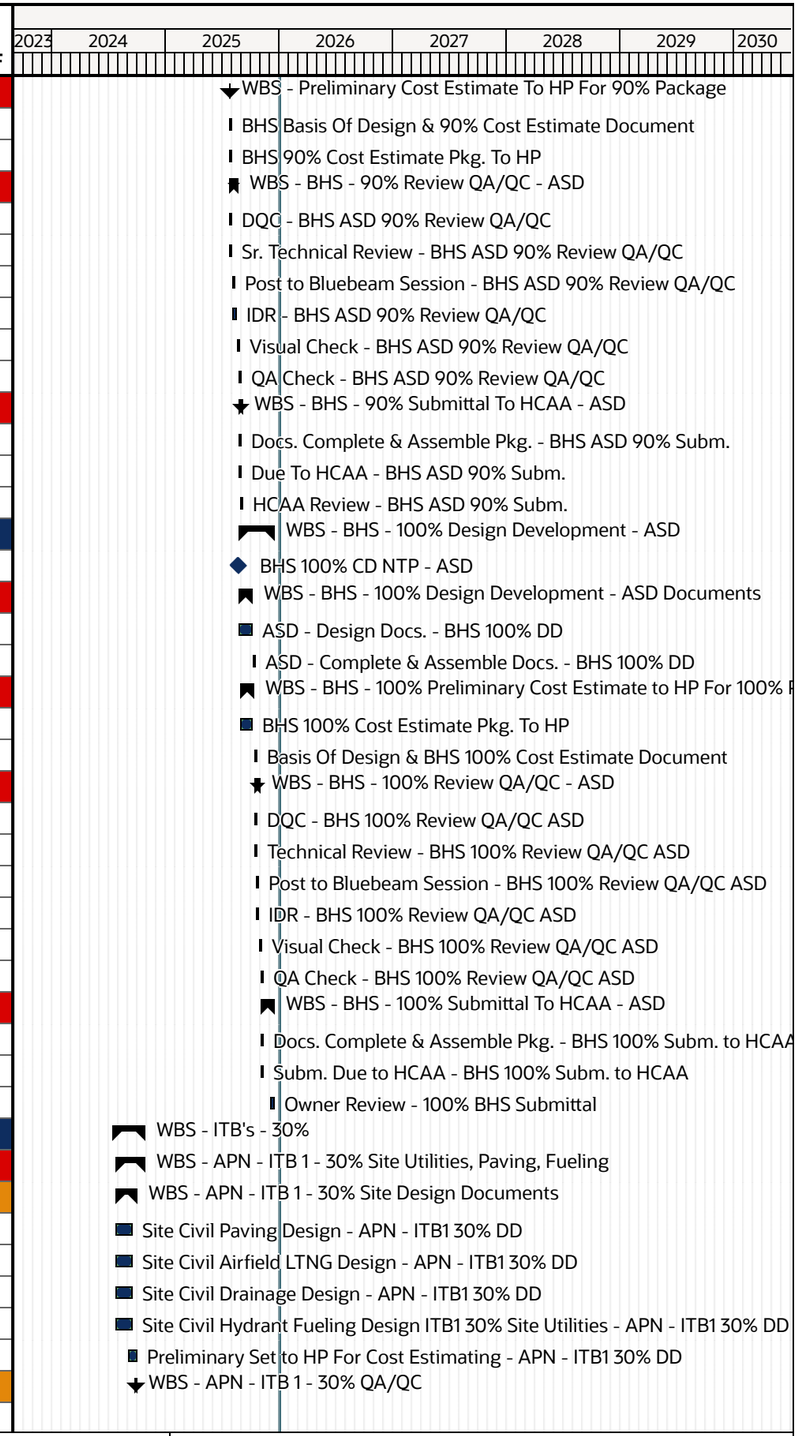

ID	Name	Dur	Start	Finish	TF
1093	DQC - APN - ITB1 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1094	Sr. Technical Review - APN - ITB1 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1095	IDR - APN - ITB1 30% QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1096	Site Utilities, Paving & Fueling Visual Check - APN - ITB1 30% QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1097	Site Utilities, Paving & Fueling QA Check - APN - ITB1 30% QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1098	WBS - APN - ITB 1 - 30% Submittal To HCAA	18.0d	30-Sep-24 A	23-Oct-24 A	
1099	Docs. Complete & Assemble Pkg. - APN - ITB1 30% Subm. QA/QC	1.0d	30-Sep-24 A	30-Sep-24 A	
1100	Due To HCAA - APN - ITB1 30% Subm. QA/QC	1.0d	1-Oct-24 A	1-Oct-24 A	
1101	HCAA Review - APN - ITB1 30% Subm. QA/QC	10.0d	2-Oct-24 A	15-Oct-24 A	
1102	Comment Resolution Mtg. - APN - ITB1 30% Subm. QA/QC	1.0d	23-Oct-24 A	23-Oct-24 A	
1103	WBS - ASD - ITB 2 - 30% PBB Design	69.0d	18-Jul-24 A	23-Oct-24 A	
1104	WBS - ASD - ITB 2 - 30% PBB Design Documents	52.0d	18-Jul-24 A	30-Sep-24 A	
1105	Architectural Design - ASD ITB 2 30% PBB DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1106	Struct. Design - ASD ITB 2 30% PBB DD	41.0d	18-Jul-24 A	13-Sep-24 A	
1107	Preliminary Set To HP For Cost Estimating - ASD ITB 2 30% PBB DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1108	WBS - ASD - ITB 2 - 30% QA/QC	10.0d	16-Sep-24 A	27-Sep-24 A	
1109	DQC - ASD ITB 2 30% PBB QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1110	Sr. Technical Review - ASD ITB 2 30% PBB QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1111	IDR - ASD ITB 2 30% PBB QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1112	Visual Check - ASD ITB 2 30% PBB QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1113	QA Check - ASD ITB 2 30% PBB QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1114	WBS - ASD - ITB 2 - 30% Submittal To HCAA	18.0d	30-Sep-24 A	23-Oct-24 A	
1115	Docs. Complete & Assemble Pkg. - ASD ITB 2 30% Subm.	1.0d	30-Sep-24 A	30-Sep-24 A	
1116	Due To HCAA - ASD ITB 2 30% Subm.	1.0d	1-Oct-24 A	1-Oct-24 A	
1117	HCAA Review - ASD ITB 2 30% Subm.	10.0d	2-Oct-24 A	15-Oct-24 A	
1118	Comment Resolution Mtg. - ASD ITB 2 30% Subm.	1.0d	23-Oct-24 A	23-Oct-24 A	
1119	WBS - GDY - ITB 3 - 30% Guideway	77.0d	8-Jul-24 A	23-Oct-24 A	
1120	WBS - GDY - ITB 3 - 30% Guideway Design Documents	60.0d	8-Jul-24 A	30-Sep-24 A	
1121	Architectural Design - GDY ITB3 30% DD	49.0d	8-Jul-24 A	13-Sep-24 A	
1122	Struct. Design - GDY ITB3 30% DD	49.0d	8-Jul-24 A	13-Sep-24 A	
1123	Preliminary Set to HP For Cost Estimating - GDY ITB3 30% DD	22.0d	29-Aug-24 A	30-Sep-24 A	
1124	WBS - GDY - ITB 3 - 30% QA/QC	10.0d	16-Sep-24 A	27-Sep-24 A	
1125	DQC - GDY ITB3 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1126	Sr. Technical Review - GDY ITB3 30% QA/QC	3.0d	16-Sep-24 A	18-Sep-24 A	
1127	IDR - GDY ITB3 30% QA/QC	5.0d	19-Sep-24 A	25-Sep-24 A	
1128	Visual Check - GDY ITB3 30% QA/QC	1.0d	26-Sep-24 A	26-Sep-24 A	
1129	QA Check - GDY ITB3 30% QA/QC	1.0d	27-Sep-24 A	27-Sep-24 A	
1130	WBS - GDY - ITB 3 - 30% Submittal To HCAA	18.0d	30-Sep-24 A	23-Oct-24 A	
1131	Docs. Complete & Assemble Pkg. - GDY ITB3 30% Subm.	1.0d	30-Sep-24 A	30-Sep-24 A	
1132	Due To HCAA - GDY ITB3 30% Subm.	1.0d	1-Oct-24 A	1-Oct-24 A	
1133	HCAA Review - GDY ITB3 30% Subm.	10.0d	2-Oct-24 A	15-Oct-24 A	
1134	Comment Resolution Mtg. - GDY ITB3 30% Subm.	1.0d	23-Oct-24 A	23-Oct-24 A	

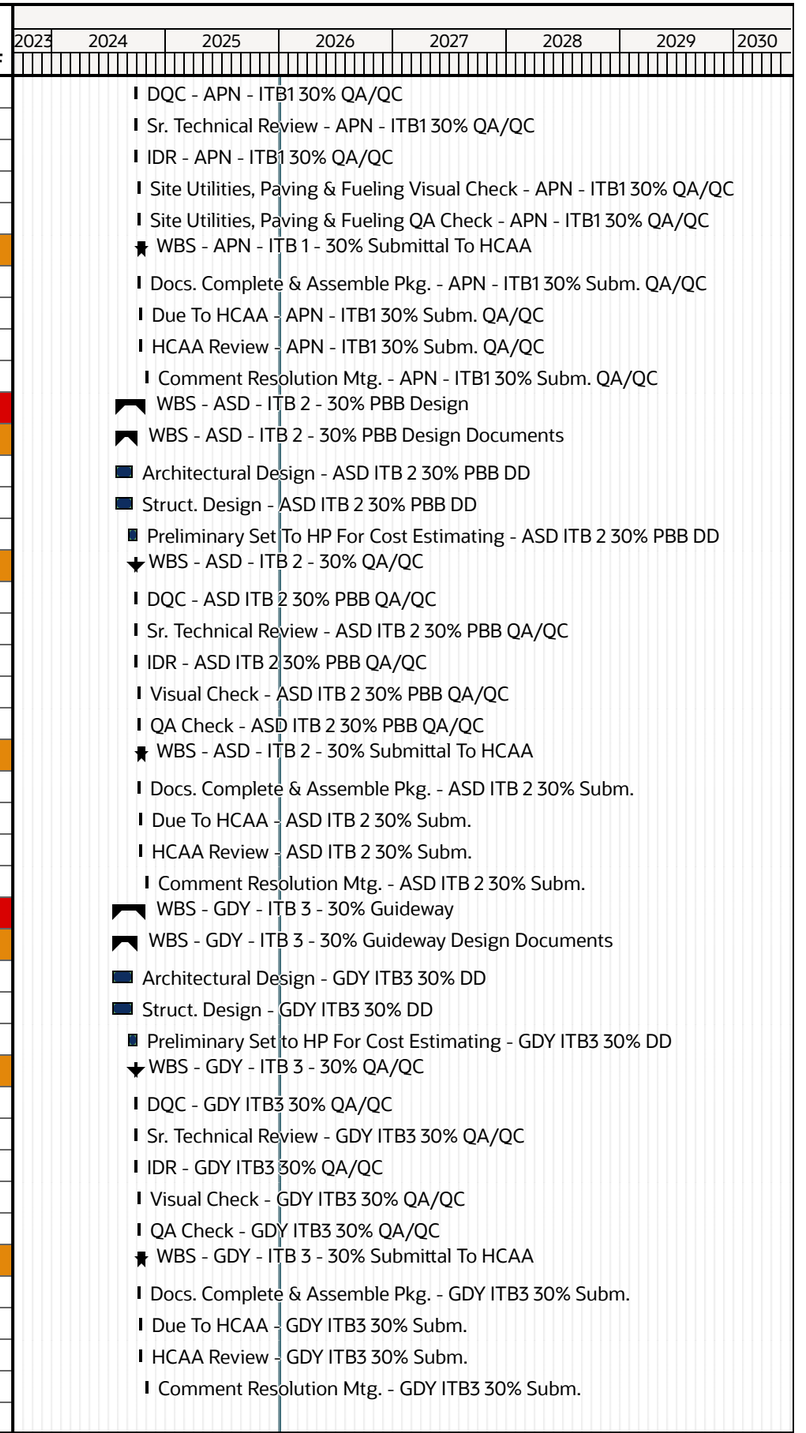


ID	Name	Dur	Start	Finish	TF
1135	WBS - ITB's - IFB/90% Submittal	87.0d	23-Dec-24 A	24-Apr-25 A	
1136	WBS - APN - ITB 1 - 90% - Paving - Hydrant Fueling	72.0d	23-Dec-24 A	3-Apr-25 A	
1137	WBS - APN - ITB 1 - 90% - Design Documents	61.0d	23-Dec-24 A	19-Mar-25 A	
1138	DS-CD-ITB1-AP-1120 — Civil - Design Docs. - APN - ITB1 90% Paving /Hydrant Fueling	40.0d	23-Dec-24 A	18-Feb-25 A	
1139	DS-CD-ITB1-AP-10 — Paving Design - Final Paving Decision ASD vs. ITB - APN - ITB1 90% Paving /H…	7.0d	17-Jan-25 A	27-Jan-25 A	
1140	DS-CD-ITB1-AP-20 — Incorporate Comments ITB1 90% - APN - ITB1 90% Paving /Hydrant Fueling	16.0d	17-Jan-25 A	7-Feb-25 A	
1141	DS-CD-ITB1-AP-1130 — Civil Focus Team Coord. Mtg. - No Comments After 2.12.25 - APN - ITB1 90% …	3.0d	10-Feb-25 A	12-Feb-25 A	
1142	DS-CD-ITB1-AP-1160 — Finalize Design Docs. - APN - ITB1 90% Paving /Hydrant Fueling	11.0d	13-Feb-25 A	27-Feb-25 A	
1143	DS-CD-ITB1-AP-40 — Preliminary Set To HP For Cost Estimating - APN - ITB1 90% Paving /Hydrant F…	22.0d	18-Feb-25 A	19-Mar-25 A	
1144	DS-CD-ITB1-AP-30 — P&D Provides Procurement with Front End Inf. - APN - ITB1 90% Paving /Hydra…	0.0d	25-Feb-25 A	25-Feb-25 A	
1145	DS-CD-ITB1-AP-1140 — Solicitation Docs. (Front End) - APN - ITB1 90% Paving /Hydrant Fueling	15.0d	26-Feb-25 A	18-Mar-25 A	
1146	DS-CD-ITB1-AP-1150 — Solicitation Docs. To Legal - APN - ITB1 90% Paving /Hydrant Fueling	1.0d	19-Mar-25 A	19-Mar-25 A	
1147	WBS - APN - ITB 1 - 90% - Review QA/QC	13.0d	28-Feb-25 A	18-Mar-25 A	
1148	DS-CD-ITB1-AP-50 — DQC - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	28-Feb-25 A	6-Mar-25 A	
1149	DS-CD-ITB1-AP-60 — Sr. Technical Review - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	28-Feb-25 A	6-Mar-25 A	
1150	DS-CD-ITB1-AP-1170 — Start QA/QC - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	0.0d	28-Feb-25 A		
1151	DS-CD-ITB1-AP-70 — IDR - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	5.0d	7-Mar-25 A	13-Mar-25 A	
1152	DS-CD-ITB1-AP-80 — Visual Check - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	2.0d	14-Mar-25 A	17-Mar-25 A	
1153	DS-CD-ITB1-AP-90 — QA Check - APN - ITB1 90% Paving /Hydrant Fueling Review QA/QC	1.0d	18-Mar-25 A	18-Mar-25 A	
1154	WBS - APN - ITB 1 - 90% - Submittal To HCAA	12.0d	19-Mar-25 A	3-Apr-25 A	
1155	DS-CD-ITB1-AP-100 — Complete Docs. & Assemble Pkg. - APN - ITB1 90% Paving /Hydrant Fueling S…	1.0d	19-Mar-25 A	19-Mar-25 A	
1156	DS-CD-ITB1-AP-110 — Bid/Permit Subm. To HCAA - APN - ITB1 90% Paving /Hydrant Fueling Subm. t…	1.0d	20-Mar-25 A	20-Mar-25 A	
1157	DS-CD-ITB1-AP-120 — HCAA Review - APN - ITB1 90% Paving /Hydrant Fueling Subm. to HCAA	10.0d	21-Mar-25 A	3-Apr-25 A	
1158	DS-CD-ITB1-AP-1180 — Solicitation Docs. Posted for Bid - APN - ITB1 90% Paving /Hydrant Fueling Su…	1.0d	21-Mar-25 A	21-Mar-25 A	
1159	WBS - ASD - ITB 2 - 90% - PBB Design	74.0d	13-Jan-25 A	24-Apr-25 A	
1160	WBS - ASD - ITB 2 - 90% - PBB Design Documents	63.0d	13-Jan-25 A	9-Apr-25 A	
1161	DS-CD-ITB2-PB-10 — Architectural Design Coord. - ASD ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1162	DS-CD-ITB2-PB-20 — ASD - ITB 2 90% PBB Dsg. Docs. - Civil Coord. - ASD - ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1163	DS-CD-ITB2-PB-30 — Utility Coord. - ASD ITB 2 90% PBB Dsg. Docs.	28.0d	13-Jan-25 A	19-Feb-25 A	
1164	DS-CD-ITB2-PB-1150 — Focus Team Coord. Mtg. - ASD ITB 2 90% PBB Dsg. Docs.	10.0d	20-Feb-25 A	5-Mar-25 A	
1165	DS-CD-ITB2-PB-1160 — Front End Information & Project Description Development - ASD ITB 2 90% PB…	9.0d	6-Mar-25 A	18-Mar-25 A	
1166	DS-CD-ITB2-PB-1200 — Finalize Design Docs. - ASD ITB 2 90% PBB Dsg. Docs.	10.0d	6-Mar-25 A	19-Mar-25 A	
1167	DS-CD-ITB2-PB-40 — Preliminary Set to HP For Cost Estimating - ASD ITB 2 90% PBB Dsg. Docs.	22.0d	11-Mar-25 A	9-Apr-25 A	
1168	DS-CD-ITB2-PB-1170 — P&D Provides Procurement with Front End Information - ASD ITB 2 90% PBB D…	1.0d	19-Mar-25 A	19-Mar-25 A	
1169	DS-CD-ITB2-PB-1180 — Solicitation Docs. (Front End) - ASD ITB 2 90% PBB Dsg. Docs.	15.0d	19-Mar-25 A	8-Apr-25 A	
1170	DS-CD-ITB2-PB-1190 — Solicitation Docs. to Legal - ASD ITB 2 90% PBB Dsg. Docs.	1.0d	9-Apr-25 A	9-Apr-25 A	
1171	WBS - ASD - ITB 2 - 90% - PBB Review QA/QC	14.0d	20-Mar-25 A	8-Apr-25 A	
1172	DS-CD-ITB2-PB-1140 — Start QA/QC - ASD ITB 2 90% PBB Review QA/QC	1.0d	20-Mar-25 A	20-Mar-25 A	
1173	DS-CD-ITB2-PB-50 — DQC - ASD ITB 2 90% PBB Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1174	DS-CD-ITB2-PB-60 — Sr. Technical Review - ASD ITB 2 90% PBB Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1175	DS-CD-ITB2-PB-70 — IDR - ASD ITB 2 90% PBB Review QA/QC	6.0d	28-Mar-25 A	4-Apr-25 A	
1176	DS-CD-ITB2-PB-80 — Visual Check - ASD ITB 2 90% PBB Review QA/QC	1.0d	7-Apr-25 A	7-Apr-25 A	

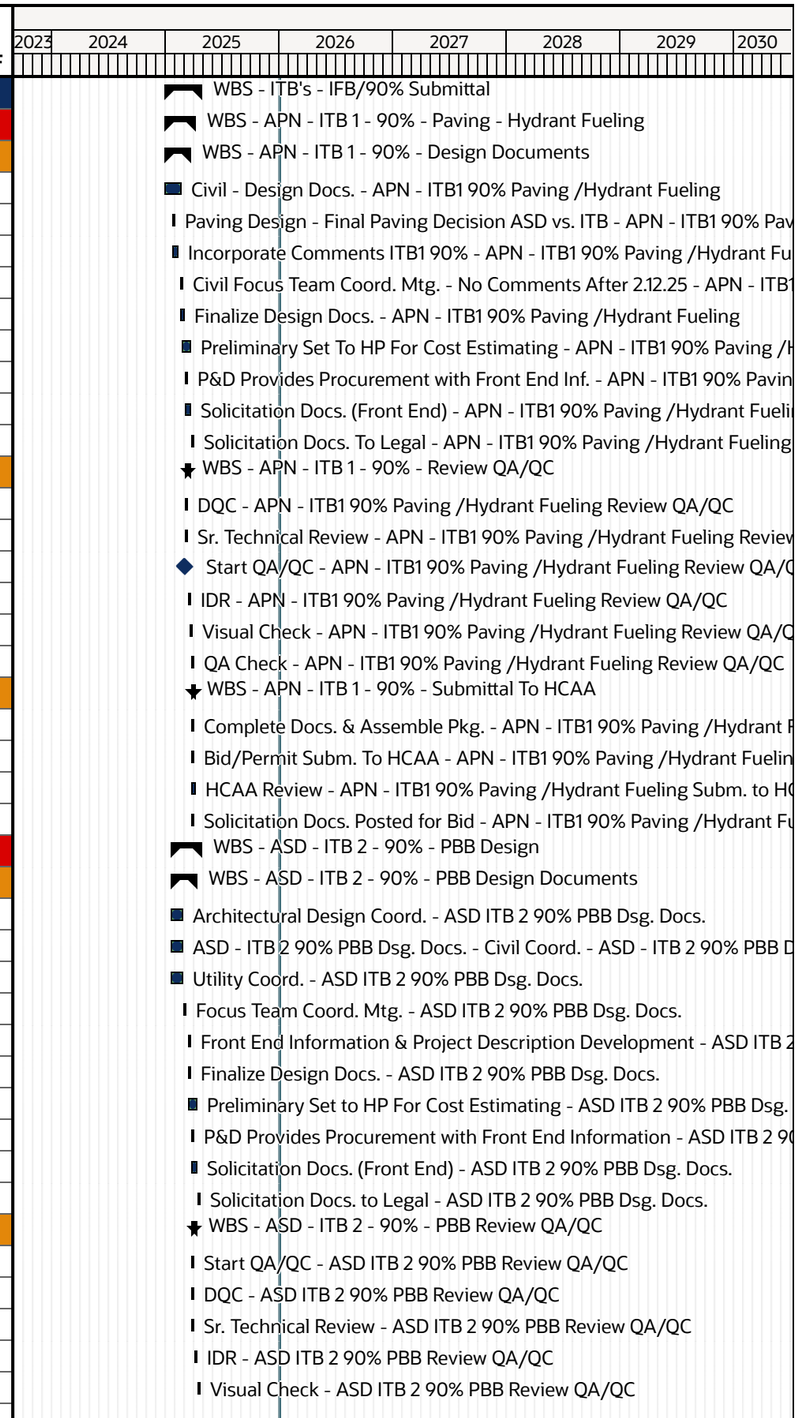


ID	Name	Dur	Start	Finish	TF
1177	DS-CD-ITB2-PB-90	QA Check - ASD ITB 2 90% PBB Review QA/QC	1.0d	8-Apr-25 A	8-Apr-25 A	
1178	WBS - ASD - ITB 2 - 90% - PBB Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
1179	DS-CD-ITB2-PB-100	Complete Docs. & Assemble Pkg. - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
1180	DS-CD-ITB2-PB-110	Subm. to HCAA - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
1181	DS-CD-ITB2-PB-120	HCAA Review- ASD ITB 2 90% PBB Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
1182	DS-CD-ITB2-PB-1130	Solicitation Docs. Posted for Bid - ASD ITB 2 90% PBB Subm. to HCAA	1.0d	16-Apr-25 A	16-Apr-25 A	
1183	WBS - GDY - ITB 3 - 90% - Guideway Structure		87.0d	23-Dec-24 A	24-Apr-25 A	
1184	WBS - GDY - ITB 3 - 90% - Guideway Design Documents		76.0d	23-Dec-24 A	9-Apr-25 A	
1185	DS-CD-ITB3-GS-10	Architectural Coord. & Design - GDY ITB3 90% GDWY Struct. DD	12.0d	23-Dec-24 A	9-Jan-25 A	
1186	DS-CD-ITB3-GS-20	Struct. Design - GDY ITB3 90% GDWY Struct. DD	12.0d	23-Dec-24 A	9-Jan-25 A	
1187	DS-CD-ITB3-GS-1140	Focus Team Coord. Mtg. - GDY ITB3 90% GDWY Struct. DD	13.0d	10-Jan-25 A	28-Jan-25 A	
1188	DS-CD-ITB3-GS-1190	Finalize Design Docs. - GDY ITB3 90% GDWY Struct. DD	36.0d	29-Jan-25 A	19-Mar-25 A	
1189	DS-CD-ITB3-GS-1150	Front End Information & Project Description Development - GDY ITB3 90% GD...	4.0d	30-Jan-25 A	4-Feb-25 A	
1190	DS-CD-ITB3-GS-1160	P&D Provides Procurement with Front End Information - GDY ITB3 90% GDWY ...	1.0d	5-Feb-25 A	5-Feb-25 A	
1191	DS-CD-ITB3-GS-1170	Solicitation Docs. (Front End) - GDY ITB3 90% GDWY Struct. DD	9.0d	6-Feb-25 A	18-Feb-25 A	
1192	DS-CD-ITB3-GS-1180	Solicitation Docs. to Legal - GDY ITB3 90% GDWY Struct. DD	1.0d	19-Feb-25 A	19-Feb-25 A	
1193	DS-CD-ITB3-GS-30	Preliminary Set to HP For Cost Estimating - GDY ITB3 90% GDWY Struct. DD	22.0d	11-Mar-25 A	9-Apr-25 A	
1194	WBS - GDY - ITB 3 - 90% - Guideway Review QA/QC		14.0d	20-Mar-25 A	8-Apr-25 A	
1195	DS-CD-ITB3-GS-1130	Start QA/QC - GDY ITB3 90% GDWY Struct. Review QA/QC	0.0d	20-Mar-25 A		
1196	DS-CD-ITB3-GS-40	DQC - GDY ITB3 90% GDWY Struct. Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1197	DS-CD-ITB3-GS-50	Sr. Technical Review - GDY ITB3 90% GDWY Struct. Review QA/QC	5.0d	21-Mar-25 A	27-Mar-25 A	
1198	DS-CD-ITB3-GS-60	IDR - GDY ITB3 90% GDWY Struct. Review QA/QC	6.0d	28-Mar-25 A	4-Apr-25 A	
1199	DS-CD-ITB3-GS-70	Visual Check - GDY ITB3 90% GDWY Struct. Review QA/QC	1.0d	7-Apr-25 A	7-Apr-25 A	
1200	DS-CD-ITB3-GS-80	QA Check - GDY ITB3 90% GDWY Struct. Review QA/QC	1.0d	8-Apr-25 A	8-Apr-25 A	
1201	WBS - GDY - ITB 3 - 90% - Guideway Submittal To HCAA		12.0d	9-Apr-25 A	24-Apr-25 A	
1202	DS-CD-ITB3-GS-90	Complete Docs. & Assemble Pkg. - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	9-Apr-25 A	9-Apr-25 A	
1203	DS-CD-ITB3-GS-100	Bid/Permit Subm. To HCAA - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	10-Apr-25 A	10-Apr-25 A	
1204	DS-CD-ITB3-GS-110	HCAA Review - GDY ITB3 90% GDWY Struct. Subm. to HCAA	10.0d	11-Apr-25 A	24-Apr-25 A	
1205	DS-CD-ITB3-GS-1120	Solicitation Docs. Posted for Bid - GDY ITB3 90% GDWY Struct. Subm. to HCAA	1.0d	16-Apr-25 A	16-Apr-25 A	
1206	WBS - ITB's - 100% (Addendum Set)		98.0d	21-Mar-25 A	7-Aug-25 A	
1207	WBS - APN - ITB 1 - 100% Paving - Hydrant Fueling (Addendum Set)		54.0d	21-Mar-25 A	5-Jun-25 A	
1208	WBS - APN - ITB 1 - 100% Paving - Design Documents		19.0d	21-Mar-25 A	16-Apr-25 A	
1209	DS-CD-ITB1-AP-1000	Civil - Paving Design - APN - ITB1 - 100% DD Paving (Addendum Set)	15.0d	21-Mar-25 A	10-Apr-25 A	
1210	DS-CD-ITB1-AP-1010	Civil - Hydrant Fueling Design Docs. - APN - ITB1 - 100% DD Paving (Addendu...	15.0d	21-Mar-25 A	10-Apr-25 A	
1211	DS-CD-ITB1-AP-1200	Bid Questions & RFI's - APN - ITB1 - 100% DD Paving (Addendum Set)	9.0d	24-Mar-25 A	3-Apr-25 A	
1212	DS-CD-ITB1-AP-1210	Pre-Bid Conference - APN - ITB1 - 100% DD Paving (Addendum Set)	1.0d	4-Apr-25 A	4-Apr-25 A	
1213	DS-CD-ITB1-AP-1220	Request for Clarification Deadline Complete - APN - ITB1 - 100% DD Paving (A...	0.0d		15-Apr-25 A	
1214	DS-CD-ITB1-AP-1230	Update Plans & Docs. - APN - ITB1 - 100% DD Paving (Addendum Set)	1.0d	16-Apr-25 A	16-Apr-25 A	
1215	DS-CD-ITB1-AP-1290	Final Addendum Posted - APN - ITB1 - 100% DD Paving (Addendum Set)	0.0d		16-Apr-25 A	
1216	WBS - APN - ITB 1 - 100% Paving - Review QA/QC		4.0d	15-Apr-25 A	18-Apr-25 A	
1217	DS-CD-ITB1-AP-1020	Hydrant Fueling - DQC - APN - ITB1 - 100% Paving (Addendum Set) Review QA...	1.0d	15-Apr-25 A	15-Apr-25 A	
1218	DS-CD-ITB1-AP-1030	Sr. Technical Review - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	16-Apr-25 A	16-Apr-25 A	




	ID	Name	Dur	Start	Finish	TF
1219	DS-CD-ITB1-AP-1040	Post to Bluebeam - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	16-Apr-25 A	16-Apr-25 A	
1220	DS-CD-ITB1-AP-1015	Start QA/QC - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	0.0d	16-Apr-25 A		
1221	DS-CD-ITB1-AP-1050	IDR - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	17-Apr-25 A	17-Apr-25 A	
1222	DS-CD-ITB1-AP-1060	Visual Check - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	18-Apr-25 A	18-Apr-25 A	
1223	DS-CD-ITB1-AP-1070	QA Check - APN - ITB1 - 100% Paving (Addendum Set) Review QA/QC	1.0d	18-Apr-25 A	18-Apr-25 A	
1224	WBS - APN - ITB 1 - 100% Paving - Submittal To HCAA		33.0d	21-Apr-25 A	5-Jun-25 A	
1225	DS-CD-ITB1-AP-1080	Complete Docs. & Assemble Pkg. - APN - ITB1 - 100% Paving (Addendum Set) ...	1.0d	21-Apr-25 A	21-Apr-25 A	
1226	DS-CD-ITB1-AP-1090	Subm. To HCAA - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HCAA	1.0d	22-Apr-25 A	22-Apr-25 A	
1227	DS-CD-ITB1-AP-1100	ITB1 Addendum Posted for Solicitation - APN - ITB1 - 100% Paving (Addendu...	4.0d	23-Apr-25 A	28-Apr-25 A	
1228	DS-CD-ITB1-AP-1280	Contractors Bid Due - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HC...	1.0d	29-Apr-25 A	29-Apr-25 A	
1229	DS-CD-ITB1-AP-1110	HCAA Review - APN - ITB1 - 100% Paving (Addendum Set) Subm. to HCAA	5.0d	30-Apr-25 A	6-May-25 A	
1230	DS-CD-ITB1-AP-1115	Notice of Intent to Award - APN - ITB1 - 100% Paving (Addendum Set) Subm. t...	1.0d	7-May-25 A	7-May-25 A	
1231	DS-CD-ITB1-AP-1260	BIL Grant Application Process - APN - ITB1 - 100% Paving (Addendum Set) Sub...	10.0d	8-May-25 A	21-May-25 A	
1232	DS-CD-ITB1-AP-1265	BIL Grant Application Submitted - APN - ITB1 - 100% Paving (Addendum Set) S...	1.0d	22-May-25 A	22-May-25 A	
1233	DS-CD-ITB1-AP-1270	HCAA Board Approval - APN - ITB1 - 100% Paving (Addendum Set) Subm. to H...	1.0d	5-Jun-25 A	5-Jun-25 A	
1234	WBS - ASD - ITB 2 100% PBB Design (Addendum Set)		83.0d	11-Apr-25 A	7-Aug-25 A	
1235	WBS - ASD - ITB 2 100% - PBB Design Documents		22.0d	11-Apr-25 A	12-May-25 A	
1236	DS-CD-ITB2-PB-1000	Architectural Design Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1237	DS-CD-ITB2-PB-1010	Civil Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1238	DS-CD-ITB2-PB-1020	Utility Coord. - ASD ITB 2 - 100% PBB DD	13.0d	11-Apr-25 A	29-Apr-25 A	
1239	DS-CD-ITB2-PB-1210	Bid Questions & RFI's - ASD ITB 2 - 100% PBB DD	9.0d	17-Apr-25 A	29-Apr-25 A	
1240	DS-CD-ITB2-PB-1220	Pre-Bid Conference - ASD ITB 2 - 100% PBB DD	1.0d	30-Apr-25 A	30-Apr-25 A	
1241	DS-CD-ITB2-PB-1225	Contractor Bid Review / Submit Clarifications - ASD ITB 2 - 100% PBB DD	6.0d	1-May-25 A	8-May-25 A	
1242	DS-CD-ITB2-PB-1230	Request for Clarification Deadline - ASD ITB 2 - 100% PBB DD	1.0d	9-May-25 A	9-May-25 A	
1243	DS-CD-ITB2-PB-1240	Update Plans & Docs. - ASD ITB 2 - 100% PBB DD	1.0d	12-May-25 A	12-May-25 A	
1244	WBS - ASD - ITB 2 100% - PBB Review QA/QC		3.0d	13-May-25 A	15-May-25 A	
1245	DS-CD-ITB2-PB-1030	DQC - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1246	DS-CD-ITB2-PB-1040	Sr. Technical Review - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1247	DS-CD-ITB2-PB-1050	Post to Bluebeam - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	13-May-25 A	13-May-25 A	
1248	DS-CD-ITB2-PB-1025	Start QA/QC - ASD ITB 2 - 100% PBB Review QA/QC	0.0d	13-May-25 A		
1249	DS-CD-ITB2-PB-1060	IDR - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	14-May-25 A	14-May-25 A	
1250	DS-CD-ITB2-PB-1070	Visual Check - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	15-May-25 A	15-May-25 A	
1251	DS-CD-ITB2-PB-1080	QA Check - ASD ITB 2 - 100% PBB Review QA/QC	1.0d	15-May-25 A	15-May-25 A	
1252	WBS - ASD - ITB 2 100% - PBB Submittal For Bid		58.0d	16-May-25 A	7-Aug-25 A	
1253	DS-CD-ITB2-PB-1090	Complete Docs. & Assemble Pkg. - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	16-May-25 A	16-May-25 A	
1254	DS-CD-ITB2-PB-1100	Addendum Subm. to HCAA Due - ASD ITB 2 - 100% PBB Subm. for Bid	0.0d	16-May-25 A	16-May-25 A	
1255	DS-CD-ITB2-PB-1110	ITB2 Addendum Posted for Solicitation - ASD ITB 2 - 100% PBB Subm. for Bid	4.0d	19-May-25 A	22-May-25 A	
1256	DS-CD-ITB2-PB-1120	HCAA Review - ASD ITB 2 - 100% PBB Subm. for Bid	10.0d	19-May-25 A	2-Jun-25 A	
1257	DS-CD-ITB2-PB-1260	Contractor Bids Due - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	28-May-25 A	28-May-25 A	
1258	DS-CD-ITB2-PB-1270	Notice of Intent to Award - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	3-Jun-25 A	3-Jun-25 A	
1259	DS-CD-ITB2-PB-1280	BIL Grant Application Submitted - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	4-Jun-25 A	4-Jun-25 A	
1260	DS-CD-ITB2-PB-1290	HCAA Board Approval - ASD ITB 2 - 100% PBB Subm. for Bid	1.0d	7-Aug-25 A	7-Aug-25 A	

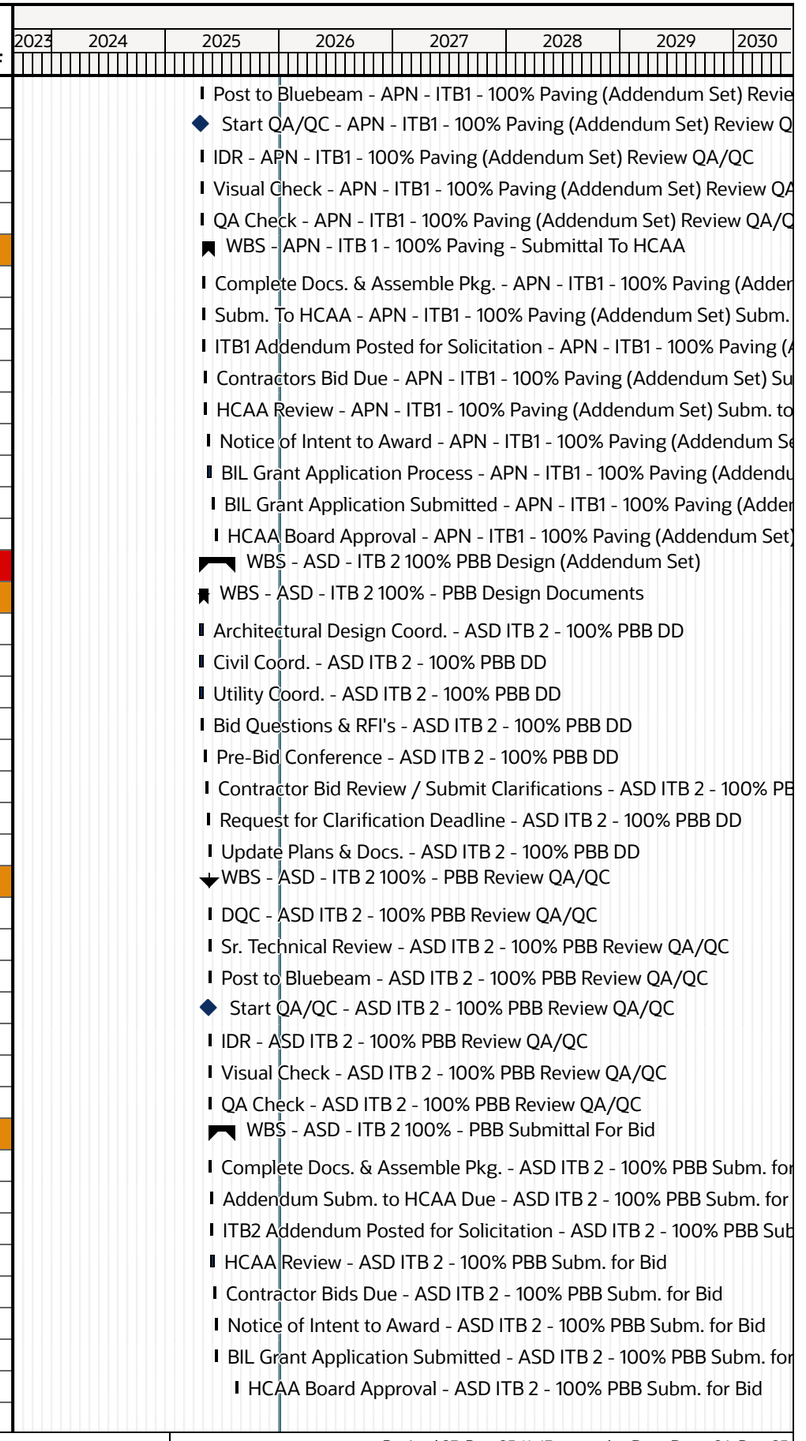


ID	Name	Dur	Start	Finish	TF
1261	WBS - GDY - ITB 3 100% - Guideway Structure (Addendum Set)	83.0d	11-Apr-25 A	7-Aug-25 A	
1262	WBS - GDY - ITB 3 100% - Guideway Design Documents	22.0d	11-Apr-25 A	12-May-25 A	
1263	DS-CD-ITB3-GS-1000 Architectural Coord. & Design - ITB 3 100% DD	15.0d	11-Apr-25 A	1-May-25 A	
1264	DS-CD-ITB3-GS-1010 Structural Design - ITB 3 100% DD	15.0d	11-Apr-25 A	1-May-25 A	
1265	DS-CD-ITB3-GS-1200 Bid Questions & RFI's - ITB 3 100% DD	9.0d	17-Apr-25 A	29-Apr-25 A	
1266	DS-CD-ITB3-GS-1210 Pre-Bid Conference - ITB 3 100% DD	1.0d	30-Apr-25 A	30-Apr-25 A	
1267	DS-CD-ITB3-GS-1215 Contractor Bid Review/ Submit Clarifications - ITB 3 100% DD	6.0d	1-May-25 A	8-May-25 A	
1268	DS-CD-ITB3-GS-1220 Request for Clarification Deadline - ITB 3 100% DD	1.0d	9-May-25 A	9-May-25 A	
1269	DS-CD-ITB3-GS-1230 Update Plans & Docs. - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	
1270	WBS - GDY - ITB 3 100% - Guideway Review QA/QC	3.0d	12-May-25 A	14-May-25 A	
1271	DS-CD-ITB3-GS-1020 DQC - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	
1272	DS-CD-ITB3-GS-1030 Sr. Technical Review - ITB 3 100% DD	1.0d	12-May-25 A	12-May-25 A	
1273	DS-CD-ITB3-GS-1015 Start QA/QC - ITB 3 100% DD	0.0d	12-May-25 A		
1274	DS-CD-ITB3-GS-1040 Post to Bluebeam - ITB 3 100% DD	0.0d		12-May-25 A	
1275	DS-CD-ITB3-GS-1050 IDR - ITB 3 100% DD	1.0d	13-May-25 A	13-May-25 A	
1276	DS-CD-ITB3-GS-1060 Visual Check - ITB 3 100% DD	1.0d	14-May-25 A	14-May-25 A	
1277	DS-CD-ITB3-GS-1070 QA Check - ITB 3 100% DD	1.0d	14-May-25 A	14-May-25 A	
1278	WBS - GDY - ITB 3 100% - Guideway Submittal For Bid	59.0d	15-May-25 A	7-Aug-25 A	
1279	DS-CD-ITB3-GS-1080 ITB 3 Complete Docs. & Assemble Pkg. - 100% Subm. for Bid	1.0d	15-May-25 A	15-May-25 A	
1280	DS-CD-ITB3-GS-1090 ITB 3 Addendum Subm. Due to HCAA - 100% Subm. for Bid	1.0d	16-May-25 A	16-May-25 A	
1281	DS-CD-ITB3-GS-1110 ITB 3 HCAA Review - 100% Subm. for Bid	9.0d	19-May-25 A	30-May-25 A	
1282	DS-CD-ITB3-GS-1095 ITB3 Resubmission of Addendum 3 - 100% Subm. for Bid	1.0d	19-May-25 A	19-May-25 A	
1283	DS-CD-ITB3-GS-1100 ITB3 Addendum Posted for Solicitation - 100% Subm. for Bid	5.0d	20-May-25 A	27-May-25 A	
1284	DS-CD-ITB3-GS-1250 ITB 3 Contractor Bids Due - 100% Subm. for Bid	1.0d	30-May-25 A	30-May-25 A	
1285	DS-CD-ITB3-GS-1260 ITB 3 Notice of Intent to Award - 100% Subm. for Bid	1.0d	2-Jun-25 A	2-Jun-25 A	
1286	DS-CD-ITB3-GS-1270 ITB 3 BIL Grant Application Submitted - 100% Subm. for Bid	1.0d	3-Jun-25 A	3-Jun-25 A	
1287	DS-CD-ITB3-GS-1280 ITB 3 HCAA Board Approval - 100% Subm. for Bid	1.0d	7-Aug-25 A	7-Aug-25 A	
1288	WBS - ASD Bulletin - LED Digital Technology Updates	23.0d	10-Nov-25 A	12-Dec-25 A	
1289	WBS - ASD - Bulletin - LED Digital Technology Updates - Design Development	23.0d	10-Nov-25 A	12-Dec-25 A	
1290	ASD-Bull-DT-290 HP/HNTB Prepare & Submit Proposal - ASD Bulletin - LED Dig. Tech. Upd.	9.0d	10-Nov-25 A	20-Nov-25 A	
1291	ASD-Bull-DT-310 HCAA Review & Approve Proposal - ASD Bulletin - LED Dig. Tech. Upd.	10.0d	26-Nov-25 A	11-Dec-25 A	
1292	ASD-Bull-DT-090 NTP - ASD - Bulletin - LED Dig. Tech. Upd.	1.0d	12-Dec-25 A	12-Dec-25 A	
1293	WBS - ASD - North Craft Parking Lot	48.0d	14-Oct-25 A	22-Dec-25 A	
1294	ASD-Bull-ET-70 Crisdel/HP Prepare & Submit 100% DD Proposal - ASD Bulletin - Craft Parking ...	14.0d	14-Oct-25 A	31-Oct-25 A	
1295	ASD-Bull-ET-90 HCAA Review & Approval Proposal - ASD Bulletin - Craft Parking Lot	4.0d	18-Nov-25 A	21-Nov-25 A	
1296	ASD-Bull-ET-110 Contract Development & Finalization - ASD Bulletin - Craft Parking Lot	5.0d	19-Nov-25 A	25-Nov-25 A	
1297	ASD-Bull-ET-100 Draft & Issue LOI - ASD Bulletin - Craft Parking Lot	3.0d	19-Nov-25 A	21-Nov-25 A	
1298	ASD-Bull-ET-120 Contract Negotiation - ASD Bulletin - Craft Parking Lot	4.0d	15-Dec-25 A	18-Dec-25 A	
1299	ASD-Bull-ET-130 Contract Execution - ASD Bulletin - Craft Parking Lot	1.0d	19-Dec-25 A	19-Dec-25 A	
1300	ASD-Bull-ET-80 NTP - ASD Bulletin - Craft Parking Lot	1.0d	22-Dec-25 A	22-Dec-25 A	
1301	WBS - ASD - PRECONSTRUCTION PHASE	605.0d	4-Aug-23 A	22-Dec-25 A	
1302	WBS - HCAA Board Approval Milestones	605.0d	4-Aug-23 A	22-Dec-25 A	

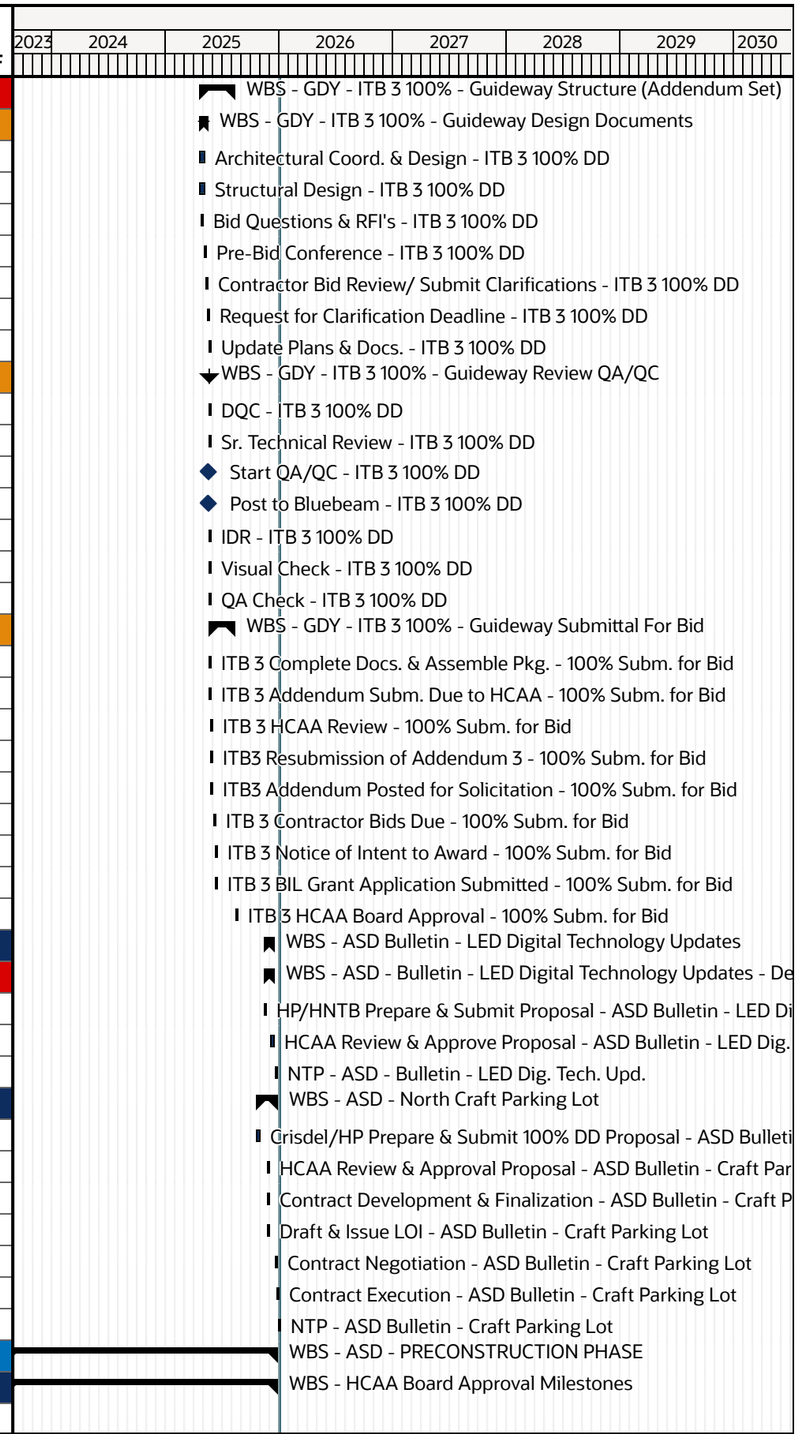

	ID	Name	Dur	Start	Finish	TF
1303	HA-BA-10	HCAA Board Award of Part 1.A Agreement (BHS) - HCAA Board Approval	1.0d	2-Oct-23 A	2-Oct-23 A	
1304	HA-BA-20	Enabling Pkg. 12.5.2024 - HCAA Board Approval	0.0d		5-Dec-24 A	
1305	HA-BA-ITB1-30	ITB 1 Pkg. 6.5.2025 - HCAA Board Approval	0.0d		5-Jun-25 A	
1306	HA-BA-50	Part 2 Supplemental A - Agreement Found. Pkg. 8.7.2025 - HCAA Board Appro...	0.0d		7-Aug-25 A	
1307	HA-BA-ITB2-3-70	ITB 2 & 3 Pkg.'s 8.7.2025 - HCAA Board Approval	0.0d		7-Aug-25 A	
1308	HA-BA-110	Part 2 Supplemental A - Agreement Found. Pkg. 8.7.2025 - Notice to Proceed	0.0d		15-Aug-25 A	
1309	HA-BA-90	Part 2 Supplemental B Agreement - Westside Checked Baggage - 10.2.25 - HC...	0.0d		2-Oct-25 A	
1310	HA-BA-95	Part 2 Supplemental B Agreement - ASD Structure (Precast & Steel) - 10.2.25 - ...	0.0d		2-Oct-25 A	
1311	WBS - HCAA Board Award of Work Order 23-01		0.0d	4-Aug-23	4-Aug-23 A	
1312	HA-WO-10	Work Order 23-01 Executed	0.0d		4-Aug-23 A	
1313	WBS - HCAA Board Award of Work Order 23-01A		0.0d	2-Oct-23	2-Oct-23 A	
1314	HA-WO-20	Work Order 23-01 A Executed (Supp. B)	0.0d		2-Oct-23 A	
1315	WBS - HCAA Board Award of Part 2 Agreement - Enabling Package		85.0d	14-Aug-24 A	13-Dec-24 A	
1316	HA-2A-EN-10	Assemble Bid Pack - HCAA Board Award of P2 Agrmt Enabling Pckg.	6.0d	14-Aug-24 A	21-Aug-24 A	
1317	HA-2A-EN-20	Subcontractor Bid Phase - HCAA Board Award of P2 Agrmt Enabling Pckg.	20.0d	22-Aug-24 A	19-Sep-24 A	
1318	HA-2A-EN-30	Issue Subcontractor Bid Pkg.s - HCAA Board Award of P2 Agrmt Enabling Pckg.	1.0d	22-Aug-24 A	22-Aug-24 A	
1319	HA-2A-EN-40	Bid Day - HCAA Board Award of P2 Agrmt Enabling Pckg.	2.0d	18-Sep-24 A	19-Sep-24 A	
1320	HA-2A-EN-50	Reconcile Bids - HCAA Board Award of P2 Agrmt Enabling Pckg.	5.0d	20-Sep-24 A	26-Sep-24 A	
1321	HA-2A-EN-60	Commence Purchase Interviews - HCAA Board Award of P2 Agrmt Enabling Pckg.	0.0d	25-Sep-24 A		
1322	HA-2A-EN-70	Purchase Interview & Issue Doc U Sign Contracts - HCAA Board Award of P2 Ag...	8.0d	25-Sep-24 A	4-Oct-24 A	
1323	HA-2A-EN-190	GMP Pkg. Assembly - HCAA Board Award of P2 Agrmt Enabling Pckg.	4.0d	4-Oct-24 A	9-Oct-24 A	
1324	HA-2A-EN-220	Draft for Comment to HCAA Complete - HCAA Board Award of P2 Agrmt Enabli...	0.0d		9-Oct-24 A	
1325	HA-2A-EN-210	Negotiate / Address Comments w/ HCAA - HCAA Board Award of P2 Agrmt En...	13.0d	10-Oct-24 A	28-Oct-24 A	
1326	HA-2A-EN-230	Approval (5 Wks Prior to Board Mtng on 12.5.2024) Complete - HCAA Board A...	0.0d		12-Nov-24 A	
1327	HA-BA-80	HCAA NTP Submission - HCAA Board Approval	6.0d	6-Dec-24 A	13-Dec-24 A	
1328	WBS - Part 2 Agreement - Enabling Package Trade Partner Purchasing		8.0d	25-Sep-24 A	4-Oct-24 A	
1329	HA-2A-EN-80	Purchase Interview Elec. - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1330	HA-2A-EN-90	Purchase Interview Security - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1331	HA-2A-EN-100	Purchase Interview Civil - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1332	HA-2A-EN-110	Purchase Interview Low Voltage - Part 2 Agreement Enabling Pckg.	1.0d	25-Sep-24 A	25-Sep-24 A	
1333	HA-2A-EN-120	Purchase Interview Trailer - Part 2 Agreement Enabling Pckg.	1.0d	30-Sep-24 A	30-Sep-24 A	
1334	HA-2A-EN-130	Purchase Interview Fencing - Part 2 Agreement Enabling Pckg.	1.0d	30-Sep-24 A	30-Sep-24 A	
1335	HA-2A-EN-140	Purchase Interview Demolition - Part 2 Agreement Enabling Pckg.	1.0d	1-Oct-24 A	1-Oct-24 A	
1336	HA-2A-EN-150	Purchase Interview Material Testing & Pilot Holes - Part 2 Agreement Enabling ...	1.0d	1-Oct-24 A	1-Oct-24 A	
1337	HA-2A-EN-160	Purchase Interview Furniture - Part 2 Agreement Enabling Pckg.	1.0d	2-Oct-24 A	2-Oct-24 A	
1338	HA-2A-EN-170	Purchase Interview Site Logistics - Part 2 Agreement Enabling Pckg.	1.0d	3-Oct-24 A	3-Oct-24 A	
1339	HA-2A-EN-180	Purchase Interview Field Engineering - Part 2 Agreement Enabling Pckg.	1.0d	3-Oct-24 A	3-Oct-24 A	
1340	HA-2A-EN-200	Purchase Interview Dewatering - Part 2 Agreement Enabling Pckg.	1.0d	4-Oct-24 A	4-Oct-24 A	
1341	WBS - HCAA Board Award of Part 2 Supplement A - Ground Improvements & Foundations Package		134.0d	8-May-25 A	14-Nov-25 A	
1342	HA-2A-10	Bid Packaging - Ground Impr. & Found. Pckg	4.0d	8-May-25 A	13-May-25 A	
1343	HA-2A-20	Bidding Period - Ground Impr. & Found. Pckg	20.0d	14-May-25 A	11-Jun-25 A	
1344	HA-2A-70	GMP Pkg. Assembly - Ground Impr. & Found. Pckg	5.0d	5-Jun-25 A	11-Jun-25 A	

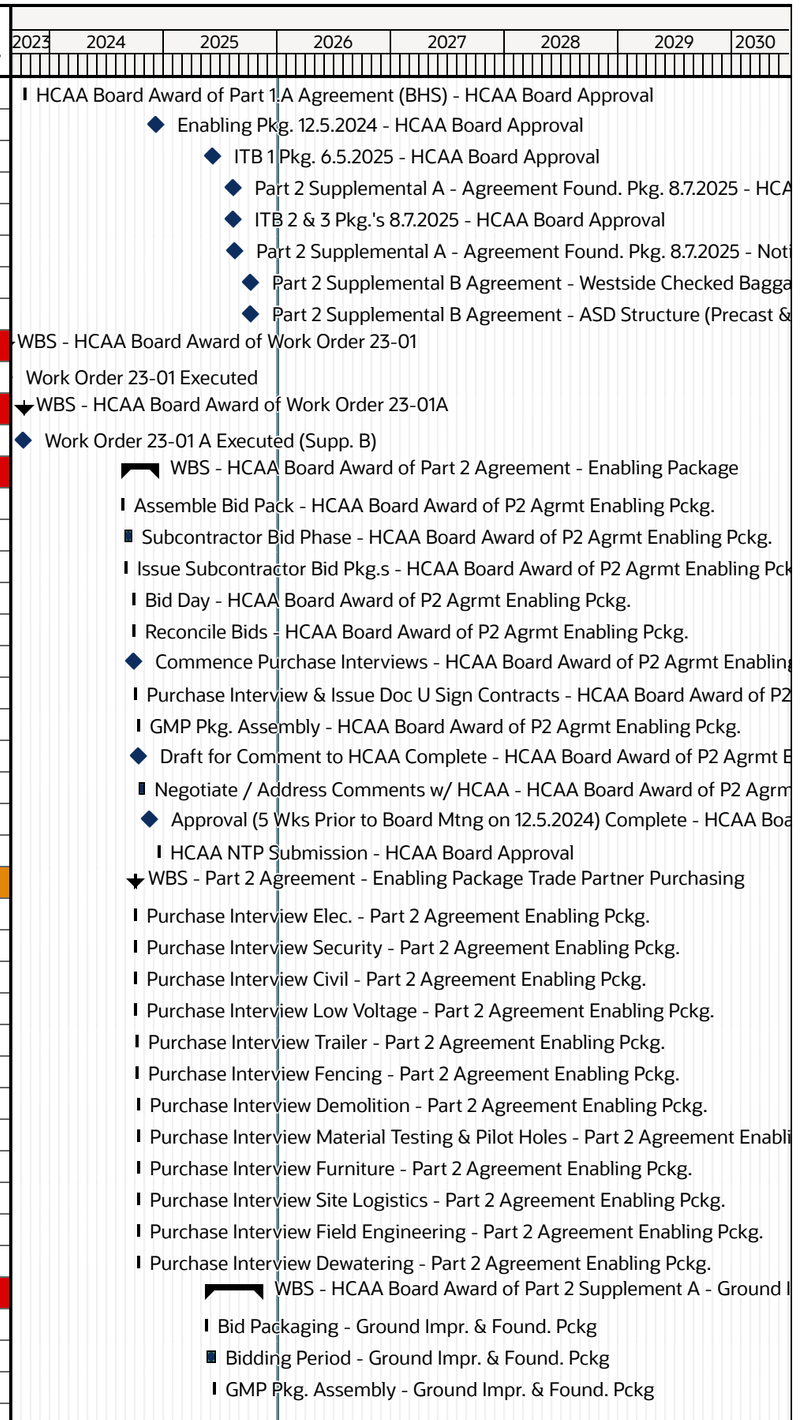


ID	Name	Dur	Start	Finish	TF
1345	HA-2A-80	Draft for Comment to HCAA Complete - Ground Impr. & Found. Pckg	0.0d		11-Jun-25 A	
1346	HA-2A-90	Negotiate / Address Comments w/ HCAA - Ground Impr. & Found. Pckg	15.0d	12-Jun-25 A	2-Jul-25 A	
1347	HA-2A-130	Bid Addendum 6.12.2025 Found. - Ground Impr. & Found. Pckg	15.0d	12-Jun-25 A	2-Jul-25 A	
1348	HA-2A-100	Approval (5 Weeks Prior to Board Mtg. on 8.7.2025) - Ground Impr. & Found. P...	0.0d		2-Jul-25 A	
1349	HA-2A-30	Contracting Period - Ground Impr. & Found. Pckg	14.0d	3-Jul-25 A	23-Jul-25 A	
1350	WBS - Part 2 Supplement A - Ground Improvements Trade Partner Purchasing		92.0d	9-Jul-25 A	14-Nov-25 A	
1351	HA-2A-140	Purchase Interview - GMF - Anchor Bolts & Structural Steel Mill Order 7/9/25	1.0d	9-Jul-25 A	9-Jul-25 A	
1352	HA-2A-150	Purchase Interview - APG - Deep UG Electric & Long Lead 7/9/25	1.0d	9-Jul-25 A	9-Jul-25 A	
1353	HA-2A-160	Purchase Interview - MC Dean - Deep UG LV 7/10/25	1.0d	10-Jul-25 A	10-Jul-25 A	
1354	HA-2A-170	Purchase Interview - BCH - Deep UG Plumbing & HVAC Long Lead 7/11/25	1.0d	11-Jul-25 A	11-Jul-25 A	
1355	HA-2A-180	Purchase Interview - Menard DIP/LTP Ground Improvement 7/11/25	1.0d	11-Jul-25 A	11-Jul-25 A	
1356	HA-2A-190	Purchase Interview - Liberty - Found. Concrete 7/23/25	1.0d	23-Jul-25 A	23-Jul-25 A	
1357	HA-2A-240	Contracting Period - Menard DIP/LTP Ground Improvement	32.0d	18-Aug-25 A	1-Oct-25 A	
1358	HA-2A-200	Contracting Period - GMF - Anchor Bolts & Structural Steel Mill Order	52.0d	18-Aug-25 A	29-Oct-25 A	
1359	HA-2A-220	Contracting Period - MC Dean - QA/QC Deep UG	46.0d	18-Aug-25 A	21-Oct-25 A	
1360	HA-2A-210	Contracting Period - APG - Deep UG Elec. & Long Lead	45.0d	18-Aug-25 A	20-Oct-25 A	
1361	HA-2A-230	Contracting Period - BCH - Deep UG Plumbing & HVAC Long Lead	30.0d	18-Aug-25 A	29-Sep-25 A	
1362	HA-2A-250	Contracting Period - Liberty - Found. Concrete	18.0d	18-Aug-25 A	11-Sep-25 A	
1363	HA-2A-290	NTP - GMF - Anchor Bolts & Structural Steel Mill Order	0.0d	26-Aug-25 A		
1364	HA-2A-270	Subcontract Execution - Liberty - Found. Concrete	0.0d		11-Sep-25 A	
1365	HA-2A-280	Subcontract Execution - BCH - Deep UG Plumbing & HVAC Long Lead	0.0d		29-Sep-25 A	
1366	HA-2A-260	Subcontract Execution - Menard DIP/LTP Ground Improvement	0.0d		1-Oct-25 A	
1367	HA-2A-320	Subcontract Execution - MC Dean - QA/QC Deep UG	0.0d		21-Oct-25 A	
1368	HA-2A-310	Subcontract Execution - APG - Deep UG Elec. & Long Lead	0.0d		5-Nov-25 A	
1369	HA-2A-300	Subcontract Execution - GMF - Structural Steel	0.0d		14-Nov-25 A	
1370	WBS - HCAA Board Award of Part 2 Supplement B - Centralized Checked Baggage Enabling		87.0d	17-Jul-25 A	17-Nov-25 A	
1371	HA-2B-CC-10	Bid Packaging - CCBS Pckg.	2.0d	17-Jul-25 A	18-Jul-25 A	
1372	HA-2B-CC-20	Bidding Period - CCBS Pckg.	14.0d	21-Jul-25 A	7-Aug-25 A	
1373	HA-2B-CC-40	GMP Pkg. Assembly - CCBS Pckg.	4.0d	8-Aug-25 A	13-Aug-25 A	
1374	HA-2B-CC-70	Submit For Approval (8 Weeks Prior to Board Mtg. on 10.2.2025) - CCBS Pckg.	0.0d		14-Aug-25 A	
1375	HA-2B-CC-30	Contracting Period - CCBS Pckg.	29.0d	15-Aug-25 A	25-Sep-25 A	
1376	HA-2B-CC-60	Negotiate / Address Comments w/ HCAA - CCBS Pckg.	7.0d	17-Sep-25 A	25-Sep-25 A	
1377	HA-2B-CC-65	Board Meeting Agenda - CCBS Pckg.	4.0d	26-Sep-25 A	2-Oct-25 A	
1378	HA-2B-CC-75	Trade Partner Contract Negotiation - CCBS Pckg.	32.0d	3-Oct-25 A	17-Nov-25 A	
1379	HA-2B-CC-85	Trade Partner Contract Execution - CCBS Pckg.	0.0d		17-Nov-25 A	
1380	WBS - Part 2 Supplement B - ASD Structure (Precast & Steel)		100.0d	17-Jul-25 A	8-Dec-25 A	
1381	HA-2B-ASD-80	Bid Packaging - ASD Structure (Precast & Steel)	2.0d	17-Jul-25 A	18-Jul-25 A	
1382	HA-2B-ASD-90	Bidding Period - ASD Structure (Precast & Steel)	14.0d	21-Jul-25 A	7-Aug-25 A	
1383	HA-2B-ASD-110	GMP Pkg. Assembly - ASD Structure (Precast & Steel)	4.0d	8-Aug-25 A	13-Aug-25 A	
1384	HA-2B-ASD-140	Submit For Approval (8 Weeks Prior to Board Mtg. on 10.2.2025) - ASD Structu...	0.0d		14-Aug-25 A	
1385	HA-2B-ASD-100	Contracting Period - ASD Structure (Precast & Steel)	29.0d	15-Aug-25 A	25-Sep-25 A	
1386	HA-2B-ASD-130	Negotiate/Address Comments w/ HCAA - ASD Structure (Precast & Steel)	7.0d	17-Sep-25 A	25-Sep-25 A	

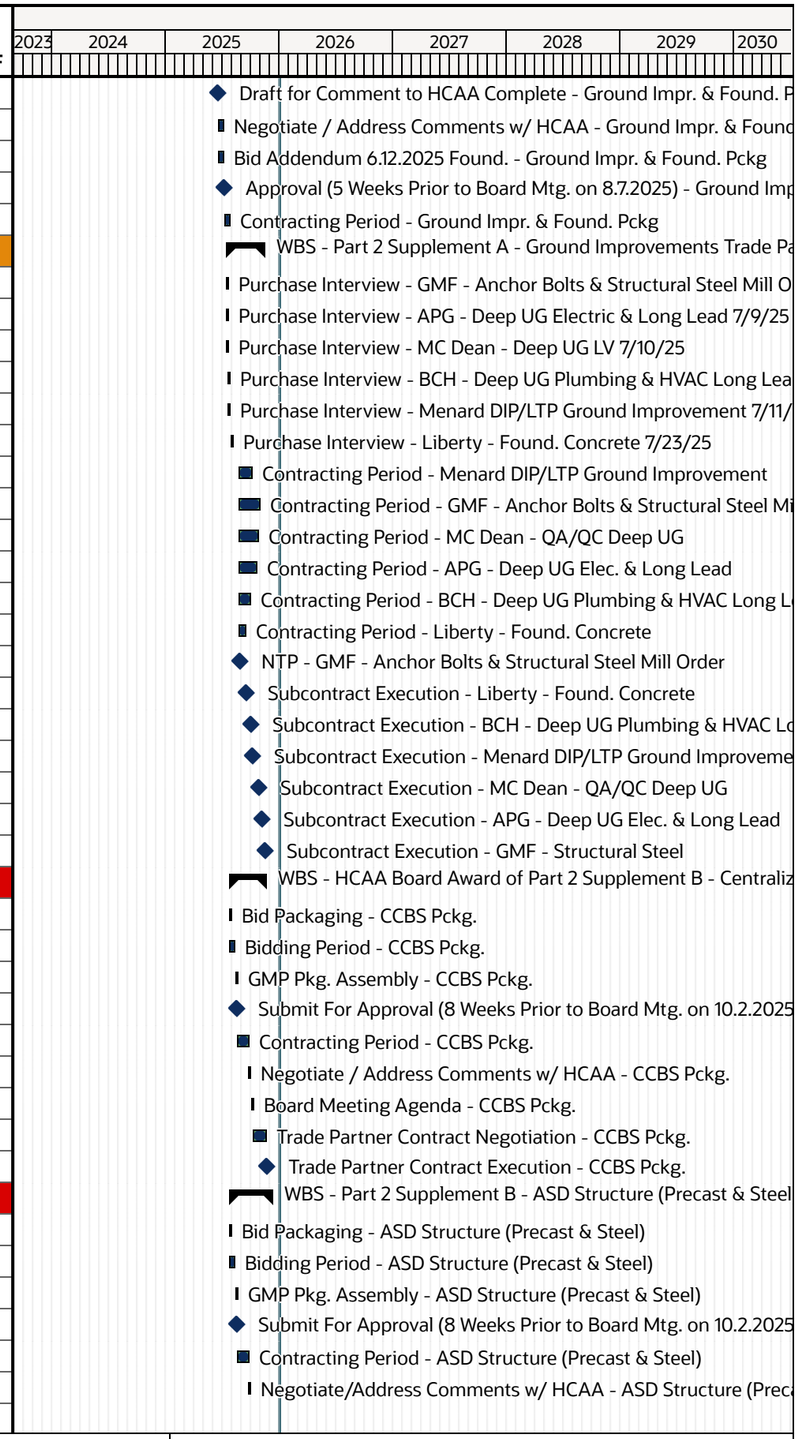


	ID	Name	Dur	Start	Finish	TF
1387	WBS - Architectural/Structural Precast		61.0d	11-Sep-25 A	8-Dec-25 A	
1388	HA-2B-ASD-160	Bidding Period - Precast	23.0d	11-Sep-25 A	13-Oct-25 A	
1389	HA-2B-ASD-170	Bid Review/Purchasing Meetings/Issue LOI - Precast	8.0d	24-Oct-25 A	4-Nov-25 A	
1390	HA-2B-ASD-180	Contracting Period - Precast	22.0d	5-Nov-25 A	8-Dec-25 A	
1391	HA-2B-ASD-190	Contract Execution Complete - Precast - Architectural/Structural	0.0d		8-Dec-25 A	
1392	WBS - HCAA Board Award of Part 2 Supplement C Wave 1 - Core & Shell Package		84.0d	22-Aug-25 A	22-Dec-25 A	
1393	HA-2C-W1-20	Bid Packaging - Part 2 Supp. C - Core & Shell Pkg.	10.0d	22-Aug-25 A	5-Sep-25 A	
1394	HA-2C-W1-30	Bidding Period - Part 2 Supp. C - Core & Shell Pkg.	37.0d	8-Sep-25 A	27-Oct-25 A	
1395	HA-2C-W1-35	Amendment 1 100% Drawings Pricing - Part 2 Supp. C - Core & Shell Pkg.	11.0d	28-Oct-25 A	11-Nov-25 A	
1396	HA-2C-W1-55	Contract Development/GMP Pkg. Assembly - Part 2 Supp. C - Core & Shell Pkg.	21.0d	12-Nov-25 A	12-Dec-25 A	
1397	HA-2C-W1-50	Bid Review/Bid Selection - Part 2 Supp. C - Core & Shell Pkg.	4.0d	12-Nov-25 A	17-Nov-25 A	
1398	HA-2C-W1-60	Submit For Approval (5 Weeks Prior to Board Mtg. on 2.5.2026 - Part 2 Supp. C ...	0.0d		12-Dec-25 A	
1399	WBS - Part 2 Supplement C Wave 1 Purchasing & Contracting		23.0d	18-Nov-25 A	22-Dec-25 A	
1400	WBS - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		12.0d	18-Nov-25 A	5-Dec-25 A	
1401	2C-W1-PC-800	Purchasing Meeting - Fire Protection Trade Partner - P2 Supp. C Wave 1 Purcha...	1.0d	18-Nov-25 A	18-Nov-25 A	
1402	2C-W1-PC-820	Contract Development, Review, & Issuance - Fire Protection Trade Partner - P2 ...	8.0d	24-Nov-25 A	5-Dec-25 A	
1403	WBS - Elevators/Escalators Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		15.0d	18-Nov-25 A	10-Dec-25 A	
1404	2C-W1-PC-740	Purchasing Meeting - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purch...	1.0d	18-Nov-25 A	18-Nov-25 A	
1405	2C-W1-PC-750	Draft & Issue LOI - Elev./Escalators Trade Partner - P2 Supp. C Wave 1 Purchasi...	3.0d	2-Dec-25 A	4-Dec-25 A	
1406	2C-W1-PC-760	Contract Development, Review, & Issuance - Elev./Escalators Trade Partner - P...	4.0d	5-Dec-25 A	10-Dec-25 A	
1407	WBS - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		8.0d	24-Nov-25 A	5-Dec-25 A	
1408	2C-W1-PC-2060	Purchasing Meeting - Terrazzo Floor Trade Partner - P2 Supp. C Wave 1 Purcha...	0.0d	24-Nov-25 A	24-Nov-25 A	
1409	2C-W1-PC-2080	Contract Development, Review, & Issuance - Terrazzo Floor Trade Partner - P2 ...	5.0d	1-Dec-25 A	5-Dec-25 A	
1410	WBS - Roofing Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	2-Dec-25 A	16-Dec-25 A	
1411	2C-W1-PC-70	Purchasing Meeting - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & ...	1.0d	2-Dec-25 A	2-Dec-25 A	
1412	2C-W1-PC-80	Draft & Issue LOI - Roofing Trade Partner - P2 Supp. C Wave 1 Purchasing & Co...	3.0d	3-Dec-25 A	5-Dec-25 A	
1413	2C-W1-PC-90	Contract Development, Review, & Issuance - Roofing Trade Partner - P2 Supp. ...	5.0d	10-Dec-25 A	16-Dec-25 A	
1414	WBS - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		12.0d	19-Nov-25 A	8-Dec-25 A	
1415	2C-W1-PC-1220	Purchasing Meeting - Acoustical Panel Ceilings Trade Partner - P2 Supp. C Wav...	1.0d	19-Nov-25 A	19-Nov-25 A	
1416	2C-W1-PC-1240	Contract Development, Review, & Issuance - Acoustical Panel Ceilings Trade Pa...	8.0d	25-Nov-25 A	8-Dec-25 A	
1417	WBS - Interior Wall Panels (Specialties/Decorative Glass) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contra...		5.0d	2-Dec-25 A	8-Dec-25 A	
1418	2C-W1-PC-370	Purchasing Meeting - Interior Wall Panels (Specialties/Decorative Glass) Trade ...	1.0d	2-Dec-25 A	2-Dec-25 A	
1419	2C-W1-PC-390	Contract Development, Review, & Issuance - Interior Wall Panels (Specialties/D...	2.0d	5-Dec-25 A	8-Dec-25 A	
1420	WBS - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		5.0d	2-Dec-25 A	8-Dec-25 A	
1421	2C-W1-PC-2120	Purchasing Meeting - Ornamental Metals Trade Partner - P2 Supp. C Wave 1 P...	1.0d	2-Dec-25 A	2-Dec-25 A	
1422	2C-W1-PC-2140	Contract Development, Review, & Issuance - Ornamental Metals Trade Partner ...	2.0d	5-Dec-25 A	8-Dec-25 A	
1423	WBS - Glass Handrail Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		1.0d	3-Dec-25 A	3-Dec-25 A	
1424	2C-W1-PC-440	Purchasing Meeting - Glass Handrail Trade Partner - P2 Supp. C Wave 1 Purcha...	1.0d	3-Dec-25 A	3-Dec-25 A	
1425	WBS - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		1.0d	3-Dec-25 A	3-Dec-25 A	
1426	2C-W1-PC-1160	Purchasing Meeting - Masonry Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	3-Dec-25 A	3-Dec-25 A	
1427	WBS - Demolition Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		11.0d	4-Dec-25 A	18-Dec-25 A	
1428	2C-W1-PC-2420	Purchasing Meeting - Demolition Trade Partner - P2 Supp. C Wave 1 Purchasin...	1.0d	4-Dec-25 A	4-Dec-25 A	




	ID	Name	Dur	Start	Finish	TF
1429	2C-W1-PC-2440	Contract Development, Review, & Issuance - Demolition Trade Partner - P2 Sup...	8.0d	9-Dec-25 A	18-Dec-25 A	
1430	WBS - Concrete SOG & SOMD Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		1.0d	4-Dec-25 A	4-Dec-25 A	
1431	2C-W1-PC-10	Purchasing Meeting - Concrete Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	4-Dec-25 A	4-Dec-25 A	
1432	WBS - Interior/Exterior Metal Wall Panels Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		8.0d	9-Dec-25 A	18-Dec-25 A	
1433	2C-W1-PC-250	Purchasing Meeting - Interior/Exterior Metal Wall Panels Trade Partner - P2 Su...	1.0d	9-Dec-25 A	9-Dec-25 A	
1434	2C-W1-PC-270	Contract Development, Review, & Issuance - Interior/Exterior Metal Wall Panels...	7.0d	10-Dec-25 A	18-Dec-25 A	
1435	WBS - Spray Fireproofing & Insulation (K-13) Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		7.0d	9-Dec-25 A	17-Dec-25 A	
1436	2C-W1-PC-130	Purchasing Meeting - Spray Fireproofing & Insulation (K-13) Trade Partner - P2...	1.0d	9-Dec-25 A	9-Dec-25 A	
1437	2C-W1-PC-150	Contract Development, Review, & Issuance - Spray Fireproofing & Insulation (K-...	5.0d	11-Dec-25 A	17-Dec-25 A	
1438	WBS - Drywall & Related Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		6.0d	10-Dec-25 A	17-Dec-25 A	
1439	2C-W1-PC-500	Purchasing Meeting - Drywall & Related Trade Partner - P2 Supp. C Wave 1 Pur...	1.0d	10-Dec-25 A	10-Dec-25 A	
1440	2C-W1-PC-520	Contract Development, Review, & Issuance - Drywall & Related Trade Partner - ...	5.0d	11-Dec-25 A	17-Dec-25 A	
1441	WBS - Glass & Glazing/Curtainwall Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		7.0d	10-Dec-25 A	18-Dec-25 A	
1442	2C-W1-PC-310	Purchasing Meeting - Glass & Glazing/Curtainwall Trade Partner - P2 Supp. C ...	1.0d	10-Dec-25 A	10-Dec-25 A	
1443	2C-W1-PC-330	Contract Development, Review, & Issuance - Glass & Glazing/Curtainwall Trade ...	6.0d	11-Dec-25 A	18-Dec-25 A	
1444	WBS - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing & Contracting		1.0d	11-Dec-25 A	11-Dec-25 A	
1445	2C-W1-PC-1040	Purchasing Meeting - Sitework Trade Partner - P2 Supp. C Wave 1 Purchasing ...	1.0d	11-Dec-25 A	11-Dec-25 A	
1446	WBS - Waterproofing, Caulks, & Sealants Trade Partner - Part 2 Supp. C Wave 1 Purchasing & Contracting		1.0d	11-Dec-25 A	11-Dec-25 A	
1447	2C-W1-PC-190	Purchasing Meeting - Waterproofing, Caulks, & Sealants Trade Partner - P2 Sup...	1.0d	11-Dec-25 A	11-Dec-25 A	
1448	WBS - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partner - Part 2 Supp. B Purchasing & Contracting		3.0d	18-Dec-25 A	22-Dec-25 A	
1449	2C-W1-PC-2540	Purchasing Meeting - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partn...	1.0d	18-Dec-25 A	18-Dec-25 A	
1450	2C-W1-PC-2560	Contract Development, Review, & Issuance - Carbon Fiber Reinforcement Poly...	1.0d	19-Dec-25 A	19-Dec-25 A	
1451	2C-W1-PC-2580	Contract Execution - Carbon Fiber Reinforcement Polymer (CFRP) Trade Partne...	1.0d	22-Dec-25 A	22-Dec-25 A	
1452	2C-W1-PC-2590	Contract Execution Complete - Carbon Fiber Reinforcement Polymer (CFRP) Tra...	0.0d		22-Dec-25 A	
1453	WBS - HCAA Alternative Procurement Preconstruction		76.0d	29-May-25 A	15-Sep-25 A	
1454	WBS - Artwork Preconstruction (Coordination with DB Team)		76.0d	29-May-25 A	15-Sep-25 A	
1455	HA-AL-AW-10	Artwork - HCAA Requests for Proposals, Review & Selection of Artists	75.0d	29-May-25 A	12-Sep-25 A	
1456	HA-AL-AW-15	Artwork - Public Art Committee Orientation Meeting	1.0d	15-Sep-25 A	15-Sep-25 A	
1457	WBS - ASD - CITY OF TAMPA PERMITTING		190.0d	20-Mar-25 A	18-Dec-25 A	
1458	WBS - Early Foundations Permit		114.0d	10-Apr-25 A	22-Sep-25 A	
1459	ASDEF-PER-10	Docs. Complete - Early Found. Permit	0.0d		10-Apr-25 A	
1460	ASDEF-PER-20	Prepare Docs. / HCAA Review / Page Turn - Early Found. Permit	10.0d	11-Apr-25 A	24-Apr-25 A	
1461	ASDEF-PER-30	Submit Found. Docs. to COT - Early Found. Permit	1.0d	3-Jul-25 A	3-Jul-25 A	
1462	ASDEF-PER-135	Threshold Letter Completion & Received from HCAA - Early Found. Permit	30.0d	7-Jul-25 A	15-Aug-25 A	
1463	ASDEF-PER-40	COT Initial Subm. Review - Early Found. Permit	15.0d	18-Aug-25 A	8-Sep-25 A	
1464	ASDEF-PER-50	COT Initial Subm. Review Comments Received - Early Found. Permit	1.0d	9-Sep-25 A	9-Sep-25 A	
1465	ASDEF-PER-70	Submit Found. Revision # 1 to COT - Early Found. Permit	1.0d	10-Sep-25 A	10-Sep-25 A	
1466	ASDEF-PER-60	Design Team Respond to Initial Comments - Early Found. Permit	1.0d	10-Sep-25 A	10-Sep-25 A	
1467	ASDEF-PER-80	COT Revision #1 Review - Early Found. Permit	7.0d	11-Sep-25 A	19-Sep-25 A	
1468	ASDEF-PER-130	Anticipated Found. Permit Approval by COT - Early Found. Permit	1.0d	22-Sep-25 A	22-Sep-25 A	
1469	WBS - ITB1 - Apron, Site and Utilities Permit (comm. Misc)		62.0d	20-Mar-25 A	17-Jun-25 A	
1470	ASDEF-PER-ITB1-140	Docs. Complete - ITB1 Apron/Site & Util.	0.0d		20-Mar-25 A	

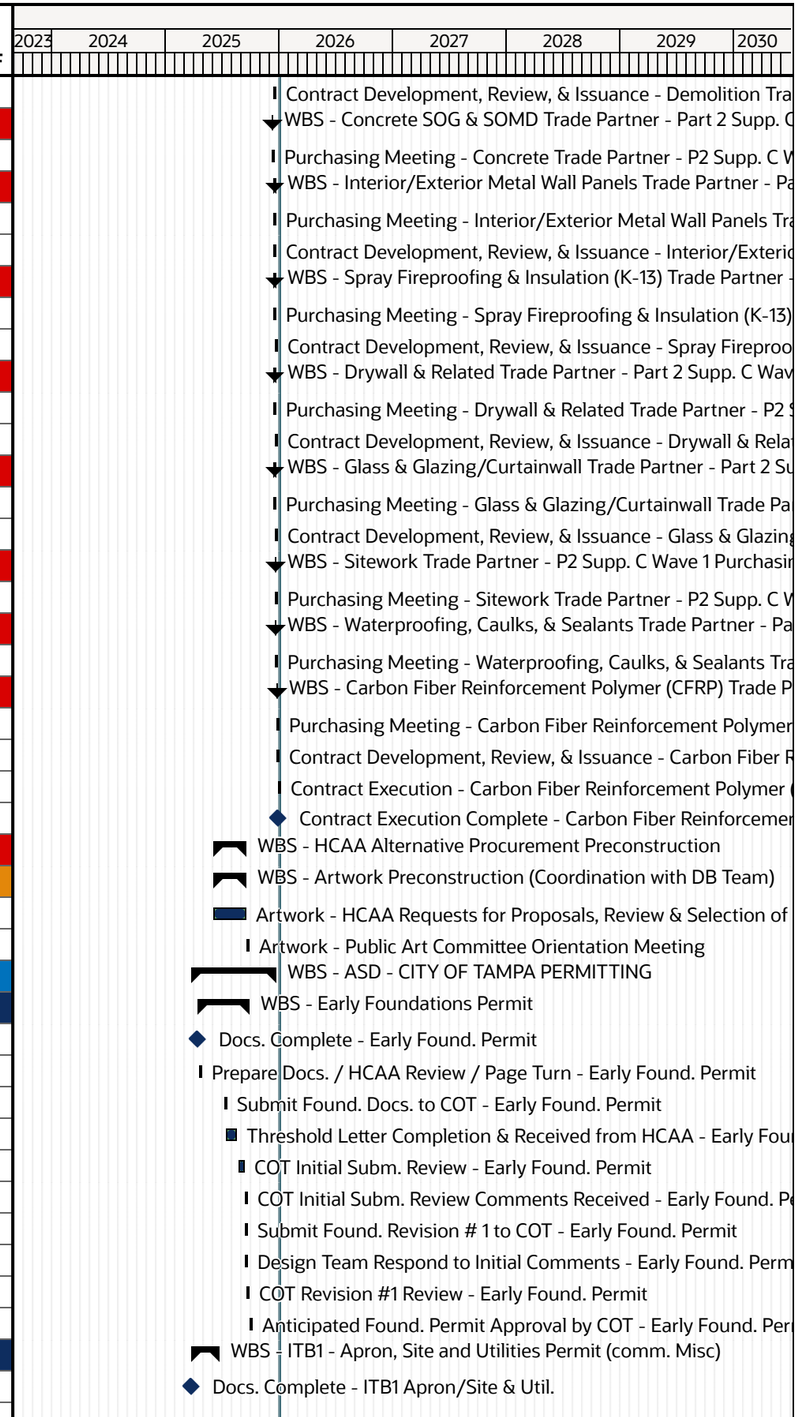


	ID	Name	Dur	Start	Finish	TF
1471	ASDEF-PER-ITB1-150	Prepare Docs. / HCAA Review / Page Turn - ITB1 Apron/Site & Util.	11.0d	21-Mar-25 A	4-Apr-25 A	
1472	ASDEF-PER-ITB1-160	Submit ITB1 Docs. to COT - ITB1 Apron/Site & Util.	1.0d	7-Apr-25 A	7-Apr-25 A	
1473	ASDEF-PER-ITB1-170	COT Initial Subm. Review - ITB1 Apron/Site & Util.	22.0d	8-Apr-25 A	7-May-25 A	
1474	ASDEF-PER-ITB1-180	COT Initial Subm. Review Comments Received - ITB1 Apron/Site & Util.	1.0d	8-May-25 A	8-May-25 A	
1475	ASDEF-PER-ITB1-190	Design Team Respond to Initial Comments - ITB1 Apron/Site & Util.	10.0d	9-May-25 A	22-May-25 A	
1476	ASDEF-PER-ITB1-200	Submit ITB1 Revision # 1 to COT - ITB1 Apron/Site & Util.	1.0d	23-May-25 A	23-May-25 A	
1477	ASDEF-PER-ITB1-210	COT Revision # 1 Review - ITB1 Apron/Site & Util.	6.0d	27-May-25 A	3-Jun-25 A	
1478	ASDEF-PER-ITB1-260	Anticipated ITB1 Permit Approval by COT - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1479	ASDEF-PER-ITB1-220	ITB 1 Revision #1 Review Comments Received - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1480	ASDEF-PER-ITB1-212	ITB 1 Permit Approval by COT (6-4-25) - ITB1 Apron/Site & Util.	1.0d	4-Jun-25 A	4-Jun-25 A	
1481	ASDEF-PER-ITB1-230	Design Team Respond to Revision #1 comments - ITB1 Apron/Site & Util.	9.0d	5-Jun-25 A	17-Jun-25 A	
1482	WBS - ITB2 - PBB Permit		107.0d	10-Apr-25 A	11-Sep-25 A	
1483	ASDEF-PER-ITB2-270	Docs. Complete - ITB2 PBB Permit	0.0d		10-Apr-25 A	
1484	ASDEF-PER-ITB2-280	Prepare Docs. / HCAA Review / Page Turn - ITB2 PBB Permit	10.0d	11-Apr-25 A	24-Apr-25 A	
1485	ASDEF-PER-ITB2-290	Submit ITB2 Docs. to COT - ITB2 PBB Permit	1.0d	15-Jul-25 A	15-Jul-25 A	
1486	ASDEF-PER-ITB2-300	COT Initial Subm. Review - ITB2 PBB Permit	17.0d	16-Jul-25 A	7-Aug-25 A	
1487	ASDEF-PER-ITB2-310	COT Initial Subm. Review Comments Received - ITB2 PBB Permit	1.0d	8-Aug-25 A	8-Aug-25 A	
1488	ASDEF-PER-ITB2-320	Design Team Respond to Initial Comments - ITB2 PBB Permit	14.0d	11-Aug-25 A	28-Aug-25 A	
1489	ASDEF-PER-ITB2-330	Submit ITB2 Revision # 1 to COT - ITB2 PBB Permit	1.0d	29-Aug-25 A	29-Aug-25 A	
1490	ASDEF-PER-ITB2-340	COT Revision #1 Review - ITB2 PBB Permit	7.0d	2-Sep-25 A	10-Sep-25 A	
1491	ASDEF-PER-ITB2-390	Anticipated ITB 2 Permit Approval by COT - ITB2 PBB Permit	1.0d	11-Sep-25 A	11-Sep-25 A	
1492	WBS - ITB3 - Structural Guideway Permit		137.0d	10-Apr-25 A	22-Oct-25 A	
1493	ASDEF-PER-ITB3-410	Prepare Docs. / HCAA Review / Page Turn - ITB3 Struct. Gdwy. Permit	1.0d	10-Apr-25 A	10-Apr-25 A	
1494	ASDEF-PER-ITB3-400	Docs. Complete - ITB3 Struct. Gdwy. Permit	0.0d		10-Apr-25 A	
1495	ASDEF-PER-ITB3-420	Submit ITB3 Docs. to COT (Submittal to HP) - ITB3 Struct. Gdwy. Permit	1.0d	3-Jul-25 A	3-Jul-25 A	
1496	ASDEF-PER-ITB3-525	Threshold Letter Completion & Received from HCAA - ITB3 Struct. Gdwy. Permit	50.0d	7-Jul-25 A	15-Sep-25 A	
1497	ASDEF-PER-ITB3-530	Submit ITB3 Docs. to COT - ITB3 Struct. Gdwy. Permit	1.0d	16-Sep-25 A	16-Sep-25 A	
1498	ASDEF-PER-ITB3-430	COT Initial Subm. Review - ITB3 Struct. Gdwy. Permit	1.0d	17-Sep-25 A	17-Sep-25 A	
1499	ASDEF-PER-ITB3-440	COT Initial Subm. Review Comments Received - ITB3 Struct. Gdwy. Permit	1.0d	1-Oct-25 A	1-Oct-25 A	
1500	ASDEF-PER-ITB3-450	Design Team Respond to Initial Comments - ITB3 Struct. Gdwy. Permit	9.0d	2-Oct-25 A	14-Oct-25 A	
1501	ASDEF-PER-ITB3-460	Submit ITB3 Initial Comment Responses to COT - ITB3 Struct. Gdwy. Permit	1.0d	15-Oct-25 A	15-Oct-25 A	
1502	ASDEF-PER-ITB3-520	ITB3 Permit Approval By COT - ITB3 Struct. Gdwy. Permit	1.0d	22-Oct-25 A	22-Oct-25 A	
1503	WBS - ASD Building Permit		66.0d	21-Aug-25 A	24-Nov-25 A	
1504	ASDEF-PER-ASD-530	Docs. Complete - ASD Building Permit	0.0d		21-Aug-25 A	
1505	ASDEF-PER-ASD-540	Prepare Docs. / HCAA Review / Page Turn - ASD Building Permit	10.0d	22-Aug-25 A	5-Sep-25 A	
1506	ASDEF-PER-ASD-550	Submit ASD Docs. to COT - ASD Building Permit	3.0d	15-Sep-25 A	17-Sep-25 A	
1507	ASDEF-PER-ASD-560	COT Initial Subm. Review - ASD Building Permit	36.0d	17-Sep-25 A	5-Nov-25 A	
1508	ASDEF-PER-ASD-570	COT Initial Subm. Review Comments Received - ASD Building Permit	1.0d	6-Nov-25 A	6-Nov-25 A	
1509	ASDEF-PER-ASD-580	Design Team Respond to Initial Comments - ASD Building Permit	9.0d	10-Nov-25 A	20-Nov-25 A	
1510	ASDEF-PER-ASD-590	Submit ASD Initial Comment Responses to COT - ASD Building Permit	2.0d	21-Nov-25 A	24-Nov-25 A	
1511	WBS - CCBS Permit Main Terminal Building		33.0d	30-Oct-25 A	18-Dec-25 A	
1512	ASDEF-PER-MTB-660	Docs. Complete - Main Terminal Build. Permit / CCBS	0.0d		30-Oct-25 A	

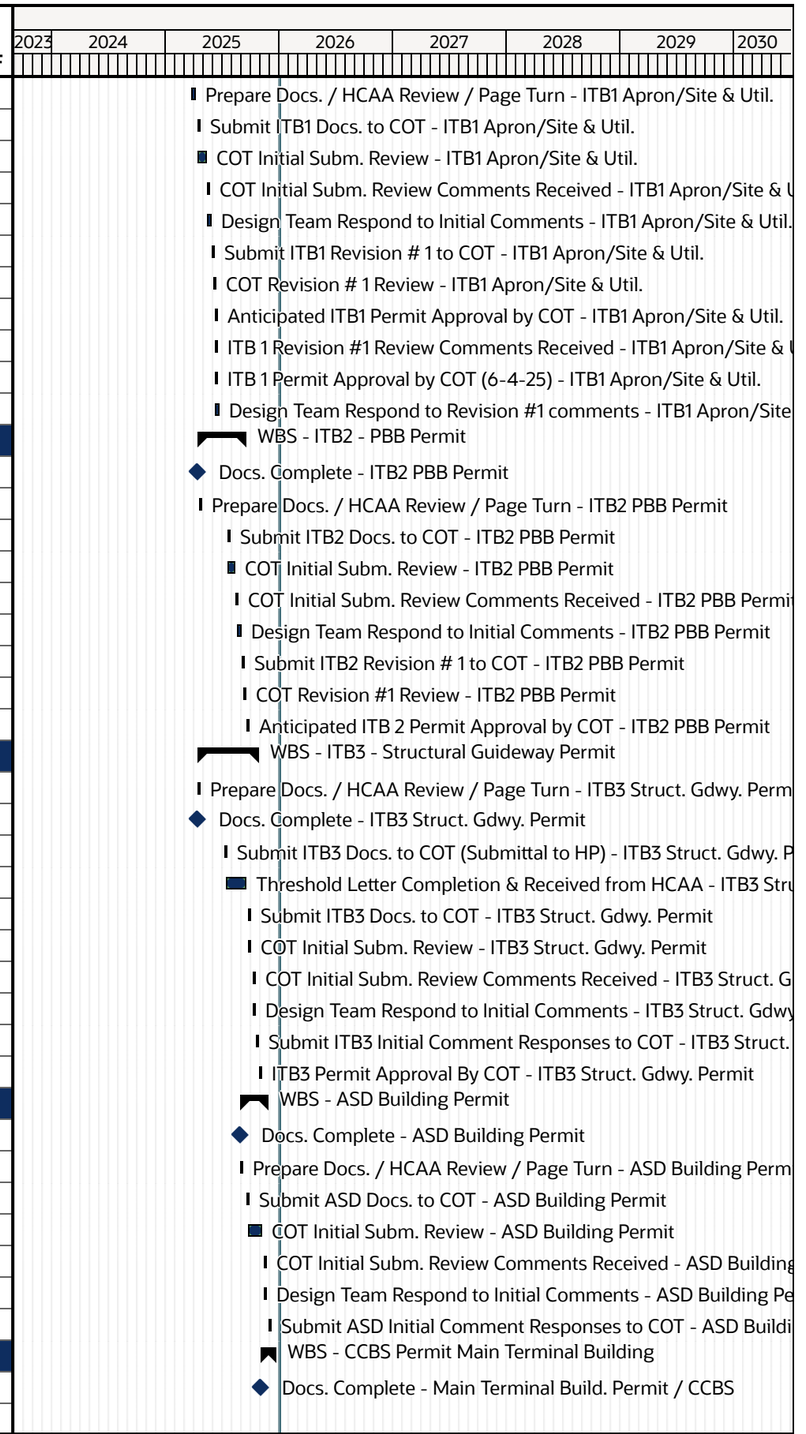


	ID	Name	Dur	Start	Finish	TF
1513	ASDEF-PER-MTB-670	Prepare Docs. / HCAA Review / Page Turn - Main Terminal Build. Permit / CCBS	3.0d	31-Oct-25 A	4-Nov-25 A	
1514	ASDEF-PER-MTB-680	Submit MT/BHS Document to HP/Beck for COT submission - Main Terminal Bui...	1.0d	5-Nov-25 A	5-Nov-25 A	
1515	ASDEF-PER-MTB-690	COT Initial Subm. Review - Main Terminal Build. Permit / CCBS	2.0d	6-Nov-25 A	7-Nov-25 A	
1516	ASDEF-PER-MTB-700	COT Initial Subm. Review Comments Received - Main Terminal Build. Permit / C...	16.0d	10-Nov-25 A	3-Dec-25 A	
1517	ASDEF-PER-MTB-705	MT BHS - COT initial comments Received - Main Terminal Build. Permit / CCBS	1.0d	4-Dec-25 A	4-Dec-25 A	
1518	ASDEF-PER-MTB-710	Design Team Respond to Initial Comments - Main Terminal Build. Permit / CCBS	9.0d	5-Dec-25 A	17-Dec-25 A	
1519	ASDEF-PER-MTB-720	Submit MT/BHS Revision #1 to COT - Main Terminal Build. Permit / CCBS	1.0d	18-Dec-25 A	18-Dec-25 A	
1520	WBS - Main Terminal Shuttle TI Permit		30.0d	30-Oct-25 A	15-Dec-25 A	
1521	ASDEF-PER-MTS-790	Docs. Complete - Main Terminal Shuttle TI Permit	0.0d		30-Oct-25 A	
1522	ASDEF-PER-MTS-800	Prepare Docs. / HCAA Review / Page Turn - Main Terminal Shuttle TI Permit	5.0d	31-Oct-25 A	6-Nov-25 A	
1523	ASDEF-PER-MTS-810	Submit MT SP Docs. to COT - Main Terminal Shuttle TI Permit	1.0d	7-Nov-25 A	7-Nov-25 A	
1524	ASDEF-PER-MTS-815	Submit MT Shuttle TI Documents to COT - Main Terminal Shuttle TI Permit	24.0d	10-Nov-25 A	15-Dec-25 A	
1525	WBS - ASD - GOVERNMENTAL/MUNICIPAL/FAA/SWFWMD/FDEP PERMITTING		329.0d	13-Aug-24 A	26-Nov-25 A	
1526	WBS - City of Tampa Utilities		311.0d	9-Sep-24 A	26-Nov-25 A	
1527	WBS - City of Tampa Water Department		248.0d	9-Sep-24 A	28-Aug-25 A	
1528	WBS - Part 2 Agreement - Enabling Package		221.0d	9-Sep-24 A	22-Jul-25 A	
1529	WBS - Enabling		221.0d	9-Sep-24 A	22-Jul-25 A	
1530	PM-P2-EN-200	Water Application Submission - Part 2 Agreement Enabling Pkg.	1.0d	9-Sep-24 A	9-Sep-24 A	
1531	PM-P2-EN-210	Water Commitment Letter - Part 2 Agreement Enabling Pkg.	151.0d	10-Sep-24 A	14-Apr-25 A	
1532	PM-P2-EN-220	Water Design Review Complete Part 2 Agreement Enabling Pkg.	68.0d	16-Apr-25 A	22-Jul-25 A	
1533	WBS - Part 1 Supplement C - Core & Shell Package		1.0d	28-Aug-25 A	28-Aug-25 A	
1534	PM-P2-2B-50	Water Application Submission - Part 2 Supp. C COT WD -Core, Shell & Finishes	1.0d	28-Aug-25 A	28-Aug-25 A	
1535	WBS - City of Tampa Waste Water Department		311.0d	9-Sep-24 A	26-Nov-25 A	
1536	WBS - Part 2 Agreement - Enabling Package		96.0d	9-Sep-24 A	24-Jan-25 A	
1537	WBS - Enabling		96.0d	9-Sep-24 A	24-Jan-25 A	
1538	PM-P2-EN-230	Wastewater Application Submission - Part 2 Enabling Pkg.	1.0d	9-Sep-24 A	9-Sep-24 A	
1539	PM-P2-EN-240	Wastewater Commitment Letter - Part 2 Enabling Pkg.	45.0d	10-Sep-24 A	11-Nov-24 A	
1540	PM-P2-EN-250	Wastewater Design Review Complete - Part 2 Enabling Pkg.	50.0d	12-Nov-24 A	24-Jan-25 A	
1541	WBS - Part 1 Supplement C- Core & Shell Package		1.0d	26-Nov-25 A	26-Nov-25 A	
1542	PM-P2-2B-70	Wastewater Application Submission - COT Core, Shell & Finishes	1.0d	26-Nov-25 A	26-Nov-25 A	
1543	WBS - City of Tampa Solid Waste		248.0d	9-Sep-24 A	28-Aug-25 A	
1544	WBS - Part 2 Agreement - Enabling Package		248.0d	9-Sep-24 A	28-Aug-25 A	
1545	WBS - Enabling		51.0d	9-Sep-24 A	18-Nov-24 A	
1546	PM-P2-2B-100	Solid Waste Application Submission - Part 2 Supp. B COT	1.0d	9-Sep-24 A	9-Sep-24 A	
1547	PM-P2-2B-110	Solid Waste Design Review Complete - Part 2 Supp. B COT	50.0d	10-Sep-24 A	18-Nov-24 A	
1548	WBS - Core & Shell		1.0d	28-Aug-25 A	28-Aug-25 A	
1549	PM-P2-2B-120	Core & Shell Solid Waste Application Submission - Part 2 Supp. C COT	1.0d	28-Aug-25 A	28-Aug-25 A	
1550	WBS - SWFWMD		59.0d	13-Aug-24 A	4-Nov-24 A	
1551	WBS - 8500 23 ASD - Site		59.0d	13-Aug-24 A	4-Nov-24 A	
1552	PM-SW-10	Site Drawing Set Pkg. Submission - 8500 23 ASD SWFWMD	1.0d	13-Aug-24 A	13-Aug-24 A	
1553	PM-SW-20	Site Drawing Set Pkg. Approval - 8500 23 ASD SWFWMD	58.0d	14-Aug-24 A	4-Nov-24 A	
1554	WBS - NPDES		62.0d	2-Sep-24 A	29-Nov-24 A	

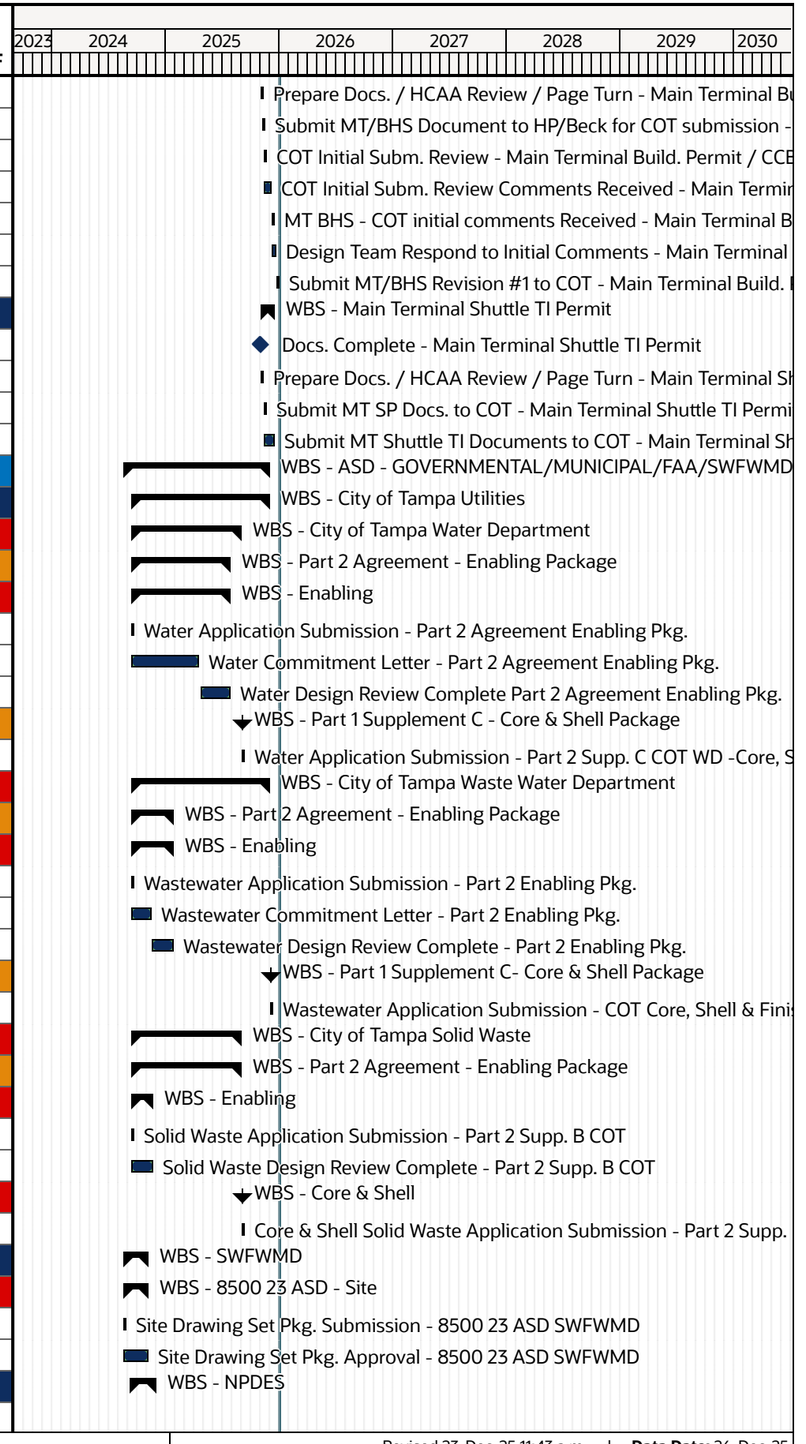


	ID	Name	Dur	Start	Finish	TF
1555	WBS - 8500 23 ASD - Site		62.0d	2-Sep-24 A	29-Nov-24 A	
1556	PM-EV-10	Site Drawing Set Pkg. Submission - 8500 23 ASD NPDES	0.0d	2-Sep-24 A	2-Sep-24 A	
1557	PM-EV-20	Site Drawing Set Pkg. Approval - 8500 23 ASD NPDES	62.0d	3-Sep-24 A	29-Nov-24 A	
1558	WBS - FDEP		217.0d	13-Dec-24 A	20-Oct-25 A	
1559	WBS - Part 2 Agreement - Enabling Package		1.0d	13-Dec-24 A	13-Dec-24 A	
1560	PM-FD-P2-EN-10	FDEP Part 2 - Enabling Drawing Pkg. Submission	1.0d	13-Dec-24 A	13-Dec-24 A	
1561	PM-FD-P2-EN-20	FDEP Part 2 - Enabling Drawing Pkg. Approval	1.0d	13-Dec-24 A	13-Dec-24 A	
1562	WBS - Part 1 Supplement C - Core & Shell Package		1.0d	20-Oct-25 A	20-Oct-25 A	
1563	PM-FD-P2-2B-20	Drawing Pkg. Submission - FDEP Part 2 Supp. C- Core, Shell & Finishes	1.0d	20-Oct-25 A	20-Oct-25 A	
1564	WBS - FAA Permit		41.0d	29-Oct-24 A	27-Dec-24 A	
1565	PM-FA-10	FAA Permit - CSPP	41.0d	29-Oct-24 A	27-Dec-24 A	
1566	PM-FA-20	FAA Permit - 7460	24.0d	21-Nov-24 A	27-Dec-24 A	
1567	WBS - City of Tampa Construction Services		292.0d	28-Aug-24 A	21-Oct-25 A	
1568	WBS - Part 2 Agreement - Enabling Package		197.0d	28-Aug-24 A	6-Jun-25 A	
1569	WBS - Enabling - Master Permit		157.0d	28-Aug-24 A	10-Apr-25 A	
1570	PM-P2-EN-10	Part 2 Master Permit Enabling Pckg. Subm. Process	24.0d	28-Aug-24 A	1-Oct-24 A	
1571	PM-P2-EN-30	Part 2 Commence Master Permit Enabling Pckg. Submission	0.0d	1-Oct-24 A		
1572	PM-P2-EN-40	Part 2 Master Permit Enabling Pckg. Review & Approval	42.0d	2-Oct-24 A	2-Dec-24 A	
1573	PM-P2-EN-110	Part 2 State Administrator Paperwork Completed Prior To Removal Of Exist. Wells	4.0d	30-Dec-24 A	3-Jan-25 A	
1574	PM-P2-EN-130	Part 2 State Administrator Paperwork Completed at Conclusion to Removal of E...	5.0d	13-Jan-25 A	17-Jan-25 A	
1575	WBS - Enabling - Trade Permits		145.0d	16-Sep-24 A	10-Apr-25 A	
1576	PM-P2-EN-20	SWFWMD Permit - Enabling Trade Permits	36.0d	16-Sep-24 A	4-Nov-24 A	
1577	PM-P2-EN-60	Elec. Trade Permit - Enabling Trade Permits	1.0d	5-Feb-25 A	5-Feb-25 A	
1578	PM-P2-EN-100	Dewatering - Enabling Trade Permits	1.0d	10-Apr-25 A	10-Apr-25 A	
1579	WBS - Trailer Complex - Master Permit		49.0d	31-Mar-25 A	6-Jun-25 A	
1580	PM-P2-EN-120	Trailer Complex Master Permit Pkg. Approval	35.0d	31-Mar-25 A	16-May-25 A	
1581	WBS - Trailer Complex - Trade Permits		14.0d	19-May-25 A	6-Jun-25 A	
1582	PM-P2-EN-140	Trade Permits- Elec. - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
1583	PM-P2-EN-150	Trade Permits- Plumbing - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
1584	PM-P2-EN-160	Trade Permits- Low Voltage - Trailer Complex	14.0d	19-May-25 A	6-Jun-25 A	
1585	WBS - ITB Trades		77.0d	2-Jul-25 A	21-Oct-25 A	
1586	WBS - ITB 1 - Apron, Site & Hydrant Fueling		0.0d	2-Jul-25	2-Jul-25 A	
1587	PM-ITB1-10	ITB1 - Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
1588	WBS - ITB 2 - Passenger Boarding Bridges		48.0d	2-Jul-25 A	10-Sep-25 A	
1589	PM-ITB2 -1-20	ITB2 - PBB Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
1590	PM-ITB2 -1-40	ITB 2 - PBB Master Permit Pkg. Approval	32.0d	28-Jul-25 A	10-Sep-25 A	
1591	WBS - ITB 3 - Guideway		77.0d	2-Jul-25 A	21-Oct-25 A	
1592	PM-ITB3-1-30	ITB 3 - GDY Master Permit Pkg. Submission Complete	0.0d		2-Jul-25 A	
1593	PM-ITB3-1-40	ITB 3 - GDY Master Permit Pkg. Approval	77.0d	3-Jul-25 A	21-Oct-25 A	
1594	WBS - Part 2 Supplement A - Foundations		56.0d	3-Jul-25 A	22-Sep-25 A	
1595	WBS - Part 2 Supplement A - Foundations - Master Permit		56.0d	3-Jul-25 A	22-Sep-25 A	
1596	PM-P2-2A-10	Commence Master Permit Pkg. Submission - Part 2 Supp. A Found.	0.0d	3-Jul-25 A		

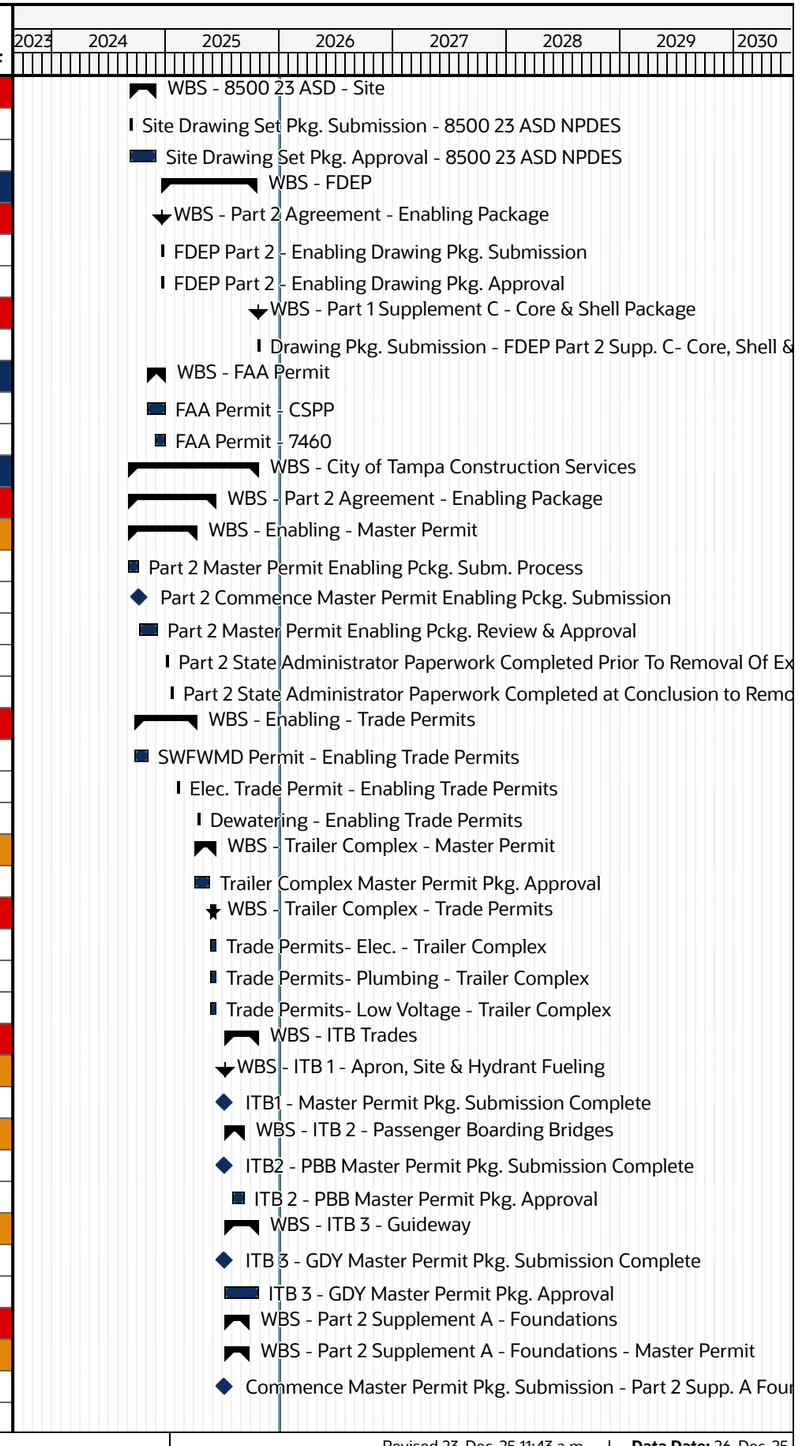


ID	Name	Dur	Start	Finish	TF
1597	PM-P2-2A-20	Master Permit Pkg. Approval - Part 2 Supp. A Found.	56.0d	3-Jul-25 A	22-Sep-25 A	
1598	WBS - Part 1 Supplement C - Core & Shell Package		1.0d	18-Sep-25 A	18-Sep-25 A	
1599	PM-P2-2B-10	Drawing Pkg. Submission - COT Const. Svs. -Part 1 Supp. C Core & Shell	1.0d	18-Sep-25 A	18-Sep-25 A	
1600	WBS - ASD - PROCUREMENT PHASE		263.0d	13-Dec-24 A	26-Dec-25 A	
1601	WBS - Contractor Furnished & Install (CFCI)		263.0d	13-Dec-24 A	26-Dec-25 A	
1602	WBS - Part 2 Agreement - Enabling Procurement		202.0d	13-Dec-24 A	29-Sep-25 A	
1603	WBS - Enabling - Priority 1 Submittals		148.0d	13-Dec-24 A	14-Jul-25 A	
1604	WBS - Enabling - Civil Sanitary Lift Station		148.0d	13-Dec-24 A	14-Jul-25 A	
1605	PR-P2-EN-20	Prep & Submit Sanitary Lift Station Submittals - Part 2 Agreement	44.0d	13-Dec-24 A	14-Feb-25 A	
1606	PR-P2-EN-740	Approve Sanitary System Lift Station Submittals - Part 2 Agreement	28.0d	17-Feb-25 A	26-Mar-25 A	
1607	PR-P2-EN-1070	Fab. & Ship Sanitary Lift Station - Part 2 Agreement	108.0d	27-Mar-25 A	14-Jul-25 A	
1608	PR-P2-EN-1420	Deliver Sanitary Lift Station - Part 2 Agreement	0.0d		14-Jul-25 A	
1609	WBS - Enabling - Civil Storm System Material		114.0d	13-Dec-24 A	23-May-25 A	
1610	PR-P2-EN-10	Prep & Submit Storm RCP System Submittals - Part 2 Agreement Syst. Material	22.0d	13-Dec-24 A	15-Jan-25 A	
1611	PR-P2-EN-730	Approve Storm RCP System Submittals - Part 2 Agreement Syst. Material	50.0d	16-Jan-25 A	26-Mar-25 A	
1612	PR-P2-EN-1060	Fab. & Ship RCP Storm System - Part 2 Agreement Syst. Material	58.0d	27-Mar-25 A	23-May-25 A	
1613	PR-P2-EN-1390	Deliver RCP Storm System - Part 2 Agreement Syst. Material	0.0d		23-May-25 A	
1614	WBS - Enabling - Electrical Switch Gear		90.0d	19-Dec-24 A	25-Apr-25 A	
1615	PR-P2-EN-90	Prep & Submit Switch Gear Submittals - Part 2 Agreement	2.0d	19-Dec-24 A	20-Dec-24 A	
1616	PR-P2-EN-630	Approve Switch Gear Submittals - Part 2 Agreement	39.0d	23-Dec-24 A	17-Feb-25 A	
1617	PR-P2-EN-950	Fab. & Ship Switch Gear Submittals - Part 2 Agreement	58.0d	18-Feb-25 A	16-Apr-25 A	
1618	PR-P2-EN-1410	Deliver Switch Gear Submittals - Part 2 Agreement	0.0d		25-Apr-25 A	
1619	WBS - Enabling - Electrical Fiber Optic Material		39.0d	13-Dec-24 A	7-Feb-25 A	
1620	PR-P2-EN-80	Prep & Submit Fiber Optic Submittals - Part 2 Agreement	25.0d	13-Dec-24 A	20-Jan-25 A	
1621	PR-P2-EN-620	Approve Fiber Optic Submittals - Part 2 Agreement	9.0d	21-Jan-25 A	31-Jan-25 A	
1622	PR-P2-EN-940	Fiber Optic Fab. & Ship - Part 2 Agreement	5.0d	3-Feb-25 A	7-Feb-25 A	
1623	PR-P2-EN-1270	Deliver Fiber Optic - Part 2 Agreement	0.0d		7-Feb-25 A	
1624	WBS - Enabling - AOA Fence		60.0d	17-Dec-24 A	12-Mar-25 A	
1625	PR-P2-EN-120	Prep & Submit Fencing Pkg. - Part 2 Agreement AOA Fence	16.0d	17-Dec-24 A	9-Jan-25 A	
1626	PR-P2-EN-410	Approve Fencing Submittals - Part 2 Agreement AOA Fence	8.0d	10-Jan-25 A	21-Jan-25 A	
1627	PR-P2-EN-580	Fab. & Ship Fencing - Part 2 Agreement AOA Fence	49.0d	22-Jan-25 A	11-Mar-25 A	
1628	PR-P2-EN-590	Deliver Fencing - Part 2 Agreement AOA Fence	0.0d		12-Mar-25 A	
1629	WBS - Enabling - Trailers		117.0d	23-Dec-24 A	6-Jun-25 A	
1630	PR-P2-EN-140	Prep & Submit Shop Drawings For Trailer Pkg. - Part 2 Agreement	29.0d	23-Dec-24 A	3-Feb-25 A	
1631	PR-P2-EN-500	Approval Of Trailer Pkg. - Part 2 Agreement	8.0d	4-Feb-25 A	13-Feb-25 A	
1632	PR-P2-EN-1290	COT Permit Review for Trailers - Part 2 Agreement	25.0d	4-Feb-25 A	10-Mar-25 A	
1633	PR-P2-EN-1370	Fab. & Ship Trailers - Part 2 Agreement	87.0d	11-Mar-25 A	6-Jun-25 A	
1634	PR-P2-EN-1400	Delivery of Trailers - Part 2 Agreement	0.0d		6-Jun-25 A	
1635	WBS - Enabling - Furniture		103.0d	18-Feb-25 A	14-Jul-25 A	
1636	PR-P2-EN-130	Prep & Submit Trailer Furniture Pkg. - Part 2 Agreement	27.0d	18-Feb-25 A	26-Mar-25 A	
1637	PR-P2-EN-1160	Approve Trailer Furniture Pkg. - Part 2 Agreement	41.0d	27-Mar-25 A	22-May-25 A	
1638	PR-P2-EN-1300	Fab. & Ship Trailer Furniture Pkg. - Part 2 Agreement	44.0d	23-May-25 A	7-Jul-25 A	

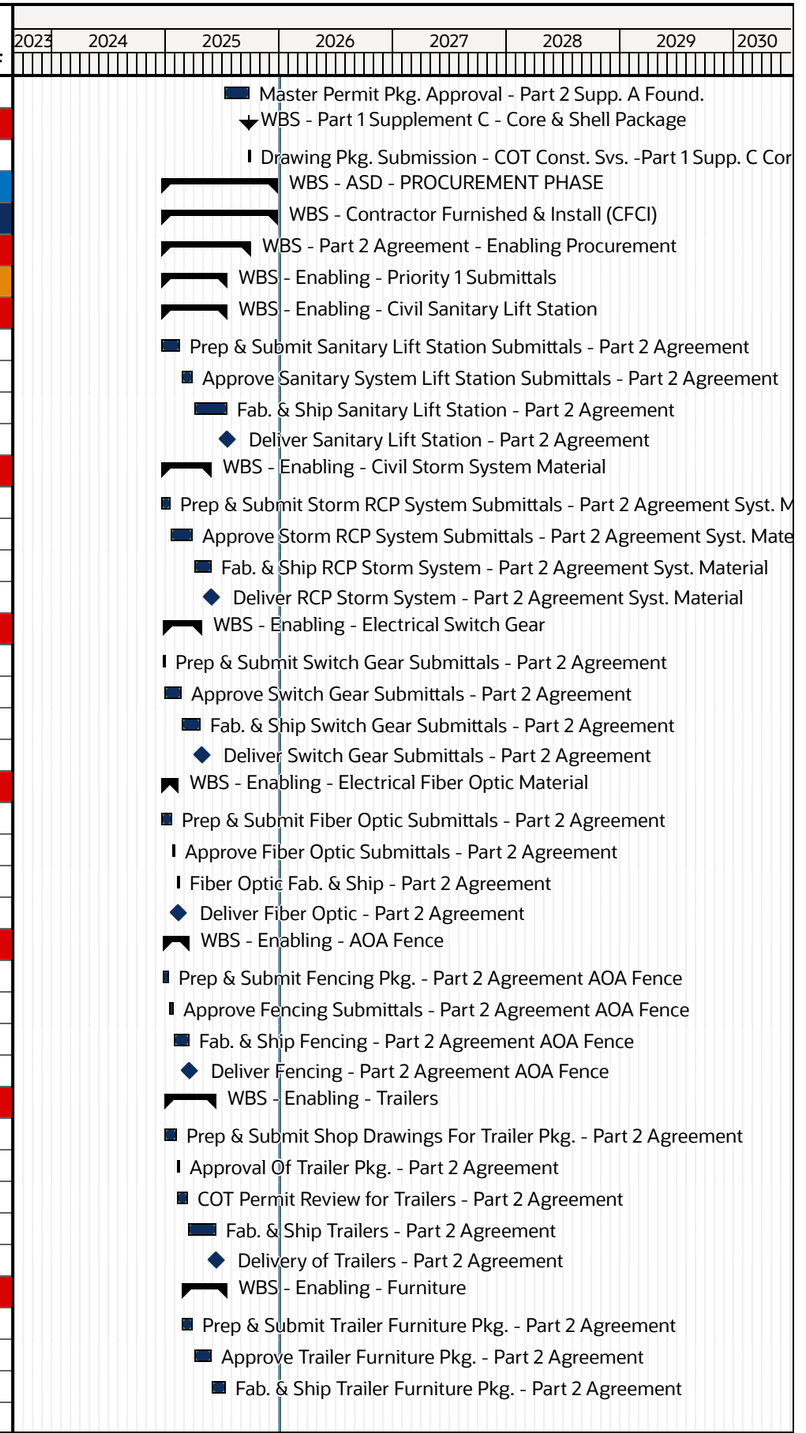


	ID	Name	Dur	Start	Finish	TF
1639	PR-P2-EN-1310	Deliver Trailer Furniture - Part 2 Agreement	0.0d		14-Jul-25 A	
1640	WBS - Enabling - Fuel Tank - Rebar		47.0d	13-Dec-24 A	19-Feb-25 A	
1641	PR-P2-EN-360	Prep & Submit Fuel Tank Rebar Pkg. - Part 2 Agreement	28.0d	13-Dec-24 A	23-Jan-25 A	
1642	PR-P2-EN-550	Approve Fuel Tank Rebar Submittals - Part 2 Agreement	11.0d	24-Jan-25 A	7-Feb-25 A	
1643	PR-P2-EN-850	Fab. & Ship Fuel Tank Rebar - Part 2 Agreement	10.0d	10-Feb-25 A	19-Feb-25 A	
1644	PR-P2-EN-1140	Deliver Fuel Tank Rebar - Part 2 Agreement	0.0d		19-Feb-25 A	
1645	WBS - Enabling - Fuel Tank - Concrete		39.0d	13-Dec-24 A	7-Feb-25 A	
1646	PR-P2-EN-370	Prep & Submit Fuel Tank Concrete Pkg. - Part 2 Agreement	24.0d	13-Dec-24 A	17-Jan-25 A	
1647	PR-P2-EN-560	Approve Fuel Tank Concrete Submittals - Part 2 Agreement	15.0d	20-Jan-25 A	7-Feb-25 A	
1648	WBS - Enabling - Fuel Tank - Electrical		49.0d	23-Dec-24 A	3-Mar-25 A	
1649	PR-P2-EN-380	Prep & Submit Fuel Tank Elec. Pkg. - Part 2 Agreement	18.0d	23-Dec-24 A	17-Jan-25 A	
1650	PR-P2-EN-570	Approve Fuel Tank Elec. Submittals - Part 2 Agreement	22.0d	20-Jan-25 A	18-Feb-25 A	
1651	PR-P2-EN-870	Fab. & Ship Fuel Tank Elec. - Part 2 Agreement	4.0d	25-Feb-25 A	28-Feb-25 A	
1652	PR-P2-EN-1260	Deliver Fuel Tank Elec. - Part 2 Agreement	0.0d		3-Mar-25 A	
1653	WBS - Enabling - Priority 2 Submittals		202.0d	13-Dec-24 A	29-Sep-25 A	
1654	WBS - Enabling - Civil Fire Line		176.0d	13-Dec-24 A	21-Aug-25 A	
1655	PR-P2-EN-60	Prep & Submit - Civil Fire Line Submittals - Priority 2	88.0d	13-Dec-24 A	17-Apr-25 A	
1656	PR-P2-EN-600	Approve Civil Fire Line Submittals - Priority 2	9.0d	18-Apr-25 A	30-Apr-25 A	
1657	PR-P2-EN-920	Fab. & Ship Civil Fire Line - Priority 2	32.0d	21-Jul-25 A	21-Aug-25 A	
1658	PR-P2-EN-1170	Deliver Civil Fire Line Complete - Priority 2	0.0d		21-Aug-25 A	
1659	WBS - Enabling - Civil Dewatering Equipment & Accessories		202.0d	13-Dec-24 A	29-Sep-25 A	
1660	PR-P2-EN-300	Prep & Submit - Civil Dewatering Equip. & Accessories Submittals - Priority 2	89.0d	13-Dec-24 A	18-Apr-25 A	
1661	PR-P2-EN-680	Approve Civil Dewatering Equip. & Accessories Submittals - Priority 2	8.0d	21-Apr-25 A	30-Apr-25 A	
1662	PR-P2-EN-1010	Fab. & Ship Civil Dewatering Equip. & Accessories - Priority 2	28.0d	1-May-25 A	29-May-25 A	
1663	PR-P2-EN-1230	Delivery Civil Dewatering Equip. & Accessories on Site - Priority 2	0.0d		29-Sep-25 A	
1664	WBS - Enabling - Civil MOT Bessie Coleman Cut Over		84.0d	13-Dec-24 A	11-Apr-25 A	
1665	PR-P2-EN-330	Prep & Submit - Civil MOT Bessie Coleman Cut Over Submittals - Priority 2	59.0d	13-Dec-24 A	7-Mar-25 A	
1666	PR-P2-EN-440	Approve Civil MOT Bessie Coleman Cut Over Submittals - Priority 2	2.0d	10-Mar-25 A	11-Mar-25 A	
1667	PR-P2-EN-710	Fab. & Ship - Civil MOT Bessie Coleman Cut Over - Priority 2	30.0d	12-Mar-25 A	10-Apr-25 A	
1668	PR-P2-EN-900	Delivery of Civil MOT Bessie Coleman Cut Over Complete - Priority 2	0.0d		11-Apr-25 A	
1669	WBS - Enabling - Lighting		123.0d	23-Dec-24 A	16-Jun-25 A	
1670	PR-P2-EN-200	Prep & Submit LTNG Submittals - Priority 2	18.0d	23-Dec-24 A	17-Jan-25 A	
1671	PR-P2-EN-790	Approve LTNG Submittals - Priority 2	26.0d	20-Jan-25 A	24-Feb-25 A	
1672	PR-P2-EN-1090	LTNG Fab. & Ship - Priority 2	111.0d	25-Feb-25 A	16-Jun-25 A	
1673	PR-P2-EN-1380	Delivery of LTNG Complete - Priority 2	0.0d		16-Jun-25 A	
1674	WBS - Enabling - Electrical Raceways & Accessories		54.0d	23-Dec-24 A	10-Mar-25 A	
1675	PR-P2-EN-220	Prep & Submit Raceways/Wiring & Accessories Submittals - Priority 2	29.0d	23-Dec-24 A	3-Feb-25 A	
1676	PR-P2-EN-640	Approve Raceways/Wiring & Accessories Submittals - Priority 2	11.0d	4-Feb-25 A	18-Feb-25 A	
1677	PR-P2-EN-970	Raceways/Wiring & Accessories Fab. & Ship - Priority 2	1.0d	19-Feb-25 A	19-Feb-25 A	
1678	PR-P2-EN-1190	Delivery of Raceways/Wiring & Accessories on Site - Priority 2	0.0d		10-Mar-25 A	
1679	WBS - Enabling - Electrical Disconnect Devices		49.0d	23-Dec-24 A	3-Mar-25 A	
1680	PR-P2-EN-230	Prep & Submit Disconnect Devices Submittals - Priority 2	29.0d	23-Dec-24 A	3-Feb-25 A	

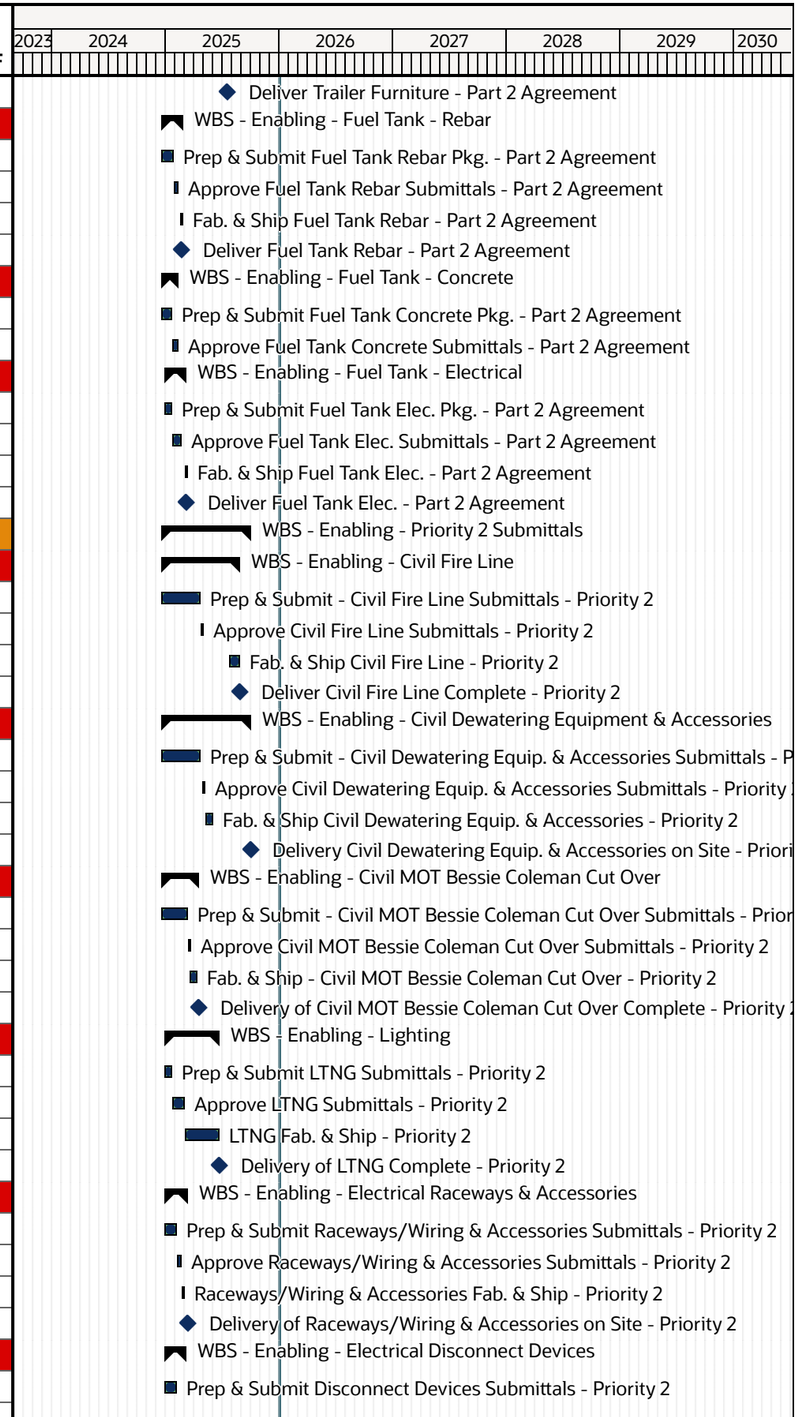

	ID	Name	Dur	Start	Finish	TF
1681	PR-P2-EN-530	Approve Disconnect Devices Submittals - Priority 2	11.0d	4-Feb-25 A	18-Feb-25 A	
1682	PR-P2-EN-800	Disconnect Devices Fab. & Ship - Priority 2	10.0d	19-Feb-25 A	28-Feb-25 A	
1683	PR-P2-EN-1050	Delivery of Disconnect Devices Complete - Priority 2	0.0d		3-Mar-25 A	
1684	WBS - Enabling - Data & Power		43.0d	25-Feb-25 A	24-Apr-25 A	
1685	PR-P2-EN-150	Design Trailer Data & Power Plan - Priority 2	30.0d	25-Feb-25 A	7-Apr-25 A	
1686	PR-P2-EN-1080	Approve Trailer Data & Power Plan - Priority 2	13.0d	8-Apr-25 A	24-Apr-25 A	
1687	WBS - Enabling - Security System		74.0d	18-Feb-25 A	2-Jun-25 A	
1688	PR-P2-EN-160	Approve Trailer Security Systems Product Data - Priority 2	15.0d	18-Feb-25 A	10-Mar-25 A	
1689	PR-P2-EN-510	Deliver Trailer Security Systems - Priority 2	0.0d		2-Jun-25 A	
1690	WBS - Enabling - Guard Booths		131.0d	4-Feb-25 A	7-Aug-25 A	
1691	PR-P2-EN-240	Prep & Submit Guard Booths Pkg. - Priority 2	15.0d	4-Feb-25 A	24-Feb-25 A	
1692	PR-P2-EN-810	Approve Guard Booths Submittals - Priority 2	30.0d	19-Mar-25 A	29-Apr-25 A	
1693	PR-P2-EN-1100	Fab. & Ship Guard Booths - Priority 2	29.0d	30-Apr-25 A	29-May-25 A	
1694	PR-P2-EN-1340	Delivery of Guard Booths Complete - Priority 2	0.0d		7-Aug-25 A	
1695	WBS - Enabling - Cameras & Poles		153.0d	20-Jan-25 A	22-Aug-25 A	
1696	PR-P2-EN-820	Approve Cameras (HCAA) & Poles Submittals - Priority 2	26.0d	20-Jan-25 A	24-Feb-25 A	
1697	PR-P2-EN-250	Prep & Submit Cameras & Poles Pkg. - Priority 2	16.0d	21-Feb-25 A	14-Mar-25 A	
1698	PR-P2-EN-1110	Fab. & Ship Cameras (HCAA) & Poles - Priority 2	111.0d	25-Feb-25 A	16-Jun-25 A	
1699	PR-P2-EN-1350	Delivery of Cameras (HCAA) & Poles Complete - Priority 2	0.0d		22-Aug-25 A	
1700	WBS - Enabling - Priority 3 Submittals		163.0d	6-Jan-25 A	22-Aug-25 A	
1701	WBS - Enabling - Civil Domestic Water Material		99.0d	1-Apr-25 A	20-Aug-25 A	
1702	PR-P2-EN-30	Prep & Submit Civil Domestic Water Submittals Material - Priority 3	12.0d	1-Apr-25 A	17-Apr-25 A	
1703	PR-P2-EN-B002-10	Bulletin 002 Conditional Commitment for Water Service Letter Received	0.0d	14-Apr-25 A		
1704	PR-P2-EN-B002-20	Bulletin 002 Water Service Letter Transmitted to HCAA for Payment	14.0d	15-Apr-25 A	2-May-25 A	
1705	PR-P2-EN-470	Approve Civil Domestic Water Submittals Material - Priority 3	9.0d	18-Apr-25 A	30-Apr-25 A	
1706	PR-P2-EN-B002-30	Bulletin 002 Tampa Water Dept Plan Review	49.0d	5-May-25 A	14-Jul-25 A	
1707	PR-P2-EN-B002-40	Bulletin 002 Tampa Water Dept Plan Approval	0.0d		16-Jul-25 A	
1708	PR-P2-EN-750	Fab. & Ship Civil Domestic Water Material - Priority 3	14.0d	17-Jul-25 A	30-Jul-25 A	
1709	PR-P2-EN-1150	Delivery of Civil Domestic Water Material Complete - Priority 3	0.0d		20-Aug-25 A	
1710	WBS - Enabling - Civil Concrete Mix		16.0d	27-Jan-25 A	17-Feb-25 A	
1711	PR-P2-EN-40	Prep & Submit Civil Concrete Mix Submittals - Priority 3	10.0d	27-Jan-25 A	7-Feb-25 A	
1712	PR-P2-EN-480	Approve Civil Concrete Mix Submittals - Priority 3	6.0d	10-Feb-25 A	17-Feb-25 A	
1713	WBS - Enabling - Civil Asphalt		8.0d	3-Mar-25 A	12-Mar-25 A	
1714	PR-P2-EN-50	Prep & Submit Civil Asphalt Submittals - Priority 3	4.0d	3-Mar-25 A	6-Mar-25 A	
1715	PR-P2-EN-490	Approve Civil Asphalt Submittals - Priority 3	5.0d	6-Mar-25 A	12-Mar-25 A	
1716	WBS - Enabling - Civil Sanitary Gravity Pipe & Accessories		56.0d	27-Jan-25 A	14-Apr-25 A	
1717	PR-P2-EN-270	Prep & Submit - Civil Sanitary Gravity Pipe & Accessories Submittals - Priority 3	21.0d	27-Jan-25 A	24-Feb-25 A	
1718	PR-P2-EN-650	Approve Civil Sanitary Gravity Pipe & Accessories Submittals - Priority 3	13.0d	25-Mar-25 A	10-Apr-25 A	
1719	PR-P2-EN-980	Fab. & Ship Civil Sanitary Gravity Pipe & Accessories - Priority 3	4.0d	11-Apr-25 A	14-Apr-25 A	
1720	PR-P2-EN-1200	Delivery of Civil Sanitary Gravity Pipe & Accessories Complete - Priority 3	0.0d		14-Apr-25 A	
1721	WBS - Enabling - Civil Underdrain Pipe & Accessories		114.0d	27-Jan-25 A	7-Jul-25 A	
1722	PR-P2-EN-290	Prep & Submit - Civil Underdrain Pipe & Accessories Submittals - Priority 3	21.0d	27-Jan-25 A	24-Feb-25 A	

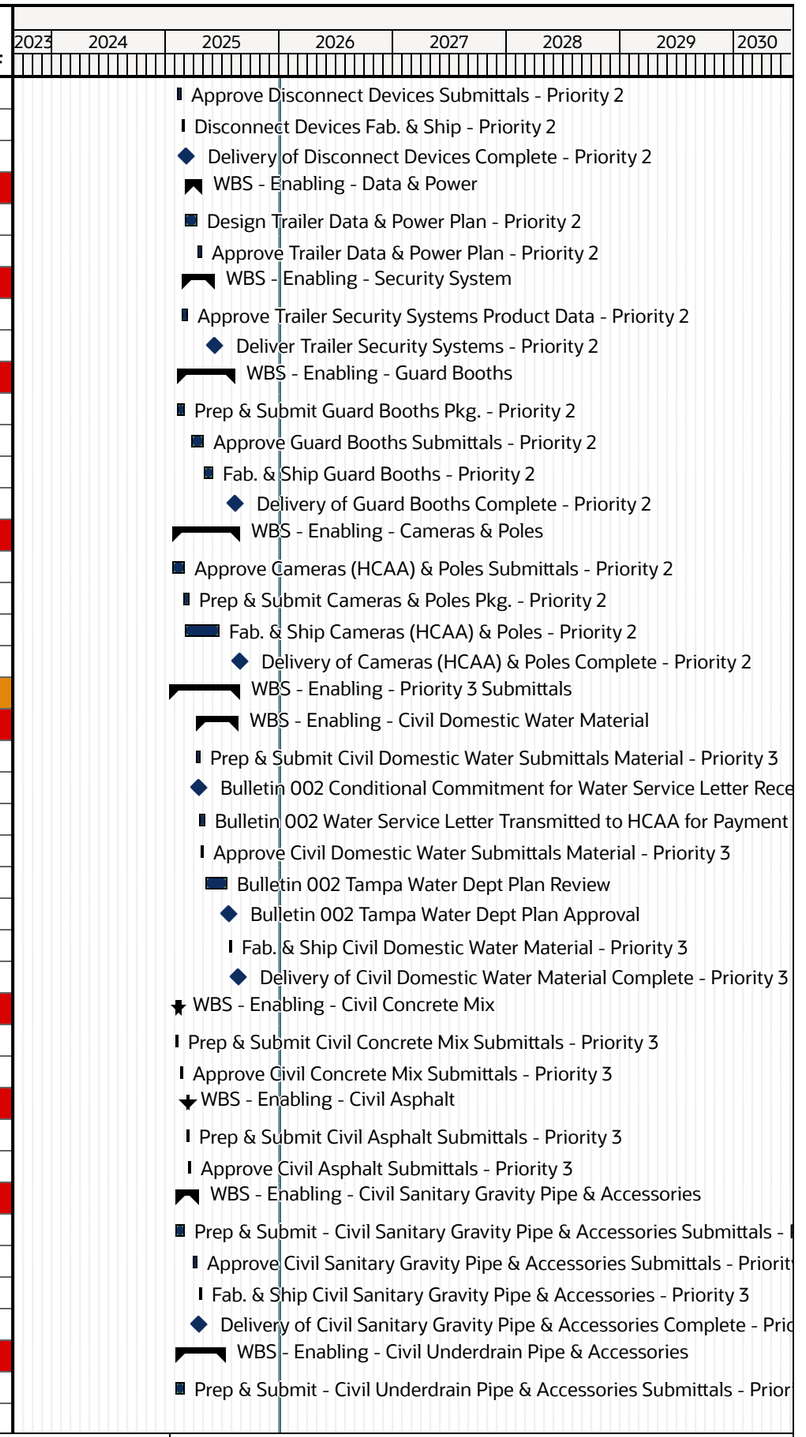

	ID	Name	Dur	Start	Finish	TF
1723	PR-P2-EN-670	Approve Civil Underdrain Pipe & Accessories Submittals - Priority 3	3.0d	18-Apr-25 A	22-Apr-25 A	
1724	PR-P2-EN-1000	Fab. & Ship Civil Underdrain Pipe & Accessories - Priority 3	54.0d	23-Apr-25 A	16-Jun-25 A	
1725	PR-P2-EN-1220	Delivery of Civil Underdrain Pipe & Accessories Complete - Priority 3	0.0d		7-Jul-25 A	
1726	WBS - Enabling - Electrical Low Voltage Material		40.0d	6-Jan-25 A	28-Feb-25 A	
1727	PR-P2-EN-70	Prep & Submit Low Voltage Material Submittals - Priority 3	9.0d	6-Jan-25 A	16-Jan-25 A	
1728	PR-P2-EN-610	Approve Low Voltage Material Submittals - Priority 3	11.0d	17-Jan-25 A	31-Jan-25 A	
1729	PR-P2-EN-930	Fab. & Ship Low Voltage Material - Priority 3	26.0d	3-Feb-25 A	28-Feb-25 A	
1730	PR-P2-EN-1180	Delivery of Low Voltage Material Complete - Priority 3	0.0d		28-Feb-25 A	
1731	WBS - Enabling - Break Shelter		51.0d	12-Jun-25 A	22-Aug-25 A	
1732	PR-P2-EN-260	Prep & Submit Break Shelter Pkg. - Priority 3	12.0d	12-Jun-25 A	27-Jun-25 A	
1733	PR-P2-EN-830	Approve Break Shelter Submittals - Priority 3	15.0d	30-Jun-25 A	21-Jul-25 A	
1734	PR-P2-EN-1120	Fab. & Ship Break Shelter - Priority 3	25.0d	22-Jul-25 A	15-Aug-25 A	
1735	PR-P2-EN-1360	Delivery of Break Shelter Complete - Priority 3	0.0d		22-Aug-25 A	
1736	WBS - Part 2 Supplement A - DIP / LTP, Foundations Package & Long Lead		130.0d	23-Jun-25 A	26-Dec-25 A	
1737	WBS - DIP / LTP Test Pile Program Materials		24.0d	23-Jun-25 A	25-Jul-25 A	
1738	PR-P2-1A-70	Prep & Submit Test Pile Program - Part 2 Supp. A DIP/LTP, Found. Package & Lo...	19.0d	23-Jun-25 A	21-Jul-25 A	
1739	PR-P2-1A-150	Approve Test Pile Program - Part 2 Supp. A DIP/LTP, Found. Package & Long Lead	13.0d	7-Jul-25 A	24-Jul-25 A	
1740	PR-P2-1A-280	Fab. & Ship Test Pile Program Materials - Part 2 Supp. A DIP/LTP, Found. Packa...	5.0d	21-Jul-25 A	25-Jul-25 A	
1741	PR-P2-1A-390	Deliver Test Pile Program Materials - Part 2 Supp. A DIP/LTP, Found. Package & ...	0.0d		25-Jul-25 A	
1742	WBS - DIP / LTP Test Pile Results		23.0d	21-Aug-25 A	23-Sep-25 A	
1743	PR-P2-1A-20	Prep & Submit DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP, Found. Packa...	11.0d	21-Aug-25 A	5-Sep-25 A	
1744	PR-P2-1A-140	Approve DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP, Found. Package & L...	7.0d	8-Sep-25 A	16-Sep-25 A	
1745	PR-P2-1A-145	Approve DIP/LTP Test Pile Results - Part 2 Supp. A DIP/LTP (Rev 1) (returned as ...	5.0d	17-Sep-25 A	23-Sep-25 A	
1746	WBS - DIP / LTP Production Design		74.0d	8-Sep-25 A	22-Dec-25 A	
1747	PR-P2-1A-800	Prep & Submit DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, ...	20.0d	8-Sep-25 A	3-Oct-25 A	
1748	PR-P2-1A-810	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	14.0d	6-Oct-25 A	23-Oct-25 A	
1749	PR-P2-1A-860	Fab. & Ship DIP/LTP Production Piles - Part 2 Supp. A DIP/LTP, Found. Package ...	22.0d	6-Oct-25 A	27-Oct-25 A	
1750	PR-P2-1A-815	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	7.0d	24-Oct-25 A	3-Nov-25 A	
1751	PR-P2-1A-820	Approve DIP/LTP Production Design Submittals - Part 2 Supp. A DIP/LTP, Foun...	22.0d	19-Nov-25 A	22-Dec-25 A	
1752	PR-P2-1A-870	Delivery of DIP/LTP Production Piles - Part 2 Supp. A DIP/LTP, Found. Package ...	0.0d		22-Dec-25 A	
1753	WBS - DIP / LTP Area 6-1 Shop Drawings		17.0d	10-Nov-25 A	4-Dec-25 A	
1754	PR-P2-1A-1860	Prep & Submit DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DIP...	15.0d	10-Nov-25 A	2-Dec-25 A	
1755	PR-P2-1A-1890	HP Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DIP/L...	1.0d	3-Dec-25 A	3-Dec-25 A	
1756	PR-P2-1A-1870	HNTB Approve DIP/LTP Area 6-1 Shop Drawings Submittals - Part 2 Supp. A DI...	0.0d	4-Dec-25 A	4-Dec-25 A	
1757	WBS - DIP / LTP Production Shoes & Caps		13.0d	15-Oct-25 A	27-Oct-25 A	
1758	PR-P2-1A-900	Fab. & Ship DIP/LTP Production Shoes & Caps - Part 2 Supp. A DIP/LTP, Found. ...	13.0d	15-Oct-25 A	27-Oct-25 A	
1759	PR-P2-1A-910	Delivery of DIP/LTP Production Shoes & Caps - Part 2 Supp. A DIP/LTP, Found. ...	0.0d		27-Oct-25 A	
1760	WBS - DIP / LTP Production Grout		6.0d	15-Oct-25 A	22-Oct-25 A	
1761	PR-P2-1A-920	Prep & Submit DIP/LTP Production Grout Submittals - Part 2 Supp. A DIP/LTP, F...	3.0d	15-Oct-25 A	19-Oct-25 A	
1762	PR-P2-1A-930	Approve DIP/LTP Production Grout Submittals - Part 2 Supp. A DIP/LTP, Found. ...	3.0d	20-Oct-25 A	22-Oct-25 A	
1763	WBS - Foundations Package		67.0d	22-Sep-25 A	26-Dec-25 A	
1764	WBS - Rebar Foundations Area 2		38.0d	10-Oct-25 A	4-Dec-25 A	

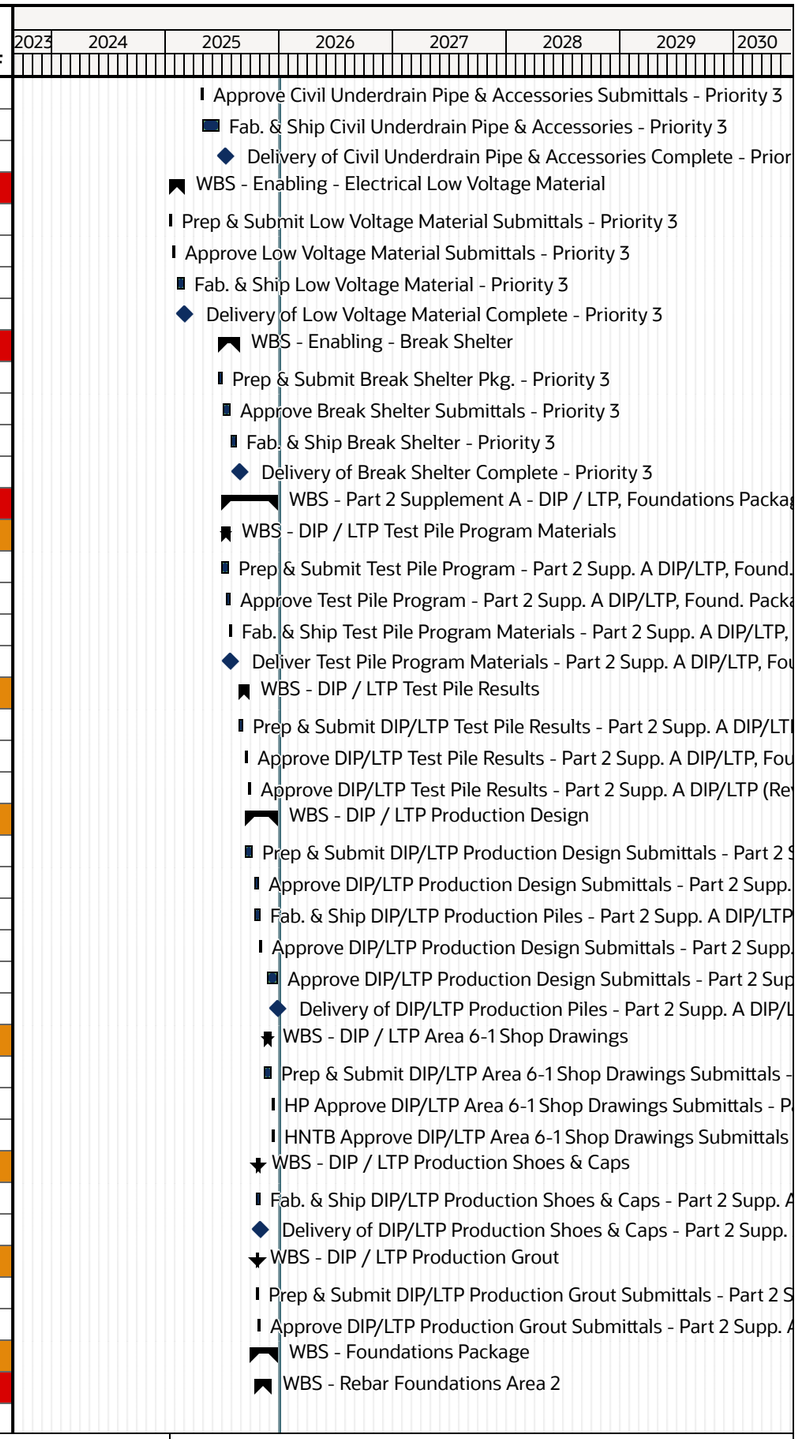

	ID	Name	Dur	Start	Finish	TF
1765	PR-P2-1A-80	Prep & Submit Rebar Found. Area 2 Submittals - Part 2 Supp. A	10.0d	10-Oct-25 A	23-Oct-25 A	
1766	PR-P2-1A-160	Approve Rebar Found. Area 2 Submittals - Part 2 Supp. A	12.0d	24-Oct-25 A	10-Nov-25 A	
1767	PR-P2-1A-1980	HCAA Approve Rebar Found. Area 2 Submittals - Part 2 Supp. A	16.0d	11-Nov-25 A	4-Dec-25 A	
1768	WBS - Rebar Foundations Area 6		59.0d	26-Sep-25 A	19-Dec-25 A	
1769	PR-P2-1A-90	Prep & Submit Rebar Found. Area 6 Submittals - Part 2 Supp. A	10.0d	26-Sep-25 A	9-Oct-25 A	
1770	PR-P2-1A-170	Approve Rebar Found. Area 6 Submittals - Part 2 Supp. A	11.0d	10-Oct-25 A	24-Oct-25 A	
1771	PR-P2-1A-410	Fab. & Ship Rebar Found. Area 6 - Part 2 Supp. A	45.0d	3-Nov-25 A	19-Dec-25 A	
1772	PR-P2-1A-420	Delivery of Rebar Found. Area 6 Complete - Part 2 Supp. A	0.0d		19-Dec-25 A	
1773	WBS - Rebar Foundations Area 1		31.0d	6-Nov-25 A	22-Dec-25 A	
1774	PR-P2-1A-1700	Prep & Submit Rebar Found. Area 1 Submittals - Part 2 Supp. A	22.0d	6-Nov-25 A	9-Dec-25 A	
1775	PR-P2-1A-1900	HP Approve Rebar Found. Area 1 Submittals - Part 2 Supp. A	9.0d	10-Dec-25 A	22-Dec-25 A	
1776	WBS - Rebar Foundations Area 3		25.0d	14-Nov-25 A	22-Dec-25 A	
1777	PR-P2-1A-1740	Prep & Submit Rebar Found. Area 3 Submittals - Part 2 Supp. A	1.0d	14-Nov-25 A	14-Nov-25 A	
1778	PR-P2-1A-1920	HP Approve Rebar Found. Area 3 Submittals - Part 2 Supp. A	24.0d	17-Nov-25 A	22-Dec-25 A	
1779	WBS - Rebar Foundations Area 5		40.0d	24-Oct-25 A	22-Dec-25 A	
1780	PR-P2-1A-1780	Prep & Submit Rebar Found. Area 5 Submittals - Part 2 Supp. A	11.0d	24-Oct-25 A	7-Nov-25 A	
1781	PR-P2-1A-1940	HP Approve Rebar Found. Area 5 Submittals - Part 2 Supp. A	29.0d	10-Nov-25 A	22-Dec-25 A	
1782	WBS - Rebar Foundations Area 4		17.0d	26-Nov-25 A	22-Dec-25 A	
1783	PR-P2-1A-1820	Prep & Submit Rebar Found. Area 4 Submittals - Part 2 Supp. A	10.0d	26-Nov-25 A	11-Dec-25 A	
1784	PR-P2-1A-1960	HP Approve Rebar Found. Area 4 Submittals - Part 2 Supp. A	7.0d	12-Dec-25 A	22-Dec-25 A	
1785	WBS - Anchor Bolts		64.0d	22-Sep-25 A	22-Dec-25 A	
1786	WBS - Anchor Bolts Pkg #2 - Area 1		56.0d	22-Sep-25 A	10-Dec-25 A	
1787	PR-P2-1A-500	GMF Detailer Drawing Completion Window - Area 1 - Part 2 Supp. A - Anchor B...	34.0d	22-Sep-25 A	6-Nov-25 A	
1788	PR-P2-1A-510	GMF DM Drawing Review - Area 1 - Part 2 Supp. A - Anchor Bolts	1.0d	7-Nov-25 A	7-Nov-25 A	
1789	PR-P2-1A-520	HP & A/E Team Review of Detail Drawing - Area 1 - Part 2 Supp. A - Anchor Bolts	7.0d	10-Nov-25 A	18-Nov-25 A	
1790	PR-P2-1A-530	Return From Approval - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		18-Nov-25 A	
1791	PR-P2-1A-740	GMF Detailer Drawing Scrub & Clean up Window - Area 1 - Part 2 Supp. A - Anc...	6.0d	19-Nov-25 A	26-Nov-25 A	
1792	PR-P2-1A-1120	GMF DM RFF Review - Area 1 - Part 2 Supp. A - Anchor Bolts	5.0d	21-Nov-25 A	1-Dec-25 A	
1793	PR-P2-1A-1130	Release for Fab. - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		1-Dec-25 A	
1794	PR-P2-1A-1140	Procurement of Material - Area 1 - Part 2 Supp. A - Anchor Bolts	7.0d	2-Dec-25 A	10-Dec-25 A	
1795	PR-P2-1A-1150	Steel on site - Abs - Start Shipping - Area 1 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	
1796	WBS - Anchor Bolts Pkg #1 Area 2		56.0d	22-Sep-25 A	10-Dec-25 A	
1797	PR-P2-1A-540	GMF Detailer Drawing Completion Window - Area 2 - Part 2 Supp. A - Anchor B...	22.0d	22-Sep-25 A	21-Oct-25 A	
1798	PR-P2-1A-550	GMF DM Drawing Review - Area 2 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Oct-25 A	21-Oct-25 A	
1799	PR-P2-1A-750	HP & A/E Team Review of Detail Drawing - Area 2 - Part 2 Supp. A - Anchor Bolts	15.0d	22-Oct-25 A	11-Nov-25 A	
1800	PR-P2-1A-570	GMF Detailer Drawing Scrub & Clean up Window - Area 2 - Part 2 Supp. A - Anc...	2.0d	7-Nov-25 A	10-Nov-25 A	
1801	PR-P2-1A-755	RFA'd 3 Days prior to 11/11 - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d	7-Nov-25 A	7-Nov-25 A	
1802	PR-P2-1A-560	Return From Approval - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		11-Nov-25 A	
1803	PR-P2-1A-940	GMF DM RFF Review - Area 2 - Part 2 Supp. A - Anchor Bolts	1.0d	12-Nov-25 A	12-Nov-25 A	
1804	PR-P2-1A-950	Release for Fab. - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		13-Nov-25 A	
1805	PR-P2-1A-960	Procurement of Material - Area 2 - Part 2 Supp. A - Anchor Bolts	17.0d	14-Nov-25 A	10-Dec-25 A	
1806	PR-P2-1A-970	Steel on site - Abs - Start Shipping - Area 2 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A	




ID	Name	Dur	Start	Finish	TF
1807	WBS - Anchor Bolts Pkg #2 Area 3	56.0d	22-Sep-25 A	10-Dec-25 A	
1808	PR-P2-1A-580	GMF Detailer Drawing Completion Window - Area 3 - Part 2 Supp. A - Anchor B...	34.0d	22-Sep-25 A	6-Nov-25 A
1809	PR-P2-1A-590	GMF DM Drawing Review - Area 3 - Part 2 Supp. A - Anchor Bolts	1.0d	7-Nov-25 A	7-Nov-25 A
1810	PR-P2-1A-600	HP & A/E Team Review of Detail Drawing - Area 3 - Part 2 Supp. A - Anchor Bolts	7.0d	10-Nov-25 A	18-Nov-25 A
1811	PR-P2-1A-610	Return From Approval - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		18-Nov-25 A
1812	PR-P2-1A-760	GMF Detailer Drawing Scrub & Clean up Window - Area 3 - Part 2 Supp. A - Anc...	6.0d	19-Nov-25 A	26-Nov-25 A
1813	PR-P2-1A-1210	GMF DM RFF Review - Area 3 - Part 2 Supp. A - Anchor Bolts	5.0d	21-Nov-25 A	1-Dec-25 A
1814	PR-P2-1A-1220	Release for Fab. - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		1-Dec-25 A
1815	PR-P2-1A-1230	Procurement of Material - Area 3 - Part 2 Supp. A - Anchor Bolts	7.0d	2-Dec-25 A	10-Dec-25 A
1816	PR-P2-1A-1240	Steel on site - Abs - Start Shipping - Area 3 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A
1817	WBS - Anchor Bolts Pkg #3 Area 4		64.0d	22-Sep-25 A	22-Dec-25 A
1818	PR-P2-1A-620	GMF Detailer Drawing Completion Window - Area 4 - Part 2 Supp. A - Anchor B...	44.0d	22-Sep-25 A	20-Nov-25 A
1819	PR-P2-1A-630	GMF DM Drawing Review - Area 4 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Nov-25 A	21-Nov-25 A
1820	PR-P2-1A-640	HP & A/E Team Review of Detail Drawing - Area 4 - Part 2 Supp. A - Anchor Bolts	14.0d	24-Nov-25 A	15-Dec-25 A
1821	PR-P2-1A-650	Return From Approval - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		15-Dec-25 A
1822	PR-P2-1A-780	GMF Detailer Drawing Scrub & Clean up Window - Area 4 - Part 2 Supp. A - Anc...	3.0d	16-Dec-25 A	18-Dec-25 A
1823	PR-P2-1A-1300	GMF DM RFF Review - Area 4 - Part 2 Supp. A - Anchor Bolts	2.0d	19-Dec-25 A	22-Dec-25 A
1824	PR-P2-1A-1310	Release for Fab. - Area 4 - Part 2 Supp. A - Anchor Bolts	0.0d		22-Dec-25 A
1825	WBS - Anchor Bolts Pkg #3 Area 5		64.0d	22-Sep-25 A	22-Dec-25 A
1826	PR-P2-1A-1340	GMF Detailer Drawing Completion Window - Area 5 - Part 2 Supp. A - Anchor B...	44.0d	22-Sep-25 A	20-Nov-25 A
1827	PR-P2-1A-1350	GMF DM Drawing Review - Area 5 - Part 2 Supp. A - Anchor Bolts	1.0d	21-Nov-25 A	21-Nov-25 A
1828	PR-P2-1A-1360	HP & A/E Team Review of Detail Drawing - Area 5 - Part 2 Supp. A - Anchor Bolts	14.0d	24-Nov-25 A	15-Dec-25 A
1829	PR-P2-1A-1370	Return From Approval - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		15-Dec-25 A
1830	PR-P2-1A-1380	GMF Detailer Drawing Scrub & Clean up Window - Area 5 - Part 2 Supp. A - Anc...	3.0d	16-Dec-25 A	18-Dec-25 A
1831	PR-P2-1A-1390	GMF DM RFF Review - Area 5 - Part 2 Supp. A - Anchor Bolts	2.0d	19-Dec-25 A	22-Dec-25 A
1832	PR-P2-1A-1400	Release for Fab. - Area 5 - Part 2 Supp. A - Anchor Bolts	0.0d		22-Dec-25 A
1833	WBS - Anchor Bolts Pkg #1 Area 6		56.0d	22-Sep-25 A	10-Dec-25 A
1834	PR-P2-1A-700	GMF Detailer Drawing Completion Window - Area 6 - Part 2 Supp. A - Anchor B...	22.0d	22-Sep-25 A	21-Oct-25 A
1835	PR-P2-1A-710	GMF DM Drawing Review - Area 6 - Part 2 Supp. A - Anchor Bolts	1.0d	22-Oct-25 A	22-Oct-25 A
1836	PR-P2-1A-790	HP & A/E Team Review of Detail Drawing - Area 6 - Part 2 Supp. A - Anchor Bolts	15.0d	22-Oct-25 A	11-Nov-25 A
1837	PR-P2-1A-730	GMF Detailer Drawing Scrub & Clean up Window - Area 6 - Part 2 Supp. A - Anc...	2.0d	7-Nov-25 A	10-Nov-25 A
1838	PR-P2-1A-720	Return From Approval - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		11-Nov-25 A
1839	PR-P2-1A-1030	GMF DM RFF Review - Area 6 - Part 2 Supp. A - Anchor Bolts	1.0d	12-Nov-25 A	12-Nov-25 A
1840	PR-P2-1A-1040	Release for Fab. - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		13-Nov-25 A
1841	PR-P2-1A-1050	Procurement of Material - Area 6 - Part 2 Supp. A - Anchor Bolts	17.0d	14-Nov-25 A	10-Dec-25 A
1842	PR-P2-1A-1060	Steel on site - Abs - Start Shipping - Area 6 - Part 2 Supp. A - Anchor Bolts	0.0d		10-Dec-25 A
1843	WBS - Embeds		67.0d	22-Sep-25 A	26-Dec-25 A
1844	WBS - Embeds - Pkg #1 - Area 1-2-3-4-5-6		56.0d	22-Sep-25 A	10-Dec-25 A
1845	PR-P2-1A-1530	Embeds Pkg #1 - GMF Detailer Drawing Completion Window - Area 1-2-3-4-5-...	28.0d	22-Sep-25 A	29-Oct-25 A
1846	PR-P2-1A-1535	Embeds Pkg #1 - GMF DM Drawing Review - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		29-Oct-25 A
1847	PR-P2-1A-1550	Embeds Pkg #1 - HP & A/E Team Review of Detail Drawing - Area 1-2-3-4-5-6 ...	9.0d	30-Oct-25 A	11-Nov-25 A
1848	PR-P2-1A-1560	Embeds Pkg #1 - Return From Approval - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		11-Nov-25 A




	ID	Name	Dur	Start	Finish	TF
1849	PR-P2-1A-1570	Embeds Pkg #1 - GMF Detailer Drawing Scrub & Clean up Window - Area 1-2-3...	3.0d	12-Nov-25 A	14-Nov-25 A	
1850	PR-P2-1A-1572	Embeds Pkg #1 - GMF DM RFF Review - Area 1-2-3-4-5-6 - Part 2 Supp. A	5.0d	12-Nov-25 A	18-Nov-25 A	
1851	PR-P2-1A-1575	Embeds Pkg #1 - Release for Fab. - Area 1-2-3-4-5-6 - Part 2 Supp. A	0.0d		18-Nov-25 A	
1852	PR-P2-1A-1600	Embeds Pkg #1 - Fab. of Embeds - Area 1-2-3-4-5-6 - Part 2 Supp. A	14.0d	19-Nov-25 A	10-Dec-25 A	
1853	PR-P2-1A-1610	Embeds Pkg #1 - Embeds on Site - Start Shipping - Area 1-2-3-4-5-6 - Part 2 ...	0.0d		10-Dec-25 A	
1854	WBS - Embeds - Pkg. #2 - Area 6.1 - Cooling Tower (If needed)		39.0d	30-Oct-25 A	26-Dec-25 A	
1855	PR-P2-1A-1620	Embeds Pkg #2 - GMF Detailer Drawing Completion Window - Area 6.1 - Part 2...	39.0d	30-Oct-25 A	26-Dec-25 A	
1856	WBS - Concrete Mix Designs		22.0d	10-Oct-25 A	10-Nov-25 A	
1857	PR-P2-1A-10	Prep & Submit Found. Concrete Mix Designs Submittals - Part 2 Supp. A Groun...	7.0d	10-Oct-25 A	20-Oct-25 A	
1858	PR-P2-1A-220	Approve Found. Concrete Mix Designs Submittals - Part 2 Supp. A Ground Impr...	15.0d	21-Oct-25 A	10-Nov-25 A	
1859	WBS - Underground Waterproofing		62.0d	8-Sep-25 A	4-Dec-25 A	
1860	PR-P2-1A-60	Prep Underground Waterproofing Submittals (Contractor) - Part 2 Supp. A	6.0d	8-Sep-25 A	15-Sep-25 A	
1861	PR-P2-1A-65	Review & Submit Underground Waterproofing Submittals (HP) - Part 2 Supp. A	11.0d	16-Sep-25 A	30-Sep-25 A	
1862	PR-P2-1A-270	Review & Approve Underground Waterproofing Submittals (HNTB) - Part 2 Sup...	10.0d	1-Oct-25 A	14-Oct-25 A	
1863	PR-P2-1A-275	Review & Approve Underground Waterproofing Submittals (HCAA) - Part 2 Sup...	35.0d	15-Oct-25 A	4-Dec-25 A	
1864	WBS - Underground Electrical Conduit		46.0d	15-Oct-25 A	19-Dec-25 A	
1865	PR-P2-1A-40	Prep Underground Elec. Conduit System Submittals (Contractor) - Part 2 Supp. A	5.0d	15-Oct-25 A	21-Oct-25 A	
1866	PR-P2-1A-42	Prep Underground Elec. Conduit System Submittals (Contractor) - Part 2 Supp. ...	4.0d	28-Oct-25 A	31-Oct-25 A	
1867	PR-P2-1A-250	Review & Approve Underground Elec. Conduit System Submittals (HNTB) - Part...	10.0d	3-Nov-25 A	14-Nov-25 A	
1868	PR-P2-1A-45	Review & Submit Underground Elec. Conduit System Submittals (HP) - Part 2 S...	1.0d	3-Nov-25 A	3-Nov-25 A	
1869	PR-P2-1A-255	Review & Approve Underground Elec. Conduit System Submittals (HCAA) - Part...	14.0d	14-Nov-25 A	5-Dec-25 A	
1870	PR-P2-1A-370	Fab. & Ship Underground Elec. Conduit System - Part 2 Supp. A	12.0d	8-Dec-25 A	19-Dec-25 A	
1871	PR-P2-1A-490	Delivery of Underground Elec. Conduit System on Site - Part 2 Supp. A	0.0d		19-Dec-25 A	
1872	WBS - Underground Chilled Water Piping & Sleeves		76.0d	8-Sep-25 A	24-Dec-25 A	
1873	PR-P2-1A-50	Prep Underground Chilled Water Sleeves Submittals (Contractor) - Part 2 Supp. A	21.0d	8-Sep-25 A	6-Oct-25 A	
1874	PR-P2-1A-55	Review & Submit Underground Chilled Water Sleeves Submittals (HP) - Part 2 S...	6.0d	20-Oct-25 A	27-Oct-25 A	
1875	PR-P2-1A-260	Review & Approve Underground Chilled Water Sleeves Submittals (HNTB) - Par...	10.0d	28-Oct-25 A	10-Nov-25 A	
1876	PR-P2-1A-265	Review & Approve Underground Chilled Water Sleeves Submittals (HCAA) - Par...	15.0d	11-Nov-25 A	3-Dec-25 A	
1877	PR-P2-1A-300	Fab. & Ship Underground Chilled Water Sleeves - Part 2 Supp. A	21.0d	4-Dec-25 A	24-Dec-25 A	
1878	PR-P2-1A-440	Delivery of Underground Chilled Water Sleeves on Site- Part 2 Supp. A	0.0d		24-Dec-25 A	
1879	WBS - Underground Plumbing Submittals - ASD		54.0d	6-Oct-25 A	22-Dec-25 A	
1880	PR-P2-1A-61	Prep Underground Plumbing Submittals (Contractor) - Part 2 Supp. A	16.0d	6-Oct-25 A	27-Oct-25 A	
1881	PR-P2-1A-63	Review & Submit Underground Plumbing Submittals (HP) - Part 2 Supp. A	5.0d	28-Oct-25 A	3-Nov-25 A	
1882	PR-P2-1A-66	Review & Approve Underground Plumbing Submittals (HNTB) - Part 2 Supp. A	10.0d	4-Nov-25 A	17-Nov-25 A	
1883	PR-P2-1A-68	Review & Approve Underground Plumbing Submittals (HCAA) - Part 2 Supp. A	17.0d	18-Nov-25 A	12-Dec-25 A	
1884	PR-P2-1A-71	Fab. & Ship Underground Plumbing - Part 2 Supp. A	2.0d	15-Dec-25 A	16-Dec-25 A	
1885	PR-P2-1A-73	Delivery of Underground Plumbing on Site - Part 2 Supp. A	0.0d		22-Dec-25 A	
1886	WBS - Long Lead Electrical		39.0d	20-Oct-25 A	15-Dec-25 A	
1887	WBS - Gear, Metering, SPD & Coordination Study		39.0d	20-Oct-25 A	15-Dec-25 A	
1888	WBS - Gear Layout Package		39.0d	20-Oct-25 A	15-Dec-25 A	
1889	PR-P2-1B-7800	Prep & Submit Gear Layout Submittals - Part 2 Supp. A	25.0d	20-Oct-25 A	21-Nov-25 A	
1890	PR-P2-1B-7810	Approve Gear Layout Submittals - Part 2 Supp. A	14.0d	24-Nov-25 A	15-Dec-25 A	



ID	Name	Dur	Start	Finish	TF
1891	WBS - Long Lead Mechanical	30.0d	12-Nov-25 A	26-Dec-25 A	
1892	WBS - Chillers Procurement	30.0d	12-Nov-25 A	26-Dec-25 A	
1893	PR-P2-1B-100 Prep & Submit Chillers Submittals - Part 2 Supp. A	30.0d	12-Nov-25 A	26-Dec-25 A	
1894	WBS - Long Lead Mill Order	20.0d	3-Nov-25 A	2-Dec-25 A	
1895	PR-P2-1B-3400 Prep & Submit Steel Mill Order Submittals - Part 2 Supp. A	20.0d	3-Nov-25 A	2-Dec-25 A	
1896	WBS - Part 2 Supplement B - ASD Steel & Precast	38.0d	31-Oct-25 A	26-Dec-25 A	
1897	WBS - Structural Steel / Misc. Metals Procurement	38.0d	31-Oct-25 A	26-Dec-25 A	
1898	WBS - Structural Steel Seq 1	33.0d	31-Oct-25 A	18-Dec-25 A	
1899	PR-P2-1B-7600 GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 1 - ...	28.0d	31-Oct-25 A	11-Dec-25 A	
1900	PR-P2-1B-7610 GMF DM Drawing Review Struct. Steel/Misc. Metals Submittals SEQ 1 - Part 2 S...	5.0d	12-Dec-25 A	18-Dec-25 A	
1901	WBS - Structural Steel Seq 2	38.0d	31-Oct-25 A	26-Dec-25 A	
1902	PR-P2-1B-3710 GMF Detailer Drawing Completion Window - Struct. Steel/Misc. Metals SEQ 2 - ...	38.0d	31-Oct-25 A	26-Dec-25 A	
1903	WBS - Precast Procurement	24.0d	11-Nov-25 A	16-Dec-25 A	
1904	WBS - Elevator Cores	24.0d	11-Nov-25 A	16-Dec-25 A	
1905	PR-P2-1B-6700 Prep & Submit Elevator Cores Submittals - Part 2 Supp. B	14.0d	11-Nov-25 A	2-Dec-25 A	
1906	PR-P2-1B-6710 HP Review & Submit Elevator Cores Submittals - Part 2 Supp. B	10.0d	3-Dec-25 A	16-Dec-25 A	
1907	WBS - Part 1 Supplement C Wave 1 - Core & Shell Procurement	40.0d	20-Oct-25 A	16-Dec-25 A	
1908	WBS - Baggage Handling System Procurement - ASD	40.0d	20-Oct-25 A	16-Dec-25 A	
1909	WBS - General BHS Submittals & Procurement - ASD	40.0d	20-Oct-25 A	16-Dec-25 A	
1910	WBS - Site Specific Safety Plans Submittals - ASD	40.0d	20-Oct-25 A	16-Dec-25 A	
1911	A109210 Prep & Submit Site Specific Safety Plans - ASD	13.0d	20-Oct-25 A	5-Nov-25 A	
1912	A109220 Review & Approve (HP) Site Specific Safety Plans - ASD	2.0d	6-Nov-25 A	7-Nov-25 A	
1913	A109230 Review & Approve (HNTB) Site Specific Safety Plans - ASD	11.0d	10-Nov-25 A	24-Nov-25 A	
1914	A109240 Review & Approve (HCAA) Site Specific Safety Plans - ASD	14.0d	25-Nov-25 A	16-Dec-25 A	
1915	WBS - VDC Coordination	53.0d	7-Oct-25 A	22-Dec-25 A	
1916	PR-VDC-10 Kickoff Meeting - VDC Coordination	0.0d	7-Oct-25 A		
1917	WBS - Deep Underground - VDC Coordination	53.0d	7-Oct-25 A	22-Dec-25 A	
1918	PR-VDC-DU-300 Model, Coordinate & Sign-off Deep UG East - VDC Coordination	29.0d	7-Oct-25 A	14-Nov-25 A	
1919	PR-VDC-DU-310 Model, Coordinate & Sign-off Deep UG West - VDC Coordination	42.0d	21-Oct-25 A	19-Dec-25 A	
1920	WBS - Deep UG East VDC Coordination	24.0d	17-Nov-25 A	22-Dec-25 A	
1921	WBS - Mechanical Shop Drawings - Deep UG East VDC Coordination	12.0d	18-Nov-25 A	5-Dec-25 A	
1922	PR-VDC-DU-4080 Prep & Submit Deep UG East Mech. Shop Drawings	2.0d	18-Nov-25 A	19-Nov-25 A	
1923	PR-VDC-DU-4090 Review & Approve (HP) Deep UG East Mech. Shop Drawings	2.0d	20-Nov-25 A	21-Nov-25 A	
1924	PR-VDC-DU-4060 Review & Approve (HNTB) Deep UG East Mech. Shop Drawings	3.0d	21-Nov-25 A	25-Nov-25 A	
1925	PR-VDC-DU-4070 Review & Approve (HCAA) Deep UG East Mech. Shop Drawings	6.0d	26-Nov-25 A	5-Dec-25 A	
1926	WBS - Electrical & Low Voltage Shop Drawings - Deep UG East VDC Coordination	15.0d	17-Nov-25 A	9-Dec-25 A	
1927	PR-VDC-DU-4160 Prep & Submit Deep UG East Elec. Shop Drawings	5.0d	17-Nov-25 A	21-Nov-25 A	
1928	PR-VDC-DU-4170 Review & Approve (HP) Deep UG East Elec.Shop Drawings	5.0d	24-Nov-25 A	2-Dec-25 A	
1929	PR-VDC-DU-4180 Review & Approve (HNTB) Deep UG East Elec. Shop Drawings	5.0d	24-Nov-25 A	2-Dec-25 A	
1930	PR-VDC-DU-4190 Review & Approve (HCAA) Deep UG East Elec. Shop Drawings	2.0d	3-Dec-25 A	4-Dec-25 A	
1931	PR-VDC-DU-4200 Fab. & Ship Deep UG East Elec. Shop Drawings	6.0d	4-Dec-25 A	9-Dec-25 A	
1932	WBS - Plumbing Shop Drawings - Deep UG East VDC Coordination	23.0d	18-Nov-25 A	22-Dec-25 A	

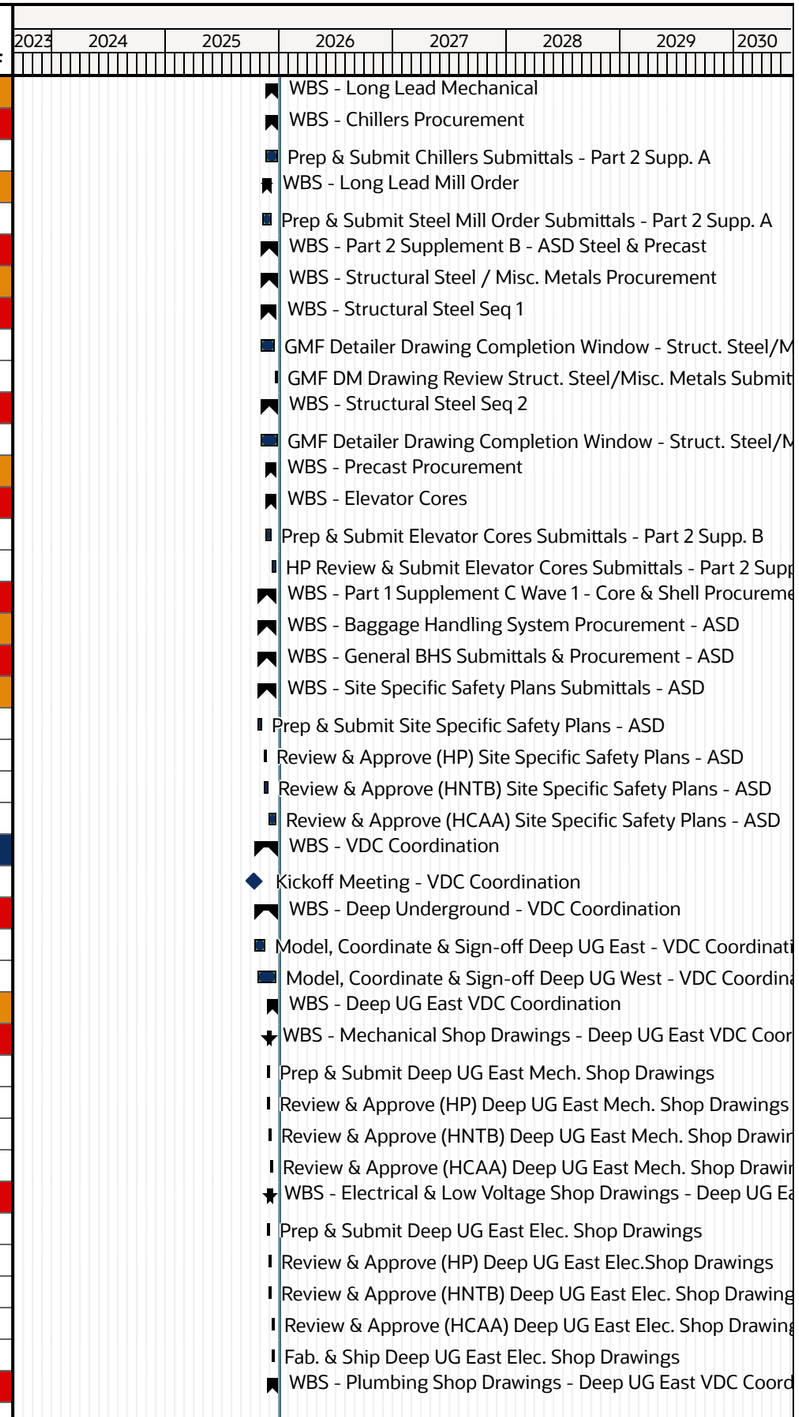


	ID	Name	Dur	Start	Finish	TF
1933	PR-VDC-DU-4110	Prep & Submit Deep UG East Plumbing Shop Drawings	2.0d	18-Nov-25 A	19-Nov-25 A	
1934	PR-VDC-DU-4120	Review & Approve (HP) Deep UG East Plumbing Shop Drawings	2.0d	20-Nov-25 A	21-Nov-25 A	
1935	PR-VDC-DU-4130	Review & Approve (HNTB) Deep UG East Plumbing Shop Drawings	3.0d	21-Nov-25 A	25-Nov-25 A	
1936	PR-VDC-DU-4140	Review & Approve (HCAA) Deep UG East Plumbing Shop Drawings	6.0d	26-Nov-25 A	5-Dec-25 A	
1937	PR-VDC-DU-4150	Fab. & Ship Deep UG East Plumbing Shop Drawings	17.0d	6-Dec-25 A	22-Dec-25 A	
1938	WBS - ASD - CONSTRUCTION PHASE		260.0d	13-Dec-24 A	22-Dec-25 A	
1939	WBS - Enabling		259.0d	13-Dec-24 A	19-Dec-25 A	
1940	WBS - Milestones		236.0d	13-Dec-24 A	14-Nov-25 A	
1941	EN-MLS-10	Notice to Proceed / Enabling Scope Construction Start	0.0d	13-Dec-24 A		
1942	EN-MLS-20	Personnel Transition to Trailers Complete	0.0d		3-Oct-25 A	
1943	EN-MLS-40	ASD - Enabling Water Line Complete	0.0d		14-Nov-25 A	
1944	WBS - Hammocks		126.0d	19-Feb-25 A	15-Aug-25 A	
1945	EN-HAM-30	Fuel Tank Relocation Scope - (LOE)	25.0d	19-Feb-25 A	25-Mar-25 A	
1946	EN-HAM-20	Bessie Coleman Closure Detour Scope - (LOE)	83.0d	21-Apr-25 A	15-Aug-25 A	
1947	WBS - Phase A Work Area		200.0d	7-Jan-25 A	16-Oct-25 A	
1948	EN-DM-PHA-10	Install Low Profile Barricades North Of VSR & SW Of VSR at TOFA Boundaries - ...	4.0d	7-Jan-25 A	10-Jan-25 A	
1949	EN-DM-PHA-20	Demo Exist. Taxiway B Markings - Phase A	2.0d	30-Jan-25 A	31-Jan-25 A	
1950	EN-DM-PHA-50	Demo Exist. Taxiway V Markings - Phase A	2.0d	31-Jan-25 A	3-Feb-25 A	
1951	EN-DM-PHA-110	Paint Edge Markings At Taxiway - Phase A	1.0d	5-Feb-25 A	5-Feb-25 A	
1952	EN-DM-PHA-80	De-Energize Exist. Taxiway Apron LTNG - Phase A	3.0d	27-Feb-25 A	3-Mar-25 A	
1953	EN-DM-PHA-40	Demo Exist. Taxiway Apron LTNG, Wiring & Conduit (Store Fixtures Safely) - Ph...	1.0d	4-Mar-25 A	4-Mar-25 A	
1954	EN-DM-PHA-30	Demo Exist. Taxiway U Markings At NE On VSR - Phase A	1.0d	14-Mar-25 A	14-Mar-25 A	
1955	EN-DM-PHA-90	Paint Directional Markings In Area At New VSR (Centerline, Edge, Stop Marking...	2.0d	18-Mar-25 A	19-Mar-25 A	
1956	EN-DM-PHA-120	Install White, Semi-Flushed Roadway Reflectors - Phase A	2.0d	18-Mar-25 A	19-Mar-25 A	
1957	EN-DM-PHA-60	Demo Exist. Taxi Lane Z/Stop Bar Markings on SW Of VSR - Phase A	1.0d	25-Apr-25 A	25-Apr-25 A	
1958	EN-DM-PHA-100	Paint Edge Markings At Zipper Roadway - Phase A	1.0d	25-Apr-25 A	25-Apr-25 A	
1959	EN-DM-PHA-130	Install Signage - Phase A	5.0d	28-Jul-25 A	1-Aug-25 A	
1960	EN-DM-PHA-70	Obscure & Demo Exist. Airfield Guidance Signage - Phase A	1.0d	16-Oct-25 A	16-Oct-25 A	
1961	WBS - Phase B Work Area		230.0d	27-Jan-25 A	19-Dec-25 A	
1962	WBS - Trailer Complex		230.0d	27-Jan-25 A	19-Dec-25 A	
1963	WBS - Parking Lot		207.0d	27-Jan-25 A	14-Nov-25 A	
1964	EN-AT-PL-10	Construct Sediment Barrier/Staked Turbidity Barrier Erosion Control - Phase B ...	10.0d	27-Jan-25 A	7-Feb-25 A	
1965	EN-AT-PL-340	Demo Exist. AOA Fence - Phase B Parking Lot	4.0d	18-Feb-25 A	21-Feb-25 A	
1966	EN-AT-PL-20	Clear & Grub - Phase B Parking Lot	8.0d	24-Feb-25 A	5-Mar-25 A	
1967	EN-AT-PL-70	Install / Shape Ditch at Parking Perimeter - Phase B Parking Lot	15.0d	24-Feb-25 A	14-Mar-25 A	
1968	EN-AT-PL-130	Cut Exist. Grade & Lvl. To Base Elevation - Phase B Parking Lot	3.0d	6-Mar-25 A	10-Mar-25 A	
1969	EN-AT-PL-160	Fill & Compact Subgrade Layer - Phase B Parking Lot	3.0d	6-Mar-25 A	10-Mar-25 A	
1970	EN-AT-PL-180	Fill & Compact 6" Base Layers - Phase B Parking Lot	3.0d	11-Mar-25 A	14-Mar-25 A	
1971	EN-AT-PL-150	Install Underg. Utilities In Parking Lot for Lights, EV Stations & Cameras - Phase...	19.0d	18-Mar-25 A	11-Apr-25 A	
1972	EN-AT-PL-30	Install Elec. Infrastructure Main to Complex - (For TECO Main) - Phase B Parkin...	42.0d	14-Apr-25 A	11-Jun-25 A	
1973	EN-AT-PL-140	Install UG Utilities/Data For New Guard Booth - Phase B Parking Lot	37.0d	23-Apr-25 A	13-Jun-25 A	
1974	EN-AT-PL-50	Install Data Infrastructure to Complex - (For Frontier Main) - Phase B Parking Lot	15.0d	27-May-25 A	16-Jun-25 A	

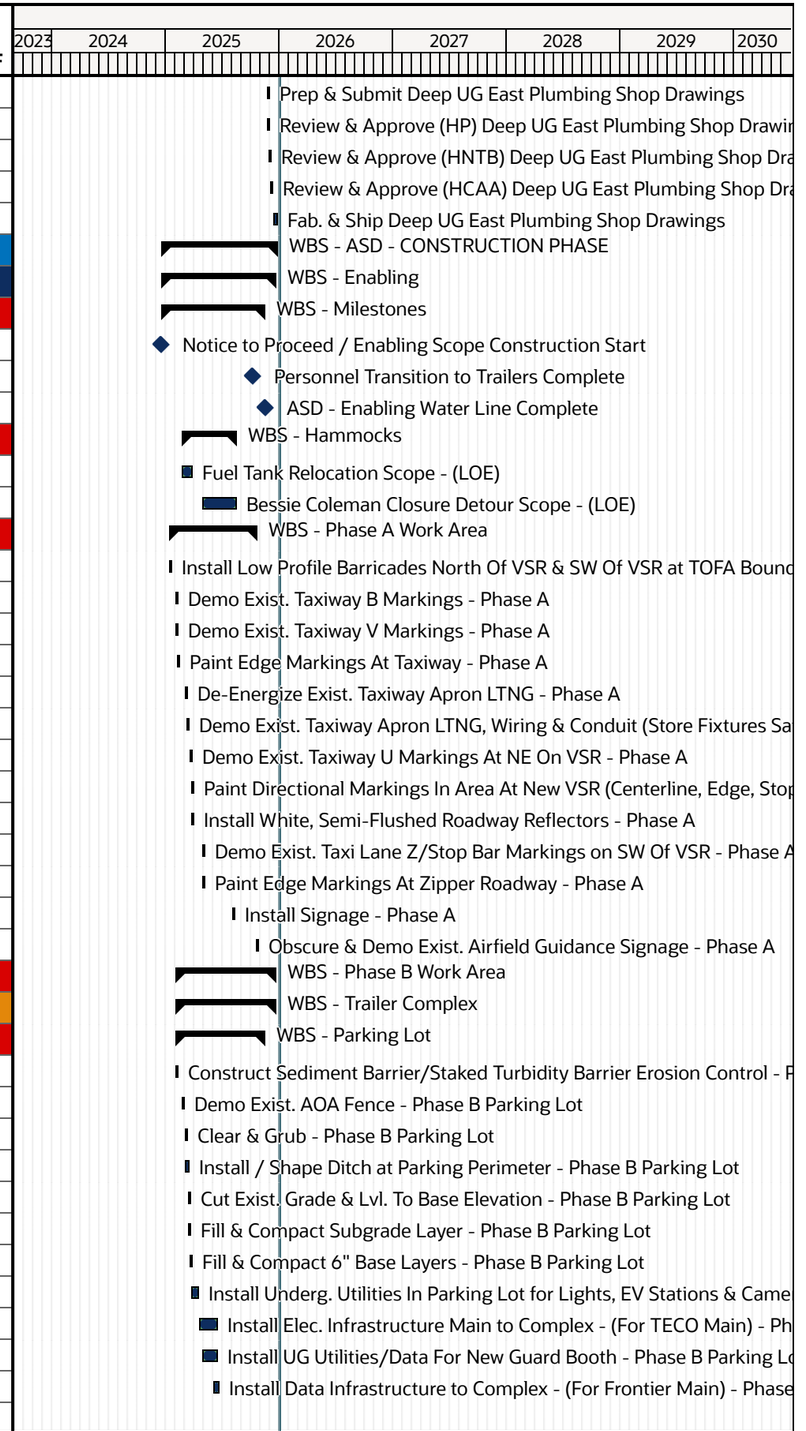


	ID	Name	Dur	Start	Finish	TF
1975	EN-AT-PL-60	Install 66' OF 14" x 23" ERCP (S-210, S-211) - Phase B Parking Lot	9.0d	27-May-25 A	6-Jun-25 A	
1976	EN-AT-PL-200	FRP Elec. Equip. Pads - Phase B Parking Lot	15.0d	3-Jun-25 A	23-Jun-25 A	
1977	EN-AT-PL-210	Set Elec. Equip. - Phase B Parking Lot	15.0d	4-Jun-25 A	24-Jun-25 A	
1978	EN-AT-PL-90	Install 6' x 2' Sumps (2 each) - Phase B Parking Lot	2.0d	9-Jun-25 A	10-Jun-25 A	
1979	EN-AT-PL-220	Install Paving - Phase B Parking Lot	4.0d	11-Jun-25 A	16-Jun-25 A	
1980	EN-AT-PL-120	Trailer Complex TECO Transformer Live - Phase B Parking Lot	0.0d		11-Jun-25 A	
1981	EN-AT-PL-80	Install 3" FM To Lift Station Location - Phase B Parking Lot	25.0d	14-Jul-25 A	15-Aug-25 A	
1982	EN-AT-PL-280	Install LTNG Poles/ Fixtures - Phase B Parking Lot	20.0d	28-Jul-25 A	22-Aug-25 A	
1983	EN-AT-PL-170	Provide Power & Disconnect to the Lift Station - Phase B Parking Lot	5.0d	28-Jul-25 A	1-Aug-25 A	
1984	EN-AT-PL-360	Precon Meeting with COT - Phase B Parking Lot	0.0d	5-Aug-25 A		
1985	EN-AT-PL-370	Perform Layout & Locates- Phase B Parking Lot	5.0d	6-Aug-25 A	12-Aug-25 A	
1986	EN-AT-PL-270	Set Guard Shack & Connect Utilities - Phase B Parking Lot	10.0d	8-Aug-25 A	21-Aug-25 A	
1987	EN-AT-PL-250	Install Sanitary Lift Station at Trailers - Phase B Parking Lot	48.0d	18-Aug-25 A	23-Oct-25 A	
1988	EN-AT-PL-40	Install 12", 10" & 6" Water Main to Complex - Phase B Parking Lot	40.0d	25-Aug-25 A	10-Oct-25 A	
1989	EN-AT-PL-240	Install Temporary Striping - Phase B Parking Lot	3.0d	26-Aug-25 A	28-Aug-25 A	
1990	EN-AT-PL-330	Install Signage - Phase B Parking Lot	46.0d	12-Sep-25 A	14-Nov-25 A	
1991	EN-AT-PL-350	Install Paving - Phase B Parking Lot - West Entrance & Tie-in to Excellence Dr.	2.0d	17-Sep-25 A	18-Sep-25 A	
1992	EN-AT-PL-310	Install EV Station Pedestals - Phase B Parking Lot	3.0d	18-Sep-25 A	22-Sep-25 A	
1993	EN-AT-PL-320	Install Permanent Striping - Phase B Parking Lot	4.0d	23-Sep-25 A	26-Sep-25 A	
1994	EN-AT-PL-300	Install Break Area Structure - Phase B Parking Lot	9.0d	7-Oct-25 A	17-Oct-25 A	
1995	EN-AT-PL-110	Lay Sod at Perimeter - Phase B Parking Lot	5.0d	21-Oct-25 A	27-Oct-25 A	
1996	EN-AT-PL-380	DEP Approval	2.0d	6-Nov-25 A	7-Nov-25 A	
1997	EN-AT-PL-190	FRP For Submeter & Backflow Preventer Assembly - Phase B Parking Lot	3.0d	10-Nov-25 A	12-Nov-25 A	
1998	EN-AT-PL-100	Install 1" Water Service to Hose Bibb at Lift Station Location From 8" Water Sup...	3.0d	12-Nov-25 A	14-Nov-25 A	
1999	WBS - Office Trailers		168.0d	23-Apr-25 A	19-Dec-25 A	
2000	EN-AT-TC-90	Install Elec. Mains to All Office Trailers - Phase B	32.0d	23-Apr-25 A	6-Jun-25 A	
2001	EN-AT-TC-20	Install 2" Fiber Conduit from North Parking Lot to Office Trailers - Phase B	56.0d	23-Apr-25 A	11-Jul-25 A	
2002	EN-AT-TC-10	Install Office Trailers - Phase B	40.0d	19-May-25 A	15-Jul-25 A	
2003	EN-AT-TC-60	Trim Out Trailer Seams & Roofing for Office Trailers - Phase B	39.0d	27-May-25 A	21-Jul-25 A	
2004	EN-AT-TC-180	Install 8" & 6" Sanitary Supply Lines to All Office Trailers - Phase B	20.0d	10-Jul-25 A	6-Aug-25 A	
2005	EN-AT-TC-100	Install Data Infrastructure to All Office Trailers - Phase B	11.0d	18-Jul-25 A	1-Aug-25 A	
2006	EN-AT-TC-80	Install Horizontal Data Cabling to Office Trailers - Phase B	15.0d	21-Jul-25 A	8-Aug-25 A	
2007	EN-AT-TC-220	Install Office Trailers' Furniture - Phase B	59.0d	21-Jul-25 A	10-Oct-25 A	
2008	EN-AT-TC-40	Install Ramp, Steps & Decks for Office Trailers - Phase B	19.0d	11-Aug-25 A	5-Sep-25 A	
2009	EN-AT-TC-110	Install 12" x 4"W Telecom Main Grounding Bar at 18" AFF To Bond All Office Tr...	5.0d	11-Aug-25 A	15-Aug-25 A	
2010	EN-AT-TC-190	Install Canopies to Office Trailers - Phase B	40.0d	18-Aug-25 A	13-Oct-25 A	
2011	EN-AT-TC-120	Terminate Data in Office Trailers IT Closet - Phase B	5.0d	18-Aug-25 A	22-Aug-25 A	
2012	EN-AT-TC-200	Install Gutters & Downspouts to Office Trailers - Phase B	21.0d	28-Aug-25 A	26-Sep-25 A	
2013	EN-AT-TC-130	IT Closet Server Install & Commission Office Trailers - Phase B	8.0d	29-Aug-25 A	10-Sep-25 A	
2014	EN-AT-TC-70	Install 8", 6", 2" & 1" Water Supply Lines w/All Associated Devices to All Office T...	29.0d	15-Sep-25 A	17-Oct-25 A	
2015	EN-AT-TC-150	Install Fire Hydrant (Office Trailers) - Phase B	1.0d	15-Sep-25 A	15-Sep-25 A	
2016	EN-AT-TC-170	Final Cleaning (Office Trailers) - Phase B	11.0d	1-Oct-25 A	15-Oct-25 A	




	ID	Name	Dur	Start	Finish	TF
2017	EN-AT-TC-230	Personnel Trans. to Office Trailers Complete - Phase B	0.0d		3-Oct-25 A	
2018	EN-AT-TC-160	Install (4) 6" Steel Fire Hydrant Protection Pipe Bollards (Office Trailers) - Phase B	4.0d	4-Nov-25 A	7-Nov-25 A	
2019	EN-AT-TC-240	Install 1" Water Service to Hose Bibb from 2" Water Supply Main for Office Trail...	4.0d	11-Nov-25 A	14-Nov-25 A	
2020	EN-AT-TC-30	Install Above Ground Submeter Assembly on Slab for Office Trailers - Phase B	2.0d	12-Nov-25 A	13-Nov-25 A	
2021	EN-AT-TC-50	Install Backflow Preventer Assembly on Slab for Office Trailers - Phase B	2.0d	13-Nov-25 A	14-Nov-25 A	
2022	EN-AT-TC-210	Office Trailers City Insp. for CO - Phase B	4.0d	17-Nov-25 A	20-Nov-25 A	
2023	EN-AT-TC-235	Construct FDOT Asphaltic Concrete Curb & a FDOT Type II Trench Drain (RFI - E...	22.0d	24-Nov-25 A	19-Dec-25 A	
2024	WBS - Road to ASD Site From Trailer Complex		202.0d	19-Feb-25 A	4-Dec-25 A	
2025	EN-AT-RD-10	TSA / CBP / HCAA / HP Walk New AOA Fence & Trans. VSR Final Configuration	1.0d	9-Sep-25 A	9-Sep-25 A	
2026	EN-AT-RD-20	TSA / CBP / HCAA Comment Correction	2.0d	10-Sep-25 A	11-Sep-25 A	
2027	EN-AT-RD-30	Final TSA/CBP/HCAA/HP AOA Fence Walk	1.0d	12-Sep-25 A	12-Sep-25 A	
2028	EN-AT-RD-40	Trans. Access Road to Final Configuration	0.0d		12-Sep-25 A	
2029	WBS - North Gate		202.0d	19-Feb-25 A	4-Dec-25 A	
2030	EN-AT-RDNG-20	Remove/ Relocate Exist. Fence as Needed - Phase B North Gate	3.0d	19-Feb-25 A	21-Feb-25 A	
2031	EN-AT-RDNG-10	Layout Road & Sidewalk Perimeters - Phase B North Gate	5.0d	25-Feb-25 A	3-Mar-25 A	
2032	EN-AT-RDNG-40	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Phase ...	3.0d	25-Feb-25 A	27-Feb-25 A	
2033	EN-AT-RDNG-80	Install 52' Of 14"x23" ERCP (S-207, S-208, S-209) - Phase B North Gate	11.0d	27-May-25 A	10-Jun-25 A	
2034	EN-AT-RDNG-30	Remove Exist. Guard Shack - Phase B North Gate	1.0d	6-Jun-25 A	6-Jun-25 A	
2035	EN-AT-RDNG-50	Clear & Grub at Roadway - Phase B North Gate	3.0d	9-Jun-25 A	11-Jun-25 A	
2036	EN-AT-RDNG-70	Install UG Utilities/Data for New Guard Booth - (Approx. 450' +/-) - Phase B No...	24.0d	12-Jun-25 A	16-Jul-25 A	
2037	EN-AT-RDNG-110	Fill & Compact Subgrade Layer - Phase B North Gate	10.0d	12-Jun-25 A	25-Jun-25 A	
2038	EN-AT-RDNG-120	Fill & Compact 6" Base Layers - Phase B North Gate	23.0d	13-Jun-25 A	16-Jul-25 A	
2039	EN-AT-RDNG-60	Connect To Exist. AOA Fence w/Sliding Gates - Phase B North GSE	34.0d	18-Jun-25 A	5-Aug-25 A	
2040	EN-AT-RDNG-90	Install (2) 6' x 2' Sumps - Phase B North Gate	2.0d	28-Jul-25 A	29-Jul-25 A	
2041	EN-AT-RDNG-160	FRP Guard Shack Concrete Pad - Phase B North Gate	1.0d	4-Aug-25 A	4-Aug-25 A	
2042	EN-AT-RDNG-220	Connect To Exist. AOA Fence w/Sliding Gates - Phase B South GSE	2.0d	4-Aug-25 A	5-Aug-25 A	
2043	EN-AT-RDNG-180	Set Guard Shack & Connect Utilities - Phase B North Gate	10.0d	8-Aug-25 A	21-Aug-25 A	
2044	EN-AT-RDNG-170	Install Light Poles - Phase B North Gate	5.0d	18-Aug-25 A	22-Aug-25 A	
2045	EN-AT-RDNG-190	Connect Guard Shack to Data/Power - Phase B North Gate	2.0d	21-Aug-25 A	22-Aug-25 A	
2046	EN-AT-RDNG-200	Install Cameras at Guard Gate - Phase B North Gate	3.0d	26-Aug-25 A	28-Aug-25 A	
2047	EN-AT-RDNG-130	Install Paving - 1st - 2" Lift - Phase B North Gate	1.0d	15-Sep-25 A	15-Sep-25 A	
2048	EN-AT-RDNG-210	Install Permanent Striping - Phase B North Gate	5.0d	15-Sep-25 A	19-Sep-25 A	
2049	EN-AT-RDNG-140	Install Paving - 2nd - 2" Lift - Phase B North Gate	1.0d	17-Sep-25 A	17-Sep-25 A	
2050	EN-AT-RDNG-150	Install Temporary Striping - Phase B North Gate	0.0d	19-Sep-25 A	19-Sep-25 A	
2051	EN-AT-RDNG-100	Lay Sod at Perimeter - Phase B North Gate	5.0d	26-Nov-25 A	4-Dec-25 A	
2052	WBS - South Gate		155.0d	20-Feb-25 A	29-Sep-25 A	
2053	EN-AT-RDSG-20	Remove AOA Exist. Fence - Phase B South Gate	5.0d	20-Feb-25 A	26-Feb-25 A	
2054	EN-AT-RDSG-10	Layout Road & Sidewalk Perimeters - Phase B South Gate	5.0d	4-Mar-25 A	10-Mar-25 A	
2055	EN-AT-RDSG-100	Fill & Compact Subgrade Layer - Phase B South Gate	4.0d	11-Mar-25 A	14-Mar-25 A	
2056	EN-AT-RDSG-30	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Phase ...	3.0d	11-Mar-25 A	13-Mar-25 A	
2057	EN-AT-RDSG-50	Install UG Utilities/Data For New Guard Booth - (Approx. 450' +/-) - Phase B So...	33.0d	27-May-25 A	11-Jul-25 A	
2058	EN-AT-RDSG-80	Install 52' Of 18" RCP To (2) 4' Of 30" RCP w/Concrete Jackets & S-200, S-201 ...	27.0d	2-Jun-25 A	9-Jul-25 A	

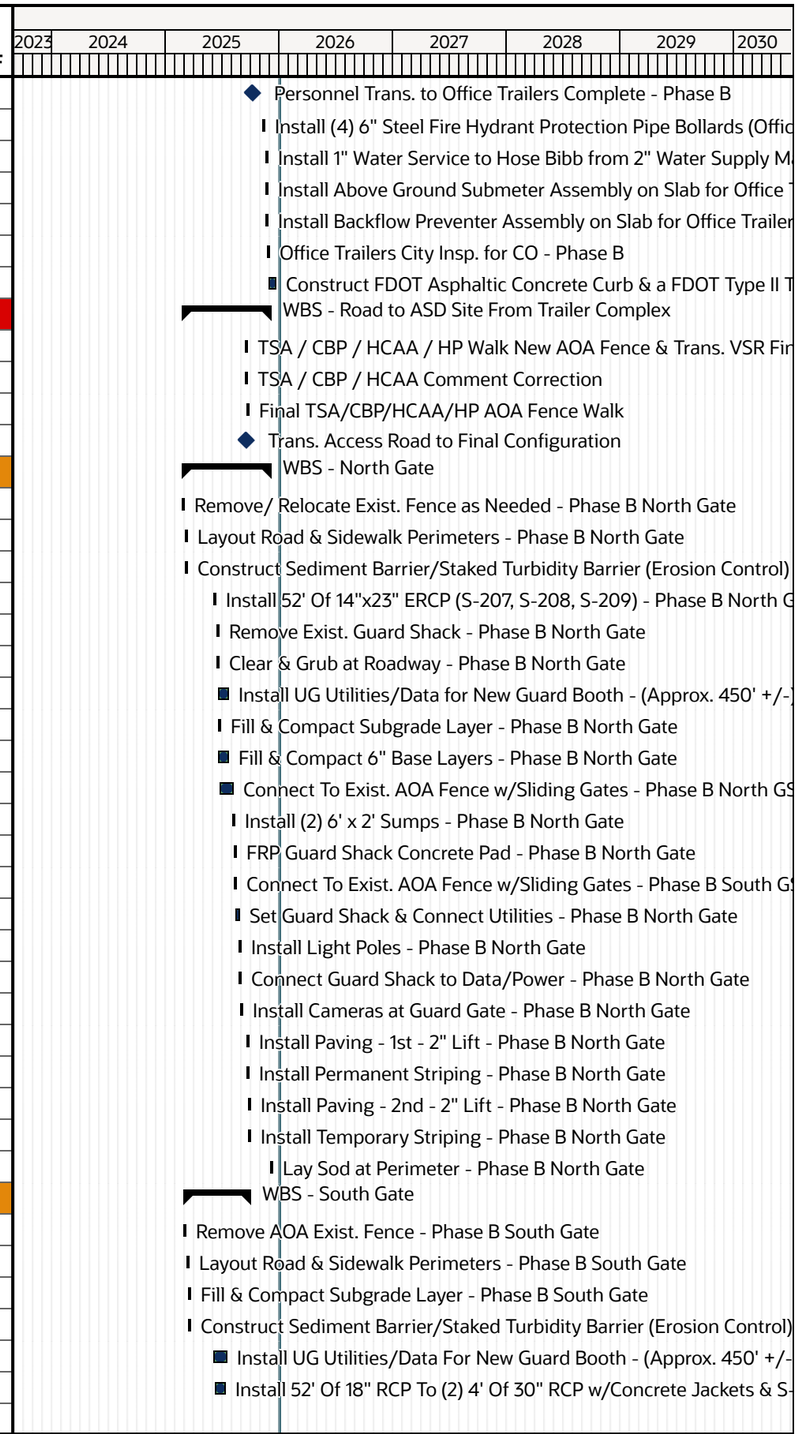


	ID	Name	Dur	Start	Finish	TF
2059	EN-AT-RDSG-60	Install 73' At 12"x18" ERCP & S-206 - Phase B South Gate	5.0d	1-Jul-25 A	8-Jul-25 A	
2060	EN-AT-RDSG-70	Install 43' Of 18" RCP & 4' Of 24" RCP To 4' Of 30" & 42" RCP w/Concrete Jack...	12.0d	10-Jul-25 A	25-Jul-25 A	
2061	EN-AT-RDSG-150	FRP Guard Shack Pad - Phase B South Gate	2.0d	28-Jul-25 A	29-Jul-25 A	
2062	EN-AT-RDSG-40	Connect To Exist. AOA Fence w/Sliding Gates - Phase B South Gate	4.0d	28-Jul-25 A	31-Jul-25 A	
2063	EN-AT-RDSG-110	Fill & Compact 6" Base Layers - Phase B South Gate	7.0d	28-Jul-25 A	5-Aug-25 A	
2064	EN-AT-RDSG-170	Set Guard Shack & Connect Utilities - Phase B South Gate	11.0d	8-Aug-25 A	22-Aug-25 A	
2065	EN-AT-RDSG-180	Connect Guard Shack to Data/Power - Phase B South Gate	2.0d	18-Aug-25 A	19-Aug-25 A	
2066	EN-AT-RDSG-160	Install Light Poles - Phase B South Gate	5.0d	18-Aug-25 A	22-Aug-25 A	
2067	EN-AT-RDSG-190	Install Cameras at Guard Shack - Phase B South Gate	3.0d	26-Aug-25 A	28-Aug-25 A	
2068	EN-AT-RDSG-120	Install Paving - 1st - 2" Lift - Phase B South Gate	1.0d	15-Sep-25 A	15-Sep-25 A	
2069	EN-AT-RDSG-130	Install Paving - 2nd - 2" Lift - Phase B South Gate	1.0d	17-Sep-25 A	17-Sep-25 A	
2070	EN-AT-RDSG-140	Install Temporary Striping - Phase B South Gate	1.0d	19-Sep-25 A	19-Sep-25 A	
2071	EN-AT-RDSG-200	Install Permanent Striping - Phase B South Gate	1.0d	26-Sep-25 A	26-Sep-25 A	
2072	EN-AT-RDSG-90	Construct Concrete Gutter Trans. Between Exist. Edge of Pavement & S-203 - P...	2.0d	26-Sep-25 A	29-Sep-25 A	
2073	WBS - Phase C Work Area		227.0d	6-Jan-25 A	21-Nov-25 A	
2074	EN-DM-PHC-40	Install Temporary Lighted Channelizing Cones for Active VSR - Phase C	5.0d	6-Jan-25 A	10-Jan-25 A	
2075	EN-DM-PHC-50	Decommission Exist. Monitor Wells - Phase C	2.0d	9-Jan-25 A	10-Jan-25 A	
2076	EN-DM-PHC-60	Layout for Fence/Sliding Guard Gate Install - Phase C	3.0d	22-Jan-25 A	24-Jan-25 A	
2077	EN-DM-PHC-30	Mobilize Site Safety & SWPPP BMPs - Phase C	5.0d	27-Jan-25 A	31-Jan-25 A	
2078	EN-DM-PHC-80	Install Signage - Phase C	5.0d	27-Jan-25 A	31-Jan-25 A	
2079	EN-DM-PHC-90	Install AOA Fencing/Sliding Guard Gate - Phase C	145.0d	29-Jan-25 A	23-Jun-25 A	
2080	EN-DM-PHC-120	De-Energize All Airfield LTNG - Phase C	1.0d	3-Feb-25 A	3-Feb-25 A	
2081	EN-DM-PHC-150	Remove Exist. Airfield LTNG Poles & Bases - Phase C	1.0d	26-Feb-25 A	26-Feb-25 A	
2082	EN-DM-PHC-70	Camera & Laser Profile Exist. Utilities Prior to Demolition - Phase C	4.0d	3-Mar-25 A	6-Mar-25 A	
2083	EN-DM-PHC-200	Trans. VSR to Perimeter of ASD AOA Fence - Phase C	1.0d	25-Apr-25 A	25-Apr-25 A	
2084	EN-DM-PHC-110	TECO - De-Energize Exist. 300kva Transformer - Phase C	1.0d	19-May-25 A	19-May-25 A	
2085	EN-DM-PHC-140	Relocate Exist. Elec. Equip. to be Reused - Phase C	1.0d	19-May-25 A	19-May-25 A	
2086	EN-DM-PHC-180	Install Non-AOA Fencing - Phase C	39.0d	2-Jun-25 A	25-Jul-25 A	
2087	EN-DM-PHC-130	Intercept Sanitary Upstream of Triturator & Cut / Cap - Phase C	3.0d	11-Jun-25 A	13-Jun-25 A	
2088	EN-DM-PHC-250	Apron Exist. Fuel Line & Utilities Removal - Phase C	18.0d	11-Jun-25 A	7-Jul-25 A	
2089	EN-DM-PHC-160	TSA / CBP / HCAA / HP Walk New AOA Fence & Trans. VSR Initial Insp. - Phase C	1.0d	8-Aug-25 A	8-Aug-25 A	
2090	EN-DM-PHC-170	TSA / CBP / HCAA Comment Correction - Phase C	5.0d	11-Aug-25 A	15-Aug-25 A	
2091	EN-DM-PHC-190	Final TSA/CBP/HCAA/HP AOA Fence Walk Insp. - Phase C	1.0d	15-Aug-25 A	15-Aug-25 A	
2092	EN-DM-PHC-210	Demo Exist. AOA Fence - Phase C	5.0d	18-Aug-25 A	22-Aug-25 A	
2093	EN-DM-PHC-100	Exist. 12" Water Main Intercept & Install Above Ground Manifold - Phase C	5.0d	17-Nov-25 A	21-Nov-25 A	
2094	WBS - Area 4		30.0d	10-Feb-25 A	21-Mar-25 A	
2095	EN-DM-A4-10	Remove Apron Concrete - Phase C Area 4	30.0d	10-Feb-25 A	21-Mar-25 A	
2096	WBS - Area 3		68.0d	27-Jan-25 A	30-Apr-25 A	
2097	EN-DM-A3-10	Remove Apron Concrete - Phase C Area 3	68.0d	27-Jan-25 A	30-Apr-25 A	
2098	WBS - Area 2		189.0d	26-Feb-25 A	20-Nov-25 A	
2099	EN-DM-A2-10	Remove Apron Concrete - Phase C Area 2	58.0d	26-Feb-25 A	16-May-25 A	
2100	EN-DM-A2-30	Commence Crushed Concrete Install at Apron Perimeter Edge - Phase C Area 2	0.0d	8-Jul-25 A		

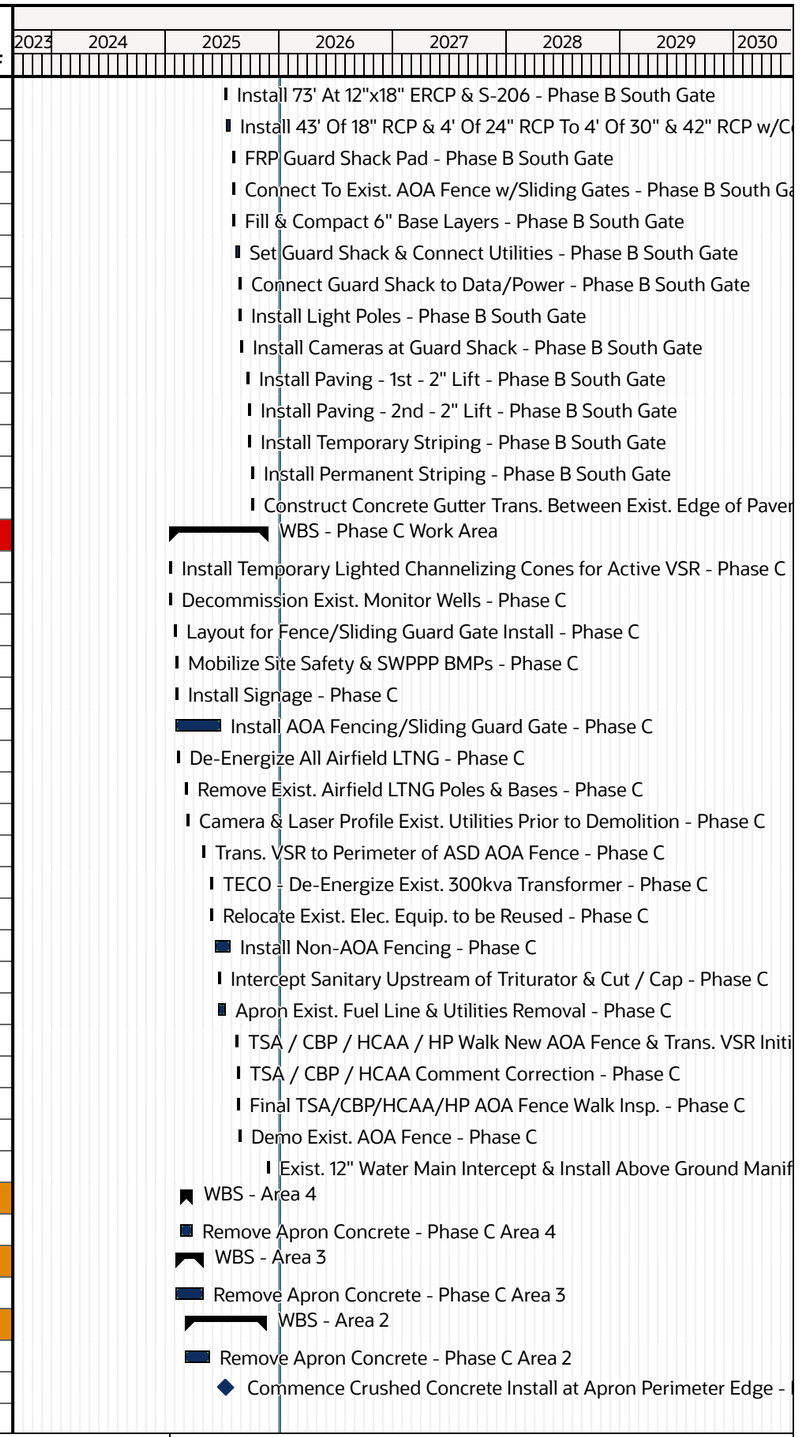


	ID	Name	Dur	Start	Finish	TF
2101	EN-DM-A2-20	Install 2" Non-Potable HDPE Water Service to Truck Wash Locations - Phase C ...	8.0d	11-Nov-25 A	20-Nov-25 A	
2102	WBS - Area 1		171.0d	10-Feb-25 A	9-Oct-25 A	
2103	EN-DM-A1-10	Saw Cut Limits of Apron Demolition - Phase C Area 1	4.0d	10-Feb-25 A	13-Feb-25 A	
2104	EN-DM-A1-70	Remove Apron Concrete - Phase C Area 1	34.0d	21-Apr-25 A	6-Jun-25 A	
2105	EN-DM-A1-100	Crushed Concrete Ready for Paving Contractor - Phase C Area 1	0.0d		6-Jun-25 A	
2106	EN-DM-A1-40	Remove Exist. Drainage Structure, Partial Drainage Pipe & Plug Pipe - Phase C ...	2.0d	11-Jun-25 A	12-Jun-25 A	
2107	EN-DM-A1-50	Demo Exist. Light Poles (Keep J-Box Active) - Phase C Area 1	2.0d	14-Jul-25 A	15-Jul-25 A	
2108	EN-DM-A1-60	All Exist. Wall Pack LTNG Inside Tunnel to Be Demolished w/Conduit & Wire - P...	5.0d	11-Aug-25 A	15-Aug-25 A	
2109	EN-DM-A1-30	Final Utility Cut & Caps & SIDA Fence Sign Offs Complete - Phase C Area 1	0.0d		15-Aug-25 A	
2110	EN-DM-A1-80	Close Bessie Coleman Service Road - Phase C Area 1	0.0d		15-Aug-25 A	
2111	EN-DM-A1-110	Demo First Half of Tunnel Structure - Phase C Area 1	34.0d	18-Aug-25 A	3-Oct-25 A	
2112	EN-DM-A1-90	Install Temporary Strut Support System at Tunnel - Phase C Area 1	29.0d	29-Aug-25 A	9-Oct-25 A	
2113	EN-DM-A1-120	Remove Exist. GDWY Pile Caps (3) - Phase C Area 1	5.0d	22-Sep-25 A	26-Sep-25 A	
2114	WBS - Soil Cut & Grade		39.0d	1-Sep-25 A	24-Oct-25 A	
2115	EN-DM-10	Cut FIS Low Area	39.0d	1-Sep-25 A	24-Oct-25 A	
2116	EN-DM-20	Cut Apron High Area	30.0d	8-Sep-25 A	17-Oct-25 A	
2117	WBS - Dewatering		35.0d	30-Sep-25 A	17-Nov-25 A	
2118	EN-DM-30	Install Underdrain Low Area - Phase C Dewatering	11.0d	30-Sep-25 A	14-Oct-25 A	
2119	EN-DM-40	Install Sump Structure - Phase C Dewatering	2.0d	30-Sep-25 A	1-Oct-25 A	
2120	EN-DM-100	Install Underdrain High Area - Phase C Dewatering	10.0d	3-Oct-25 A	16-Oct-25 A	
2121	EN-DM-50	Install Settlement Tanks - Phase C Dewatering	1.0d	6-Oct-25 A	6-Oct-25 A	
2122	EN-DM-80	Install Piping from Sump to Discharge - Phase C Dewatering	22.0d	17-Oct-25 A	17-Nov-25 A	
2123	EN-DM-70	Install Pumps - Phase C Dewatering	5.0d	31-Oct-25 A	6-Nov-25 A	
2124	EN-DM-90	Dewatering System Active - Phase C Dewatering	0.0d		17-Nov-25 A	
2125	WBS - Fuel Tank Relocation		24.0d	20-Feb-25 A	25-Mar-25 A	
2126	EN-UR-FT-100	Remove & Replace Exist. Curb/Gutter to Maintain Drainage - Phase C Tank Relo	1.0d	20-Feb-25 A	20-Feb-25 A	
2127	EN-UR-FT-110	Demo & Replace Pavement To Provide Lvl. Ground for Fuel Tank - Phase C Tank...	1.0d	20-Feb-25 A	20-Feb-25 A	
2128	EN-UR-FT-20	FRP New Pad - Phase C Tank Relo	14.0d	21-Feb-25 A	12-Mar-25 A	
2129	EN-UR-FT-90	Install Elec. Service Feed to Tank - Phase C Tank Relo	6.0d	3-Mar-25 A	10-Mar-25 A	
2130	EN-UR-FT-50	Demo Exist. MBLC Panel - Phase C Tank Relo	1.0d	3-Mar-25 A	3-Mar-25 A	
2131	EN-UR-FT-120	Install NEMA 3R 240v/60A MCB 1PH Panel w/(4) 20A Breakers to Serve Reloca...	1.0d	10-Mar-25 A	10-Mar-25 A	
2132	EN-UR-FT-40	7 Day Cure on Concrete - Phase C Tank Relo	4.0d	12-Mar-25 A	15-Mar-25 A	
2133	EN-UR-FT-80	Decommission Exist. Tank - Phase C Tank Relo	1.0d	14-Mar-25 A	14-Mar-25 A	
2134	EN-UR-FT-30	Pressure Test Prior to Move - Phase C Tank Relo	1.0d	17-Mar-25 A	17-Mar-25 A	
2135	EN-UR-FT-60	Demo Exist. Shut Off Switch & Conduit - Phase C Tank Relo	2.0d	17-Mar-25 A	18-Mar-25 A	
2136	EN-UR-FT-70	Exist. Timer Removal (Salvage for Relocation to New Panel) - Phase C Tank Relo	1.0d	17-Mar-25 A	17-Mar-25 A	
2137	EN-UR-FT-150	Relocate Fuel Tank - Phase C Tank Relo	1.0d	18-Mar-25 A	18-Mar-25 A	
2138	EN-UR-FT-140	Relocate/Install Exist. Timer - Phase C Tank Relo	1.0d	20-Mar-25 A	20-Mar-25 A	
2139	EN-UR-FT-160	Pressure Test Post Relocation - Phase C Tank Relo	1.0d	24-Mar-25 A	24-Mar-25 A	
2140	EN-UR-FT-130	Install Conduit & Emergency Shut Off Switch - Phase C Tank Relo	1.0d	24-Mar-25 A	24-Mar-25 A	
2141	EN-UR-FT-170	Refill Fuel Tank - Phase C Tank Relo	0.0d		25-Mar-25 A	
2142	WBS - Bessie Coleman Closure Detour		132.0d	21-Apr-25 A	24-Oct-25 A	

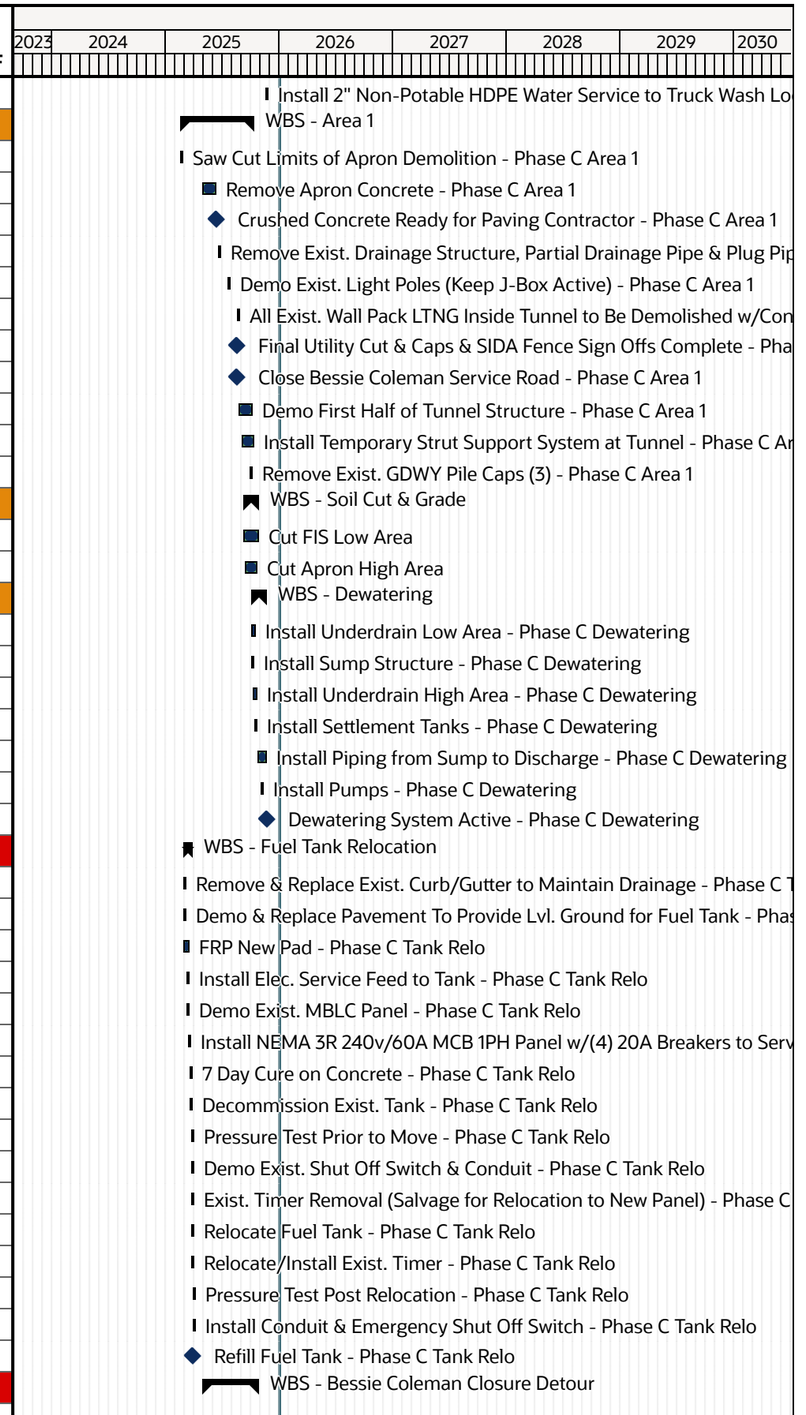


	ID	Name	Dur	Start	Finish	TF
2143	EN-BC-20	Remove Exist. Oak Tree - Bessie Coleman Closure	5.0d	21-Apr-25 A	25-Apr-25 A	
2144	EN-BC-30	Construct Sediment Barrier/Staked Turbidity Barrier (Erosion Control) - Bessie ...	1.0d	21-Apr-25 A	21-Apr-25 A	
2145	EN-BC-40	Cut & Clear for Curb/Asphalt - Vacuum Excavate - Bessie Coleman Closure	11.0d	25-Apr-25 A	9-May-25 A	
2146	EN-BC-50	Reclaim Water Valves to Be Adjusted - Bessie Coleman Closure	4.0d	30-Apr-25 A	5-May-25 A	
2147	EN-BC-10	Install MOT & Temp Fence - Bessie Coleman Closure	7.0d	1-May-25 A	9-May-25 A	
2148	EN-BC-60	Fill & Compact Subgrade Layer - Bessie Coleman Closure	5.0d	6-May-25 A	12-May-25 A	
2149	EN-BC-80	Form & Pour Curbs - Bessie Coleman Closure	4.0d	14-May-25 A	19-May-25 A	
2150	EN-BC-70	Fill & Compact 6" Base Layers - Bessie Coleman Closure	6.0d	21-May-25 A	29-May-25 A	
2151	EN-BC-RFI056-10	Procure Revised Signage per RFI 00056 - Bessie Coleman Closure	31.0d	23-May-25 A	8-Jul-25 A	
2152	EN-BC-90	Install Asphalt 1st - 2" Lift - Bessie Coleman Closure	1.0d	9-Jun-25 A	9-Jun-25 A	
2153	EN-BC-120	Install Asphalt 2nd - 2" Lift - Bessie Coleman Closure	1.0d	9-Jun-25 A	9-Jun-25 A	
2154	EN-BC-110	Install All Detour/Road Closure/Directional Signage (Area 1) - Bessie Coleman ...	5.0d	10-Jul-25 A	16-Jul-25 A	
2155	EN-BC-130	Install Temporary Striping (Area 1) - Bessie Coleman Closure	1.0d	14-Jul-25 A	14-Jul-25 A	
2156	EN-BC-100	Install FDOT Type 3 Barricades (Signs Mounted on Barricade) - Bessie Coleman ...	1.0d	15-Aug-25 A	15-Aug-25 A	
2157	EN-BC-140	Install Permanent Striping (Area 1) - Bessie Coleman Closure	2.0d	26-Aug-25 A	27-Aug-25 A	
2158	EN-BC-150	Stabilize Soil Post Grade Cut & Dewatering Install	5.0d	20-Oct-25 A	24-Oct-25 A	
2159	WBS - Weather Calendar Enabling		18.0d	28-Oct-25 A	14-Nov-25 A	
2160	EN-WE-10	Weather Days for Enabling Scope Dec 2024 thru Dec 2025	10.0d	28-Oct-25 A	6-Nov-25 A	
2161	EN-WE-20	Weather Surplus Days for Enabling Scope Dec 2024 thru Dec 2025	8.0d	7-Nov-25 A	14-Nov-25 A	
2162	WBS - Enabling Scope Substantial Completion		26.0d	21-Oct-25 A	25-Nov-25 A	
2163	EN-BC-160	QC Punch Walk for Demo Completion	4.0d	21-Oct-25 A	24-Oct-25 A	
2164	EN-PLA-10	Prep & Submit Pre-SC Documentation - Enabling Scope	1.0d	17-Nov-25 A	17-Nov-25 A	
2165	EN-PLA-40	HP/HCAA Substantial Completion Walk - Enabling Scope	1.0d	17-Nov-25 A	17-Nov-25 A	
2166	EN-PLA-30	HCAA Review & Approve Documentation - Enabling Scope	6.0d	18-Nov-25 A	25-Nov-25 A	
2167	WBS - Ground Improvements		99.0d	25-Jul-25 A	15-Dec-25 A	
2168	WBS - Milestones		71.0d	25-Jul-25 A	3-Nov-25 A	
2169	GI-HAM-20	Test Pile Program LOE - DIP/LTP	19.0d	25-Jul-25 A	20-Aug-25 A	
2170	GI-100	Test Pile Program Complete - DIP/LTP	0.0d		20-Aug-25 A	
2171	GI-30	Mobilize For Production Install - DIP/LTP	6.0d	27-Oct-25 A	3-Nov-25 A	
2172	WBS - Test Pile Program		18.0d	28-Jul-25 A	20-Aug-25 A	
2173	GI-40	Mobilize Equip. & Materials for Test Pile - DIP/LTP	5.0d	28-Jul-25 A	1-Aug-25 A	
2174	GI-70	Drill Reaction Piles - DIP/LTP	5.0d	4-Aug-25 A	8-Aug-25 A	
2175	GI-90	Test (4) Single Element DIPs - DIP/LTP	5.0d	11-Aug-25 A	15-Aug-25 A	
2176	GI-80	Install LTP on F6 & F8 Test Area - DIP/LTP	5.0d	11-Aug-25 A	15-Aug-25 A	
2177	GI-50	Test F8 Footing - DIP/LTP	2.0d	18-Aug-25 A	19-Aug-25 A	
2178	GI-60	Test F6 Footing - DIP/LTP	1.0d	20-Aug-25 A	20-Aug-25 A	
2179	WBS - Rigid Inclusions - Area 6		21.0d	3-Nov-25 A	3-Dec-25 A	
2180	GI-A6-20	DIP Install - RI DIPS Area 6	12.0d	3-Nov-25 A	18-Nov-25 A	
2181	GI-A6-30	Excavate - RI DIPS Area 6	8.0d	7-Nov-25 A	18-Nov-25 A	
2182	GI-A6-40	Cut Dip & Install Grout - RI DIPS Area 6	15.0d	11-Nov-25 A	3-Dec-25 A	
2183	GI-A6-50	Install Steel Caps - RI DIPS Area 6	15.0d	11-Nov-25 A	3-Dec-25 A	
2184	WBS - Rigid Inclusions - Area 2		25.0d	7-Nov-25 A	15-Dec-25 A	

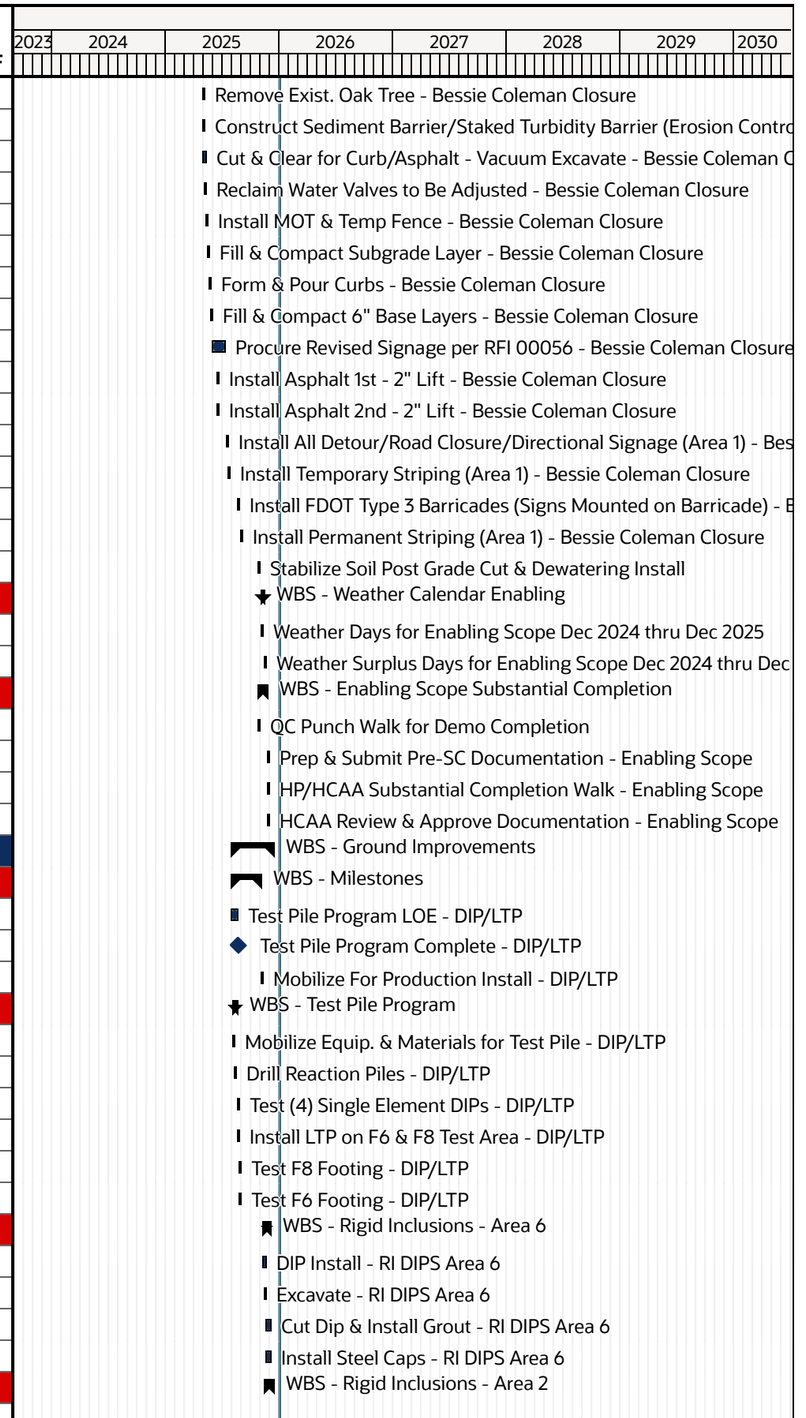


ID	Name	Dur	Start	Finish	TF
2185	GI-A2-100	DIP Install - RI DIPS Area 2	24.0d	7-Nov-25 A	12-Dec-25 A	
2186	GI-A2-110	Excavate - RI DIPS Area 2	11.0d	1-Dec-25 A	15-Dec-25 A	
2187	WBS - Foundations & Deep Underground		19.0d	24-Nov-25 A	22-Dec-25 A	
2188	WBS - Milestones		3.0d	24-Nov-25 A	28-Nov-25 A	
2189	GI-FS1000	Found. - Mobilize	3.0d	24-Nov-25 A	28-Nov-25 A	
2190	WBS - Foundations - Area 6		11.0d	1-Dec-25 A	15-Dec-25 A	
2191	GI-FS-A1-6810	Excavate Area For Found. - Area 6	11.0d	1-Dec-25 A	15-Dec-25 A	
2192	WBS - Deep Underground MEP - All Areas		5.0d	16-Dec-25 A	22-Dec-25 A	
2193	WBS - Deep Underground MEP - Area 2		5.0d	16-Dec-25 A	22-Dec-25 A	
2194	GI-FS-A2-5410	Excavate - Deep UG Sanitary- Plumber - Area 2.B.1	5.0d	16-Dec-25 A	22-Dec-25 A	
2195	GI-FS-A2-5470	Excavate - Deep UG Conduit - Elec. - Area 2.B.1	5.0d	16-Dec-25 A	22-Dec-25 A	
2196	GI-FS-A2-5550	Excavate - Deep UG Sanitary - Plumbing - Area 2.B.2	4.0d	17-Dec-25 A	22-Dec-25 A	
2197	WBS - Civil		2.0d	14-Oct-25 A	15-Oct-25 A	
2198	WBS - Truck Court		2.0d	14-Oct-25 A	15-Oct-25 A	
2199	WBS - Underground Utilities - Truck Court		2.0d	14-Oct-25 A	15-Oct-25 A	
2200	WBS - Pipe Bursting		2.0d	14-Oct-25 A	15-Oct-25 A	
2201	UND-PB-2700	CCTV For Design - Pipe Bursting	2.0d	14-Oct-25 A	15-Oct-25 A	
2202	WBS - Invitation To Bid (ITB)		40.0d	22-Aug-25 A	21-Oct-25 A	
2203	WBS - ITB -1 - Apron Pavement & Hydrant Fueling Construction		40.0d	22-Aug-25 A	21-Oct-25 A	
2204	WBS - Inter Project Relationships (IPR)		40.0d	22-Aug-25 A	21-Oct-25 A	
2205	IPR-ITB1-MLS18	MLS18 - Enabling Works - Demo Exist. AOA Fence - Phase C Complete	0.0d		22-Aug-25 A	
2206	IPR-ITB1-MLS19	MLS - Demolition of Half of the Tunnel Structure Complete	0.0d		3-Oct-25 A	
2207	IPR-ITB1-MLS1	MLS1 - Start Fuel Main Re-route (Crisdel)	0.0d	21-Oct-25 A		
2208	WBS - CENTRALIZED CHECKED BAGGAGE SYSTEM RELOCATION AND UPGRADES		97.0d	8-Aug-25 A	26-Dec-25 A	
2209	WBS - CCBS - DESIGN & ENGINEERING PHASE		76.0d	8-Aug-25 A	24-Nov-25 A	
2210	WBS - CFRP - Design		76.0d	8-Aug-25 A	24-Nov-25 A	
2211	CFRP-CC-DD-100	CFRP - Kick off Structural Requirements - Basis of Design (BOD)	1.0d	8-Aug-25 A	8-Aug-25 A	
2212	CFRP-CC-DD-110	CFRP - Design Proposal (HNTB-Base) Submit to HP	2.0d	11-Aug-25 A	12-Aug-25 A	
2213	WBS - CFRP Design Document Part 1		37.0d	13-Aug-25 A	3-Oct-25 A	
2214	CFRP-CC-DD-120	CFRP - Basis of Design Documents - Part 1	28.0d	13-Aug-25 A	22-Sep-25 A	
2215	CFRP-CC-DD-130	CFRP - Submit Part 1 Documents - Base to HNTB	1.0d	23-Sep-25 A	23-Sep-25 A	
2216	CFRP-CC-DD-140	CFRP - HNTB Review & Submit Documents to Structural Tec / HP Part 1	1.0d	23-Sep-25 A	23-Sep-25 A	
2217	CFRP-CC-DD-150	CFRP - Structural Tec. Design Part 1 (first 2 sectors)	3.0d	24-Sep-25 A	26-Sep-25 A	
2218	CFRP-CC-DD-160	CFRP - Structural Tec. Submits Design Part 1 (first 2 sectors)	5.0d	29-Sep-25 A	3-Oct-25 A	
2219	WBS - CFRP Design Document Part 2		44.0d	24-Sep-25 A	24-Nov-25 A	
2220	CFRP-CC-DD-170	CFRP - Basis of Design Documents - Part 2	9.0d	24-Sep-25 A	6-Oct-25 A	
2221	CFRP-CC-DD-175	CFRP - Submit Part 2 Documents - Base to HNTB	1.0d	7-Oct-25 A	7-Oct-25 A	
2222	CFRP-CC-DD-180	CFRP - HNTB Review & Submit Documents to Structural Tec / HP Part 2	1.0d	8-Oct-25 A	8-Oct-25 A	
2223	CFRP-CC-DD-185	CFRP - Structural Tec. Design Part 2 (second 2 sectors)	8.0d	9-Oct-25 A	20-Oct-25 A	
2224	CFRP-CC-DD-190	CFRP - Structural Tec. Submits Design Part 2 (second 2 sectors)	1.0d	21-Oct-25 A	21-Oct-25 A	
2225	CFRP-CC-DD-200	CFRP - DB / Structural Tec. Verification Review	1.0d	22-Oct-25 A	22-Oct-25 A	
2226	CFRP-CC-DD-210	CFRP - Base to Respond to Comment (as applicable)	1.0d	23-Oct-25 A	23-Oct-25 A	

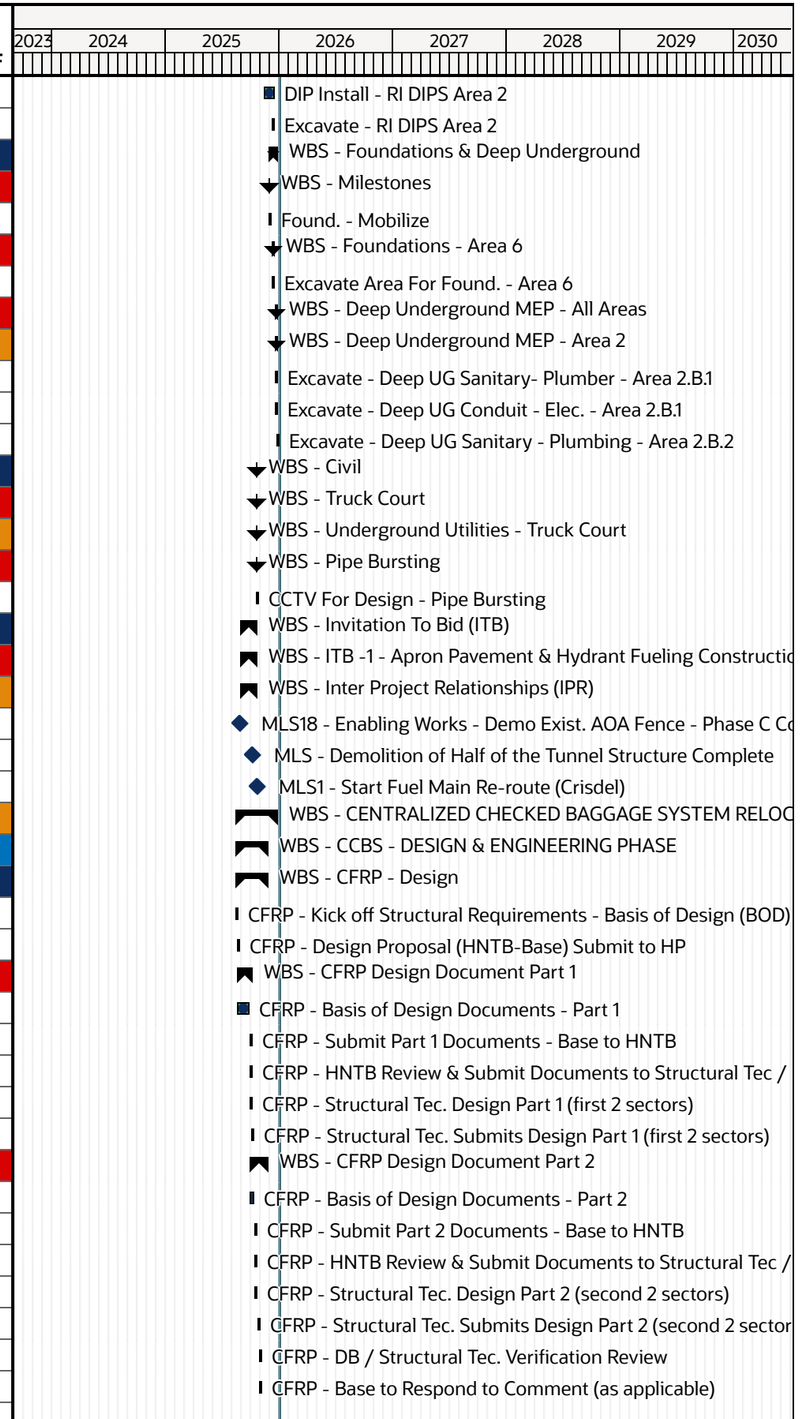

ID	Name	Dur	Start	Finish	TF
2227	CFRP-CC-DD-220 CFRP Contract Finalization	20.0d	28-Oct-25 A	24-Nov-25 A	
2228	WBS - CCBS - PROCUREMENT PHASE	51.0d	14-Oct-25 A	26-Dec-25 A	
2229	WBS - Owner Furnished Contractor Installed (OFCI)	41.0d	14-Oct-25 A	11-Dec-25 A	
2230	WBS - Tag & Trace Submittals	41.0d	14-Oct-25 A	11-Dec-25 A	
2231	WBS - Electrical Tag & Trace Submittals	41.0d	14-Oct-25 A	11-Dec-25 A	
2232	A64120 Prep & Submit Product Data for Elec. Tag & Trace Relocation	11.0d	14-Oct-25 A	28-Oct-25 A	
2233	A106440 Review & Approve (HP) Product Data for Elec.Tag & Trace Relocation	4.0d	29-Oct-25 A	3-Nov-25 A	
2234	A64130 Review & Approve (HNTB) Product Data for Elec. Tag & Trace Relocation	10.0d	4-Nov-25 A	17-Nov-25 A	
2235	A64140 HCAA Review & Approve Product Data for Elec. Tag & Trace Relocation	16.0d	18-Nov-25 A	11-Dec-25 A	
2236	WBS - Contractor Furnished & Install (CFCI)	47.0d	20-Oct-25 A	26-Dec-25 A	
2237	WBS - Part 2 Supplement B - Centralized Checked Baggage Etc.	47.0d	20-Oct-25 A	26-Dec-25 A	
2238	WBS - Baggage Handling System Procurement - CCBS - Part 2 Supp. B	47.0d	20-Oct-25 A	26-Dec-25 A	
2239	WBS - General BHS Submittals & Procurement - Part 2 Supp. B	35.0d	20-Oct-25 A	9-Dec-25 A	
2240	WBS - Site Specific Safety Plans Submittals - Part 2 Supp. B	35.0d	20-Oct-25 A	9-Dec-25 A	
2241	A101330 Prep & Submit Site Specific Safety Plans	13.0d	20-Oct-25 A	5-Nov-25 A	
2242	A101360 Review & Approve (HP) Site Specific Safety Plans	2.0d	6-Nov-25 A	7-Nov-25 A	
2243	A106590 Review & Approve (HNTB) Site Specific Safety Plans	11.0d	10-Nov-25 A	24-Nov-25 A	
2244	A106600 Review & Approve (HCAA) Site Specific Safety Plans	9.0d	25-Nov-25 A	9-Dec-25 A	
2245	WBS - Mechanical BHS Submittals & Procurement - Part 2 Supp. B	41.0d	28-Oct-25 A	26-Dec-25 A	
2246	WBS - General Mechanical BHS Submittals & Procurement - Part 2 Supp. B	41.0d	28-Oct-25 A	26-Dec-25 A	
2247	WBS - Mechanical Catalog Cut / Equipment Specs Submittals - Part 2 Supp. B	41.0d	28-Oct-25 A	26-Dec-25 A	
2248	A101620 Prep & Submit Mech. Catalog Cut / Equip. Specs	11.0d	28-Oct-25 A	11-Nov-25 A	
2249	A106820 Review & Approve (HP) Mech. Catalog Cut / Equip. Specs	2.0d	12-Nov-25 A	13-Nov-25 A	
2250	A106810 Review & Approve (HNTB) Mech. Catalog Cut / Equip. Specs	15.0d	14-Nov-25 A	8-Dec-25 A	
2251	A110550 Revise & Resubmit (Daifuku) Mech. Catalog Cut / Equip. Specs	13.0d	9-Dec-25 A	26-Dec-25 A	
2252	WBS - General Mechanical Assembly Detail Drawings Submittals - Part 2 Supp. B	26.0d	28-Oct-25 A	4-Dec-25 A	
2253	A101590 Prep & Submit General Mech. Assembly Detail Drawings	11.0d	28-Oct-25 A	11-Nov-25 A	
2254	A101650 Review & Approve (HP) General Mech. Assembly Detail Drawings	4.0d	12-Nov-25 A	17-Nov-25 A	
2255	A106870 Review & Approve (HNTB) General Mech. Assembly Detail Drawings	11.0d	18-Nov-25 A	4-Dec-25 A	
2256	WBS - Seq 1-Stage 1-Step 1 - Part 2 Supp. B	20.0d	18-Nov-25 A	17-Dec-25 A	
2257	WBS - BHS Mechanical Submittals [01-01-01]	20.0d	18-Nov-25 A	17-Dec-25 A	
2258	D1092 Prep & Submit Mech. Plan & Elev Dwg Set [01-01-01]	9.0d	18-Nov-25 A	2-Dec-25 A	
2259	D3536 Review & Approve (HP) Mech Plan & Elev Dwg Set [01-01-01]	2.0d	3-Dec-25 A	4-Dec-25 A	
2260	D3546 Review & Approve (HNTB) Mech Plan & Elev Dwg Set [01-01-01]	9.0d	5-Dec-25 A	17-Dec-25 A	
2261	WBS - Seq 1 - Stage 1 - Step 2	10.0d	2-Dec-25 A	15-Dec-25 A	
2262	WBS - BHS Mechanical Submittals [01-01-02]	10.0d	2-Dec-25 A	15-Dec-25 A	
2263	D1100 Prep & Submit Mech. Plan & Elev Dwg Set [01-01-02]	8.0d	2-Dec-25 A	11-Dec-25 A	
2264	D3586 Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-02]	2.0d	12-Dec-25 A	15-Dec-25 A	
2265	WBS - Seq 1 - Stage 1 - Step 3	10.0d	2-Dec-25 A	15-Dec-25 A	
2266	WBS - BHS Mechanical Submittals [01-01-03]	10.0d	2-Dec-25 A	15-Dec-25 A	
2267	D1108 Prep & Submit Mech. Plan & Elev Dwg Set [01-01-03]	8.0d	2-Dec-25 A	11-Dec-25 A	
2268	D3616 Review & Approve Mech Plan & Elev Dwg Set (HP)t [01-01-03]	3.0d	11-Dec-25 A	15-Dec-25 A	

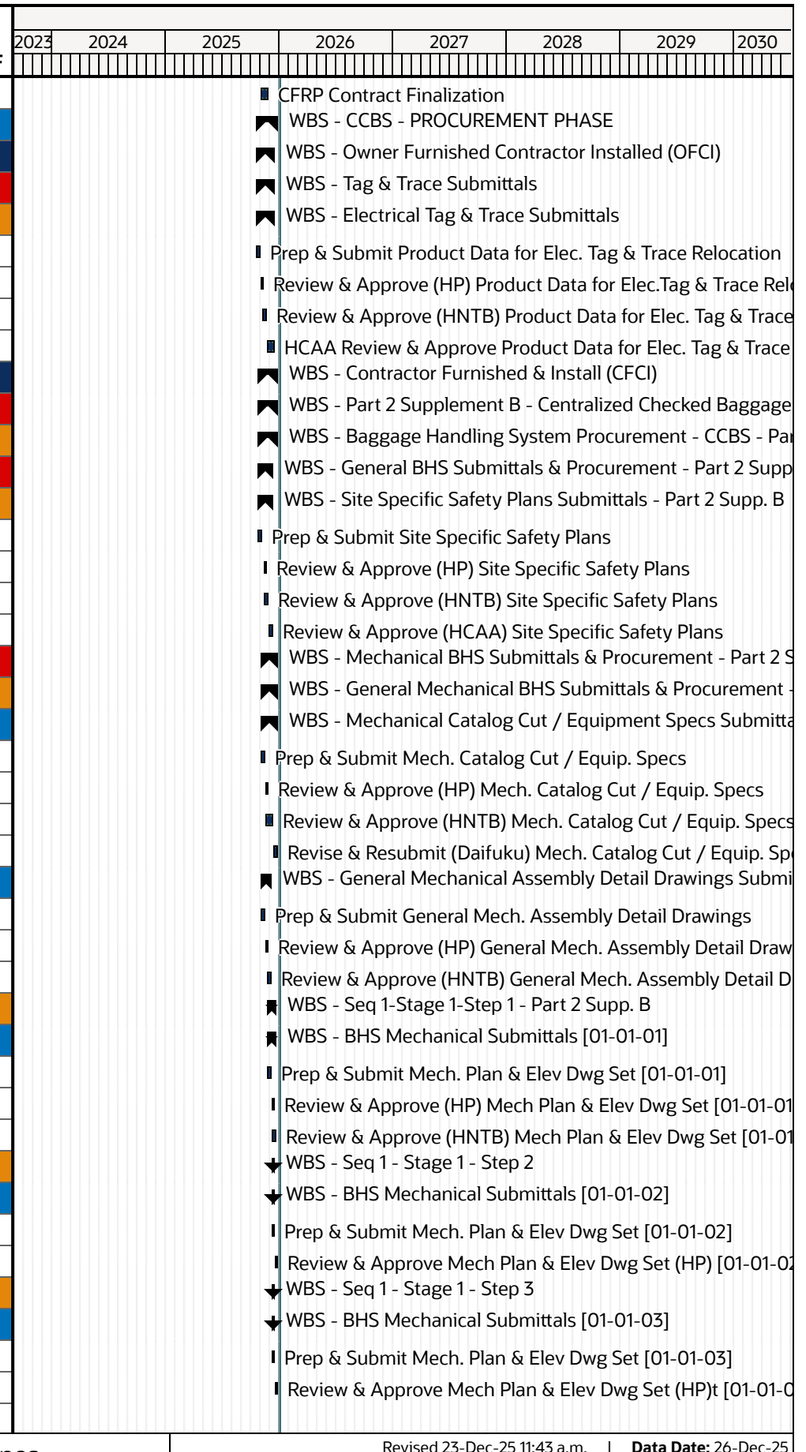

ID	Name	Dur	Start	Finish	TF
2269	WBS - Seq 1 - Stage 1 - Step 4	10.0d	2-Dec-25 A	15-Dec-25 A	
2270	WBS - BHS Mechanical Submittals [01-01-04]	10.0d	2-Dec-25 A	15-Dec-25 A	
2271	D1115	Prep & Submit Mech. Plan & Elev Dwg Set [01-01-04]	8.0d	2-Dec-25 A	11-Dec-25 A
2272	D3656	Review & Approve Mech Plan & Elev Dwg Set (HP) [01-01-04]	2.0d	12-Dec-25 A	15-Dec-25 A
2273	WBS - CCBS - CONSTRUCTION PHASE	23.0d	20-Oct-25 A	19-Nov-25 A	
2274	WBS - Main Terminal CCBS Consolidation	23.0d	20-Oct-25 A	19-Nov-25 A	
2275	WBS - CCBS - Building Infrastructure	23.0d	20-Oct-25 A	19-Nov-25 A	
2276	WBS - BHS ROW Prep	23.0d	20-Oct-25 A	19-Nov-25 A	
2277	WBS - Tag & Trace	23.0d	20-Oct-25 A	19-Nov-25 A	
2278	WBS - Tag & Trace - Sequence 1 - Stage 1	23.0d	20-Oct-25 A	19-Nov-25 A	
2279	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 1	21.0d	20-Oct-25 A	17-Nov-25 A	
2280	TT-SQ1-SG1-A1-10	Tag & Trace - Sequence 1 - Stage 1 - Area 1	21.0d	20-Oct-25 A	17-Nov-25 A
2281	WBS - Tag & Trace - Sequence 1 - Stage 1 - Area 2	6.0d	12-Nov-25 A	19-Nov-25 A	
2282	TT-SQ1-SG1-A2-10	Tag & Trace - Sequence 1 - Stage 1 - Area 2	6.0d	12-Nov-25 A	19-Nov-25 A

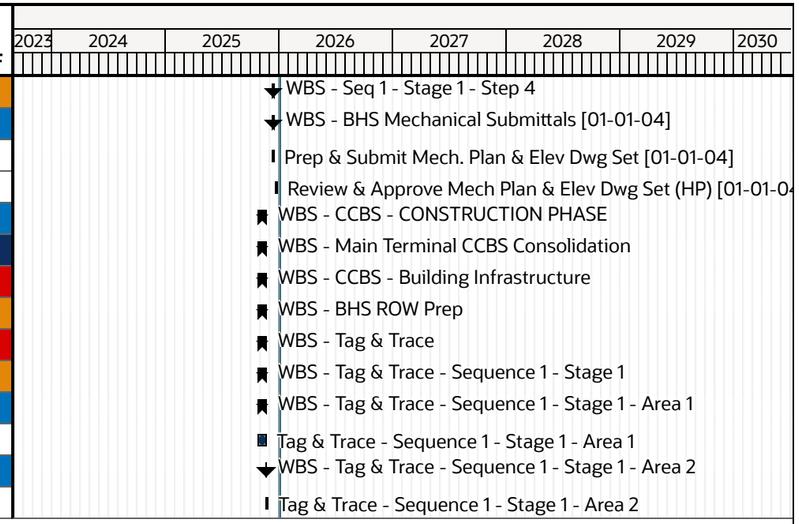

This submission requests funding for Airside D and CCBS Envelope and Interior Trades. Contracting recommendations will be submitted prior to any expenditure of funds, in accordance with our estimating plan. The basis of pricing for this GMP is as follows:

- CCBS 100% Drawing Set dated October 30, 2025
- ASD 100% Drawing Set dated October 30, 2025

SECTION 01020 - OWNER'S ALLOWANCES

PART 1 - GENERAL

1.01 DESCRIPTION OF REQUIREMENTS

A. Owner's allowances in the amounts indicated and as described below have been established for certain types of work. The Design-Builder will perform such Work only upon receipt of written work orders from the Owner. For this purpose, a Work Order will have the same meaning for requirements pertaining to submittals, approvals, etc., as modified, except the Work Order is only signed by the Owner.

B. If the Work Order directs that the allowance work be performed, the provisions of this Part 2 Contract, as modified, will govern the conduct and payment for this Work.

C. Definitions and Explanations: All Work, including any allowance work if authorized, shall be performed in full compliance with the requirements of the Contract. All allowance work, if and when authorized, shall be performed by the Design-Builder in accordance with the Work Order.

1. The Design-Builder shall coordinate allowance Work with related Work to ensure that each selection is completely integrated and interfaced with related Work, and shall include all aspects of work to fully integrate the work with all other Work and Related Work.

D. Work Order Data: Where applicable, include in each Work Order proposal the quantities of products being purchased, units requested, and labor hours, and furnish data to substantiate quantities. Indicate applicable taxes, delivery charges, and amounts of applicable trade discounts. Refer to this Part 2 Contract, Article 8, Changes in the Work for supporting documentation requirements.

E. Upon issuance of a Work Order, the Work Order funds will be tracked separately by Work Order number. If multiple subcontractors are employed for the Work Order, each Subcontractor's Pay Application will include a separate line with the Work Order number. Once work is complete on the Work Order, the Design-Builder must reconcile the Work Order no later than 30 days following completion of the work associated with the Work Order, as follows:

1. Provide Owner Project Management with a package containing cost support documents totaling the Cost of the Work Order.

2. Calculate mark-ups and fee using the same formula/calculations used to create the original Work Order budget.

3. Any unused Work Order funds will be returned to the Owner's Allowance budget via a negative Work Order.

The Contractor will forfeit their fee on the Work Order for any Work Orders that have not been reconciled within 30 days of the completion of the work associated with the Work Order, unless an extension is granted during the 30-day period in writing by the Owner, following the process above.

PART 2 - PRODUCTS

Not used.

PART 3 - EXECUTION

3.01 SCHEDULE OF OWNER'S ALLOWANCES

A. These allowances will cover the total cost of all Work authorized under a Work Order, including but not limited to design, cost of materials and equipment delivered and unloaded at the Project site, and all applicable taxes, permits, fees, labor, installation costs, and integration. The Design-Builder's fee for the work associated with the Work Order will be included in the Work Order amount.

B. Should the aggregate of charges for all approved Work Orders issued by the Owner under the allowances be less than the amount of the allowance, the Final GMP Contract Sum will be decreased by the amount of the difference. No Work will be performed that would cause total charges under the allowances to exceed the authorized allowance amount. The authorized allowance amount may be increased by Change Order. Should the aggregate charge for an approved Work Order issued by the Owner under the Allowance be less than the amount of the Work Order, the Owner may issue another Work Order in a negative amount to reconcile the Work Order. Such reconciliation Work Orders do not require executive management approval.

C. The following allowance amount will be included in the Guaranteed Maximum Price Proposal:

OWNER'S ALLOWANCE: Allow an amount of $48,000,000 of the GMP Contract Sum for:

1. **Utilities**: Repair, modify, removal, or replacement of existing utilities (sanitary, storm sewer, potable water, fire protection, mechanical systems, electrical systems, communications systems, security systems, etc.) when found to be deteriorated, damaged, or deficient that is not included in the contract scope of work.

2. **Structural Elements**: Repair, modify, removal, or replacement of existing structural elements when found to be deteriorated, damaged, or deficient that is not included in the contract scope of work.

3. **Airport Tenants & Entities**: Relocation, realignment and adjustments of Work required to accommodate airport tenants' space (airlines, car rental companies, concessions, FAA, TSA, etc.) and other common areas that is not included in the contract scope of work. Include all disciplines: civil,

architectural, structural, mechanical, plumbing, electrical, communications, fire protection, security, etc.

4. **Coordination with Other Projects**: Resolution between proposed work and the work of tenants and other contracts that is not included in the contract scope of work. Include all disciplines: civil, architectural, structural, mechanical, plumbing, electrical, communications, fire protection, shuttle systems, etc.

5. **Signage:** Additional Owner requested wayfinding, roadway, airfield, and dynamic signage that is not included in the Design-Builder's scope.

6. **Protection and MOT:** Additional Owner requested building or roadway protection and MOT that is not included in the Design-Builder's scope.

7. **Common Spaces Adjacent to Work**: Additional improvements related to common areas that are not included in the Design-Builder's scope of work.

8. **HCAA Departments**: Work associated with other HCAA Departments (Parking, Maintenance, IT, Operations, etc.) that is required but the scope of work is outside of the Design-Builder's scope of work.

9. **Unforeseen Conditions**: Any work that is required to address unforeseen conditions that is outside of the GMP scope of Work. The determination of "outside the scope of Work" would be at the absolute and sole discretion of the Owner.

10. **Airfield Improvements**: Additional Owner requested airfield improvements necessary for Airside D construction.

11. **Owner Trailer**: Additional Owner requested improvements to the Owner's Construction trailer.

12. Any Work not shown in the Contract Documents, but which is necessary to complete the Project, with the approval of Executive Management.

13. Any additional work associated with coordinating this Project with Alstom and ITB projects 1 - Apron, Site and Hydrant Fueling, 2 - Passenger Boarding Bridges, and 3 –Guideway that is not included in the contract scope, with the approval of Executive Management.

14. **Federal Tax/Tariff:** Owner's Allowance may be used for costs for any after-imposed Federal tax or tariff, provided Design-Builder warrants in writing that no amount for such newly imposed Federal tax or tariff was included in the GMP Sum as a contingency or otherwise.

15. **Sensory Room**: Any additional work associated with alterations or fit out of the Airside D Sensory room that is outside of the Design-Builder's scope of work.

16. **LED Installation**: Any work or coordination associated with the Light-Emitting Diode (LED) panels that is required but the work is outside of the Design-Builder's scope of work.

17. **Artwork:** All work associated with the installation of Owner provided artwork that is not included in the Design-Builder's scope of work. This includes, but is not limited to, coordination with artist team(s), design of structure(s) to support art, access to artwork for installation, rental of any materials, equipment, or temporary structures to support install of art, incorporation of artwork and associated structures into BIM model and project schedule.

18. **Contractor Allowances:** Costs associated with increasing funds in the event of a Contractor Allowance budget overrun, with approval of executive management.

19. **Acceleration:** Owner's Allowance may be used to accelerate the Work, or any portion of the Work, with approval of Owner's executive management.

20. **TSA Breakroom:** Any additional work associated with the Airside D TSA Breakroom that is outside of the Design-Builders scope of work.

21. **CCBS Trend Items:** Costs associated with additional scope related to the Centralized Checked Baggage System trend items.

D. Contract Time will not be extended as a result of the issuance of any Work Order under this Section 01020 – OWNER'S ALLOWANCES.

E. The GMP Contract Sum will not be adjusted for any costs of acceleration resulting from the issuance of Work Orders under this Section 01020 – OWNER'S ALLOWANCES. In addition, the Contract Sum will not be adjusted for any costs of acceleration of the whole work resulting from the issuance of Work Orders under this Section 01020 – OWNER'S ALLOWANCES.

END OF SECTION

Milestone #	Activity ID	Hensel Phelps Supplemental C Milestone Summary (Note 3)	Completion Date	Liquidated Damages
2	MLS-SUPP.C-02	Demo Second Half of Tunnel Structure Complete	12-Feb-26	See Note 1.
3	MLS-SUPP.C-03	Barrier Mounted AOA Fence Relocation Complete	25-Aug-26	See Note 1.
7	MLS-SUPP.C-07	*Alstom Early Turnover	8-Apr-27	$5,000 Per Day Liquidated Damage. See Note 2.
5	MLS-SUPP.C-05	Install of VGDS Found. & Conduits Complete	10-Nov-27	See Note 1.
10	MLS-SUPP.C-10	Concessions White Box	1-Jun-28	See Note 1.
11	MLS-SUPP.C-11	Complete Delta Tenant Spaces White Box - Apron Level	2-Jun-28	See Note 1.
17	MLS-SUPP.C-17	Complete Delta Tenant Spaces White Box - Concourse Level	18-Apr-28	See Note 1.
18	MLS-SUPP.C-18	Complete Delta Tenant Spaces White Box - Mezzanine Level	10-Dec-27	See Note 1.
8	MLS-SUPP.C-08	Complete Paving & Utilities Interface for PBB Installation Start	13-Jul-28	See Note 1.
12	MLS-SUPP.C-12	SSCP Area Ready for TSA Equipment Installation	21-Aug-28	See Note 1.
13	MLS-SUPP.C-13	CBP Area Finishes Complete	10-Oct-28	See Note 1.
14	MLS-SUPP.C-14	TSA ISAT BHS Testing Complete	13-Dec-28	See Note 1.
15	MLS-SUPP.C-15	Supplement C Project Substantial Completion (Phase 1)	2-Mar-29	$25,000 Per Day Liquidated Damage.
16	MLS-SUPP.C-16	Supplement C Project Substantial Completion (Phase 2 - CCBS 2-2)	14-Sep-29	$5,000 Per Day Liquidated Damage.

Note 1: The Owner may withhold whole or partial application for payment in accordance with the Part 2 contract terms.

Note 2: Train tube temporary dry-in, 110v temporary power available within 100 ft of space, Temporary conditioning of PDS/UPS room, and available temporary lighting.

Note 3: The milestone activity IDs, descriptions, and dates are established from Hensel Phelps Supplemental C GMP schedule dated December 26, 2025.

SECTION 01021 – DESIGN-BUILDER'S ALLOWANCES

PART 1 - GENERAL

1.01 DESCRIPTION OF REQUIREMENTS

A. Design-Builder's allowances in the amounts indicated and as described below have been established for certain types of work.

B. The provisions of this Part 2 Contract, as modified, will govern the conduct and payment for this Work.

C. Definitions and Explanations: All Work, including any allowance work if authorized, shall be performed in full compliance with the requirements of the Contract.

1. Coordinate allowance Work with related Work to ensure that each selection is completely integrated and interfaced with related Work and shall include all aspects of work to fully integrate the work with all other Work and Related Work.

D. Reserved.

E. Design-Builder's Allowance funds will be tracked separately on the Design-Builder's Schedule of Values by category and the amount of the Cost of Work. If multiple subcontractors are employed for the category, each Subcontractor's Pay Requisition will include a separate line with the category that will flow to the Design-Builder's Schedule of Values. Once Design-Builder's Allowance work is complete for a category of Work, the Design-Builder has 30 days in which to reconcile the Design-Builder's Allowance work, as follows:

1. Provide Owner Project Management with a package containing cost support documents totaling the Cost of Work.

2. Calculate mark-ups and fee using the same formula/calculations used to create the original Design-Builder's Allowance budget.

3. Any unused Design-Builder's Allowance funds will be returned to the Design-Builder's allowance budget.

The Design-Builder will forfeit their fee on the Design-Builder's Allowance Work for any work that has not been reconciled within 30 days of the completion of the work, following the process above.

PART 2 - PRODUCTS

Not used.

PART 3 - EXECUTION

3.01 SCHEDULE OF DESIGN-BUILDER'S ALLOWANCES

A. These allowances will cover the total cost of all Work authorized under a Design-Builder's Allowance category, including but not limited to design, cost of materials and equipment delivered and unloaded at the Project site, and all applicable taxes, permits, fees, labor, installation costs and integration as applicable. The Design-Builder's percentage, overhead and profit for the allowance are excluded from the Design-Builder's Allowance amount, but are included in the GMP.

B. Should the charges for each category of Design-Builder's Allowances be less than the amount of the allowance, the Final GMP Contract Sum will be decreased by the amount of the difference. No Work will be performed that would cause total charges under the allowances to exceed the authorized allowance amount. The authorized allowance amount may be increased by Change Order.

C. The following allowance amounts will be included in the Guaranteed Maximum Price Proposal:

DESIGN-BUILDER'S ALLOWANCE: For Projects 8500 23 & 8515 24, allow an amount of $40,415,268 of the GMP Contract Sum for:

1. Subcontractor Insurance Premiums - $500,000
   Liability Insurance wrap-up program has been included. In our purchasing interviews subcontractors have expressed concern at the requested insurance limits. Design-Builder is working to gather cost increases associated with unusually high insurance premiums for Automotive Liability, Professional Liability, Environmental Impairment (Pollution) Liability, Cyber Liability & Data Storage, and Utility and Railroad Protective. An allowance has been included to potentially cure any deficiencies in coverage in the subcontractor policies.

2. Division 01 Changes - $100,000
   General Requirements issued to the subcontractors are draft specification sections as HCAA is in the process of updating these sections. Once complete Design-Builder will provide these specification sections to the subcontractors proposed for award and allow them to price any impacts associated with changes made to the draft specifications. The basis for changes shall be the specifications issued to the subcontractors as part of the bid packages viewable in the links provided in the "Bid Documents" section of this GMP submission.

3. Trade delta to Second Place Bids - $1,200,000
   In the event of a subcontractor termination resulting in higher costs for replacing a subcontractor, (or recommended subcontractor) after GMP establishment which are not covered by surety, sufficient evidence to document the added costs will be submitted. A Contractor Allowance has been included in the GMP associated with this potential cost. This Allowance will sunset on 3/31/25. Should trade partner purchasing not be completed by this date, Design-Builder may request approval of

an extension to this sunset date.

4. Contaminated Soils, Asbestos Fuel Pipe, and Water Management - $3,000,000
Contamination with aviation fuel in soil and water. Aviation fuel contaminated soil and ground water have been identified in the Airside D footprint per the November 30, 2023, report submitted to HCAA. This allowance has been established for the removal, disposal and replacement of contaminated materials within the limits of the identified plumes for the enabling program only. Subsequent GMPs will assess similar program needs and adjustments to costs and systems may be required. This allowance may also be used to fund ancillary items related to the contamination such as Industrial Hygienist (IH) costs, and consumables items necessary as part of the cleanup operation.

    i. Contaminated Soils
        a. When working in the area of the existing fuel line and/or areas that soils tests result in an OVA reading of above 400ppm, the material must either be placed back in the same location from which it was excavated or, if an installation results in displacement of soils, the contaminated soils will be hauled to a lined dumpster for disposal to a class 1 landfill. Design-Builder will construct an exchange yard in its trailer park to store a stockpile of clean fill adjacent to a series for roll off/lined dumpsters. If a trade is excavating materials and they are determined to be over 400ppm and cannot be returned to the original location, the trade will haul the materials to the exchange yard and deposit the contaminated fill into the lined dumpster and then use the clean fill to back fill their operations. Exchange yard establishment, clean fill materials, and haul off/disposal of contaminated soils will be applied to the $3m allowance.

    ii. Contaminated Water
        a. Design-Builder has confirmed with City of Tampa (COT) Wastewater (WW) that there is no requirement to pretreat the dewatering discharge, as the contaminated water samples submitted to the City of Tampa from 2023 water sampling showed levels being below COT WW pretreatment levels. However, metering of discharge and pay an impact fee of $5.56/CCF (748 gallons) to COT Wastewater.
        b. Design Builder is currently in the permitting process with COT Building Dept to permit discharge into the sanitary system after the approval from COT WW. Once COT Building Dept provides any additional direction it will be shared with the Owner.
        c. Due to flow limits through the existing campus sanitary system the project may be required to treat the water on site to remove contaminates and discharge to the stormwater system.

d. Design Build team will continue the design, sizing and permitting of the dewatering process. If at any point during this process a challenge arises to the above outlined process, Design-Builder reserves the right to make a claim.

iii. Third Party Industrial Hygienist
1. Develop the following for compliance with working with contaminated soils and water:
a. Health and Safety Plan – Develop for their work along with review, comment and inspection of trade partners plans
b. Soil Management Plan – Will work with trade partners to develop site specifics plan to trade partners means and methods
c. Dewatering Plan and Permit support – Will work with trade partners to develop site specifics plan to trade partners means and methods

iv. Asbestos Fuel Pipe
1. Cost to abate asbestos fuel pipe.

5. Relocation / Moving Costs - $1,075,000
Utilization of a lump sum value for relocation costs per position for Design-Builder personnel to be relocated to Tampa for the Airside D program. The rate per position will cover all relocation expenses inclusive of travel, moving, and all other necessary costs. Design-Builder will inform the owner prior to the relocation of employees. The allowance value is established from the budgets listed in the table below.

Moving & Relocate (AS/PE/LeadVDC)	18	EACH	$ 25,000	$ 450,000
Moving & Relocate (OE/FE)	25	EACH	$ 15,000	$ 375,000
Moving & Relocate (PM/PS/QCM/SM)	5	EACH	$ 50,000	$ 250,000

6. Temporary Housing Costs - $192,000
This allowance shall cover temporary housing in the form of a furnished apartment, including utilities and associated ancillary costs, for employees assigned to the project who are not permanently relocating to the Airside D program. This allowance is based upon a duration of 48 months of housing at a rate of $4,000 per month.

The aforementioned options will only be applicable to persons that will be relocating to the Airside D program from a distance greater than 60 miles to the Project.

7. Subcontractor Bonds - $9,671,966
This allowance shall be utilized to fund subcontractor bonds. This allowance shall be allocated to the subcontractor's respective lump sum subcontract and paid on an actual cost basis. This allowance will be reduced to $200,000 six (6) months from Supplemental C's Notice to proceed.

8. Art Infrastructure Allowance - $1,000,000
   This allowance will be utilized to fund all construction and design costs that result from Owner's Art Selections, including, but not limited to, structural support, art specific lighting, public barriers, modifications to HVAC, modifications to building technology systems.

9. Owner Enclosure Consultant Allowance - $200,000
   This allowance shall be utilized to incorporate all construction and design costs that result from changes in the Work from the Owner's enclosure consultants Walker Consultants, French Engineering, or other similar consultants employed by the Owner.

10. ITB Contractor Fence Allowance - $500,000
    This allowance shall be utilized for all construction costs related to relocating fencing for the benefit of paving operations and security of the ITB 1 contractor. This is a scope shift from ITB 1 to the Design-Builder.

11. Trade Delta to Second Place Bids Allowance - $5,000,000
    This allowance shall be utilized in the event the apparent low bidder fails to execute its contract and provide required bonds with the Design-Builder. This allowance will sunset six (6) months from Supplemental C's Notice to proceed.

13. Owner Directed Interior Expanded Mockup Allowance - $225,000
    This allowance shall be utilized to contract and construct final mock-ups coordinated with the Owner as commented during the 90% Owner drawing review. This allowance will sunset sixteen (16) months from Supplemental C's Notice to proceed.

14. Municipal Utilities Permit and Field Comments Allowance - $1,000,000
    This allowance shall be utilized to incorporate all construction and design costs that result from municipal utilities permit and field comments. This allowance will sunset 12 months from Supplemental C's Notice to proceed.

15. Customs and Border Protection (CBP) Required UPS Allowance - $591,470
    This allowance shall be utilized to accommodate changes to the design and all construction costs associated with incorporating CBP's requirements for Uninterrupted Power Supply (UPS) back-up.

16. Centralized Checked Baggage System (CCBS) Trend Allowance - $5,000,000
    This allowance shall be utilized for the design and construction costs associated with the following trend estimates for the CCBS project:
    TE #205A – Non-Baggage Handling System (BHS) ROW Work for Added Explosive Detection System (EDS) Lines in Main Terminal due to A&C Inclusion.
    TE #211 – Unified High-Level Controls.
    TE #216 – Transportation Security Administration (TSA) RFV for the Usage of Liftgate Conveyors in the Checked Baggage Resolution Areas (CBRA).

TE #225 – Changes to the design based on TSA Review comments of the 100% TSA submission scheduled for 2/6/26.
TE #226 – Temporary UPS for Temporary AS3 EDS Machine.
TE #227 – Survey & Investigation of Existing EDS Condensate Drains. The Design-Builder will verify all floor drains in the Main Terminal's future Checked Baggage Inspection System (CBIS) function correctly.

17. Doors Frames, and Hardware Allowance - $4,429,300
    This allowance will be utilized to furnish and install Doors, Frames & Hardware. These elements remain in design and are pending final approval from the Owner. This allowance will sunset 6 months from Supplemental C's Notice to proceed.
18. Play Structures Allowance - $70,000
    This allowance will be utilized to furnish, install, and certify the play structures within Airside D.

19. Furniture, Fixtures, & Equipment (FF&E) Allowance - $6,660,532
    This allowance will be utilized to furnish and install FF&E for Airside D & CCBS.

D. Contract Time will not be extended as a result of the issuance of any Work under this Section 01021 – DESIGN-BUILDER'S ALLOWANCES.

1. Notwithstanding the foregoing, for the Work associated with the following allowances: Owner's Enclosure Consultant Allowance, Municipal Utilities Permit Comments Allowance, CPB Required UPS Allowance, CCBS Trend Estimates Group Allowance and Furniture Fixtures and Equipment (FF&E) Allowance. the Design-Builder may make a claim for an increase in the Contract Time pursuant to Article 10 of the Part 2 Contract and Section 01315 of the Division 01 General Requirements. Such claims will include at a minimum a Time Impact Analysis demonstrating a delay to the current Project Completion date. The Owner will review the claim pursuant to the Part 2 Contract.

E. The GMP Contract Sum will not be adjusted for any costs of acceleration resulting from Design-Builders Allowance Work under this Section 01021 – DESIGN-BUILDER'S ALLOWANCES. In addition, the Contract Sum will not be adjusted for any costs of acceleration of the whole work resulting from the Design-Builders Allowance Work under this Section 01021 – DESIGN-BUILDER'S ALLOWANCES.

F. Any allowance funds remaining after the Sunset dates will be deducted from the GMP via deductive change order.

END OF SECTION
